

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting


General Topics:

- Stop & thinks start today - 1 per day this week
- Red flags - holiday tomorrow


UTILITY LEVEL MOD1

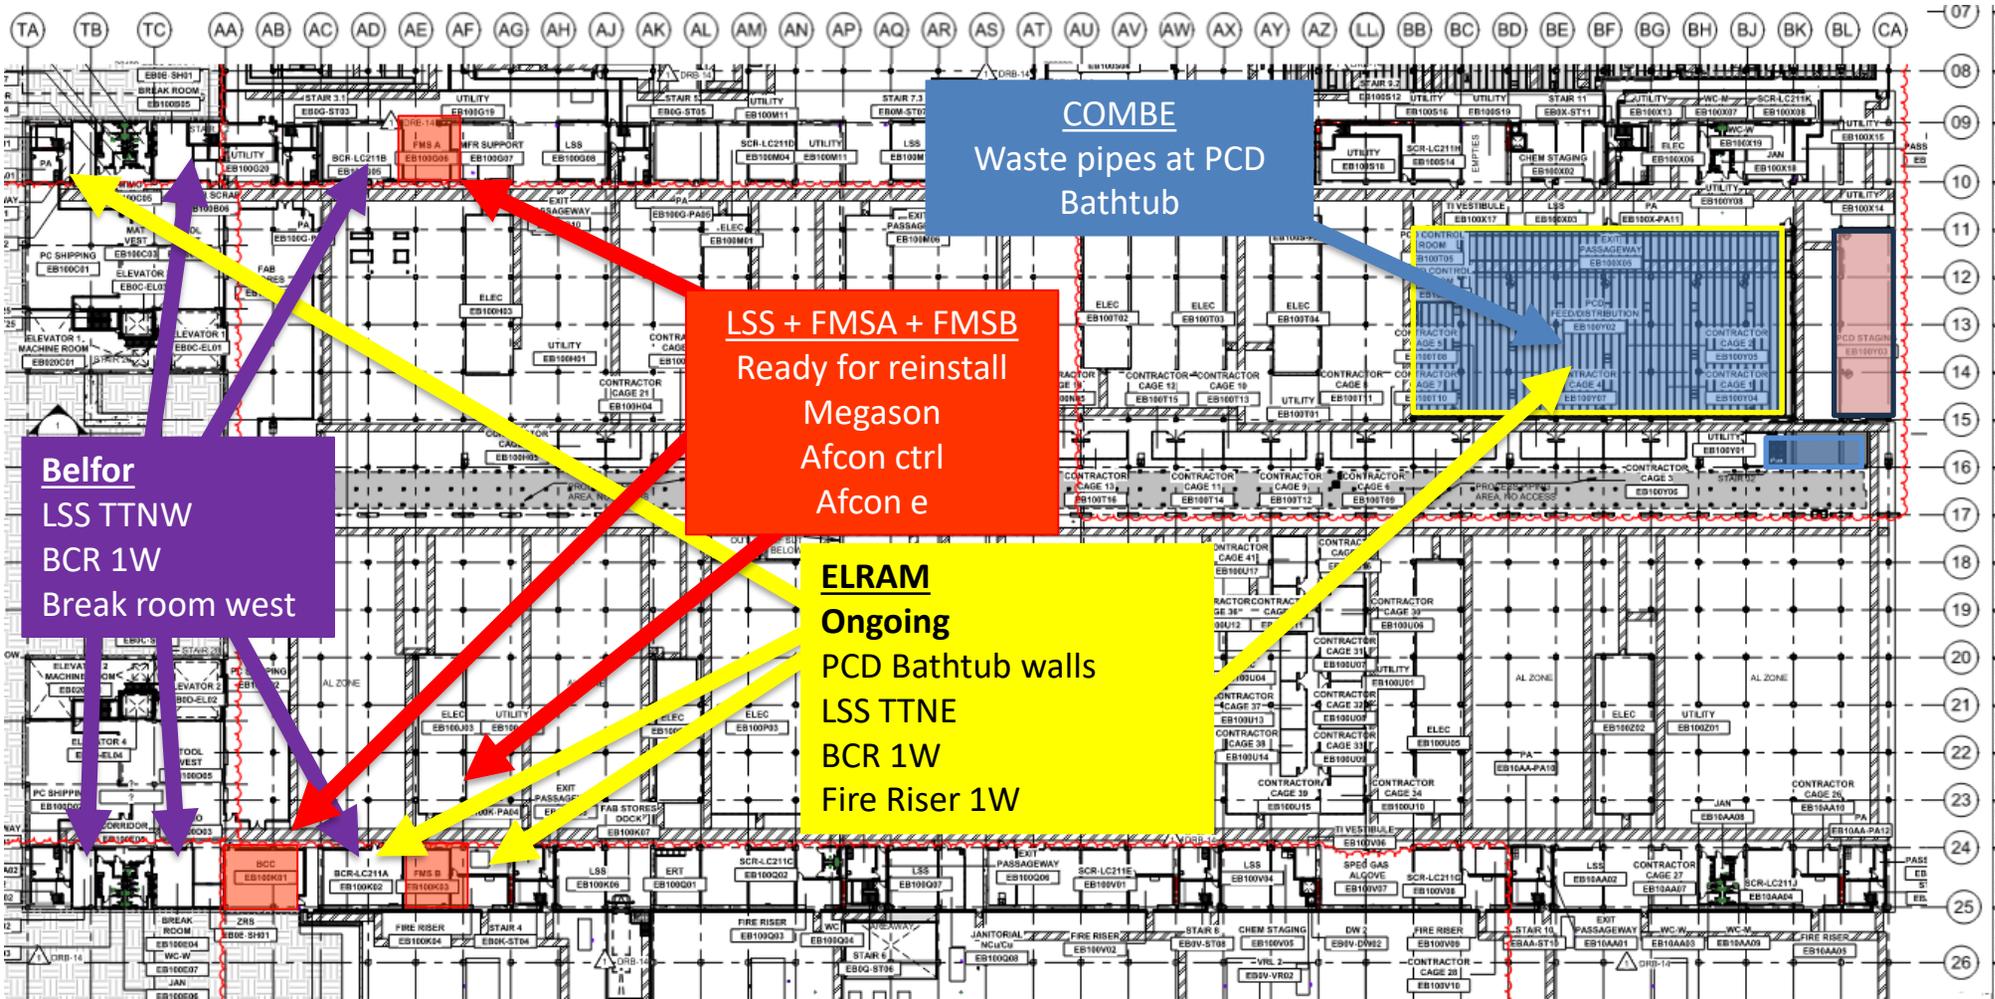


UTILITY LEVEL MOD2

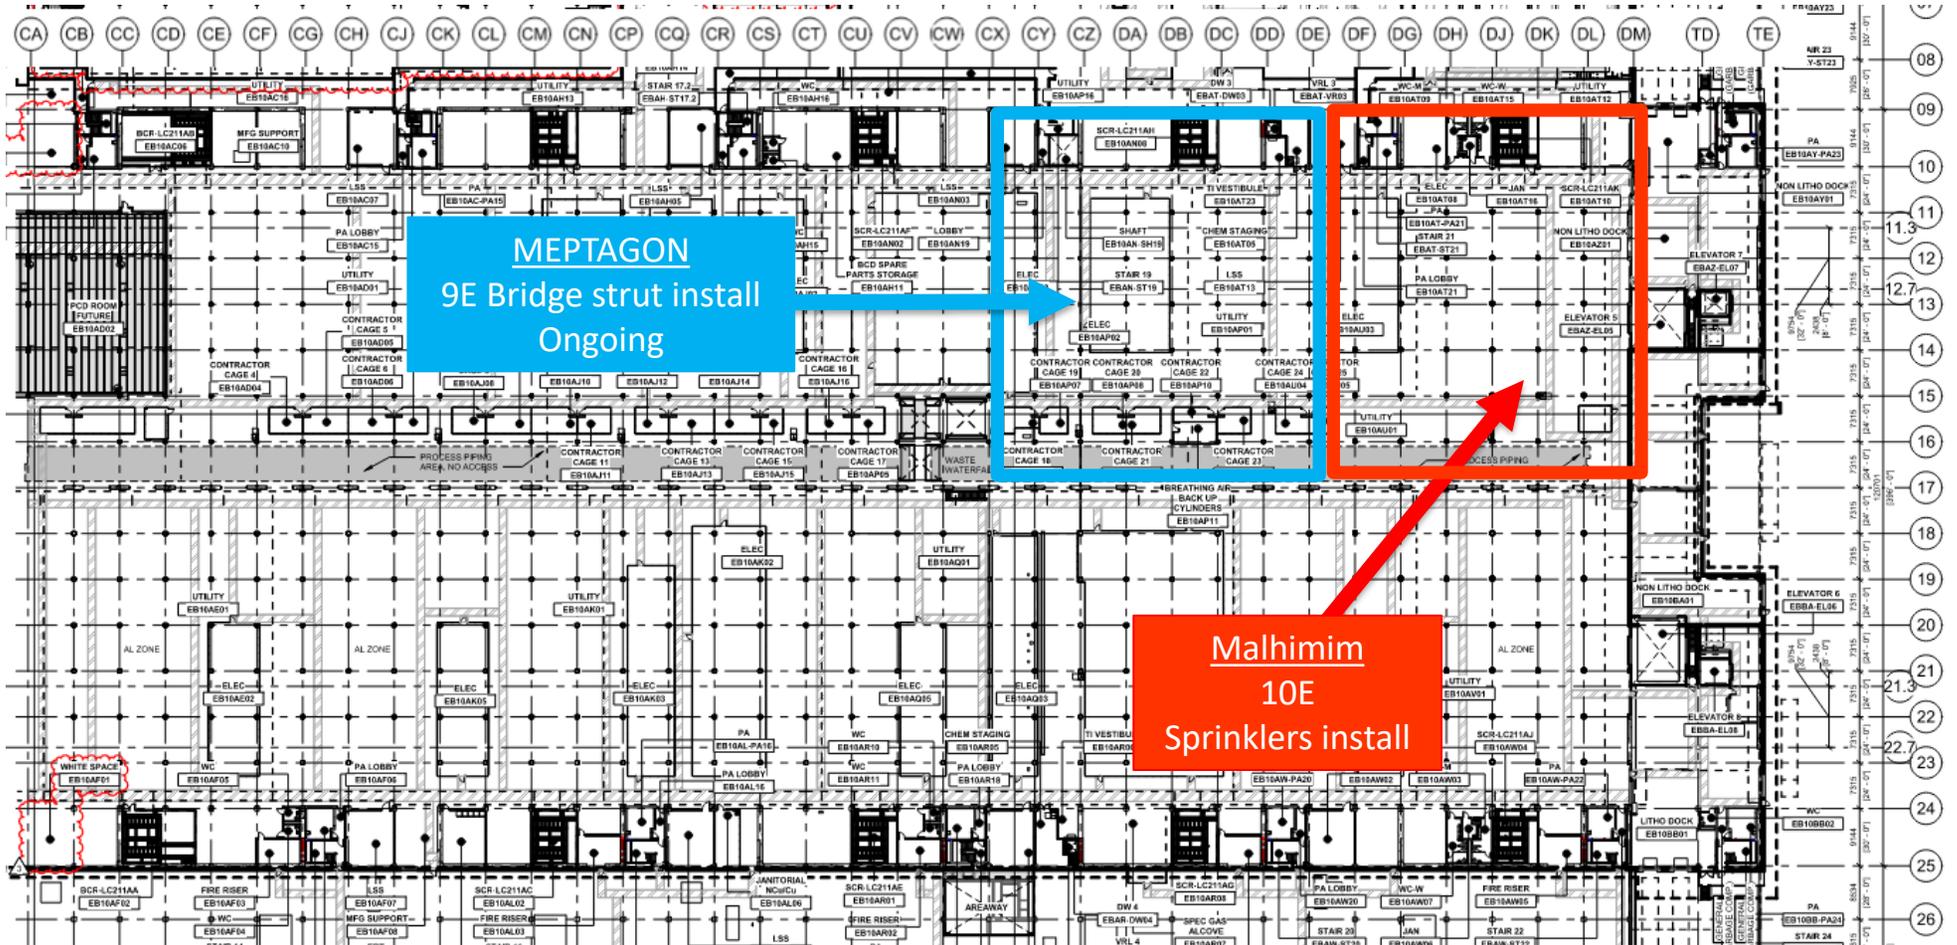

SUT 38.1 LEVEL

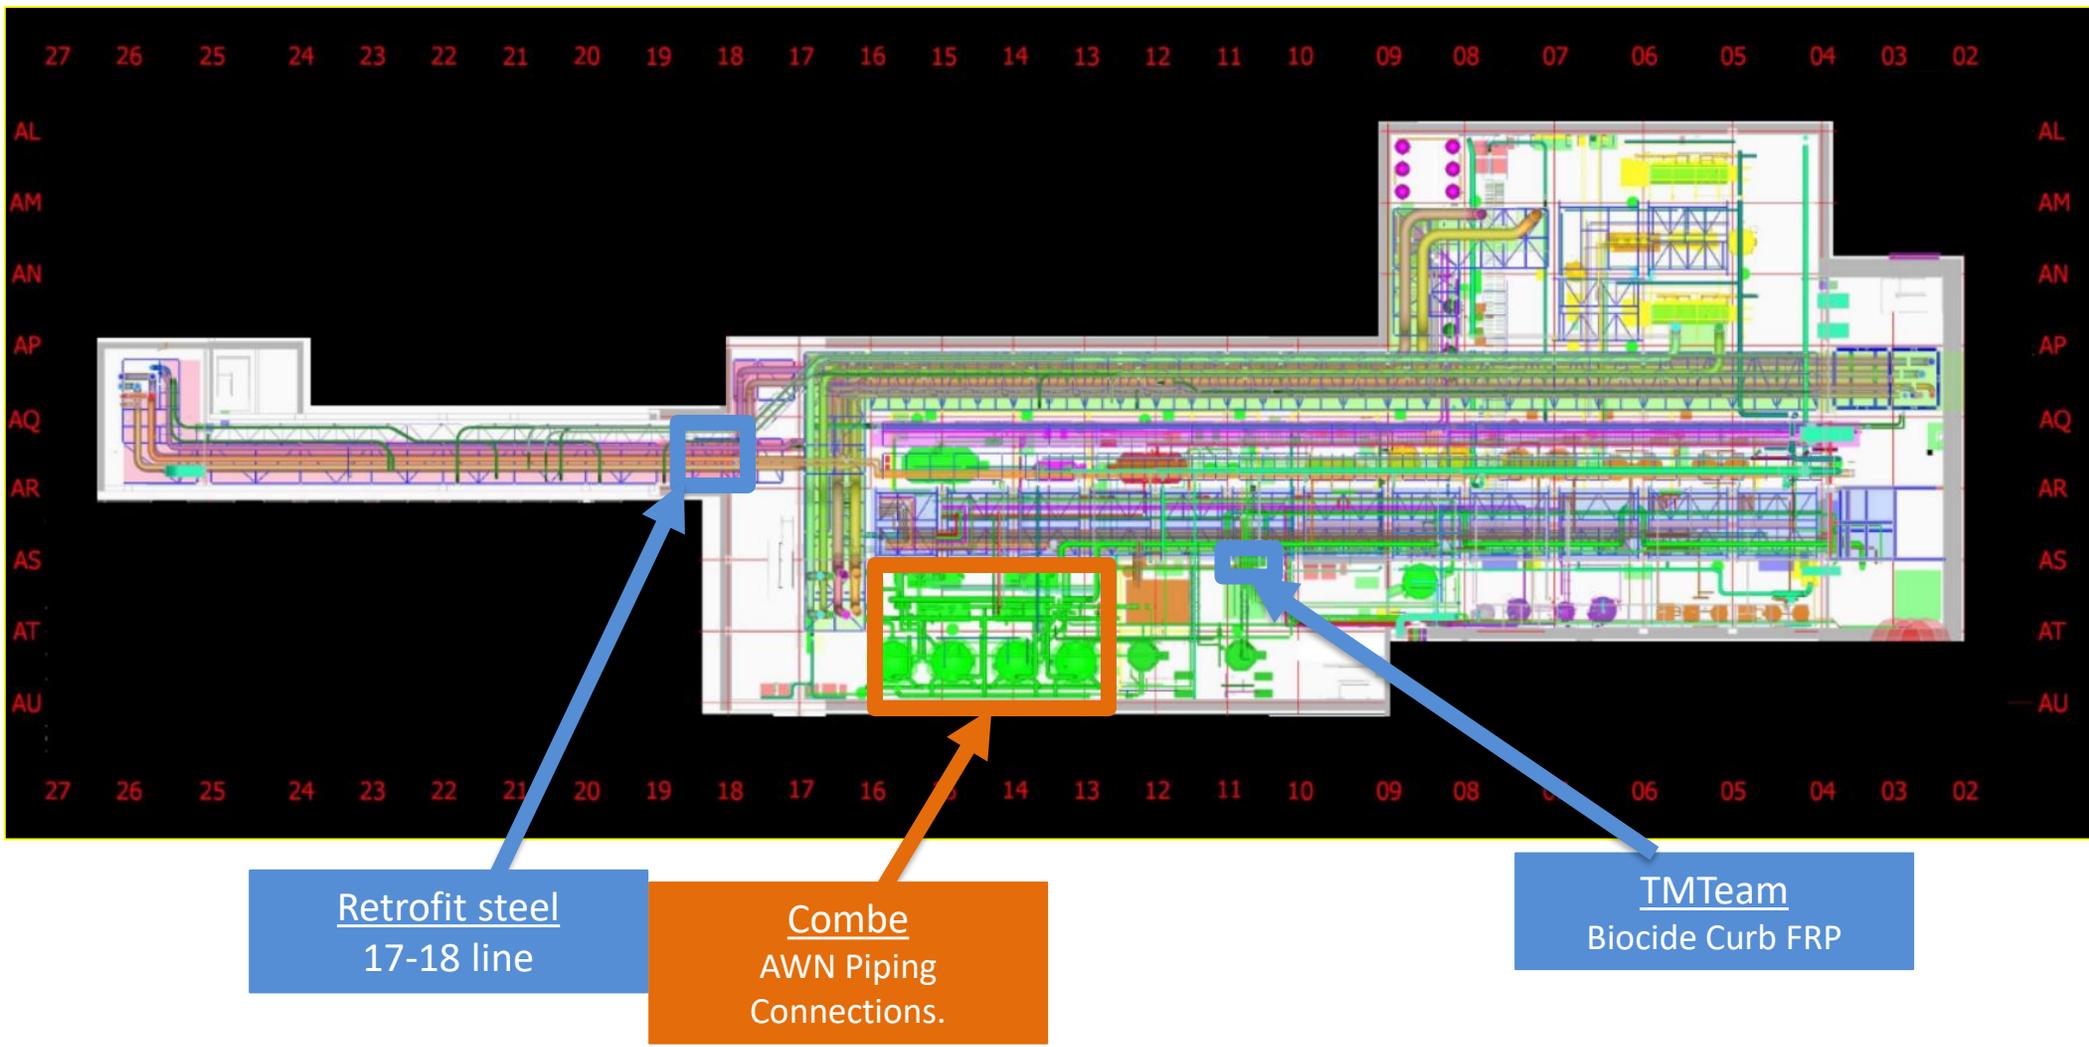

SUT 38.2 LEVEL

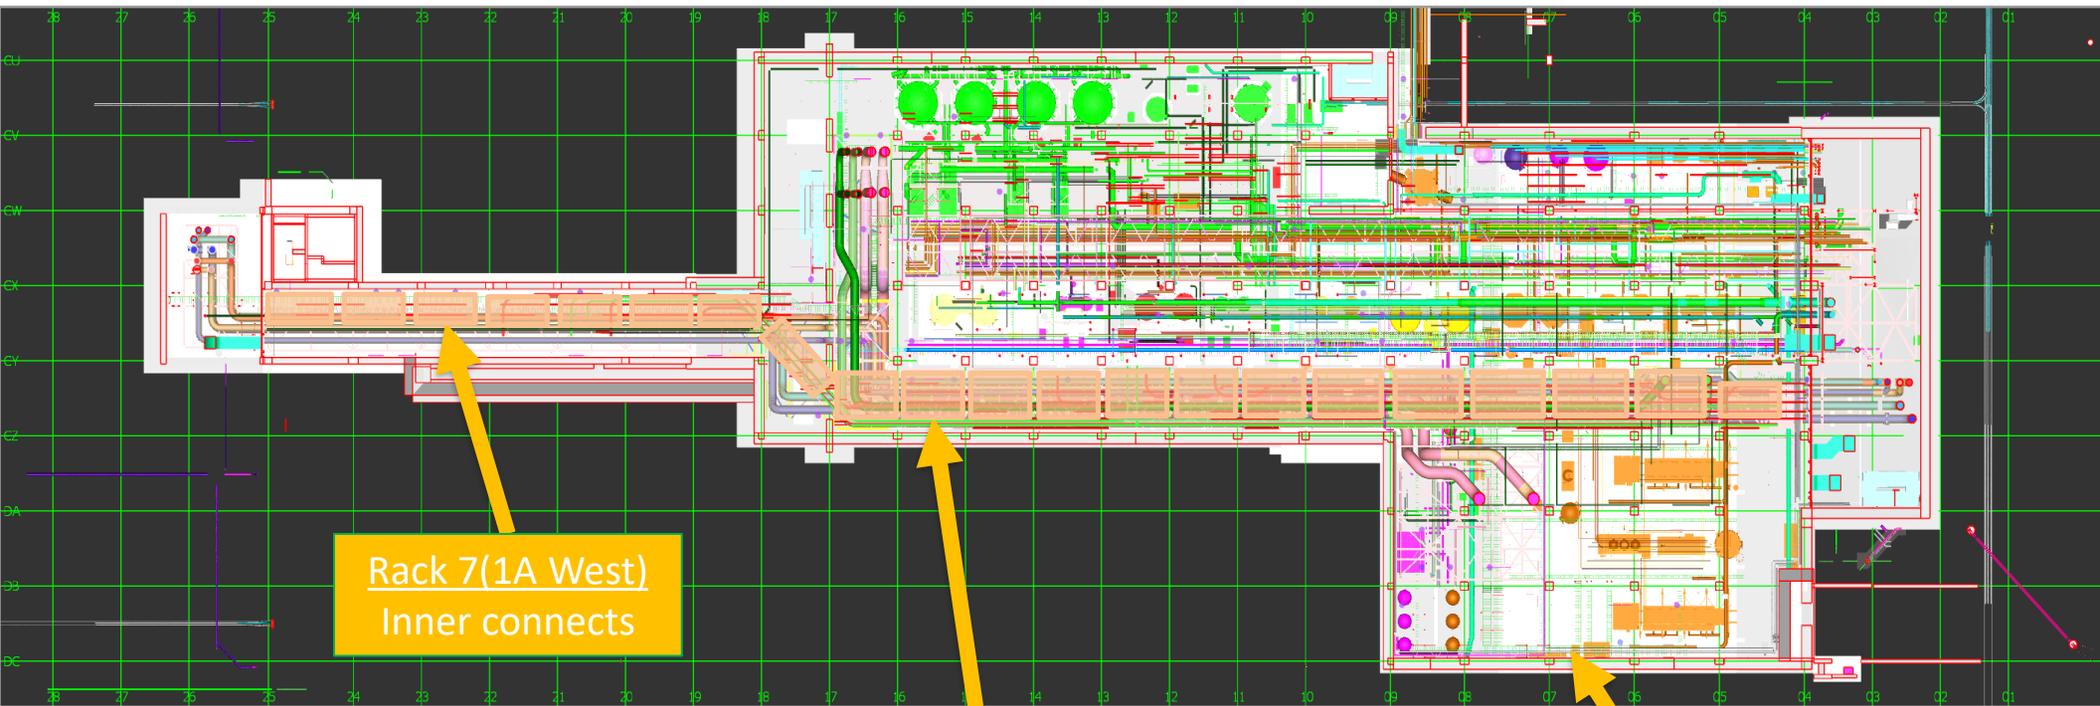


Rack 7(1A West)
Inner connects

1A Rack
Inner connects


8 Rack
Lifting

Vesda
H&T
Not actively installing

SUBFAB BUILDOUT MOD 1

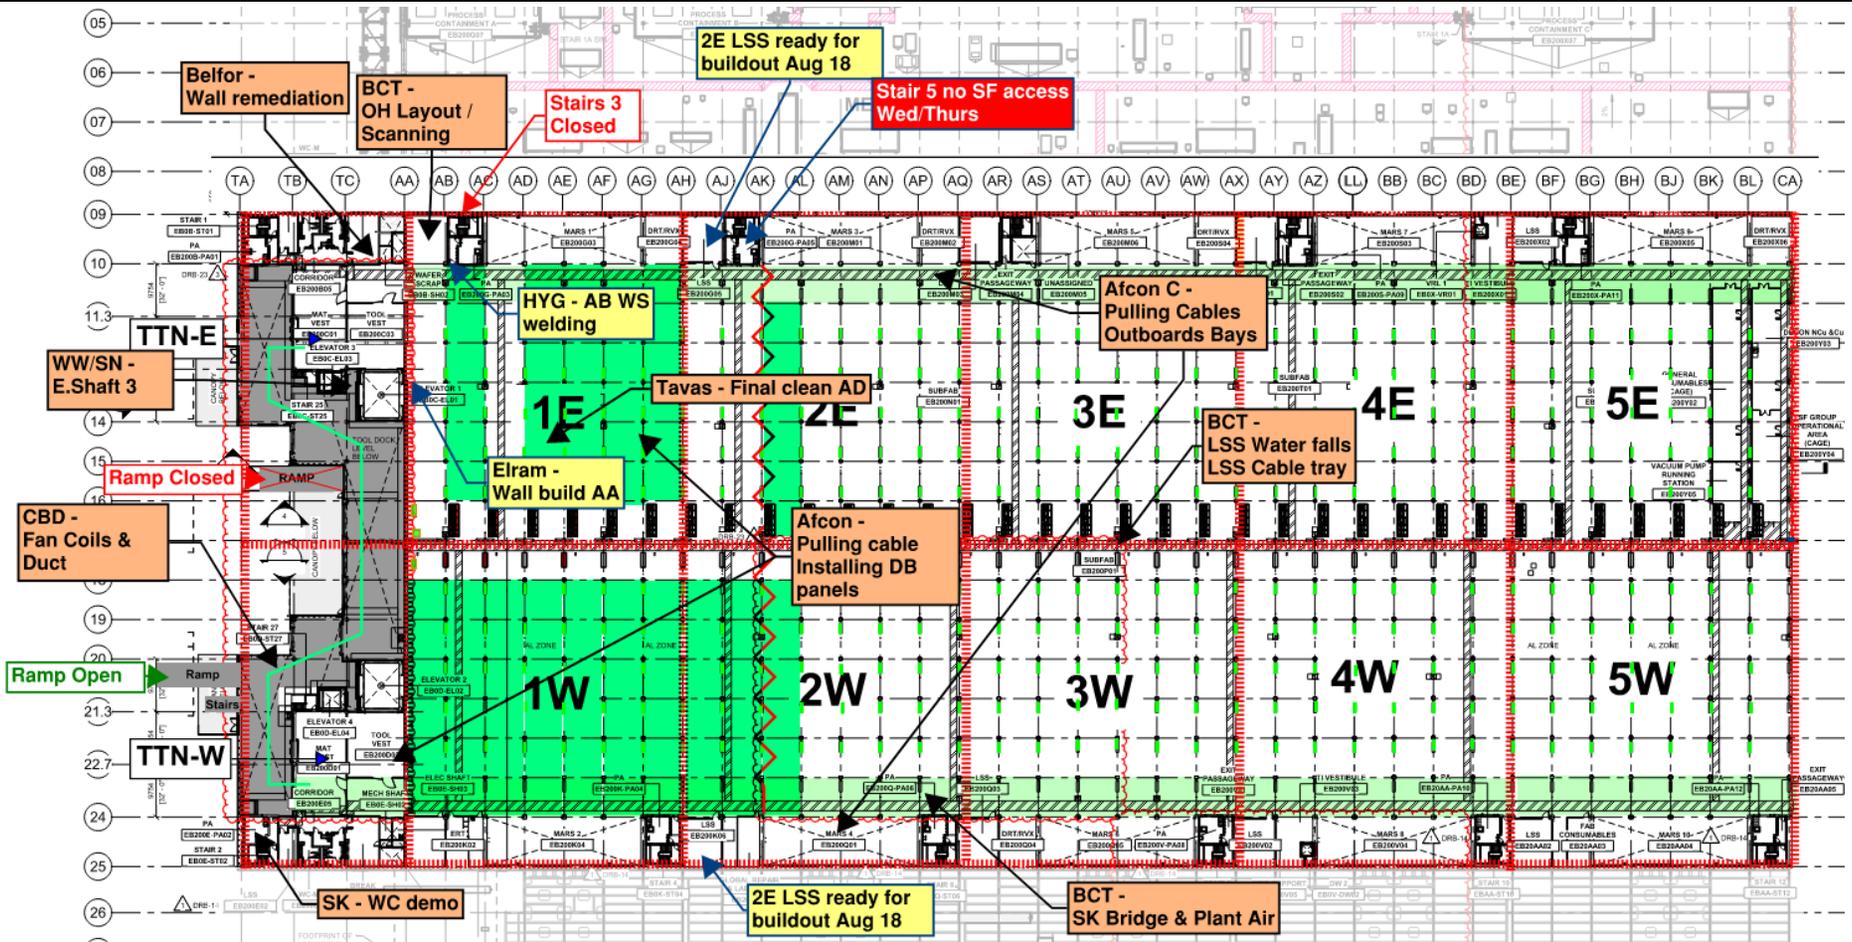

SUBFAB BUILDOUT MOD 2

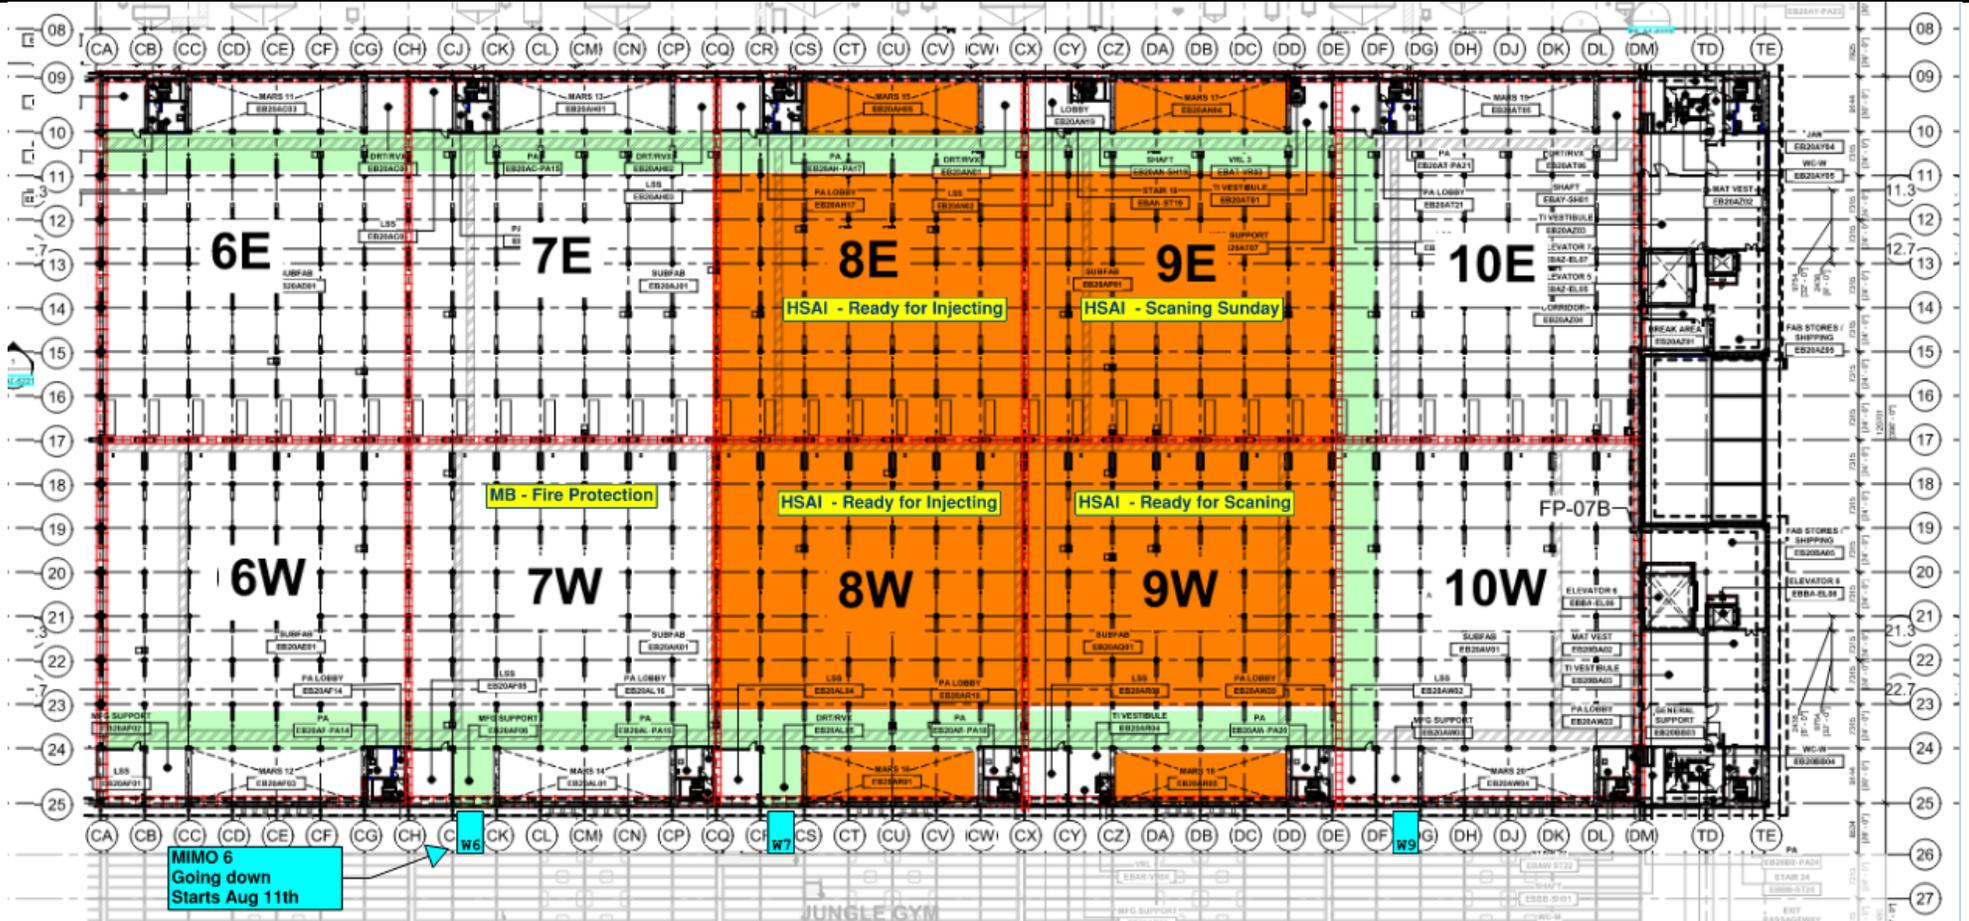


CRC Beauty Cote Work Plan.


Be well prepared to protect CRC

1. Nothing touches the floor, All must be on wheels.
2. Carts & MEWPs wheels must be replaced with a cleaner type (White).
3. Always have protective sheets/board on site to use for cover areas.
4. Damaging CRC will cause unnecessary and painful expenses to your company.

**1W South
Starts Aug 11**


**1W North
Ongoing**

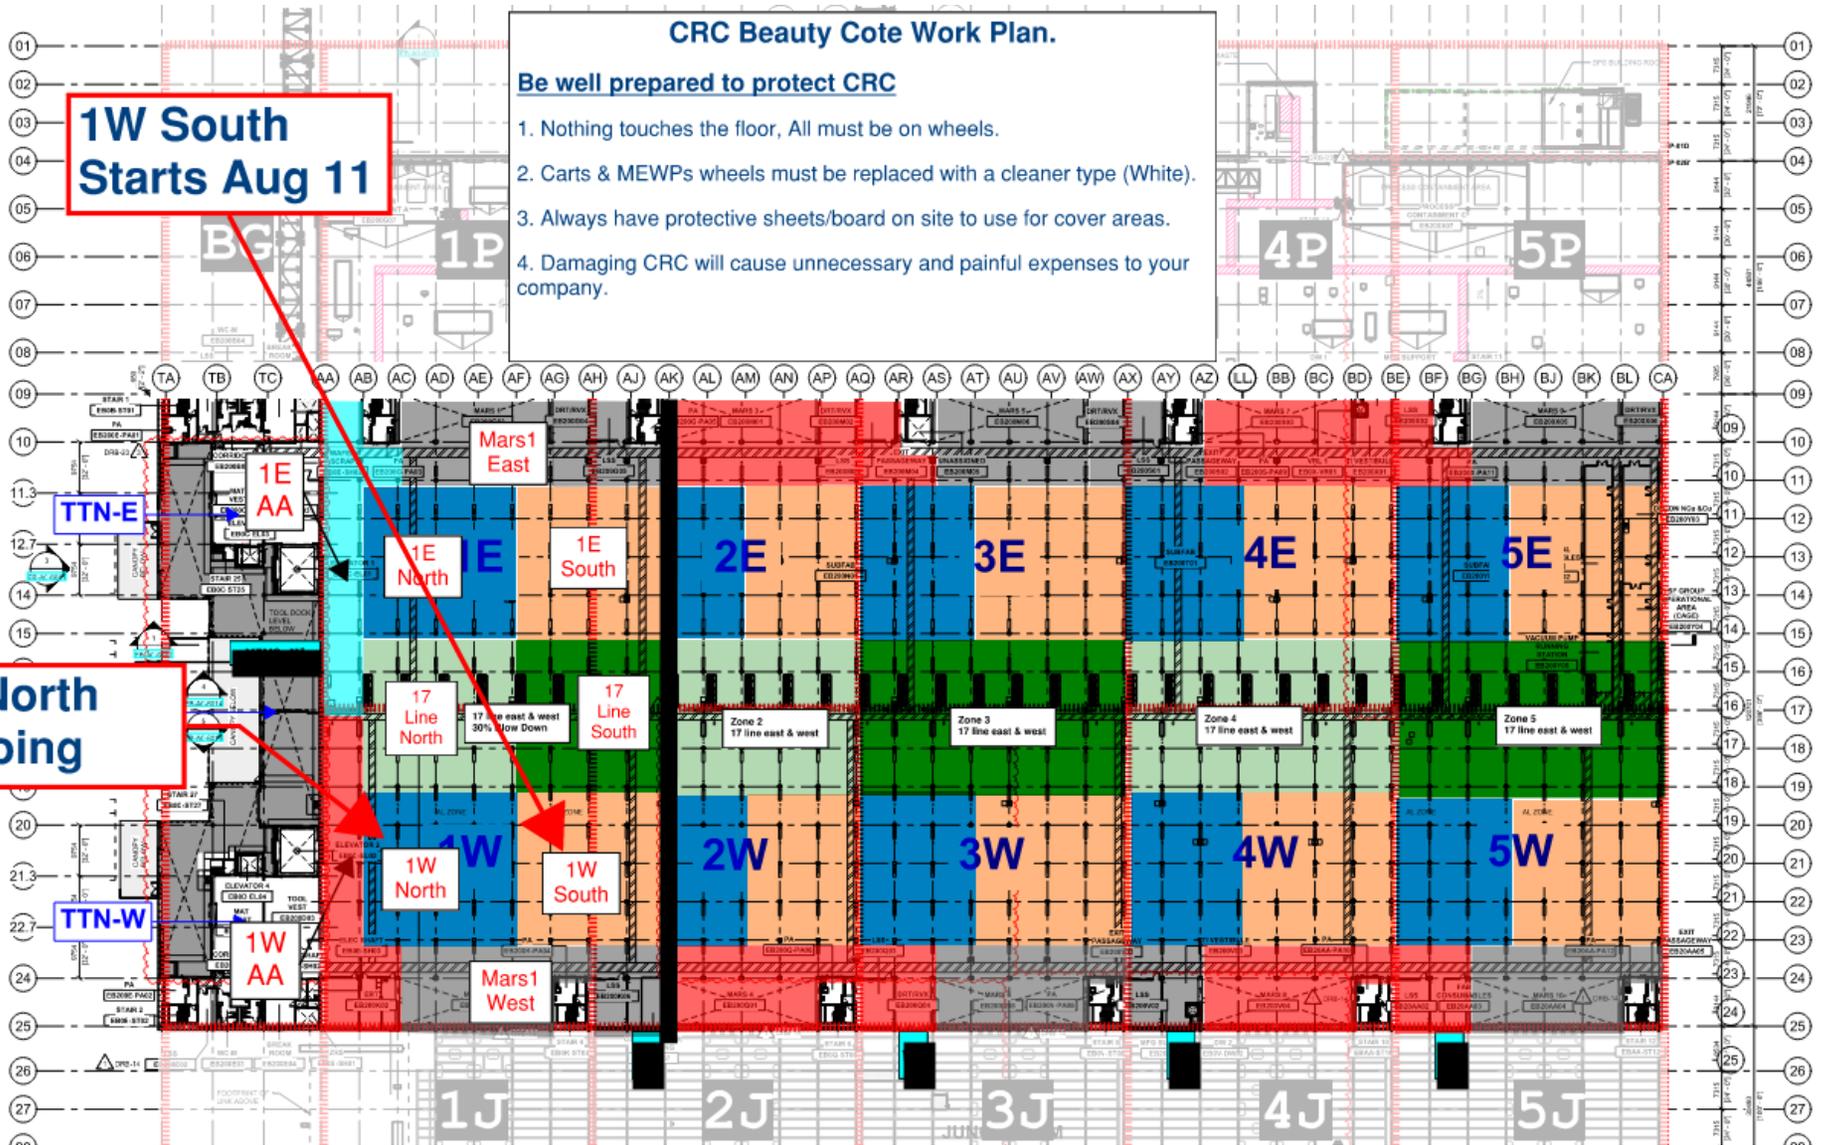

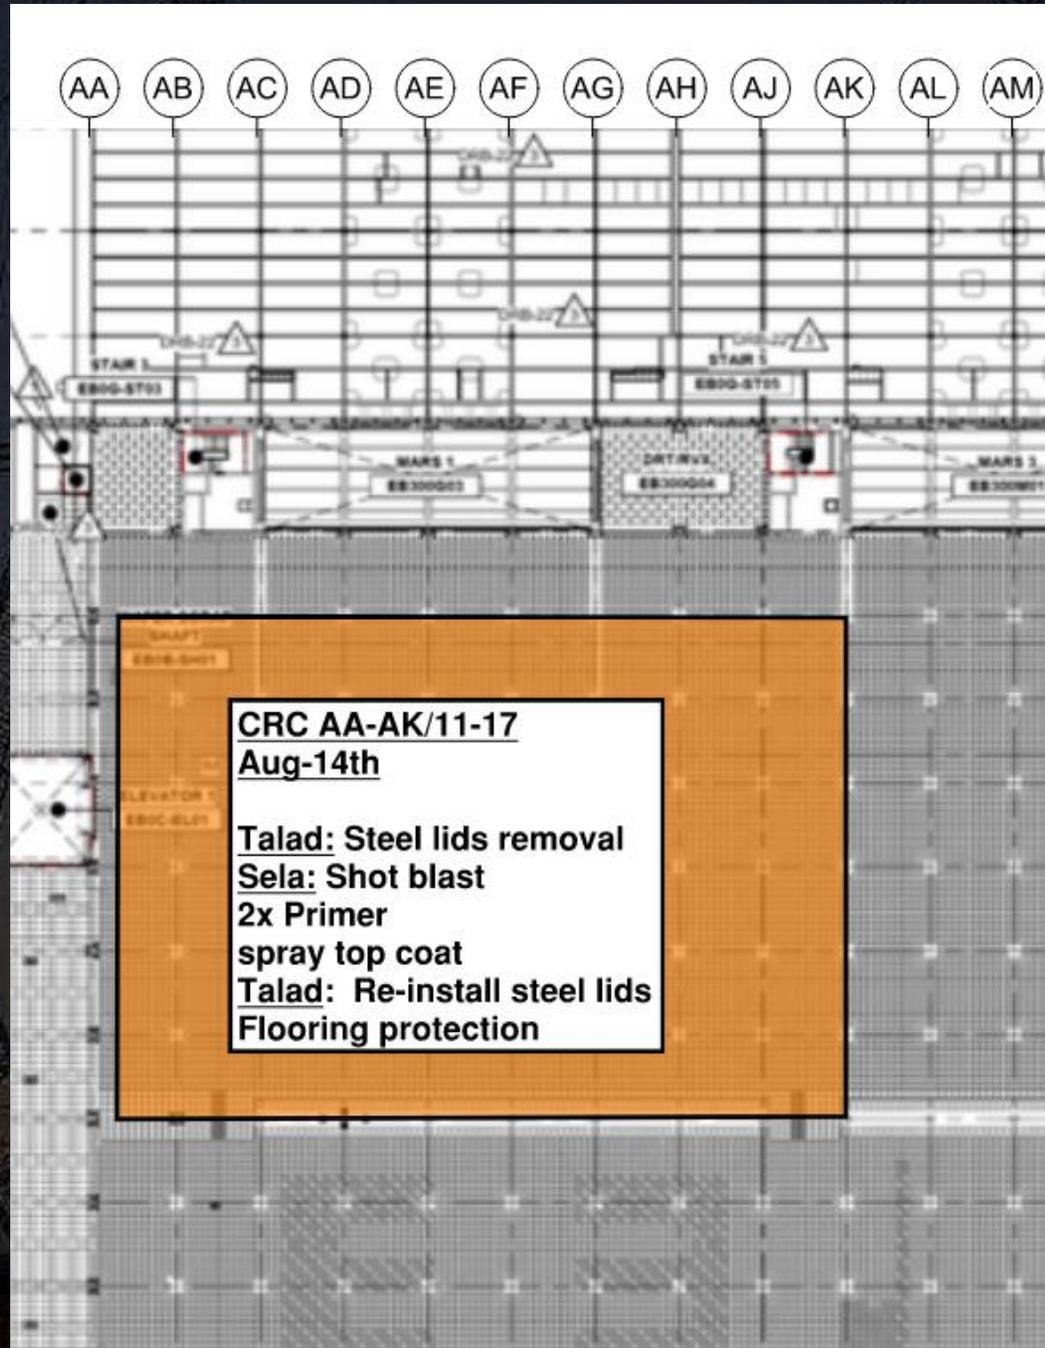

Int. level

- WW/SN - 2W penetrations
- Chemo- 10" pipe racks 2E-2W started
- Afcon - Cable trays, modules, cable pulling 1E,2E,1W,2w
- HYG - 5RA added beams 2E
- MB- 2E-2W preparations for test WW33
- C-B duct - 1W-2W to schedule test WW33
- Elram - Column wraps 9,10,24 lines
- RP- FP 4DA 3E-3W
- Tzur-Esh - Steel paint 4E-4W
- Megasone - Small wires+ speakers 3E+2E

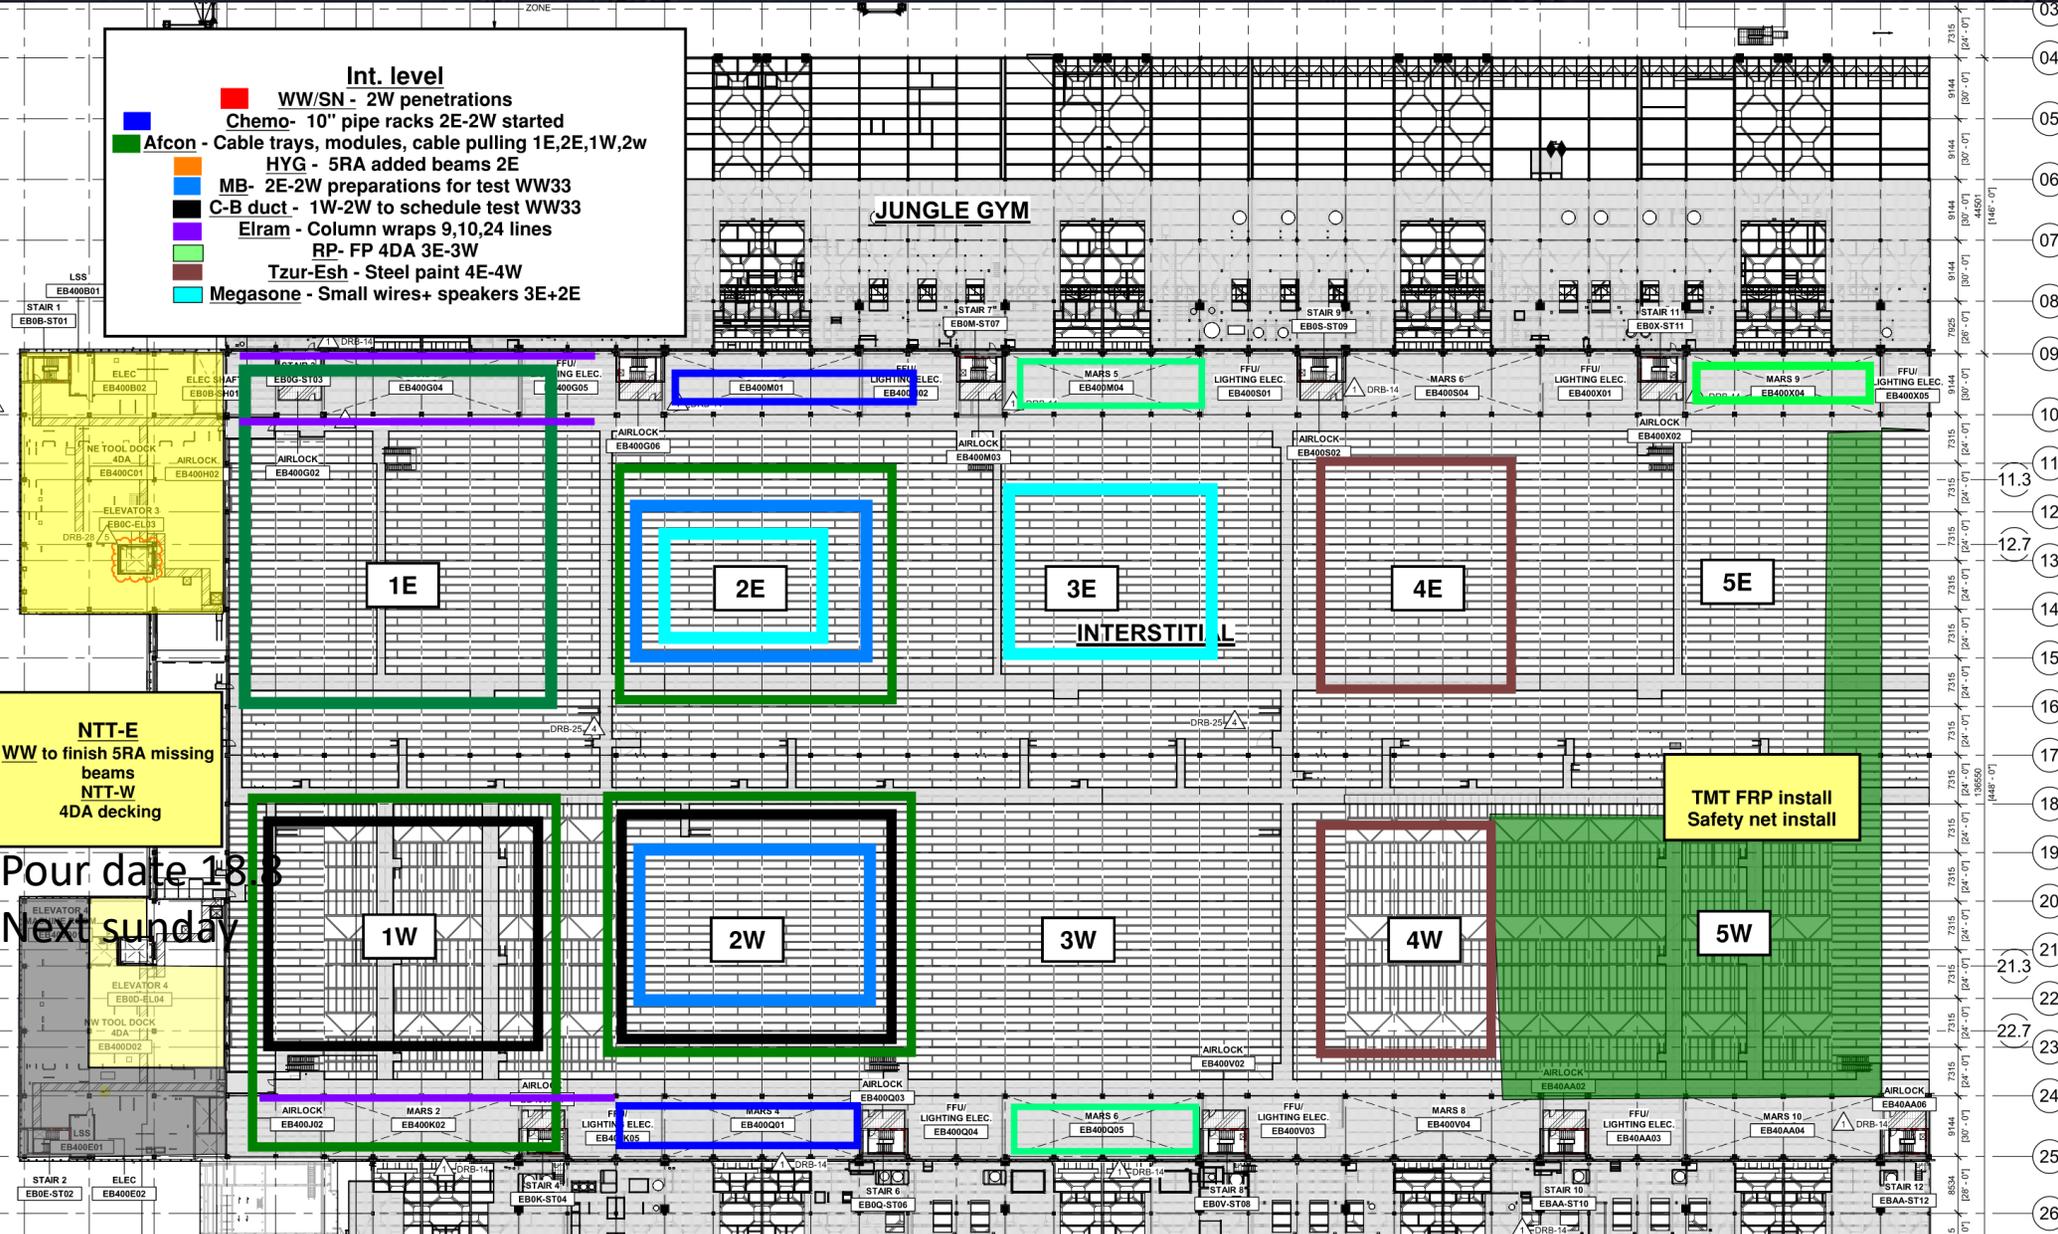

NTT-E
 WW to finish 5RA missing beams
 NTT-W
 4DA decking

Pour date 1/3/18
Next sunday

TMT FRP install
Safety net install

1W

2W

3W

4W

5W

JUNGLE GYM

INTERSTITIAL

1E

2E

3E

4E

5E

STAIR 7
EB08-ST01

STAIR 7
EB08-ST07

STAIR 9
EB08-ST09

STAIR 11
EB08-ST11

STAIR 2
EB08-ST02

STAIR 4
EB08-ST04


STAIR 6
EB08-ST06

STAIR 8
EB08-ST08

STAIR 10
EB08-ST10

STAIR 12
EB08-ST12

03
04
05
06
07
08
09
10
11.3
12.7
13
14
15
16
17
18
19
20
21
22
22.7
23
24
25
26

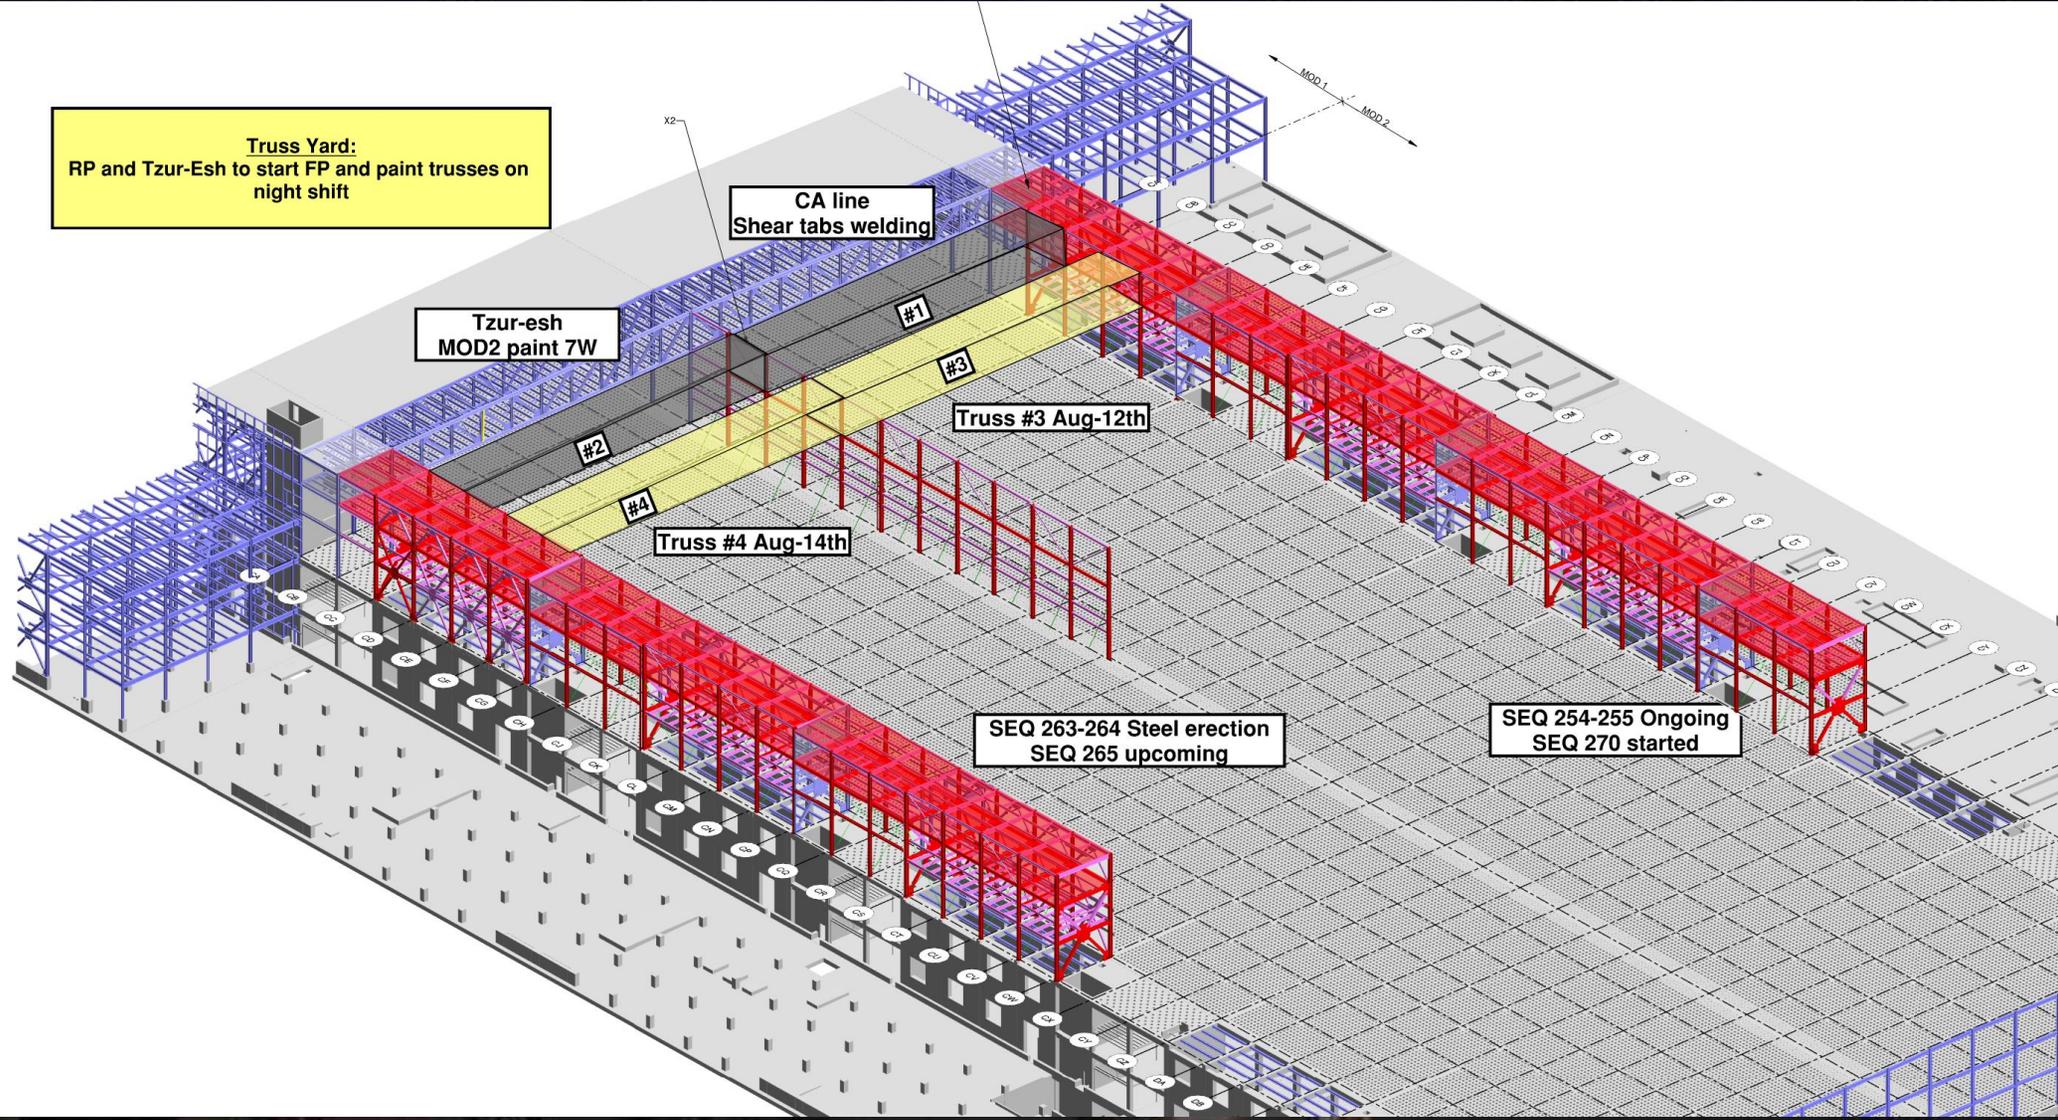

Truss Yard:
RP and Tzur-Esh to start FP and paint trusses on night shift

CA line
Shear tabs welding


Tzur-esh
MOD2 paint 7W

Truss #3 Aug-12th

Truss #4 Aug-14th

SEQ 263-264 Steel erection
SEQ 265 upcoming

SEQ 254-255 Ongoing
SEQ 270 started

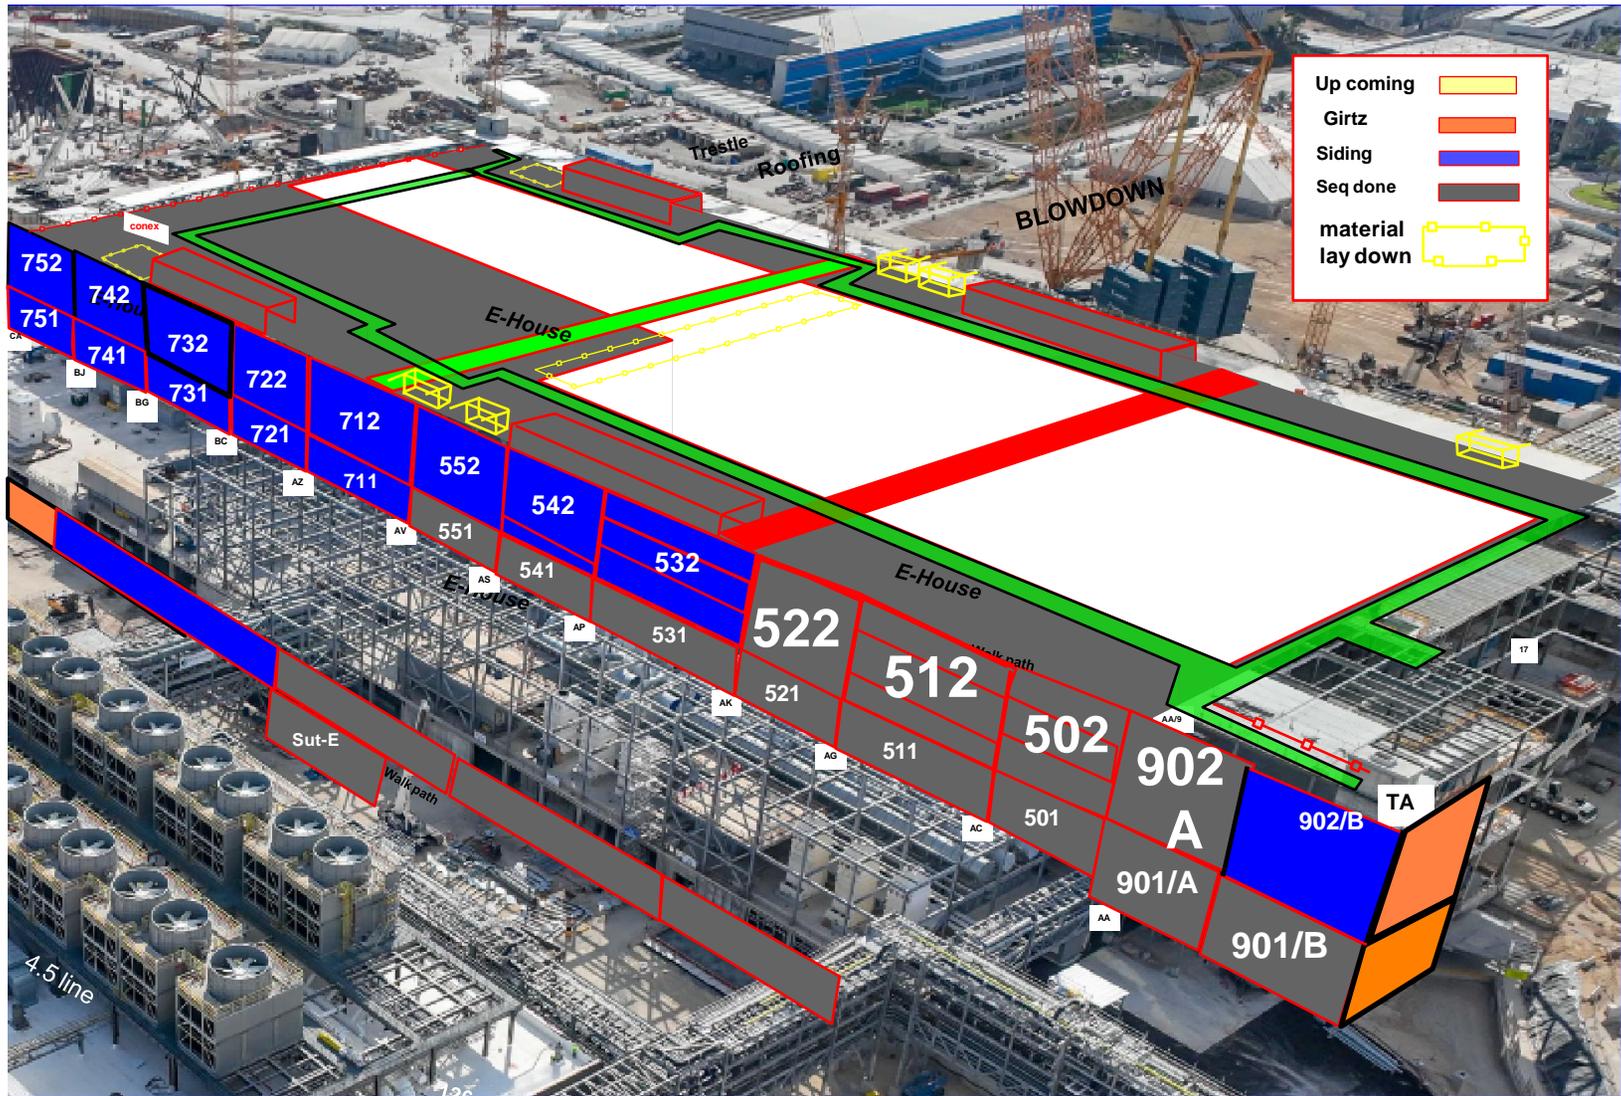

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

752

751

742

741

732

731

722

721

712

711

552

551

542

541

532

531

522

521

512

511

502

501

902

901/A

902/B

901/B

TA

AA

AC

AG

AK

AP

AS

AV

AZ

BC

BG

BJ

conex

17

4.5 line

Sut-E

Walk path

126

Walk path

Trestle

Roofing


BLOWDOWN


E-House

E-House

E-House

Walk path

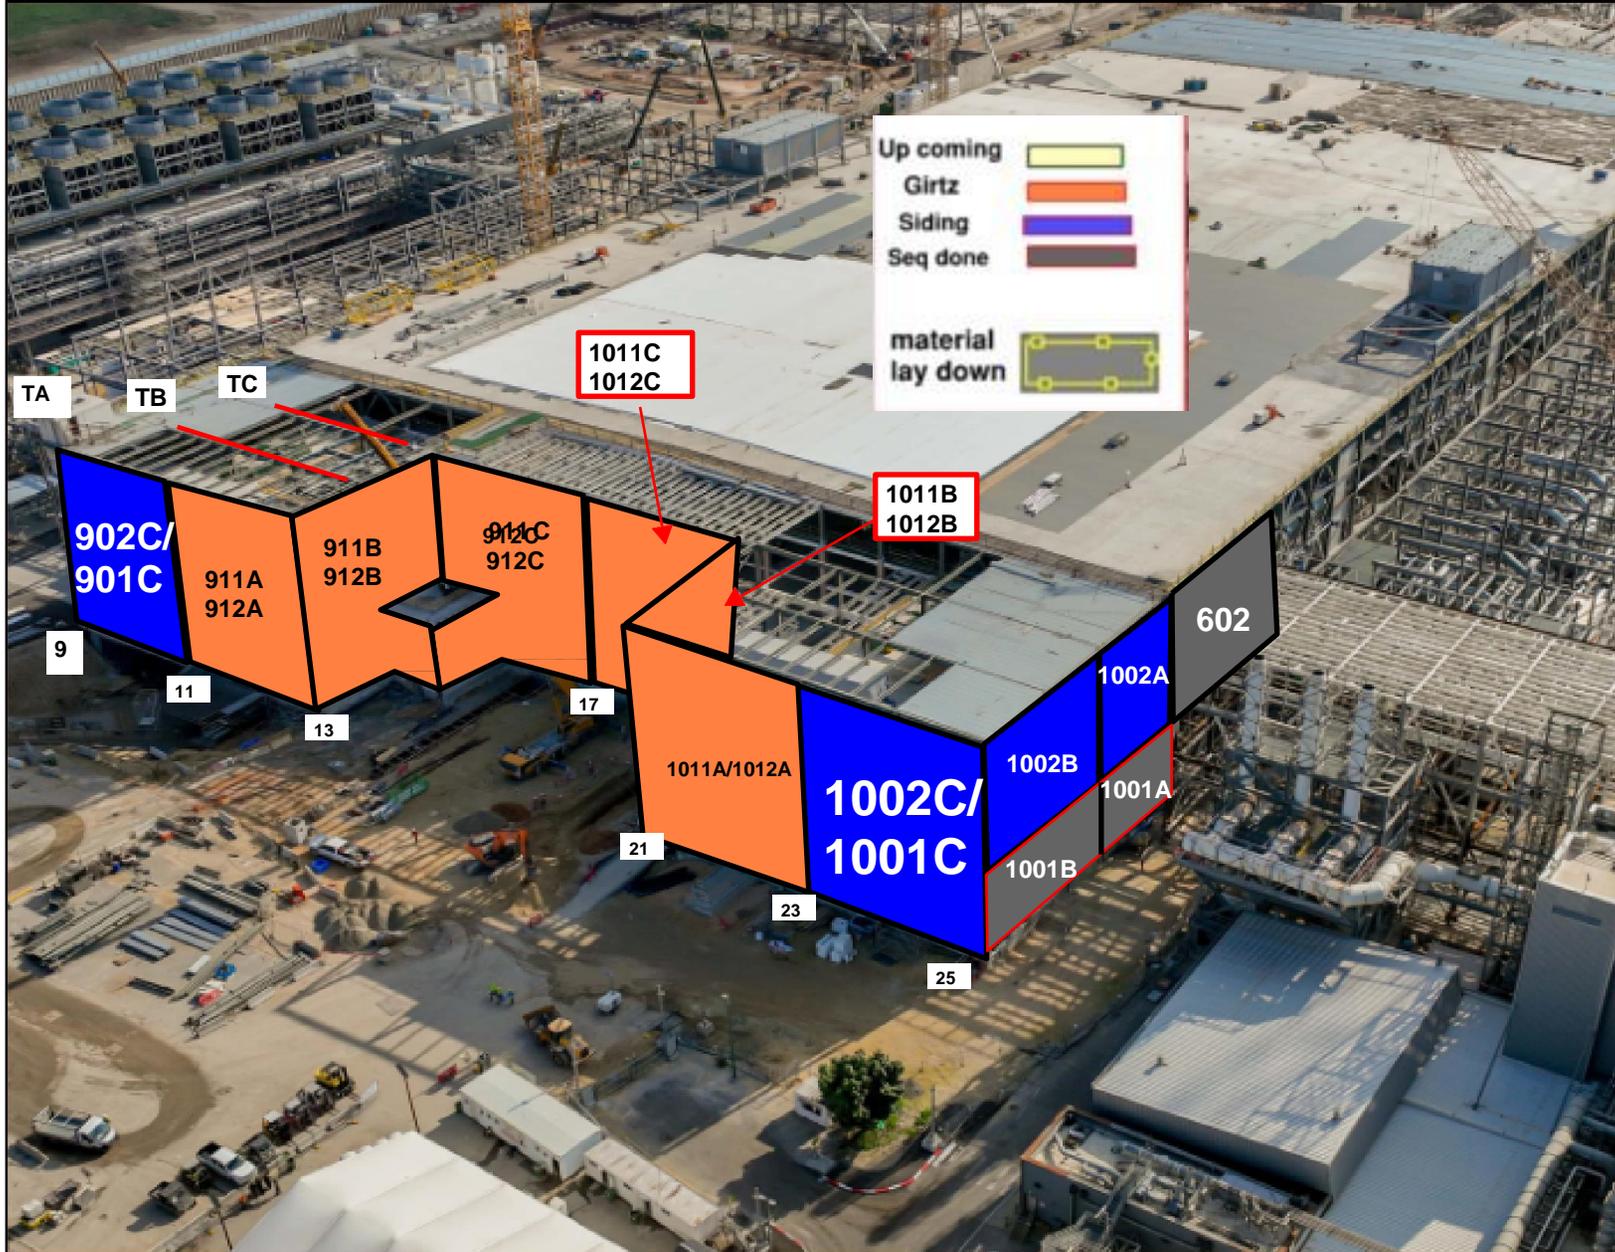


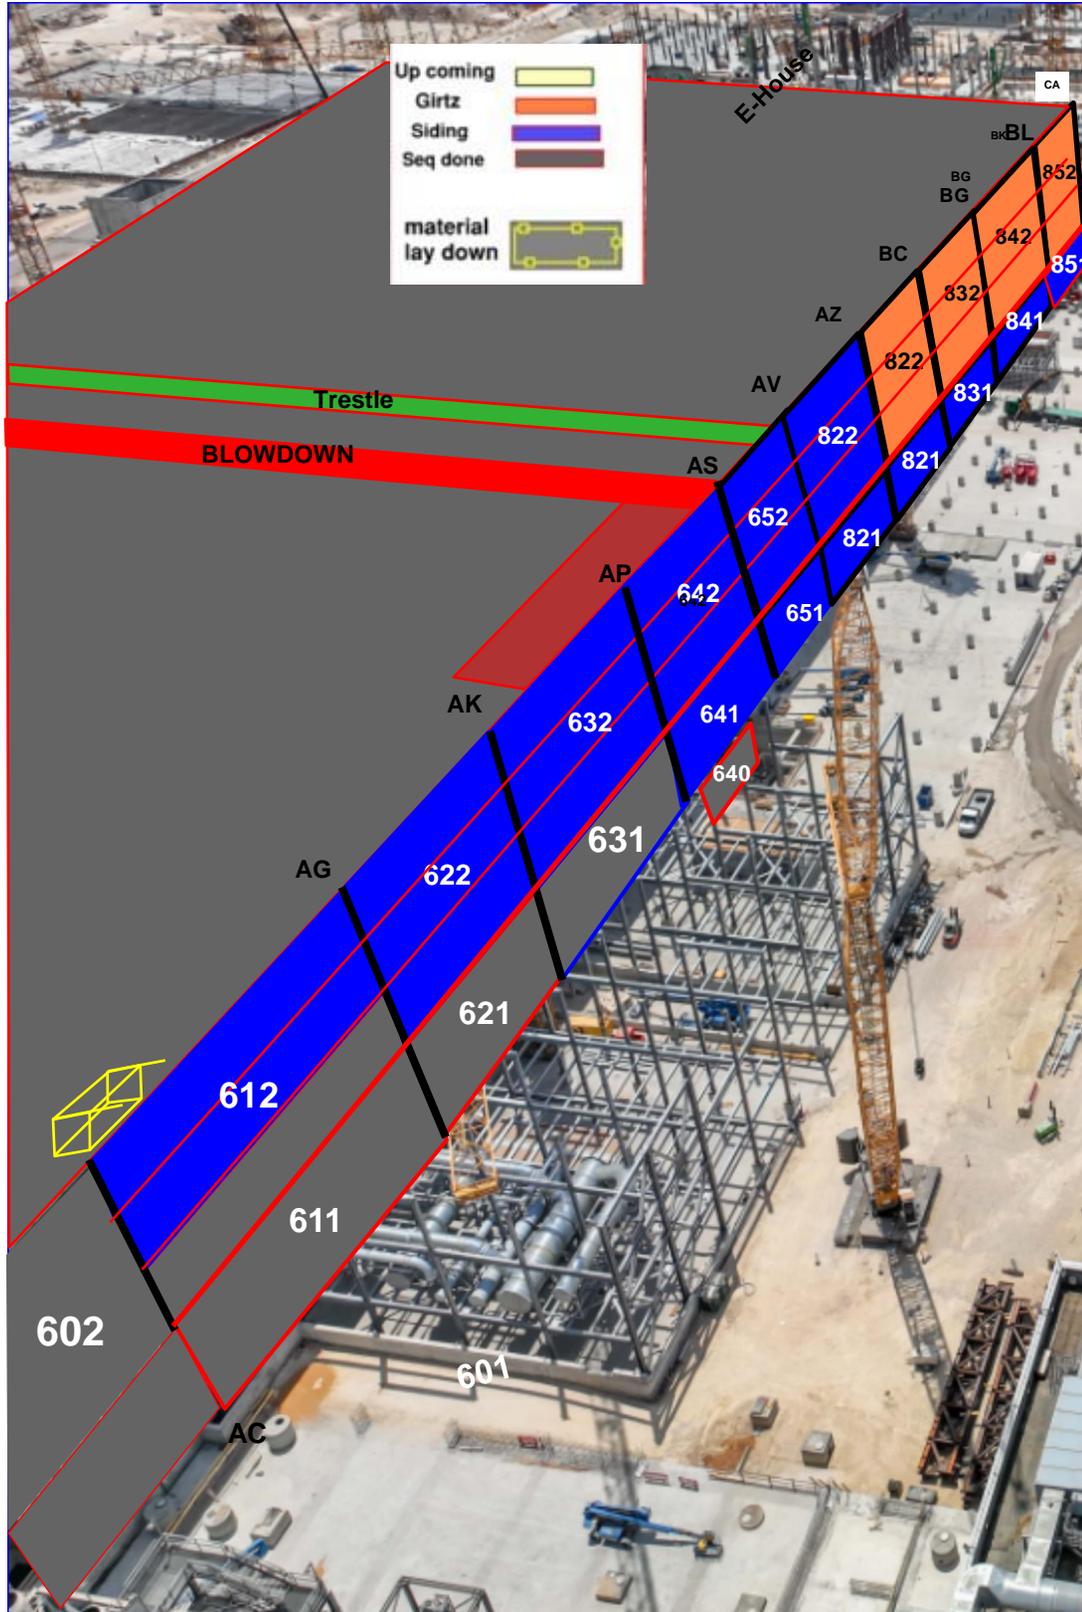

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

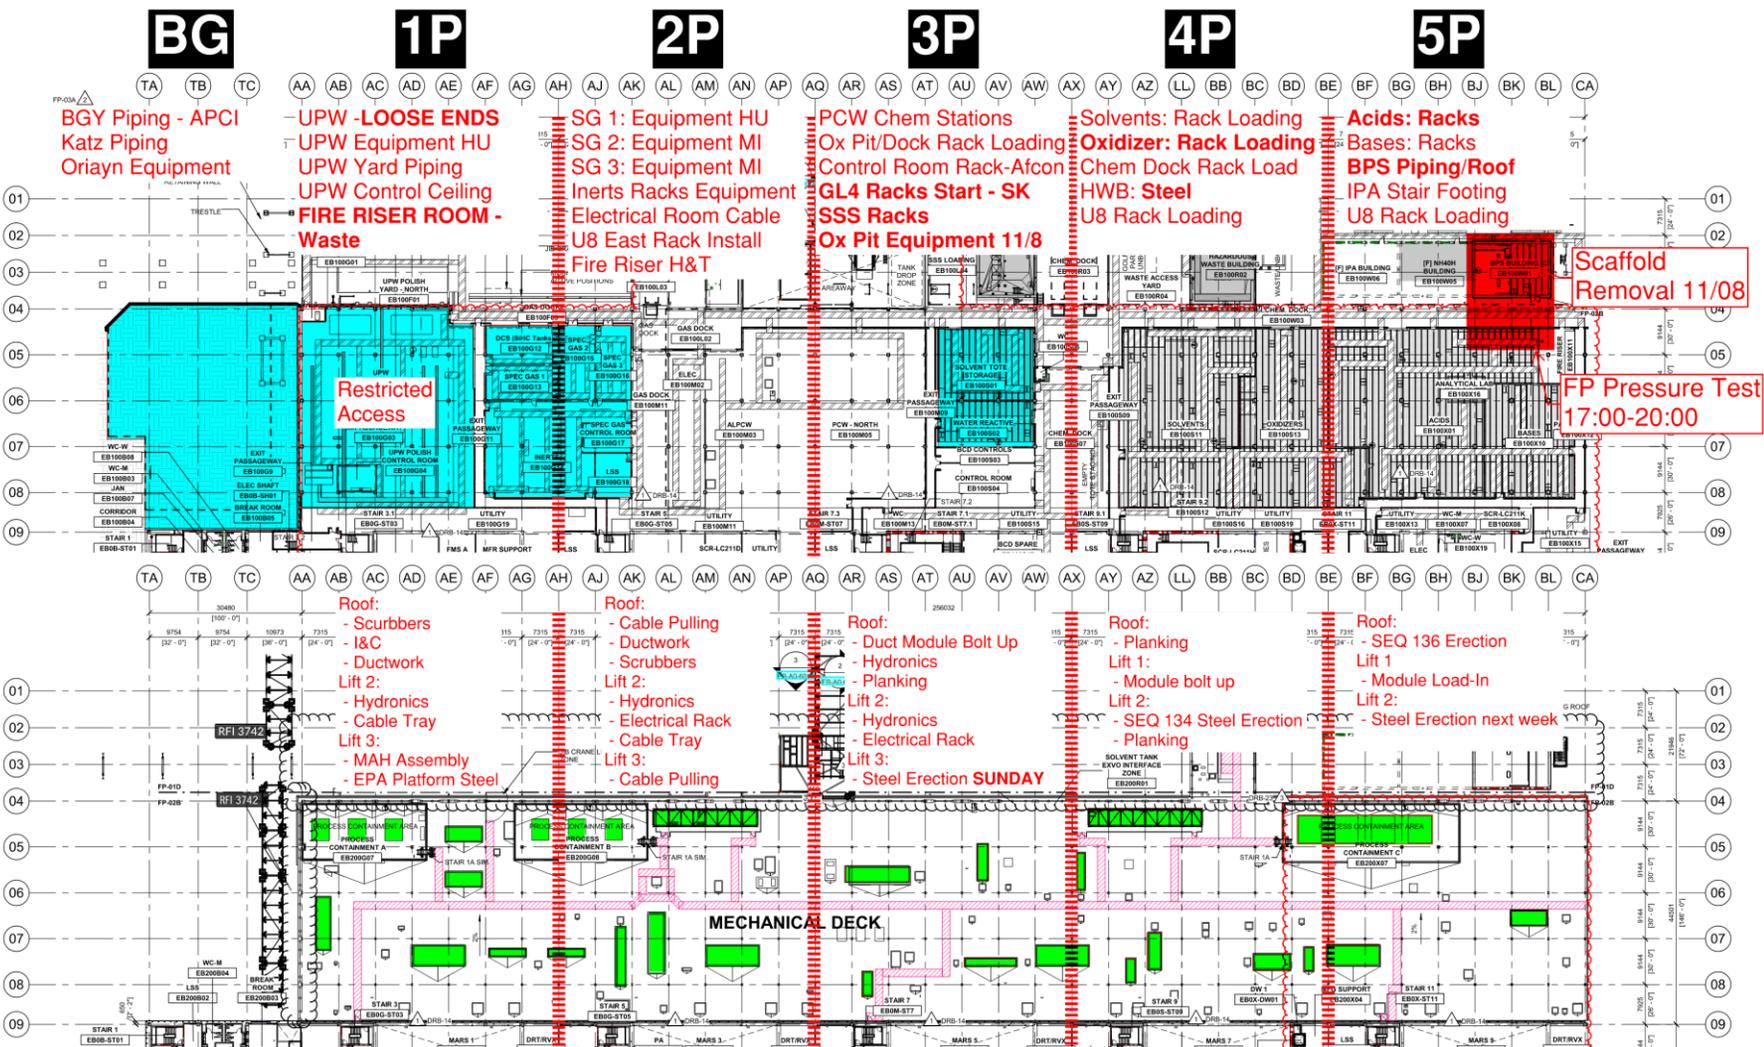


WJG 01J, 02J LIFT 2 & 3





WJG 03J, 04J, 05J LIFT 2 & 3

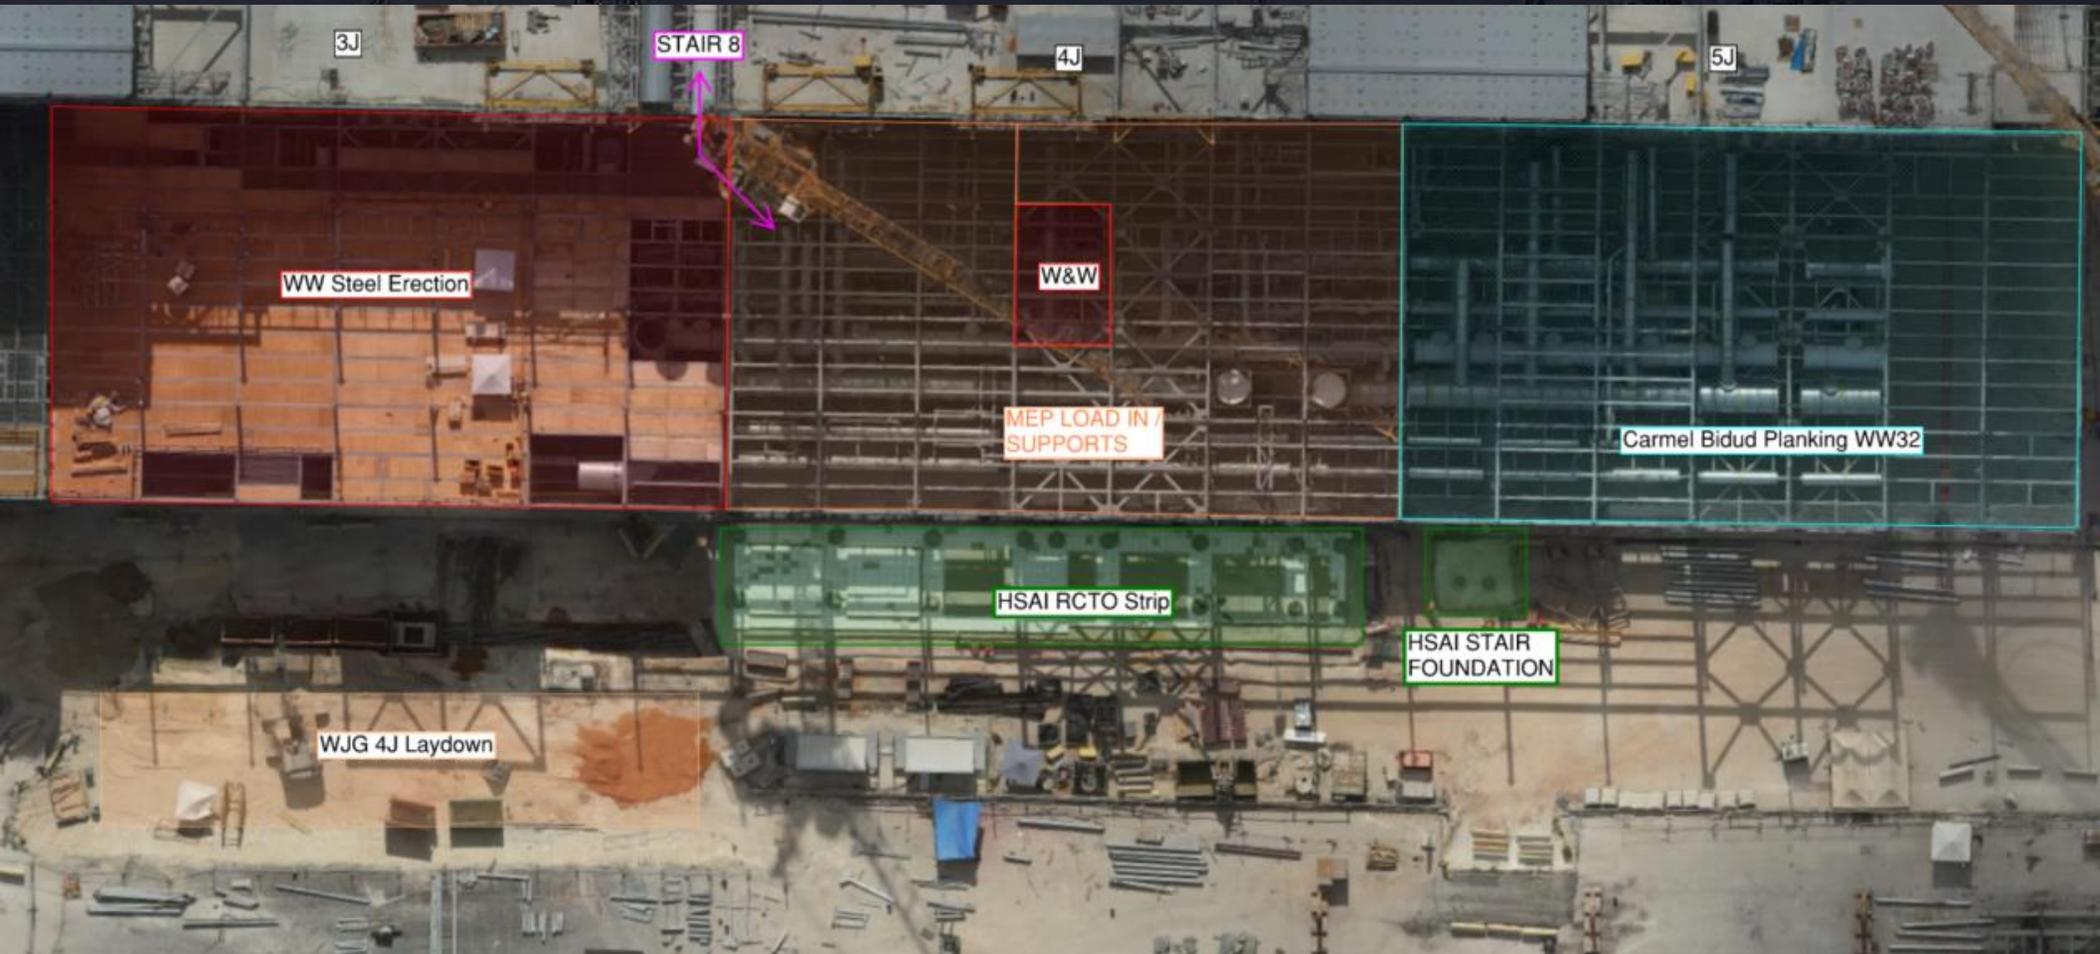



WJG UTILITY LEVEL BUILD OUT

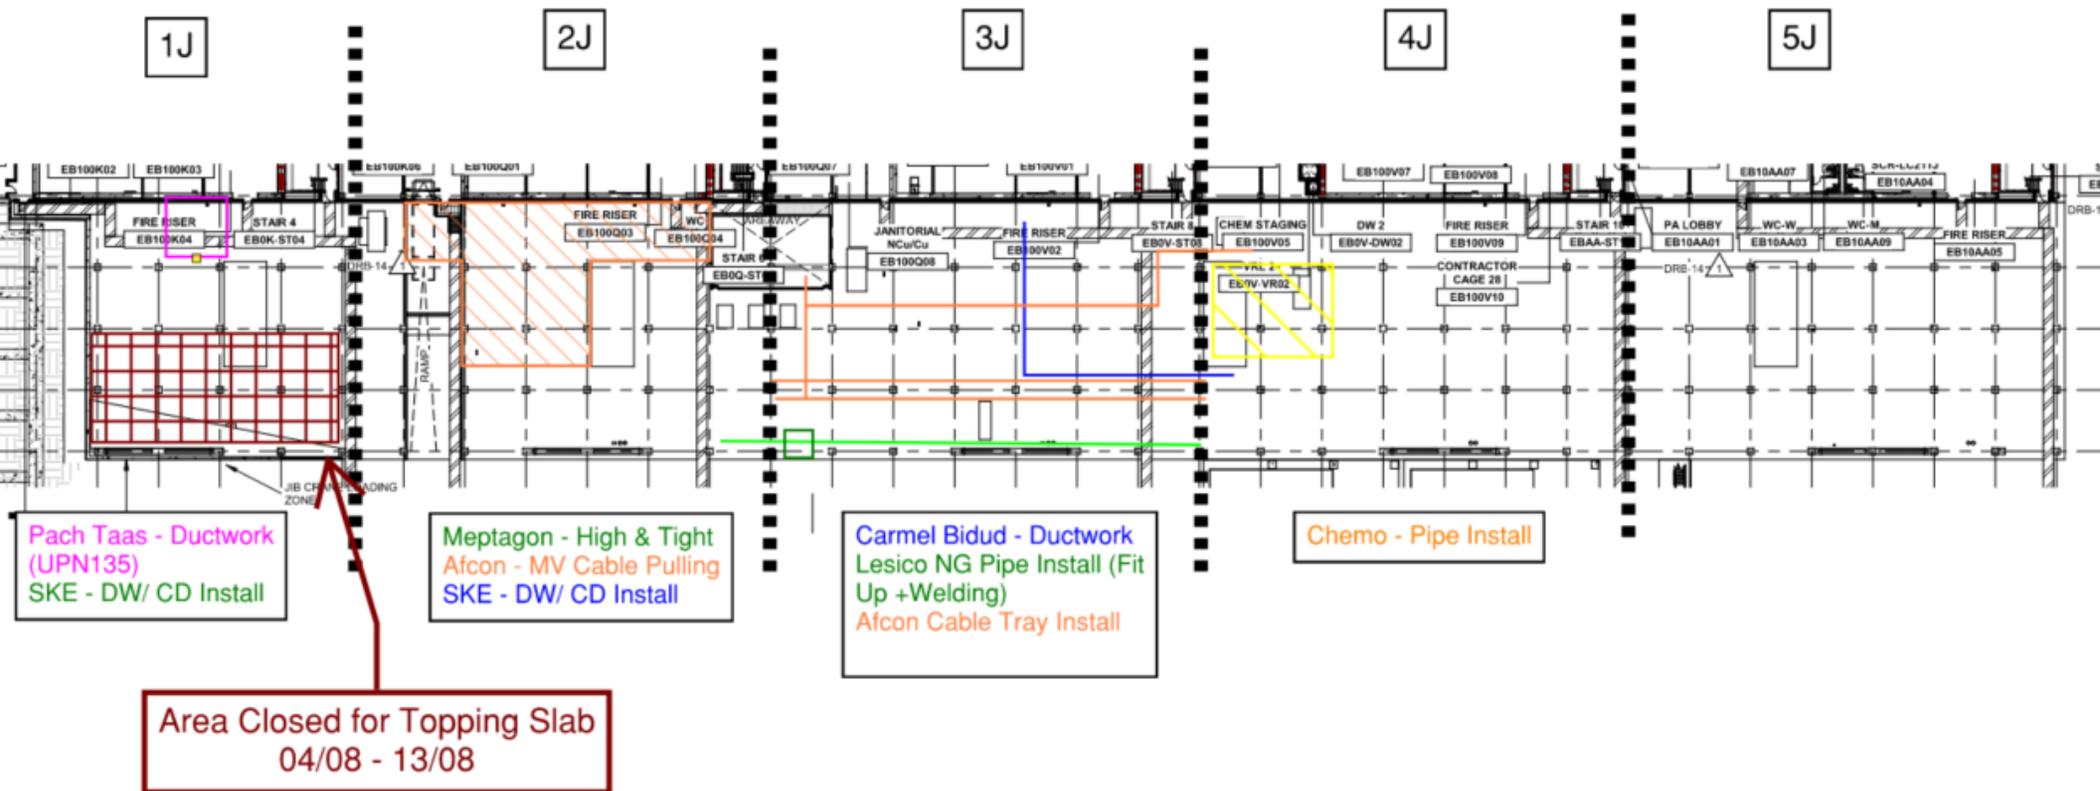


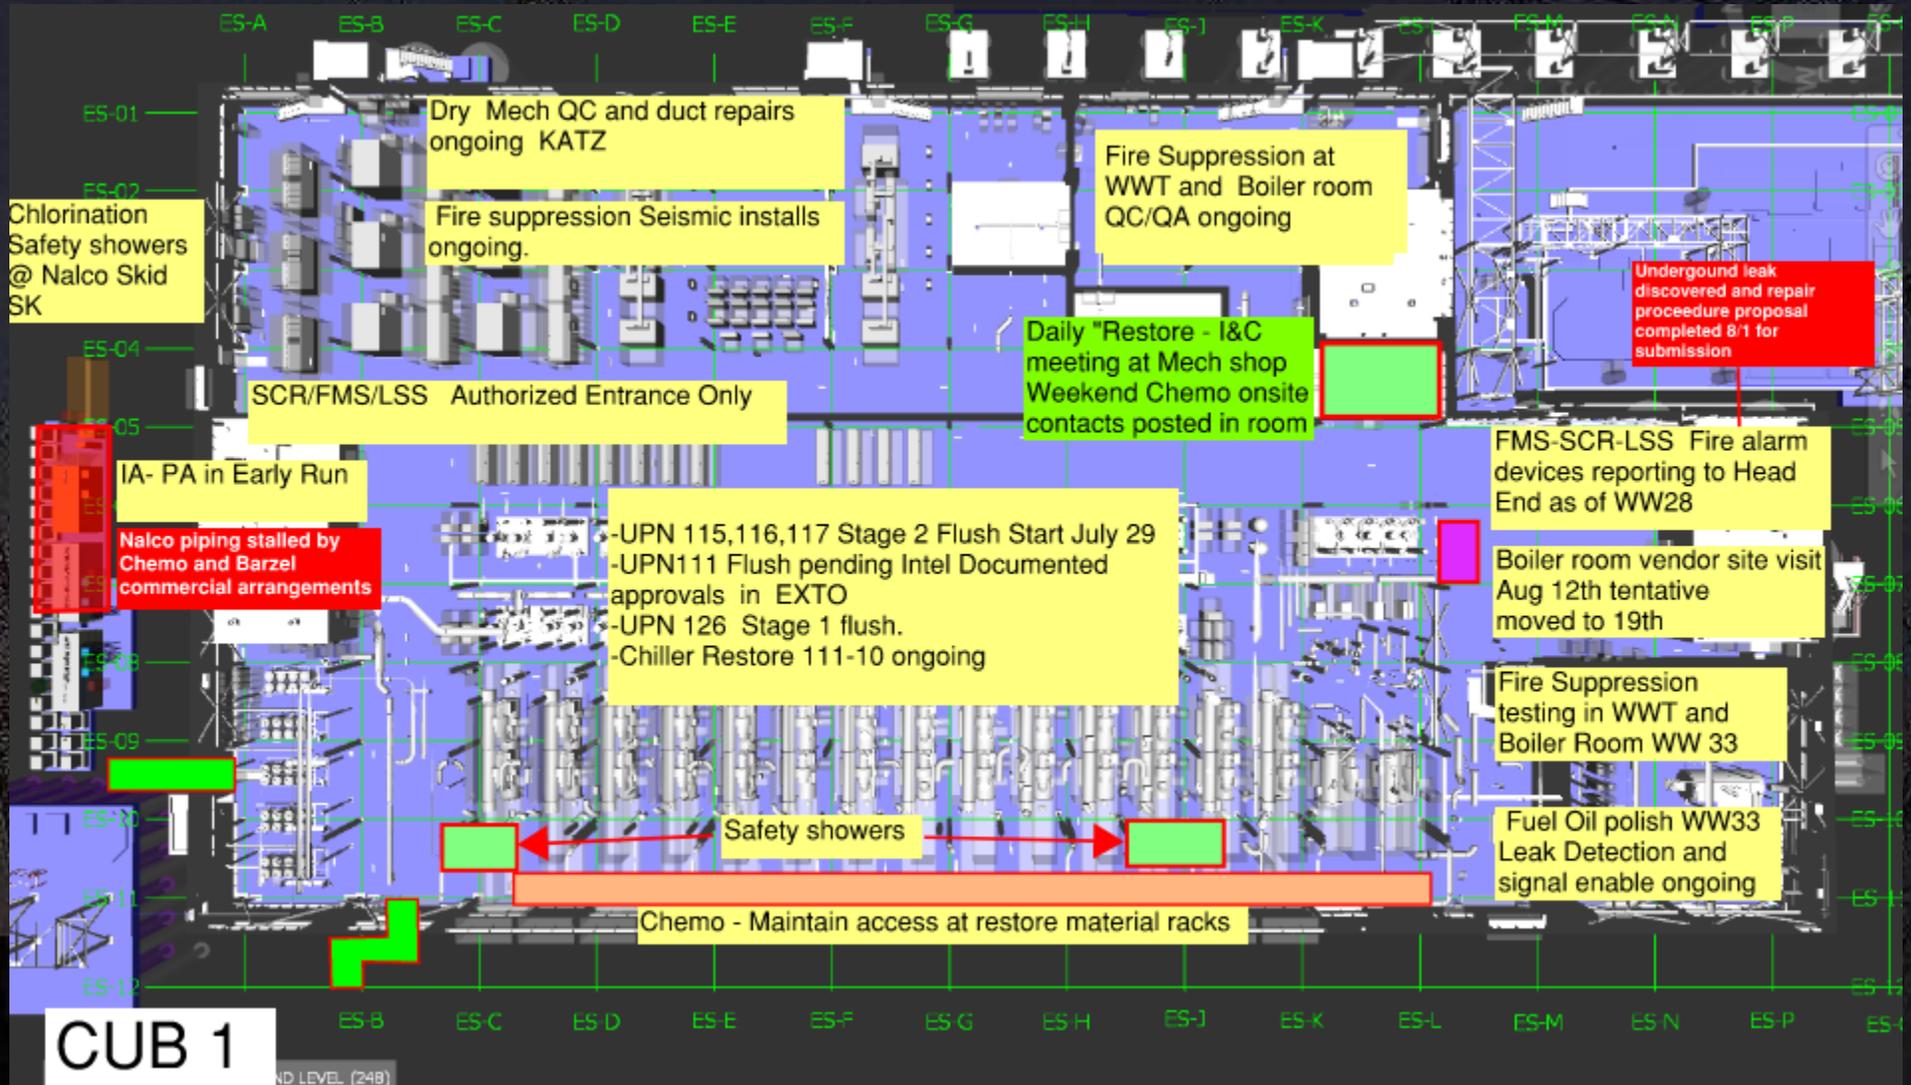

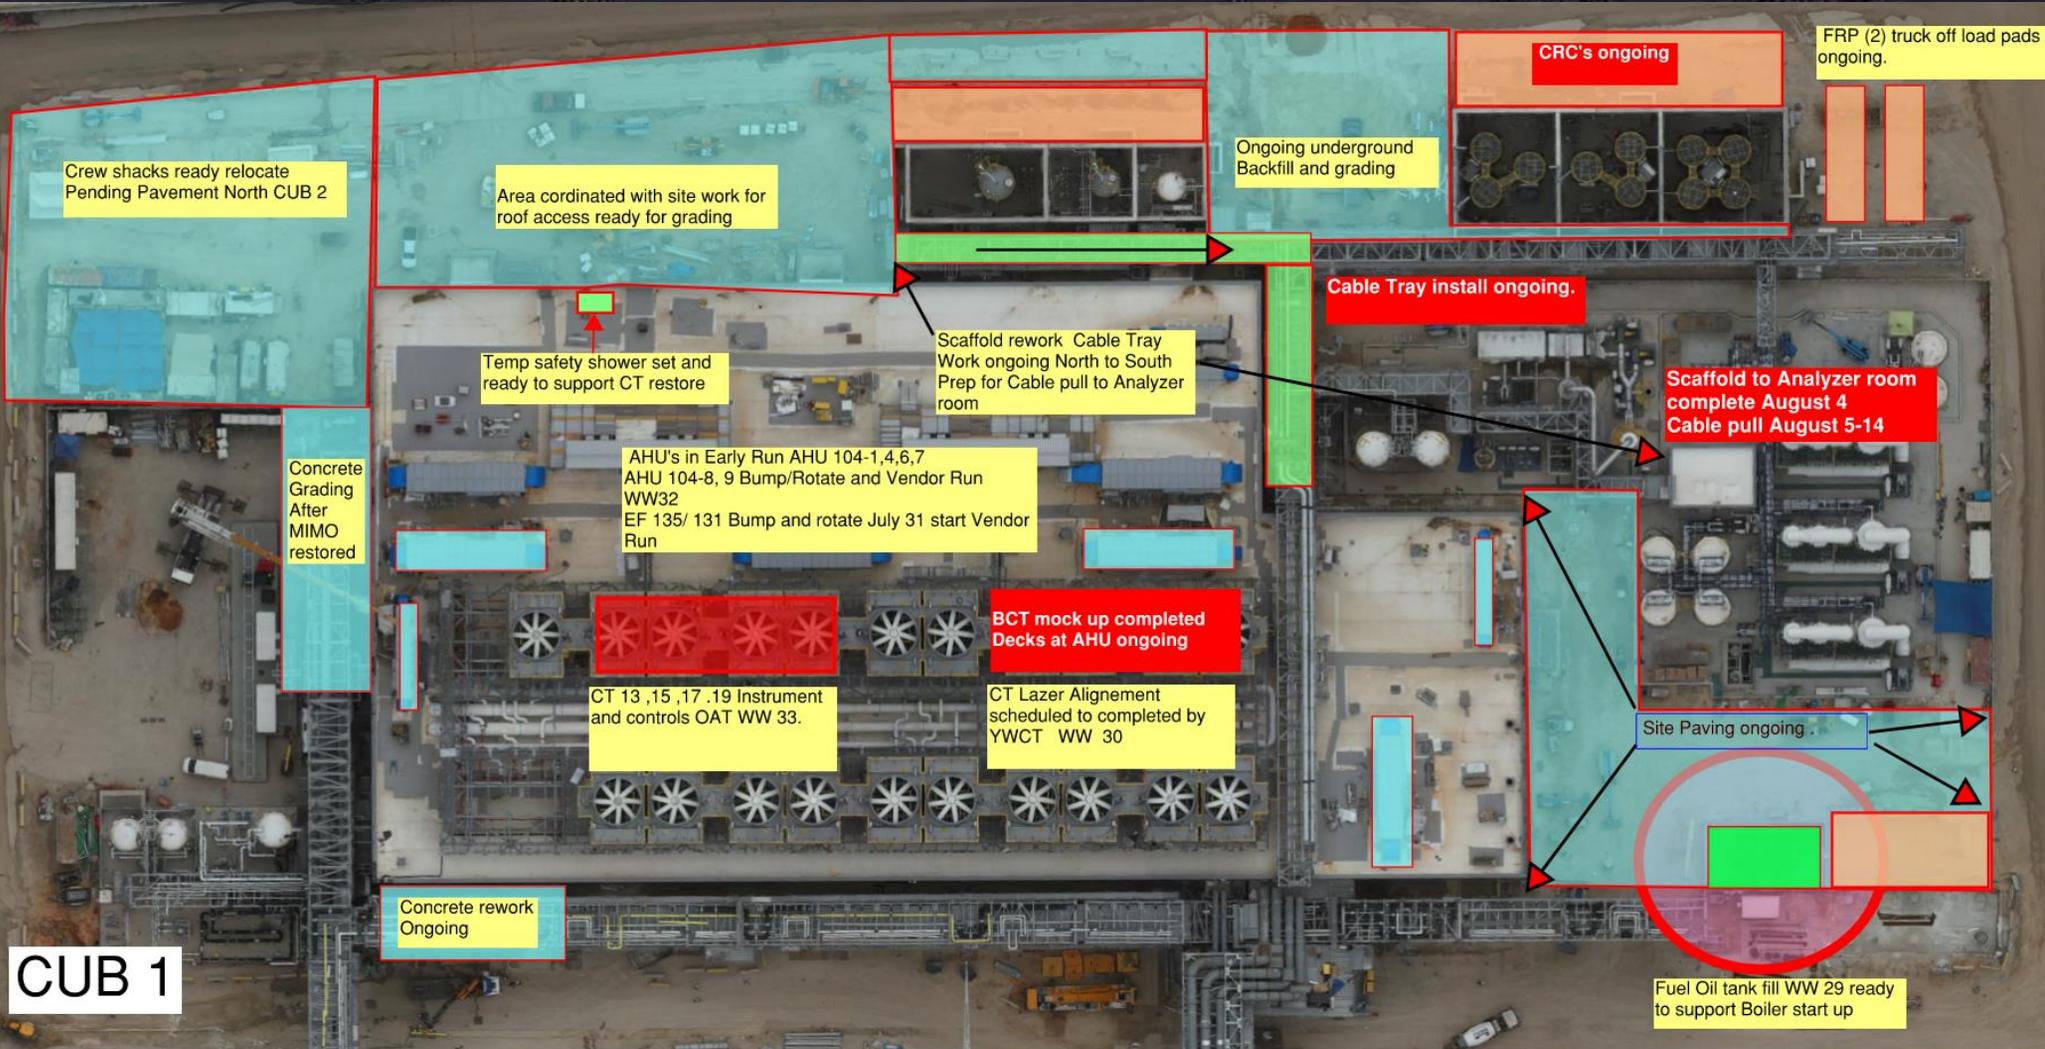

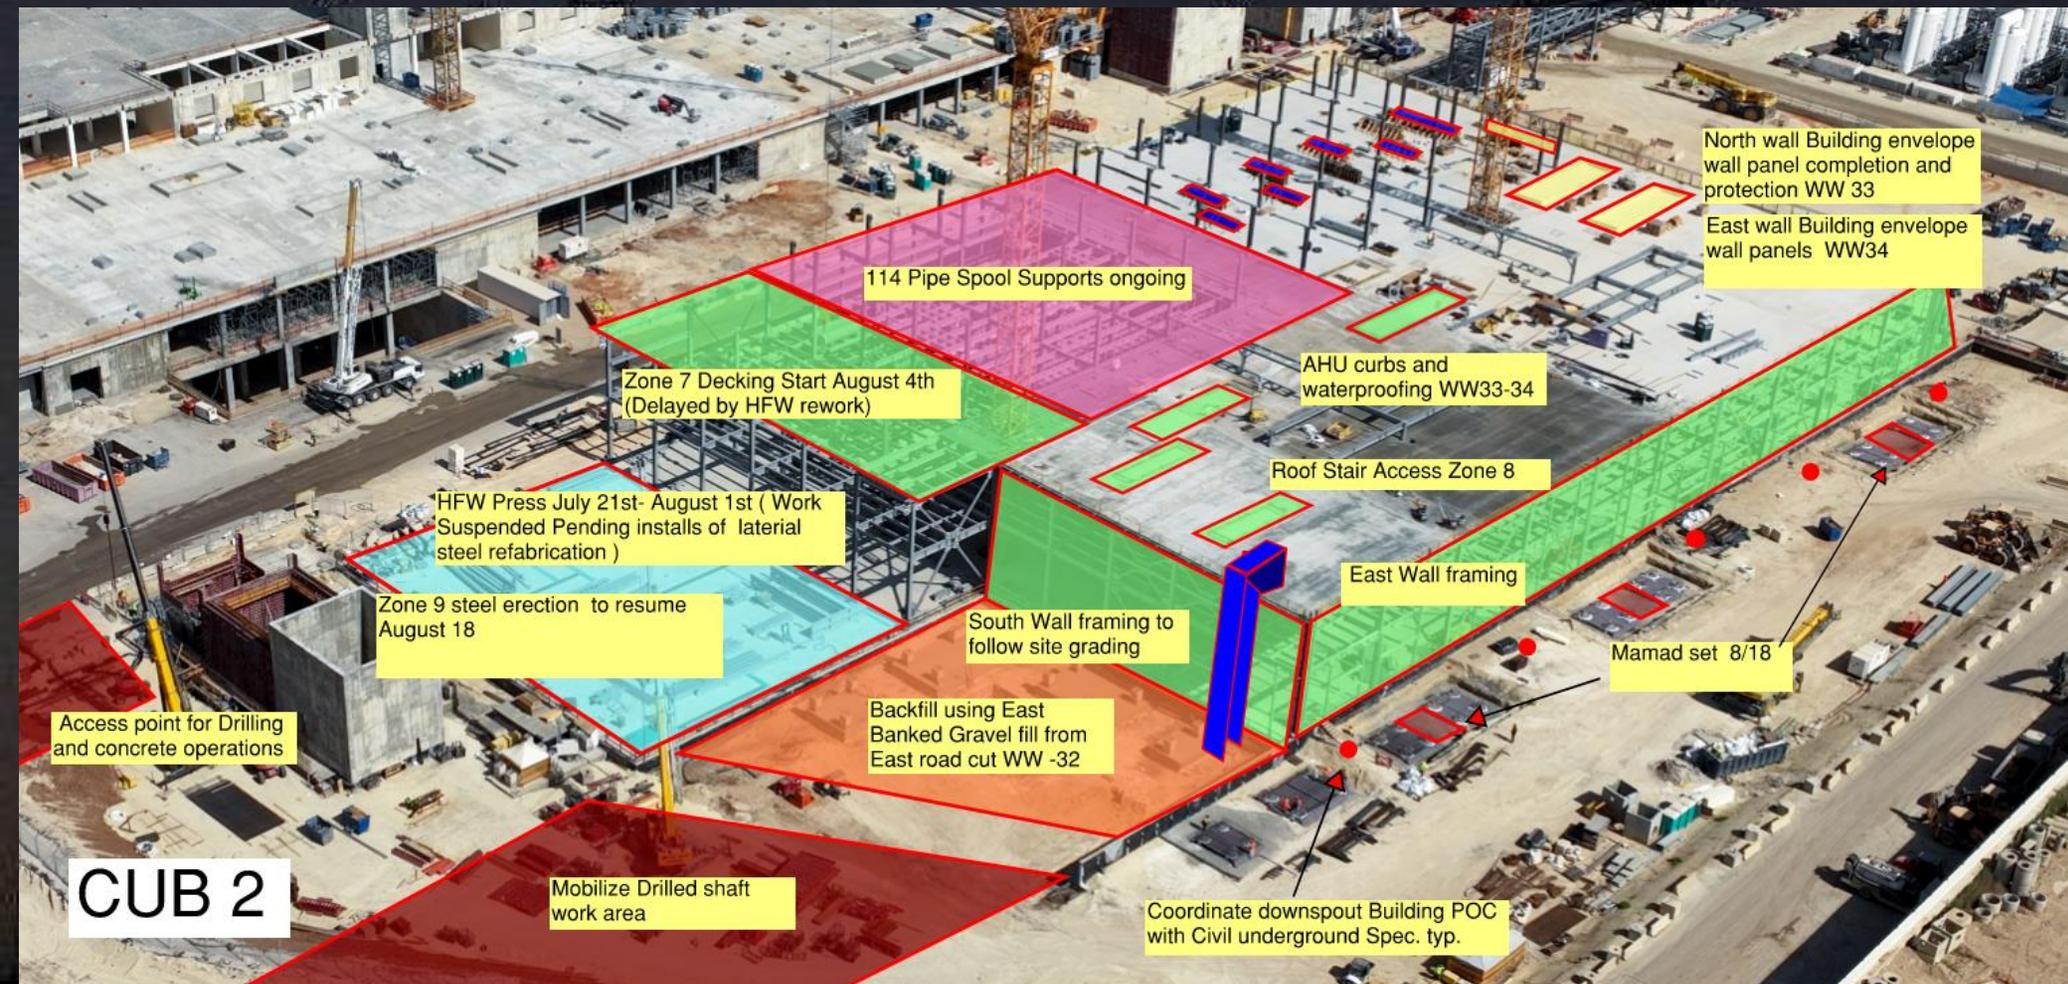

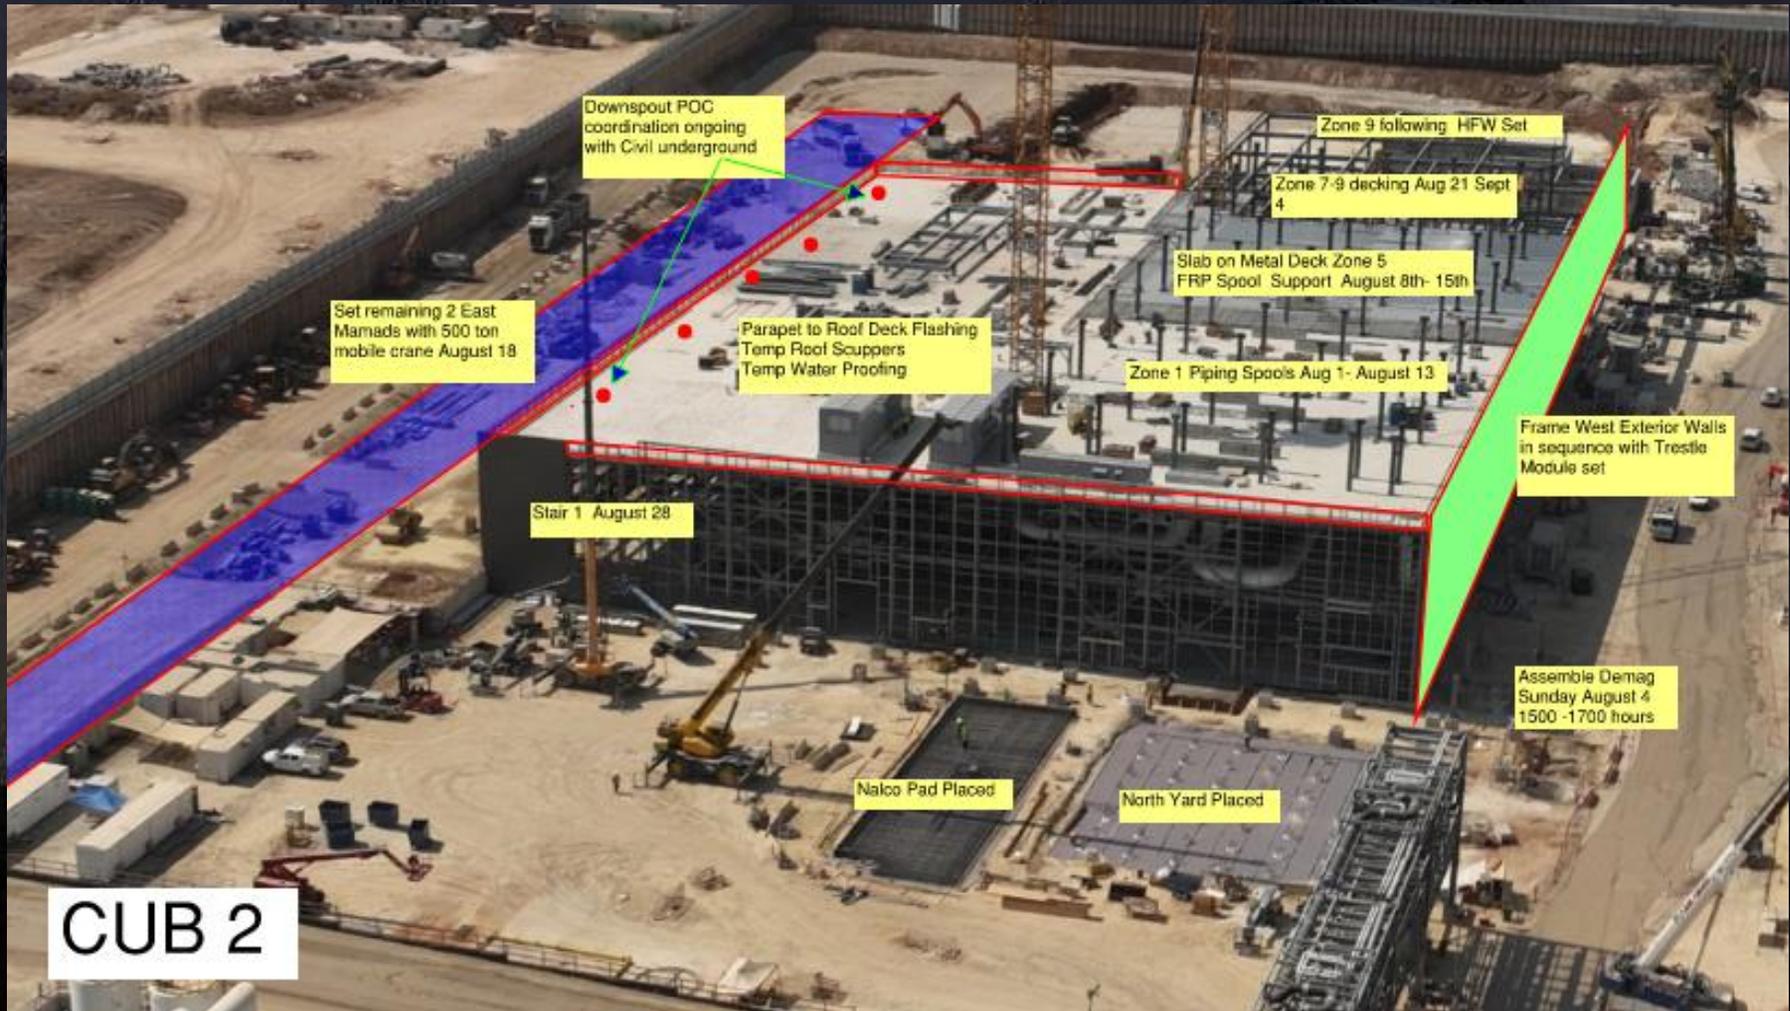

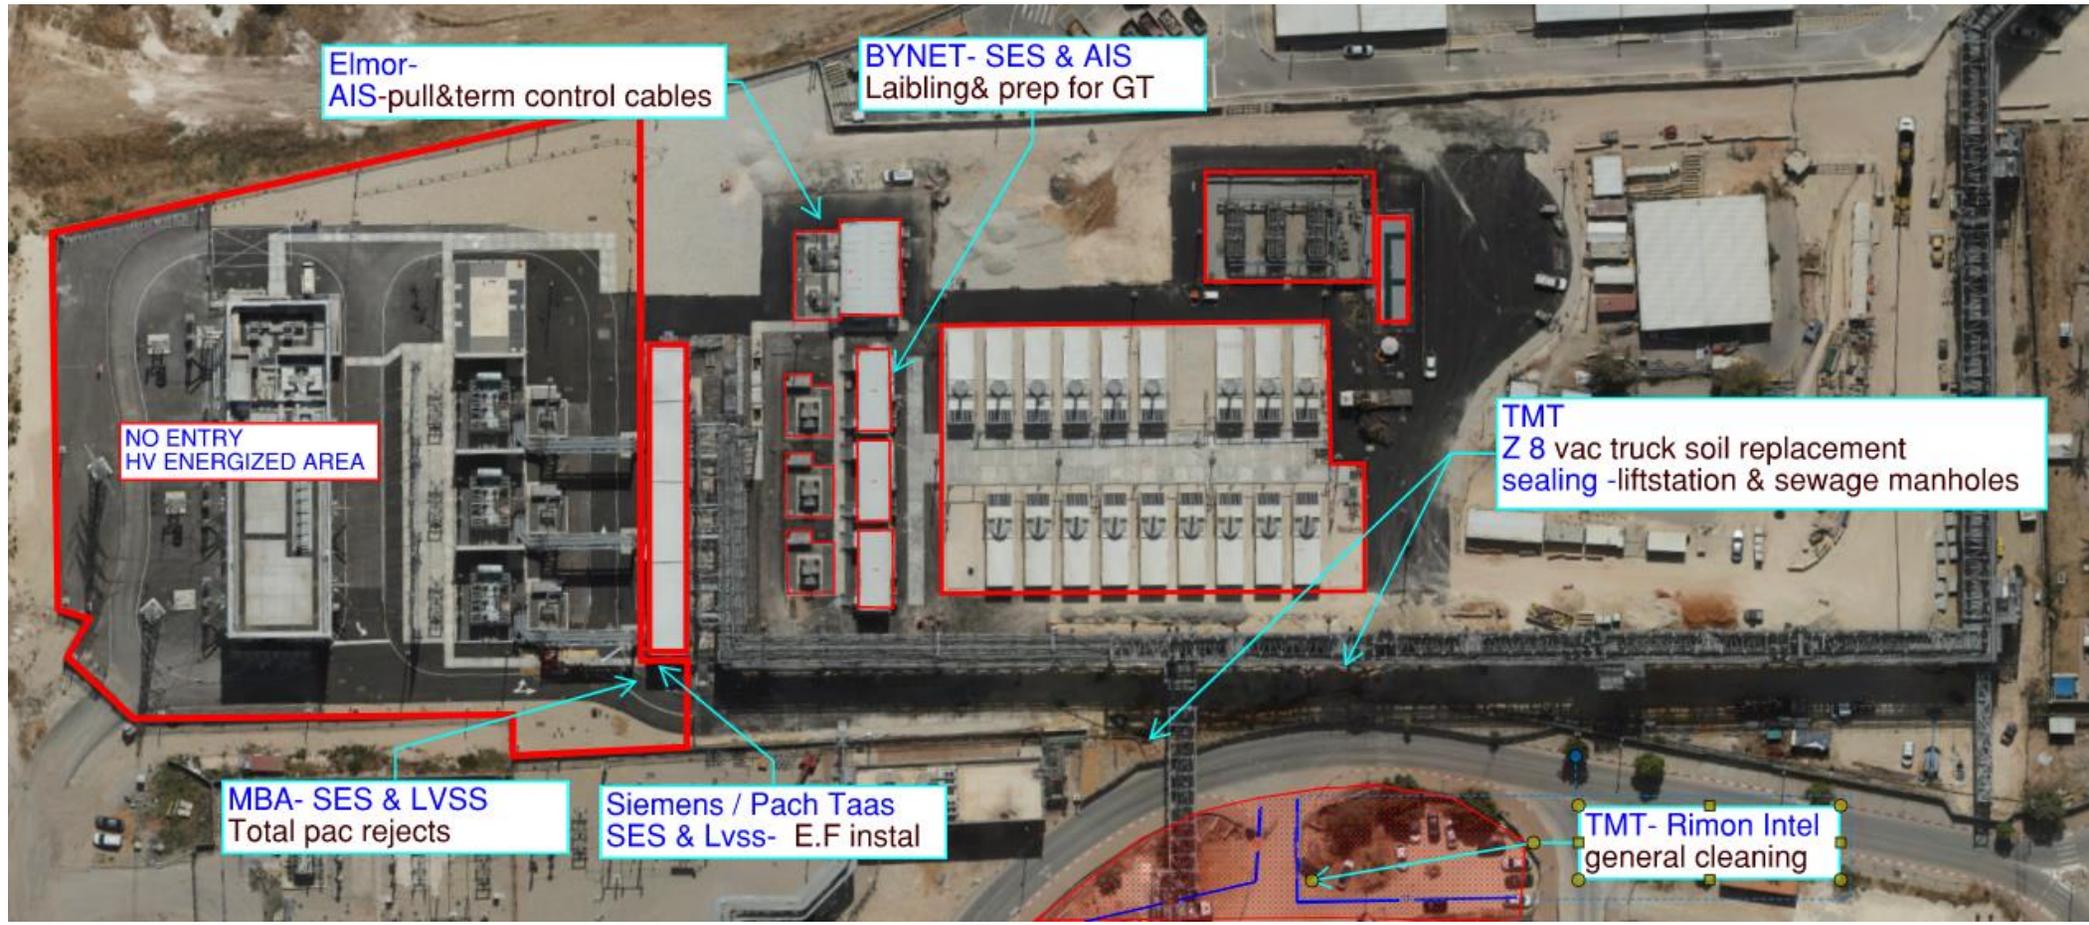

Elmor-
AIS-pull&term control cables

BYNET- SES & AIS
Laibling& prep for GT

NO ENTRY
HV ENERGIZED AREA

TMT
Z 8 vac truck soil replacement
sealing -liftstation & sewage manholes

MBA- SES & LVSS
Total pac rejects


Siemens / Pach Taas
SES & Lvss- E.F instal

TMT- Rimon Intel
general cleaning




Trestle - MOD 2 Steel erection


T-17 Lvl 1

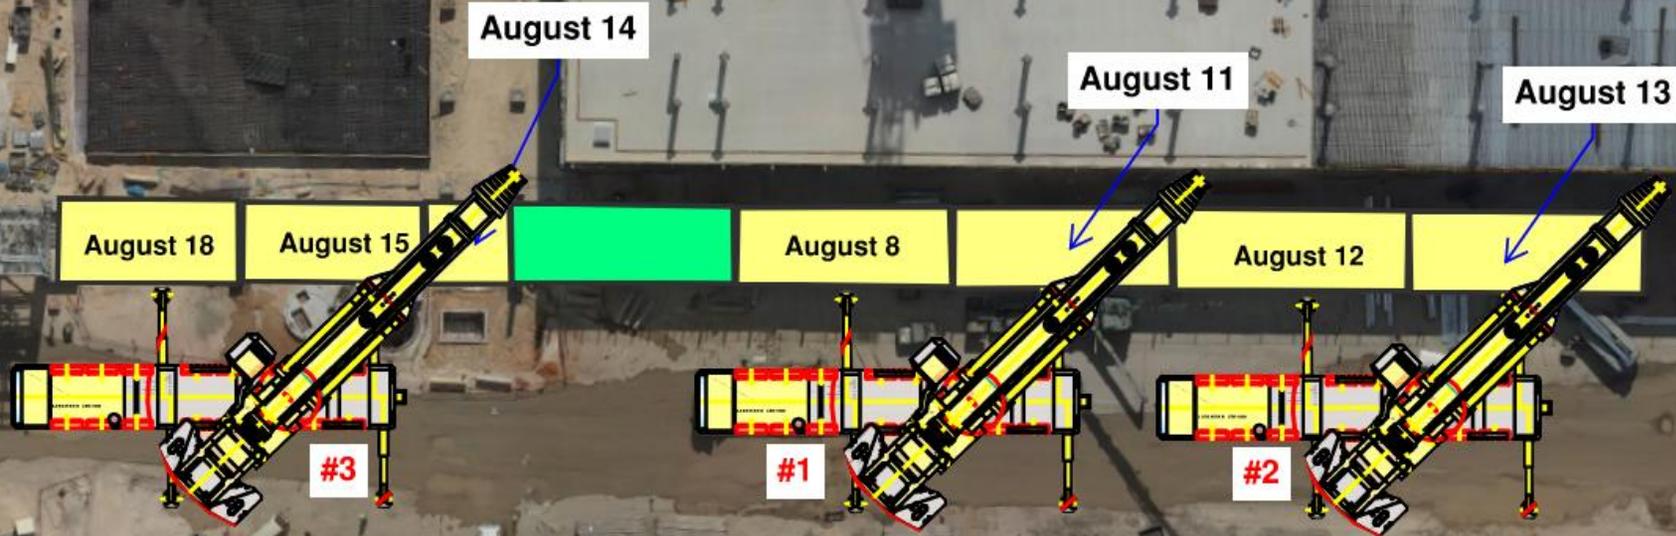

Trestle - MOD 2 Steel erection


T-17 Lvl 2

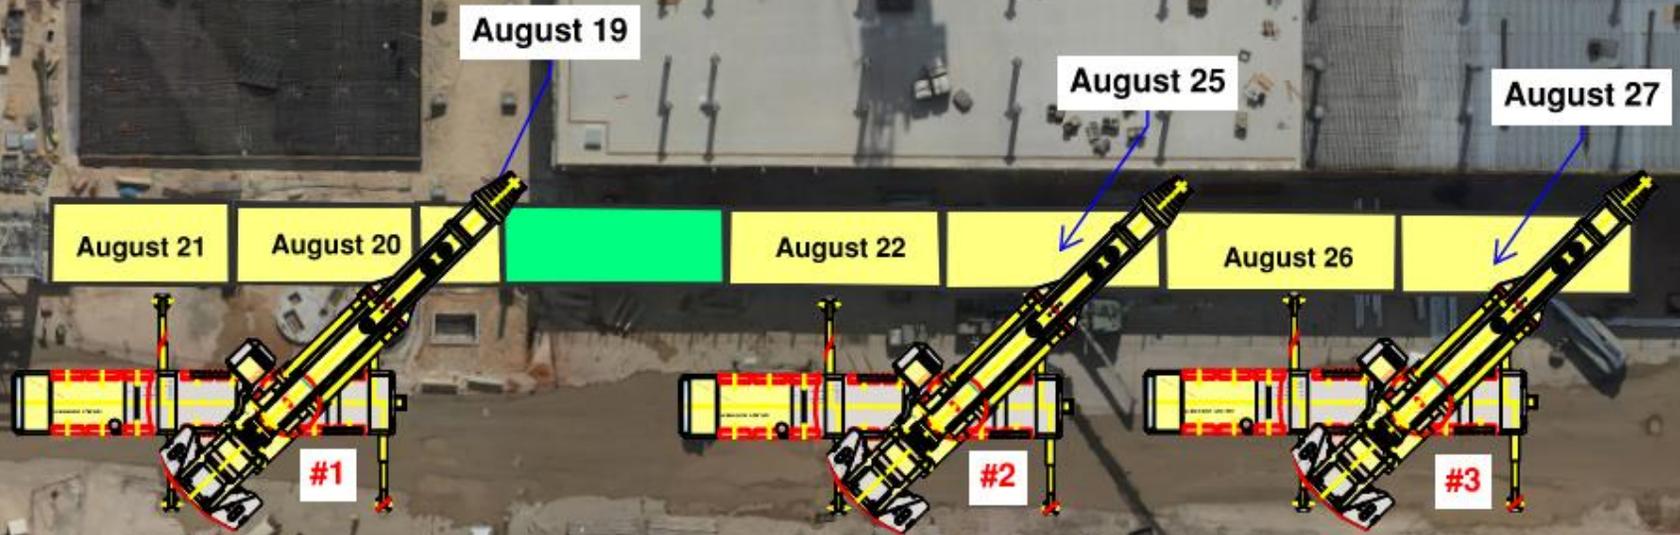

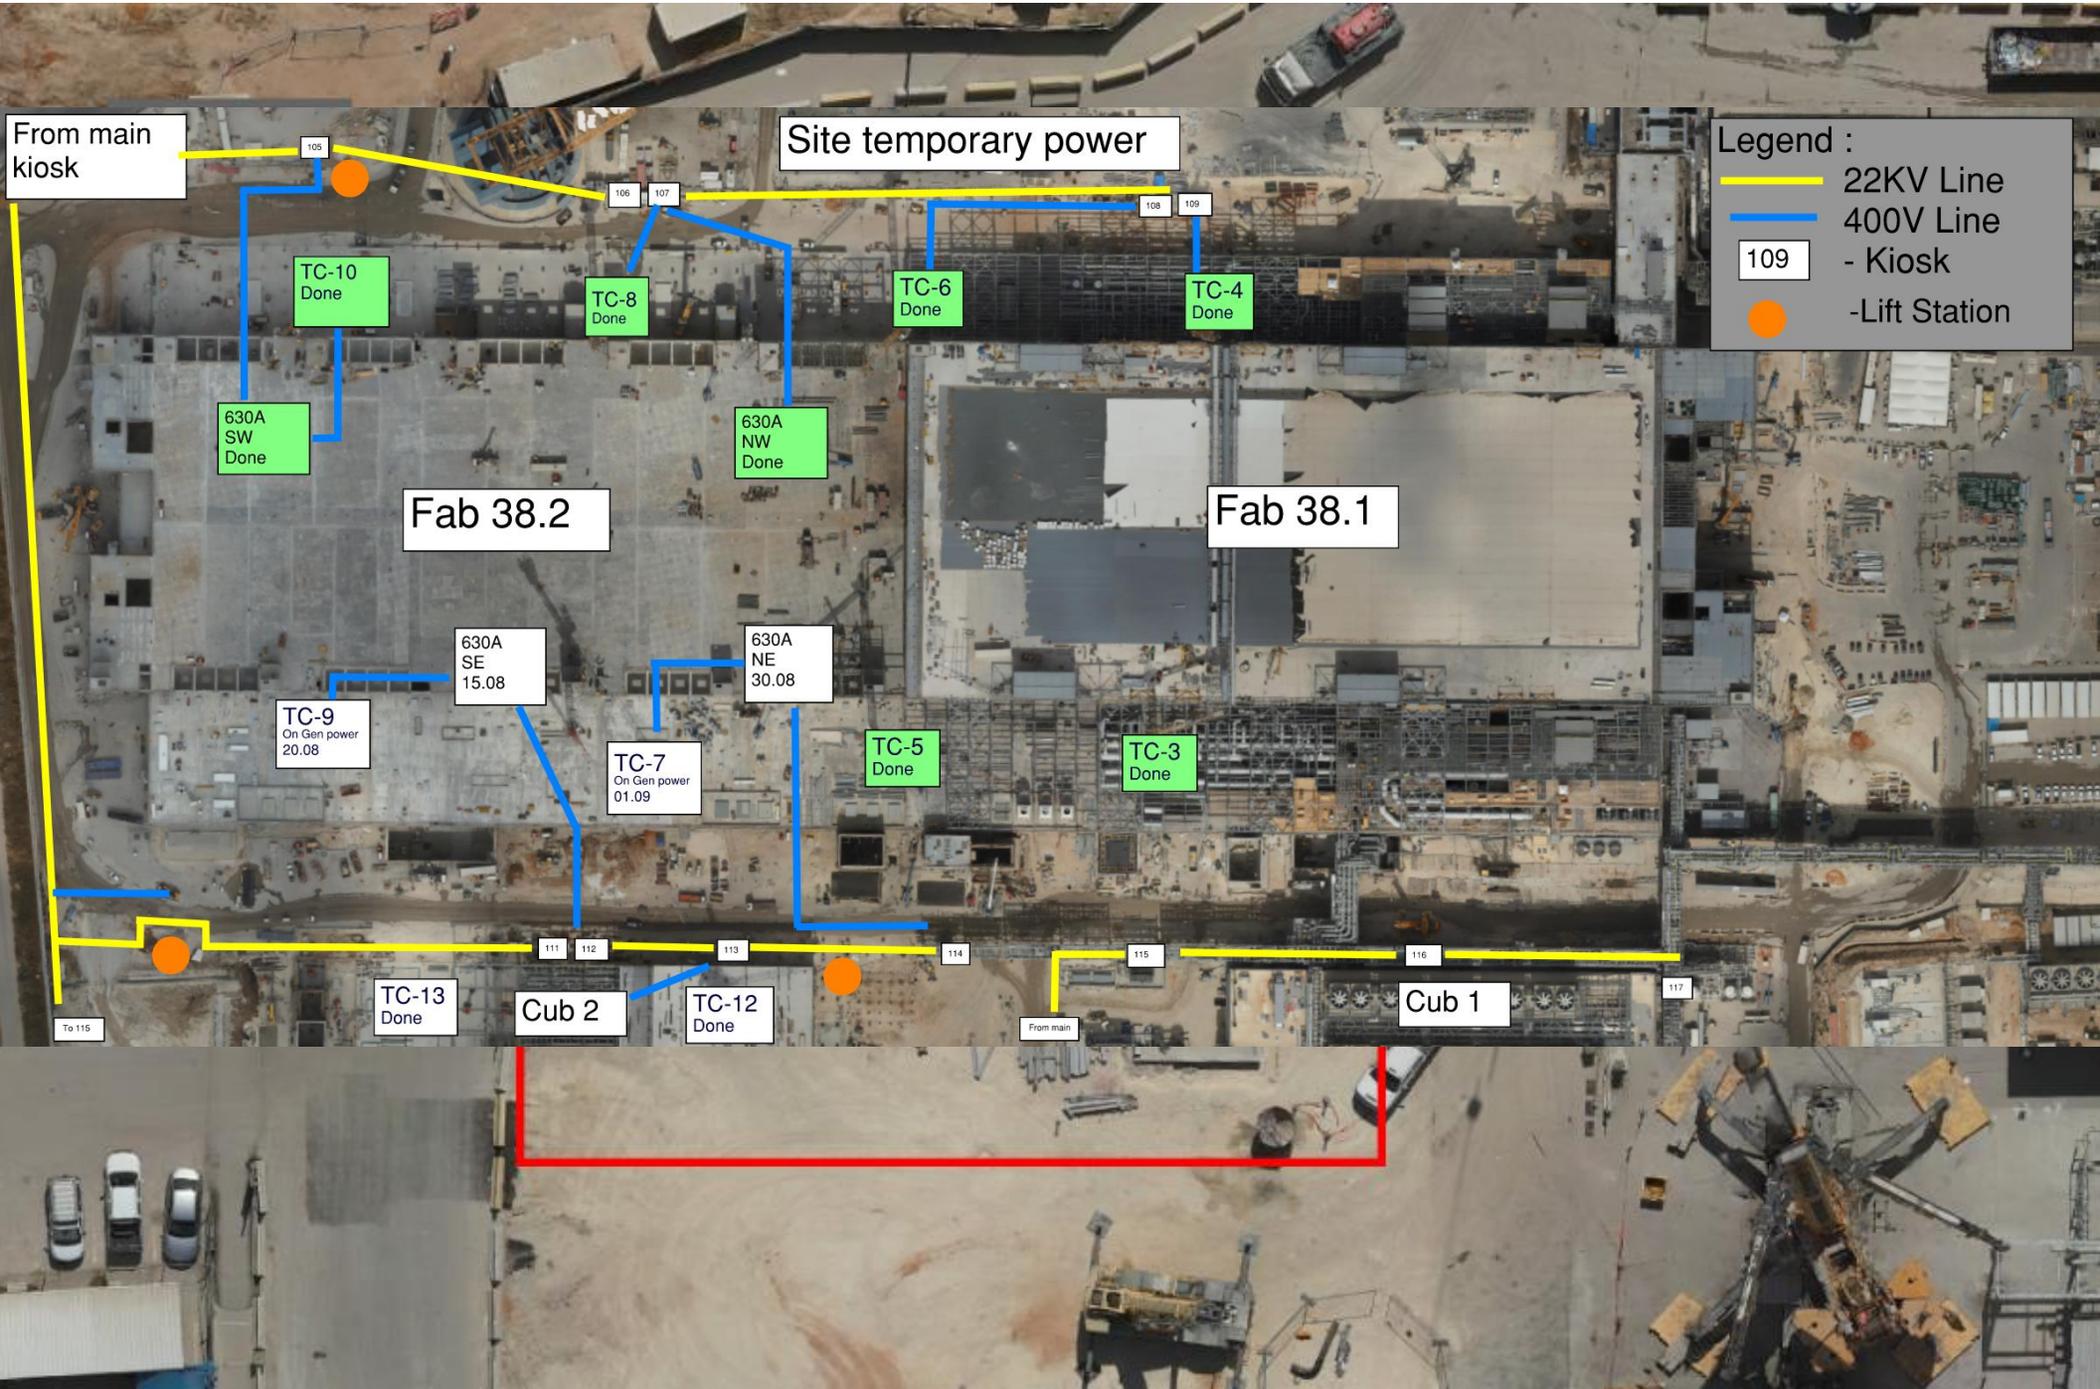

Daily Coordination Meeting

Site Logistics
North Gate B

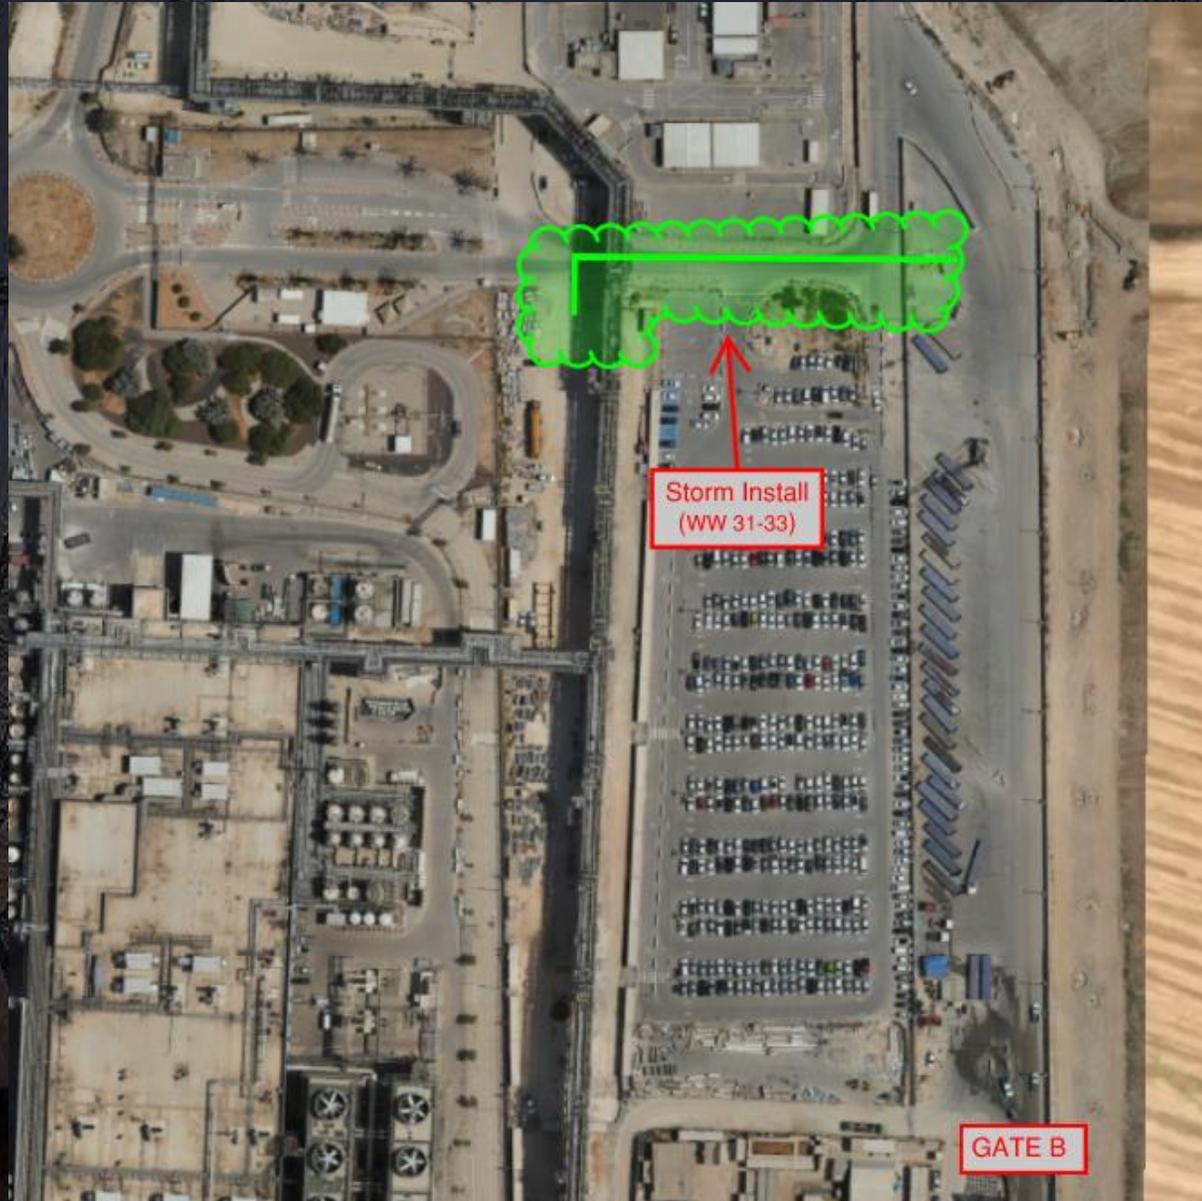

Daily Coordination Meeting

Site Logistics


North



Daily Coordination Meeting

Site Logistics


South

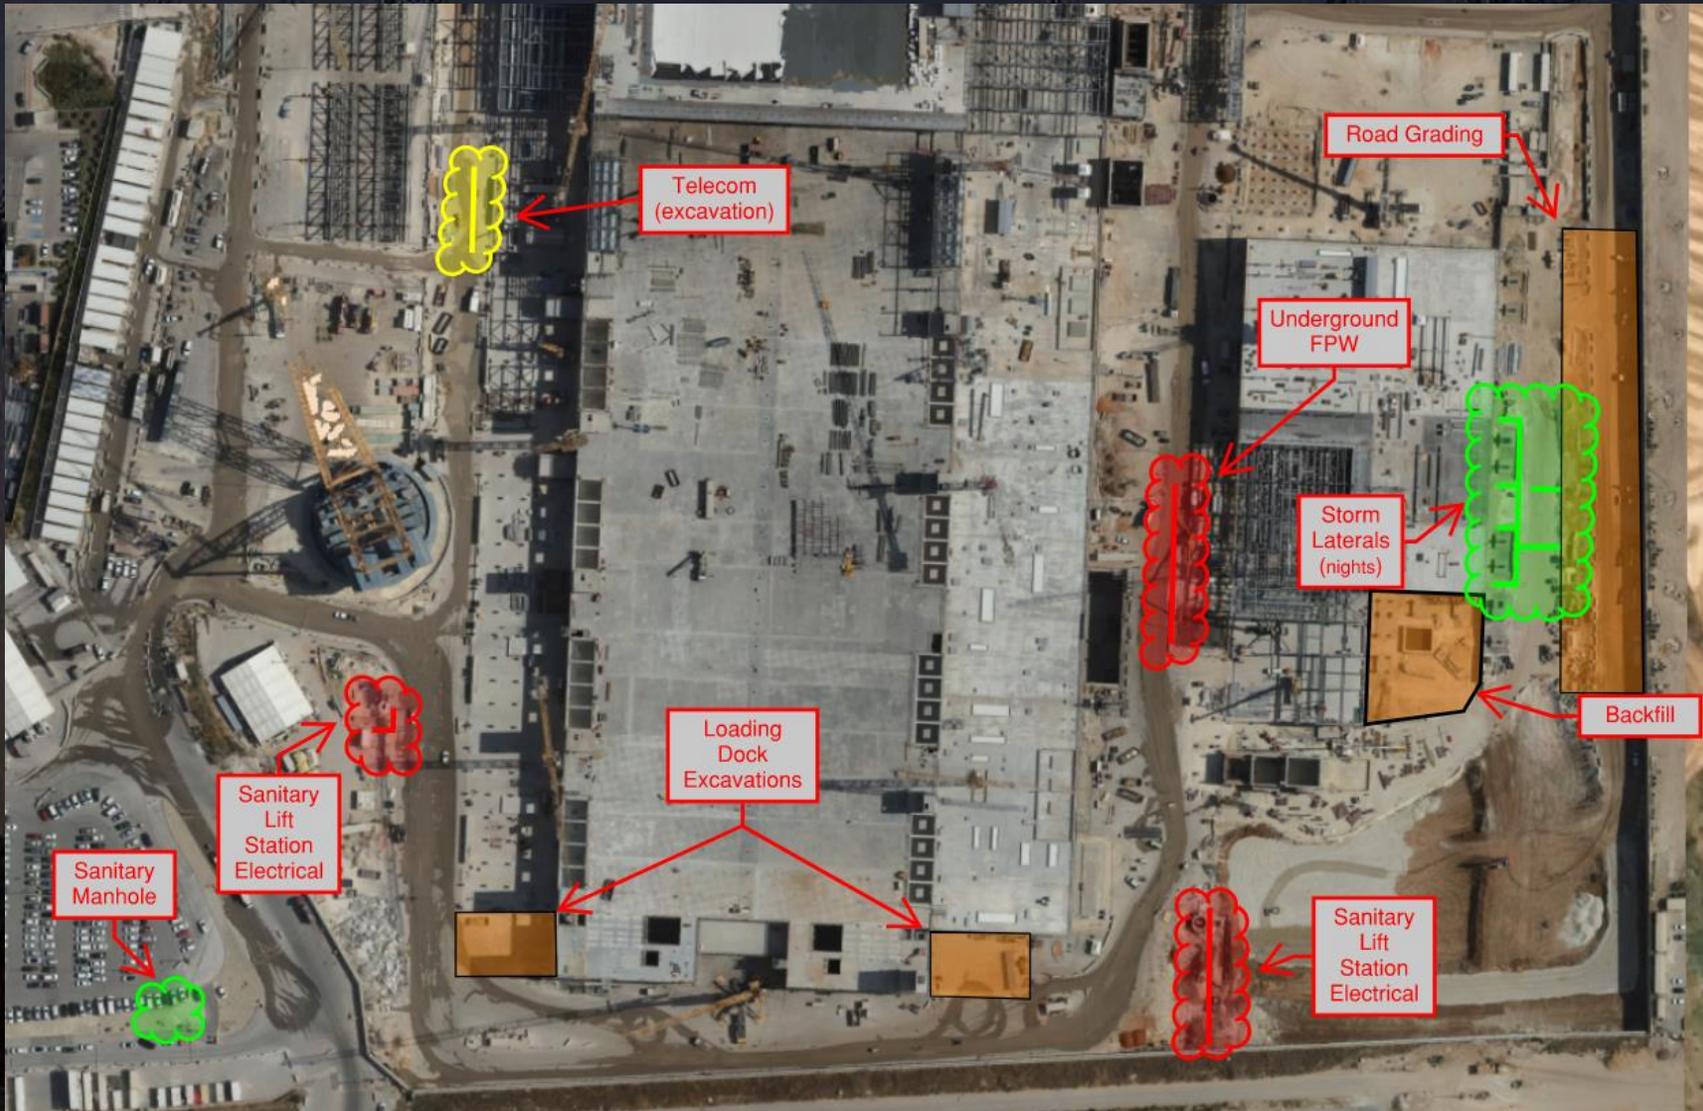


Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

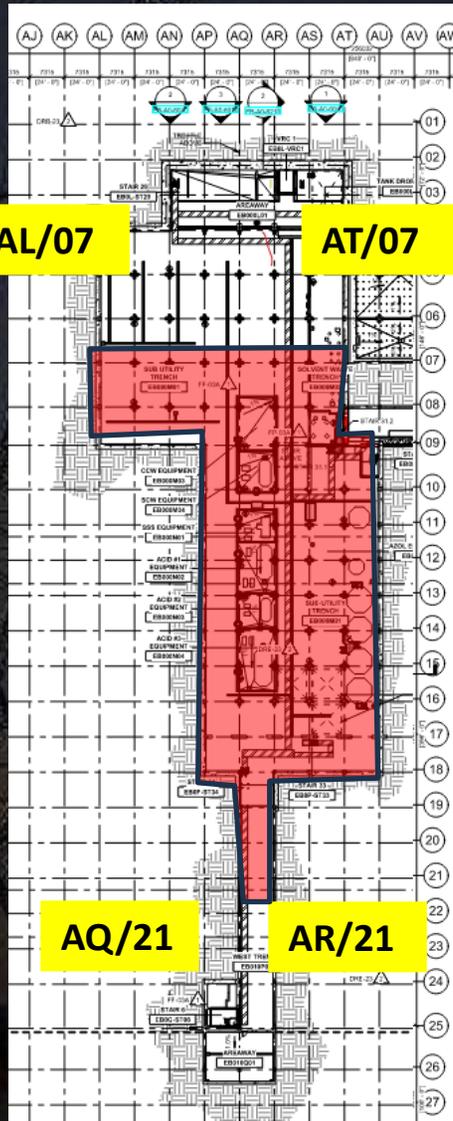


SUT2

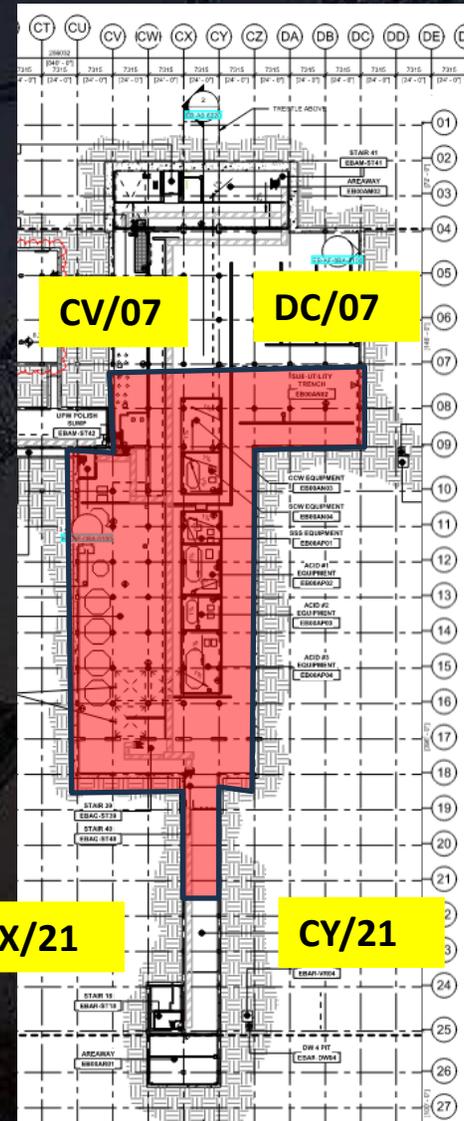

Daily Coordination Meeting


Site Logistics - Protected Areas (Utility Level)

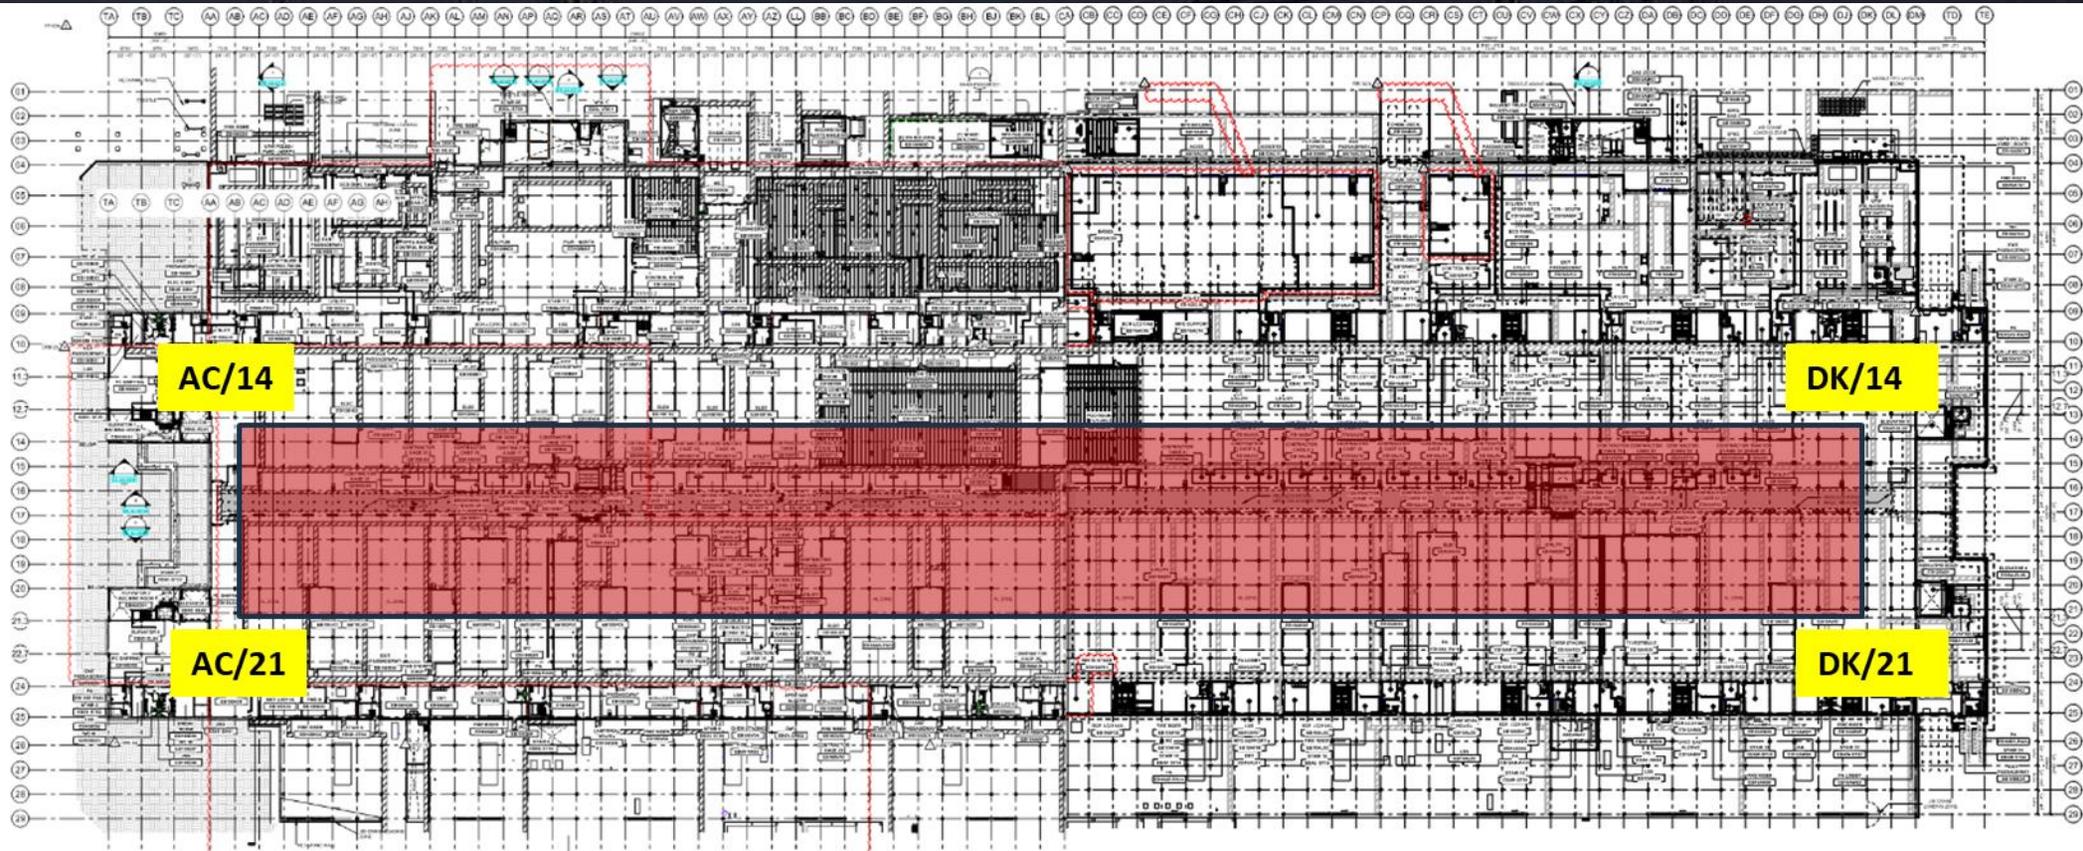

Daily Coordination Meeting


Site Logistics

Protected Areas

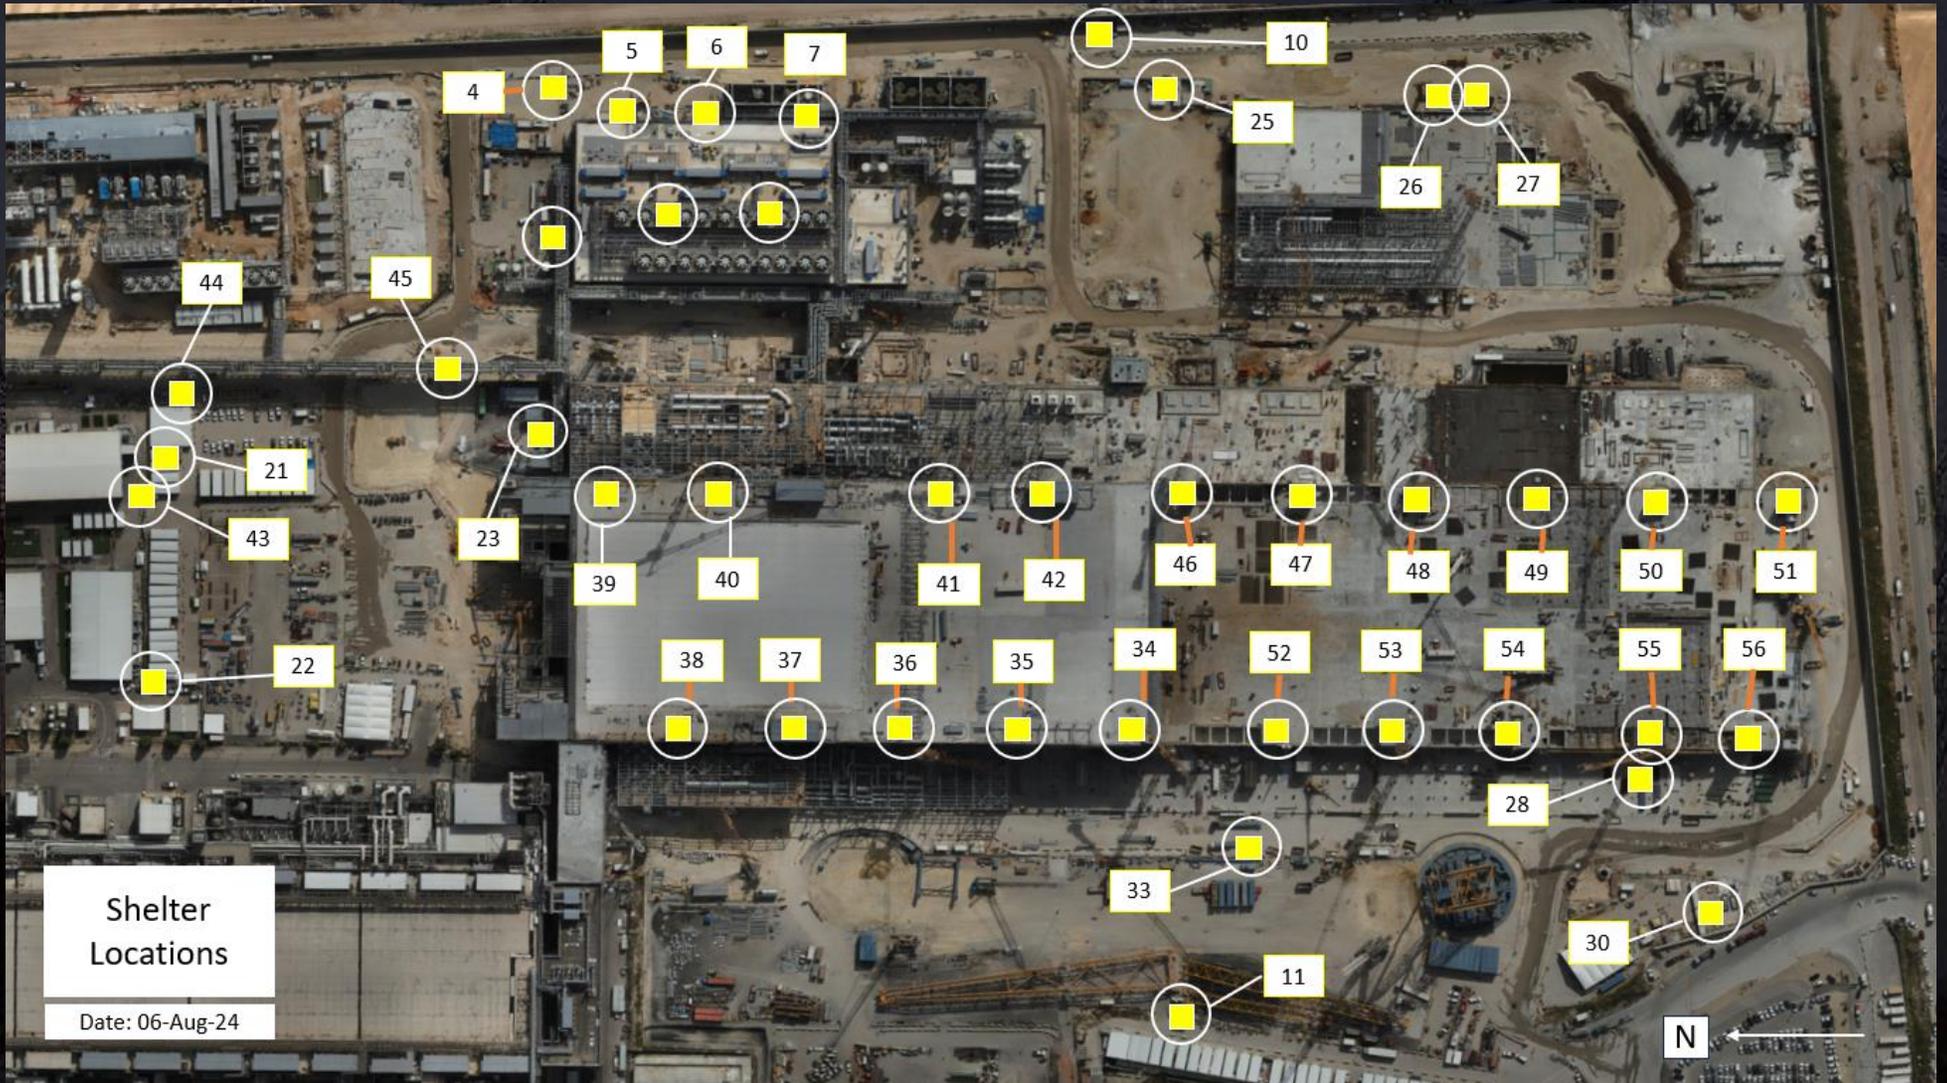

Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

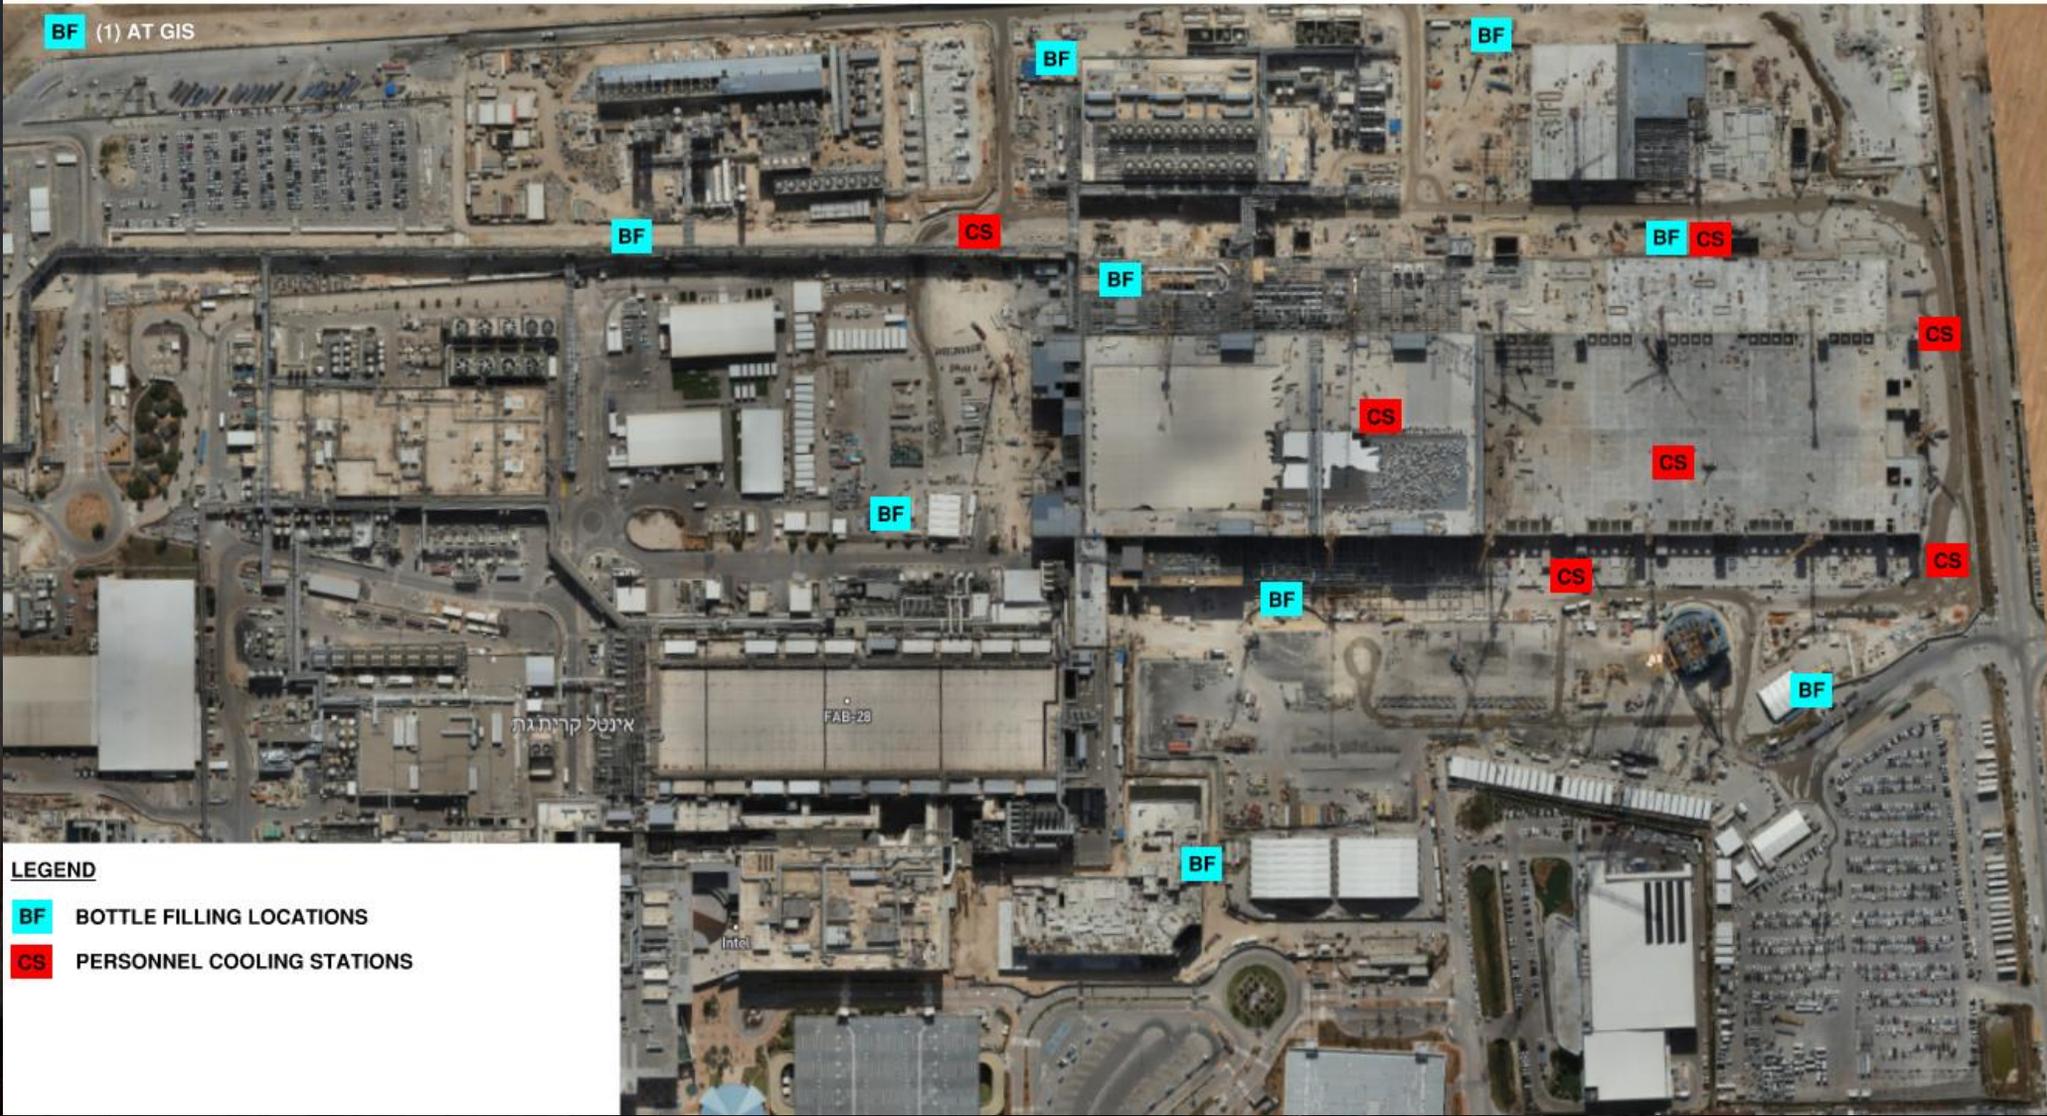


LEGEND
BF BOTTLE FILLING LOCATIONS
CS PERSONNEL COOLING STATIONS

PTP for Every Task

- Each task must have a plan. We document this plan using the PTP forms.
- This includes tasks that aren't strictly productive- such as changing out attachments on equipment, clearing access for our activities, etc.
- We have seen some improvement in our planning, but are still finding crews working without proper plans, without area assessments, and without good communication.
- Yesterday, we had two people injured. Neither crew had a PTP for the work that they were doing, one of the injured workers did not have a PTP at all.

Stop and Think- We've Got the Power

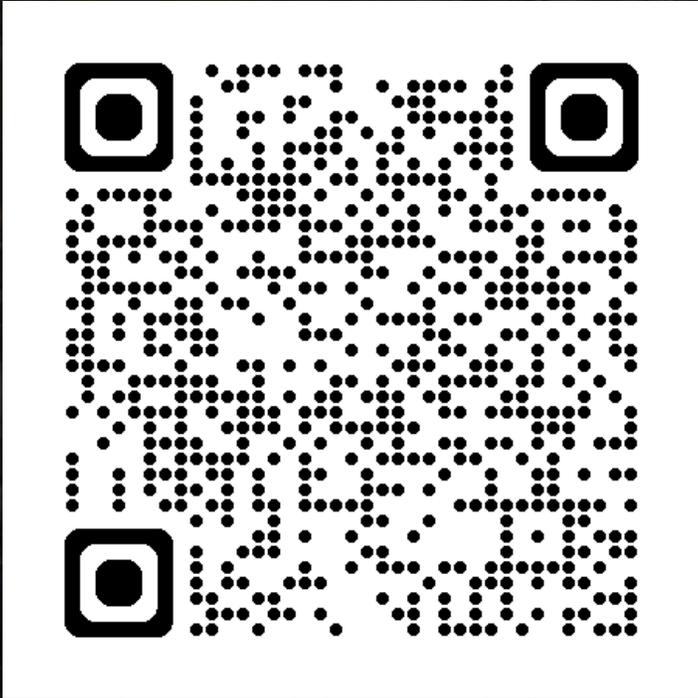

Are you aware of the power that was recently introduced on site? What type of power is it? *

How does this affect you? *

What other live systems are you working around? *

What are you going to do to protect yourself and others from this hazardous energy? *

Complete 1 per day



Heat Index- August 13th

		temperature (°F)														
		80	82	84	86	88	90	92	94	96	98	100	102	104	106	108
Relative Humidity (%)	40	80	81	83	85	88	91	94	101	105	109	114	119	124	130	136
	45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137
	50	81	83	85	88	91	95	99	103	108	113	118	124	131	137	
	55	81	84	86	89	93	97	101	106	112	117	124	130	137		
	60	82	84	88	91	95	100	105	110	116	123	129	137			
	65	82	85	89	93	98	103	108	114	121	128	136				
	70	83	86	90	95	100	105	112	119	126	134					
	75	84	88	92	97	103	109	116	124	132						
	80	84	89	94	100	106	113	121	129							
	85	85	90	96	102	110	117	126	135							
	90	86	91	98	105	113	122	131								
	95	86	93	100	108	117	127									
100	87	95	103	112	121	132										

Caution
 Extreme Caution
 Danger
 Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



14:00 Sign In
