

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:


- Have a nice day



UTILITY LEVEL TRUSS

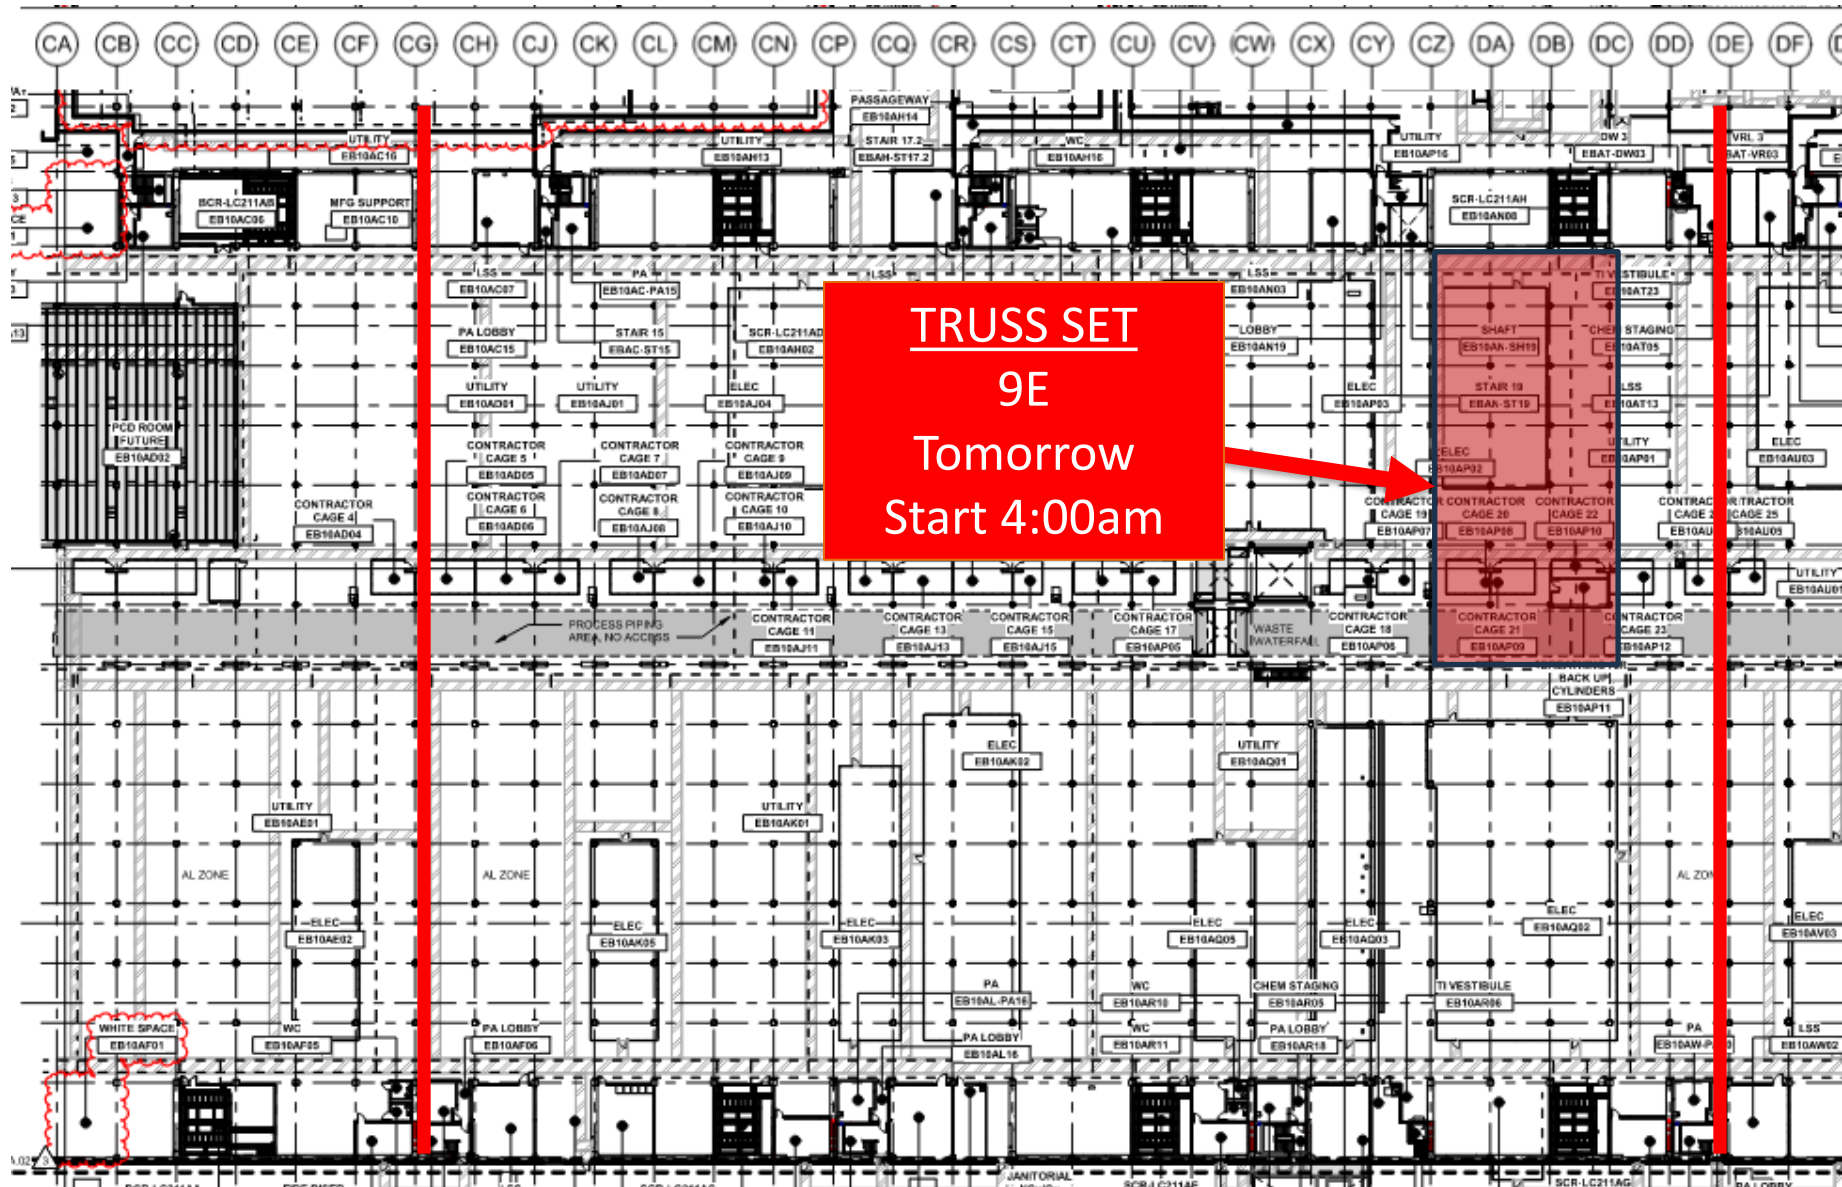

UTILITY LEVEL MOD1

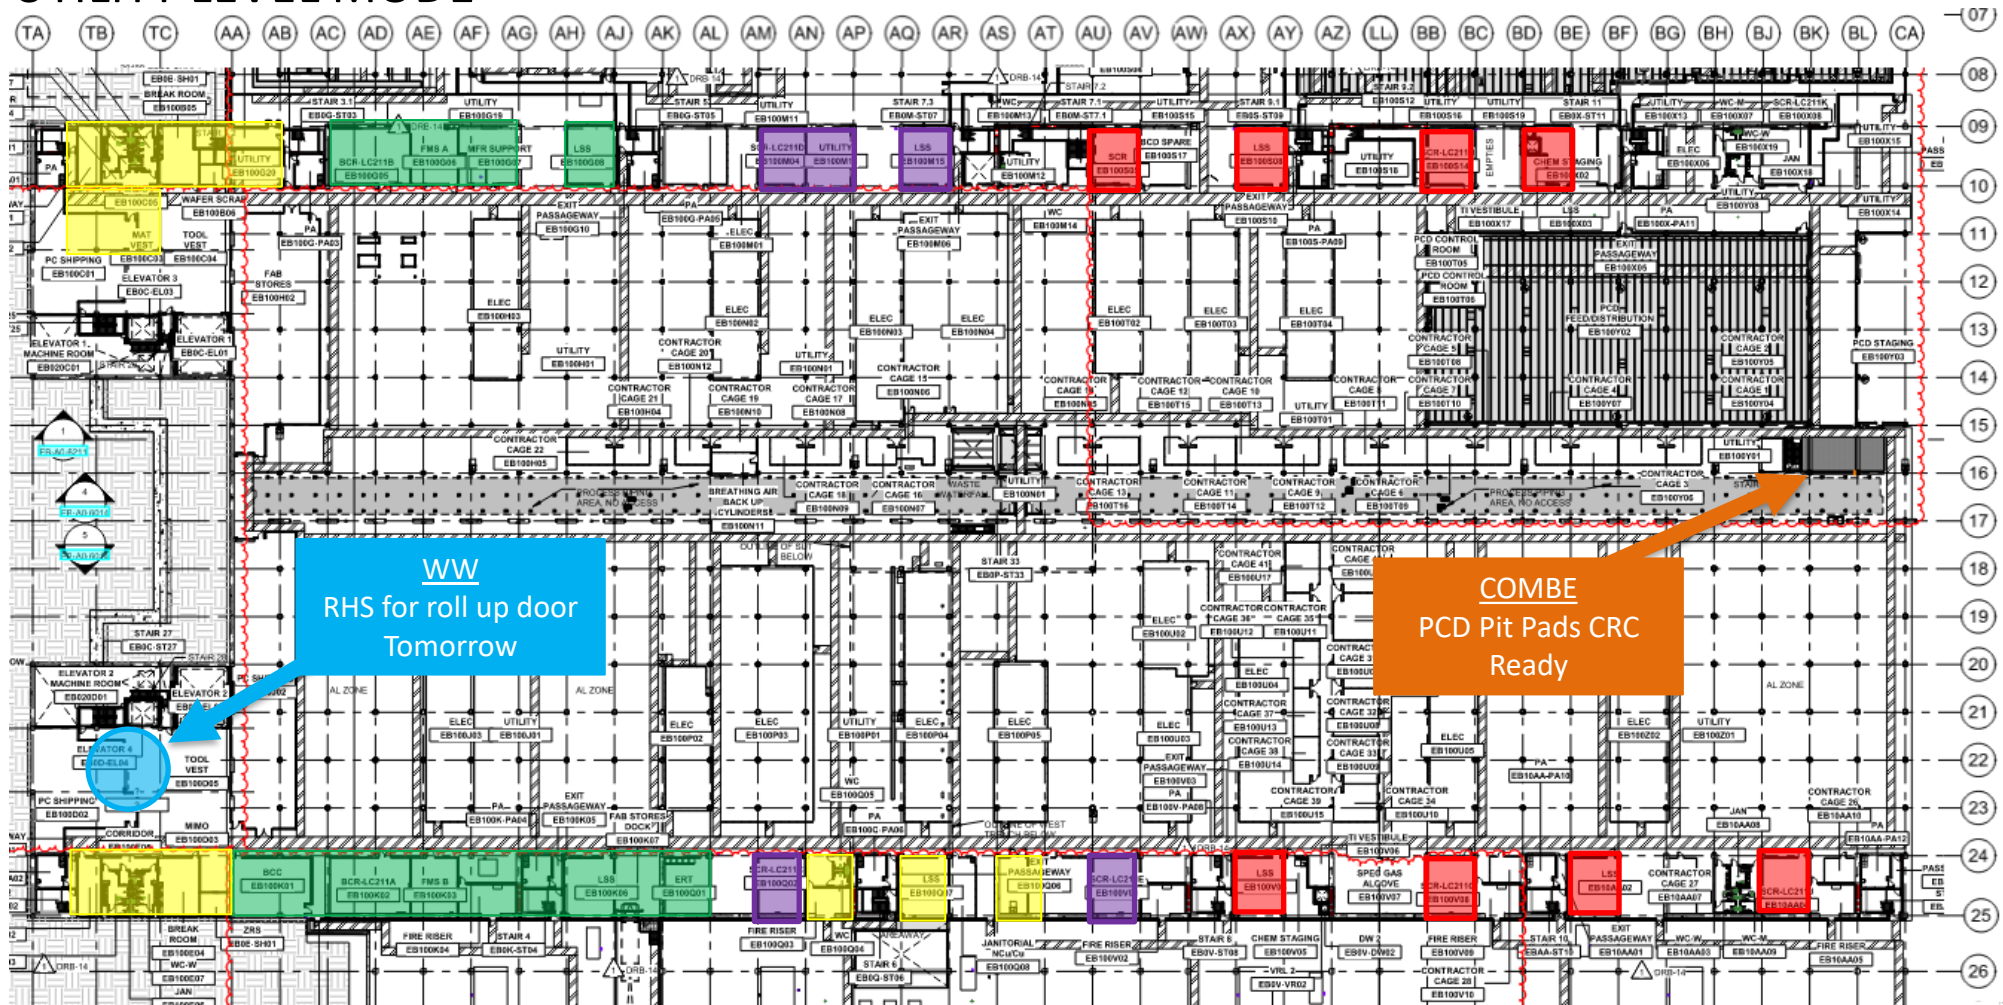

Pre-mold Rem dismantle
Should be uninstll


BELFOR
Mold remediation

ELRAM
Drywall install

MEP+Elctrical
Ready for re-install




UTILITY LEVEL MOD2

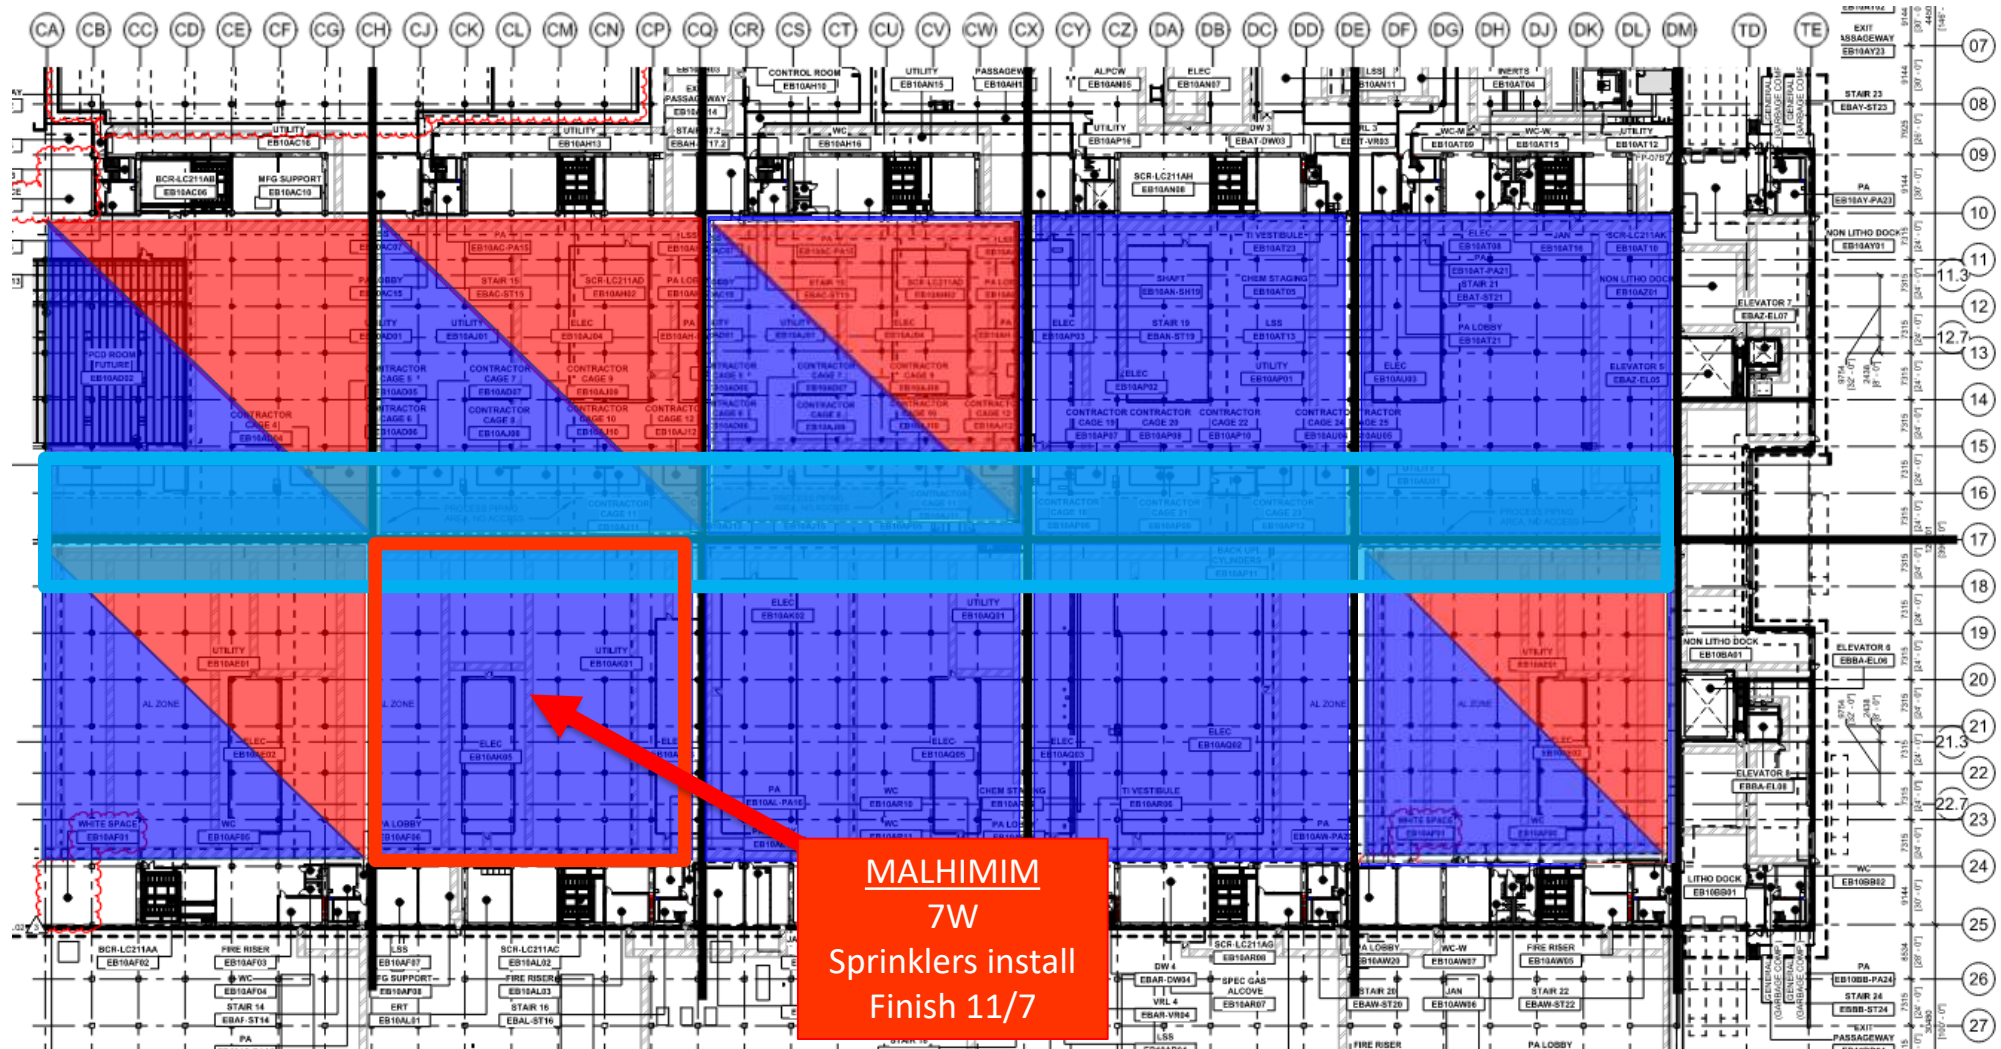





SUT 38.1 LEVEL

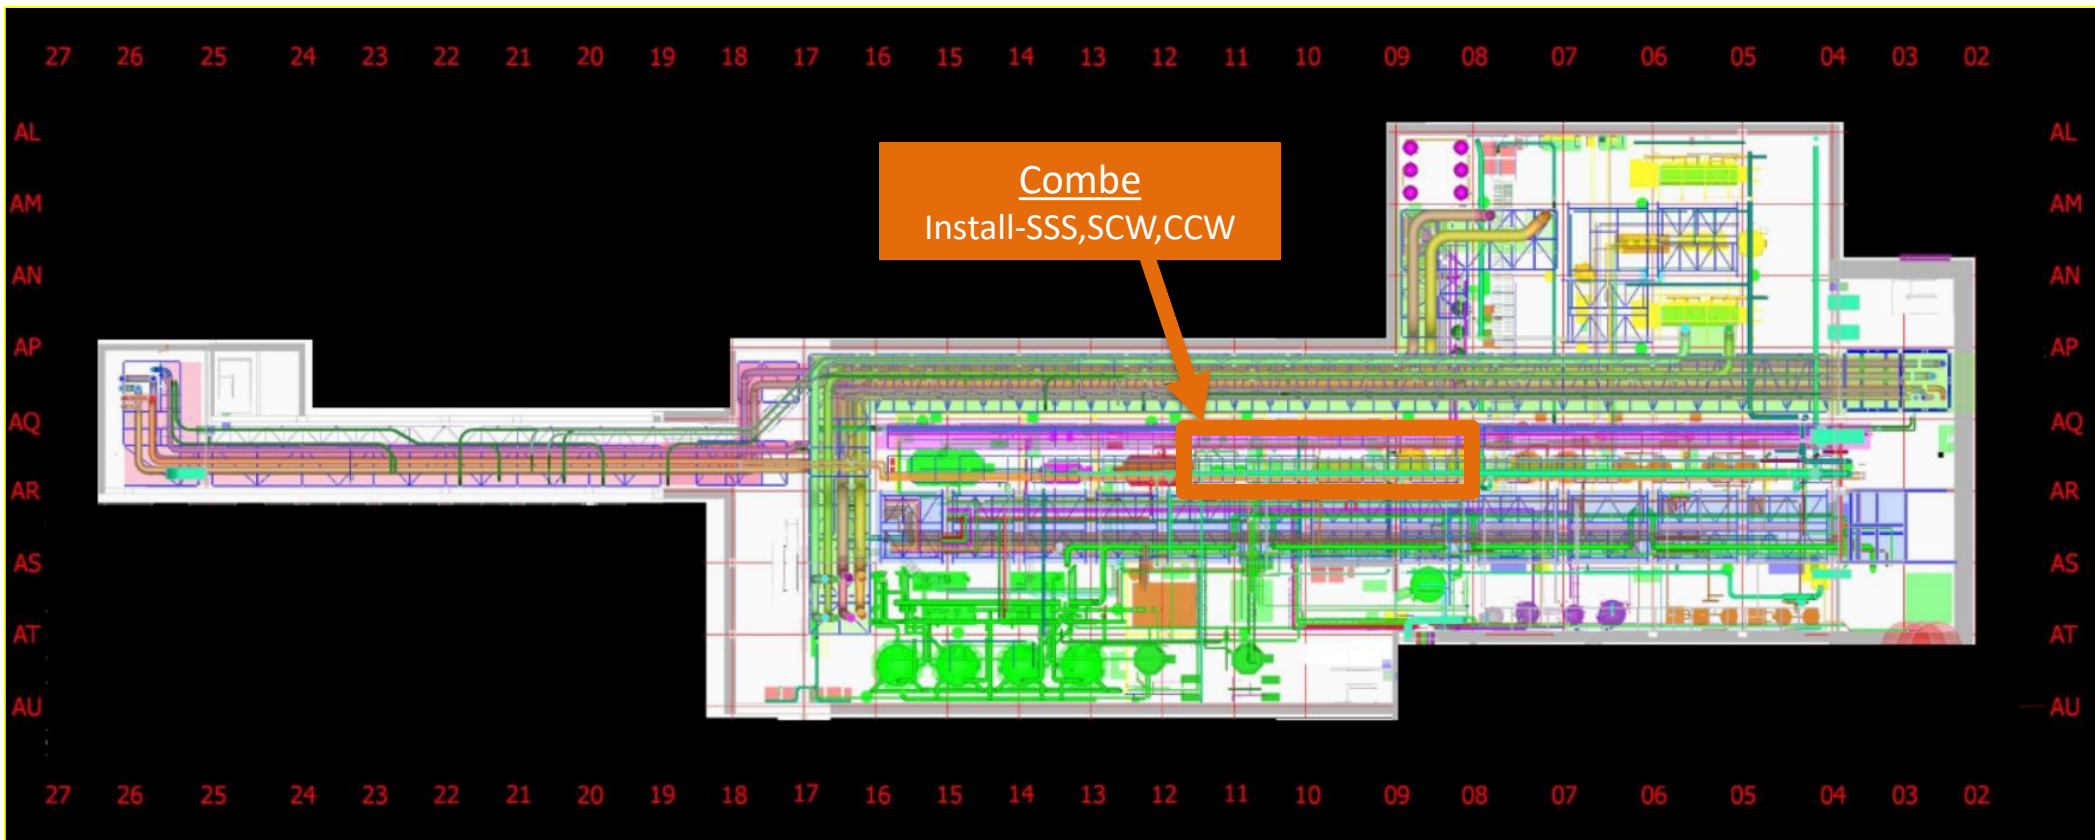


SUT 38.2 LEVEL

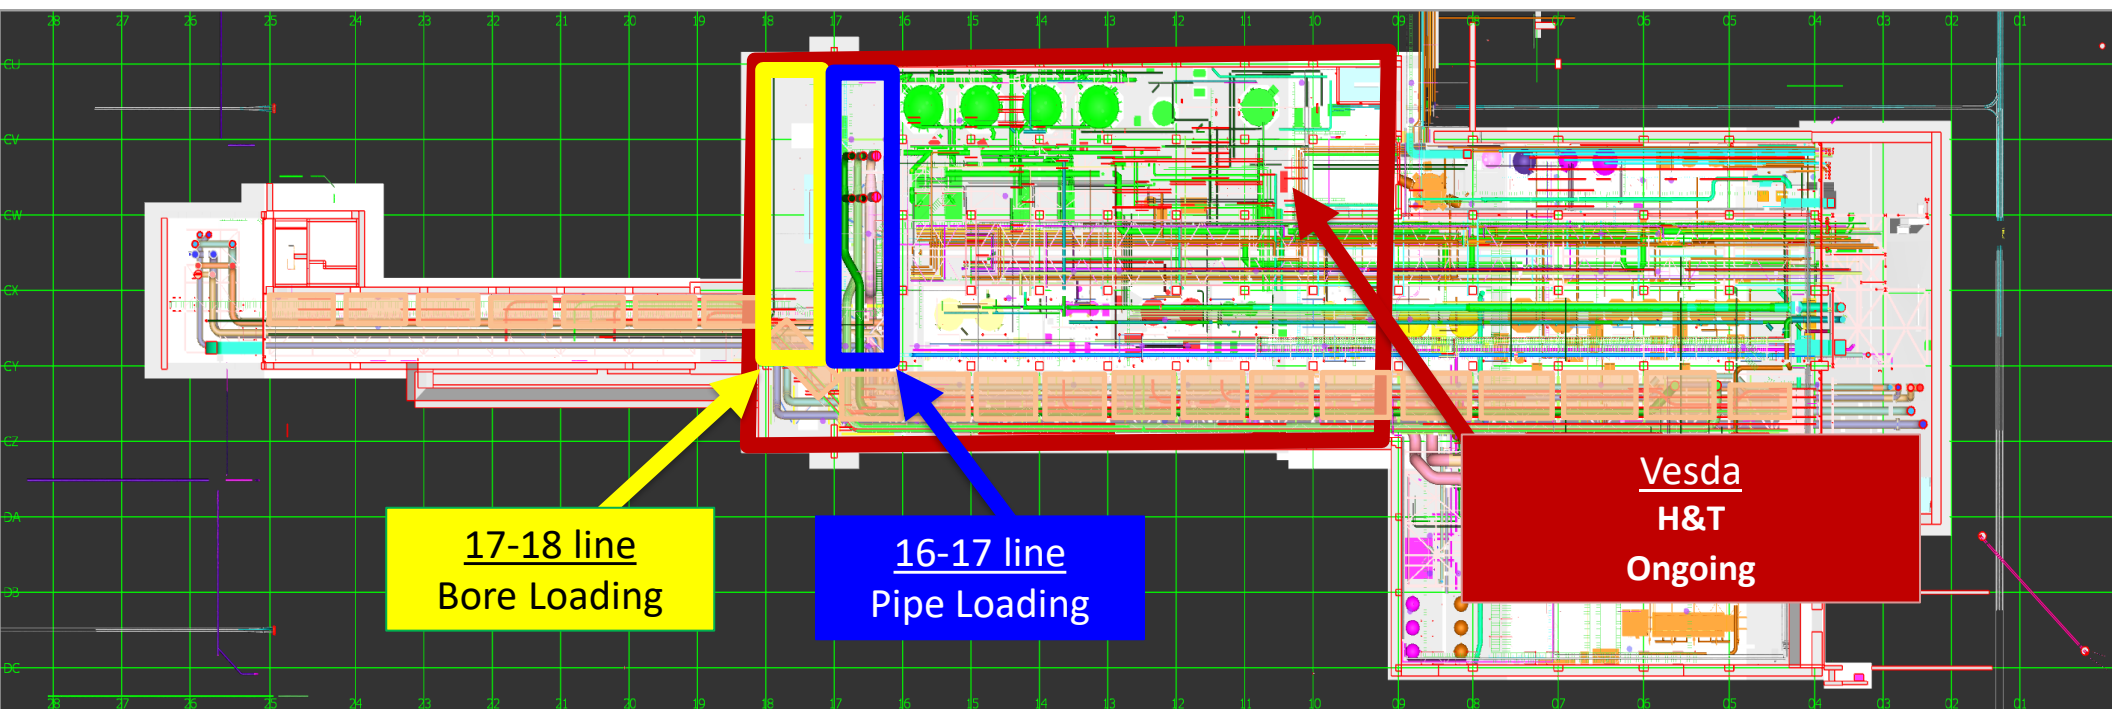


SUBFAB BUILDOUT MOD 1

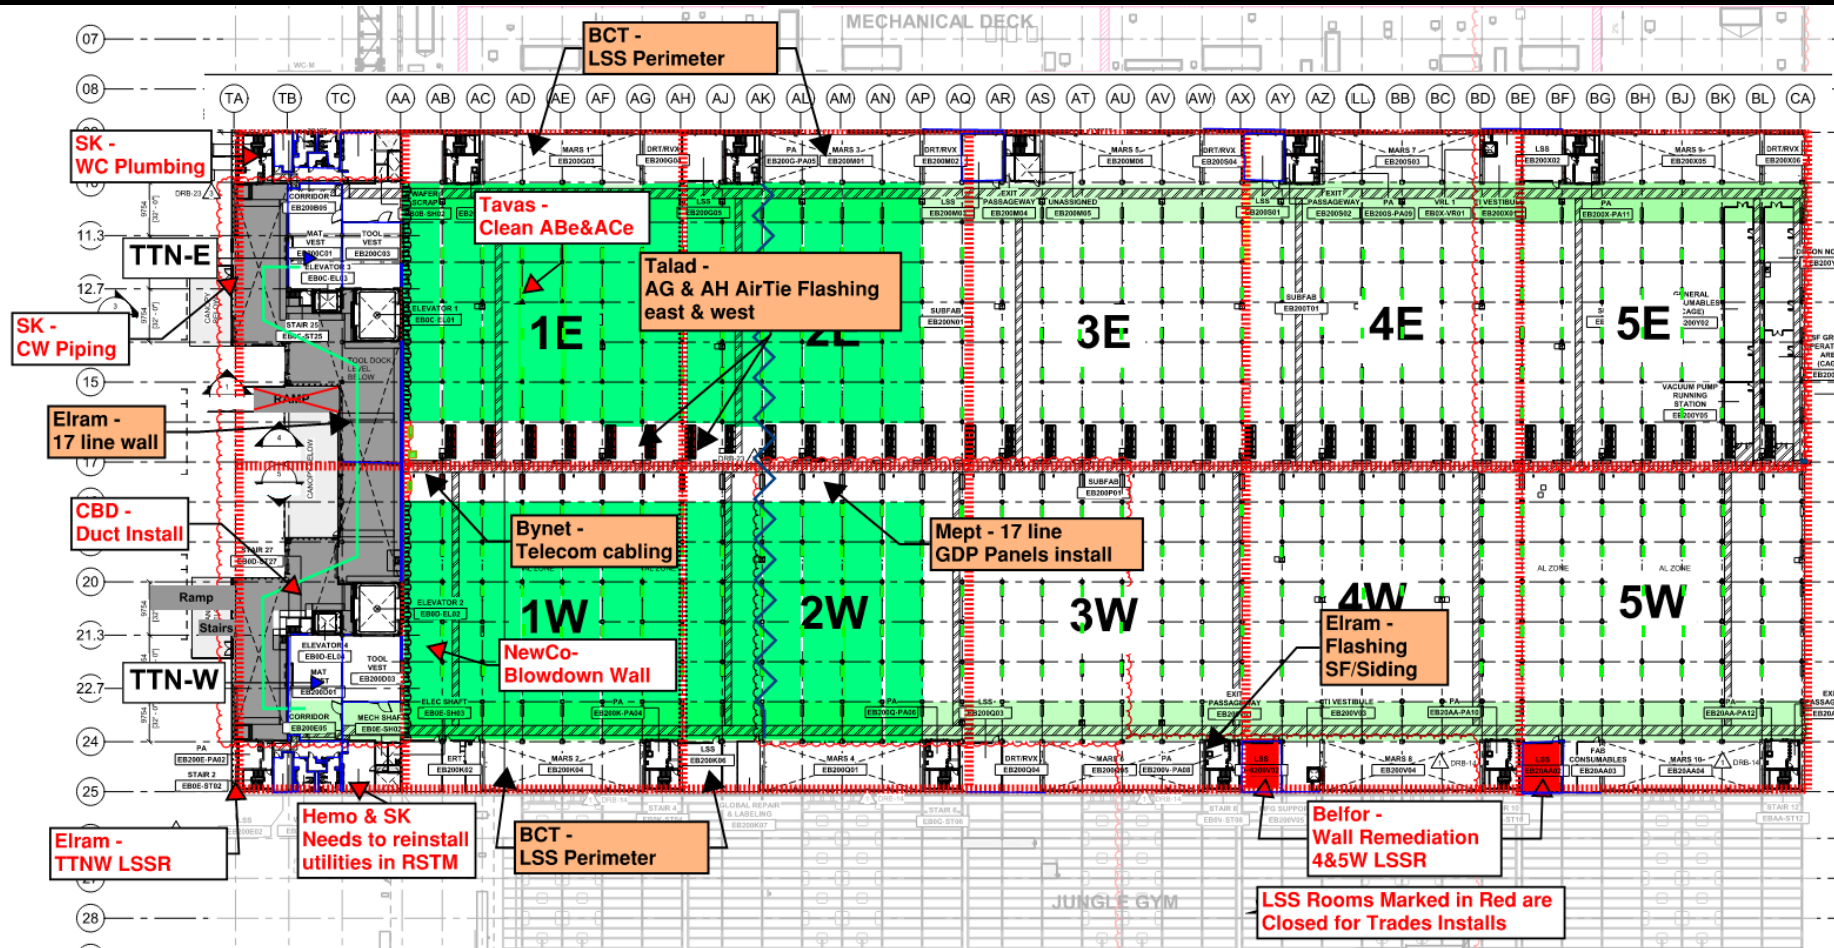


SUBFAB CRC TOPCOAT

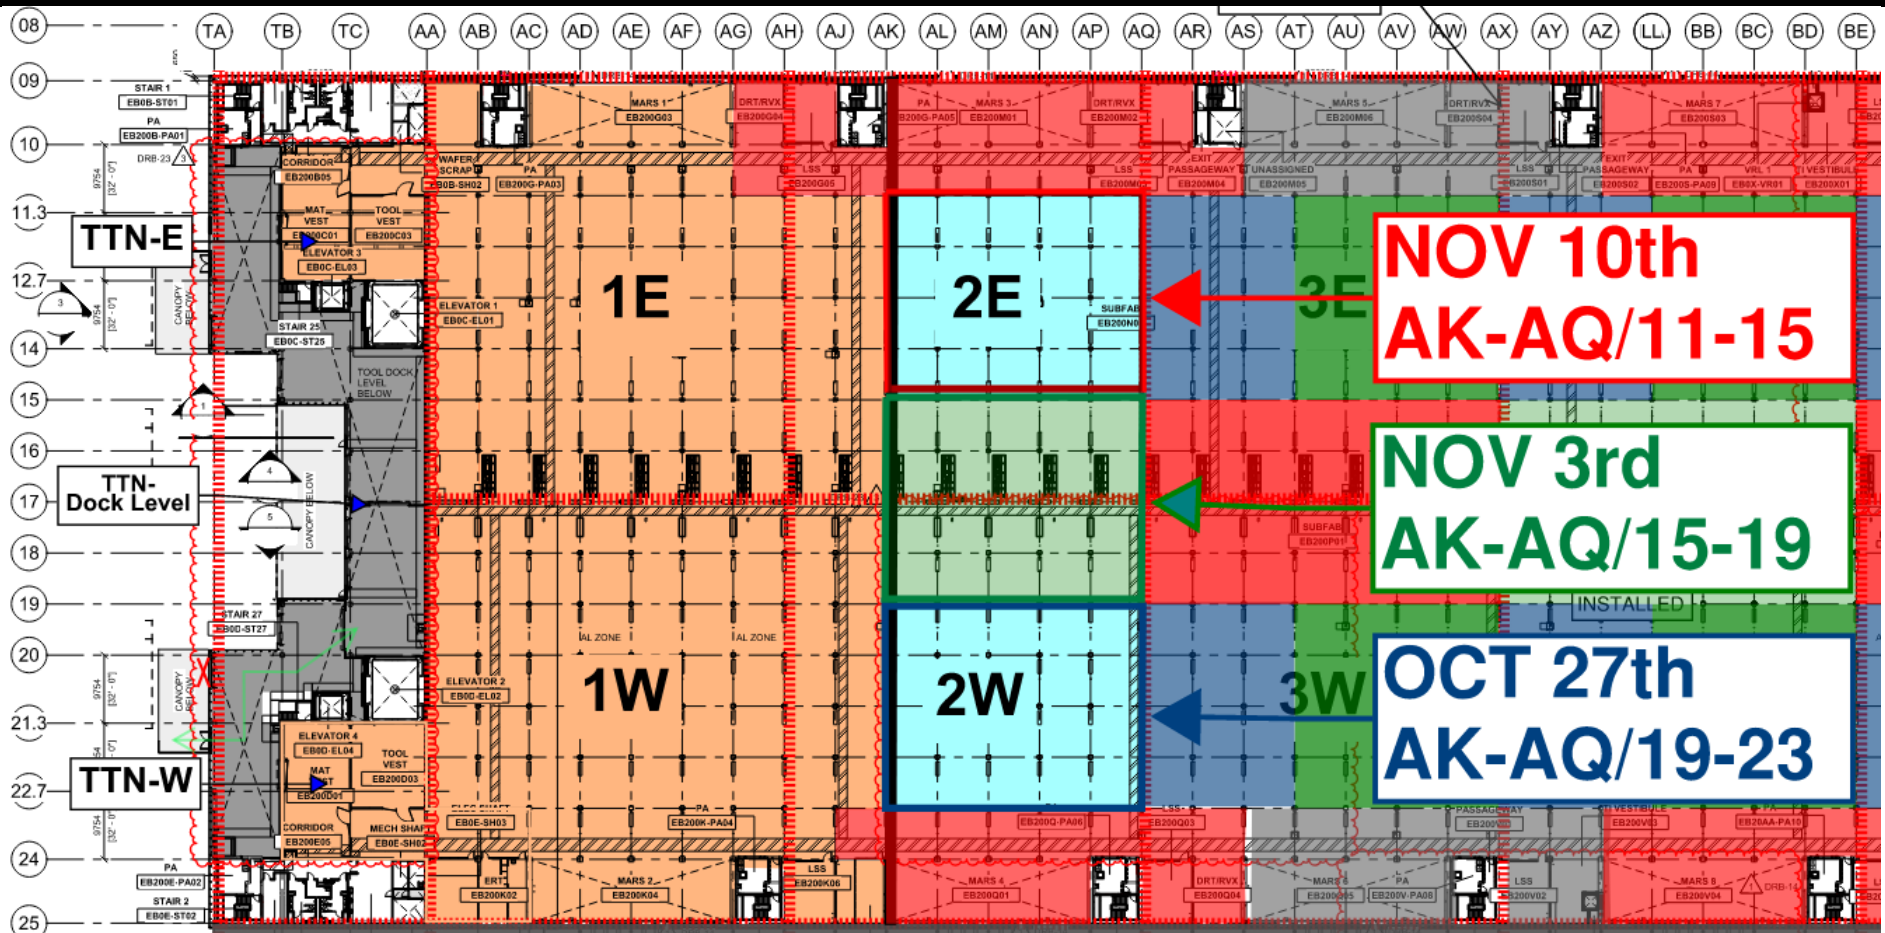

BCT Pressure Test

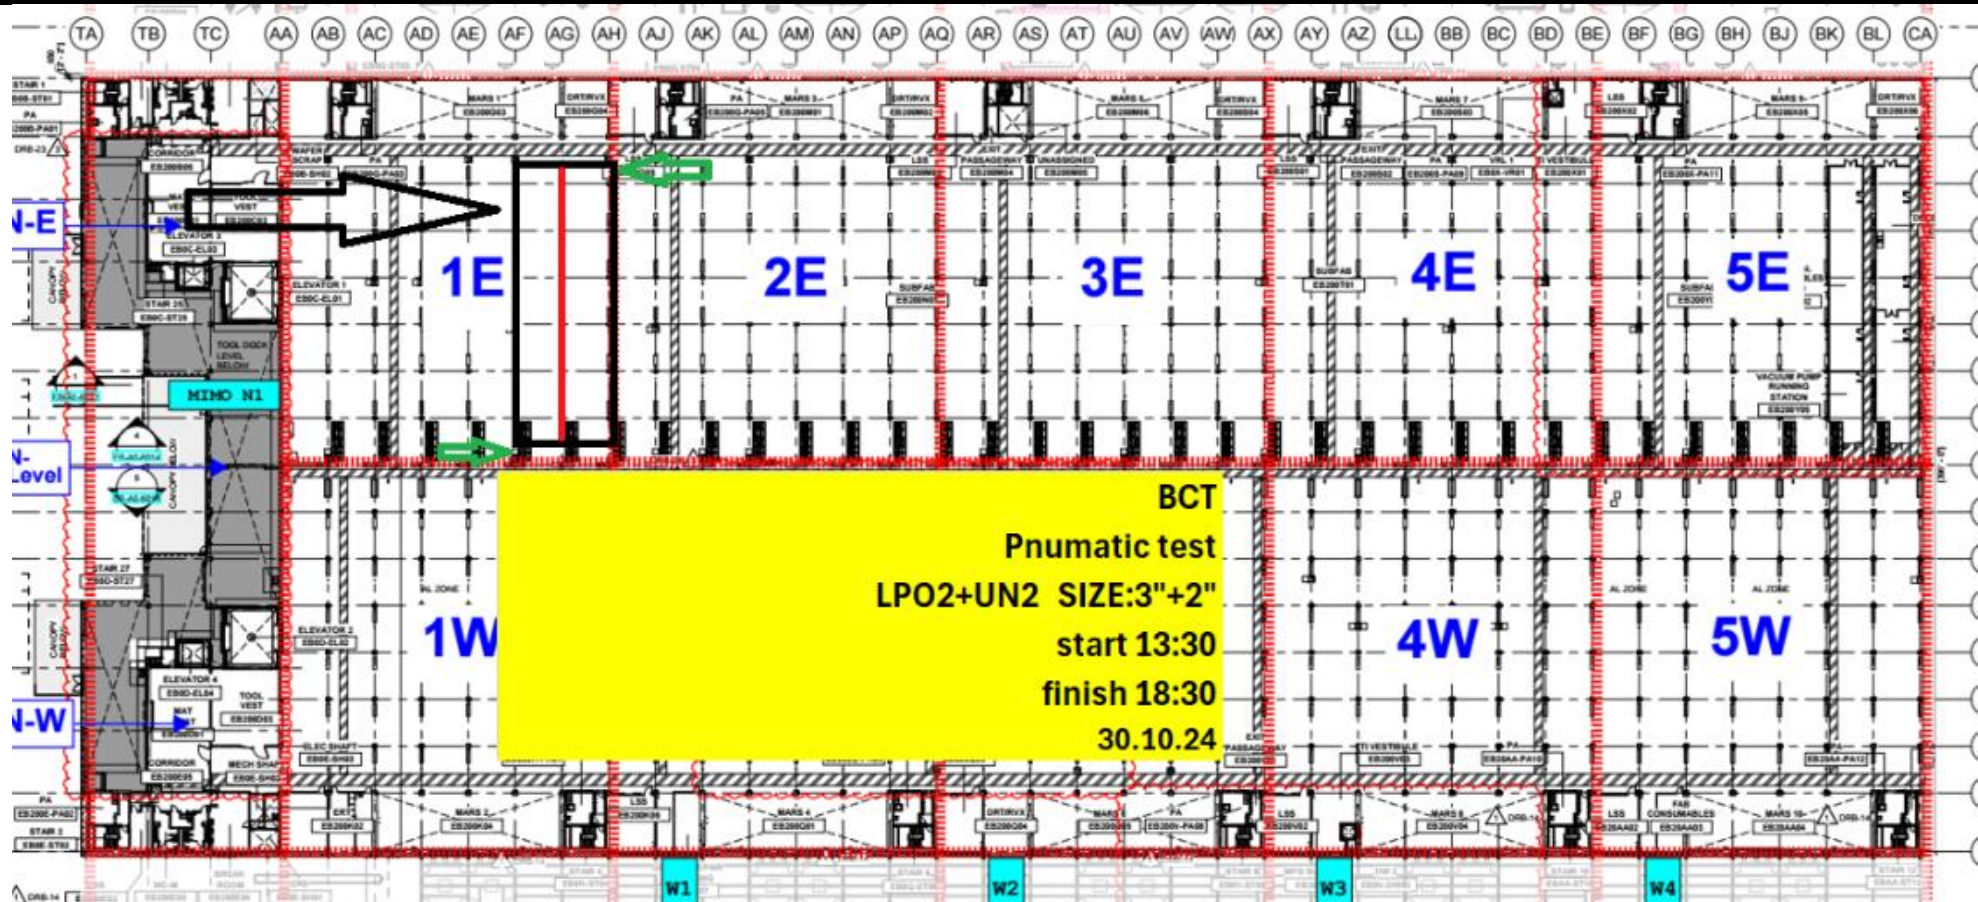

SUBFAB BUILDOUT MOD 2

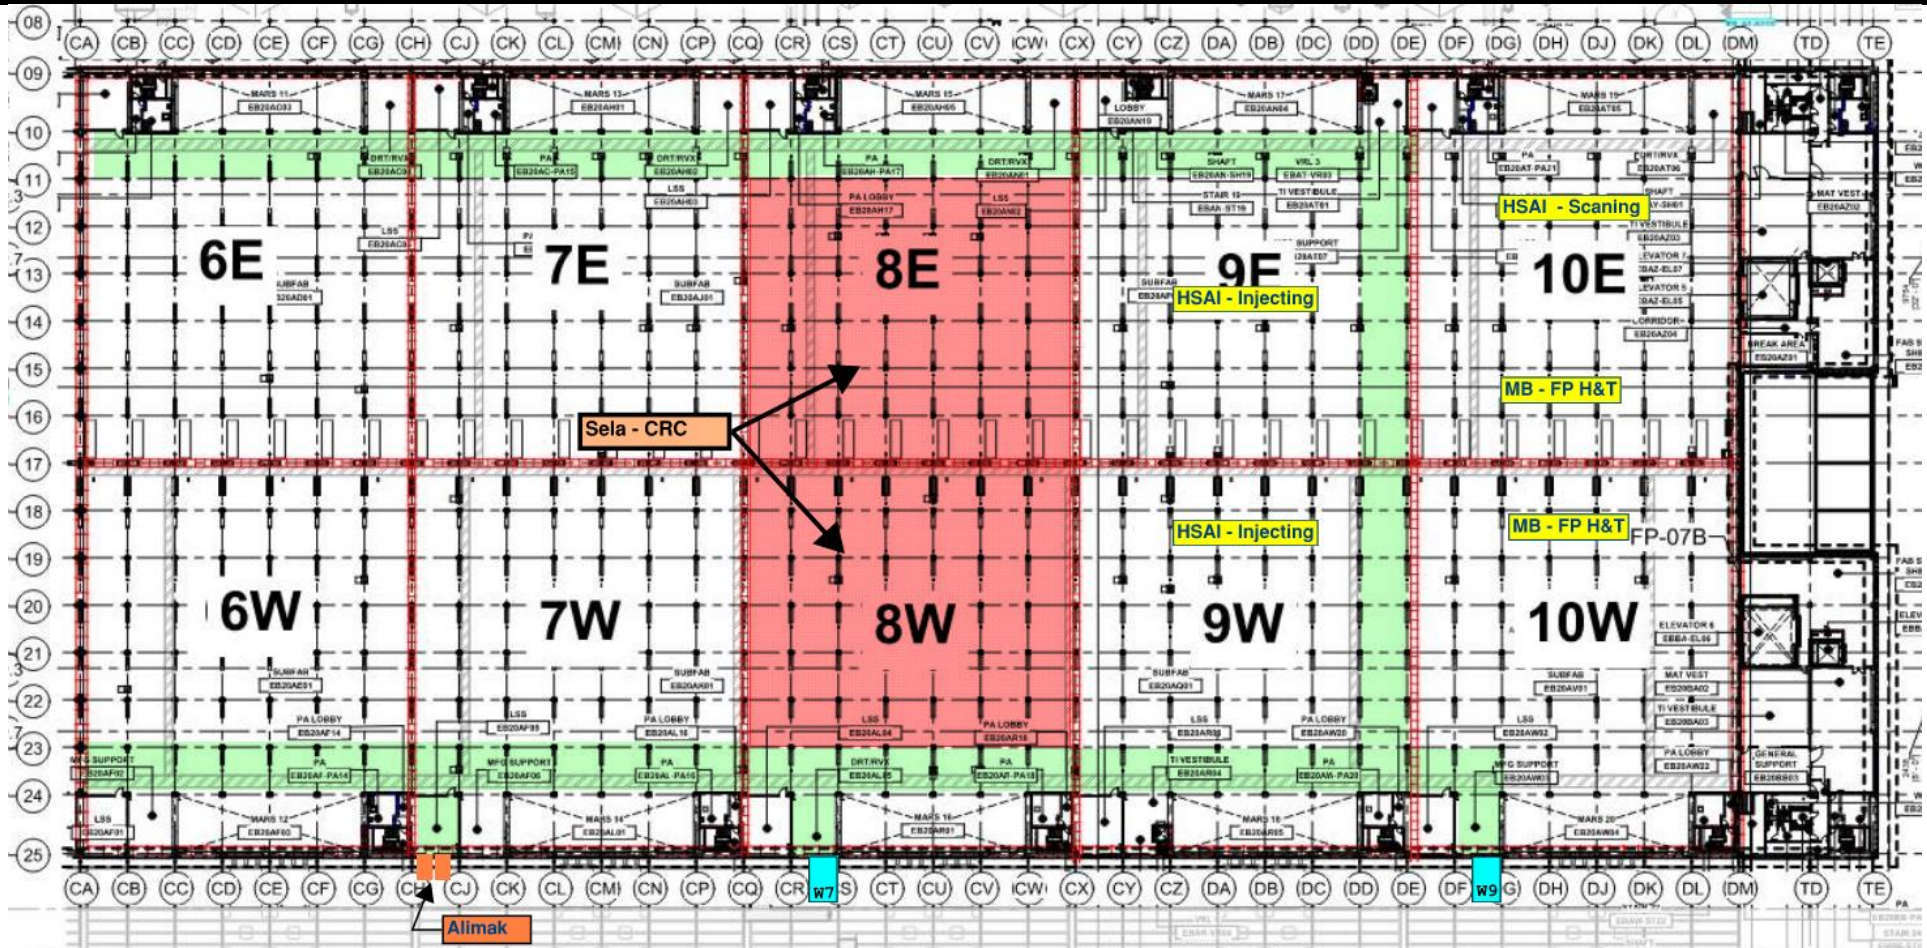

Tavas + Talent
solution
P1 cleaning 1E

ELRAM started
installing rhs's 9:10 L

BLOWDOWN IS COMING
NOV 14TH! 14 WD LEFT.

CR level:
Afcon - Cable trays, modules and stickers, 2E, 2W, 3E, 3W, 4E
MB - 1W/drops, 2E - 2W pipes and drops
Elram - 9-10, 24-25 columns/shaft walls. AA line column wraps
VW/JS - 17-18 line added beams + AS south stocker beams
Meptagon - I&C 2W
D&P - 5E blades install.
Tarr-esh - 5E blades, 1W-1E shaft walls
HYG - 5W Litho crane steel
T - Duct prep for test AA-AH east
Talad - 1W 4DA holes drilling, 1W cutting around steel, 17 line bracing
TMT - Safety net install

D&P 5RA
MISSING
BLADES

WW-TC
LINE HSS
FRAMING

RPC FRP
PAINT 5RA
BEAMS+BLADES

Sela-Ww 45 shotblast

D&P blades
install

Elram - AA line
columns+G1 wall
mock-up
Chemo- Hangers
install
SN - Beams layout

1E
All trades should do
training and use
correct equipment to
work in this area

CRC AA-AK/17-23

Sela: CRC Done

Talad - Cutting around lids

SELA CRC PREP

2

3

45

L
I
N
K

2E

3E

4E

5E

2W

3W

4W

5N

Talad-ongoing beam bracing across 17 line+aa/ab

Link
Pach-Taas - exhaust duct install and tie in
SIG - Mobile scaffold install
Afcon - Rack install
Newcotech - temp wall
Afcon - cable tray & racks install

Staircase # 4
Exit to cr level
blocked

דרישות חובה לכל קבלני החדר הנקי

אין להכניס אוכל ושתייה מלבד מים

- פחי אשפה מלוכלכים יש לנקות את החלק הפנימי והחיצוני של הפח.
- פוליגלים/ משטחי עבודה קרועים באזורי האחסון.
- כלי שינוע וציוד מלוכלכים יש לבצע נקיון יסודי של החיתול ושל הבמה באמצעות מגבונים.
- בכל אזורי האחסון והעבודה של כל קבלני החדר הנקי.

Mandatory requirements for all cr contractors

No food or liquids other than water.

Dirty trash cans Clean the inside and outside of the trash cans.


- Polygals/torn work surfaces in the storage areas.
- Dirty transport tools and equipment.

All diapers and booms must be thoroughly cleaned with wipes.

all storage and work areas of all clean room's areas.



HOFFMAN CONSTRUCTION COMPANY

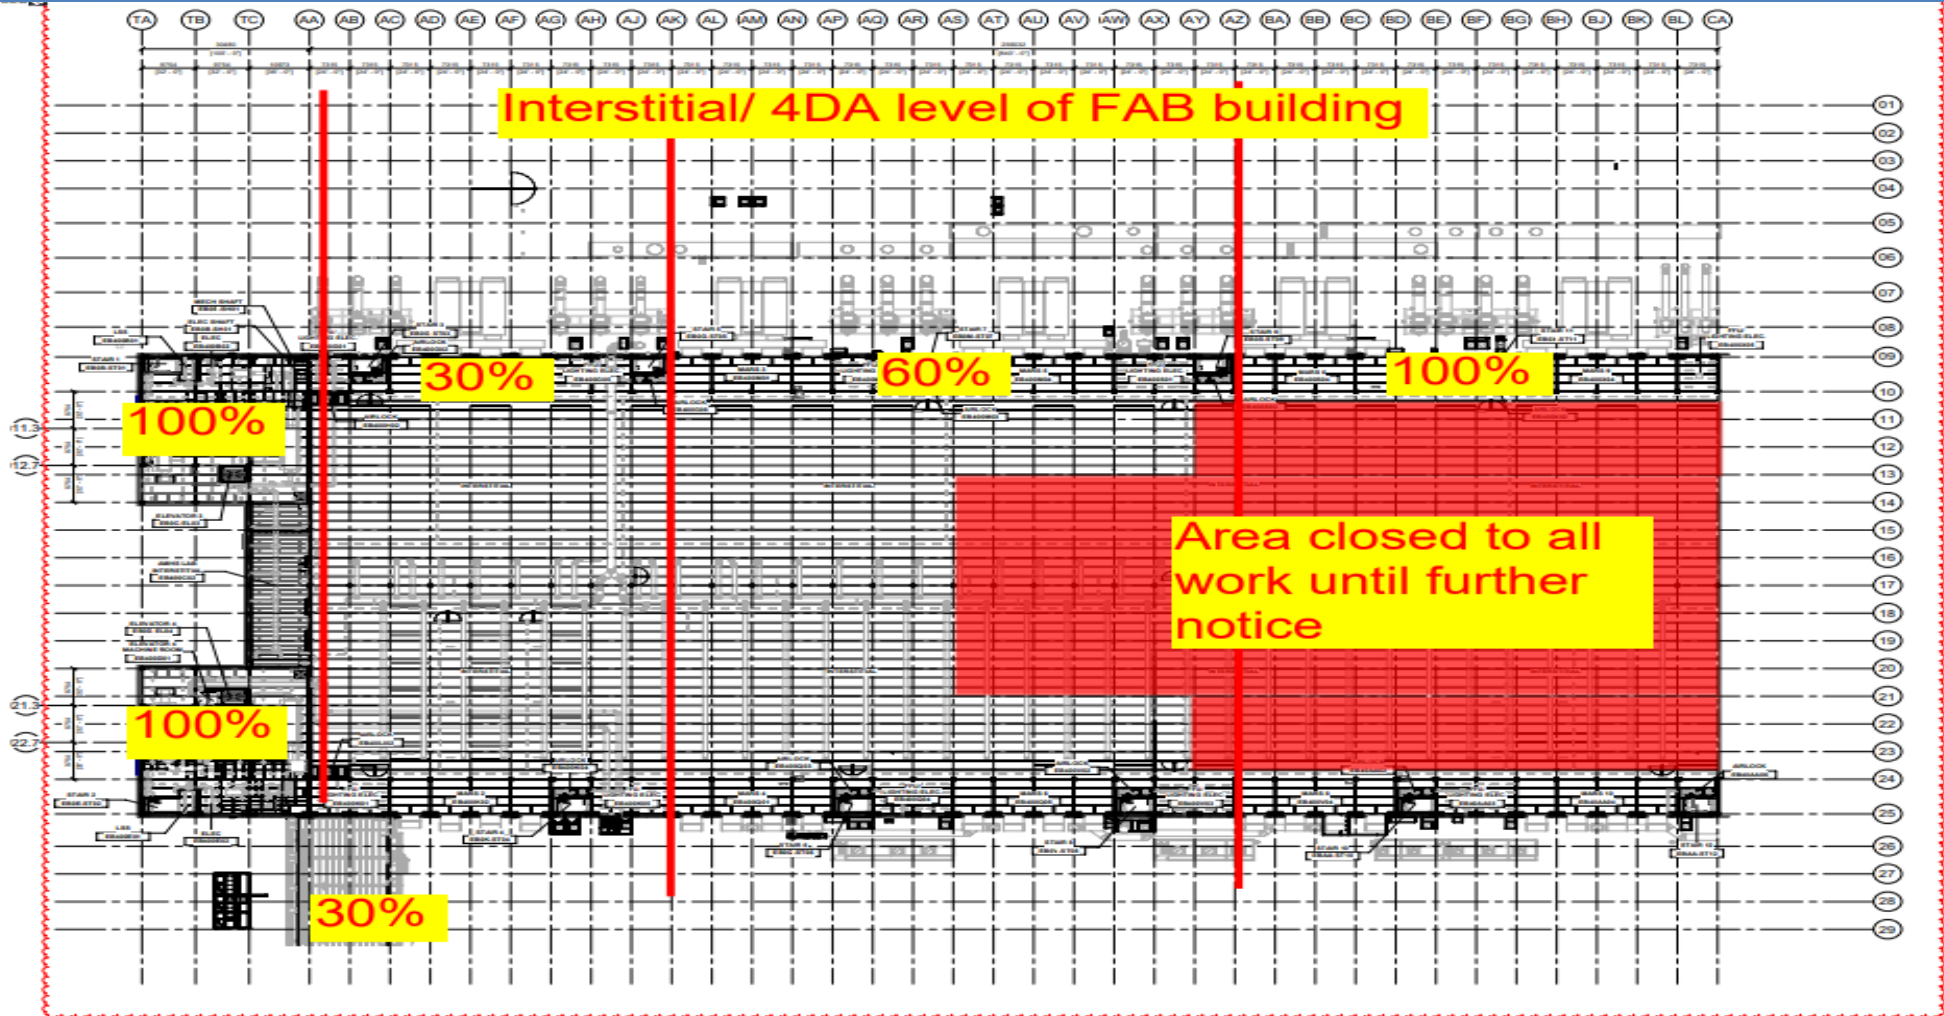

Clean Room Wall Of Shame

ELRAM #1




ELRAM #2



Clean Room Wall Of Shame



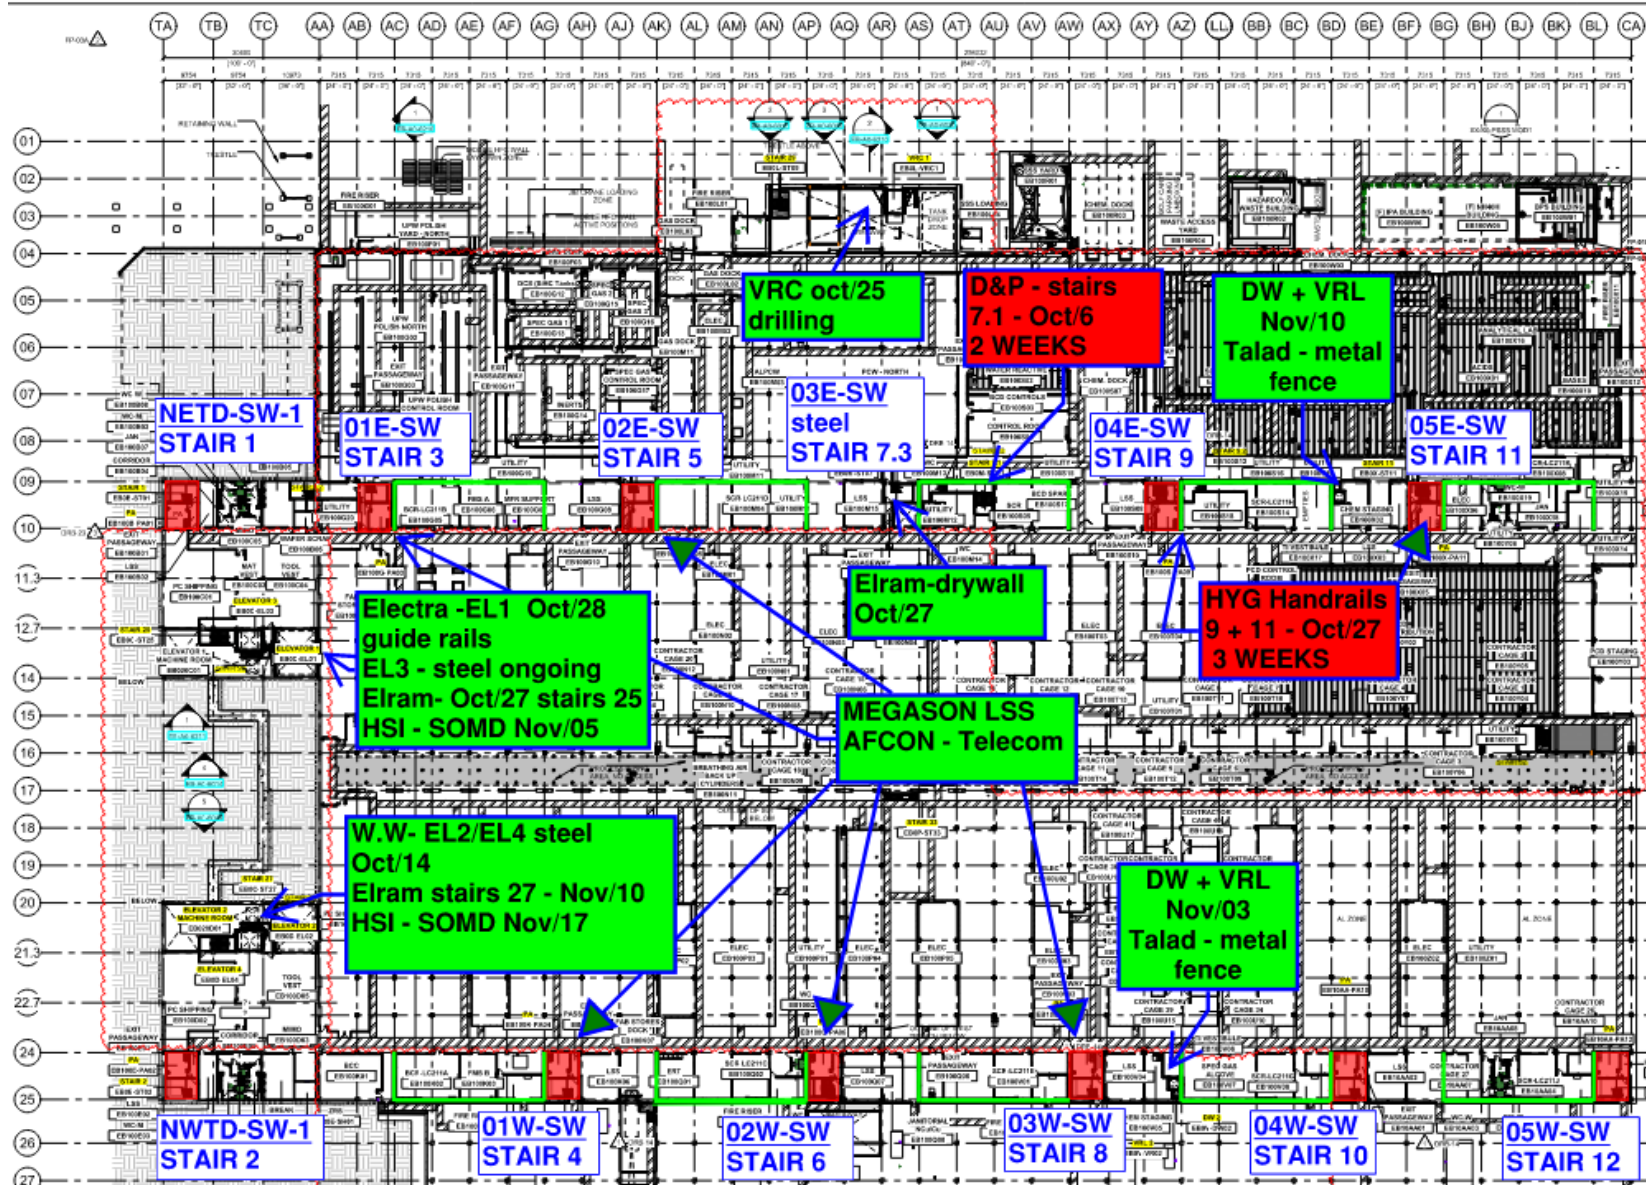

	Siding - East FAB - PSSS
--	--------------------------


DEMO


Siding - West FAB - JYG


BLOWDOWN 30%

[illegible]

SUT - West		
AP	AG	AR
5	5	
5	5	
100%	100%	
1	1	
1	1	
1	1	
1	1	
1	1	
1	1	
1	1	
ED-00A-SUB-UTILITY = 132,797		

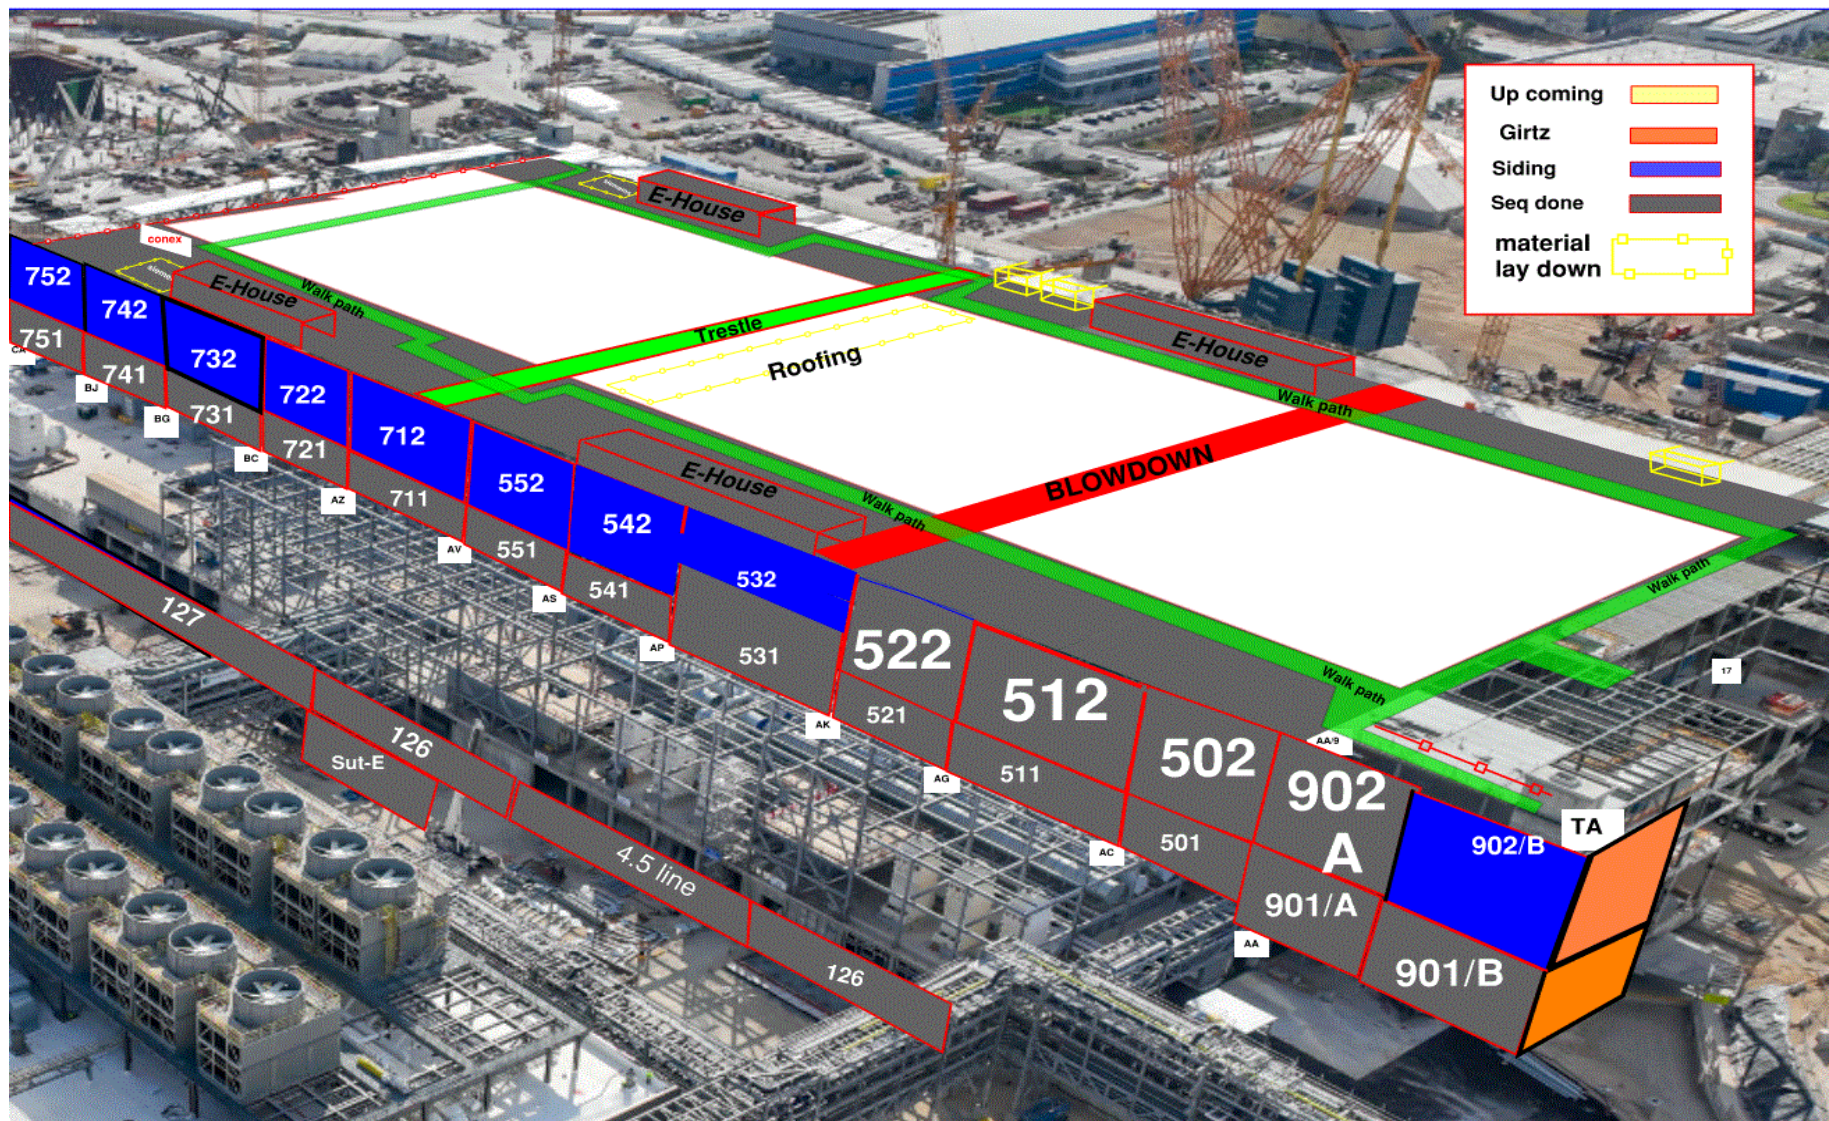


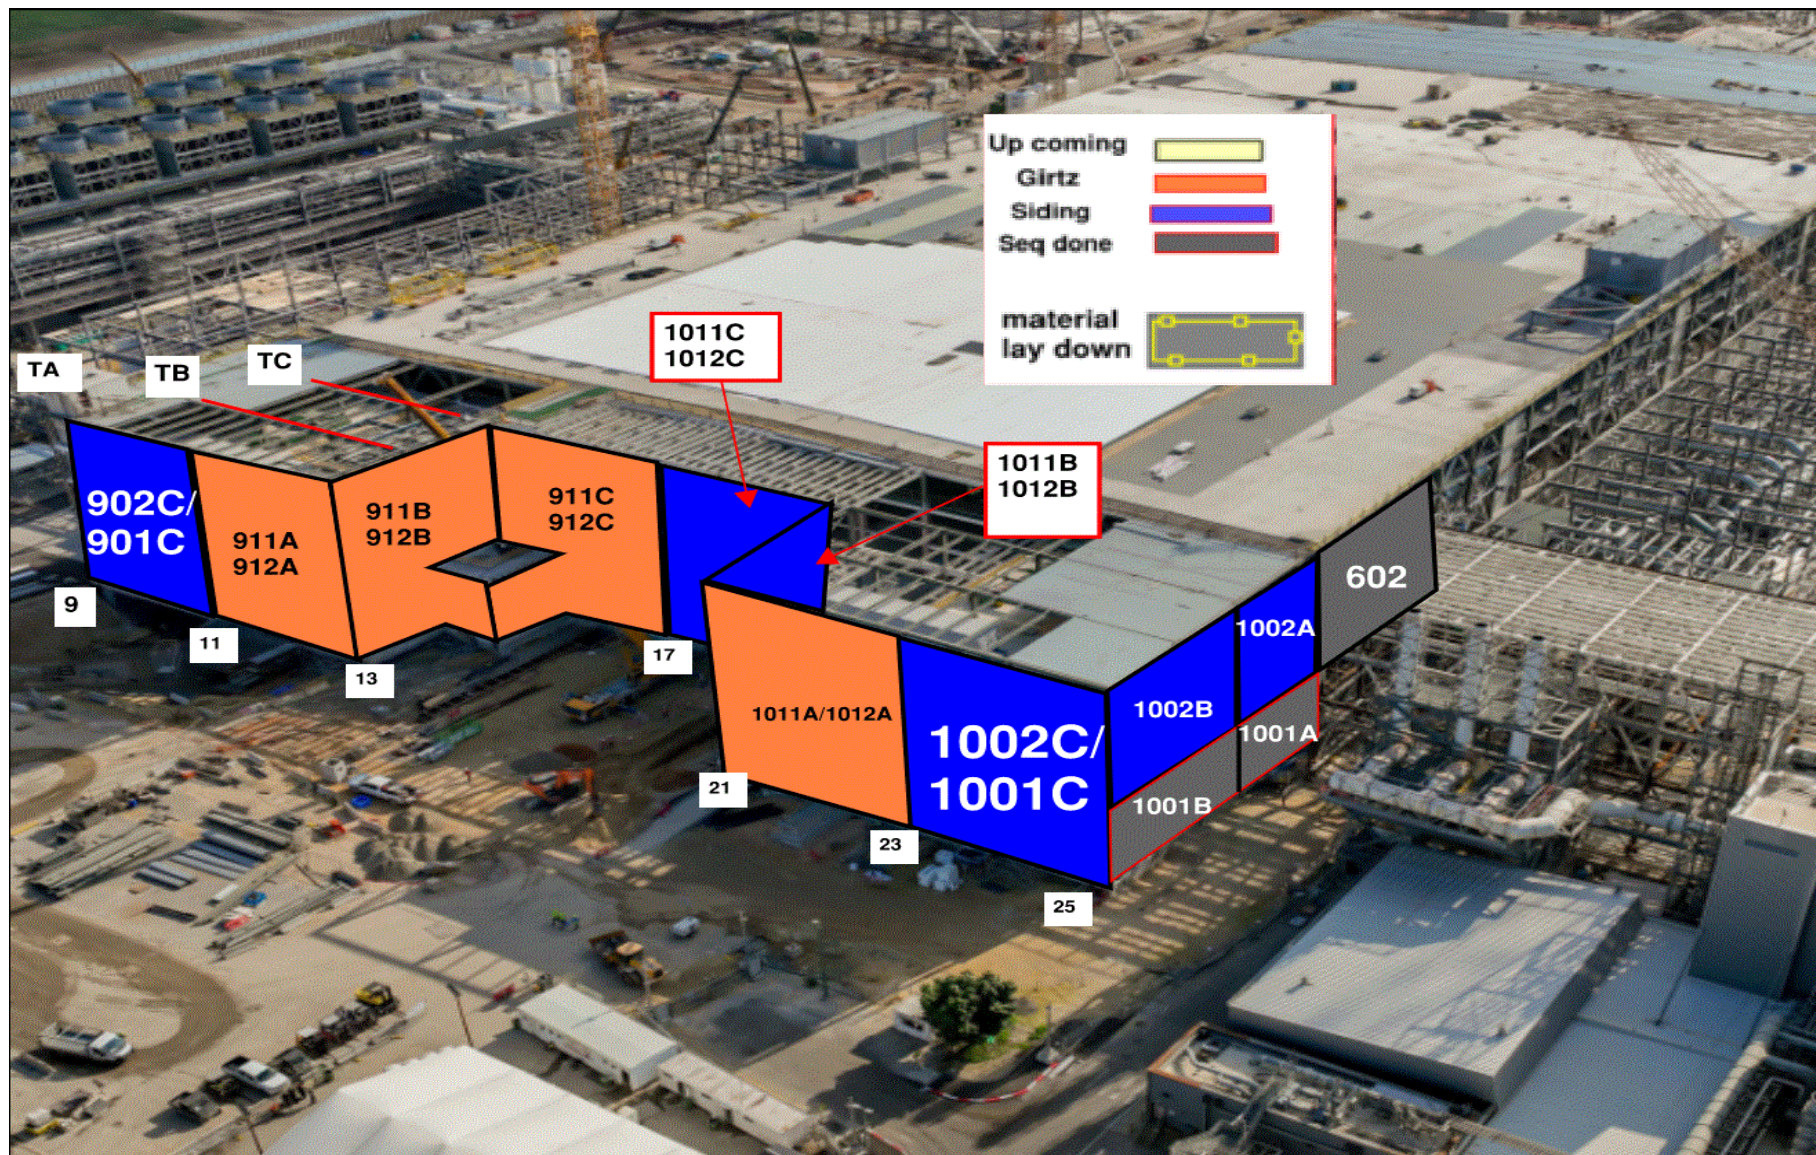

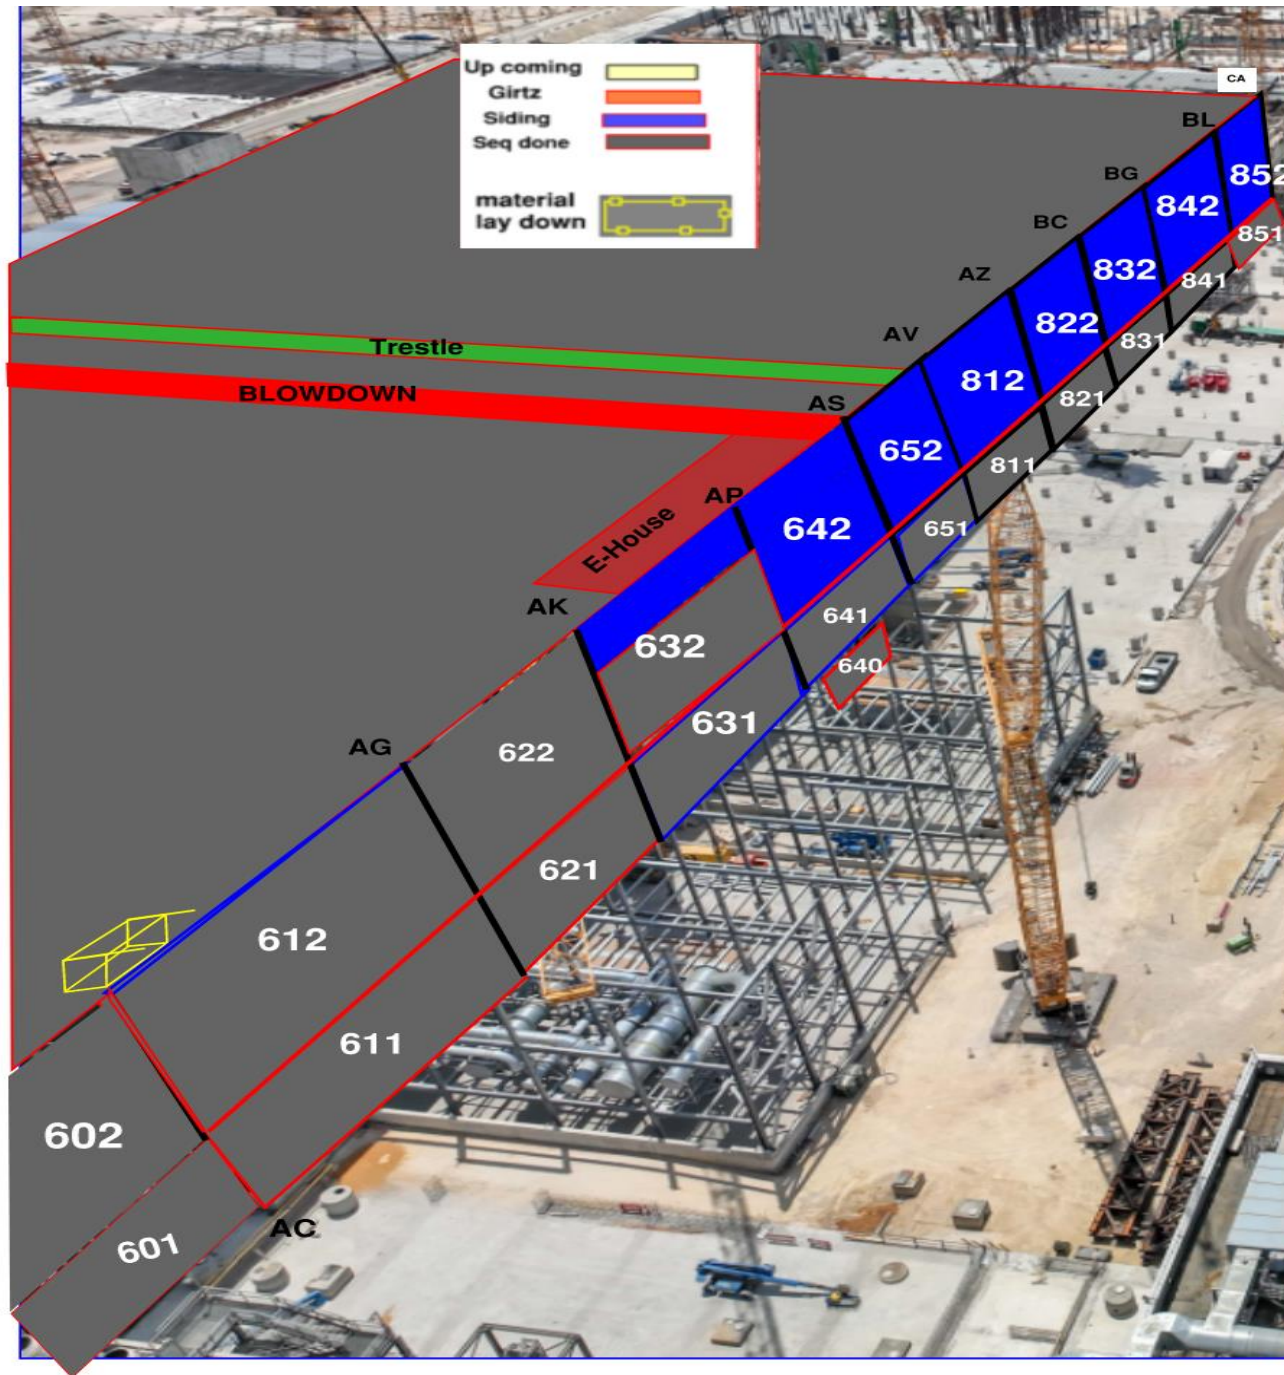


PSSS.1

Utility Level
1YA

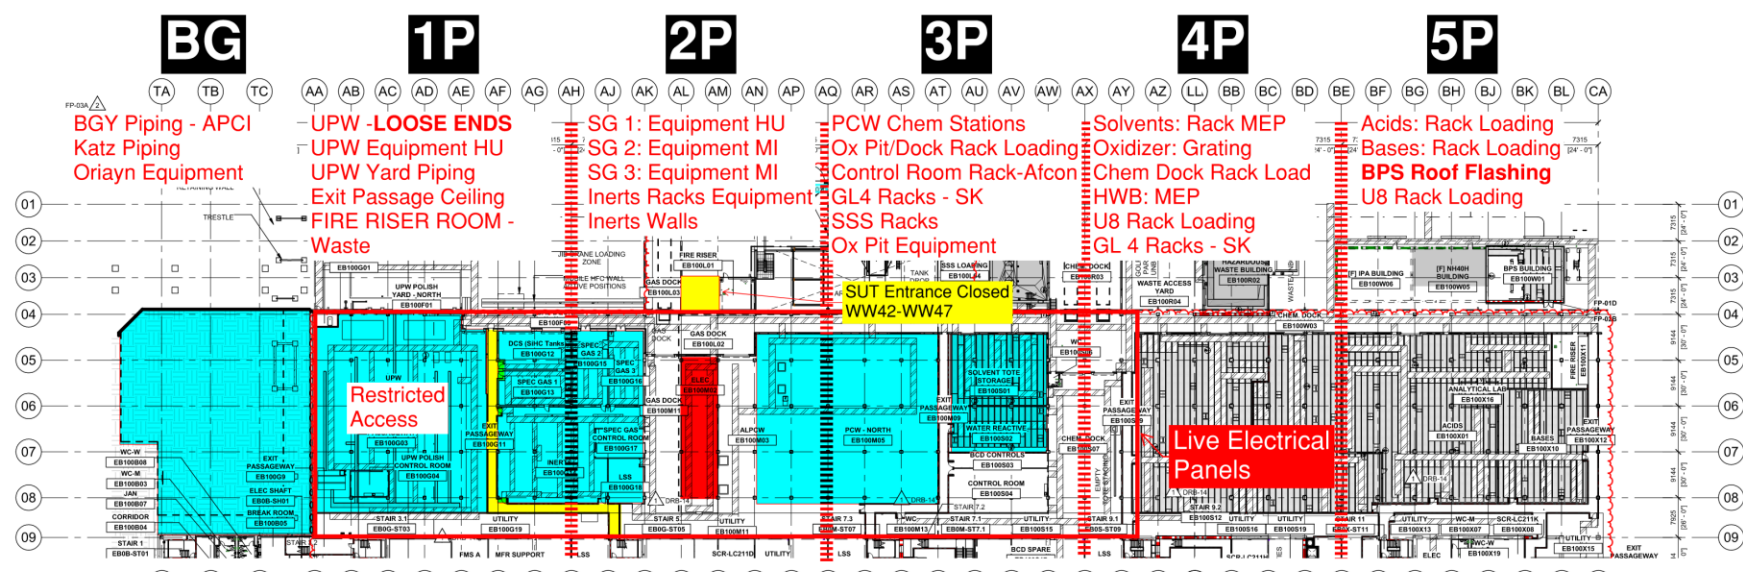


PSSS Roof
2SA

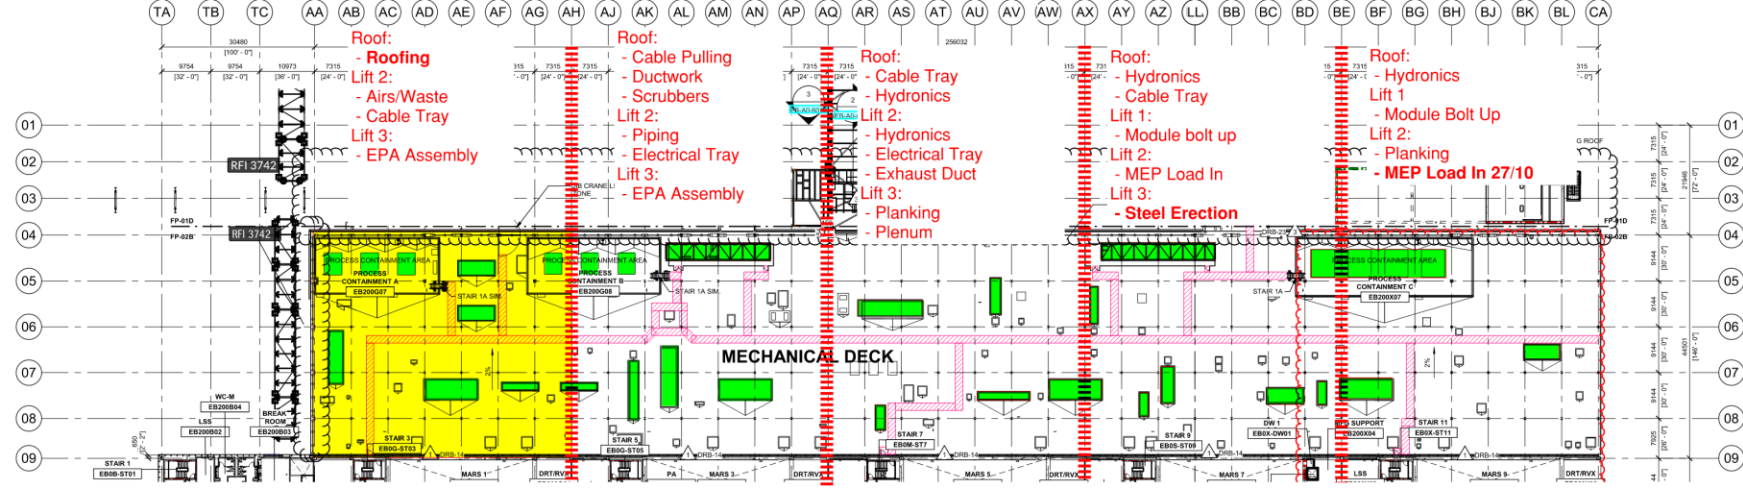


PSSS.2


Utility Level 1YA

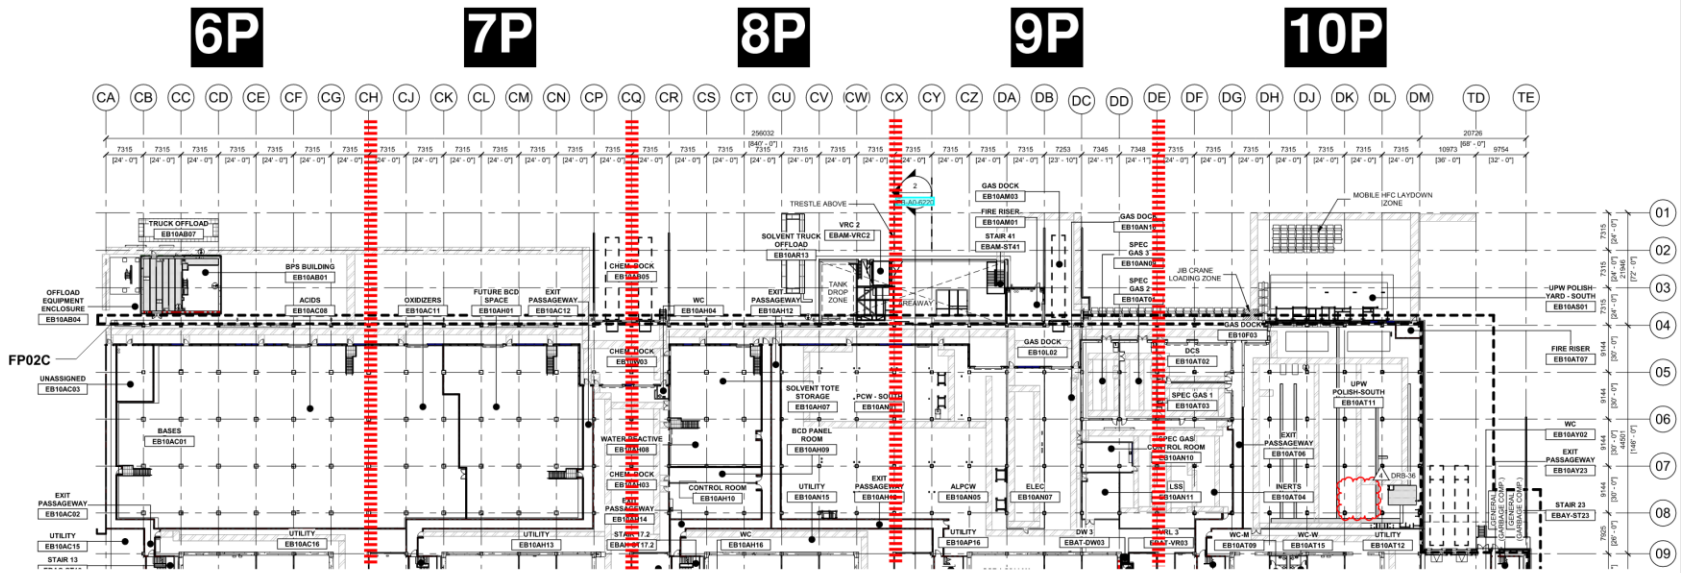

PSSS Roof 2SA

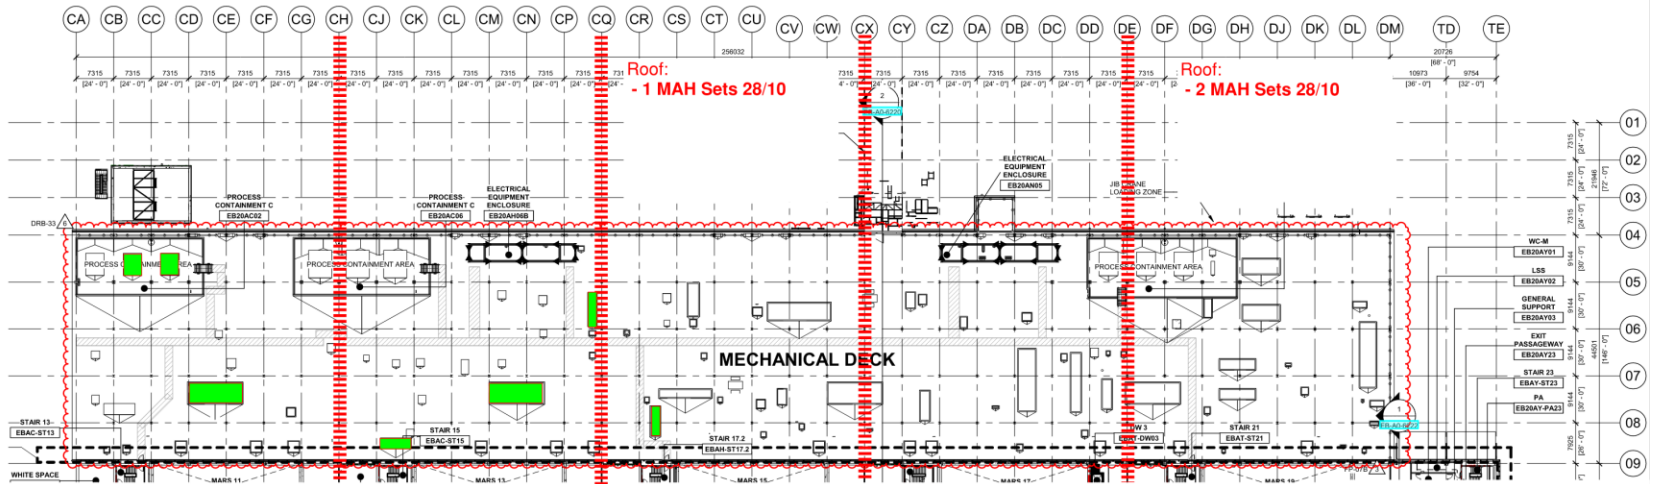


DMA G
MOVE SOUTH
31/10 @
13:00

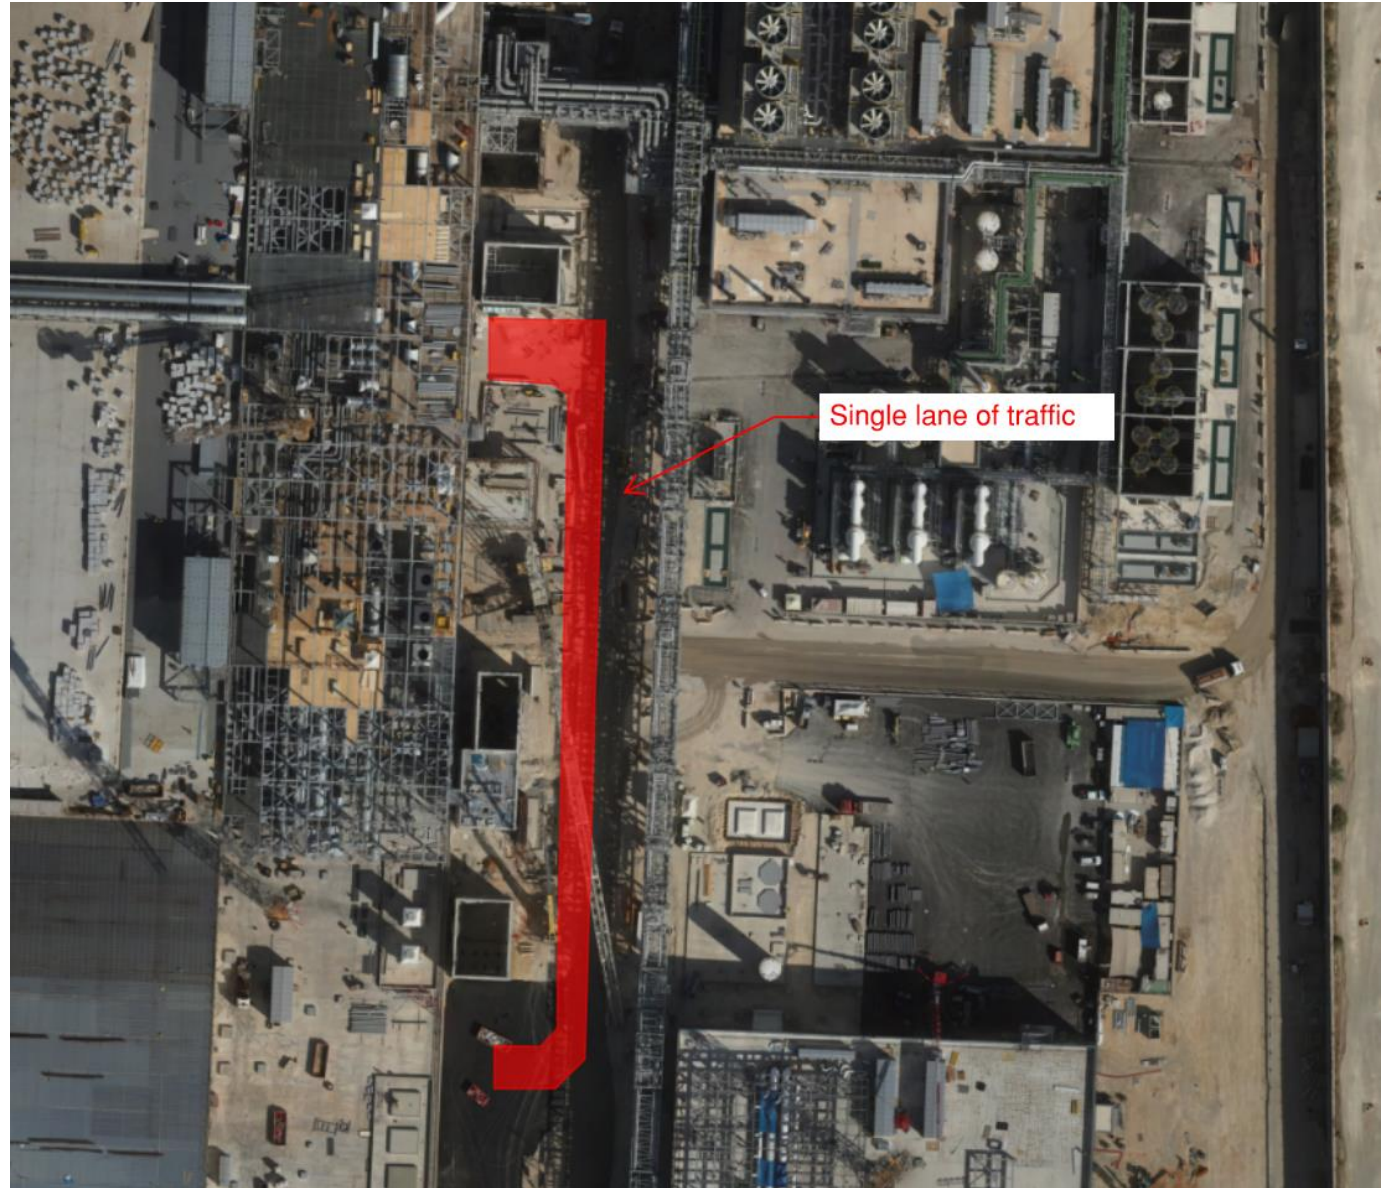


DMA G MOVE
SOUTH
31/10 @ 17:00
thru
01/11 @ 12:00





WJG 01J, 02J LIFT 2 & 3

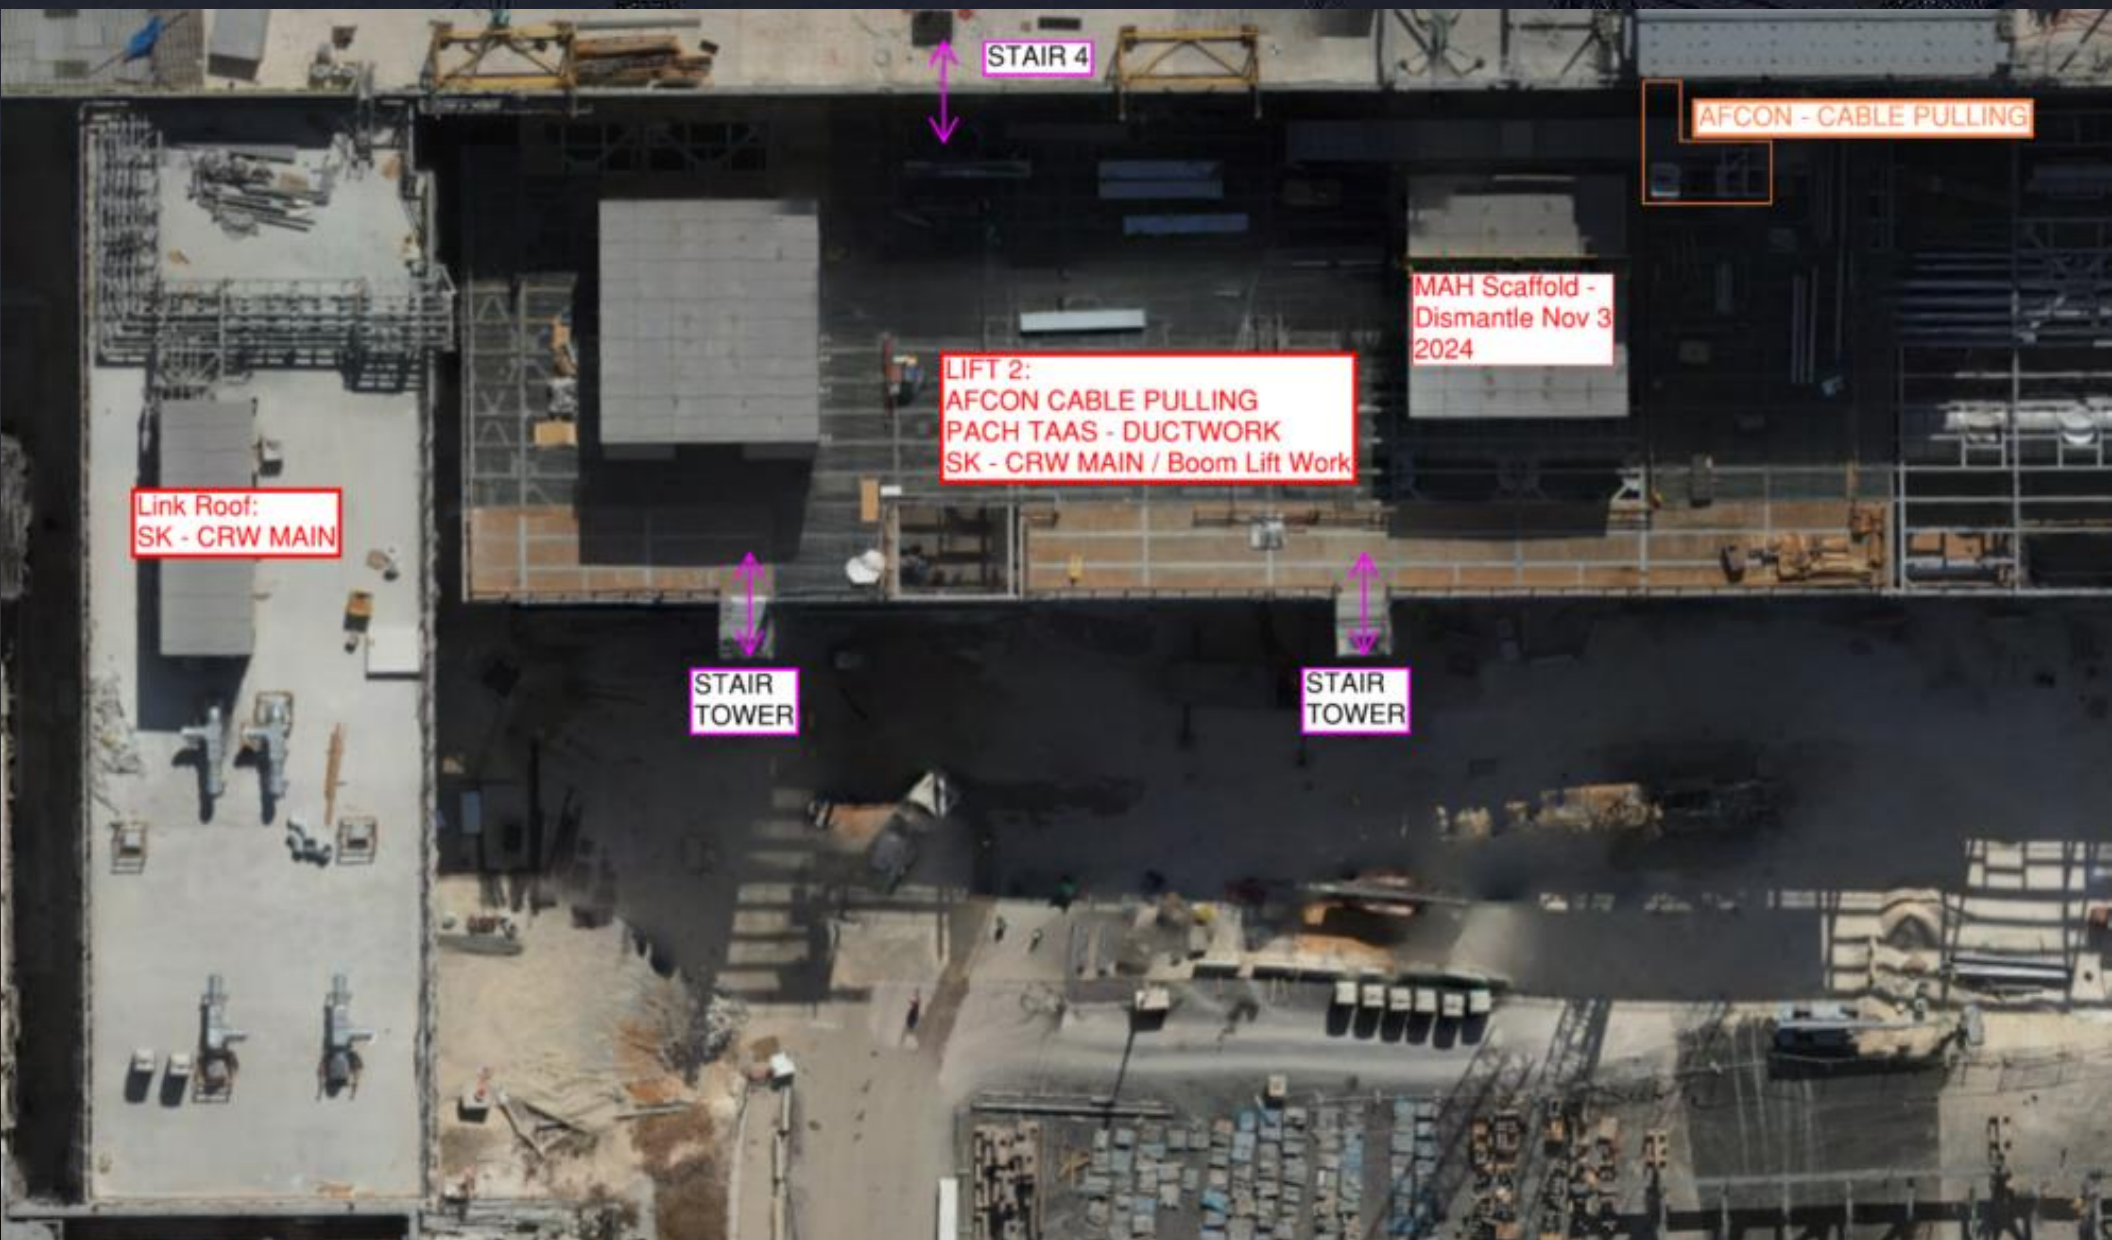




WJG 03J, 04J, 05J LIFT 2 & 3







Walk Path Reroute WW43 & WW44

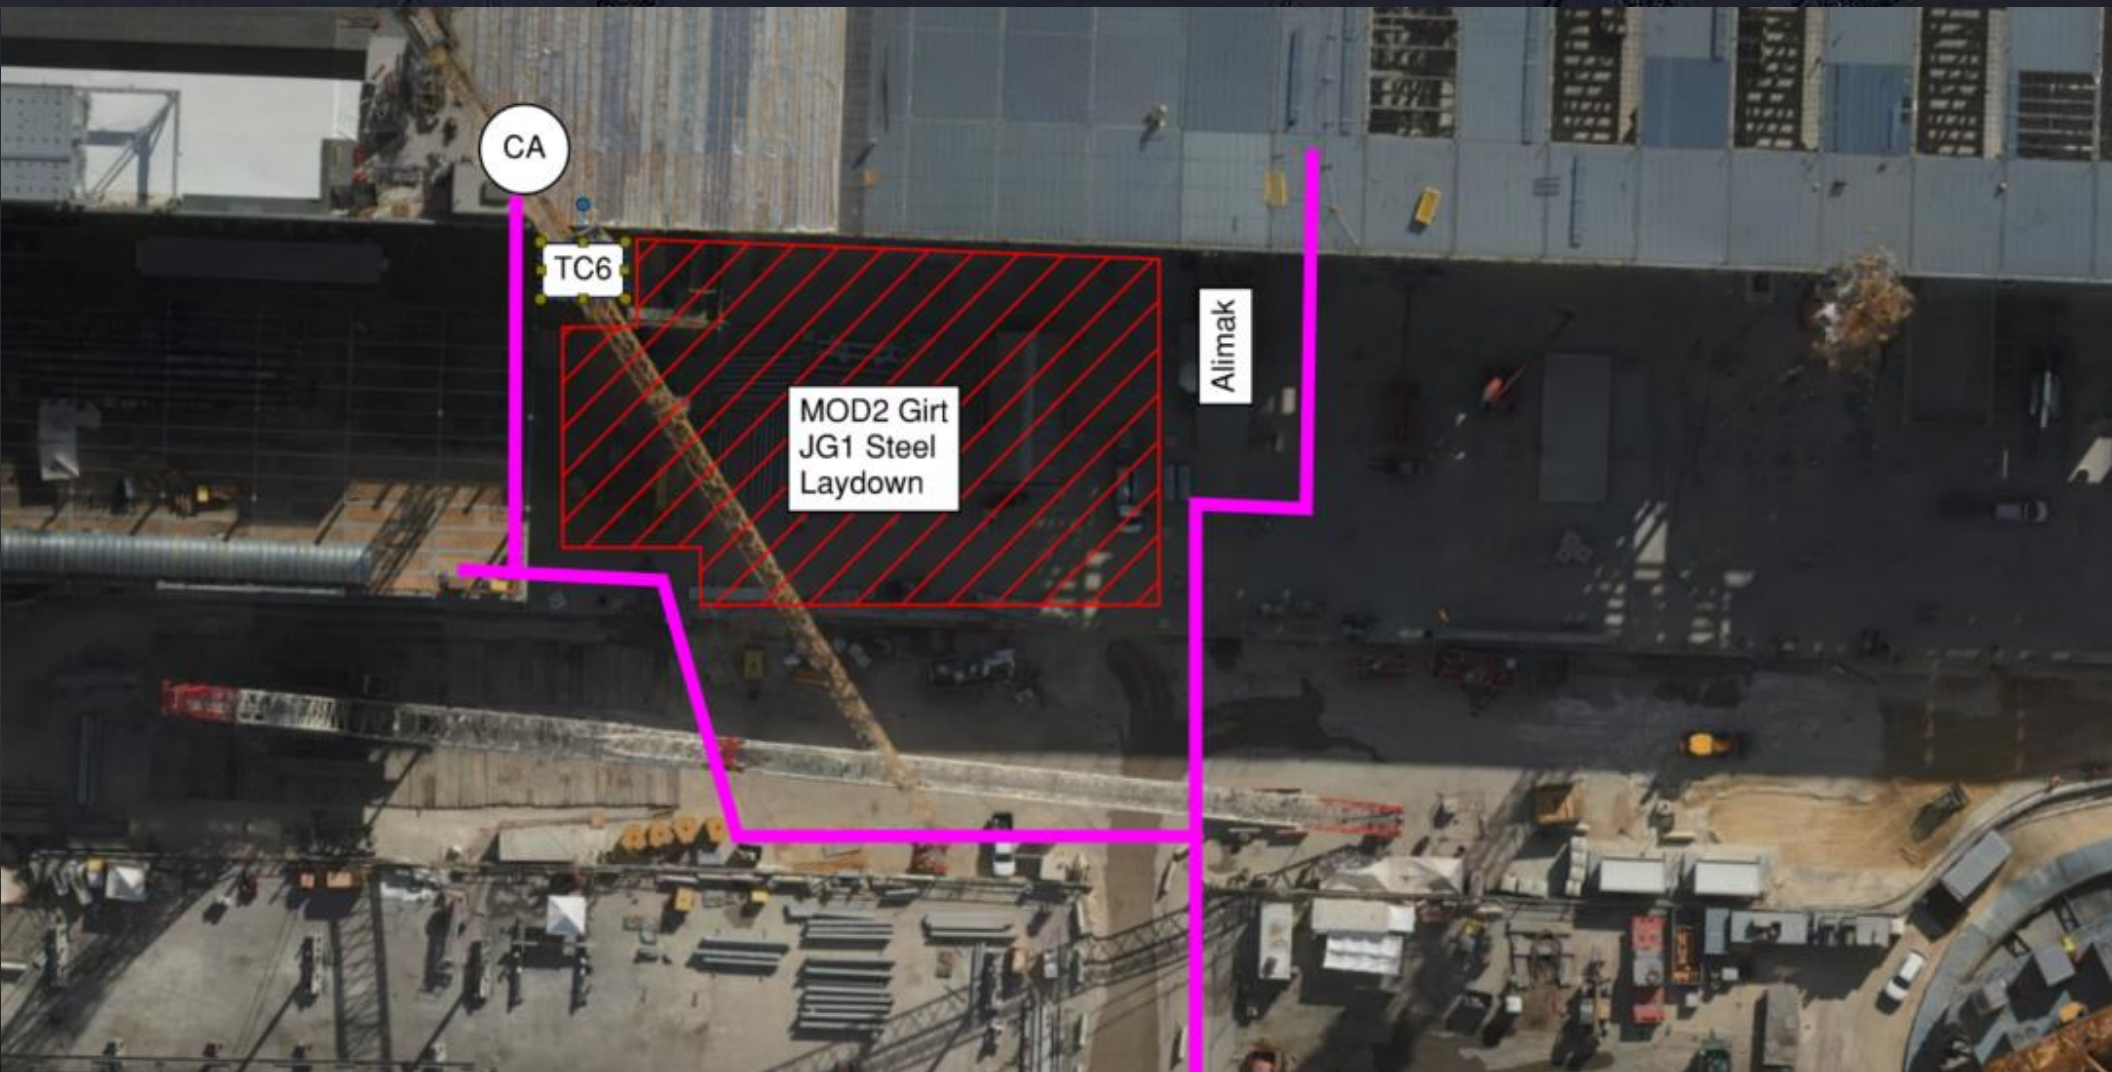

AH104-22-00 Set – 29/10

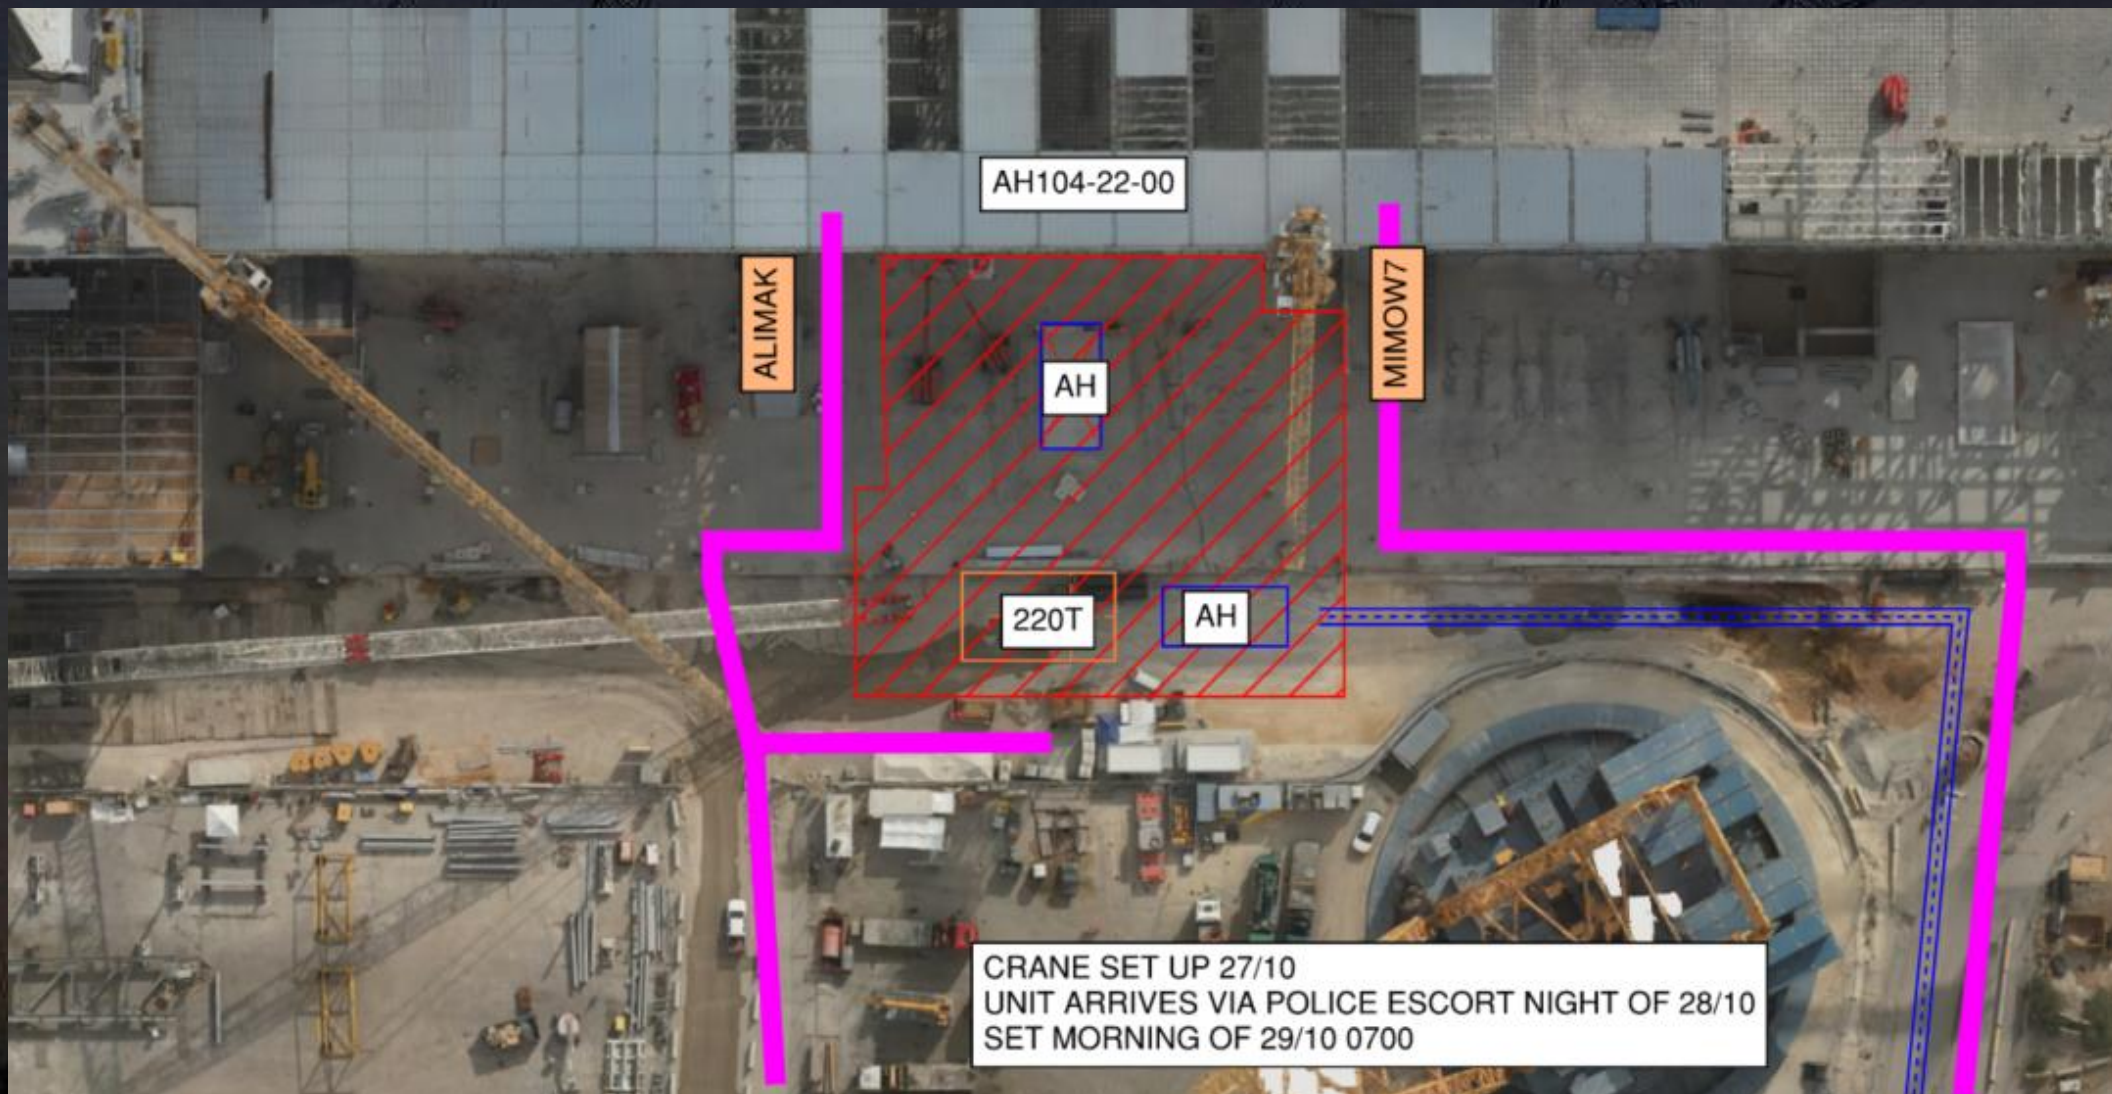


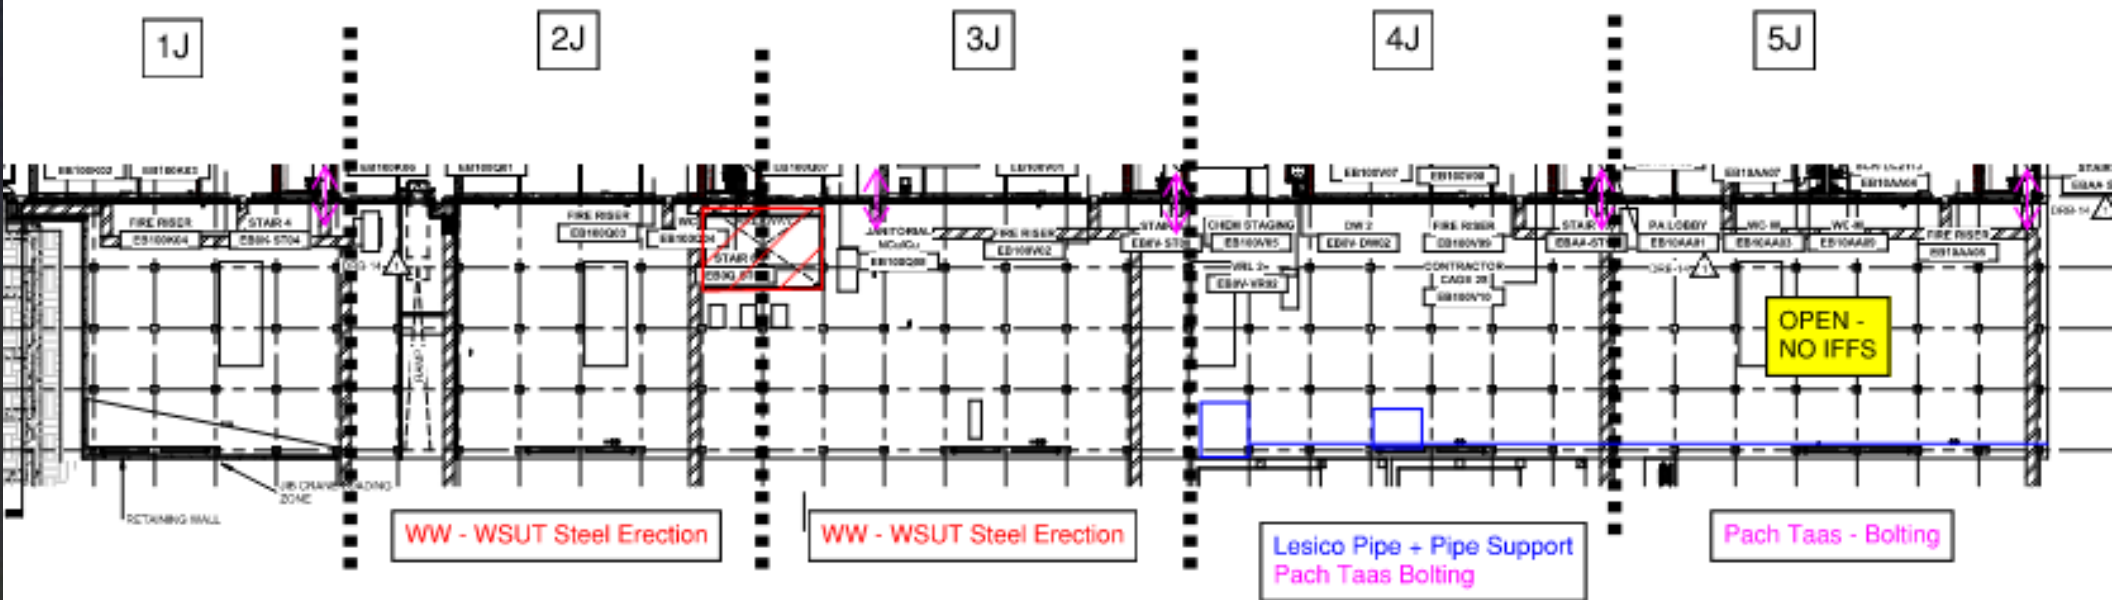



NDT TESTING

WEDNESDAY 30/10/2024: 2000 - 0500

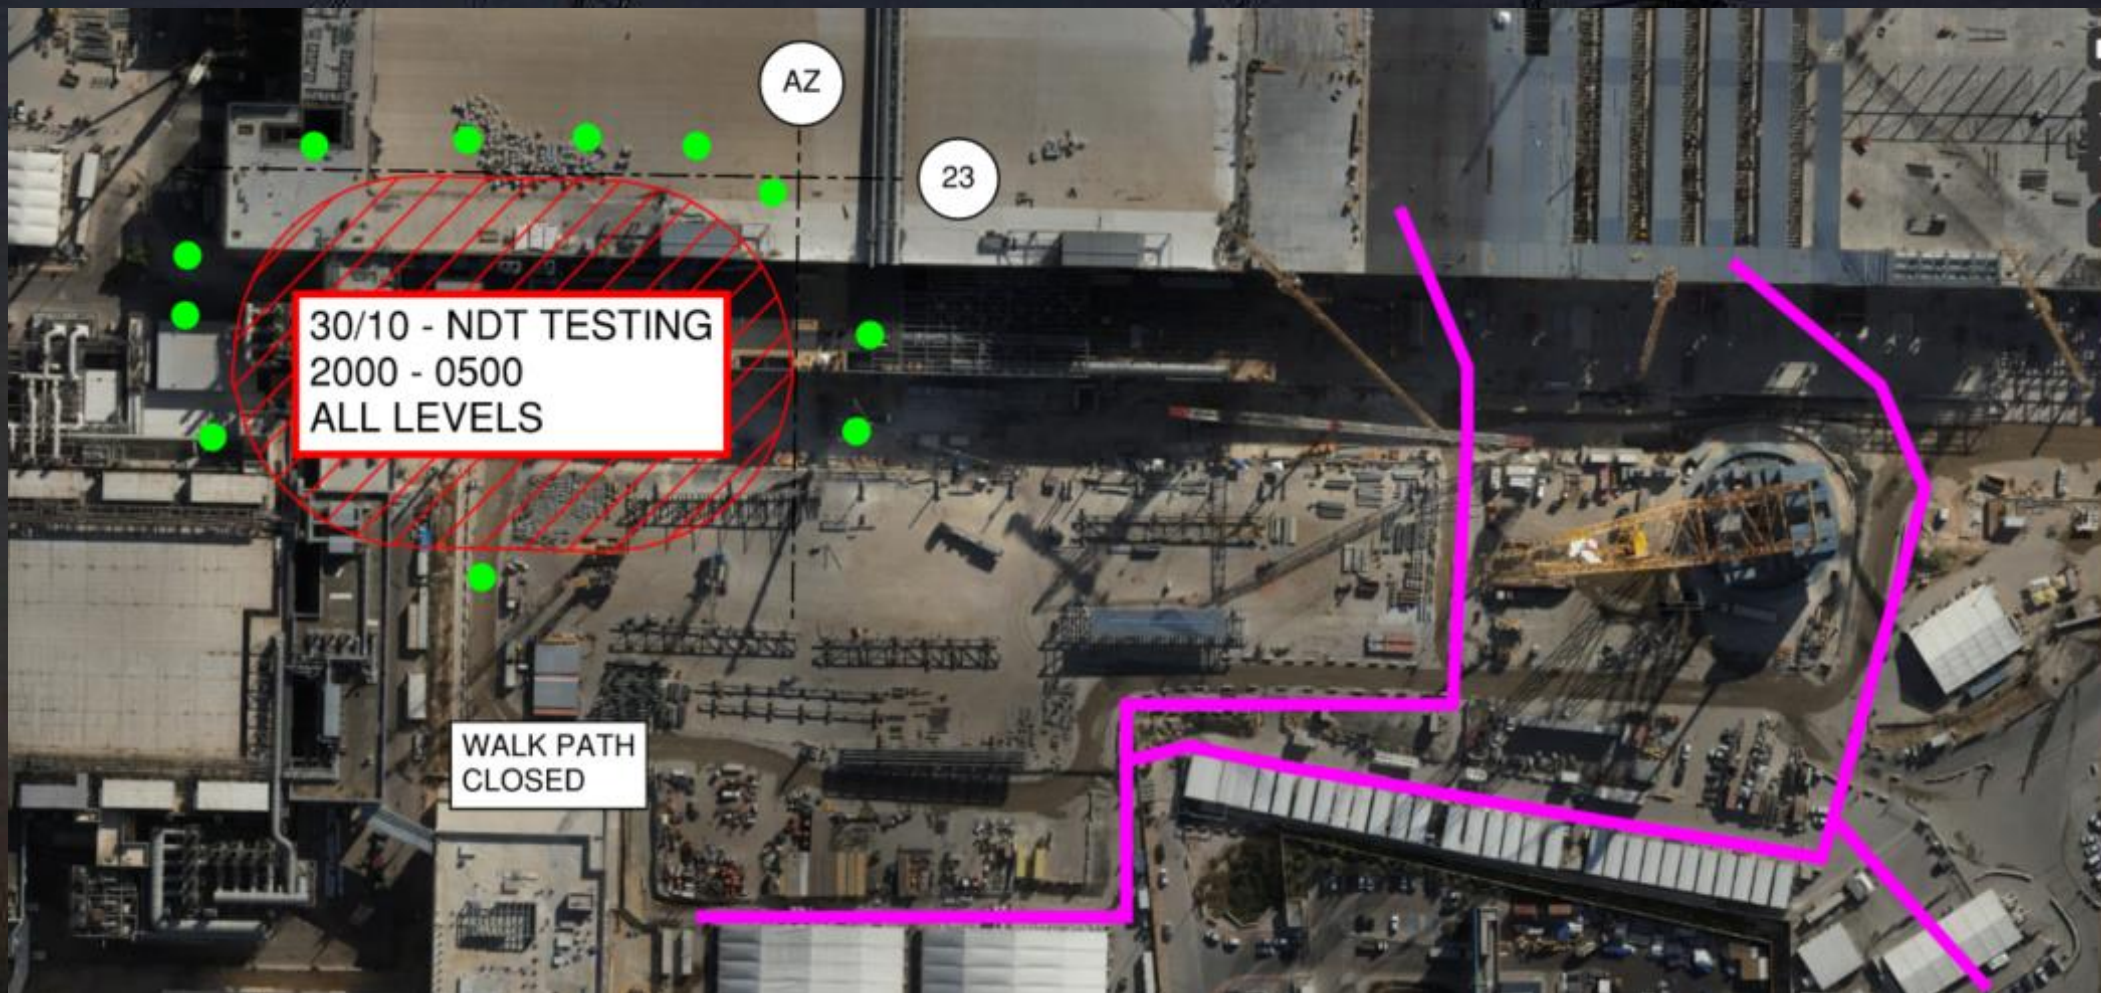



NDT TESTING THURSDAY 31/10/2024: 2000 - 0500






CUB 1


CUB 1 COORDINATION MAP

UPDATED

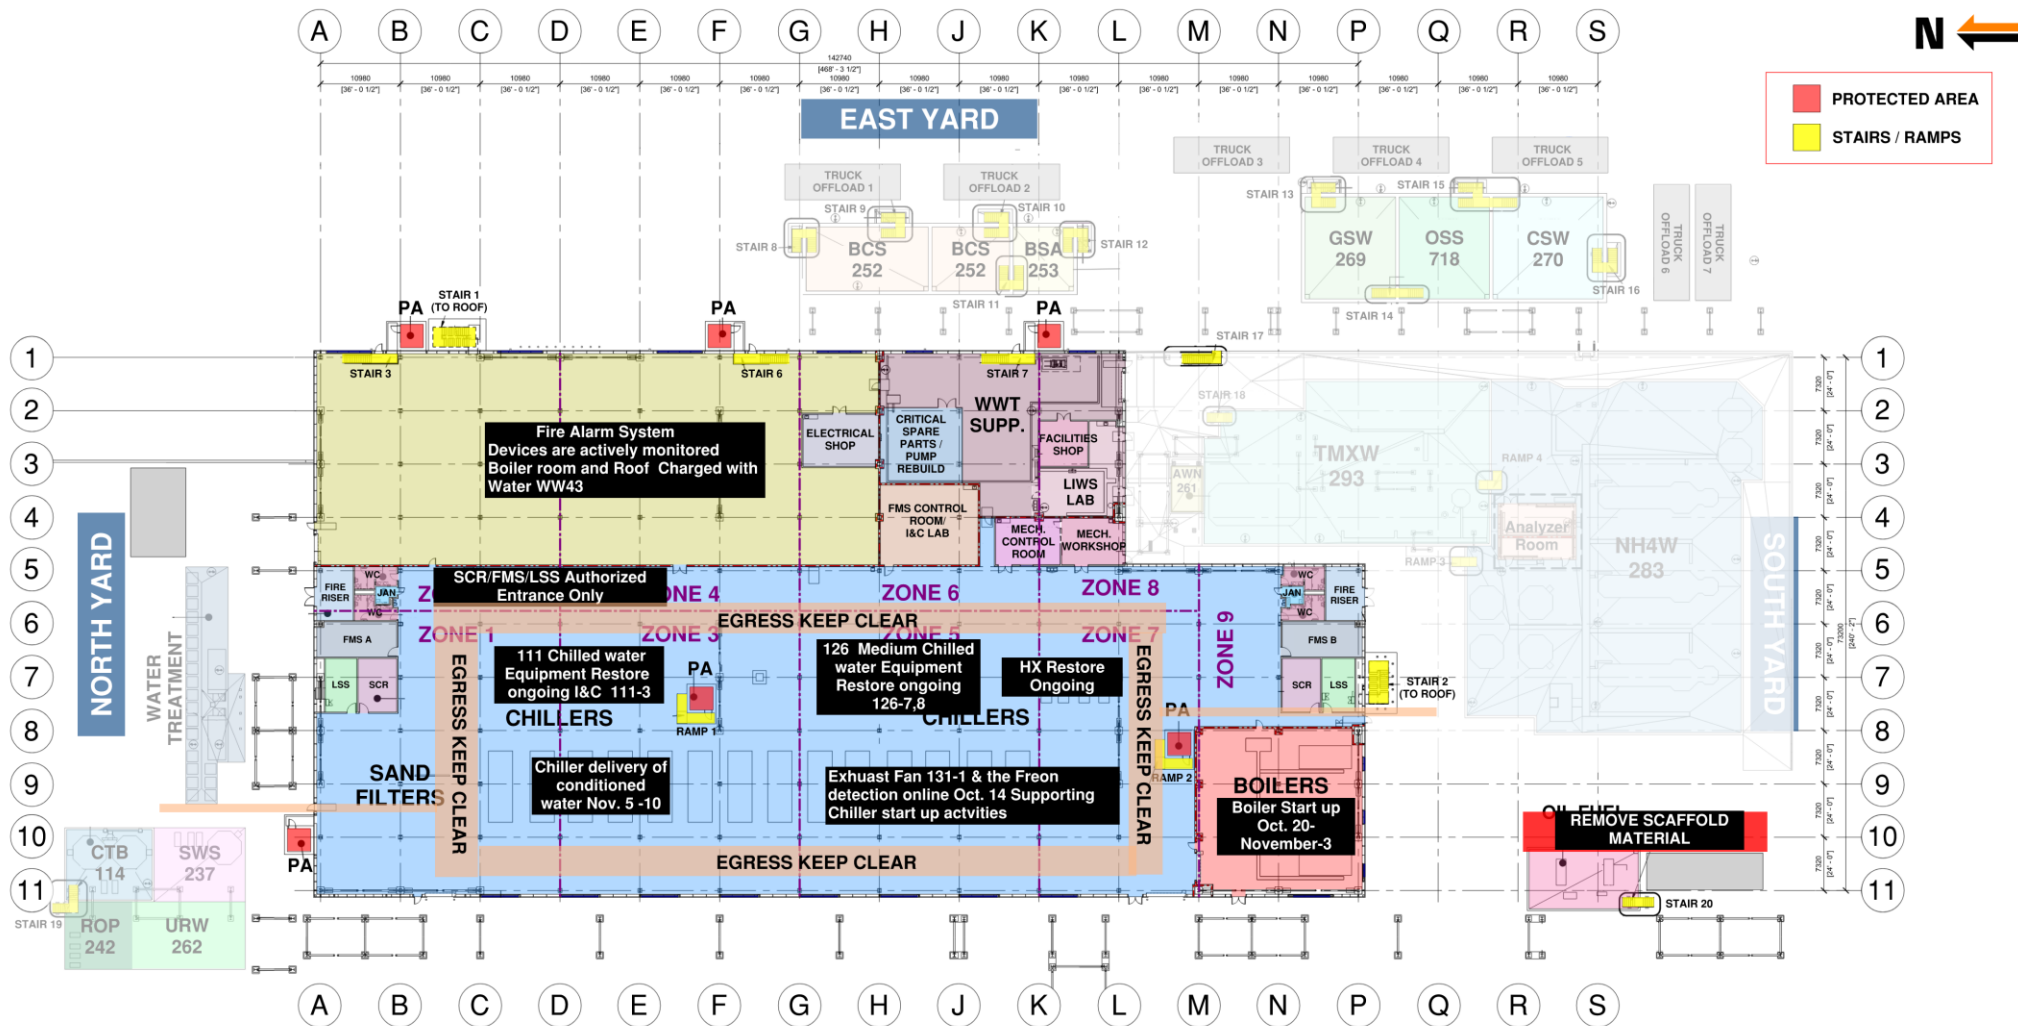

CUB 1 COORDINATION MAP

1. REFRIGERANT DETECTION SYSTEM IS LIVE.
2. IF ANY ALARM IS SOUNDED - ALL WORKERS MUST EVACUATE THE BUILDING. HORNS AND STROBES WILL SOUND AND INDICATE A GAS LEAK.
3. EVACUATION LOCATION TO BE IN NORTH YARD OF CUB 1. UNTIL AREA IS SAFE TO RETURN

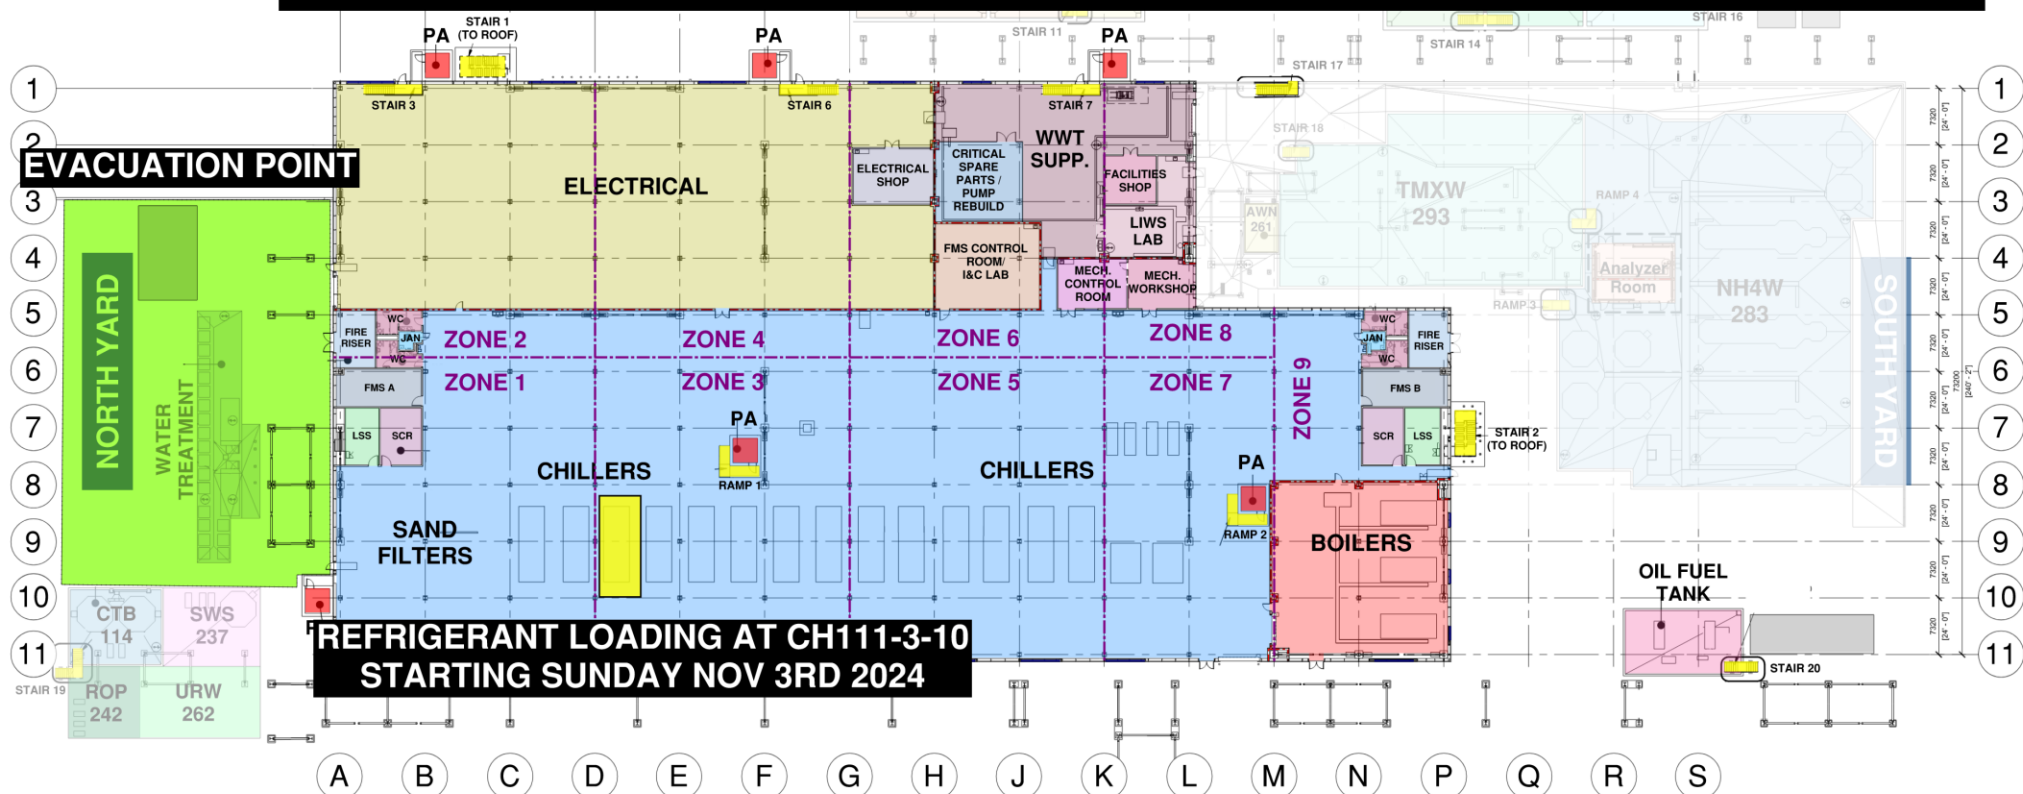

CUB 1 – EXTERIOR/ROOF







CUB 2

CUB 2 COORDINATION MAP


NORTH YARD

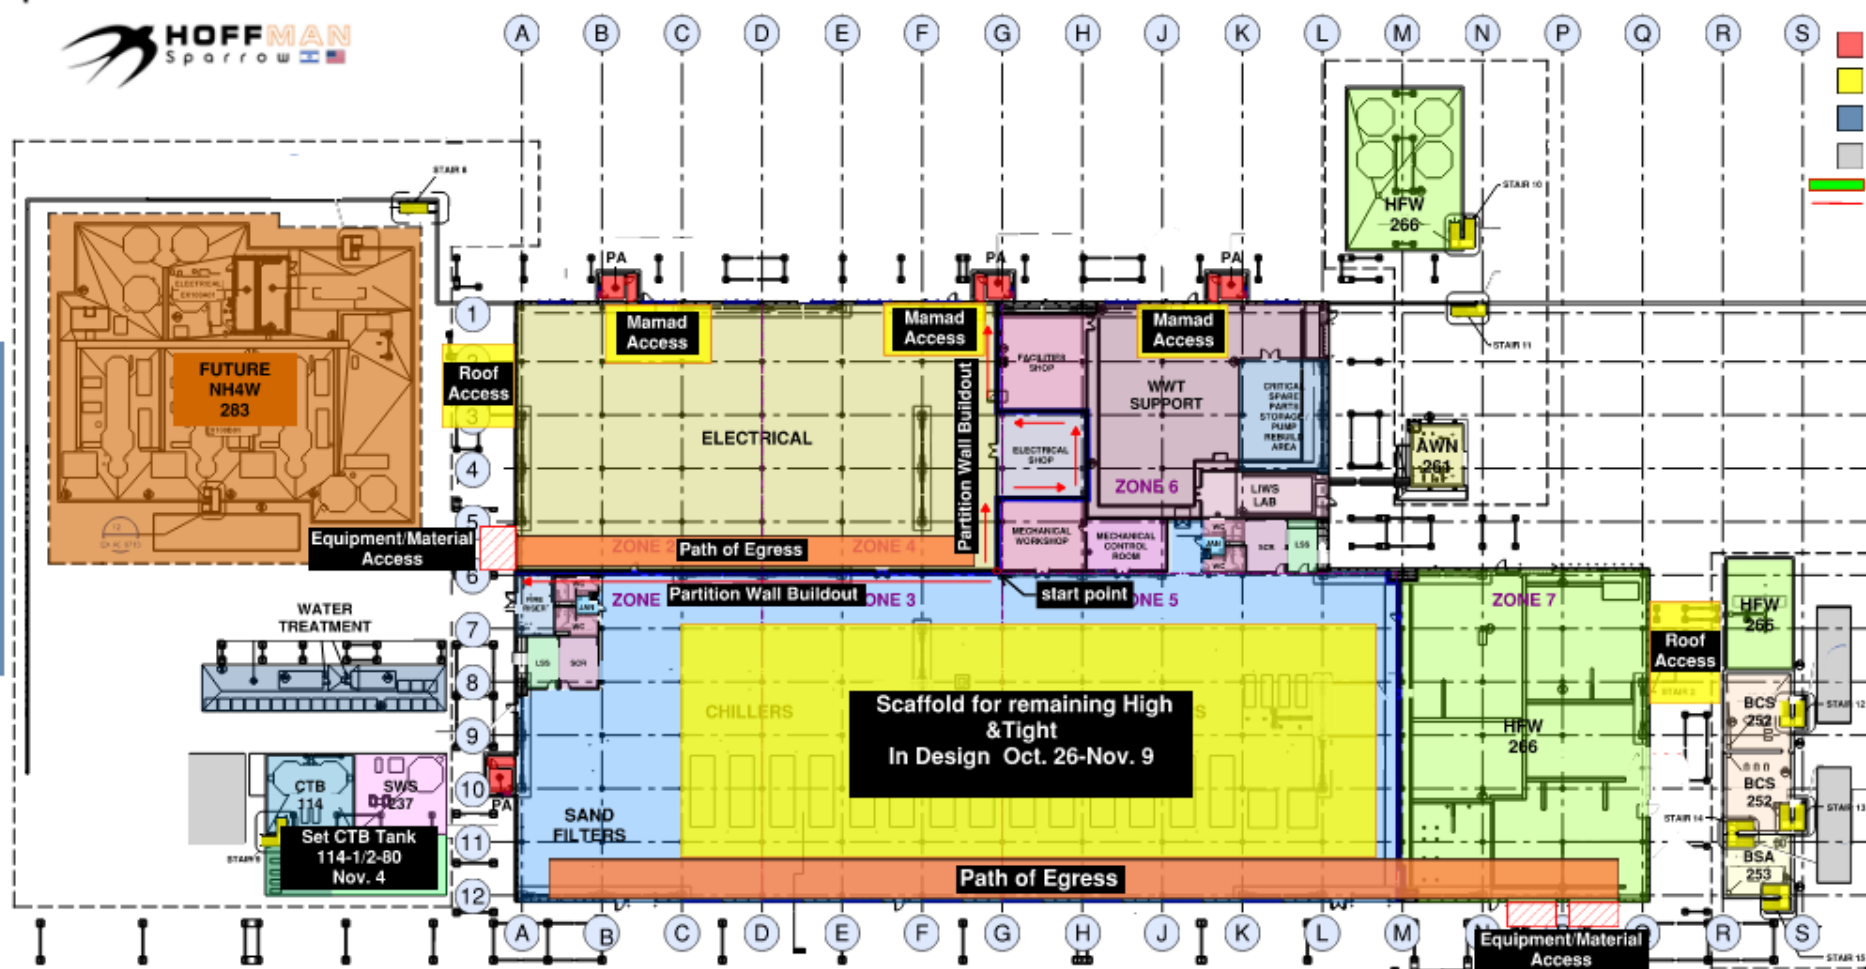


CUB 2 – EXTERIOR/ROOF

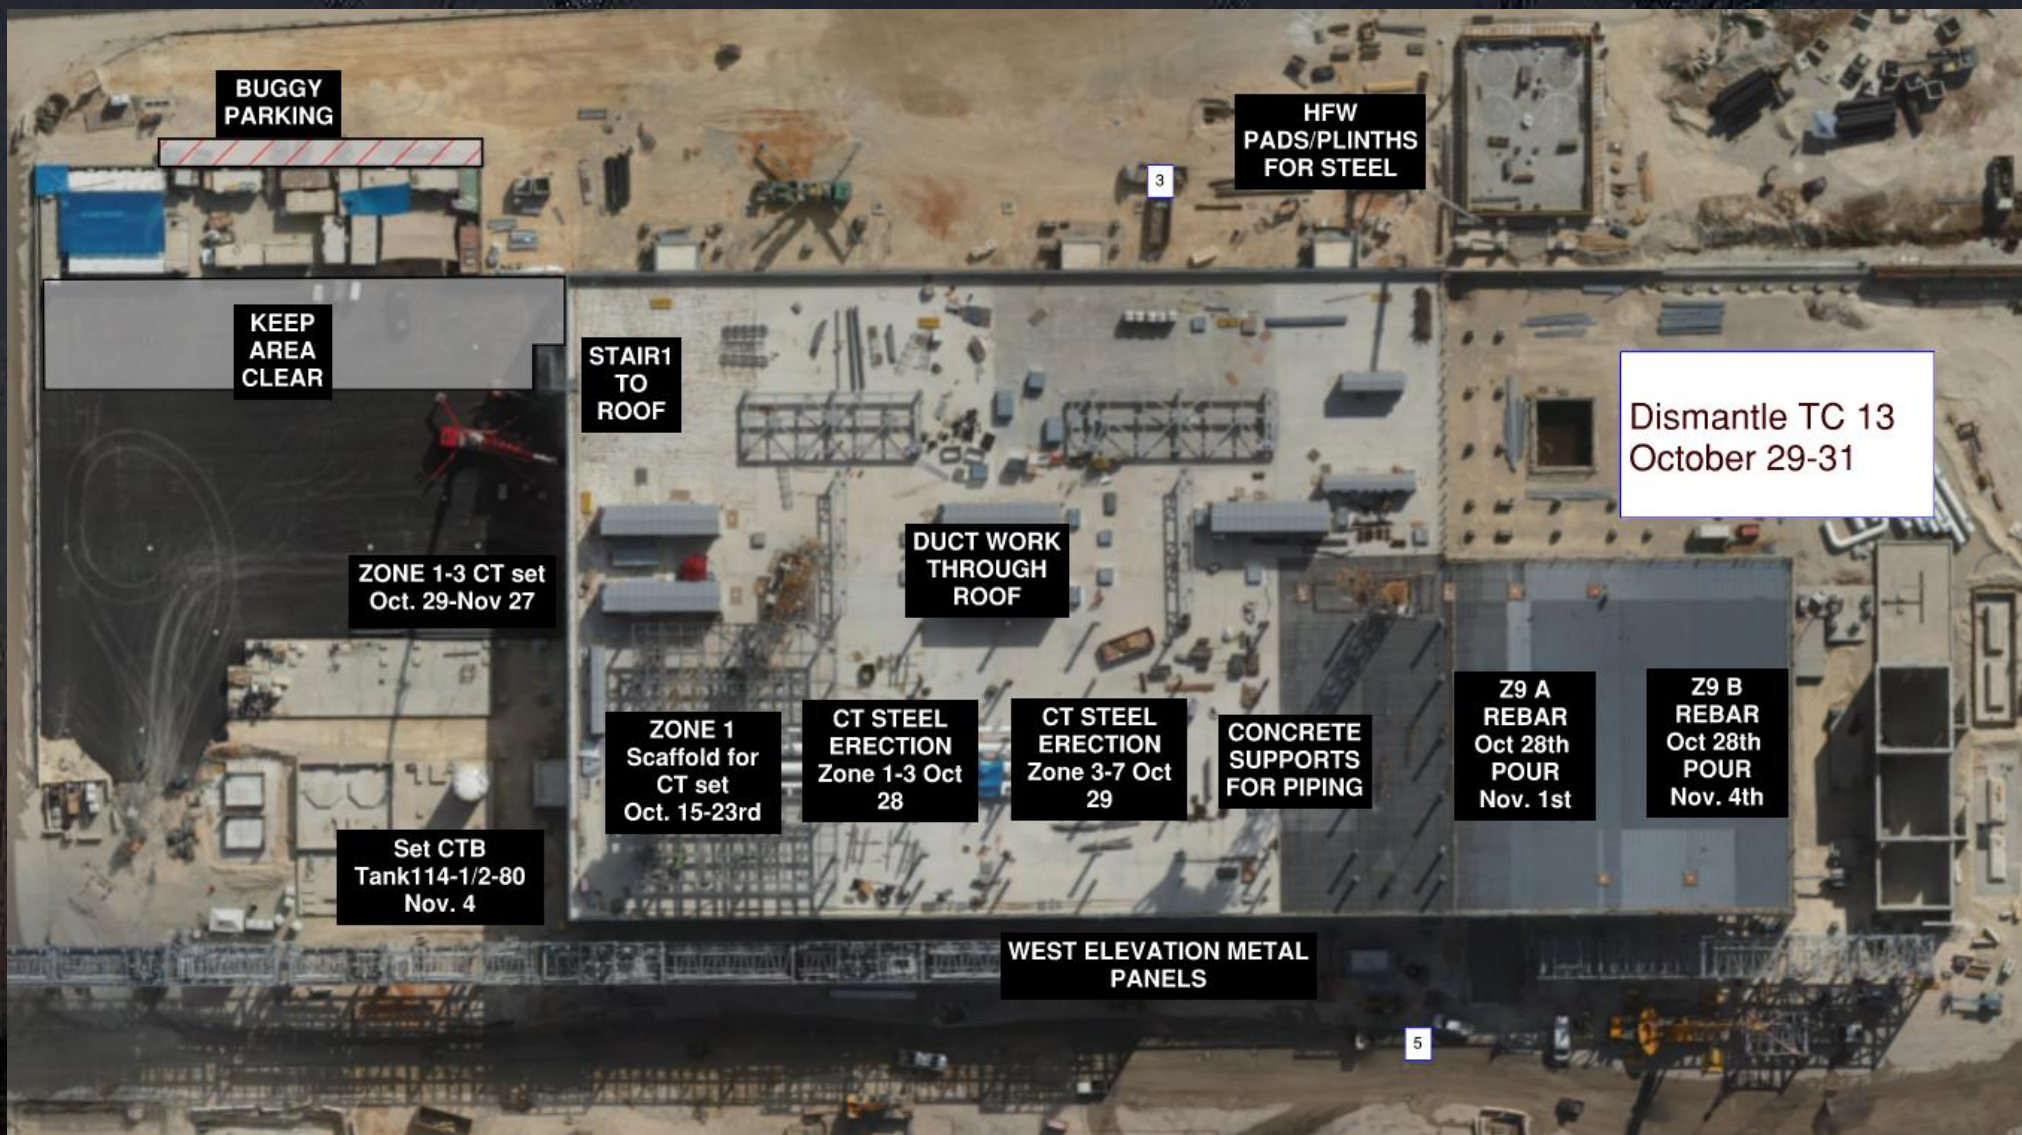


CUB 2 – Crane Logistics

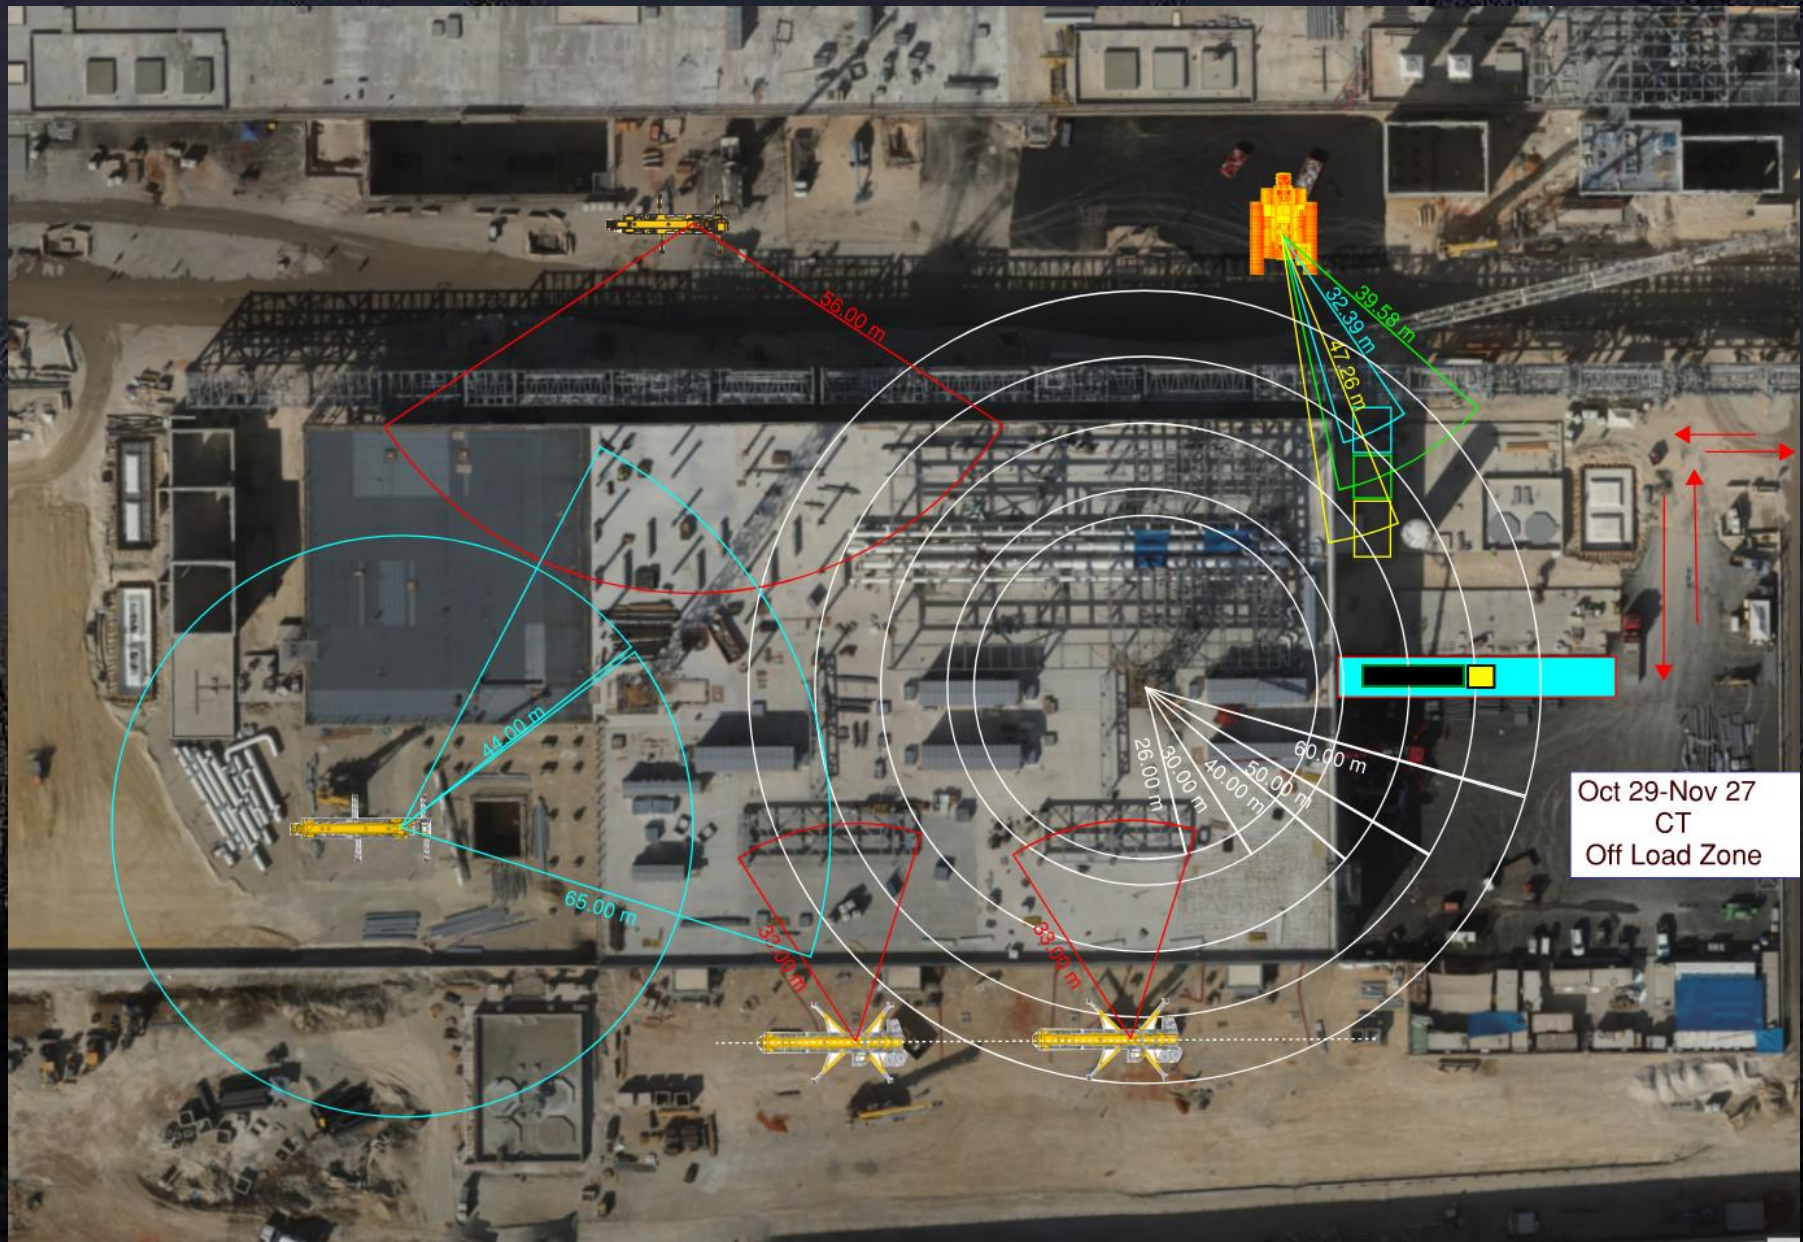

CUB 2 – Crane Logistics

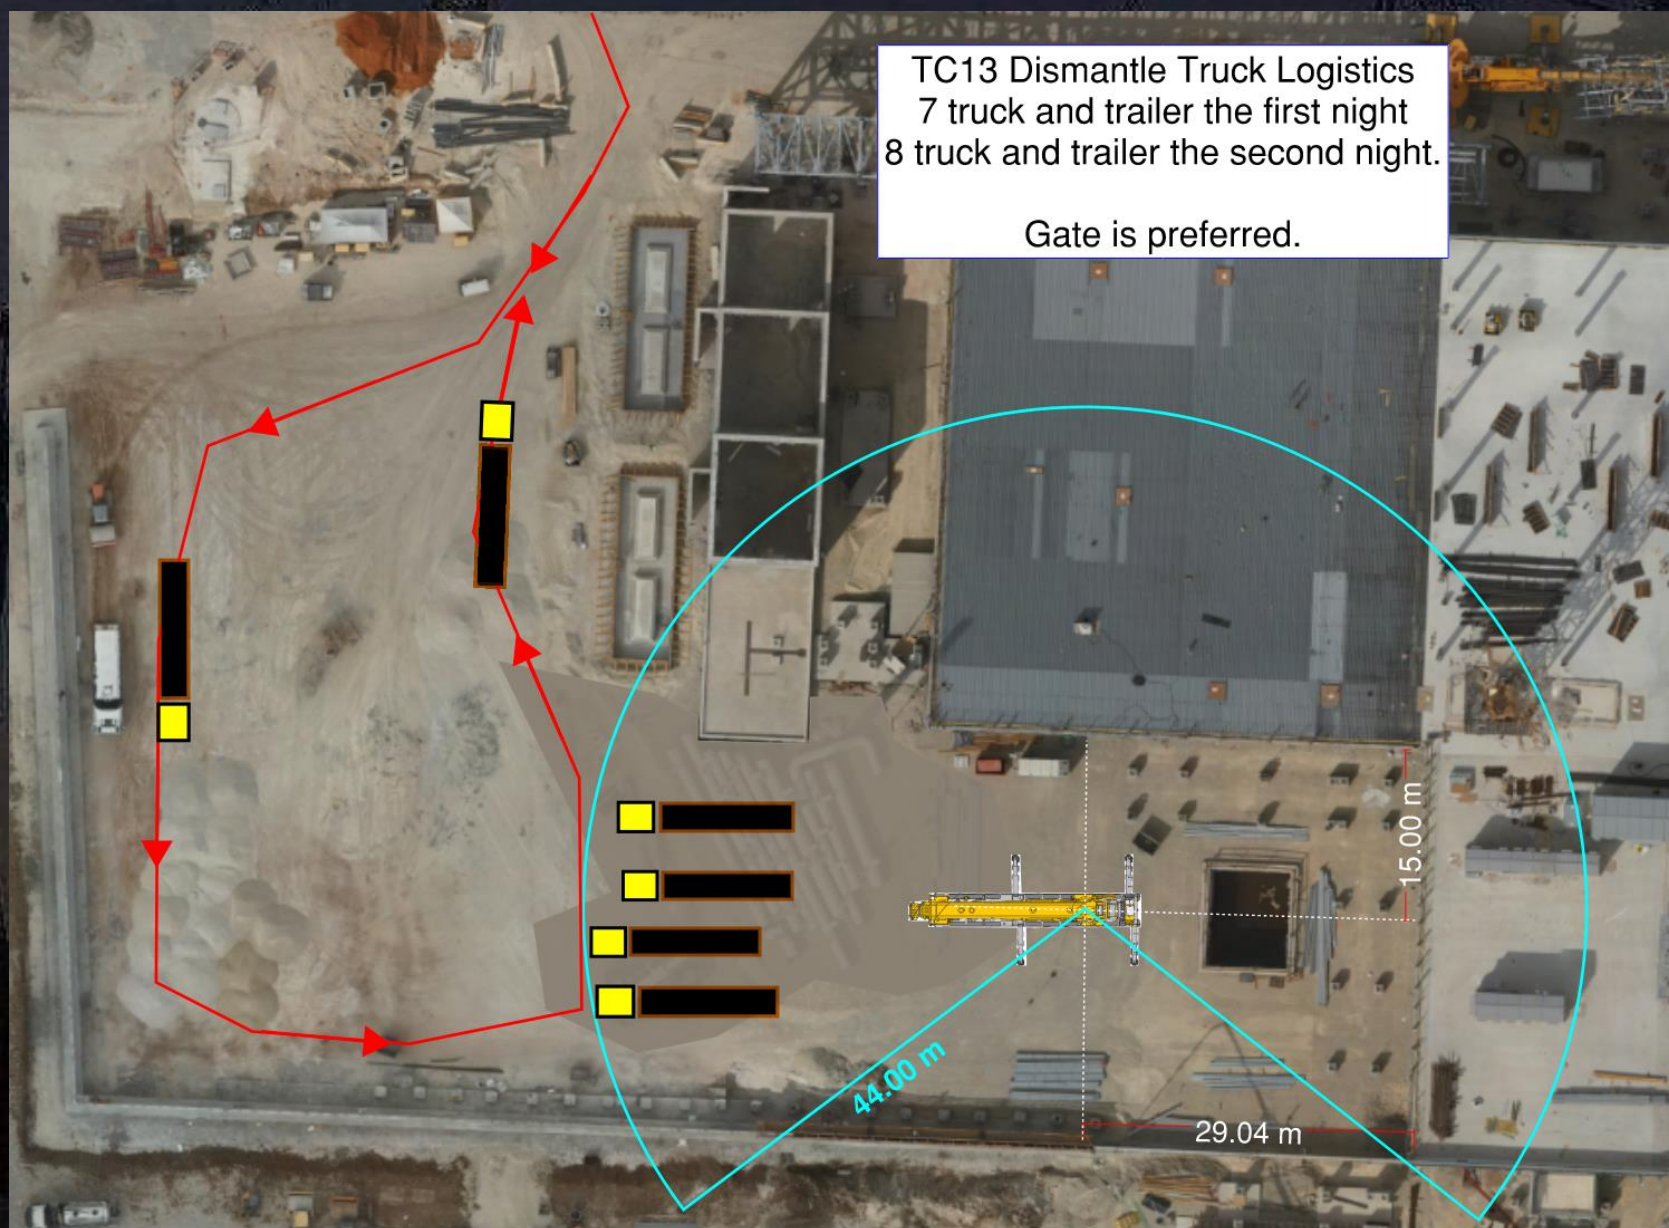





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

T18

CUB 2 - NOV 3th - NOV 11rh

nov 7th




nov 6th

nov 5th

nov 3th


nov 10th

nov 11th



5m






HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

IW 24" - pressure test- 31/10/2024



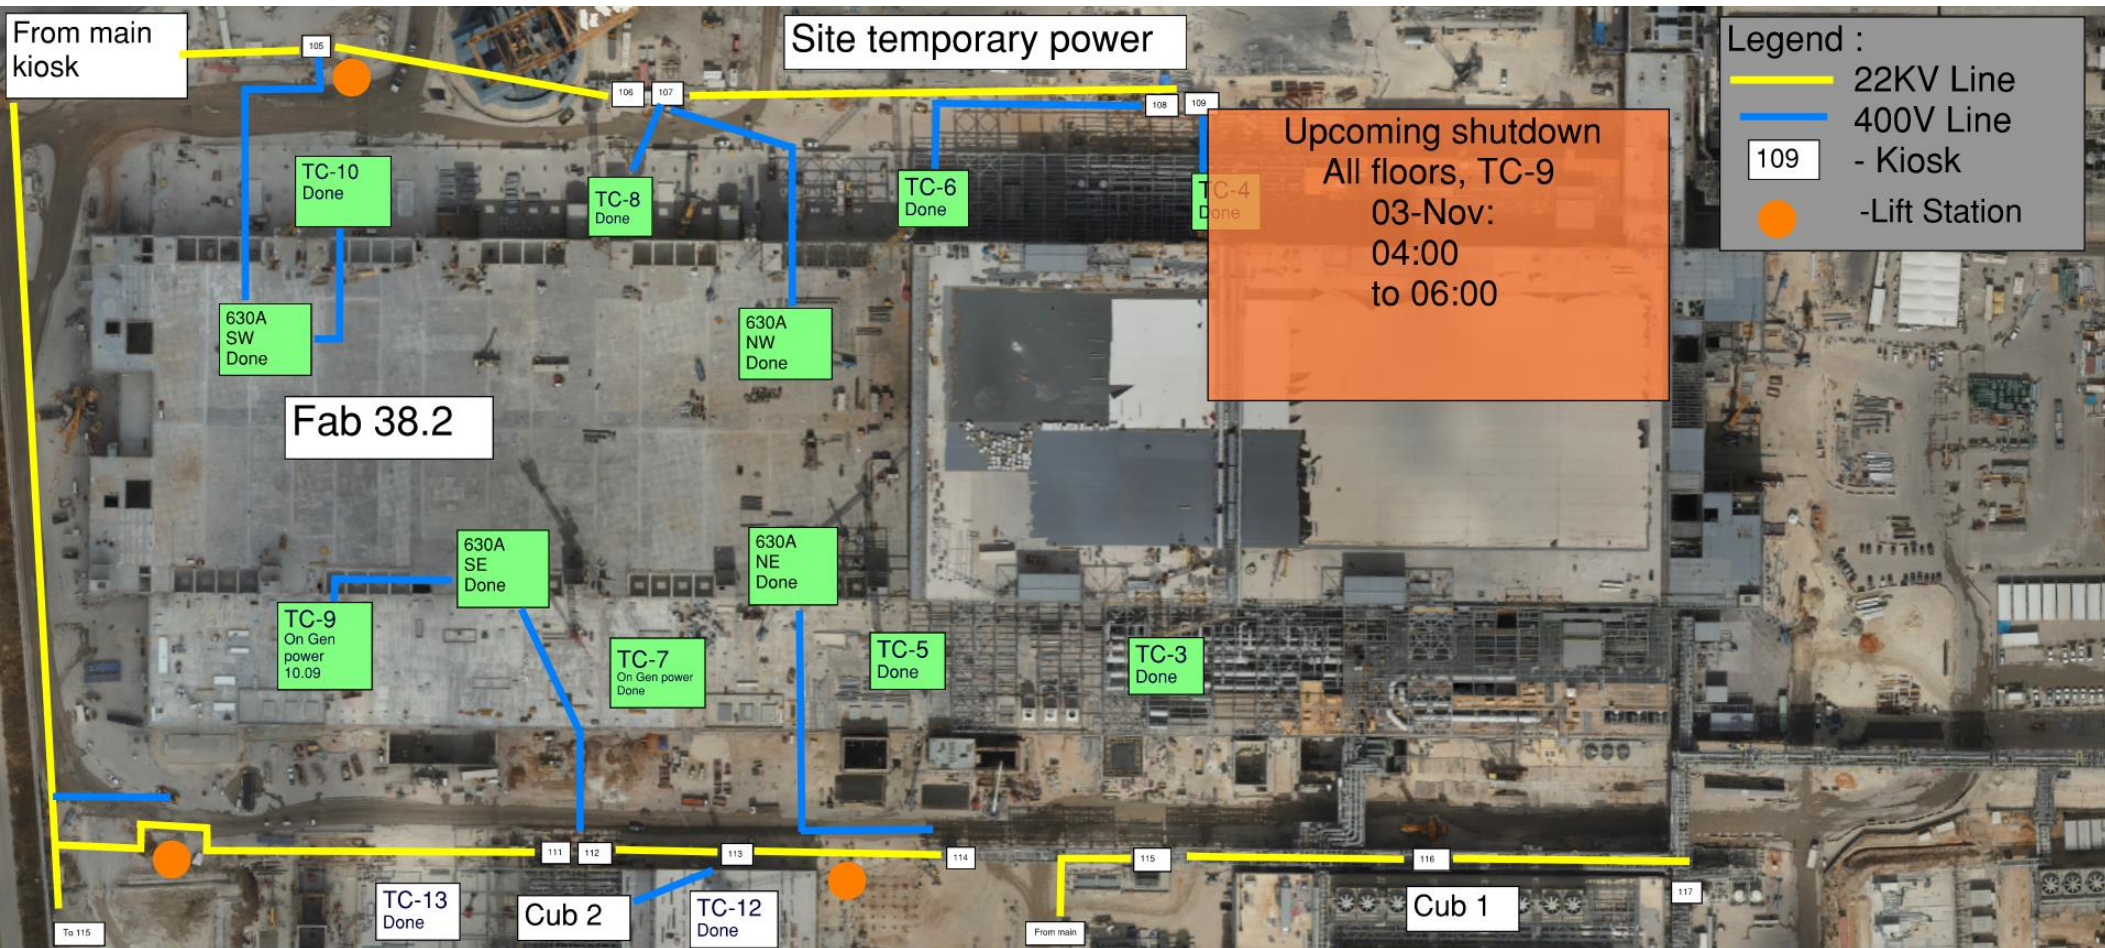



Daily Coordination Meeting

Site Logistics


North



Daily Coordination Meeting

Site Logistics

South

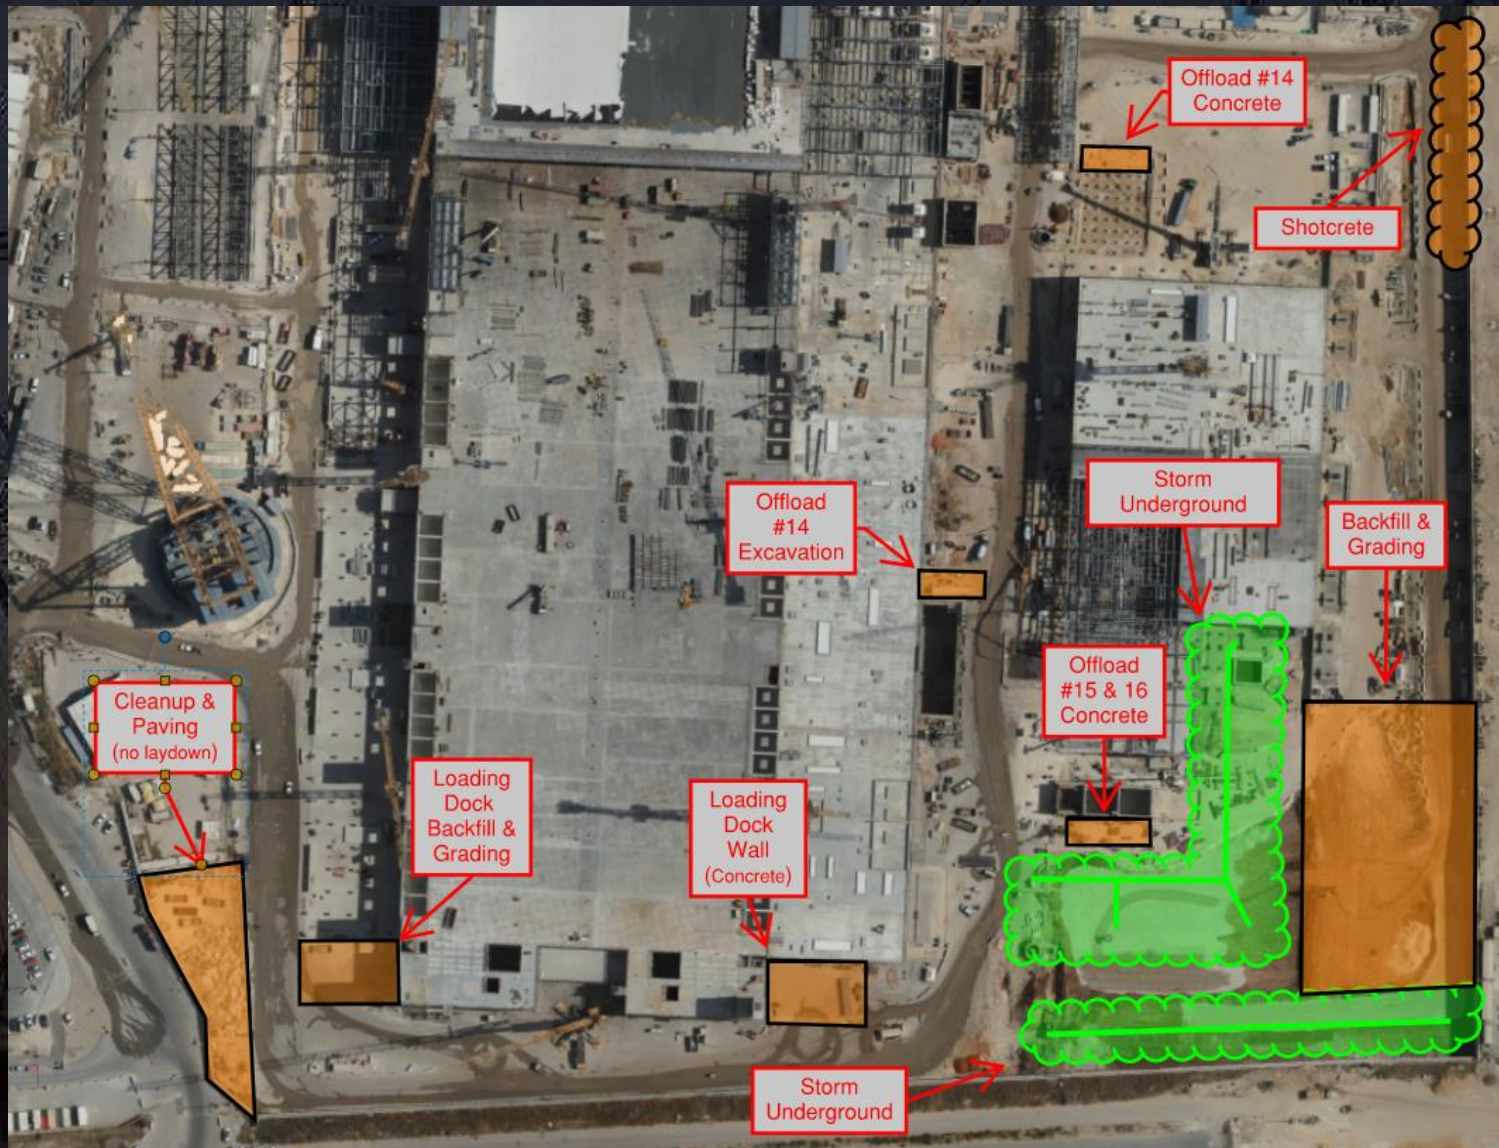

MEWP Use

- Select the proper sized lift- ensure it isn't too large for the work area
- Spotters for ALL movement. Including vertical.
- Identify obstructions- on the ground and overhead
- Keep hands off the rails while moving
- No stepping on toe-board, mid-rail, or top-rail
- **Render it dead hit the red** whenever the MEWP is not being actively moved.
- Lower MEWP before you travel- and pull in the extendable platform
- Inspect the MEWP before use
- Diapers installed on all MEWPs cannot obstruct the safety functions of the MEWP- emergency release, stop button, etc.

Daily Coordination Meeting



14:00 Sign In
