

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- Back to basics- complacency
- • Power in Fab tomorrow- 33kv
- • Buggy stickers (see QR code)




UTILITY LEVEL MOD1

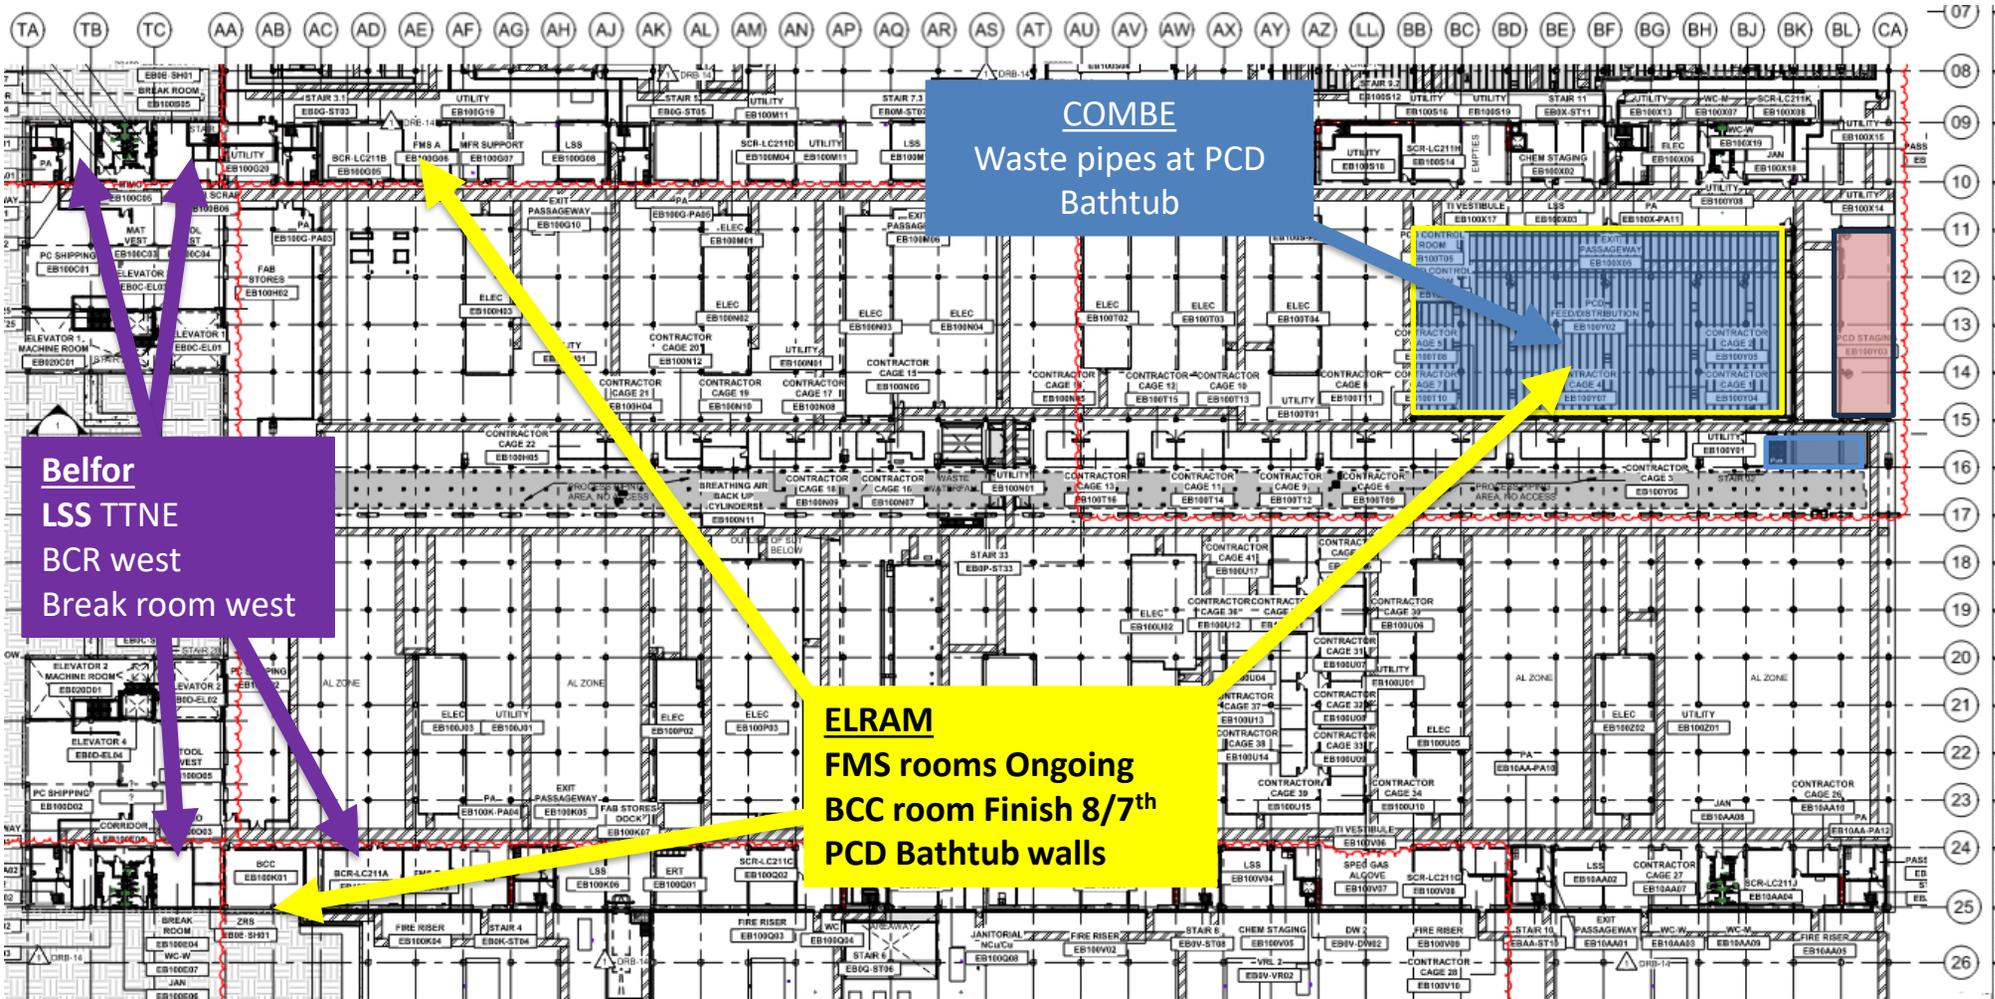


COMBE
Waste pipes at PCD
Bathtub

Belfor
LSS TTNE
BCR west
Break room west


ELRAM
FMS rooms Ongoing
BCC room Finish 8/7th
PCD Bathtub walls




UTILITY LEVEL MOD2

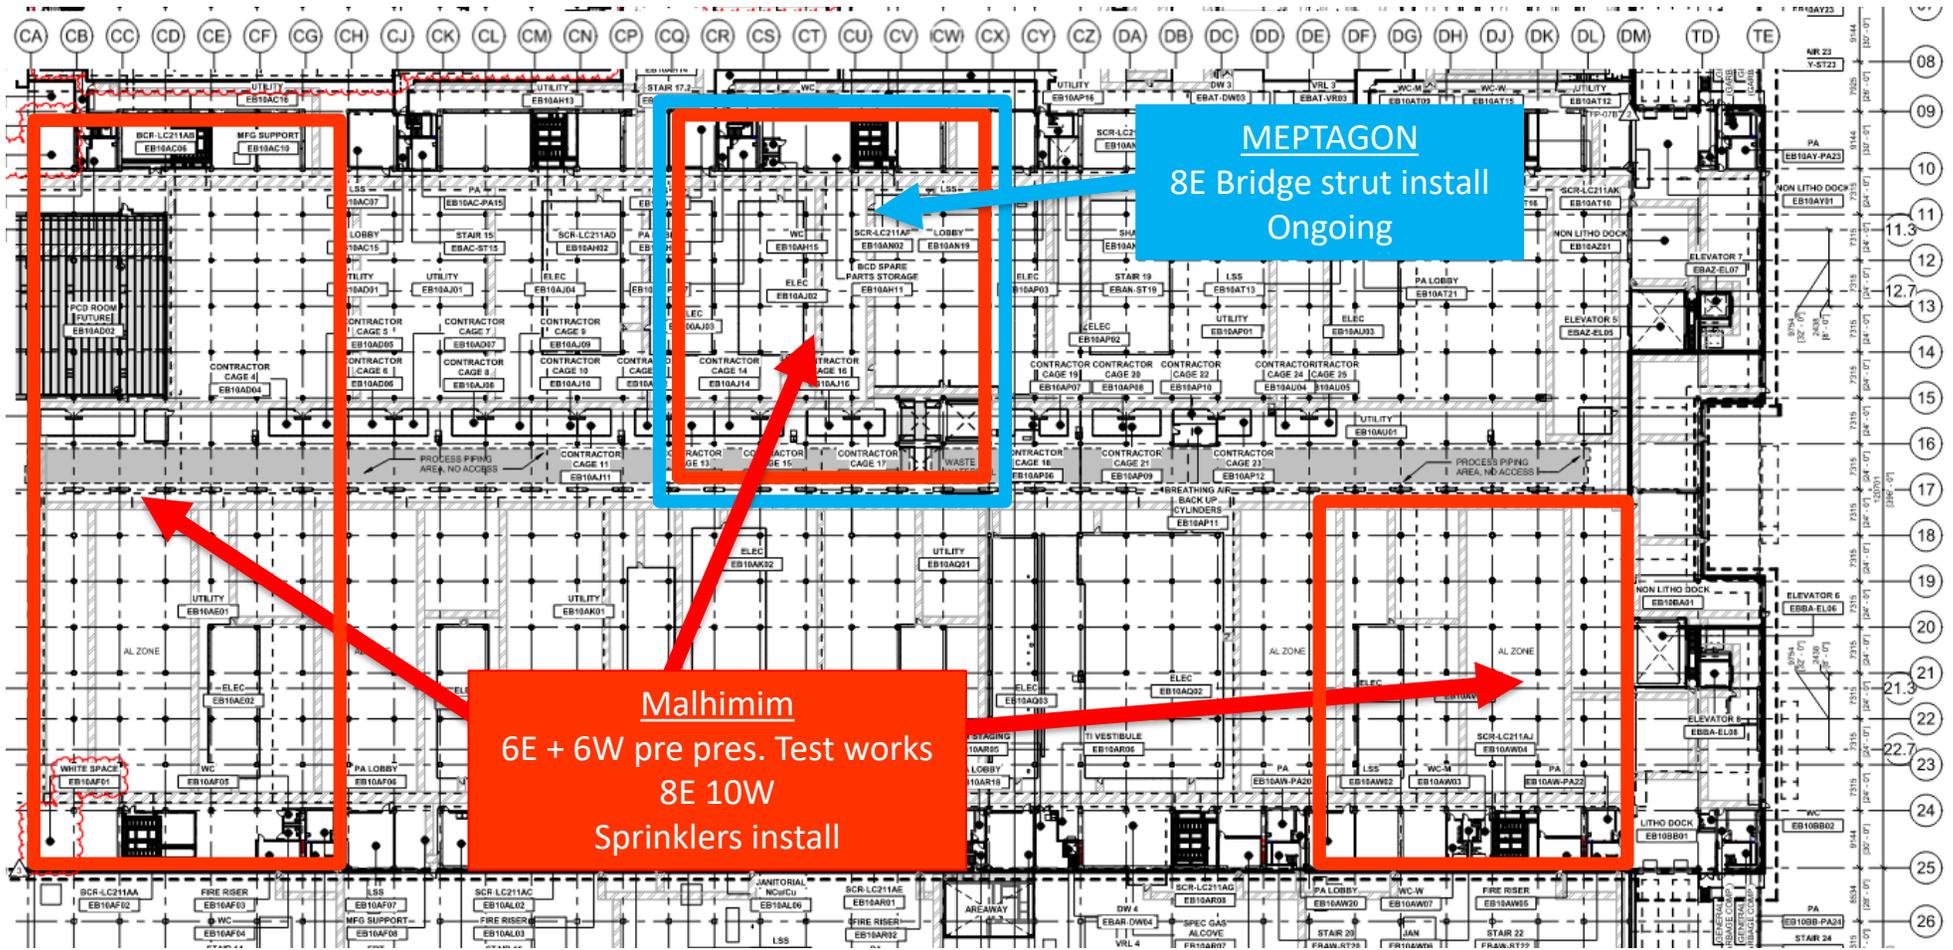

SUT 38.1 LEVEL

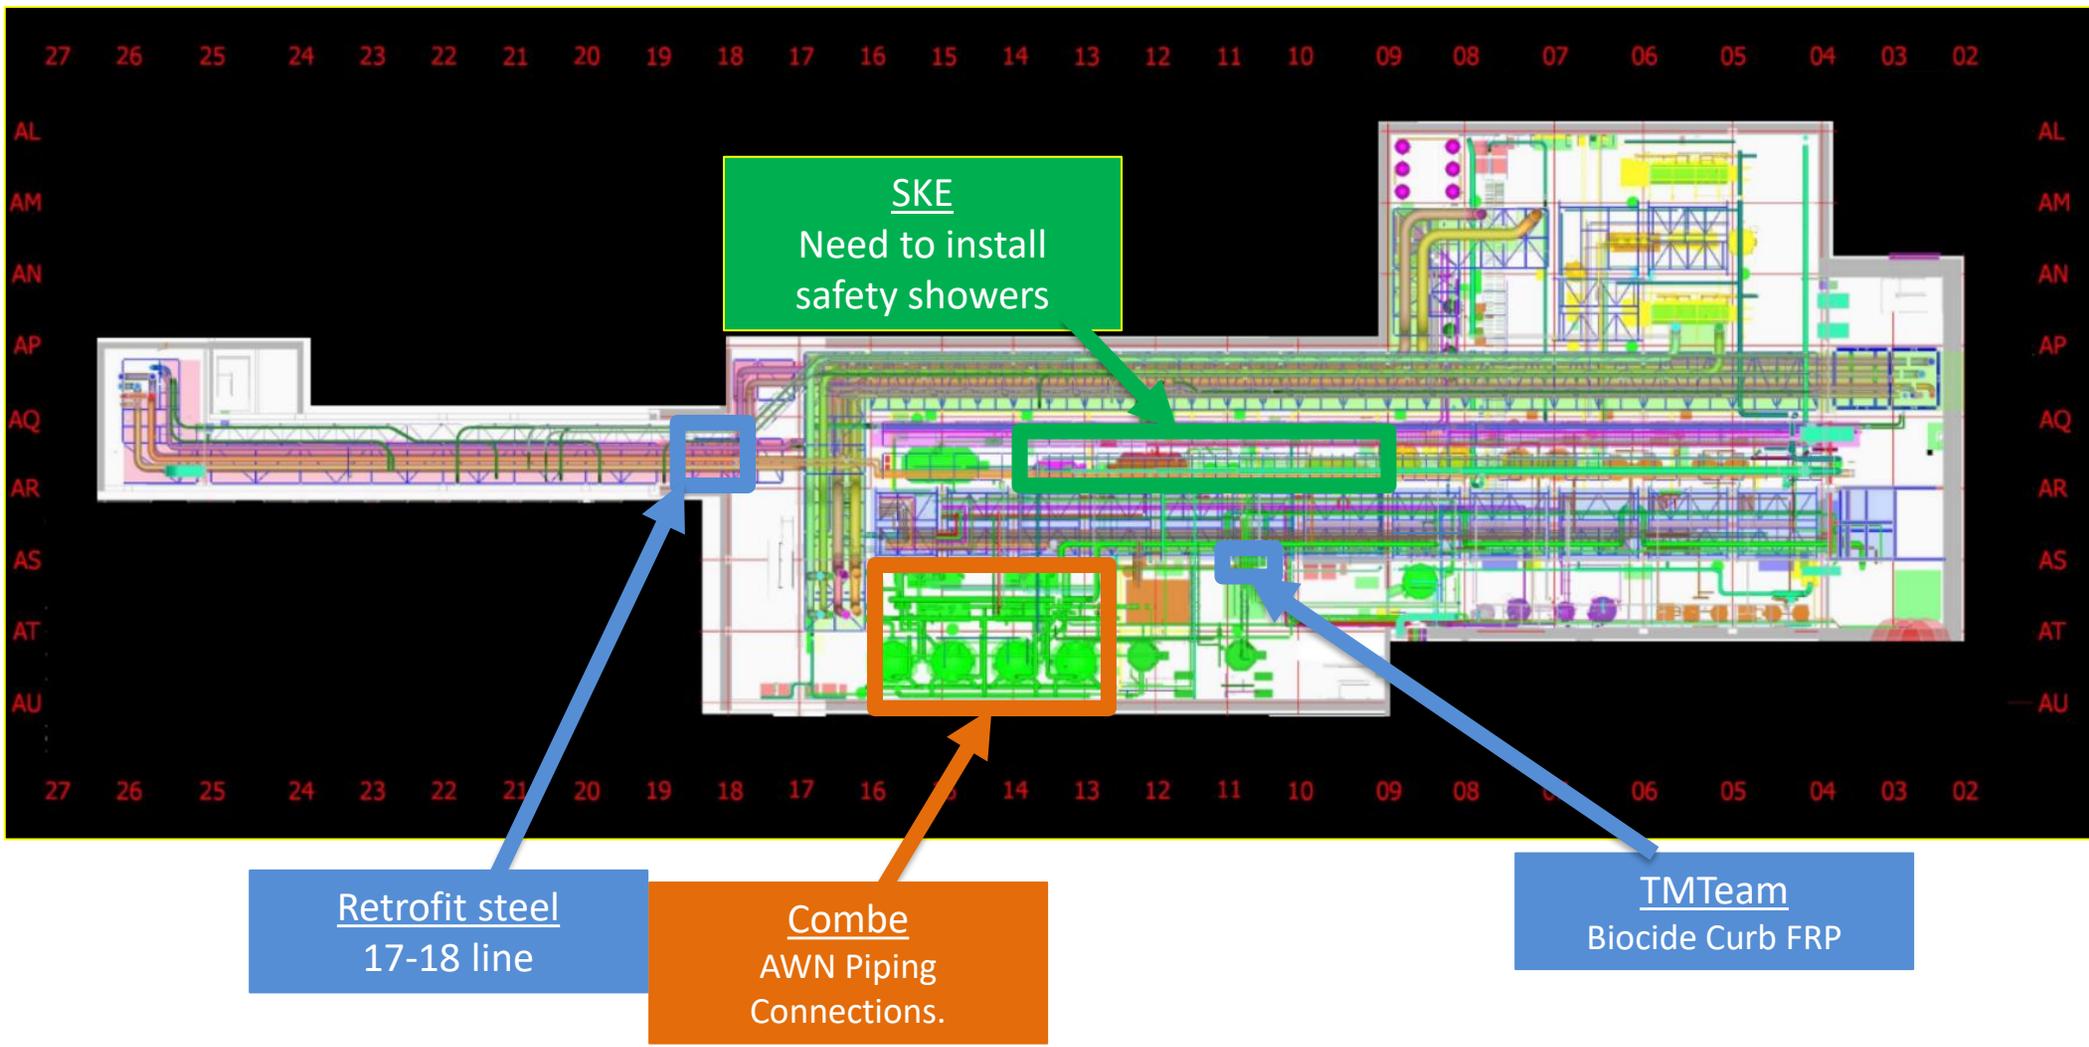

SUT 38.2 LEVEL

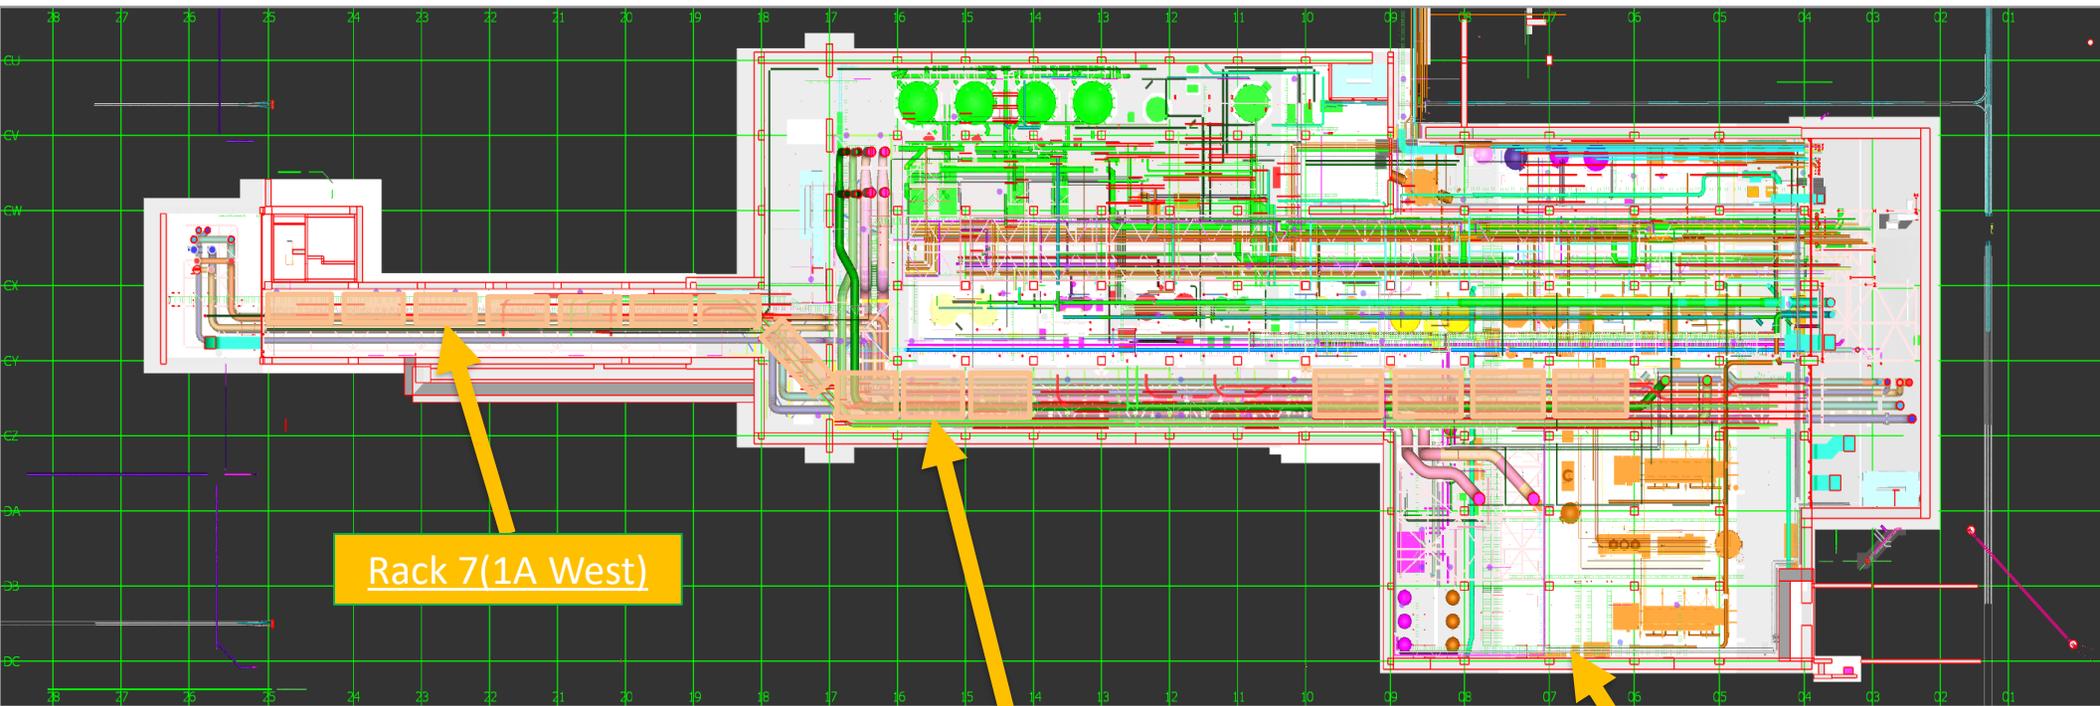

Rack 7 (1A West)


1A Rack Lifting

8 Rack


SKE
H&T
CRW
Move-In date ?

Vesda
H&T

SUBFAB BUILDOUT MOD 1

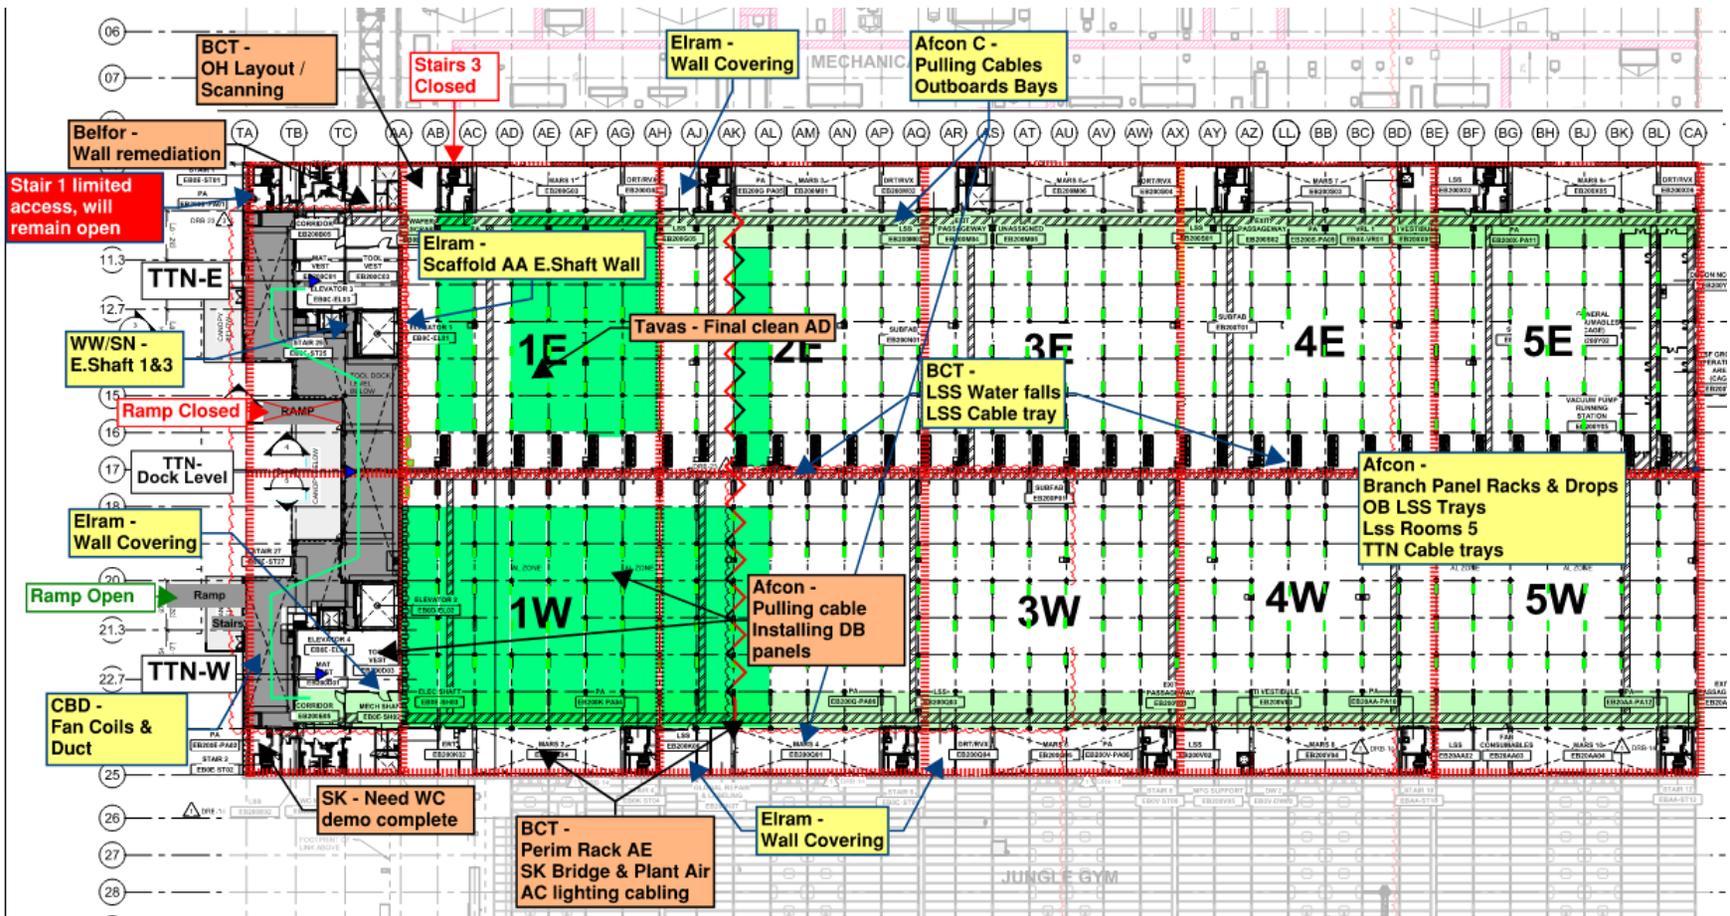

SUBFAB BUILDOUT MOD 2

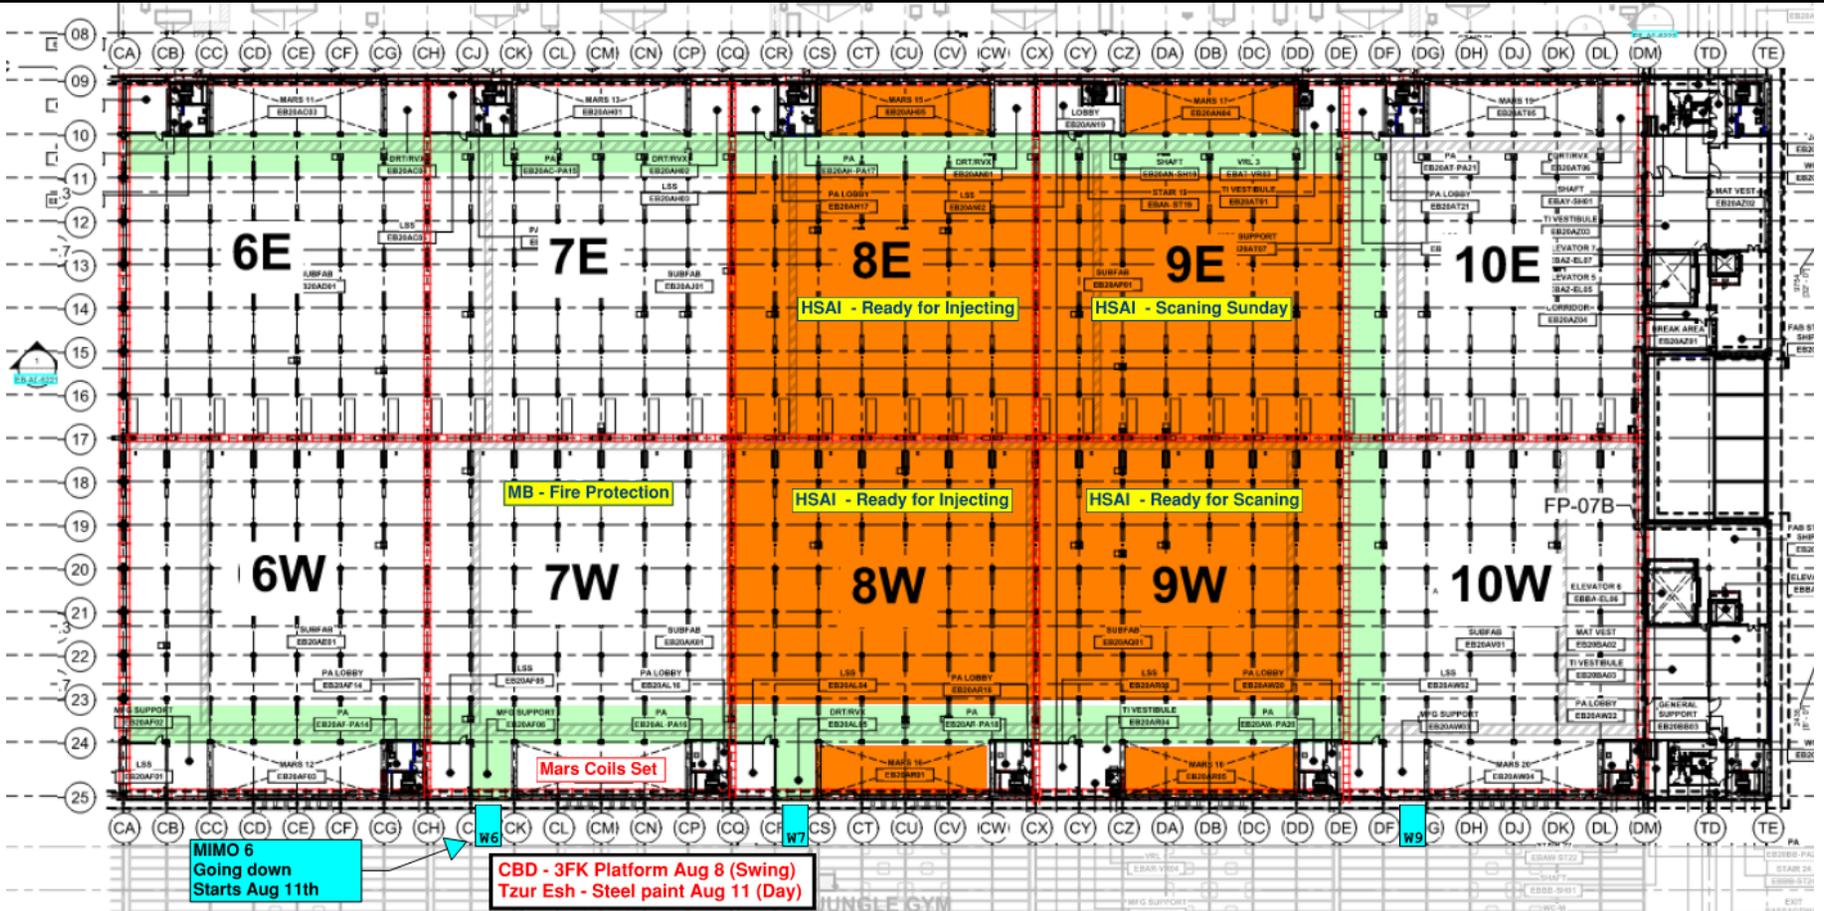


CRC Beauty Cote Work Plan.

Be well prepared to protect CRC

1. Nothing touches the floor, All must be on wheels.
2. Carts & MEWPs wheels must be replaced with a cleaner type (White).
3. Always have protective sheets/board on site to use for cover areas.
4. Damaging CRC will cause unnecessary and painful expenses to your company.

**1W South
Starts Aug 11**


**1W North
Ongoing**

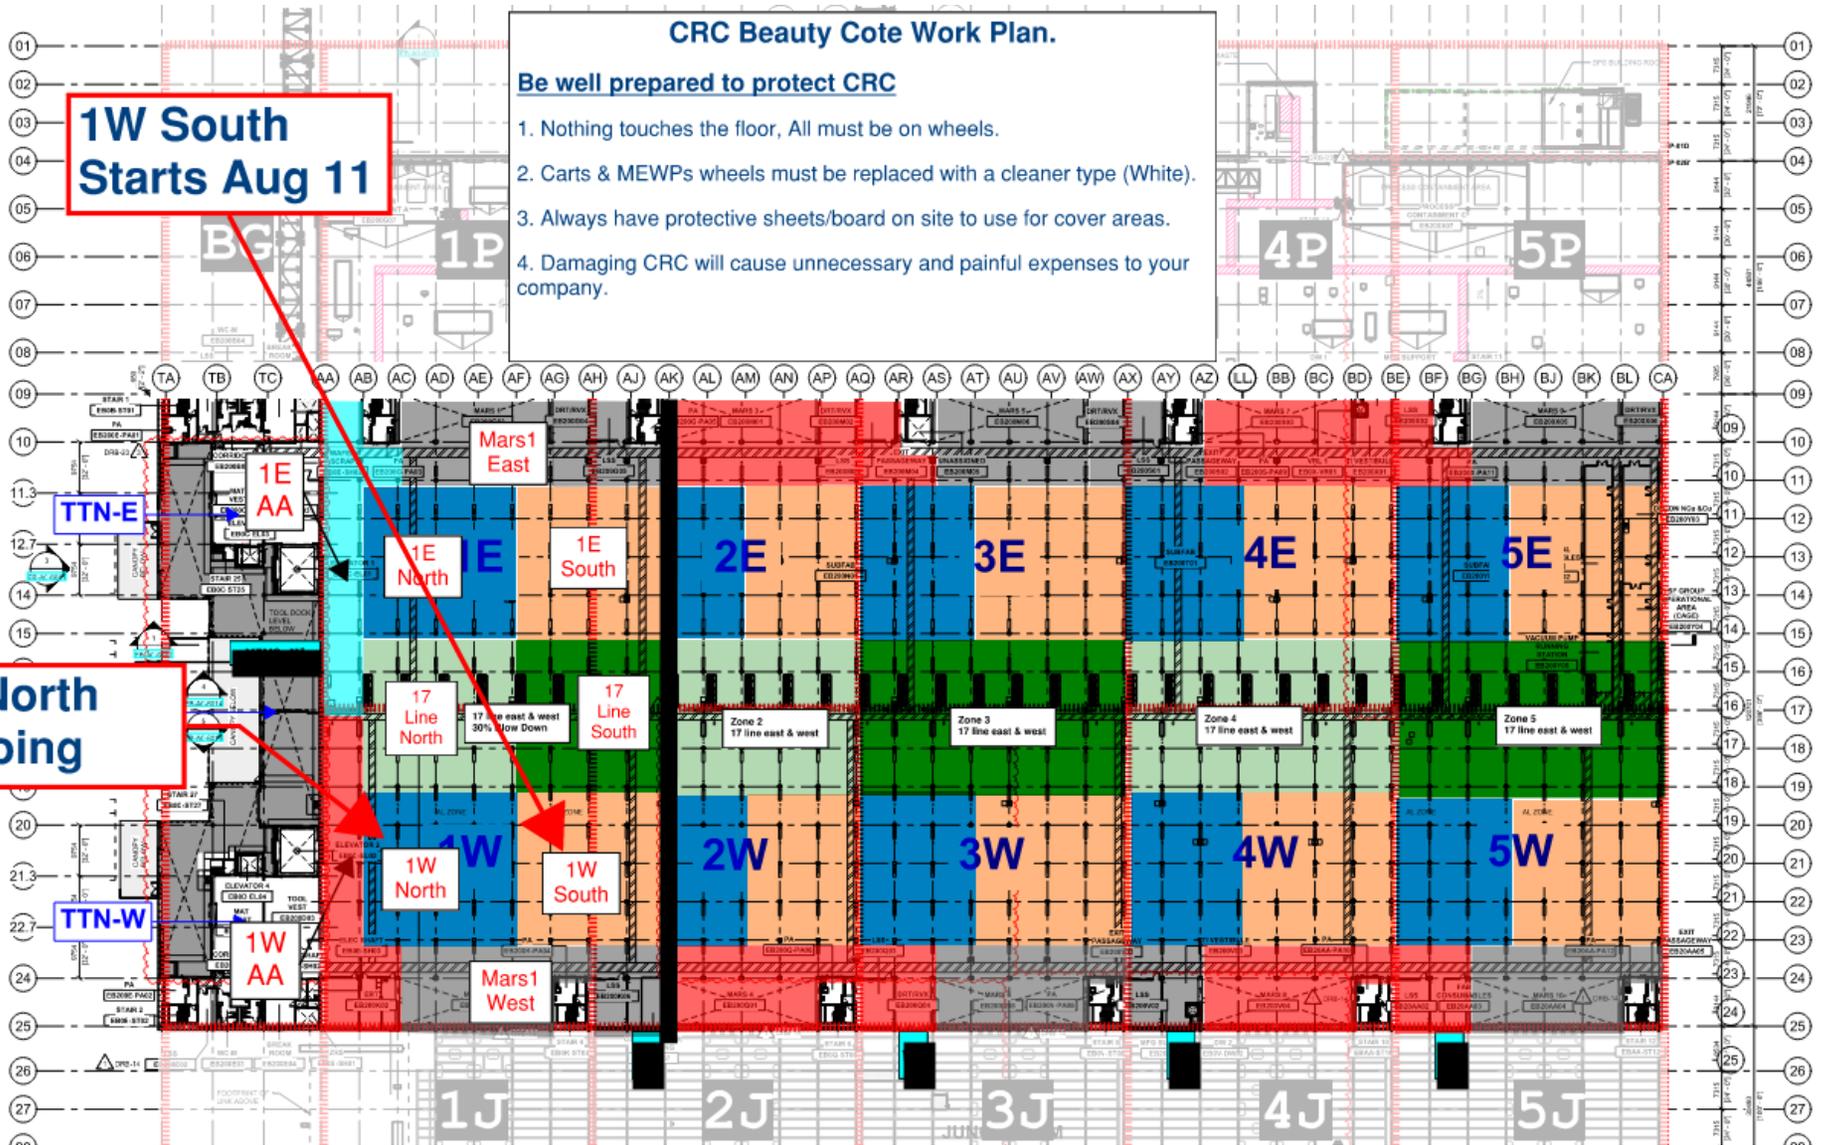


NTTE/W
 WW/SN - west side welding tabs and replacing beams
 Elram - East/West floor done QA/QC
 SK - east side pipes needs to be completed
 HYG - East to finish steel
 West receiving material

CR level:
 Alcon - Cable trays, modules and stickers 1W,2E, 2W
 MB - 1E drops, 1W drops. 2E- drops
 Elram - 10, 24 columns/shaft walls
 WW/JS - 17-18 line added beams+ AS south stocker beams
 Meptagon - I&C 1E
 D&P - Ceiling rods 1E, 5E blades install.
 Tzur-esh - 24-25 lines. 4E-4W
 HYG- 1W Litho crane QA, 5W Litho crane steel
 PT - Duct prep for test AA-AH east
 Talad- Blades install 24-25 lines
 Belfor - AA/TC lines

Belfor
 AA/TC line

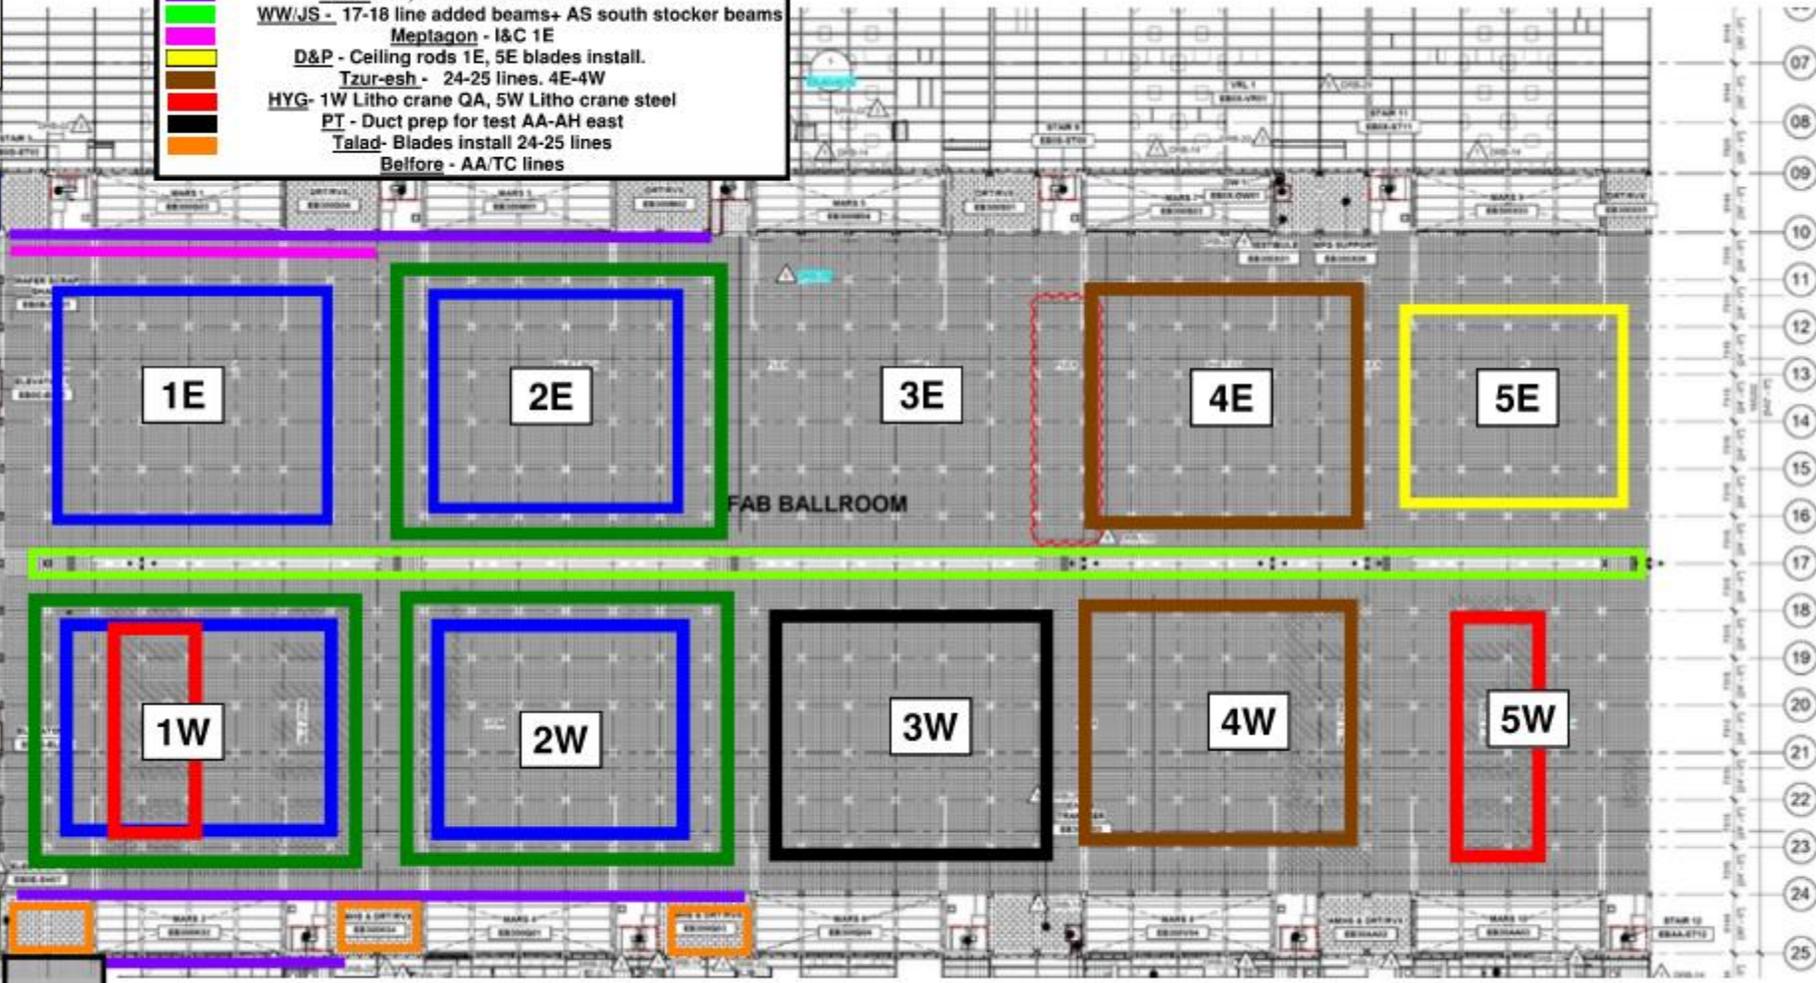

Link
 RP - FP 5RA level
 MB - To start WW33

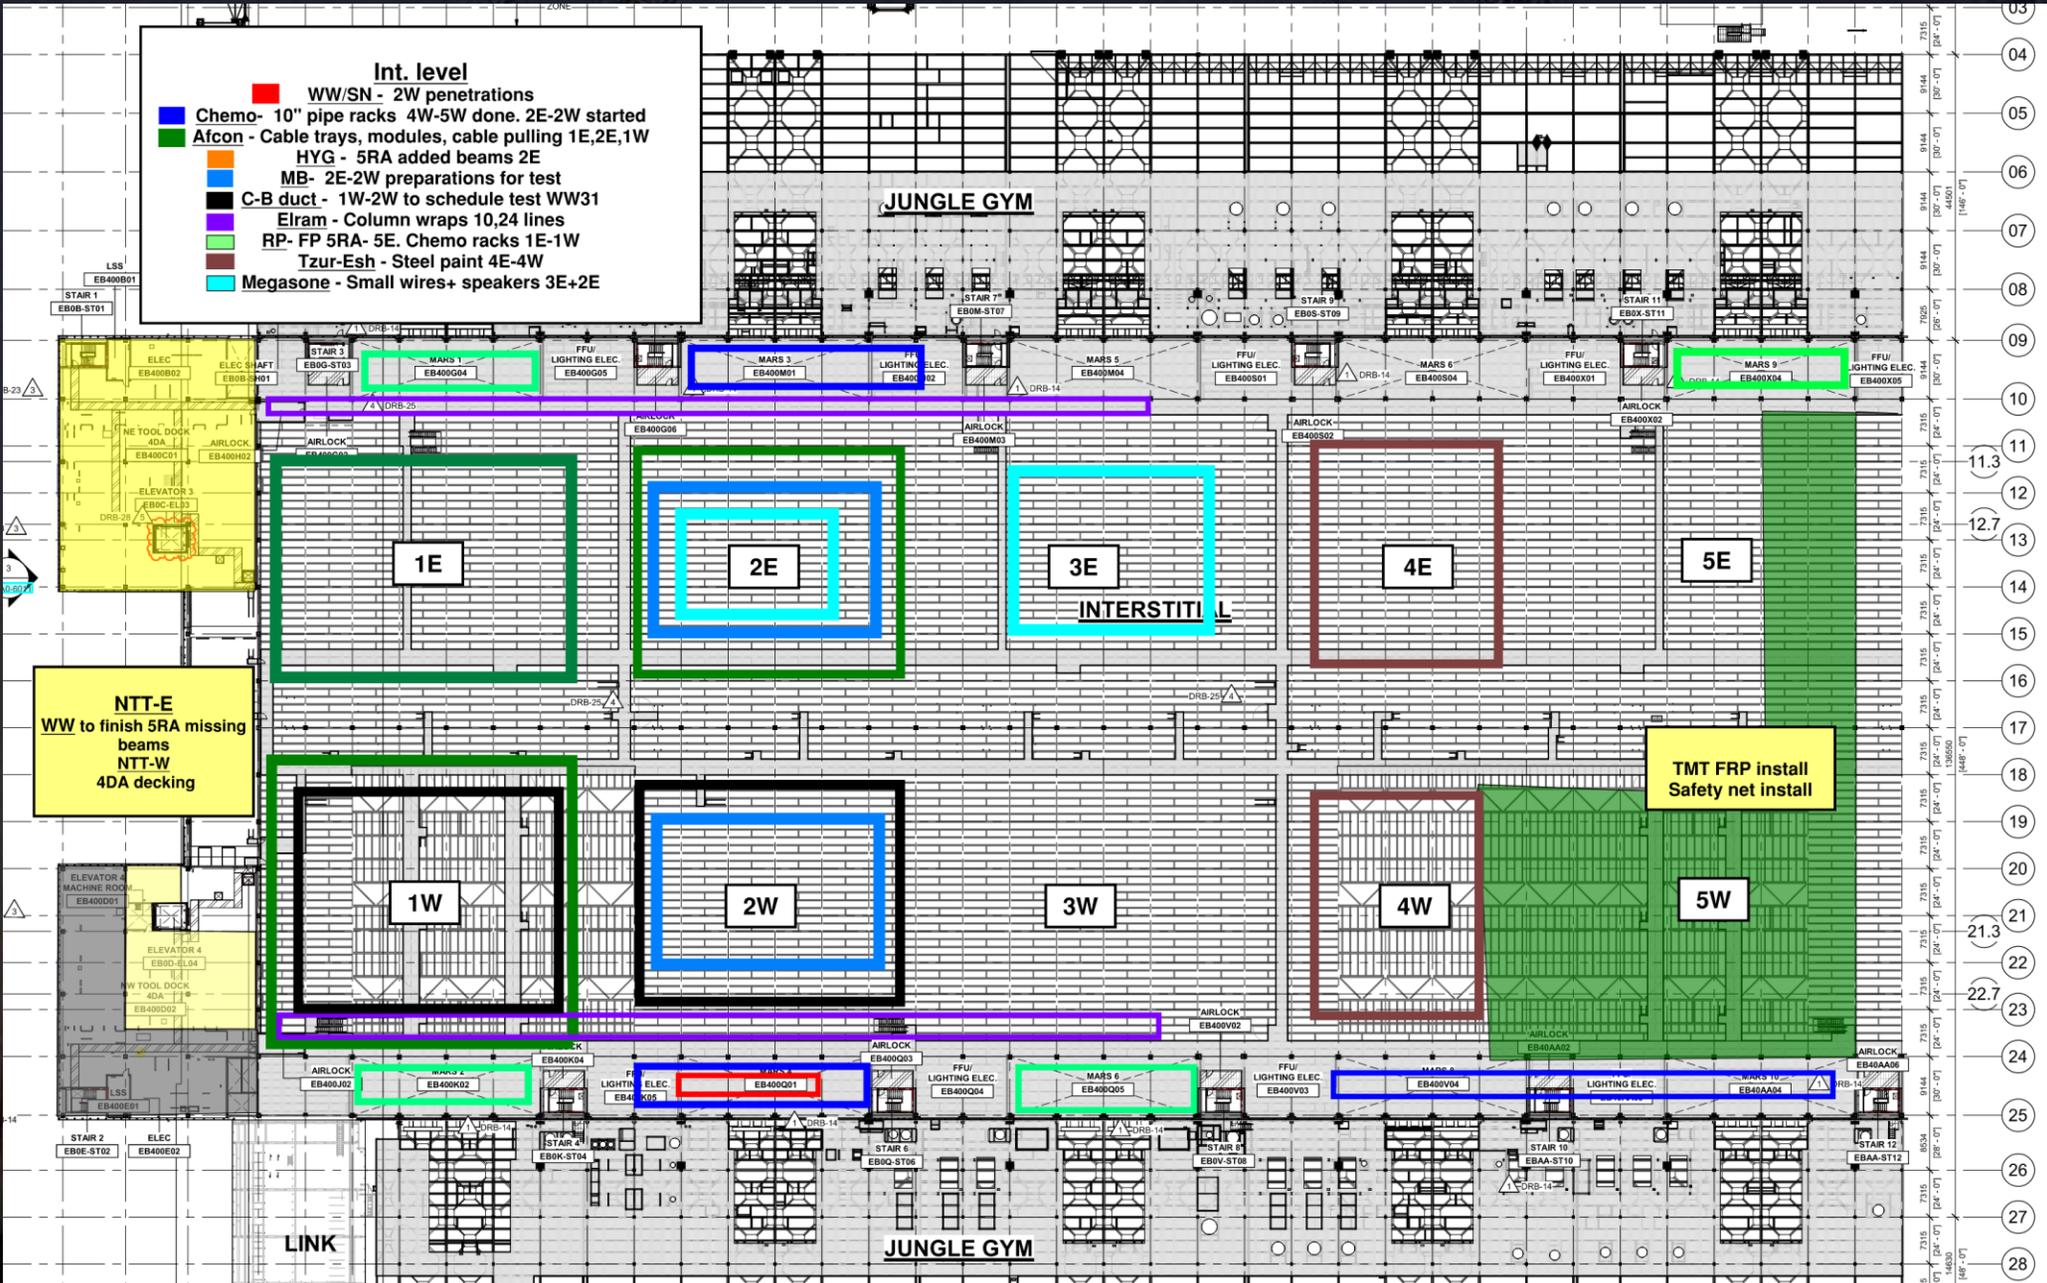

Int. level

- WW/SN - 2W penetrations
- Chemo- 10" pipe racks 4W-5W done. 2E-2W started
- Afcon - Cable trays, modules, cable pulling 1E,2E,1W
- HYG - 5RA added beams 2E
- MB- 2E-2W preparations for test
- C-B duct - 1W-2W to schedule test WW31
- Elram - Column wraps 10,24 lines
- RP- FP 5RA- 5E. Chemo racks 1E-1W
- Tzur-Esh - Steel paint 4E-4W
- Megasone - Small wires+ speakers 3E+2E

NTT-E
 WW to finish 5RA missing beams
 NTT-W
 4DA decking

TMT FRP install
 Safety net install

LINK

JUNGLE GYM

JUNGLE GYM

INTERSTITIAL

1E

2E

3E

4E

5E

1W


2W

3W

4W

5W

03
04
05
06
07
08
09
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26
27
28

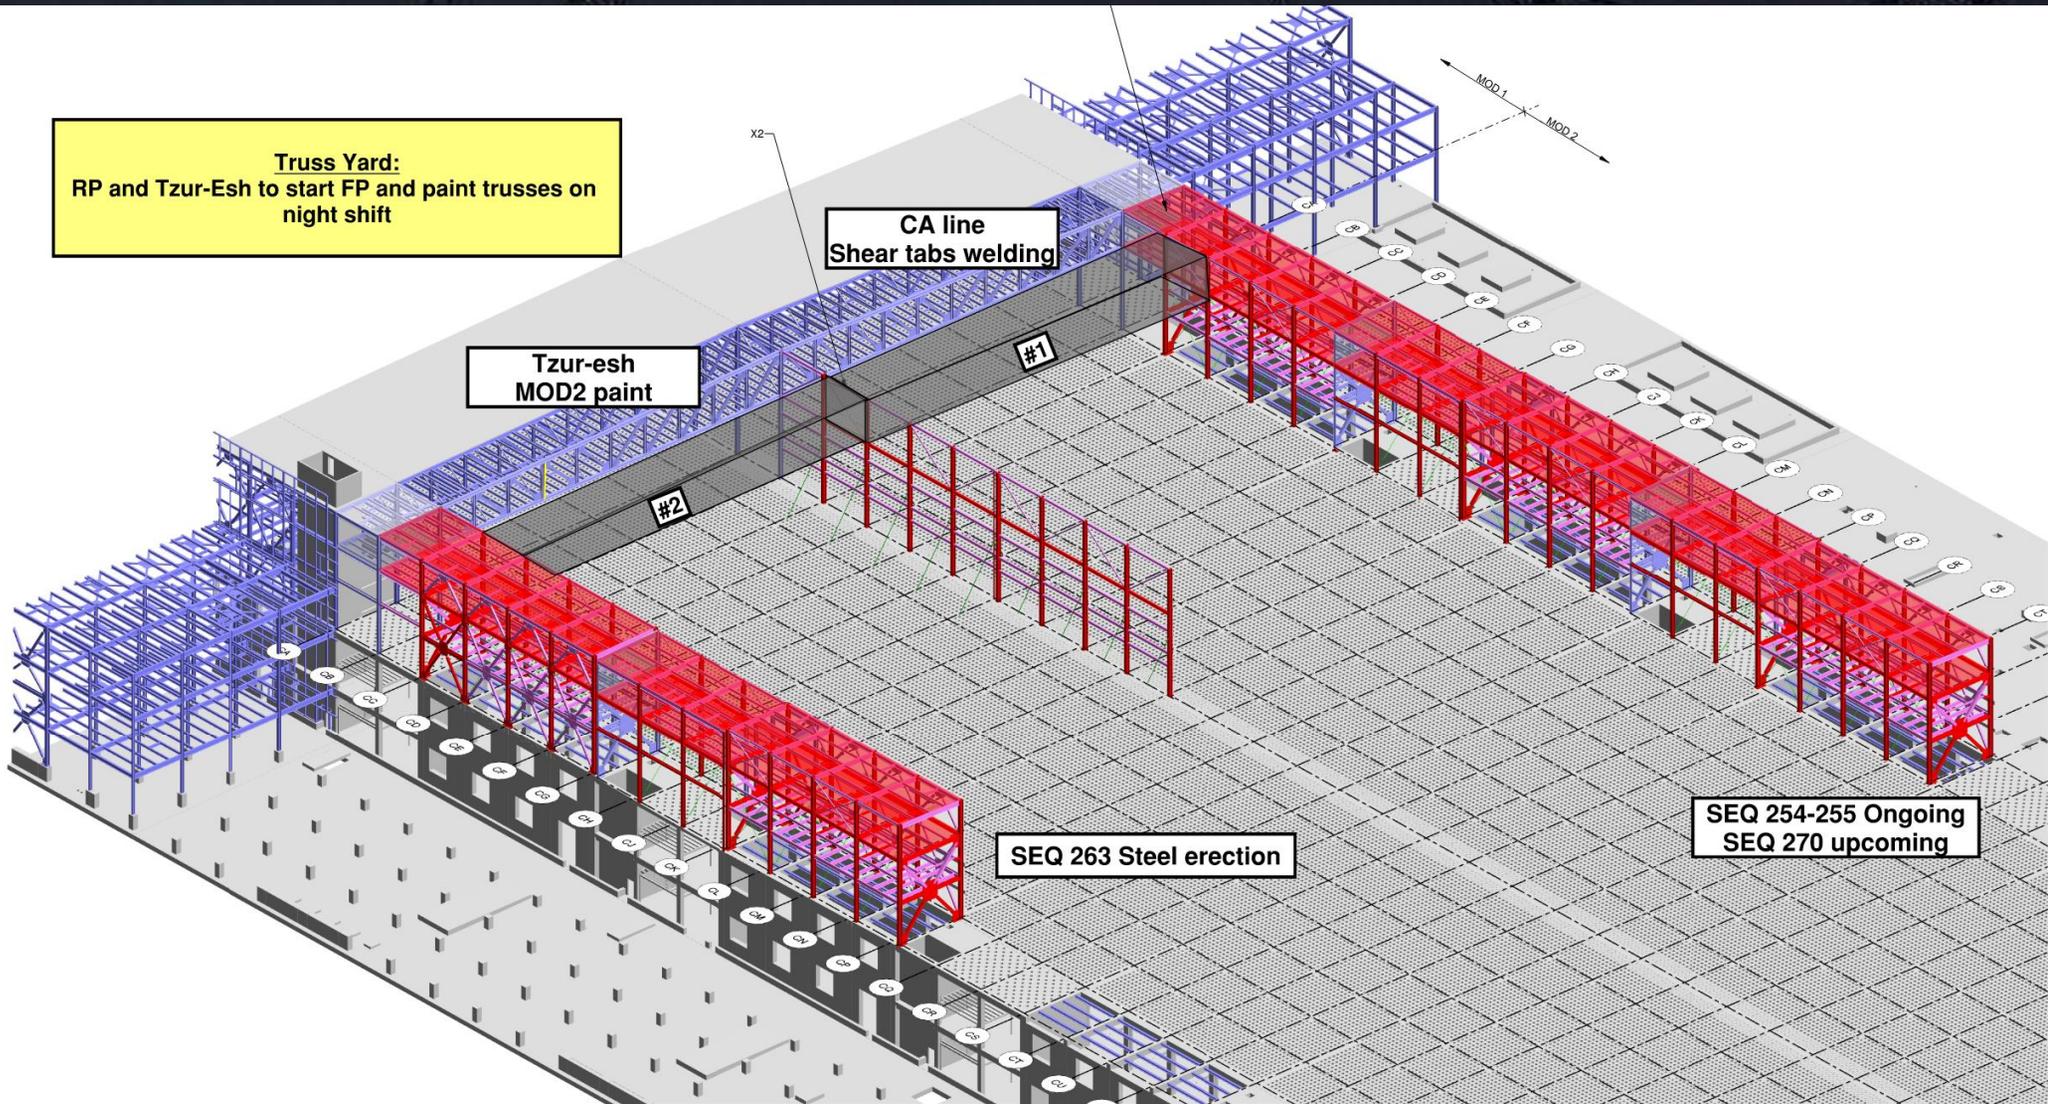

Truss Yard:
RP and Tzur-Esh to start FP and paint trusses on night shift

CA line
Shear tabs welding

Tzur-esh
MOD2 paint

SEQ 263 Steel erection

SEQ 254-255 Ongoing
SEQ 270 upcoming


#2


#1


x2-

MOD 1

MOD 2

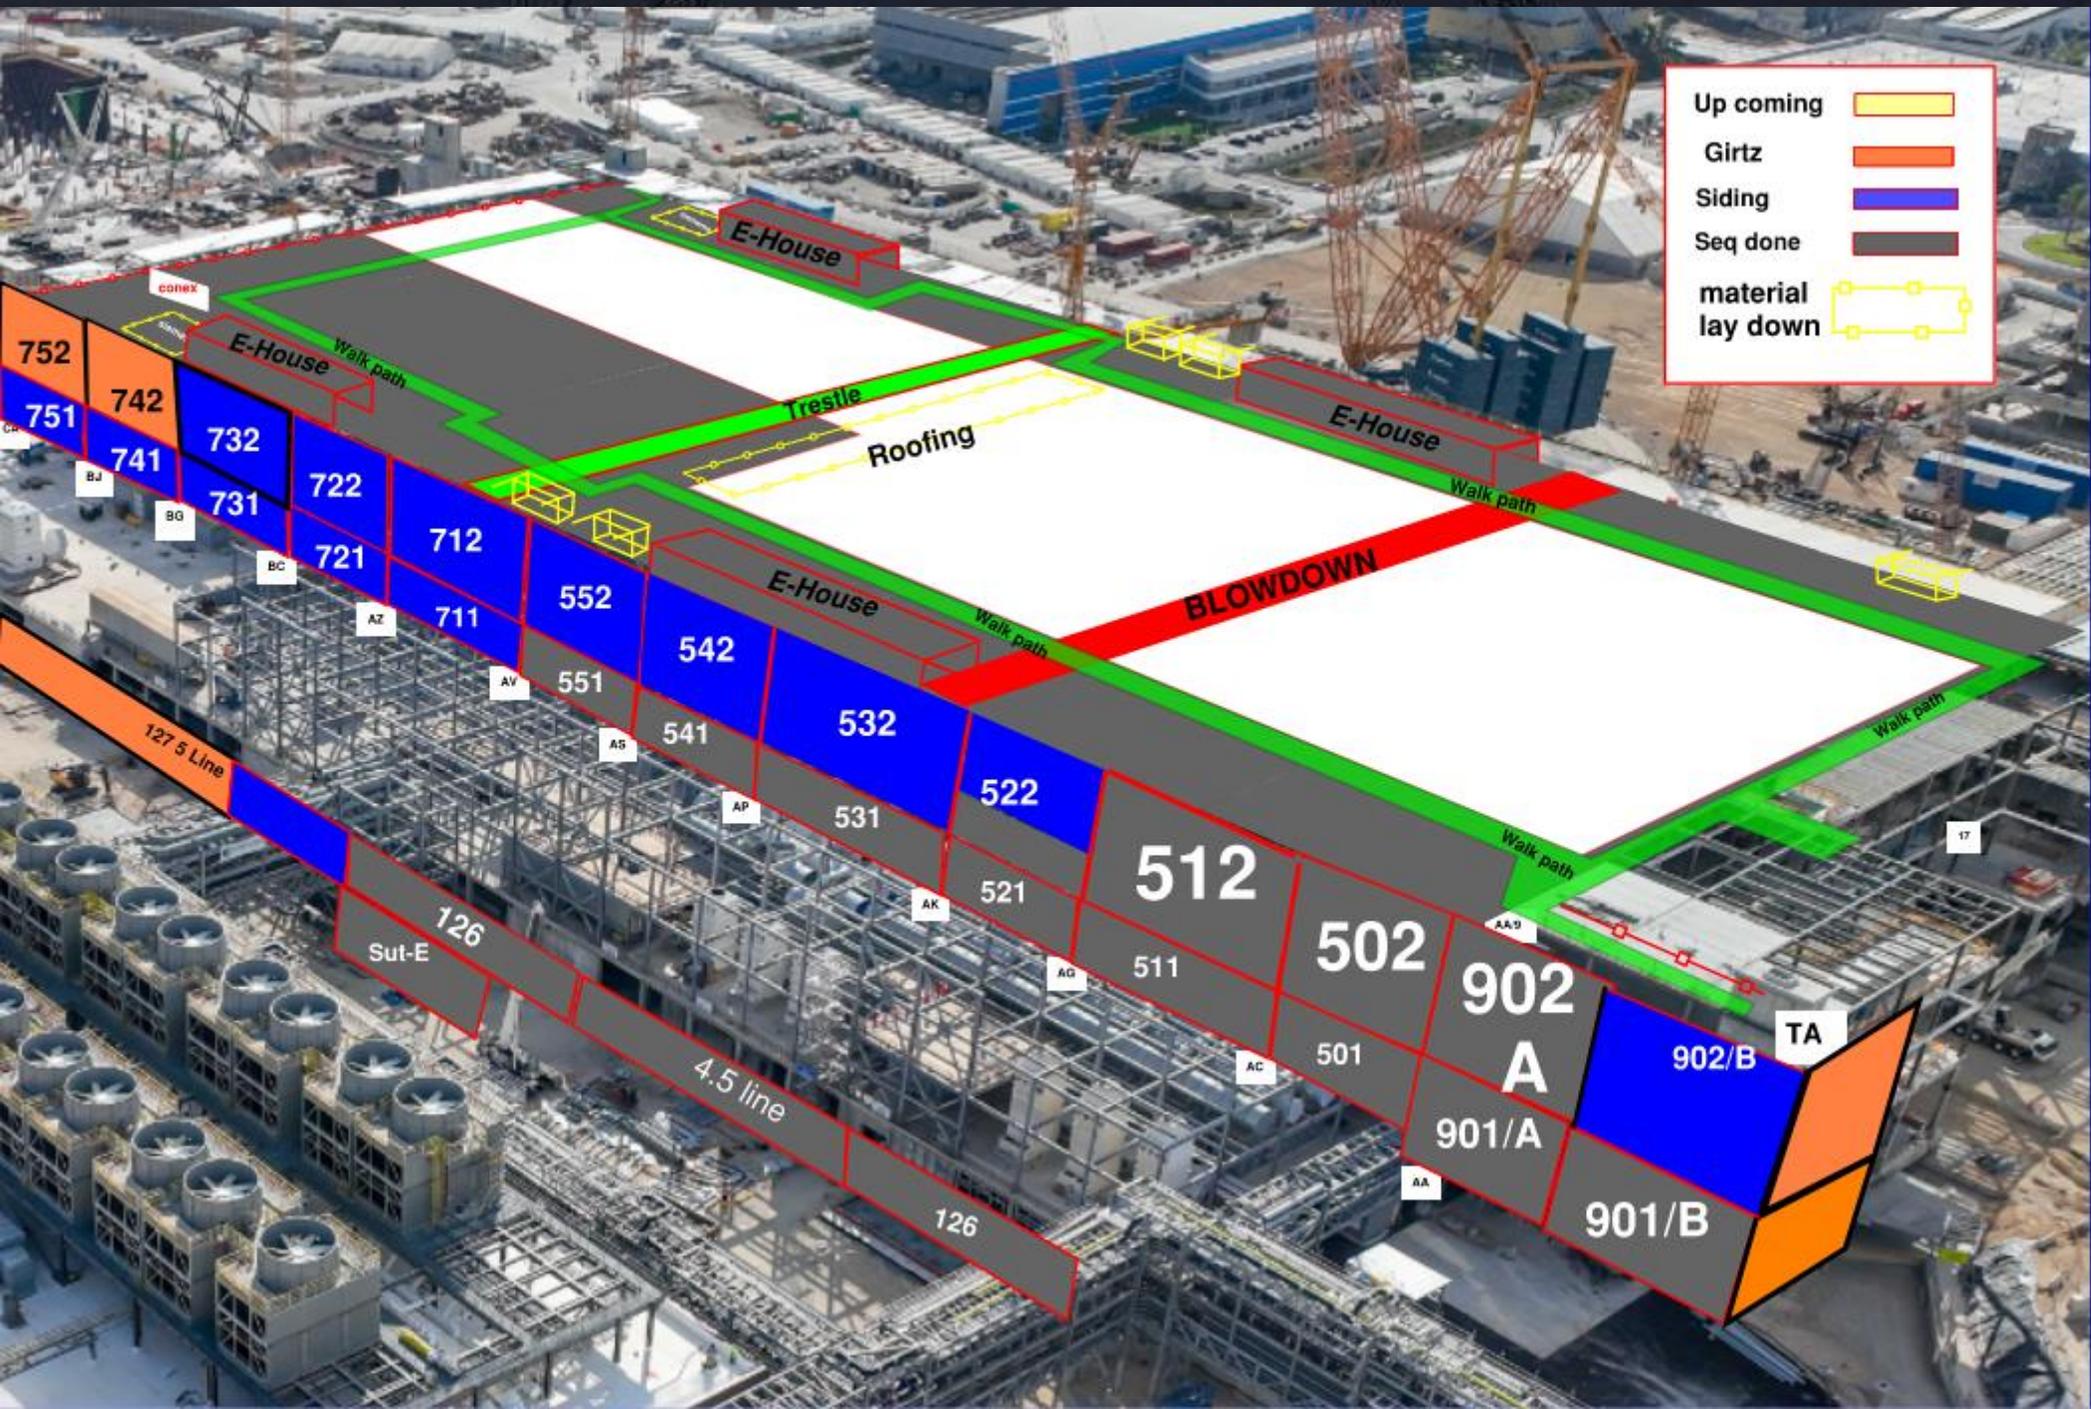

| | |
|-------------------|---|
| Up coming |  |
| Girtz |  |
| Siding |  |
| Seq done |  |
| material lay down |  |

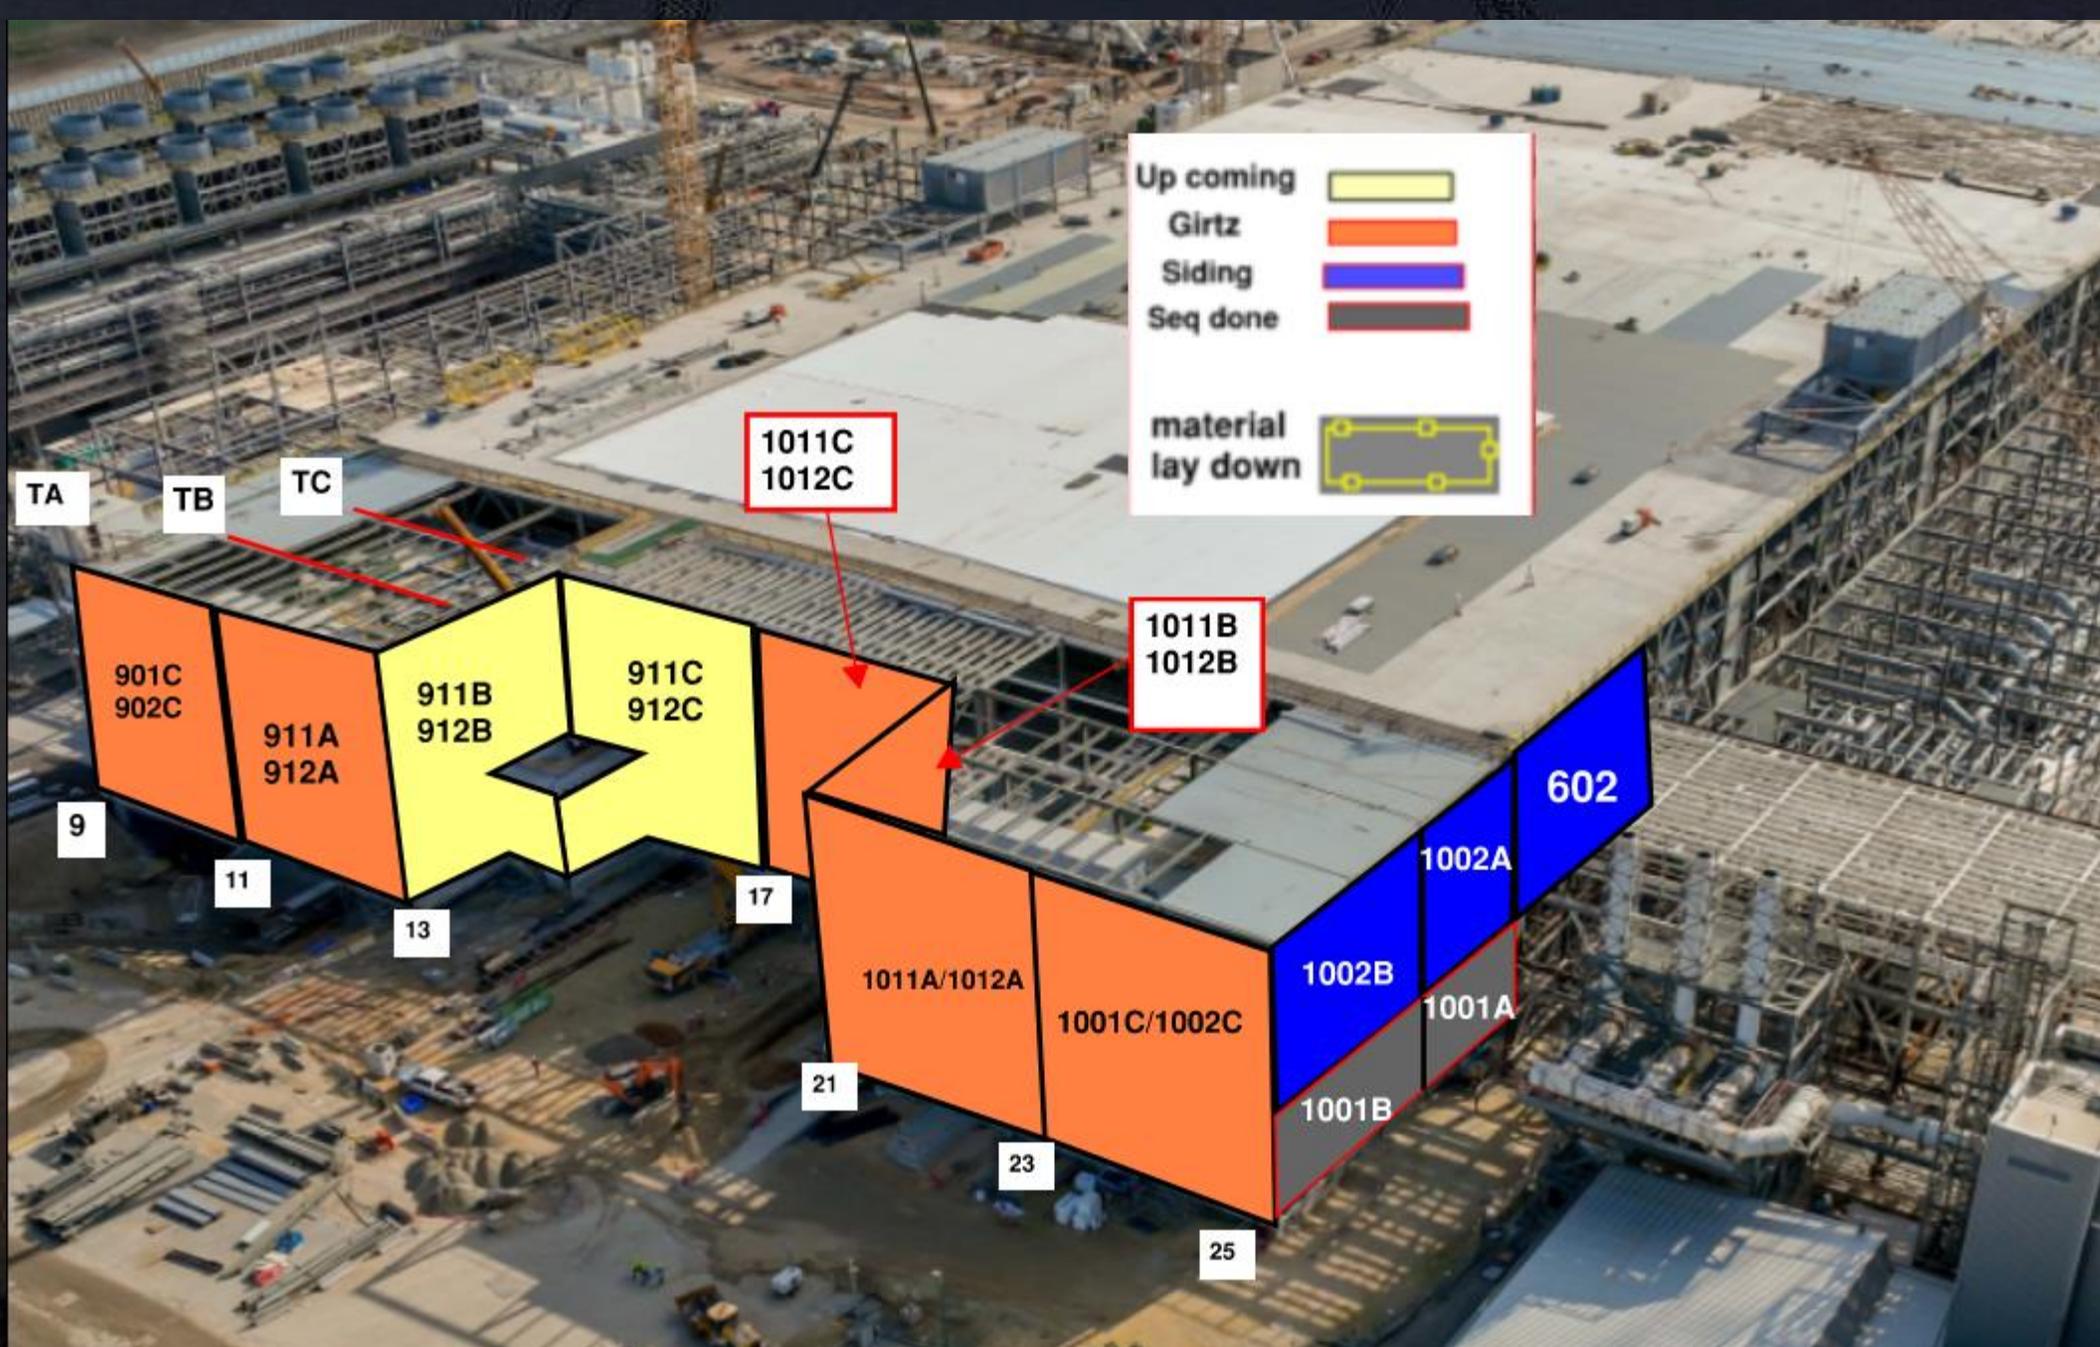

| | |
|-------------------|---|
| Up coming |  |
| Girtz |  |
| Siding |  |
| Seq done |  |
| material lay down |  |

TA

TB

TC

1011C
1012C

1011B
1012B

9

11

13

17

21

23

25

901C
902C

911A
912A

911B
912B

911C
912C

1011A/1012A

1001C/1002C


1002B

1001A

1001B

602


1002A

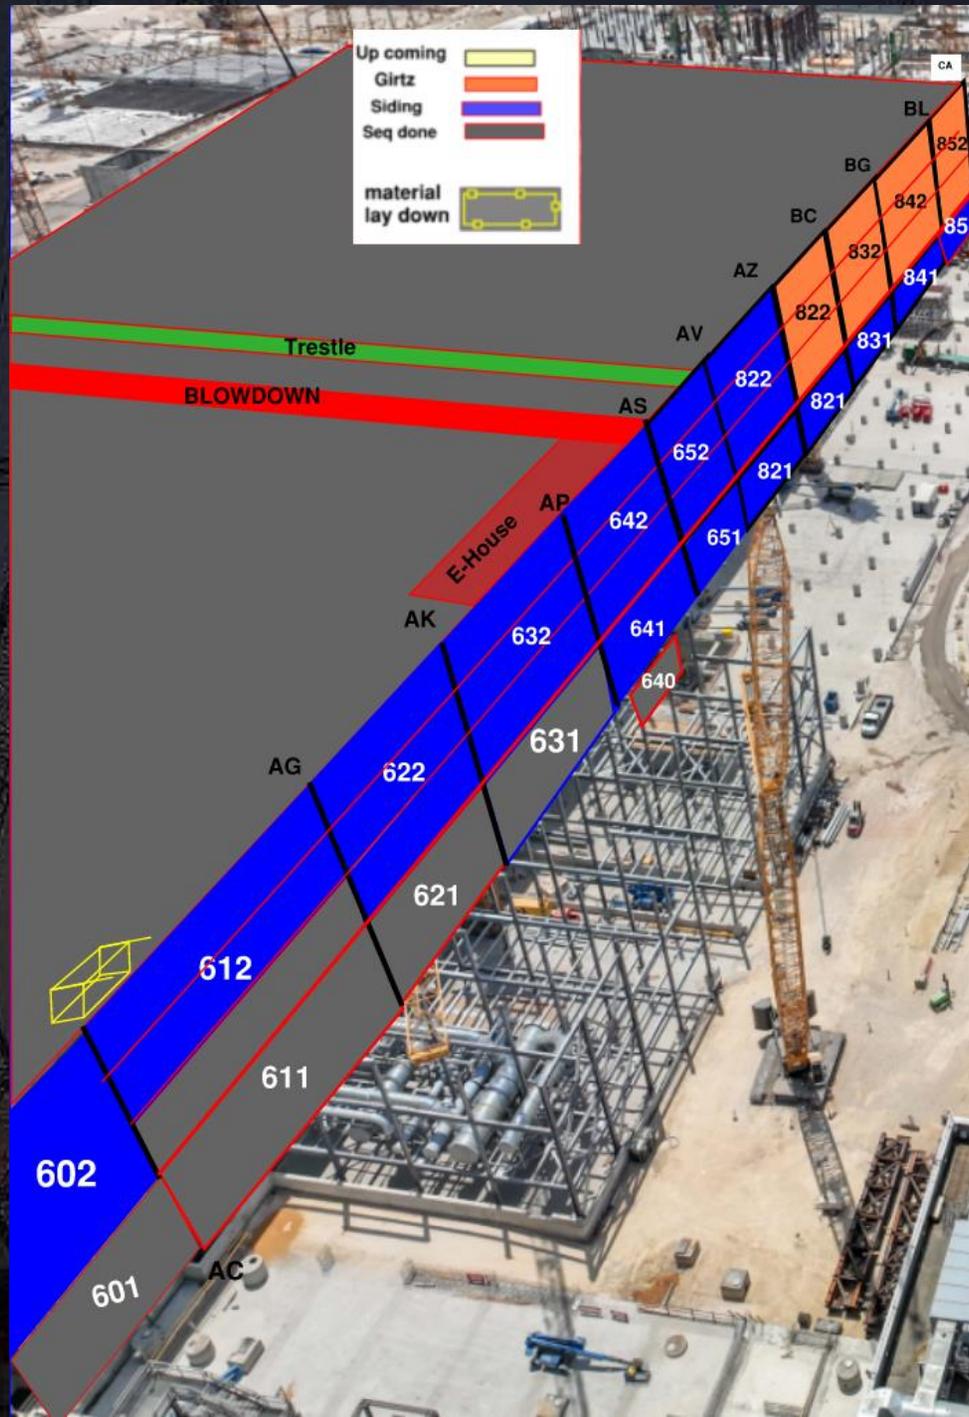

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

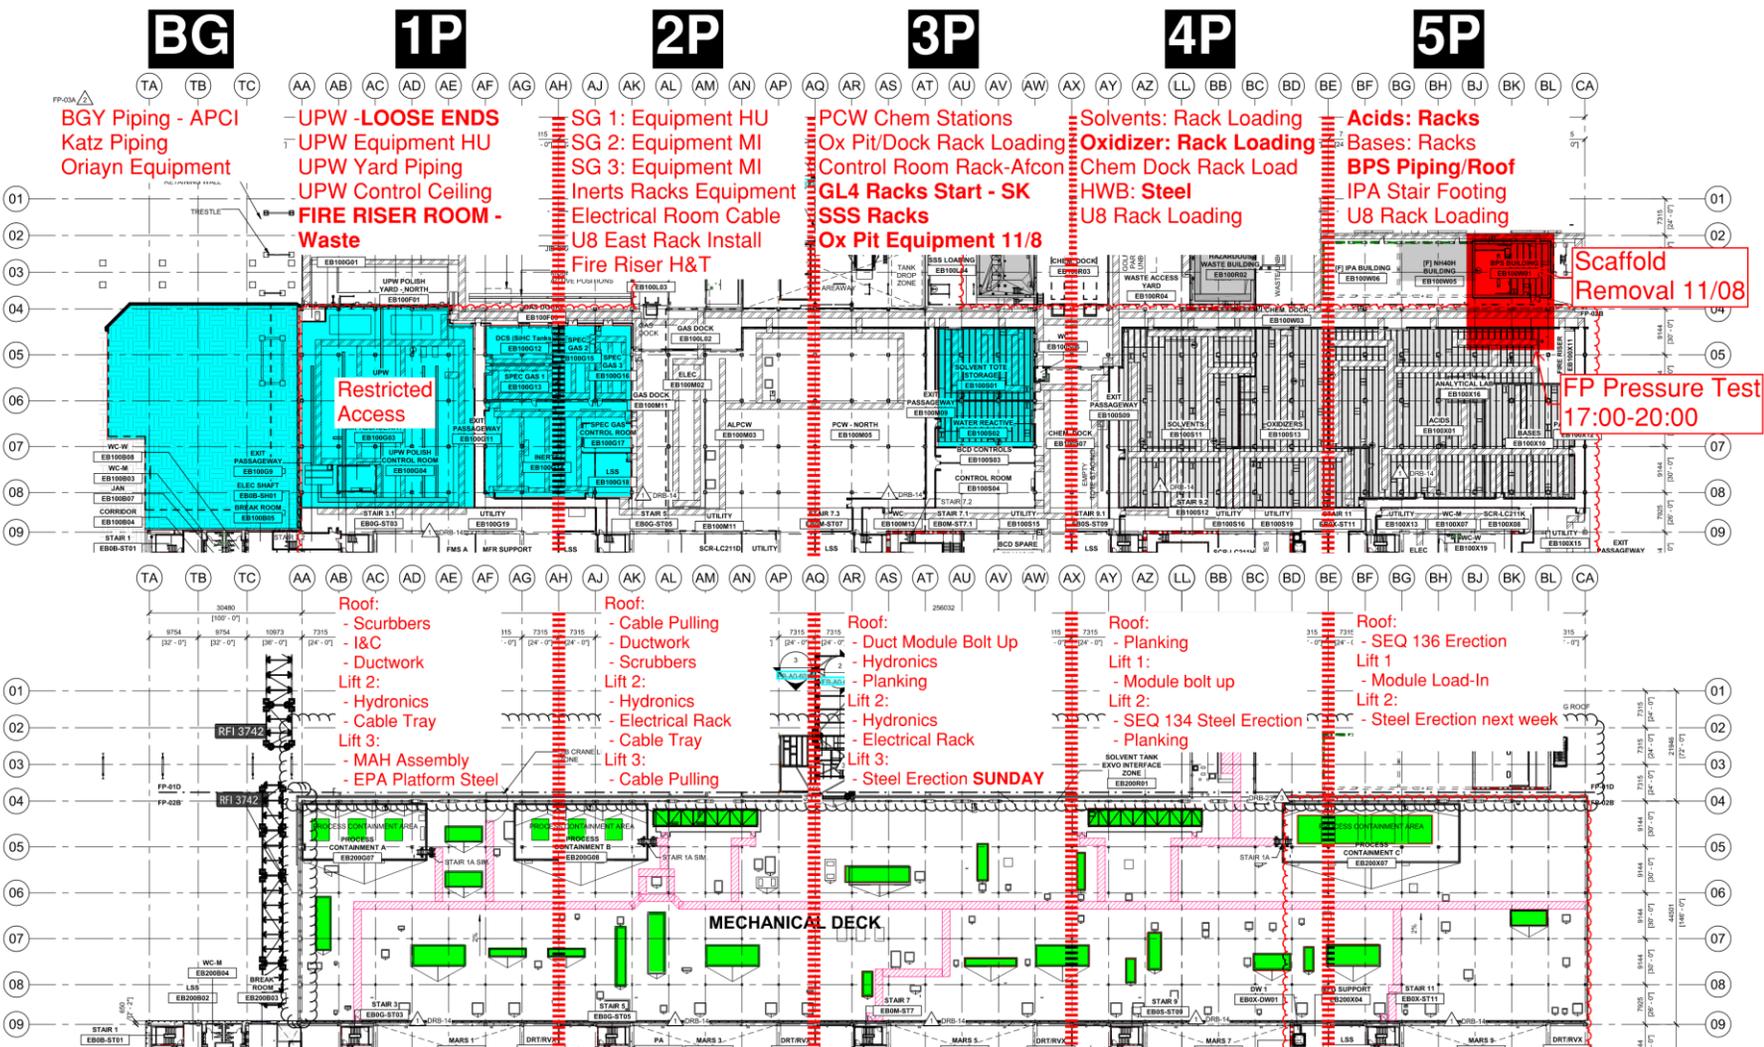


WJG 01J, 02J LIFT 2 & 3





WJG 03J, 04J, 05J LIFT 2 & 3

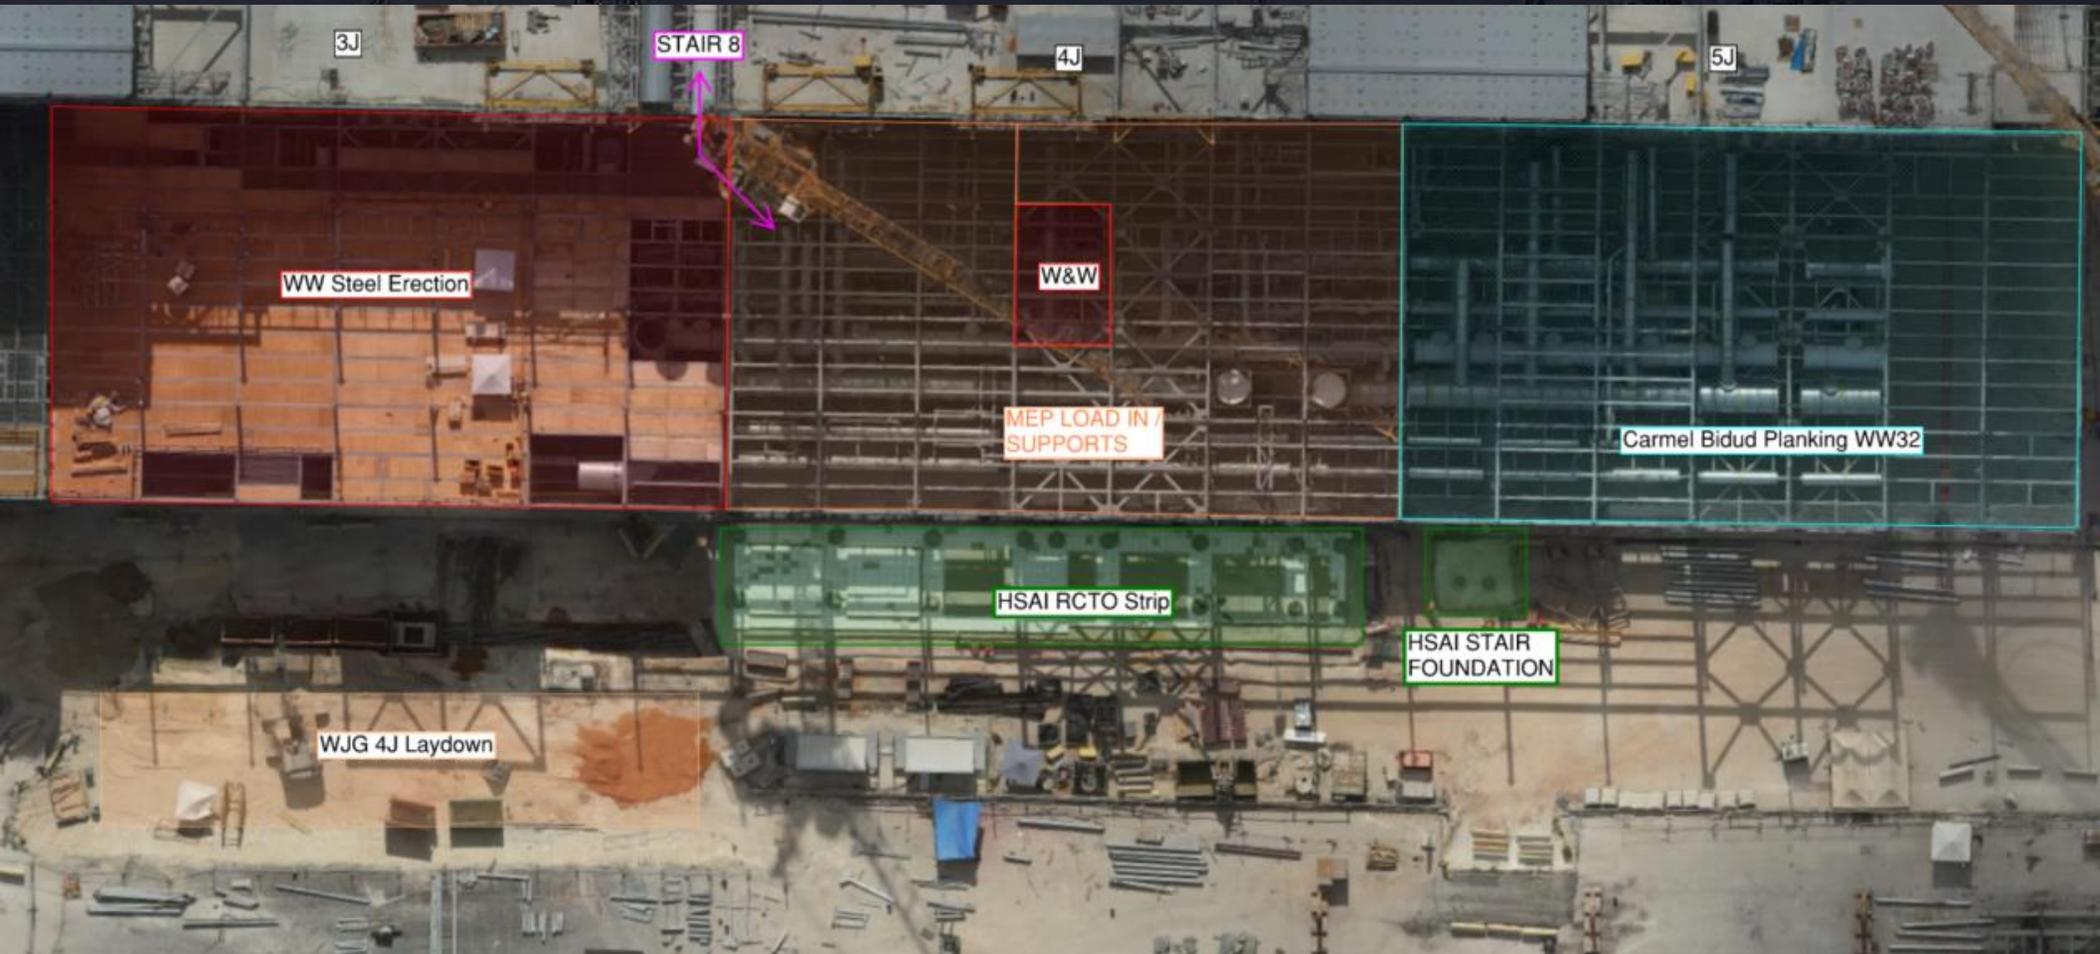


WJG UTILITY LEVEL BUILD OUT

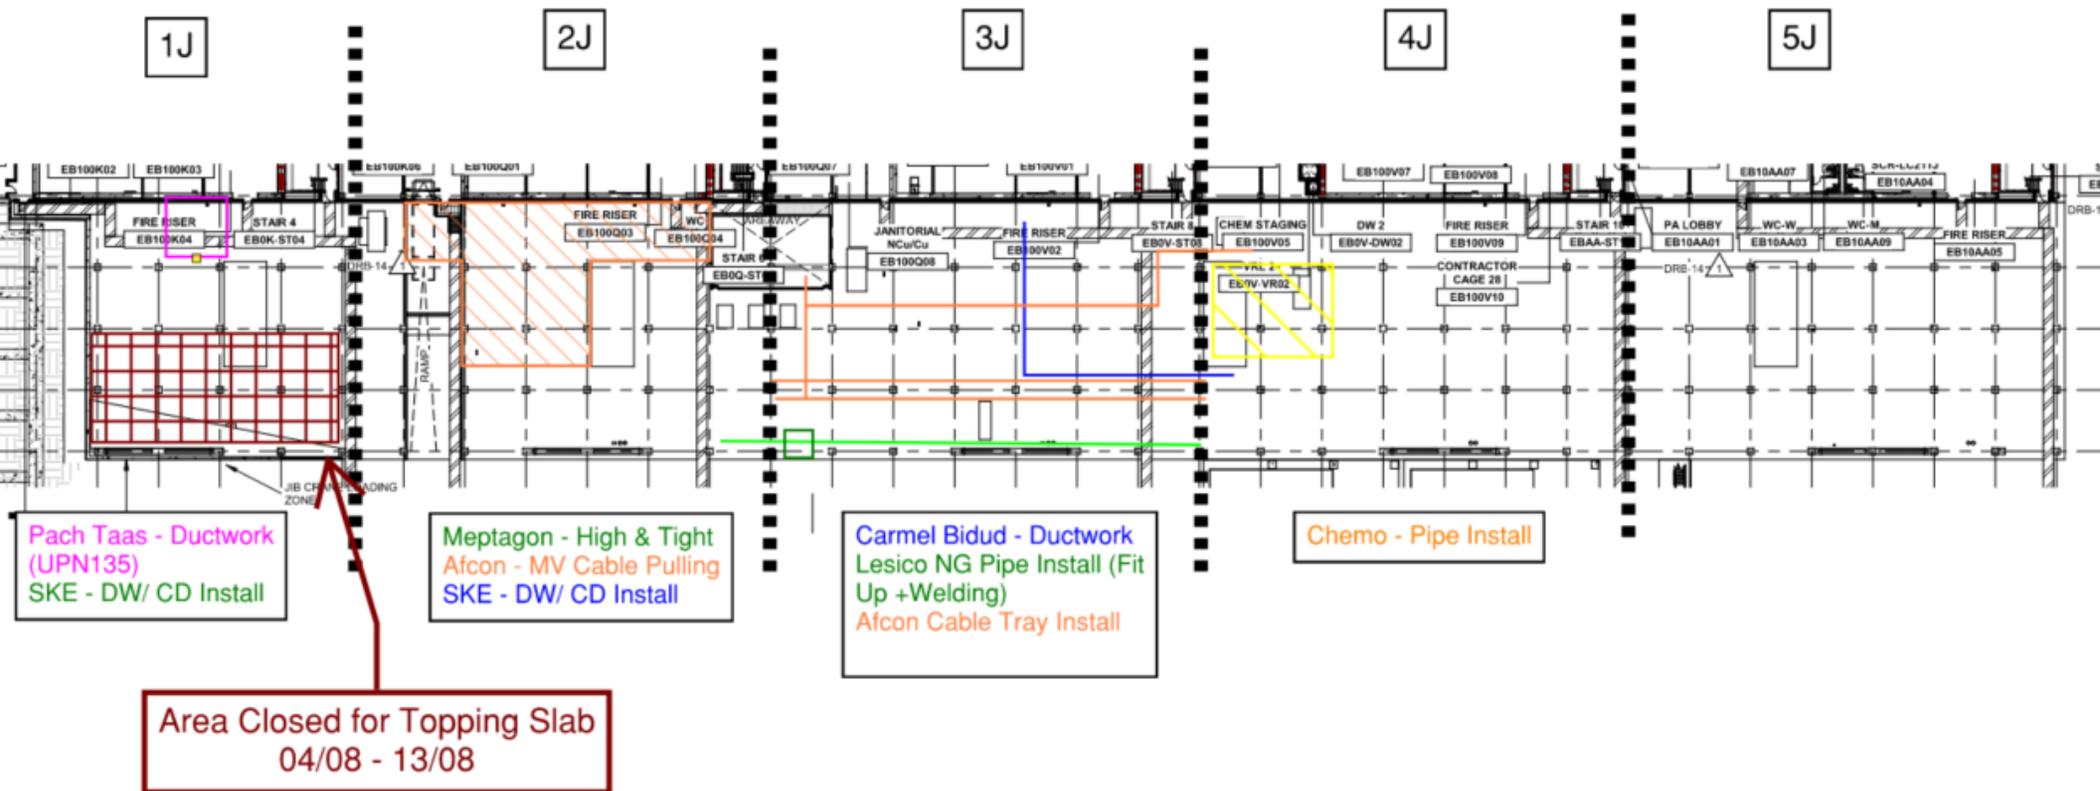

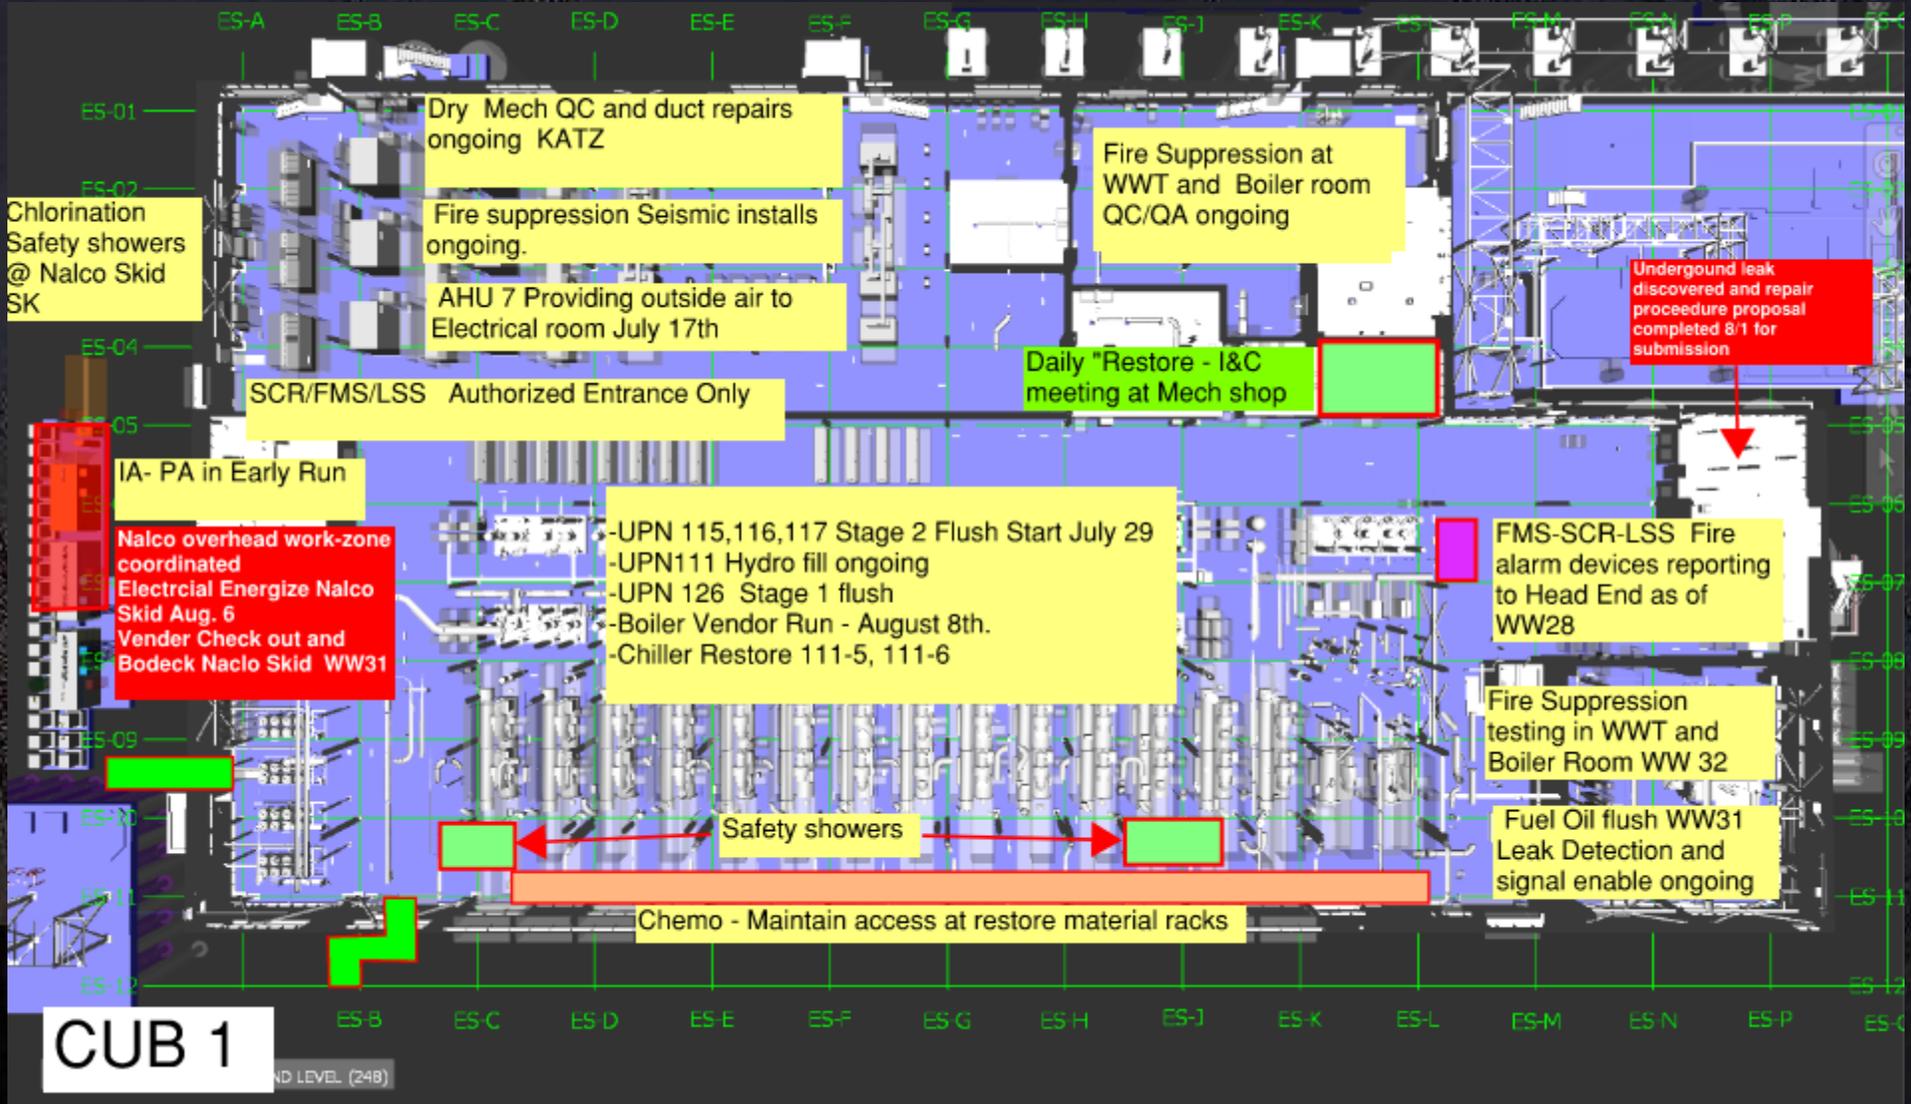

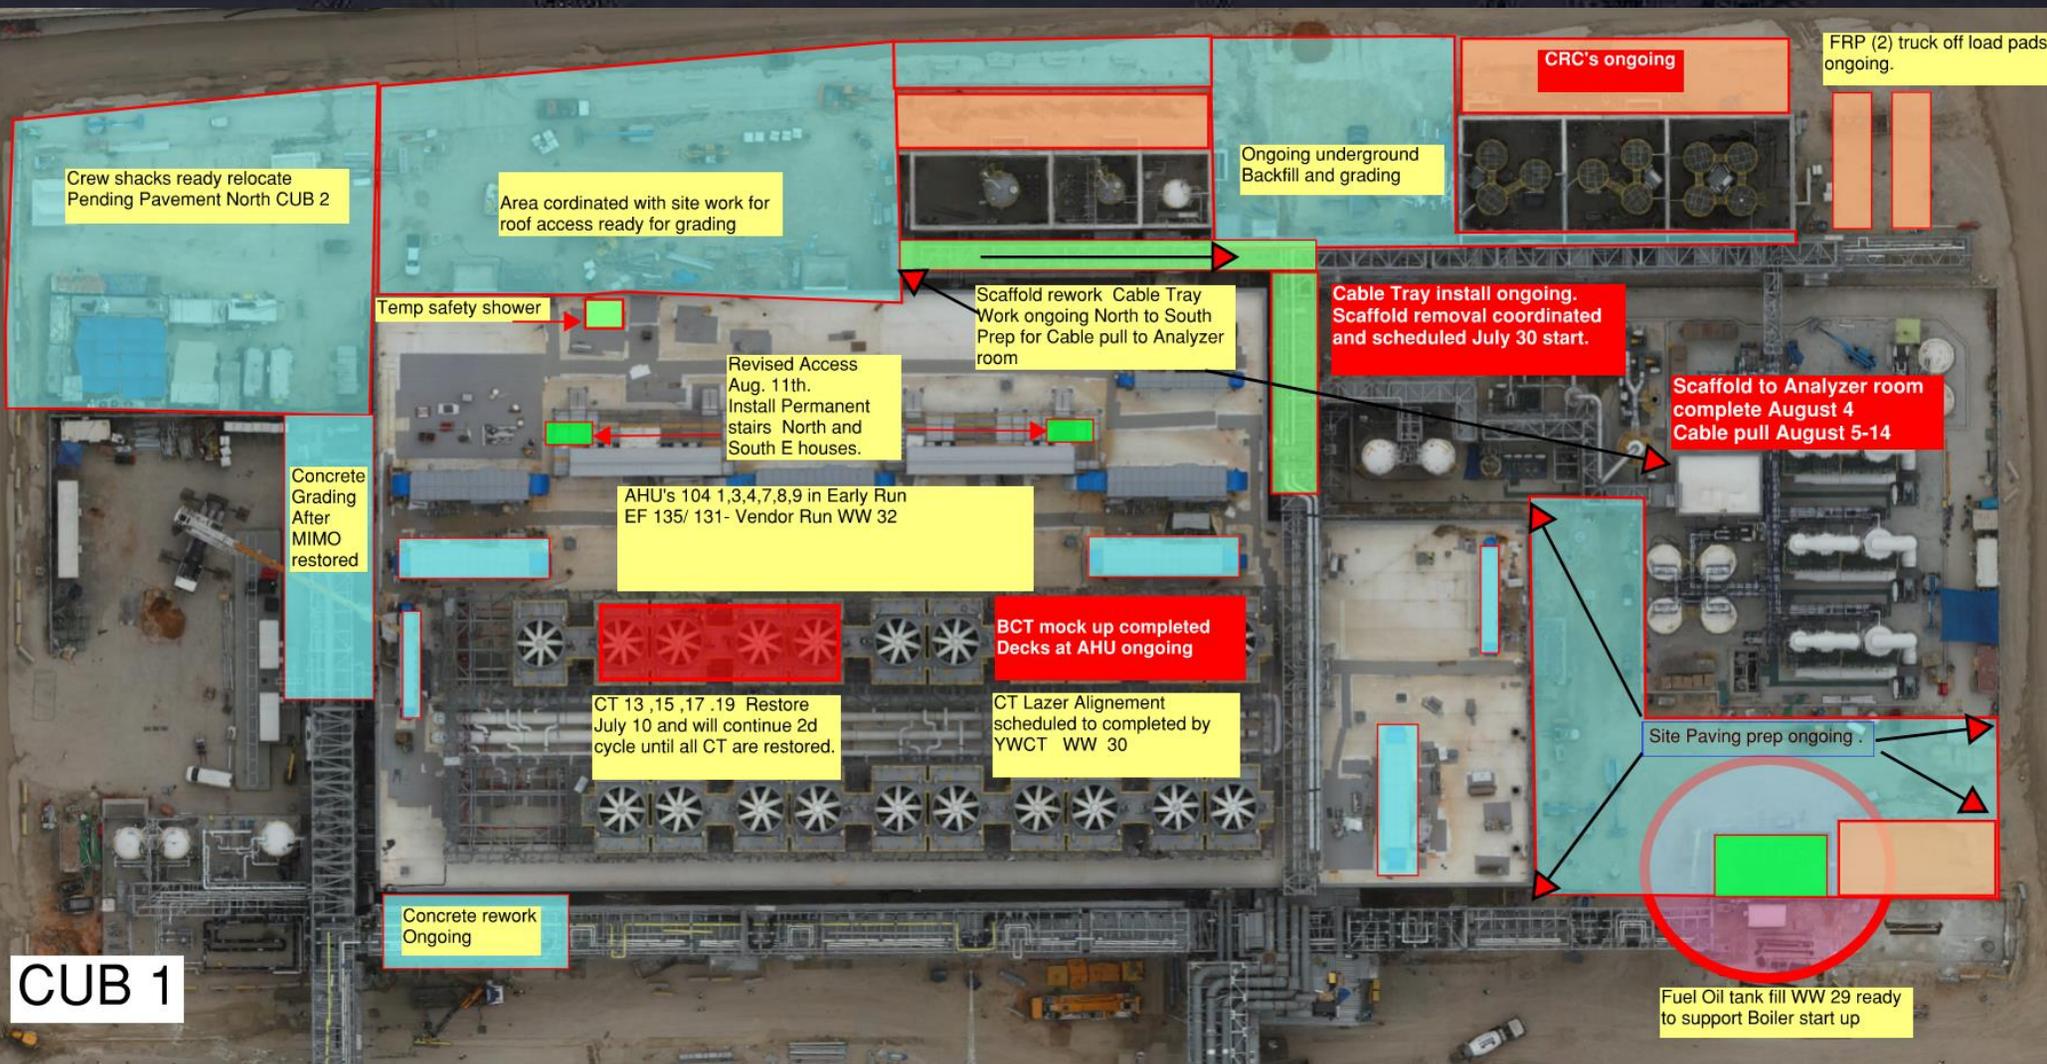

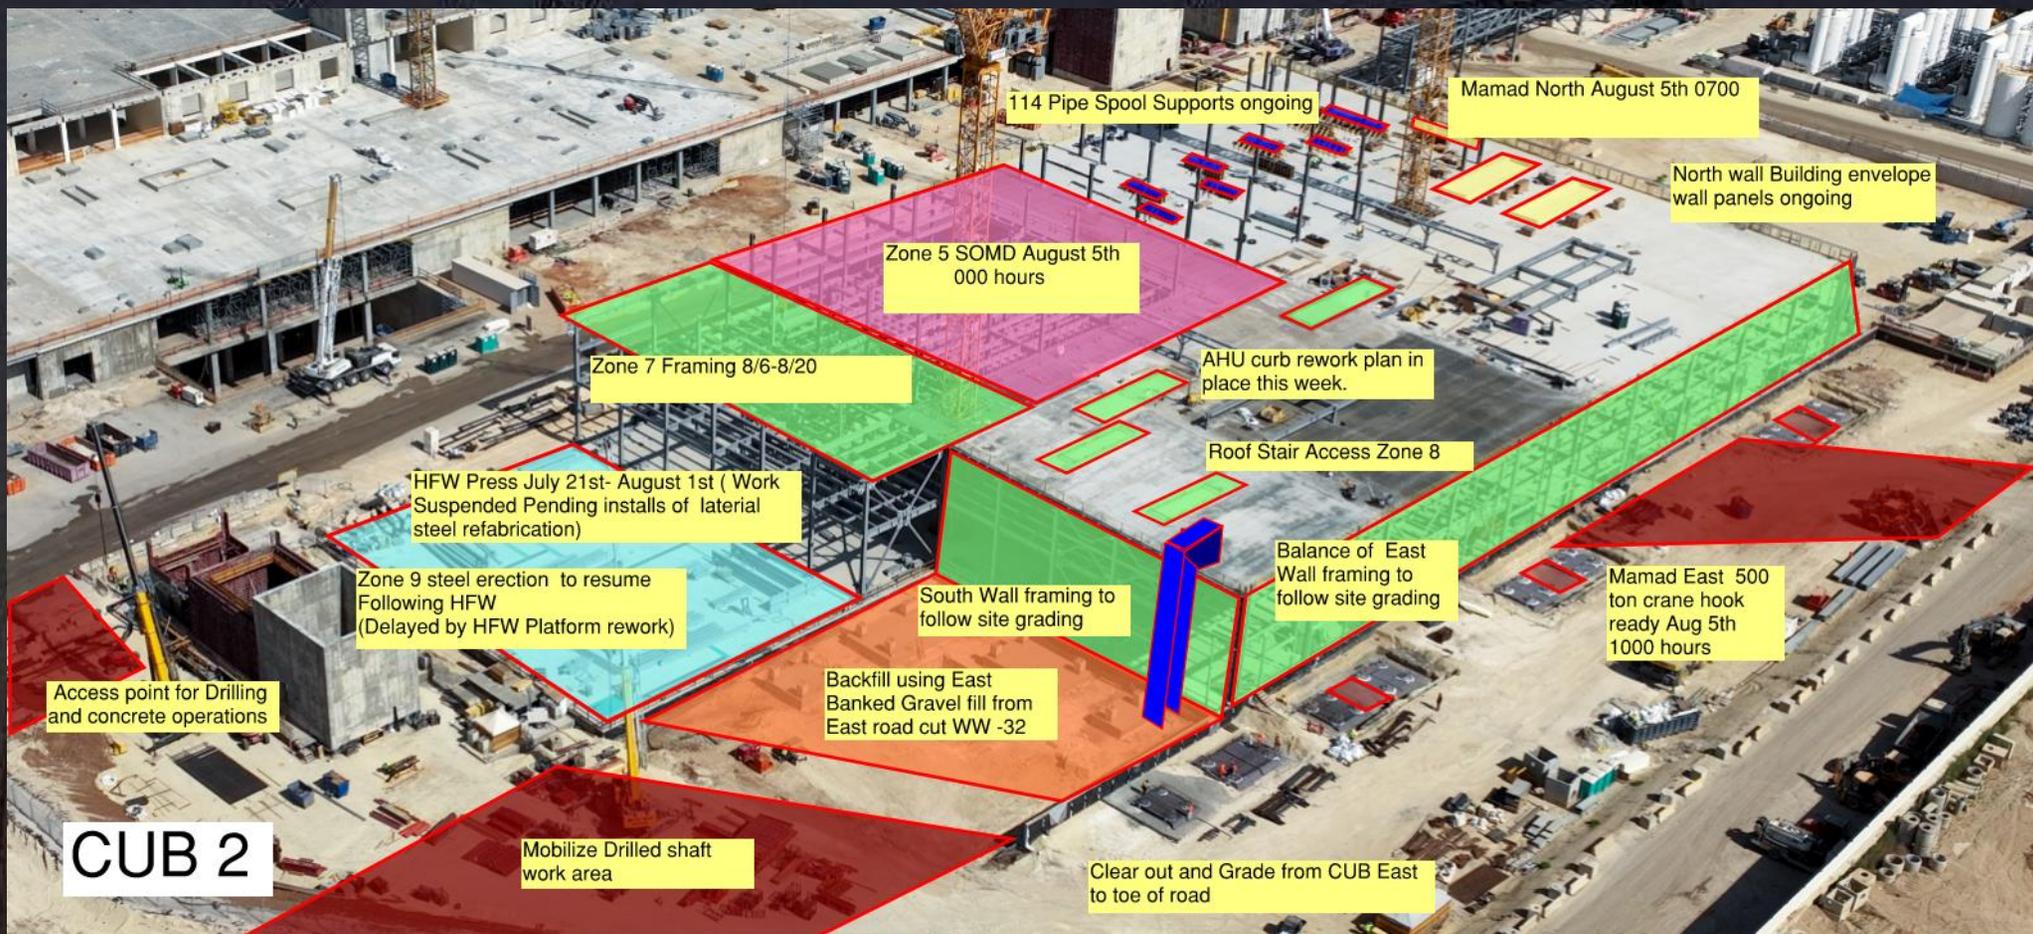

114 Pipe Spool Supports ongoing

Mamad North August 5th 0700

North wall Building envelope wall panels ongoing

Zone 5 SOMD August 5th 000 hours

Zone 7 Framing 8/6-8/20

AHU curb rework plan in place this week.

Roof Stair Access Zone 8

HFW Press July 21st- August 1st (Work Suspended Pending installs of lateral steel refabrication)

Balance of East Wall framing to follow site grading

Mamad East 500 ton crane hook ready Aug 5th 1000 hours

Zone 9 steel erection to resume Following HFW (Delayed by HFW Platform rework)

South Wall framing to follow site grading


Access point for Drilling and concrete operations

Backfill using East Banked Gravel fill from East road cut WW -32

CUB 2


Mobilize Drilled shaft work area


Clear out and Grade from CUB East to toe of road

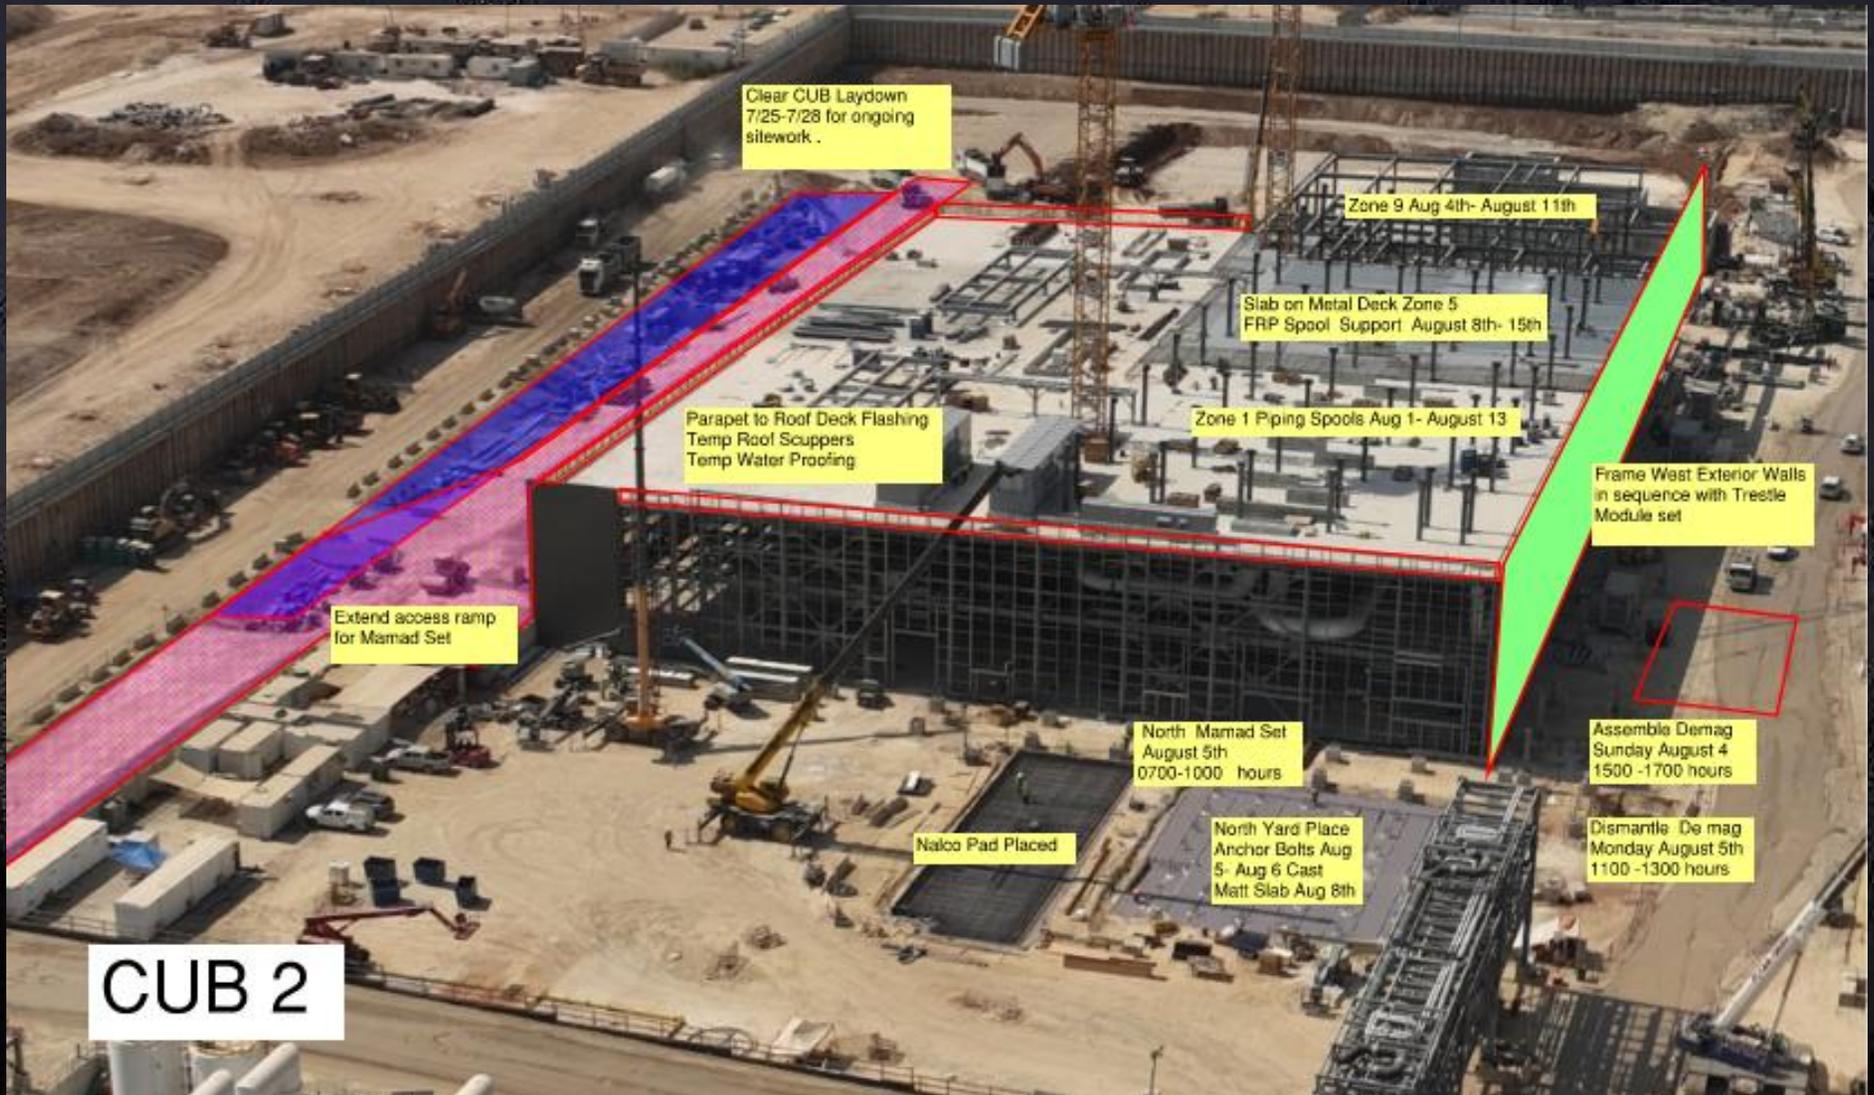

INSTRUMENT AIR PRESSURE TEST - NORTH YARD CUB1 - 17:00-22:00 - AUGUST 7TH

EXCLUSION ZONE

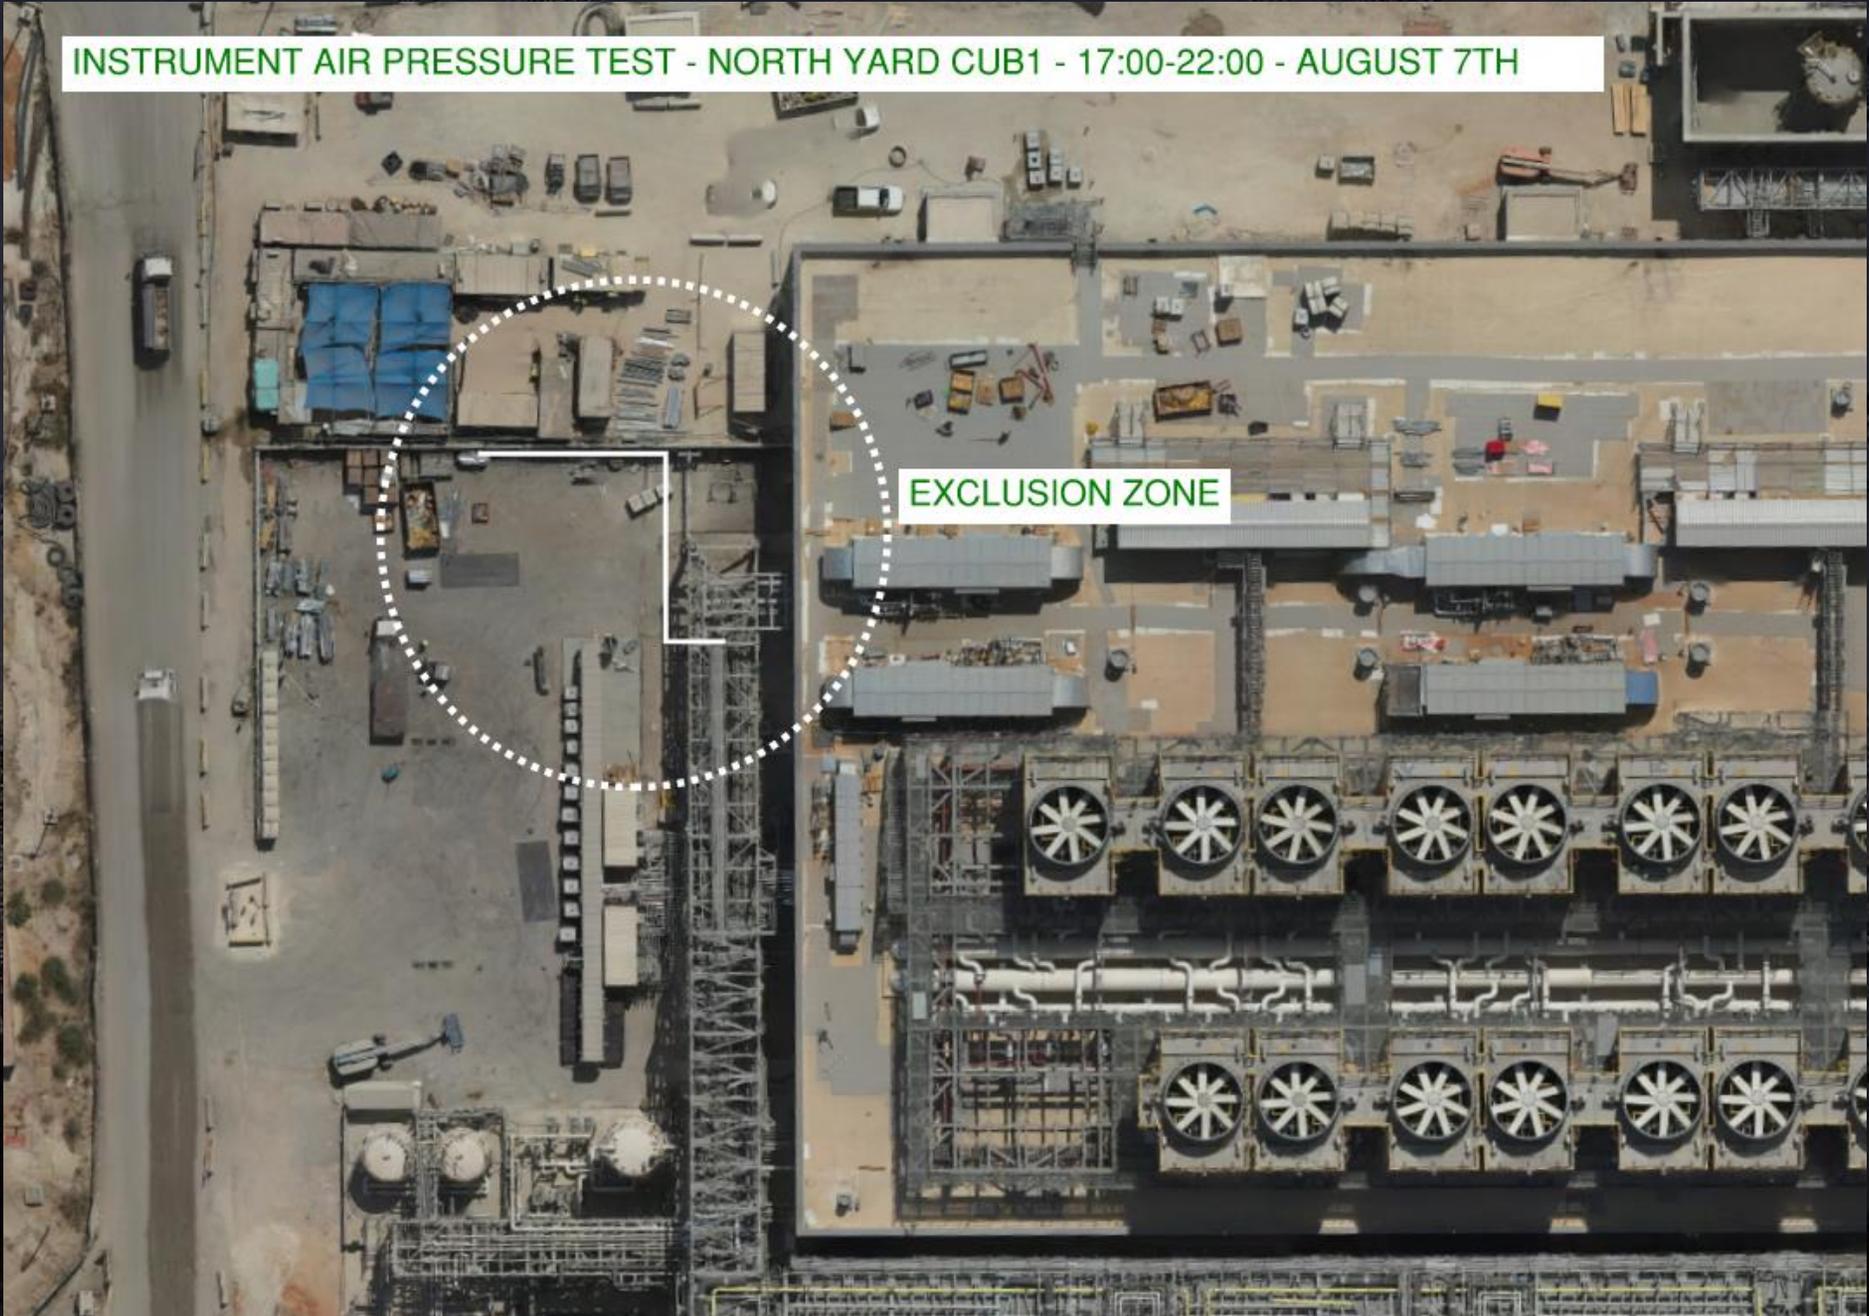

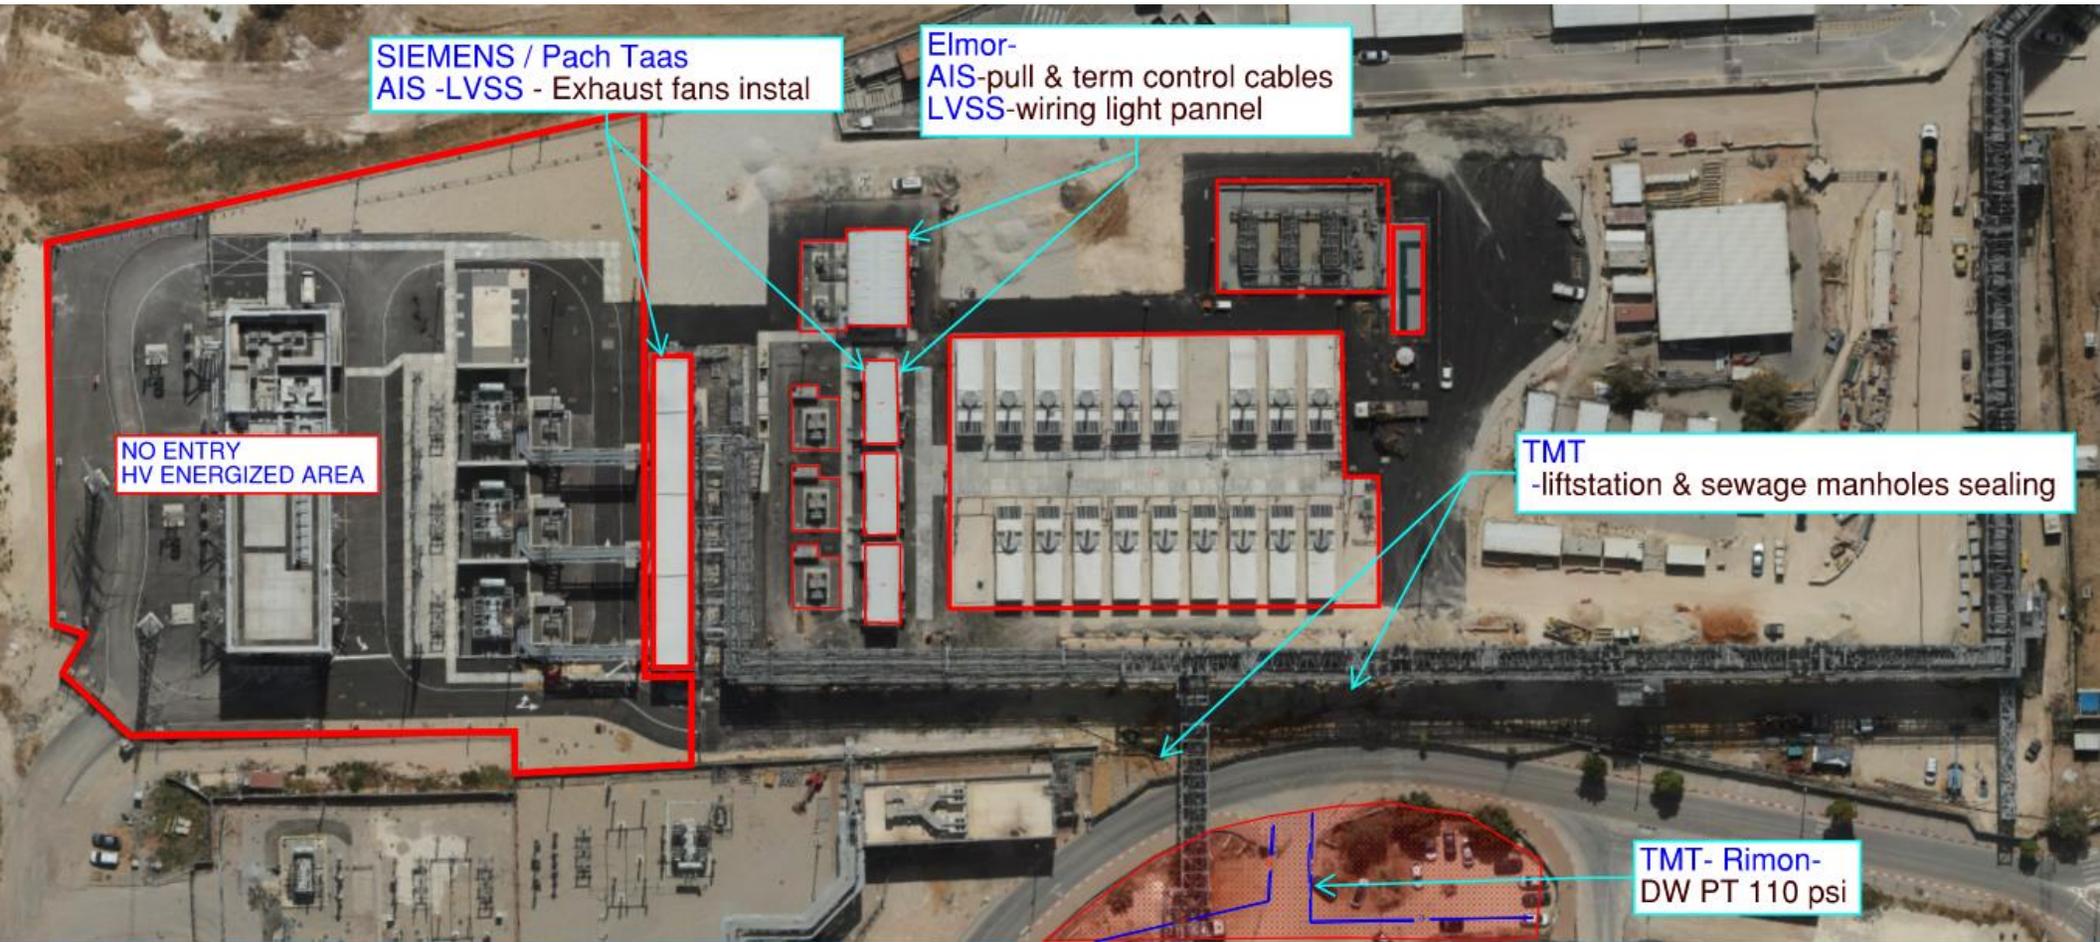

SIEMENS / Pach Taas
AIS -LVSS - Exhaust fans instal

Elmor-
AIS-pull & term control cables
LVSS-wiring light panel

NO ENTRY
HV ENERGIZED AREA


TMT
-liftstation & sewage manholes sealing

TMT- Rimon-
DW PT 110 psi




Trestle - MOD 2 Steel erection


T-17 Lvl 1

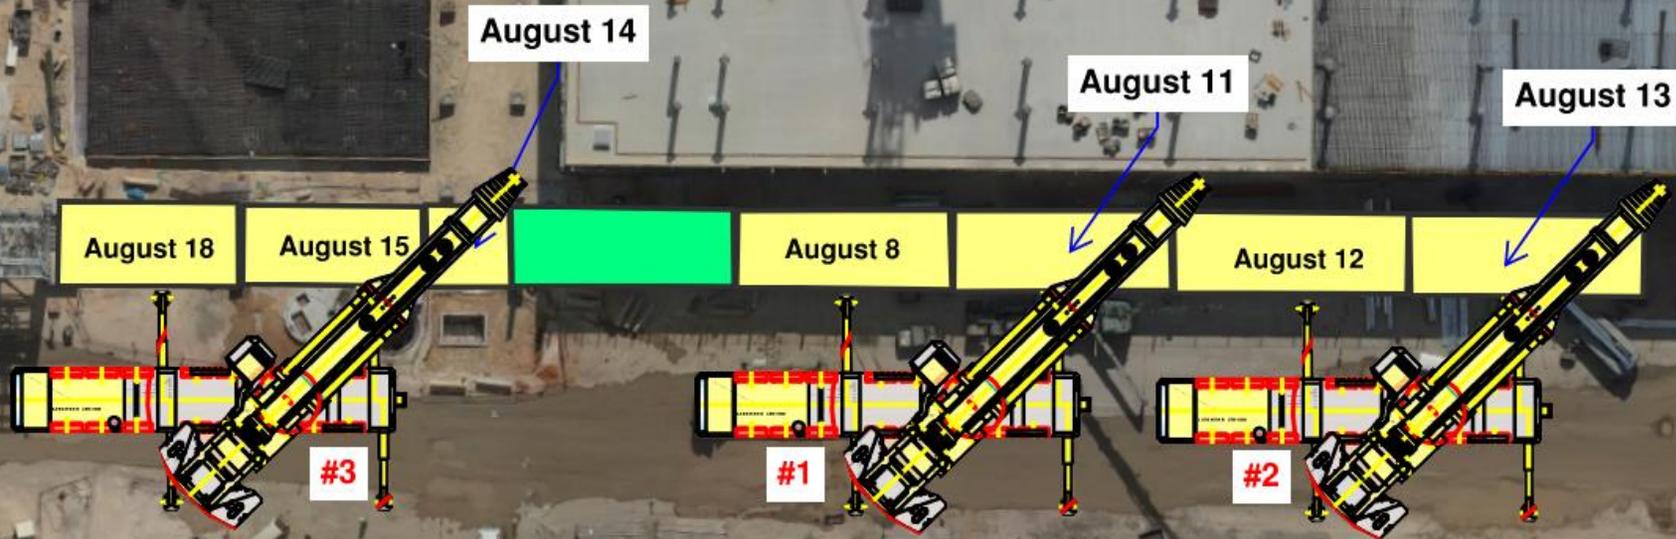

Trestle - MOD 2 Steel erection

T-17 Lvl 2

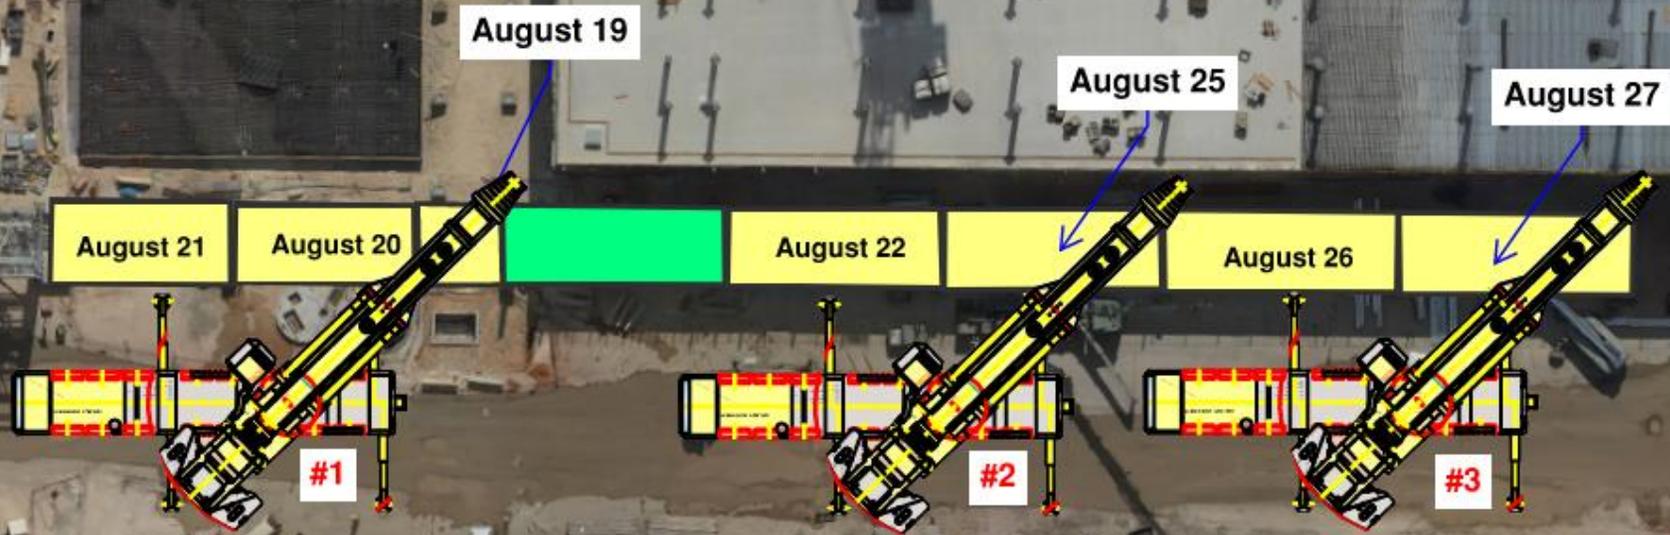




HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

BSGS

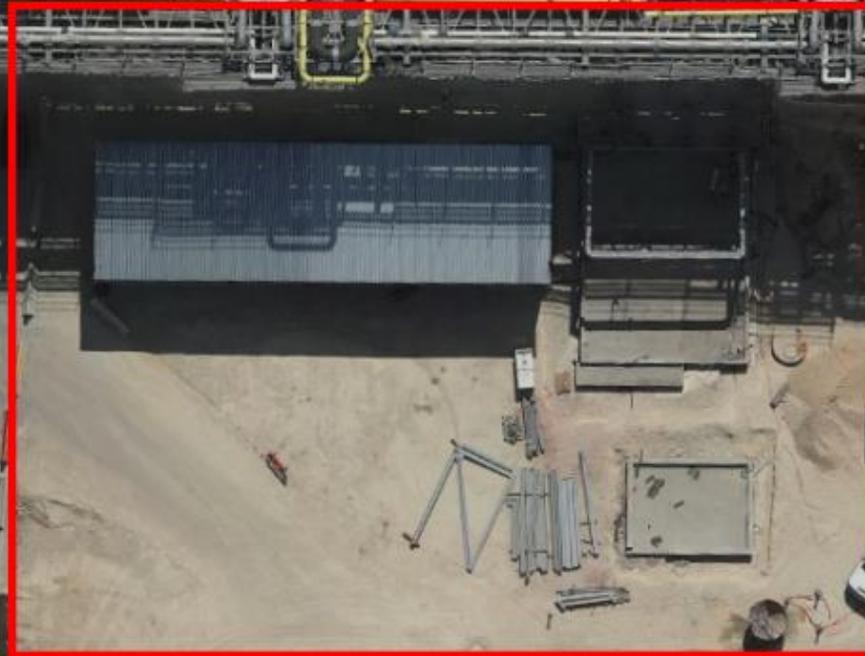


From main kiosk

Site temporary power

Legend :

- 22KV Line
- 400V Line
- 109 - Kiosk

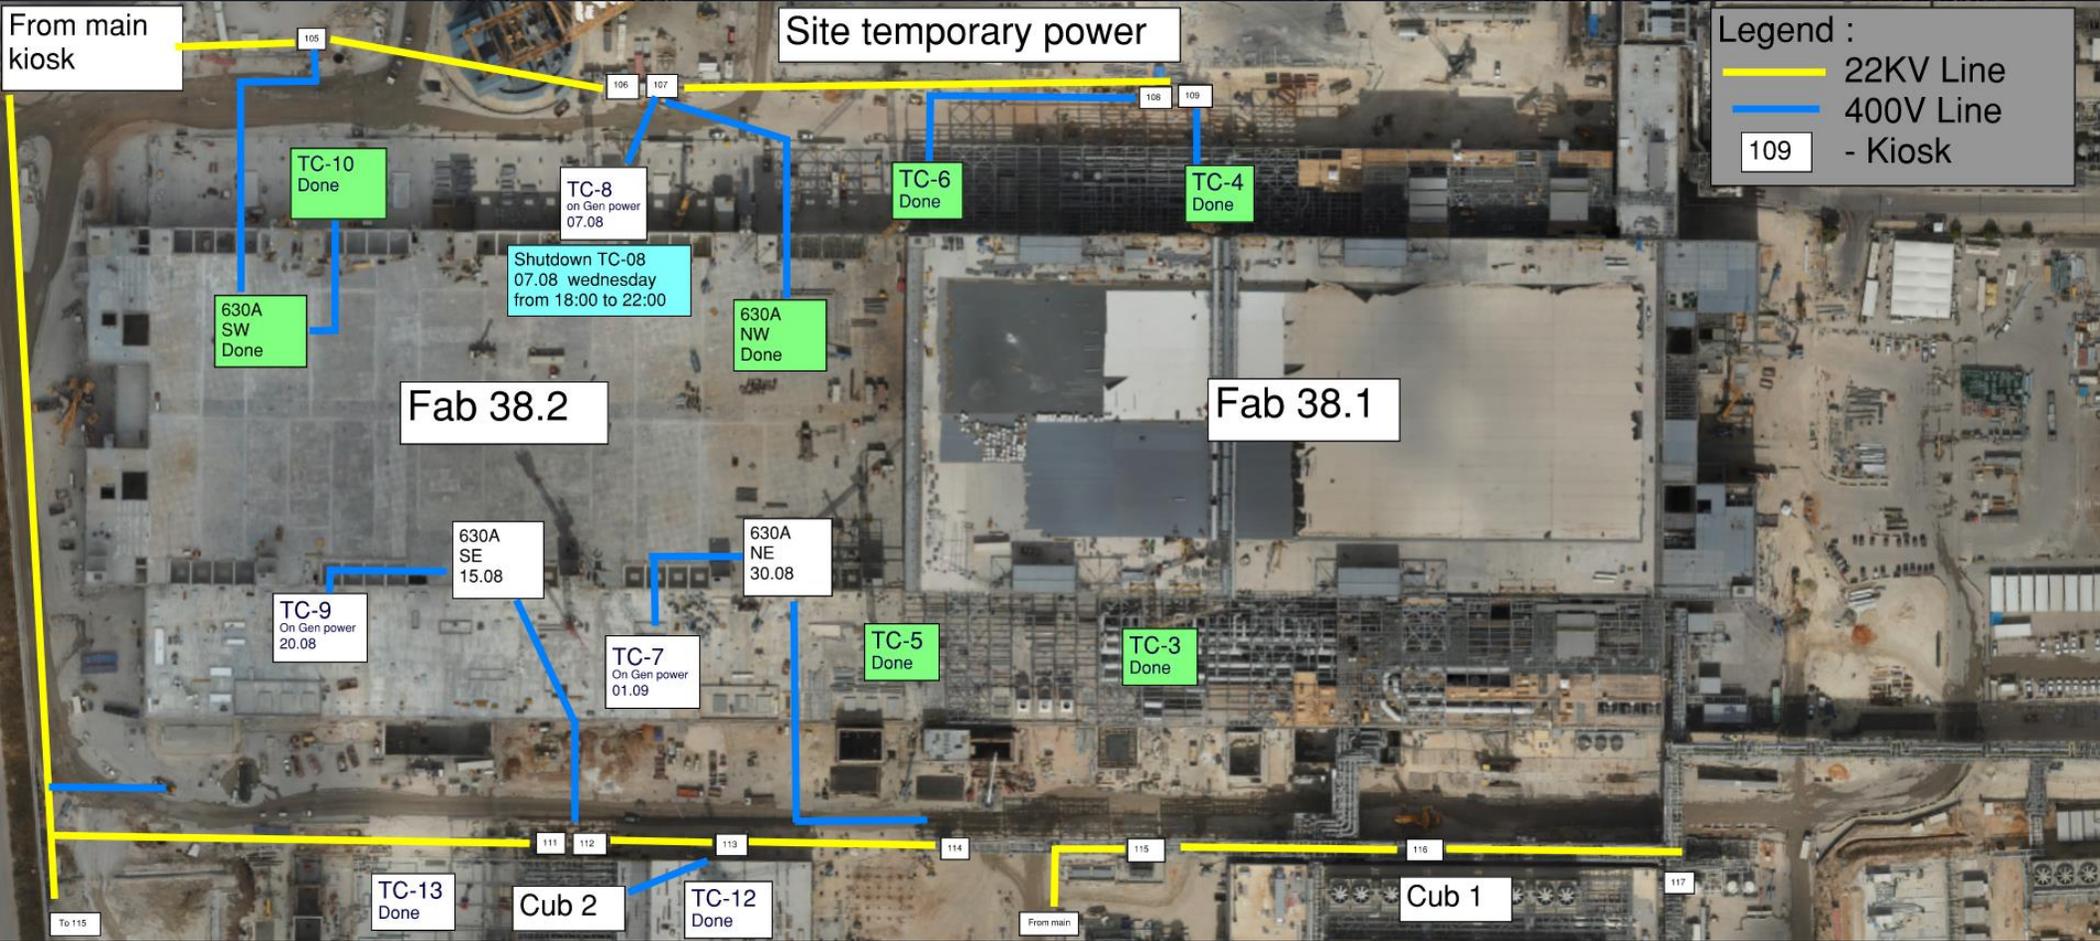

Fab 38.2

Fab 38.1

Cub 2

Cub 1

630A SE
15.08

630A NE
30.08

TC-8
on Gen power
07.08

TC-9
On Gen power
20.08

TC-7
On Gen power
01.09

TC-10
Done

TC-5
Done

TC-3
Done

TC-6
Done

TC-4
Done

630A SW
Done

630A NW
Done

TC-13
Done

TC-12
Done


To 115

From main

Shutdown TC-8
07.08 wednesday
from 18:00 to 22:00

Daily Coordination Meeting


Site Logistics
North Gate B

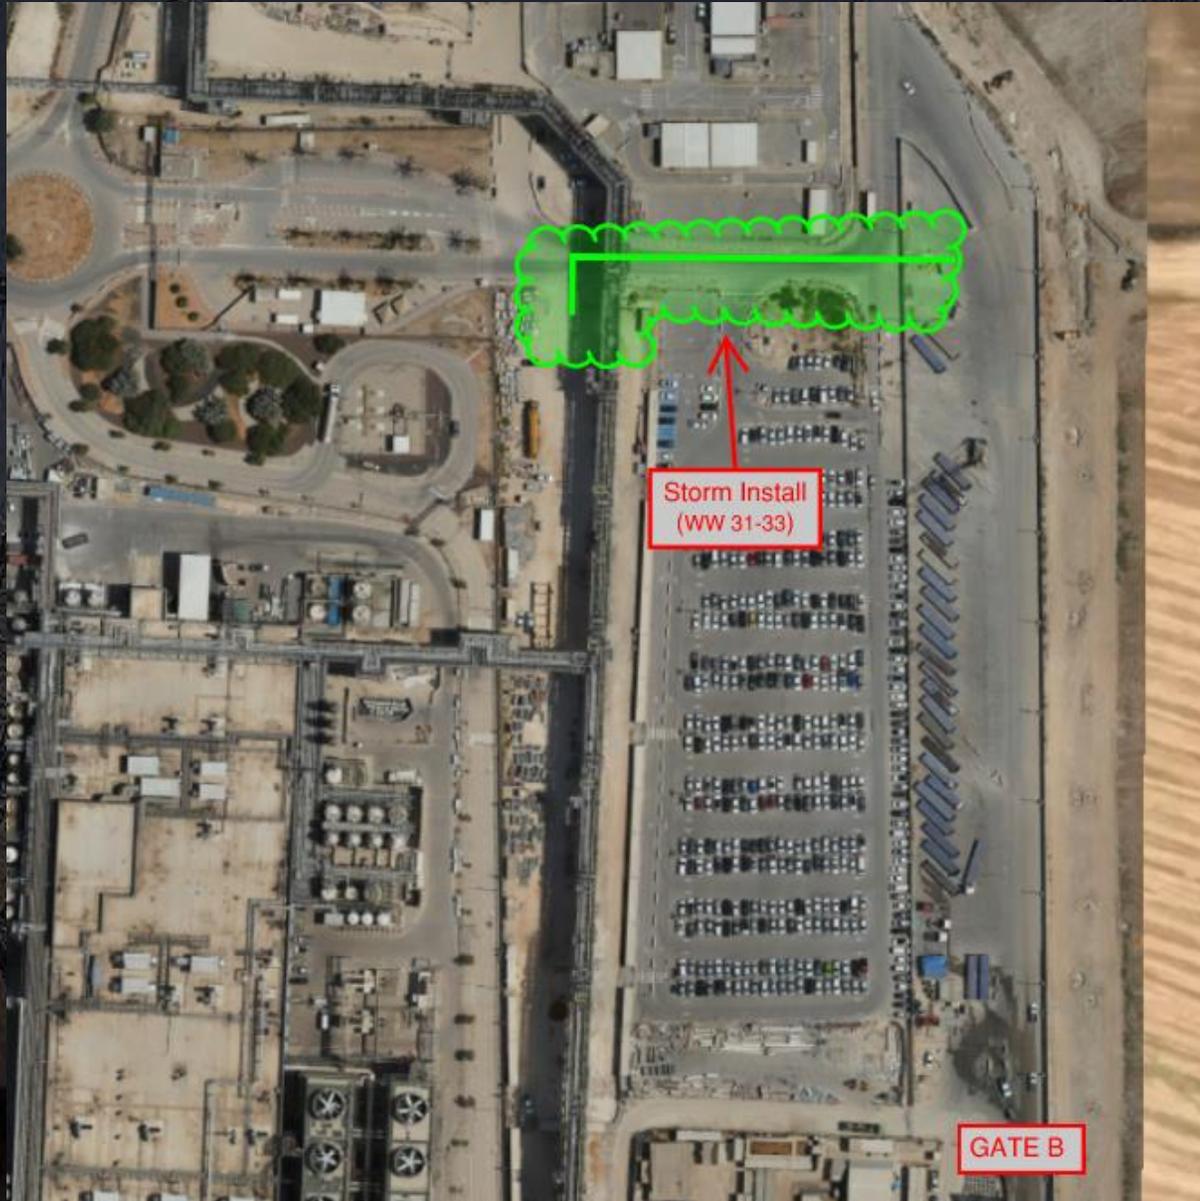

Daily Coordination Meeting

Site Logistics

North

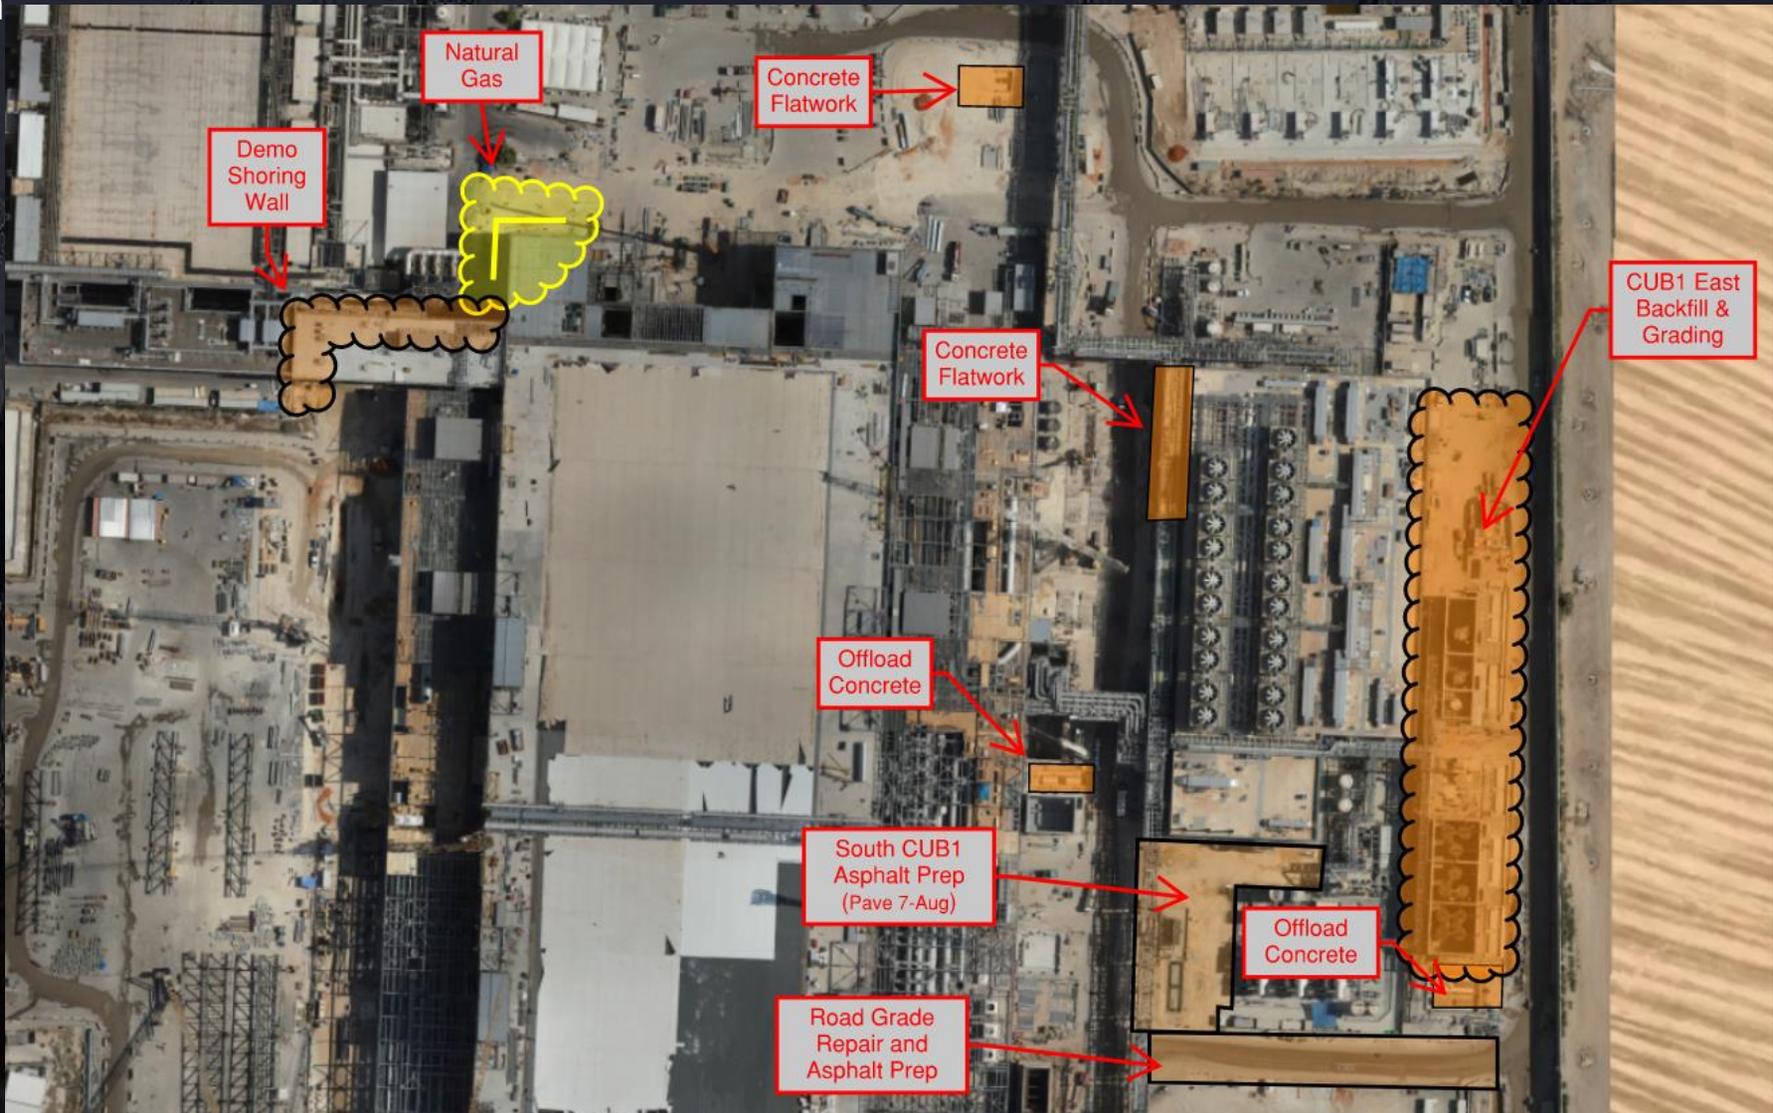

Daily Coordination Meeting

Site Logistics

South







Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

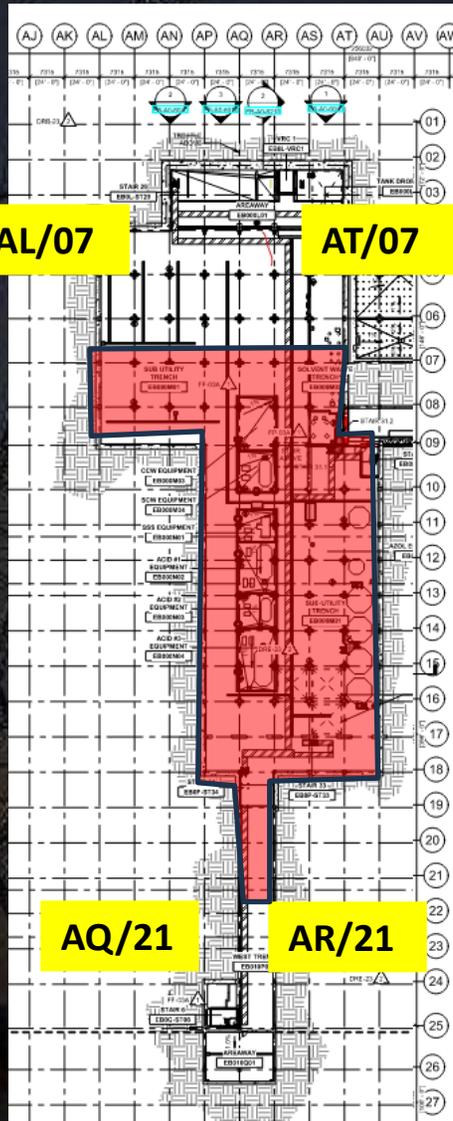


SUT2

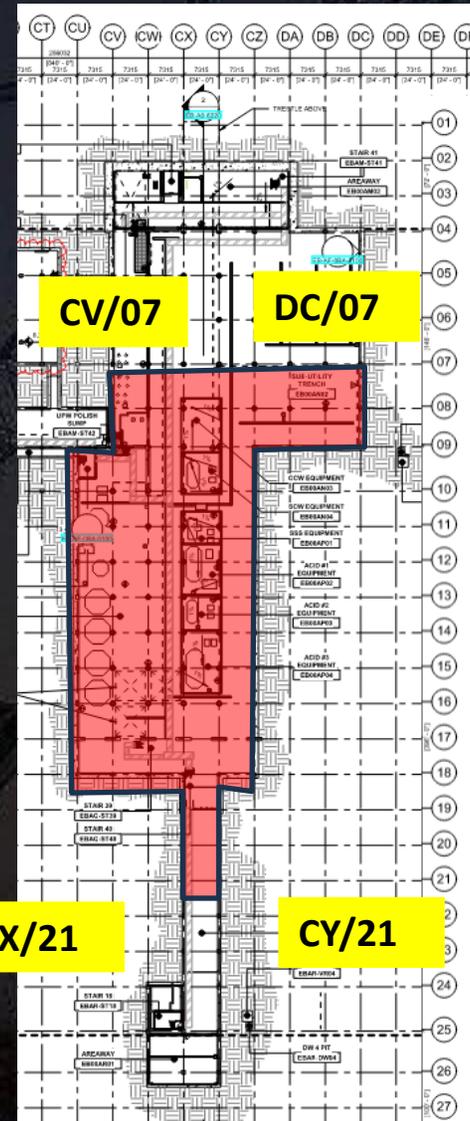

Daily Coordination Meeting


Site Logistics - Protected Areas (Utility Level)

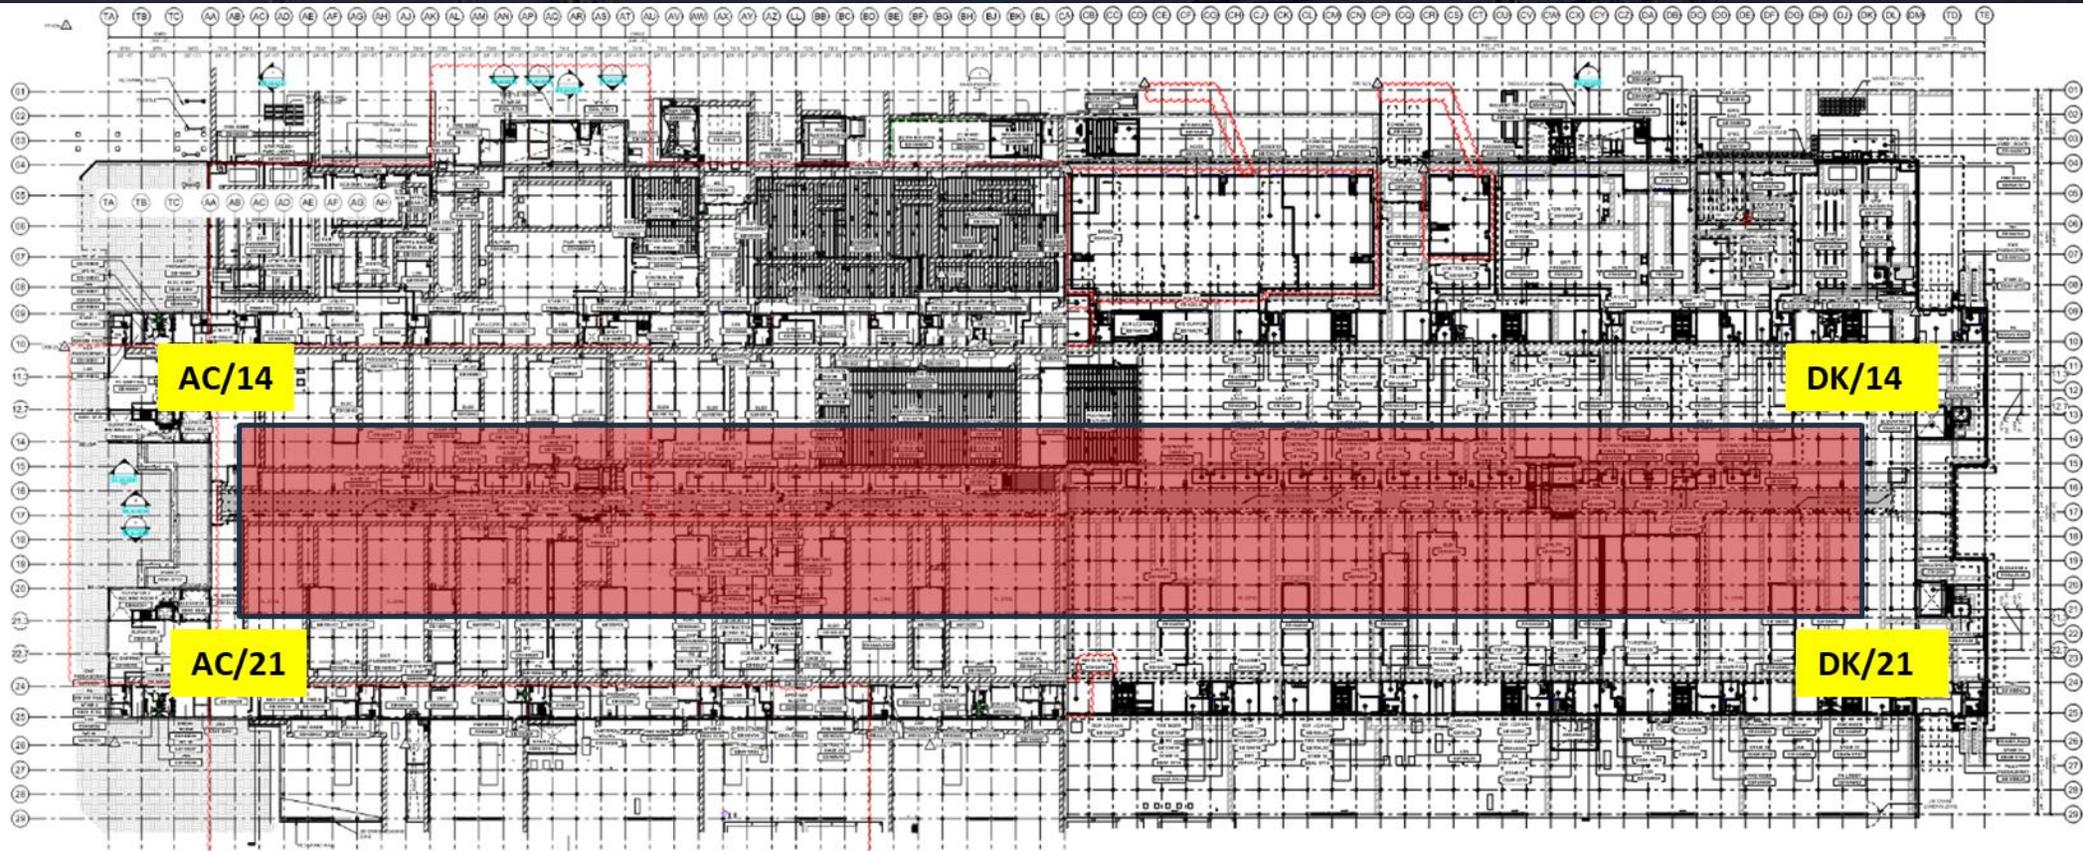



Daily Coordination Meeting


Site Logistics - Protected Areas (Subfab Level)

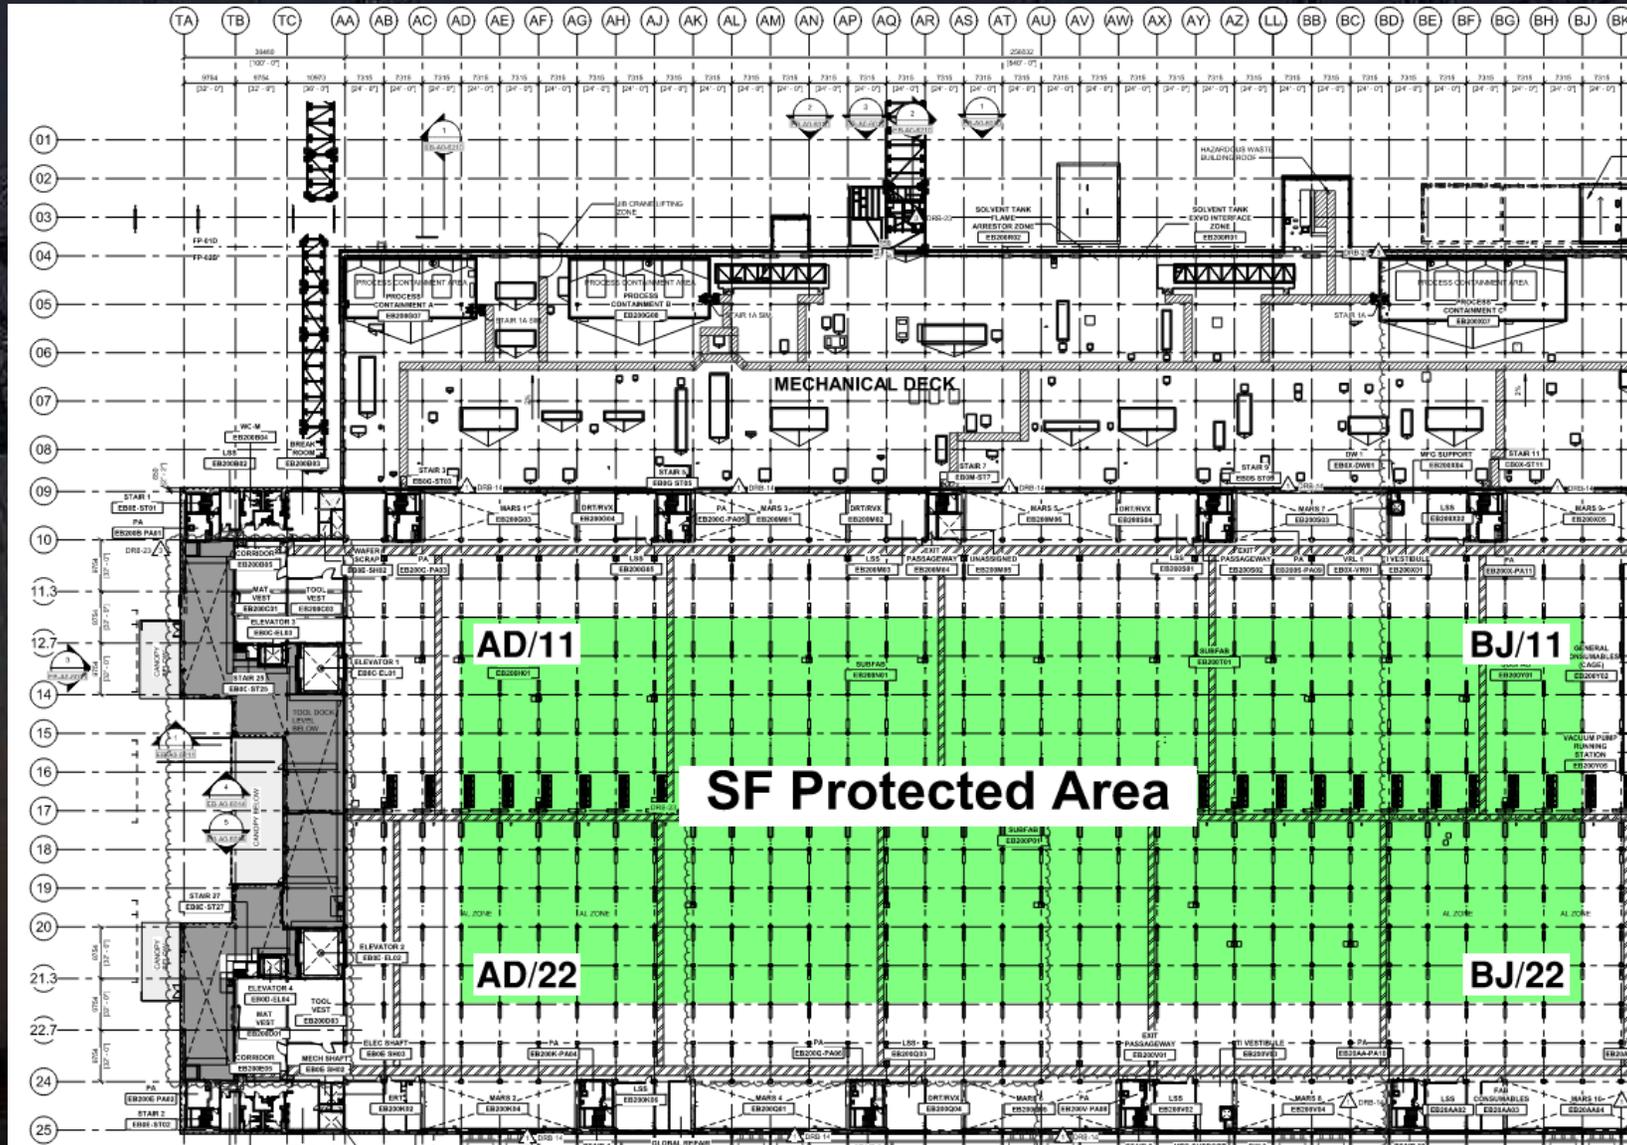

Daily Coordination Meeting


Site Logistics

Protected Areas

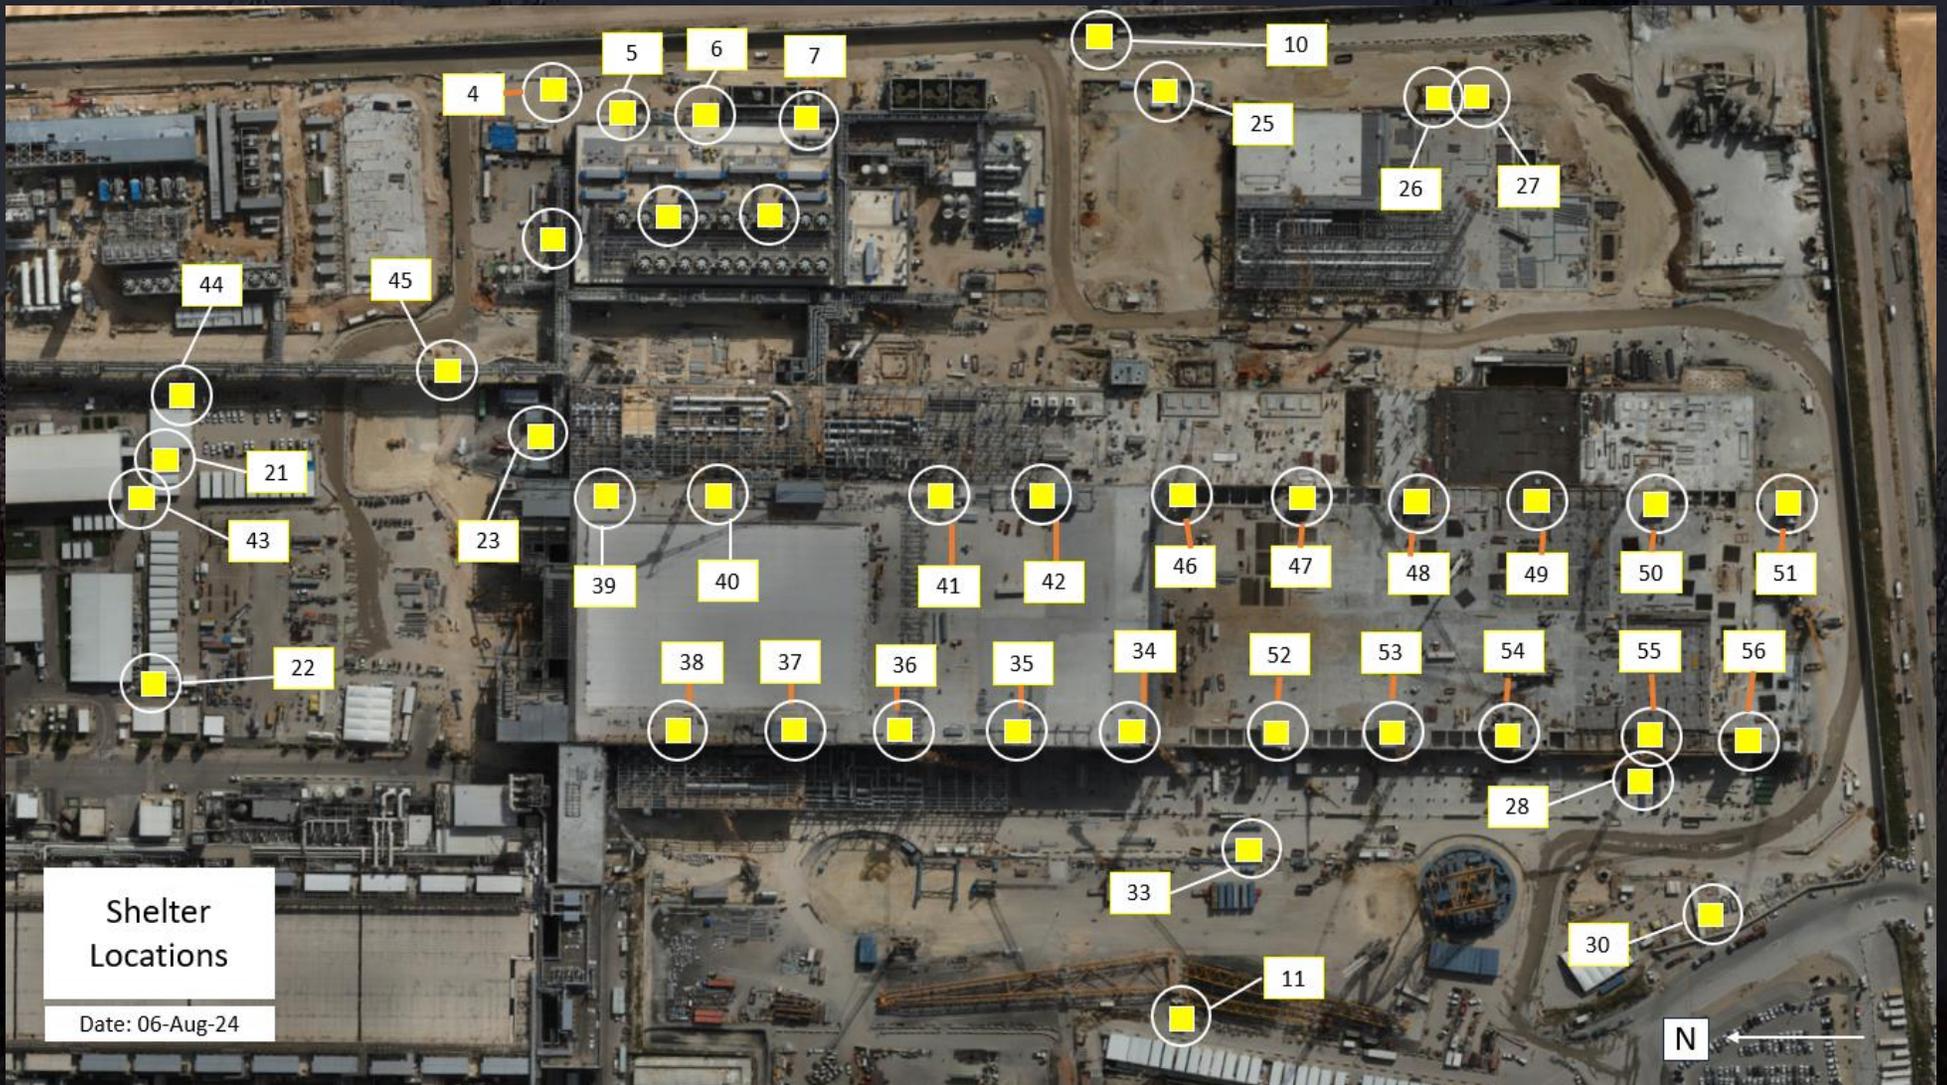

Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

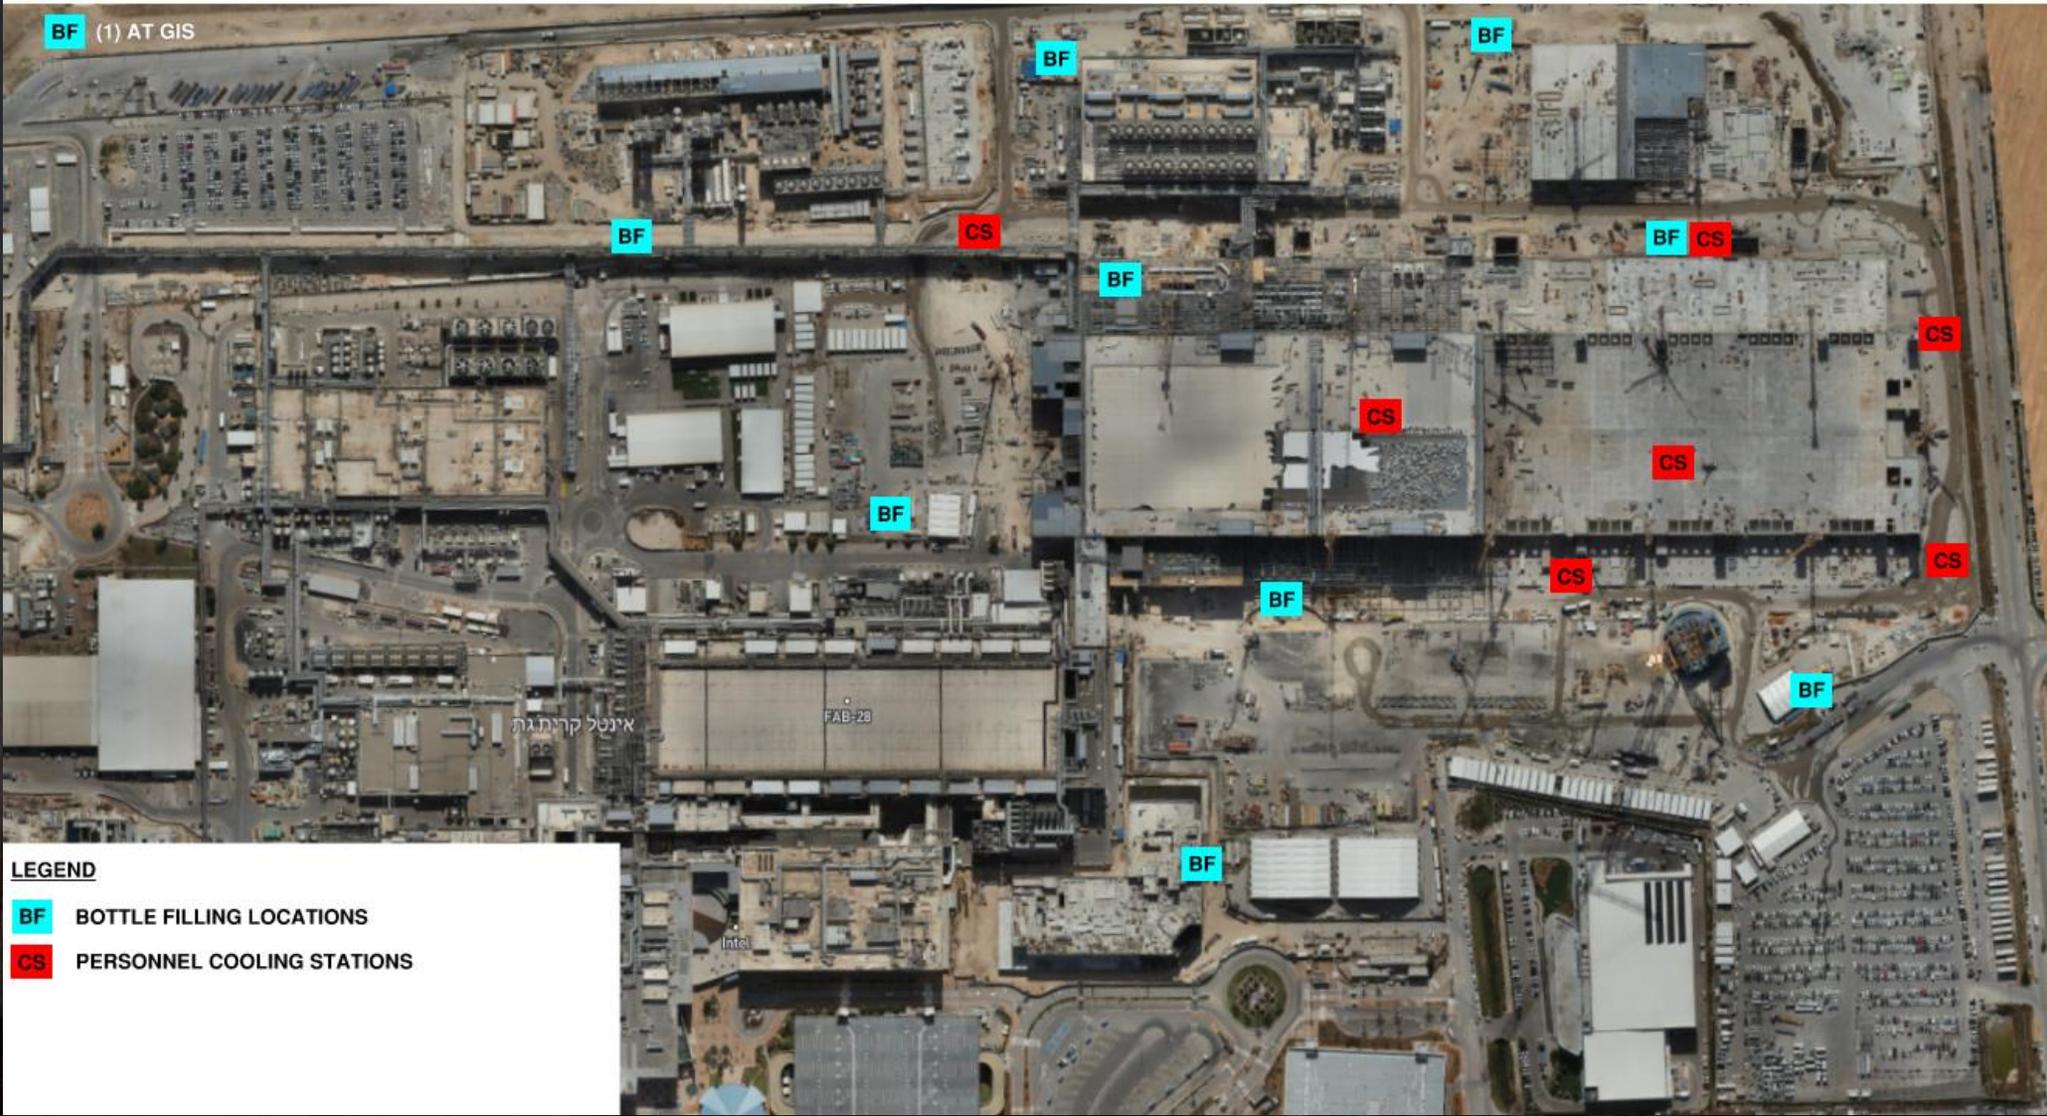

Communication



Communication

- Even the best thought out plans mean nothing if they aren't effectively communicated.
- Engage your field supervision and craft in the direction you are giving them. Have them tell *you* the plan to make sure they understand it fully before they start their tasks.
- Remember that if the last time you talked about fall protection, barricading, or PPE use was months ago- people forget, you have new hires, etc.
- If you think you've communicated enough- you haven't.



Heat Index- August 8th

| | | temperature (°F) | | | | | | | | | | | | | | | |
|-----------------------|----|------------------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|
| | | 80 | 82 | 84 | 86 | 88 | 90 | 92 | 94 | 96 | 98 | 100 | 102 | 104 | 106 | 108 | 110 |
| Relative Humidity (%) | 40 | 80 | 81 | 83 | 85 | 88 | 91 | 94 | 97 | 101 | 105 | 109 | 114 | 119 | 124 | 130 | 136 |
| | 45 | 80 | 82 | 84 | 87 | 89 | 93 | 96 | 100 | 104 | 109 | 114 | 119 | 124 | 130 | 137 | |
| | 50 | 81 | 83 | 85 | 88 | 91 | 95 | 99 | 103 | 108 | 113 | 118 | 124 | 131 | 137 | | |
| | 55 | 81 | 84 | 86 | 89 | 93 | 97 | 101 | 106 | 112 | 117 | 124 | 130 | 137 | | | |
| | 60 | 82 | 84 | 88 | 91 | 95 | 100 | 105 | 110 | 116 | 123 | 129 | 137 | | | | |
| | 65 | 82 | 85 | 89 | 93 | 98 | 103 | 108 | 114 | 121 | 128 | 136 | | | | | |
| | 70 | 83 | 86 | 90 | 95 | 100 | 105 | 112 | 119 | 126 | 134 | | | | | | |
| | 75 | 84 | 88 | 92 | 97 | 103 | 109 | 116 | 124 | 132 | | | | | | | |
| | 80 | 84 | 89 | 94 | 100 | 106 | 113 | 121 | 129 | | | | | | | | |
| | 85 | 85 | 90 | 96 | 102 | 110 | 117 | 126 | 135 | | | | | | | | |
| | 90 | 86 | 91 | 98 | 105 | 113 | 122 | 131 | | | | | | | | | |
| | 95 | 86 | 93 | 100 | 108 | 117 | 127 | | | | | | | | | | |
| 100 | 87 | 95 | 103 | 112 | 121 | 132 | | | | | | | | | | | |

Caution

Extreme Caution

Danger

Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



14:00 Sign In
