

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Mentoring – ensure your programs are being followed



SUT 2 Plinths
5:00 am

NWTD Int. EQ.
pad
3:00 am

1J topping slab
4:00 am

NWTD Interstitial Eq.
pad
3:00am

1J topping slab
4:00am

SUT 2 plinths
5:00 am


אינטל קרית גת

FAB-28

AB-18



UTILITY LEVEL MOD1

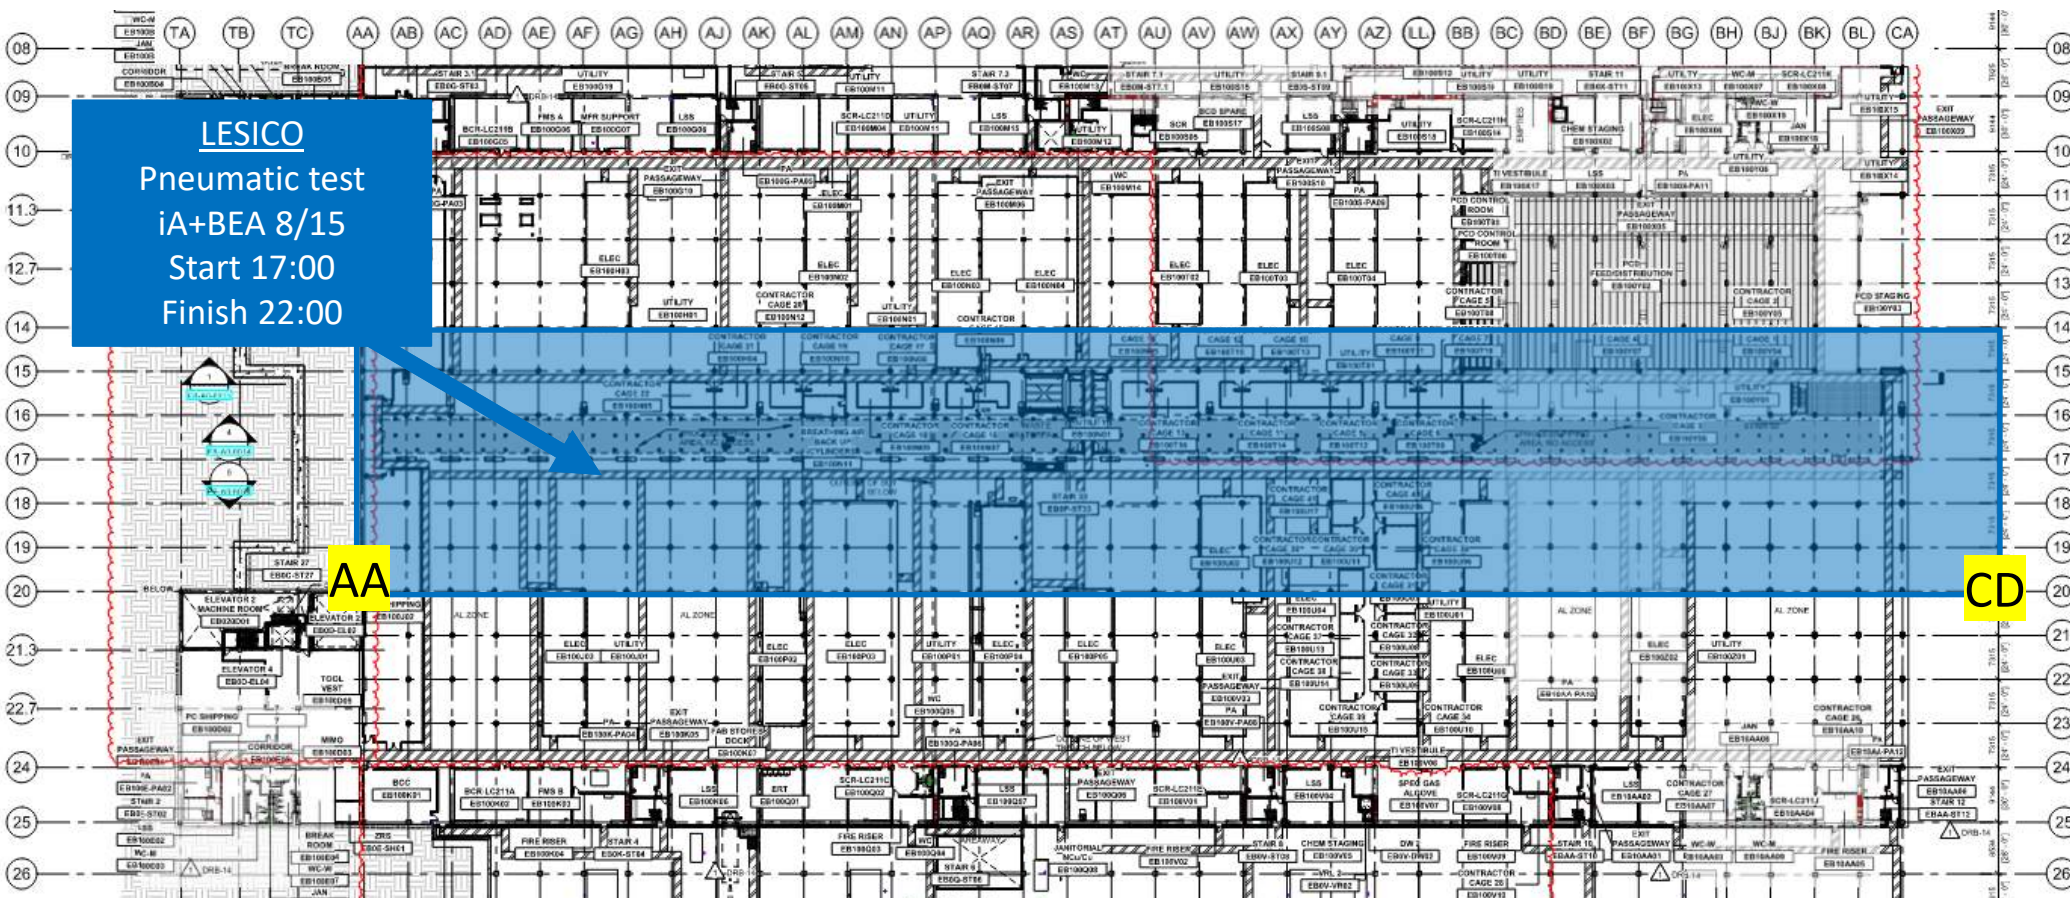




HOFFMAN CONSTRUCTION COMPANY




SUT LEVEL

LESICO
Pneumatic test
iA+BEA 8/15
Start 17:00
Finish 22:00

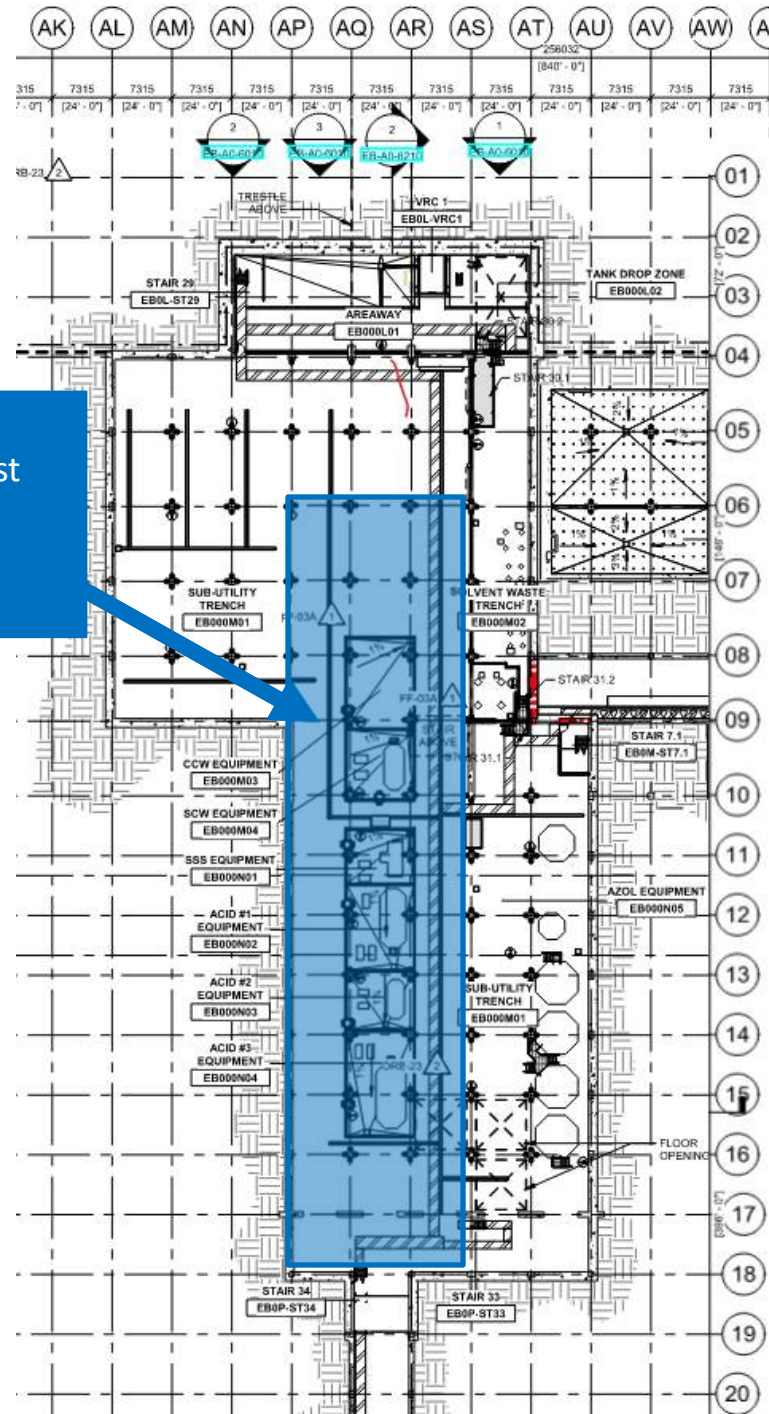




UTILITY LEVEL MOD1

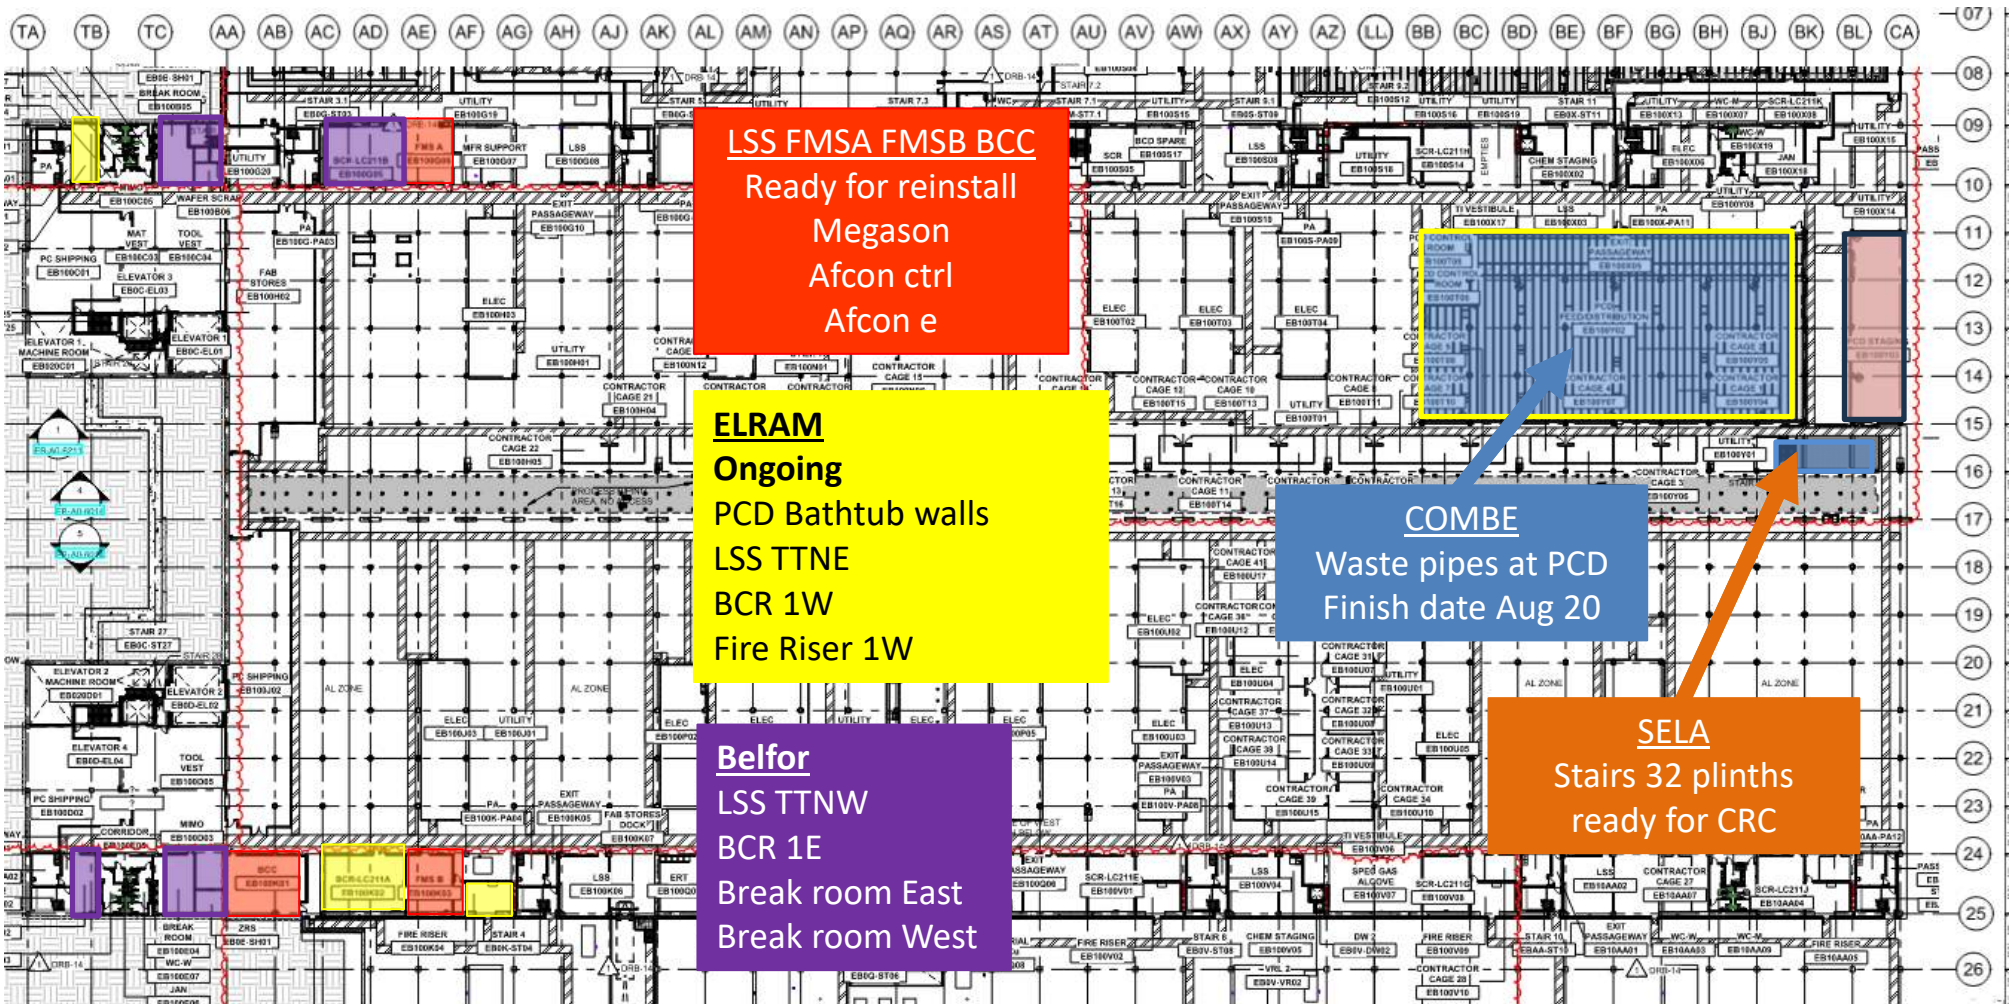




UTILITY LEVEL MOD1

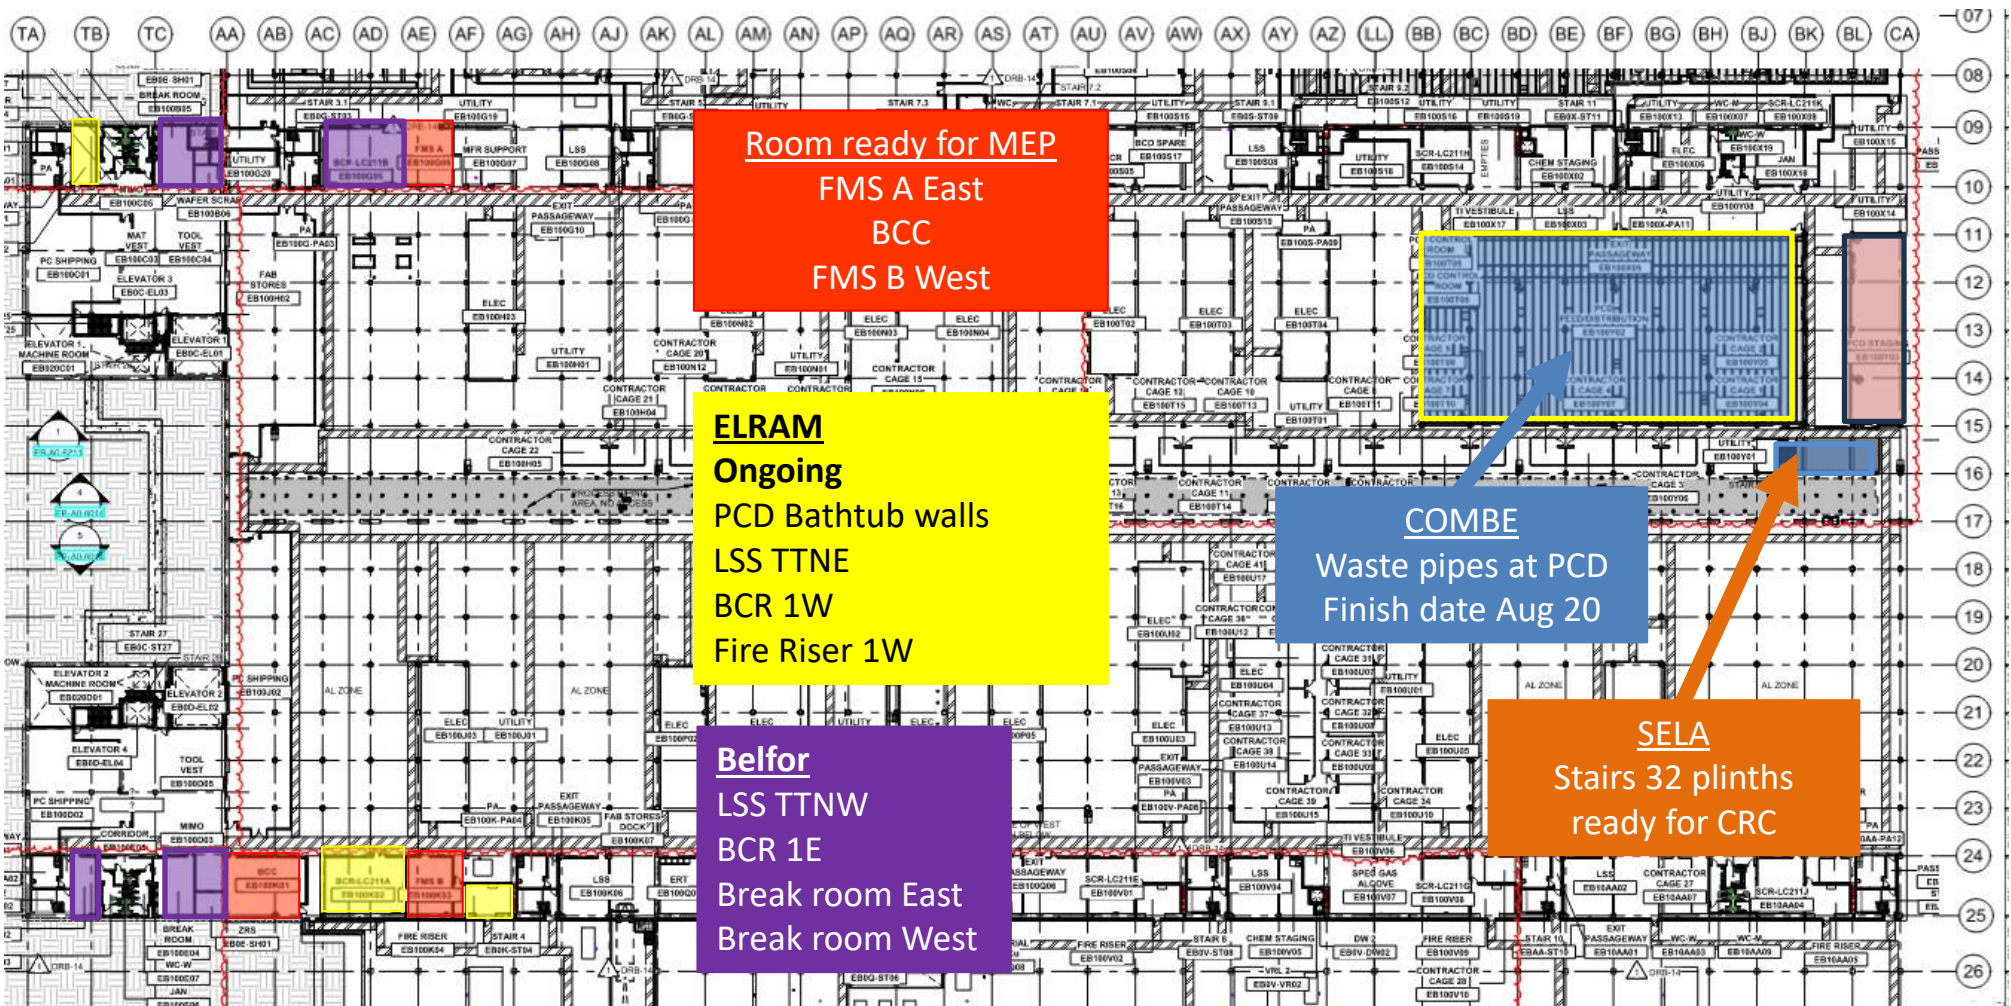


UTILITY LEVEL MOD2

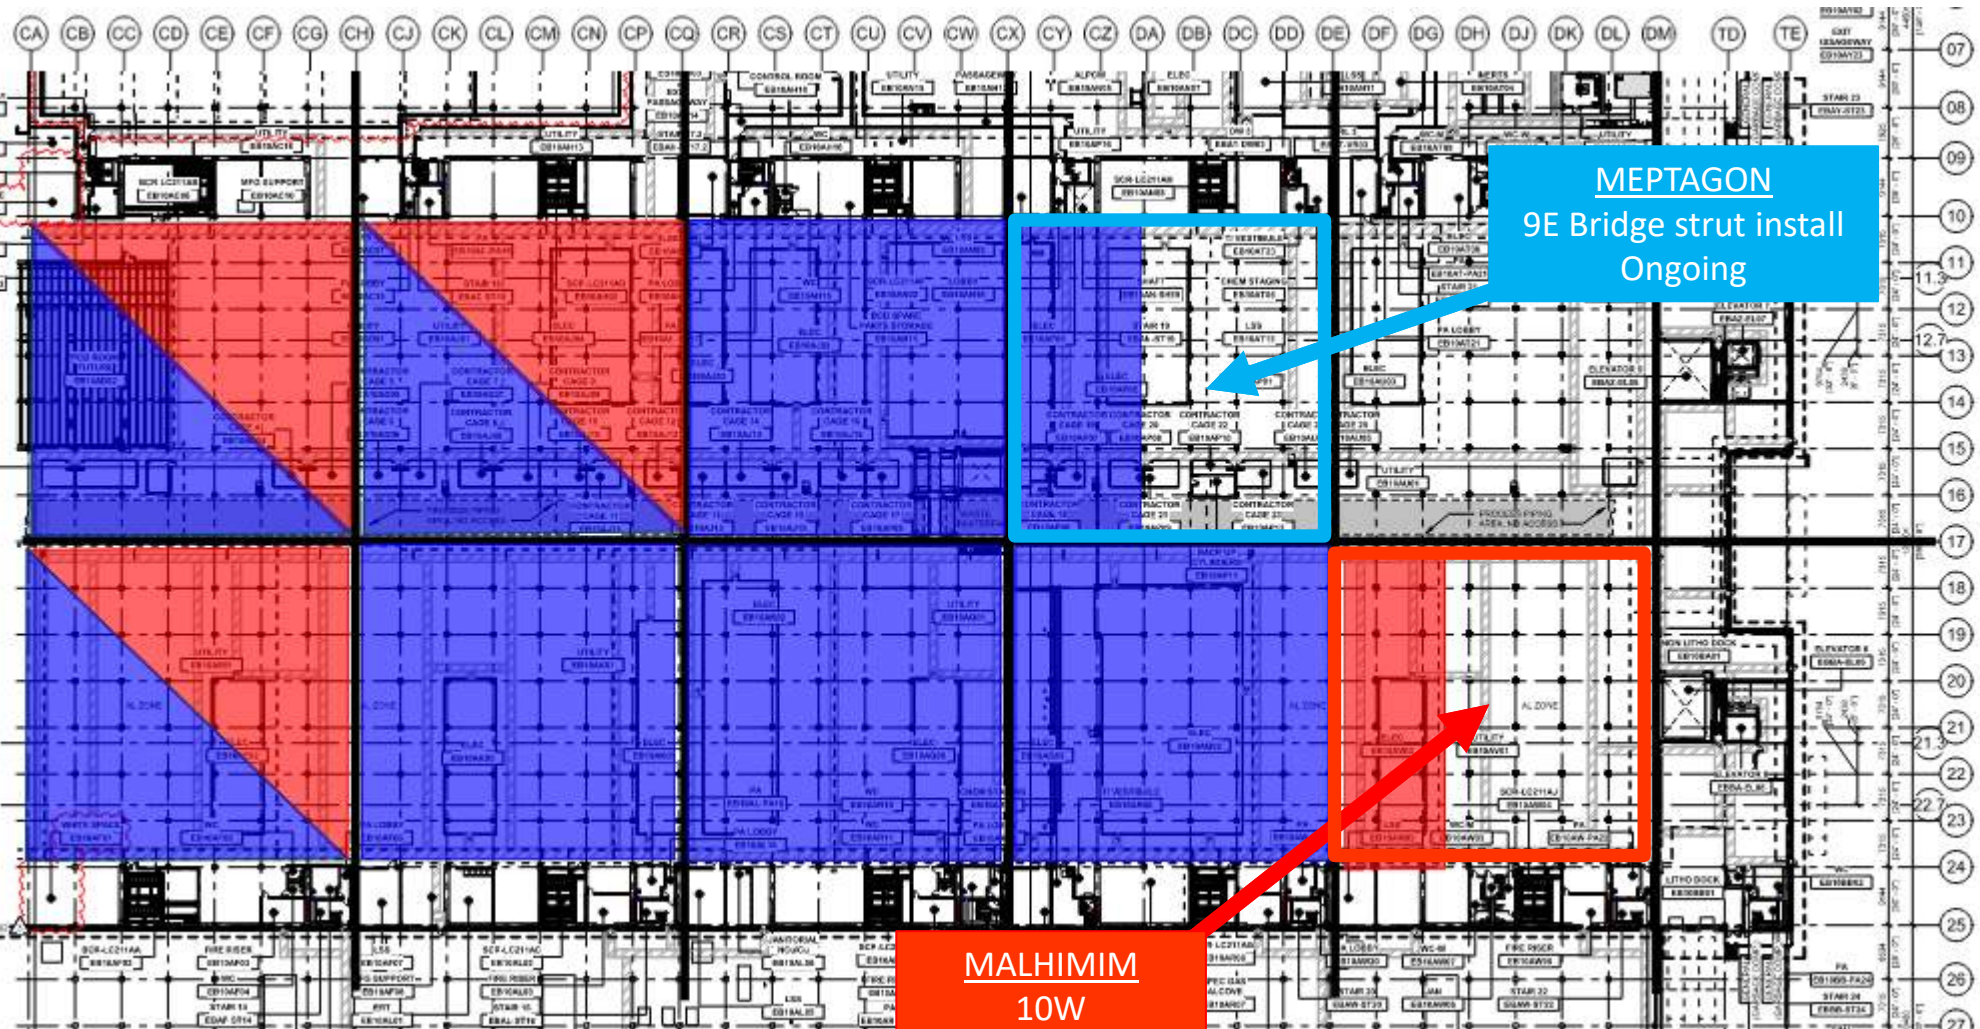

MEPTAGON
9E Bridge strut install
Ongoing


MALHIMIM
10W
Sprinklers install

SUT 38.1 LEVEL

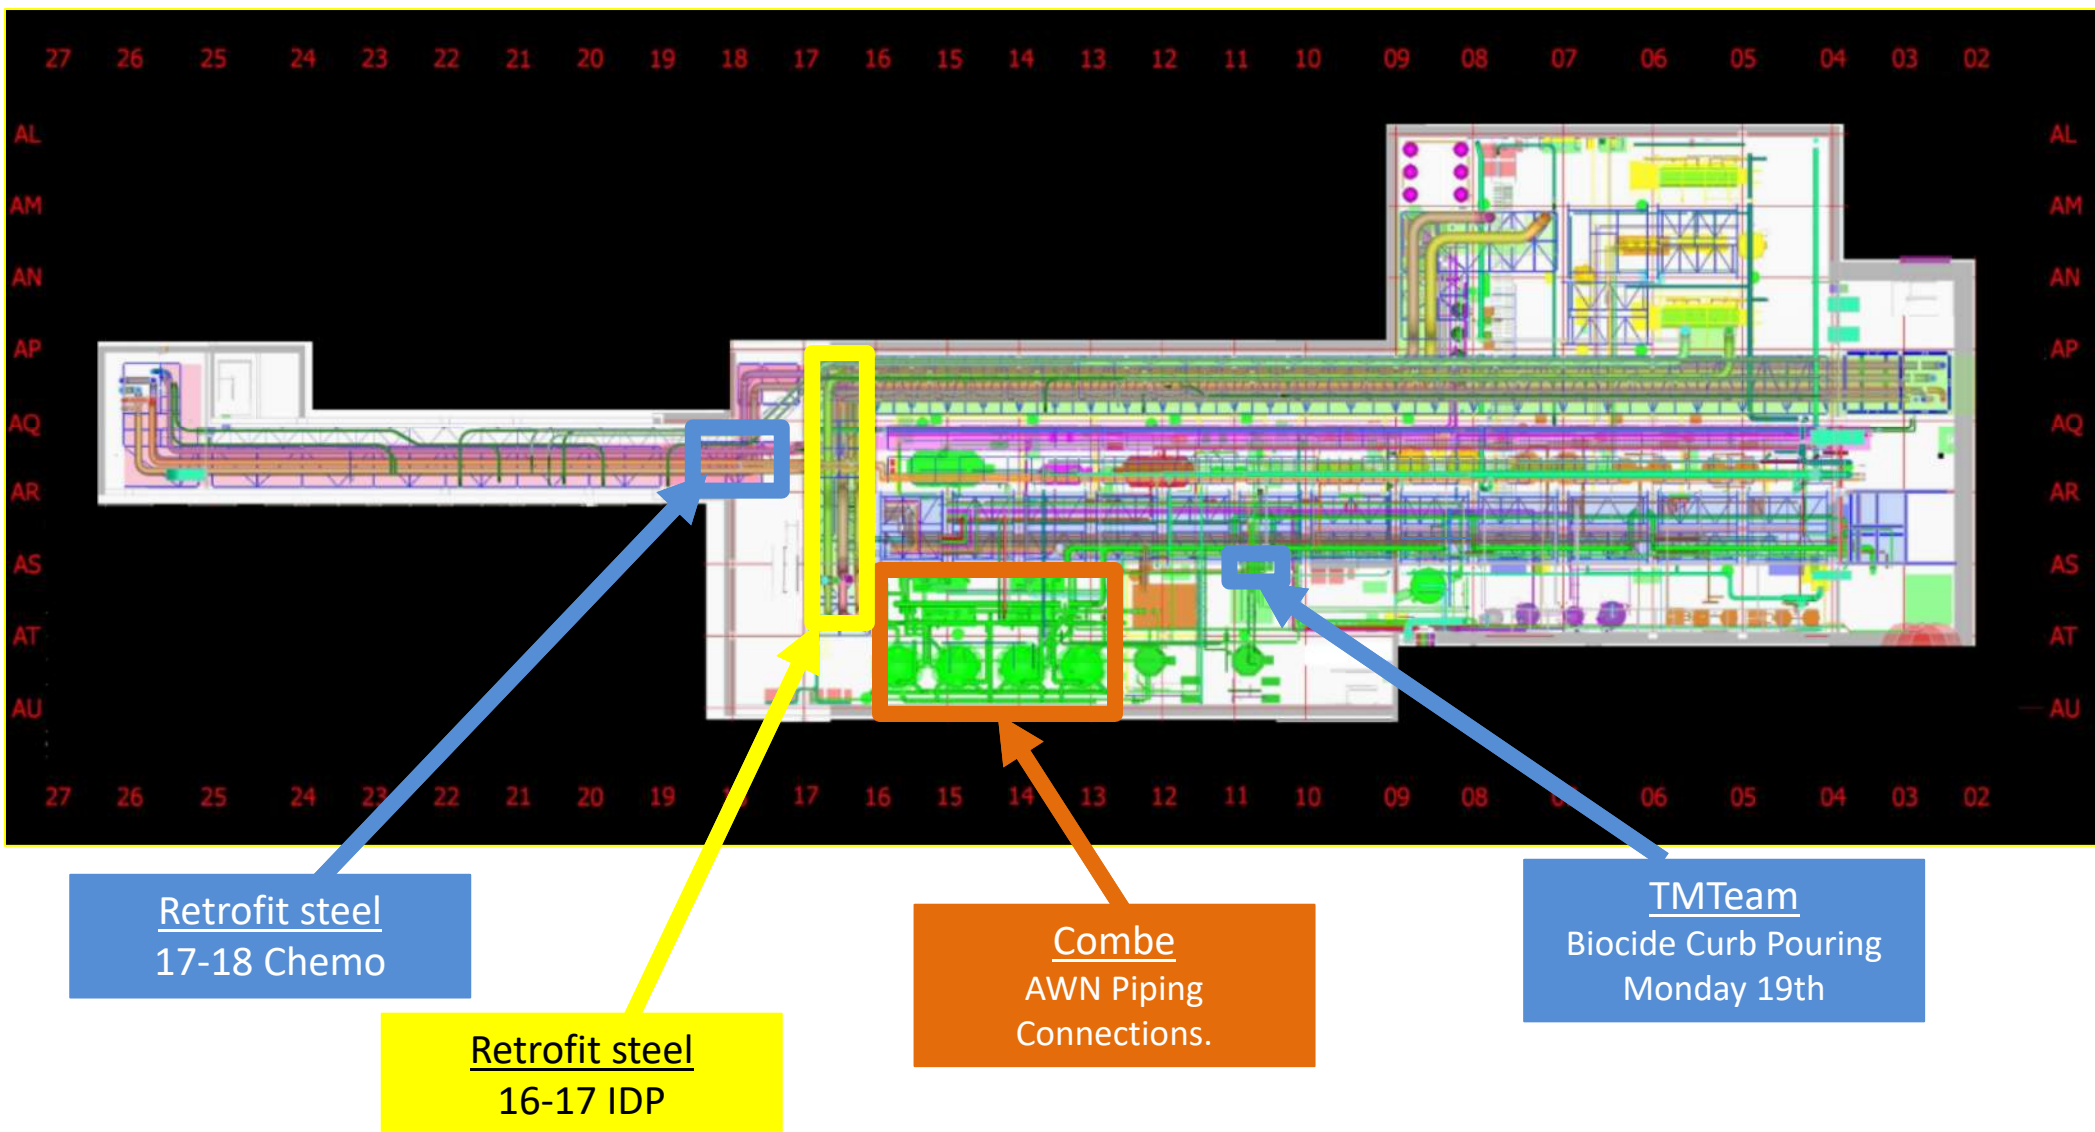



SUT 38.2 LEVEL

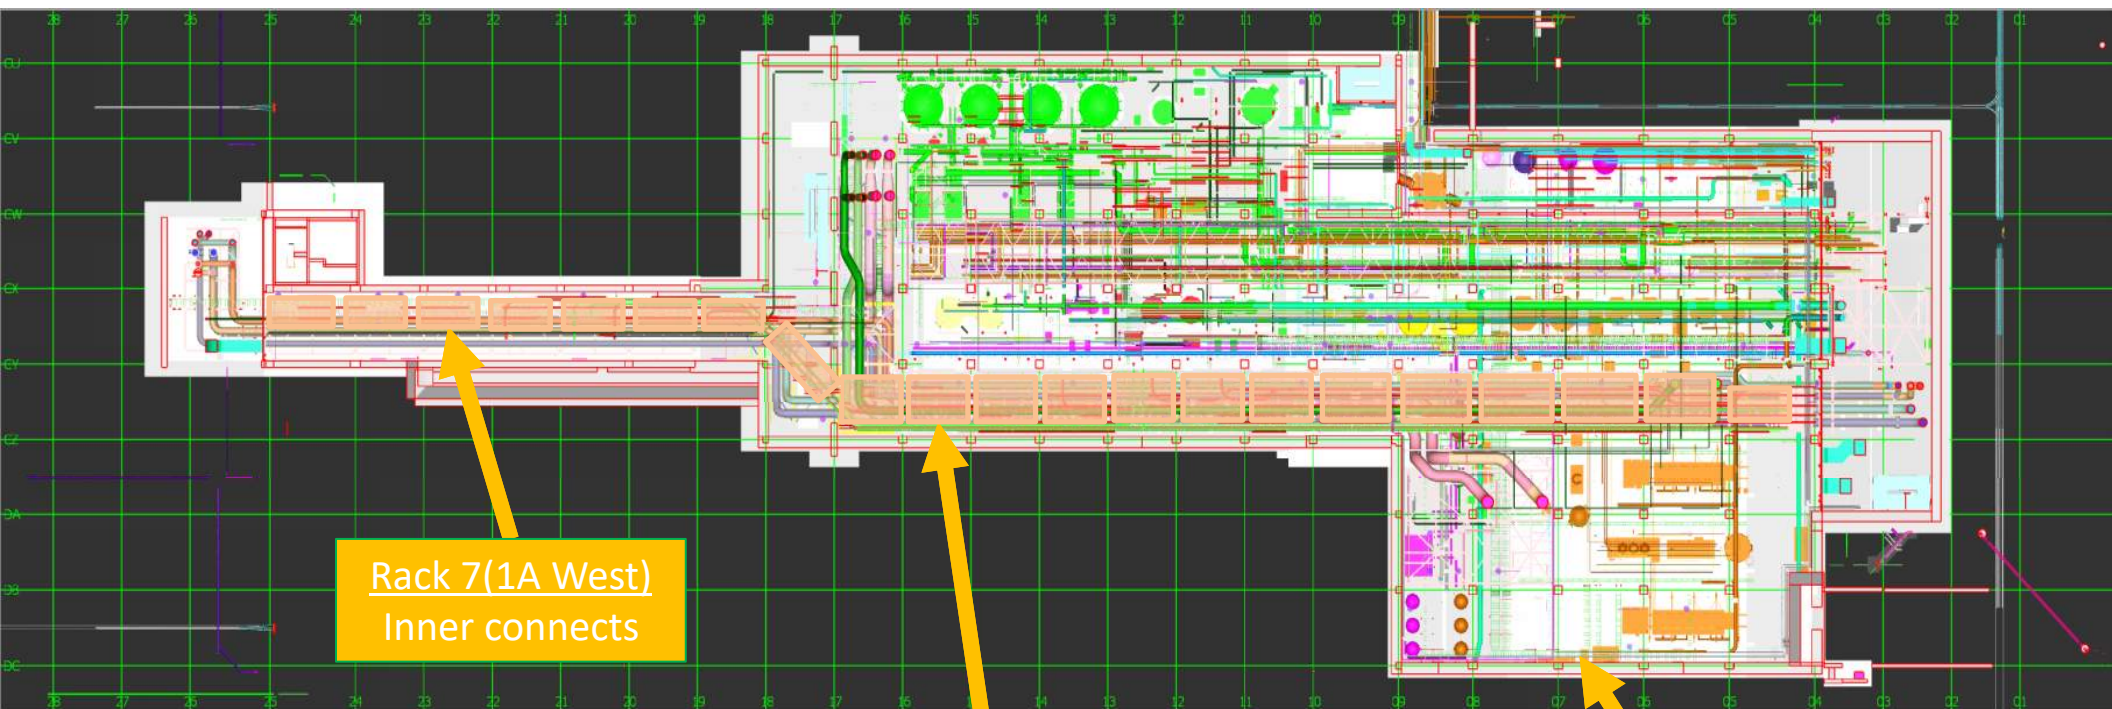

Rack 7(1A West)
Inner connects


CRW
H&T
Need to be installed

Vesda
H&T
Not actively installing


1A Rack
Inner connects

8 Rack
Lifting


SUBFAB BUILDOUT MOD 1

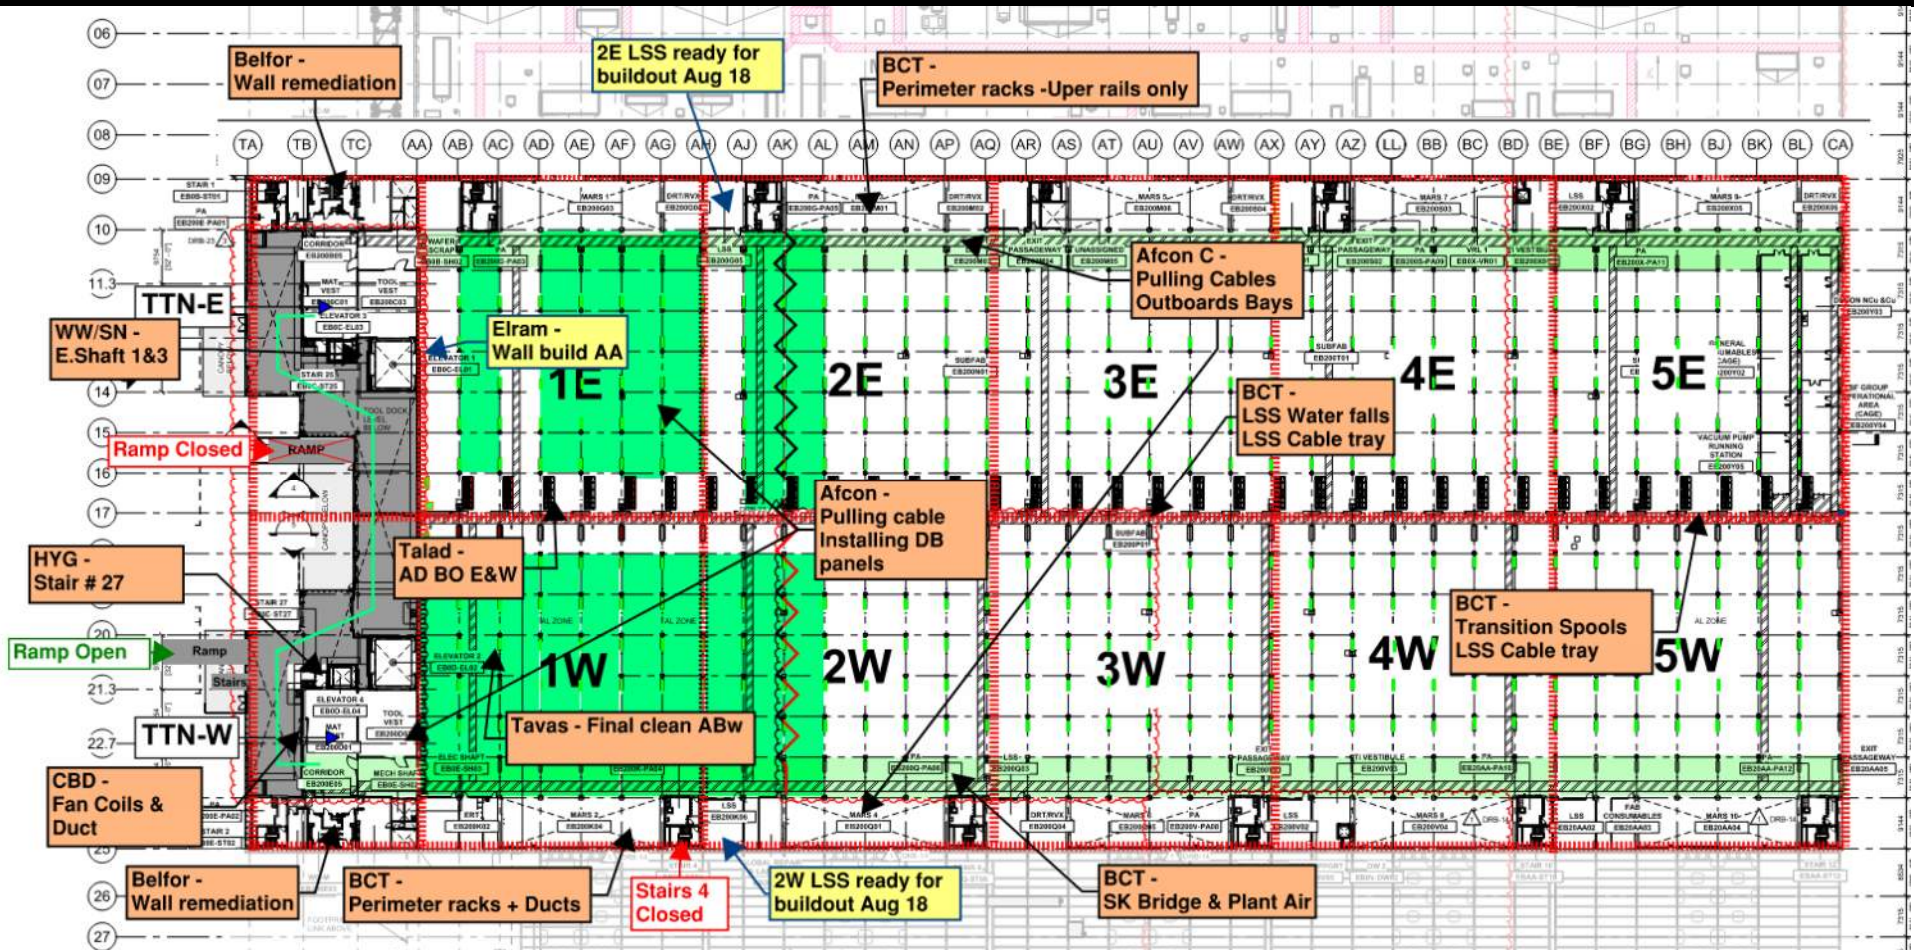

SUBFAB BUILDOUT MOD 2

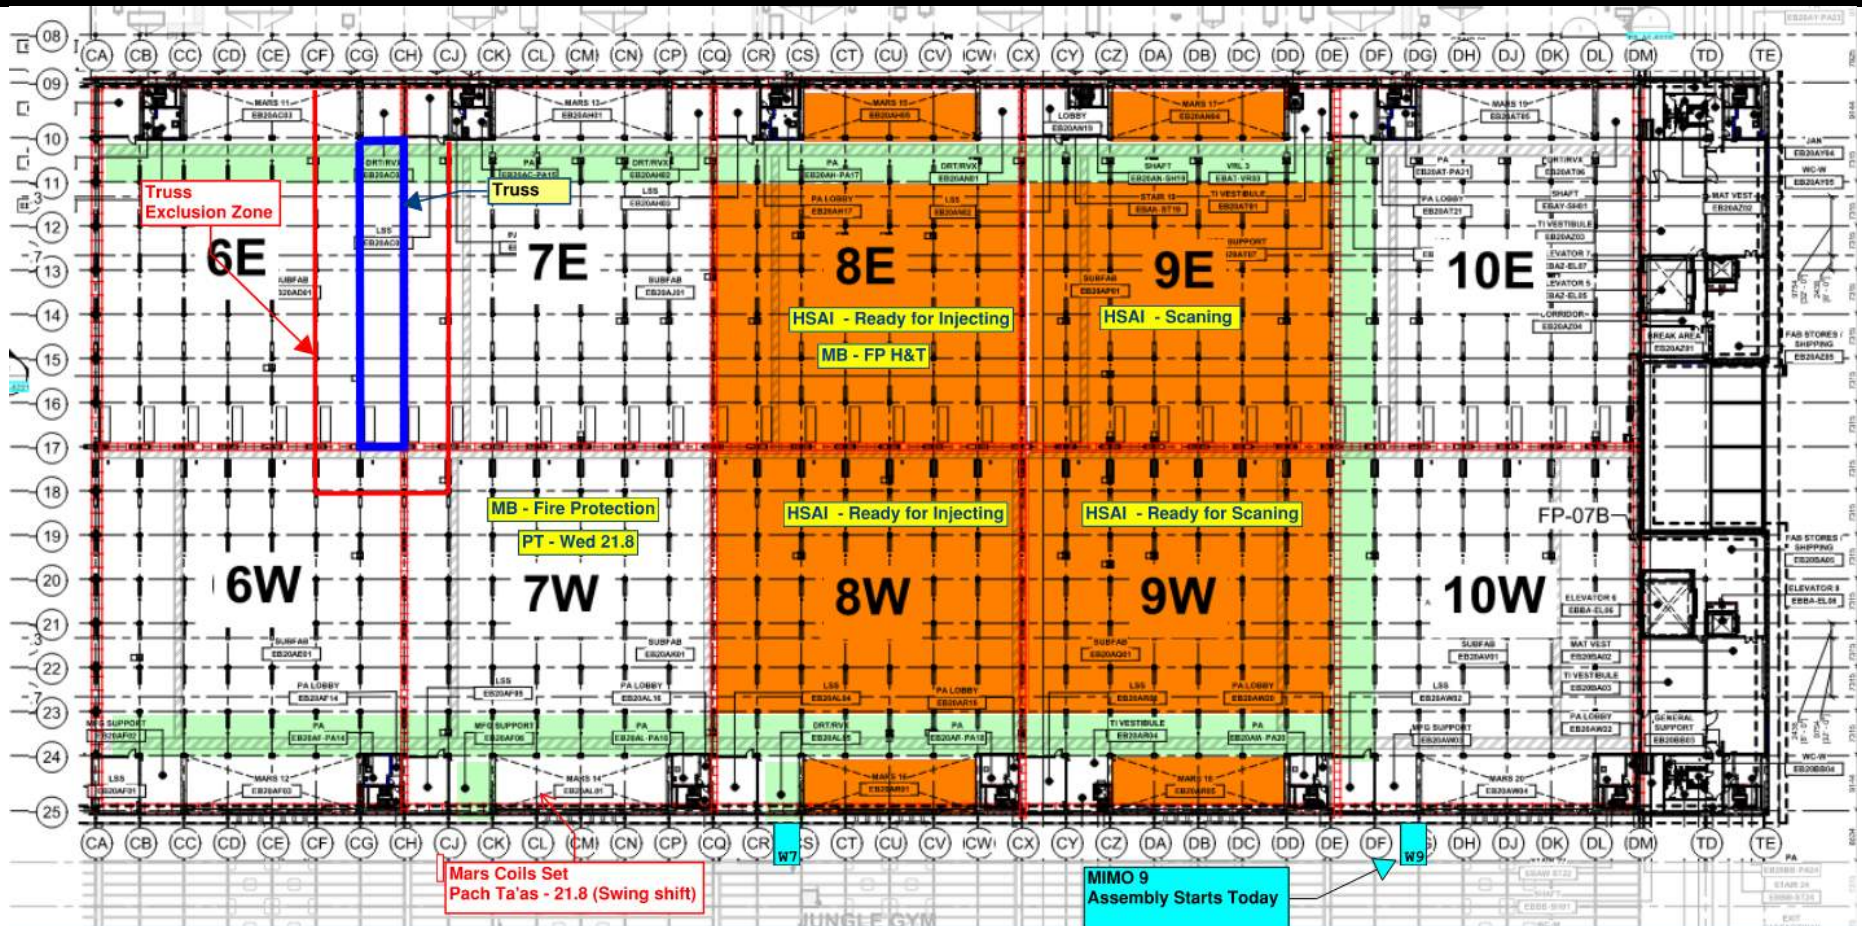

SUBFAB CRC TOPCOAT

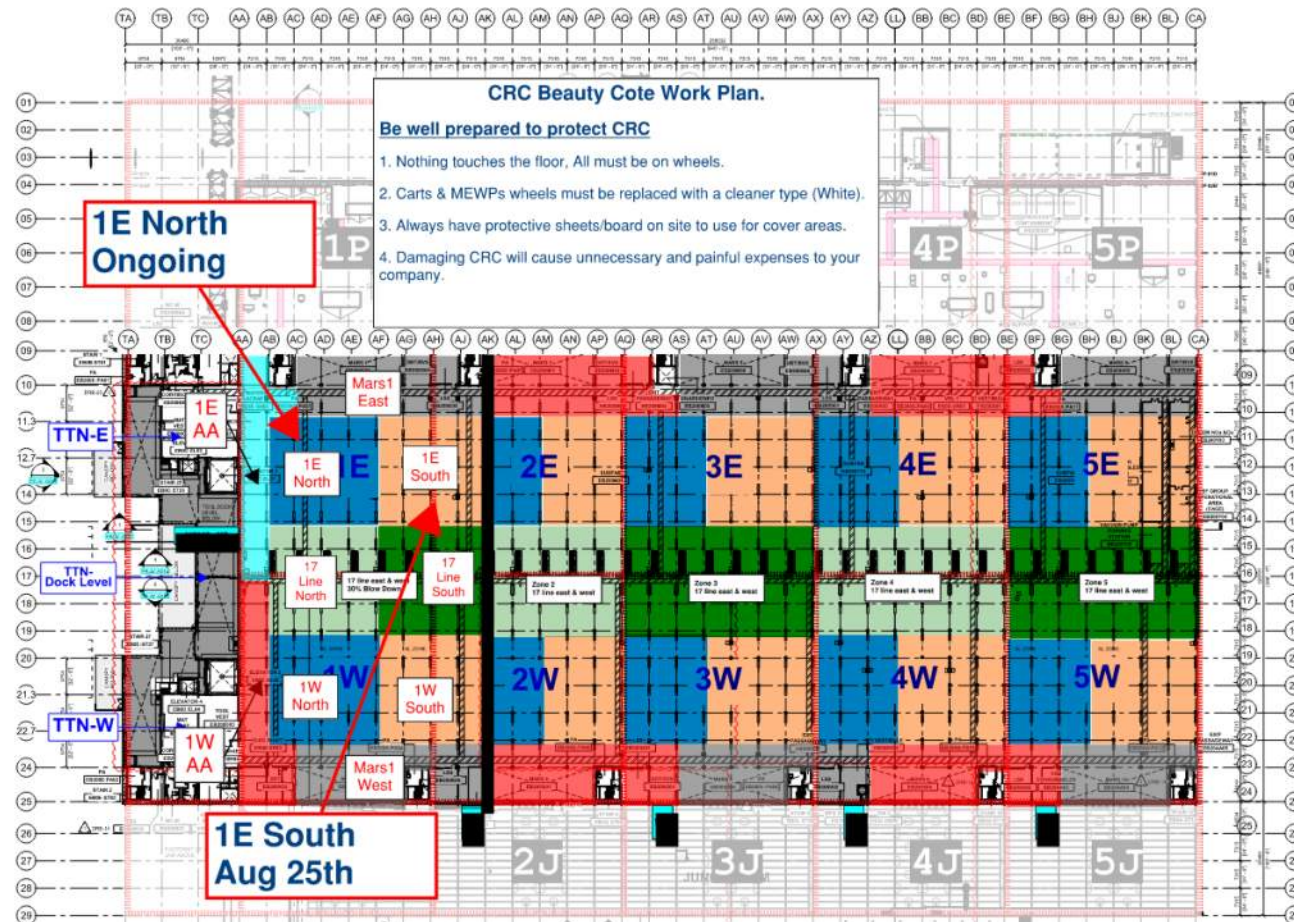



NTTE/W
 WW/SN - west side welding tabs and replacing beams
 Elram - East/West floor done QA/QC
 SK - east side pipes needs to be completed
 HYG - East to finish steel, West receiving material

Belfor
 AA/TC line


FINISH ON WED.

CR level:
 Afcon - Cable trays, modules and stickers 1W,2E, 2W,3W
 MB - 1E drops, 1W drops. 2E- drops
 Elram - 10, 24 columns/shaft walls
 WW/JS - 17-18 line added beams+ AS south stocker beams
 Meptagon - I&C 1E
 D&P - Ceiling rods 1E, 5E blades install.
 Tzur-esh - 24-25 lines. 4E-4W blades
 HYG- 1W Litho crane QA, 5W Litho crane steel
 PT - Duct prep for test AA-AH east
 Talad- Blades install 24-25 lines
 Belfor - AA/TC lines

TALAD- Prepping up 1E aa-ak line for sela idp's crc
 AFCON-started installing modules on 3E+3W.


D@P-finishng ceiling rods on 1E&5E.
 HYG-ongoing 5W litho crane white steel.

East loading dock-girtzteam 1M duration

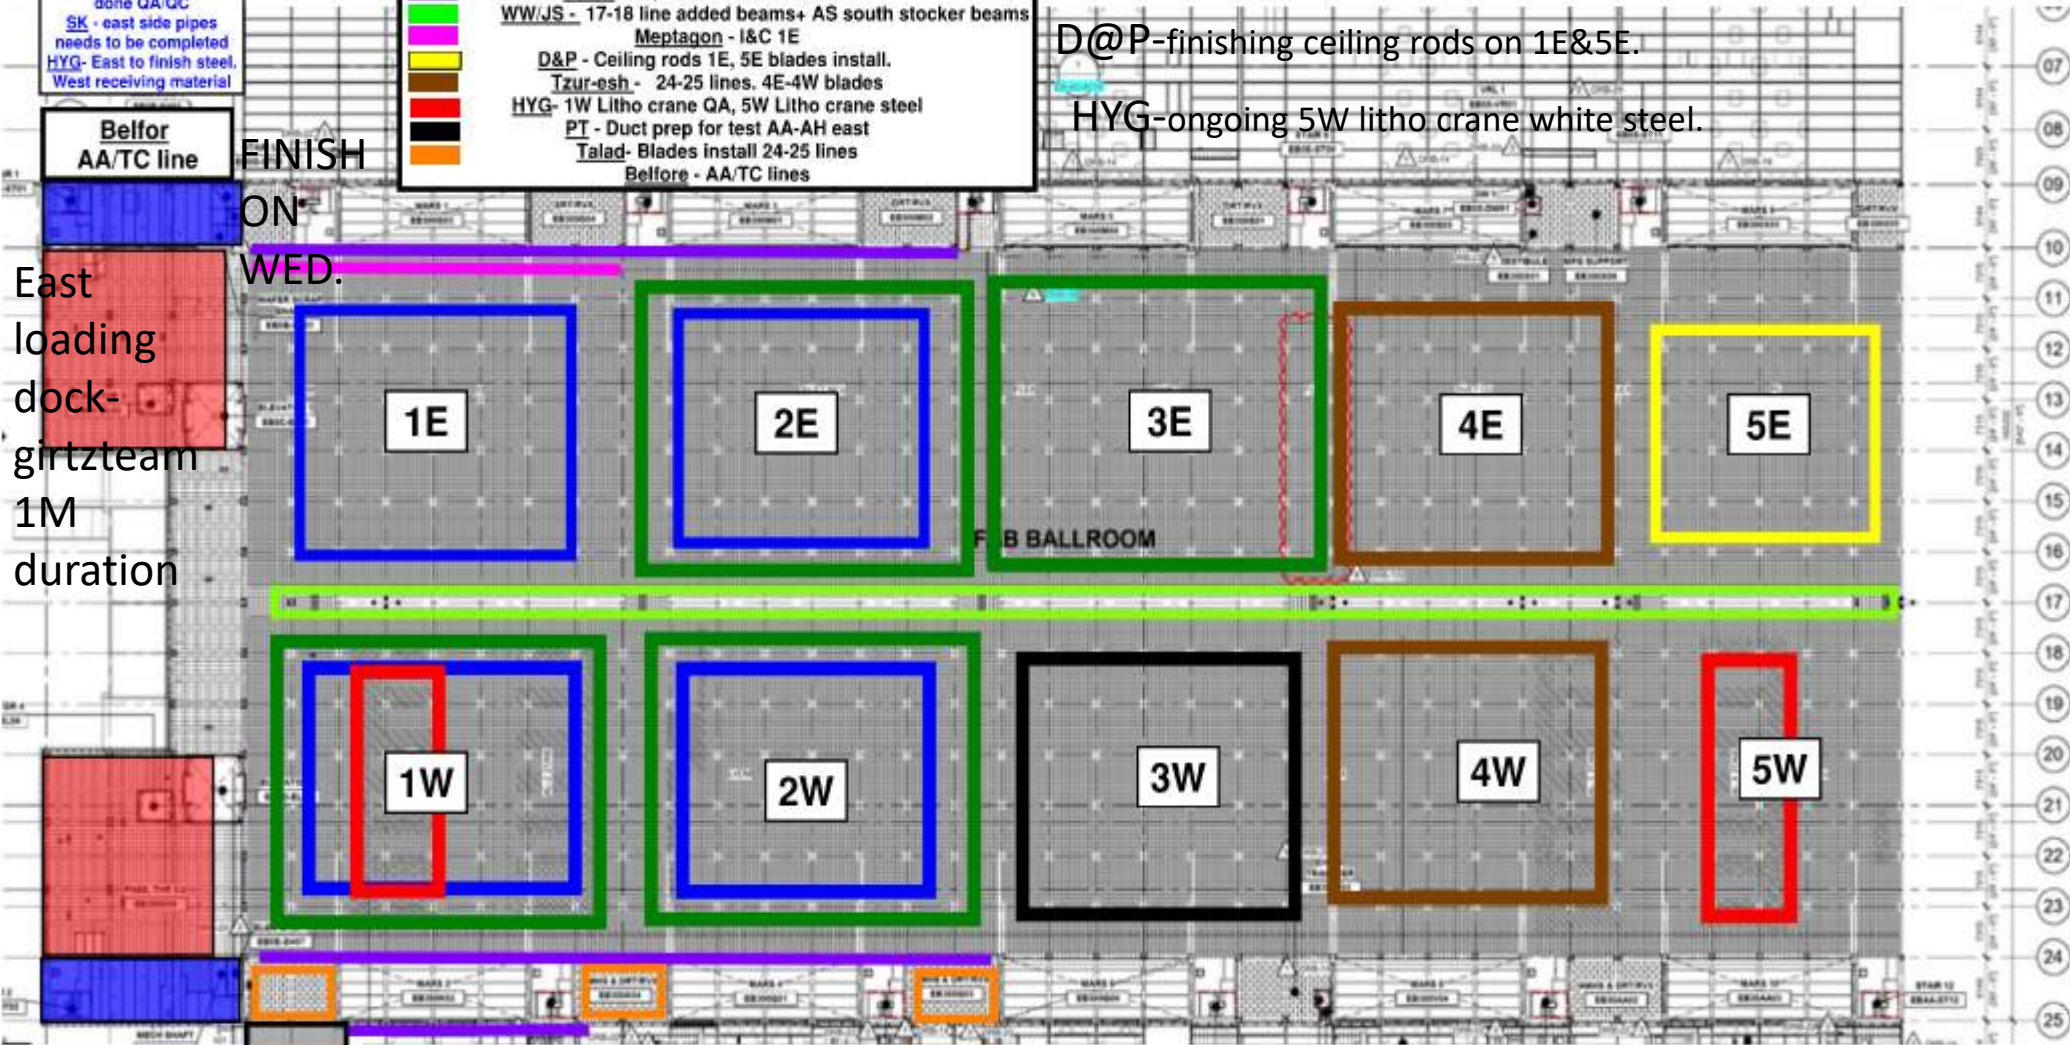

Link
 RP - FP 5RA level
 MB - To start WW34
 PT- To start WW34

MB-installing supports for high & tight activities

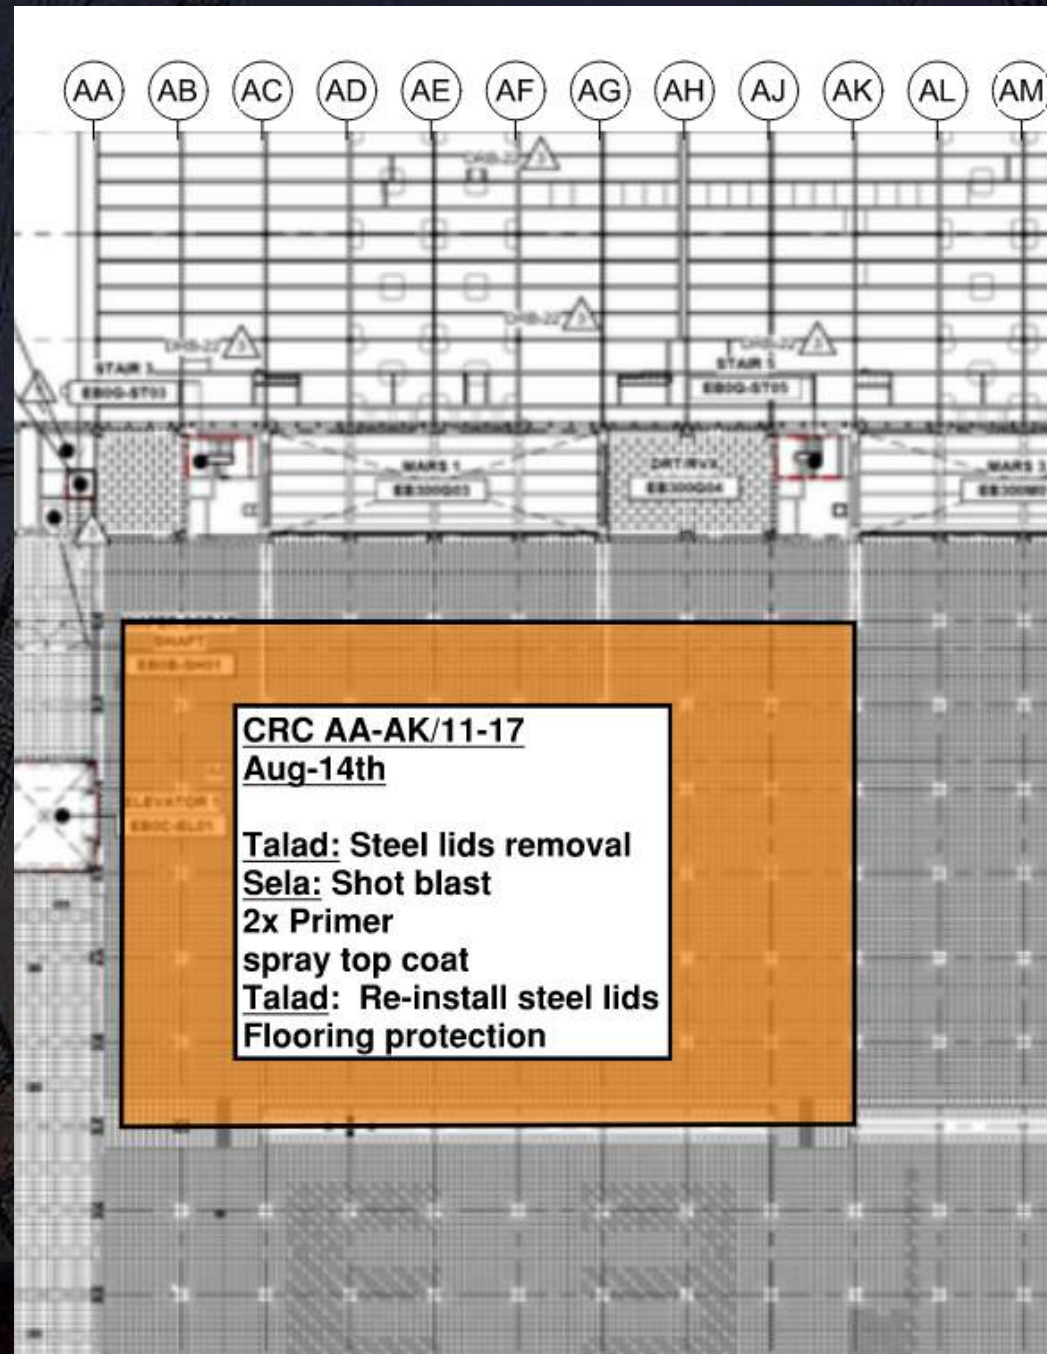





Carmel bidud pressure test need
all documentation done


Int. level


- WW/SN - 2W penetrations
- Chemo- 10" pipe racks 2E-2W started
- Afcon - Cable trays, modules, cable pulling 1E,2E,1W,2w
- HYG - 5RA added beams 2E
- MB- 2E-2W preparations for test WW33
- C-B duct - 1W-2W to schedule test WW33
- Eiram - Column wraps 9,10,24 lines
- RP- FP 4DA 3E-3W
- Tzur-Esh - Steel paint 4E-4W
- Megasone - Small wires+ speakers 3E+2E

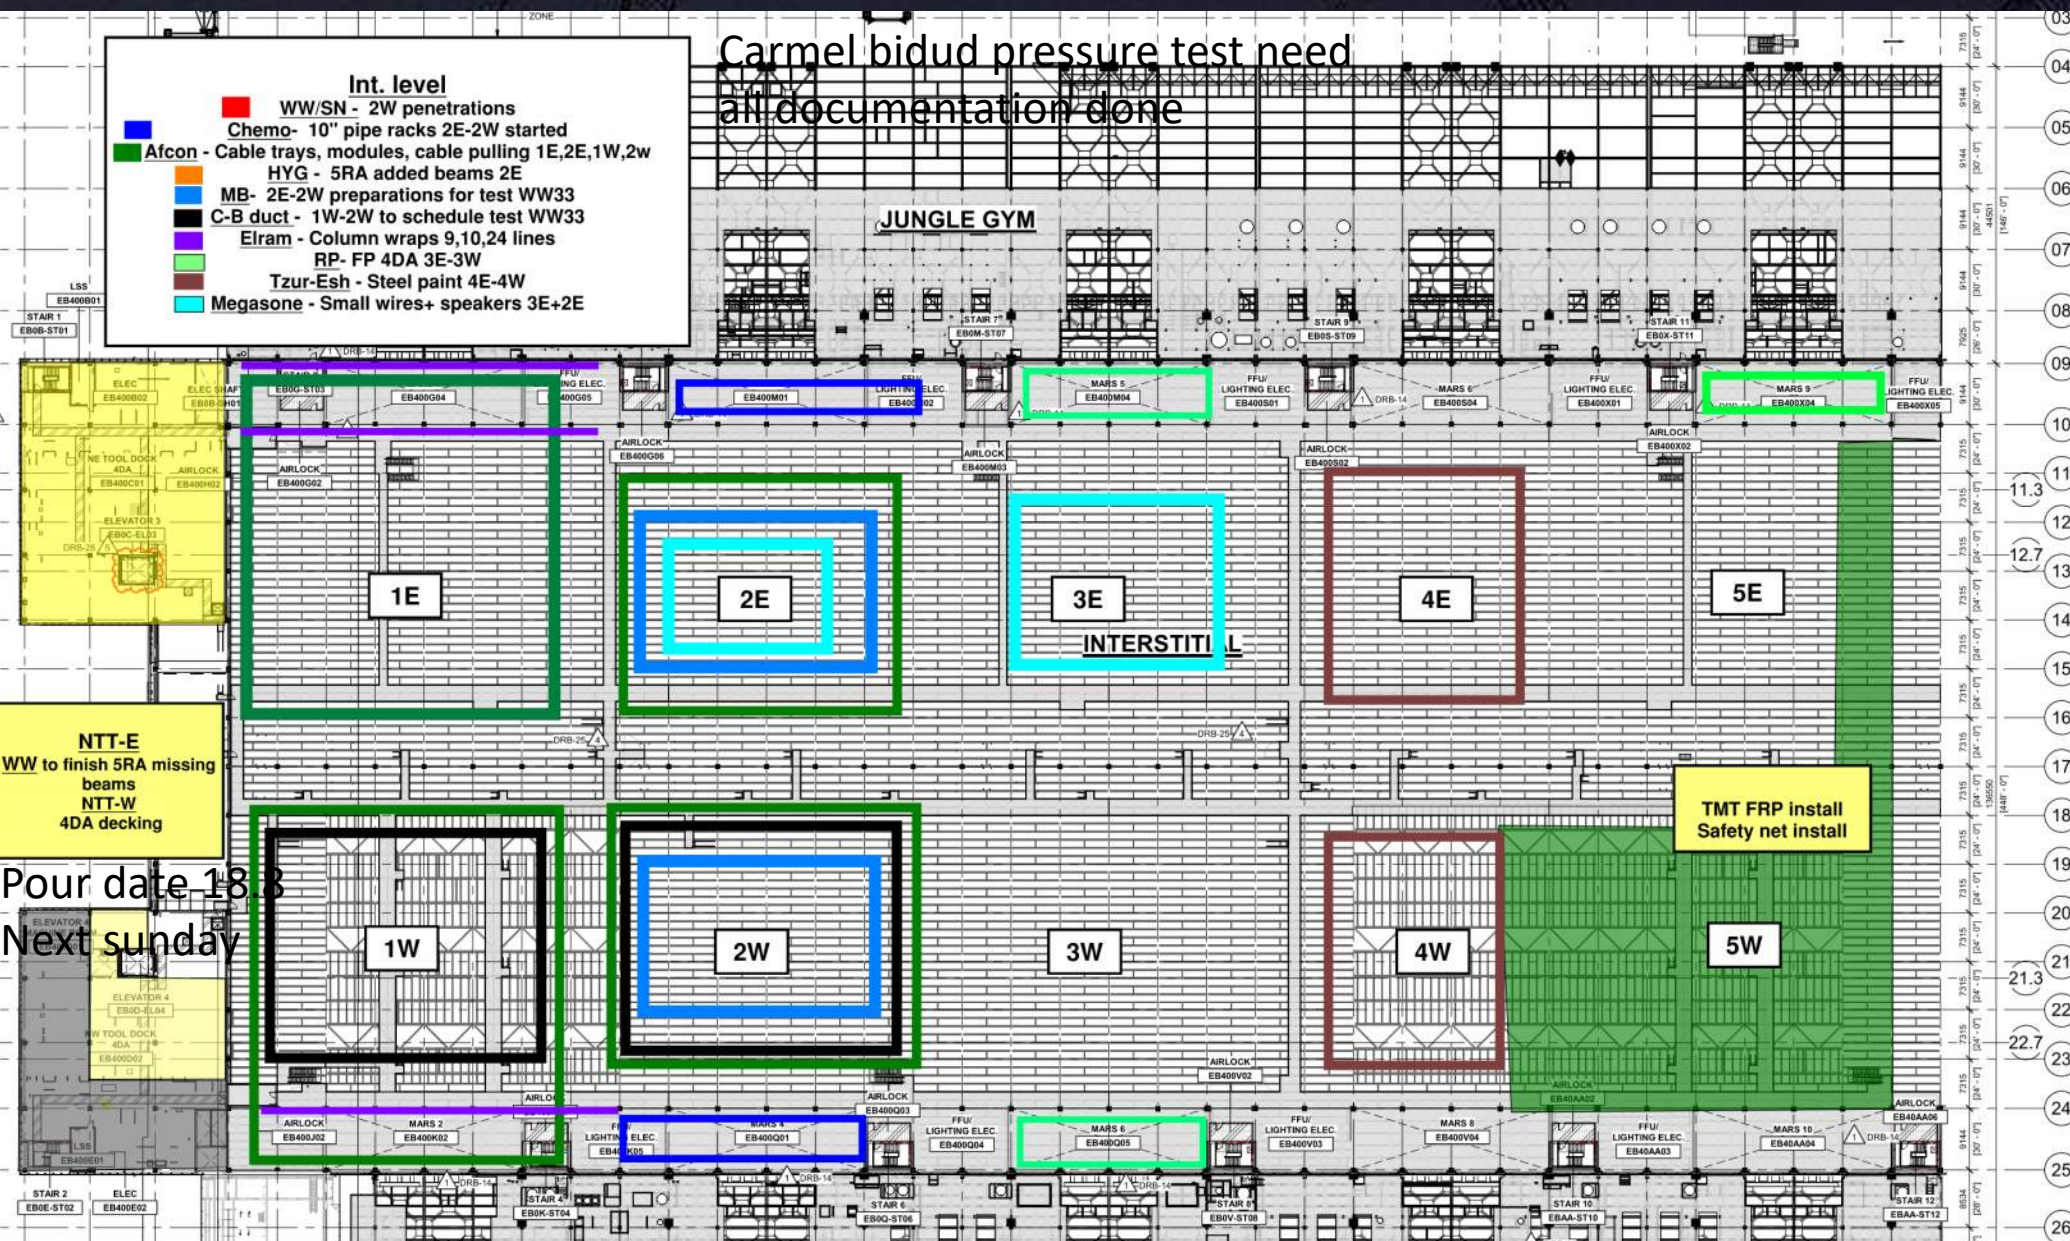


Pour date 18.3
Next sunday

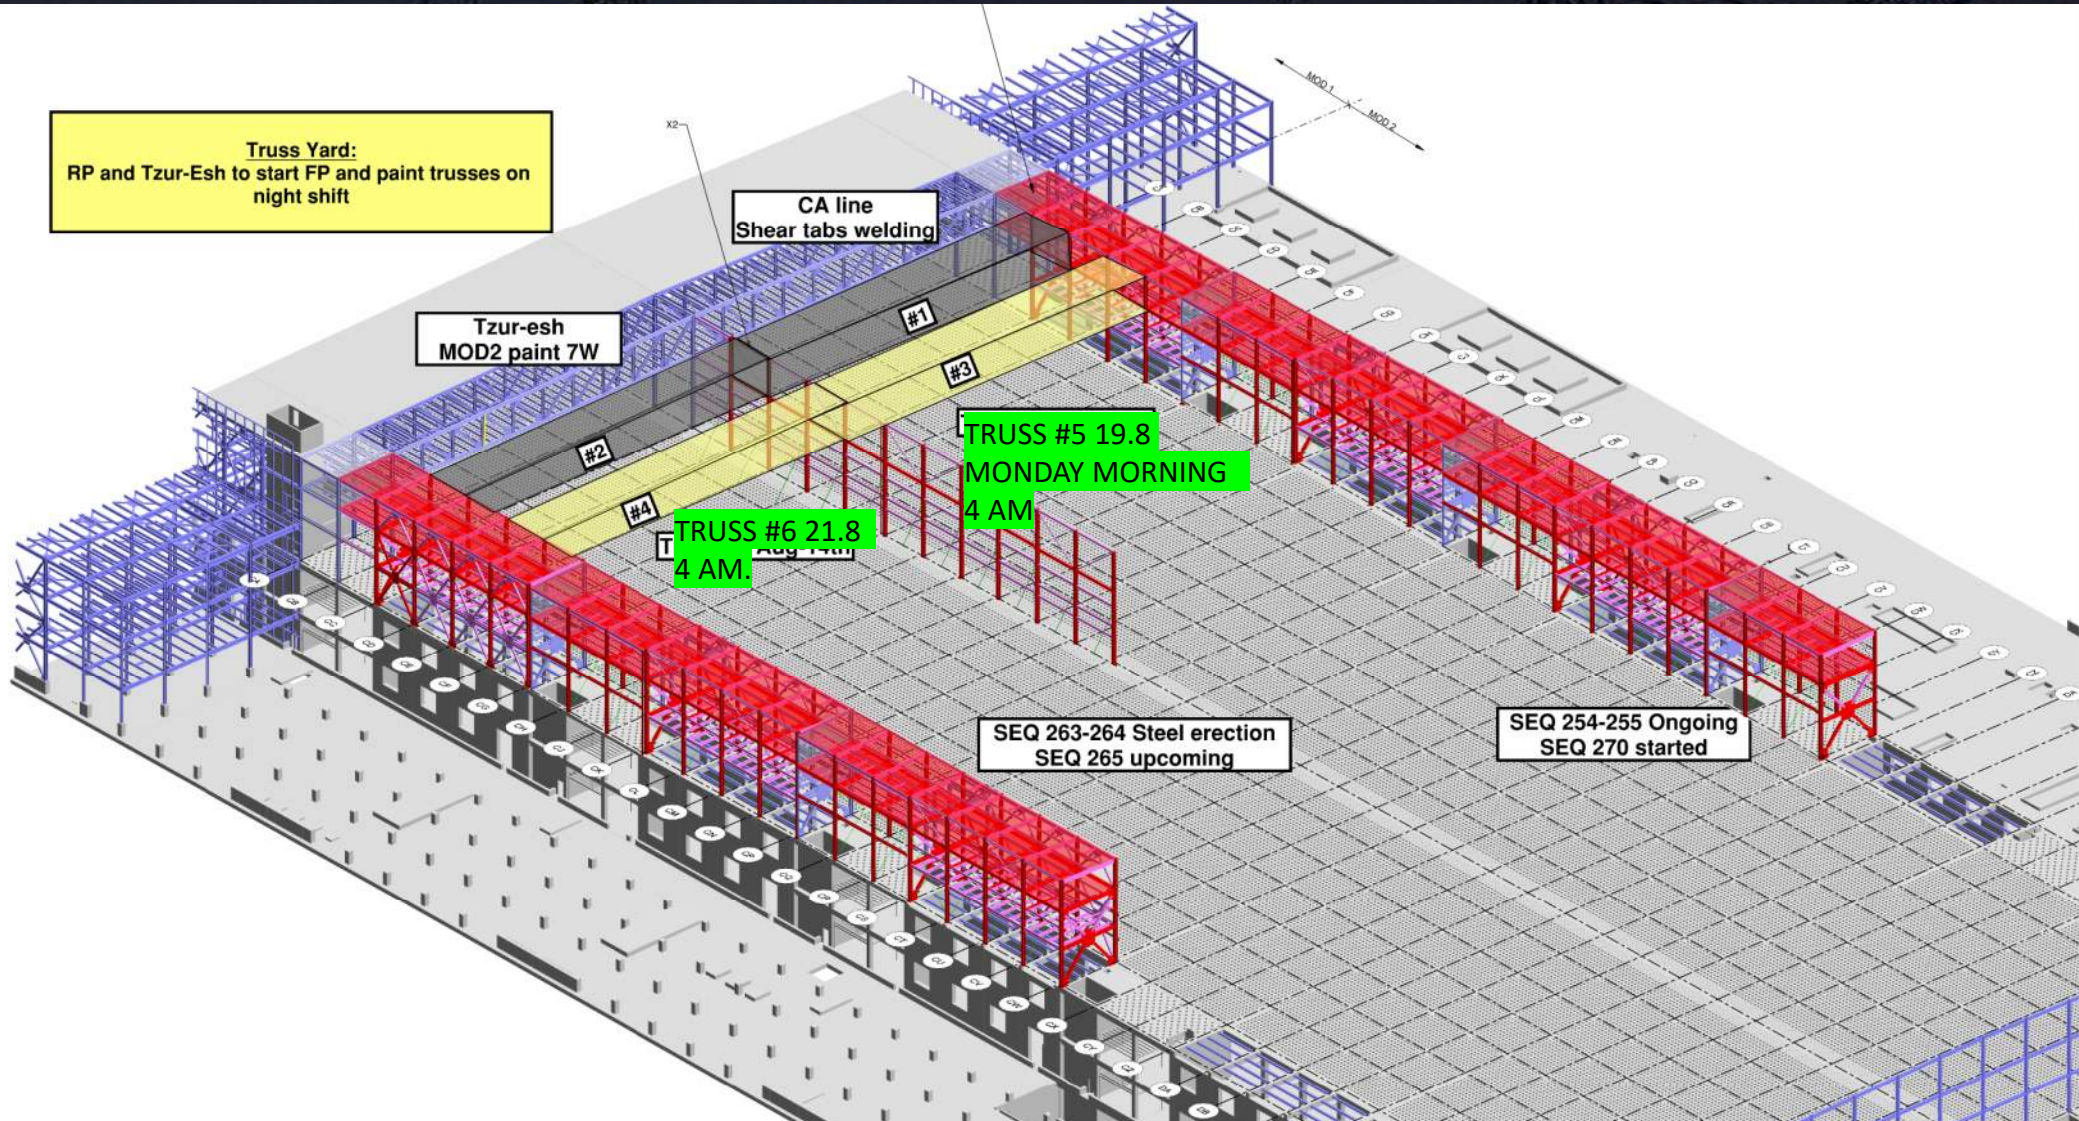


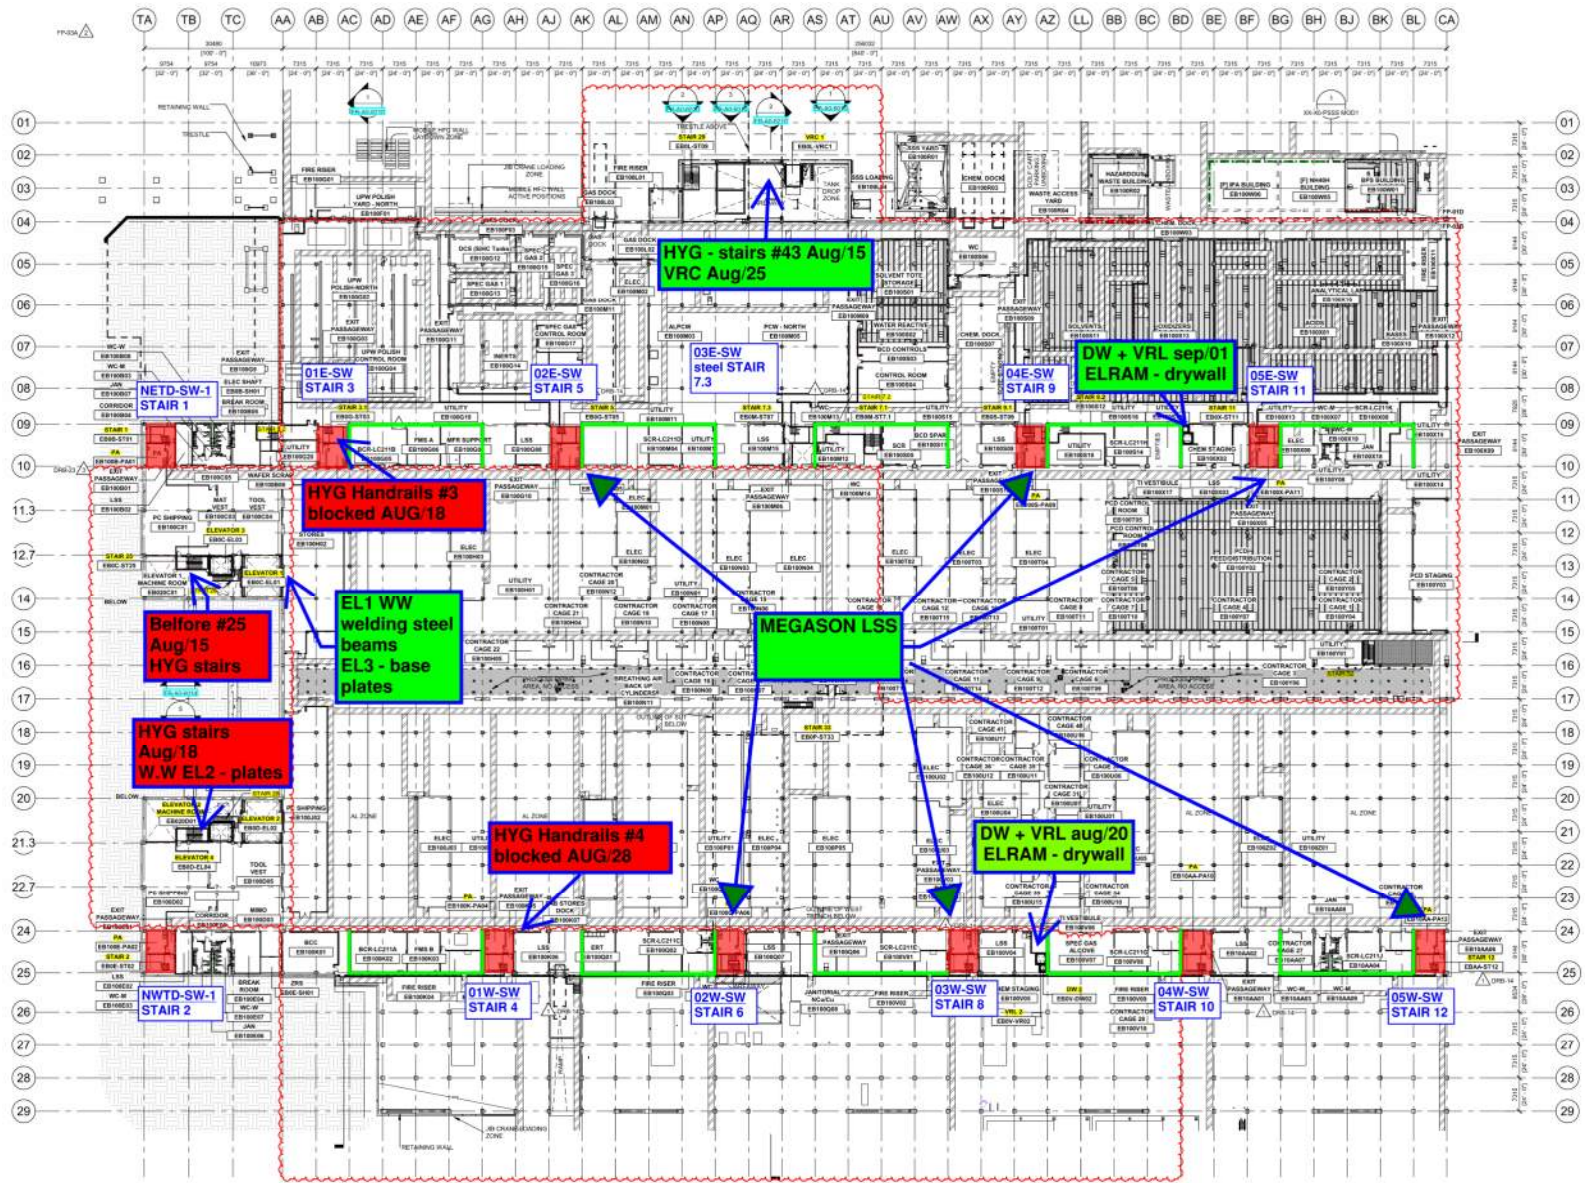

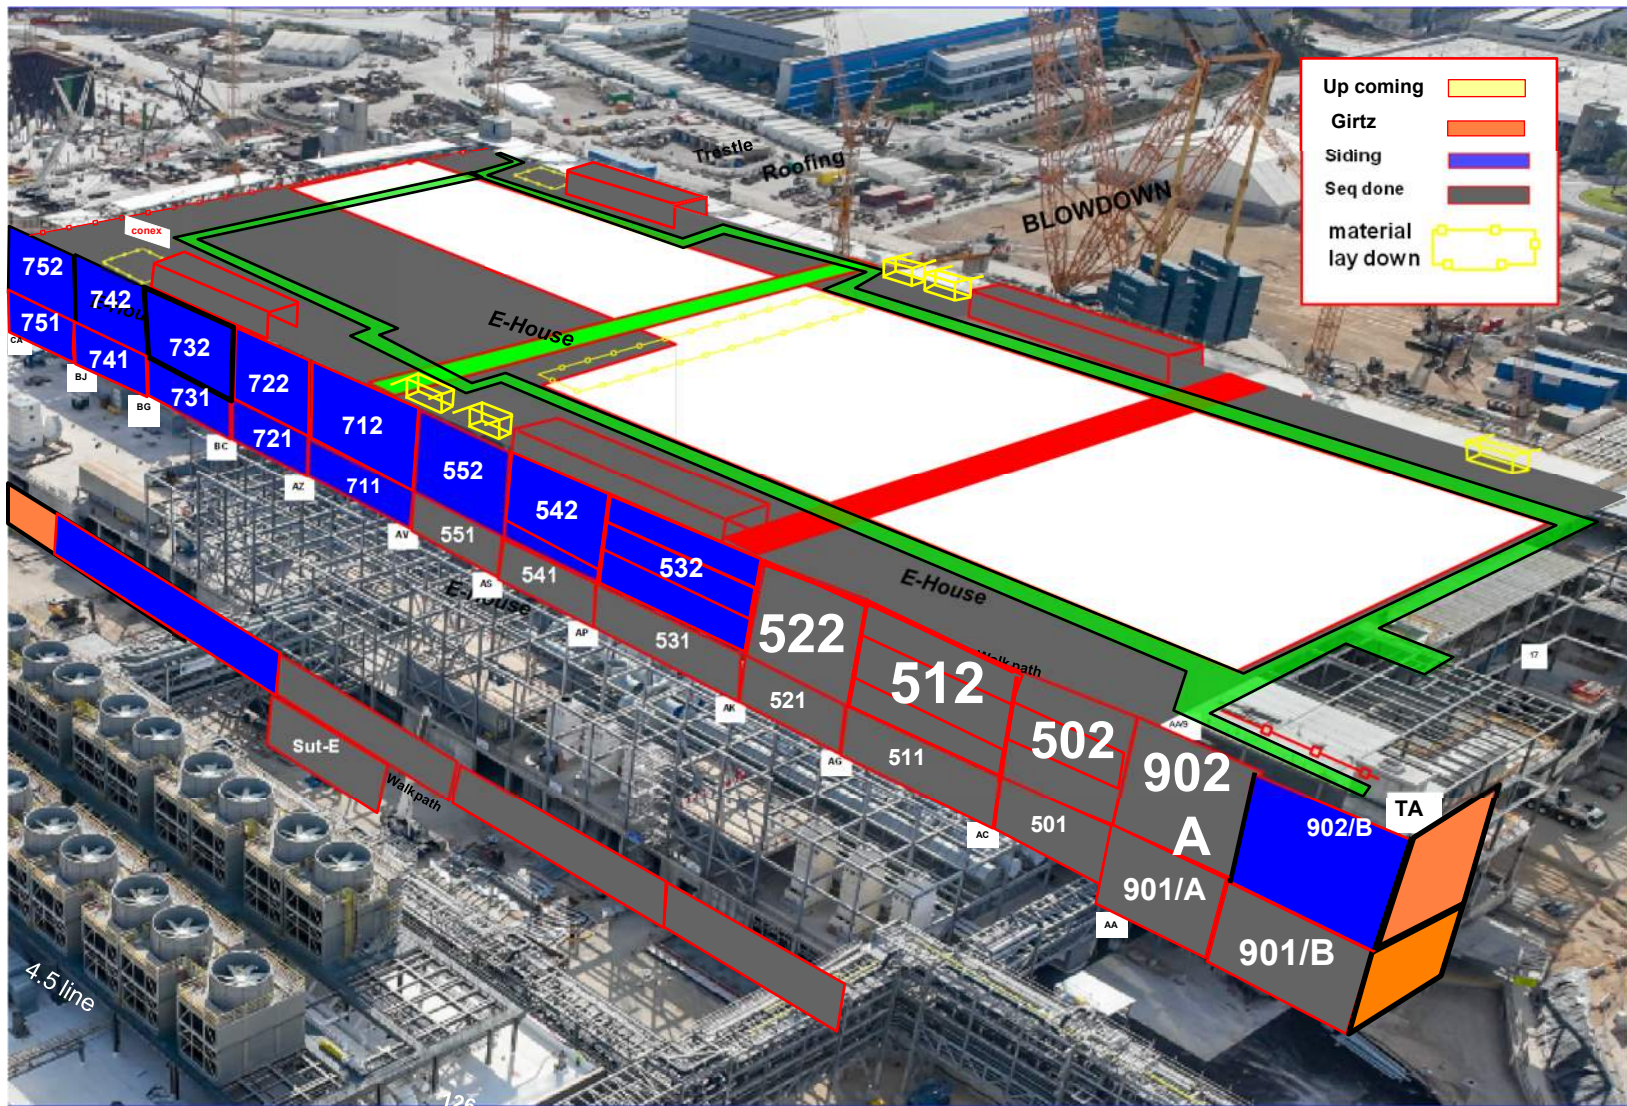

Walkpath

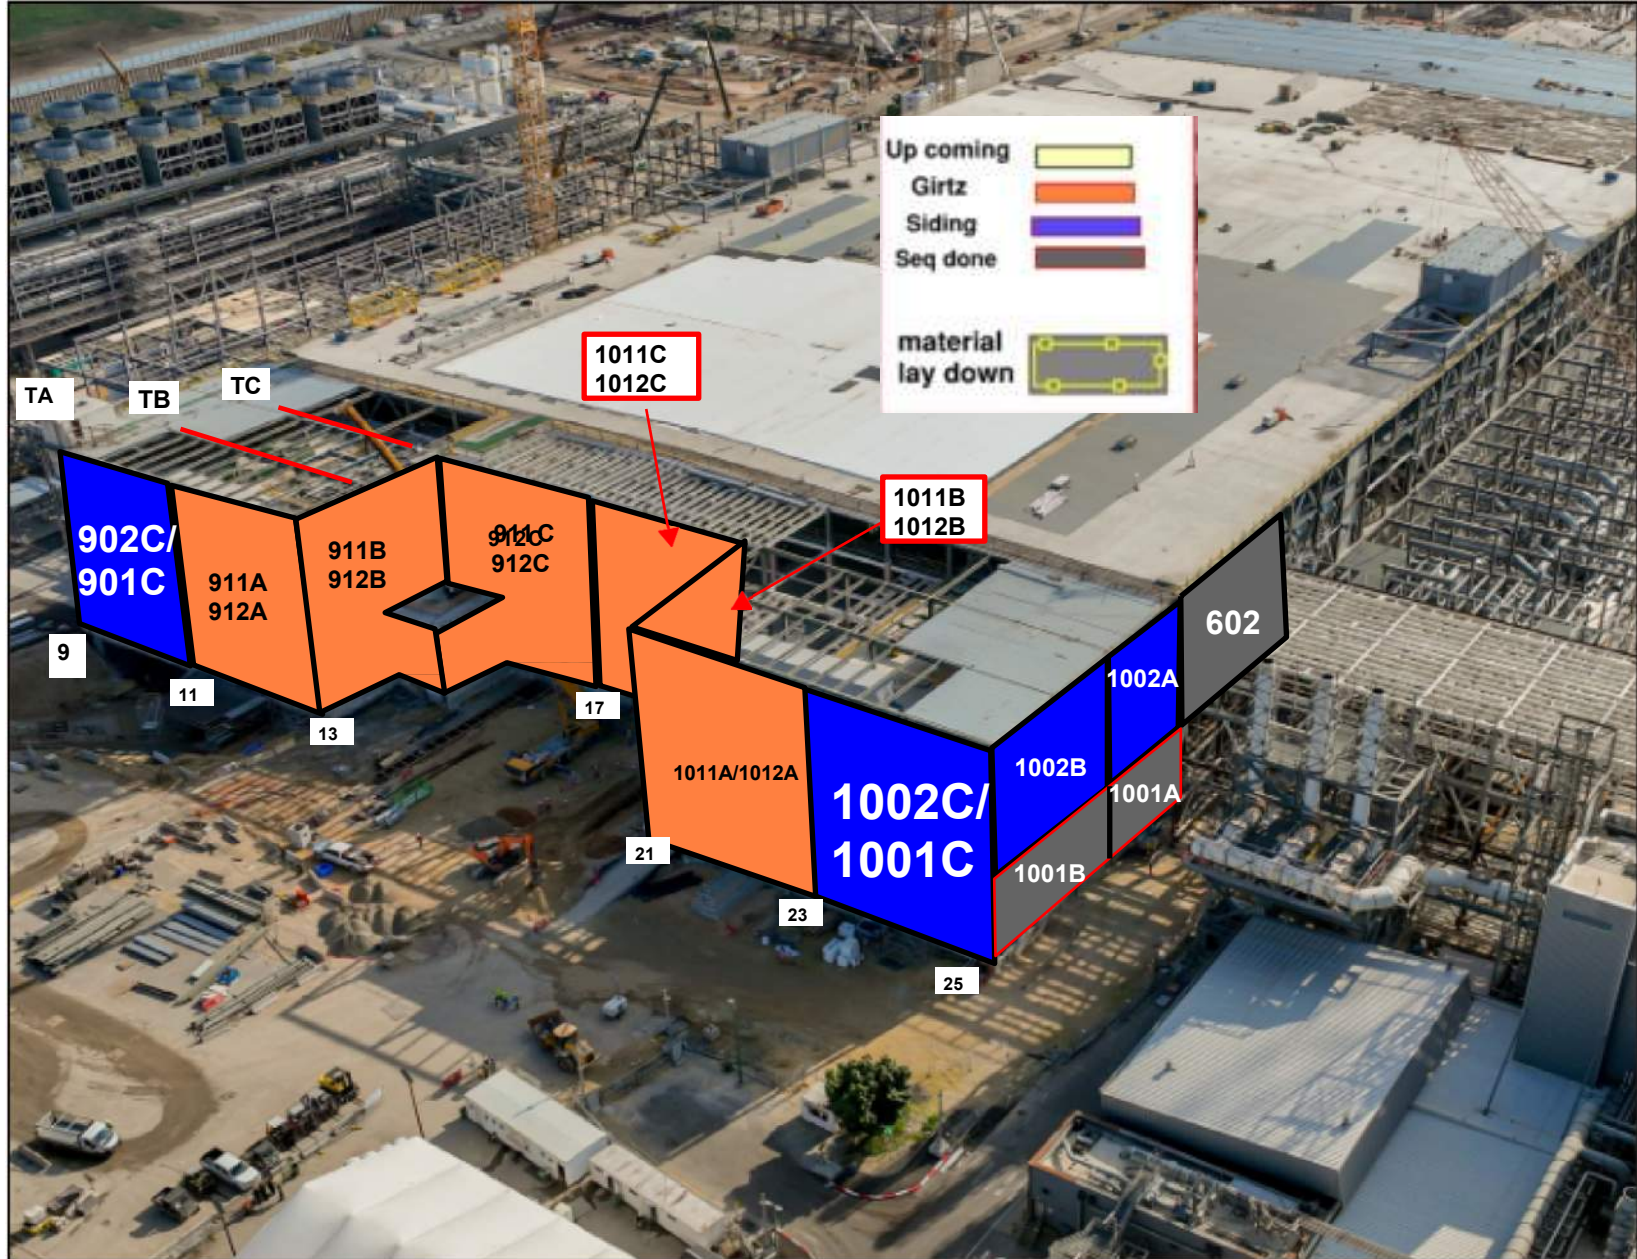


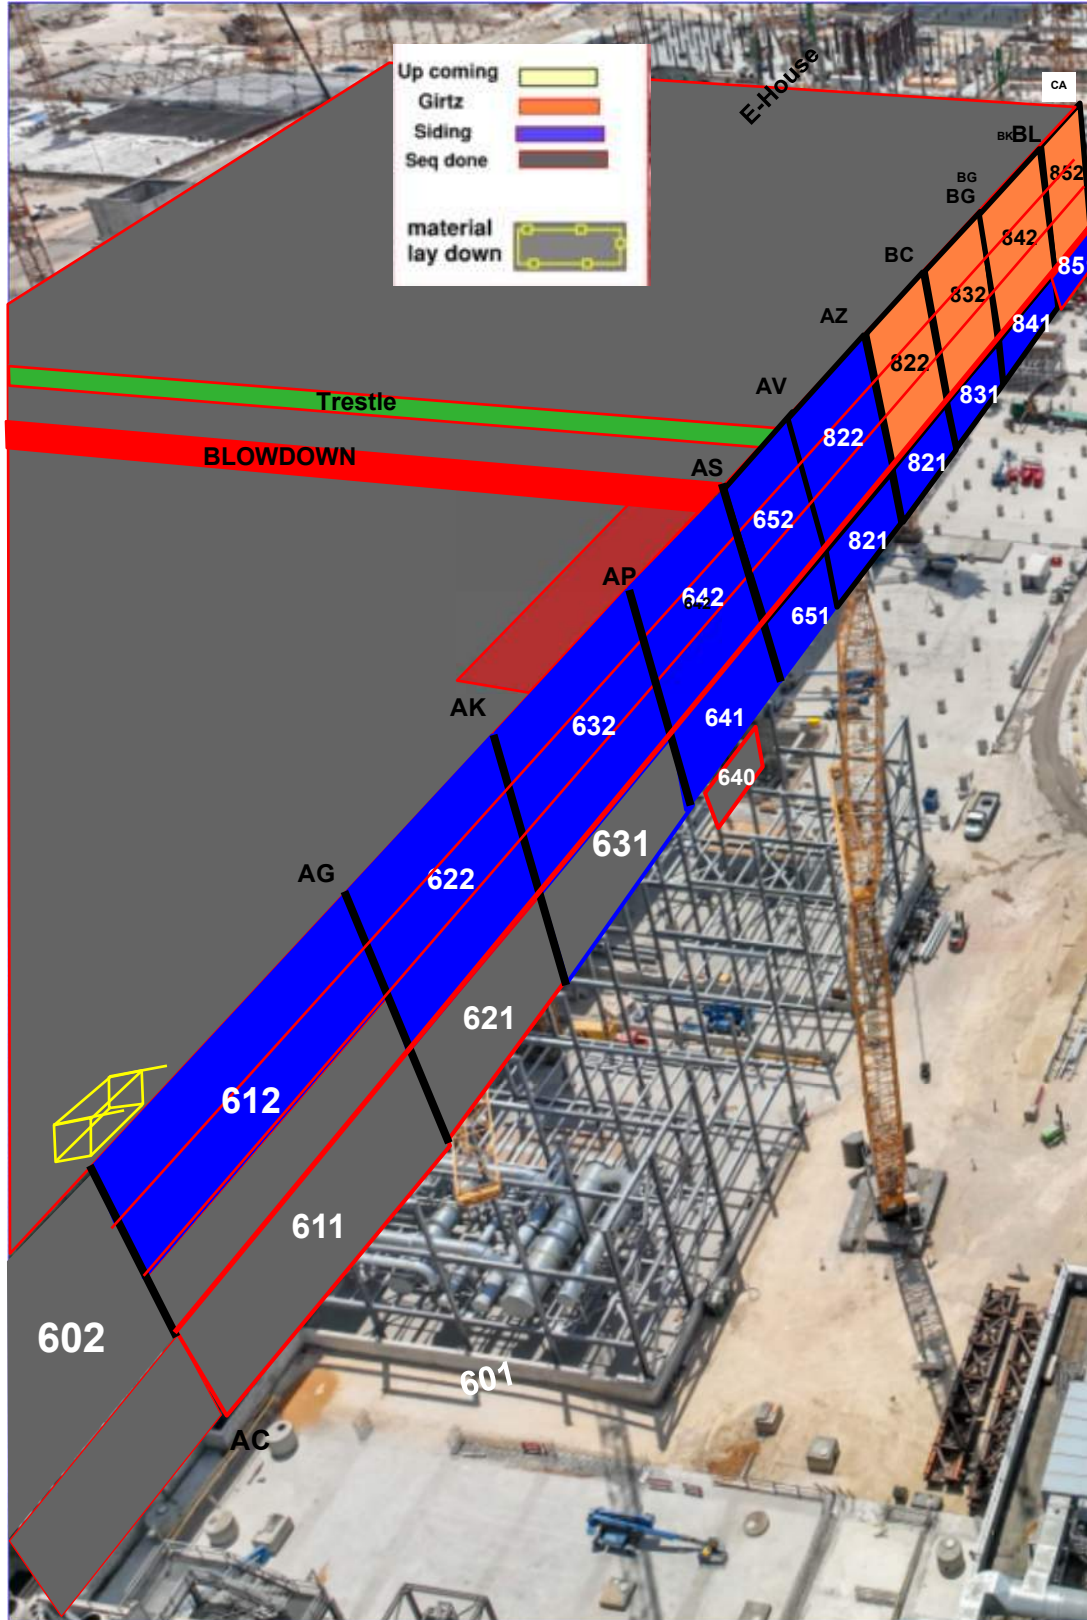

PSSS.1

Utility Level
1YA

PSSS Roof
2SA

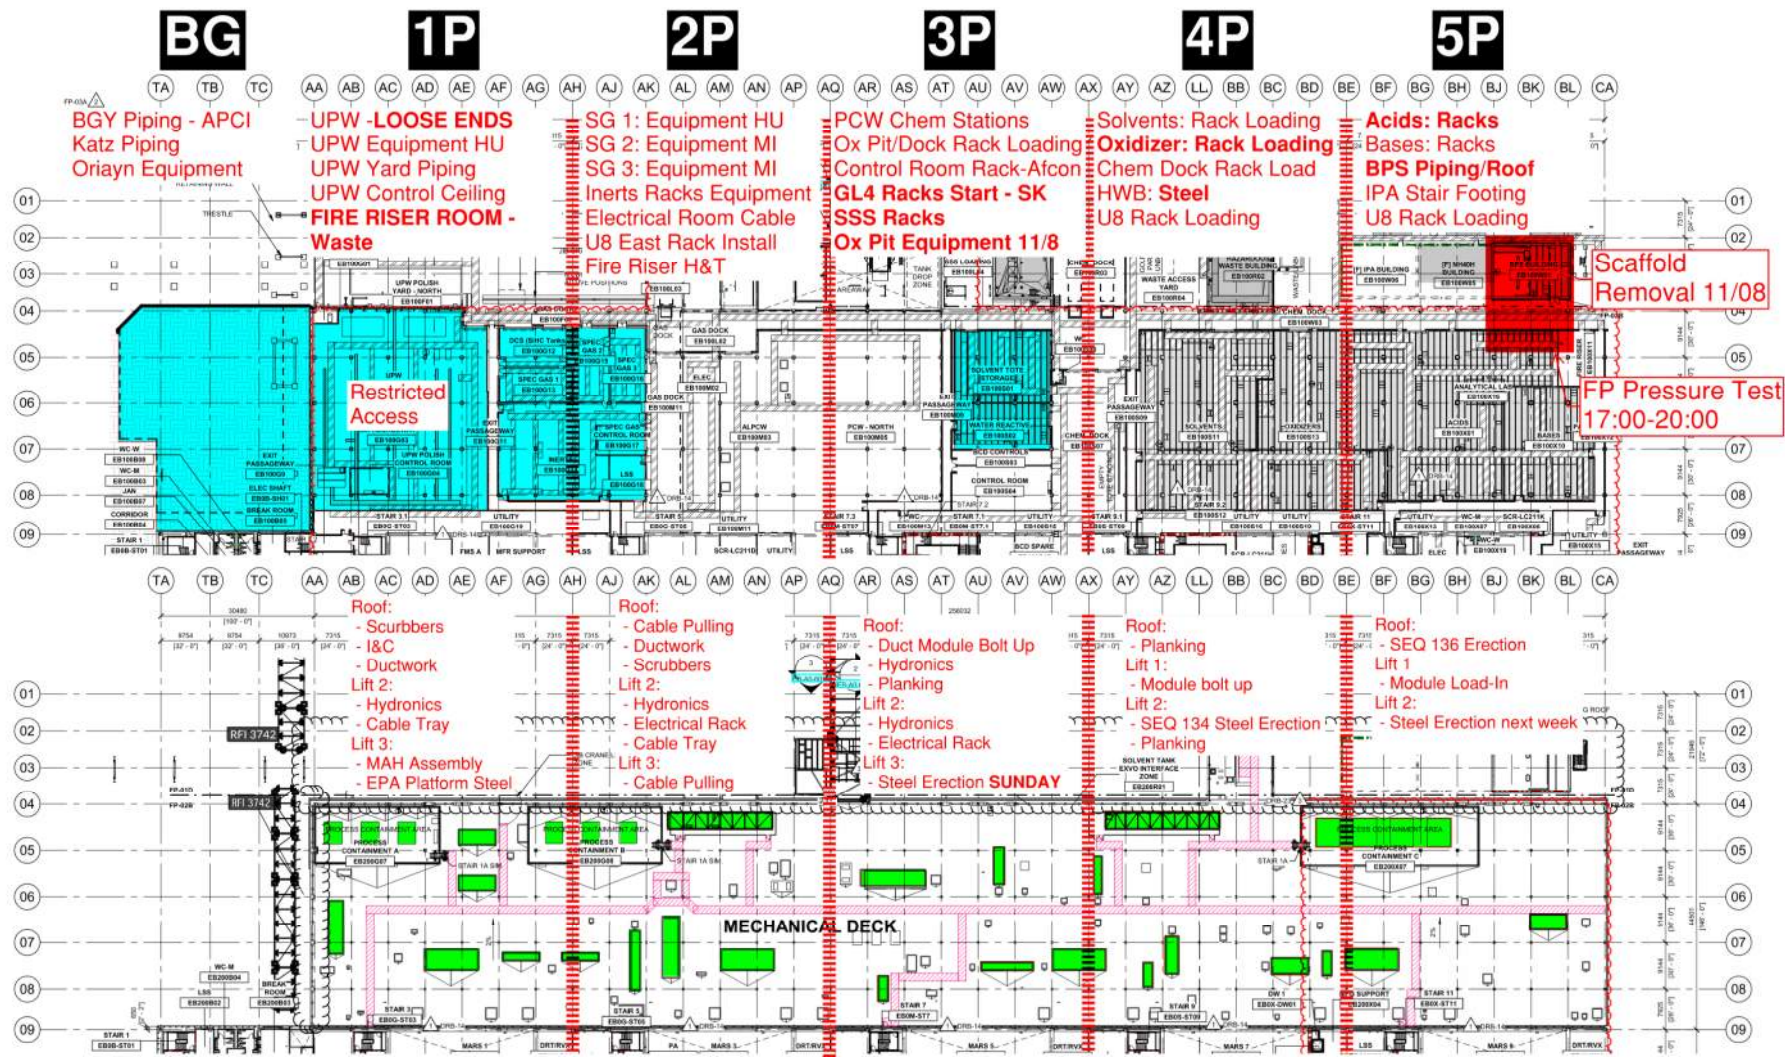

Scaffold
Removal 11/08

FP Pressure Test
17:00-20:00



PSSS P1
PachTaas Operation
Plates: 15-08-2024
Air Blower: 20-08-2024
EPA Platform: 26-08-2024

Single
EPA Platform

Fan





WJG 01J, 02J LIFT 2 & 3





WJG 03J, 04J, 05J LIFT 2 & 3




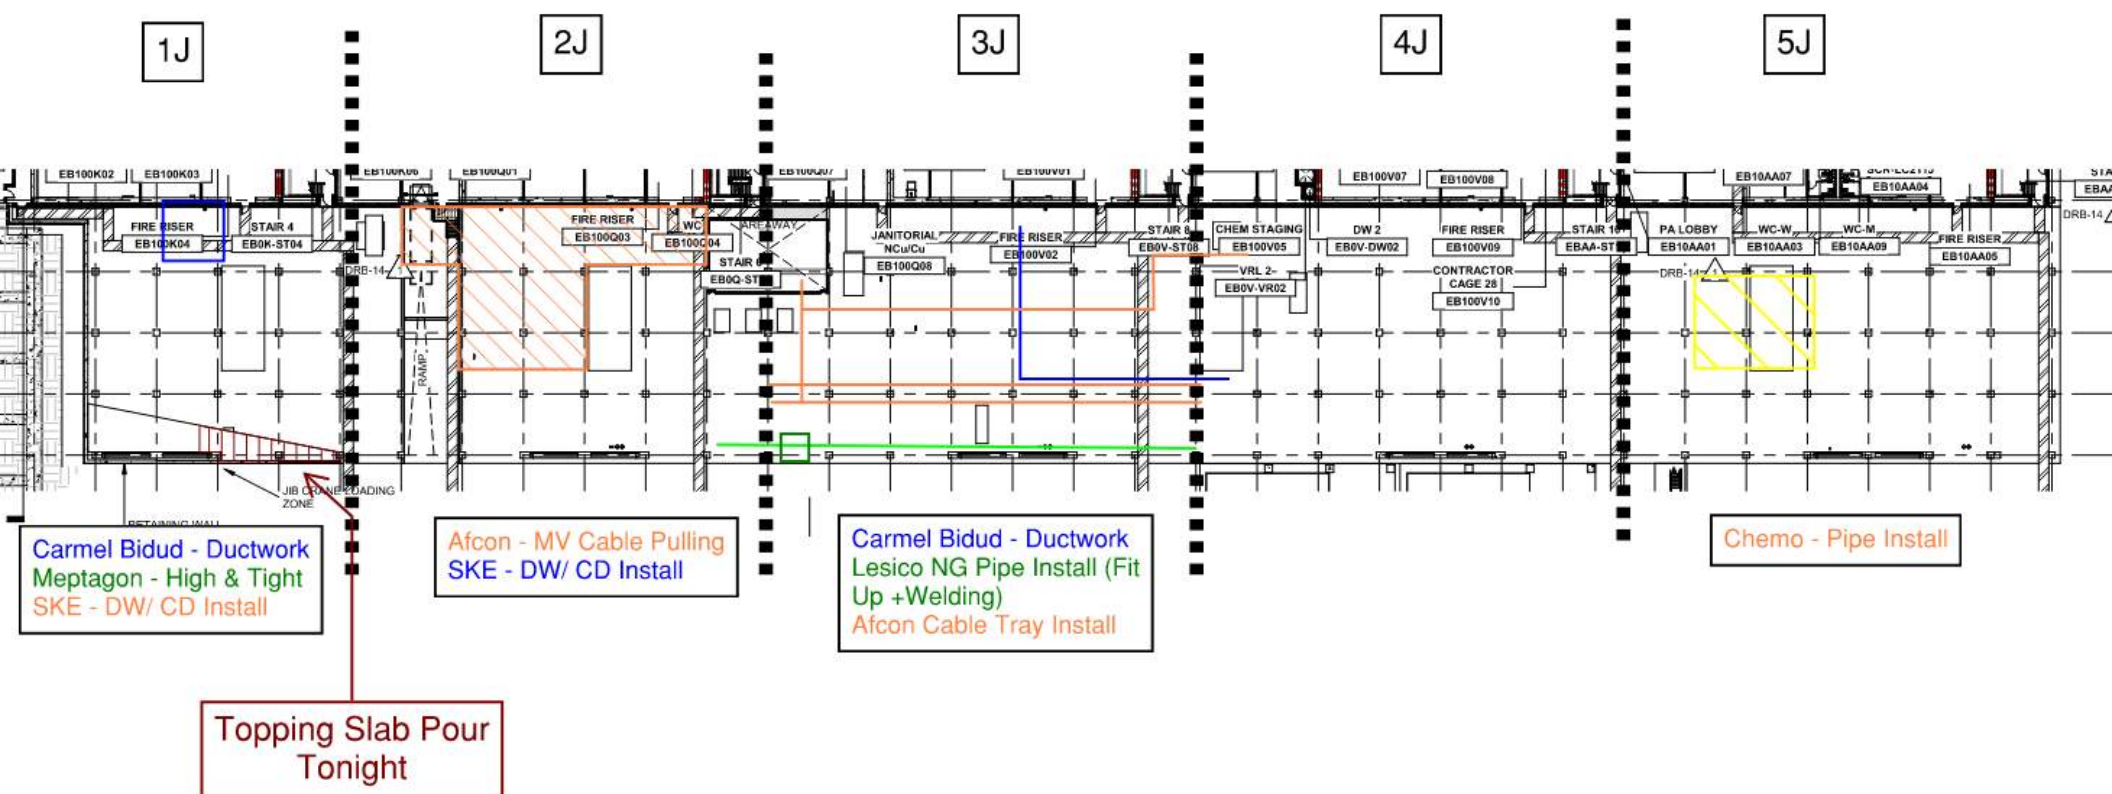


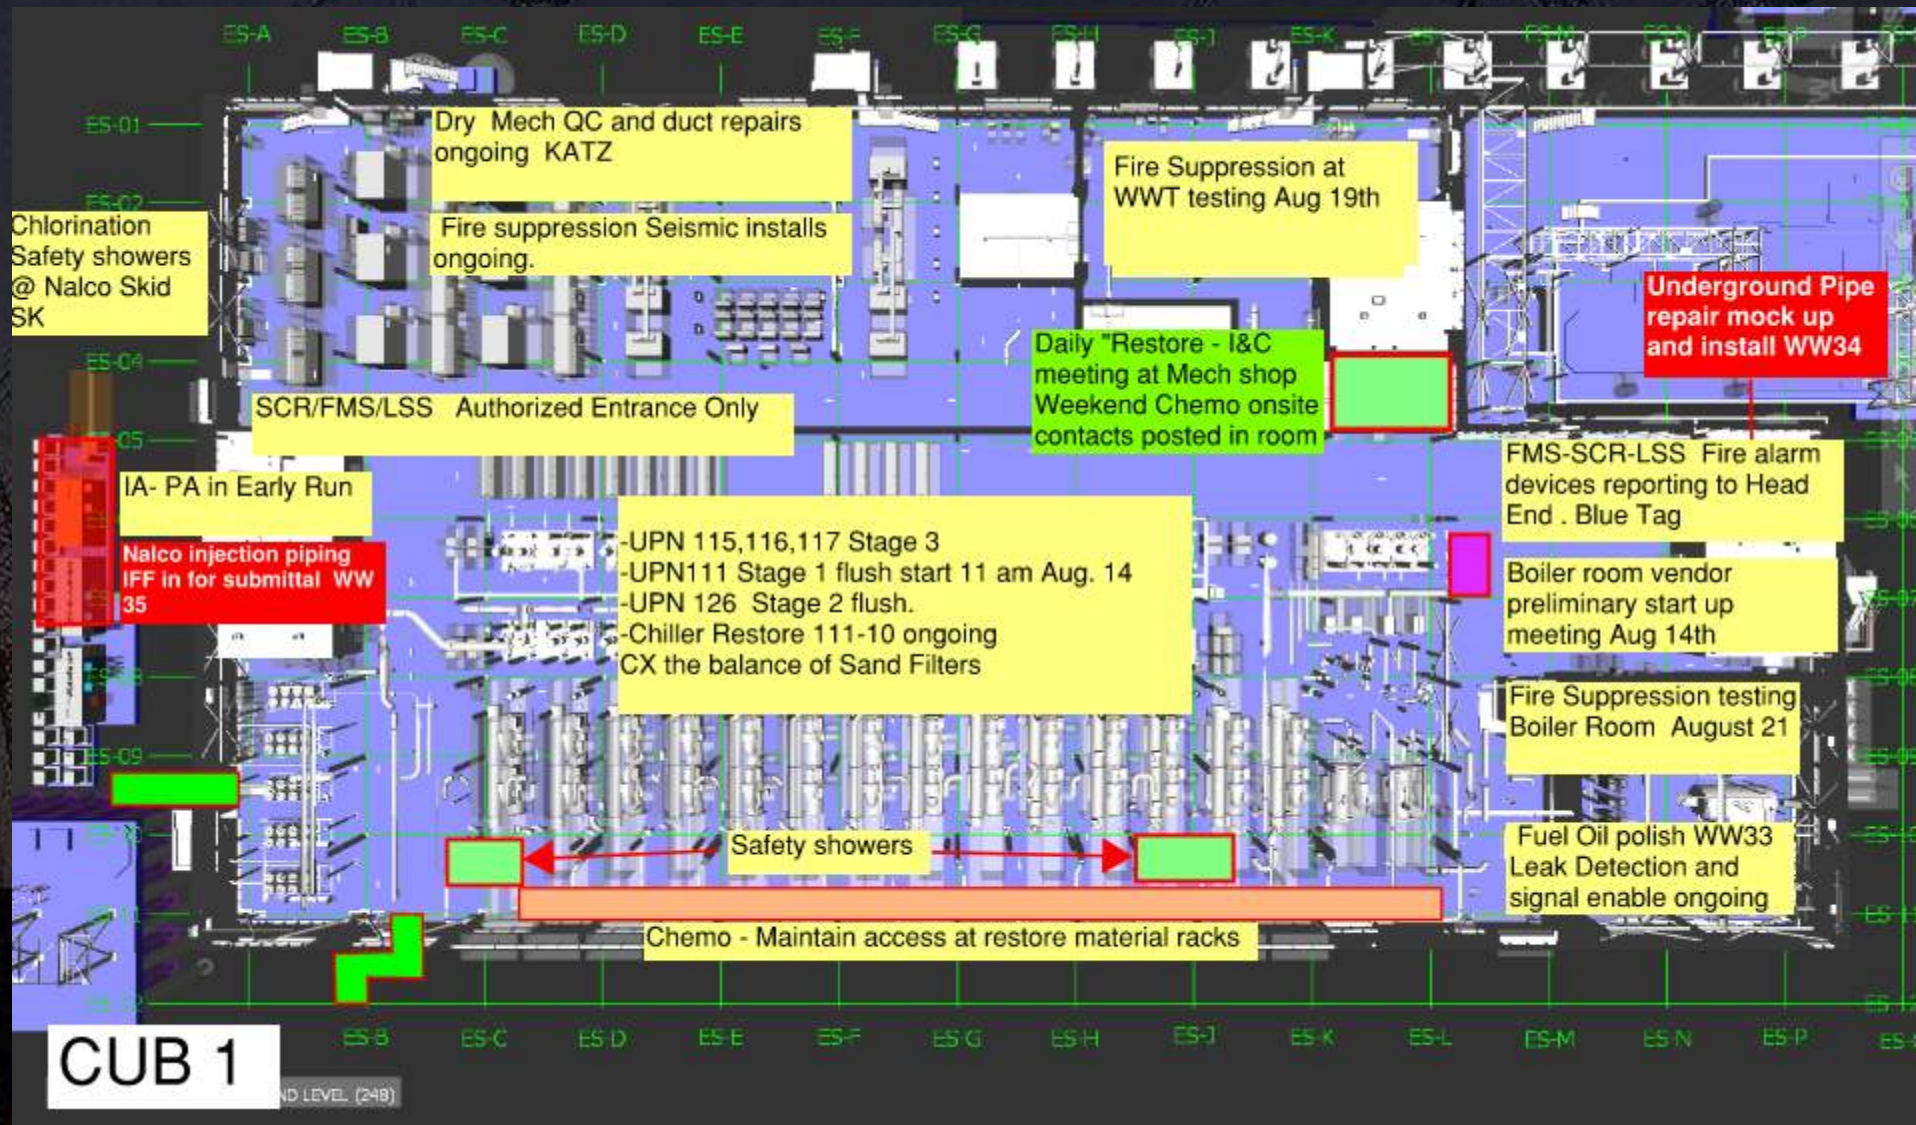


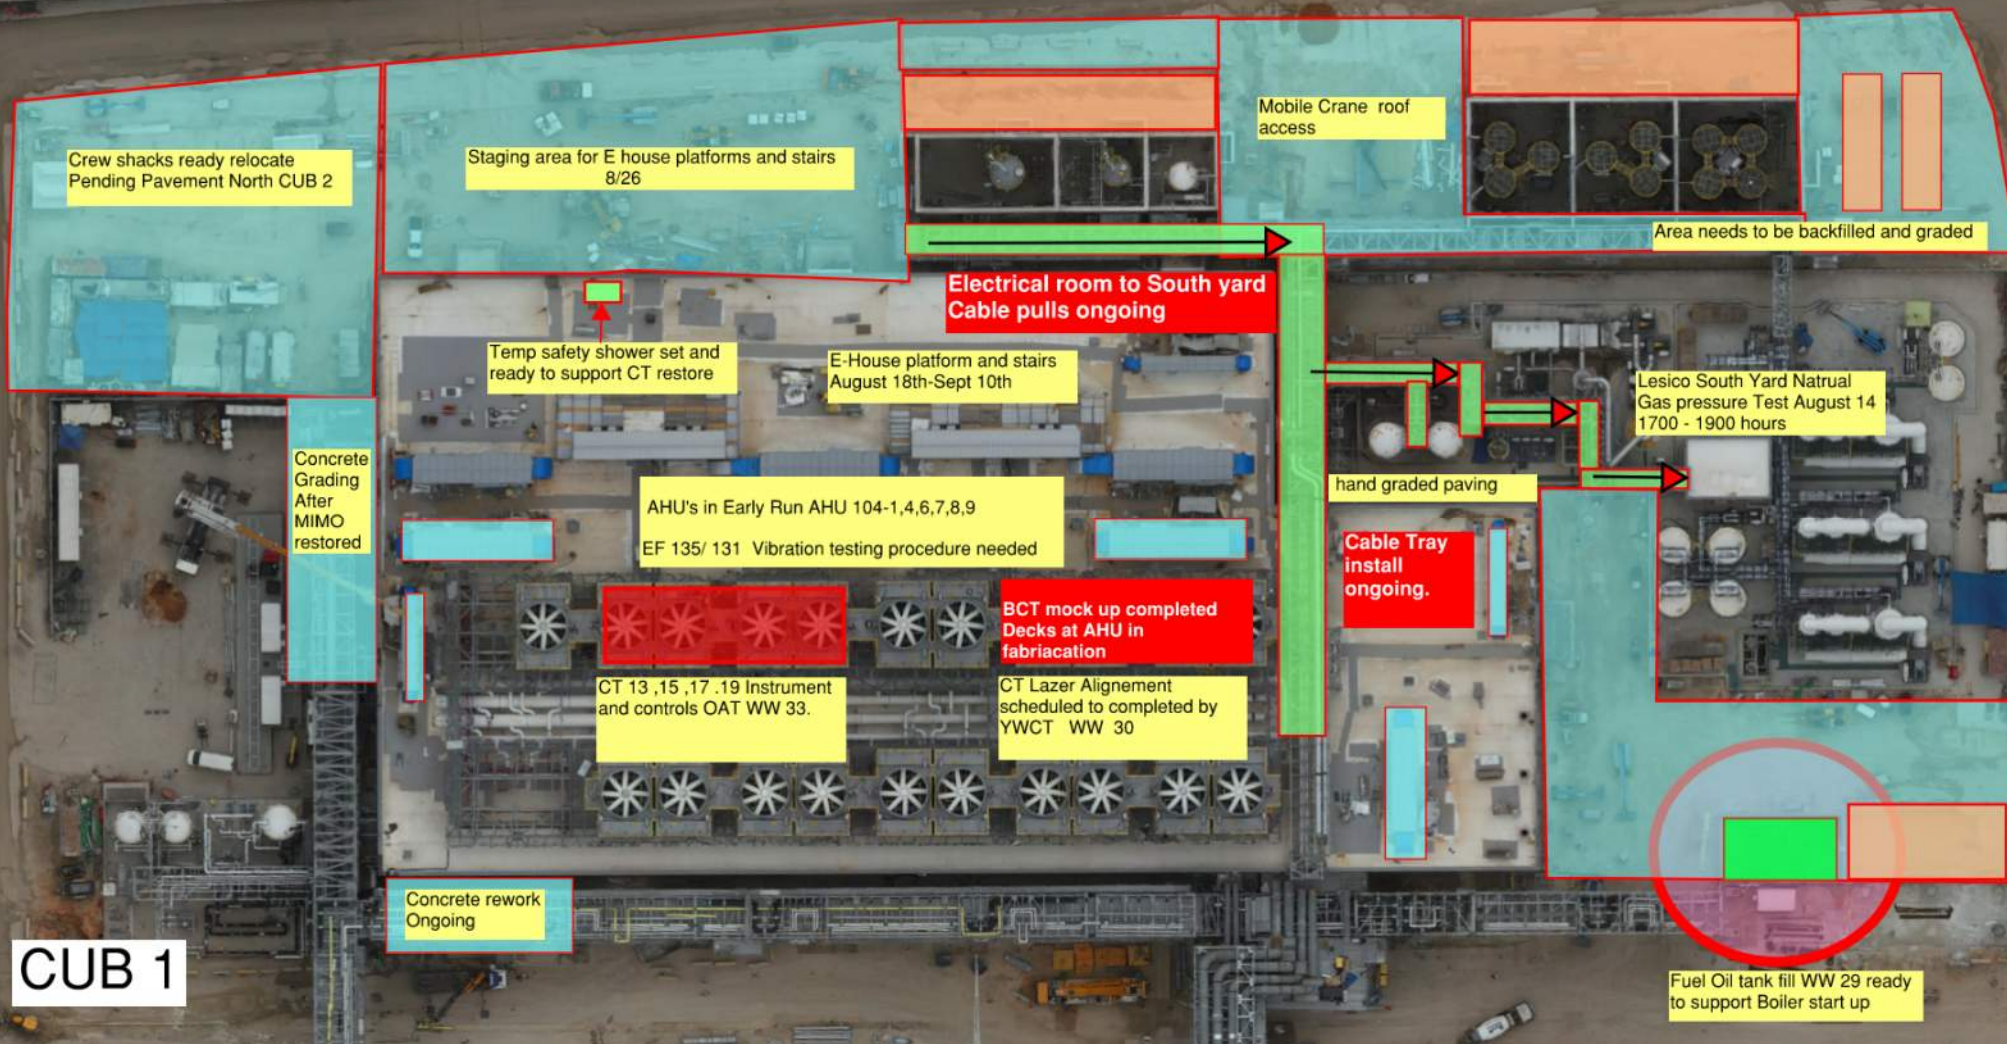

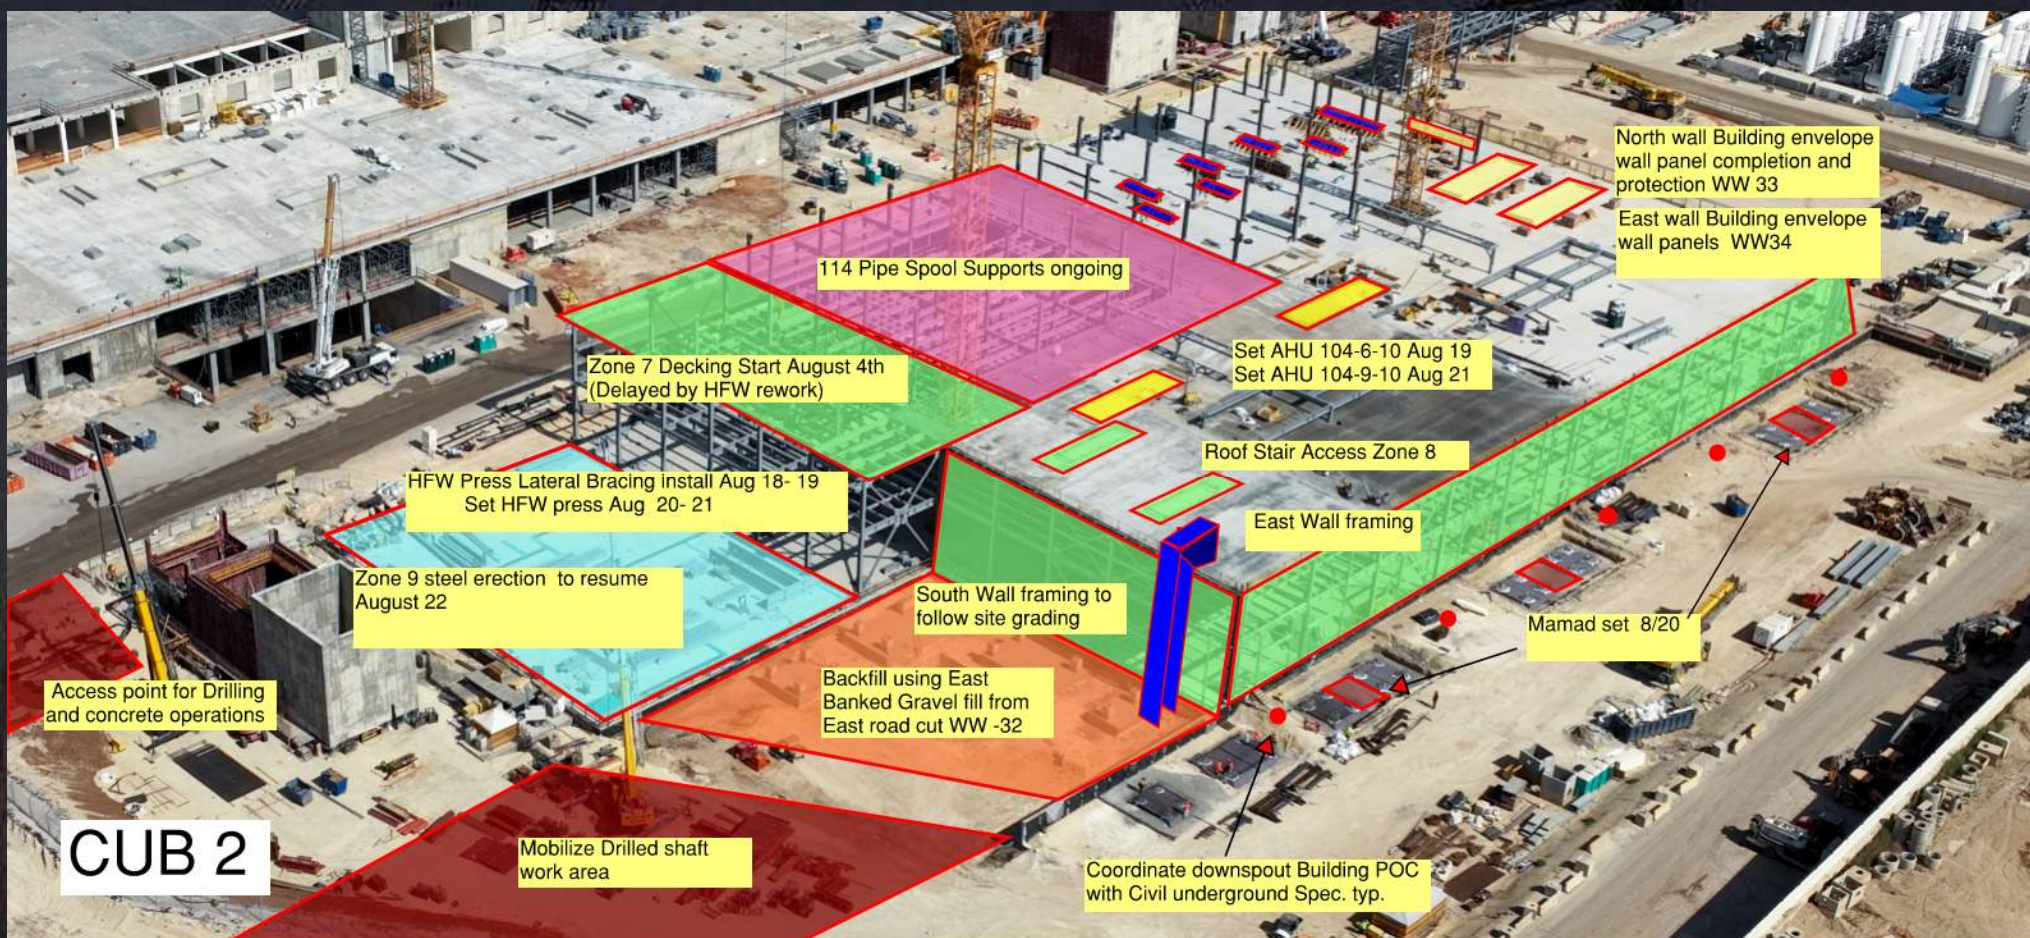

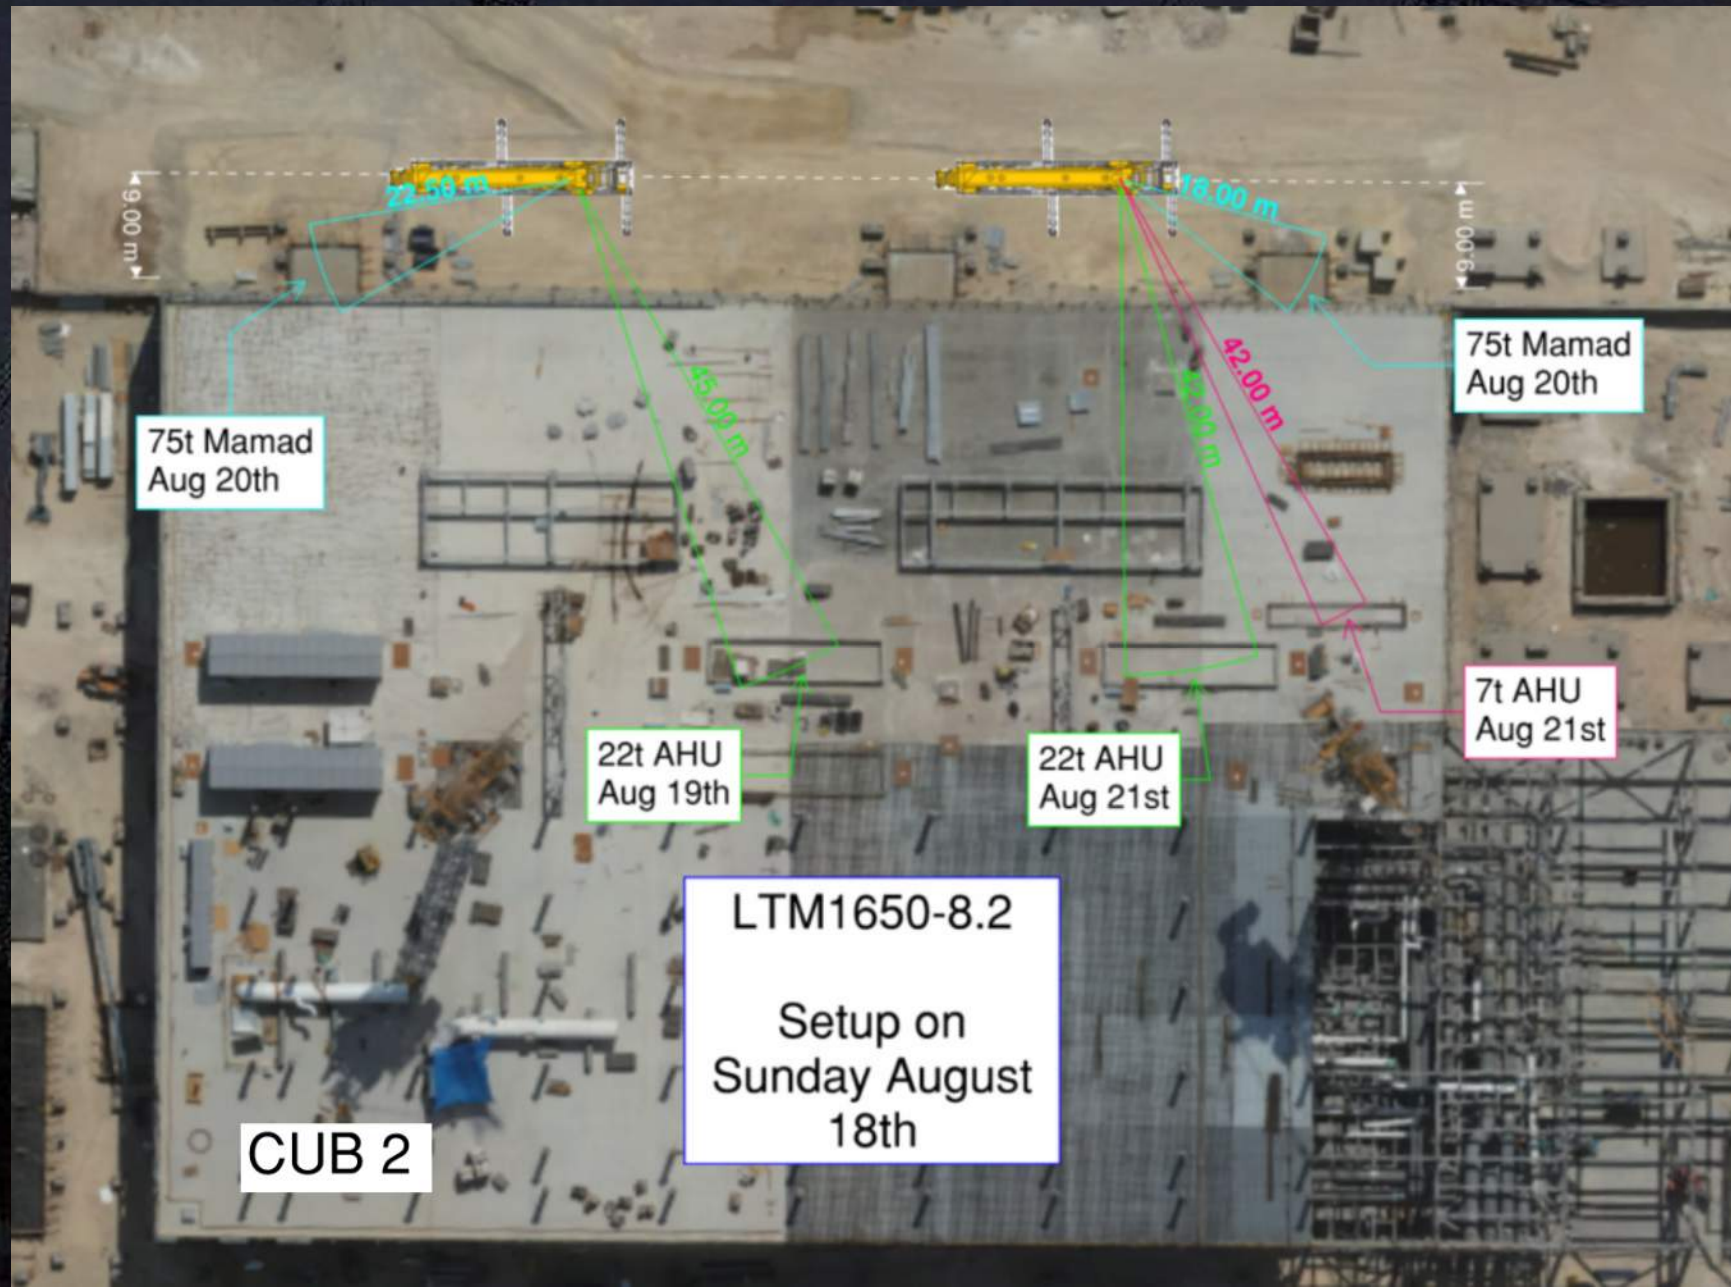


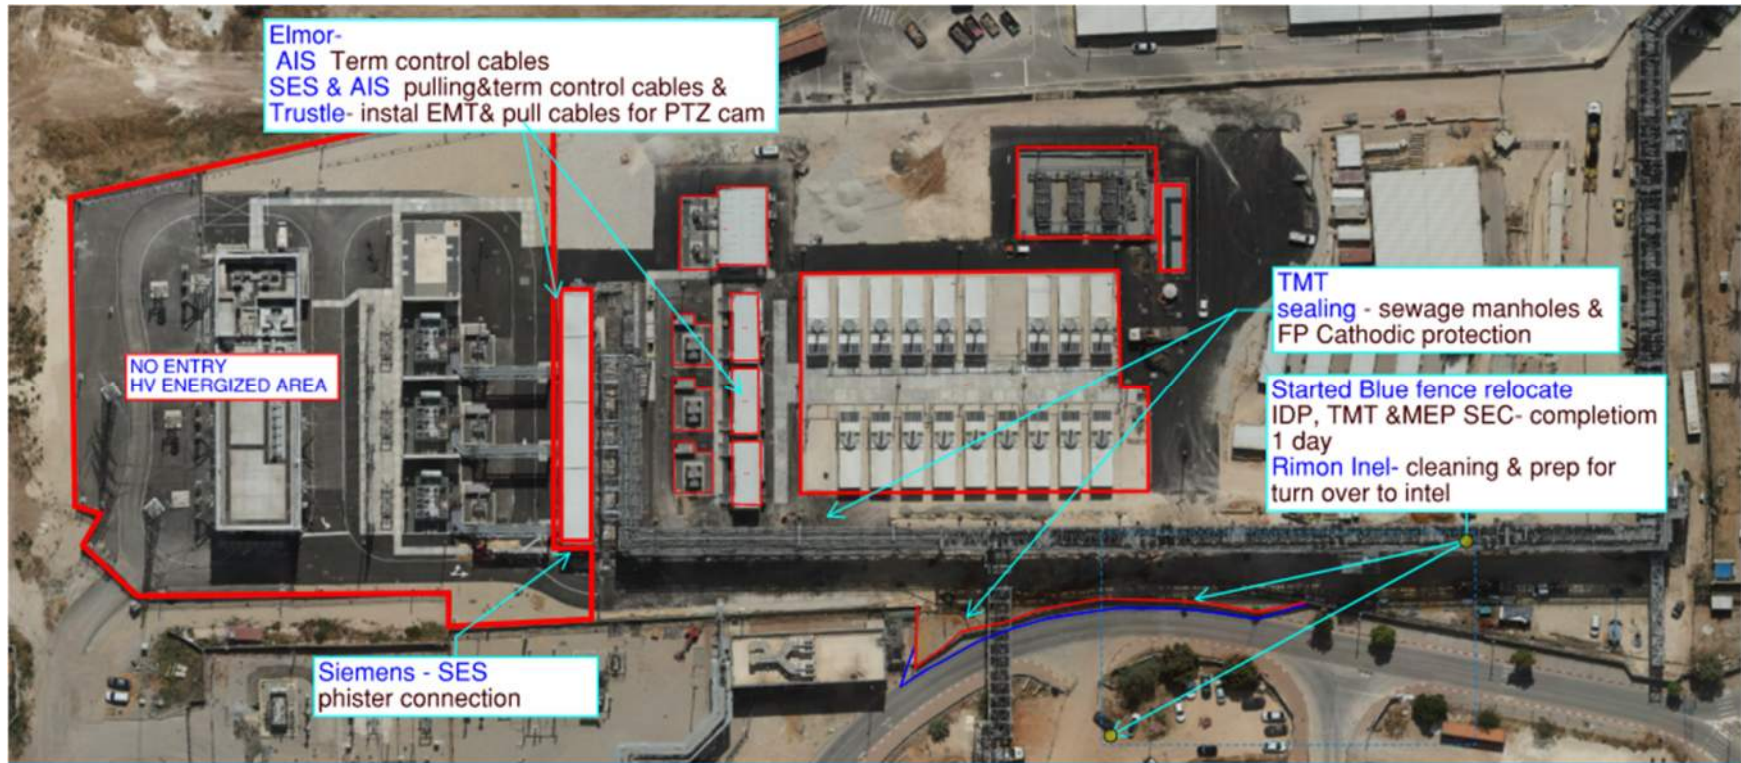

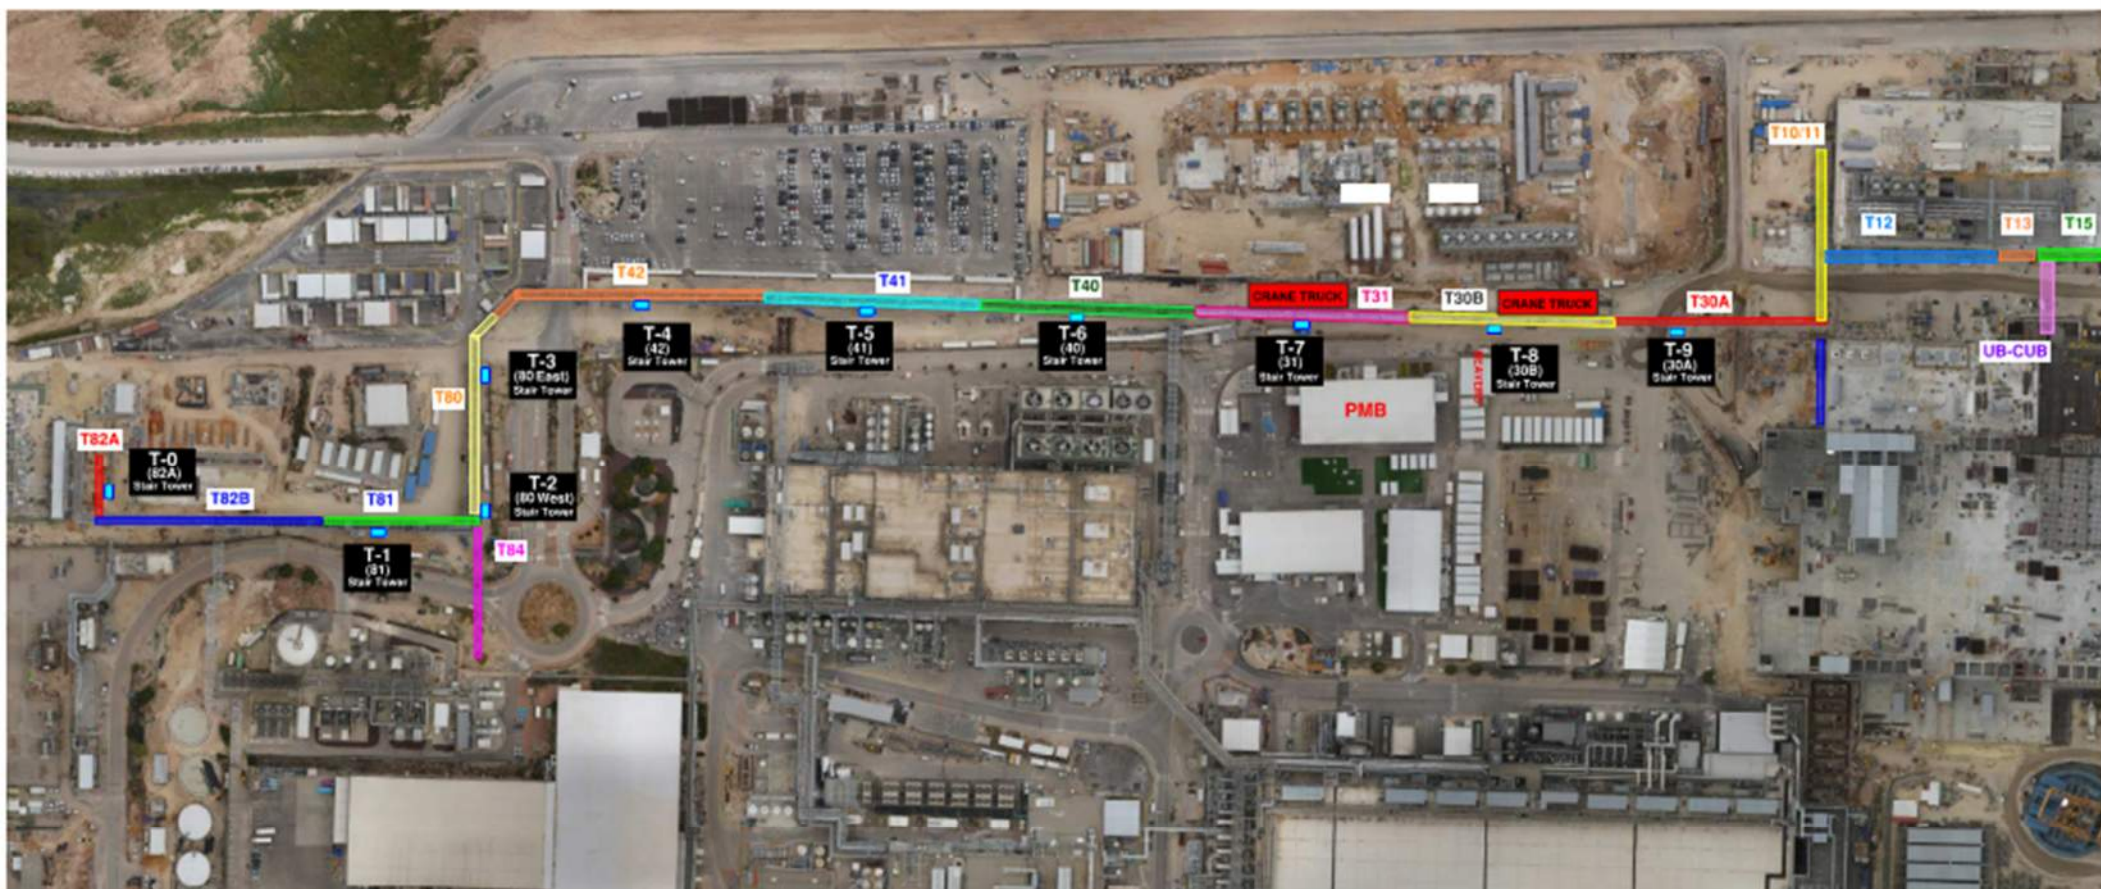


Trestle - MOD 2 Steel erection


T-17 Lvl 1

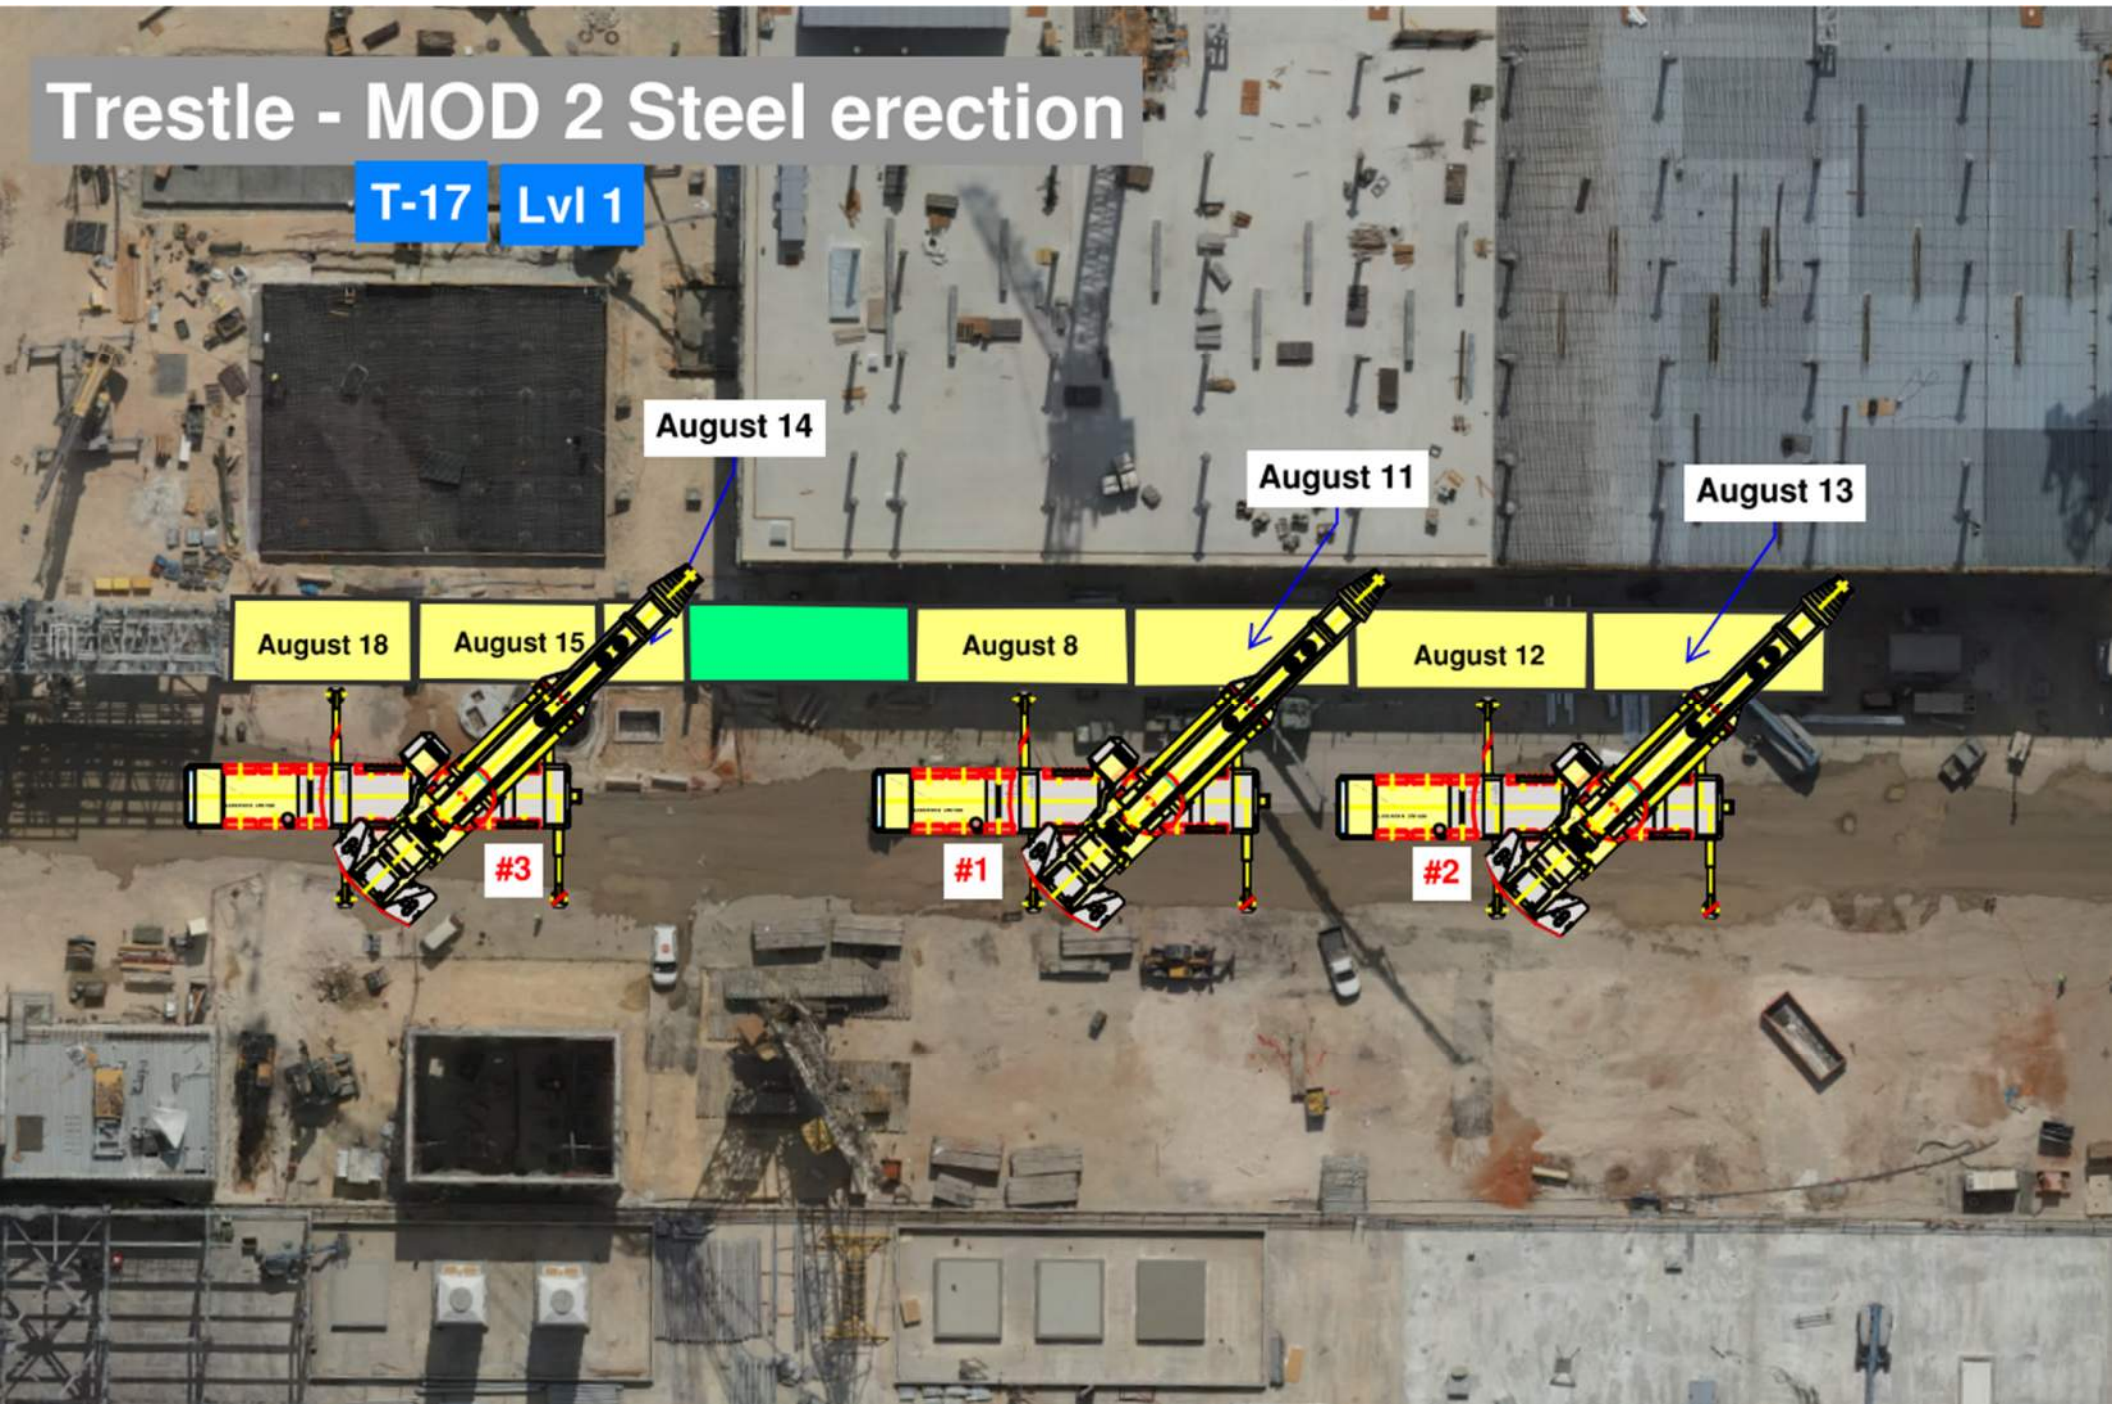

Trestle - MOD 2 Steel erection

T-17 Lvl 2

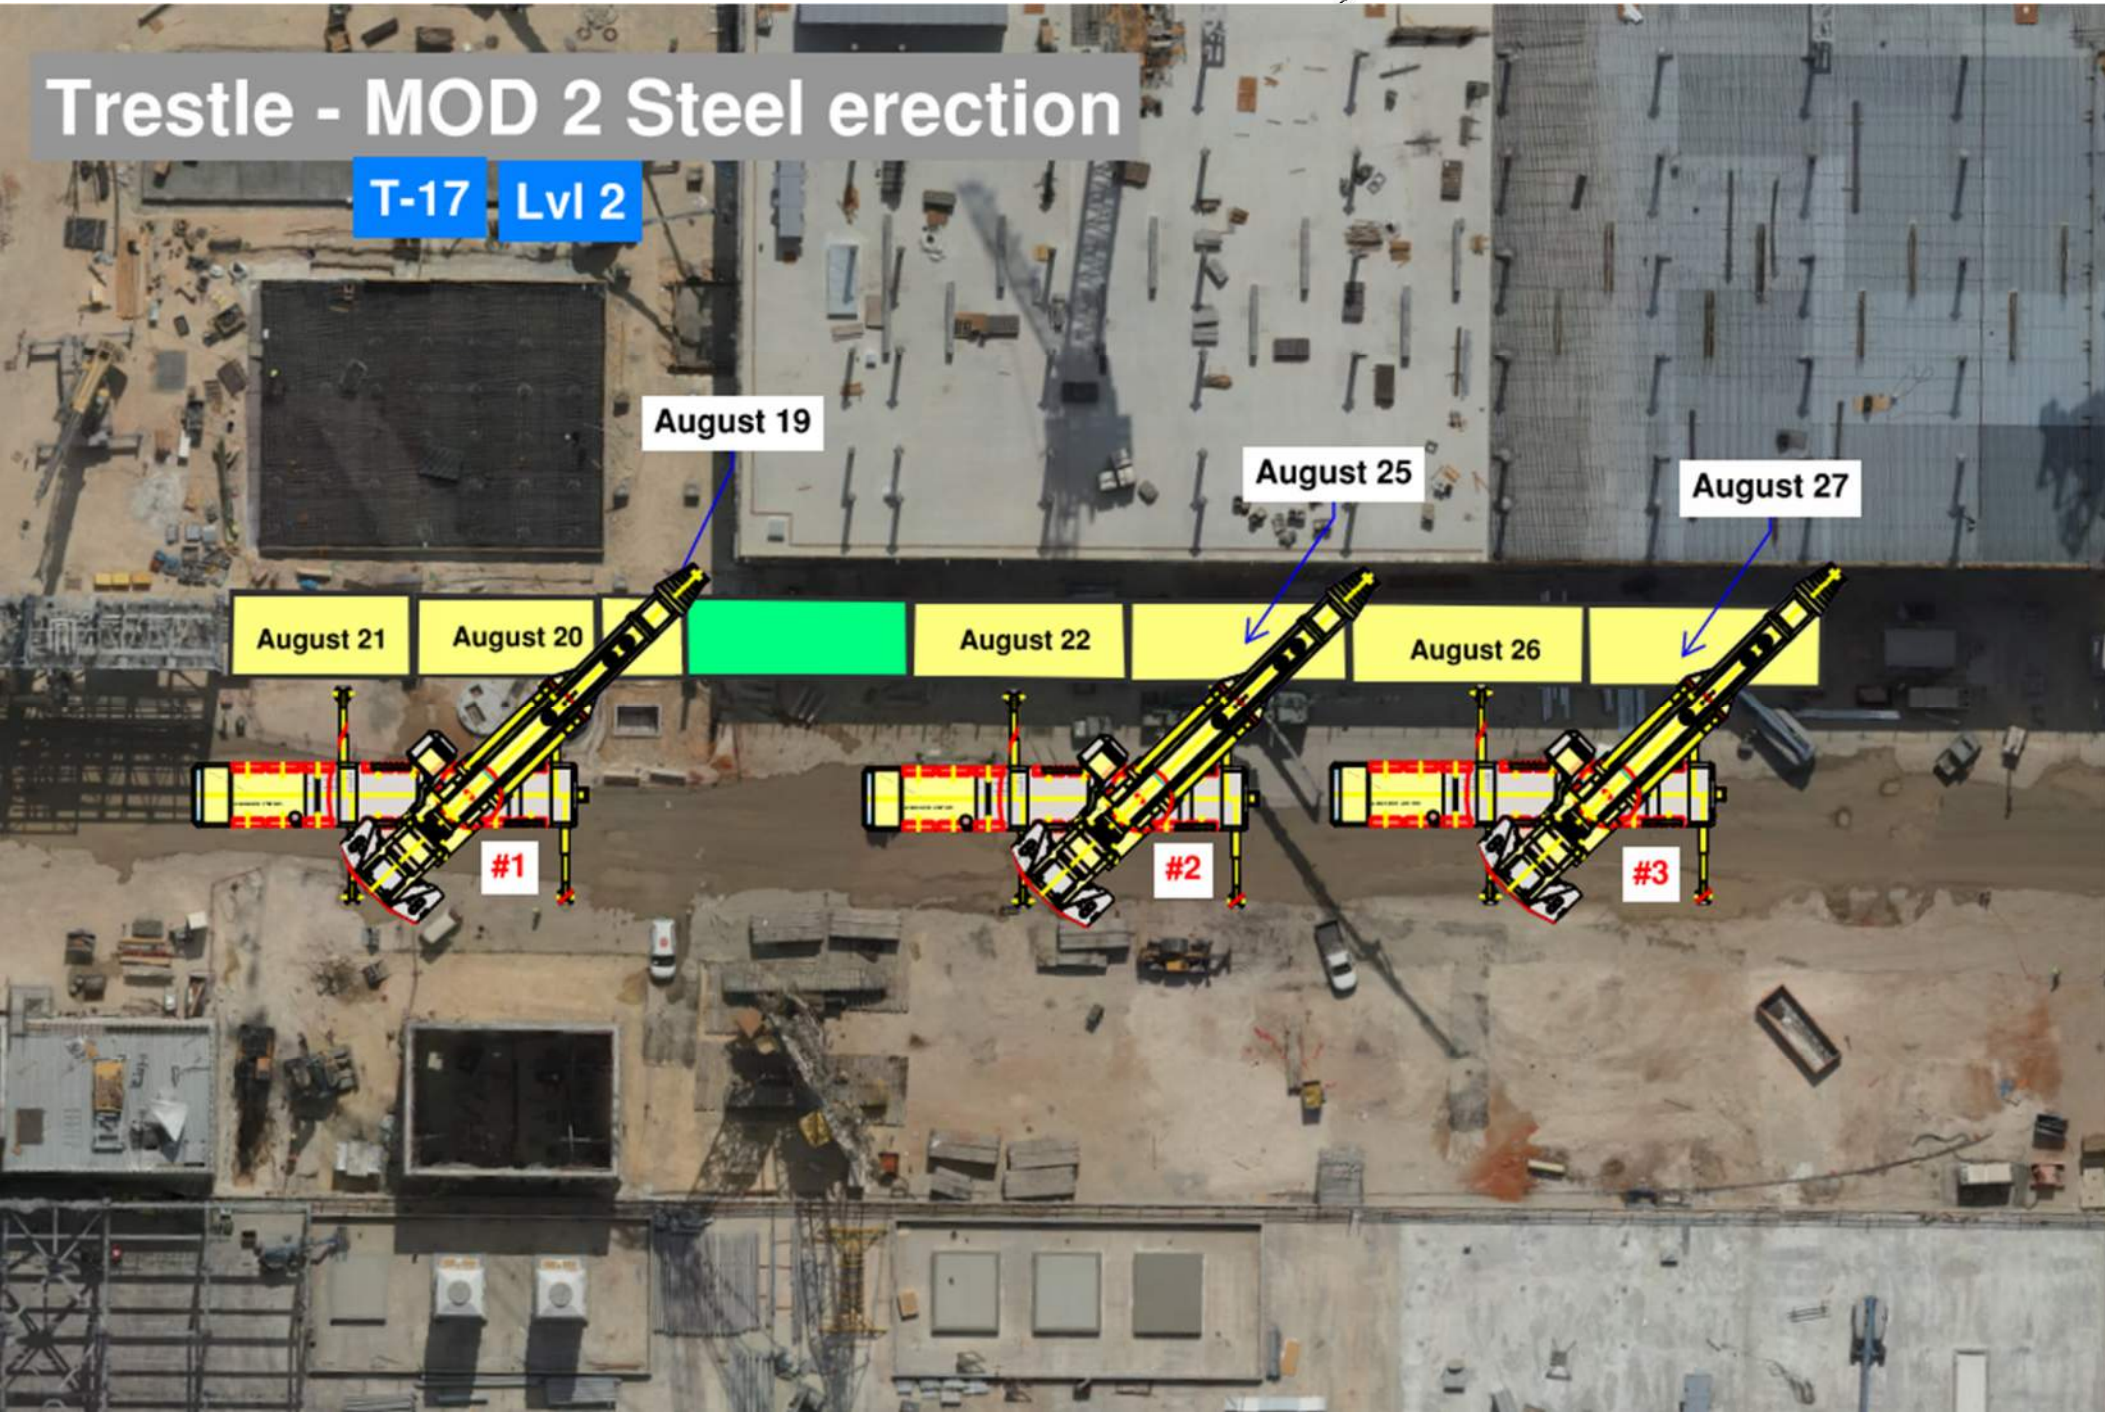




HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  


BSGS

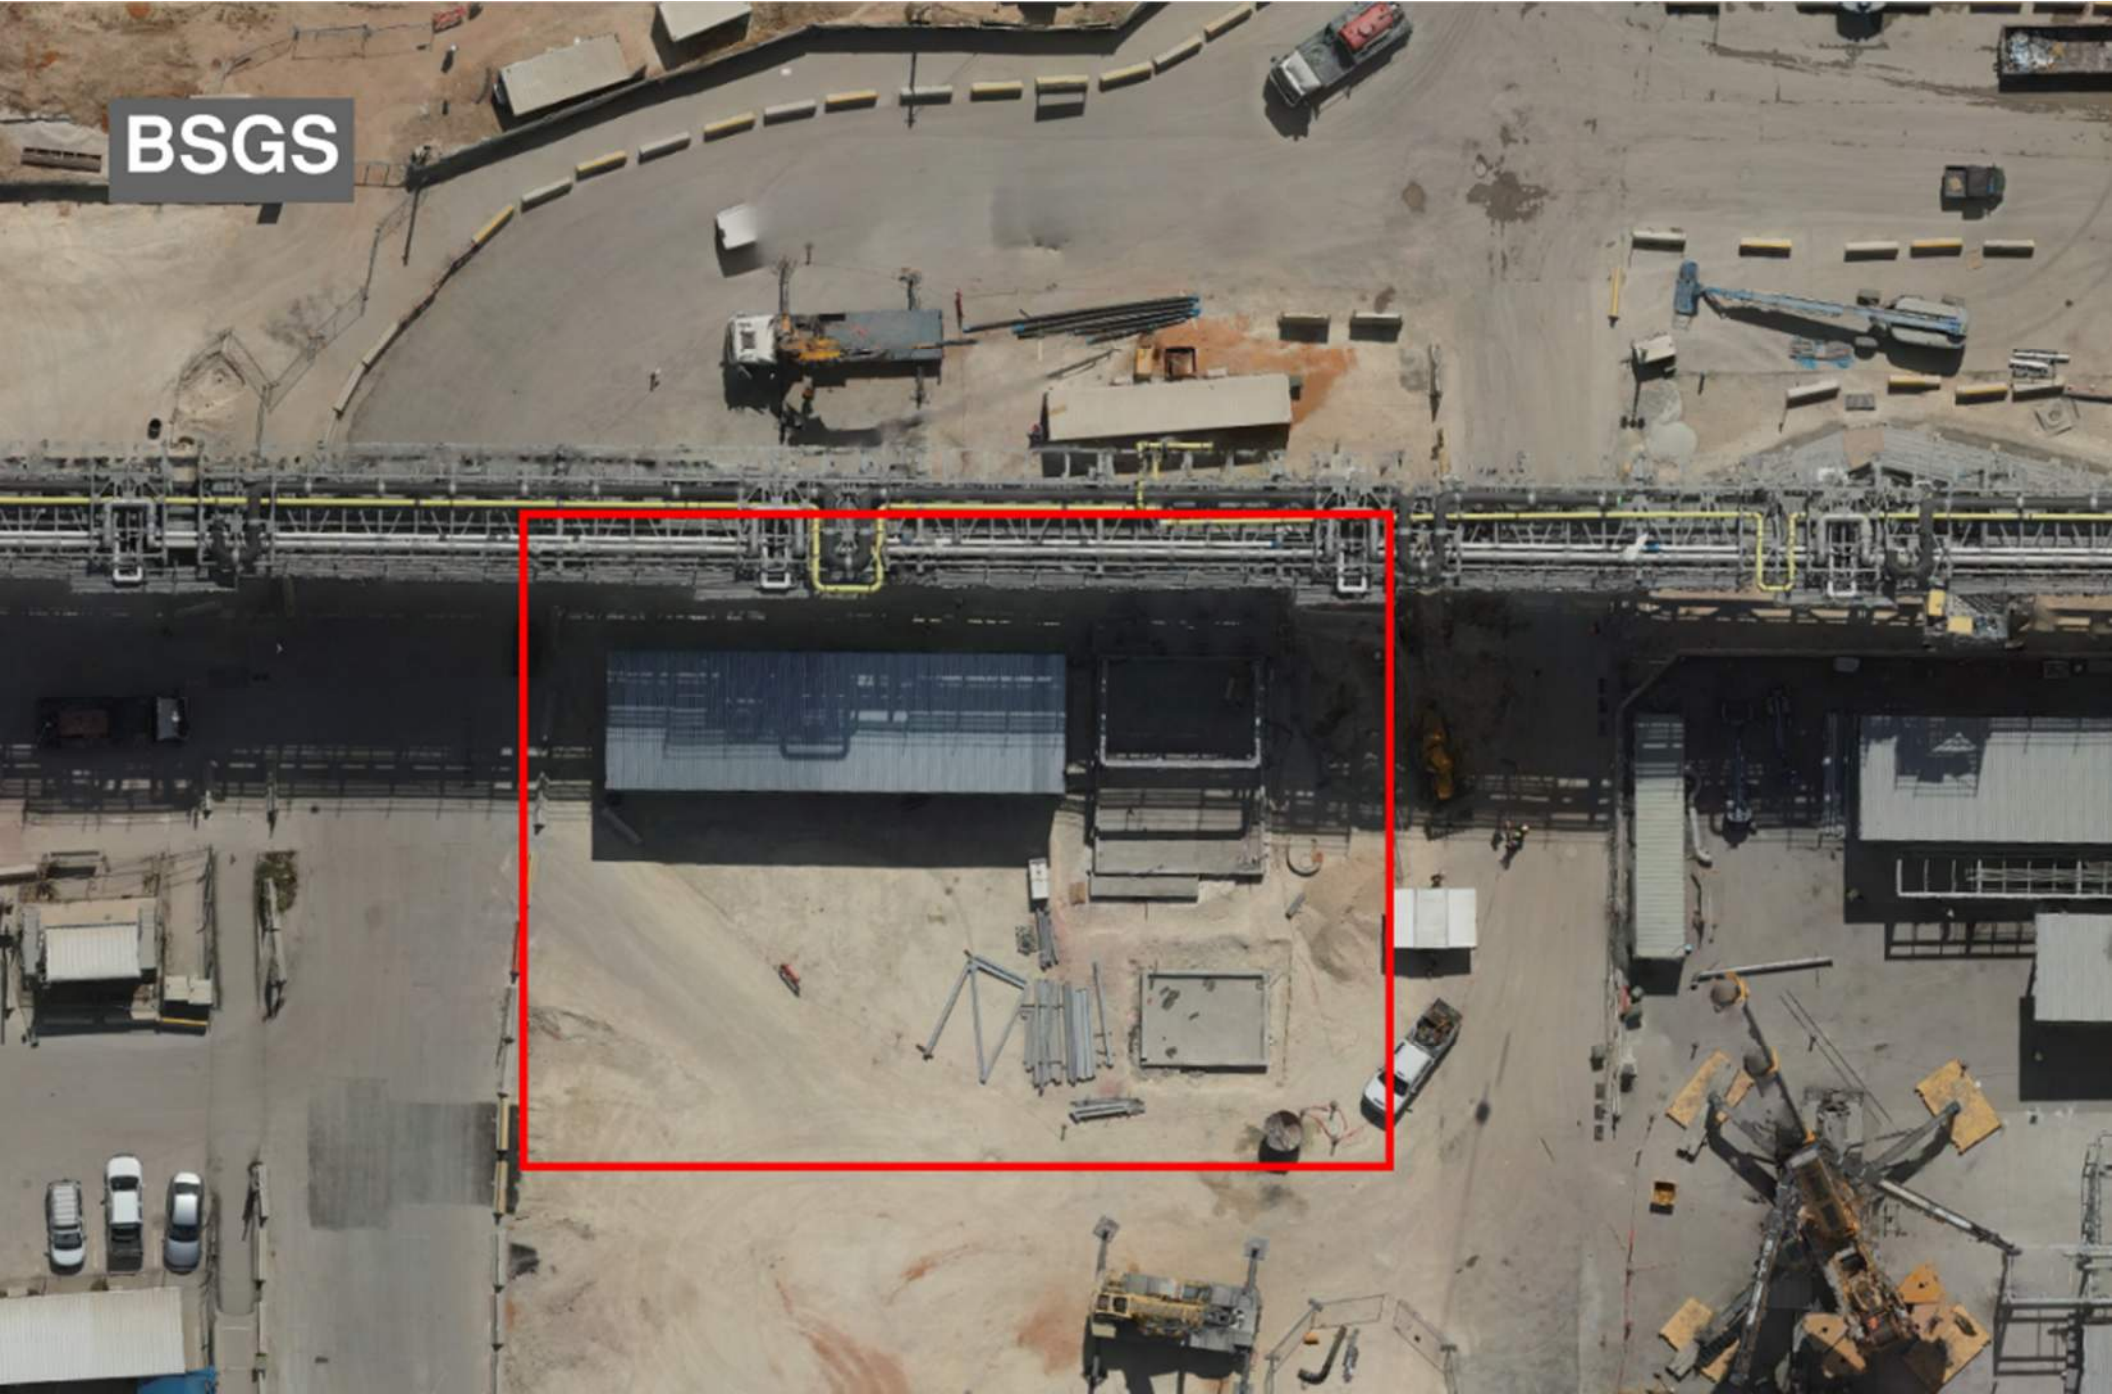


TRESTLE

Lesico 12" natural gas pipe pressure test exclusion zone

Wednesday, August 21st 1800 -Thursday, Aug 22nd 0100

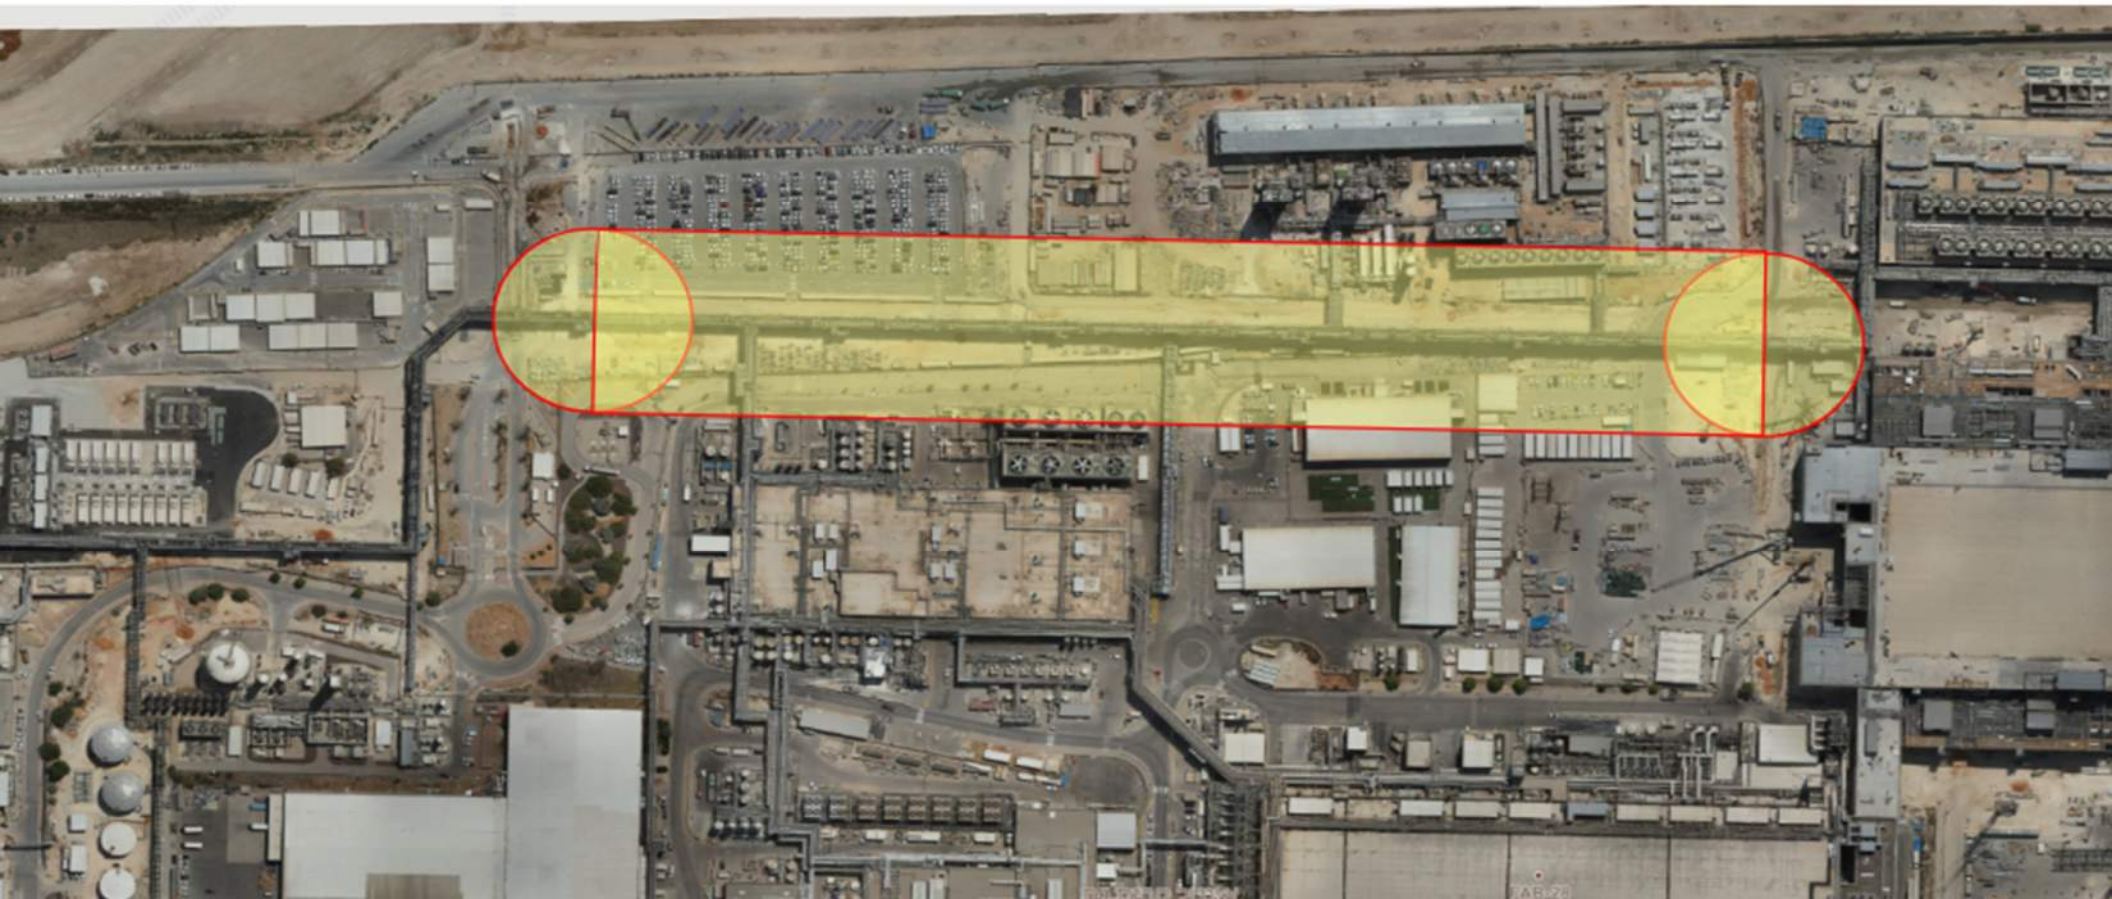

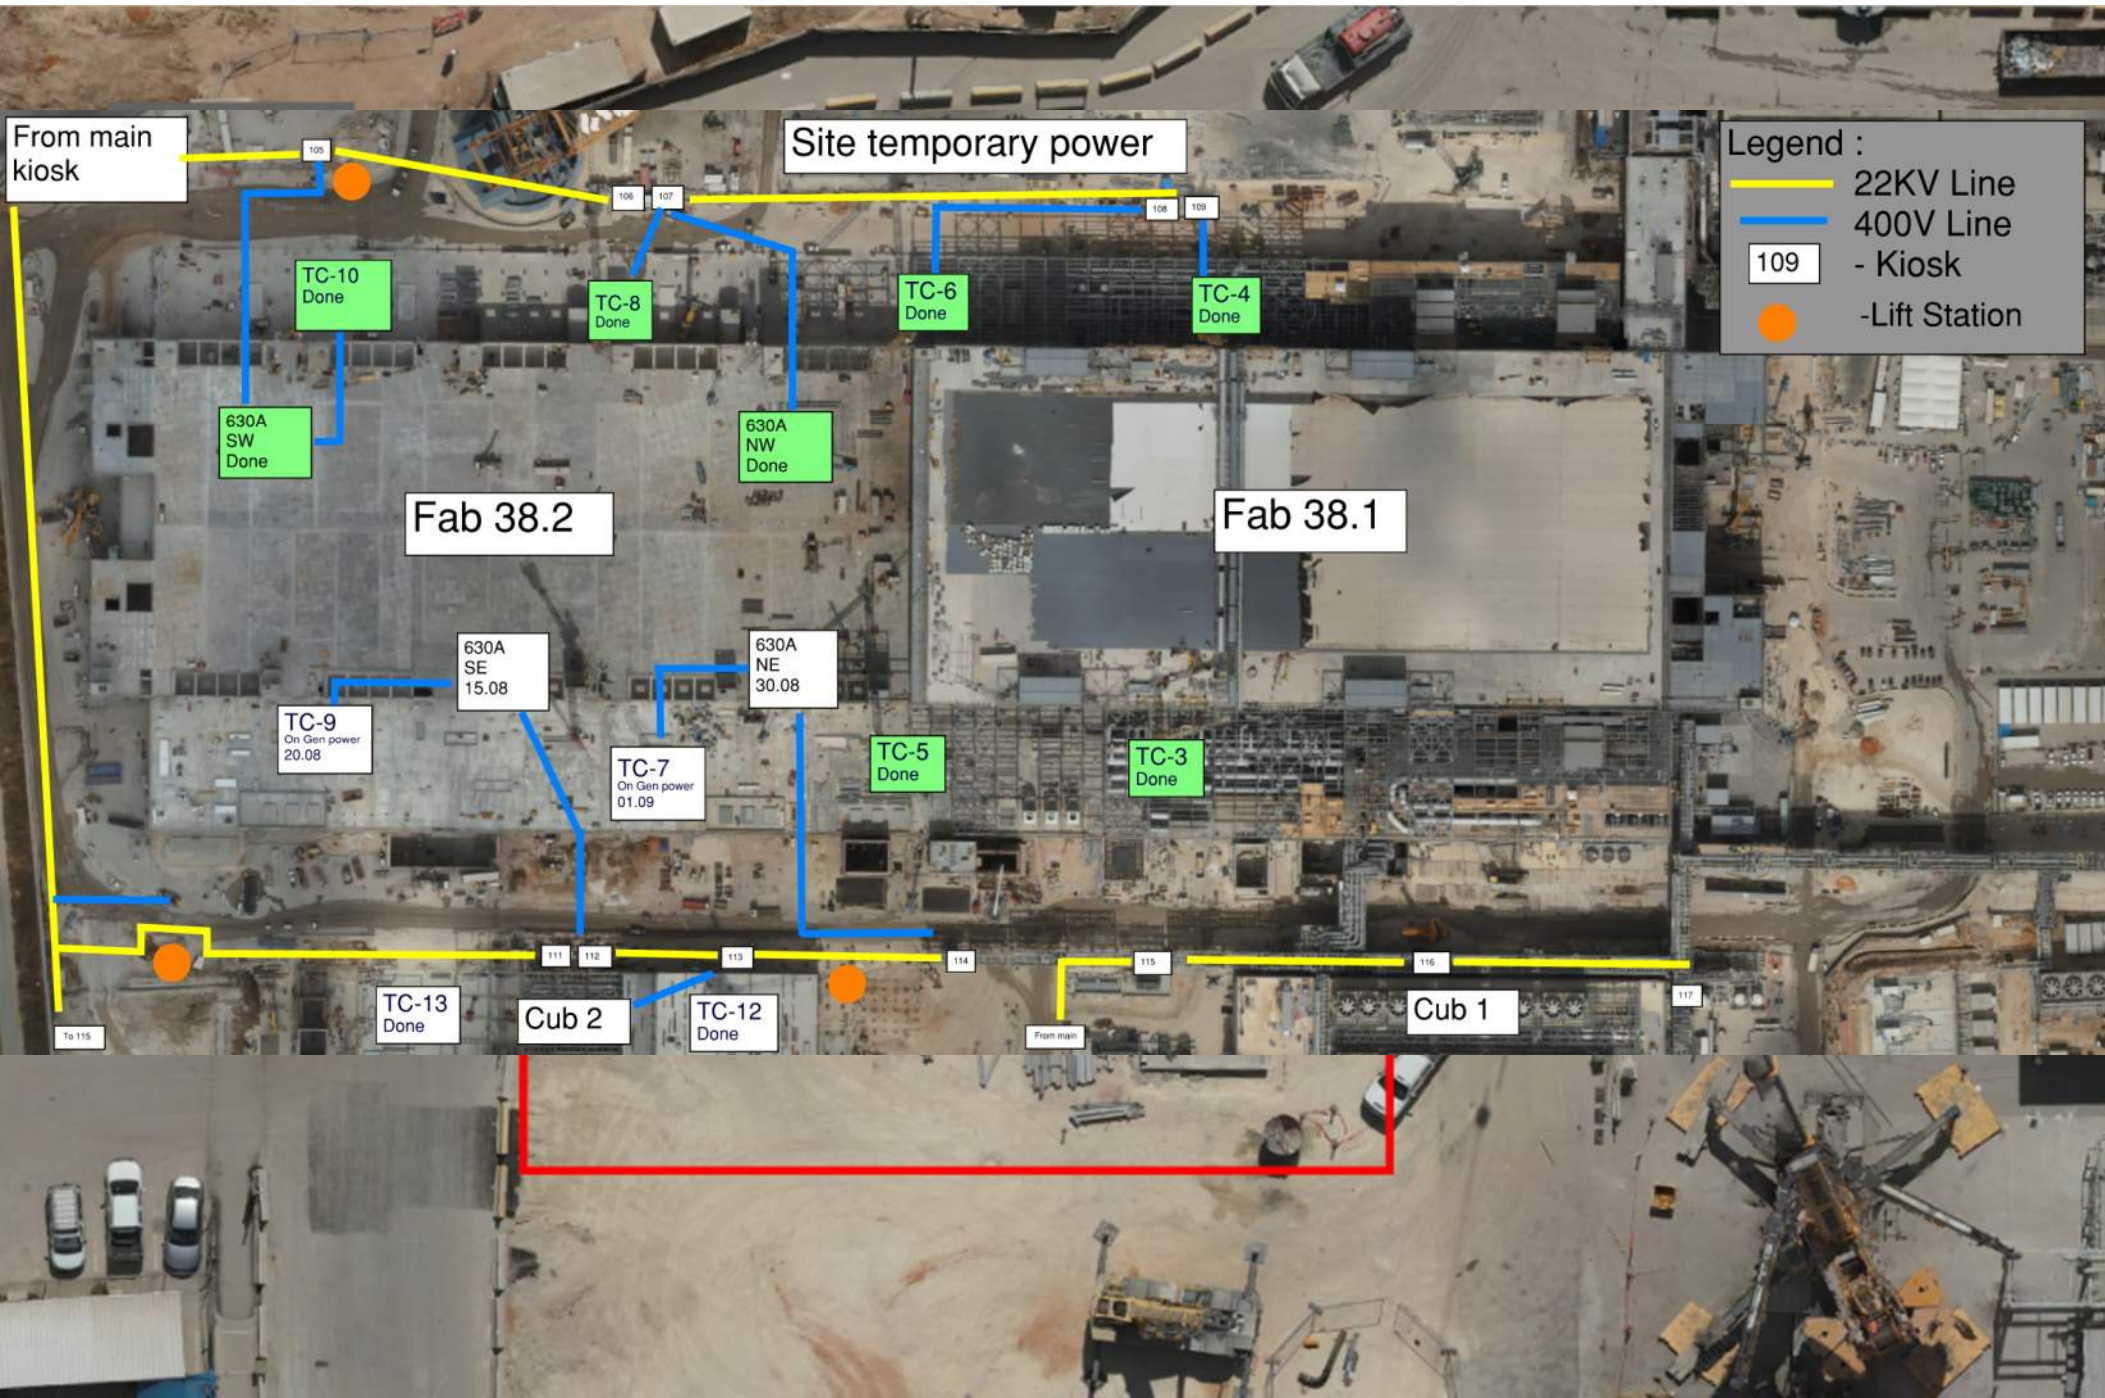



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Gate B






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

Traffic Plan

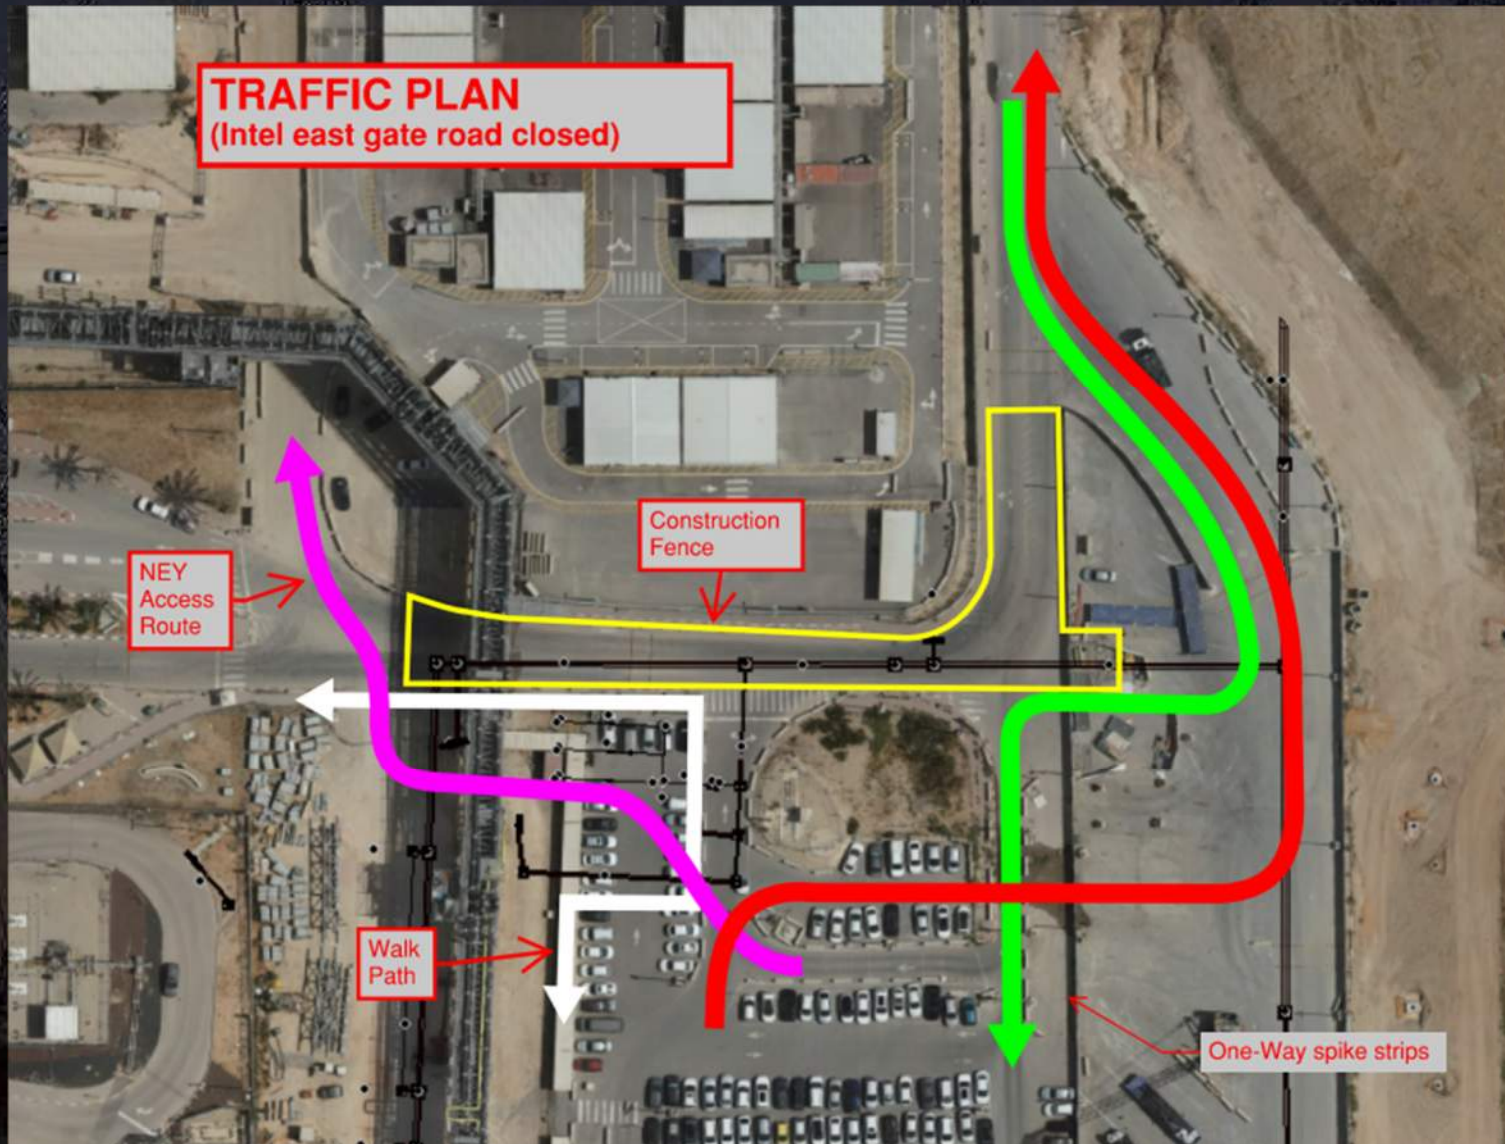




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North

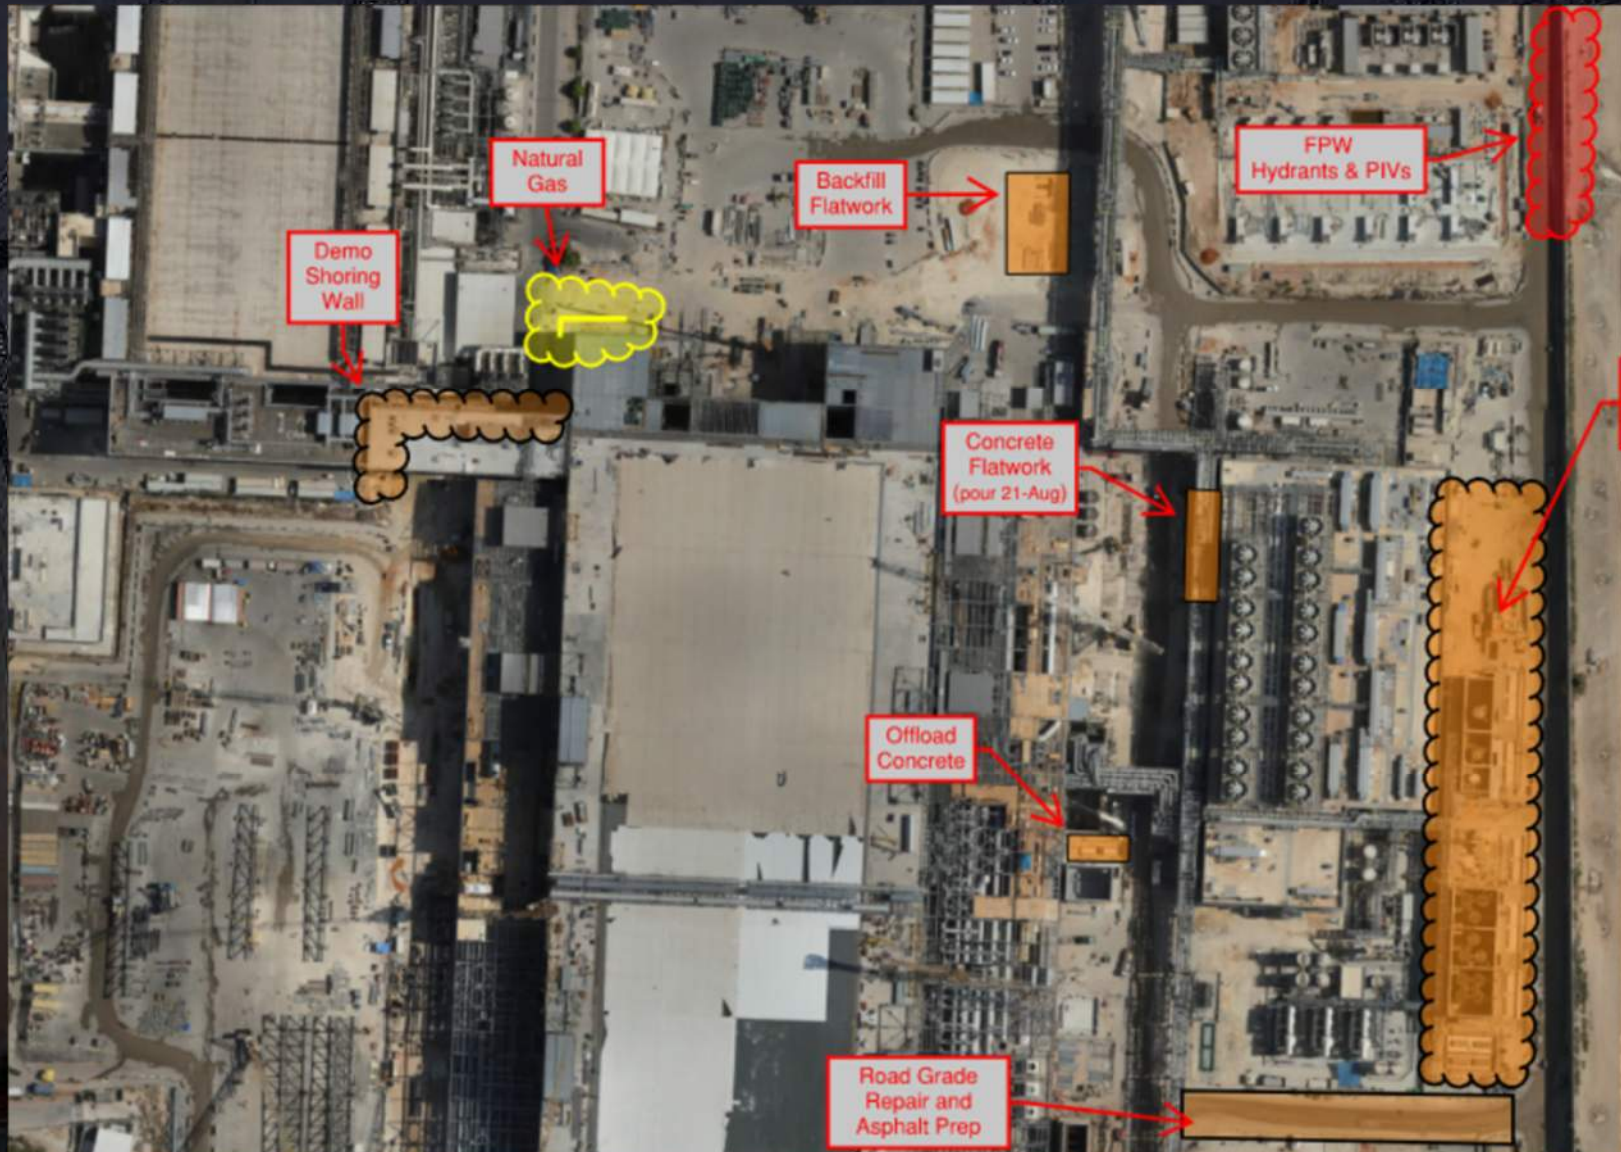



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South







Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

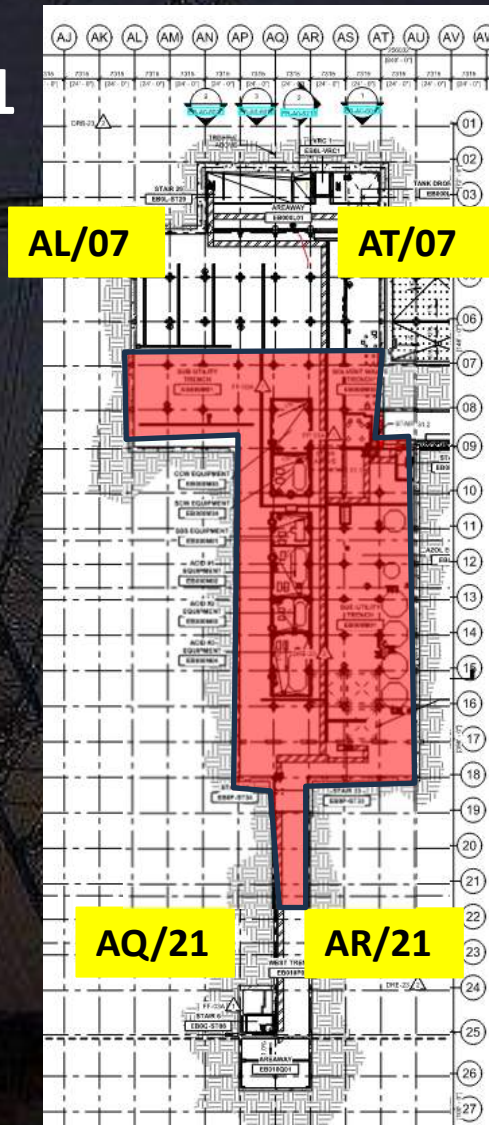


SUT2

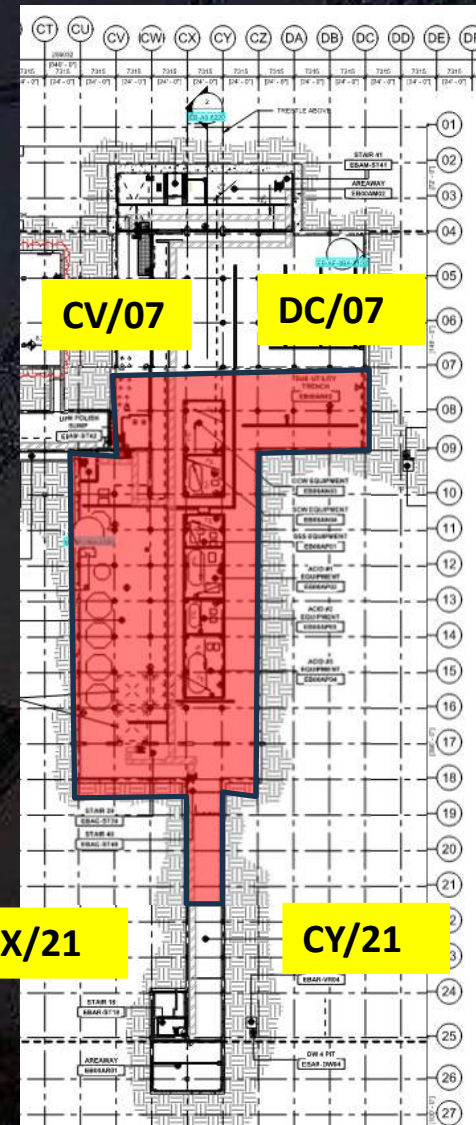


Daily Coordination Meeting

Site Logistics - Protected Areas (Utility Level)

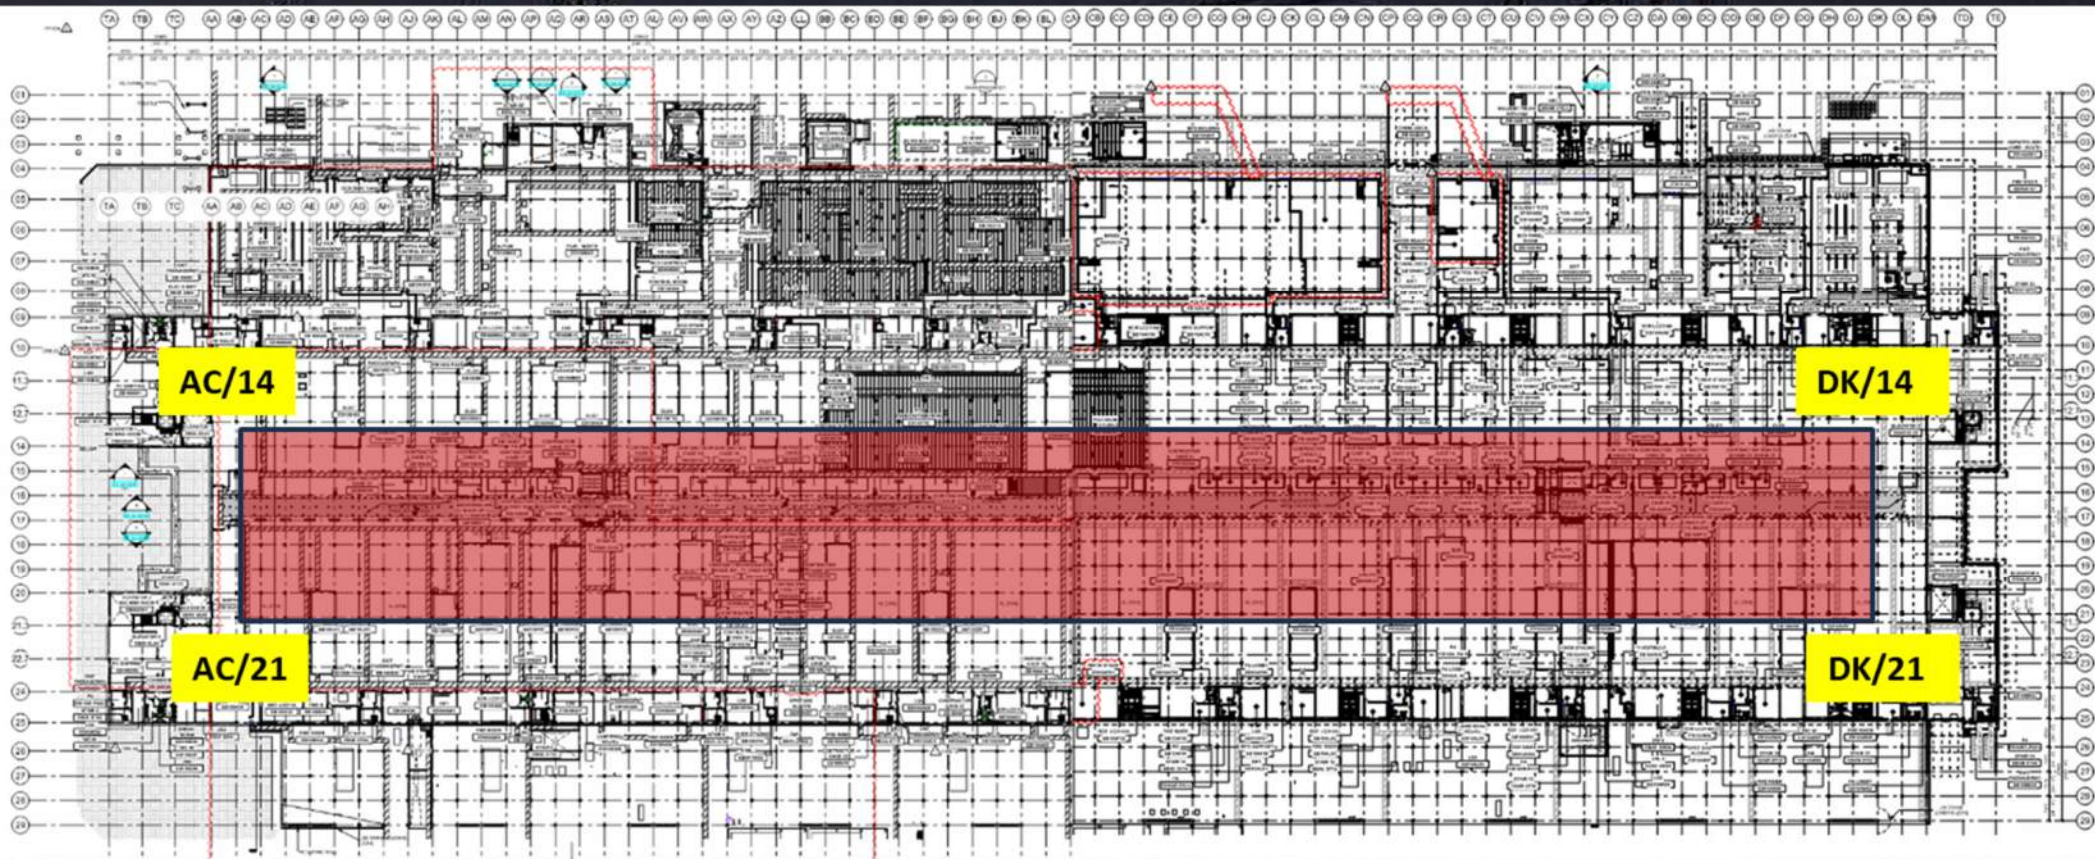

Daily Coordination Meeting

Site Logistics - Protected Areas (Subfab Level)

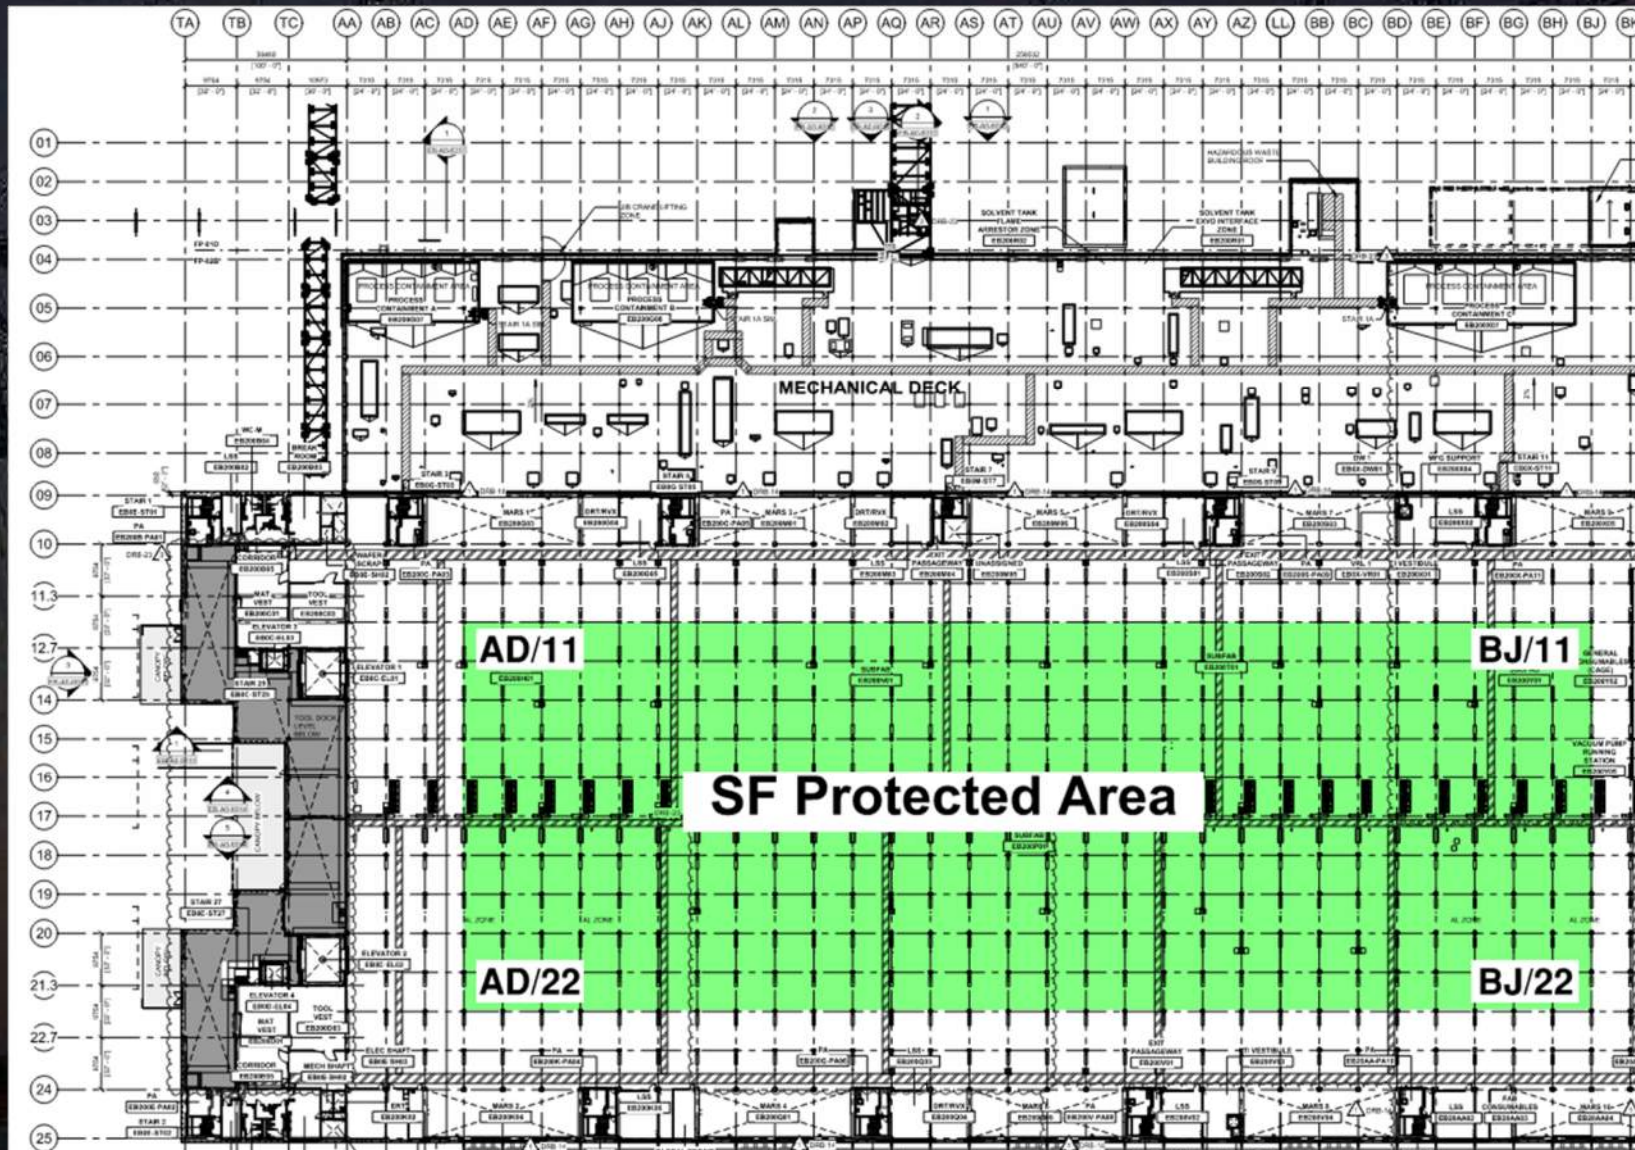




Daily Coordination Meeting

Site Logistics

Protected Areas

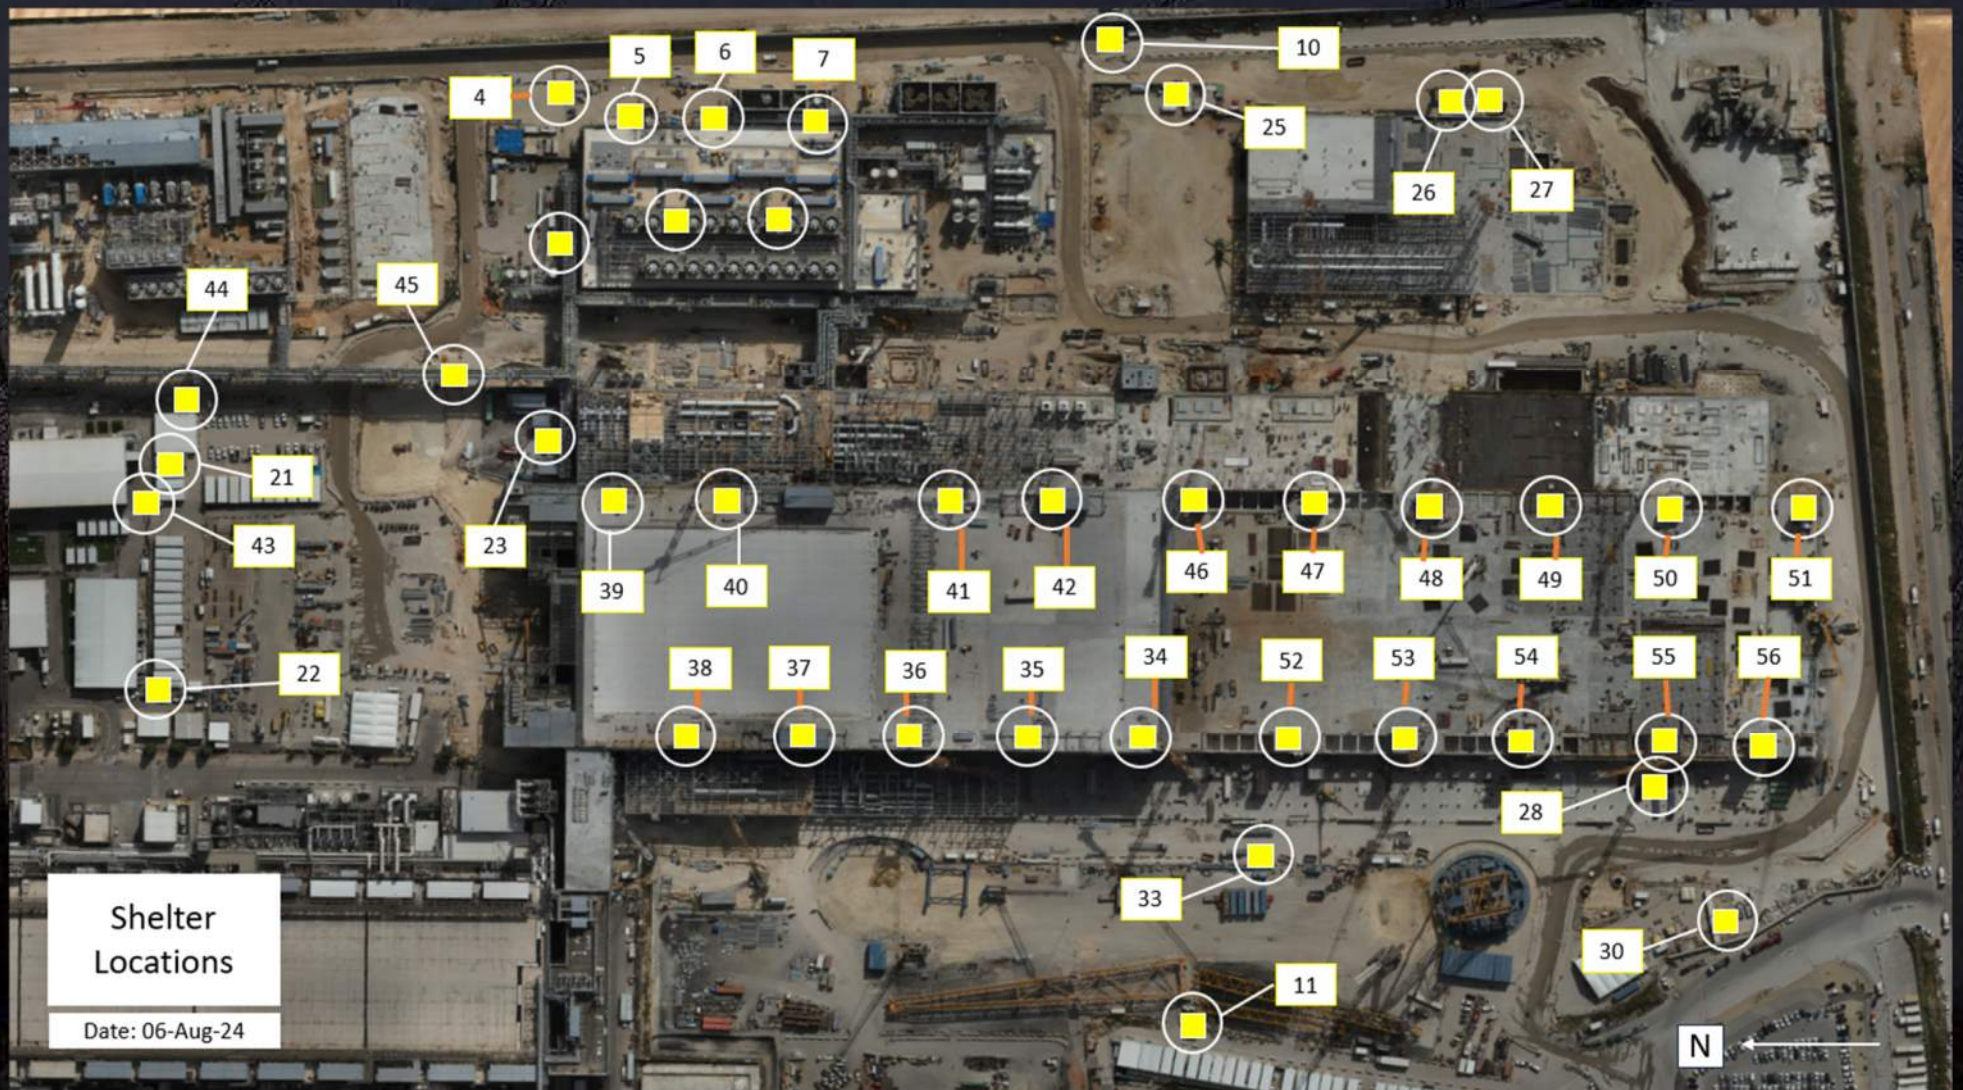




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

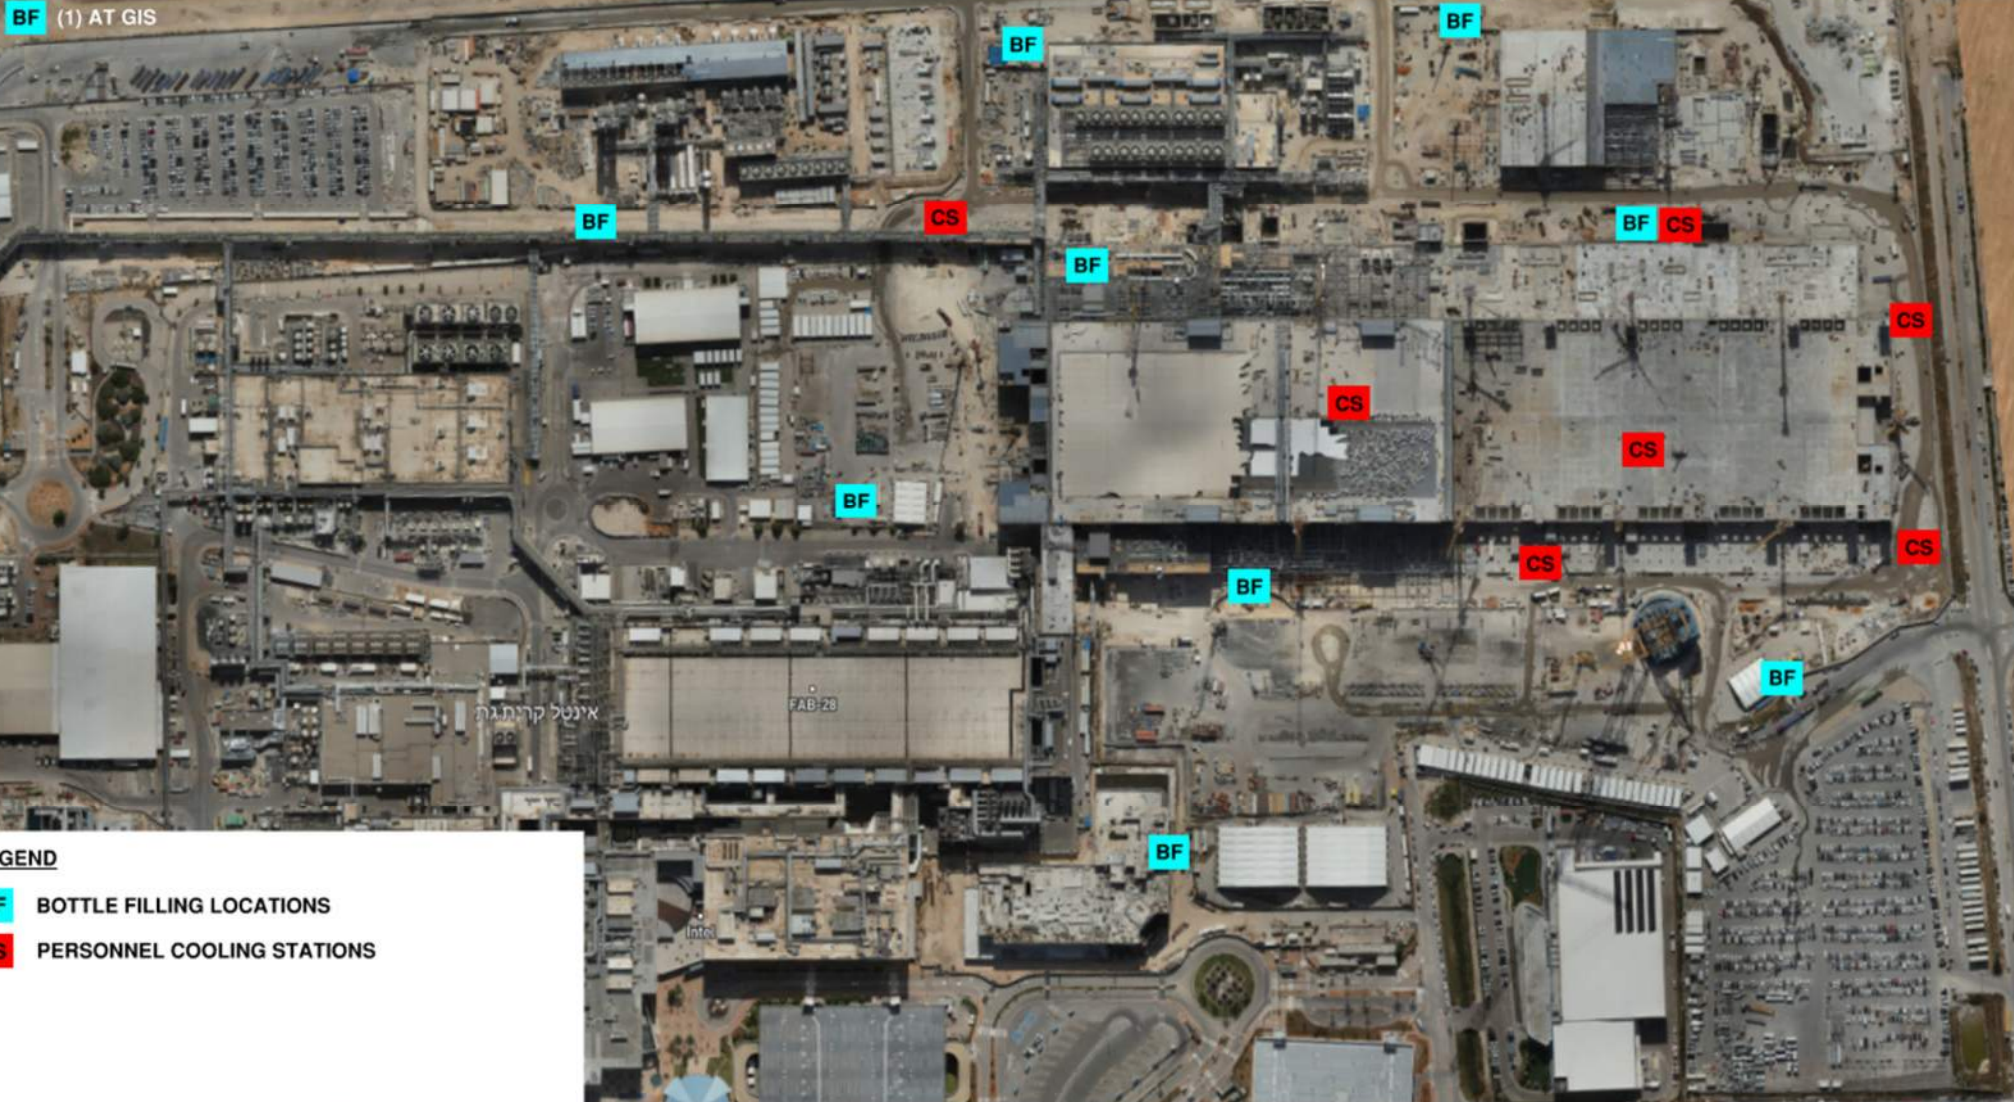

LEGEND

- BF** BOTTLE FILLING LOCATIONS
- CS** PERSONNEL COOLING STATIONS

Deep Cleaning of Break Tent B on Friday 16th Aug






Open CORs by Subcontractor

WW 33 – 468 CORs

WW 34 – 477 CORs

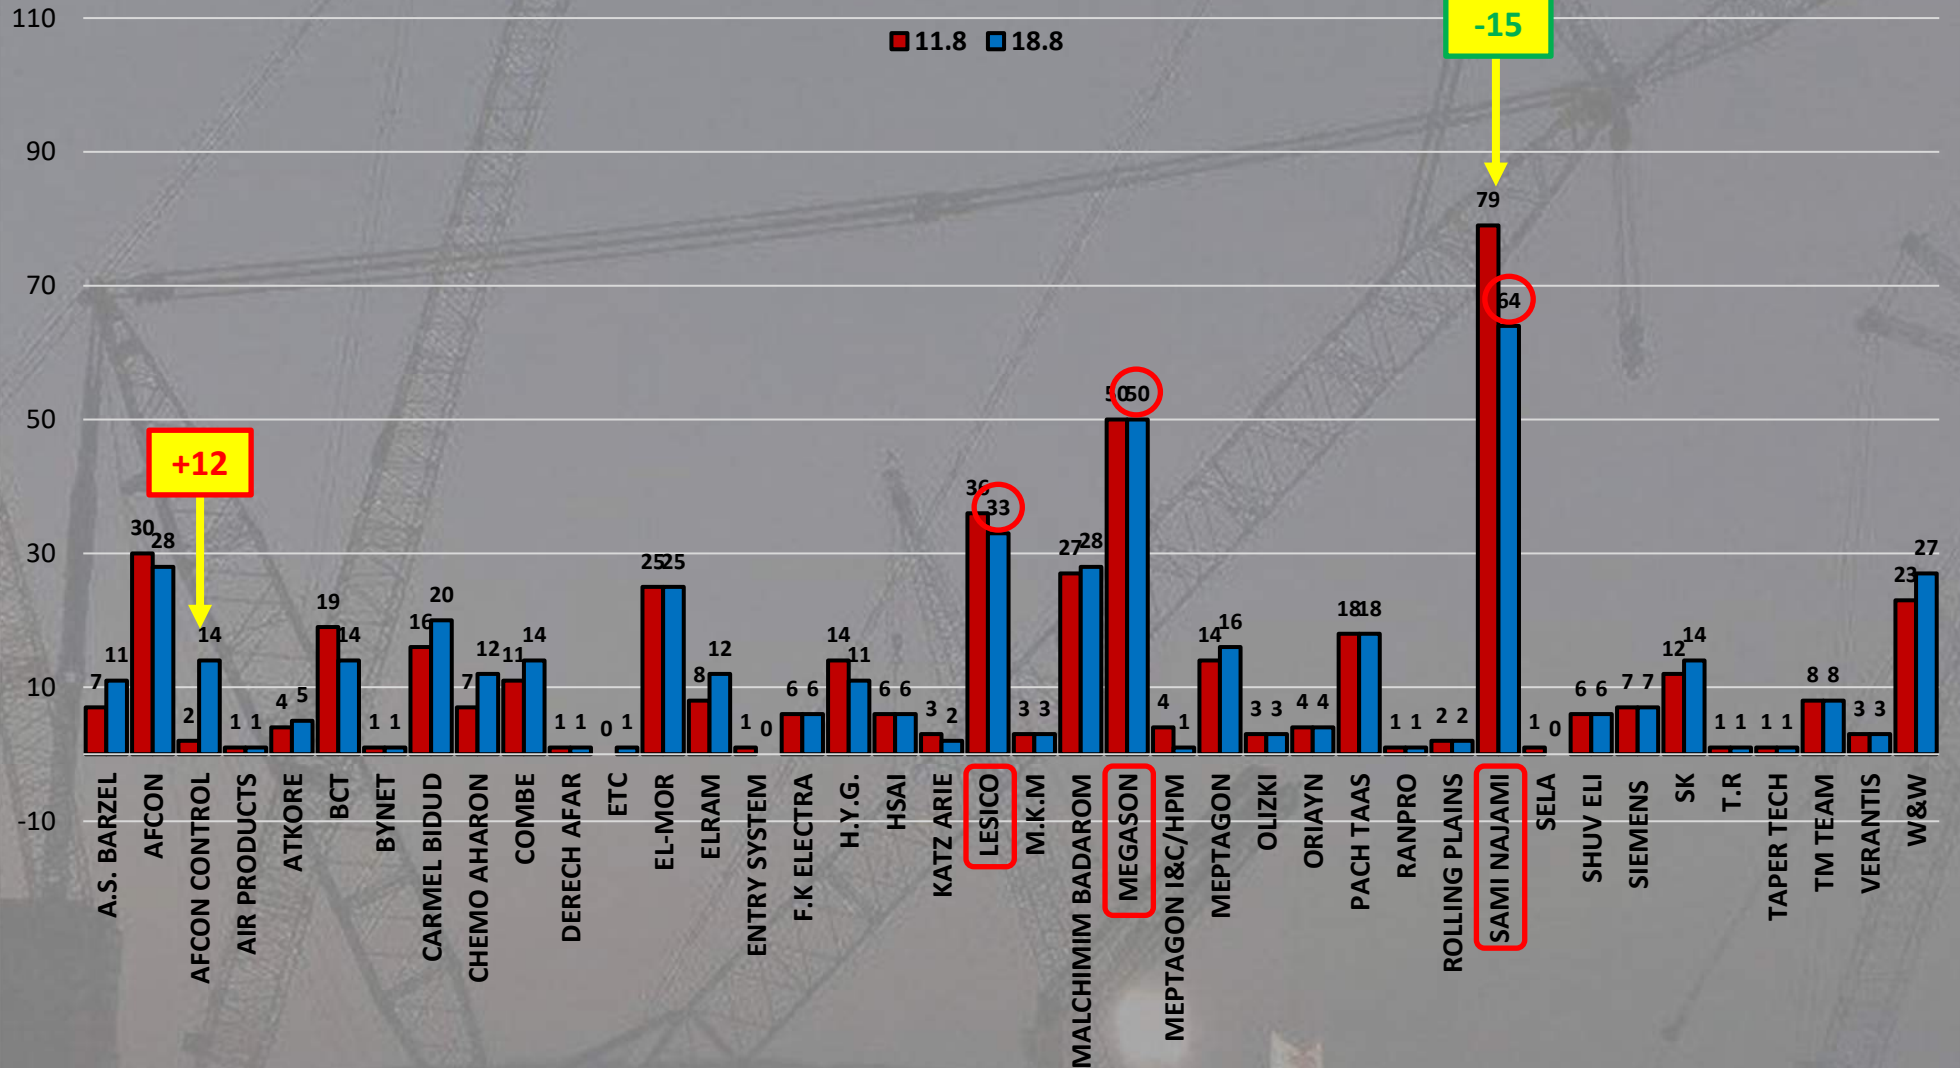




Overdue CORs by Subcontractor

WW 33 – 129 Overdue CORs

WW 34 – 191 Overdue CORs

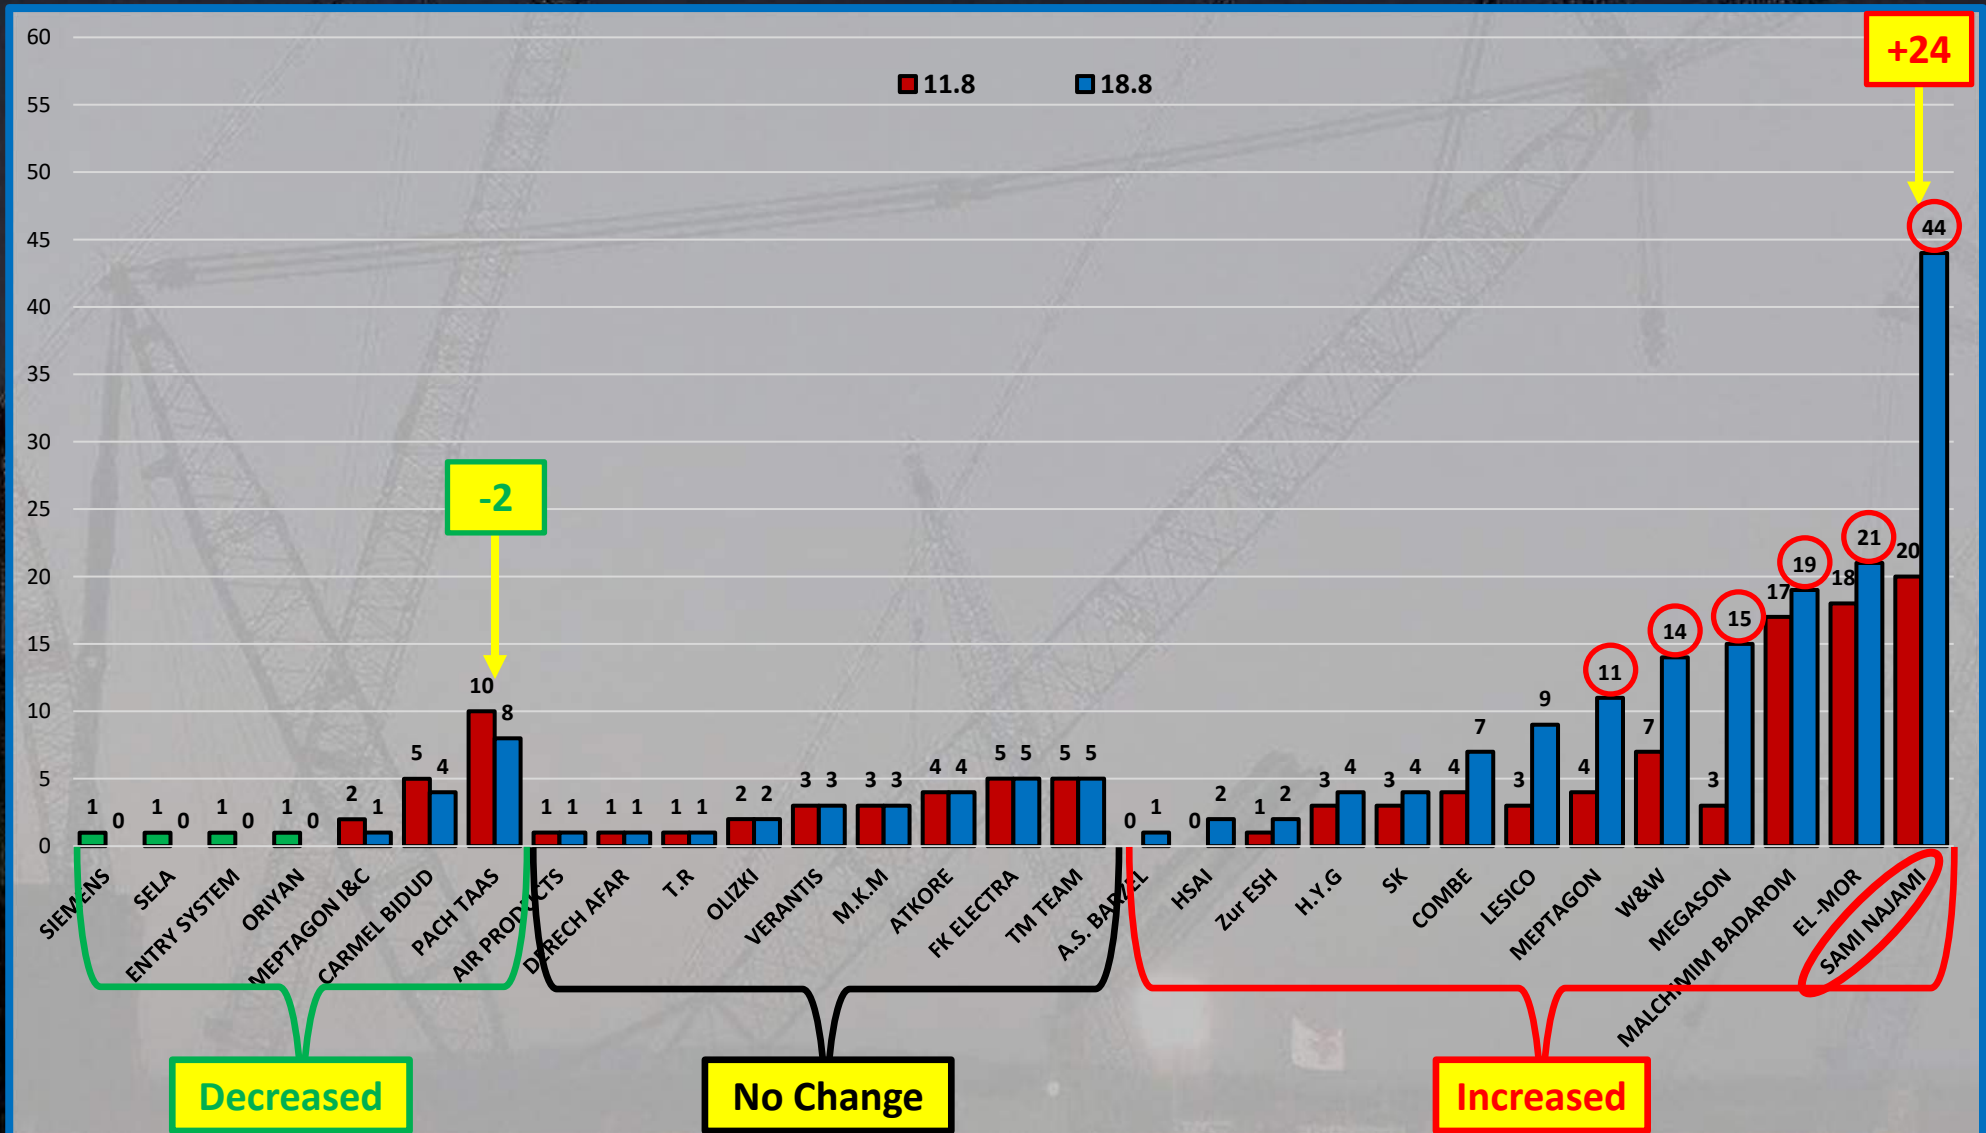

New Hires Must Be Mentored


- Please ensure that all of your new hires are being properly mentored.
- Your program should have some sort of documentation to record when someone completed their mentorship program and show that they understand the basics of the site, their job, and it should identify who their mentor was.
- We will be auditing these starting this week and issuing corrective actions to companies found deficient.
- Remember, new hires must be in a mentorship program for 4 weeks, with someone that is not EHS or a supervisor.

Stop and Think- We've Got the Power


Subs that DID NOT complete a Stop and Think



Atkor
Avi Cranes
Binyan Haretz
EL Fire Proof
Electra
Elram
Siemens Industrial
Skyline Cranes & Technologies



Complete 1 per day



Stop and Think- We've Got the Power

Stop and Think Participation

Company	Number of Stop and Thinks Performed	Number Expected (1 per 50 workers per day)	% Complete
Electra	0	4	0%
Elram	0	4	0%
Siemens Industrial	0	4	0%
Combe	2	20	10%
Carmel Bidud	4	20	20%
Afcon Controls	1	4	25%
Katz Arie Stainless Steel	3	12	25%
Megason Electric	1	4	25%
W&W - AFCO Steel LLC	1	4	25%
Meptagon	5	20	25%
A.S. Barzel	2	8	25%
BCT Pipeline Processes	4	12	33%
Sami Najami Engineering & Project	12	32	38%
Afcon Contracting Services	17	40	43%
Chemo Aharon	20	40	50%
El-Mor Electric	2	4	50%
Shuv Eli Electric Engineering	4	8	50%
TM TEAM - Job service	4	8	50%
Ranpro	2	4	50%

Company	Number of Stop and Thinks Performed	Number Expected (1 per 50 workers per day)	% Complete
TM TEAM	3	4	75%
DVIR.IE	3	4	75%
Derech Afar	4	4	100%
Talad	4	4	100%
Brand	4	4	100%
HYG Steel	4	4	100%
SIG Industrial	4	4	100%
Malchimim Badarom	9	8	113%
SK Engineering and Project	5	4	125%
Belfor	6	4	150%
D&P Clean Room	6	4	150%
Stage Design	7	4	175%
Oriyan	7	4	175%
Rehatot Be'er Sheva	8	4	200%
ByNet System Application	9	4	225%
Pach Taas	28	12	233%
Tzur Esh Projects	10	4	250%
Olitzki	11	4	275%

Heat Index- August 18th

	temperature (°F)																
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110	
Relative Humidity (%)	40	80	81	83	85	88	91	94	97		105	109	114	119	124	130	136
	45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
	50	81	83	85	88	91	95	99	103	108	113	118	124	131	137		
	55	81	84	86	89	93	97	101	106	112	117	124	130	137			
	60	82	84	88	91	95	100	105	110	116	123	129	137				
	65	82	85	89	93	98	103	108	114	121	128	136					
	70	83	86	90	95	100	105	112	119	126	134						
	75	84	88	92	97	103	109	116	124	132							
	80	84	89	94	100	106	113	121	129								
	85	85	90	96	102	110	117	126	135								
	90	86	91	98	105	113	122	131									
	95	86	93	100	108	117	127										
100	87	95	103	112	121	132											

 Caution

 Extreme Caution

 Danger

 Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



14:00 Sign In
