

Daily Coordination Meeting



Daily Coordination Meeting

General Topics:

- Temp power – don't touch
- Weekend work



UTILITY LEVEL PRESS TEST

LESICO

Press test UN2

3/20

From 19:00


till 5:00

Safe exclusion zone for UN2 Pressure test
56.5-meter radius

CJ



UTILITY LEVEL MOD1

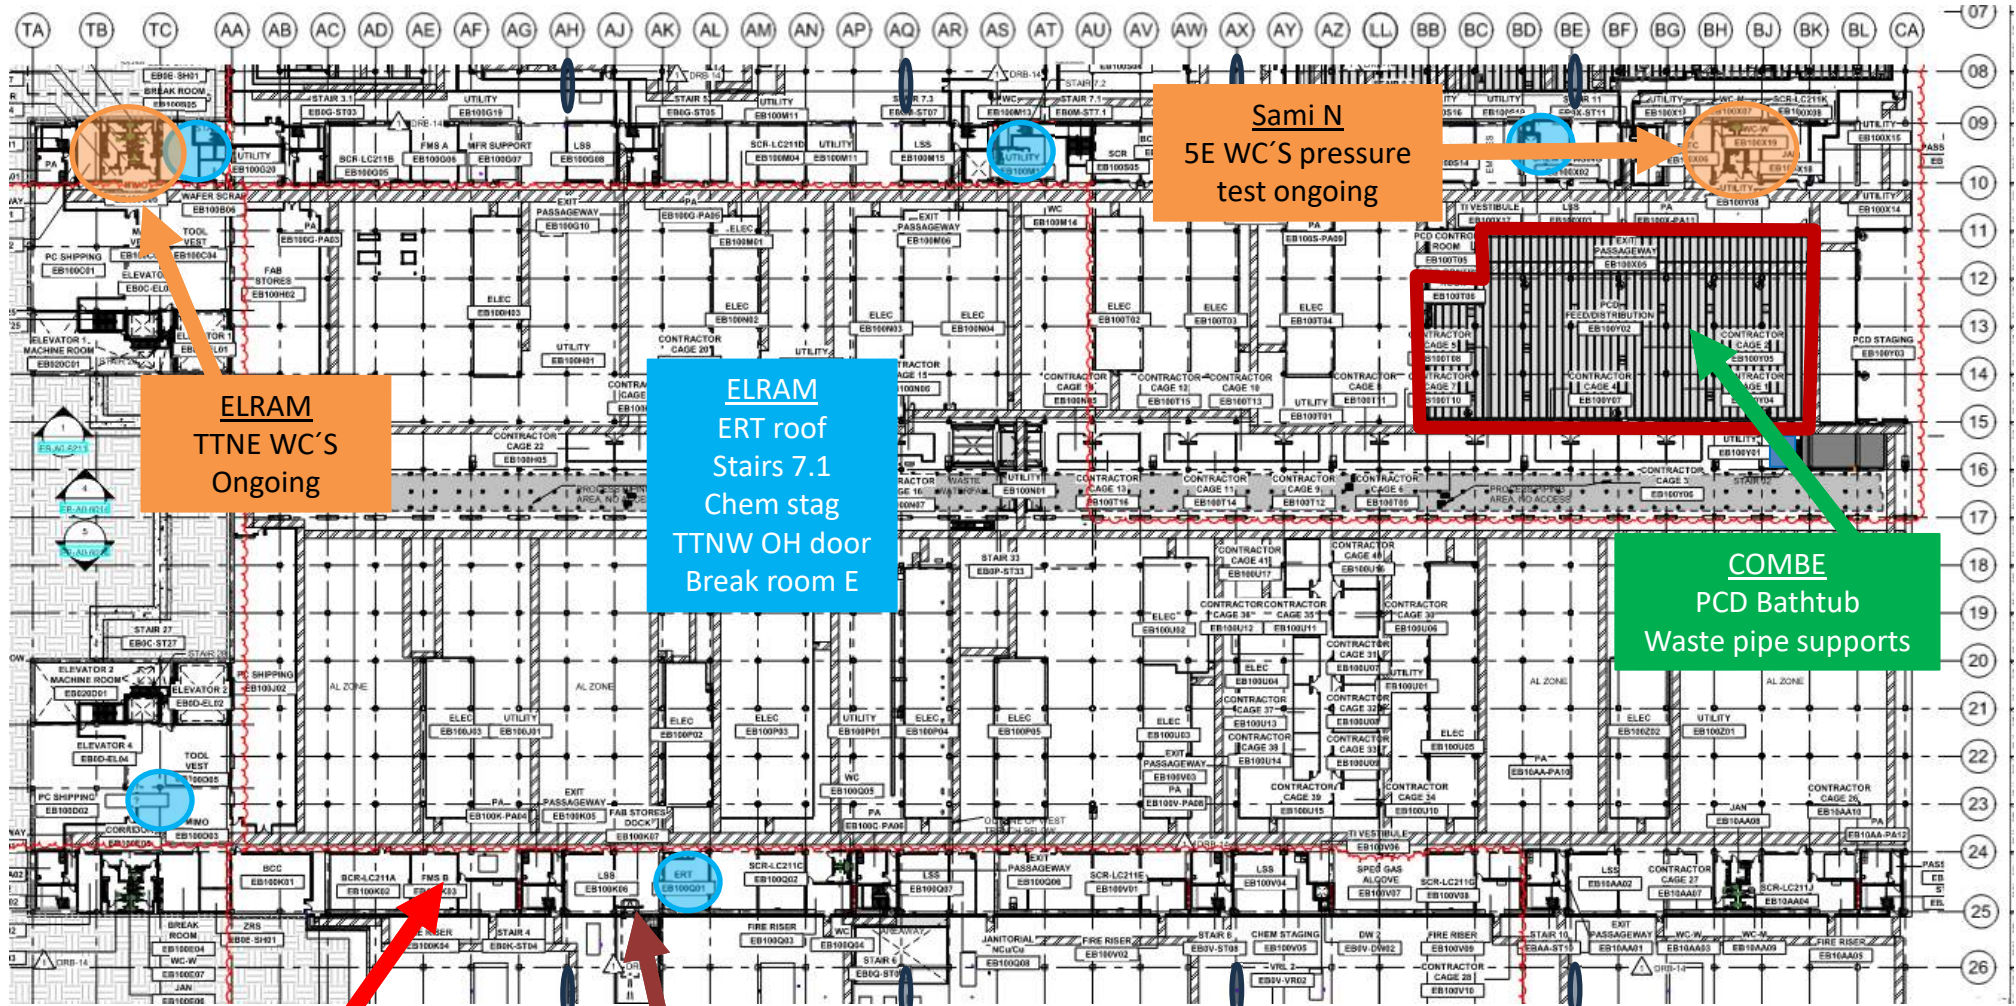

Sami N
5E WC'S pressure
test ongoing

ELRAM
TTNE WC'S
Ongoing

ELRAM
ERT roof
Stairs 7.1
Chem stag
TTNW OH door
Break room E


COMBE
PCD Bathtub
Waste pipe supports

HYG
FMS B
3/18
Carmel back
3/23


SHEARIM
Need start
date !?




SUT 38.1 LEVEL


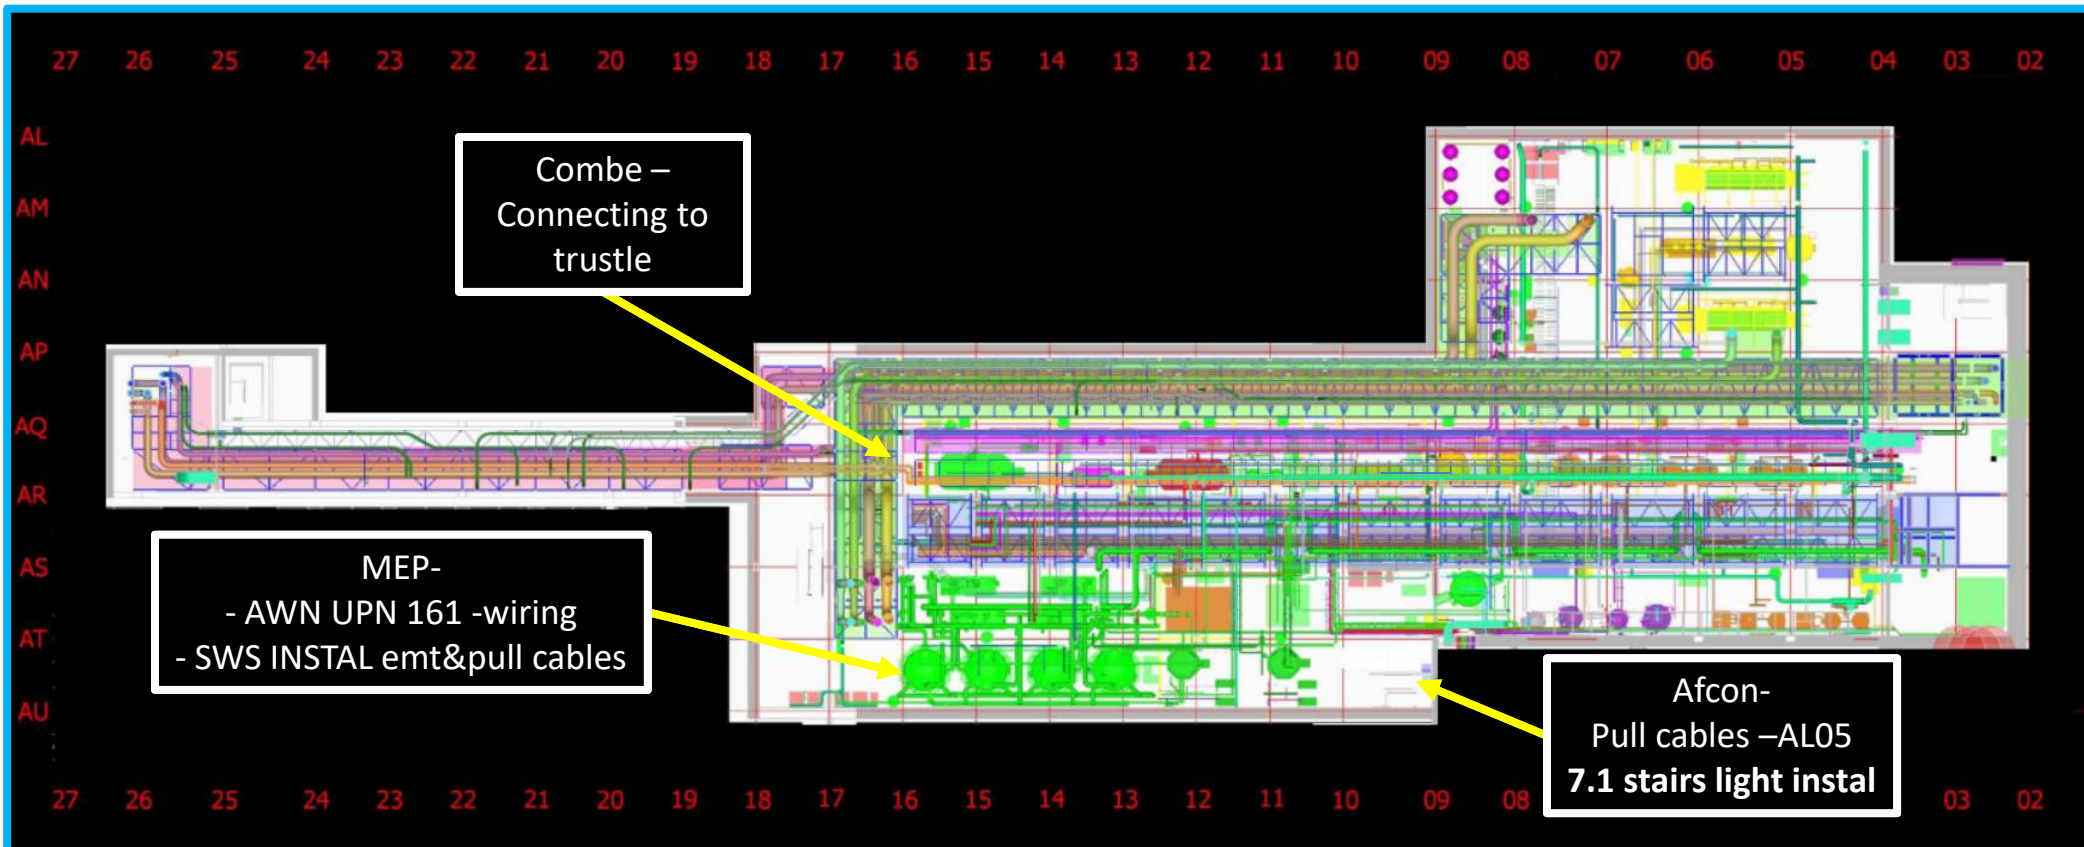


SUT 38.2 LEVEL

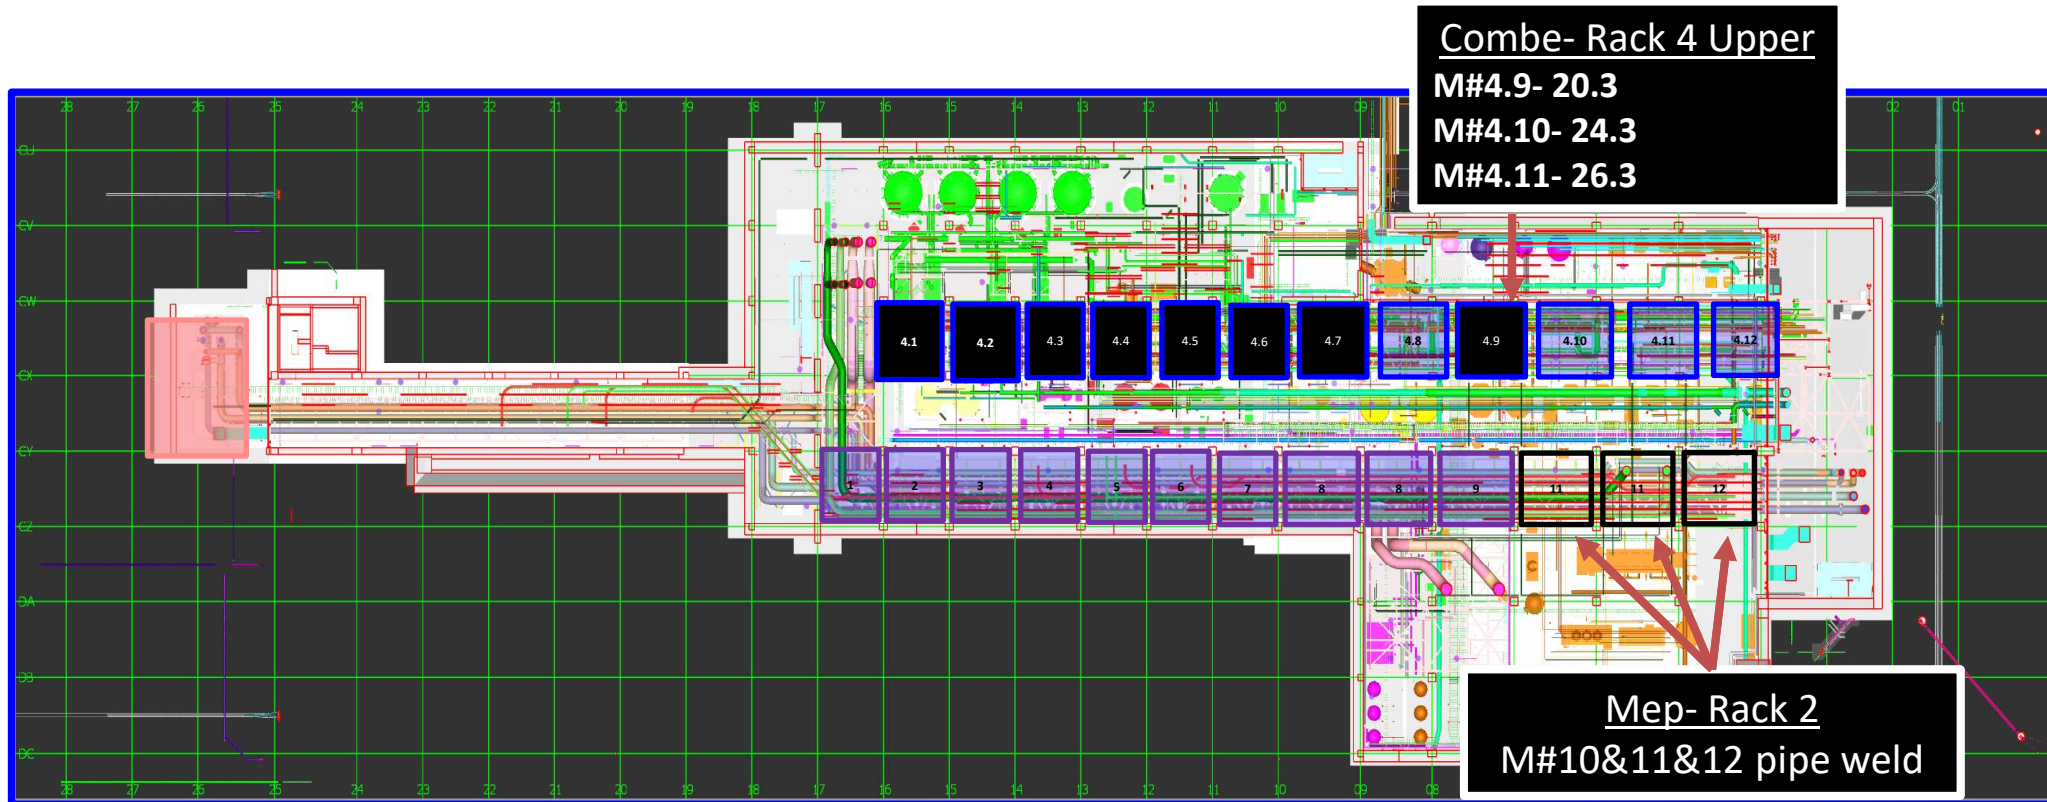


SUT 38.1 LEVEL

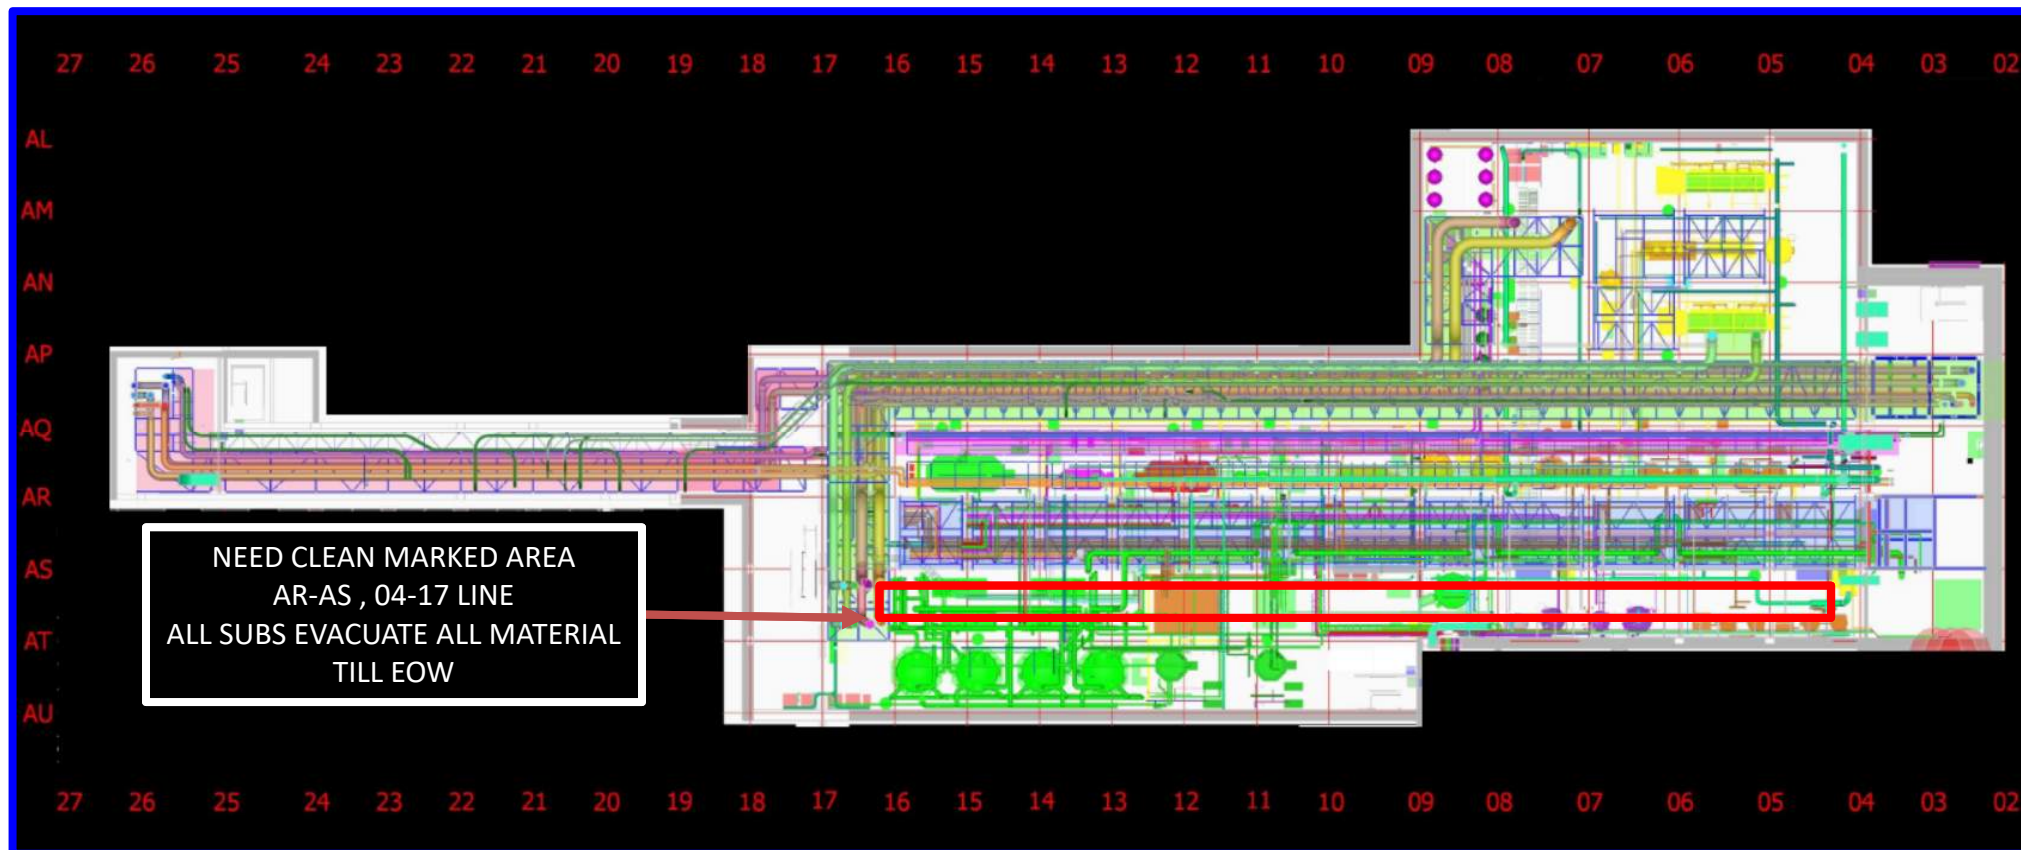

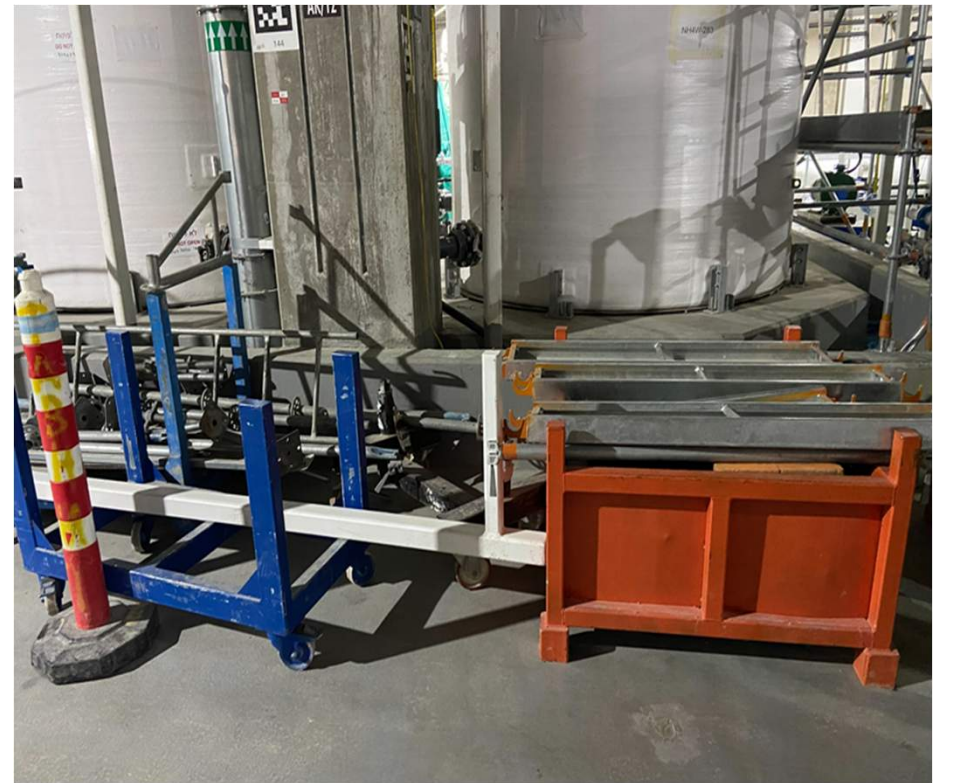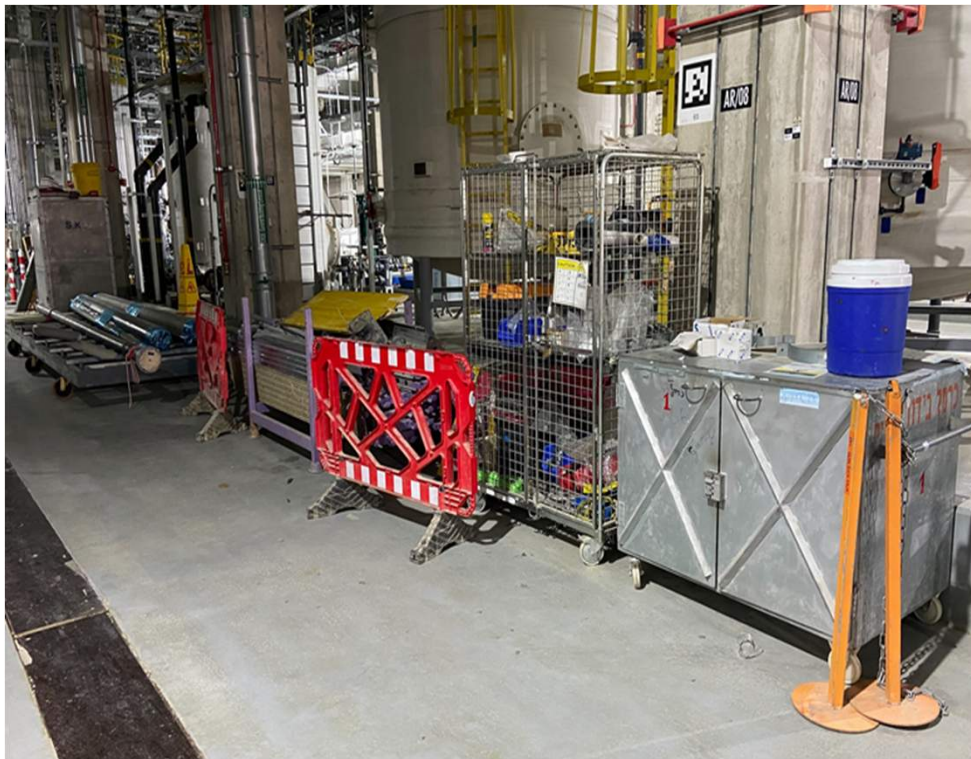




SUBFAB BUILDOUT MOD 1

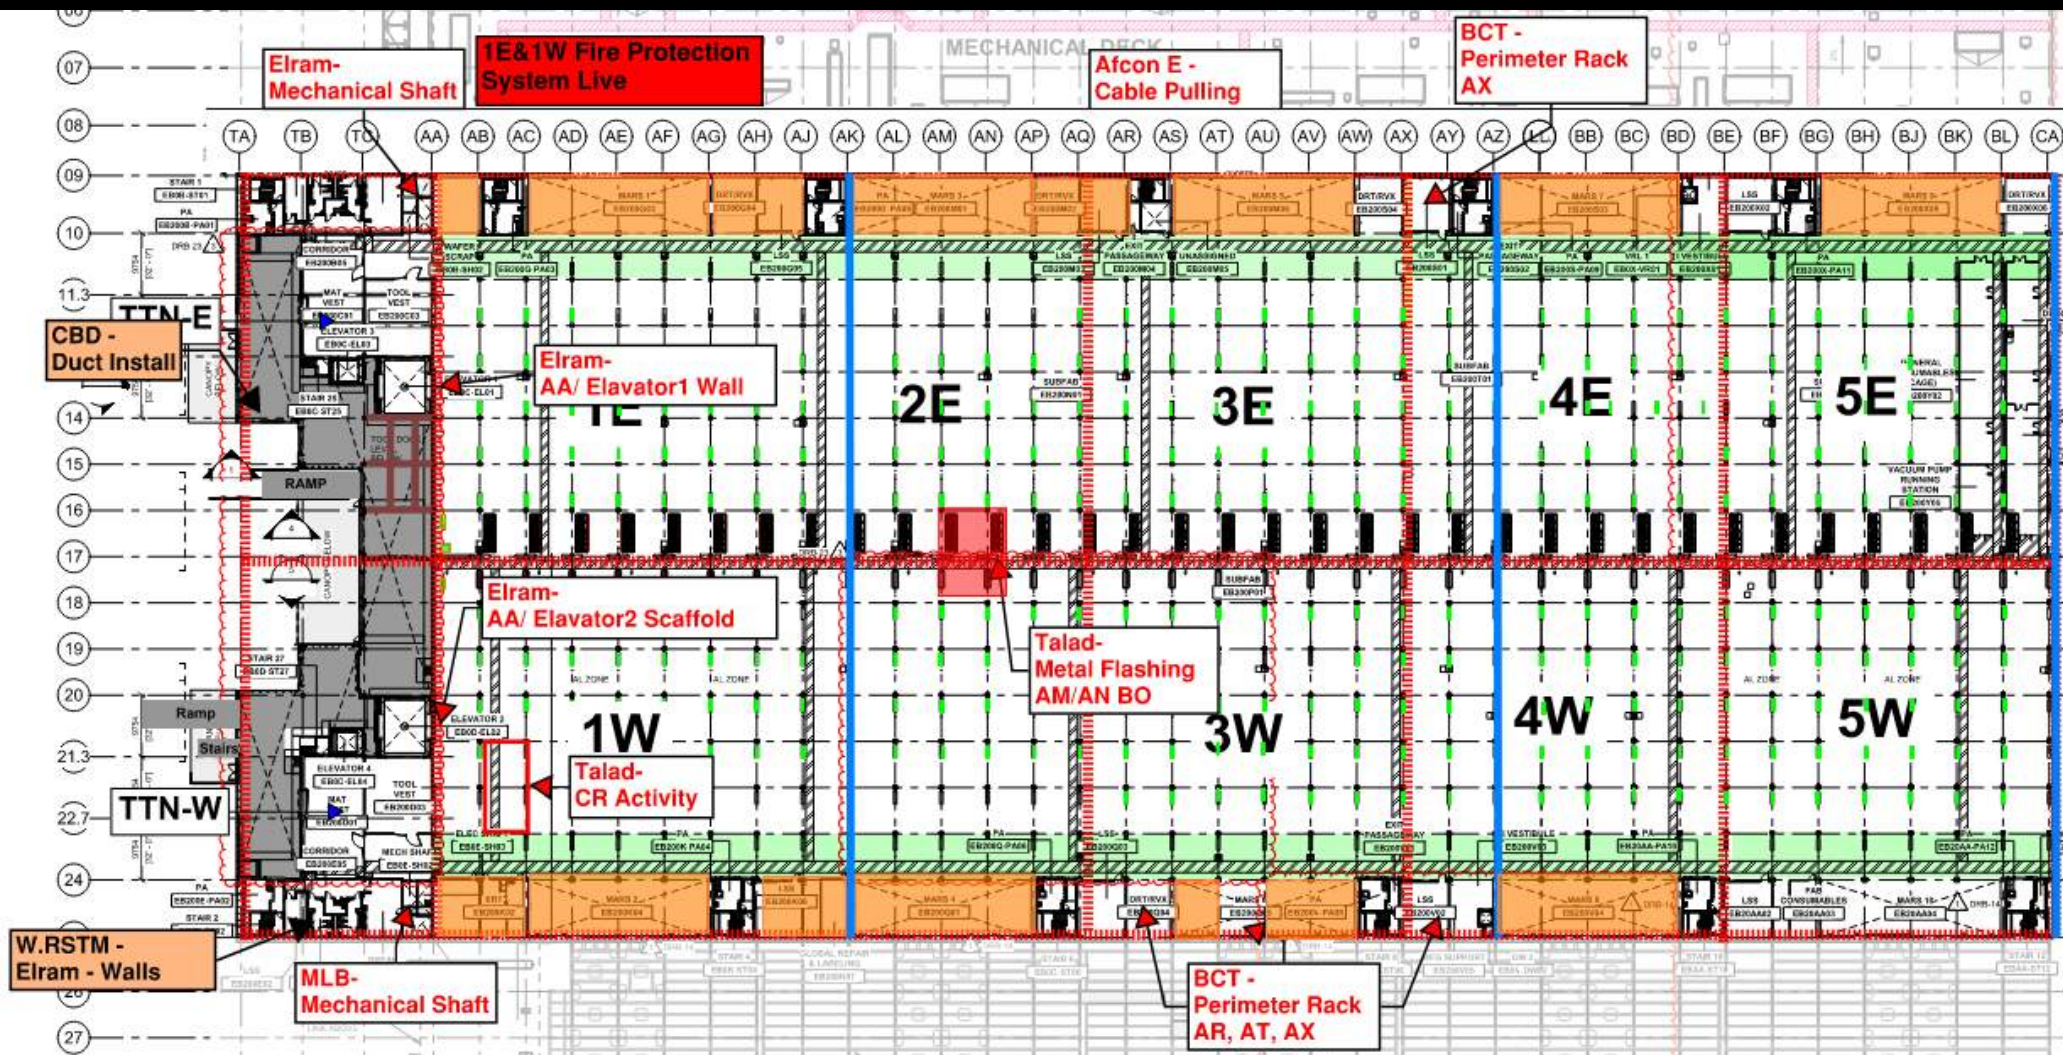


AM17 AN17 Block outs



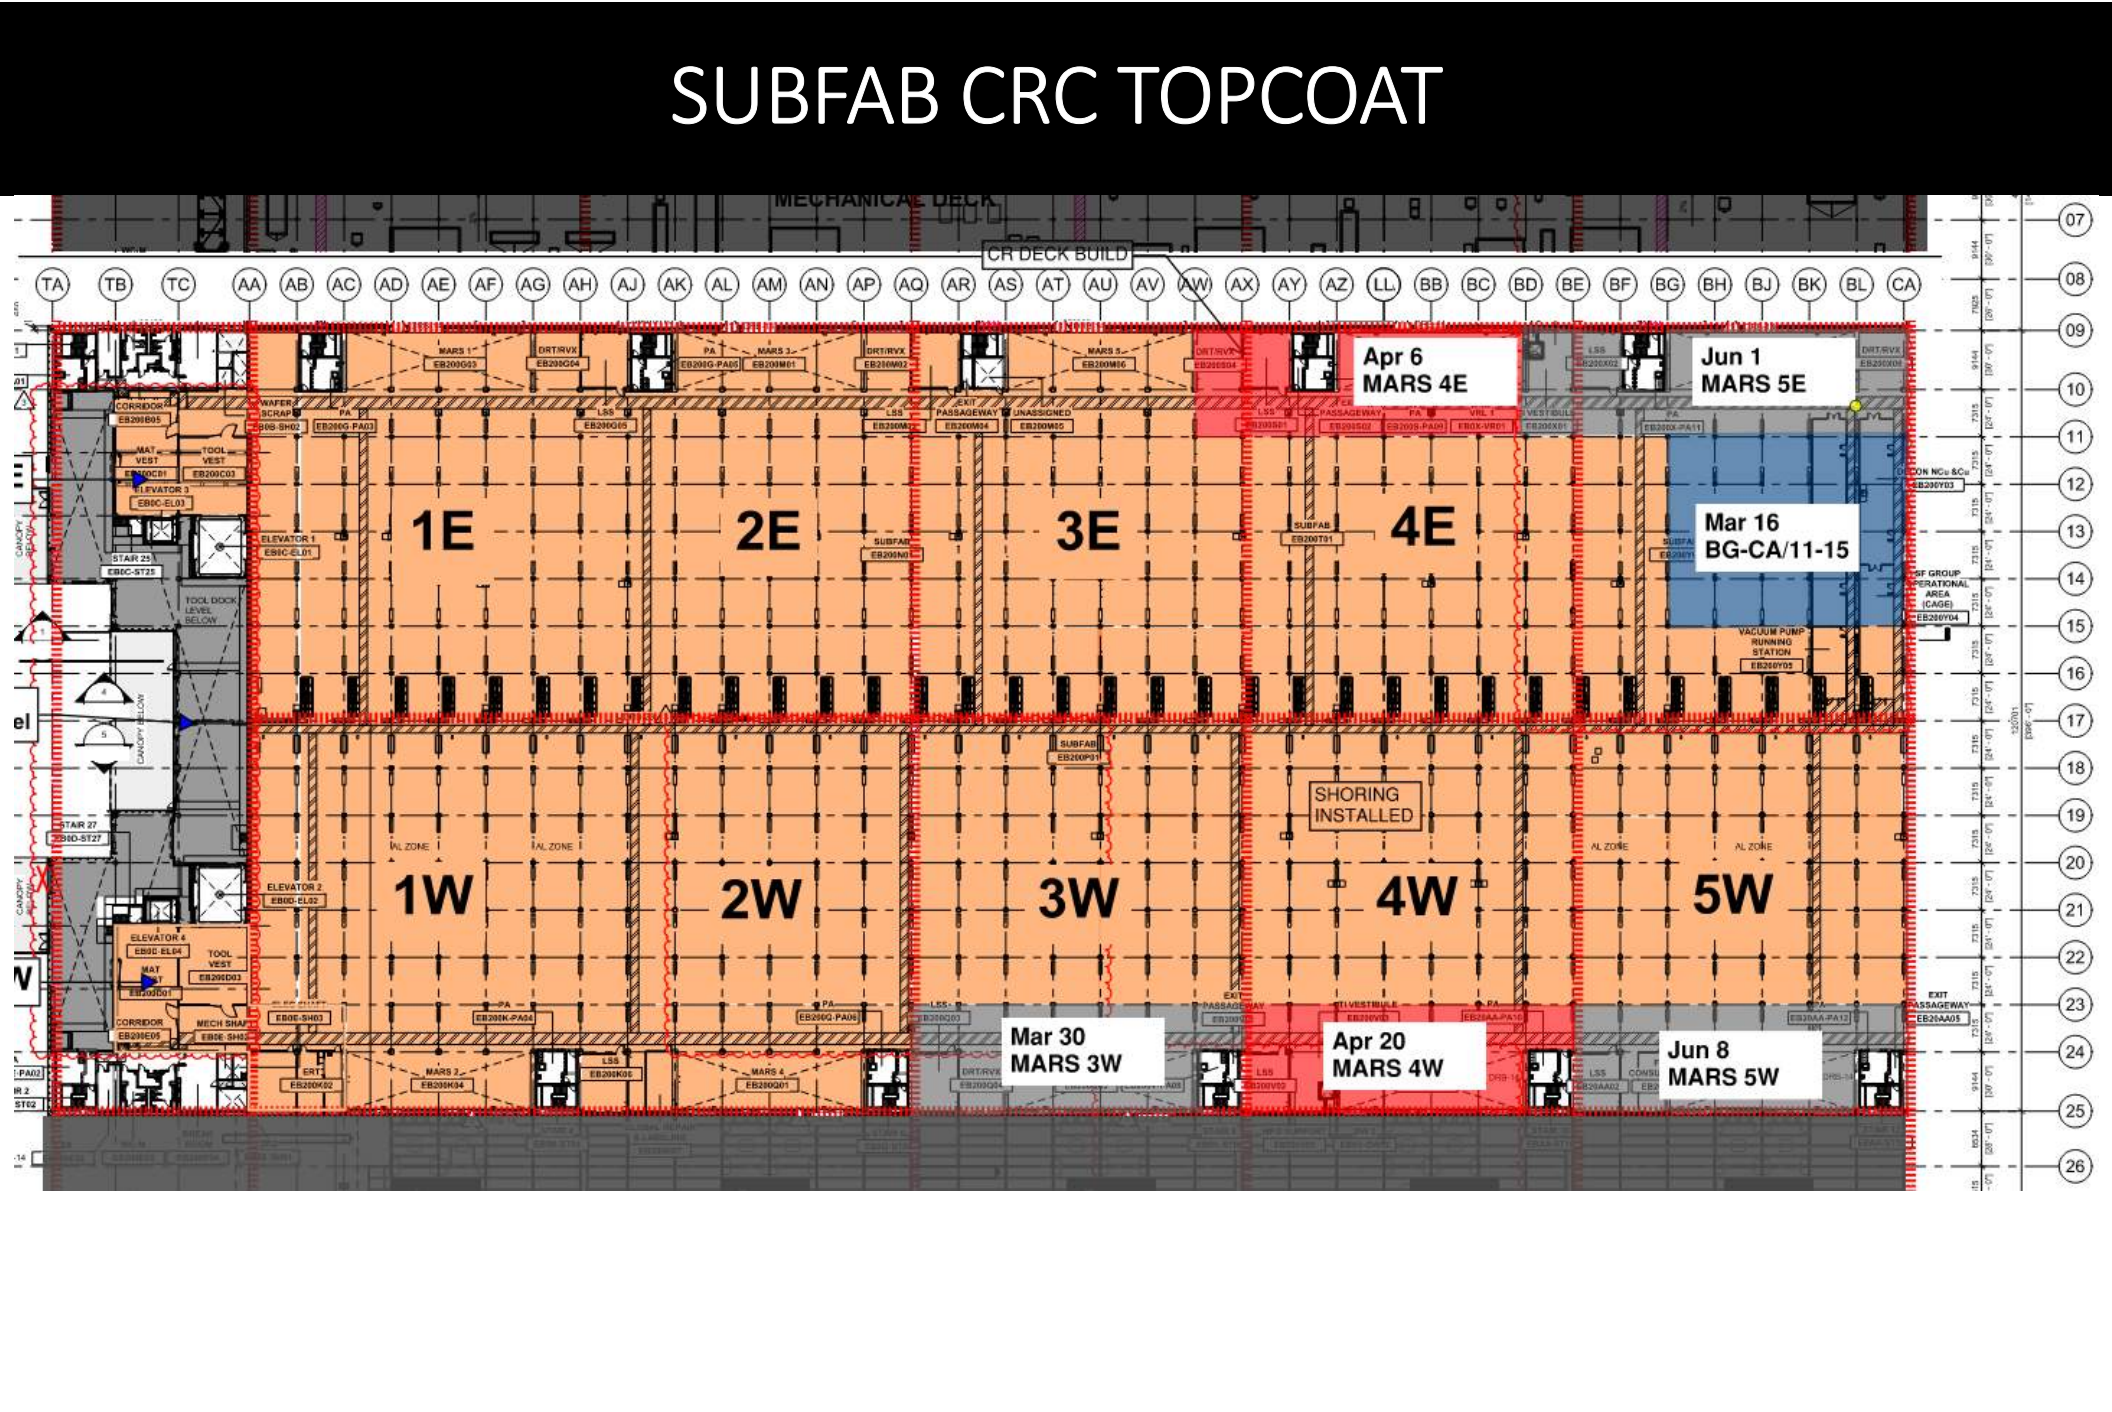

Lesico Pressure Test Today

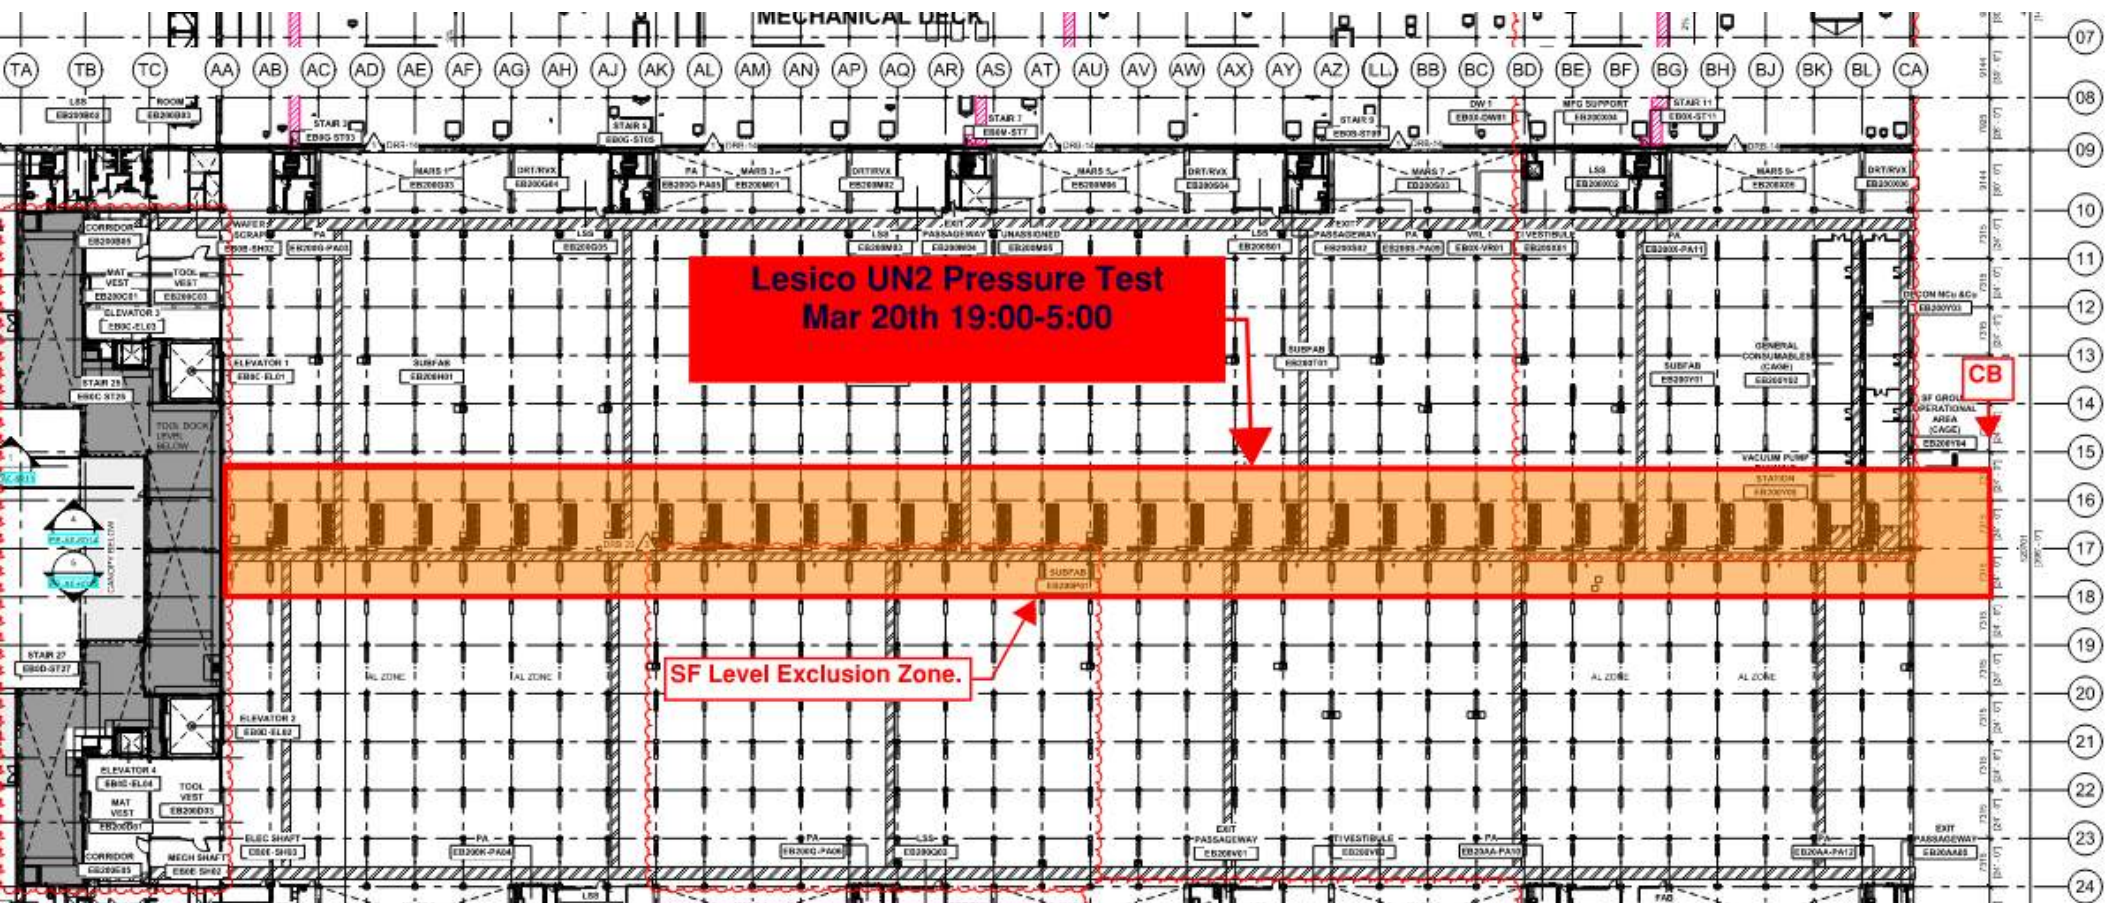


[illegible]


BCT/Lesico Pneumatic Pressure Test
Mar 21th 11:30-13:00
AZw,BAw

SF Level Exclusion Zone.

Lines being tested

SUBFAB BUILDOUT MOD 2

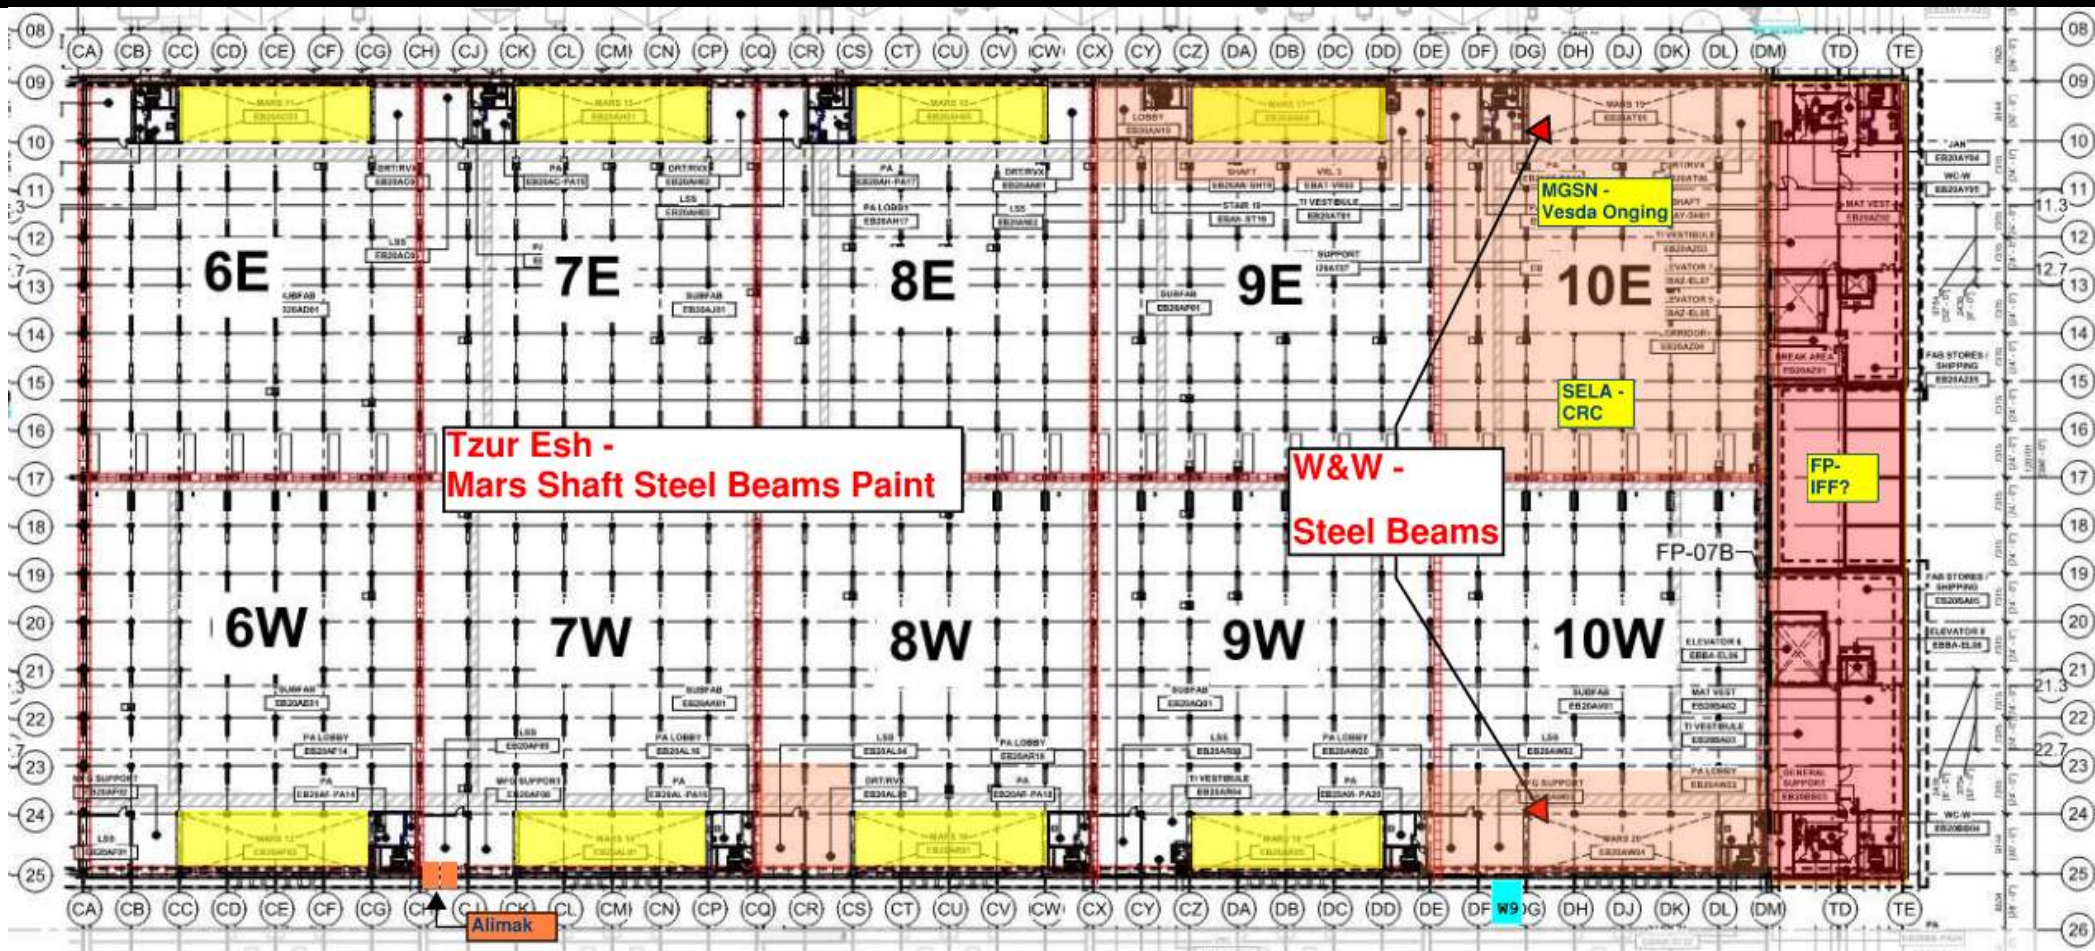

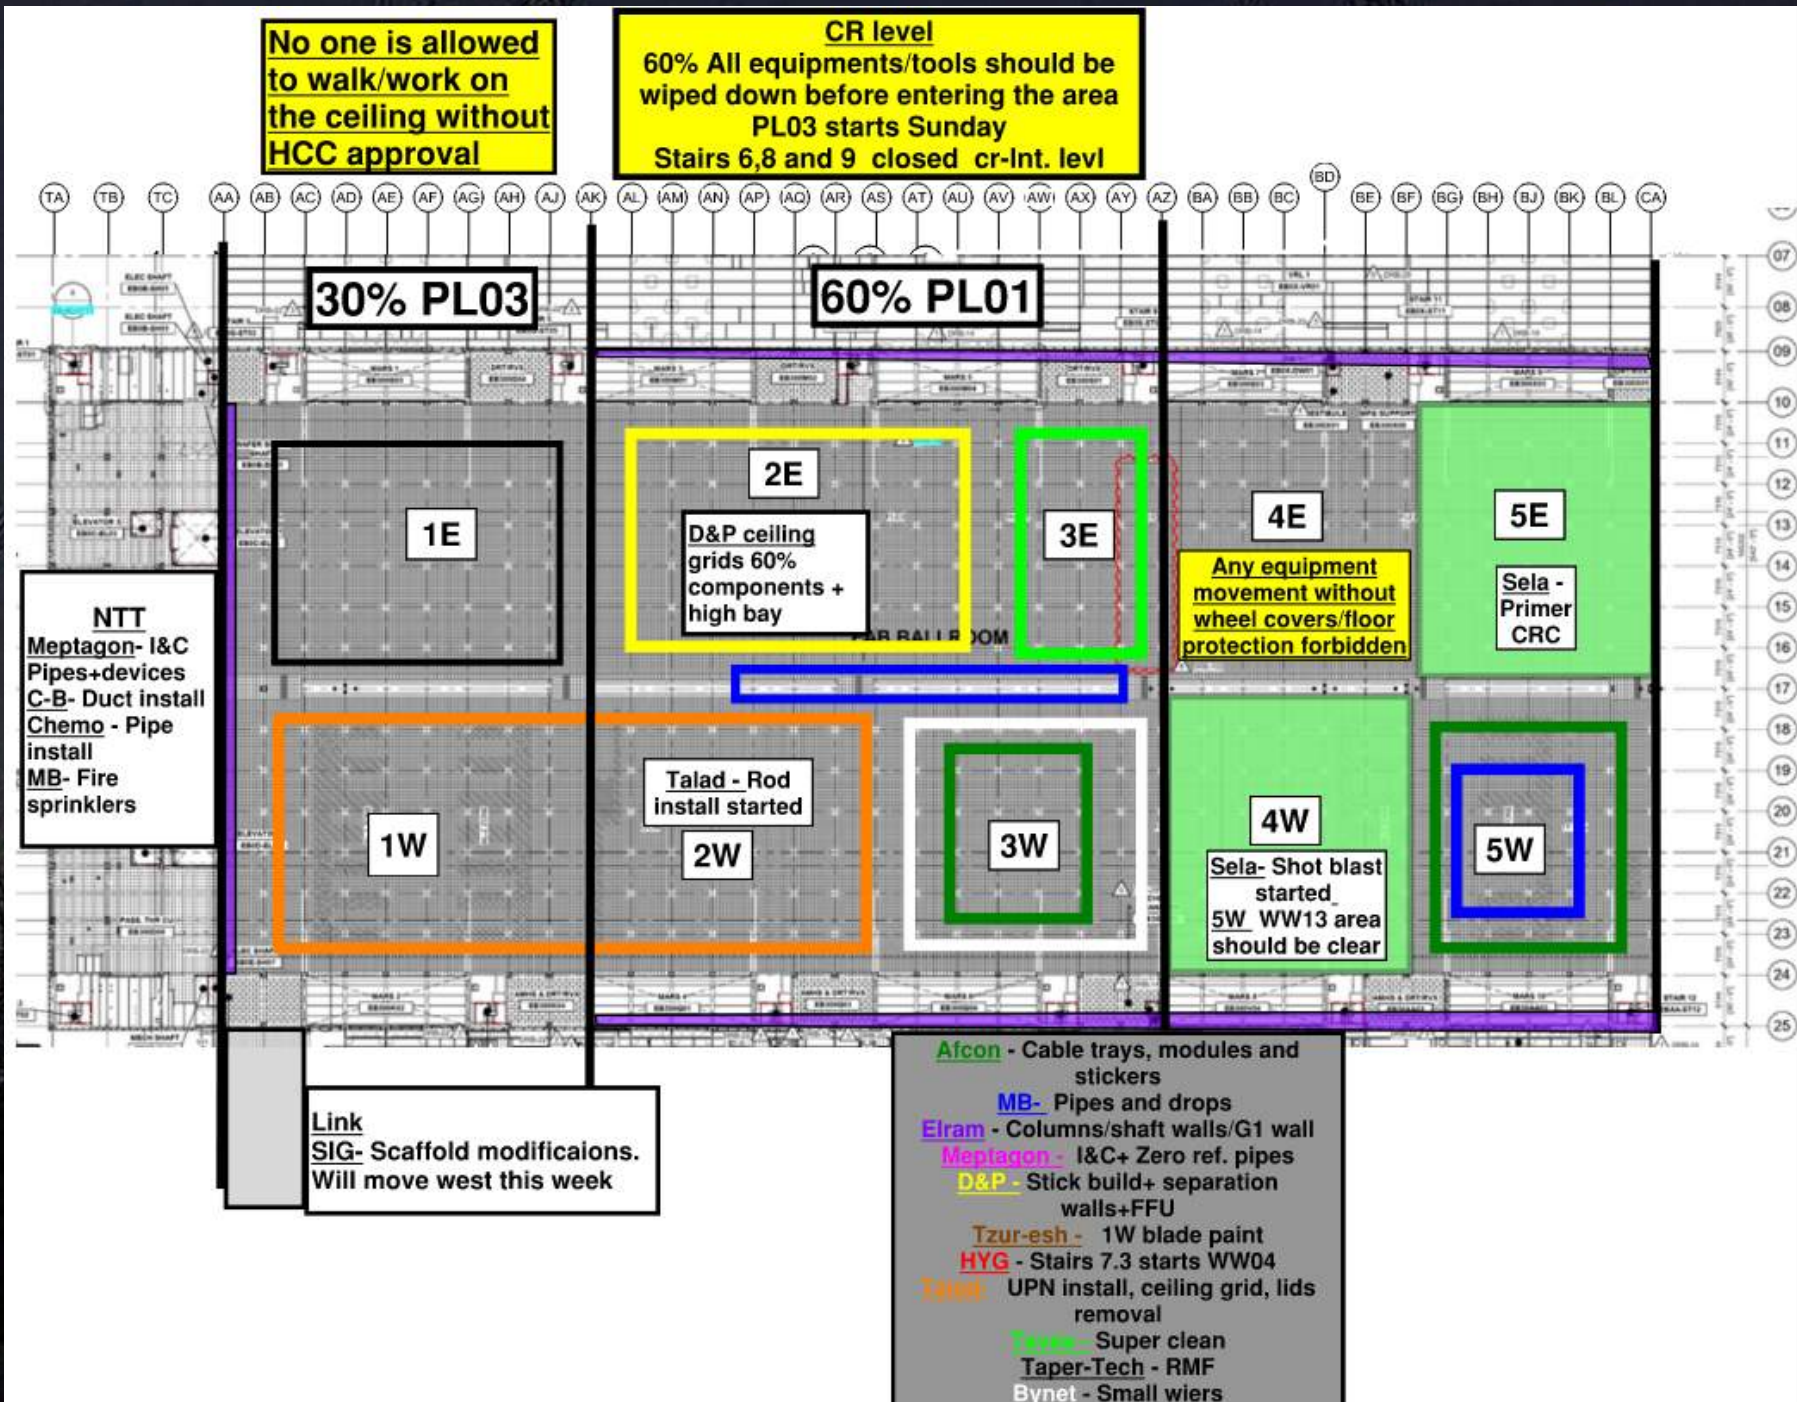



Afcon - Cable trays, modules and stickers
MB - Fire sprinklers
Elram - Gypsum/G1 wall
Chemo - Skids and pipes
SK - IA pipes
Tzur-esh - Paint+ touch ups
WW - Cat walk
RPC - 4DA/5DA FP
Tavas - Super clean
Bynet - Communication weirs
Megasone - Speakers
Meptagon - I&C

Int. level
60% All equipments/tools
should be wiped down before
entering the area
Taper-tech - Started to install
fence at 100%


30%


60%


NETT
Chemo- Racks+pipes
ongoing
Megasone - Small
wires+Speakers
RPC- FP rack/girts
NWTT
Chemo- Racks
MB- FS install
AFA- Vesda
RPC- started FP racks

WW/SN - Handrail install
Elram - G1 metal sheet

TMT - Penetrations for
Afcon, D&P, Talad and
MB

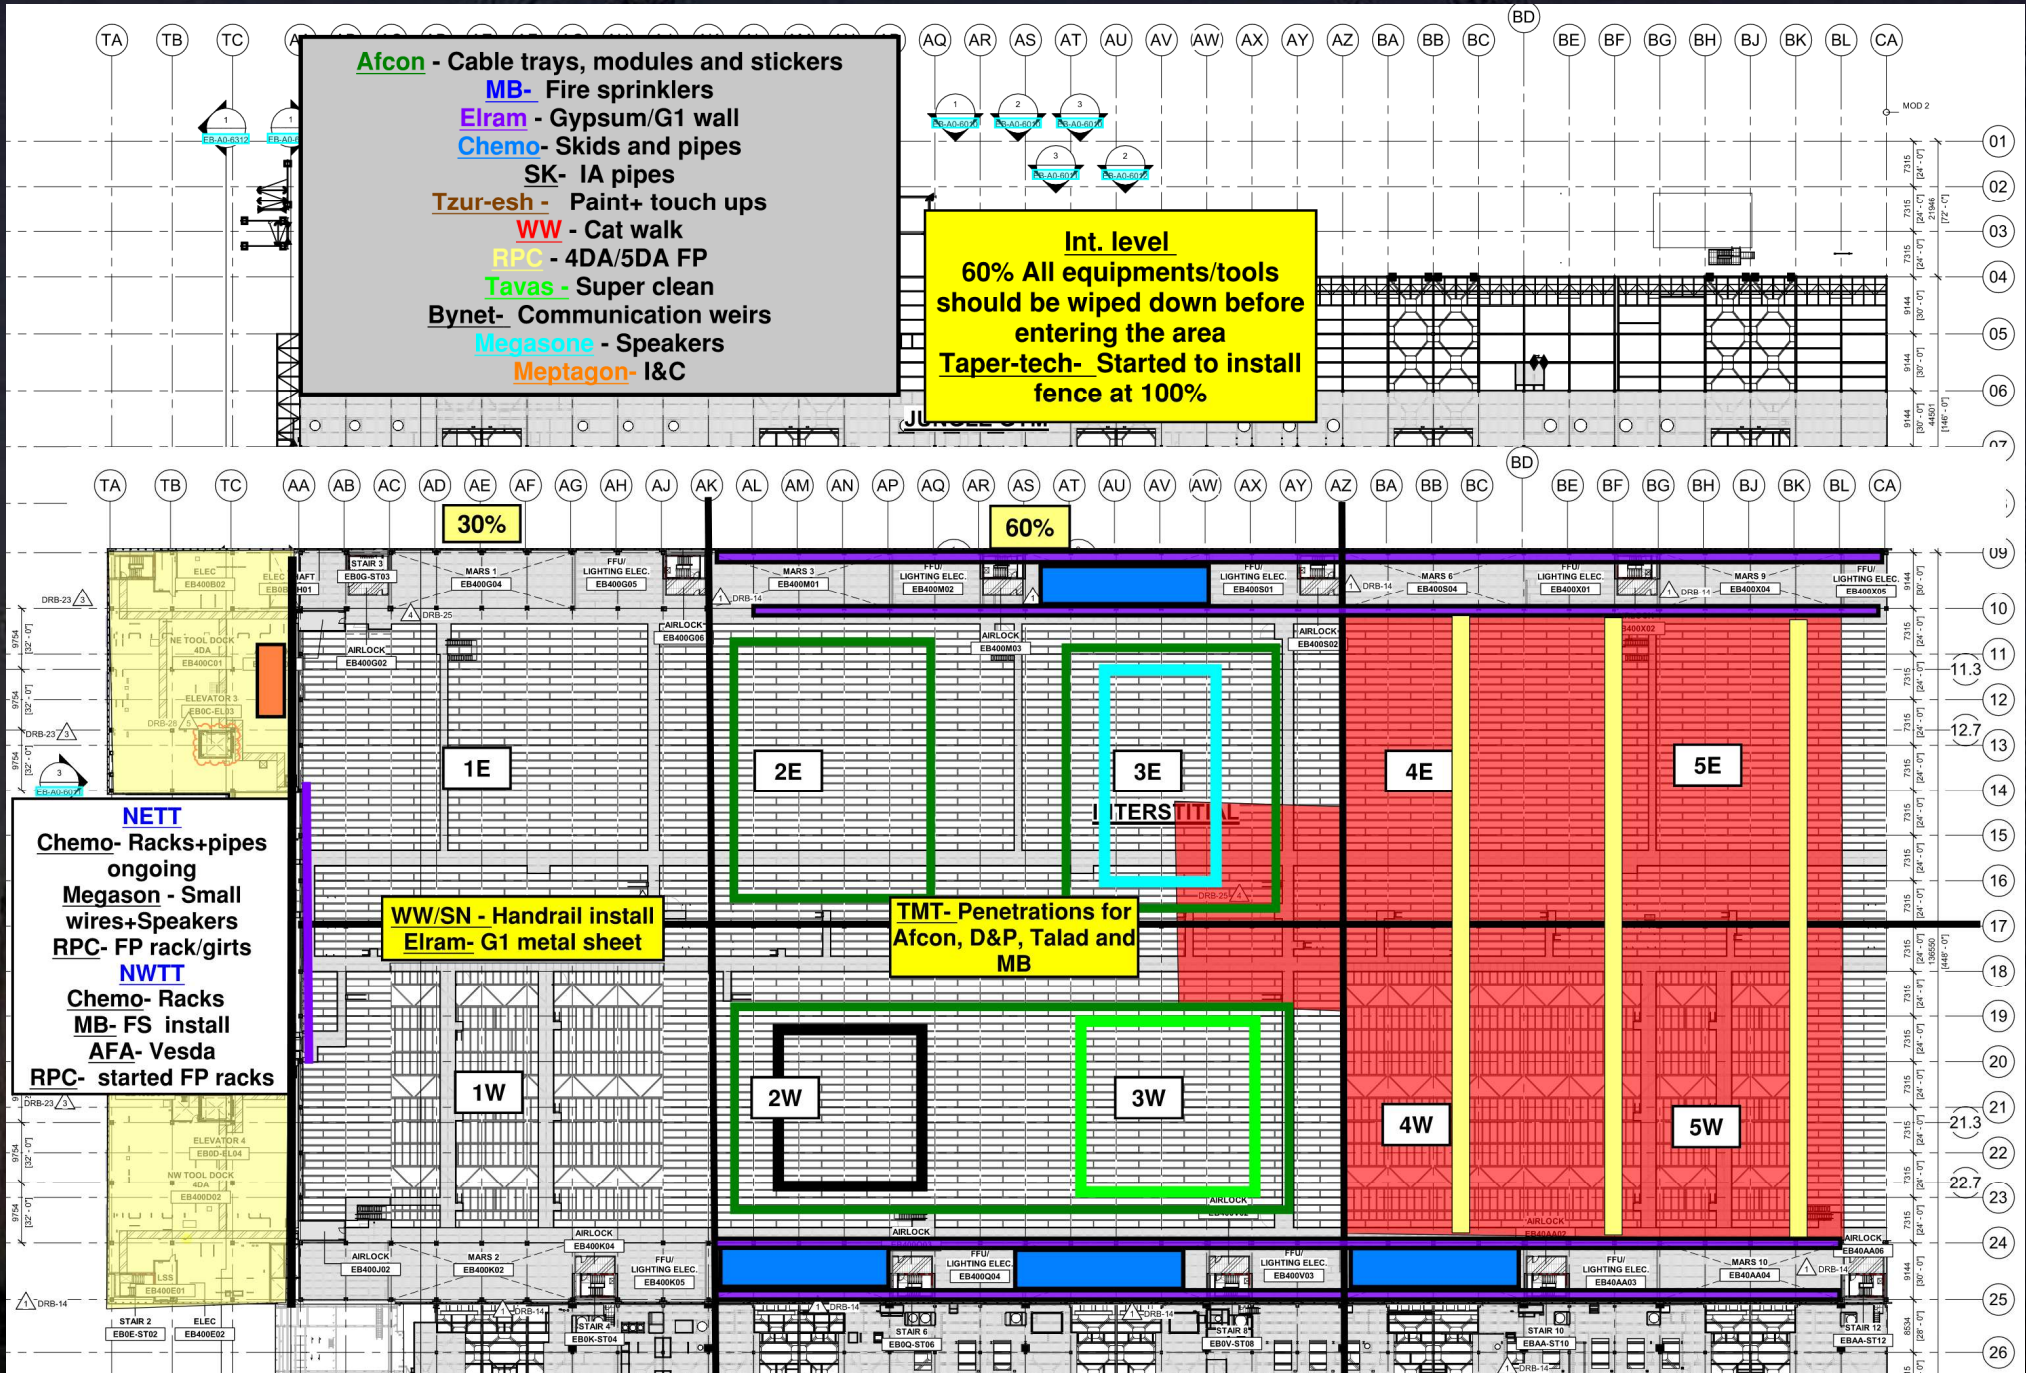

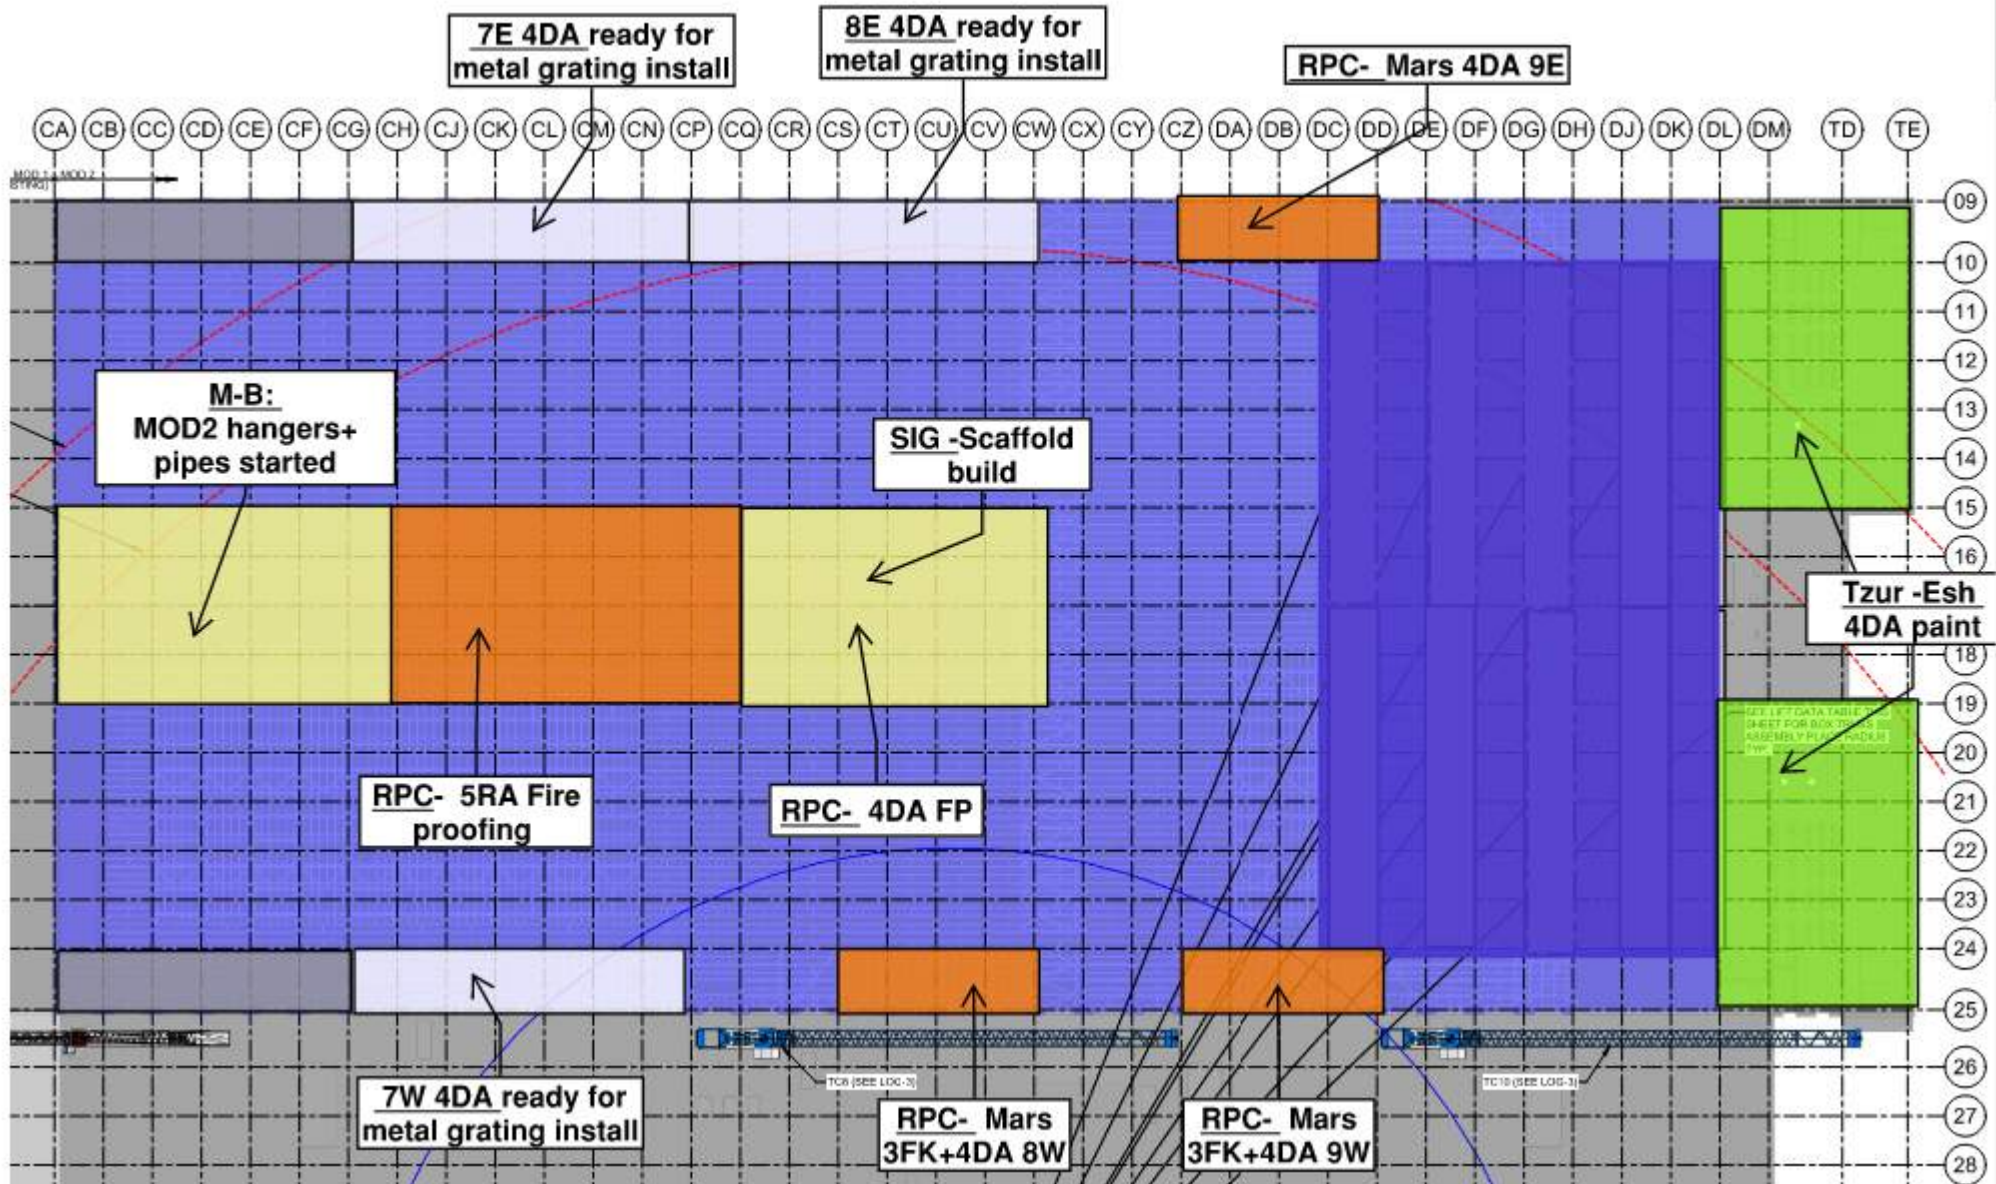





HOFFMAN CONSTRUCTION COMPANY



Siding Penetration Request Form



Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

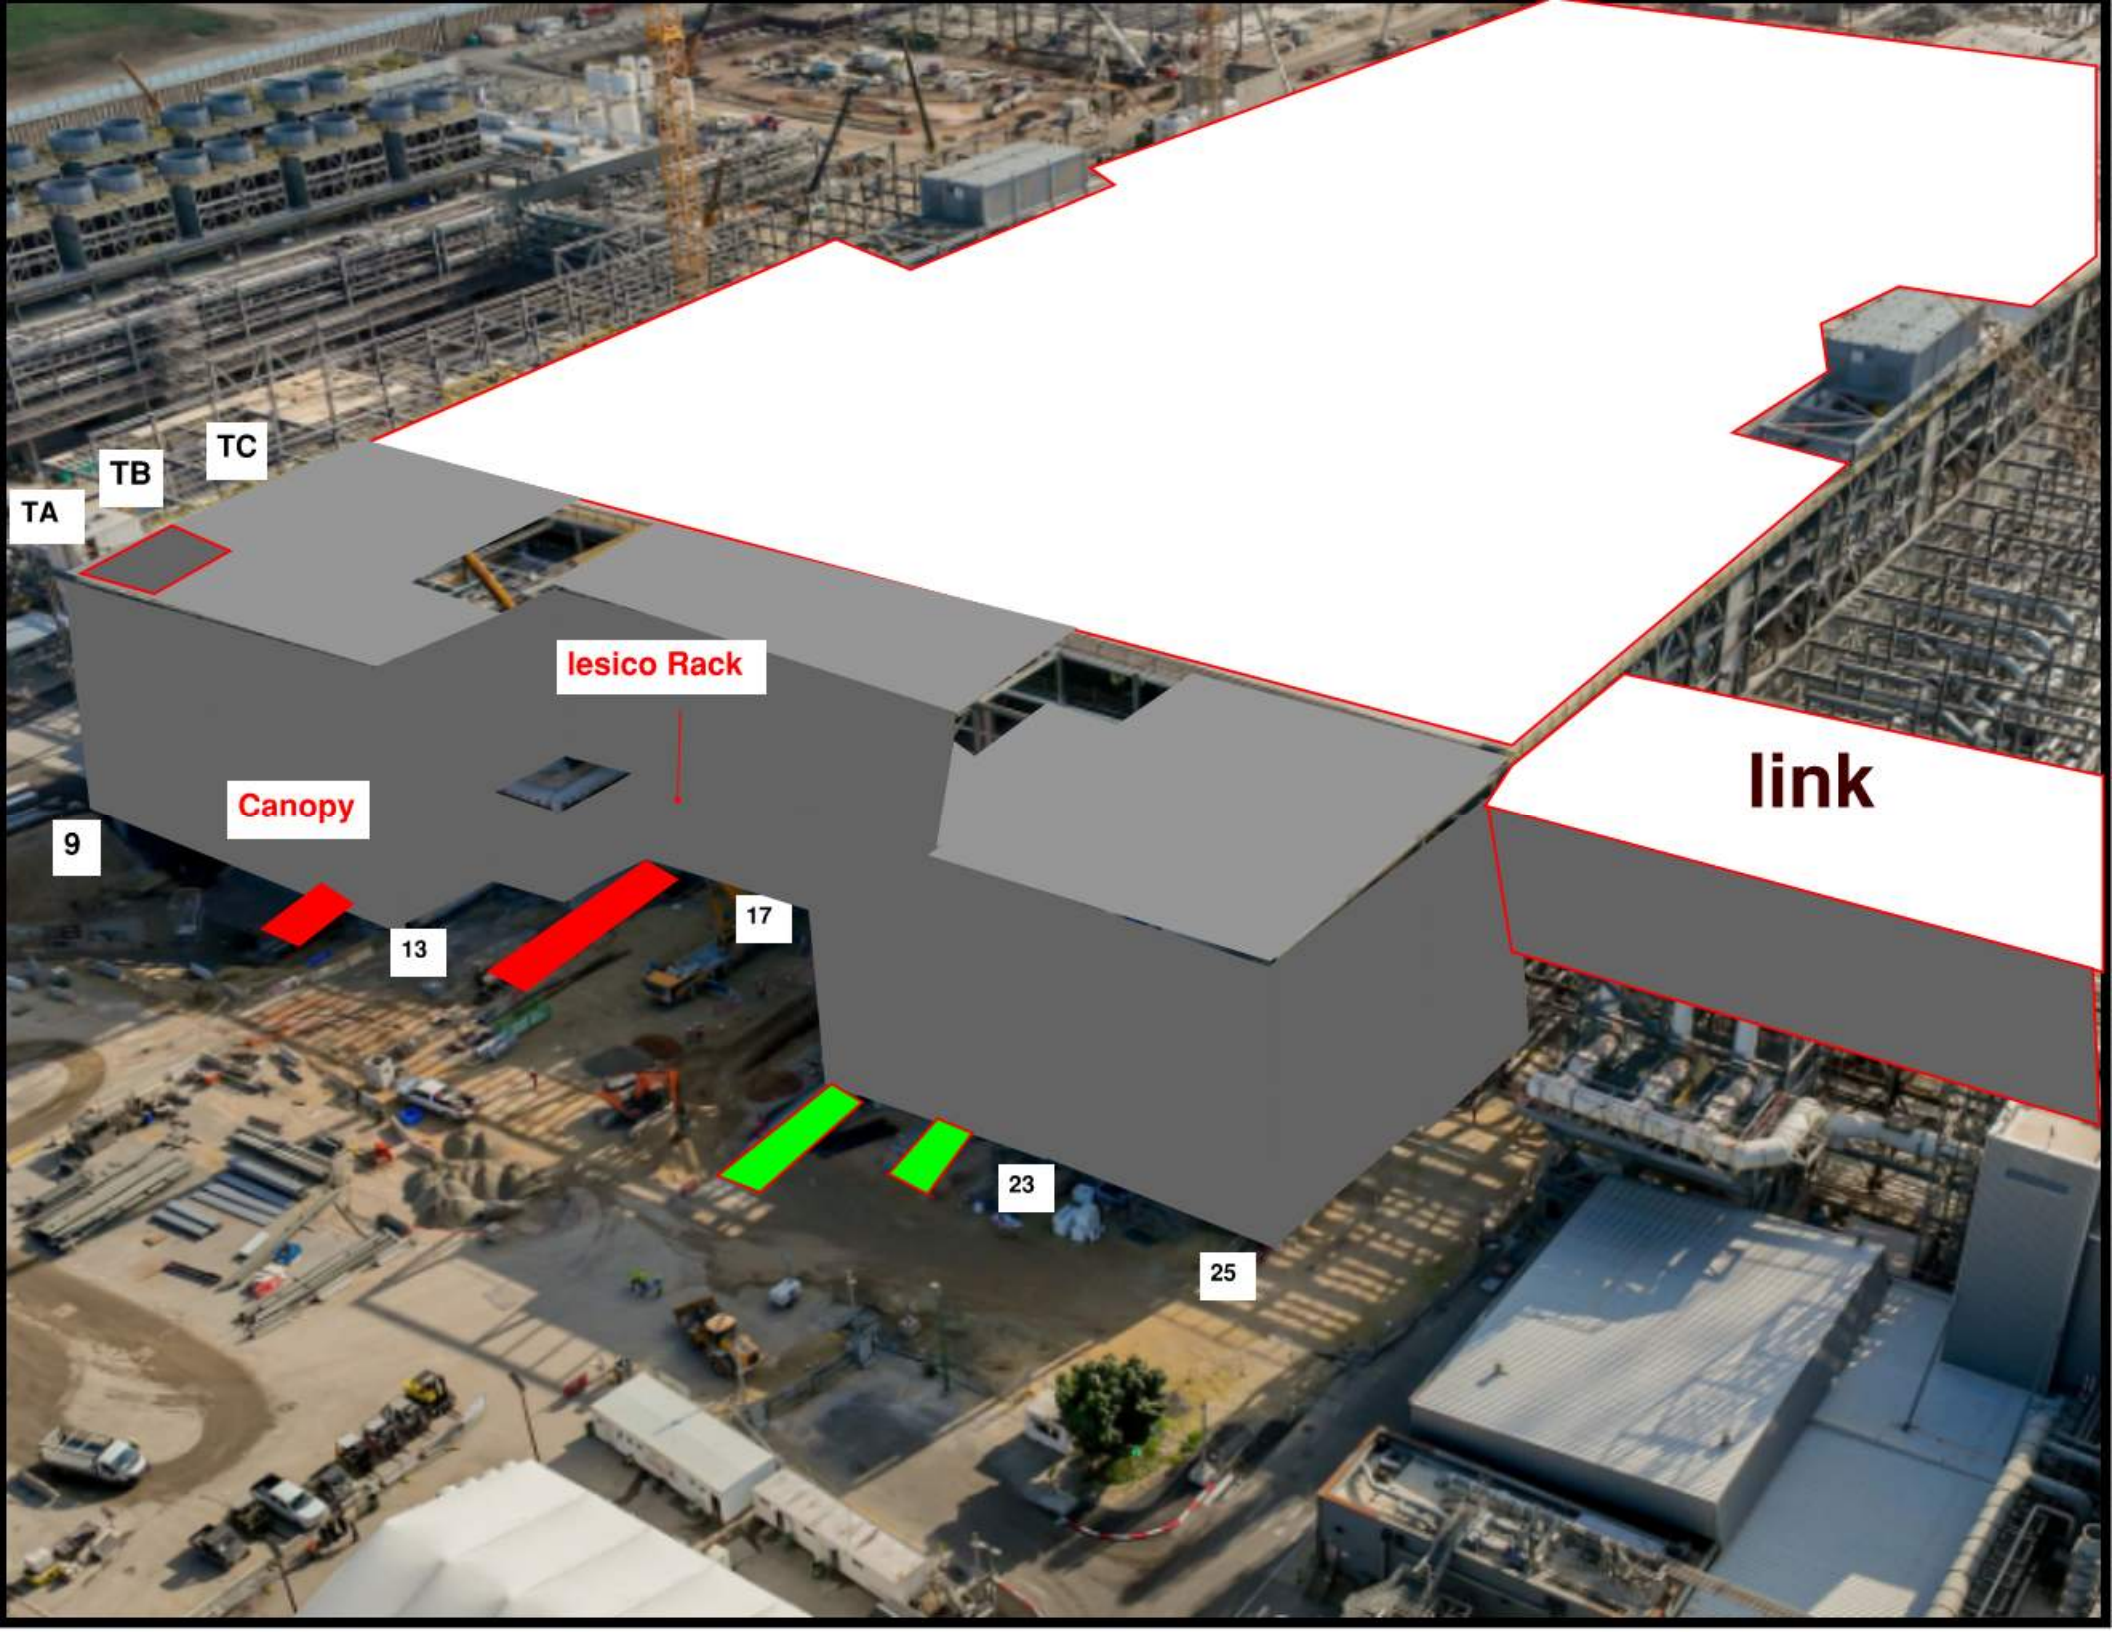

TA

TB

TC

lesico Rack

Canopy

link

9

13

17

23

25



MOD 2 EASTSIDE GIRTS/SIDING

2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

MOD 2 WESTSIDE GIRTS/SIDING

READY FOR GIRTS 

INSTALLING GIRTS 

READY FOR PANELS 


PANELS INSTALLED 



PSSS.1

Utility Level 1YA

PSSS Roof 2SA

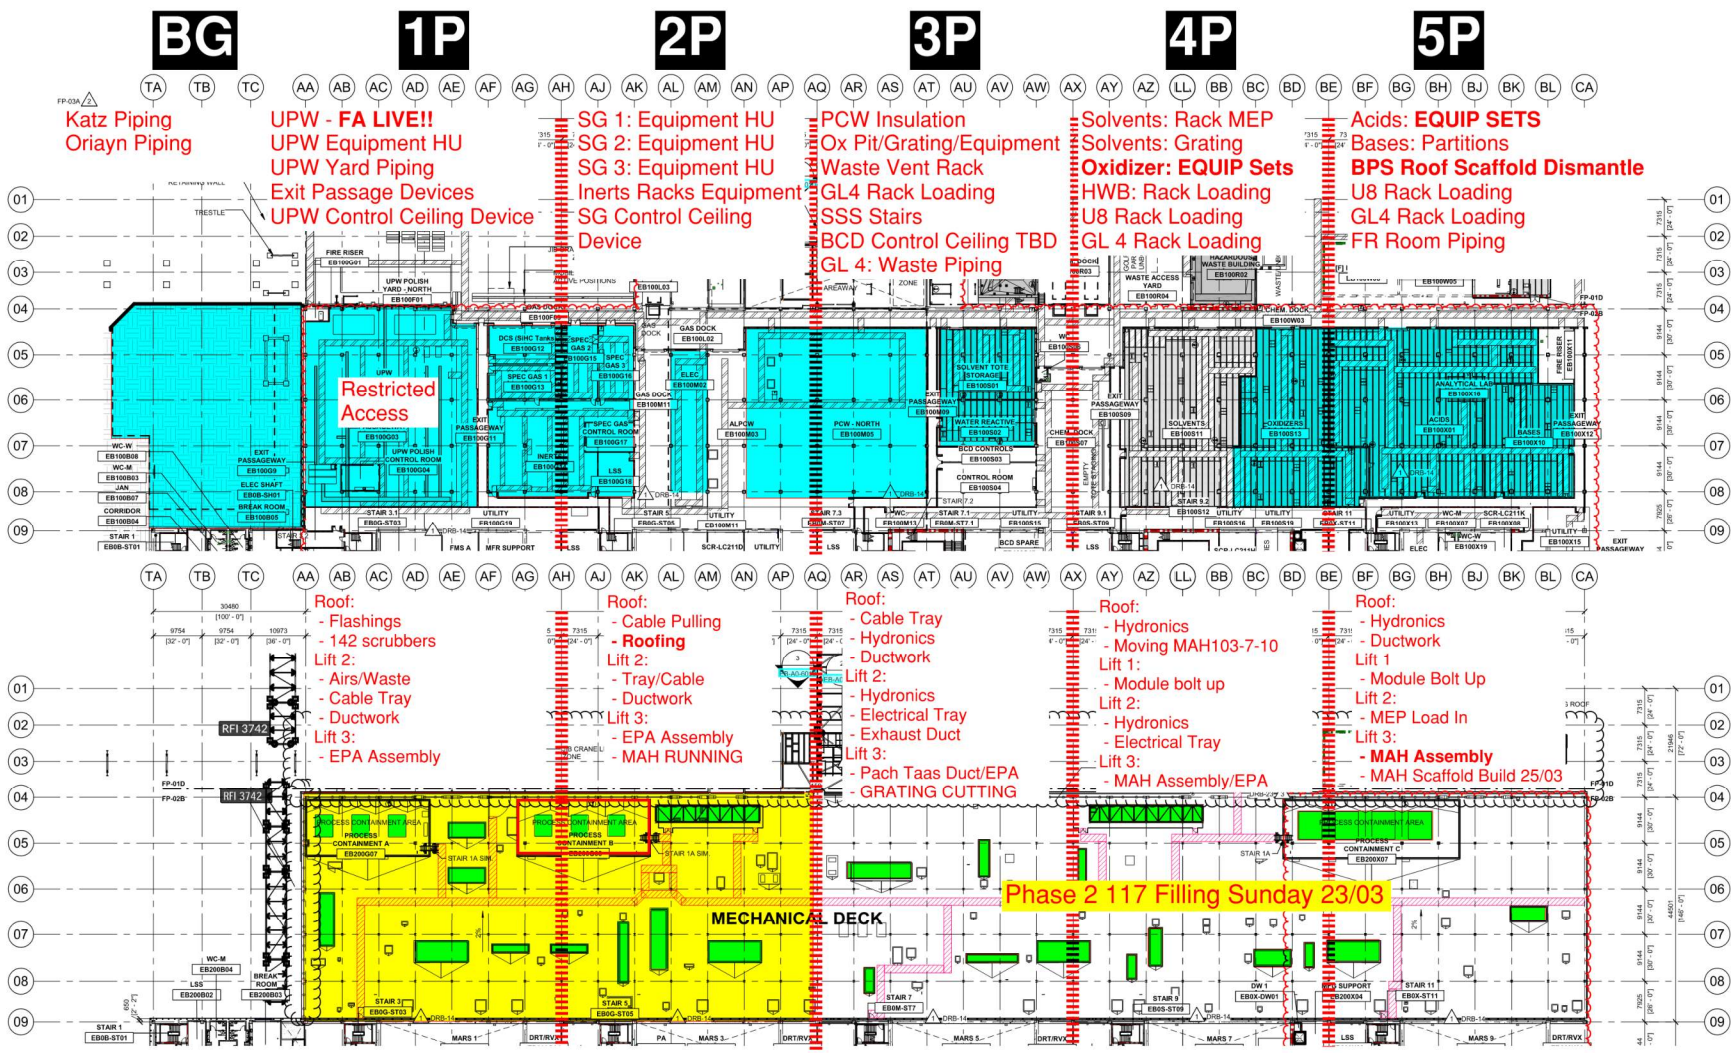

PSSS.2

6P


7P

8P


9P

10P

Utility Level
1YA

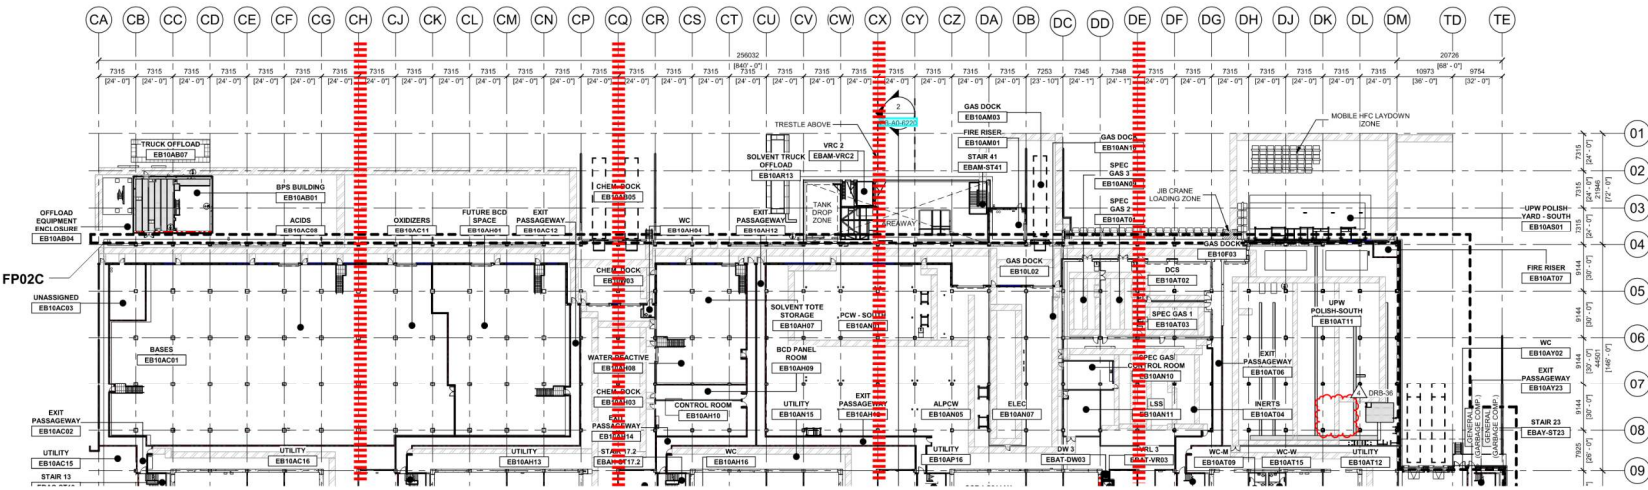


PSSS Roof
2SA

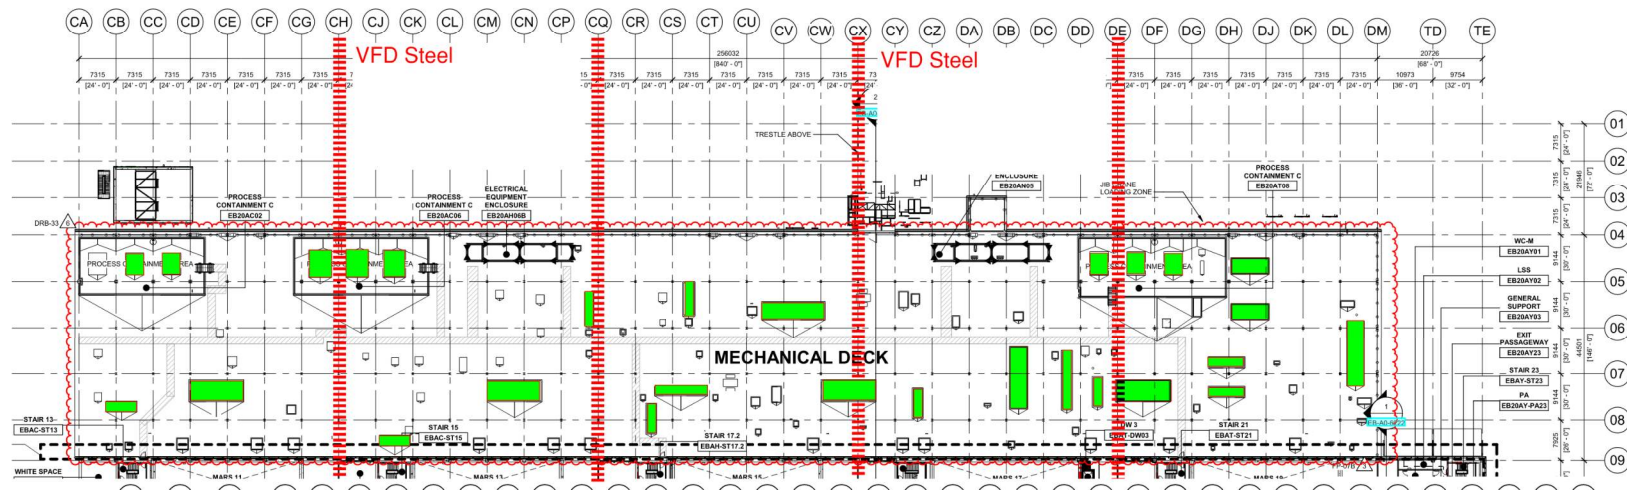

PSSS Pressure Testing

Utility Level
1YA

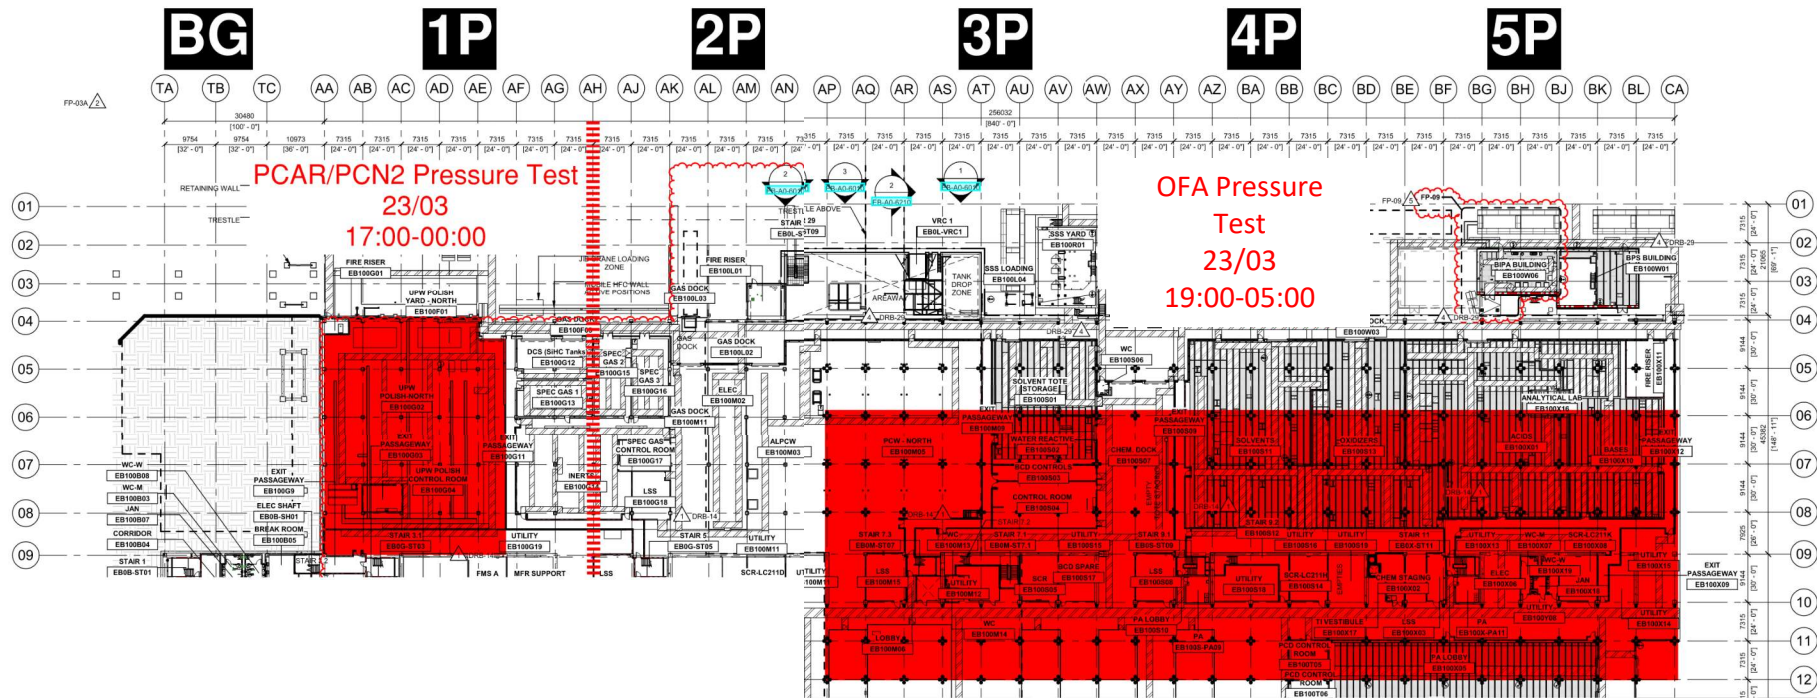

BGY GN2 Bursting Zone WW13




WJG – UL

*Pach Taas - installation of modules in west SUT.
* Pach Taas - completion of spools and lindapters on UPN 138

*Afcon - Installation of lighting and cable pulling

* Carmel Bidud - installation of air ducts from AH

* BCT - installation of permanent stairs to AHU
* SK - working on new cooper piping

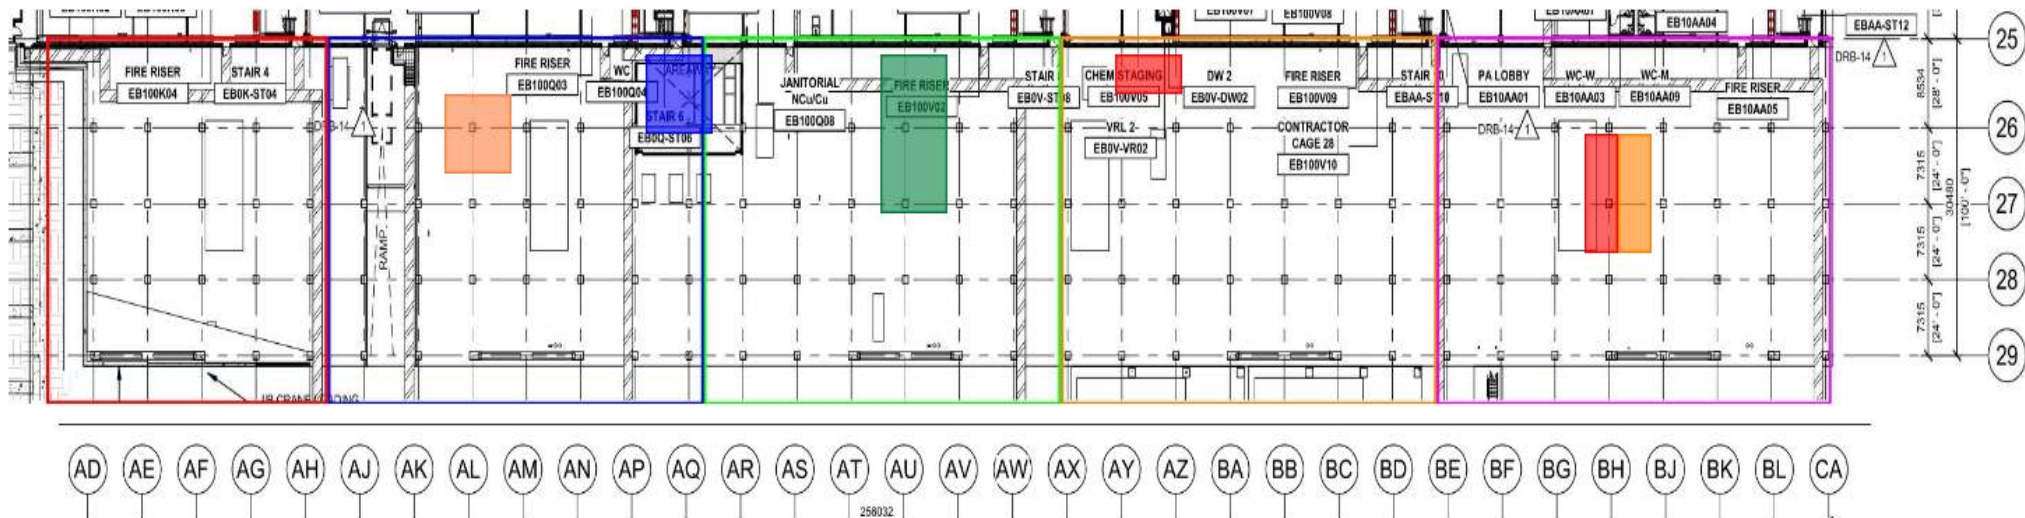


WJG – Lift 2

* Chemo - performing flushing to UPN 113 MARS pipes

* Meptagon - wiring of PCZ

* SN - installing handrails on lift 1

* Carmel Bidud - MAH scaffold waiting for green tag

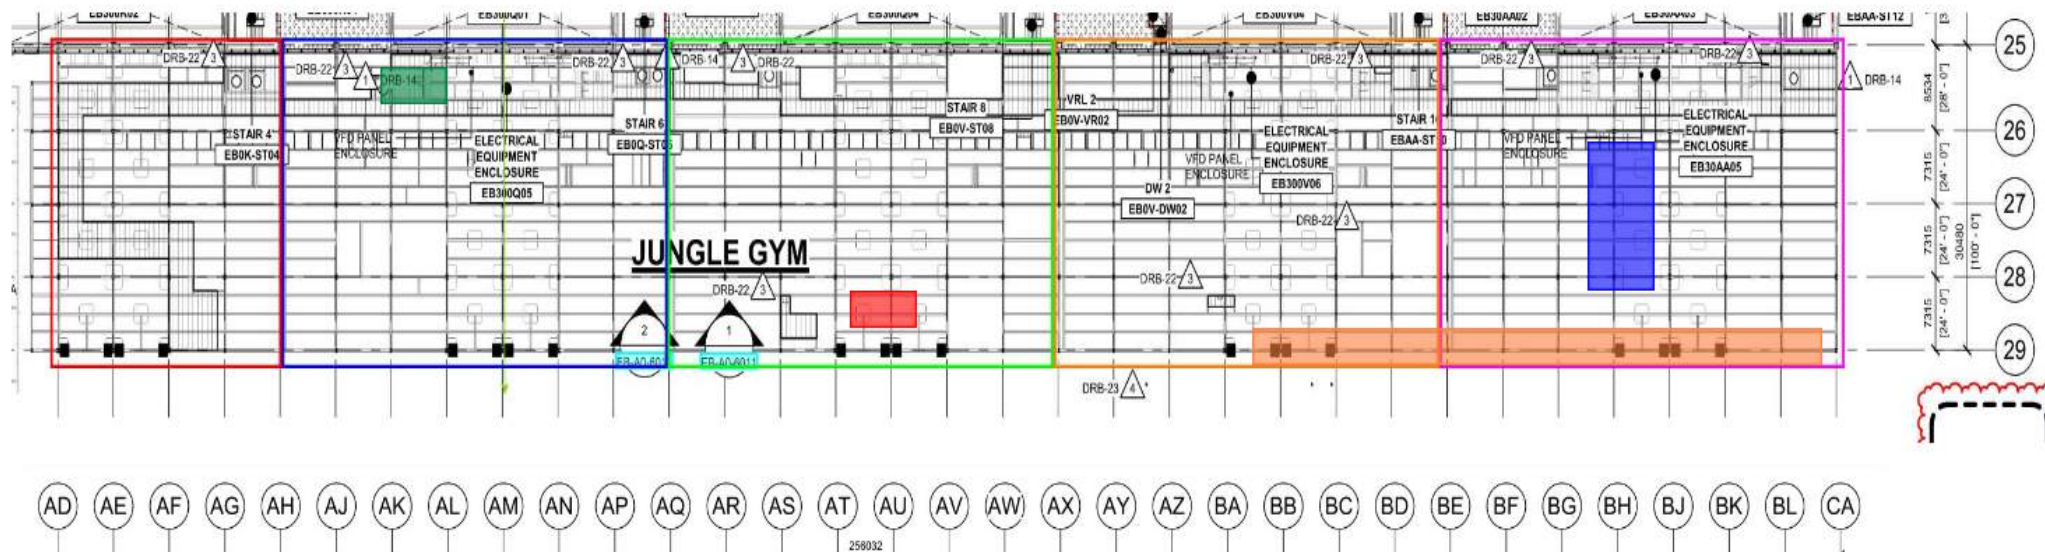


WJG – Lift 3

		* SN removing, cutting gratings and welding supports	* Pach Taas - working on Bypass structure	* SN -cutting grating penetrations
--	--	--	---	------------------------------------







CUB 1

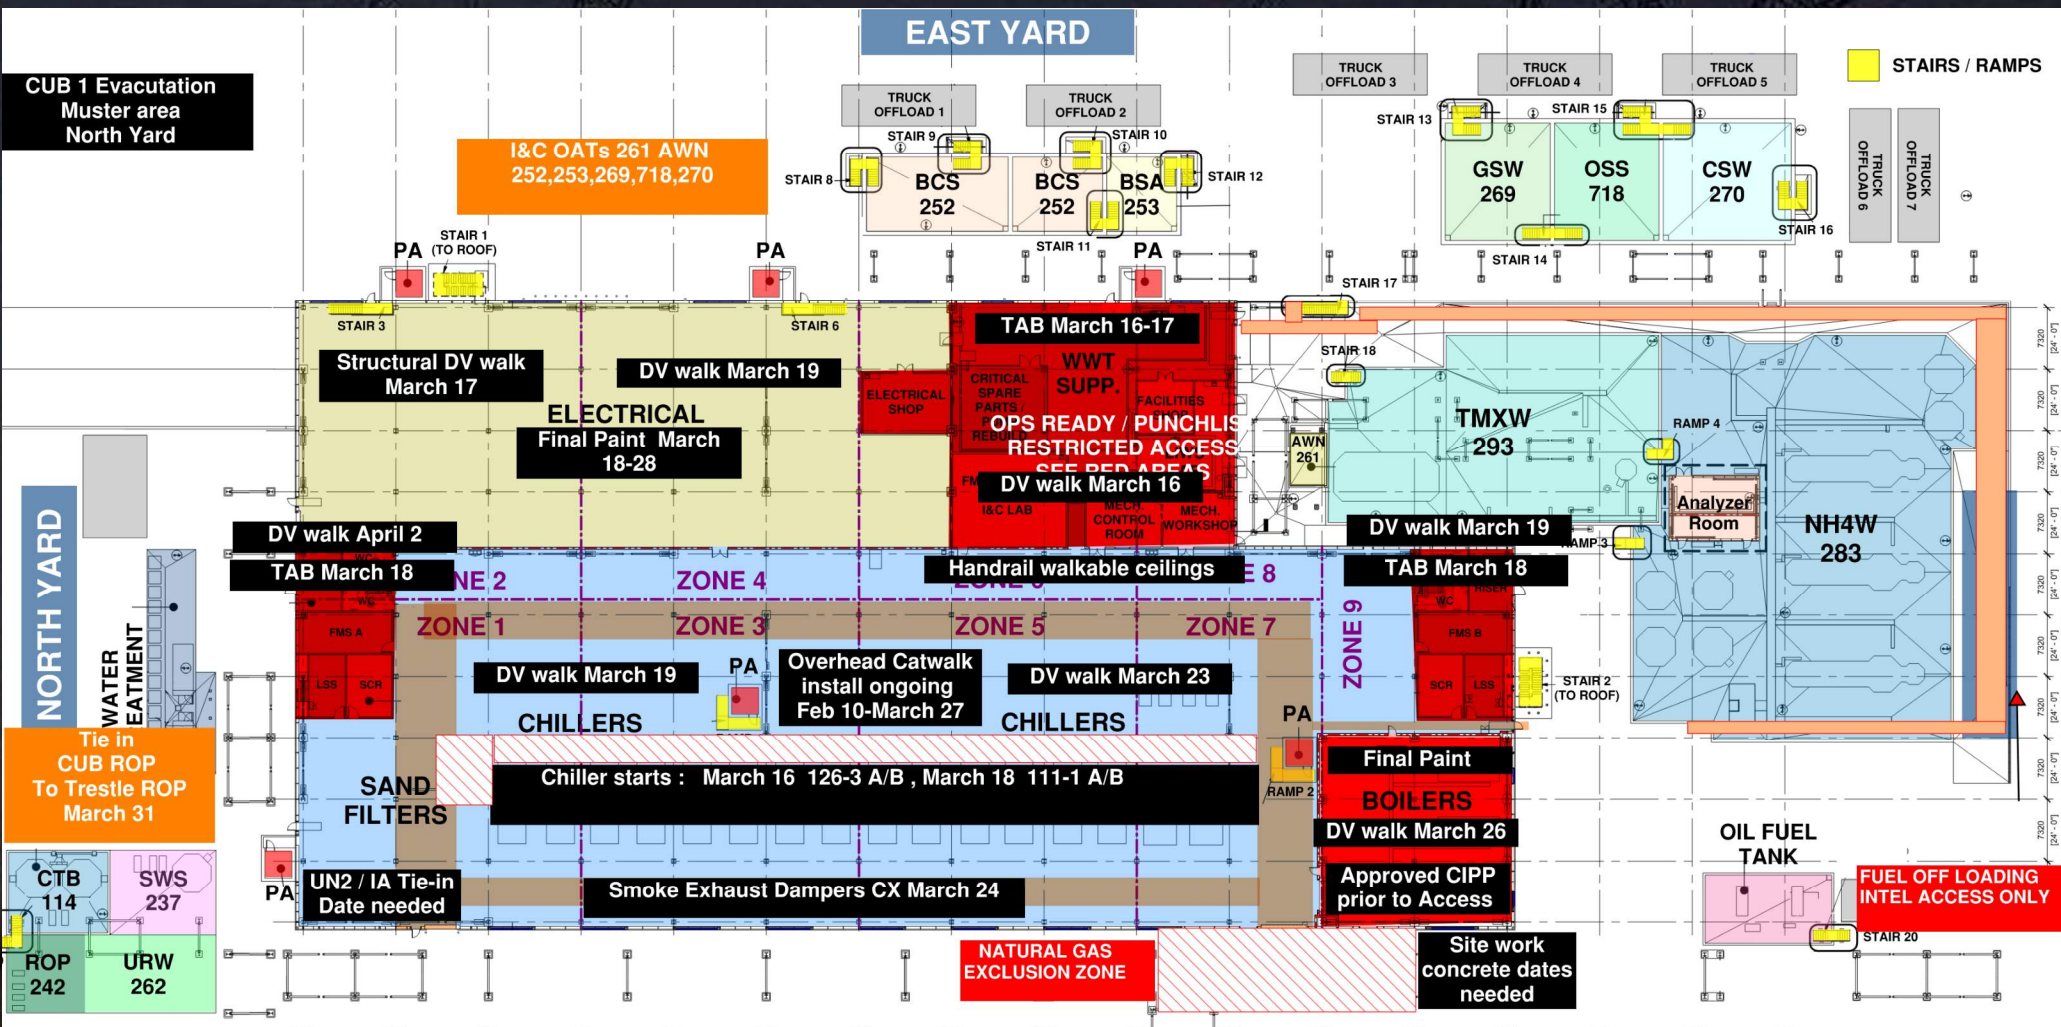


CUB 1 – EXTERIOR/ROOF

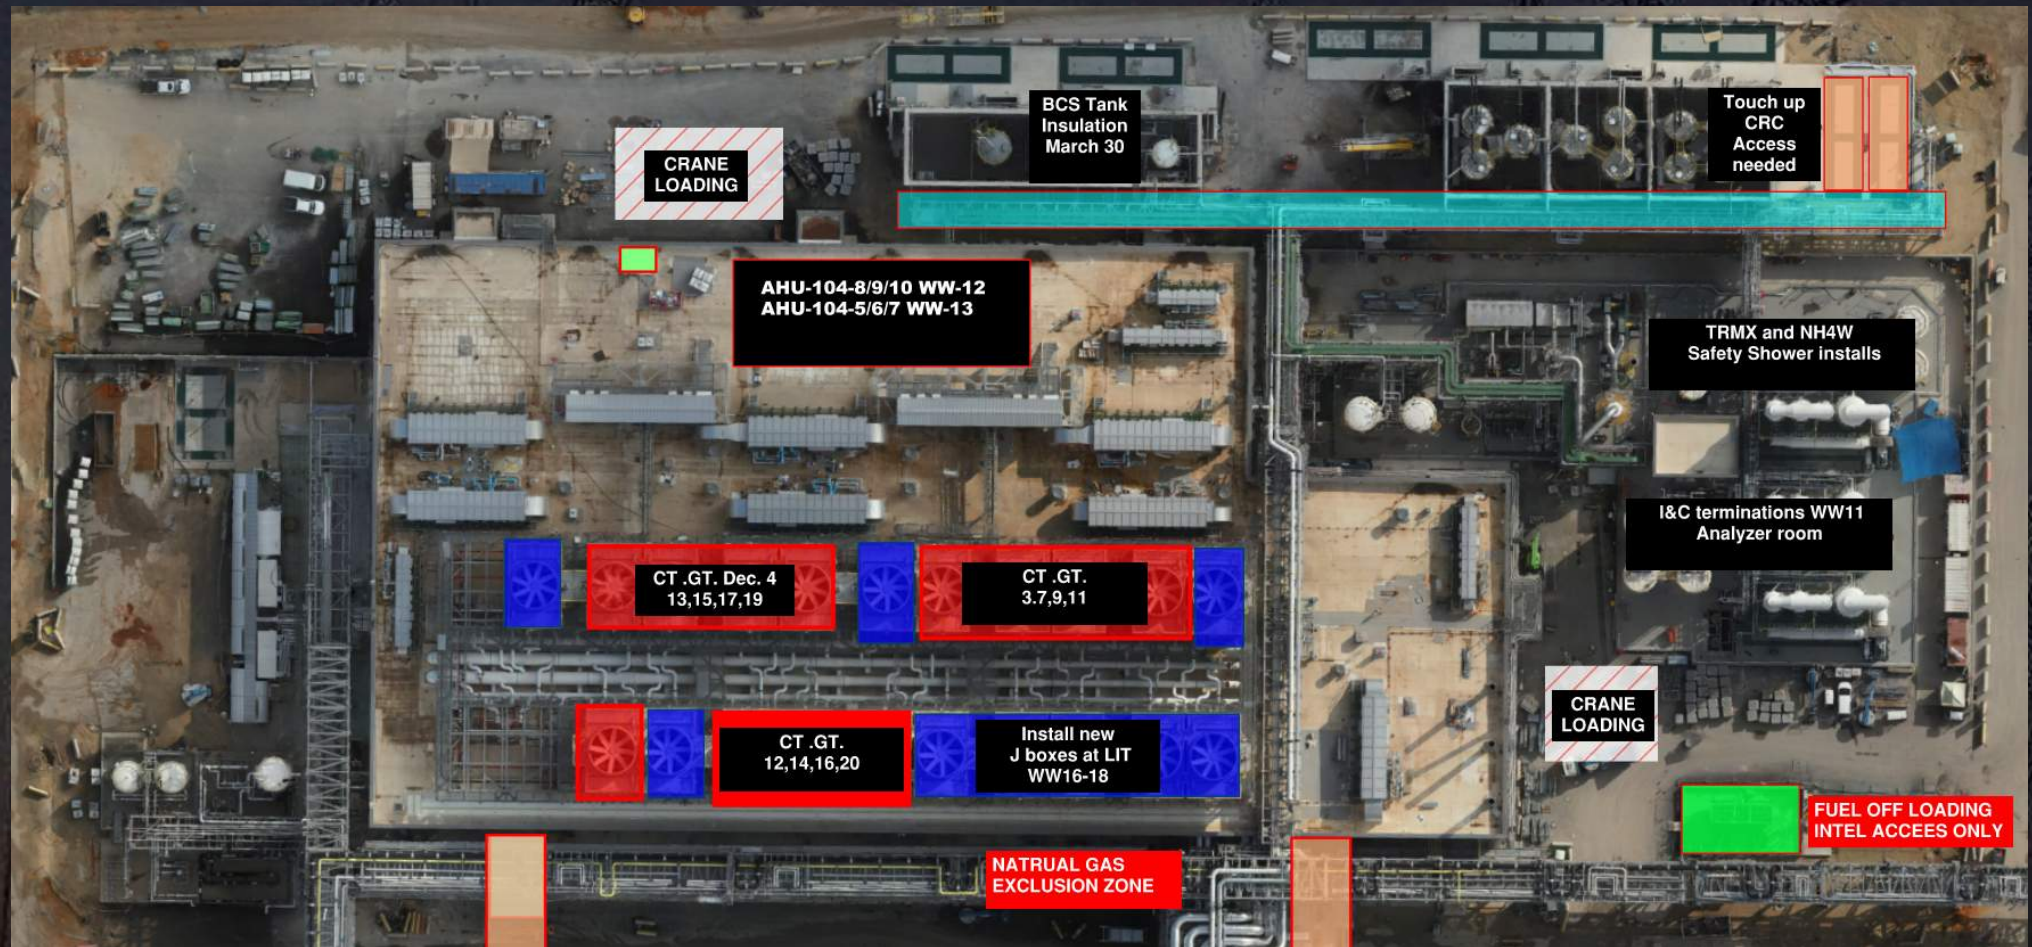


CUB 2- Load in & H&T

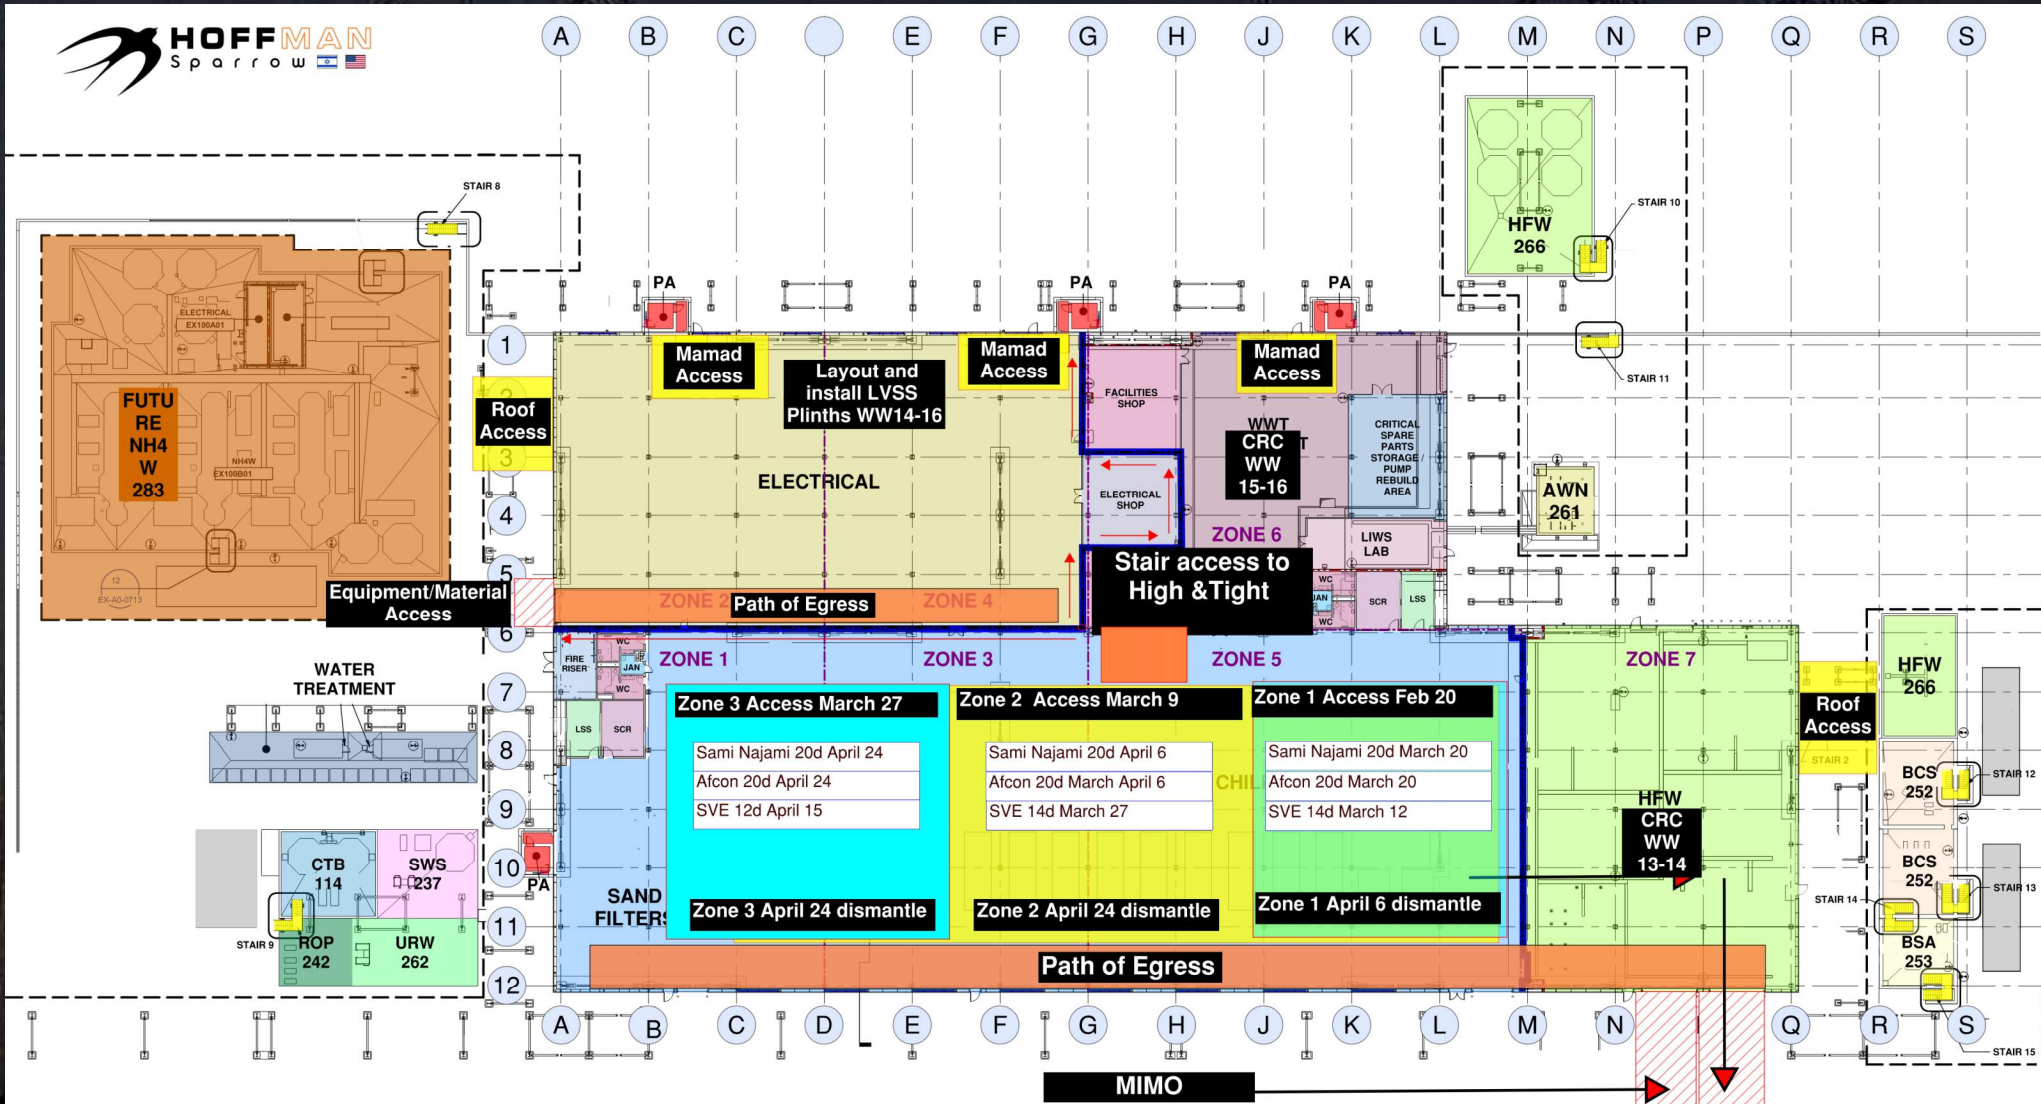



CUB 2 – EXTERIOR/ROOF

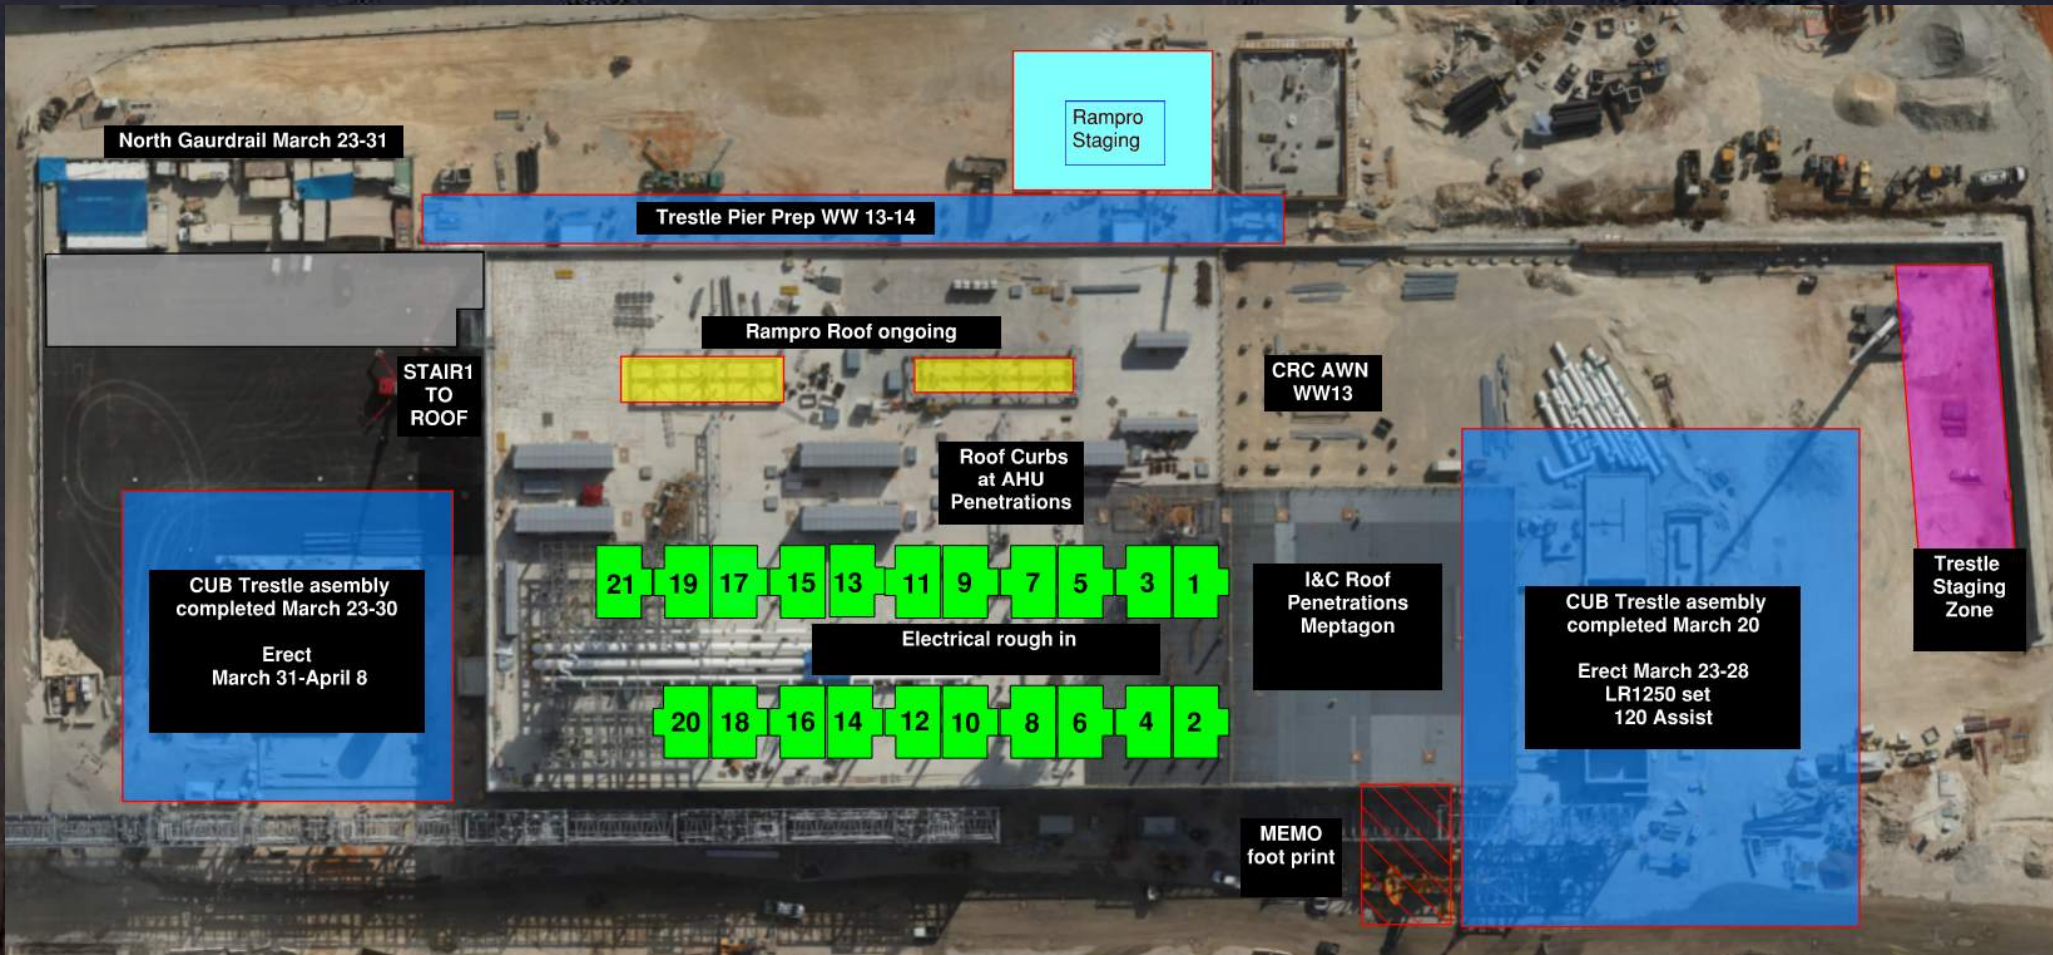



HOFFMAN CONSTRUCTION COMPANY

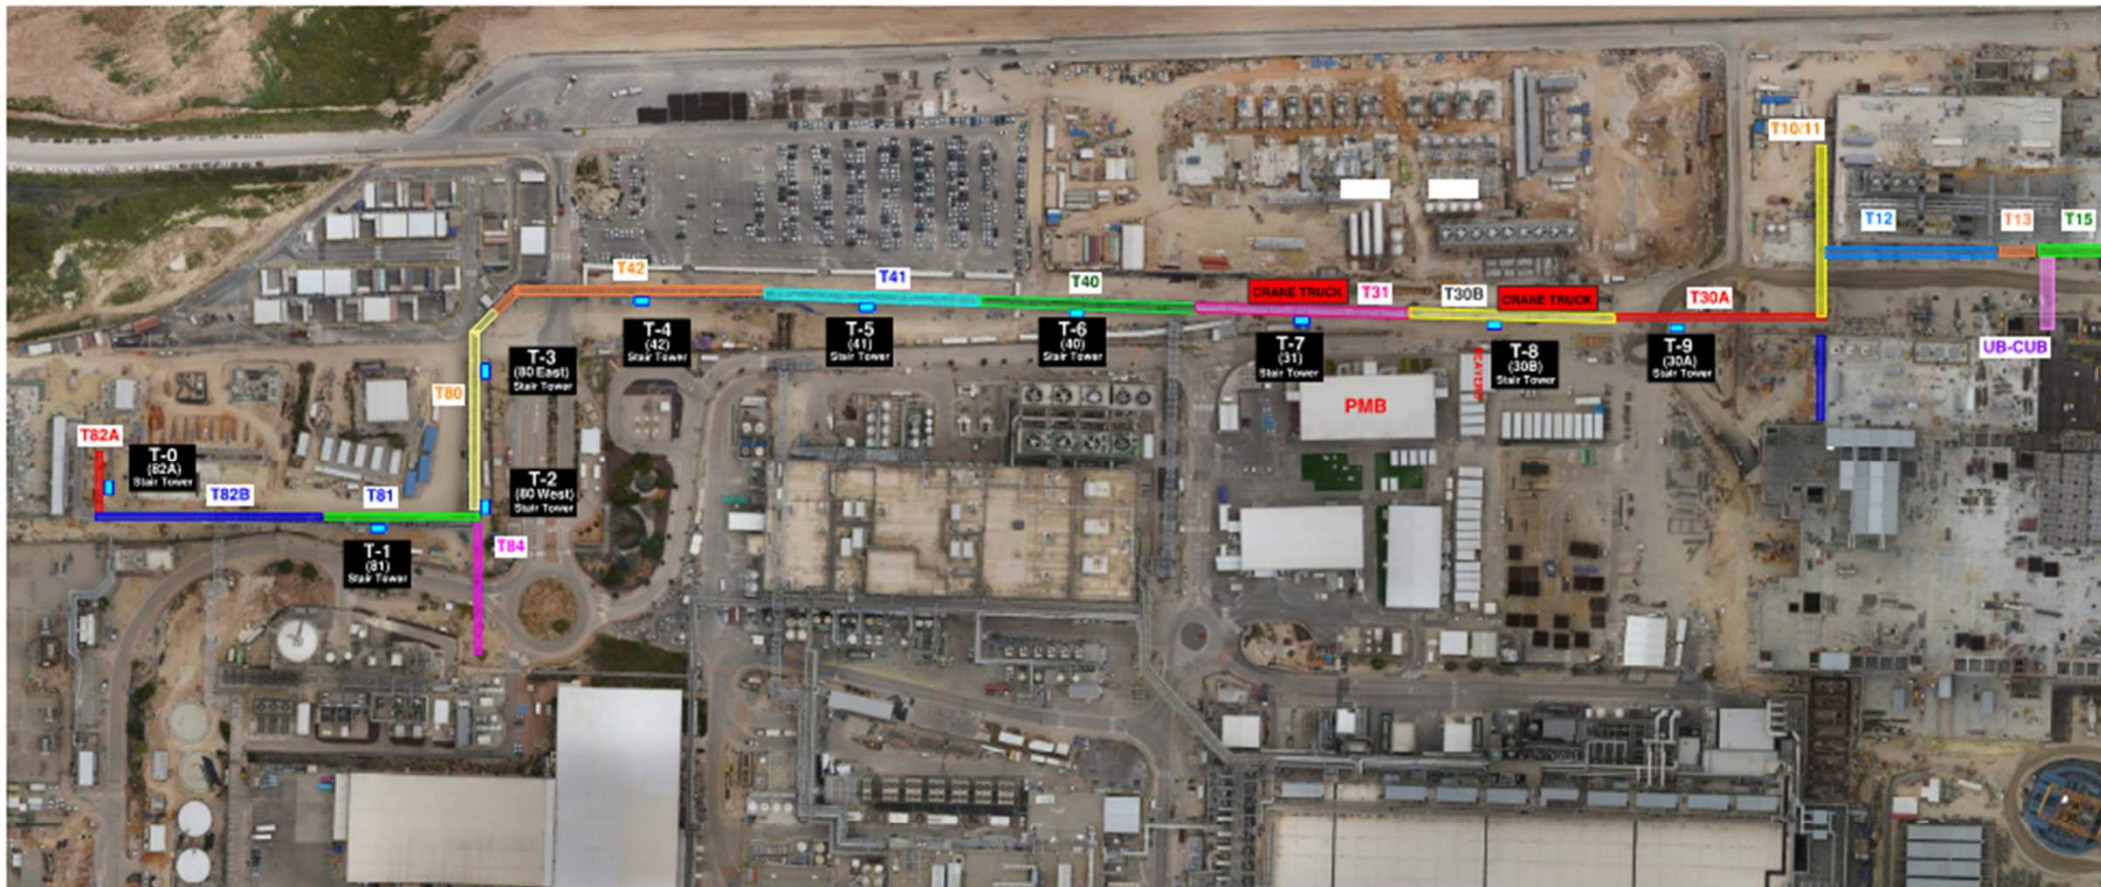

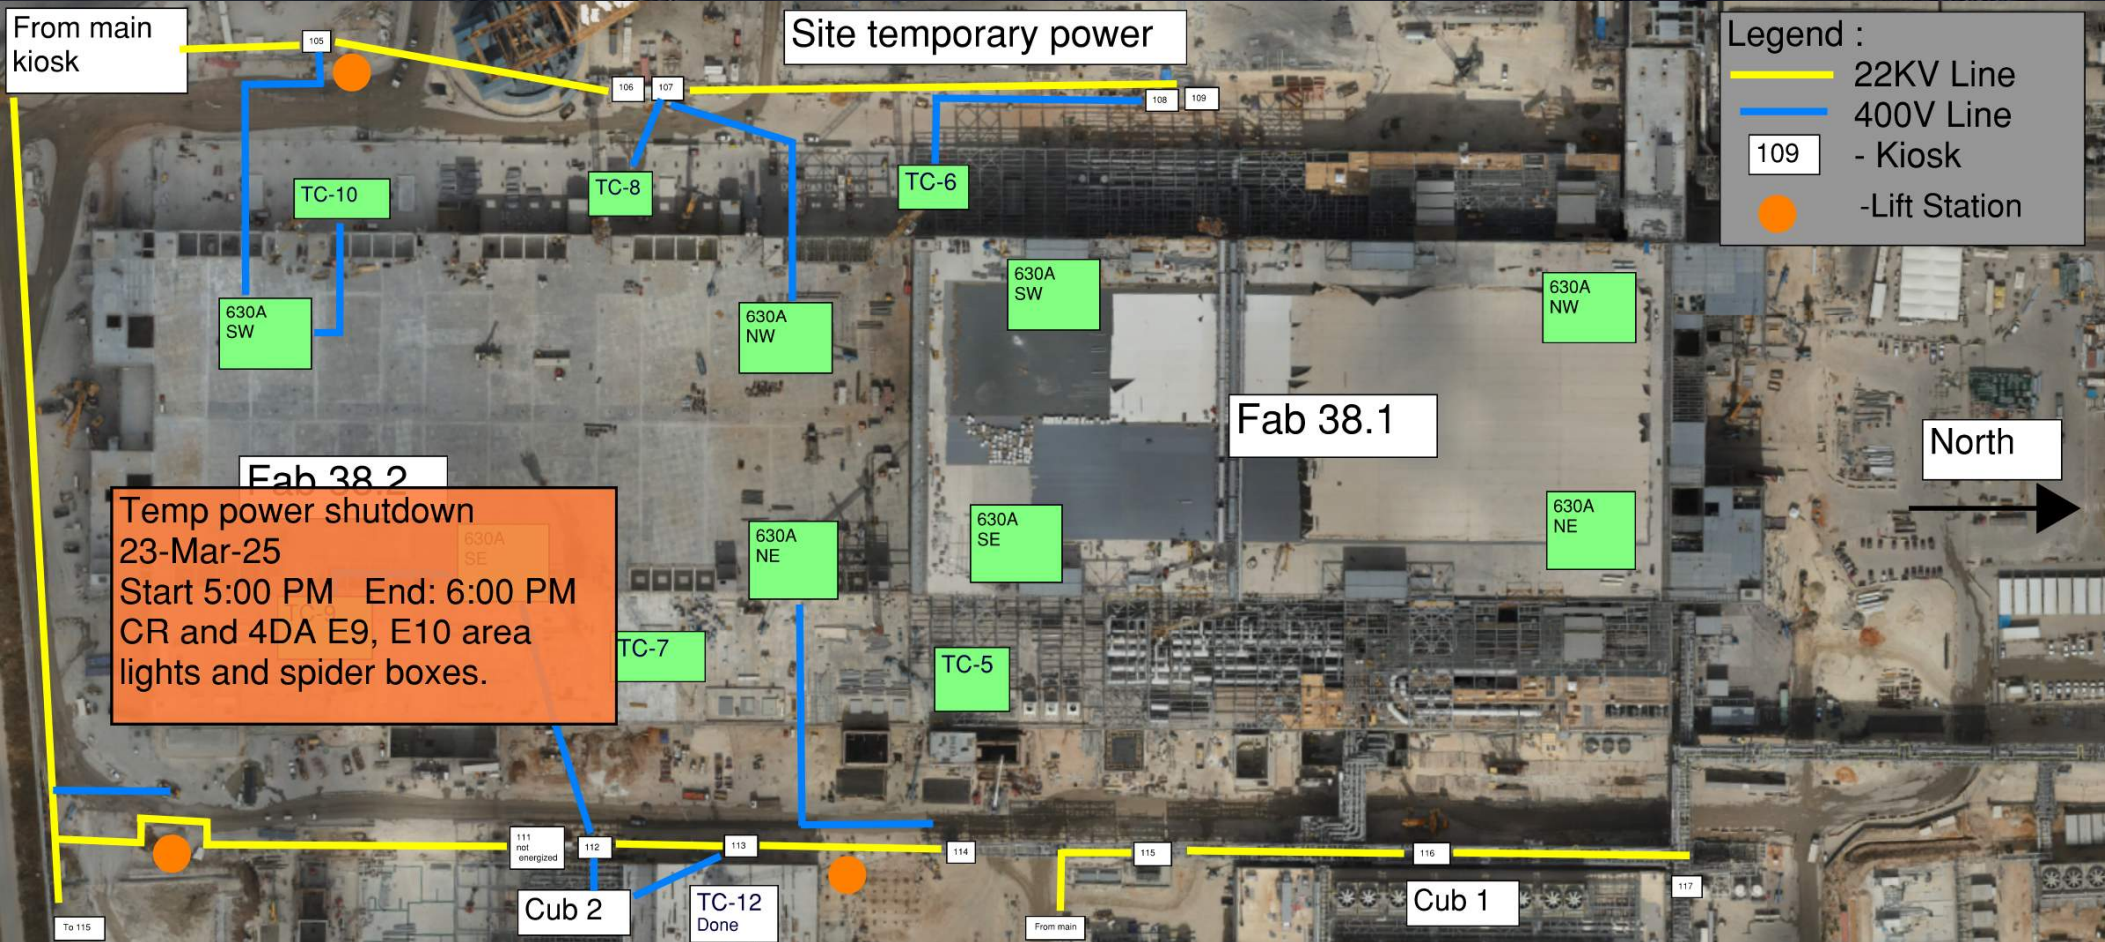




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North

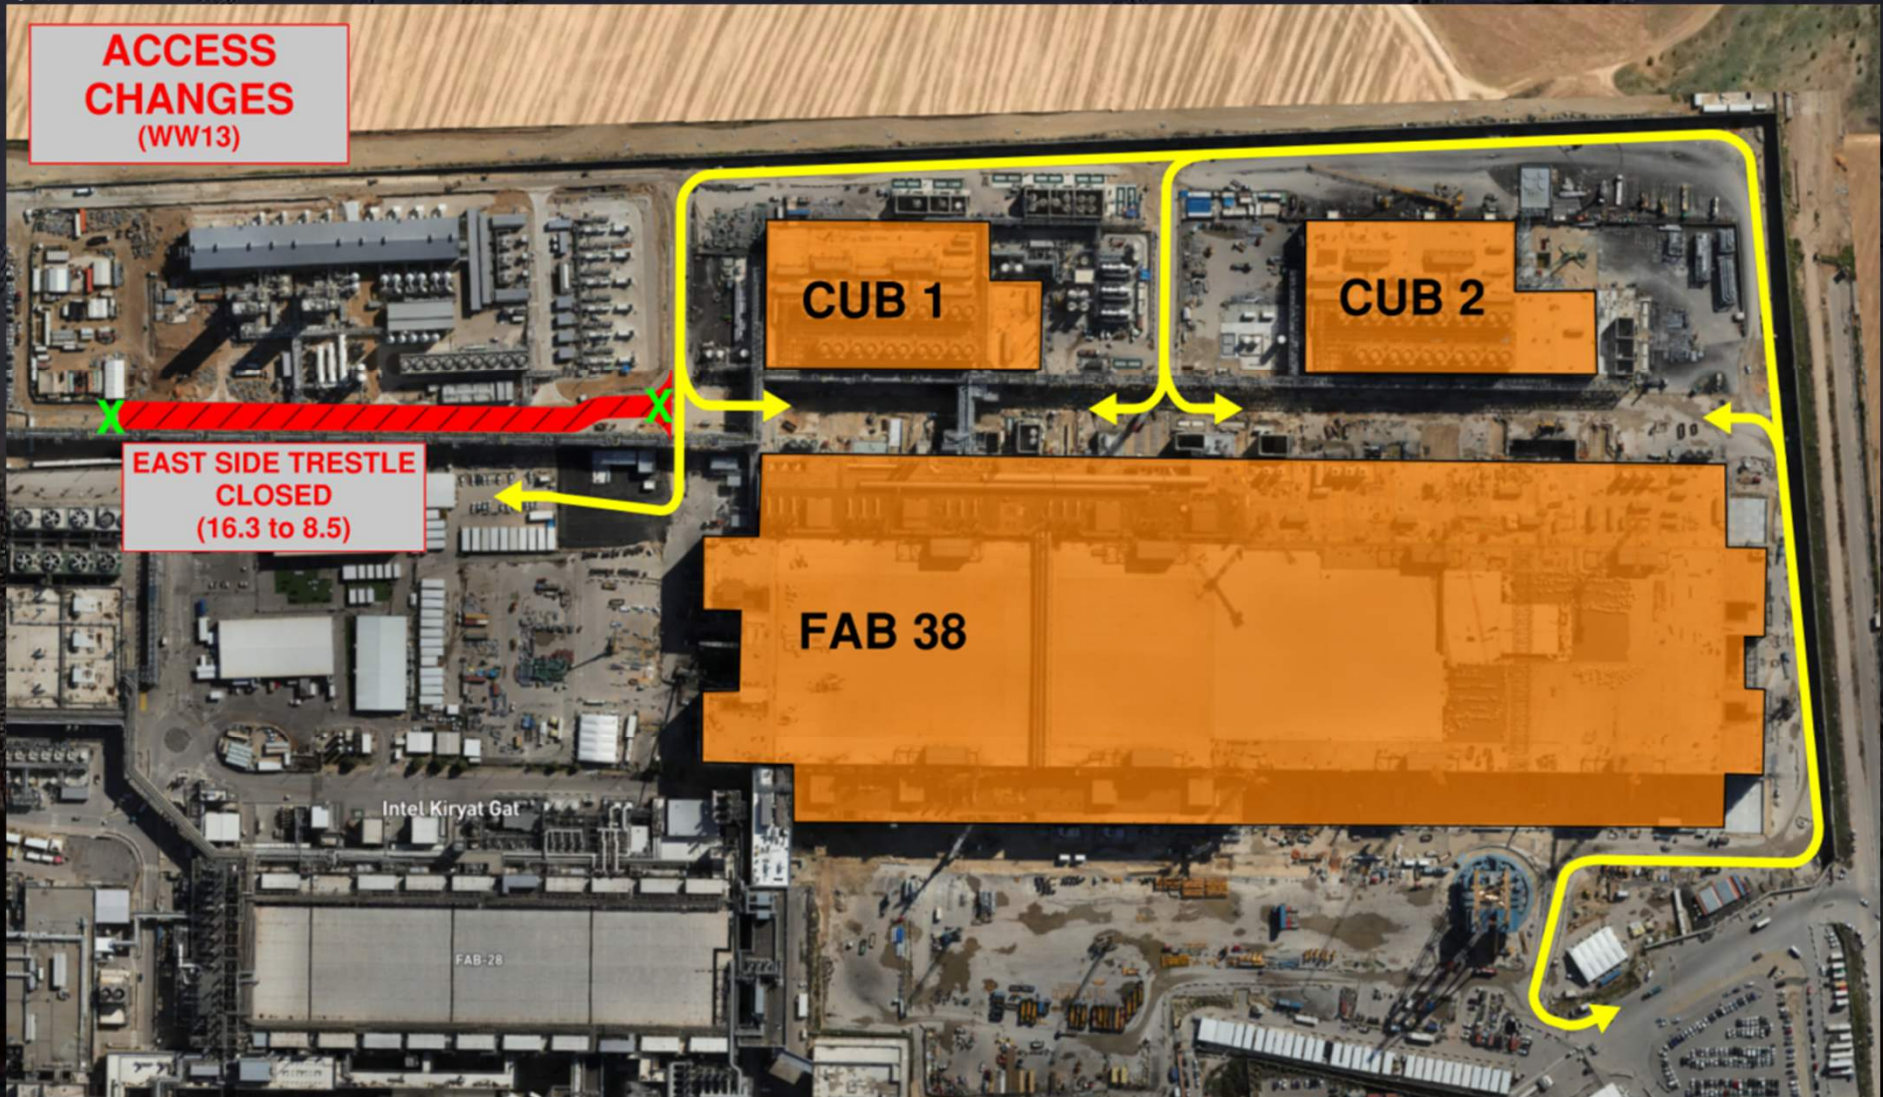



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

MAMAD Locations

MAMAD LOCATIONS (19-March-2025)

■ LARGE
■ SMALL
■ BUILDING



The use of a 9-inch grinder is prohibited on site starting today

- After two serious injuries occurred on our project involving this type of grinder, the use of this specific tool is now prohibited at the Hoffman site.
- We understand this may come as a surprise to everyone.
- If there are specific cases where you claim that only a 9-inch grinder can be used, you must submit a detailed reason for this, and the matter will be reviewed and addressed accordingly.

HCC/EHS Weekend Work- 21.03.2025

White Board Meeting in Beavers at 06:30

Superintendents

Brian-Grevious - 052-5394339
David Kanzevich - 052-2045446
Igor Shuster - 054-4743767
John McCrudden - 052-3756957
Michael-Ohehir - 052-4168879

CSA CM

Charles-Aitken - 052-6041443
Brandon-Britton - 052-6042828
Boris-Gruman - 054-7886568
Kenneth McGuirk - 052-5415017
Andy bJollands - 052-9659290

Crane

Craig Mowry - 052-300-2769
Yossi Atias - 052-3060790

Cx

John-Renwick - 052-3820589
Hadar-Swissa - 052-3467273

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Officer - Arkady Gerber-050-6851432 Arkady-Garber@Hoffmancorp.com

Subcontractor Weekend Work- 21.03.2025

FAB

Utility level/ SUT

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- **Megason**
 - LSS Rooms, 10E Vesda
 - Israel: 0526869393
- **Afcon E**
 - All Over SF
 - Avi Eli: 0526008487
- **Lesico**
 - 3W,3E PT
 - Gabriel 0549892929
- **Talad**
 - 1W
 - Ezat: 0543098001

Clean Room

- **Talad** – 30 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Maty 0504887477, Super Igor 0544509386)
- **Chemo** – 45 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2 guys (Liran 0532323696, Eden 0585335445)
- **Sig** – 16 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- **Rolling Plains** – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Oleg 0542689370, EHS Ovidiu 0546993648)
- **Tavas** – 18 guys , 12 cleanroom maintenance, 6 at interstitial (Super Inas 0537148630, EHS Vadia 0528412021)
- **W&W** 20 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- **Tapertech** – 13 guys CAF installation 1E/1W (EHS Amit 0549249356 Supervisor Igor 0547953798)
- **Tavas** – Cleanroom clean Maintenance 1-2E/1-2W (Supervisor Ilan 0522758886, EHS Stas)

Subcontractor Weekend Work- 21.03.2025

PSSS

- **Afcon Electrical** – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- **Chemo A.** – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- **Combe Waste** – 2P Waste Piping at GL4/Lift 2 Waste Piping
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Lesico** – Low Point Drains on PSSS Roof/OFA in Solvents
 - Foreman – Suju Pally – 052-7755967
 - Safety – Tal Madar – 052-8229109
- **SK Engineering** – Lift 2 MAH 4P/DW Punchlist
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **W&W** – Grating Cutting Lift 3 1P
 - Foreman –
 - Safety –

WJG

Chemo:

Safety: Erez Megidish - 0549716840

Foreman: Maor - 0509889071

Afcon:

Safety: Steven Shartho – 0559129333

Foreman: Mantu Singh – 0559116973

Lesico:

Safety: Michael Gisri – 0526060223

Foreman: Rajesh Francis – 0549375380

SK:

Safety: Marzouk Amor – 0548830263

Foreman: Marcelo – 0542072784

SN:

Safety: Wisam - 0509828381

Foreman: Sorov – 0552837973

Subcontractor Weekend Work- 21.03.2025

CUB

Chemo Aharon:

Dudu - 0509808846

Leonid - 054-8883878

Carmel Bidud:

Fahri - 0526105266

Moyat - 0524335060

Trestle

Site

- **Derech Afar** – Shotcrete wall
 - Supervision = Raed: 054-244203
 - EHS = Alex: 054-5403849
- **Olizki** – Offload 10, Link and East BGC road
 - Supervision = Or: 052-4917313
 - EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
