

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:

- * 27 Dec site closure
- * GIS gate closes 29 Dec

UTILITY LEVEL MOD1

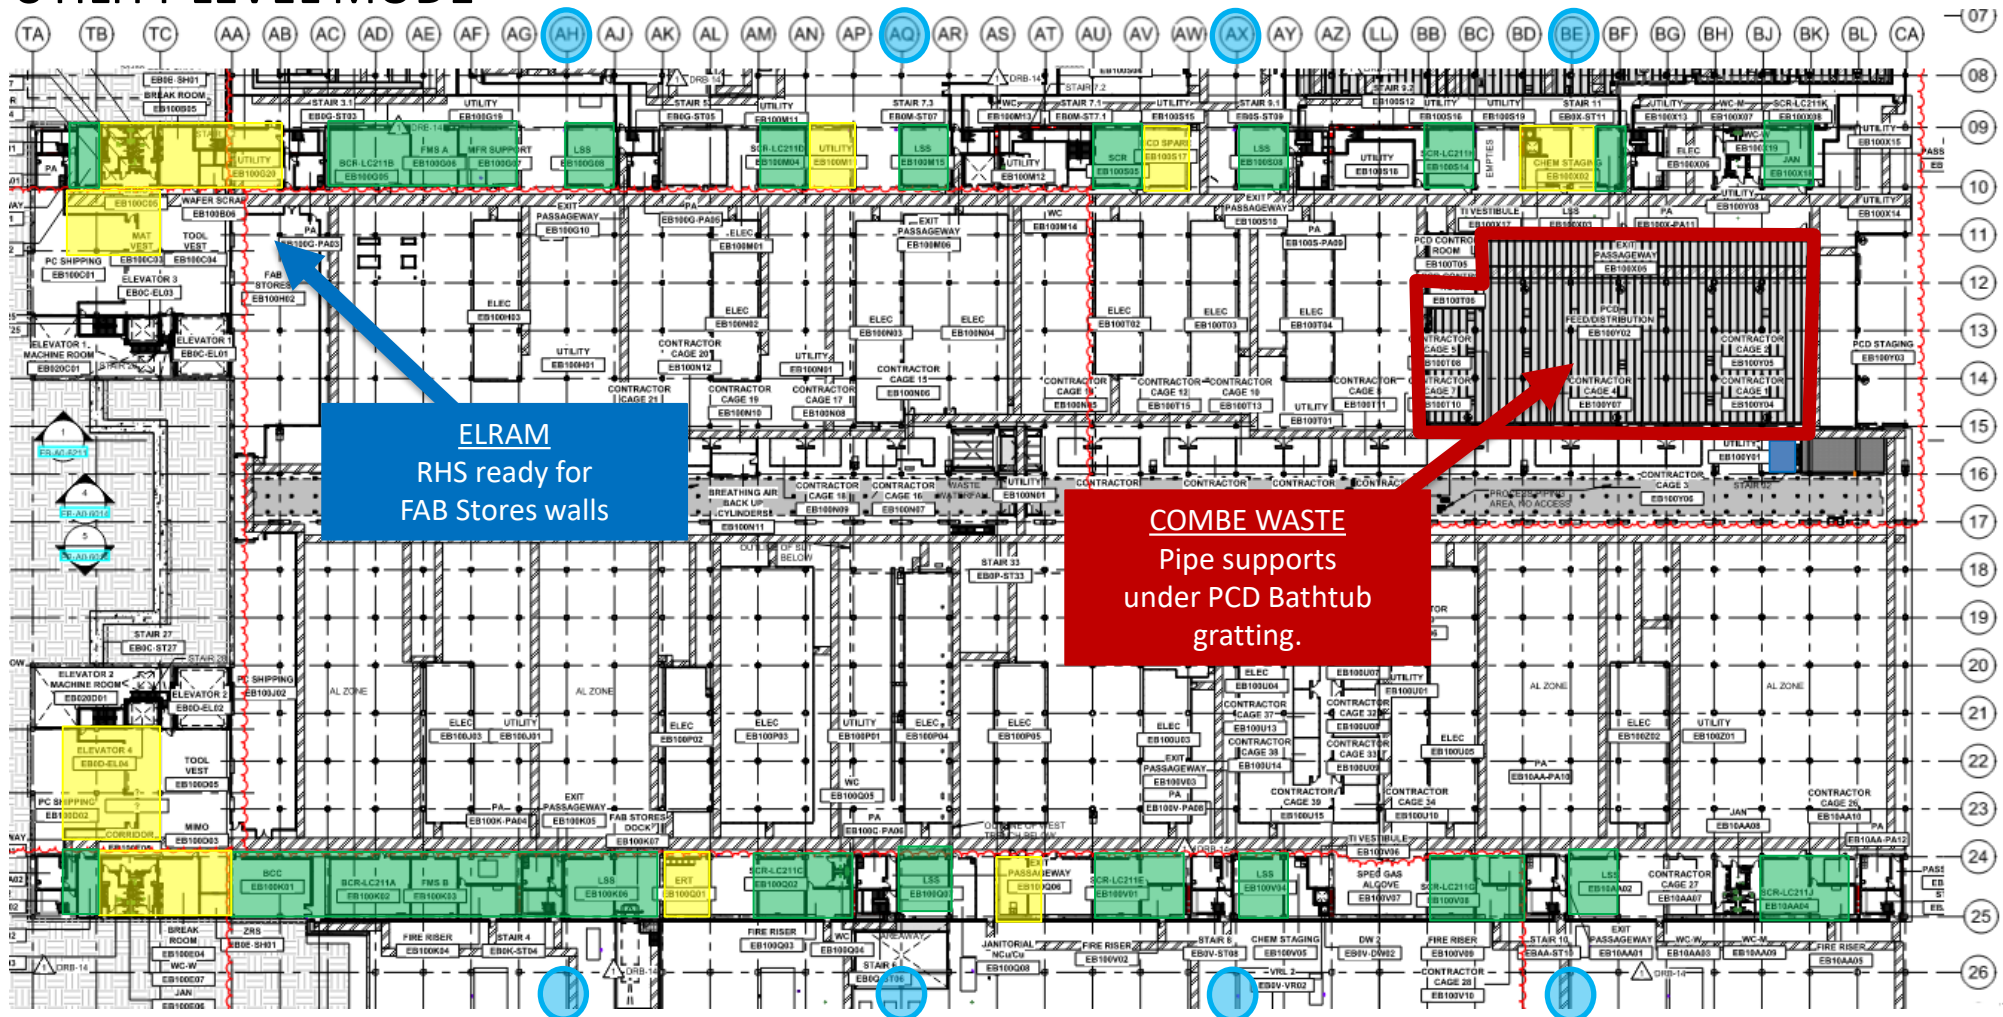


ELRAM
Drywall install

MEP+Electrical
Ready for re-install

[illegible]


MALHIMIM
8W & 9W
Ongoing

SUT 38.1 LEVEL

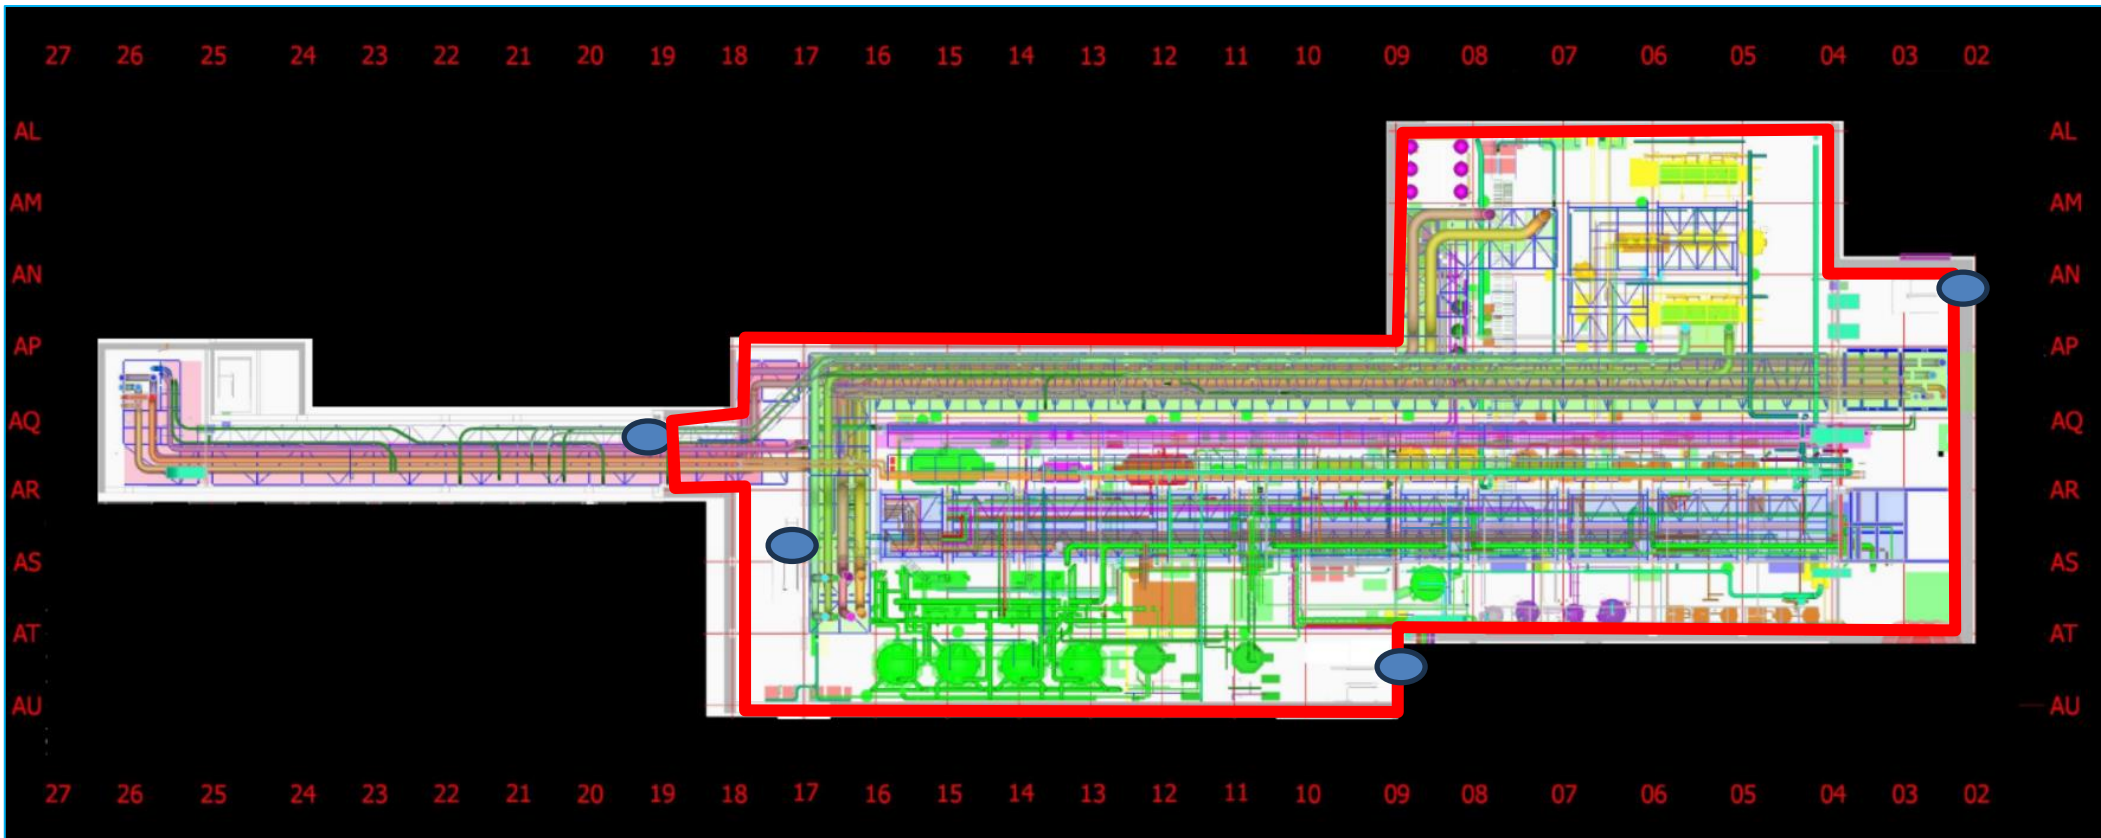

SKE City water line **internal** Pneumatic
pressure test
138PSI
24/Dec 18:00-23:00 Tuesday


SUT 38.1 LEVEL

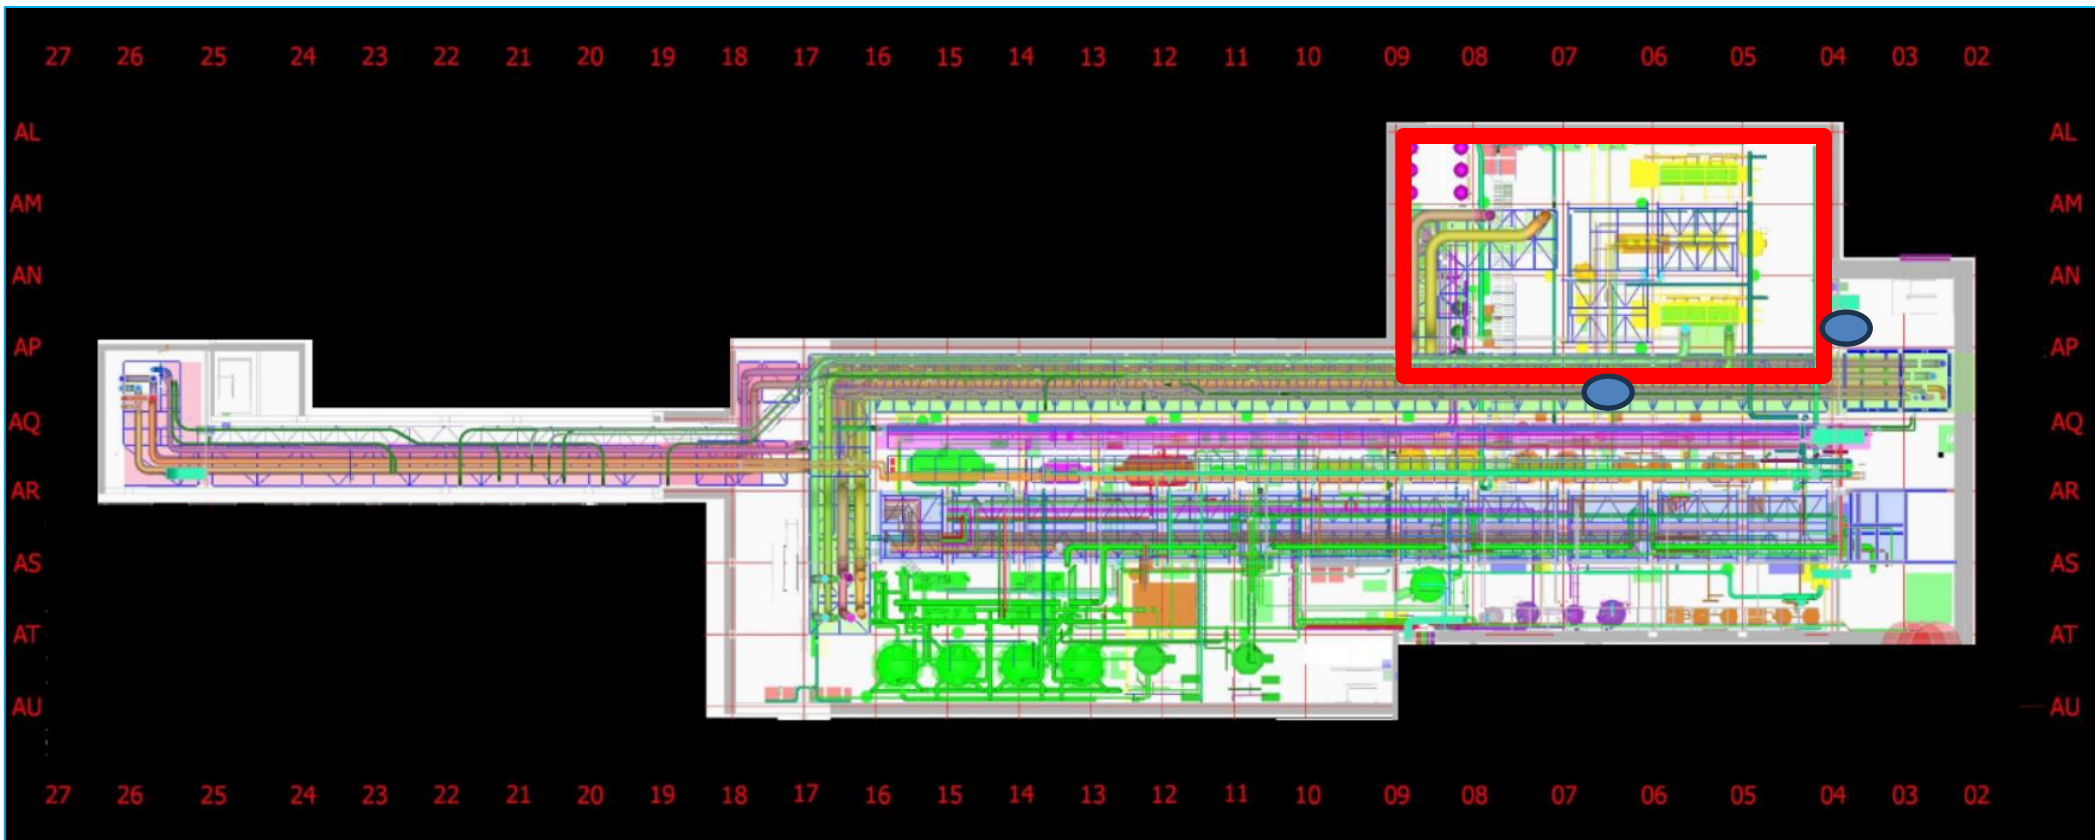

SKE IA/PA **official** Pneumatic pressure
test
140PSI
23/Dec 18:00-23:00 Monday



SUT 38.1 LEVEL

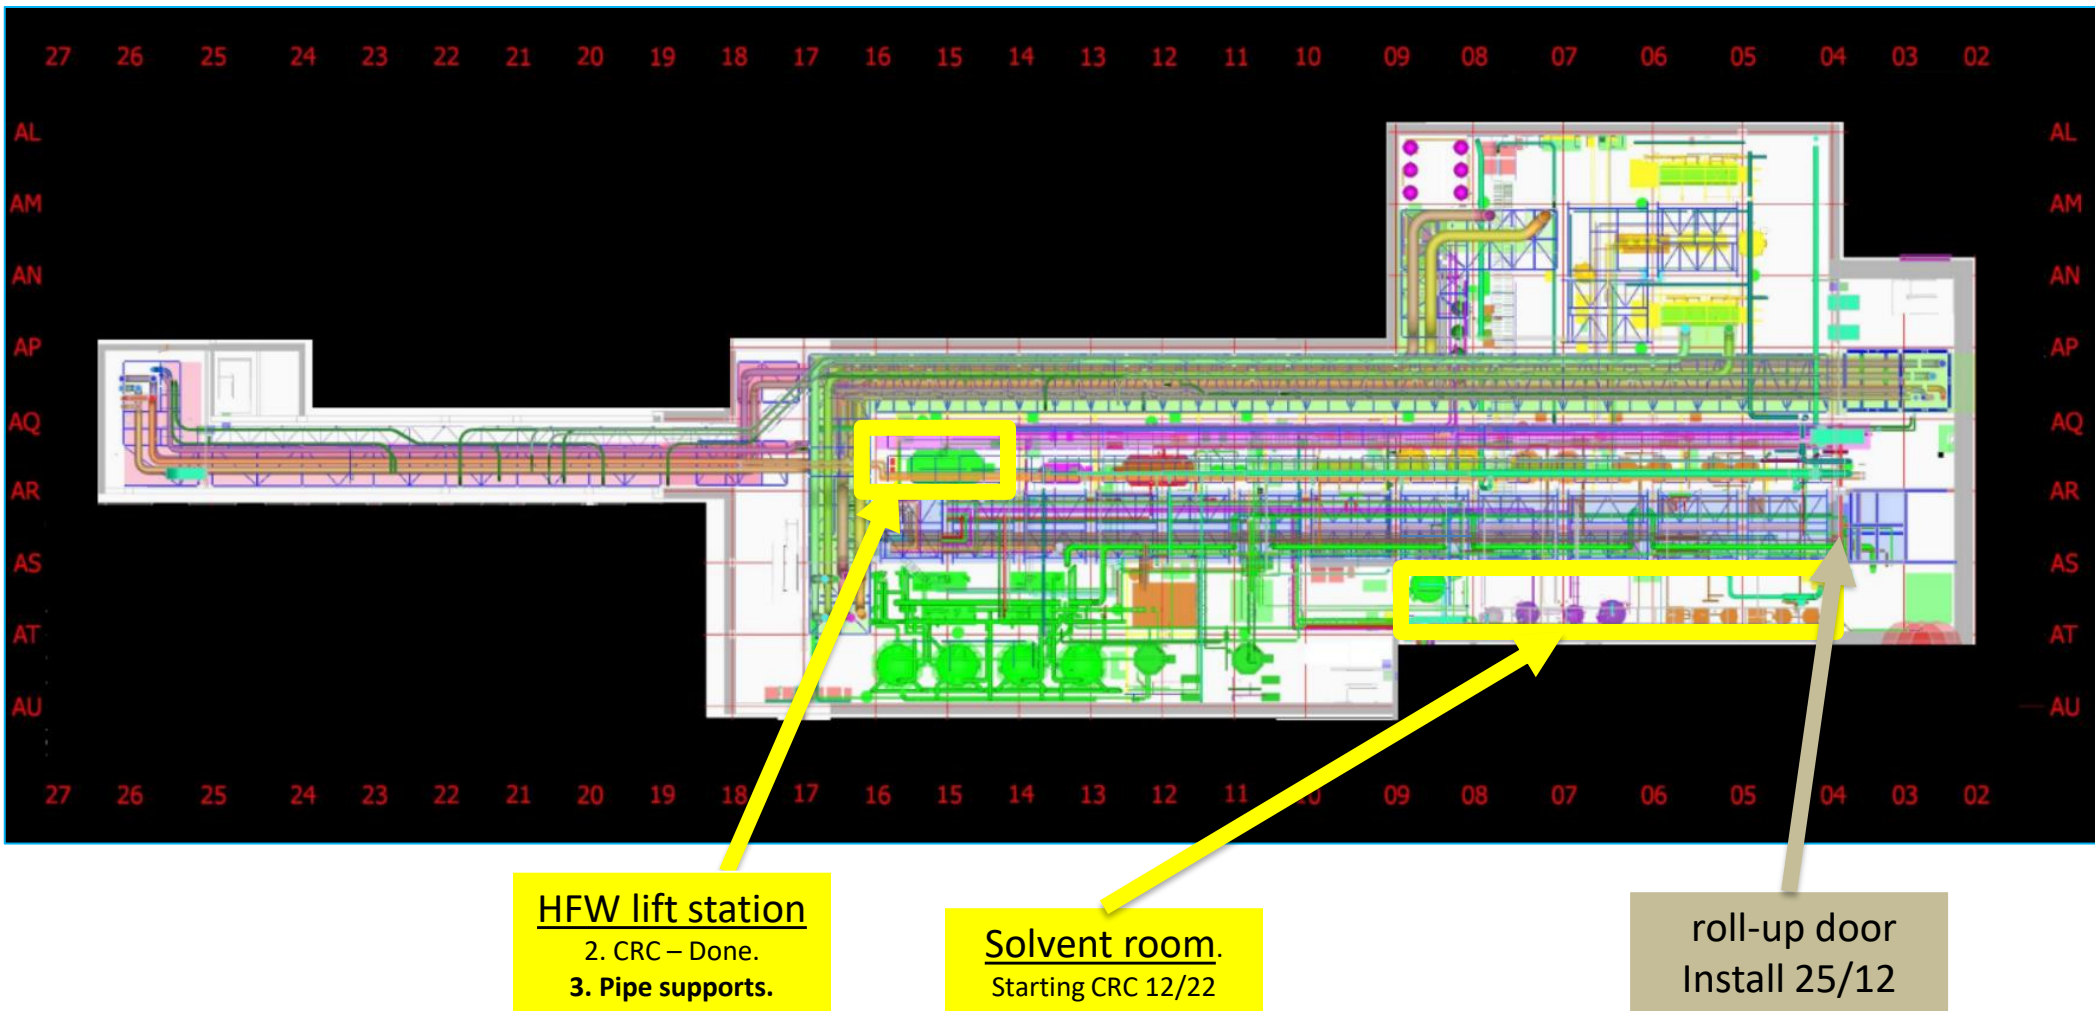


SUT 38.2 LEVEL

Rack 4b

Lifting
schedule

#5 – 26/12

#6 – 30/12

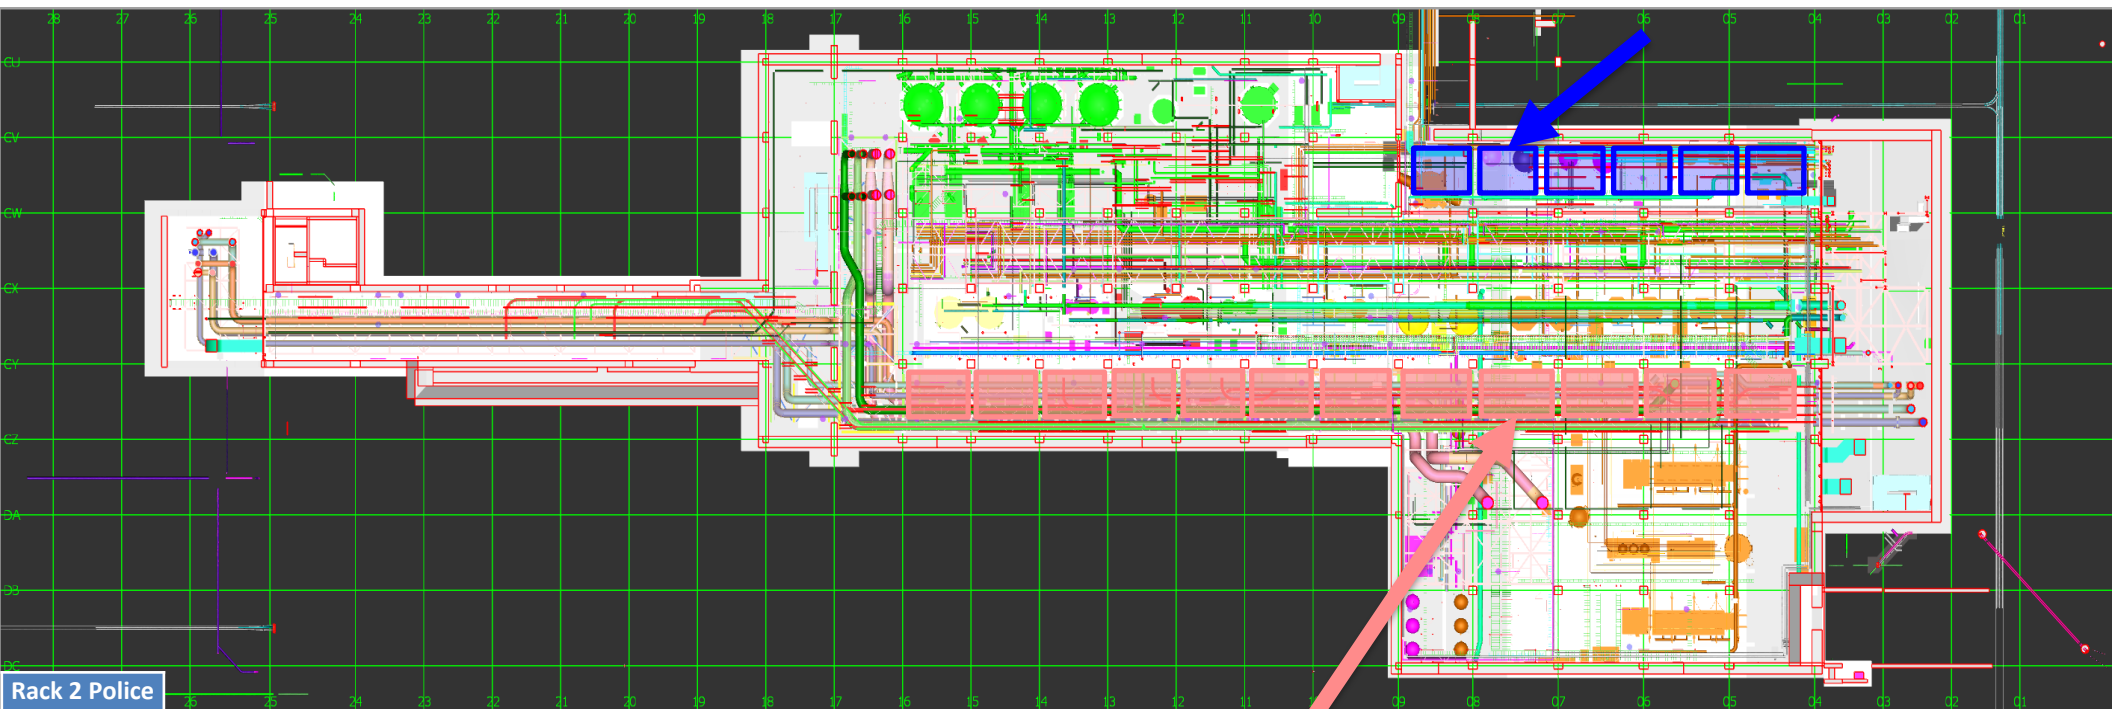


**Rack 2 Police
escort dates**


v24.11.24
v25.11.24
v3.12.24
v9.12.24
v12.12.24
v15.12.24
v17.12.24
v22.12.24
5.1.25
14.1.25
2.2.25
9.2.25

Rack 2
MIMO -
Module #9
5th of Jan


SUT 38.2 SKE
pressure test
17:30-20:00
CRW
100PSI 6-4inch
pipe

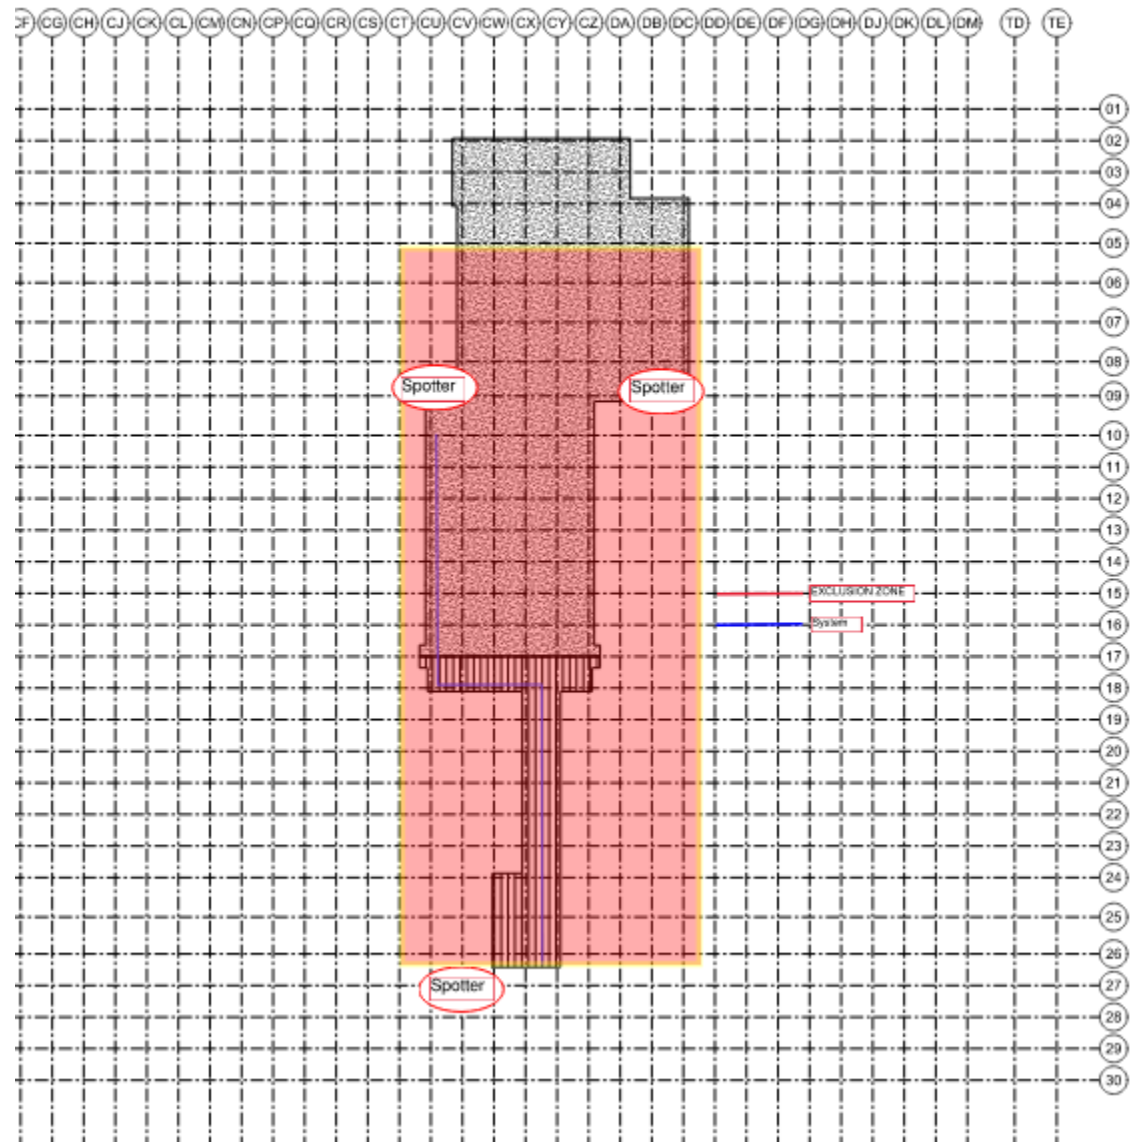


SUBFAB BUILDOUT MOD 1

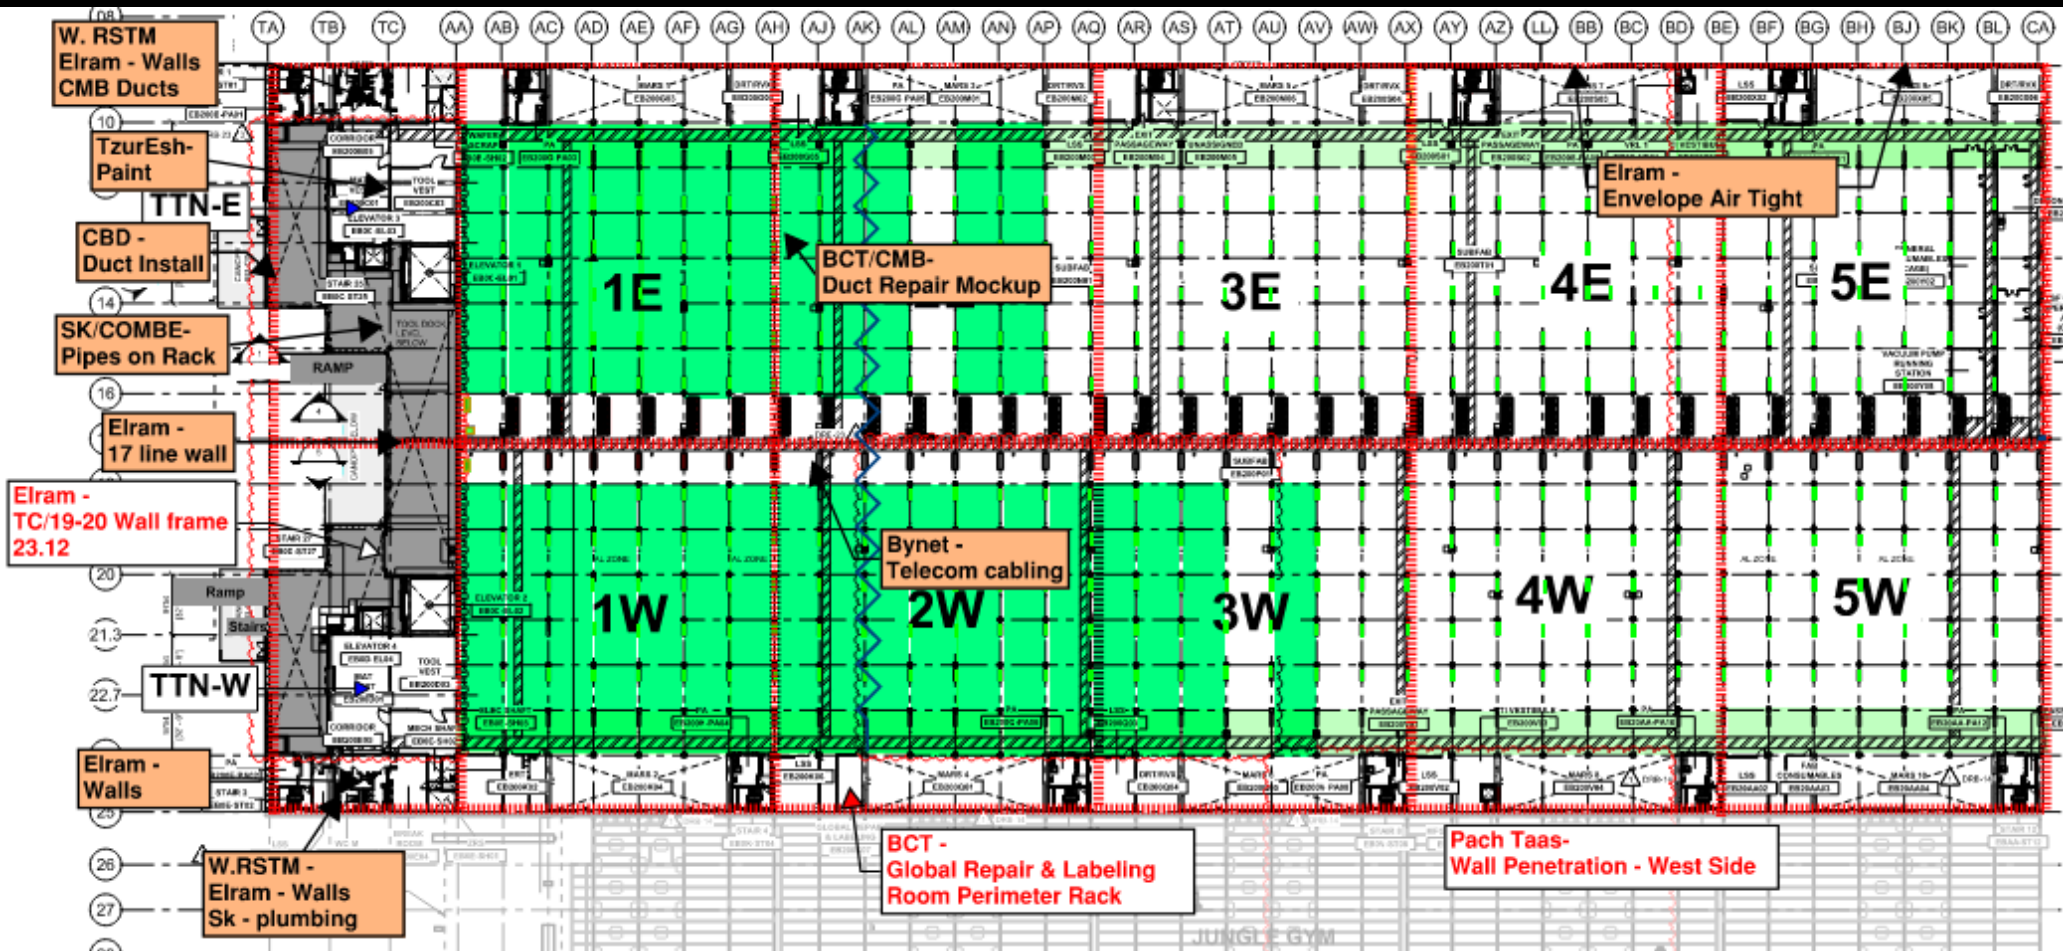


SUBFAB CRC TOPCOAT

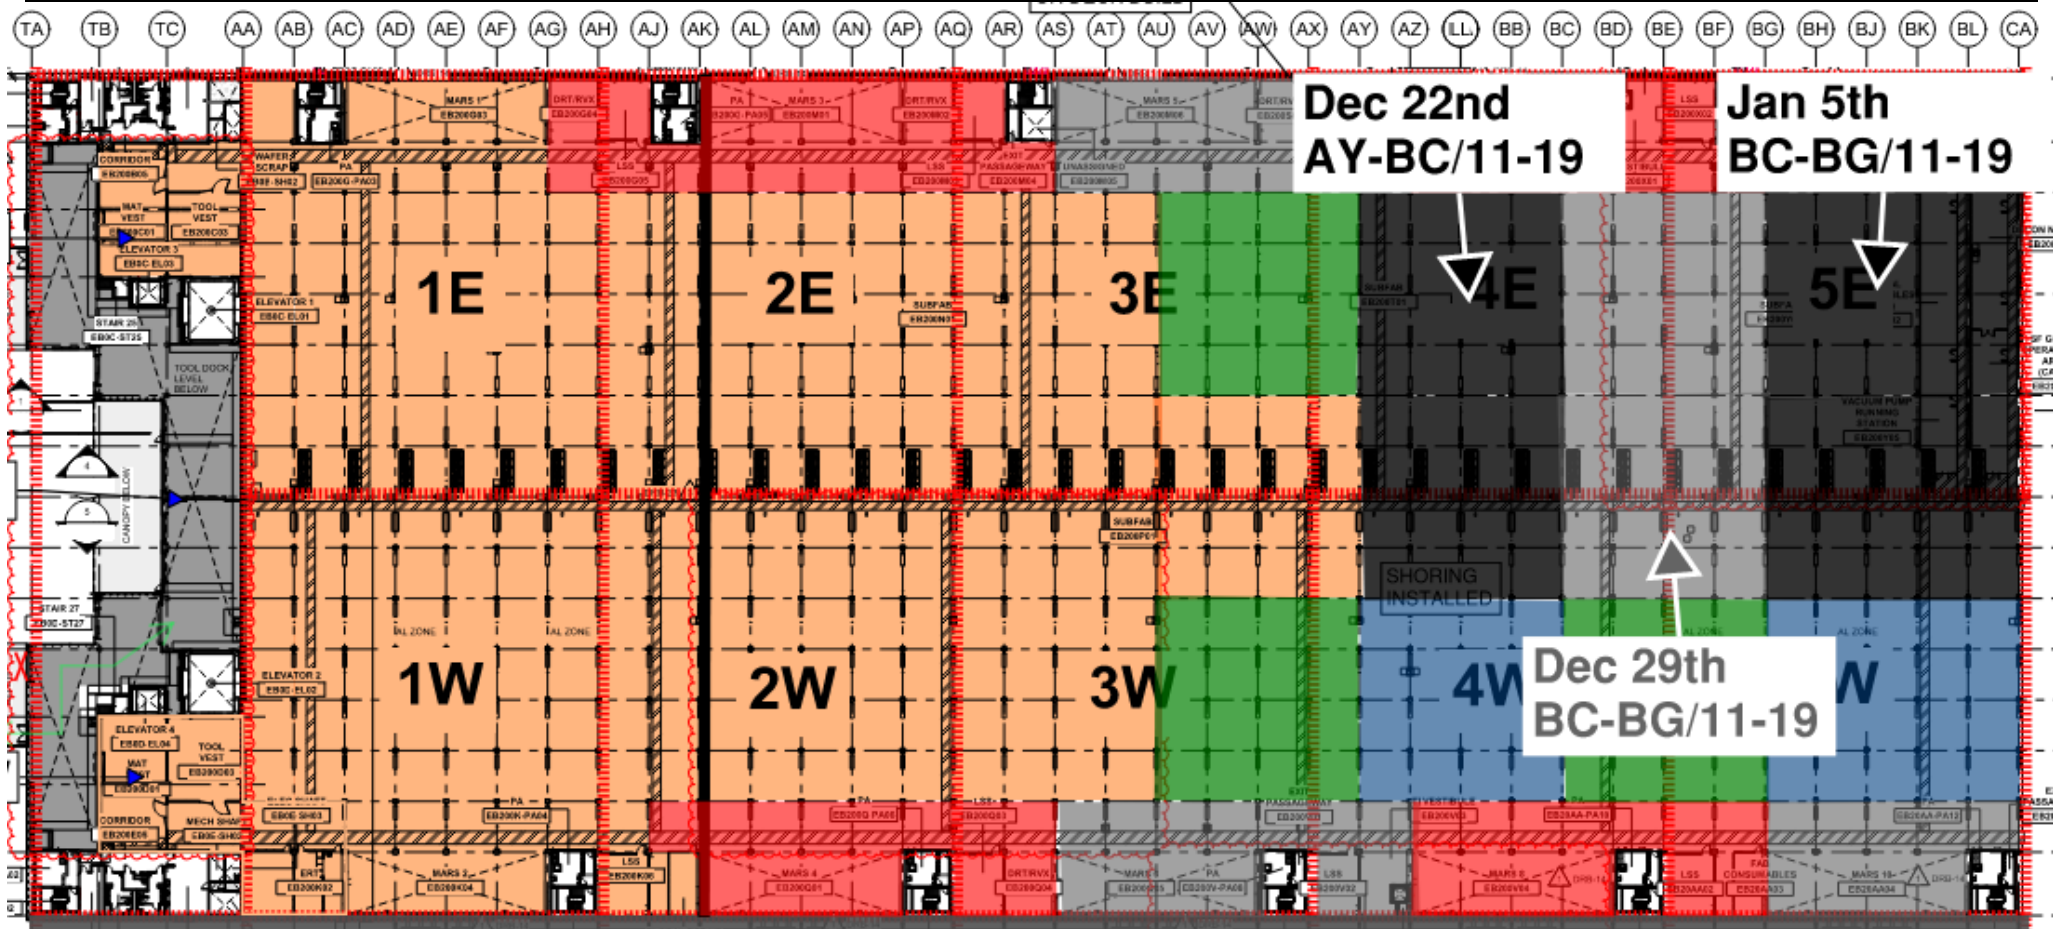


BCT Pressure Test Today

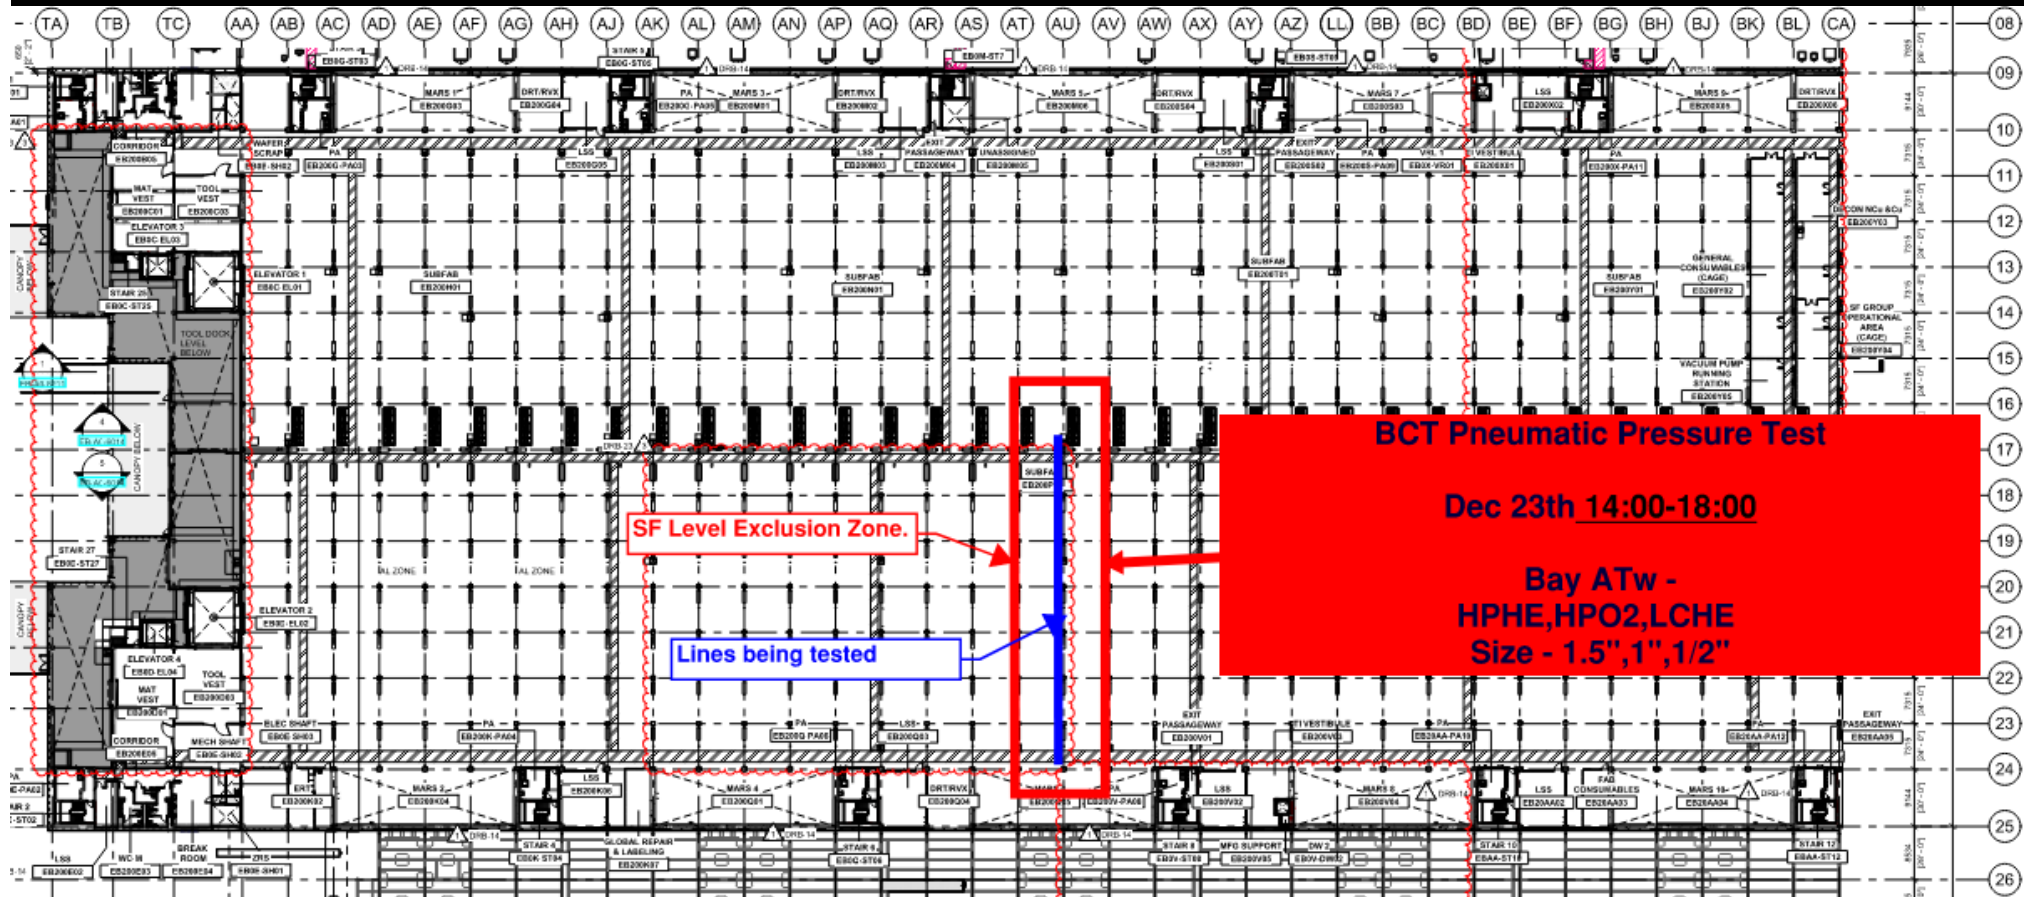



BCT Pressure Test Tomorrow

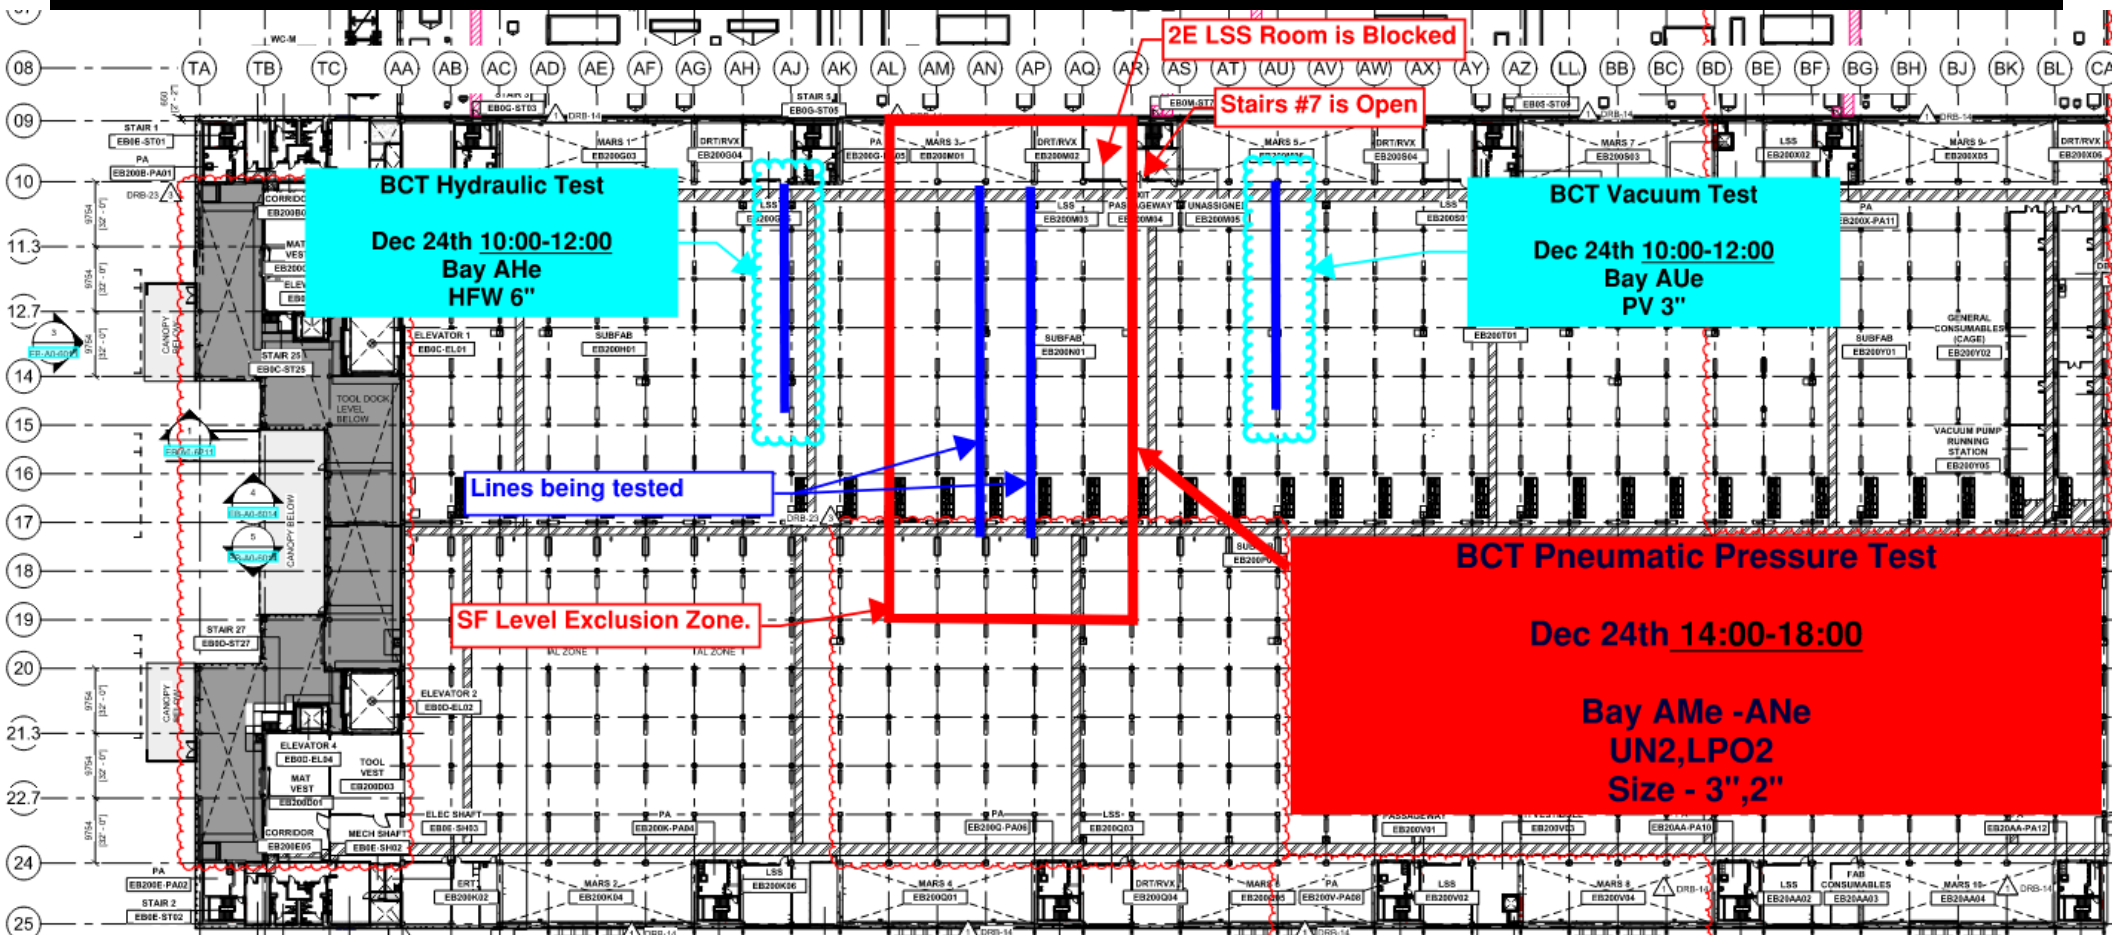



SUBFAB BUILDOUT MOD 2

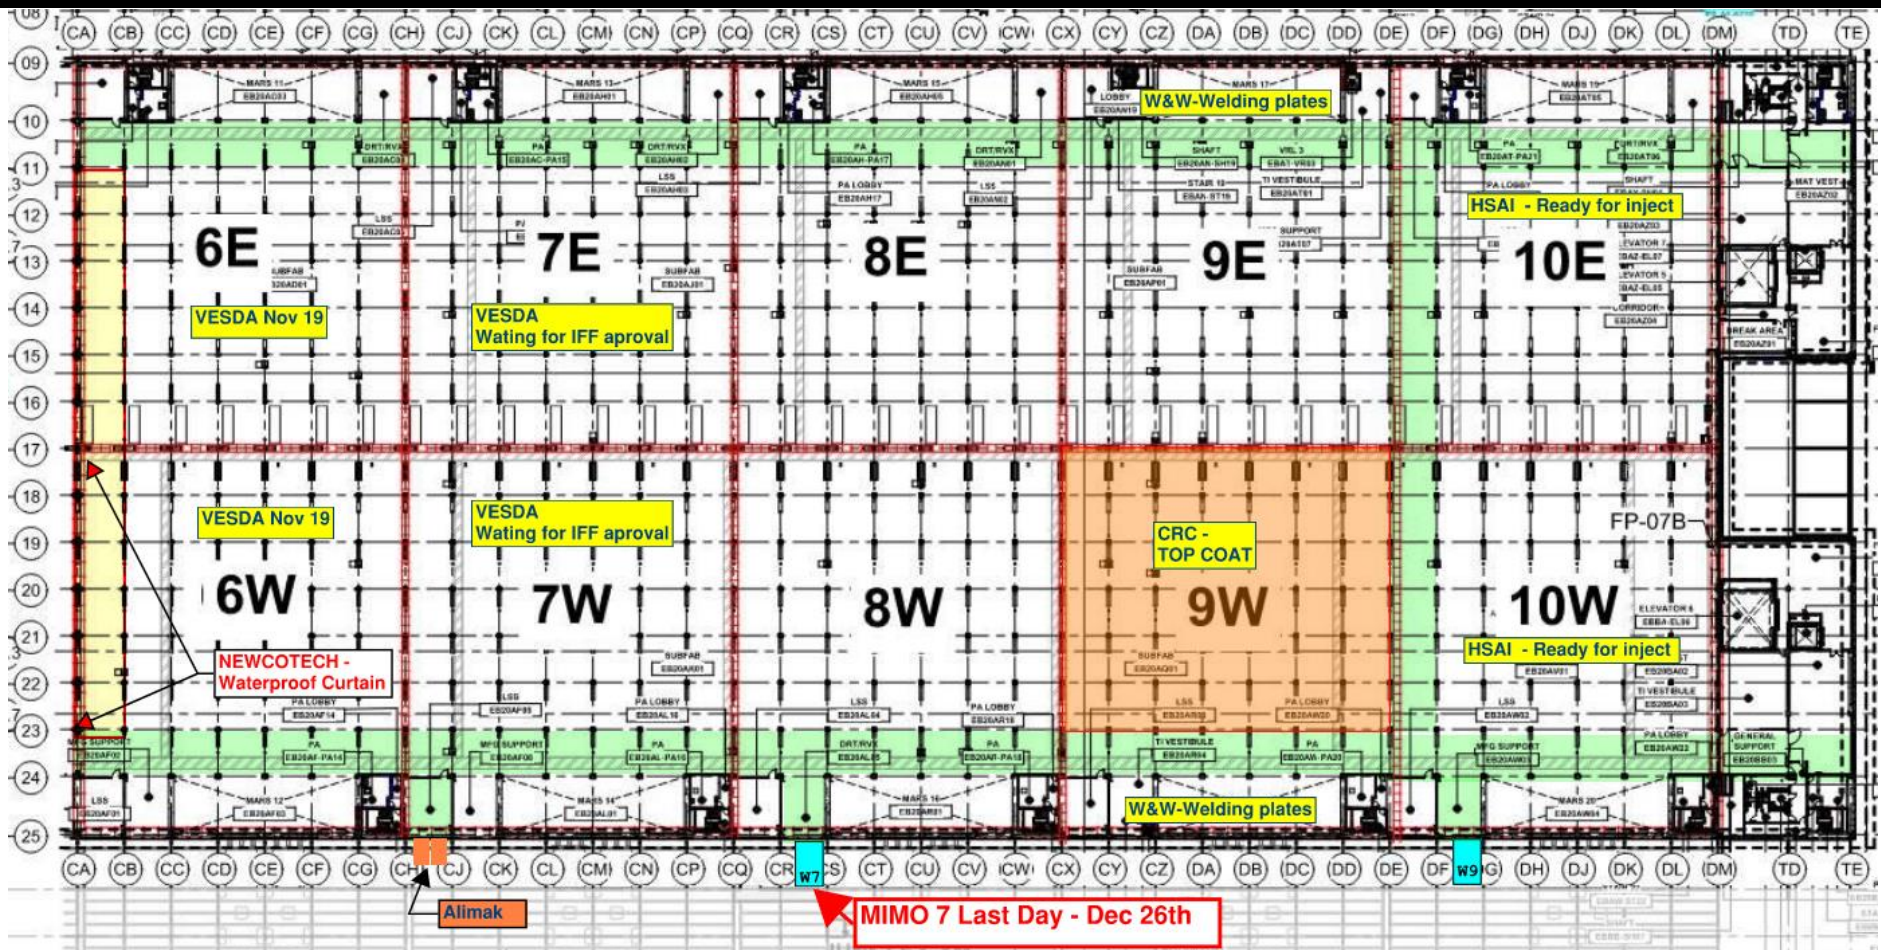

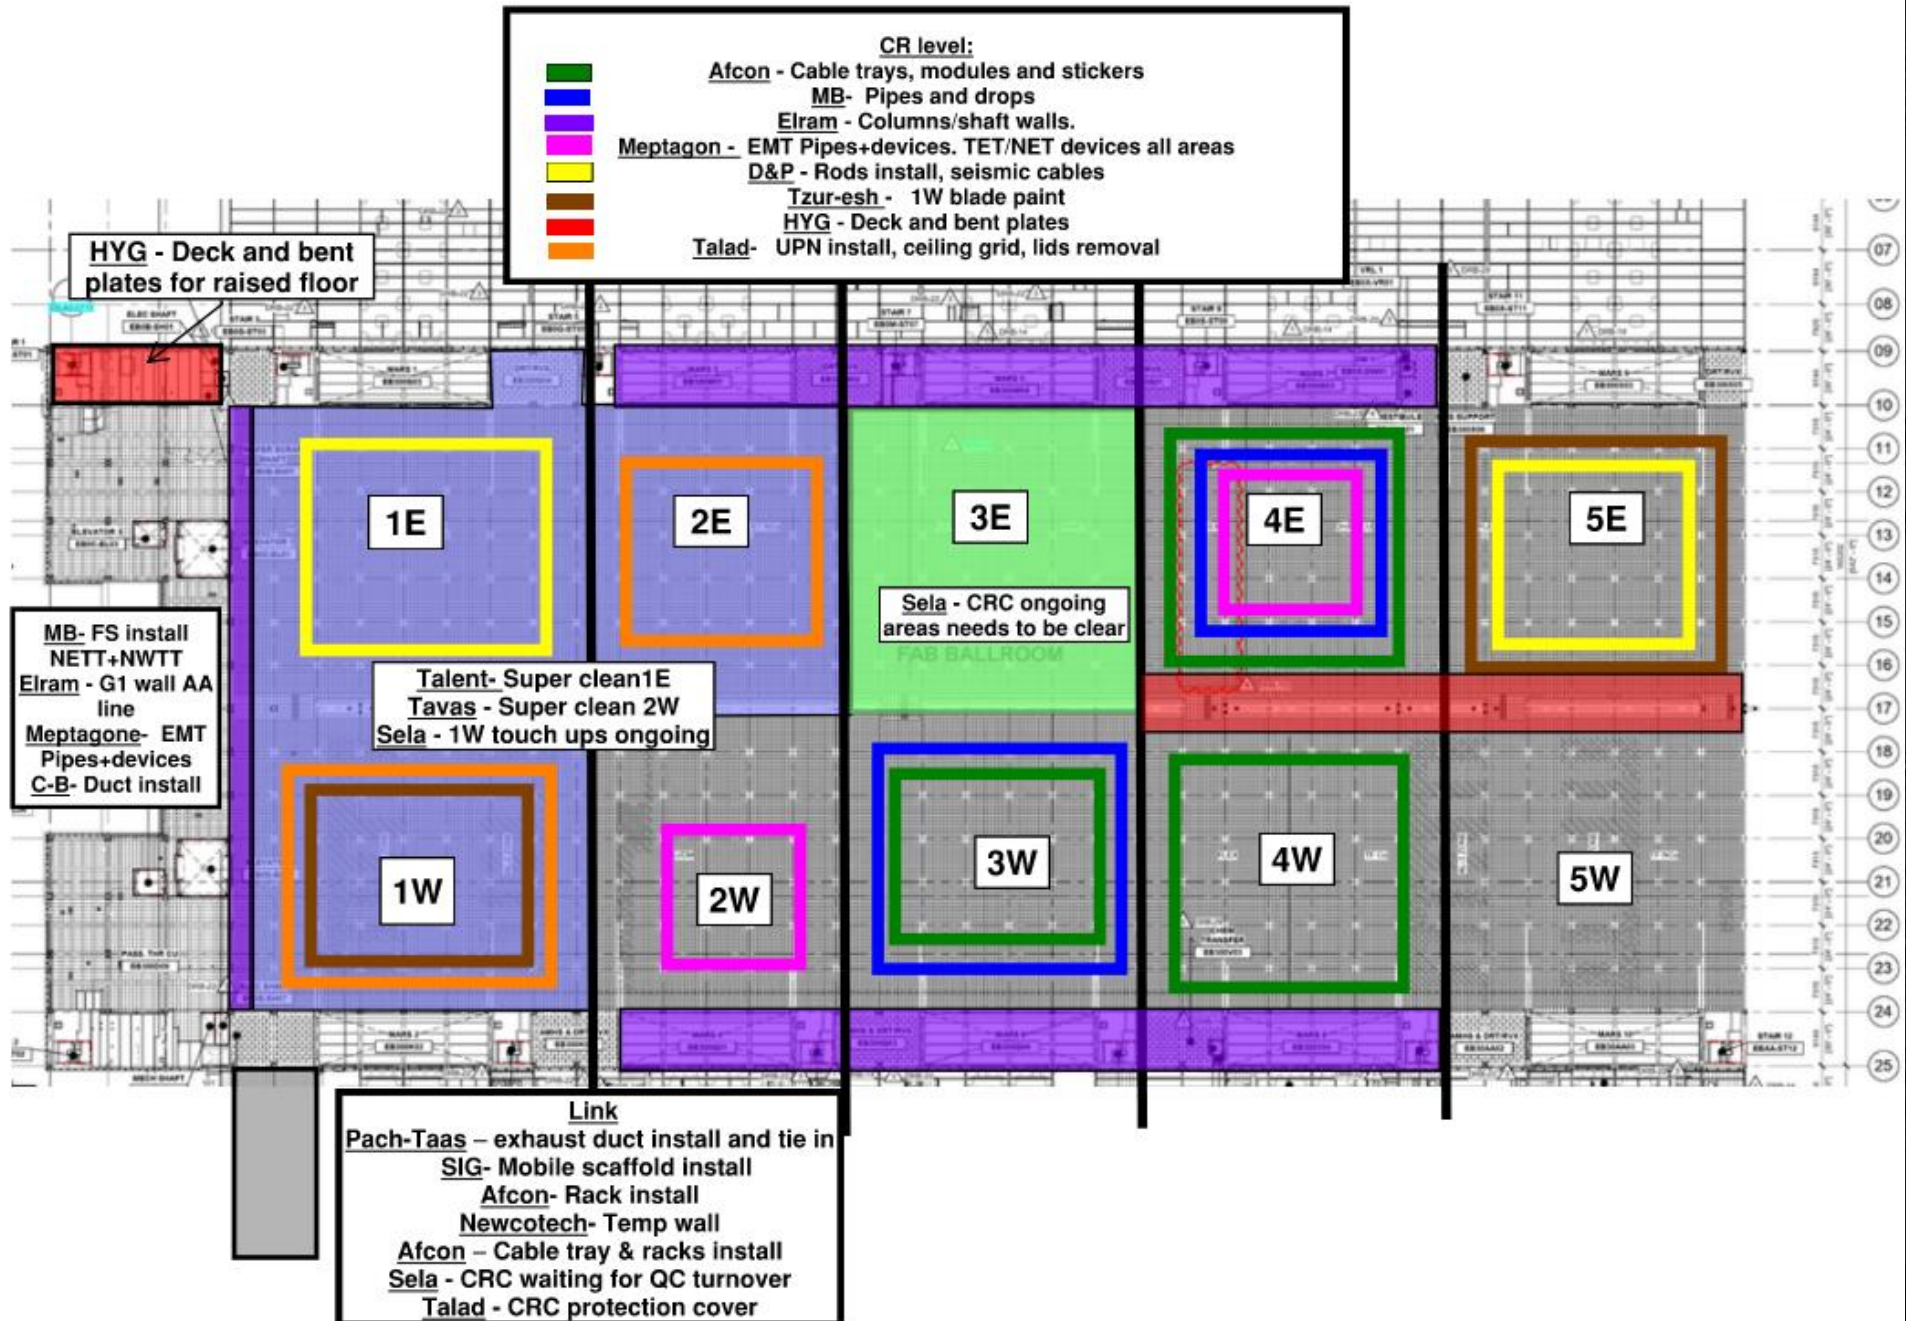

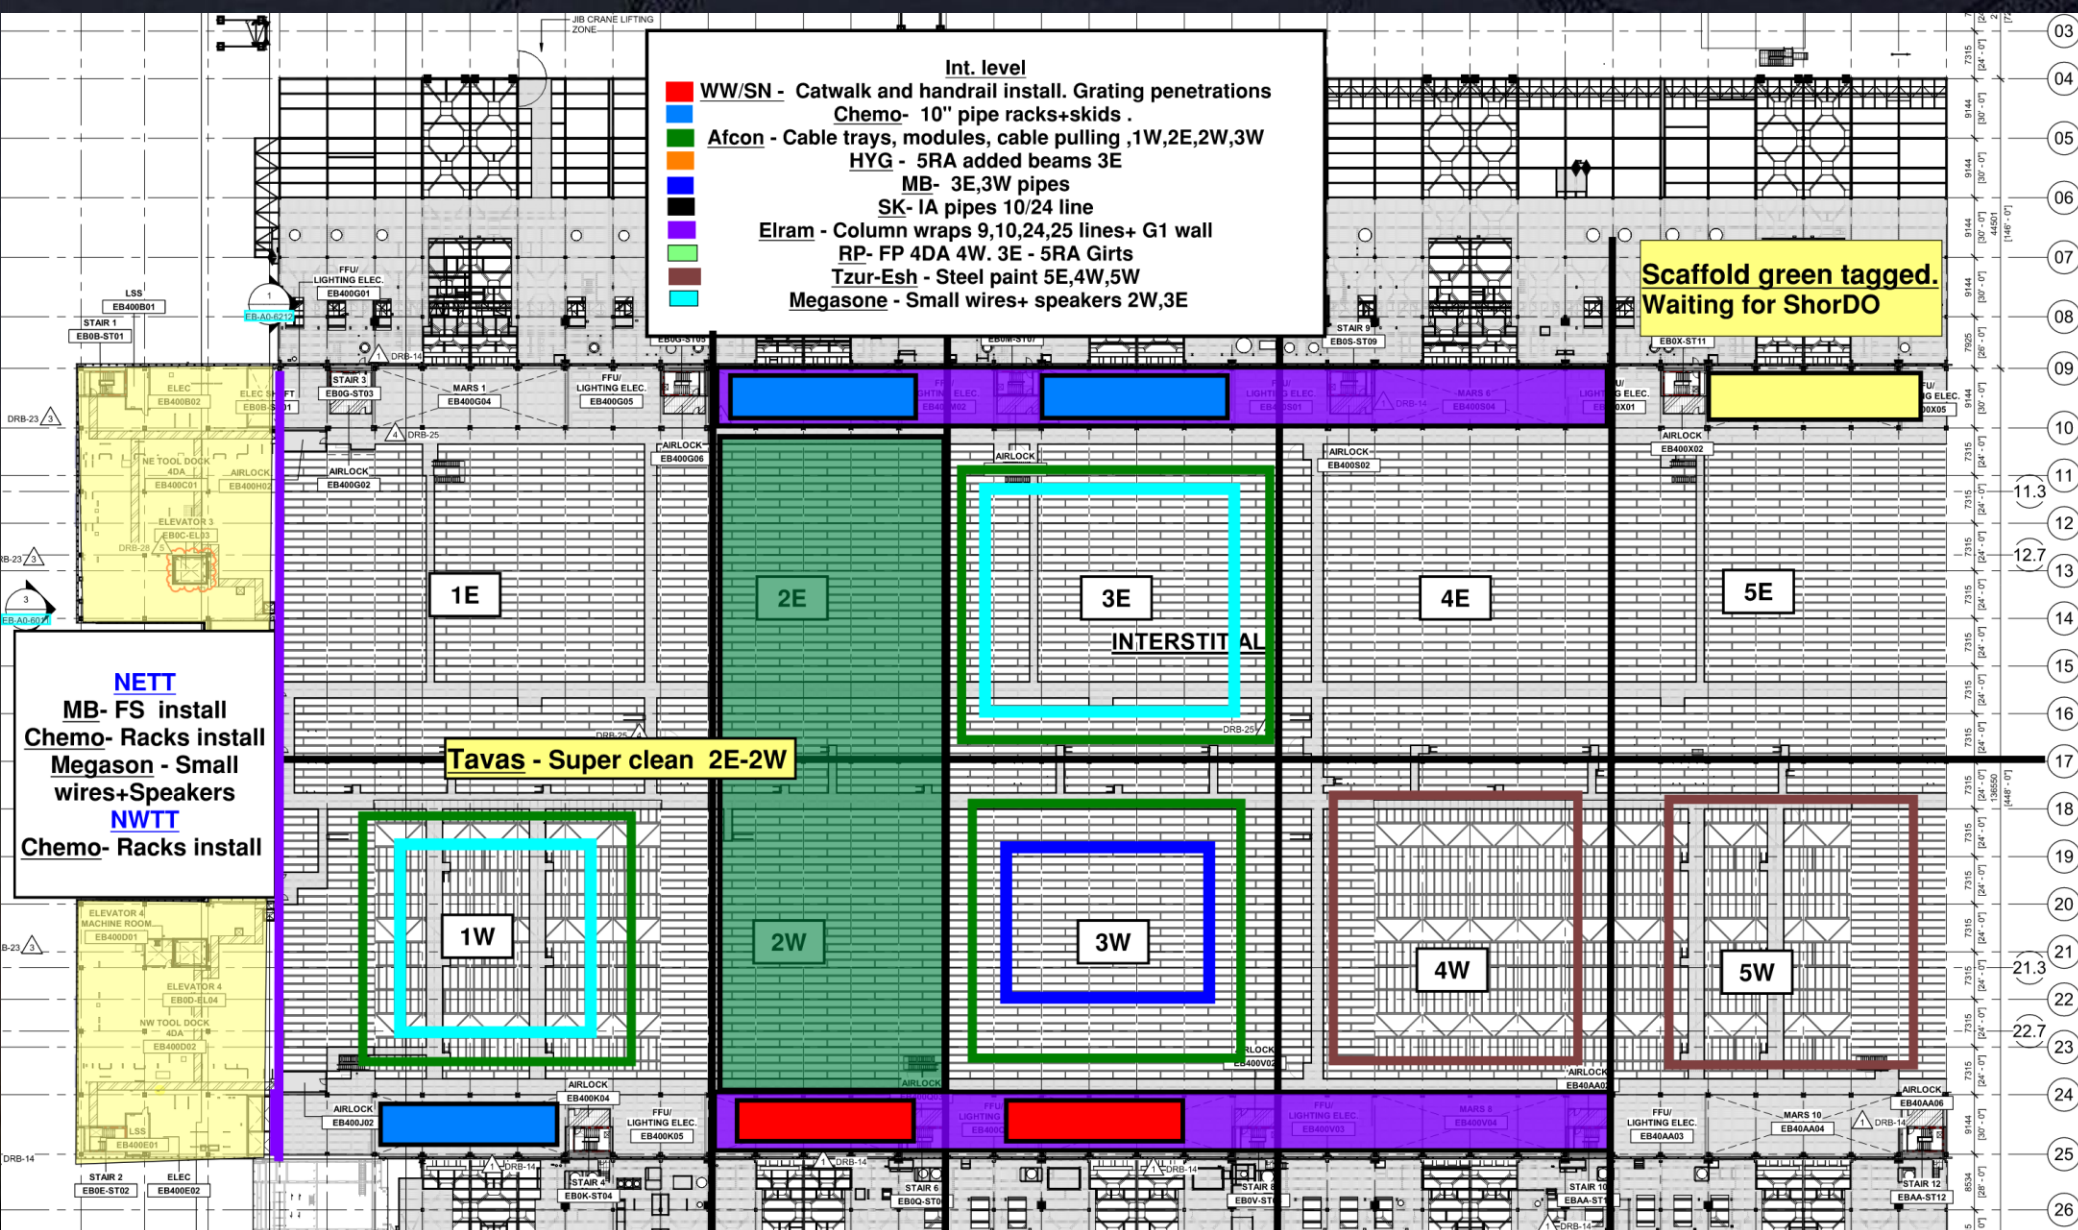

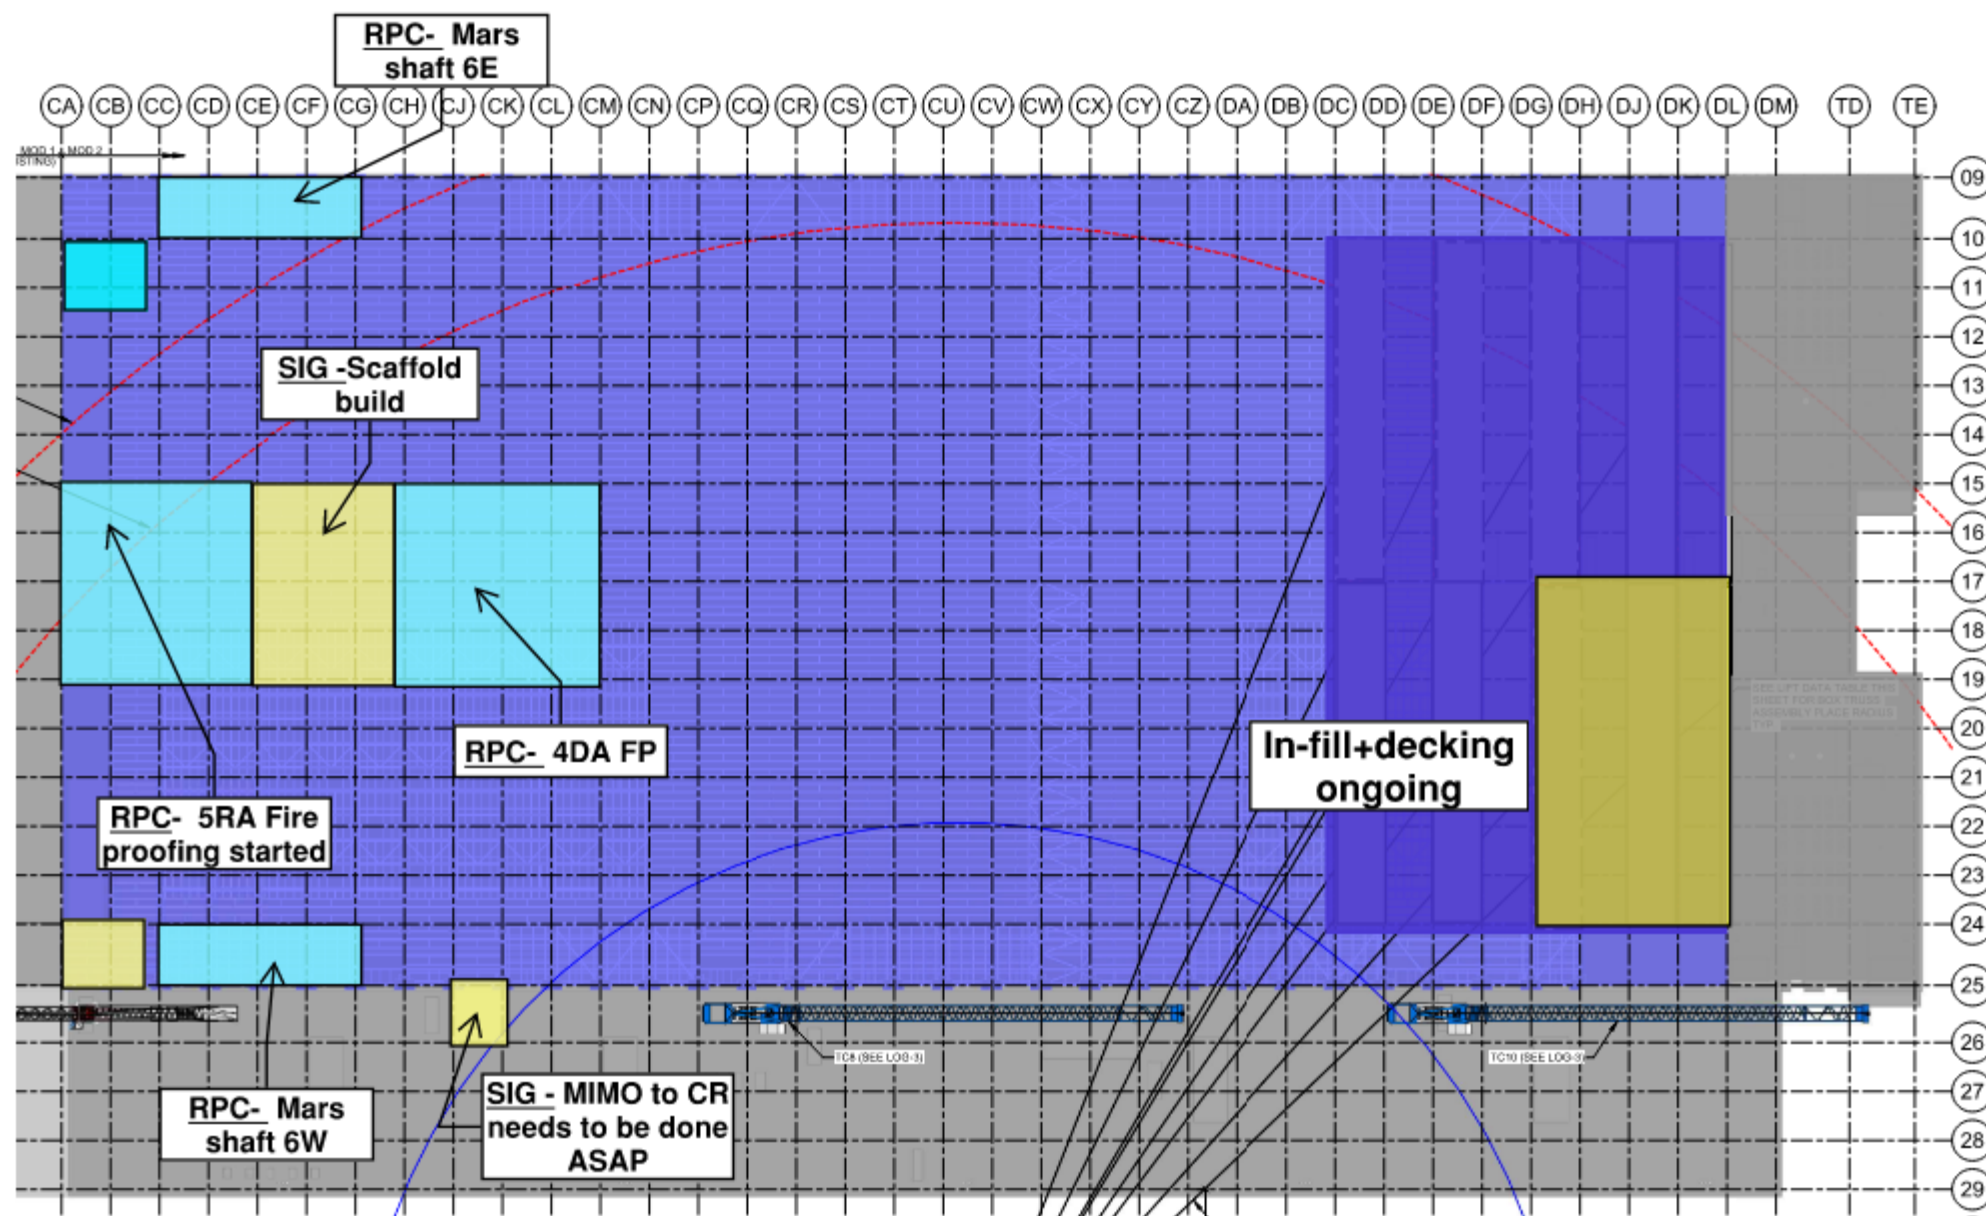

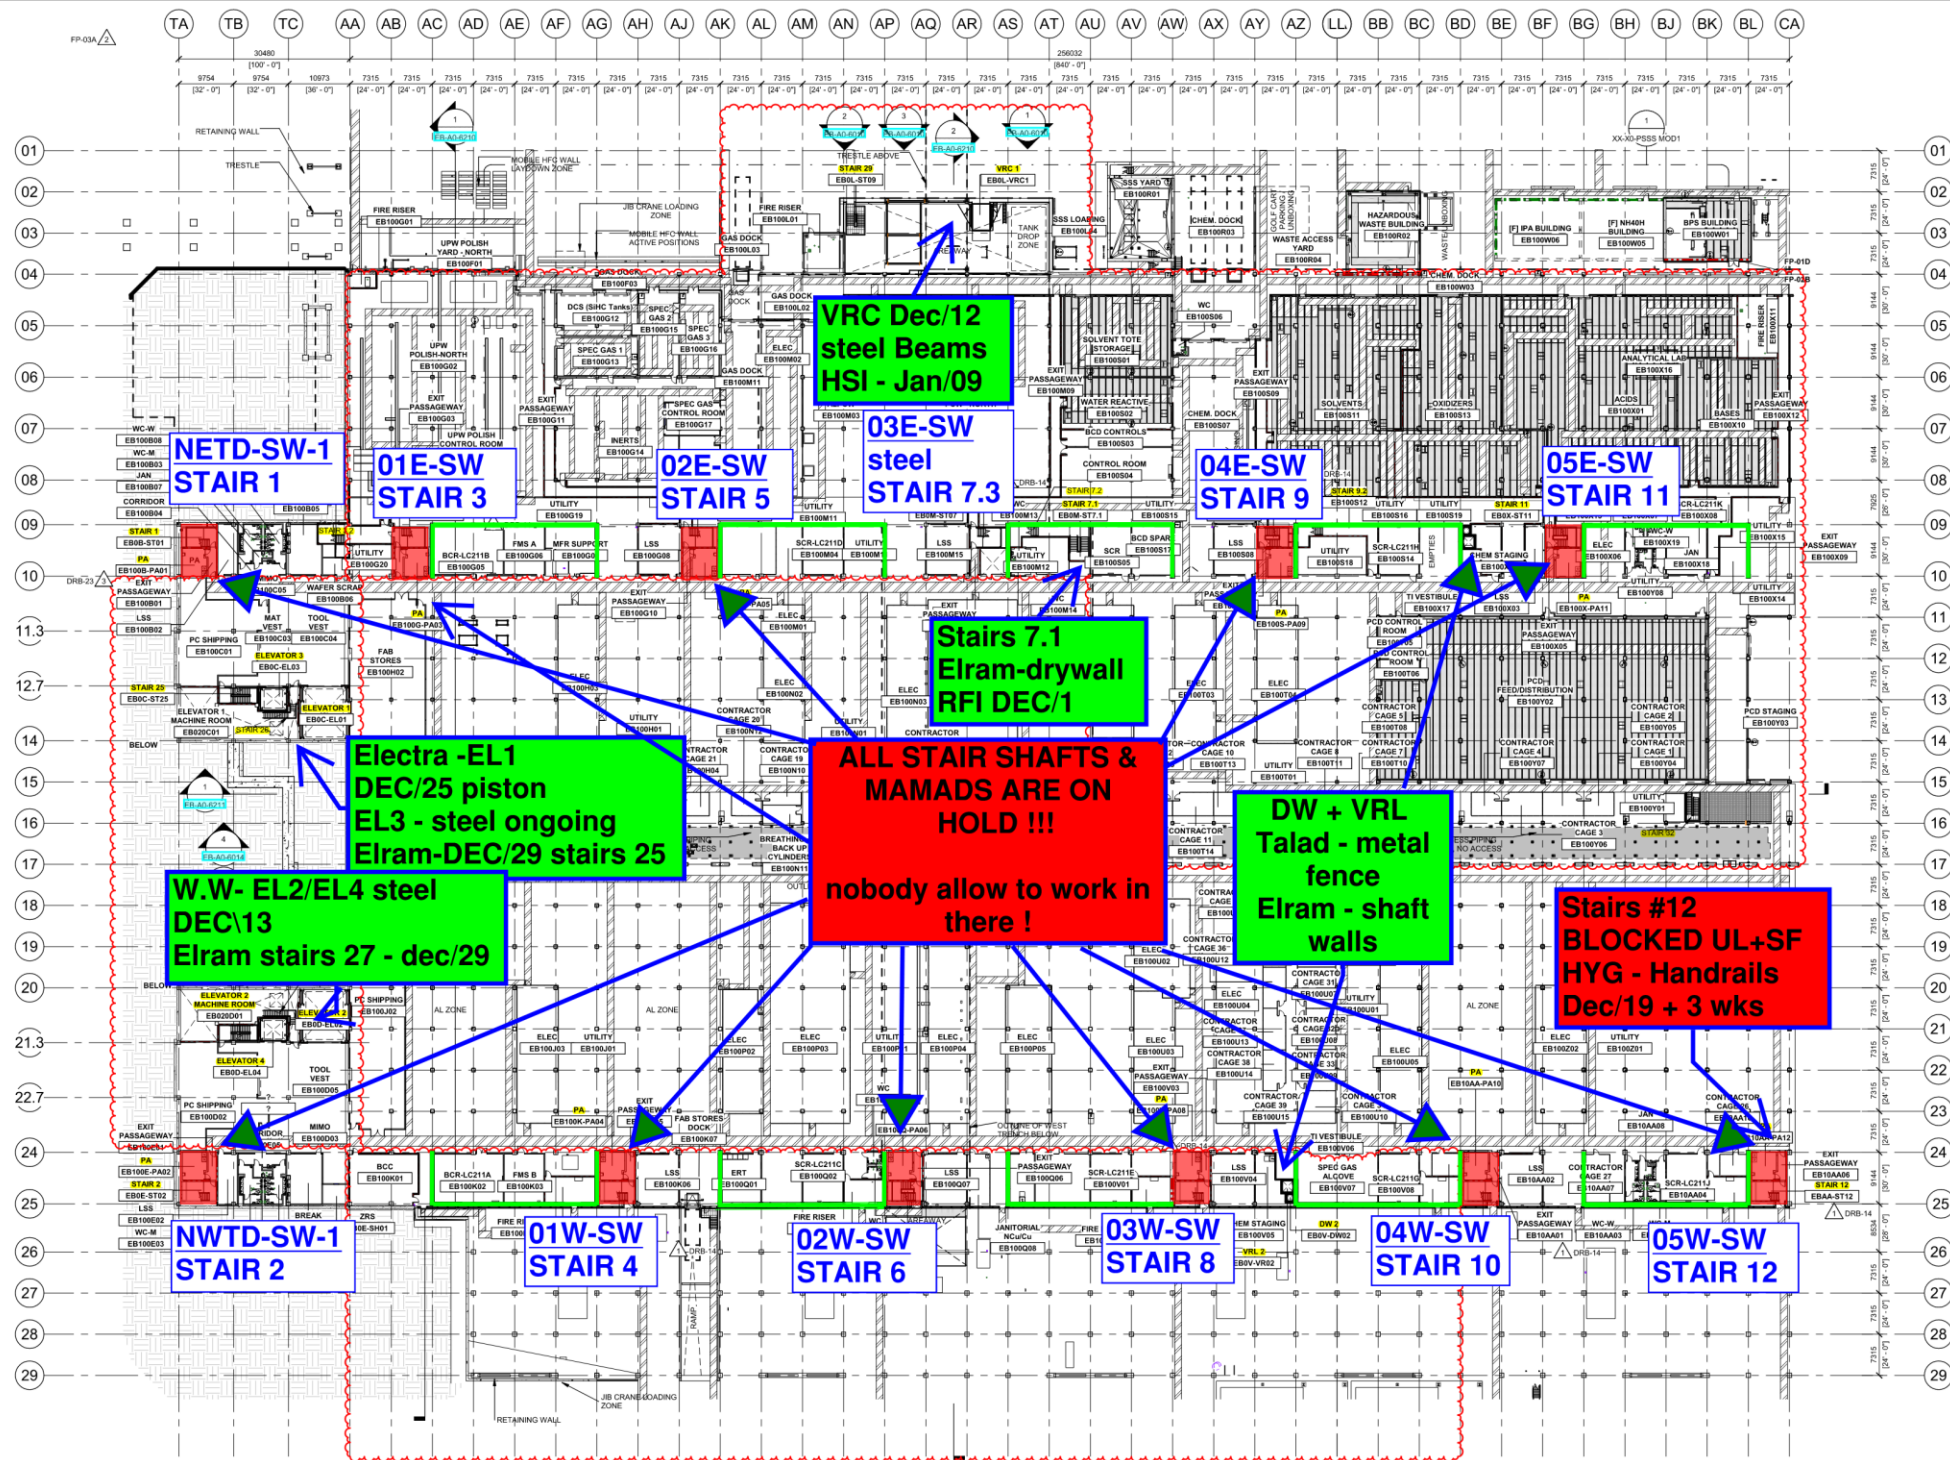

Siding - West FAB - JYG


BLOWDOWN 30%

	TA	TE	TC	AA	AE	AC	AD	AE	AF	AG	AH	AJ	AK	AL	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BK	BL	CA
	1001 / 1002			601 / 602		611 / 612				621 / 622				631 / 632				641 / 642			651 / 652			611 / 612			621 / 622			631 / 632				641 / 642				651 / 652	
Total	20	20	20	15	10		31	31	31	31	31	31	31	31	30	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31
Installed	20	20	10	15	10		31	31	31	31	31	31	31	31	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20	20
%	100%	100%	50%	100%	100%		100%	100%	100%	100%	100%	100%	100%	100%	100%	90%	90%	90%	90%	100%	100%	87%	77%	77%	81%	100%	65%	100%	81%	81%	81%	65%	65%	65%	100%	90%	65%	65%	65%
SRA			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
4DA			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
3FK			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
3FA			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
2SA SF			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	
UL			0												0	0	0				0	0	0	0		0		0	0	0	0	0	0		0	0	0	0	


Link


[illegible]

		Siding - North FAB																											
		100% - BLOWDOWN																											
		9	10	11	12	13	14	TA	TB	TC	14	15	15	15.5	16.5	17.5	18.5	19	19.5	20	TC	TB	TA	20	21	22	23	24	25
	Total	901C / 902C		911A / 912A				911B / 912B			911C / 912C					1011C / 1012C						1011B / 1012B			1011A / 1012A			1001C / 1002C	
	Installed	29	29	29	29	29		29	29		27	18	9	27	27	27	27	9	9	0		29	29		29	29	29	29	29
	%	100%	100%	24%	0%	0%		0%	24%		33%	0%	100%	100%	100%	100%	100%	33%	100%	0%		31%	31%		100%	100%	100%	100%	100%
5RA-ROOF - 172166.8	27	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	26	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	25	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	24	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
4DA-EQ DECK - 167798.0	23	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	22	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	21	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	20	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
3FL-FAB - 162,789.20	19	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	18	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	17	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	16	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
3FA-FAB WAFFLE - 156,825.2	15	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	14	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	13	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	12	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	11	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	10	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
	9	1	1	0	0	0		0	0		0	0	0	1	1	1	0	0	0		0	0		1	1	1	1	1	
2SA SUBFAB - 149,433.8	8	1	1	0	0	0		0	0		0	1	1	1	1	1	1	1	1		1	1		1	1	1	1	1	
	7	1	1	0	0	0		0	0		0	1	1	1	1	1	1	1	1		1	1		1	1	1	1	1	
	6	1	1	0	0	0		0	1		0	1	1	1	1	1	1	1	1		1	1		1	1	1	1	1	
	5	1	1	0	0	0		0	1		0	1	1	1	1	1	1	1	1		1	1		1	1	1	1	1	
	4	1	1	0	0	0		0	1		0	1	1	1	1	1	1	1	1		1	1		1	1	1	1	1	
	3	1	1	0	0	0		0	1		0	1	1	1	1	1	1	1	1		1	1		1	1	1	1	1	
	2	1	1	0	0	0		0	1		0	1	1	1	1	1	1	1	1		1	1		1	1	1	1	1	
	1	1	1	0	0	0		0	1		0	1	1	1	1	1	1	1	1		1	1		1	1	1	1	1	
1YE-TOOL-DOCK - 147,700.0																													

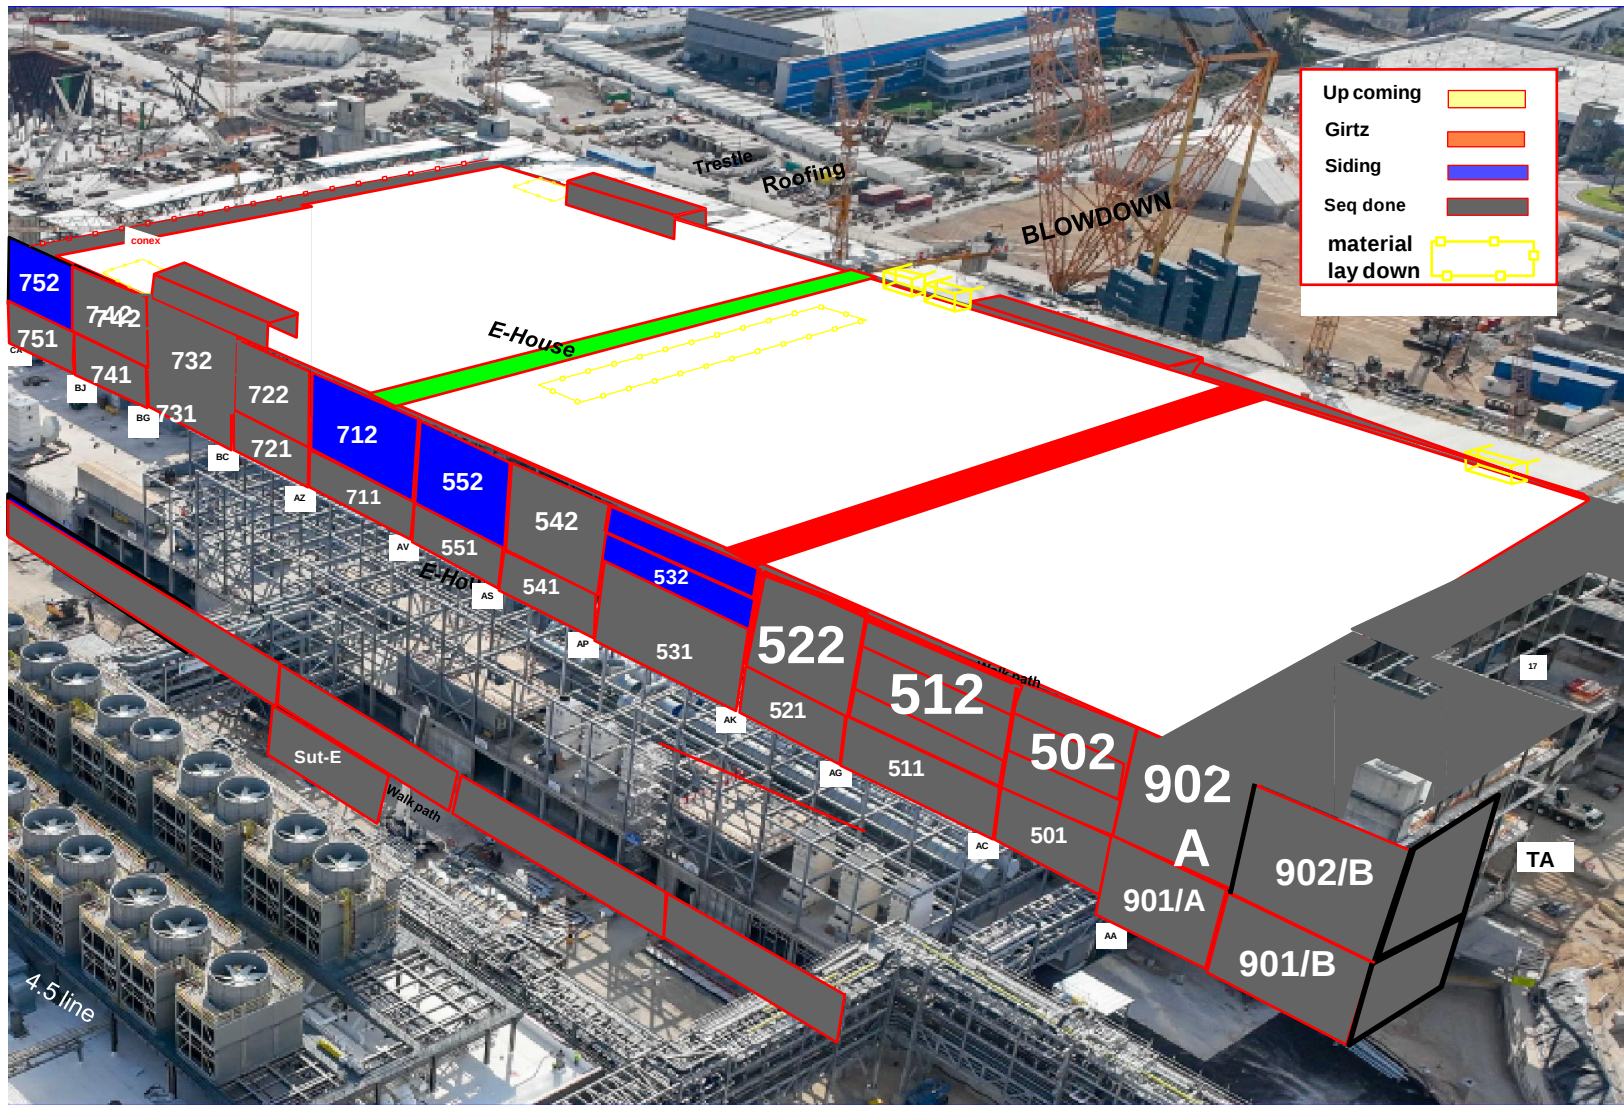


Walk path

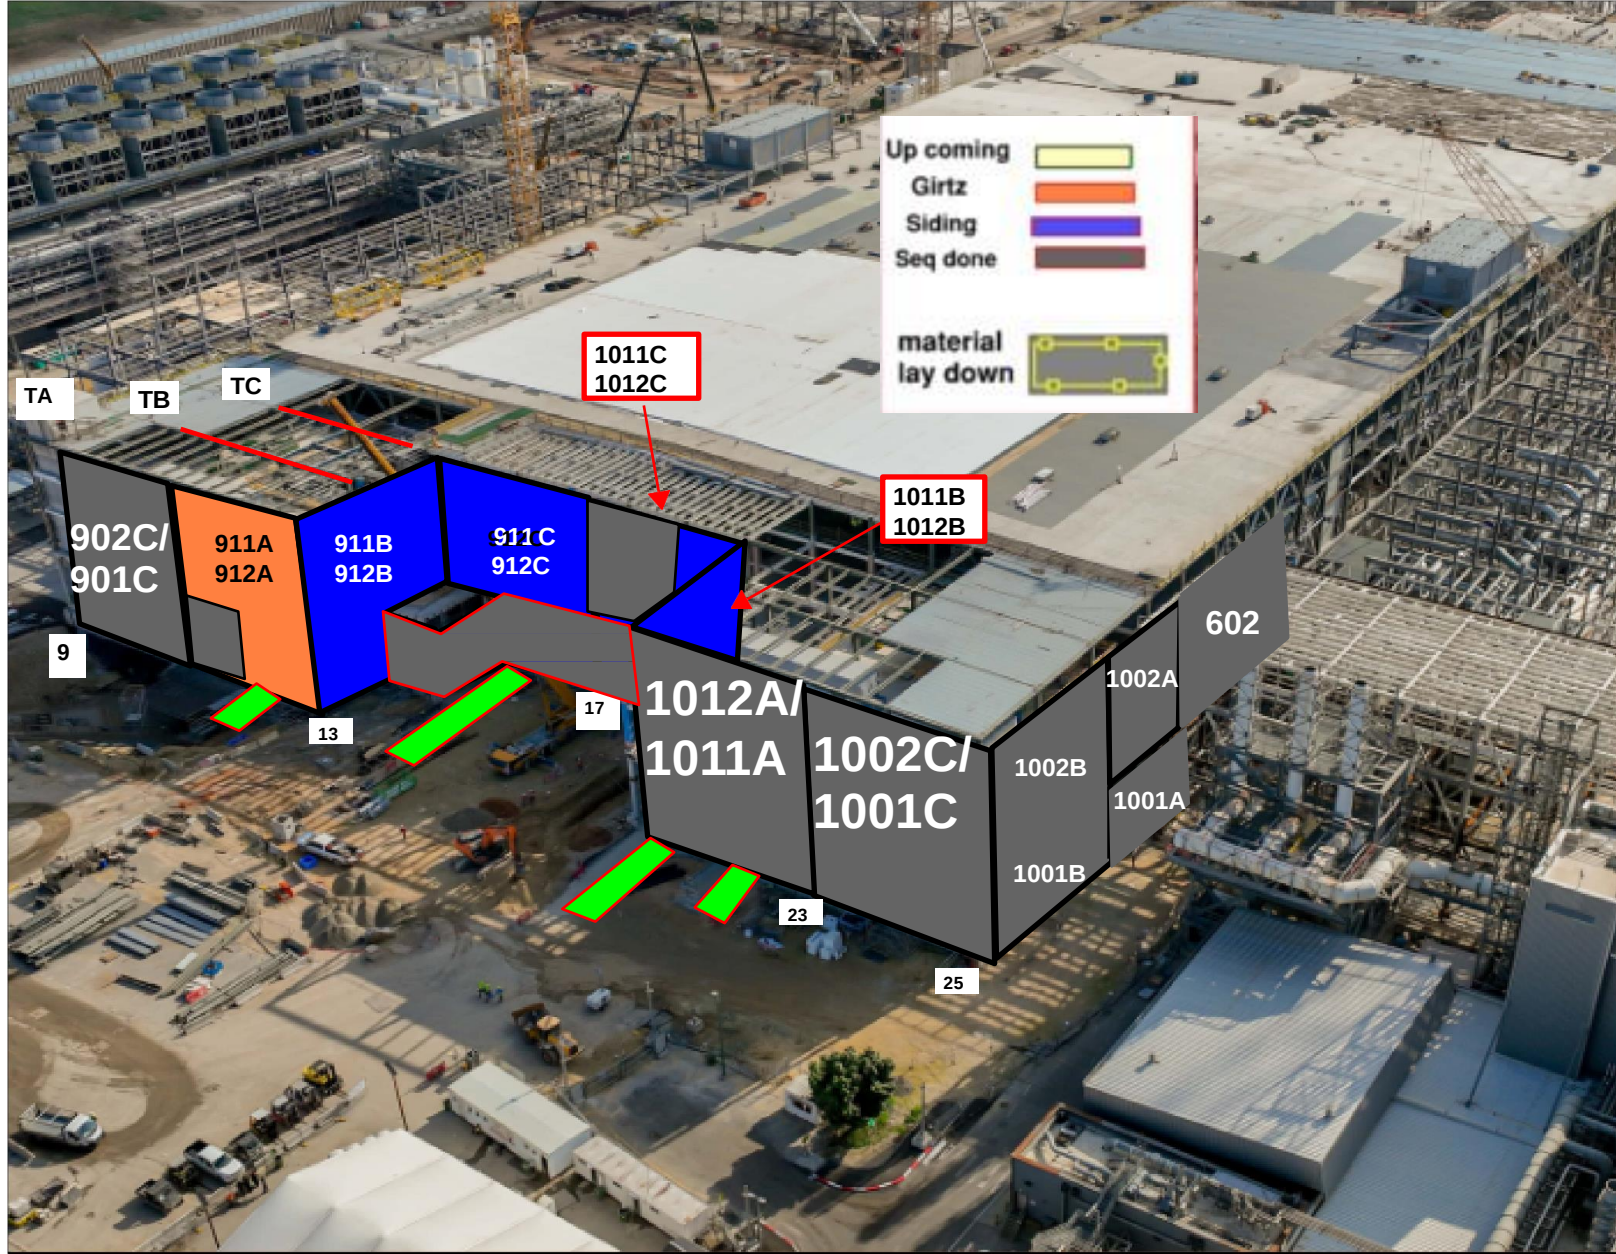

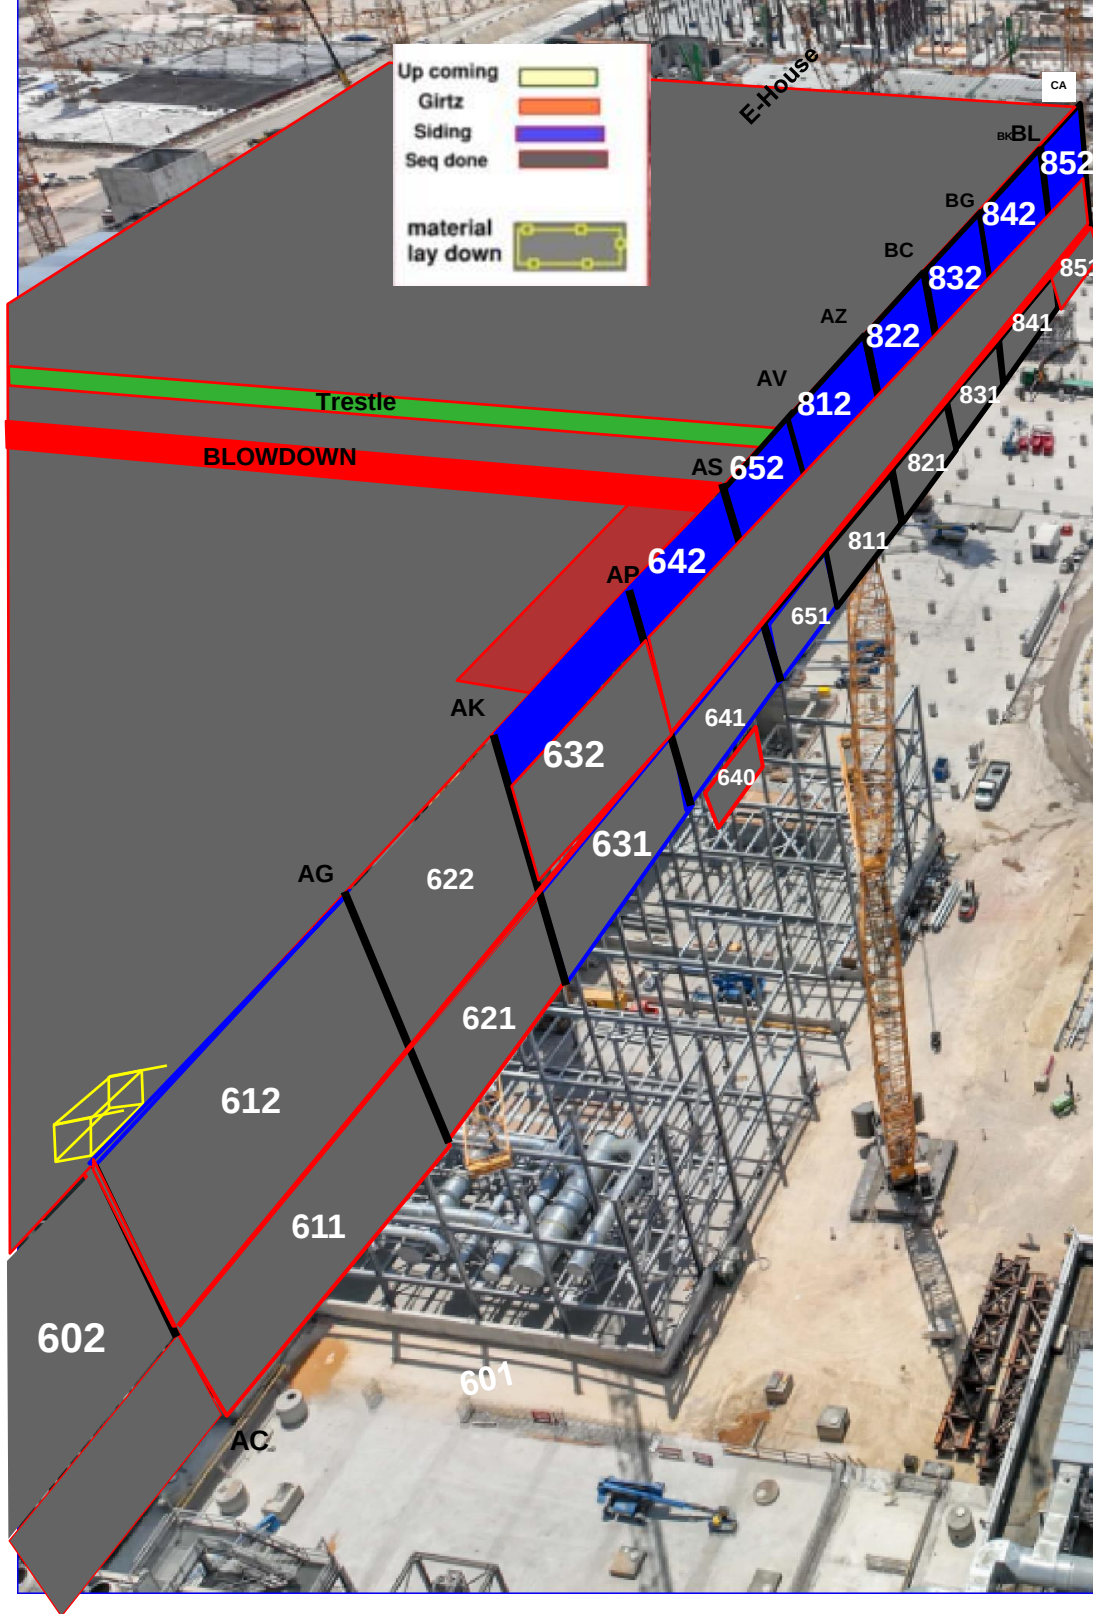


PSSS.1

Utility Level 1YA

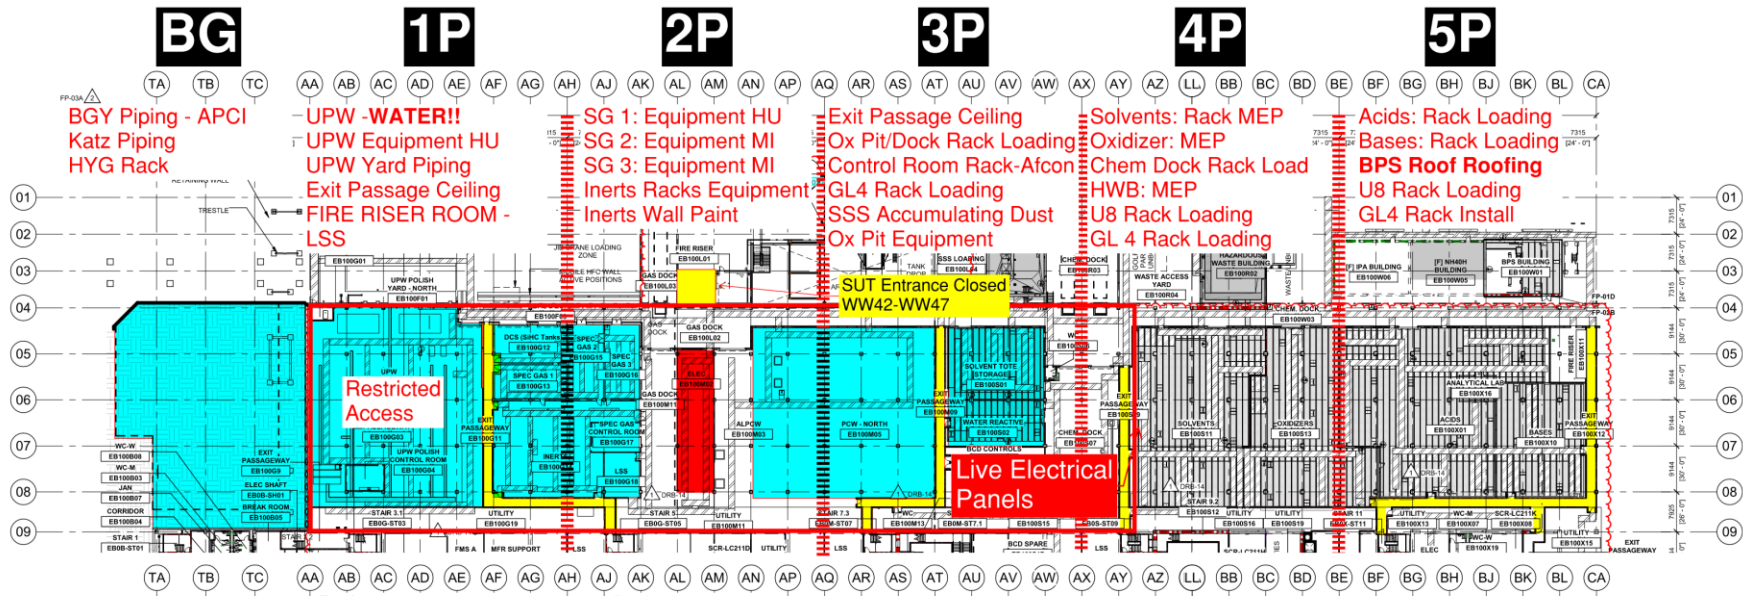


PSSS Roof 2SA

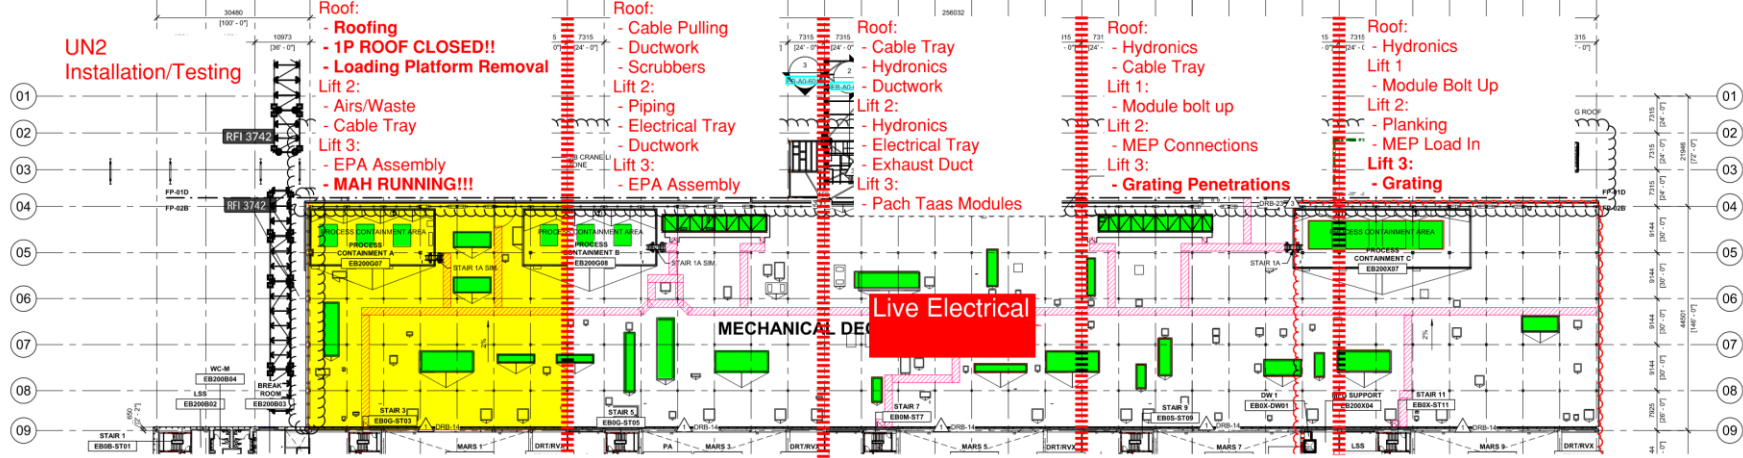


PSSS.2

Utility Level
1YA


PSSS Roof
2SA

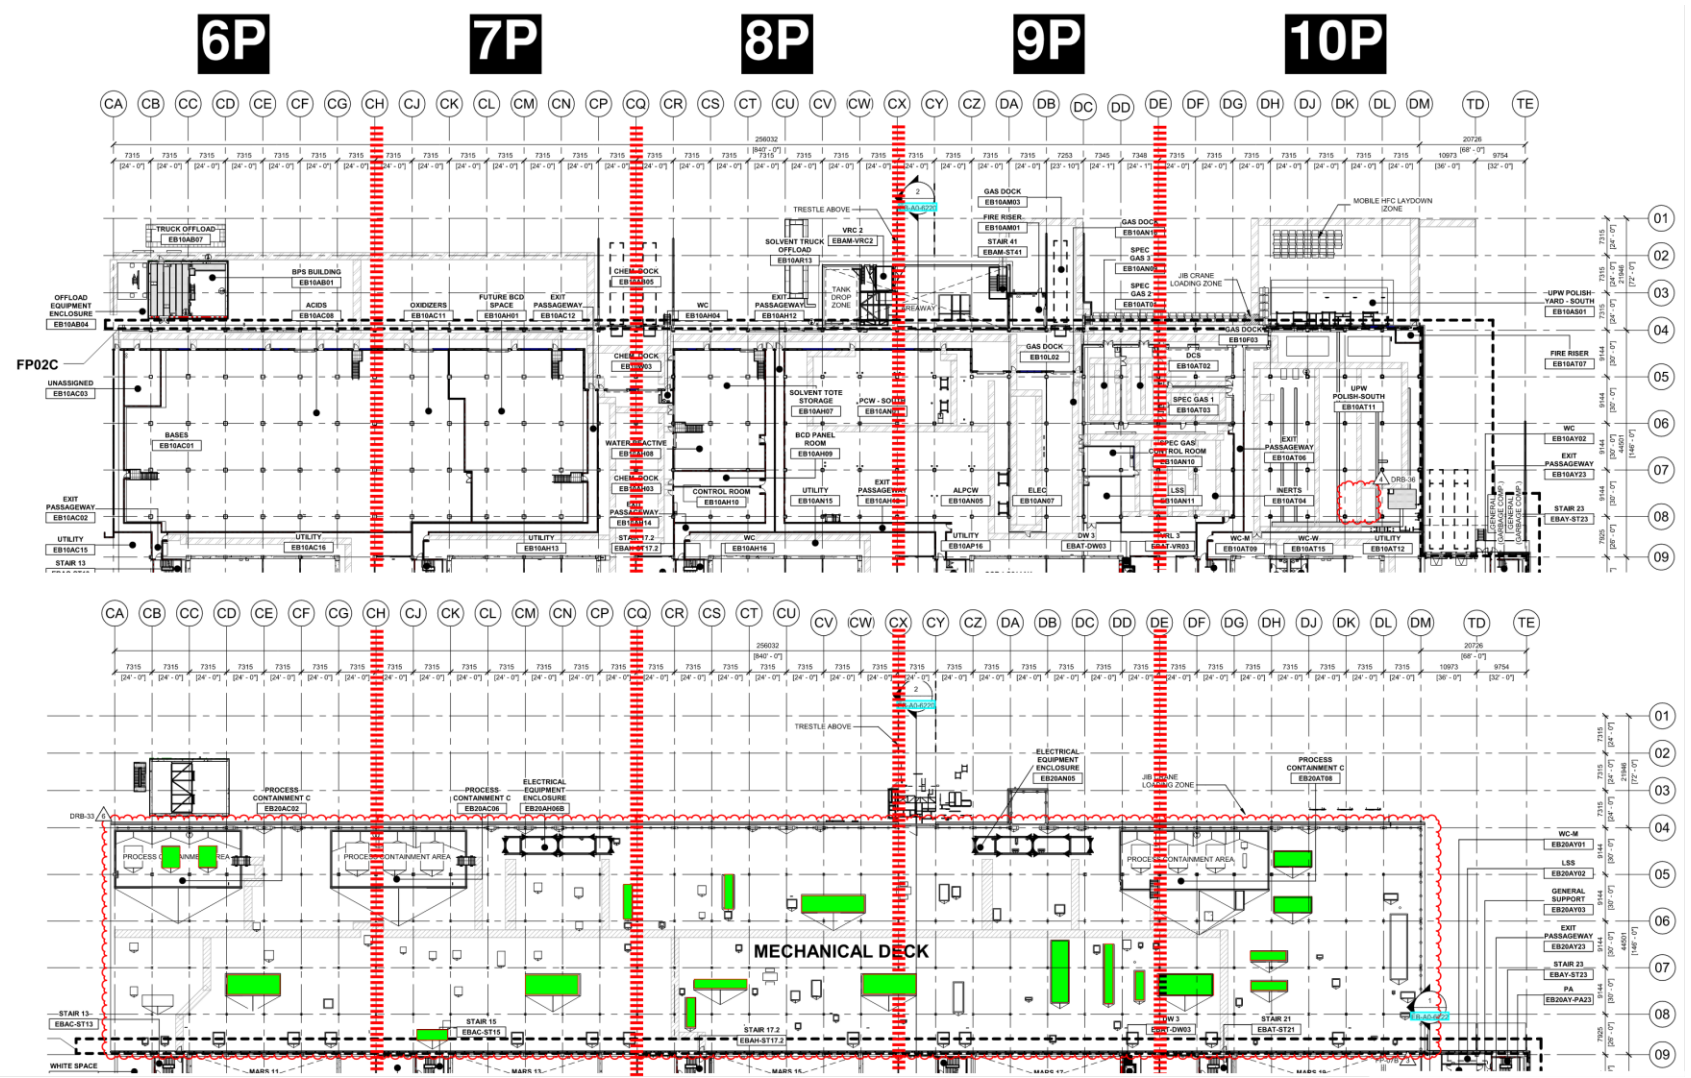

3800
Build
22nd_
26th

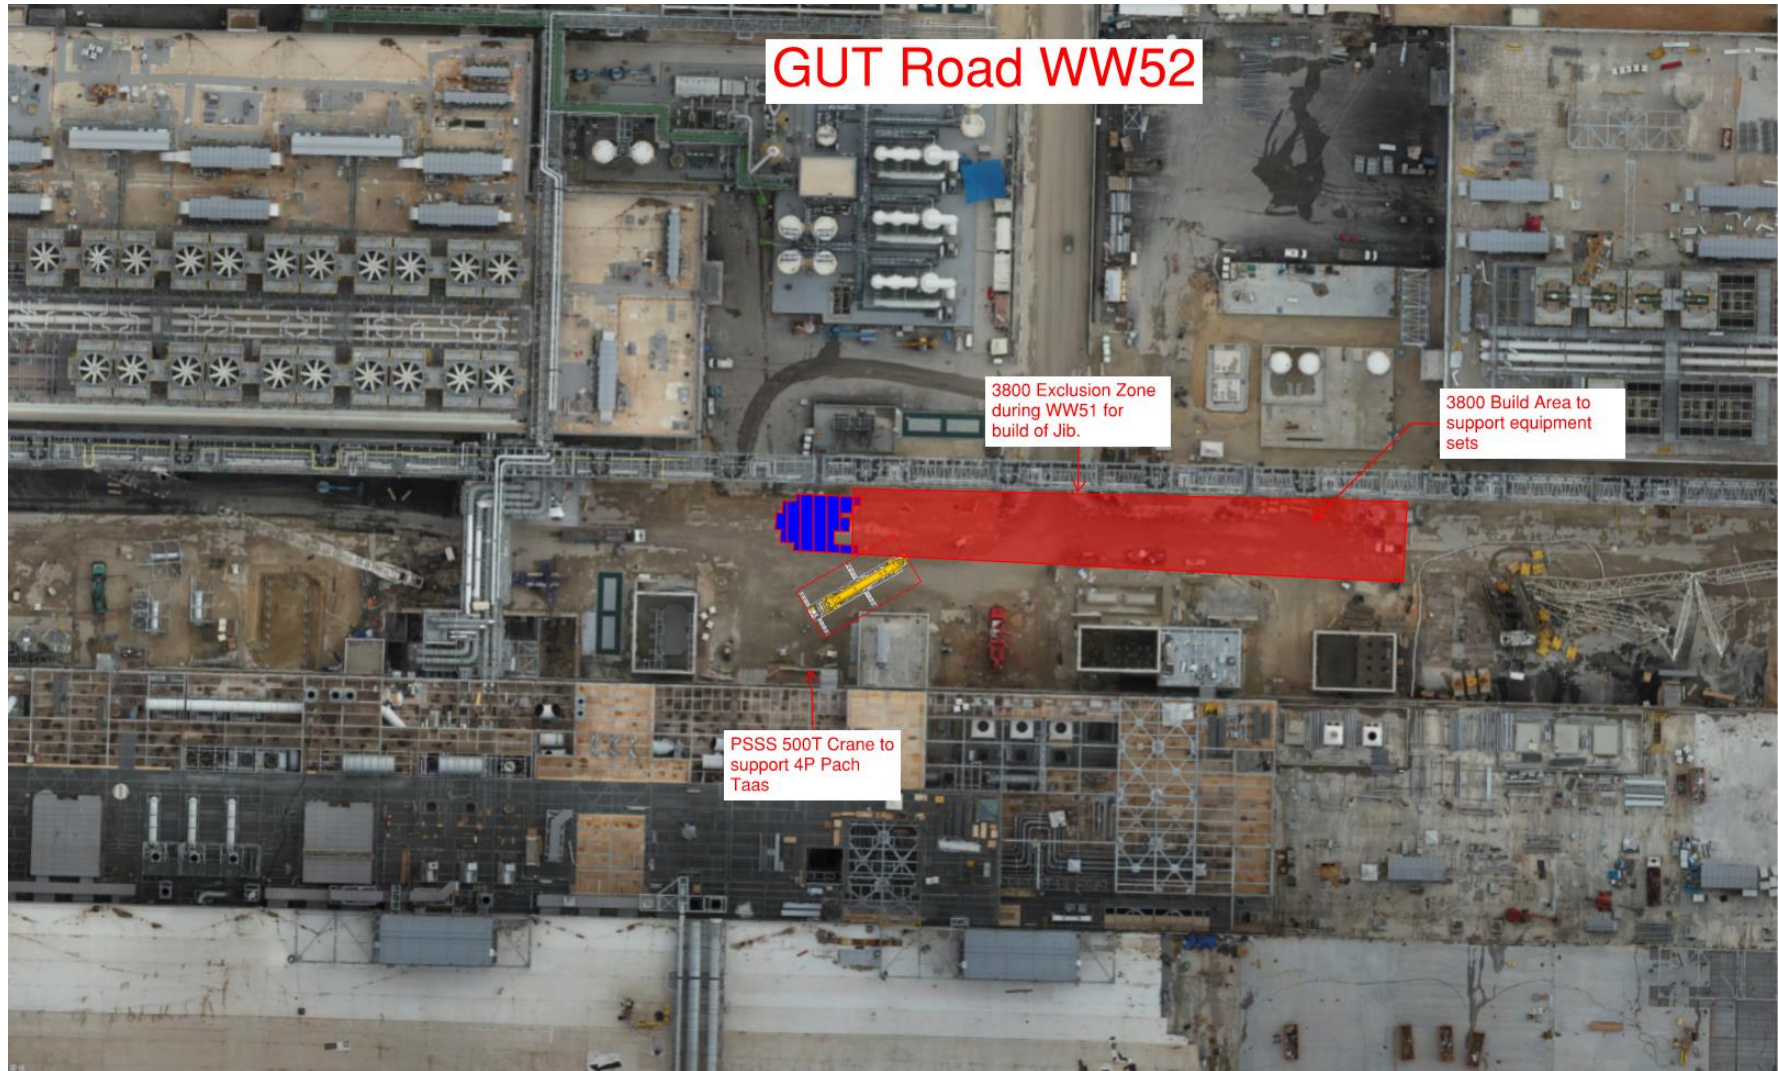


UN2
BGY
Pressure
Test
23/12
@11:00
– 17:00

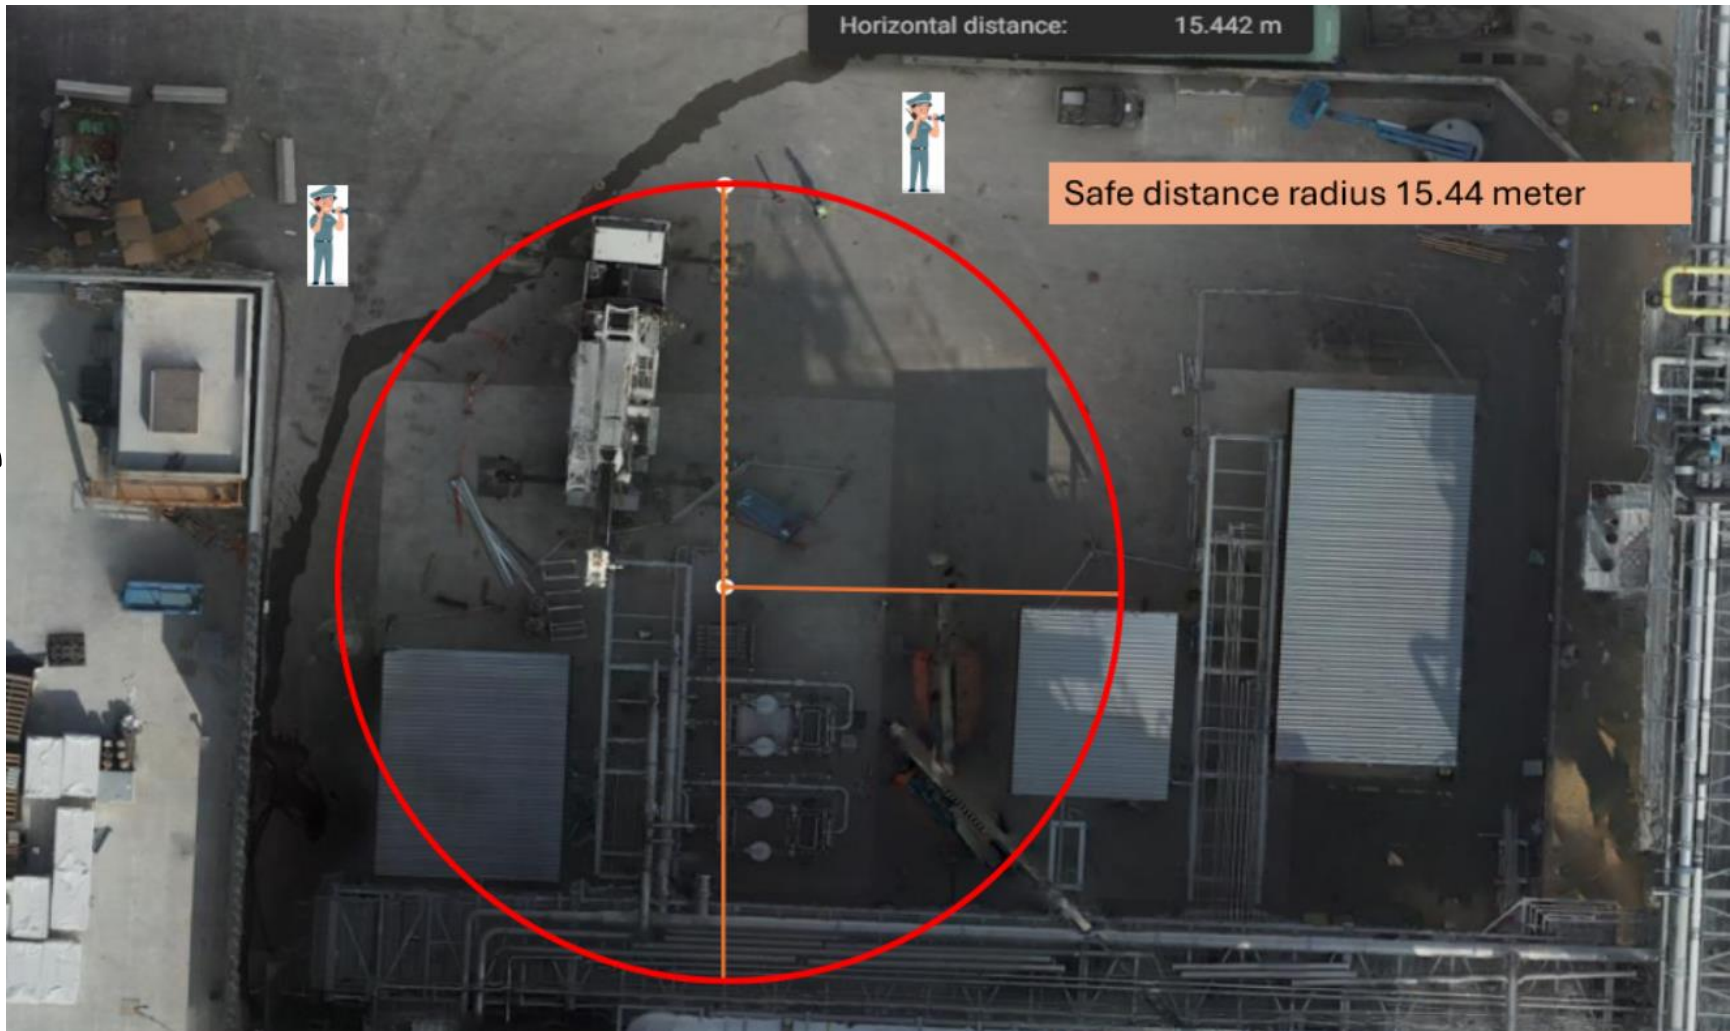


IA/PA Pressure Test

23/12

17:00

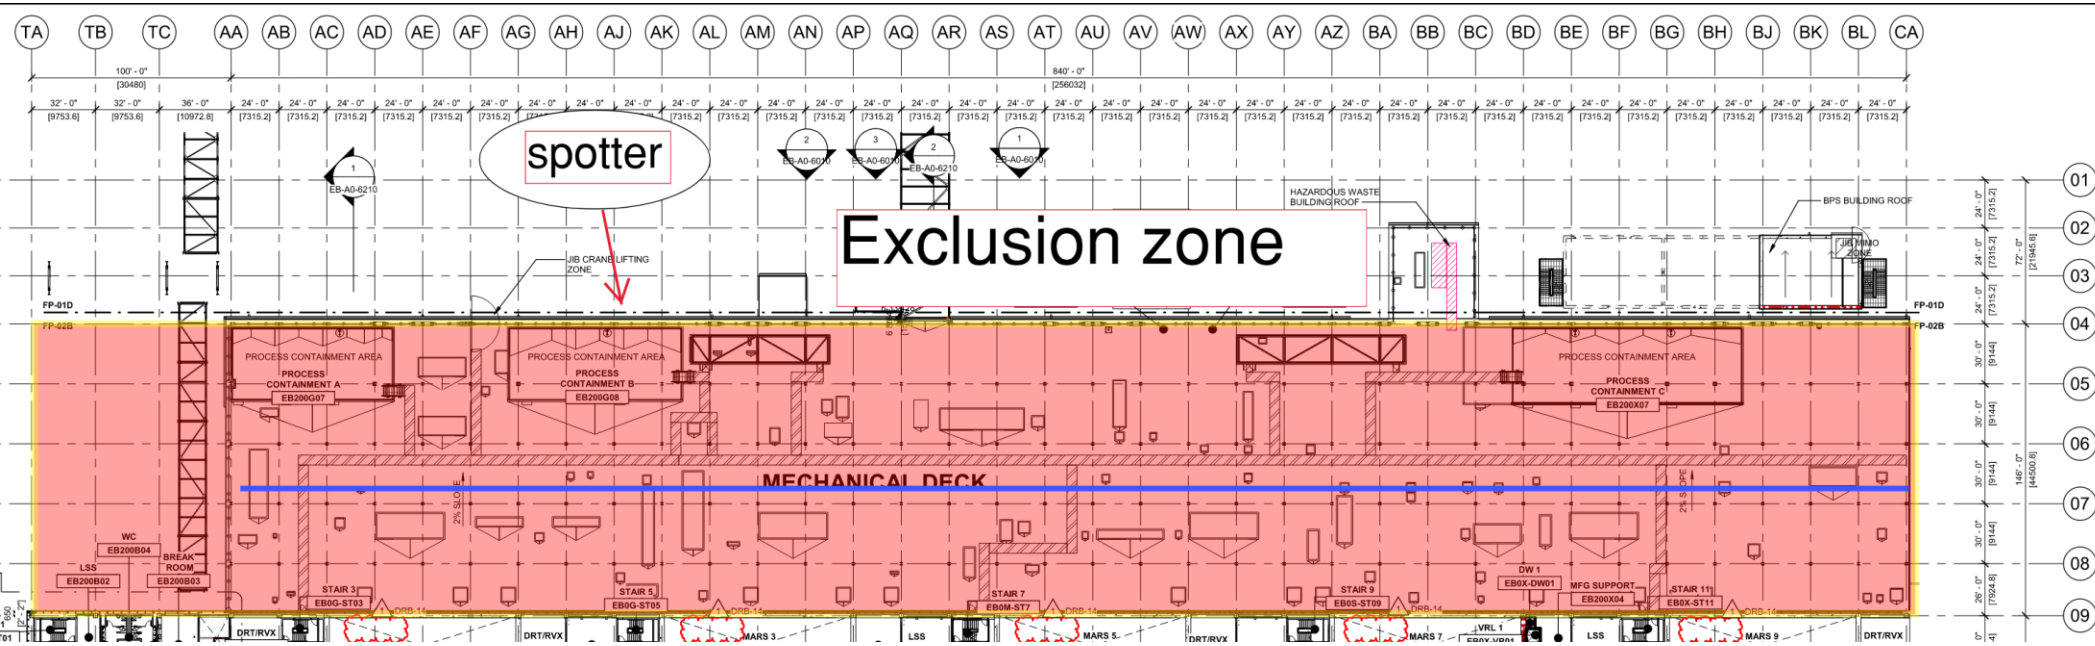

PCW/
ALPCW
Test
24/12
17:00 –
05:00

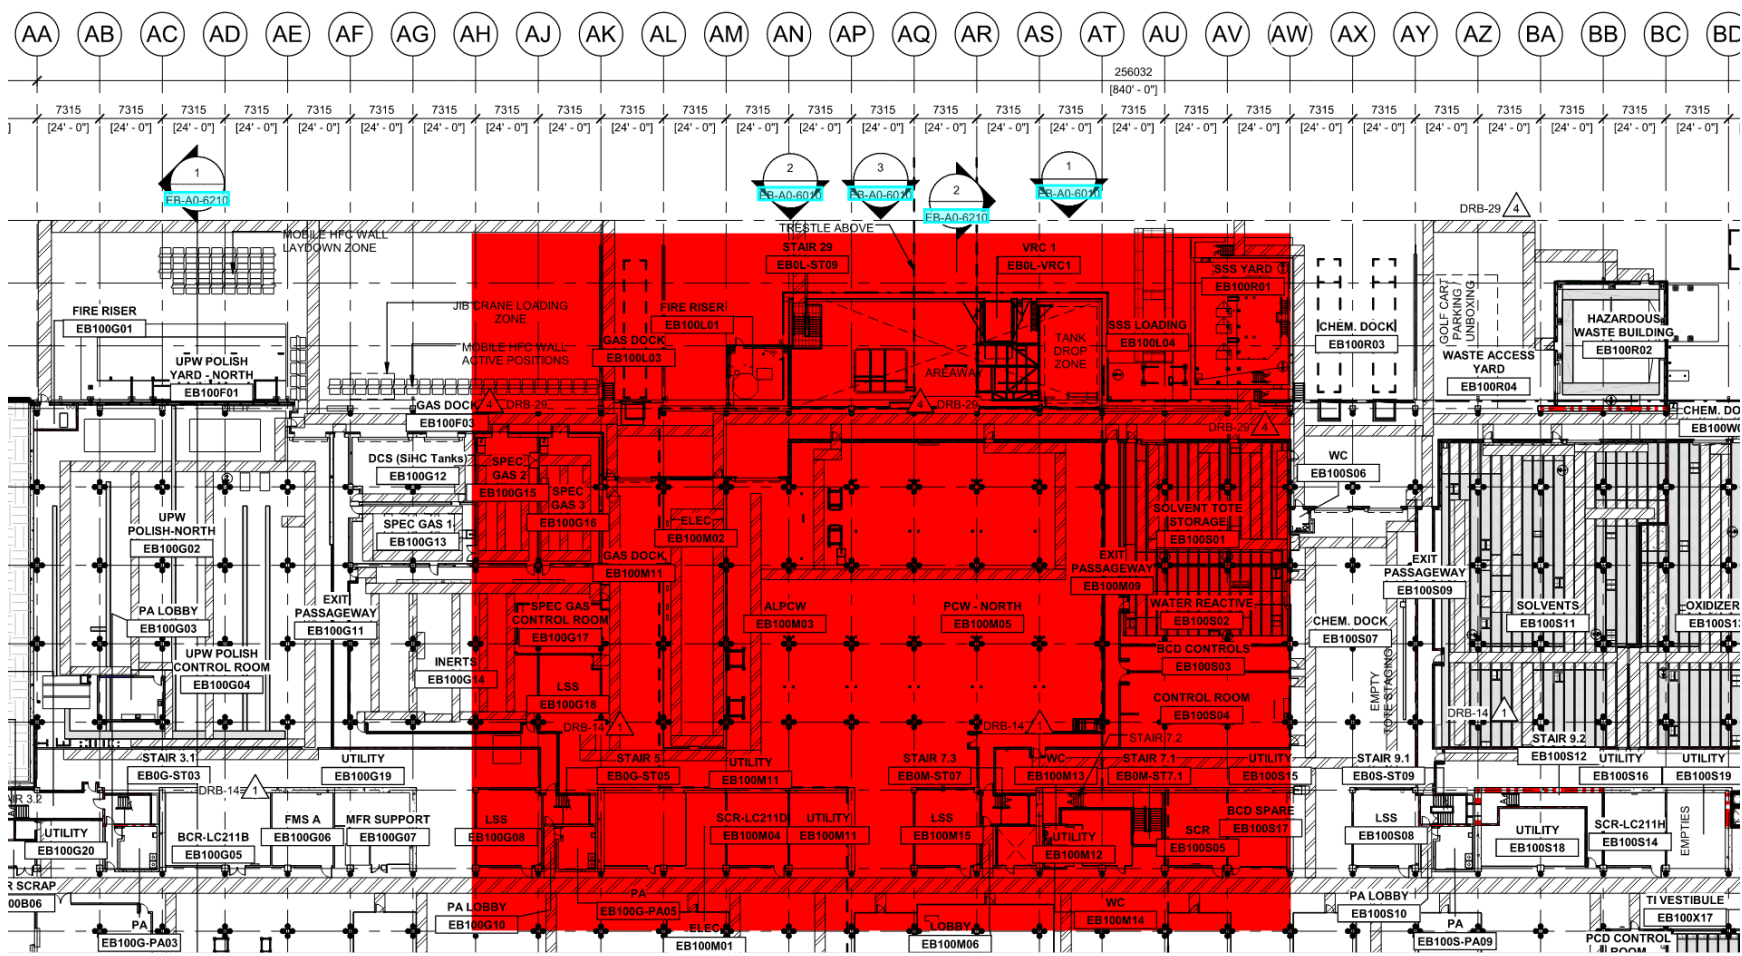



WJG 01J, 02J LIFT 2 & 3





WJG 03J, 04J, 05J LIFT 2 & 3



1J

EB100K02 EB100K03
FIRE RISER EB100K04
Stair 4 Access Closed
DRB-14
RAMPS
JIB CRANE LADING ZONE

2J

EB100U00 EB100U01
FIRE RISER EB100Q03
WC EB100Q04
STAIR EB100V-ST
FIRE RISEWAY
JANITORIAL NCU/Cu EB100Q08
FIRE RISER EB100V02

3J

EB100V07 EB100V01
STAIR EB100V-ST
CHEM STAGING EB100V05
DW 2 EB100V-DW02
FIRE RISER EB100V09
CONTRACTOR CAGE 28 EB100V10

4J

EB10AA07 EB10AA04
PA LOBBY EB10AA01
WC-W EB10AA03
WC-M EB10AA09
FIRE RISER EB10AA05
DRB-14


5J

STAIR EB10AA-ST
DRB-14

Callout Boxes:

- Meptagon - All Over**
Pach Taas - UPN 138
Afcon Lighting / Electrical Cable Pulling
- Meptagon - All Over**
- Afcon - Cable Pulling**
PH2.0 - Pump Connections
- Lesico Pipe + Pipe Support**
Pach Taas Bolting
TC4 - Build Back
- Pach Taas - Bolting**
Afcon - Cable Tray


CUB 1

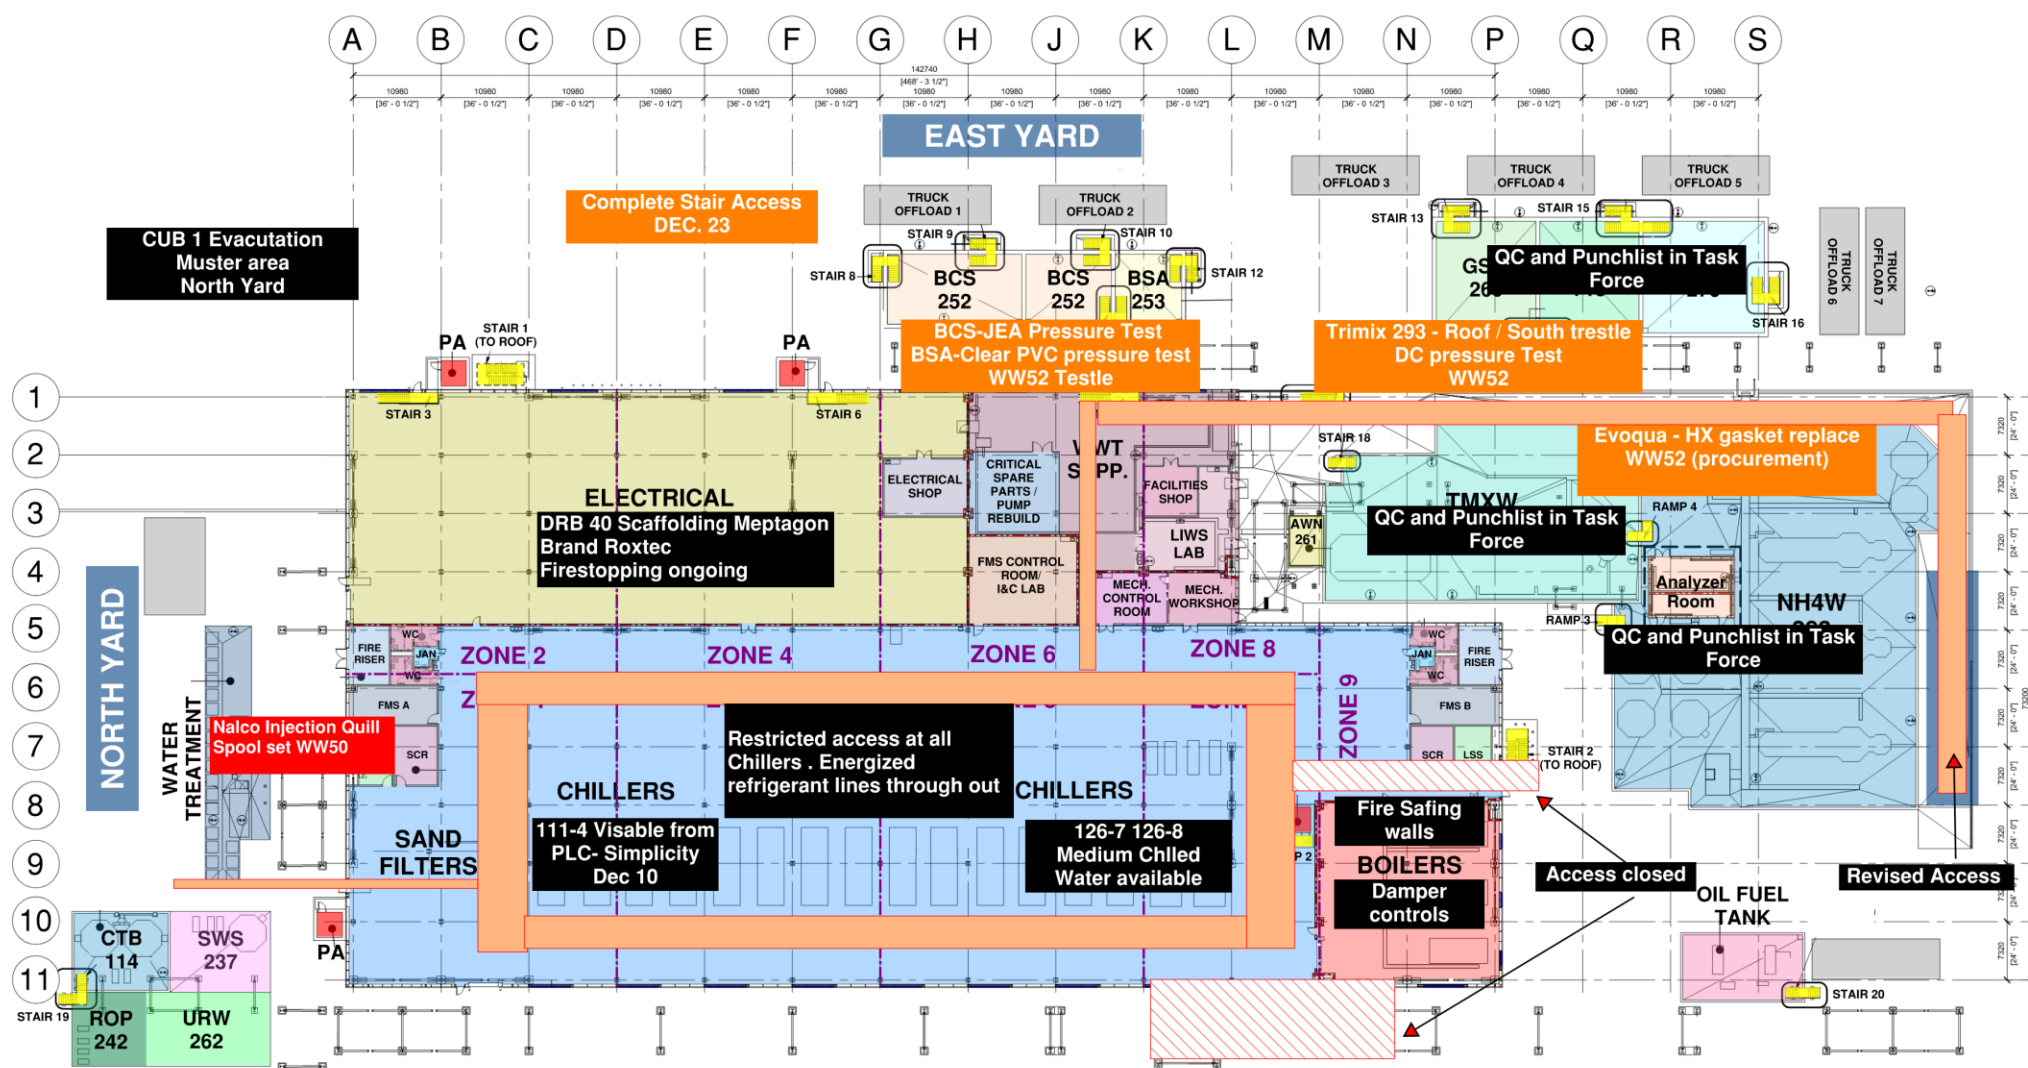


CUB 1 – EXTERIOR/ROOF




CUB 2- Load in and H&T

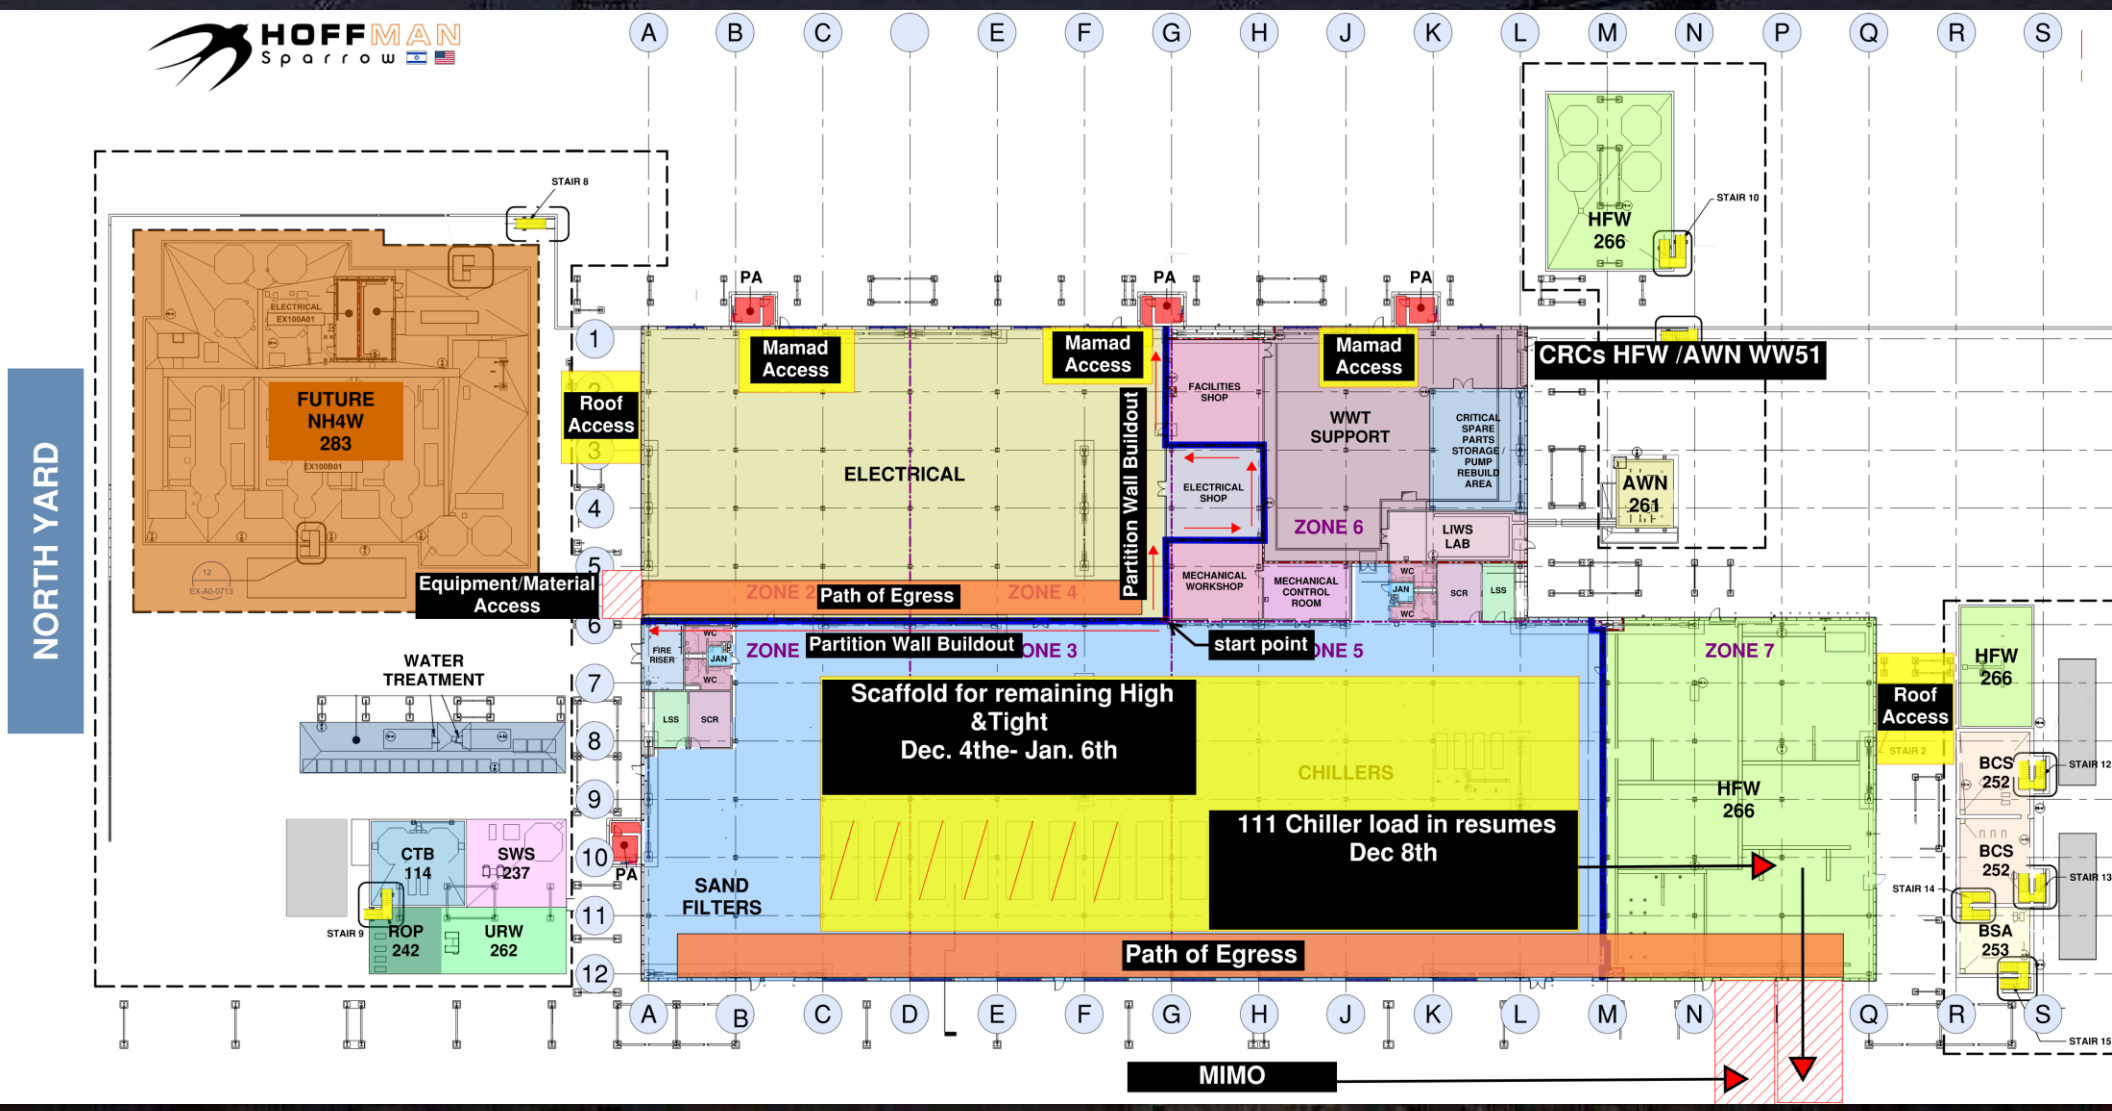

CUB 2 – EXTERIOR/ROOF

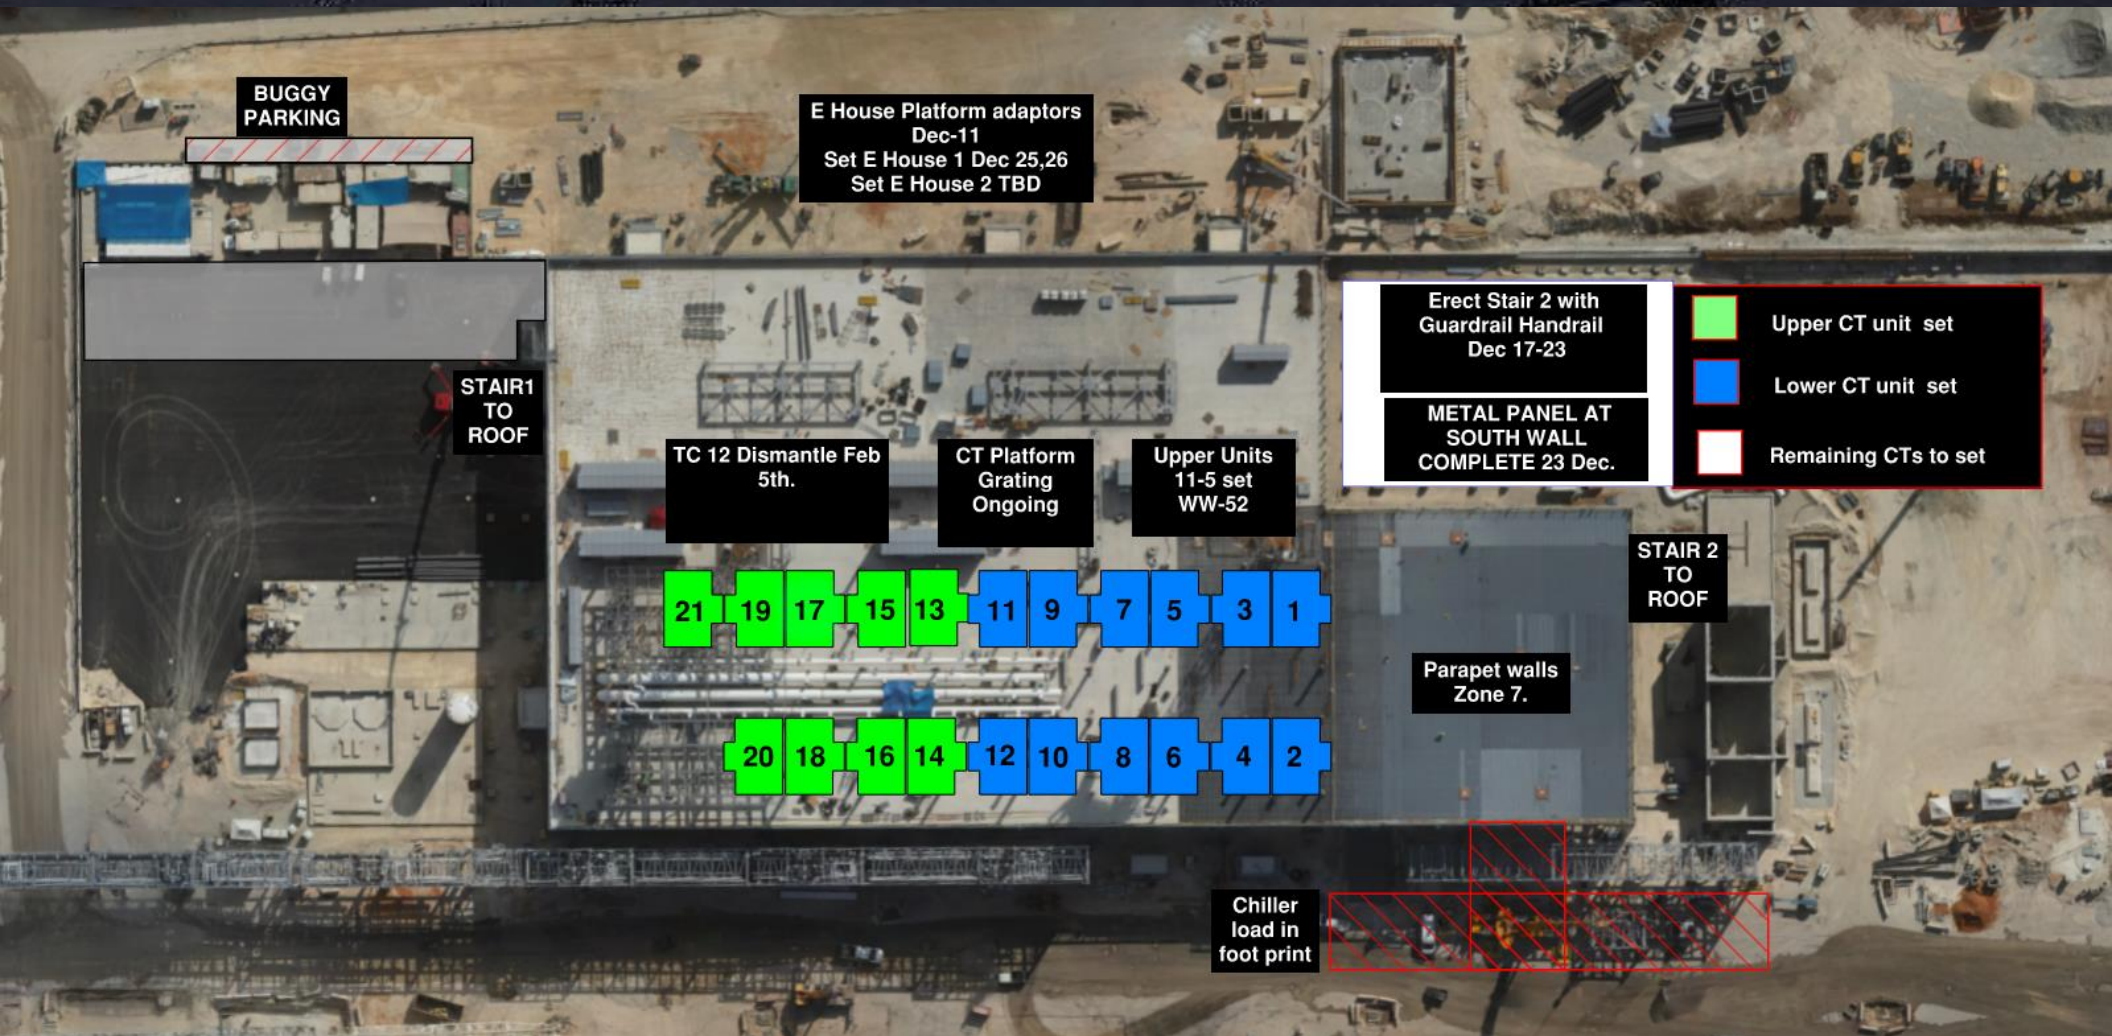

GIS GATE
closed 29/Dec /2024

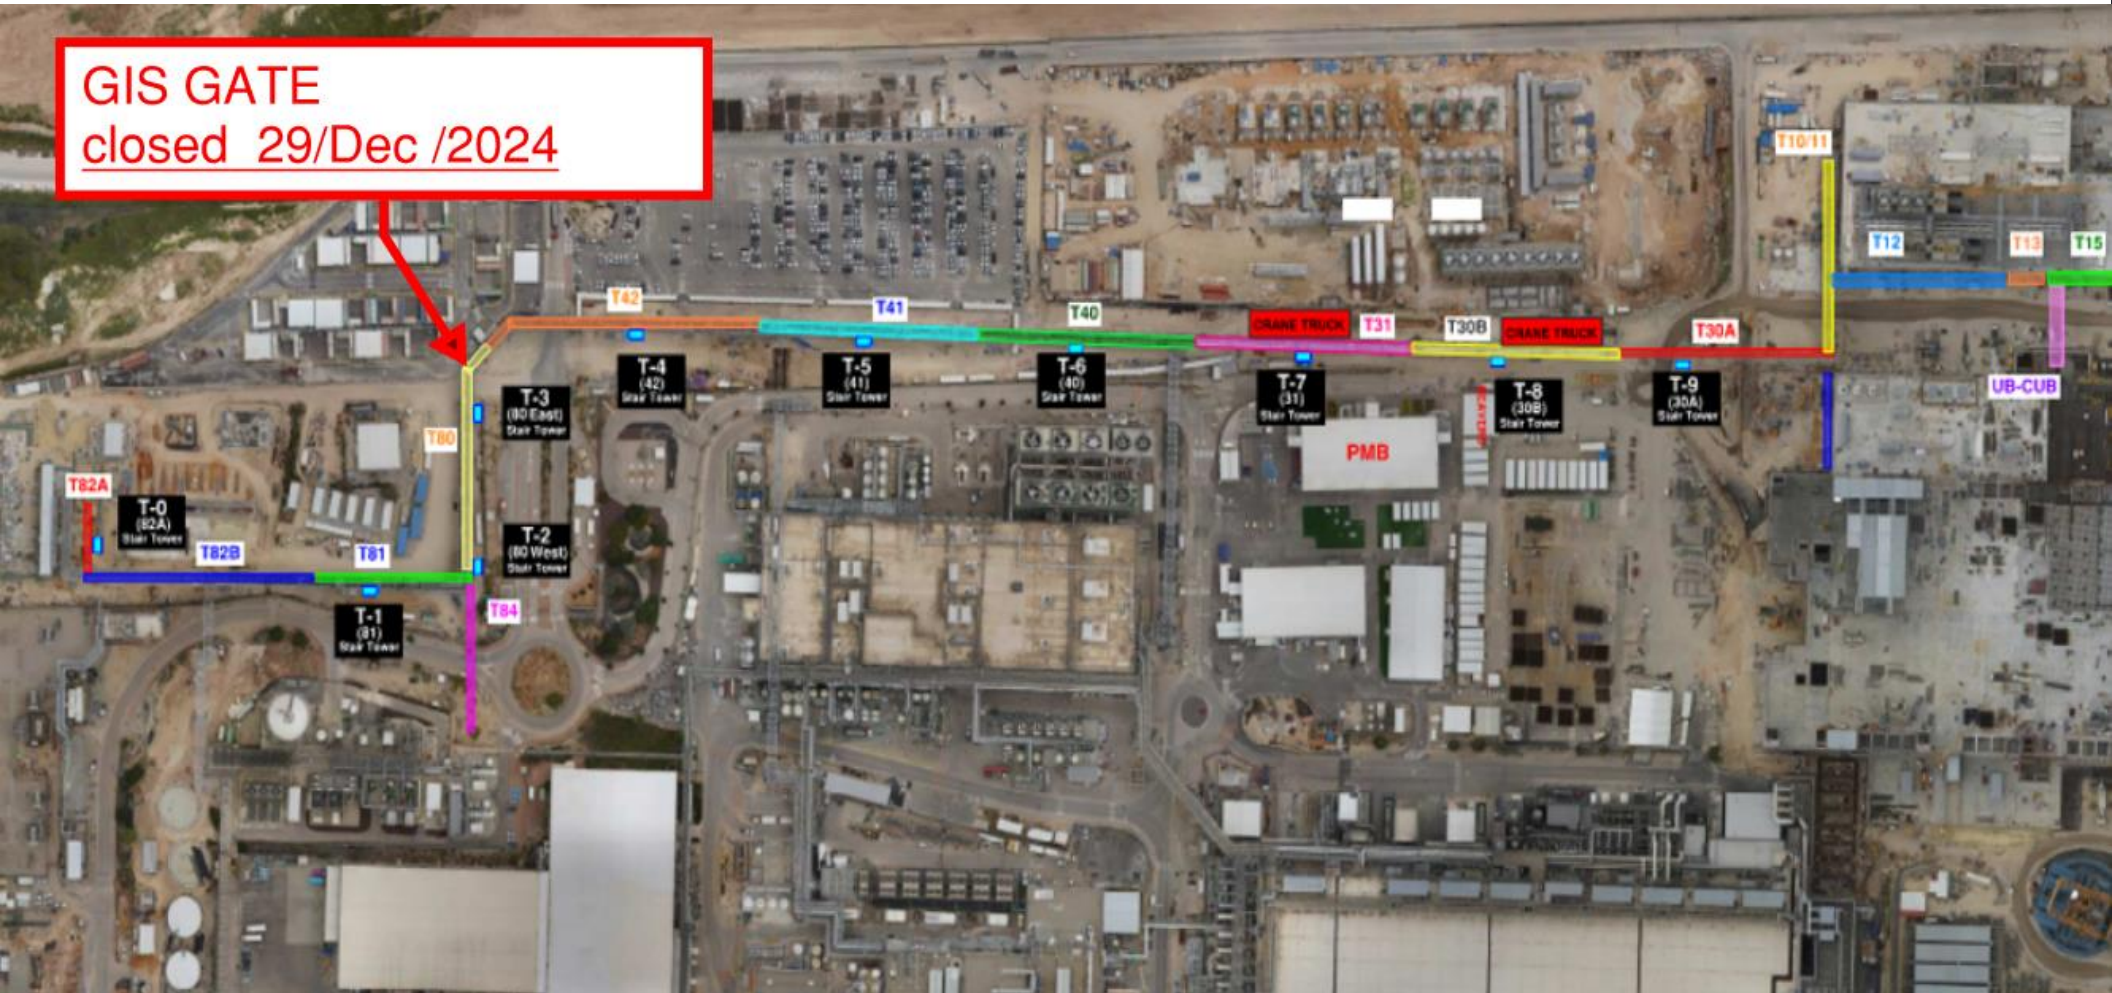

SUT

UB CUB - STAIRCASE DISMA

24/12/2024

CU

BGC - NDT

Starting -Monday December 23rd night at 19:00
Finish Tuesday December 24th at 05:00am.

Starting -Tuesday December 24th at 19:00
Finish Wednesday December 25th at 05:00am


Starting -Wednesday December 25th at 19:00
Finish Thursday December 26th at 05:00am


No impact on PMB
entrance\Exit

Safety spotter

Safety spotter

Safety spotter

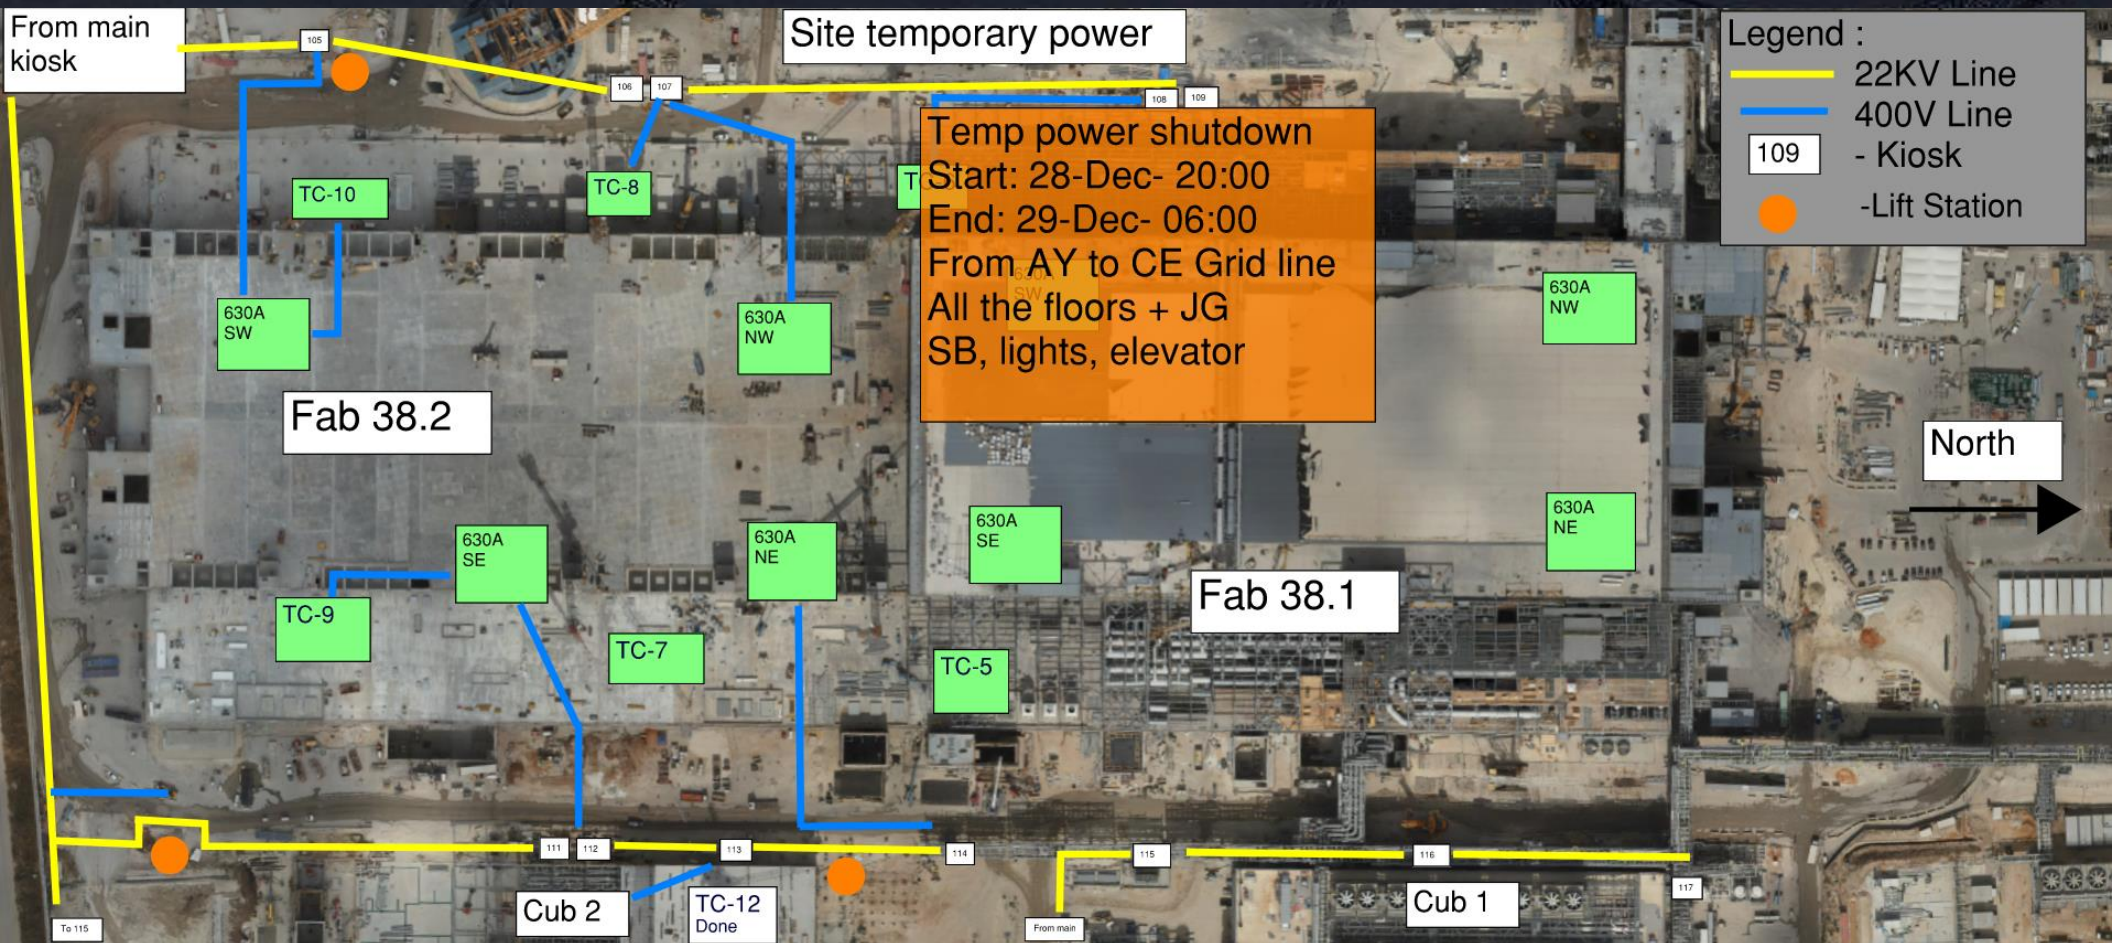

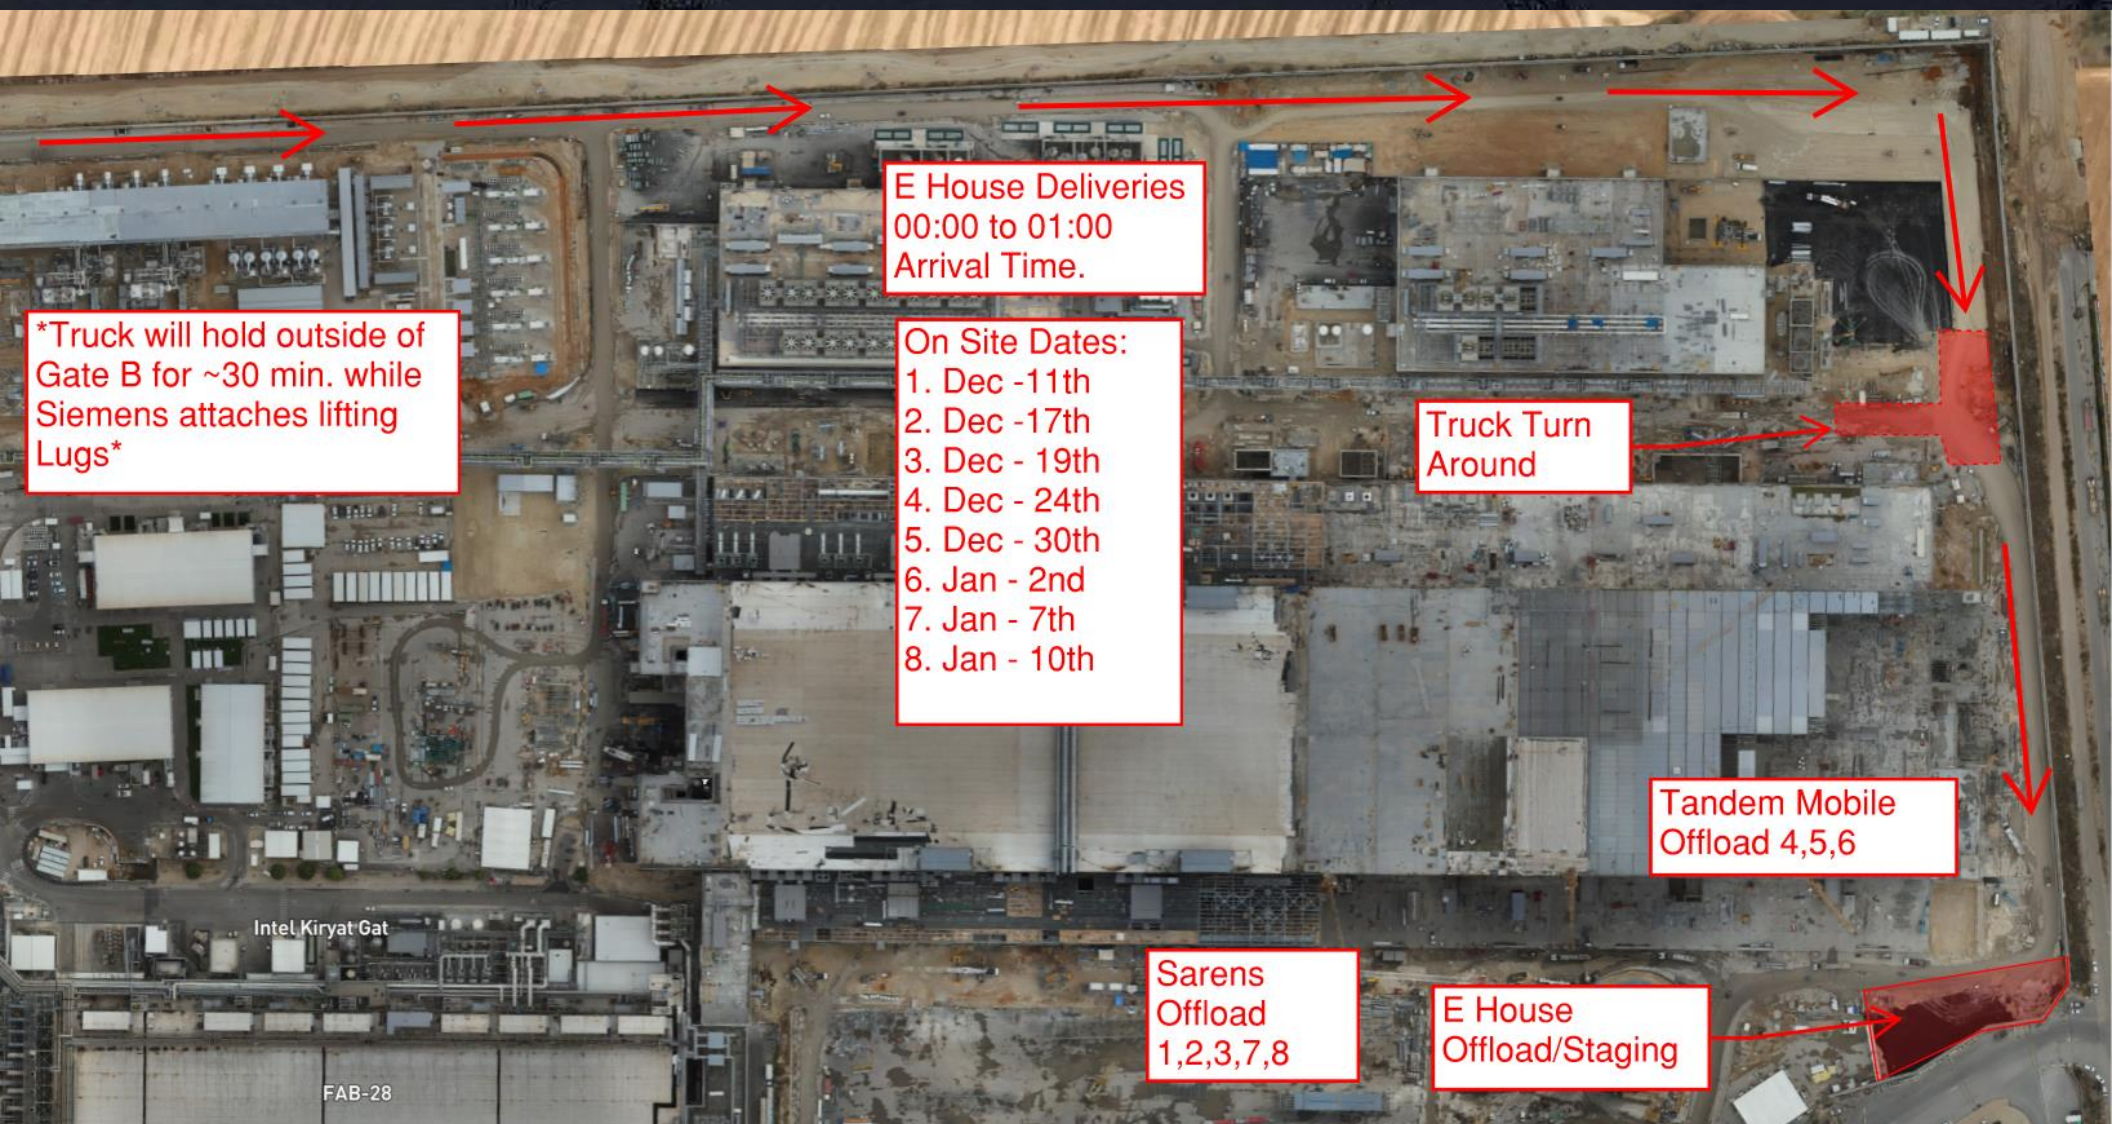

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:

1. Dec -11th
2. Dec -17th
3. Dec -19th
4. Dec -24th
5. Dec -30th
6. Jan -2nd
7. Jan -7th
8. Jan -10th

*Truck will hold outside of
Gate B for ~30 min. while
Siemens attaches lifting
Lugs*

Truck Turn
Around

Tandem Mobile
Offload 4,5,6

Sarens
Offload
1,2,3,7,8

E House
Offload/Staging

Intel Kiryat Gat

FAB-28



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
North






Daily Coordination Meeting

Site Logistics

East CUB1 Road Closure

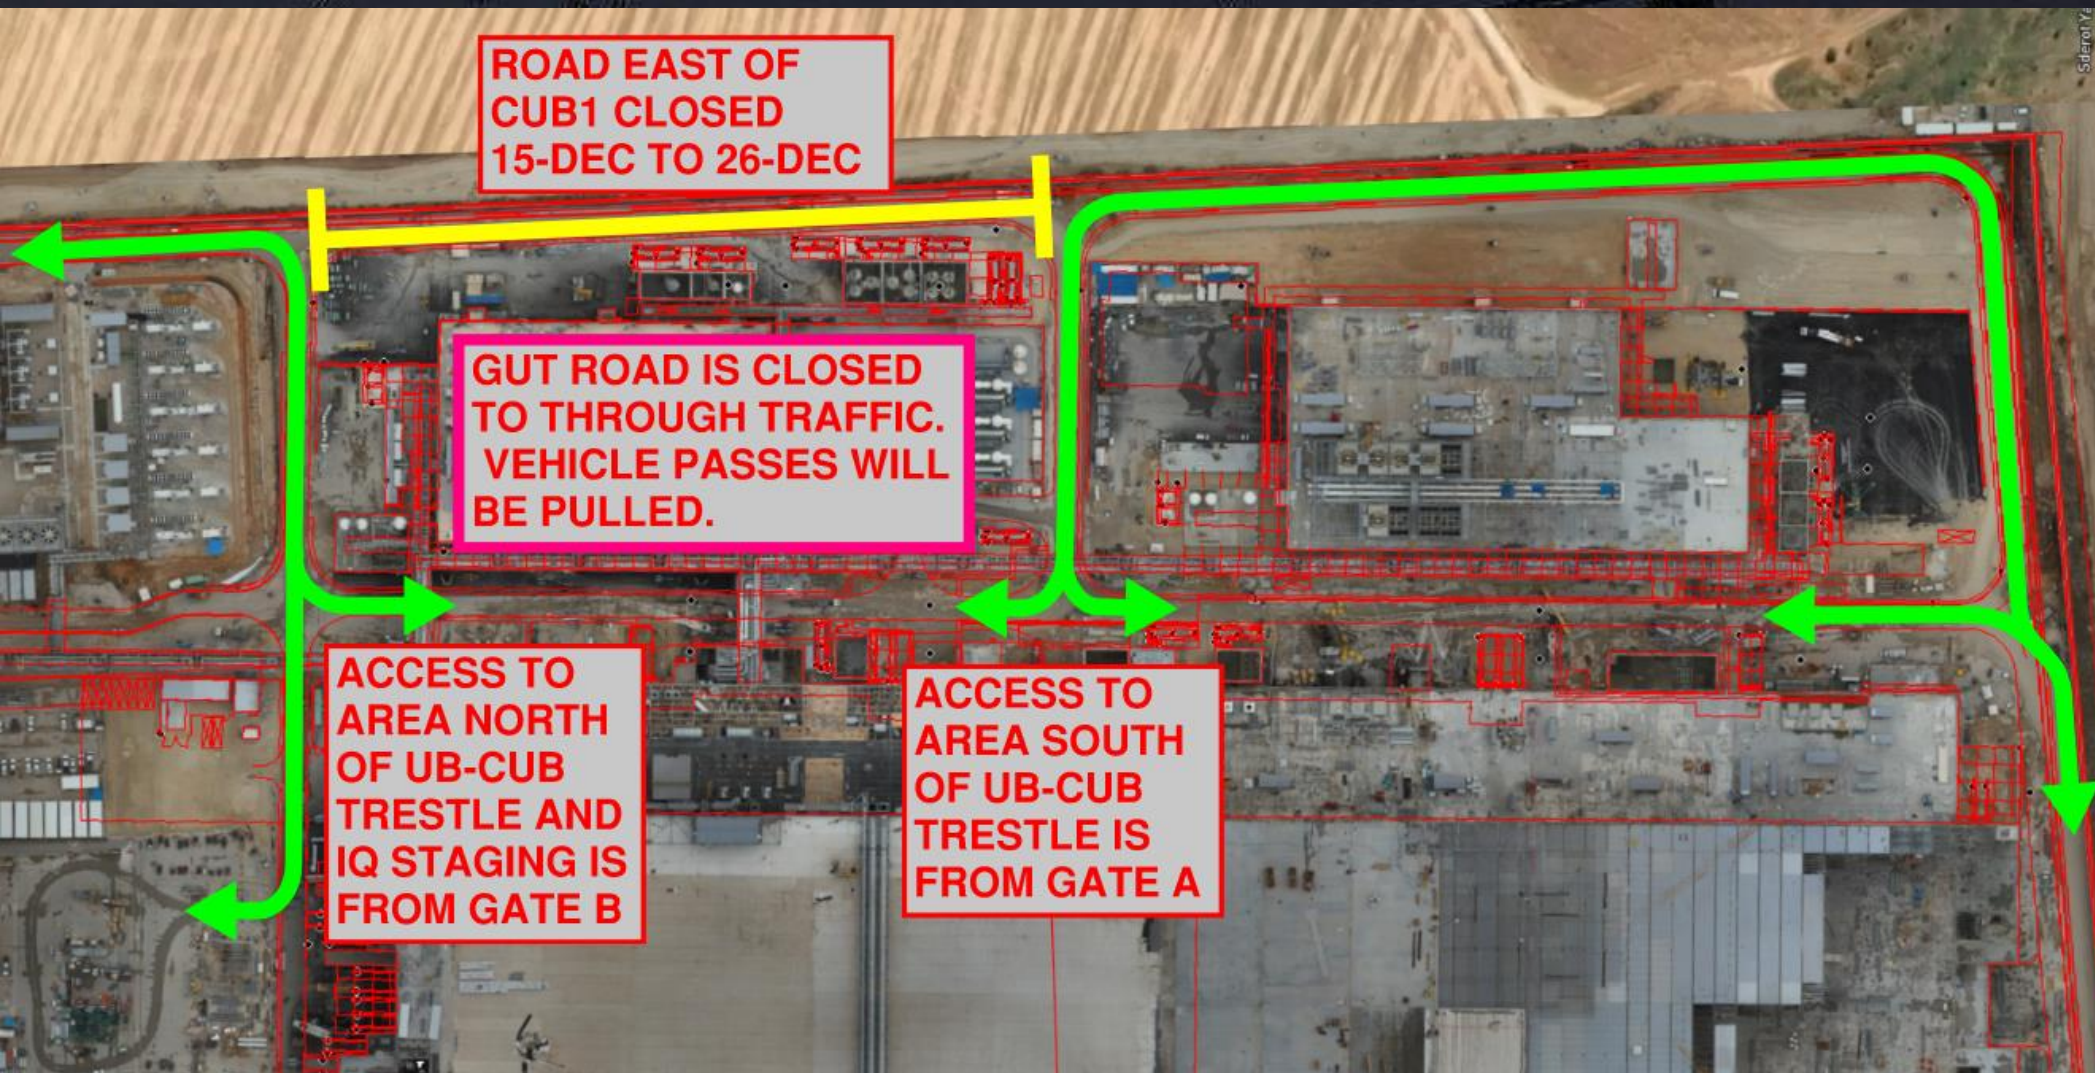

Daily Coordination Meeting

Site Logistics
South



Access Hazards

- If you create an access hazard, you must physically protect people from hurting themselves.
- This includes hazards from; falls, open holes, trips, overhead obstructions, etc.
- Do not just put red rope up and hope for the best. Additional reminder that you cannot leave red rope up over night.
- We had 2 people injured last week after steps were removed from a stair and the people stepped through the hole.
- We cannot leave access hazards that are not physically guarded.

Daily Coordination Meeting



14:00 Sign In
