

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:





UTILITY LEVEL MOD1

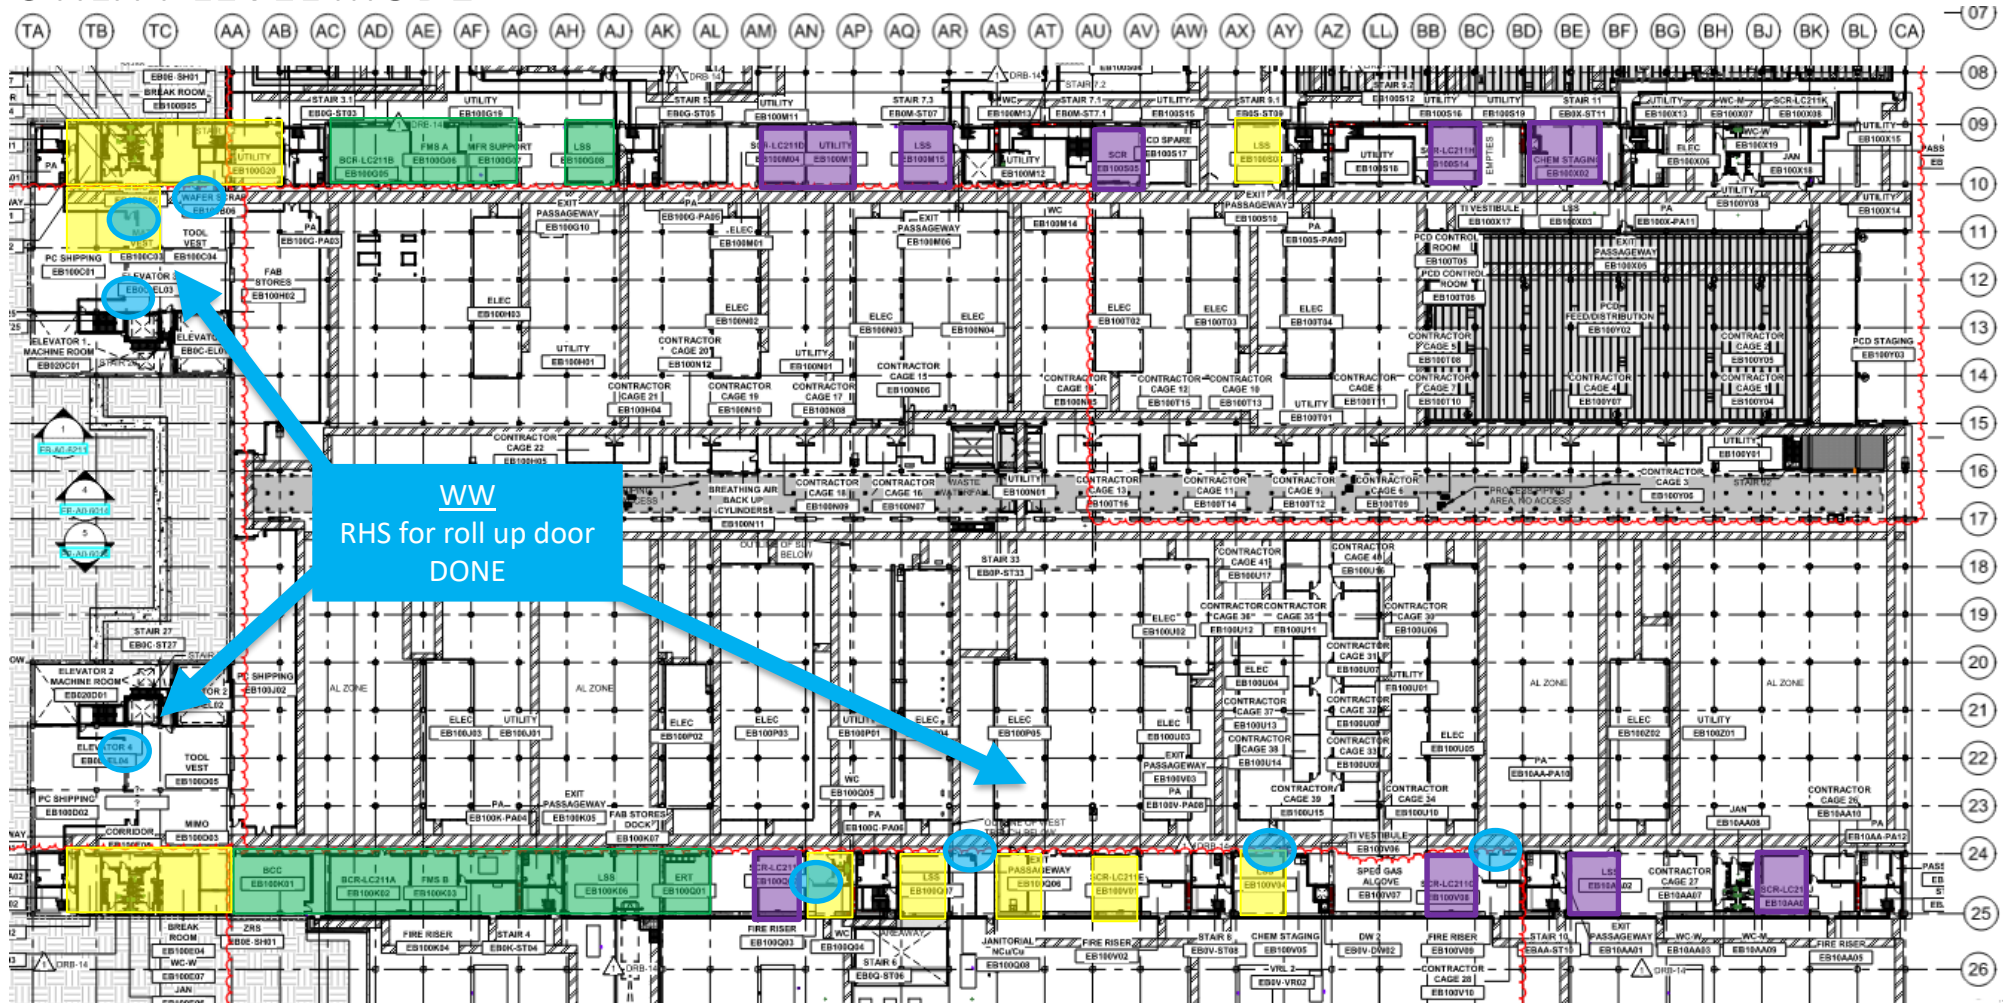


BELFOR
Mold remediation

ELRAM
Drywall install


MEP+Electrical
Ready for re-install

UTILITY LEVEL MOD2

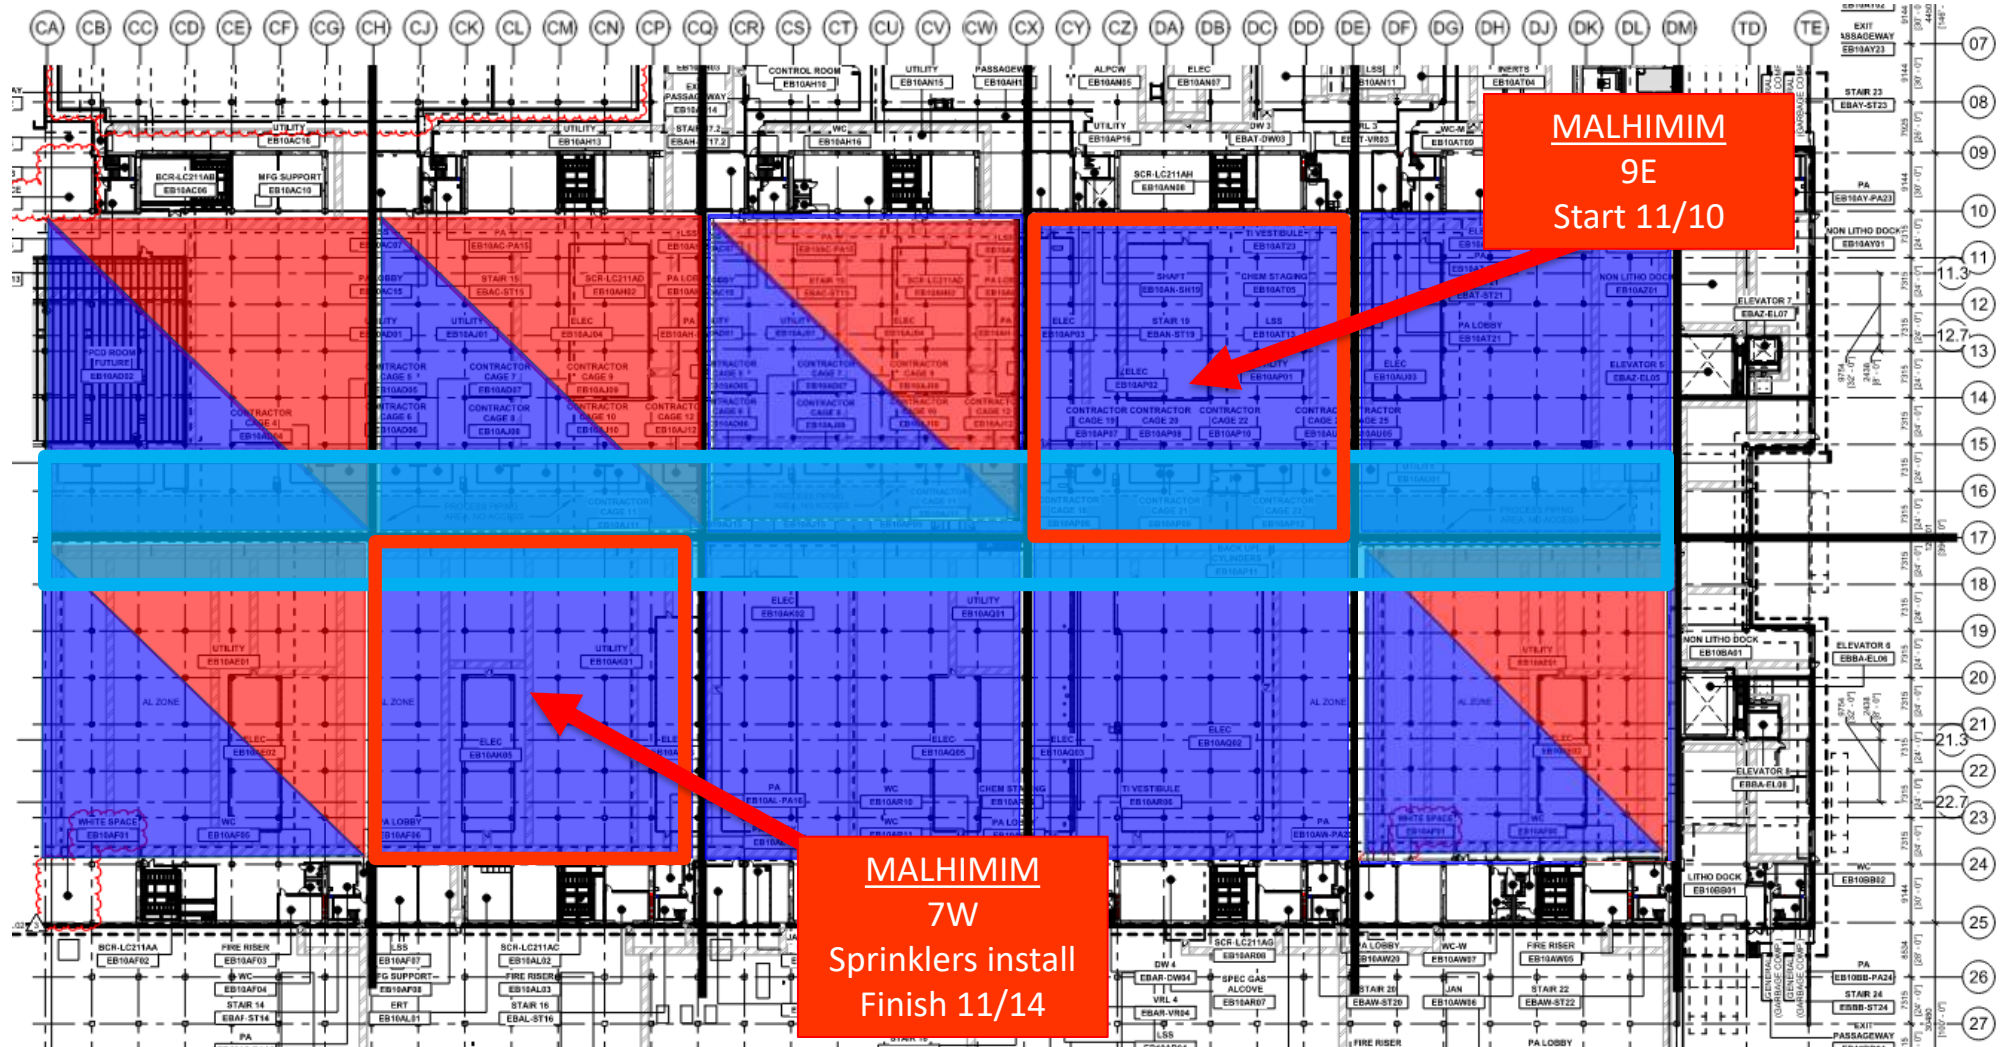





SUT 38.1 LEVEL

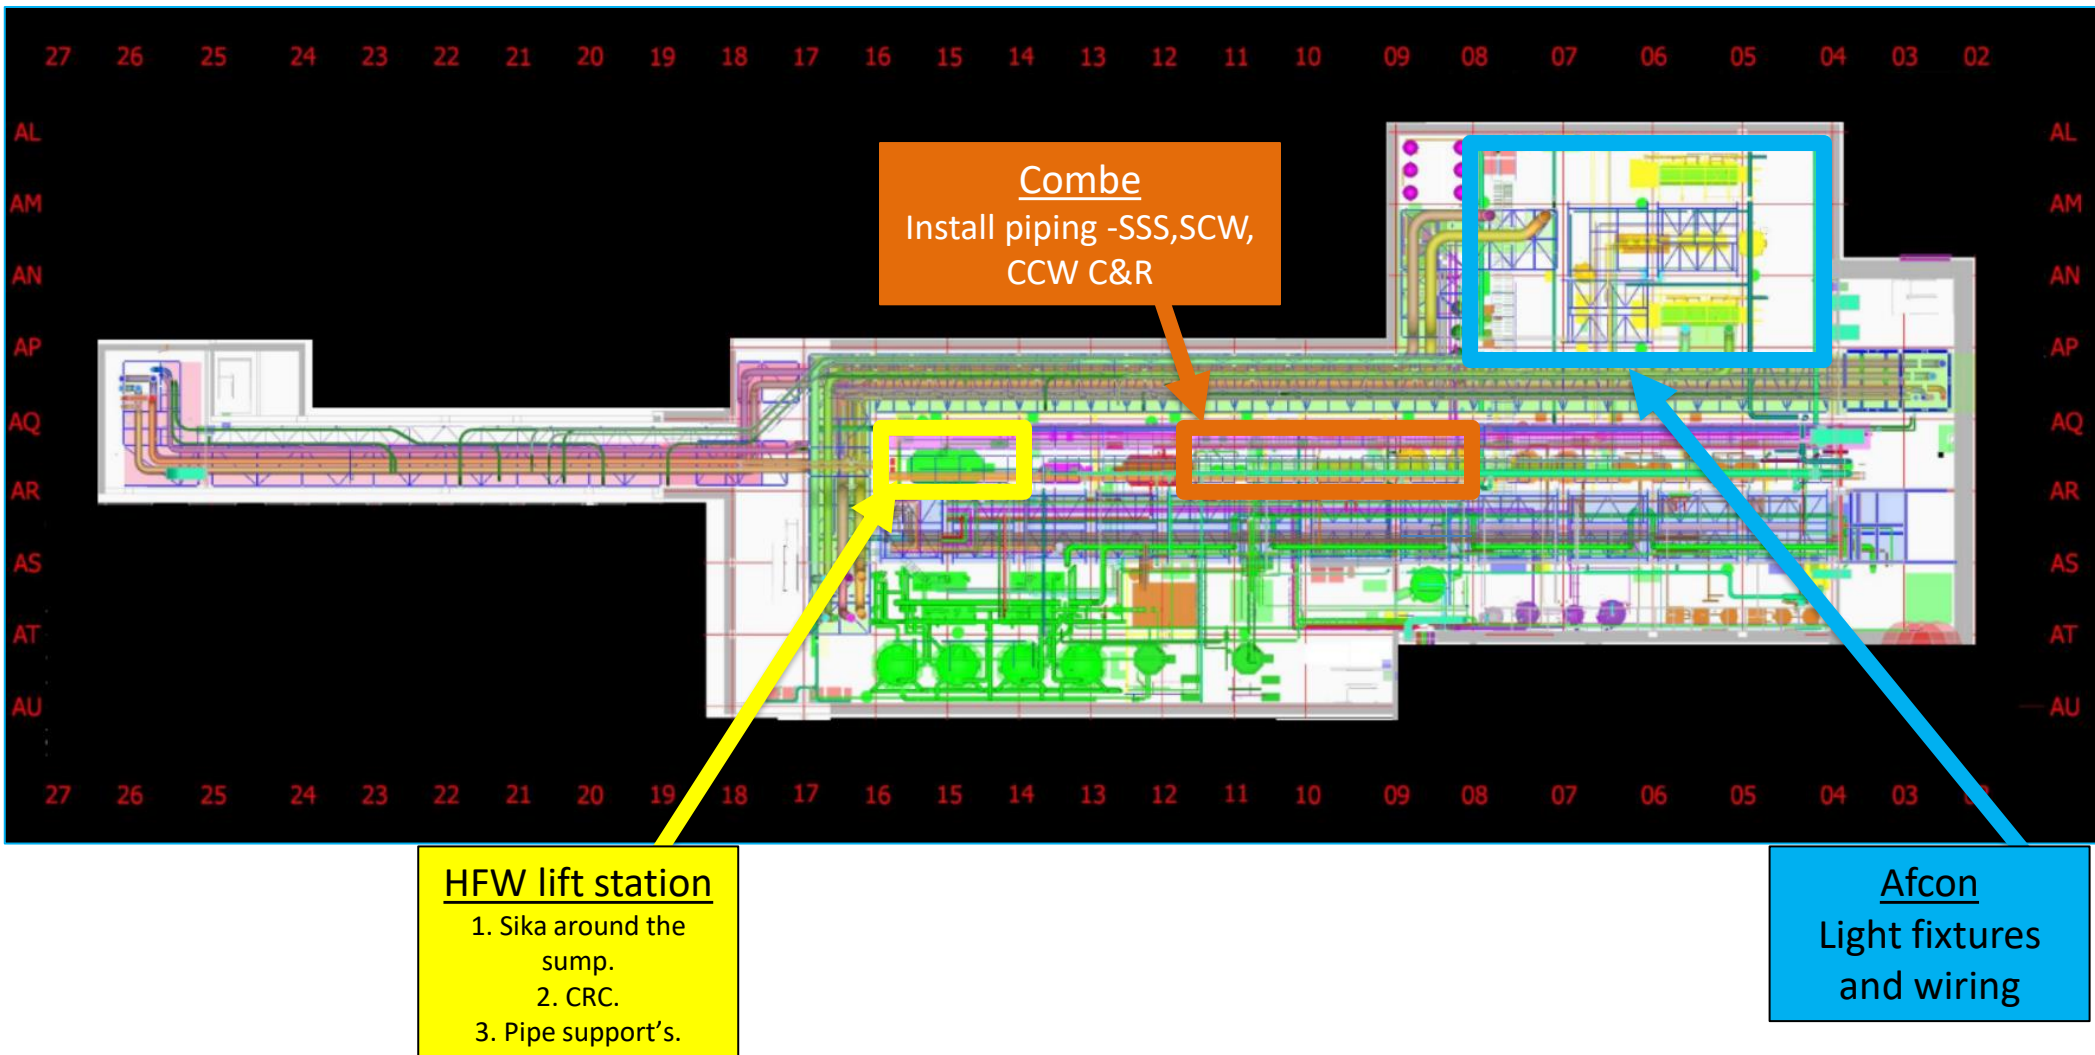


SUT 38.2 LEVEL

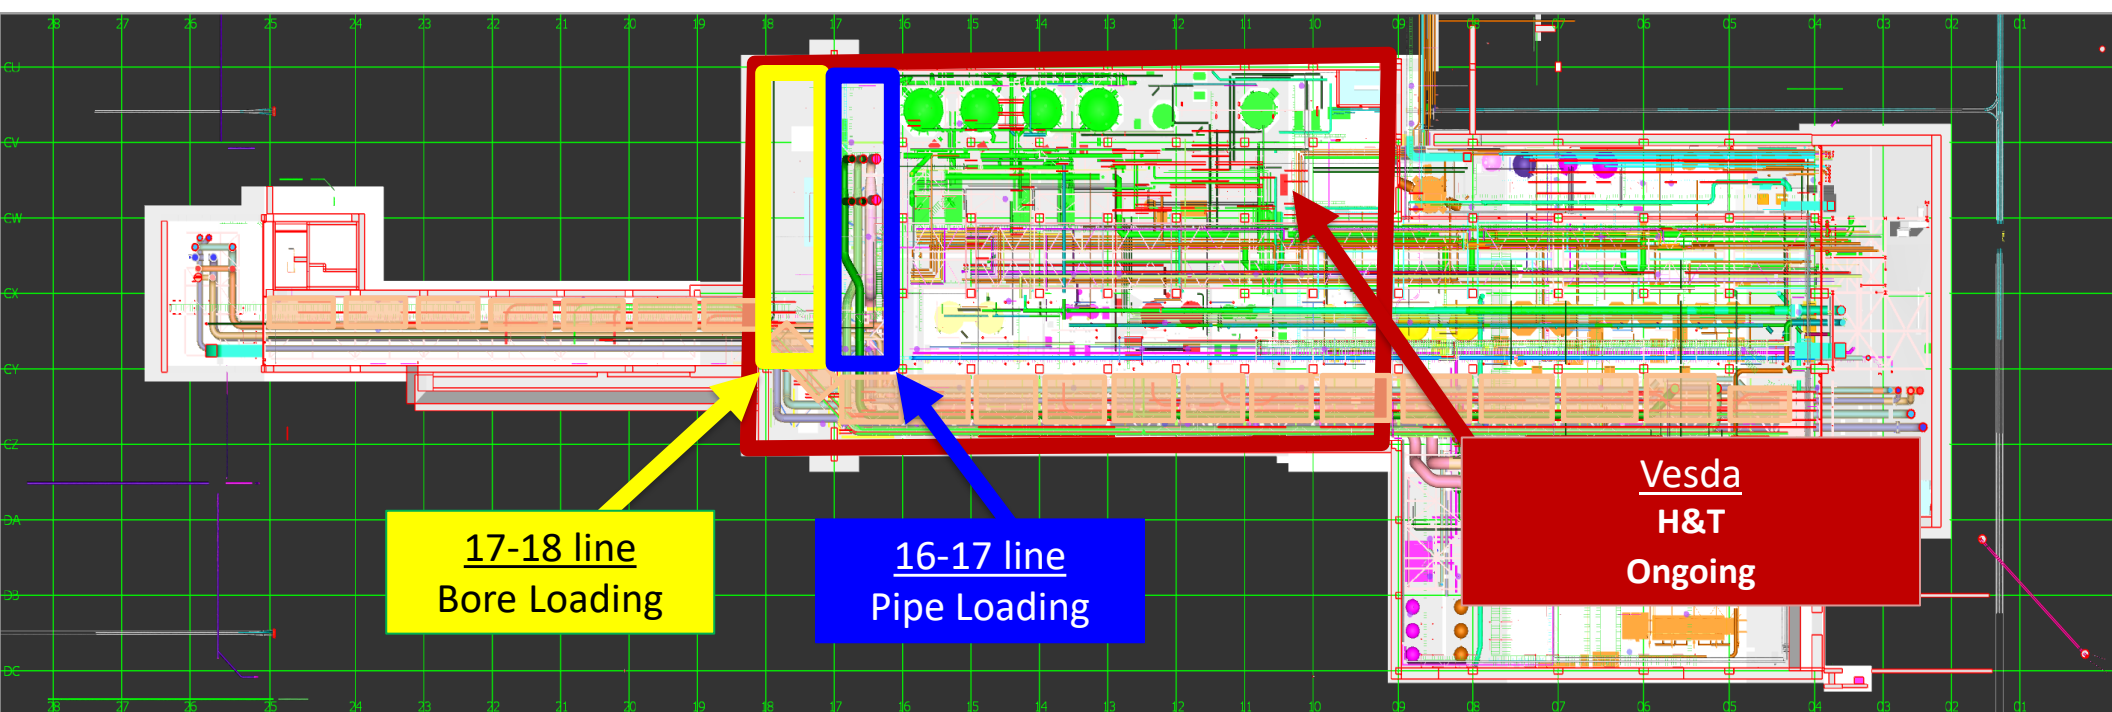


SUBFAB BUILDOUT MOD 1

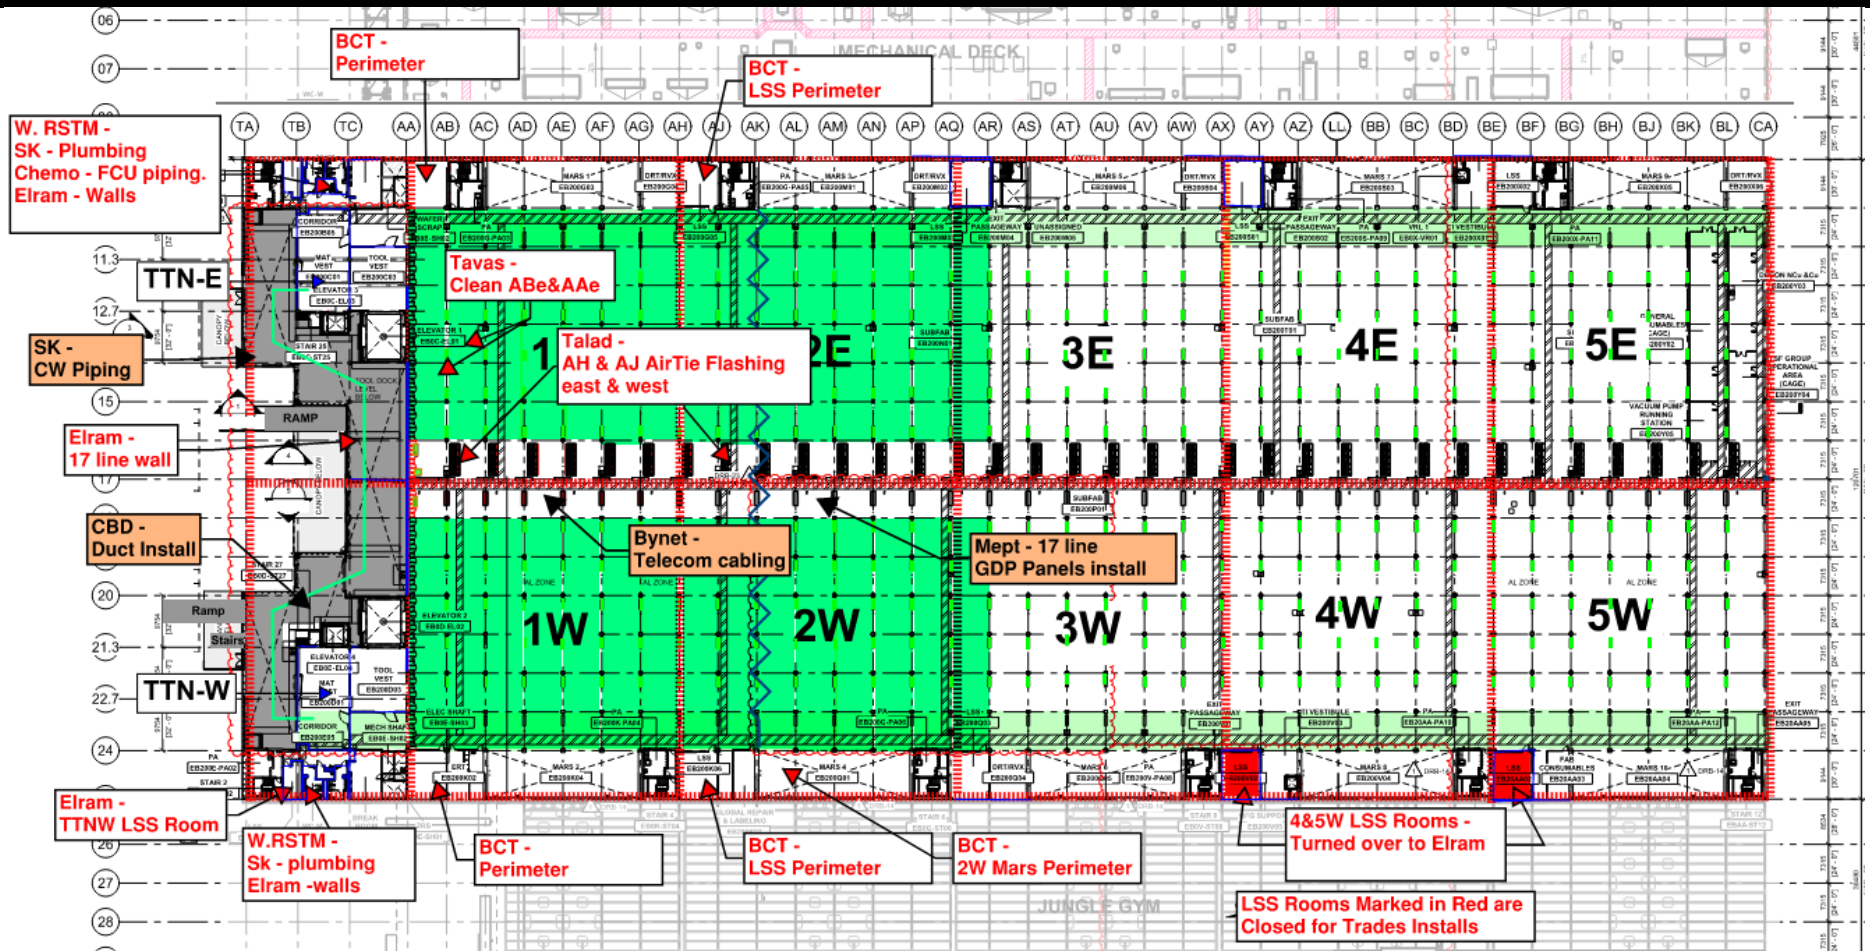


SUBFAB CRC TOPCOAT

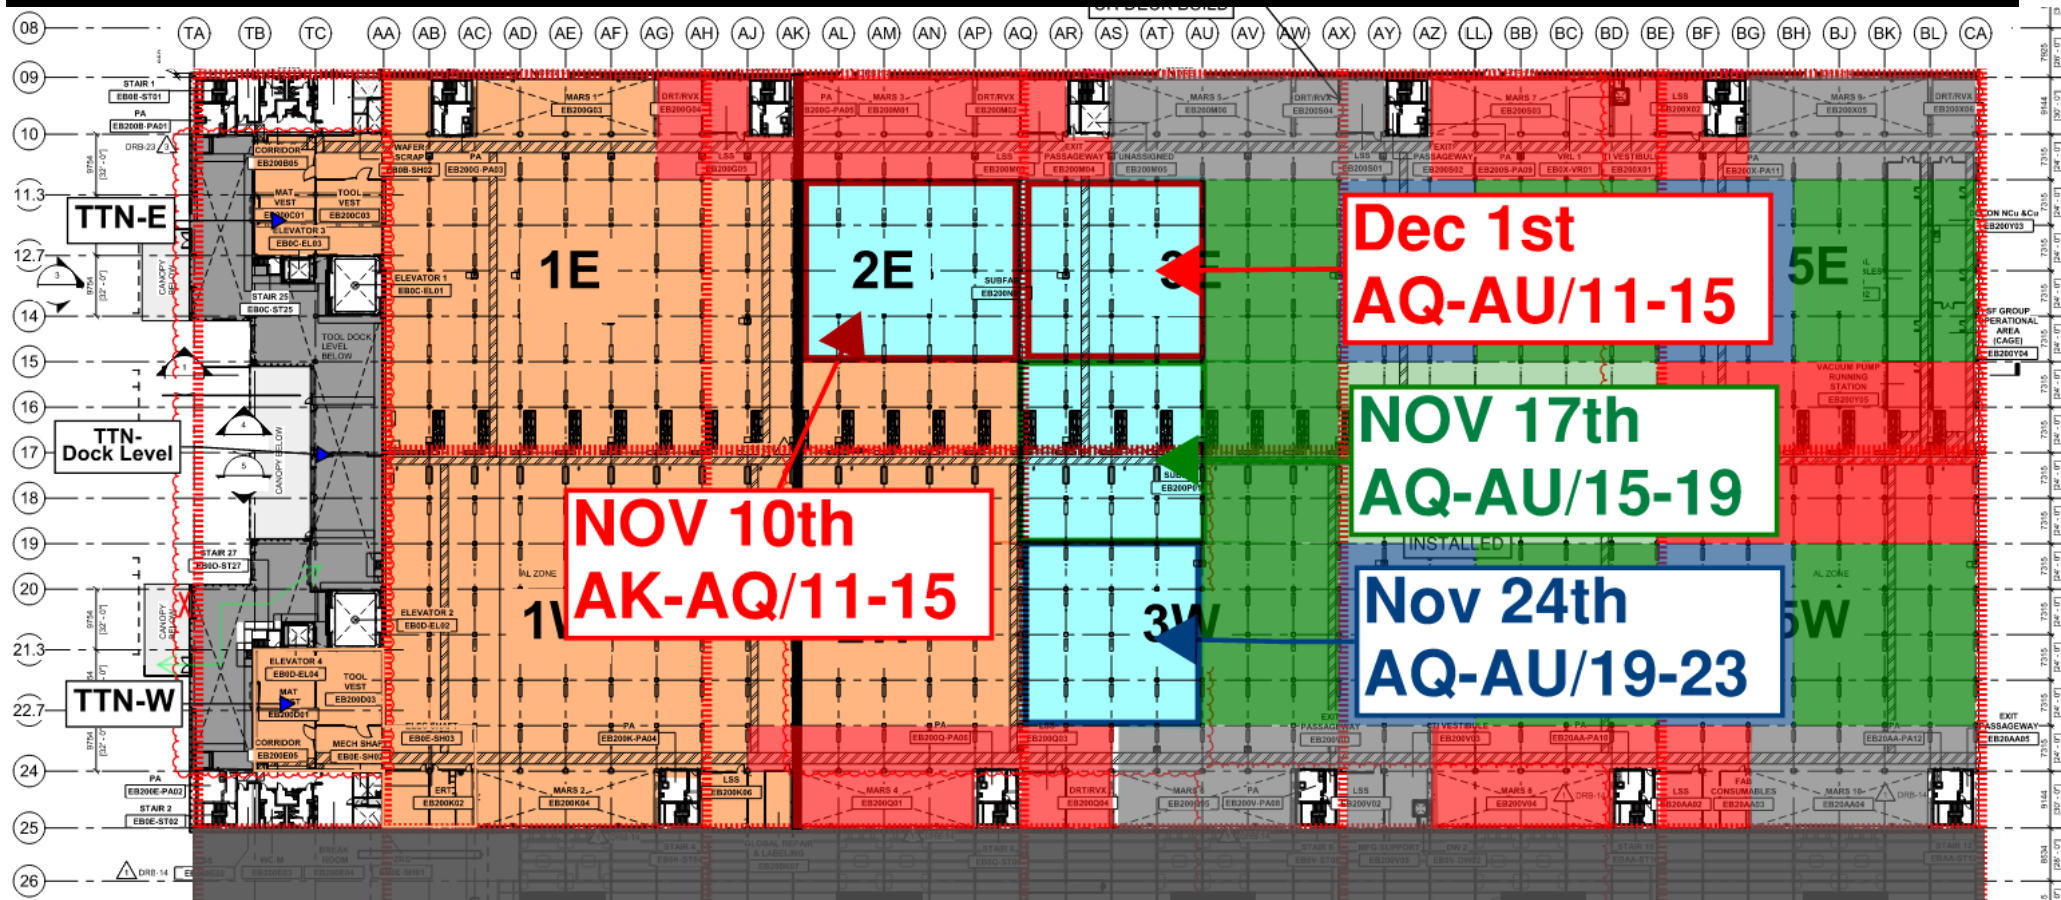

BCT Pressure Test Sunday

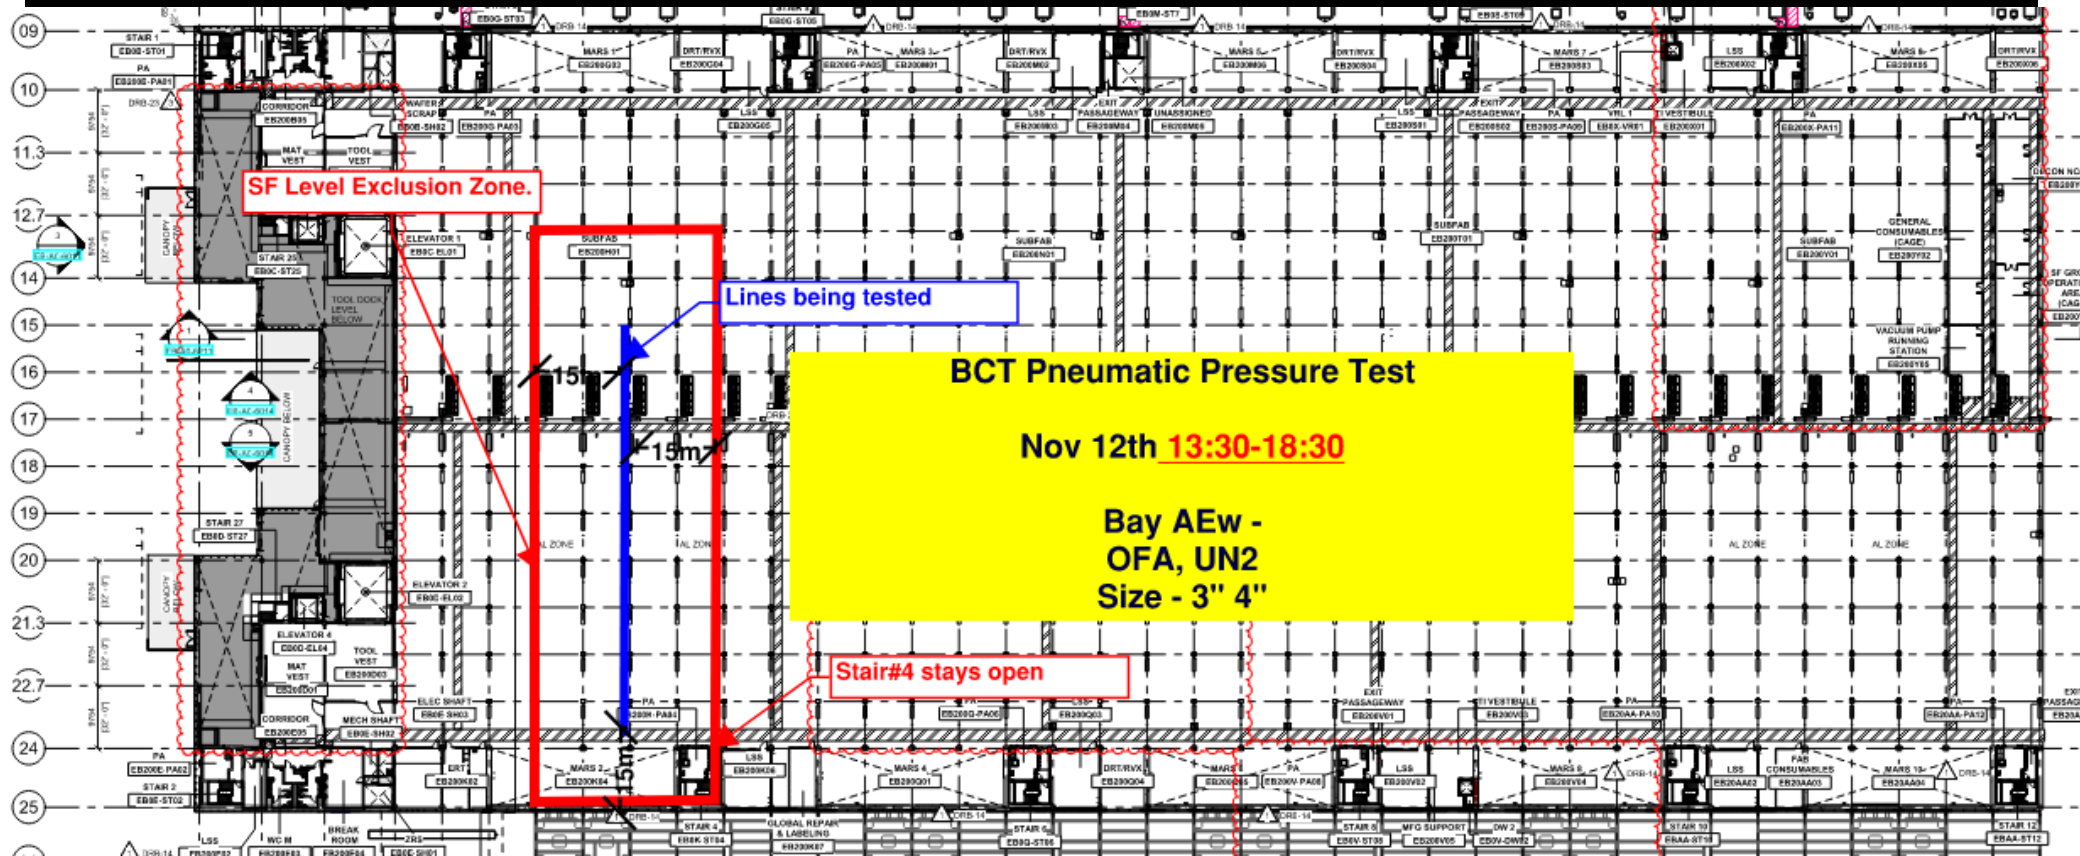


SUBFAB BUILDOUT MOD 2

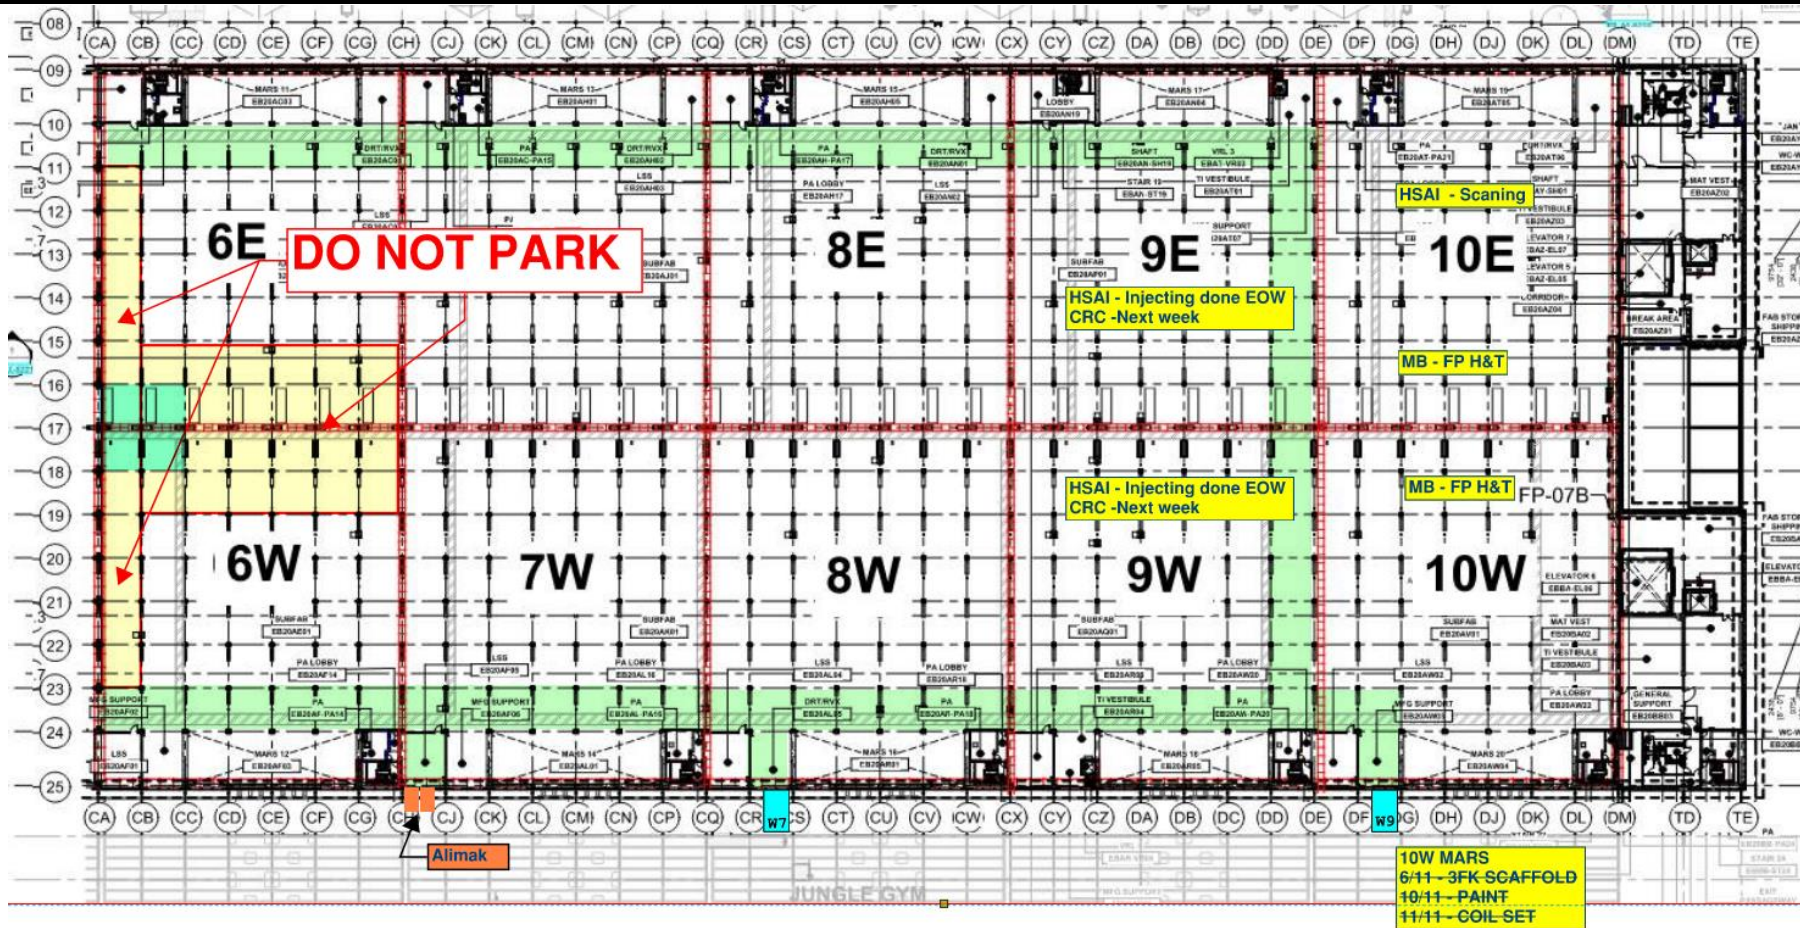







CR level:


-  Afcon - Cable trays, modules and stickers
-  MB - Pipes and drops
-  Elram - 9-10,24-25 columns/shaft walls. AA line column wraps
-  Meptagon - EMT Pipes+devices. TET/NET devices all areas
-  Meptagon - I&C 2W
-  D&P - Rods install. Blades waiting for survey
-  Tzur-esh - 5E blades. Paint rust on columns
-  HYG - Shaft beams install
-  PT - Duct prep for test AA-AH east
- Talad - 1W cutting around steel lids. UPN install

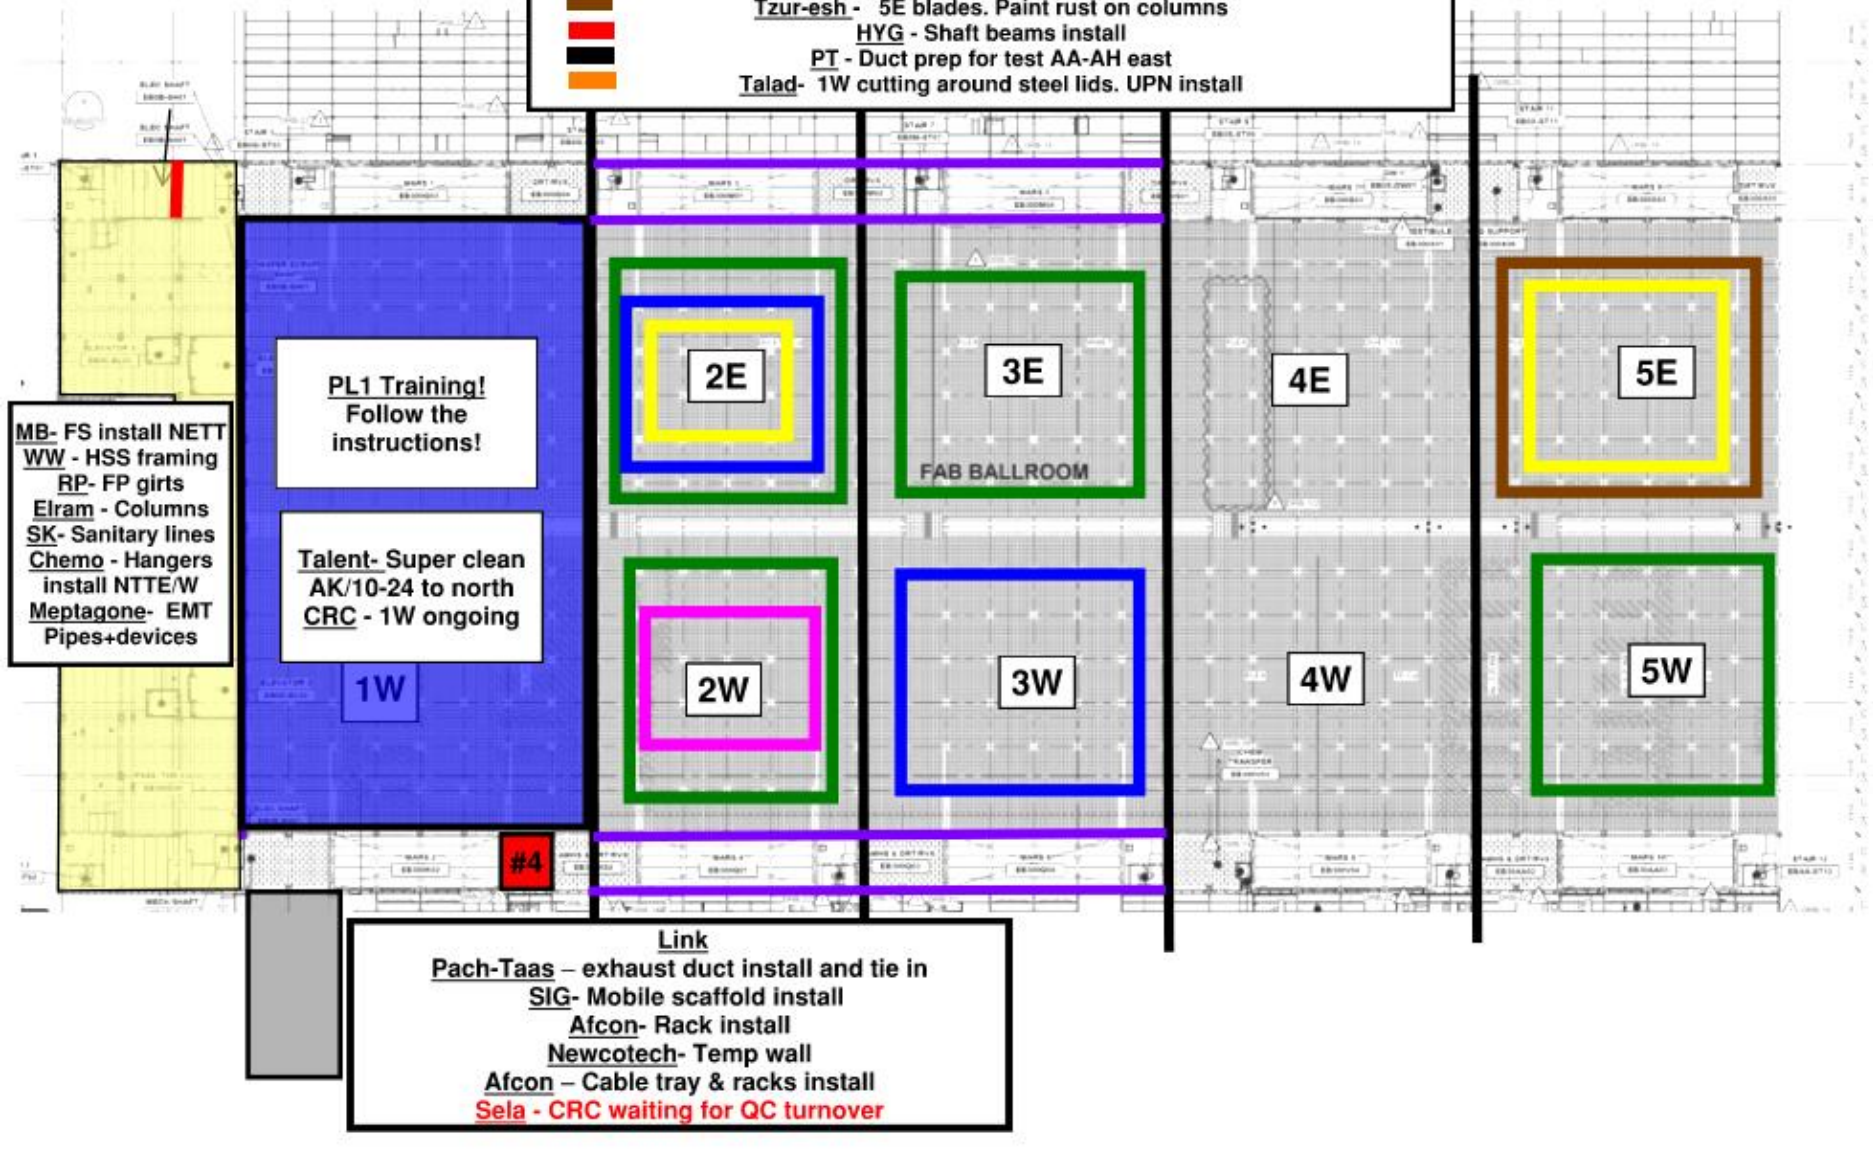

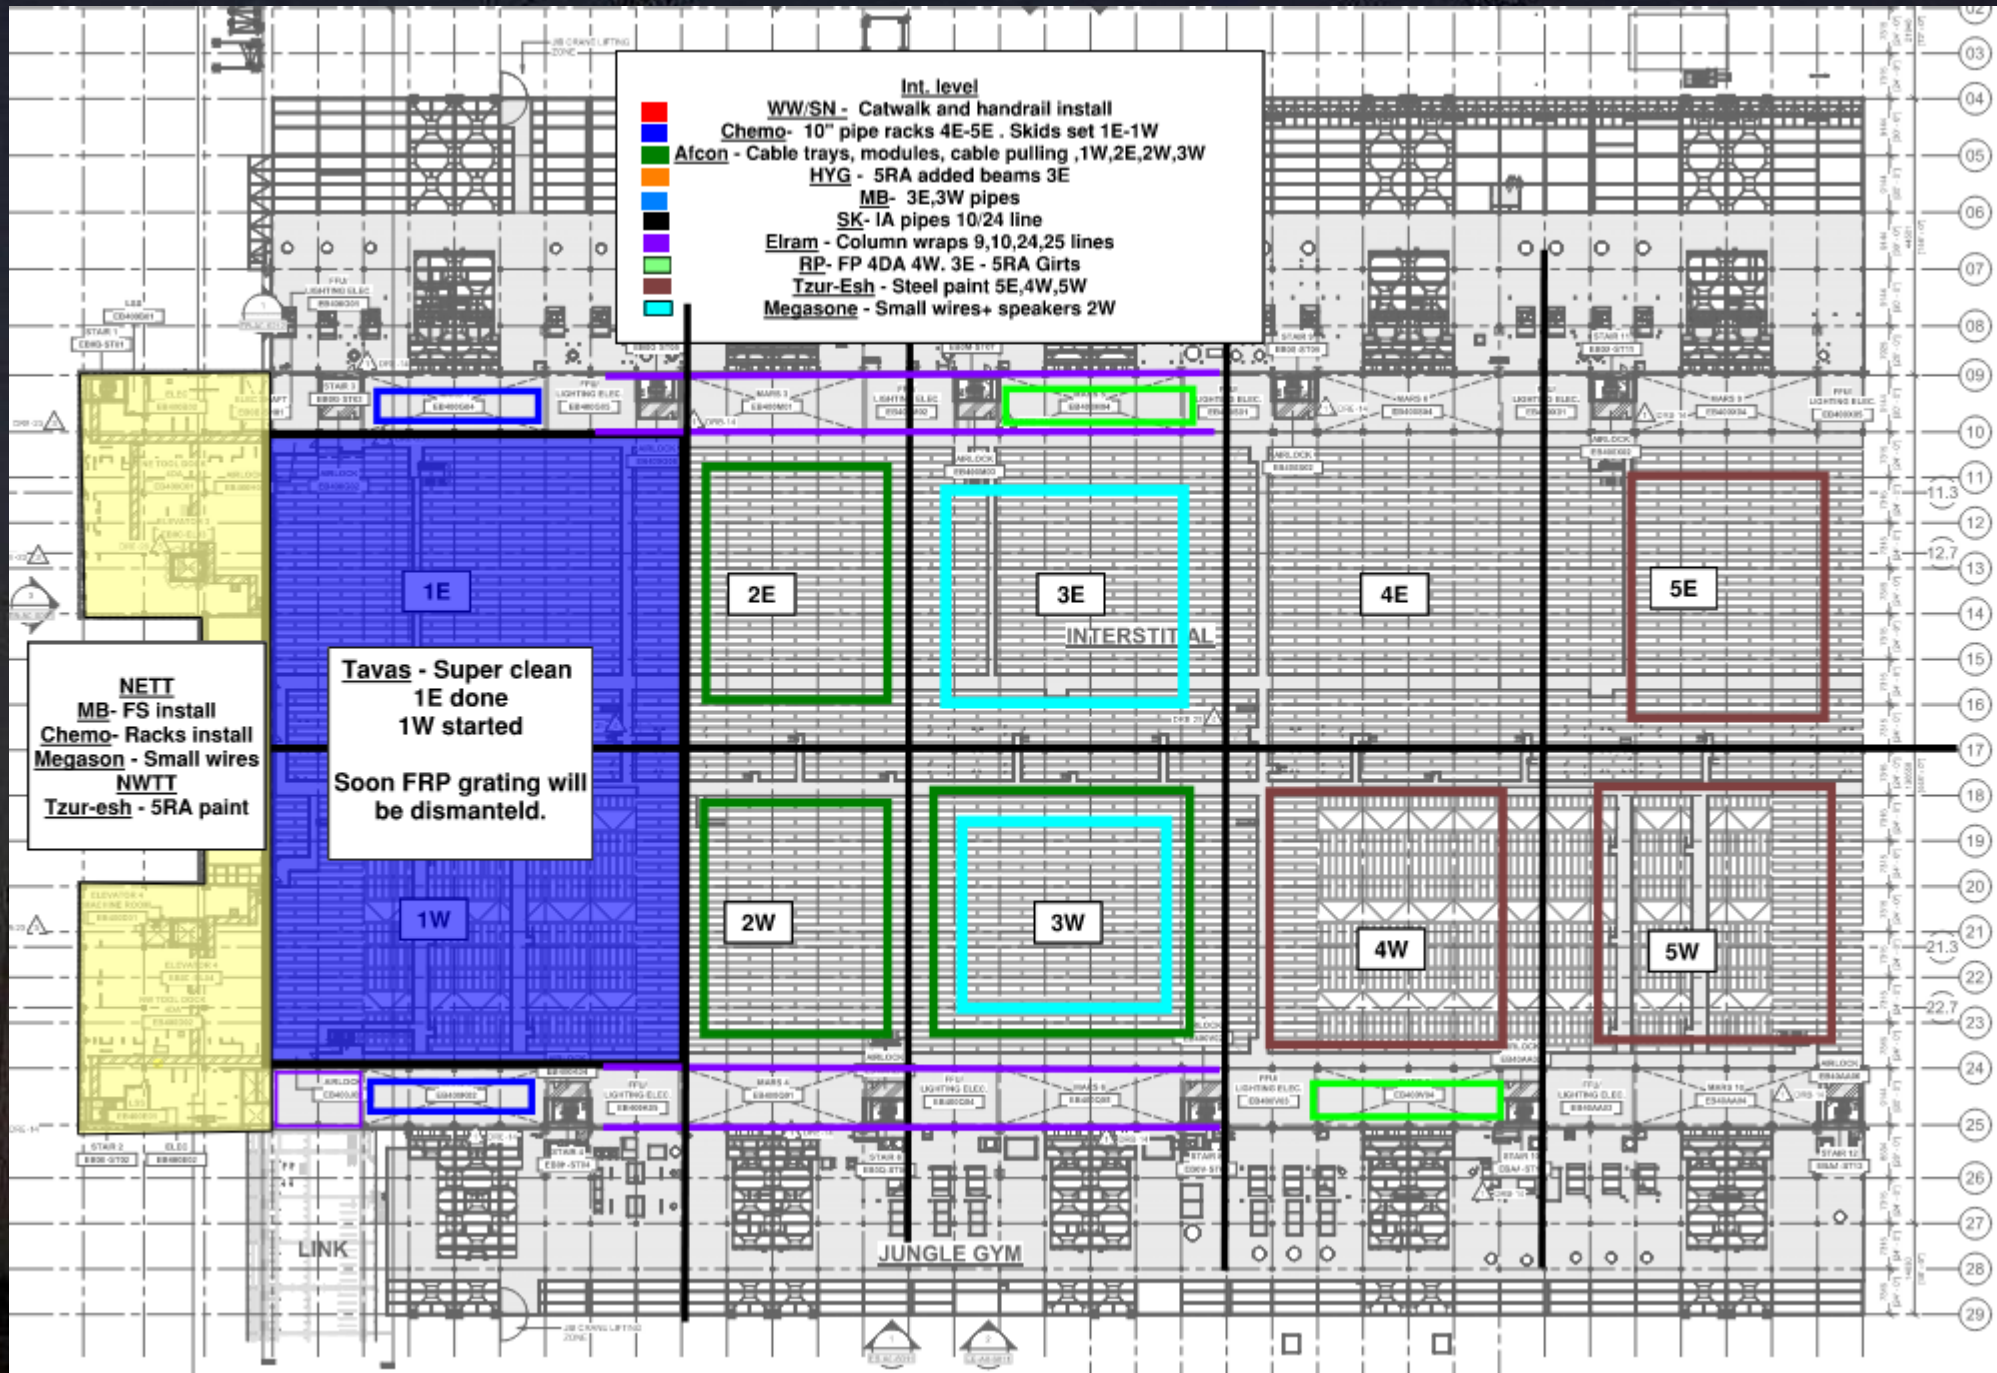

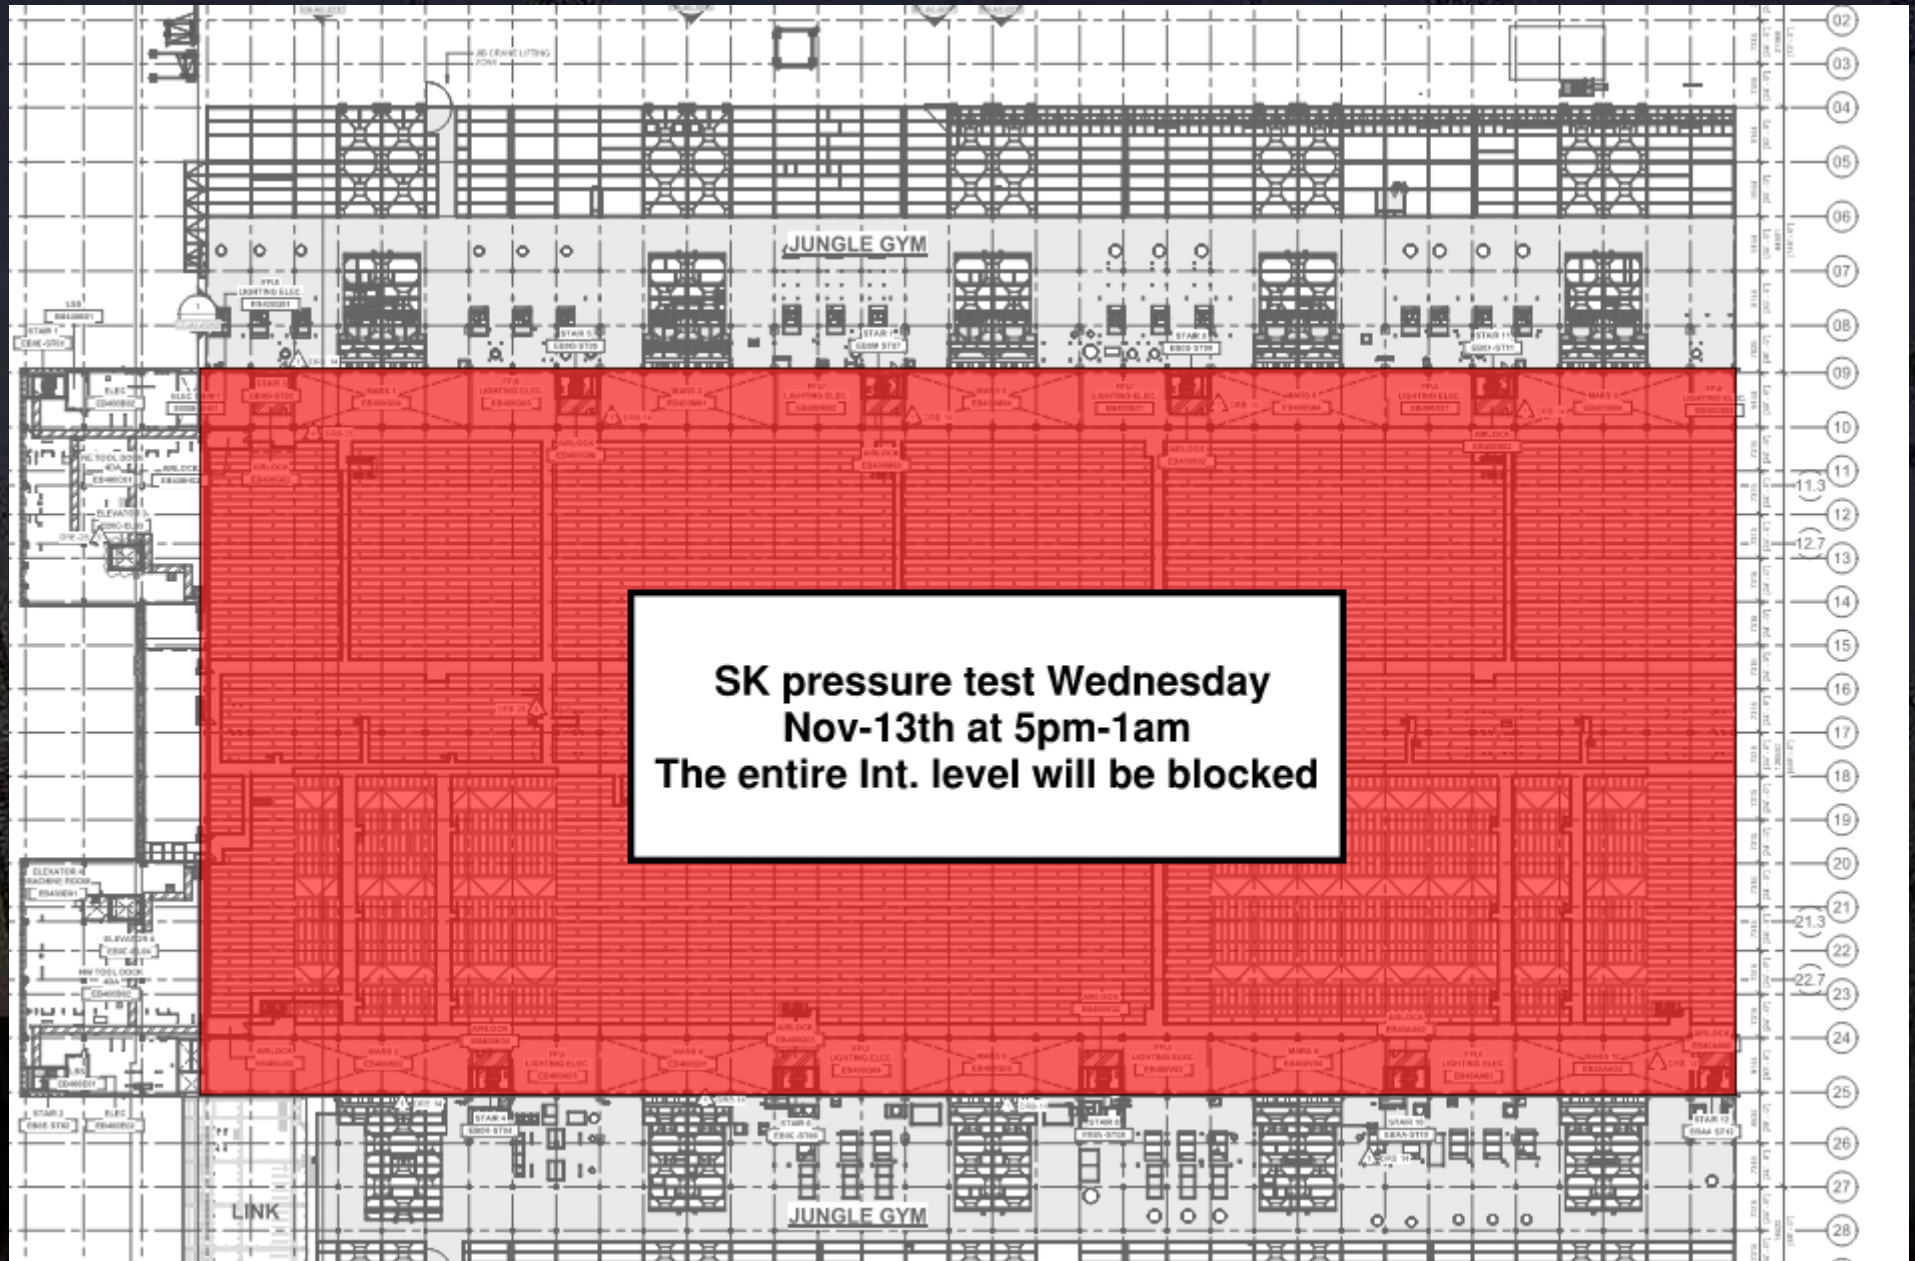

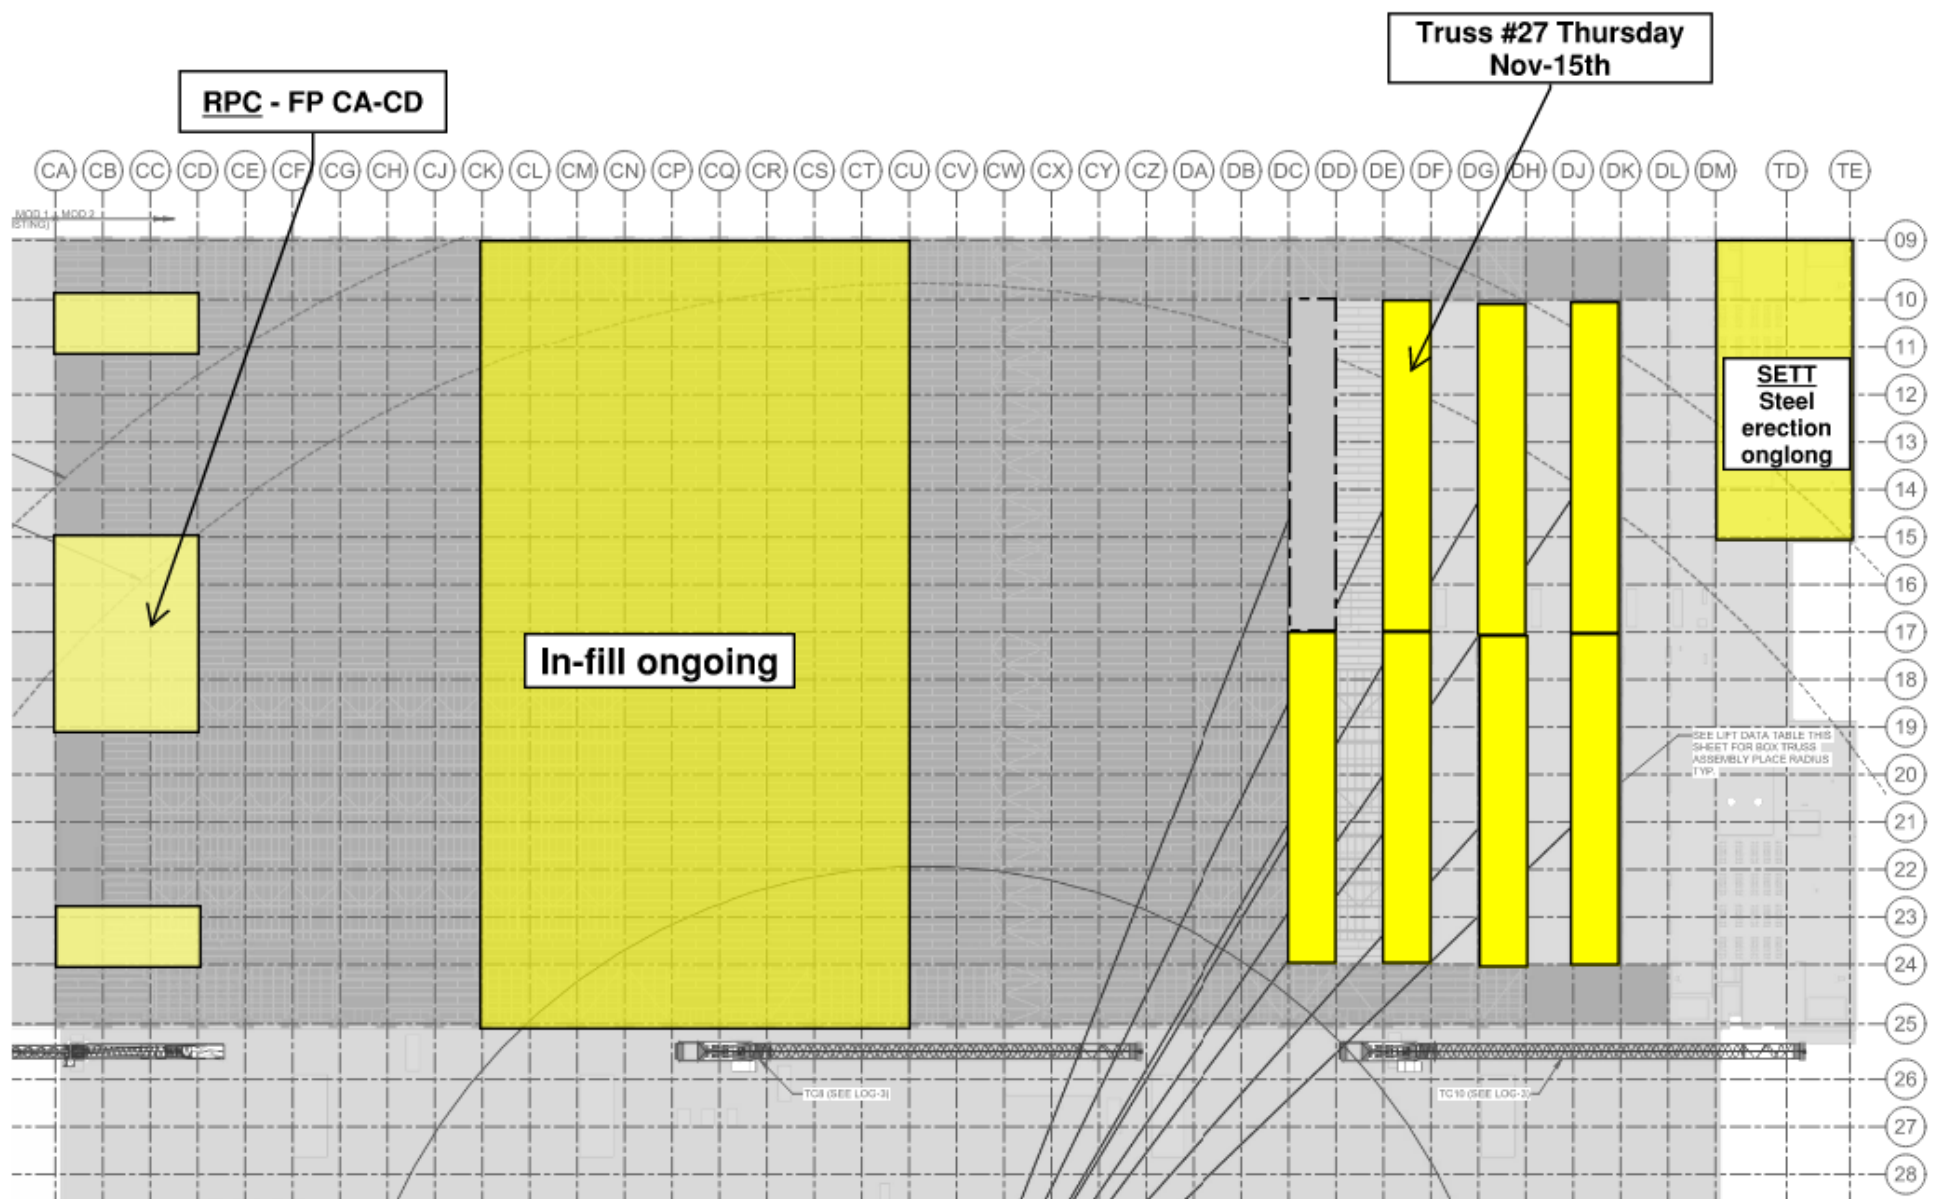





Clean Room Wall Of Shame

Trade damage

Afcon

D&P

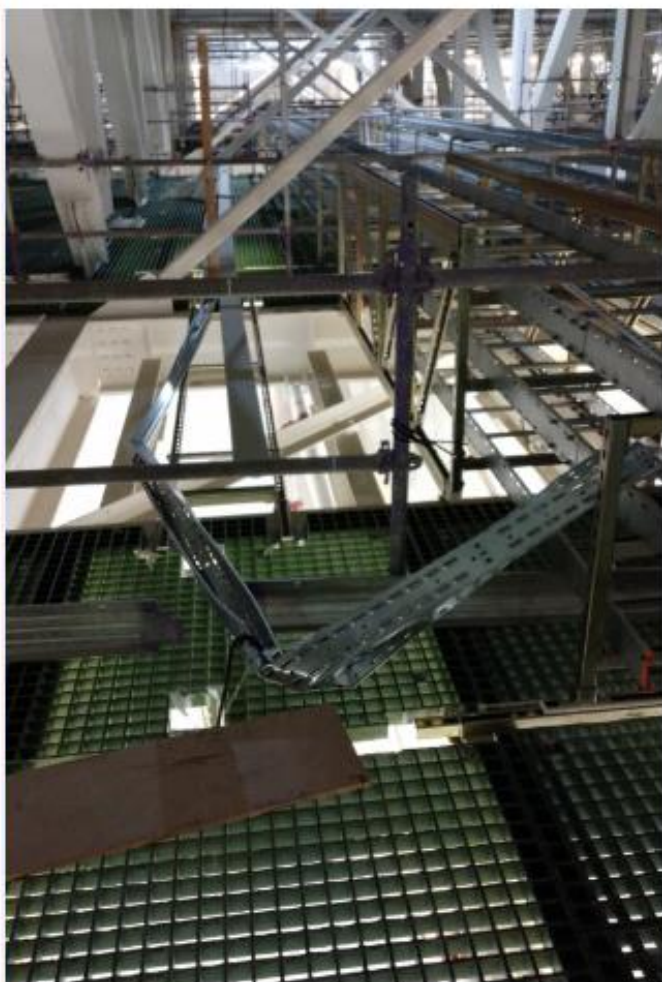

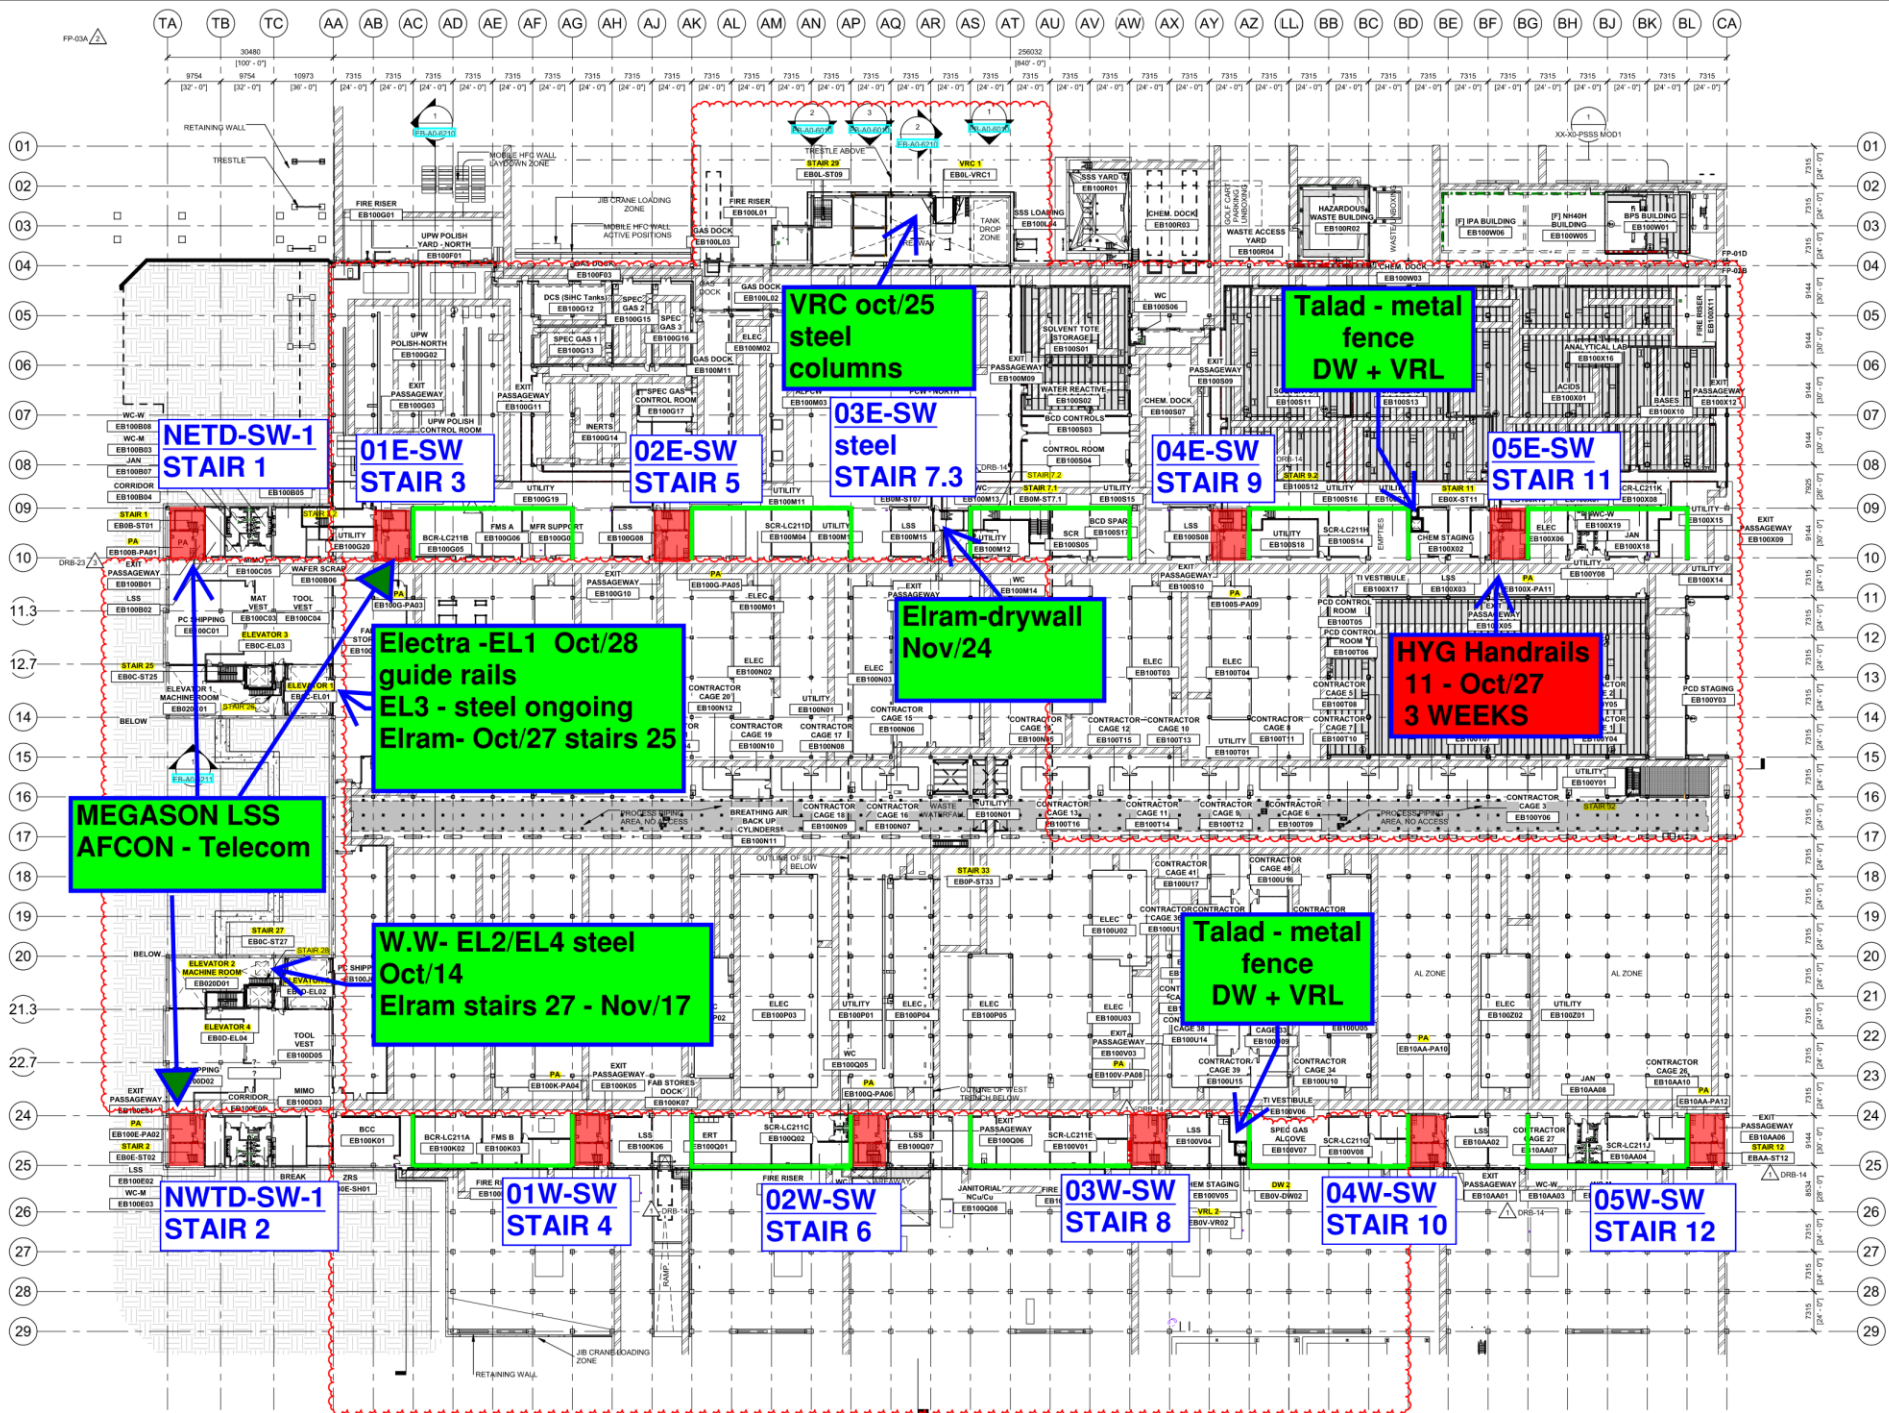


Siding - West FAB - JYG


BLOWDOWN 30%


[illegible]

Siding - East FAB - PSSS

[illegible]

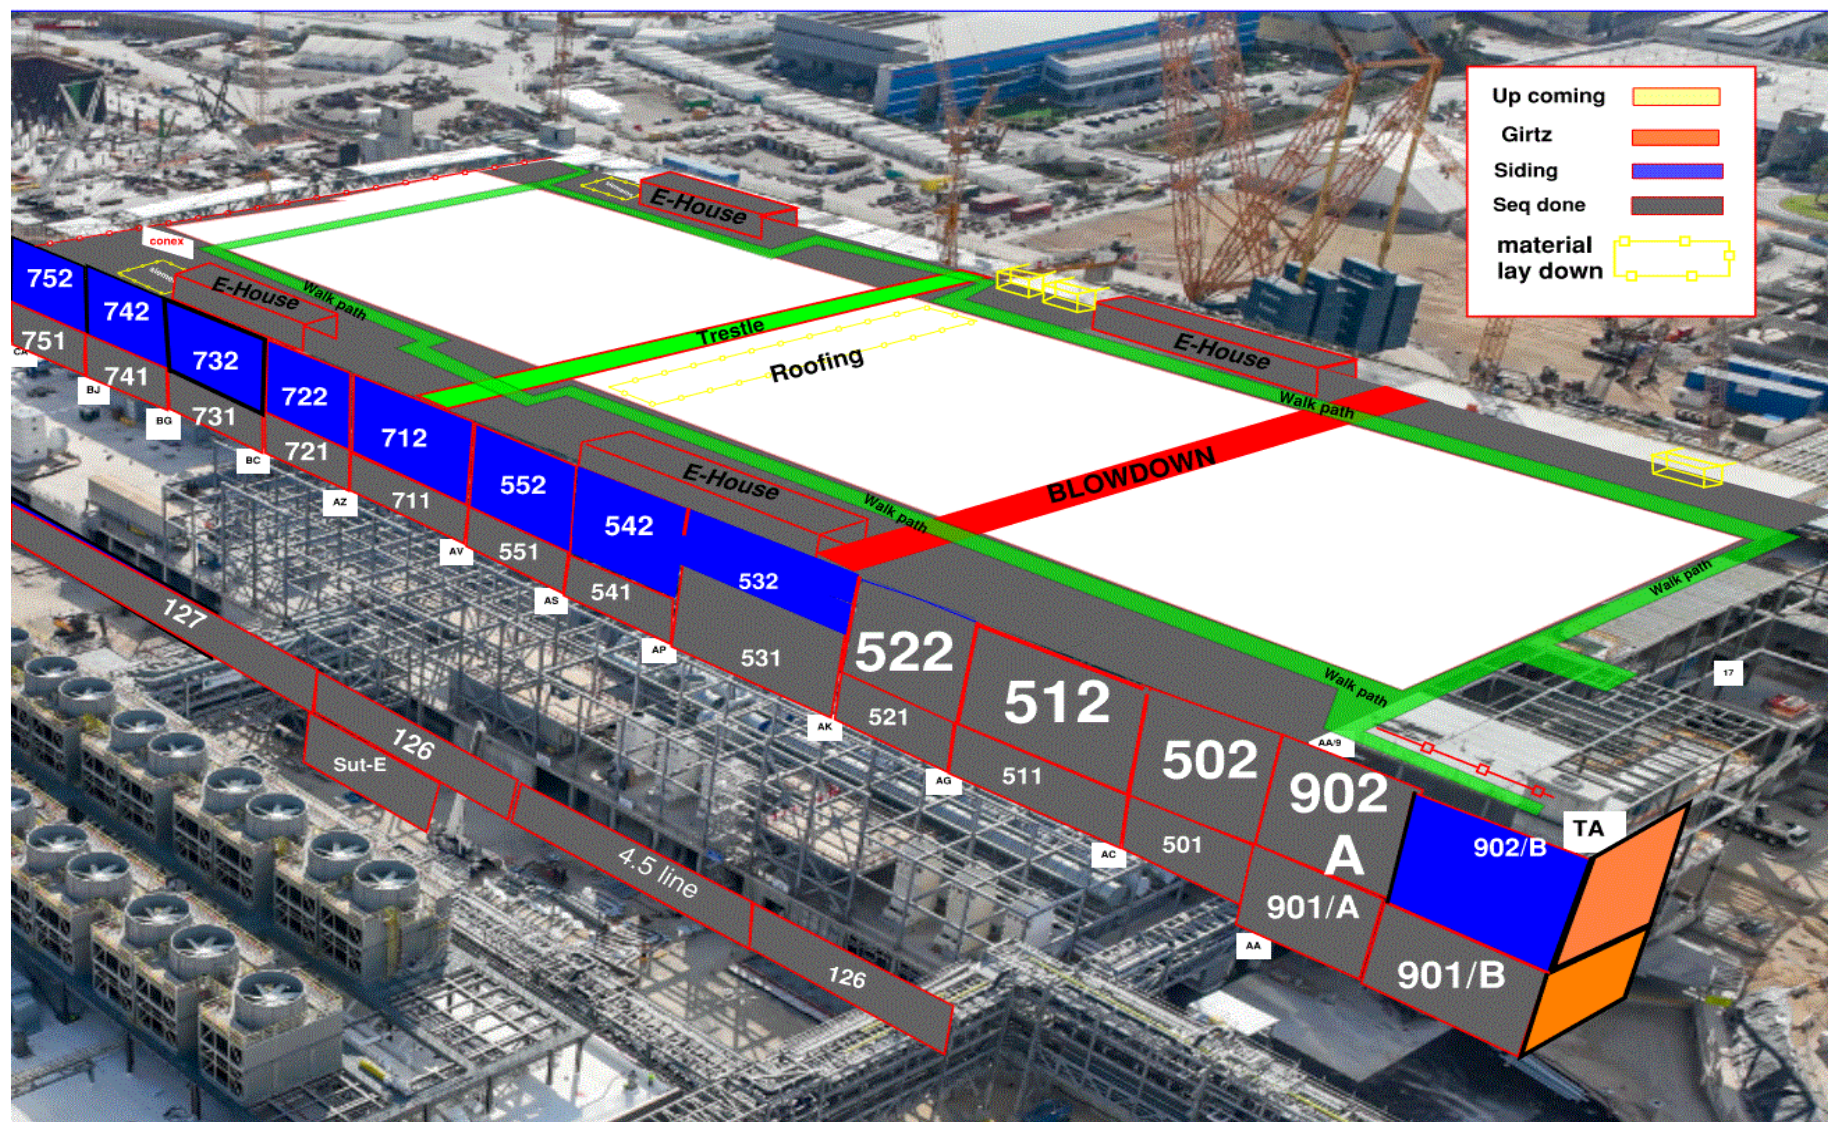

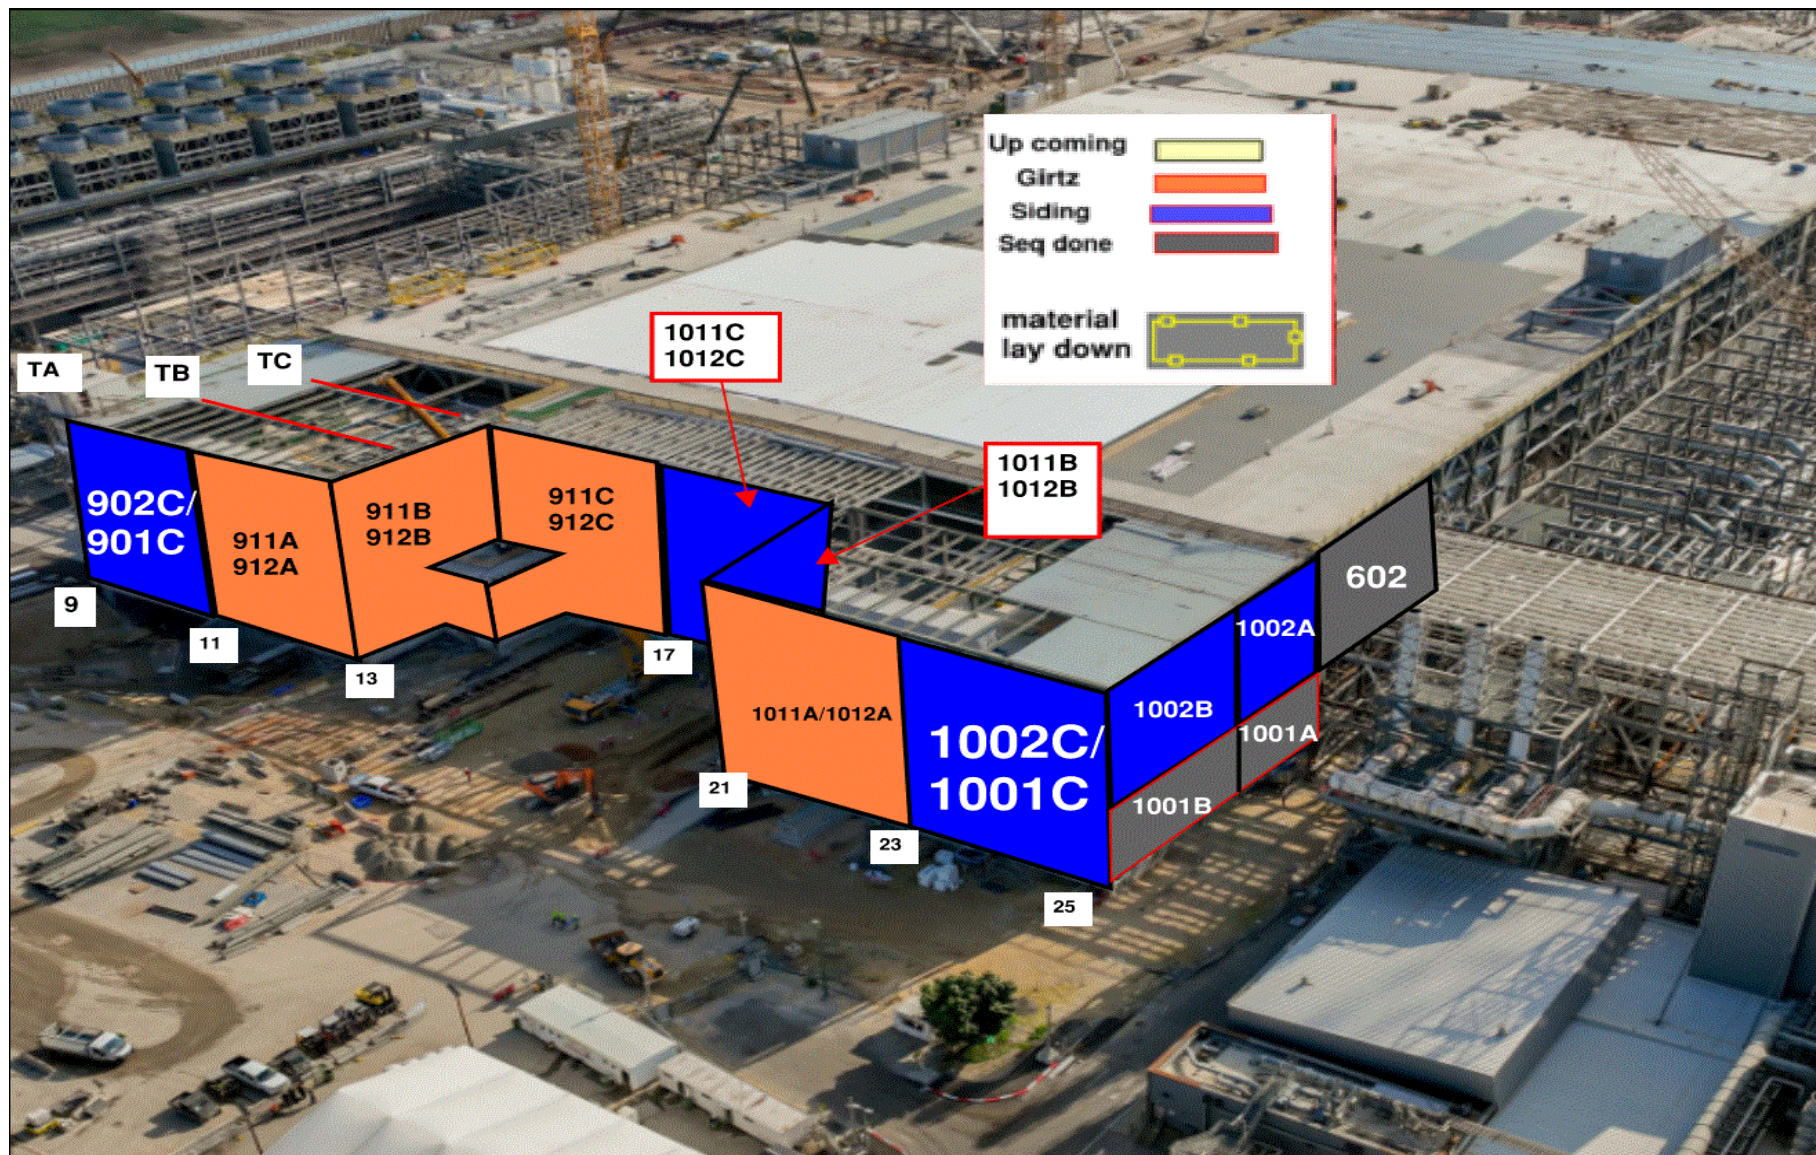


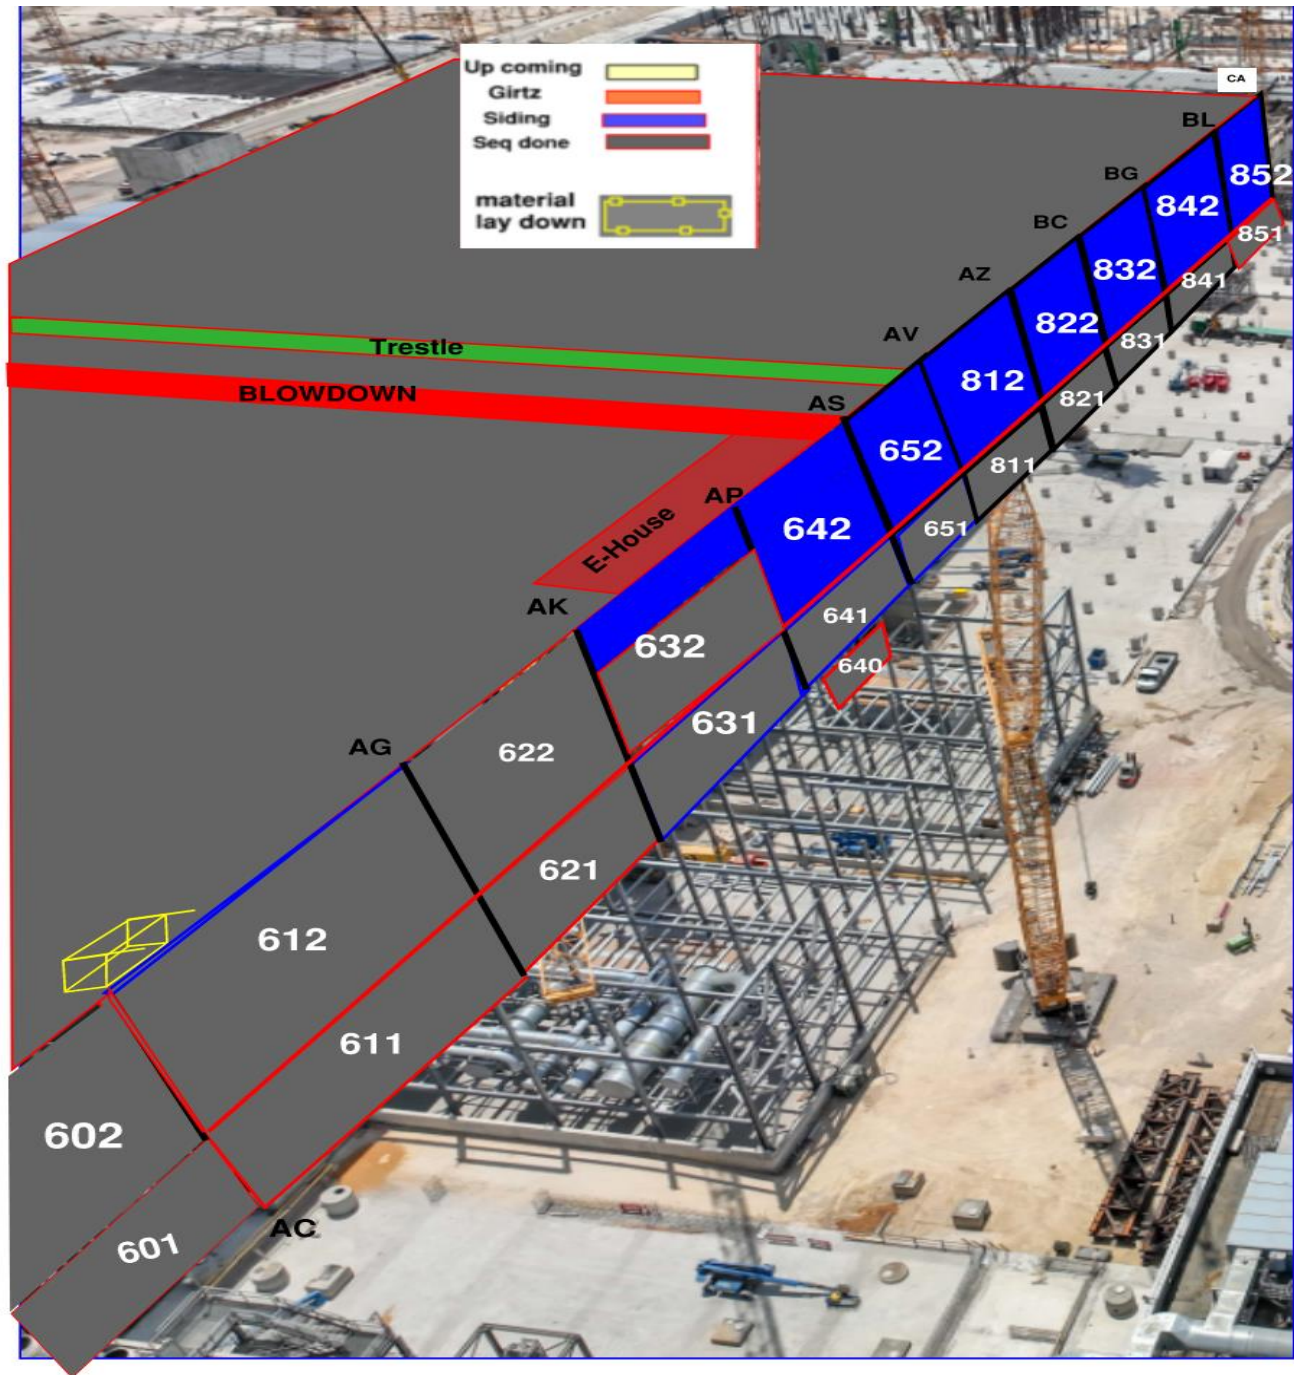

PSSS.1

Utility Level 1YA

PSSS Roof 2SA

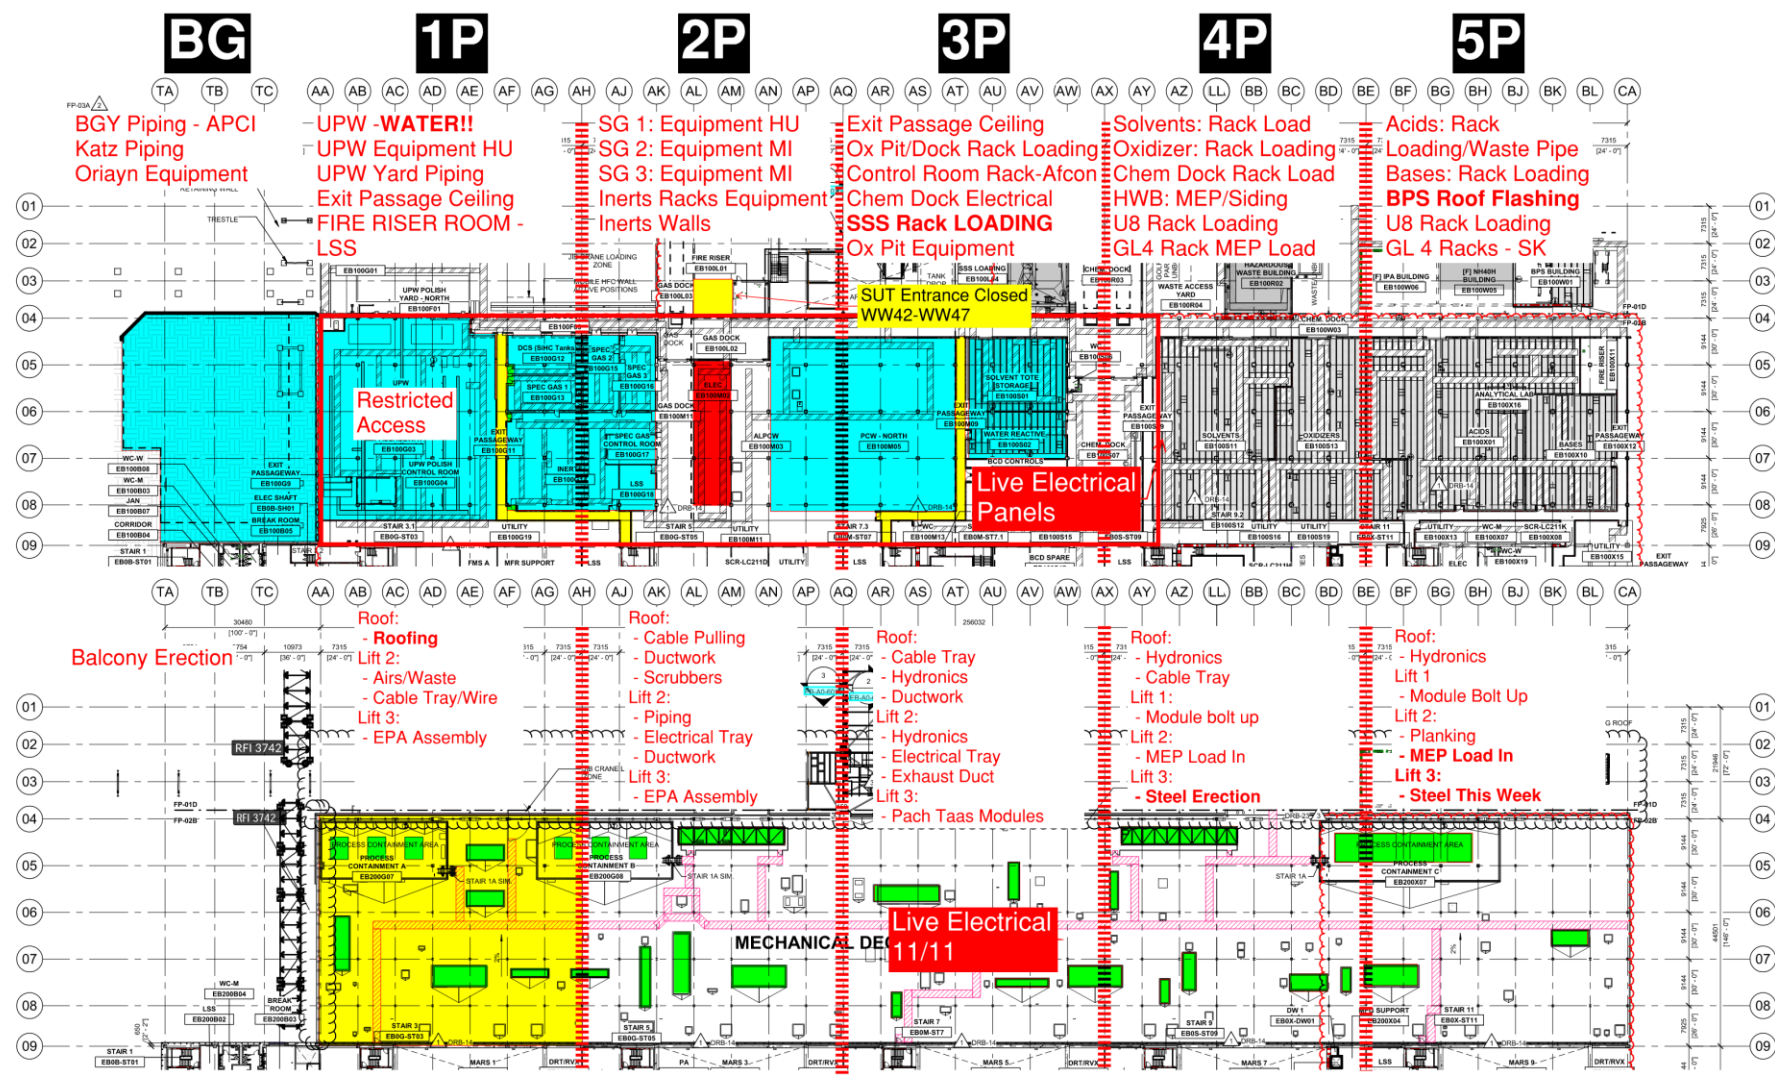

PSSS.2




AHU Sets 13 & 14

500T Build for PSSS 11/11- 12/11




TC3
Dismantle
13/11
14/11
(Nights)

650T Set
up
NOW

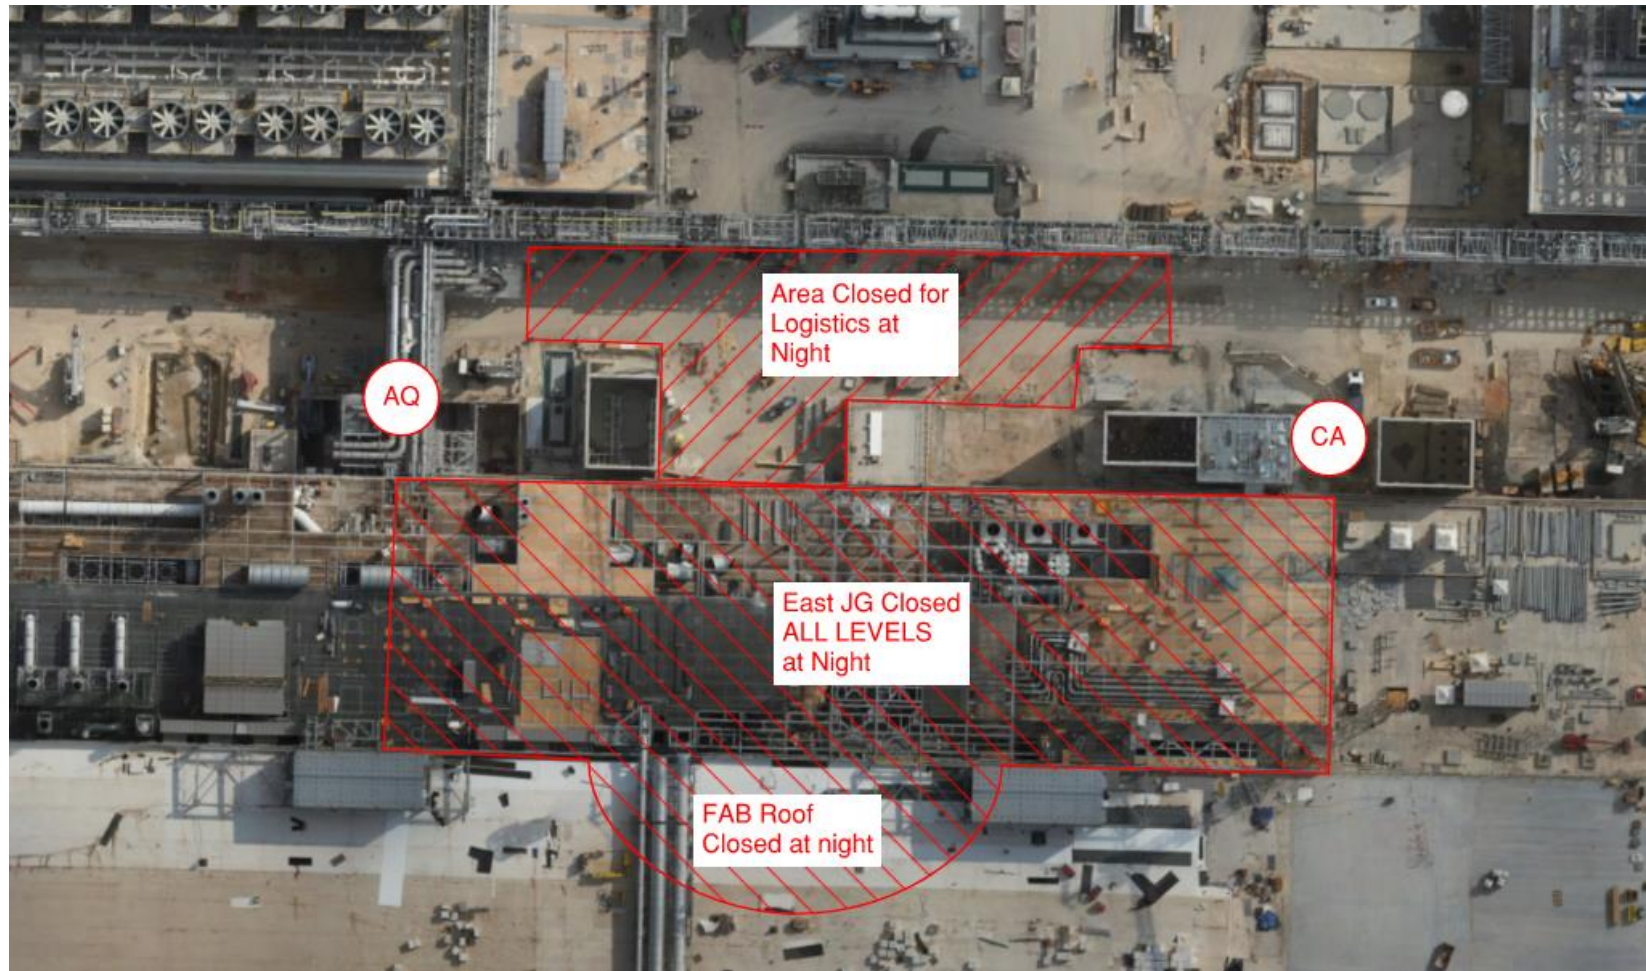

IA
Pressure
Test
13/11
17:00-
04:00

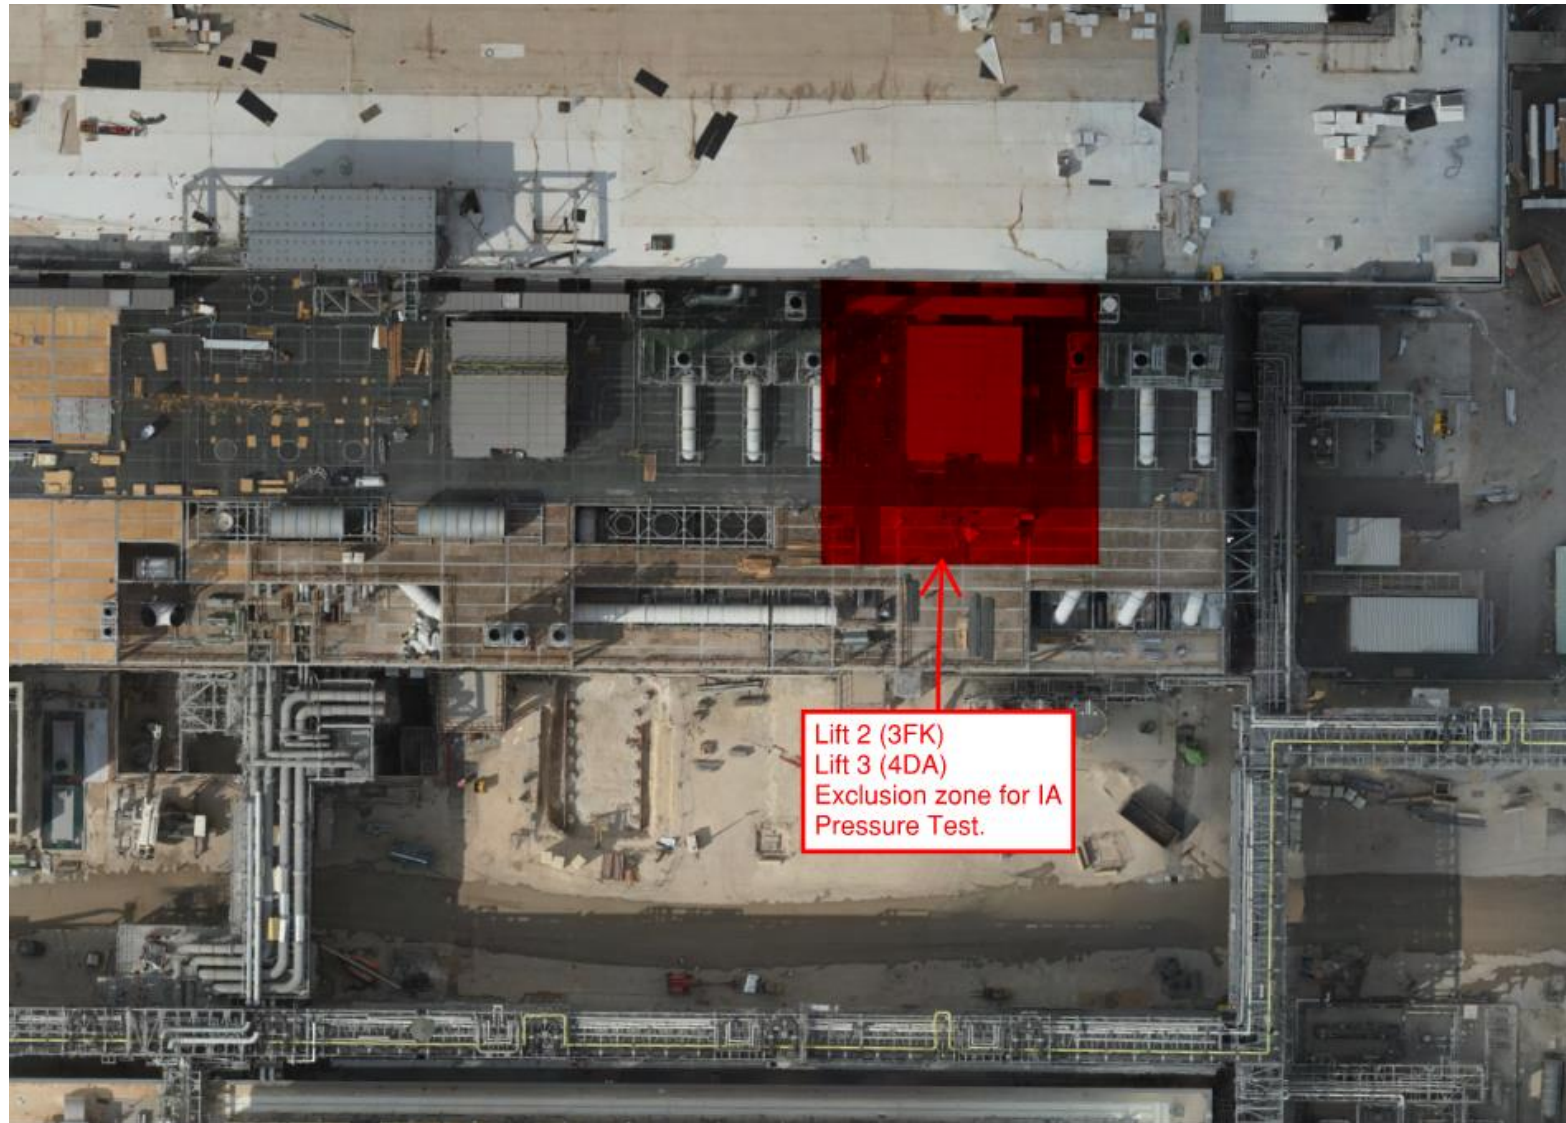



WJG 01J, 02J LIFT 2 & 3






WJG 03J, 04J, 05J LIFT 2 & 3






IA Pressure test Exclusion Zone 12/11/2024 Night Shift

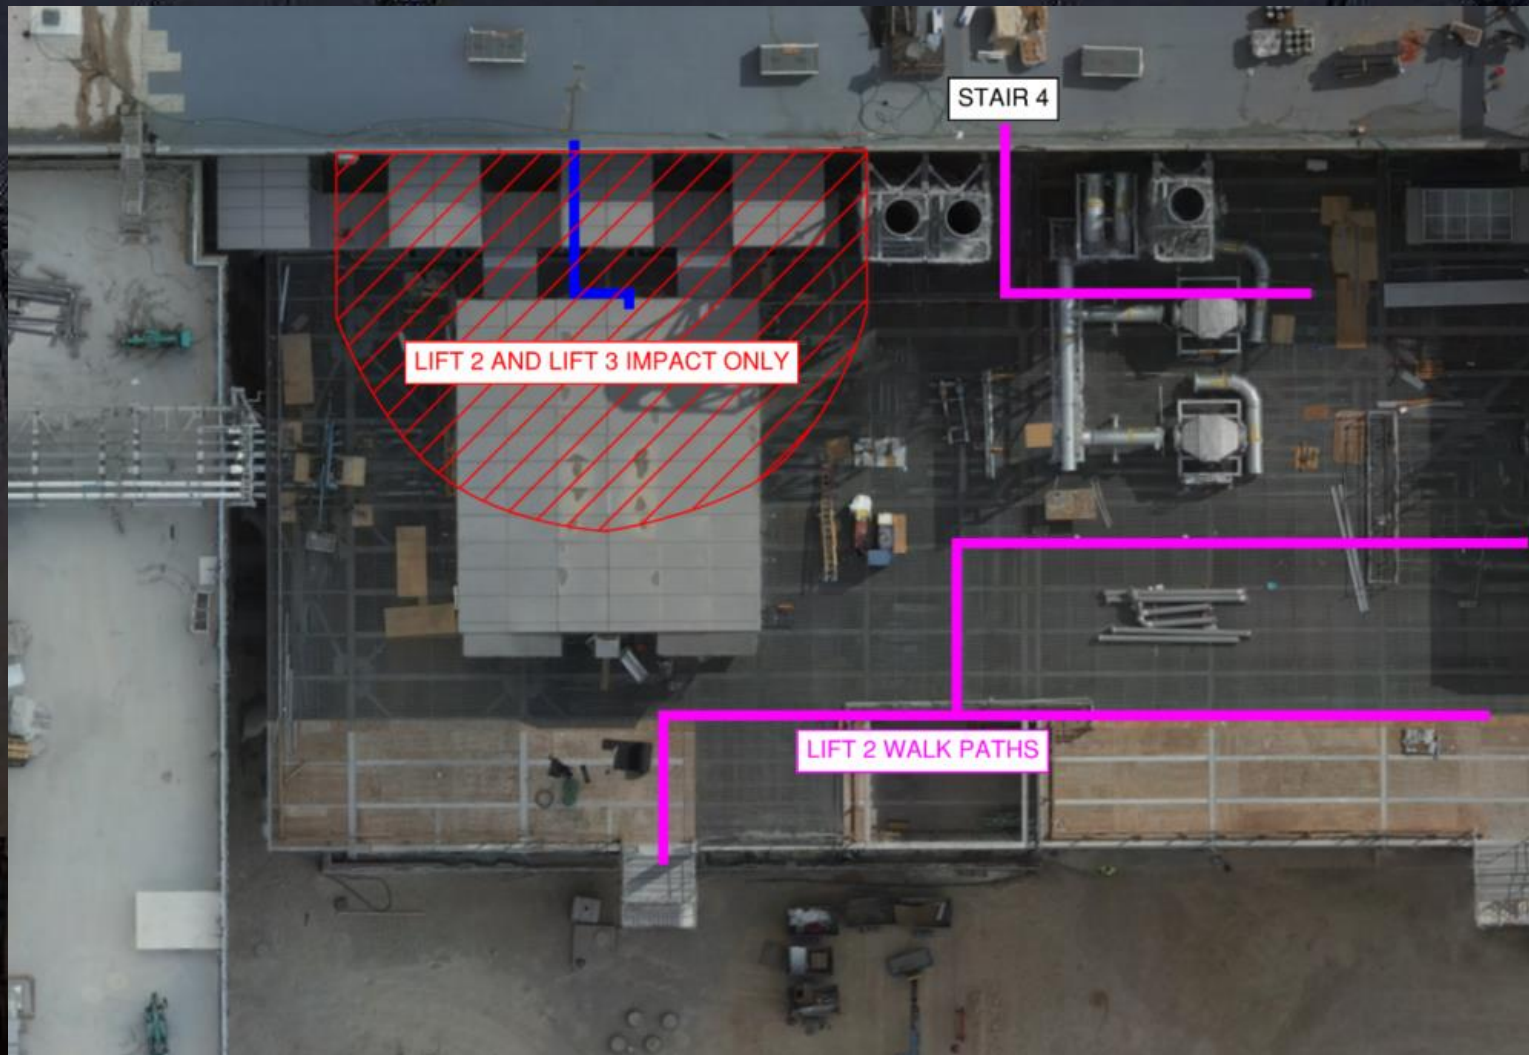



WJG UTILITY LEVEL BUILD OUT

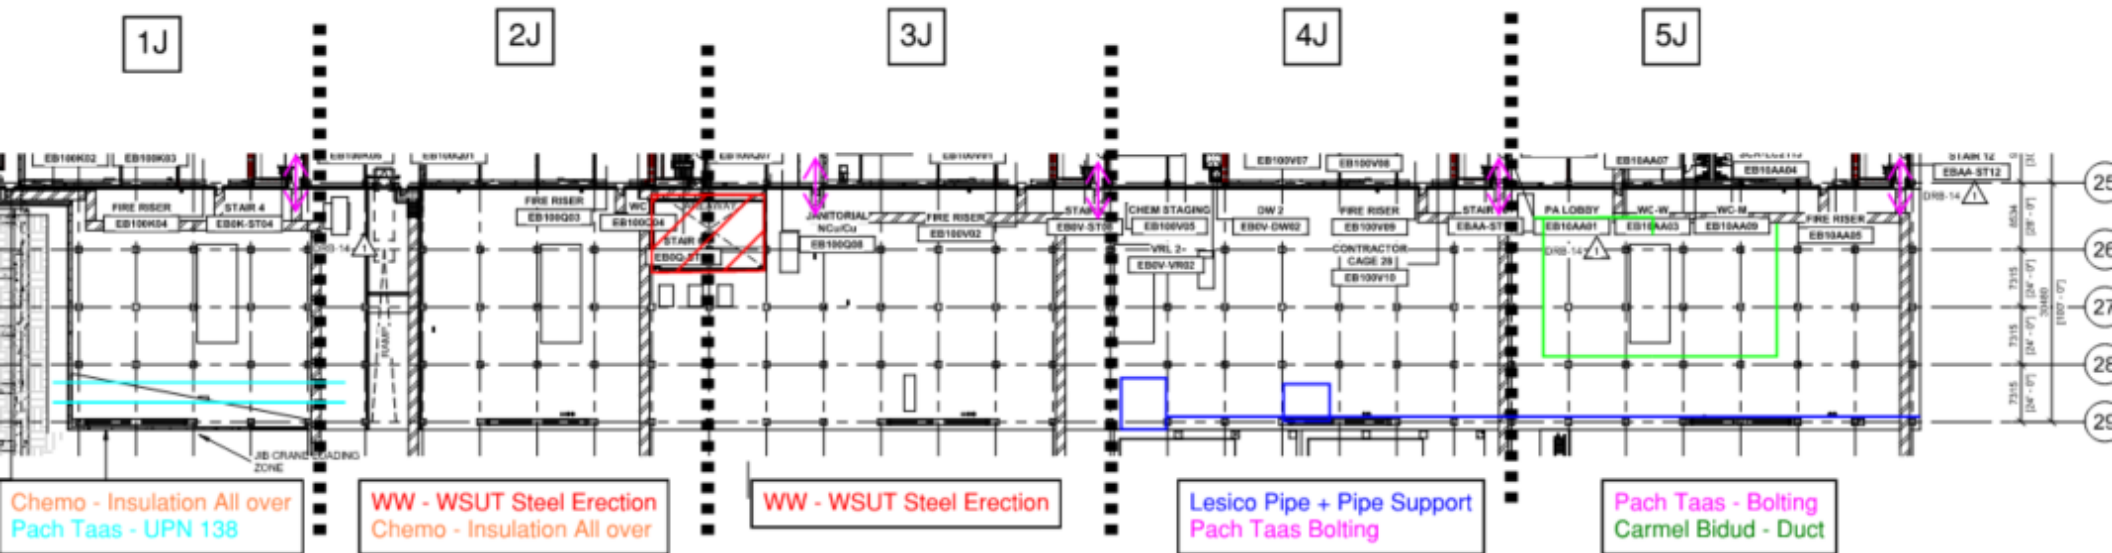

CUB 1 EVACUATION MUSTER LOCATION

NORTH YARD

WATER TREATMENT

SAND FILTERS

CHILLERS


BOILERS

EGRESS KEEP CLEAR

NOTE:

1. REFRIGERANT DETECTION SYSTEM IS LIVE.
2. IF ANY ALARM IS SOUNDED-ALL WORKERS MUST EVACUATE THE BUILDING
3. EVACUATION LOCATION TO E IN NORTH YARD OF CUB 1

CUB 1 – EXTERIOR/ROOF

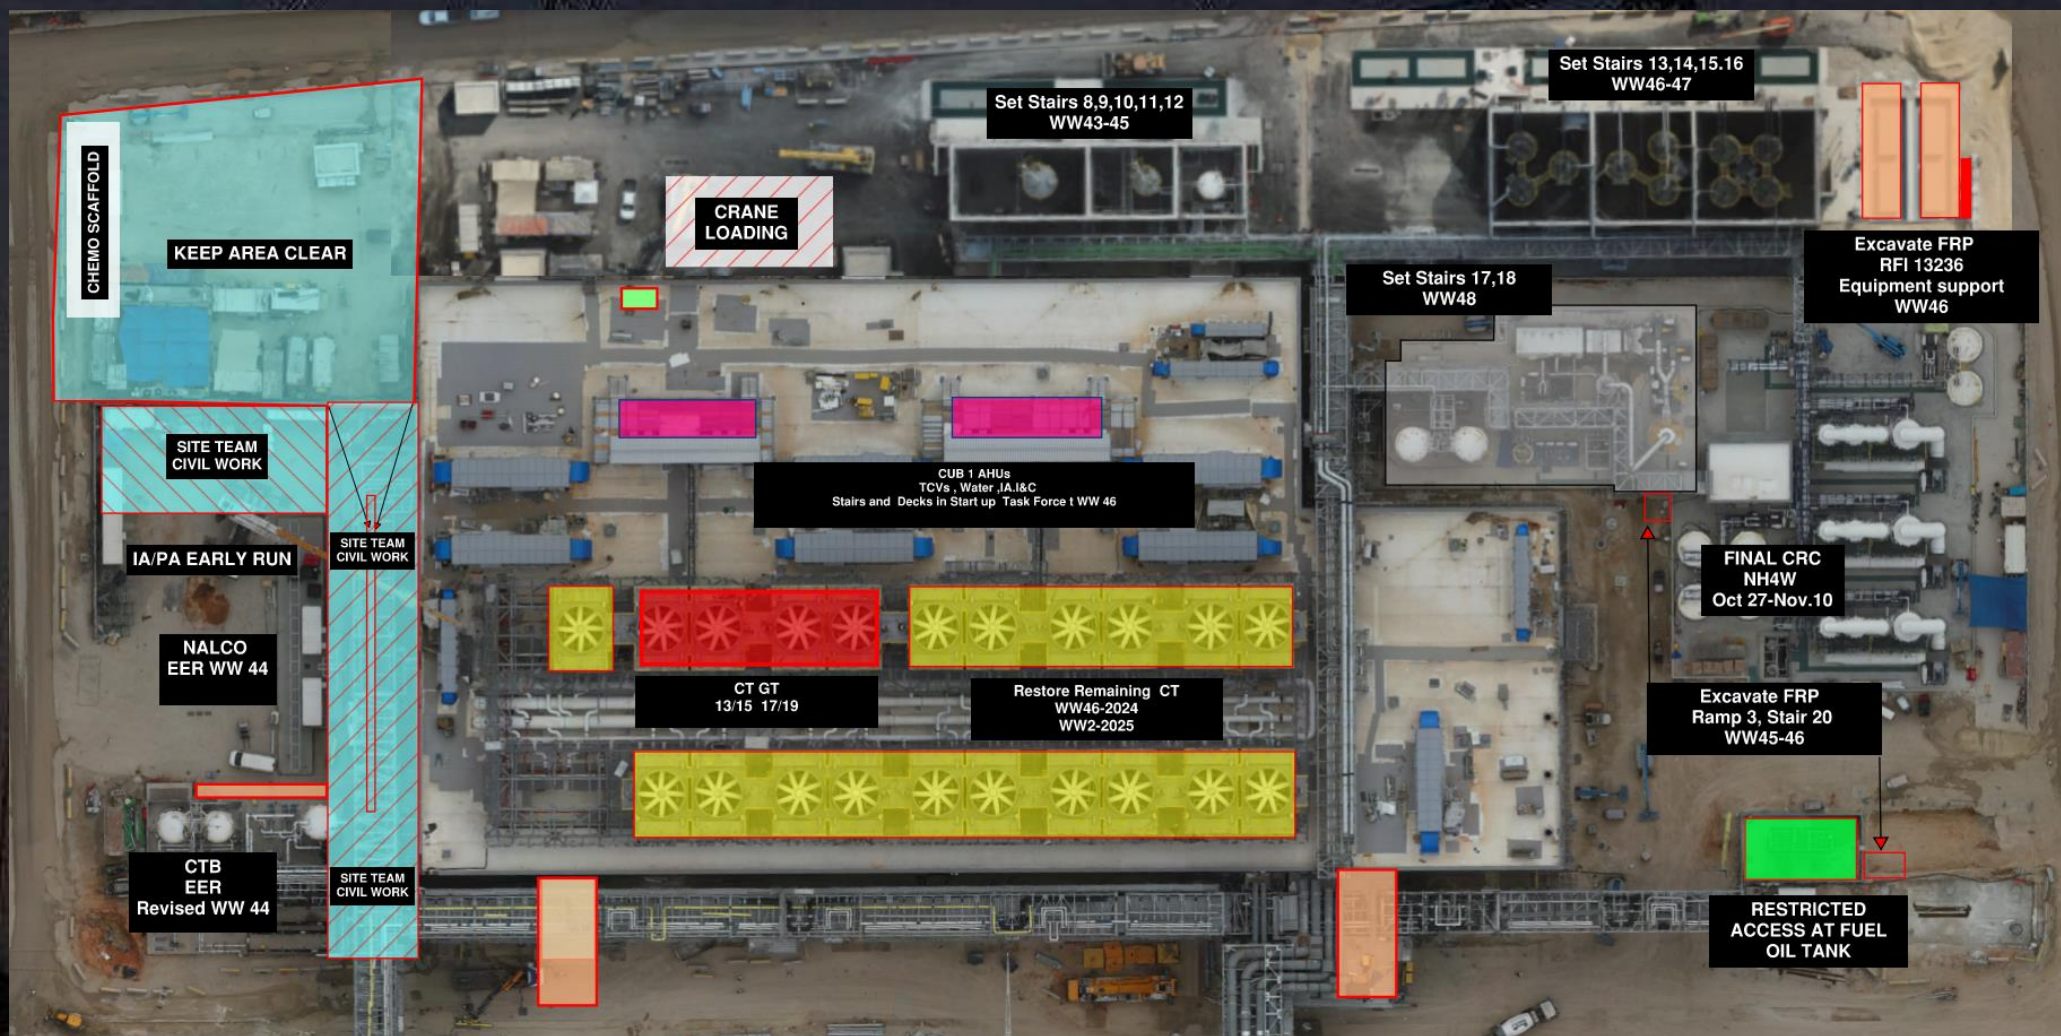

HOFFMAN CONSTRUCTION COMPANY
 OF ISRAEL

HOFFMAN Sparrow

NORTH YARD

Future NH4W 283

ELECTRICAL

Zone 2

Zone 3

Zone 4

Zone 5

Zone 6

Zone 7

Chillers

Sand Filters

Water Treatment

CTB 114

SWS 237

Set CTB Tank 114-1/2-80 Pending

HFW 266

BCS 252

BSA 253

MIMO

Path of Egress

Scaffold for remaining High & Tight In Design Oct. 26-Nov. 9

Load in Heat Exchangers Nov 27 Access Via Gut Road

Partition Wall Buildout

Mamad Access

Roof Access

Equipment/Material Access

Stair 8

Stair 9

Stair 10

Stair 11

Stair 12

Stair 13

Stair 14

Stair 15

PA

WC

JAN

LSS

SCR

MECHANICAL WORKSHOP

MECHANICAL CONTROL ROOM

LIWS LAB

CRITICAL SPARE PARTS STORAGE PUMP REBUILD AREA

WWT SUPPORT

FACILITIES SHOP

ELECTRICAL SHOP

AWN 261

HFW 266

BCS 252

BSA 253

Stair 2


Stair 12

Stair 13

Stair 14

Stair 15

CUB 2 – EXTERIOR/ROOF

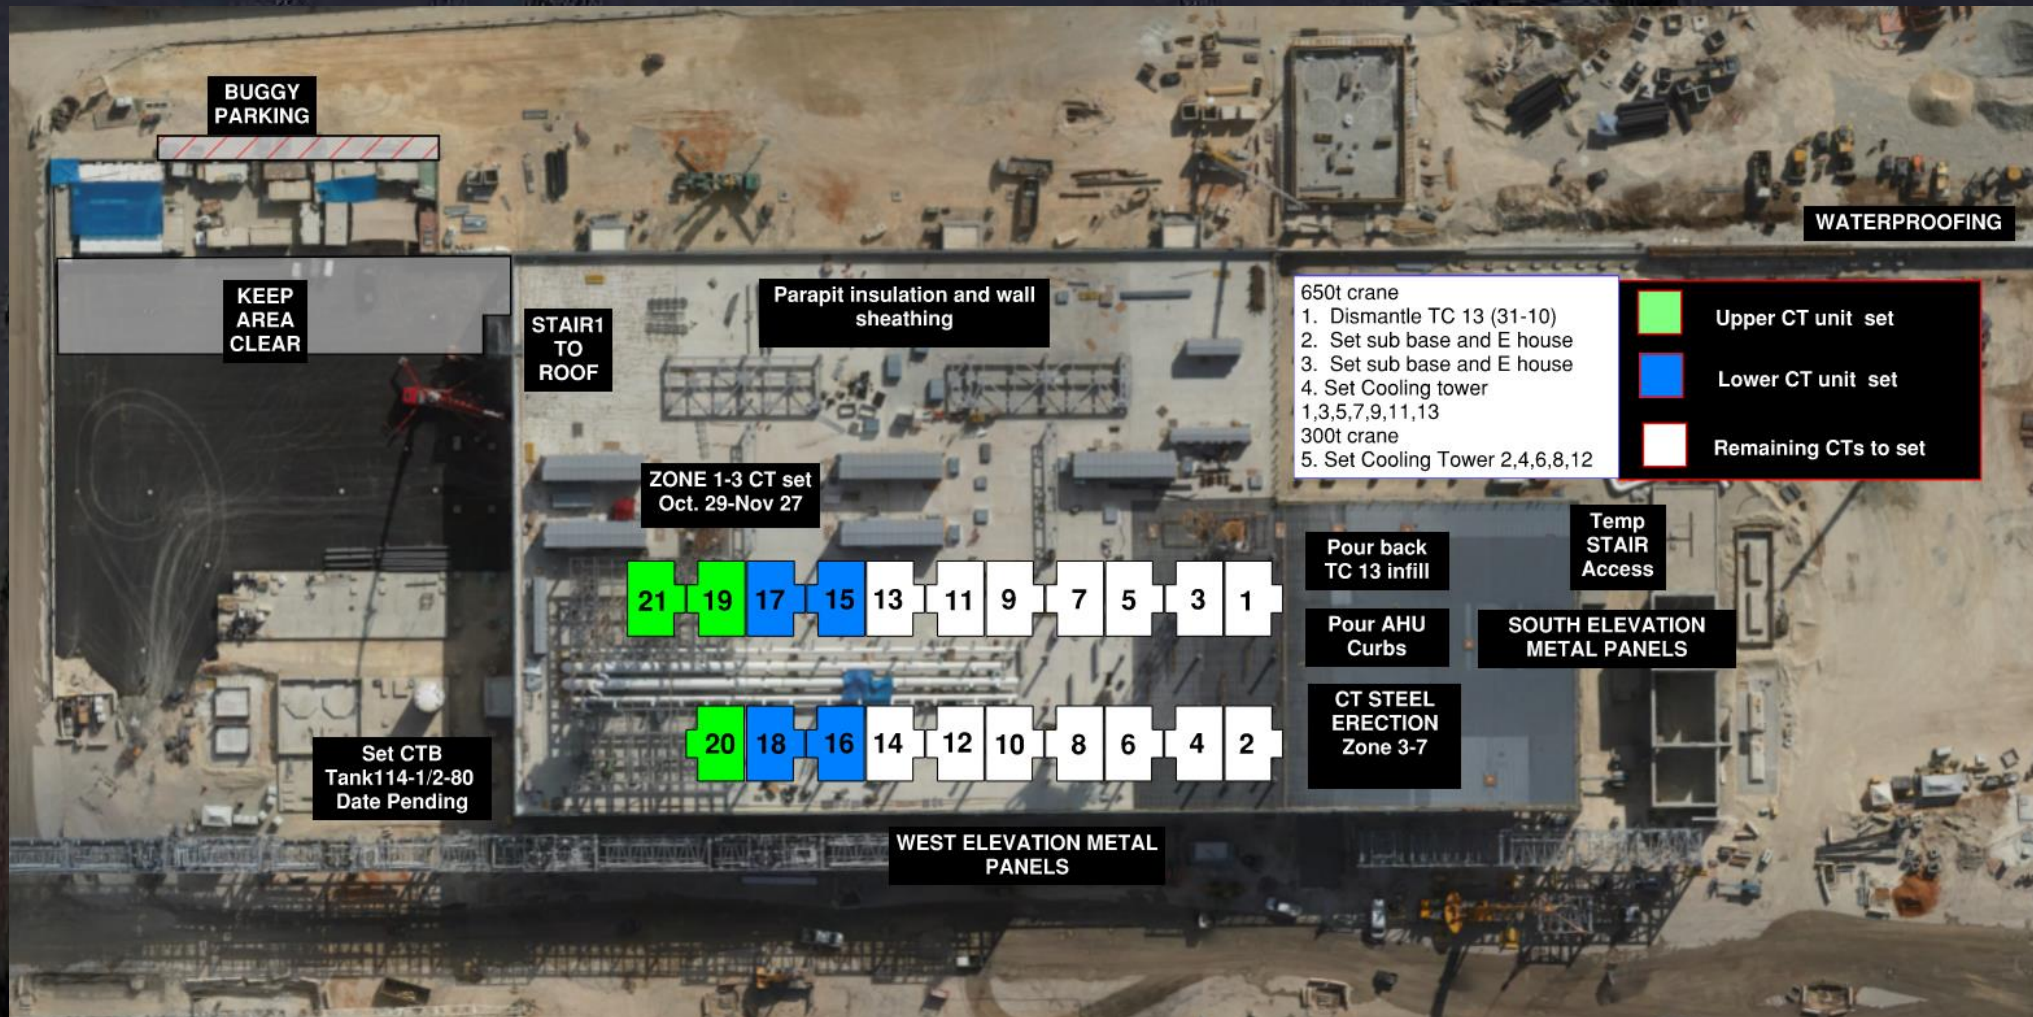


CUB 2 – Crane Logistics


PROPOSE TO ADD
12M JIB
EXTENSION TO
SUPPORT
COOLING TOWER
STEEL ERECTION

NEW RADIUS
SHOWN IN RED


FOR REVIEW

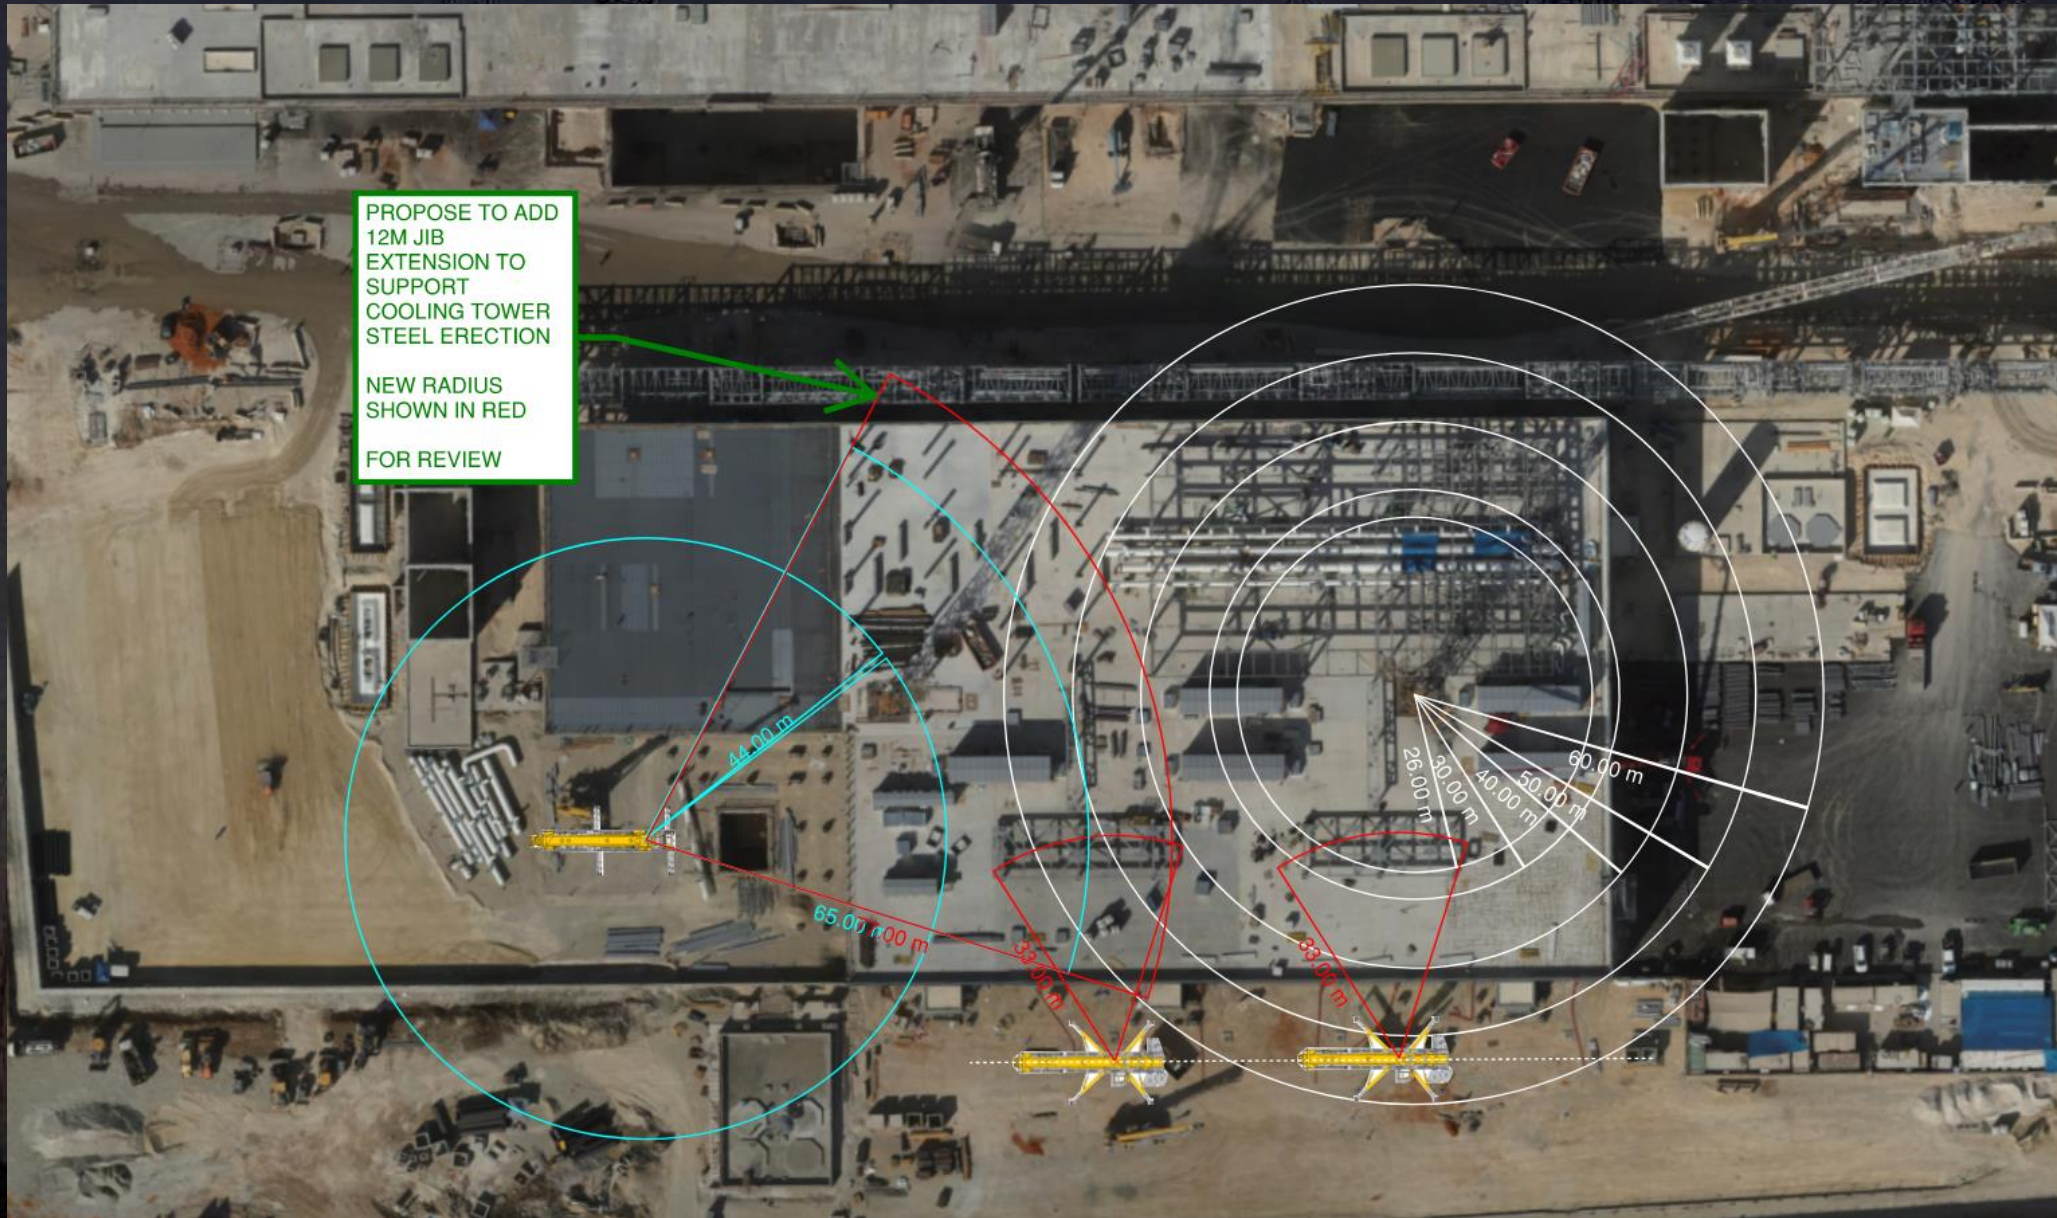





HOFFMAN CONSTRUCTION COMPANY

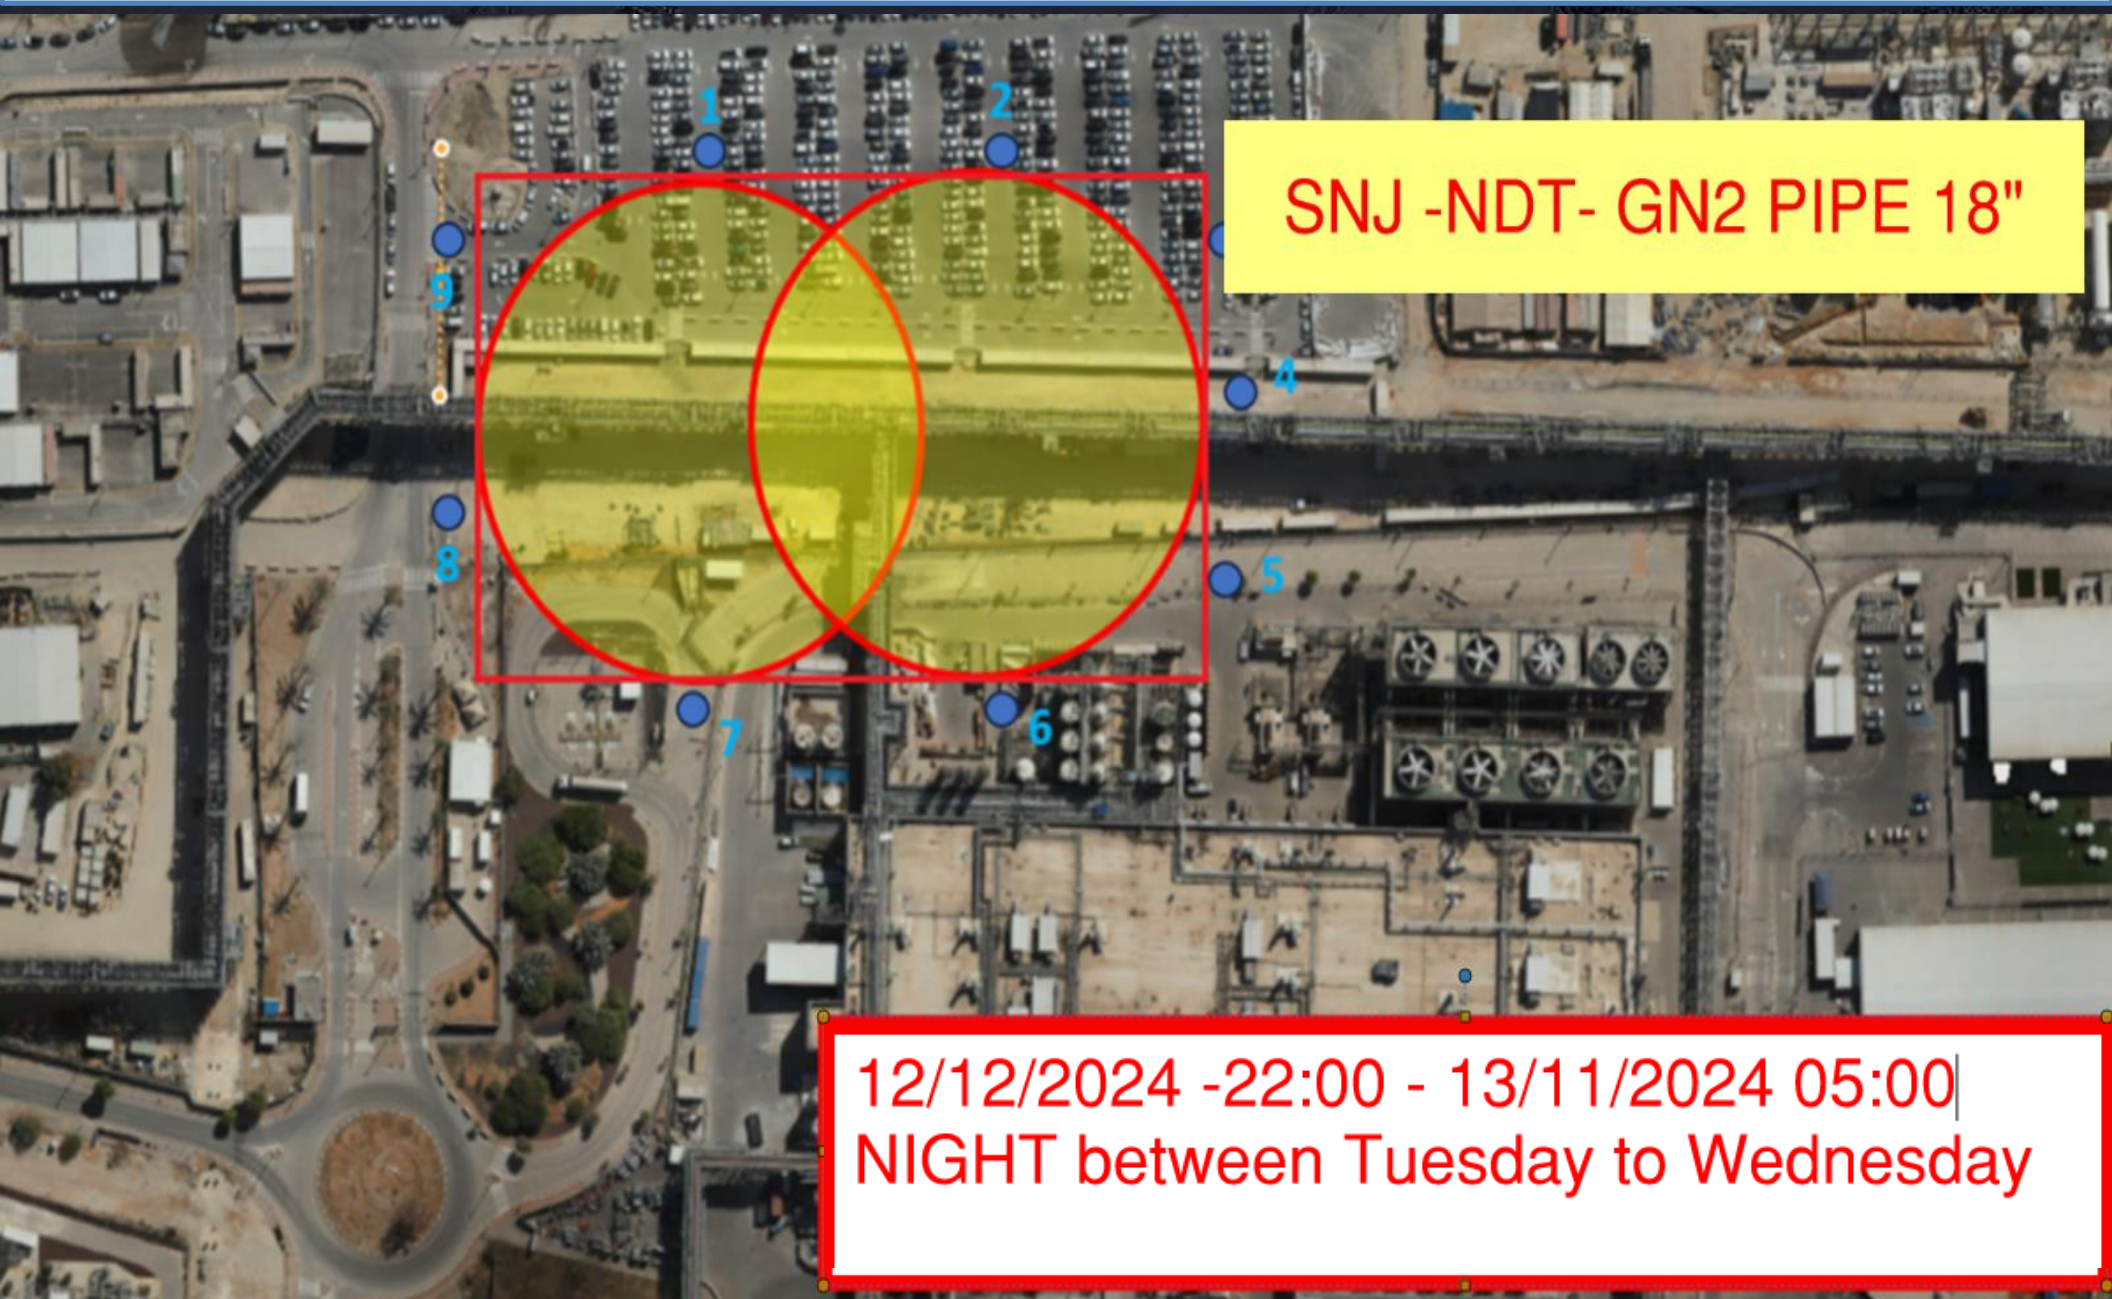

SNJ -NDT- GN2 PIPE 18"

**12/12/2024 -22:00 - 13/11/2024 05:00|
NIGHT between Tuesday to Wednesday**

Daily Coordination Meeting

Site Logistics


North



Daily Coordination Meeting

Site Logistics

South

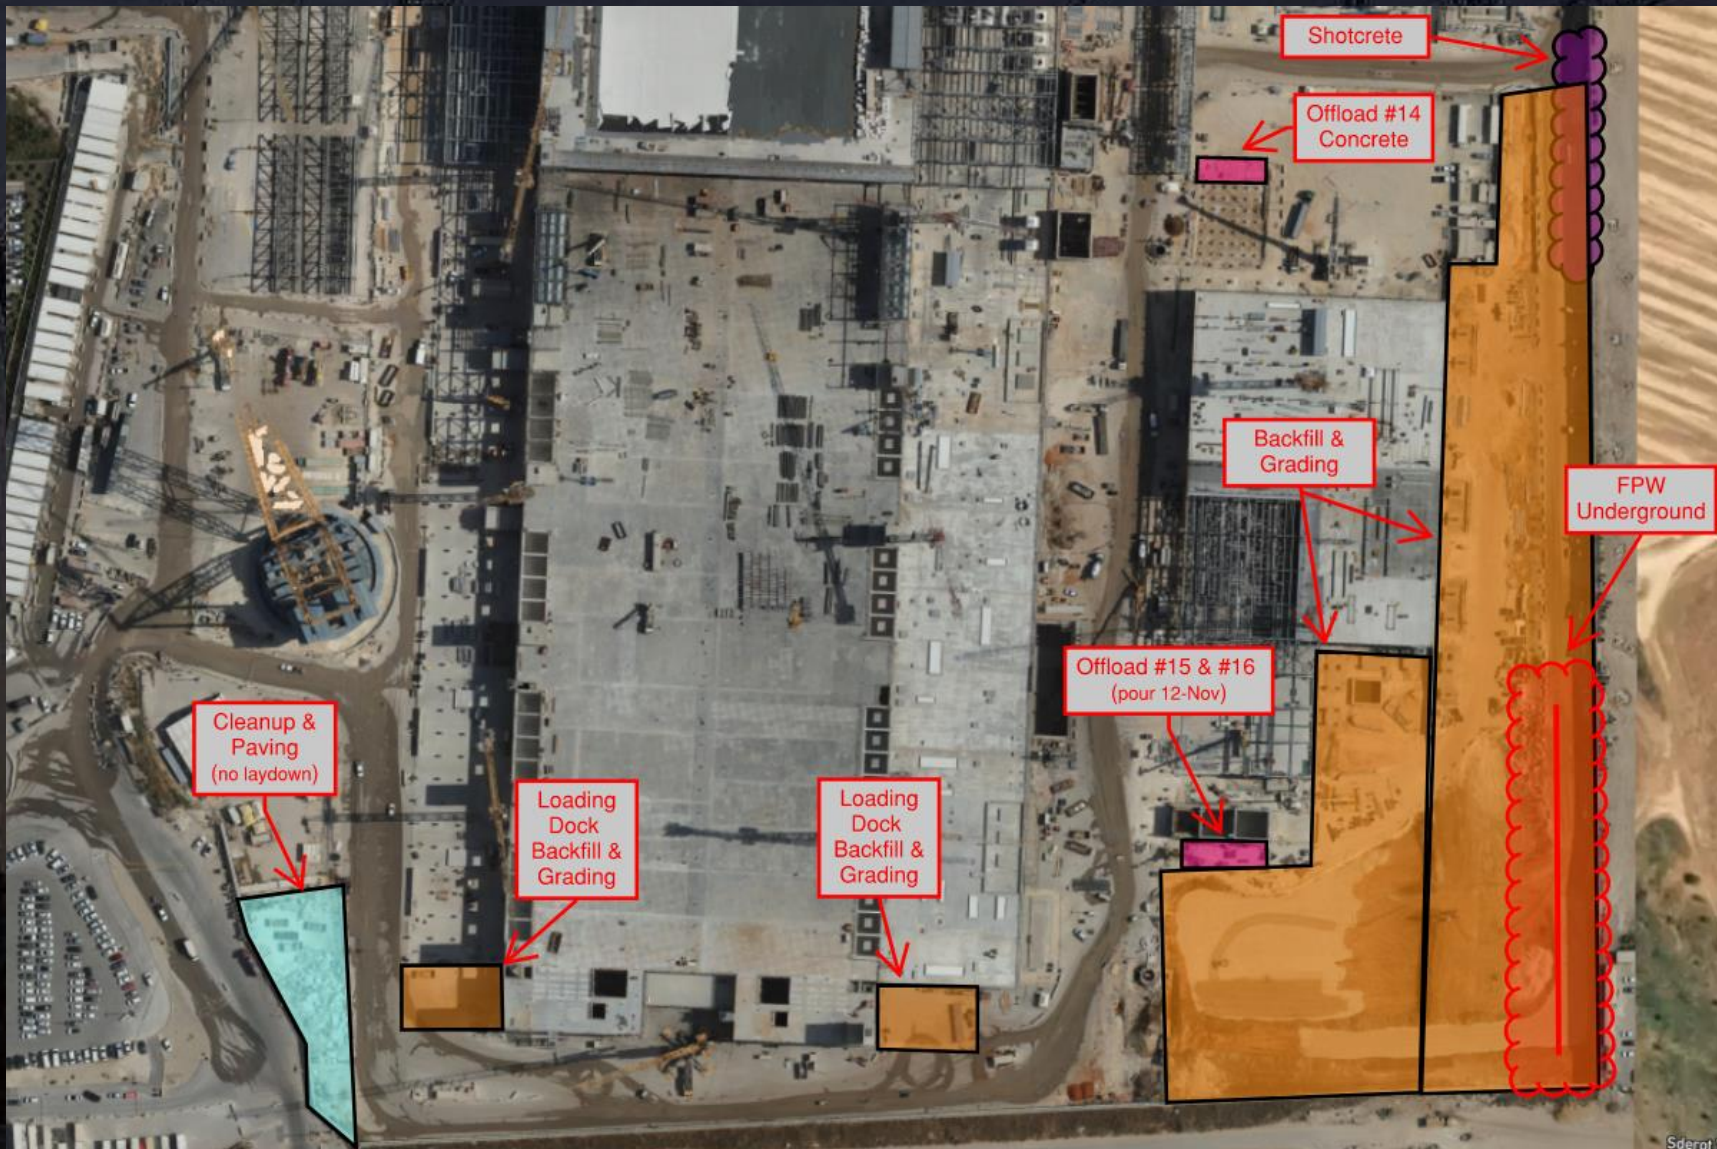

Work Plans and Fall Protection Plans

Daily Coordination Meeting



14:00 Sign In
