

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:


- Loose ends → Finish activities 100%
- Plan today, for end of week cleanup & cord roll up tomorrow

UTILITY LEVEL MOD1

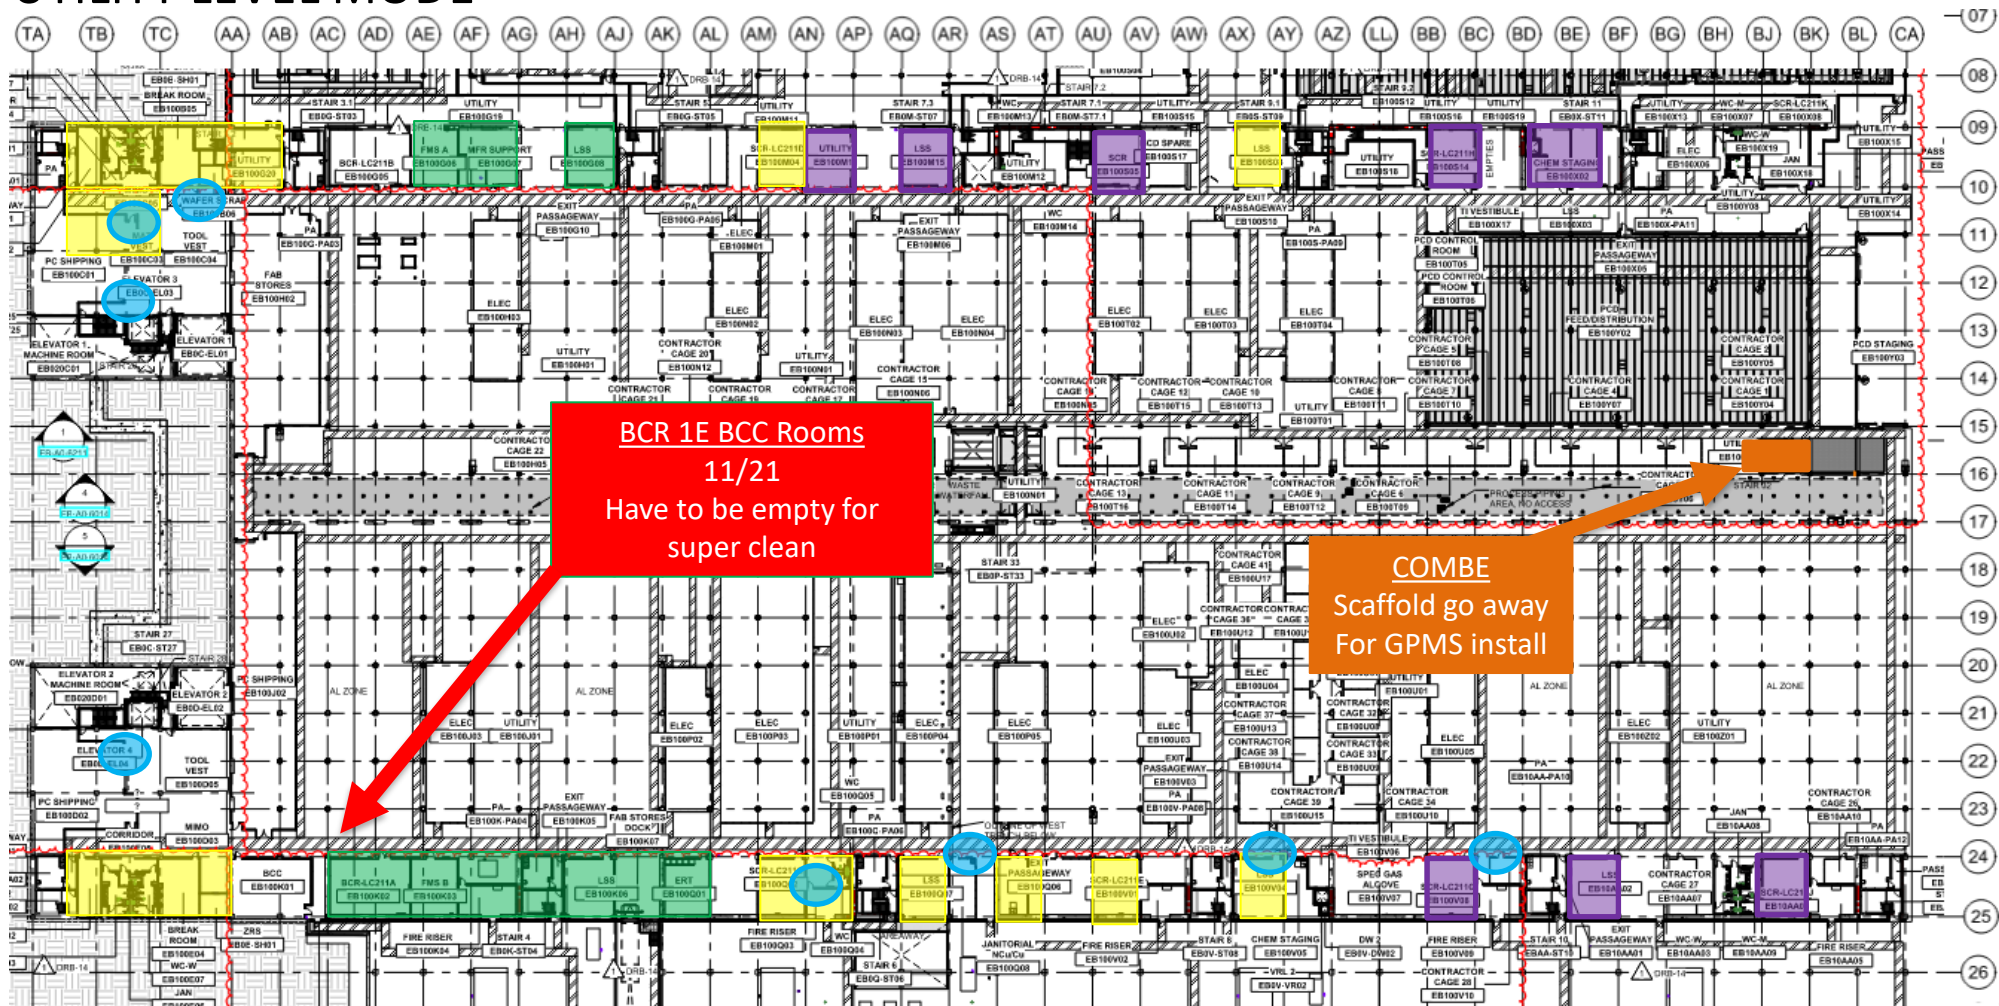





SUT 38.1 LEVEL

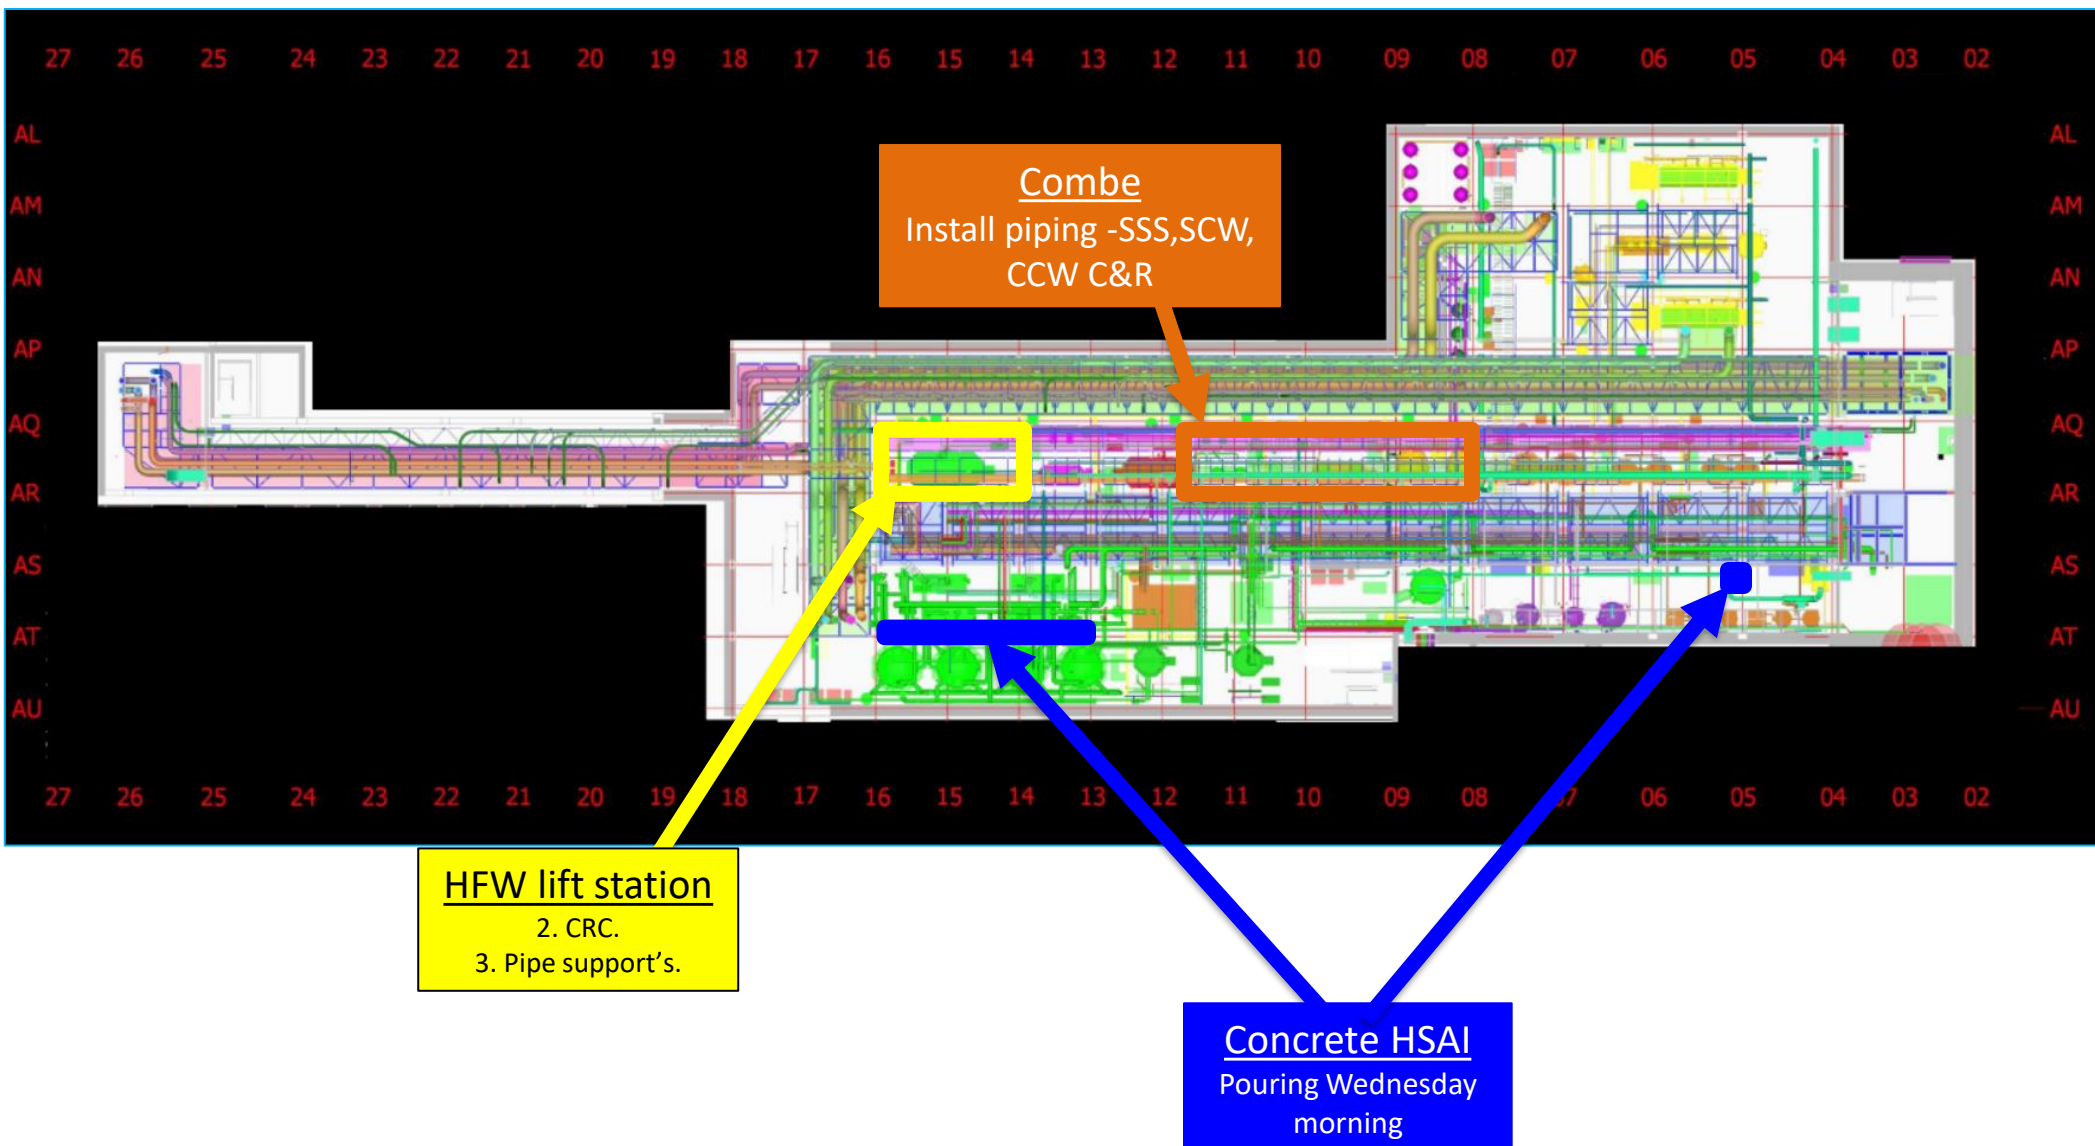


SUT 38.2 LEVEL

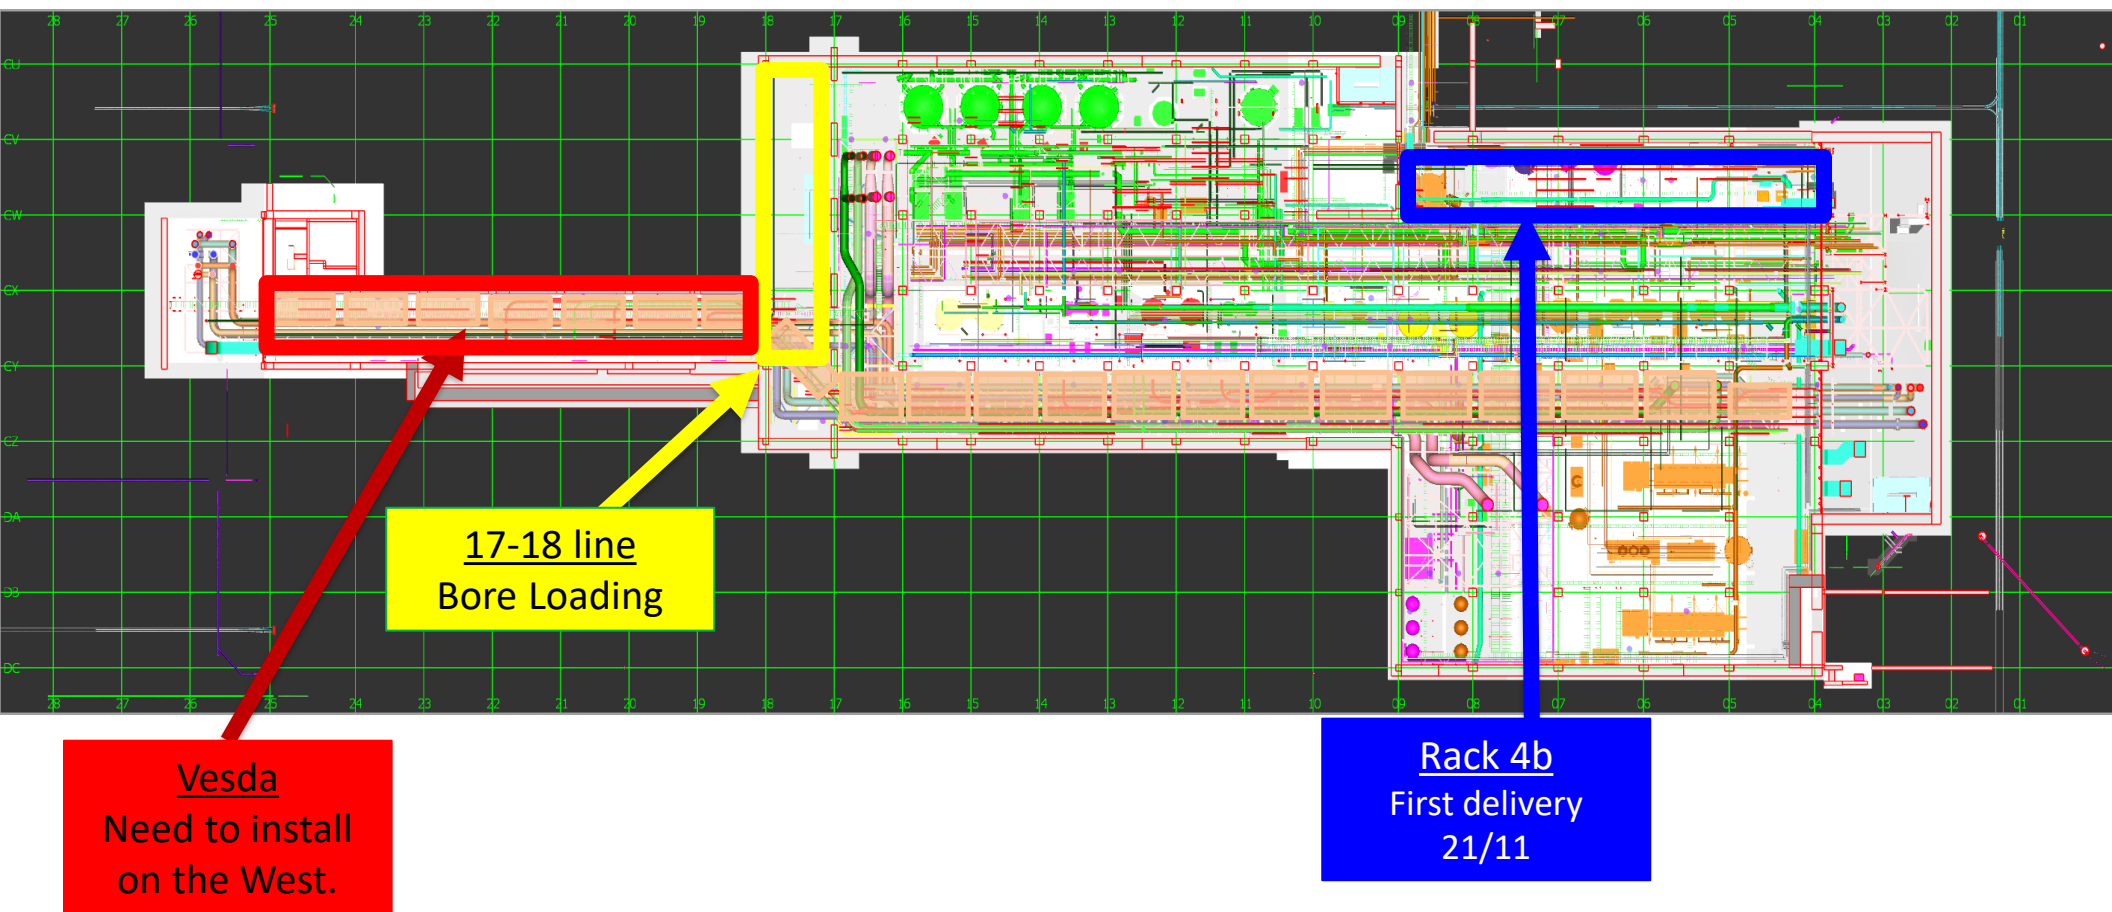


SUBFAB BUILDOUT MOD 1

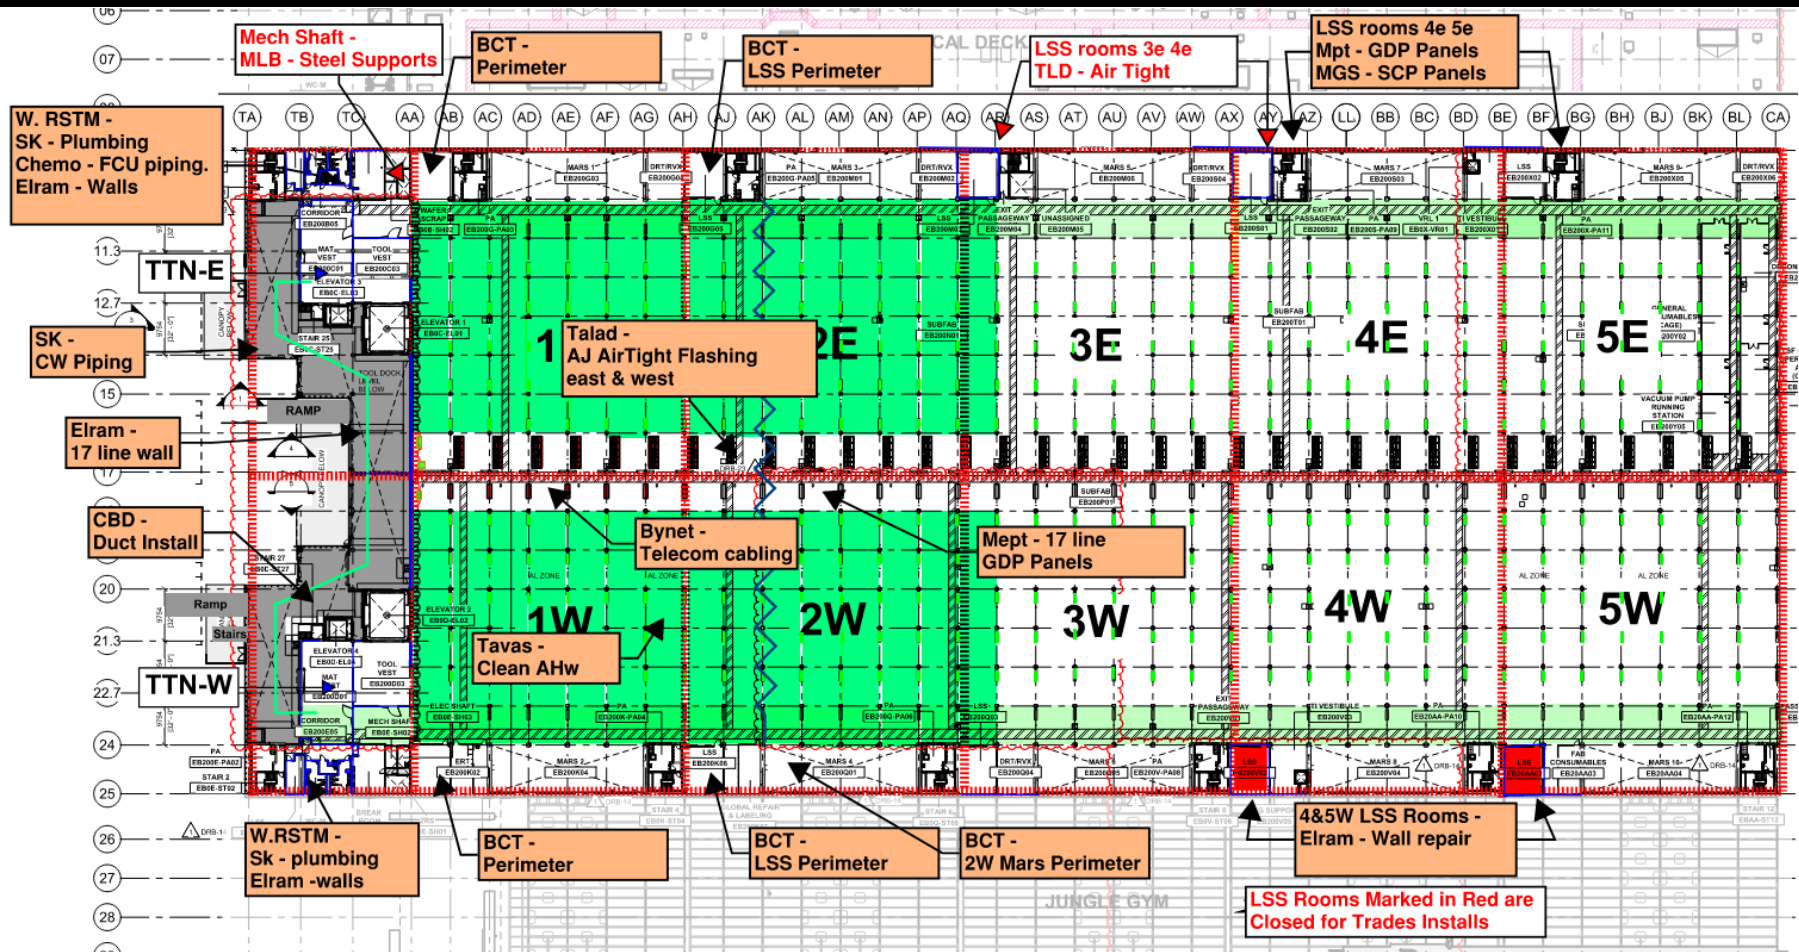


SUBFAB CRC TOPCOAT

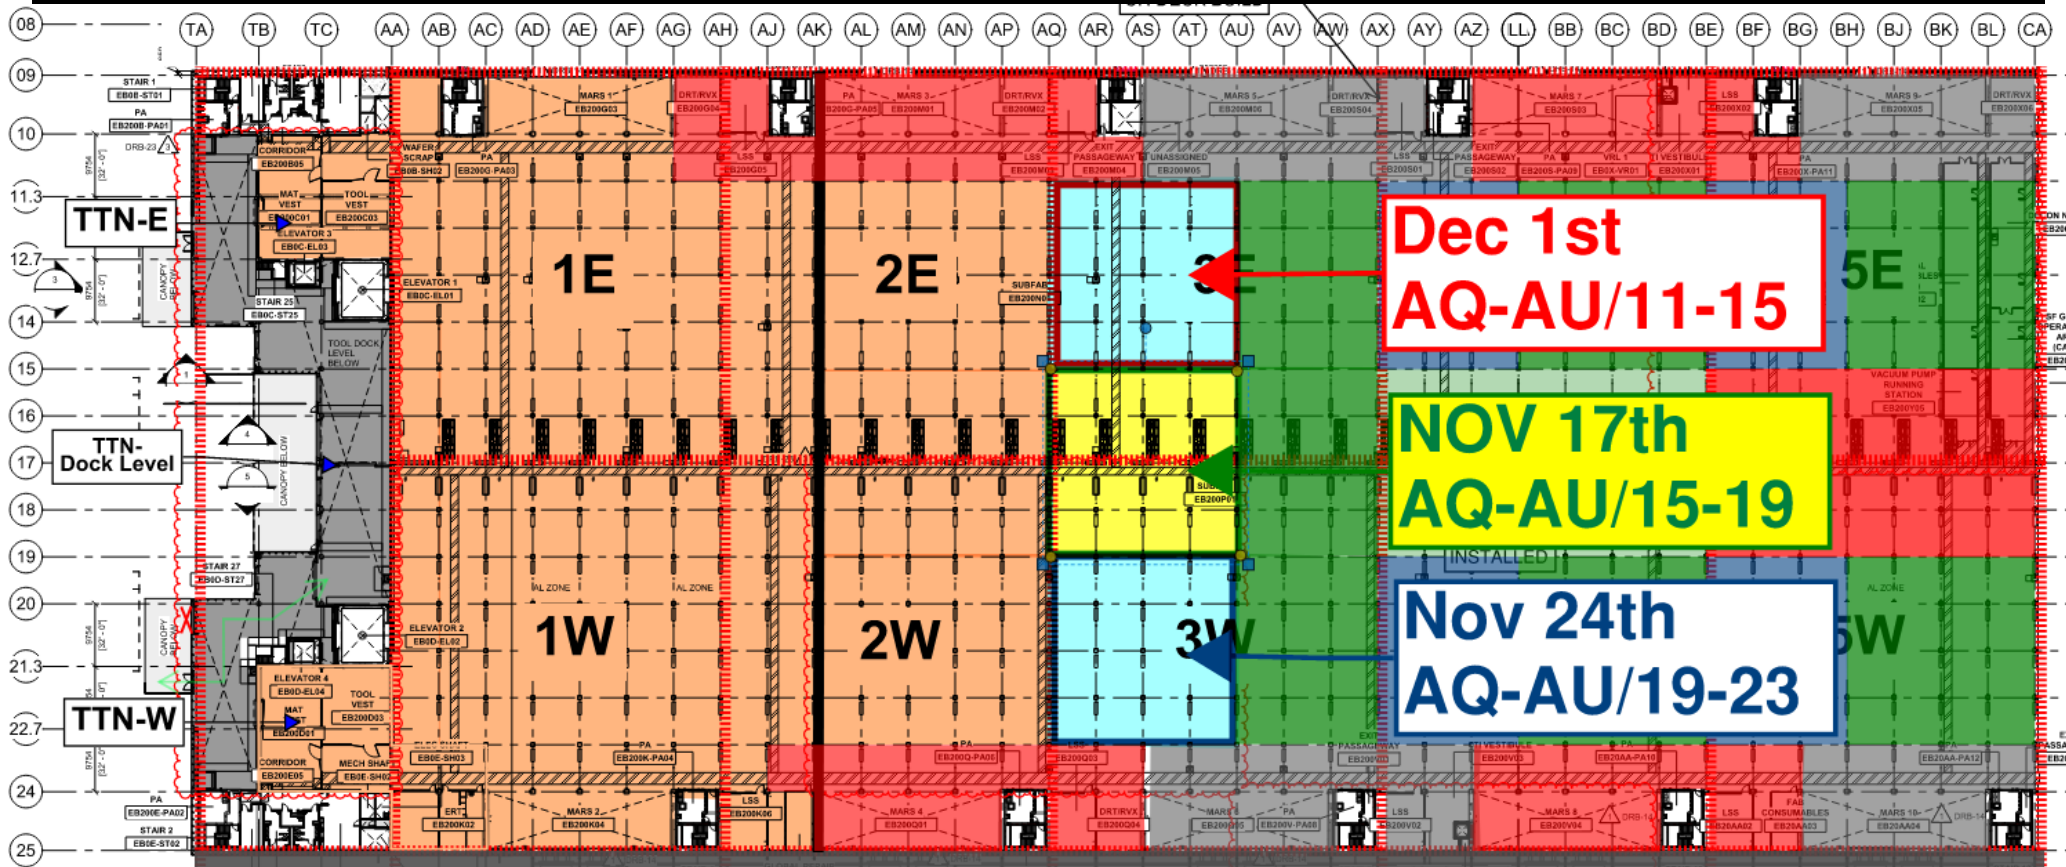


BCT Pressure Test Today

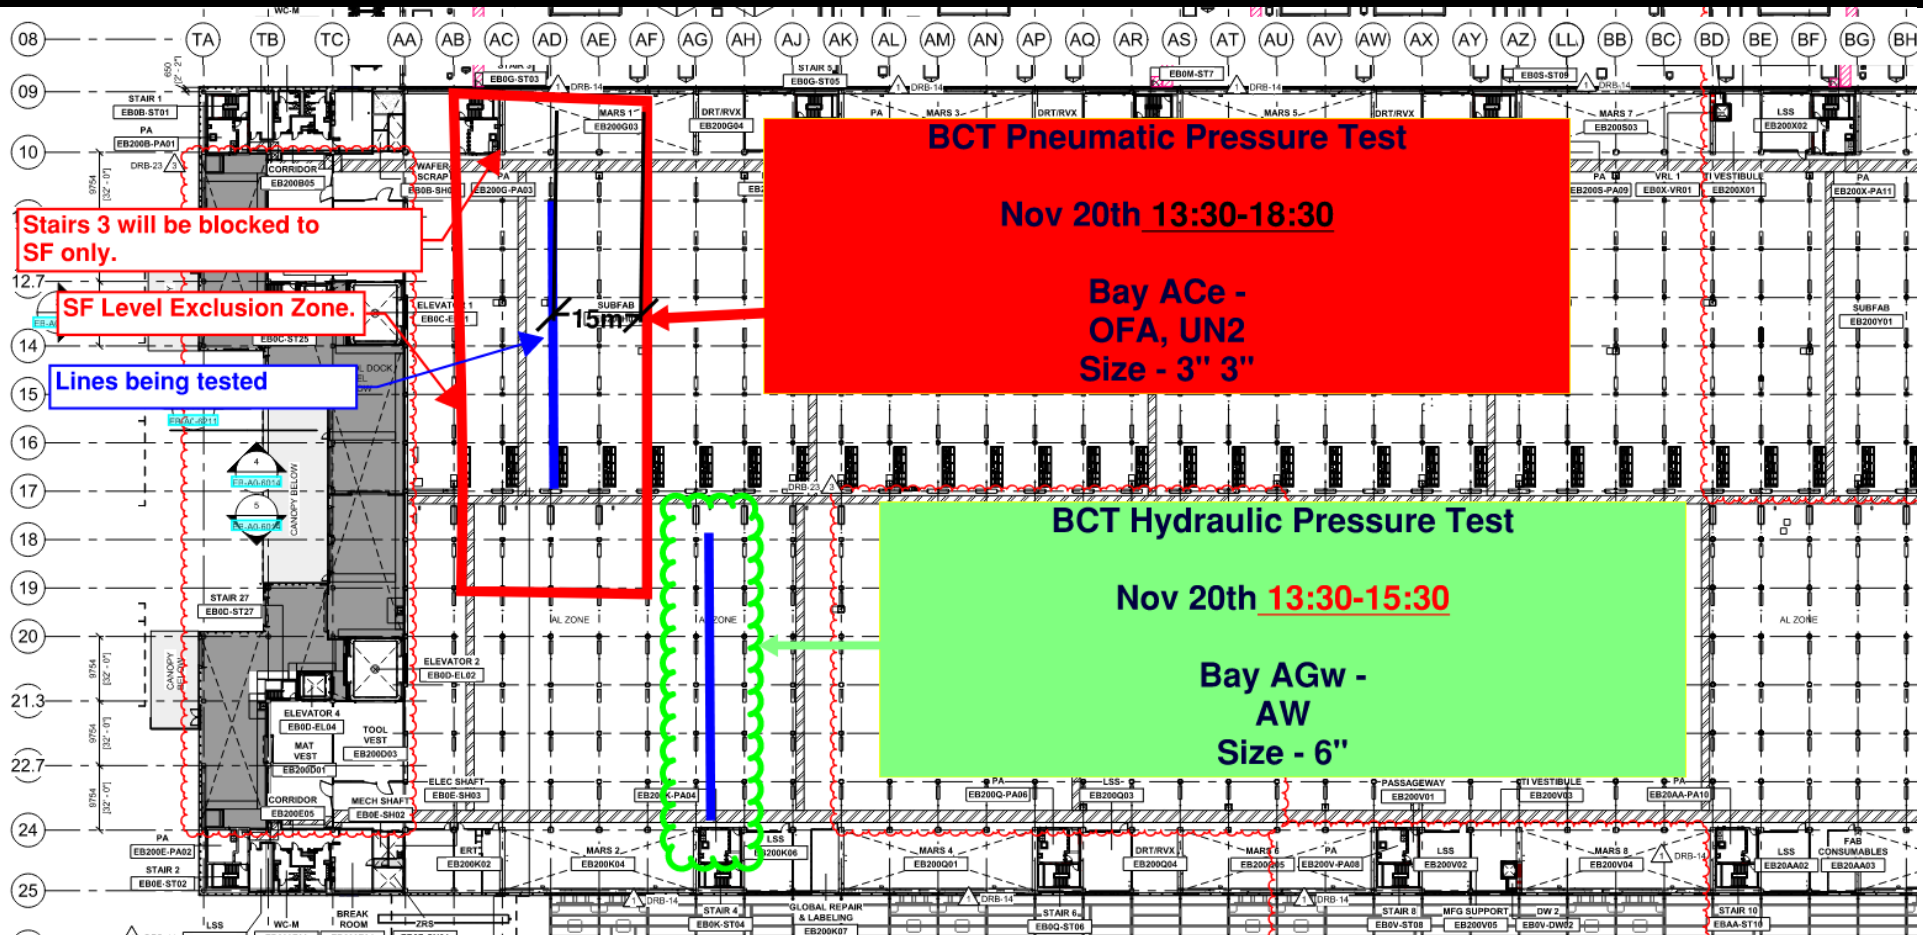




BCT Pressure Test Tomorrow

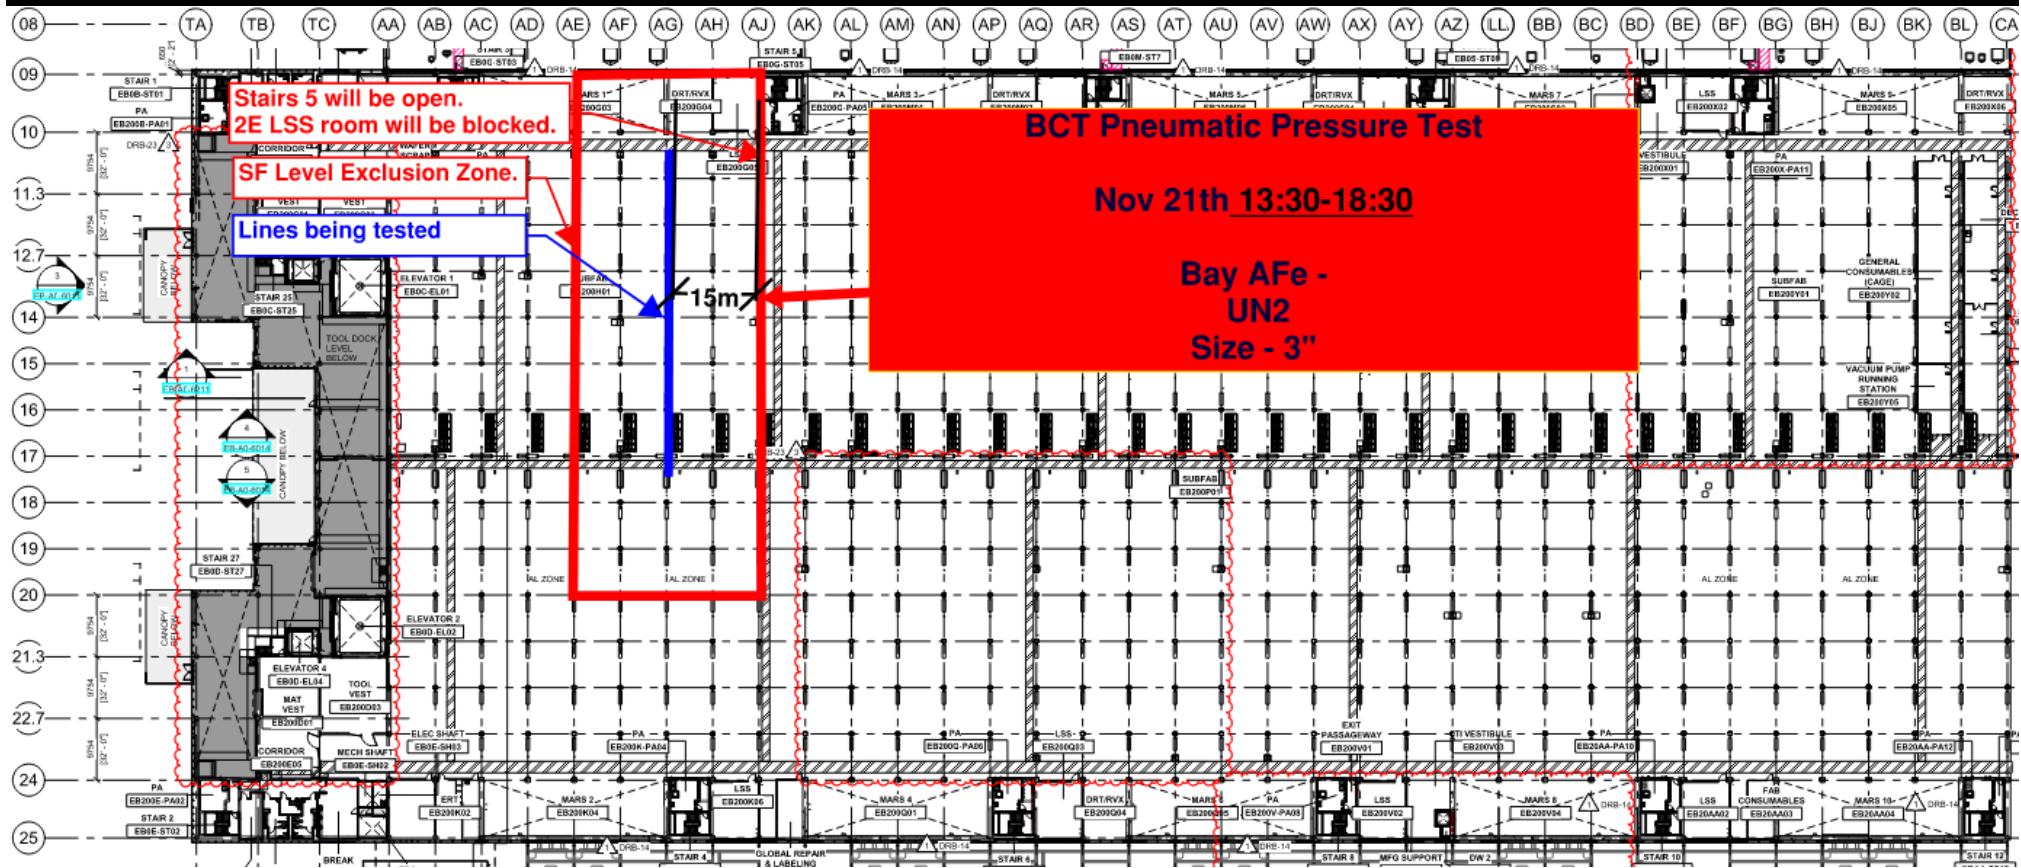

SUBFAB BUILDOUT MOD 2

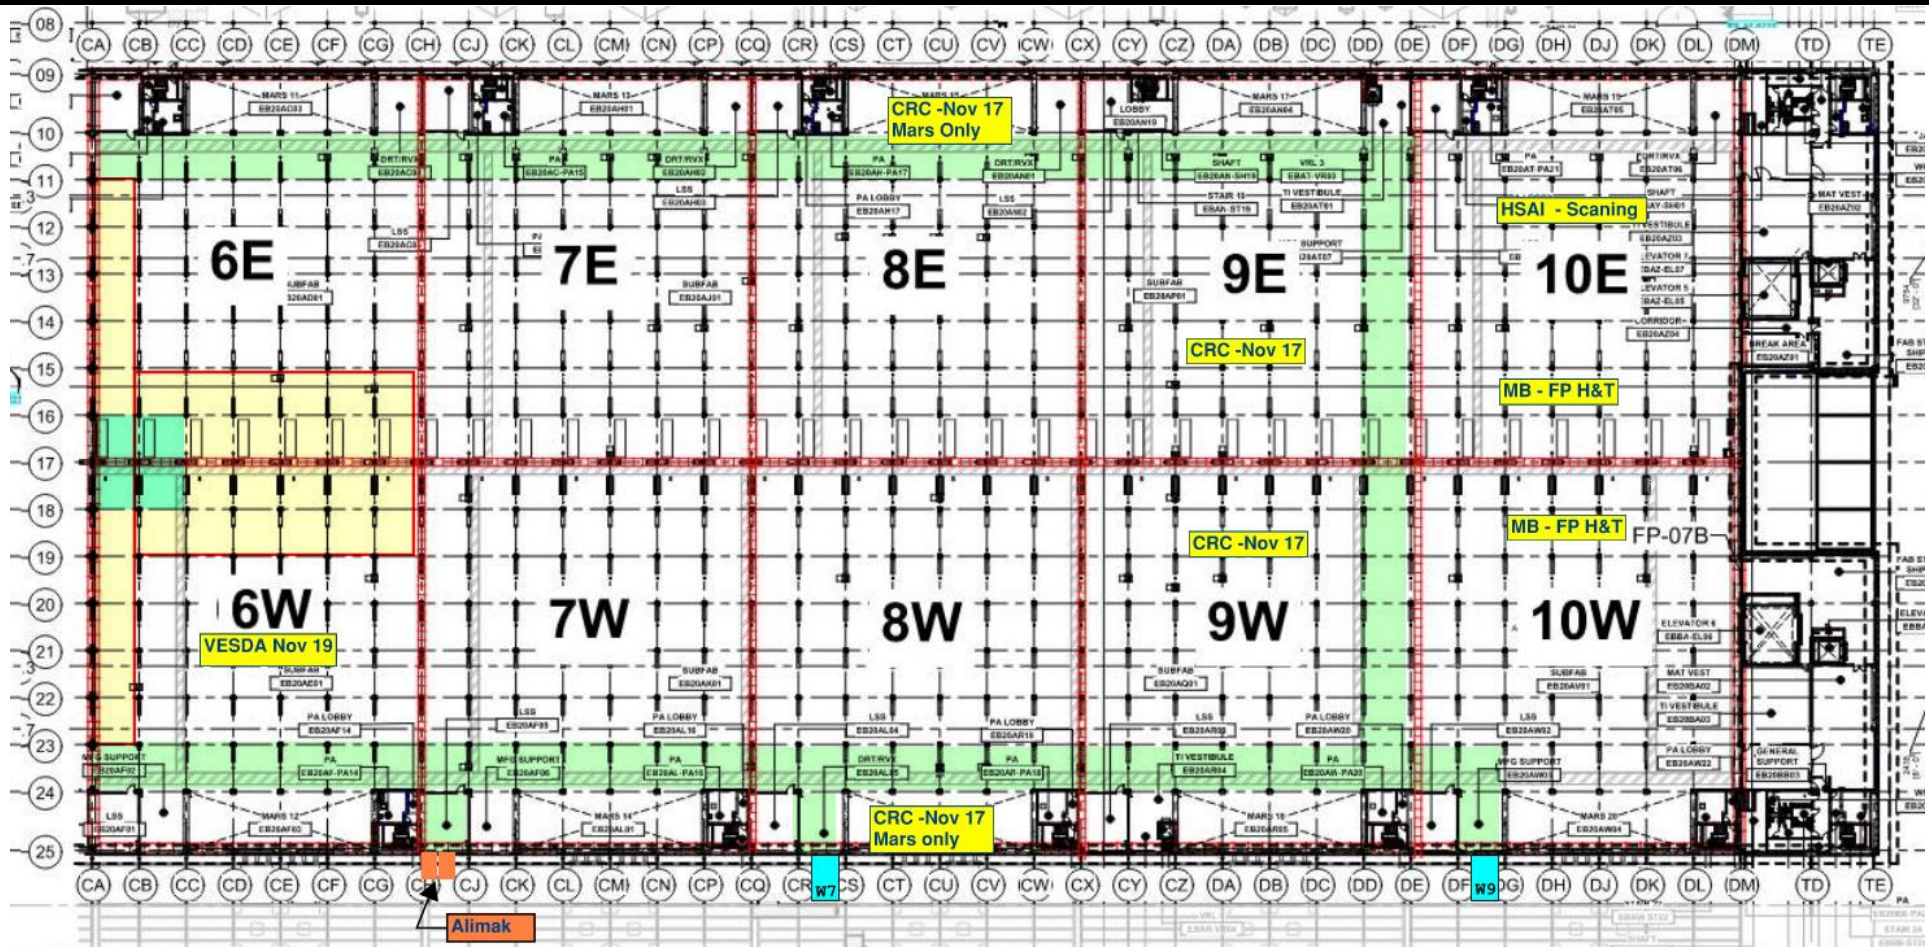

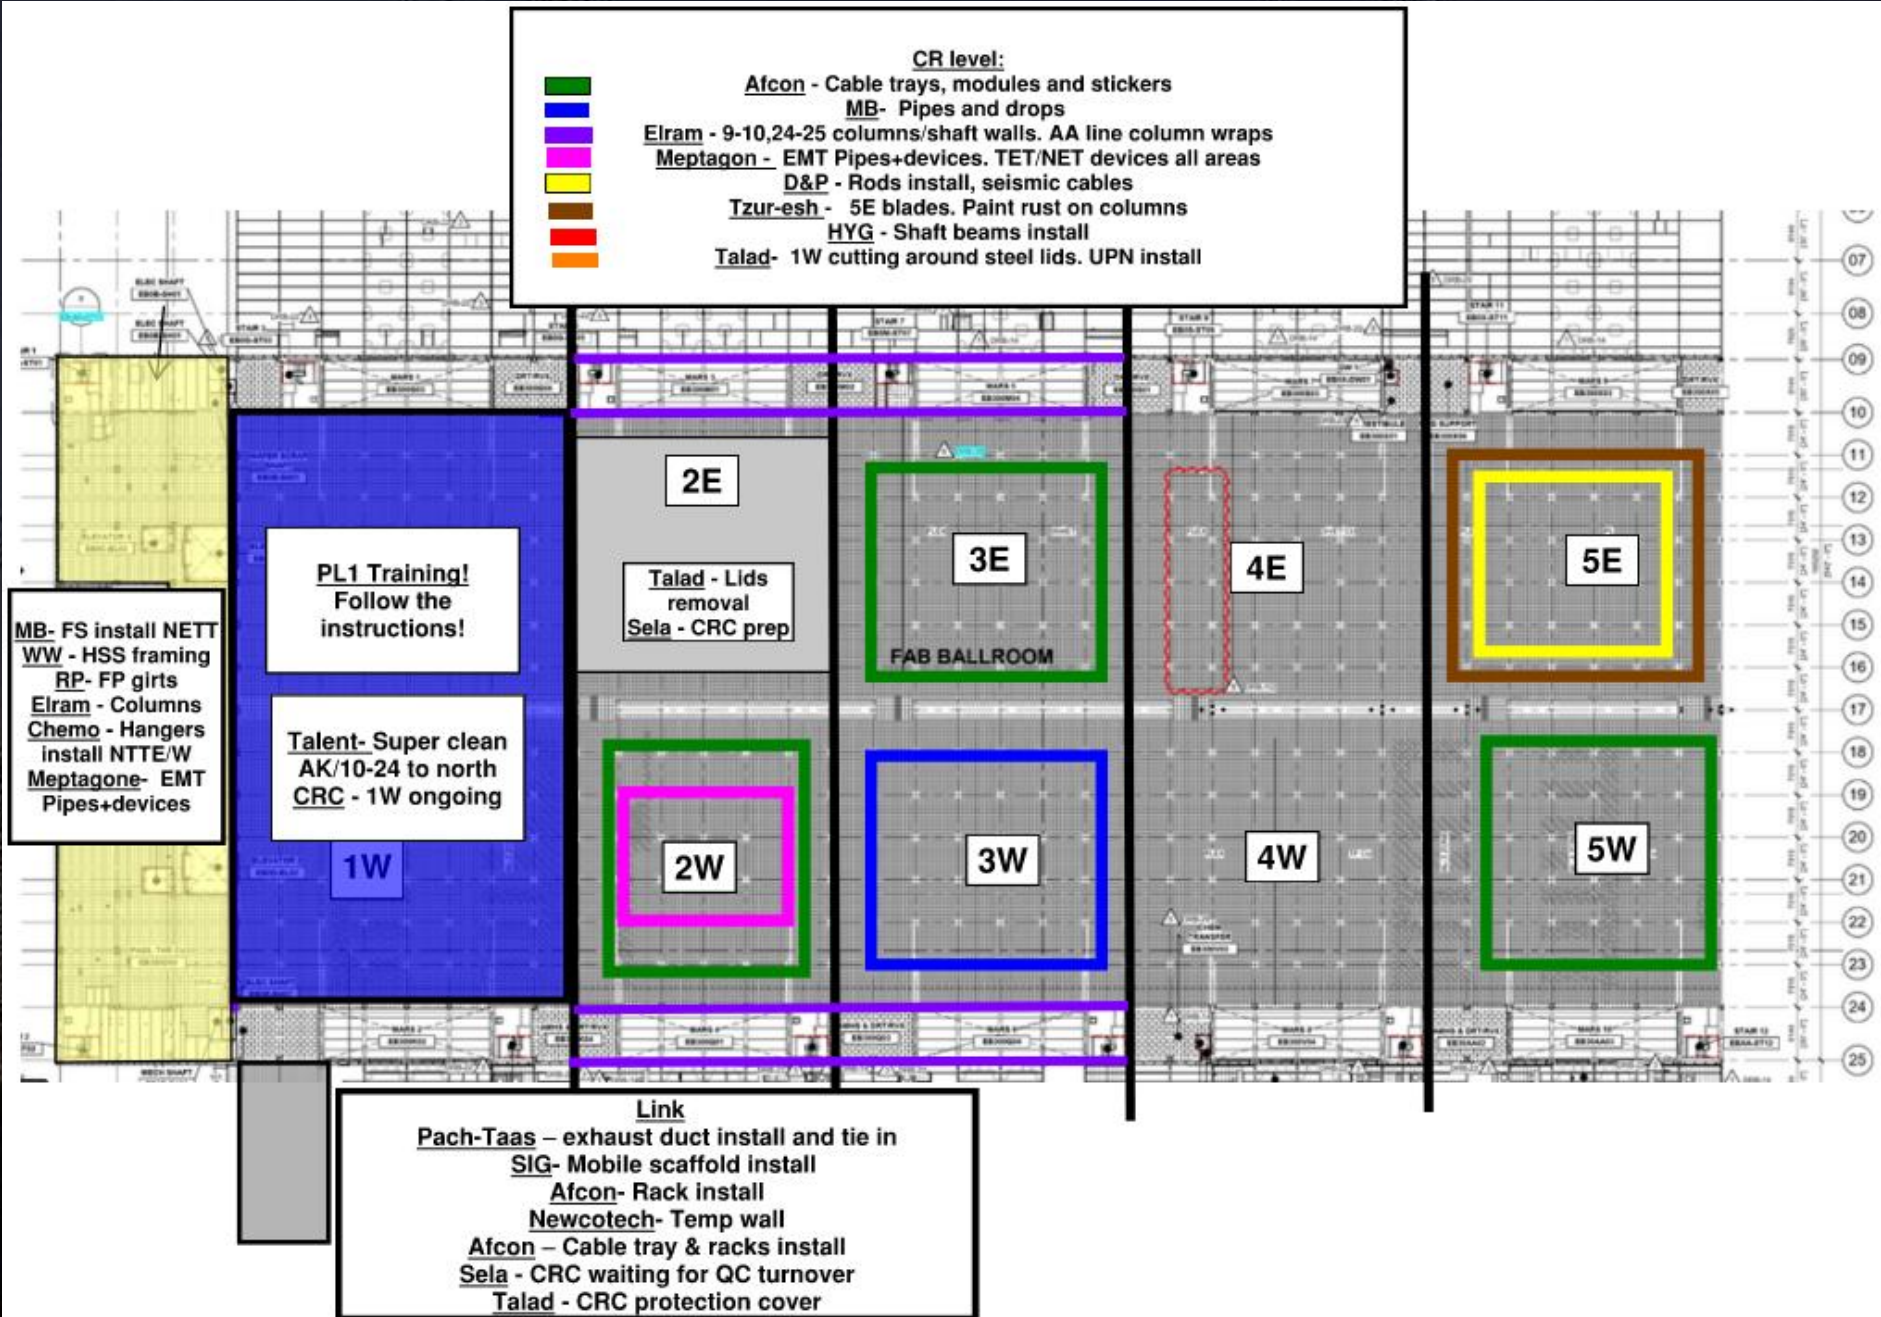

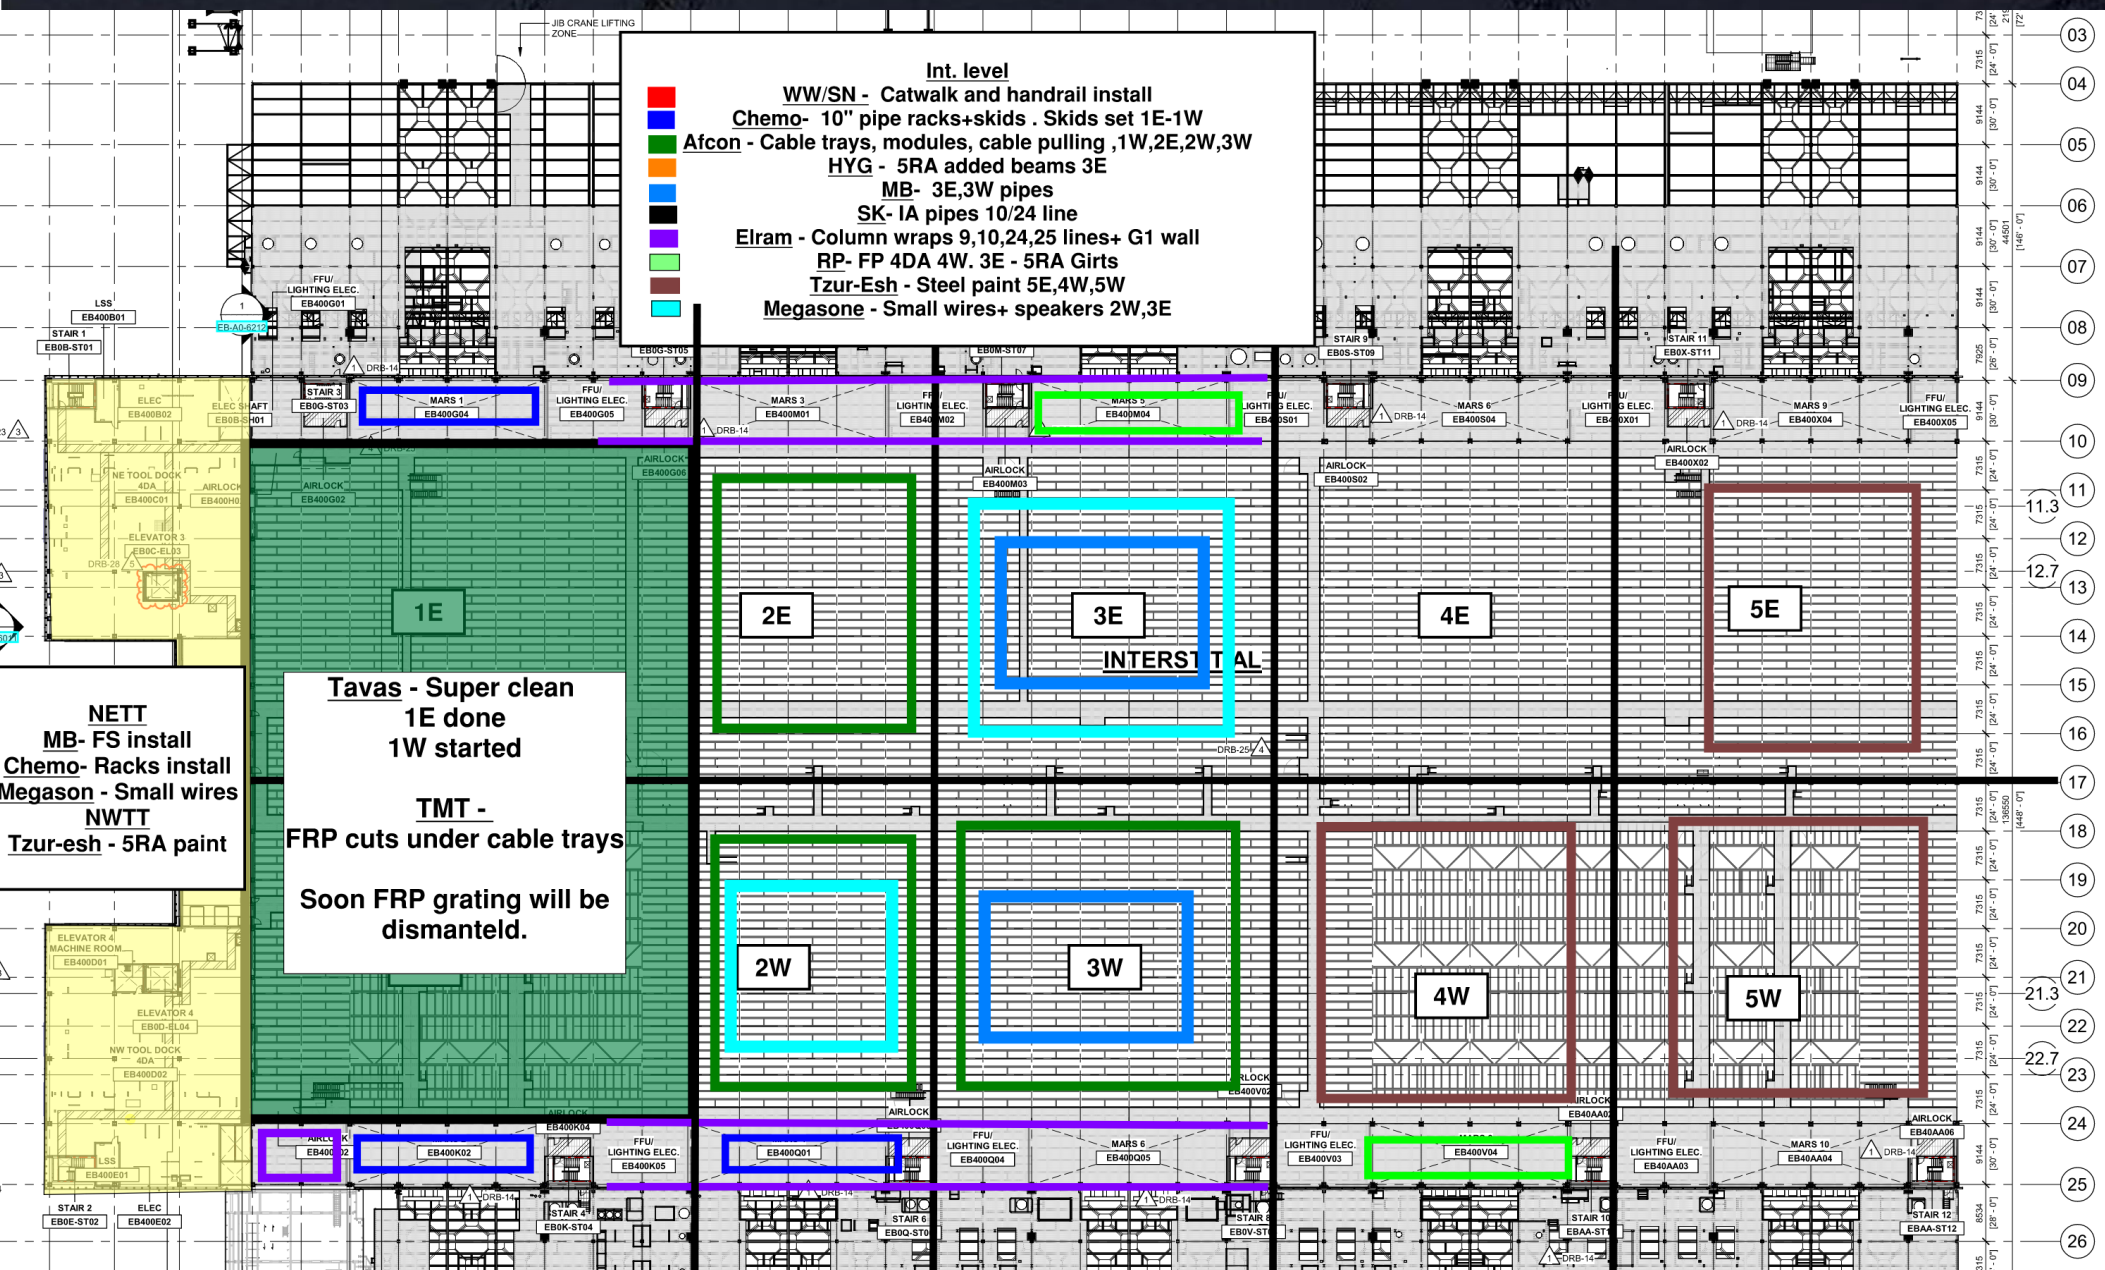



RPC - FP CA-CD
Tzur-esh - 4DA paint

In-fill ongoing

SETT
Steel
erection
onglong

Truss #24 set
Wednesday Nov-20th

SEE LIFT DATA TABLE THIS
SHEET FOR BOX TRUSS
ASSEMBLY PLACE RADIUS
TYP.


TC8 (SEE LOG-3)

TC10 (SEE LOG-3)

GRID 11 END

C.P.

113' - 10 5/8"
(34.7 m)

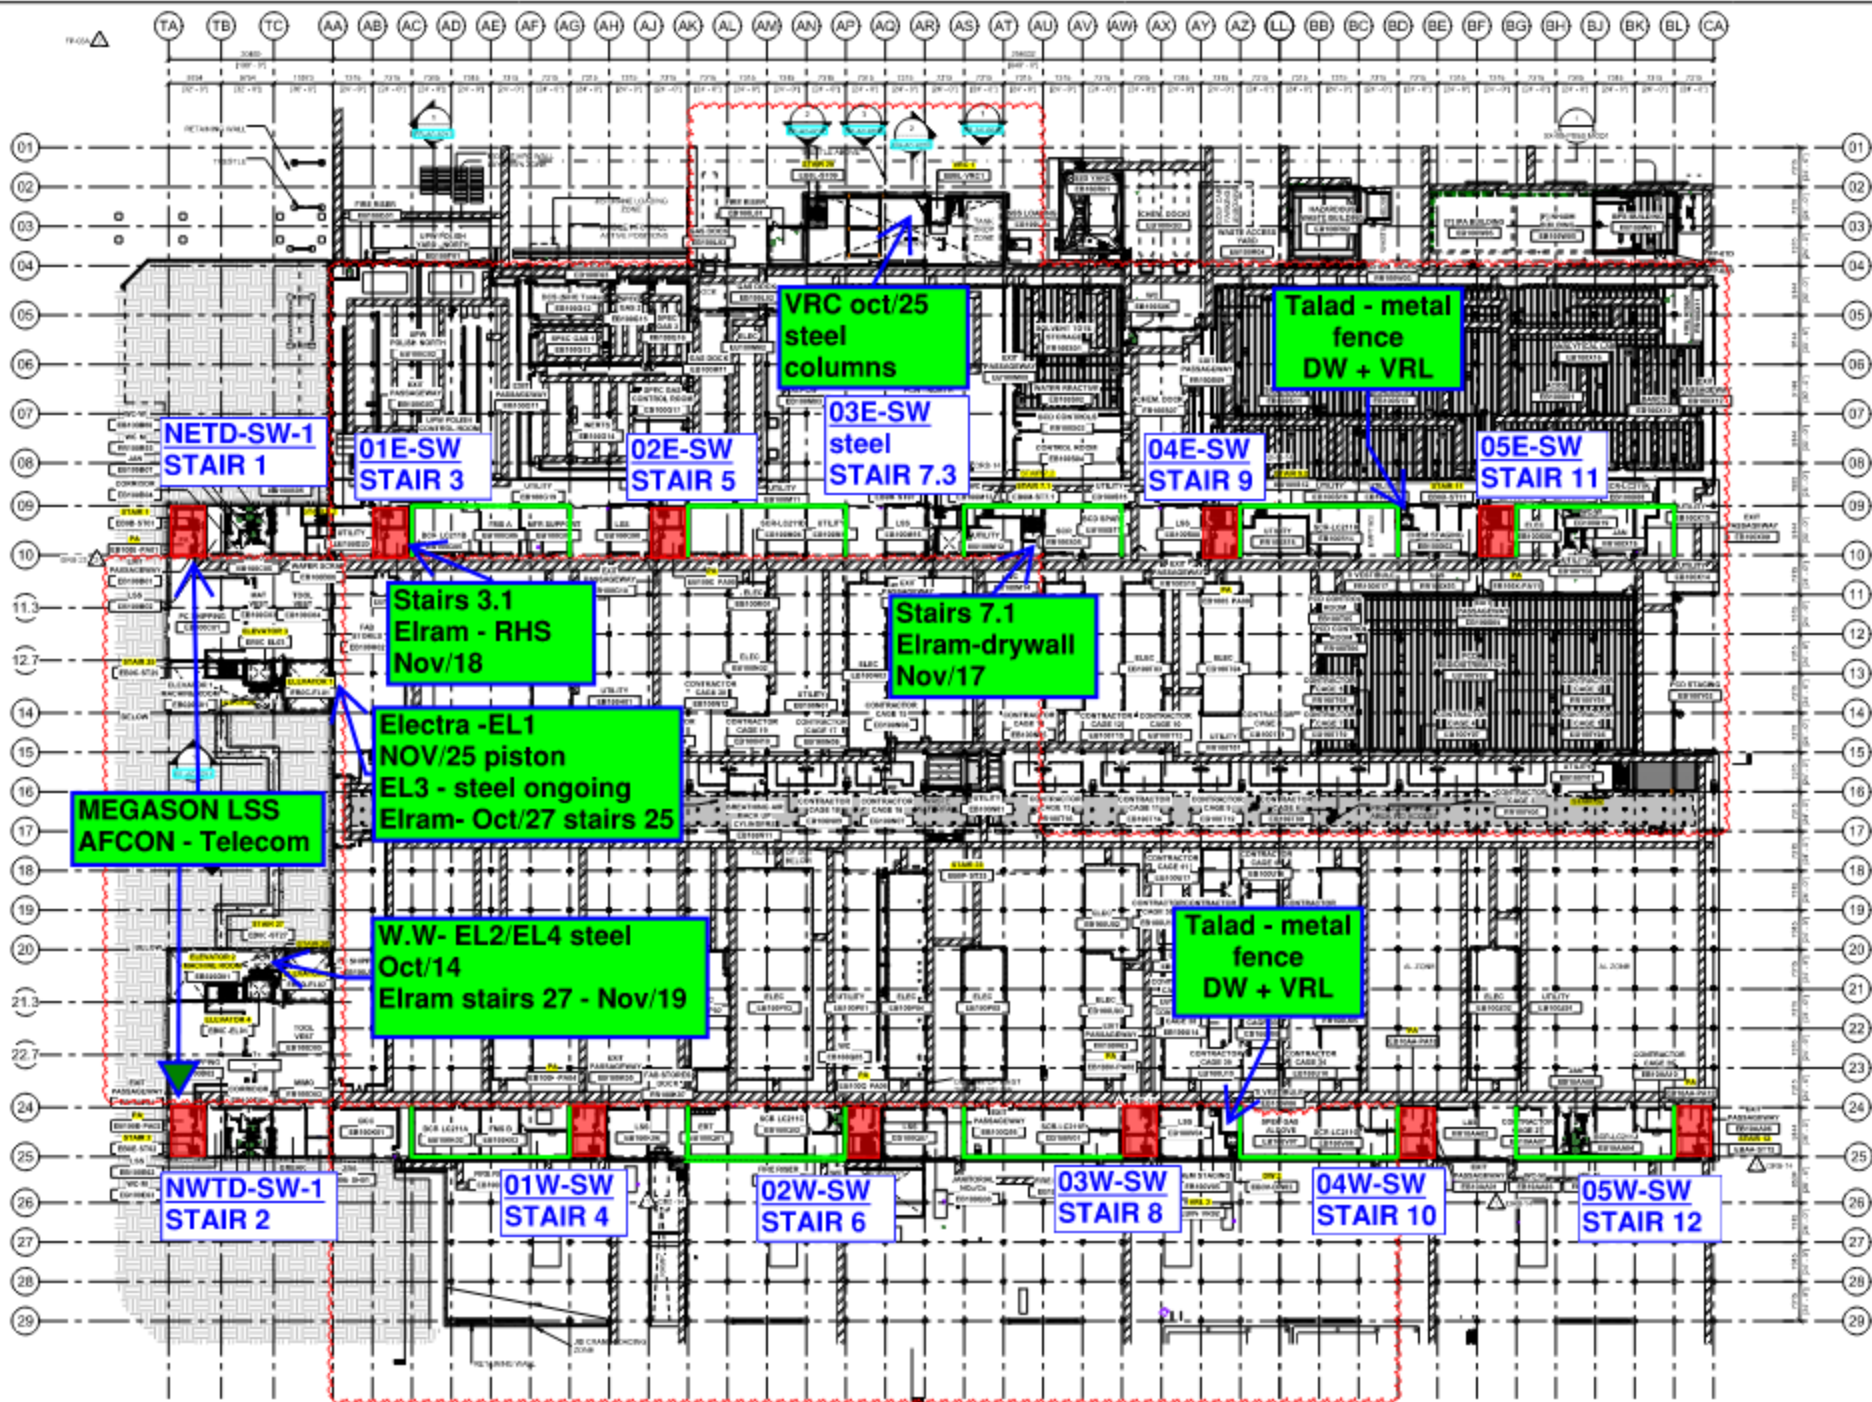


Siding - West FAB - JYG


BLOWDOWN 30%


[illegible]

[illegible][illegible]

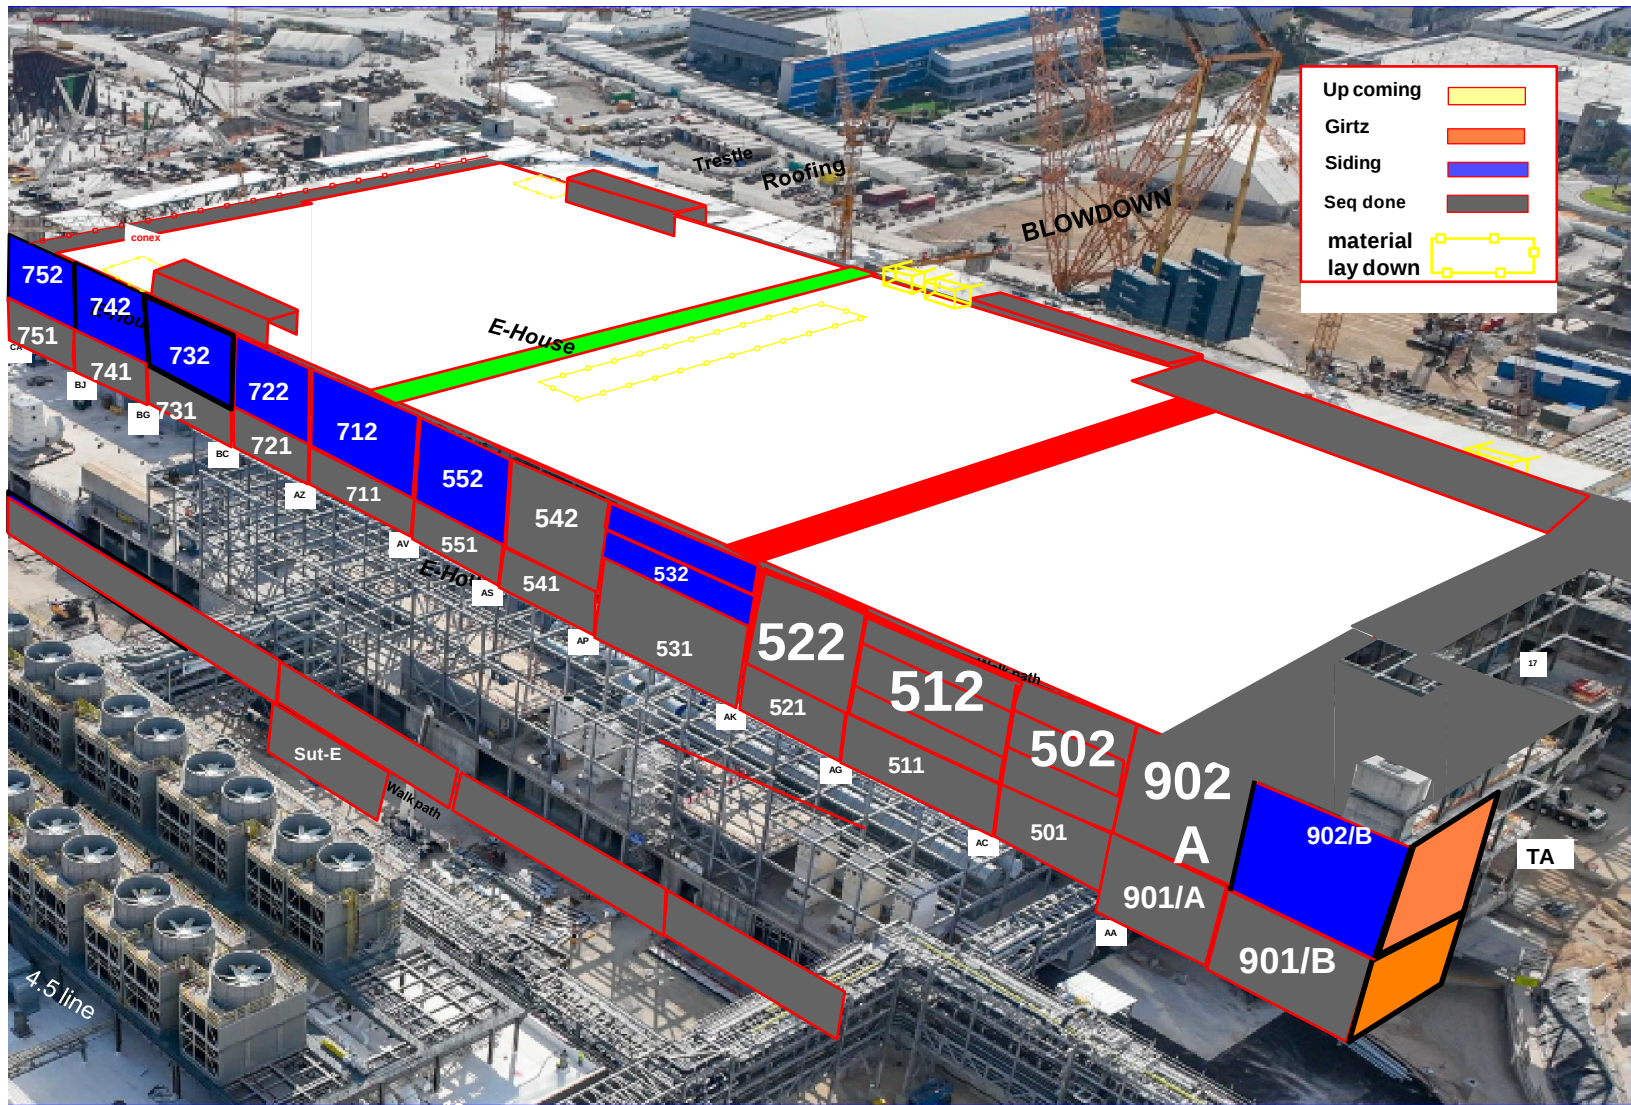

Walk path

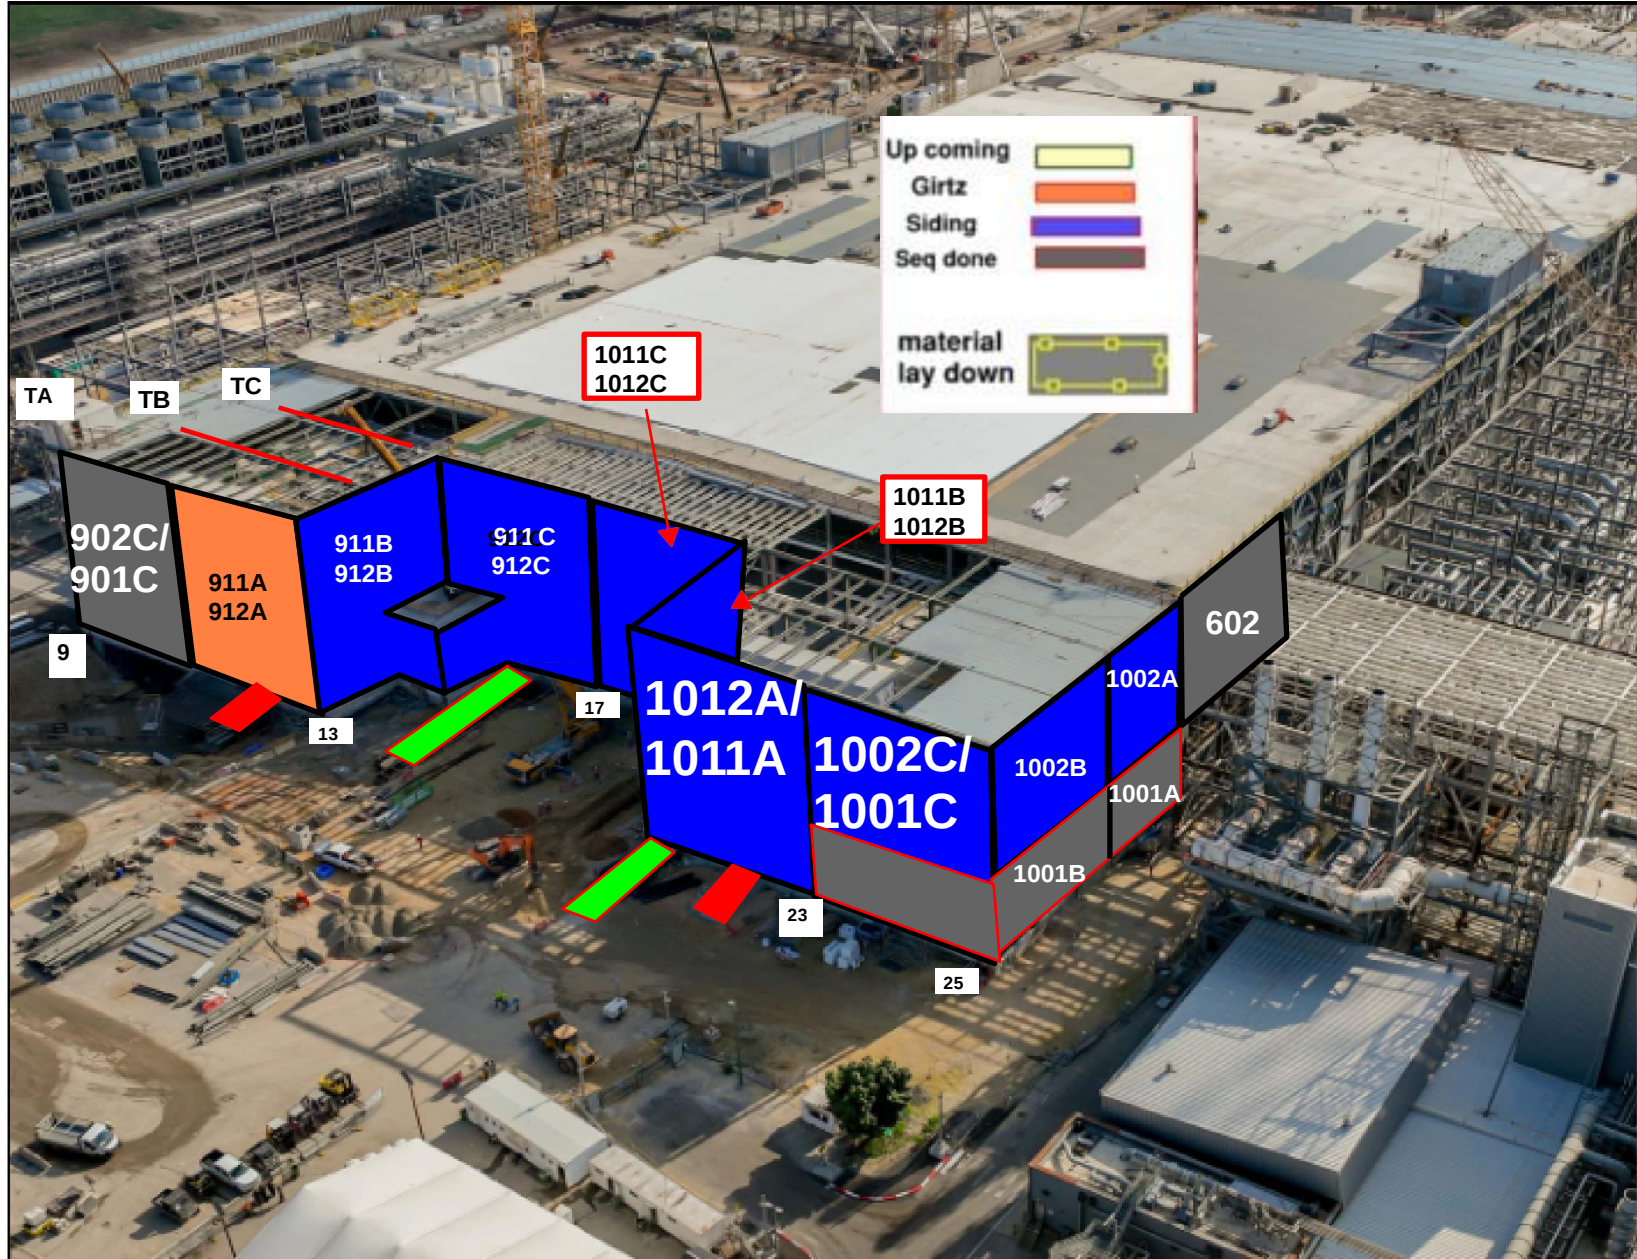


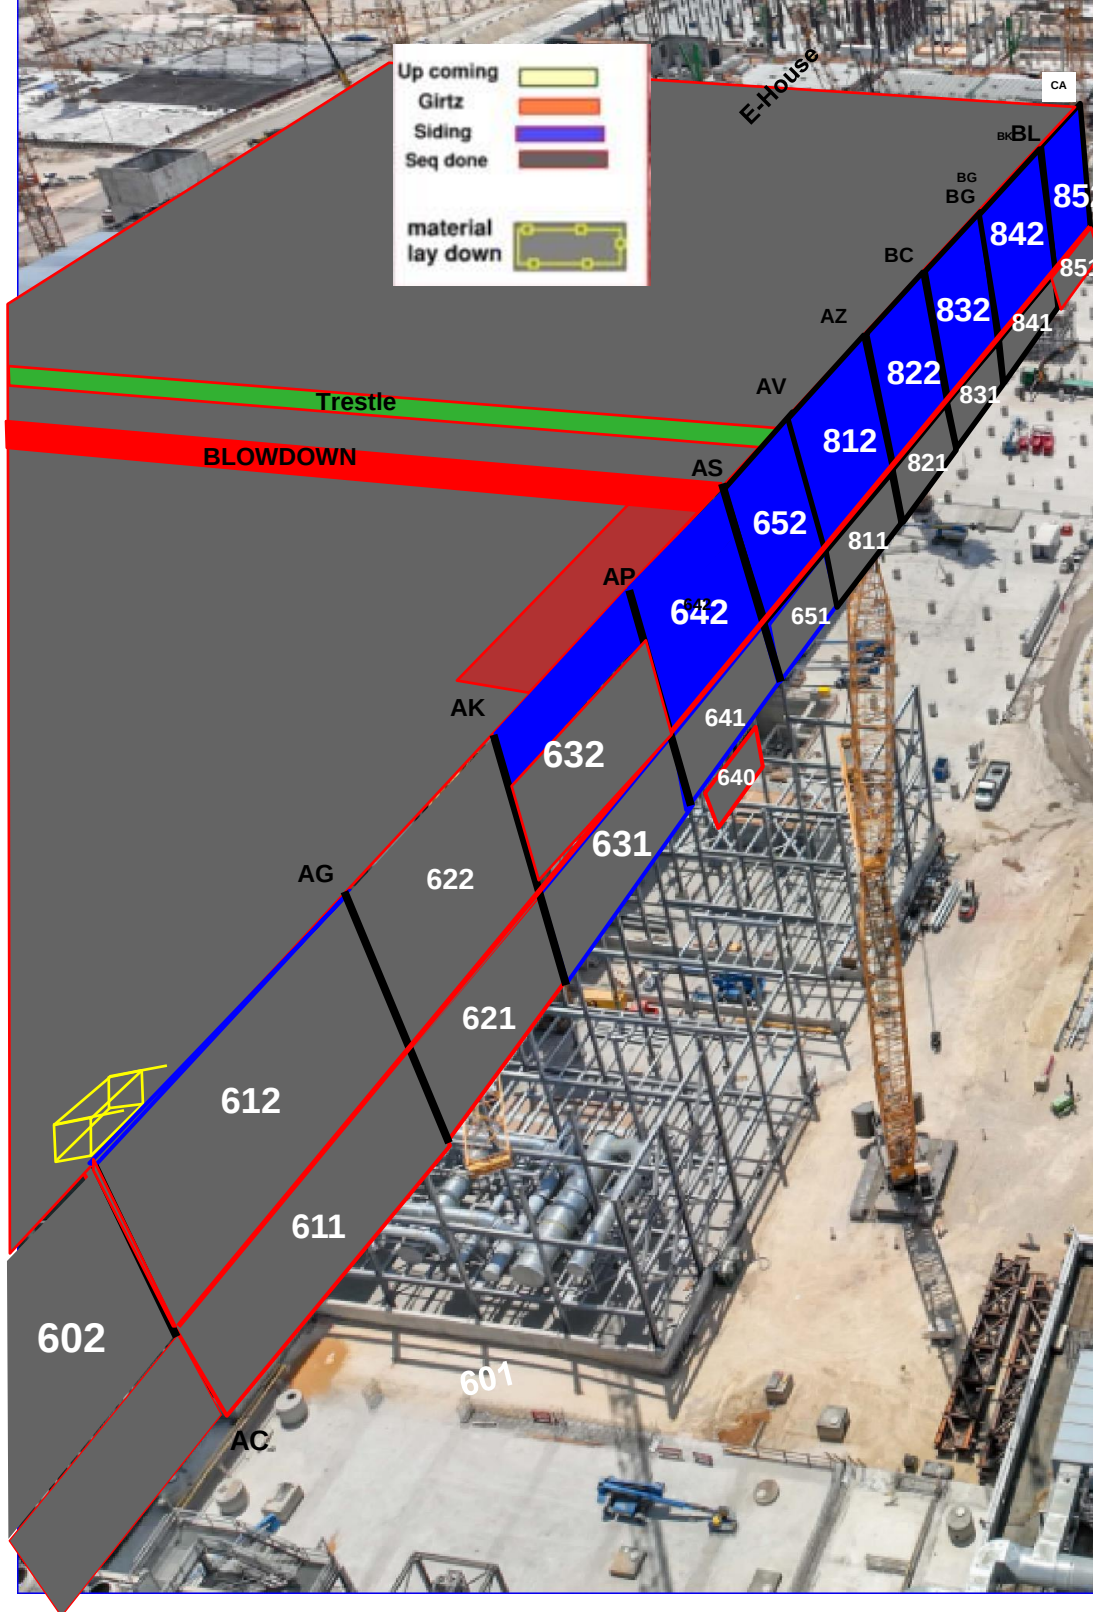

PSSS.1

Utility Level 1YA


PSSS Roof 2SA

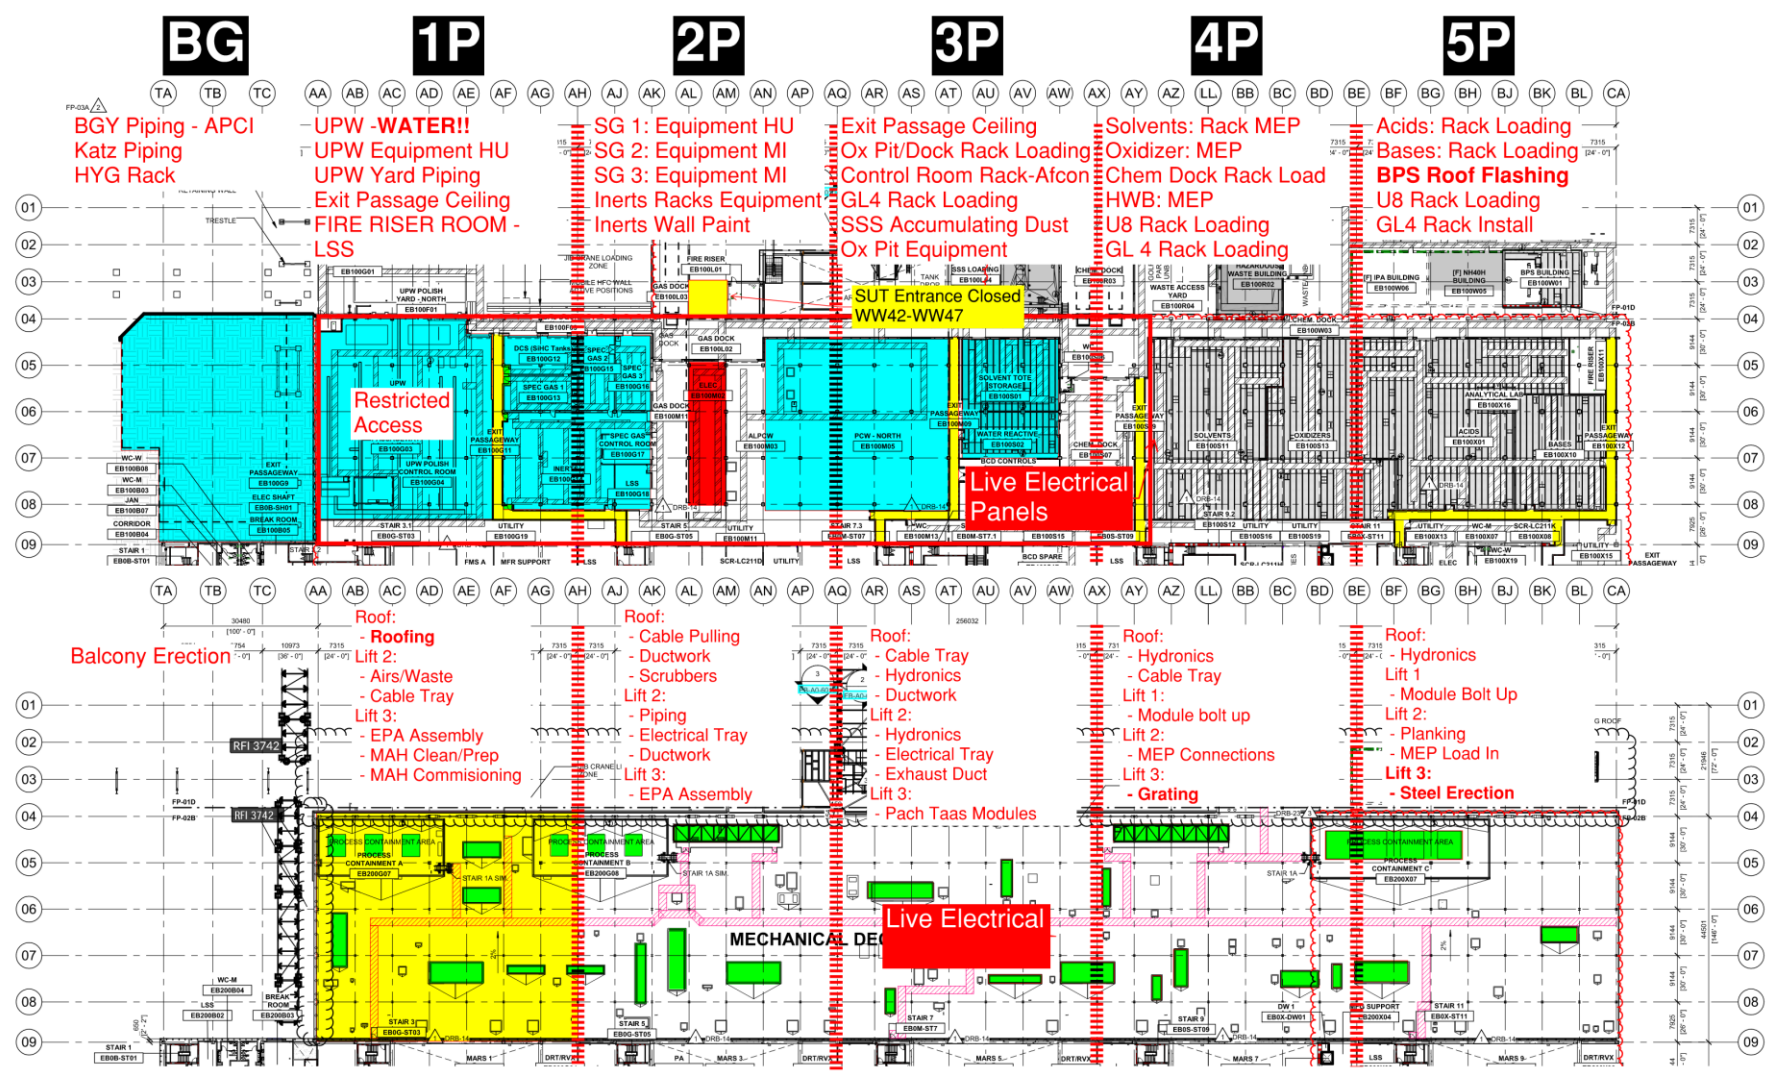


PSSS.2

Utility Level
1YA


PSSS Roof
2SA

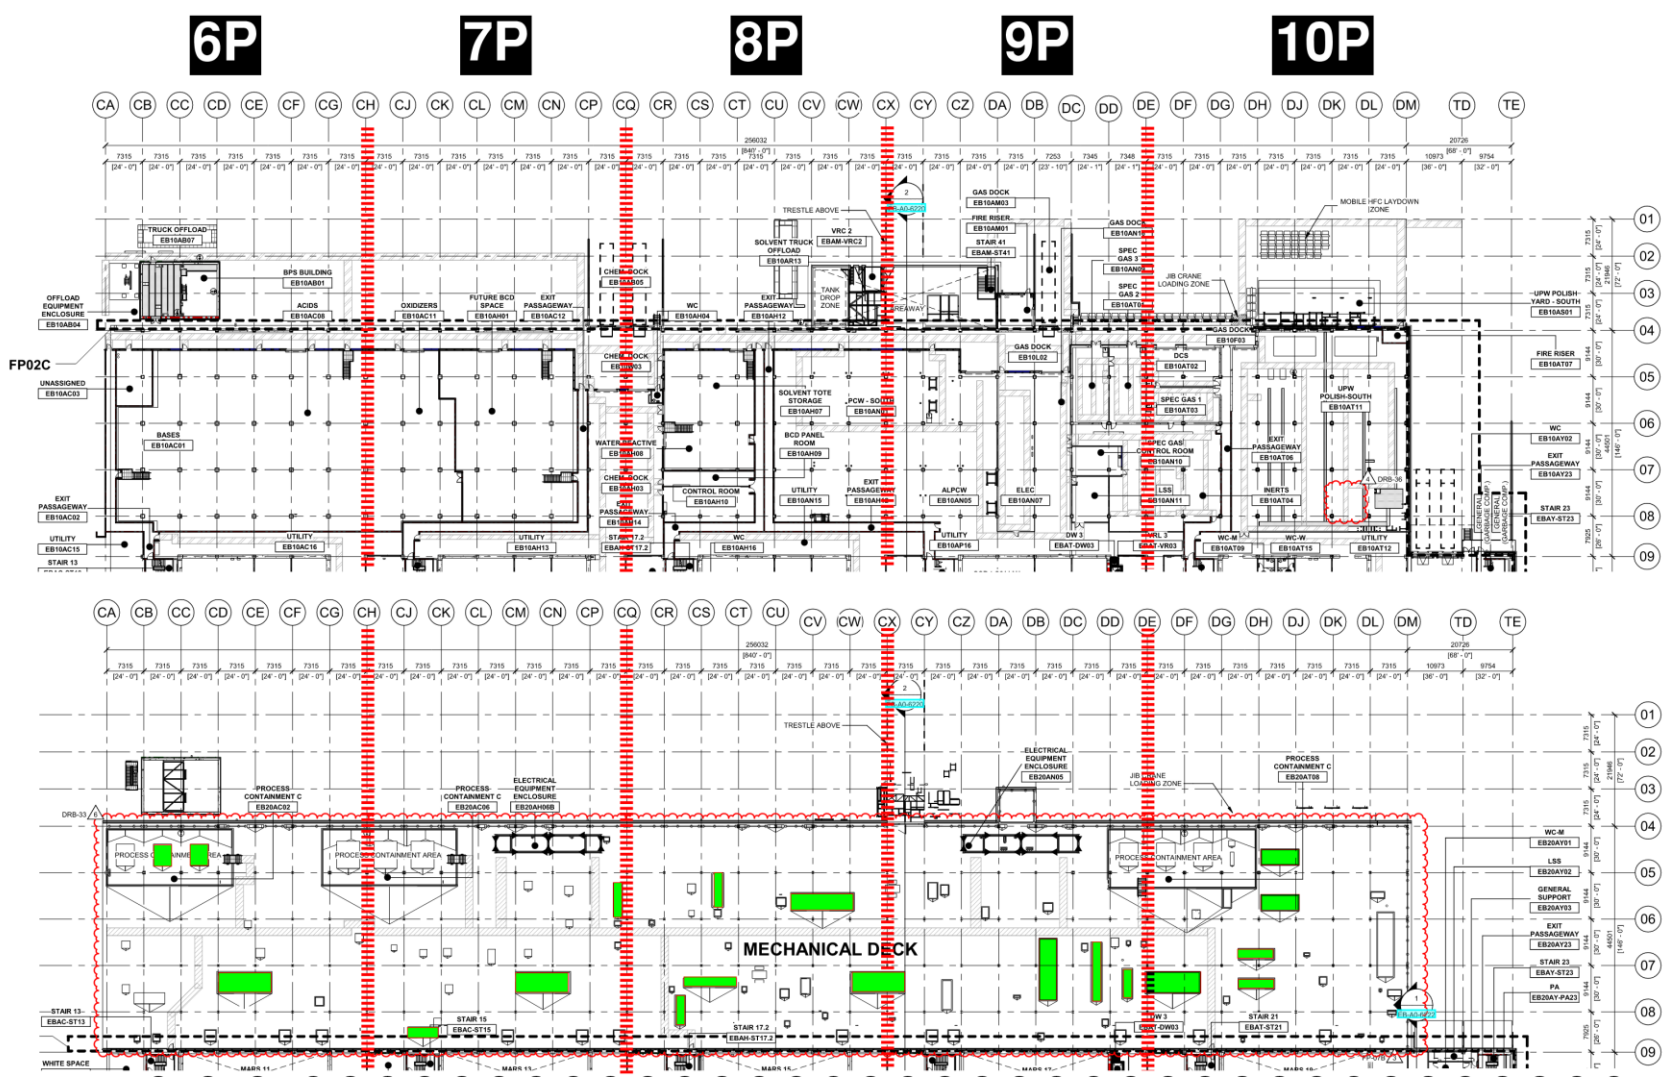


WJG 01J, 02J LIFT 2 & 3

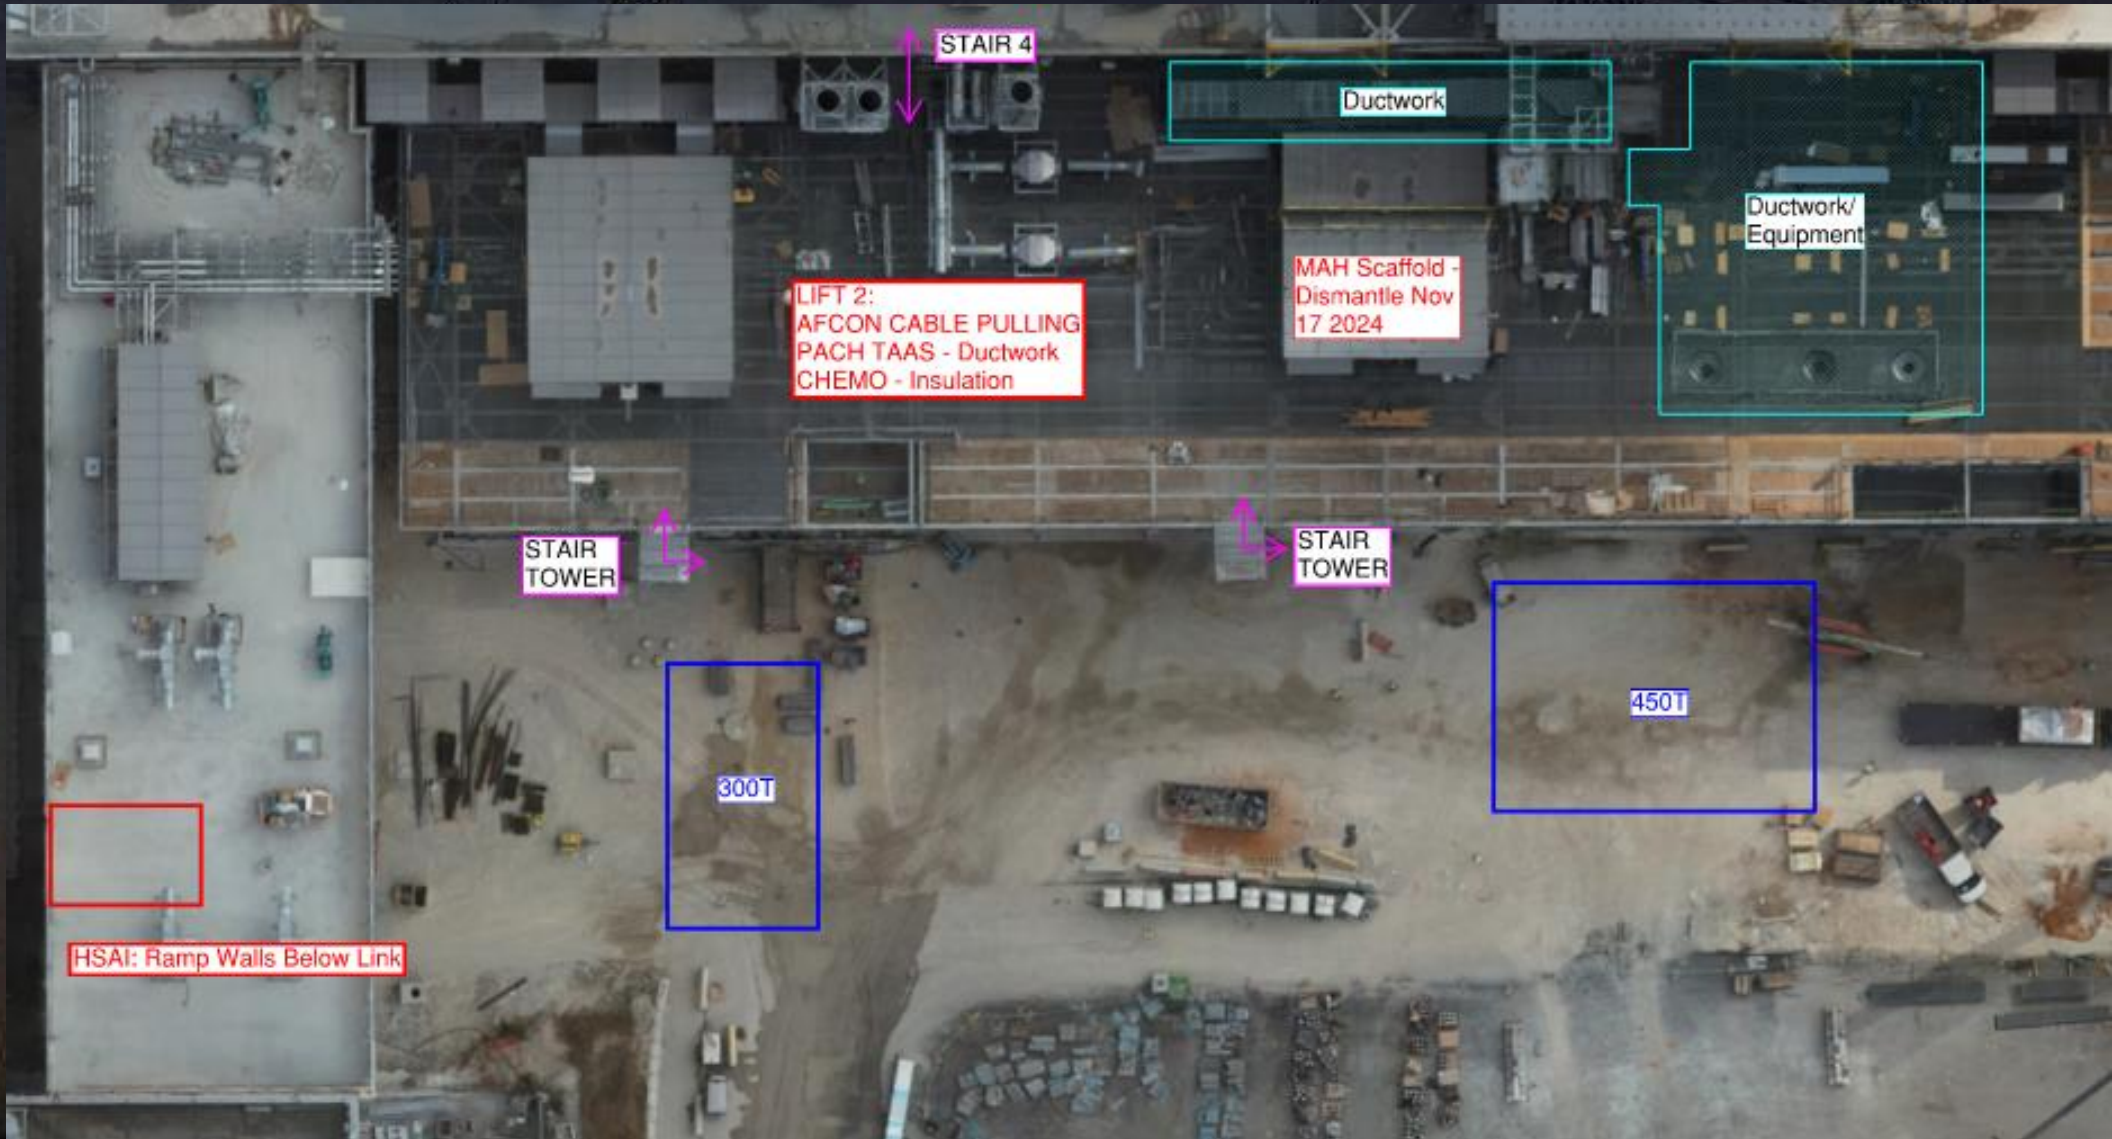


WJG 03J, 04J, 05J LIFT 2 & 3

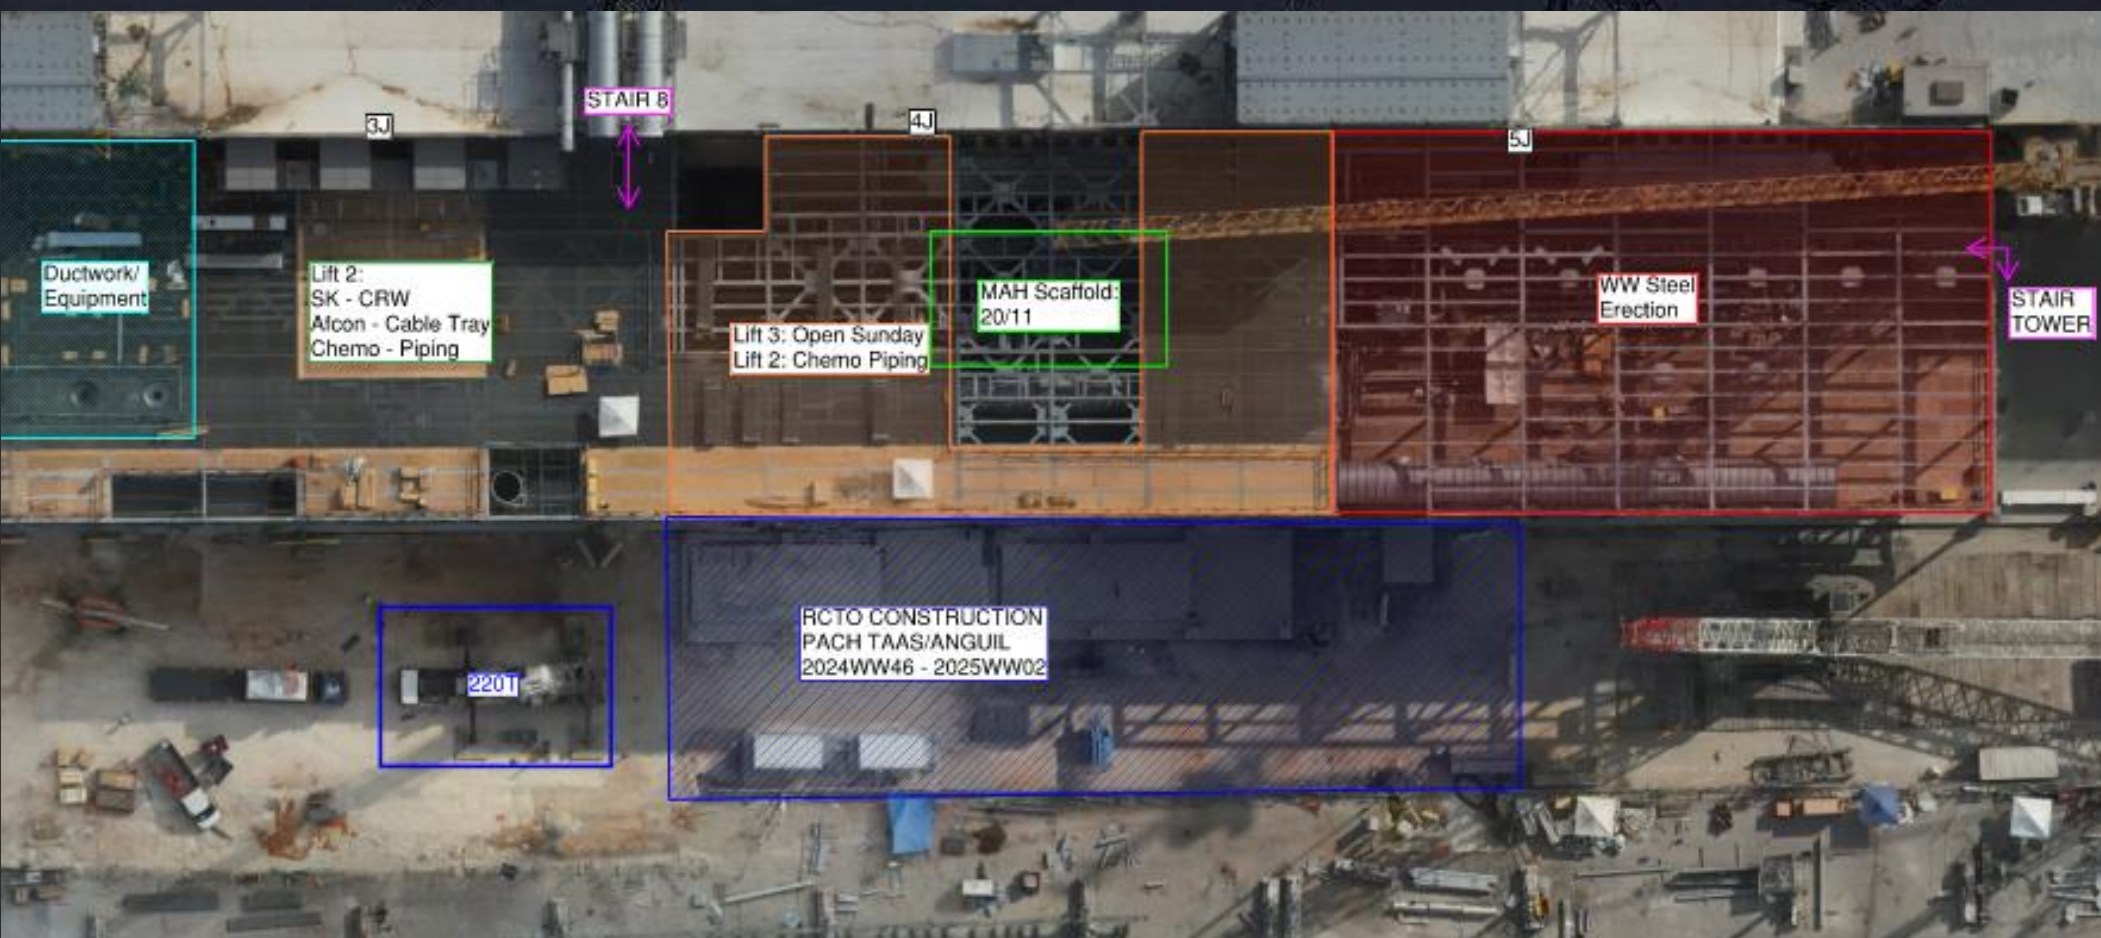




MAH101-7/8-00 Set WW47

MAH 101-7/8-00
STARTING @ 1700
17/11 - SET 1 UNIT
18/11 - SET 1 UNIT
19/11 - SET 1 UNIT + PLENUM
4J COMPLETELY CLOSED (expected
1/2 night)
5J CLOSED DURING HOIST

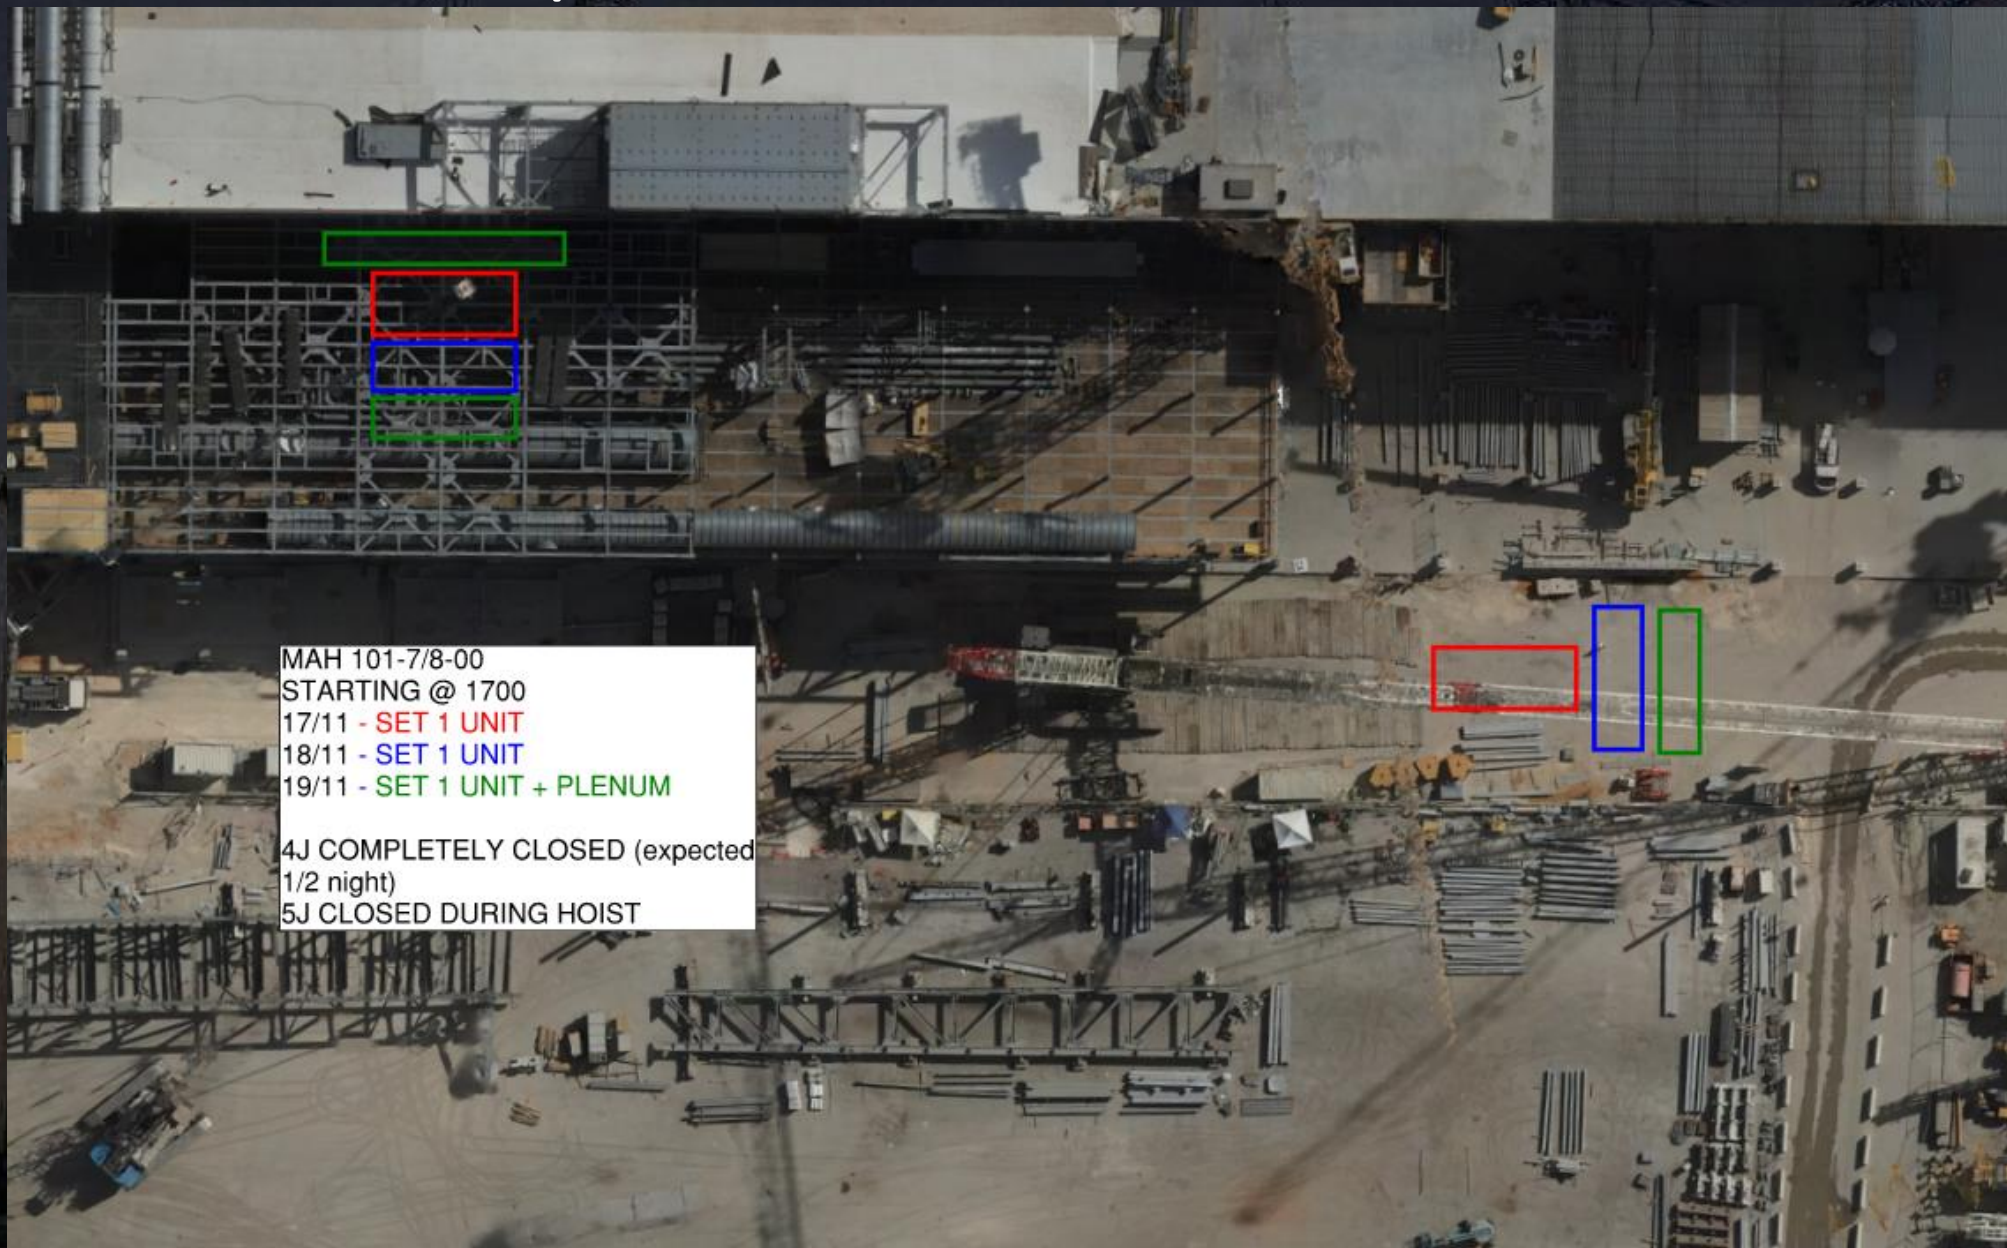

WJG UTILITY LEVEL BUILD OUT

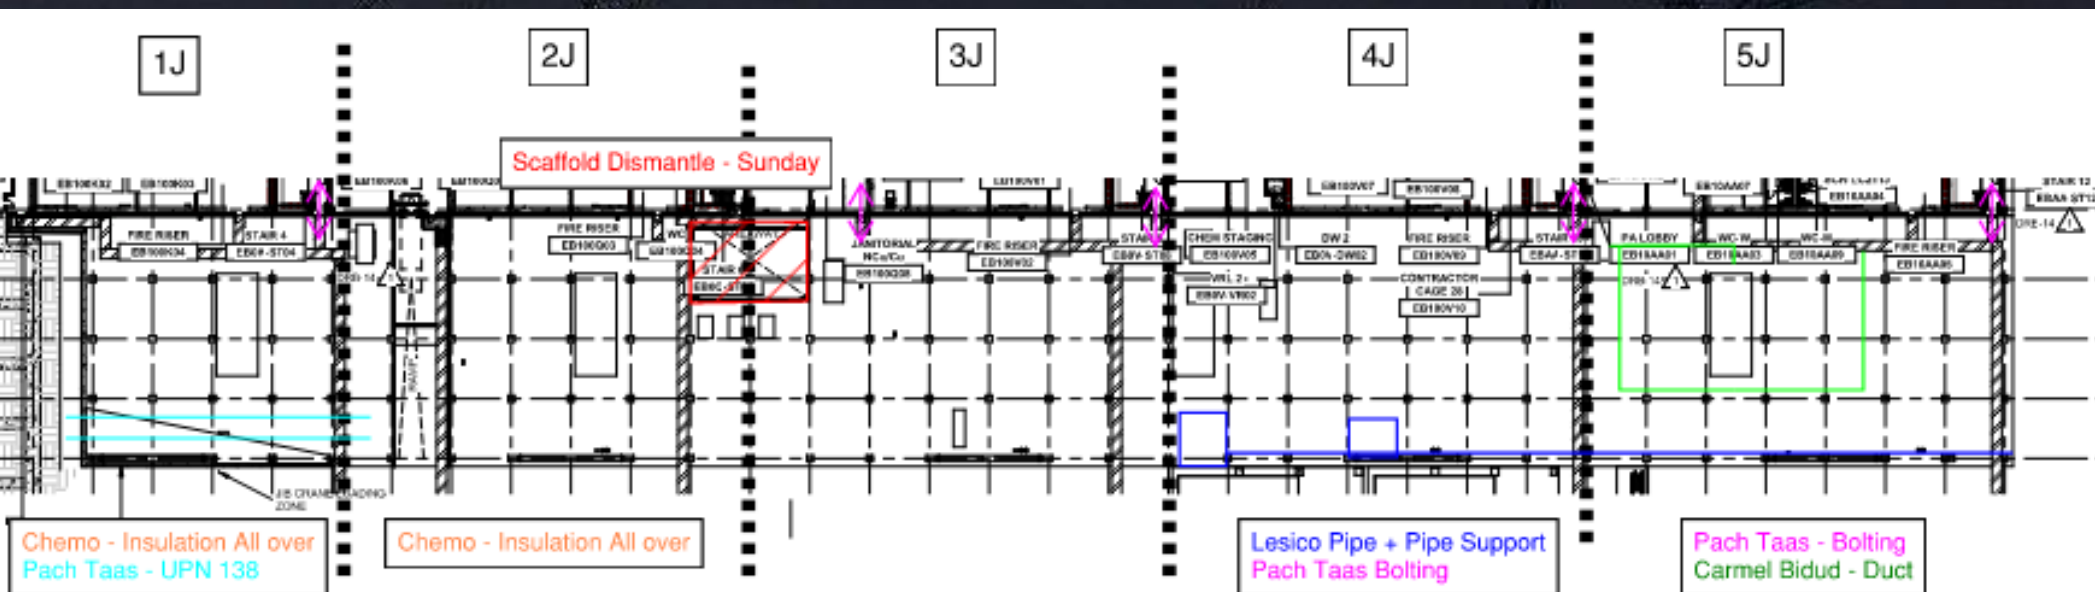

CUB 1 EVACUATION MUSTER LOCATION

NORTH YARD

WATER TREATMENT

SAND FILTERS

CHILLERS


BOILERS

EGRESS KEEP CLEAR

NOTE:


1. REFRIGERANT DETECTION SYSTEM IS LIVE.
2. IF ANY ALARM IS SOUNDED-ALL WORKERS MUST EVACUATE THE BUILDING
3. EVACUATION LOCATION TO E IN NORTH YARD OF CUB 1

CUB 1 – EXTERIOR/ROOF

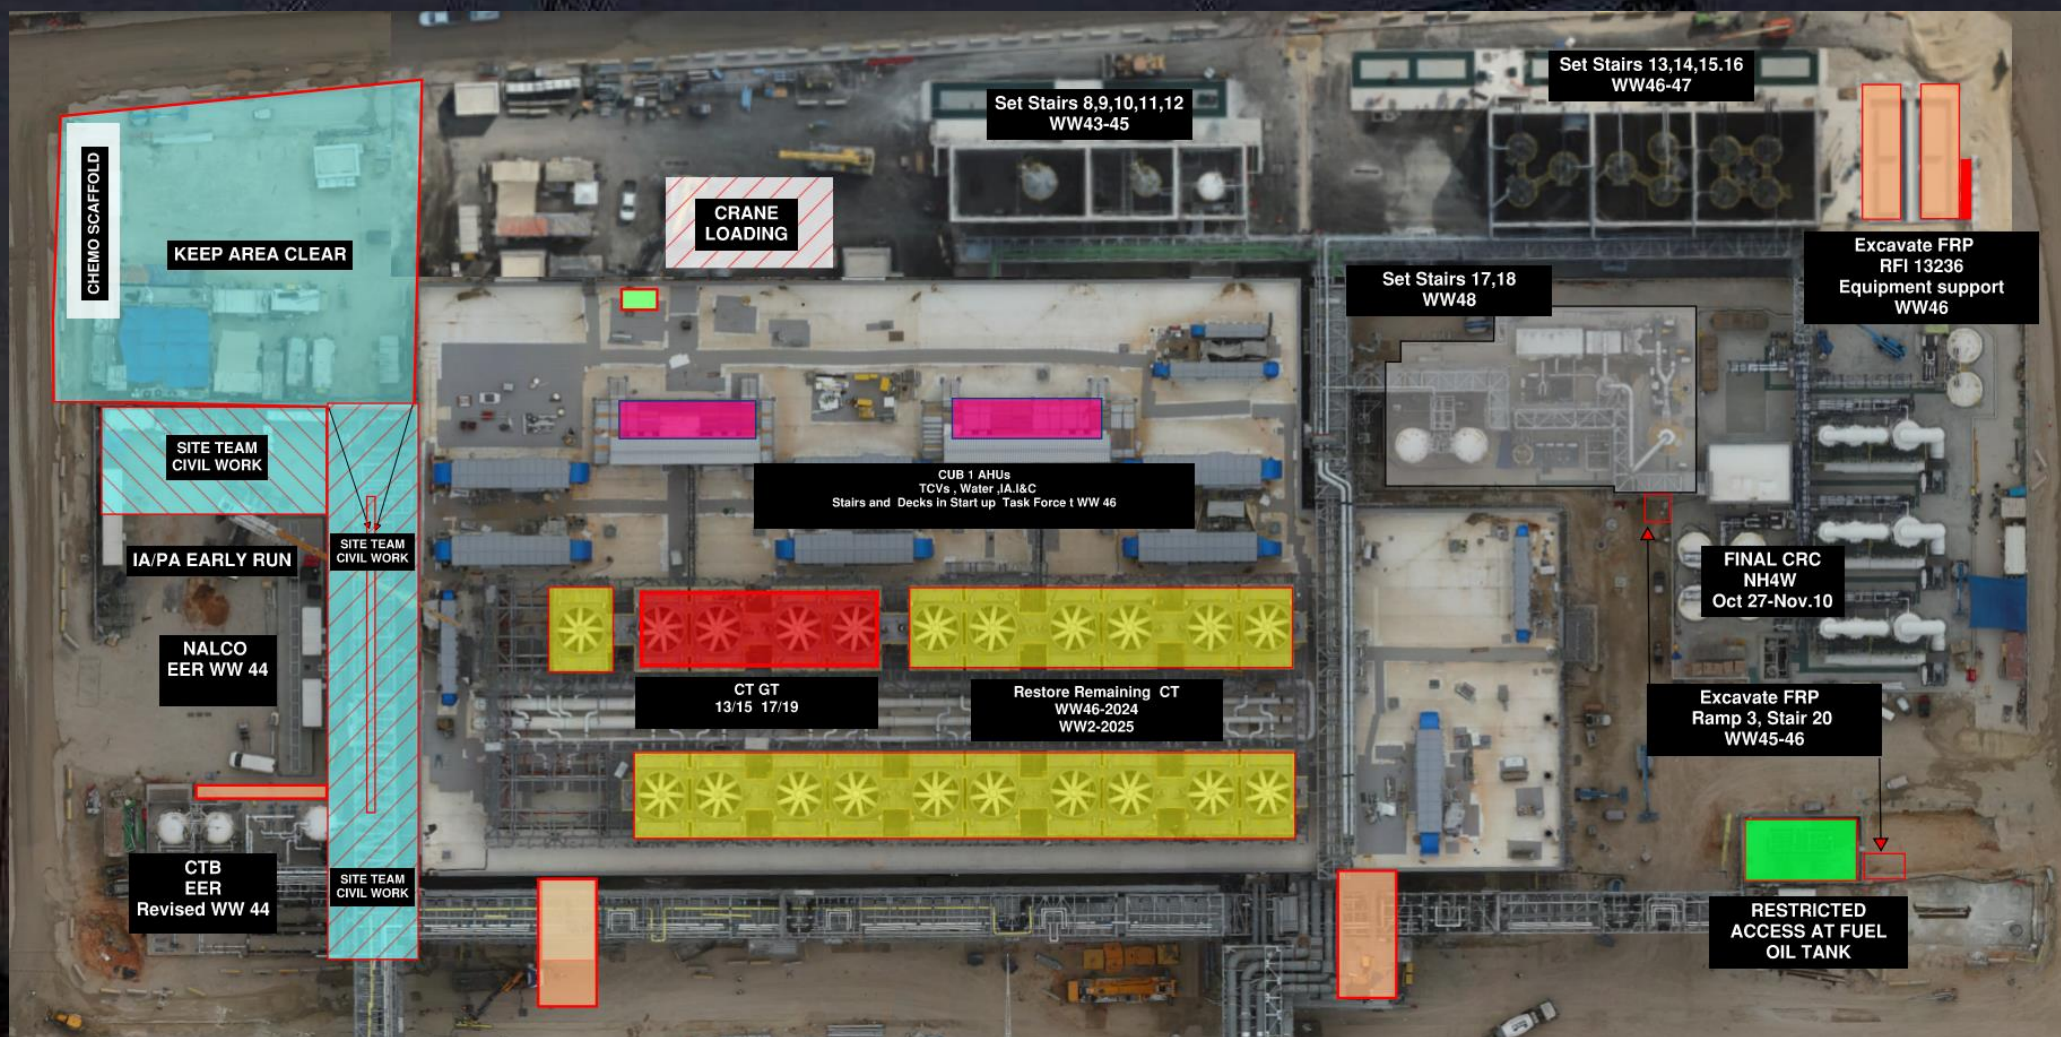

HOFFMAN CONSTRUCTION COMPANY
 OF ISRAEL


CUB 2 – EXTERIOR/ROOF

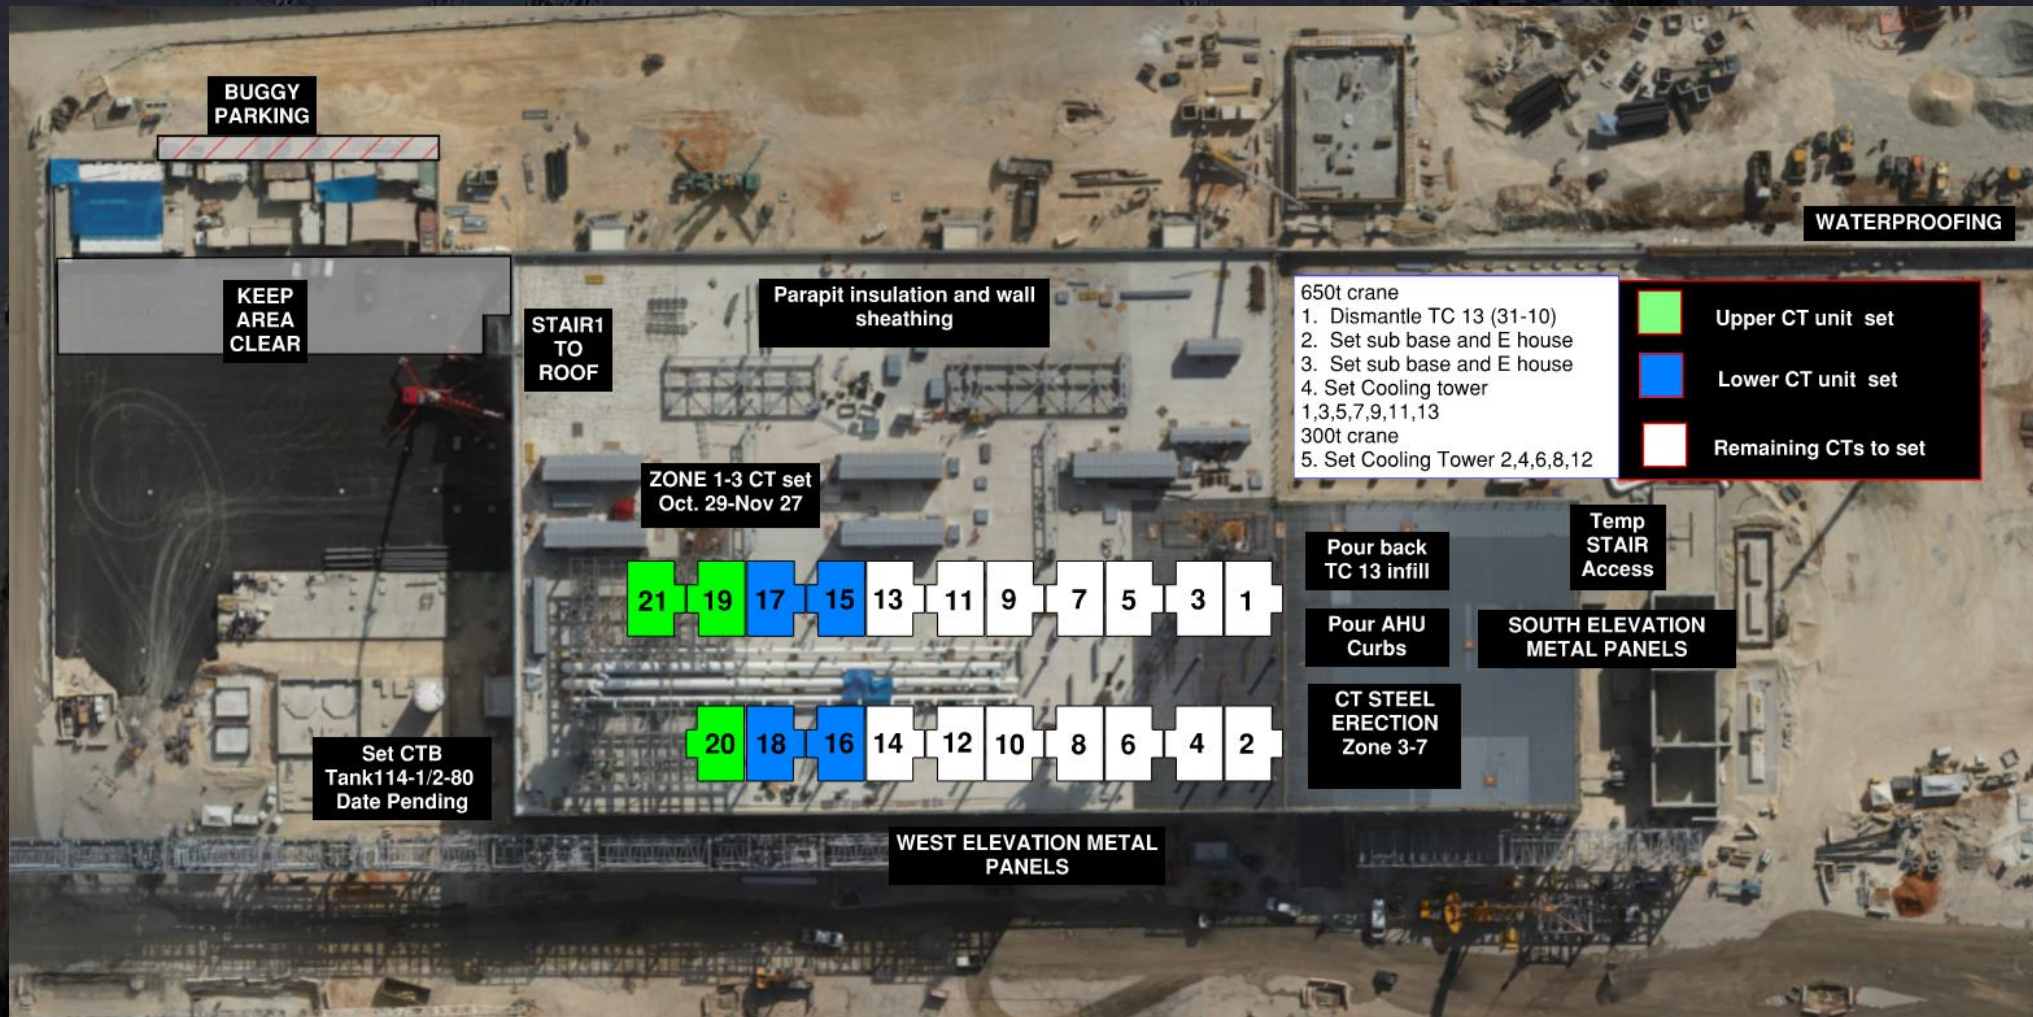

PROPOSE TO ADD
12M JIB
EXTENSION TO
SUPPORT
COOLING TOWER
STEEL ERECTION

NEW RADIUS
SHOWN IN RED

FOR REVIEW

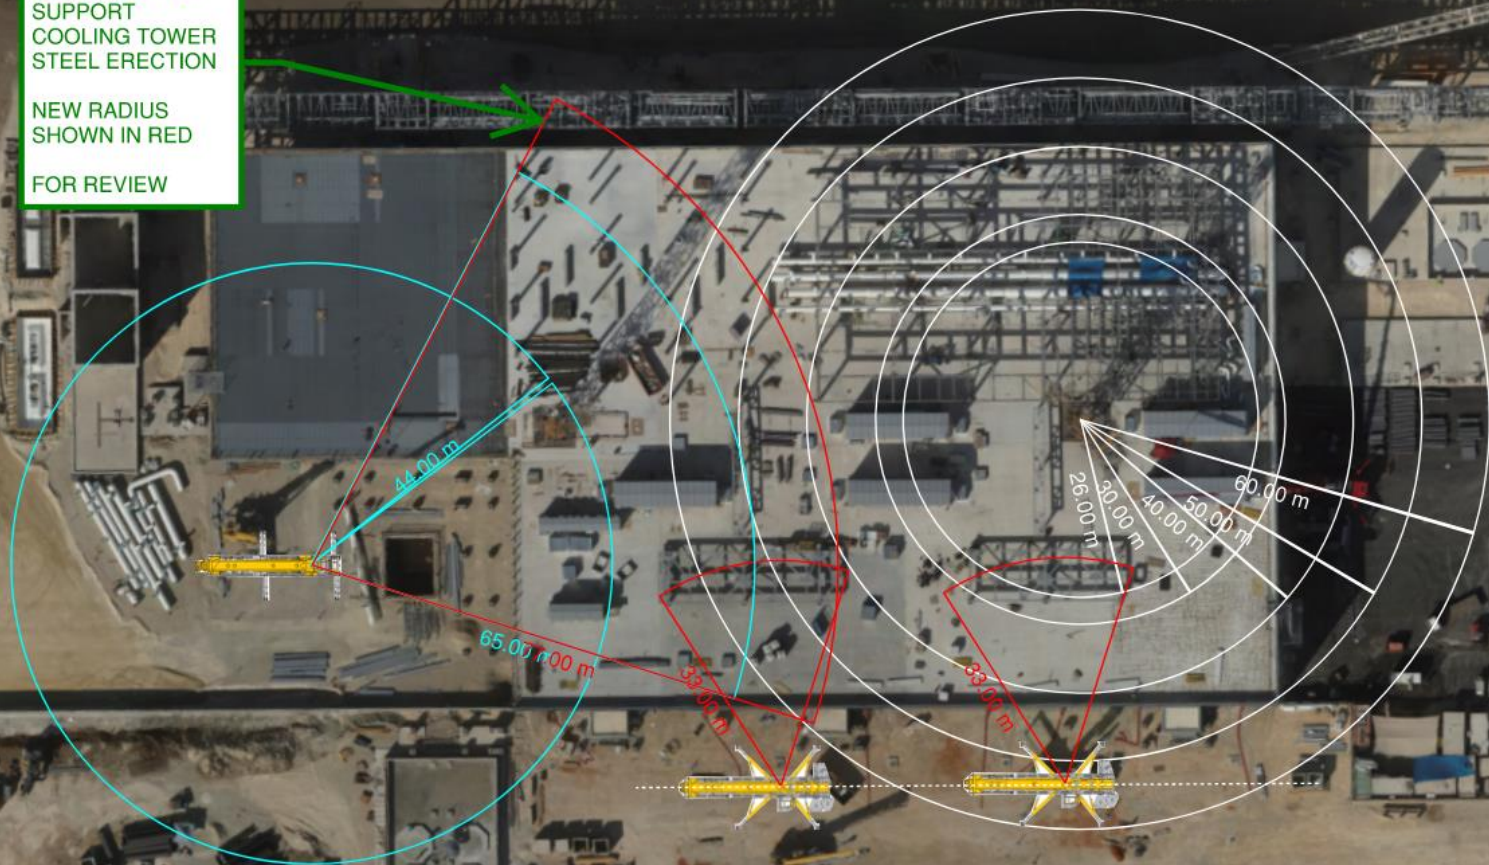




Daily Coordination Meeting

Site Logistics

North

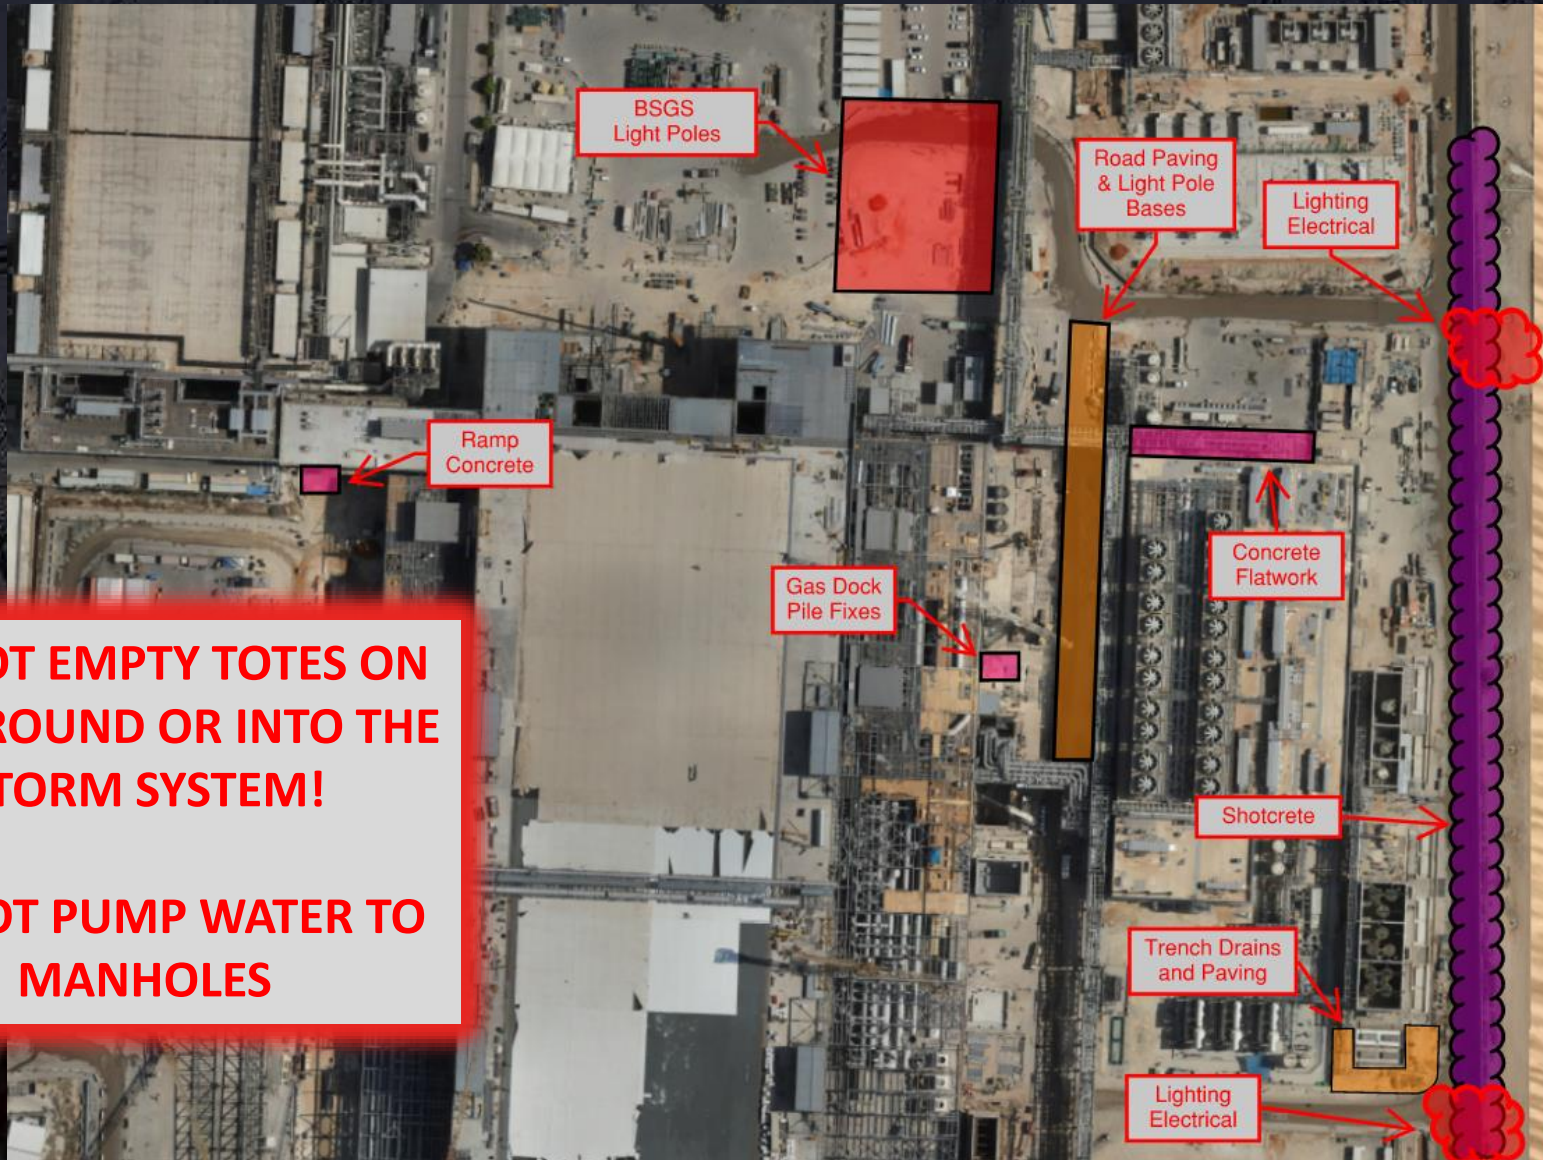

**DO NOT EMPTY TOTES ON
THE GROUND OR INTO THE
STORM SYSTEM!**


**DO NOT PUMP WATER TO
MANHOLES**



Daily Coordination Meeting

Site Logistics

South

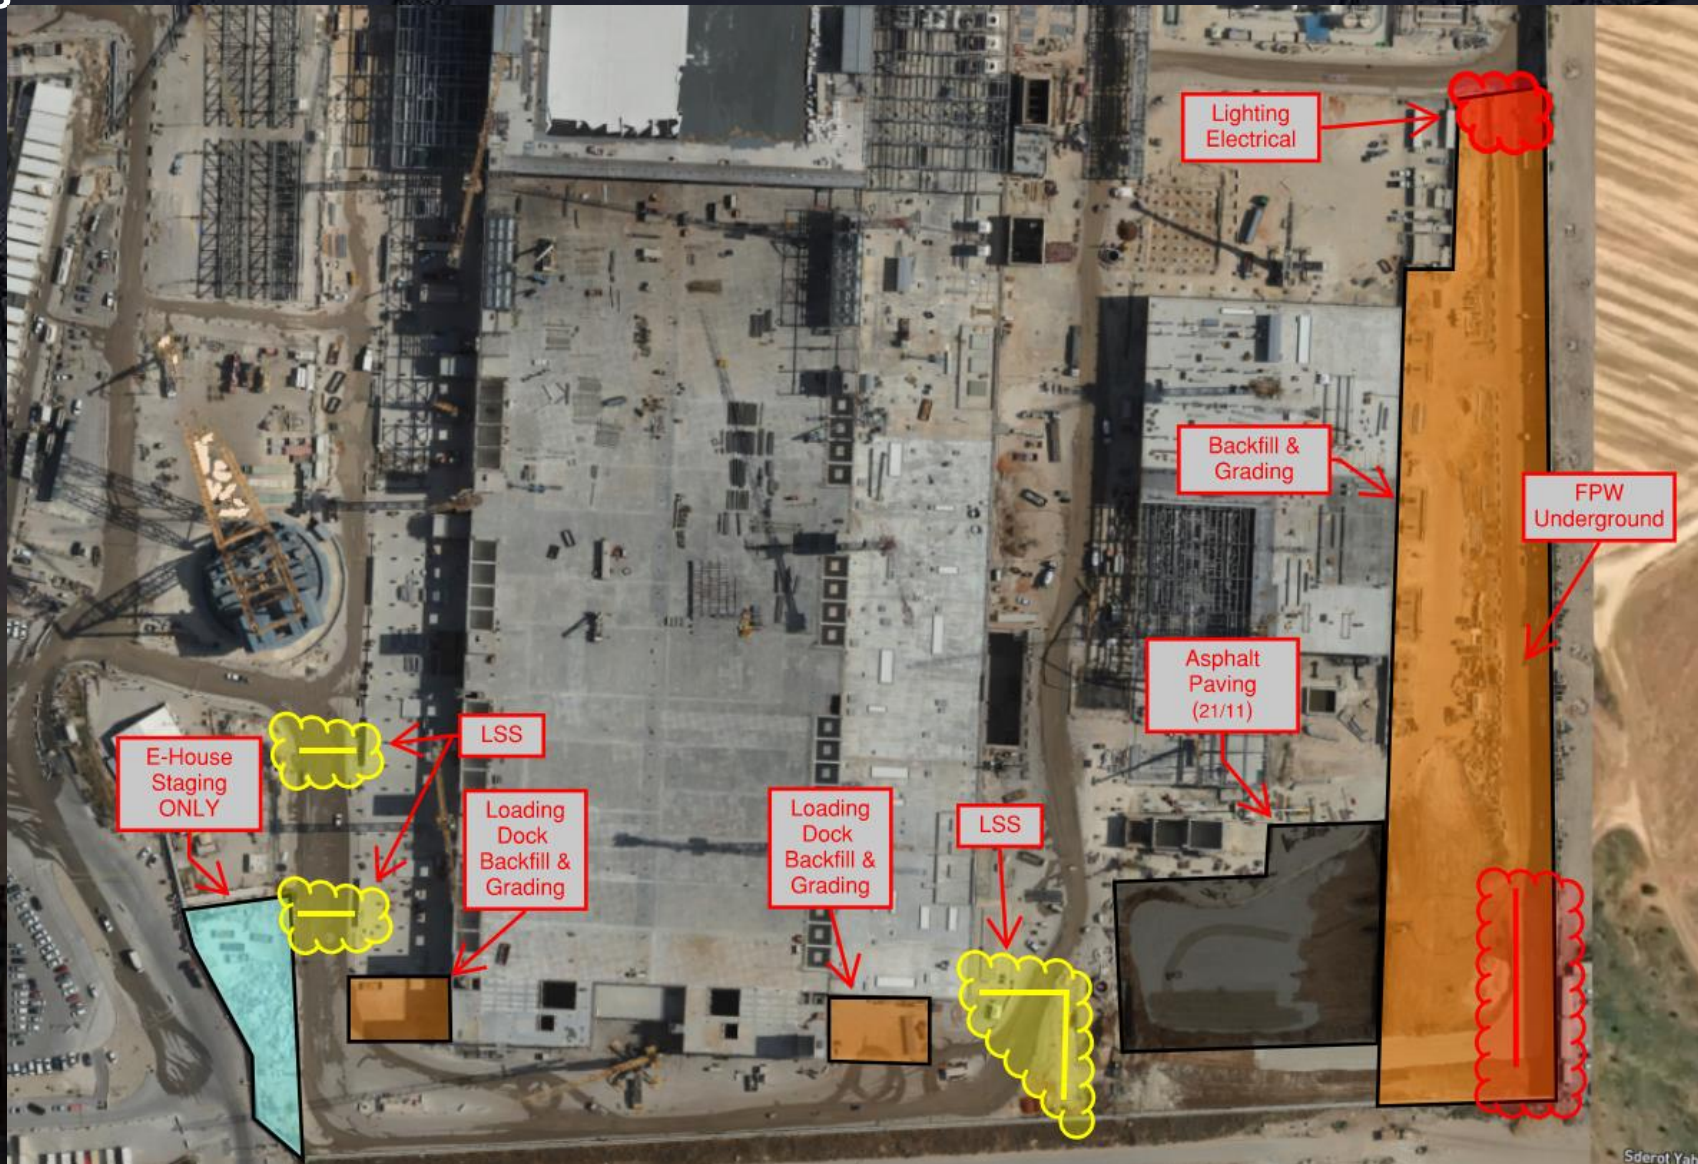



Safe Use of MEWP

There has been an increase in work-related injuries involving MEWPs. Here are key safety guidelines:

- Complete a checklist to inspect the MEWP before use.
- Identify and remove hazards if possible (e.g., sharp objects) in the work area.
- Always face the ladder while climbing.
- Avoid placing hands in areas where they could be trapped or crushed.
- Exit the MEWP cautiously and avoid awkward body positions.
- Never extend any body part outside the platform or rest hands on the rails.

Following these guidelines ensures a safer work environment when using MEWPs.

Daily Coordination Meeting



14:00 Sign In
