

Daily Coordination Meeting



Daily Coordination Meeting

General Topics:

- Meeting attendance mandatory:
- whiteboard, 14:00, subcontractor.
- All workers must attend MSM, or they don't work on the jobsite.

25M HOUR BBQ – 08 APRIL

Volunteer sign-up:



25M HOUR BBQ – 08 APRIL

Please see what is the designated hour for your company

A.S Barzel	11:30-12:15 A
Afcon Contracting Services	
Afcon Control and Automation Ltd	
Avi Cranes	
BCT PIPELINE PROCESSES LTD	
BRAND INDUSTRIAL LTD	
ByNet System Application Ltd	
DVIR.IE LTD	
D&P Clean Room Ltd	
Stage Design Ltd	
GLOBUS WORLDWIDE LOGISTICS	
Yerushalmi Water Cooling Tower LTD	

Carmel Bidud LTD (FAB + PSSS)	13:00-13:45 C
CHEMO AHARON LTD (FAB)	
COMBE LTD	
Derech Afar LTD	
E.L Fireproof LTD	
ELECTROSAFE LTD	
Electra Elevator	
EL-MORE ELECTRIC	
ELRAM PROJECT LTD	
ETC Systems LTD	
ORIAYN ADVANCED TECHNOLOGY SYSTEMS, LTD	
Olizki Infrastructures LTD	
ES Entry Systems LTD	
Sami Najami Engineering & Project LTD	


Hoffman Construction	12:15-13:00 B
Talad T.S LTD	
Tavas Cleaning and Security LTD	
TEAM3 LTD	
TM TEAM LTD- Job service	
TM TEAM LTD	
MALCHIMIM BADAROM	
TZUR ESH PROJECTS LTD	
W&W - AFKO Steel LLC	
INTEL	
JACOBS	
HB	
QA- AMTS, Q+,DPS	

Katz Arie Stainless Steel	13:45-14:30 D
HYG STEEL 1990 LTD	
Lesico LTD	
MEGASON ELECTRONIC & CONTROL 1987 LTD	
Meptagon LTD - I&C/ LSS	
Newco - Tec LTD	
Pach Taas LTF (Ashkelon)	
Ranpro LTD	
Rolling Plains Constriction Inc	
Sela Industrial Maintenance 2006LTD	
Shuv Eli Electric Engineering Ltd	
Siemens Industrial LTD	
SIG Industrial LTD	
SK ENGINEERING & PROJECT (CUB)	
Skyline Cranes& Technologies	



KATZ
Press test HPH2
4/2
Night shift

UTILITY LEVEL MOD1

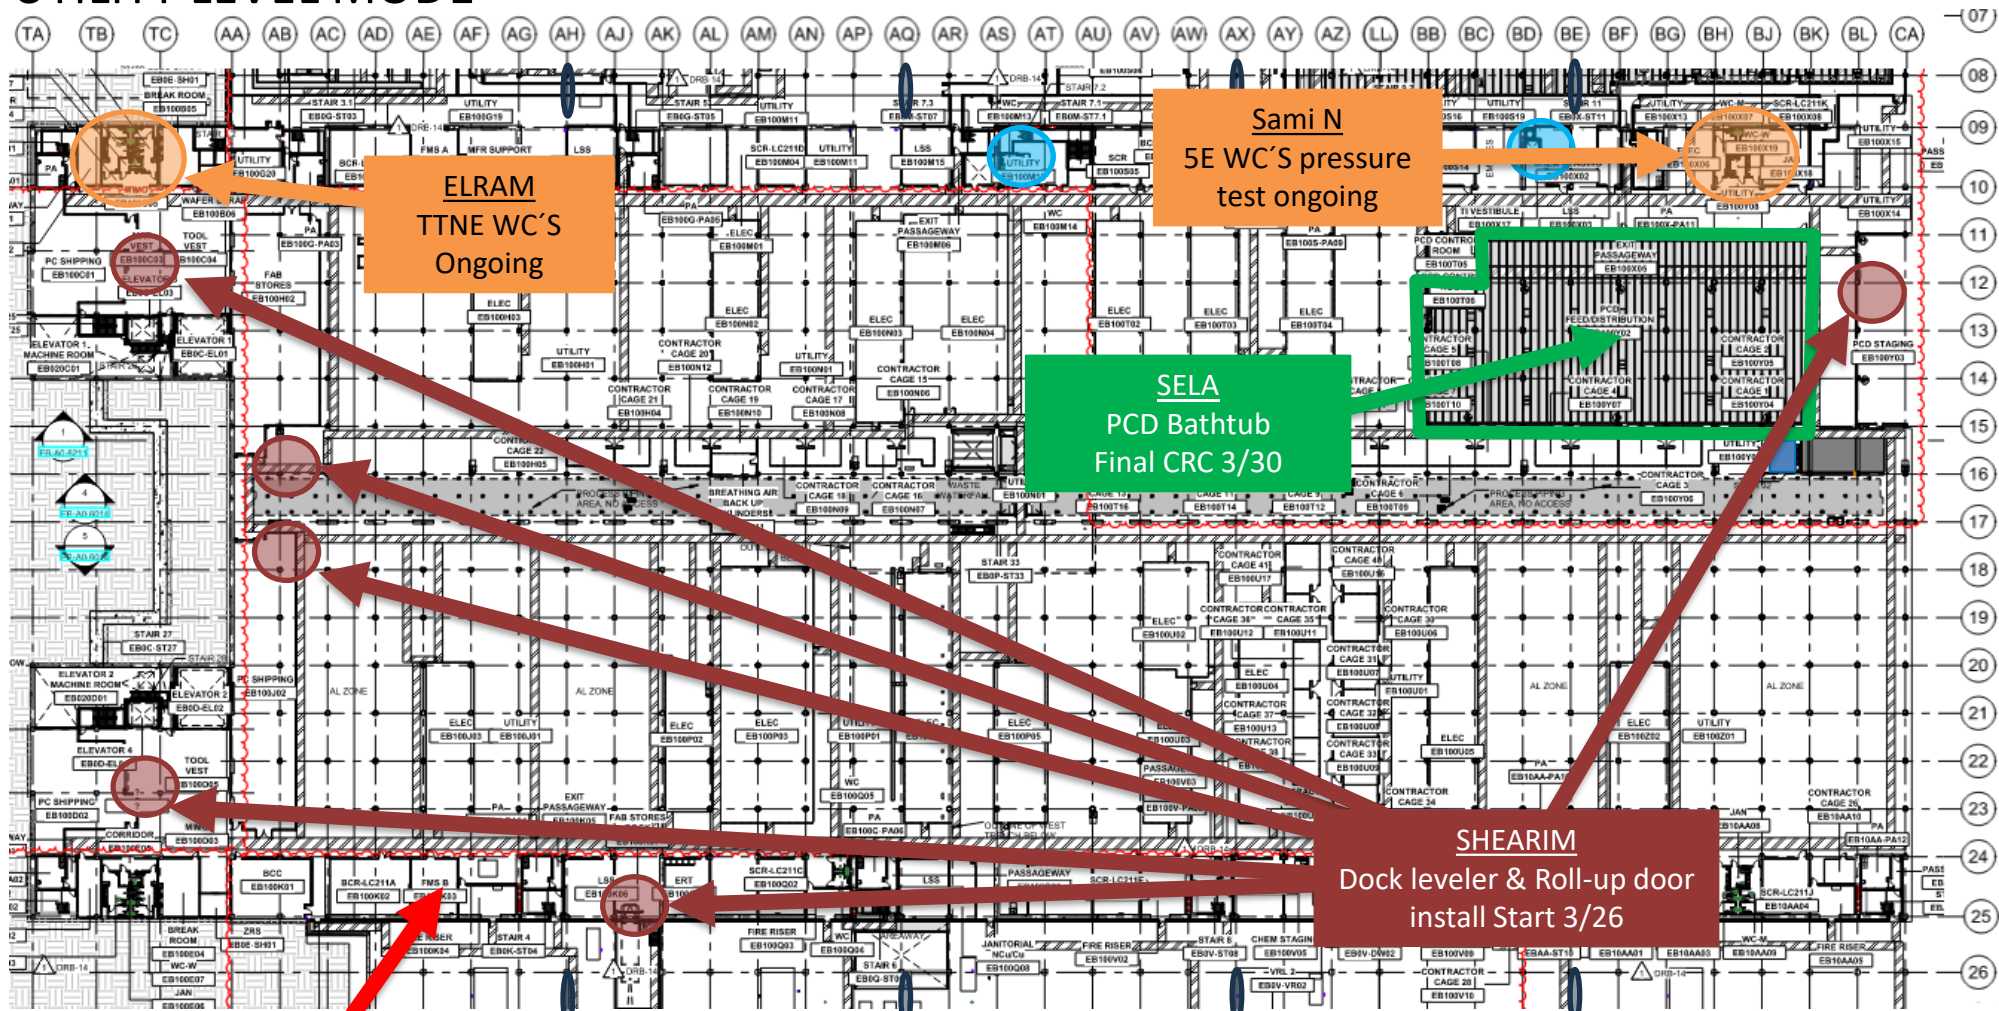

ELRAM
TTNE WC'S
Ongoing

Sami N
5E WC'S pressure
test ongoing

SELA
PCD Bathtub
Final CRC 3/30

SHEARIM
Dock leveler & Roll-up door
install Start 3/26

Carmel Duct
FMS-B
Removing scaffold
4/2


ELRAM
Stairs 7.1
Chem stag
TTNW OH door
Break room E




HOFFMAN CONSTRUCTION COMPANY




SUT 38.1 LEVEL


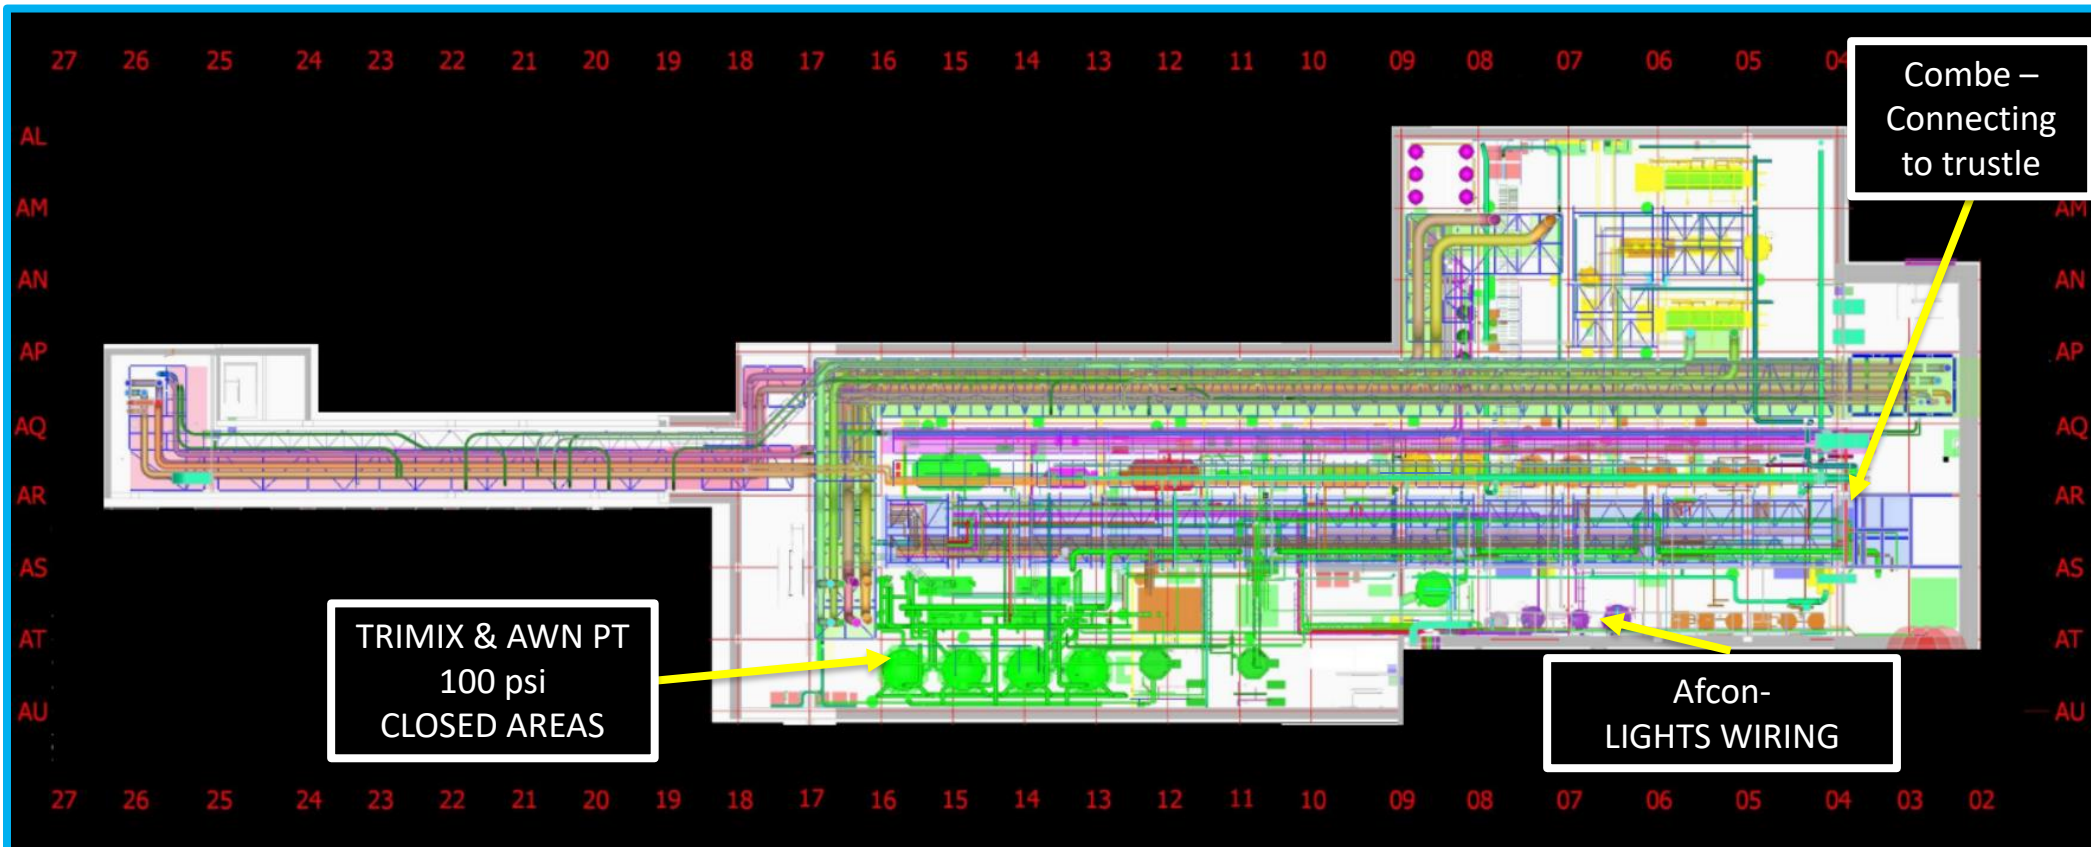


SUT 38.2 LEVEL

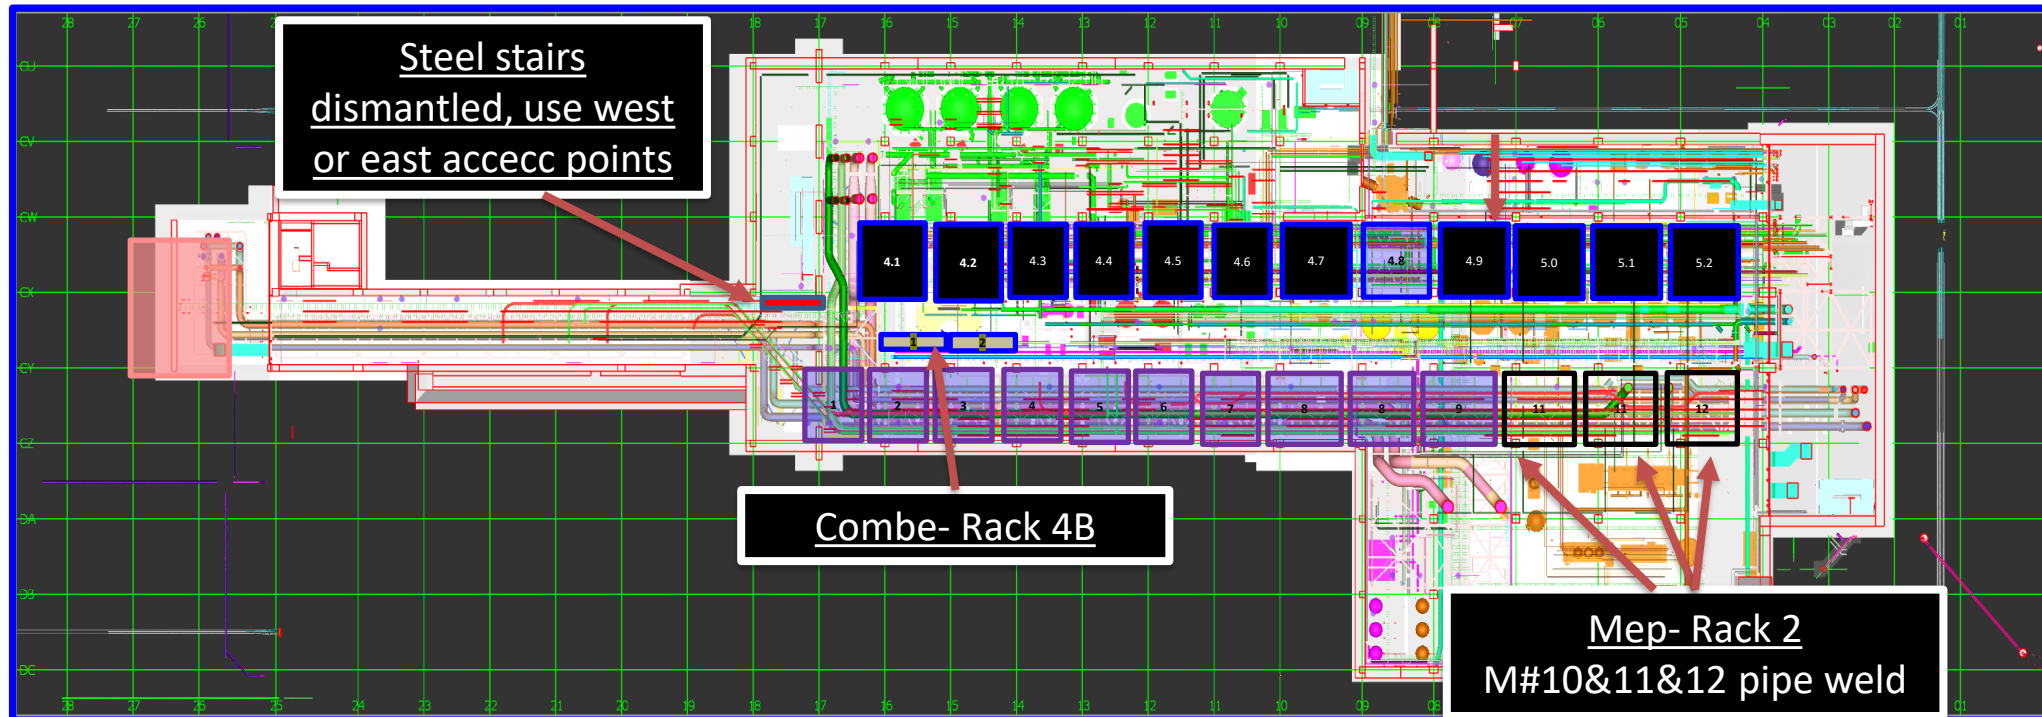


SUT 38.1 LEVEL

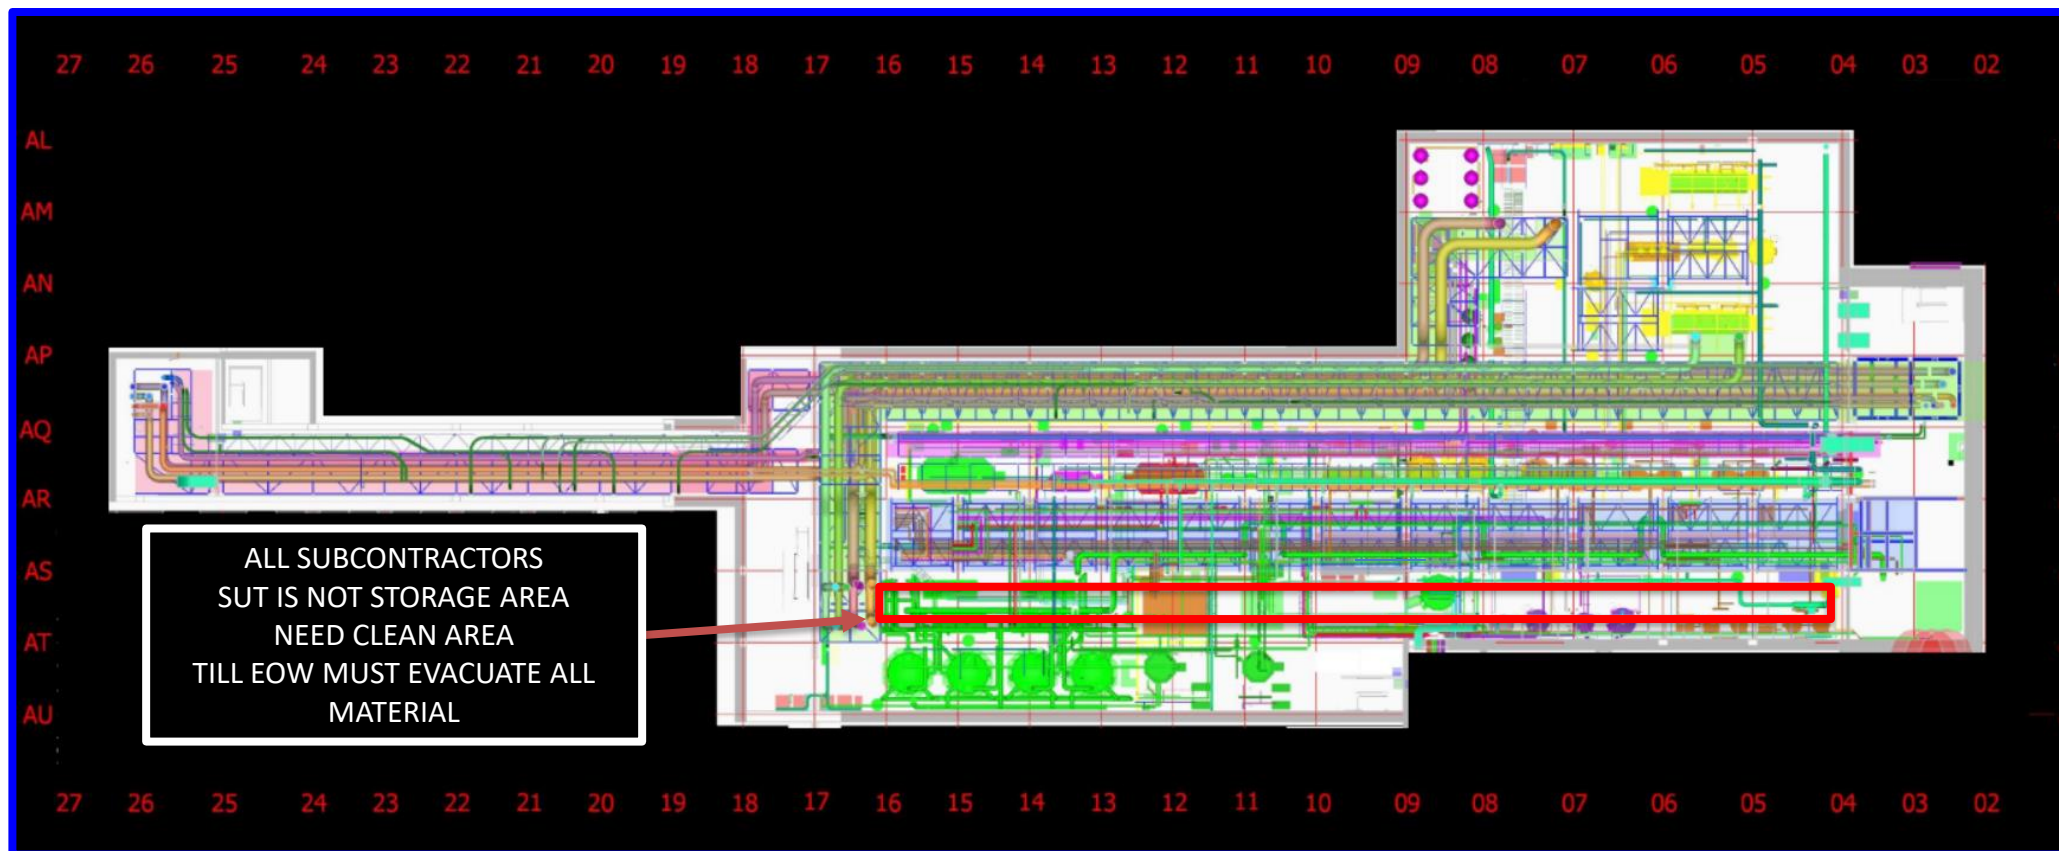

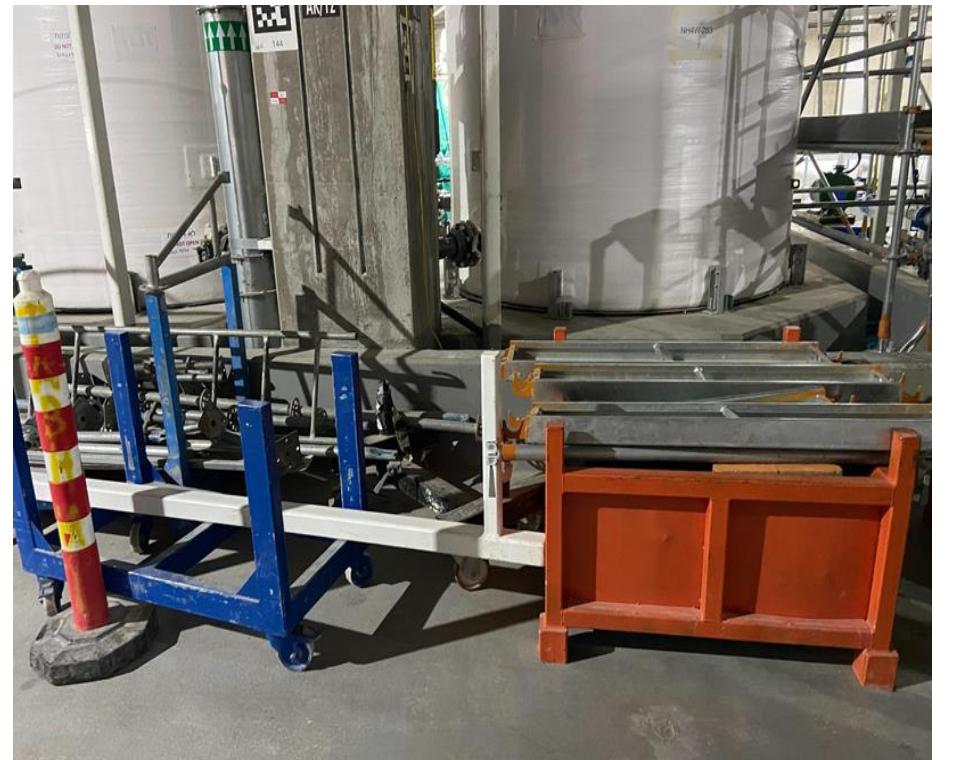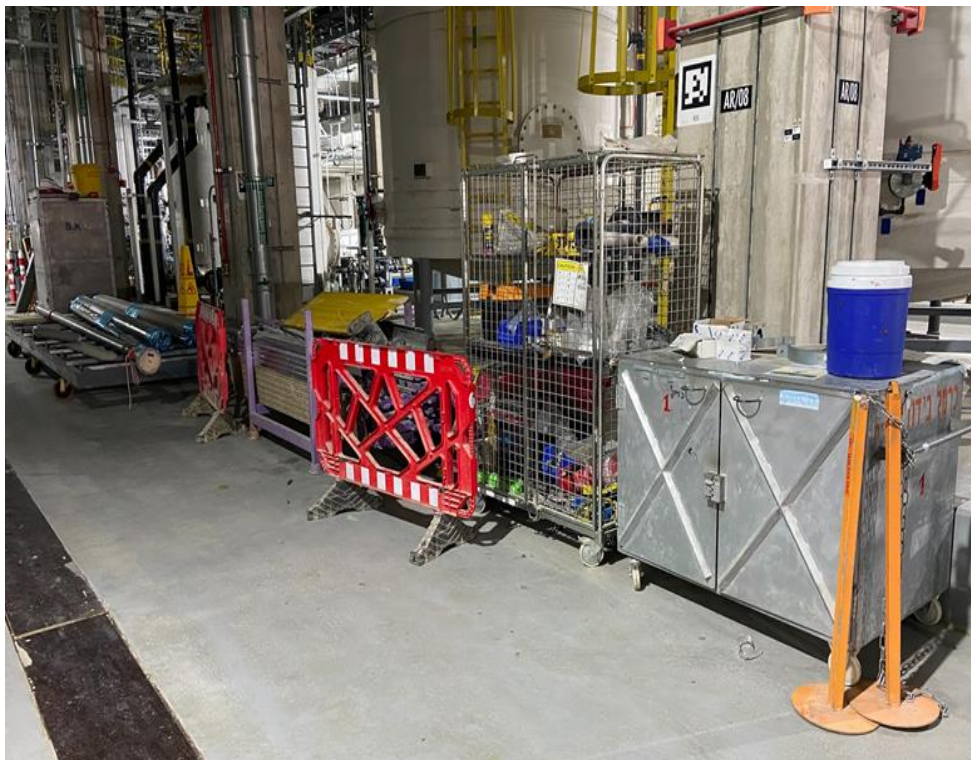





SUBFAB BUILDOUT MOD 1

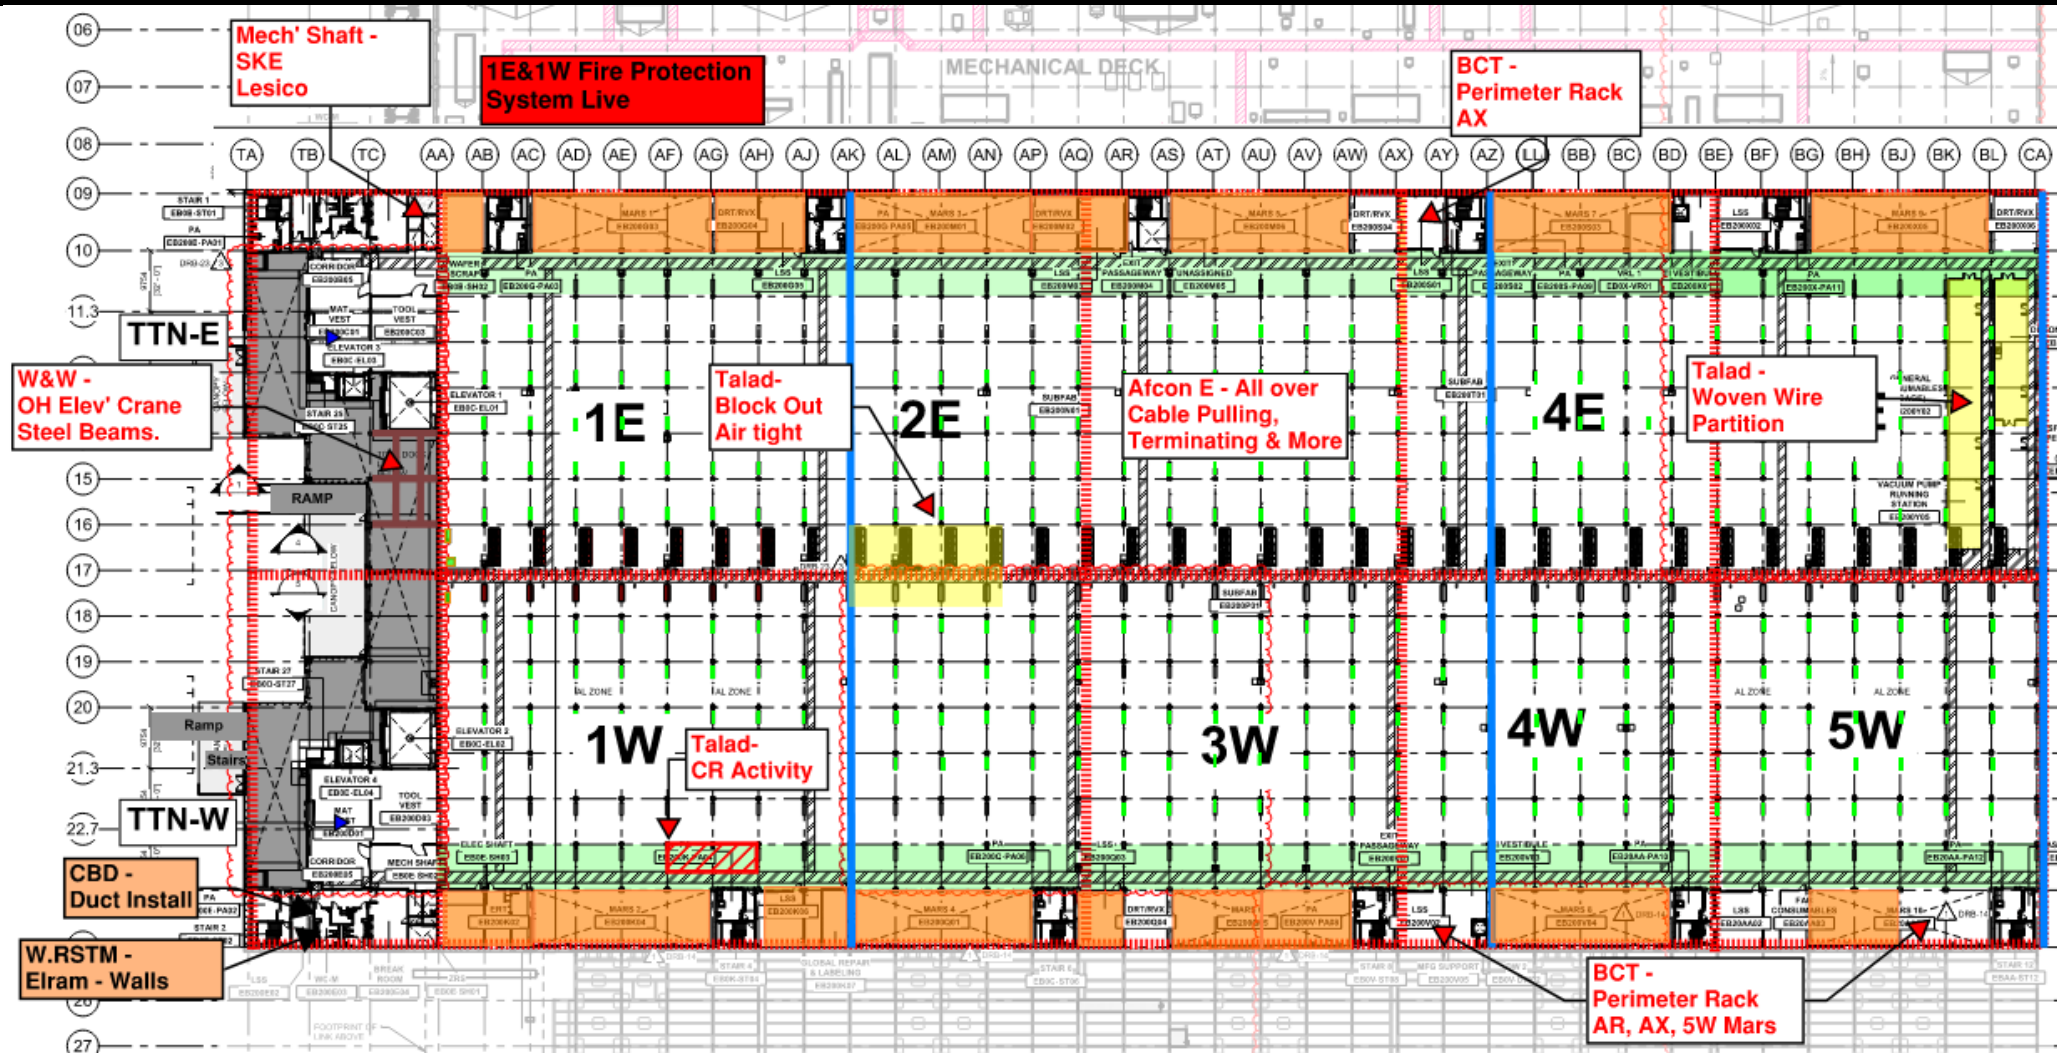



SUBFAR CRC TOPCOAT

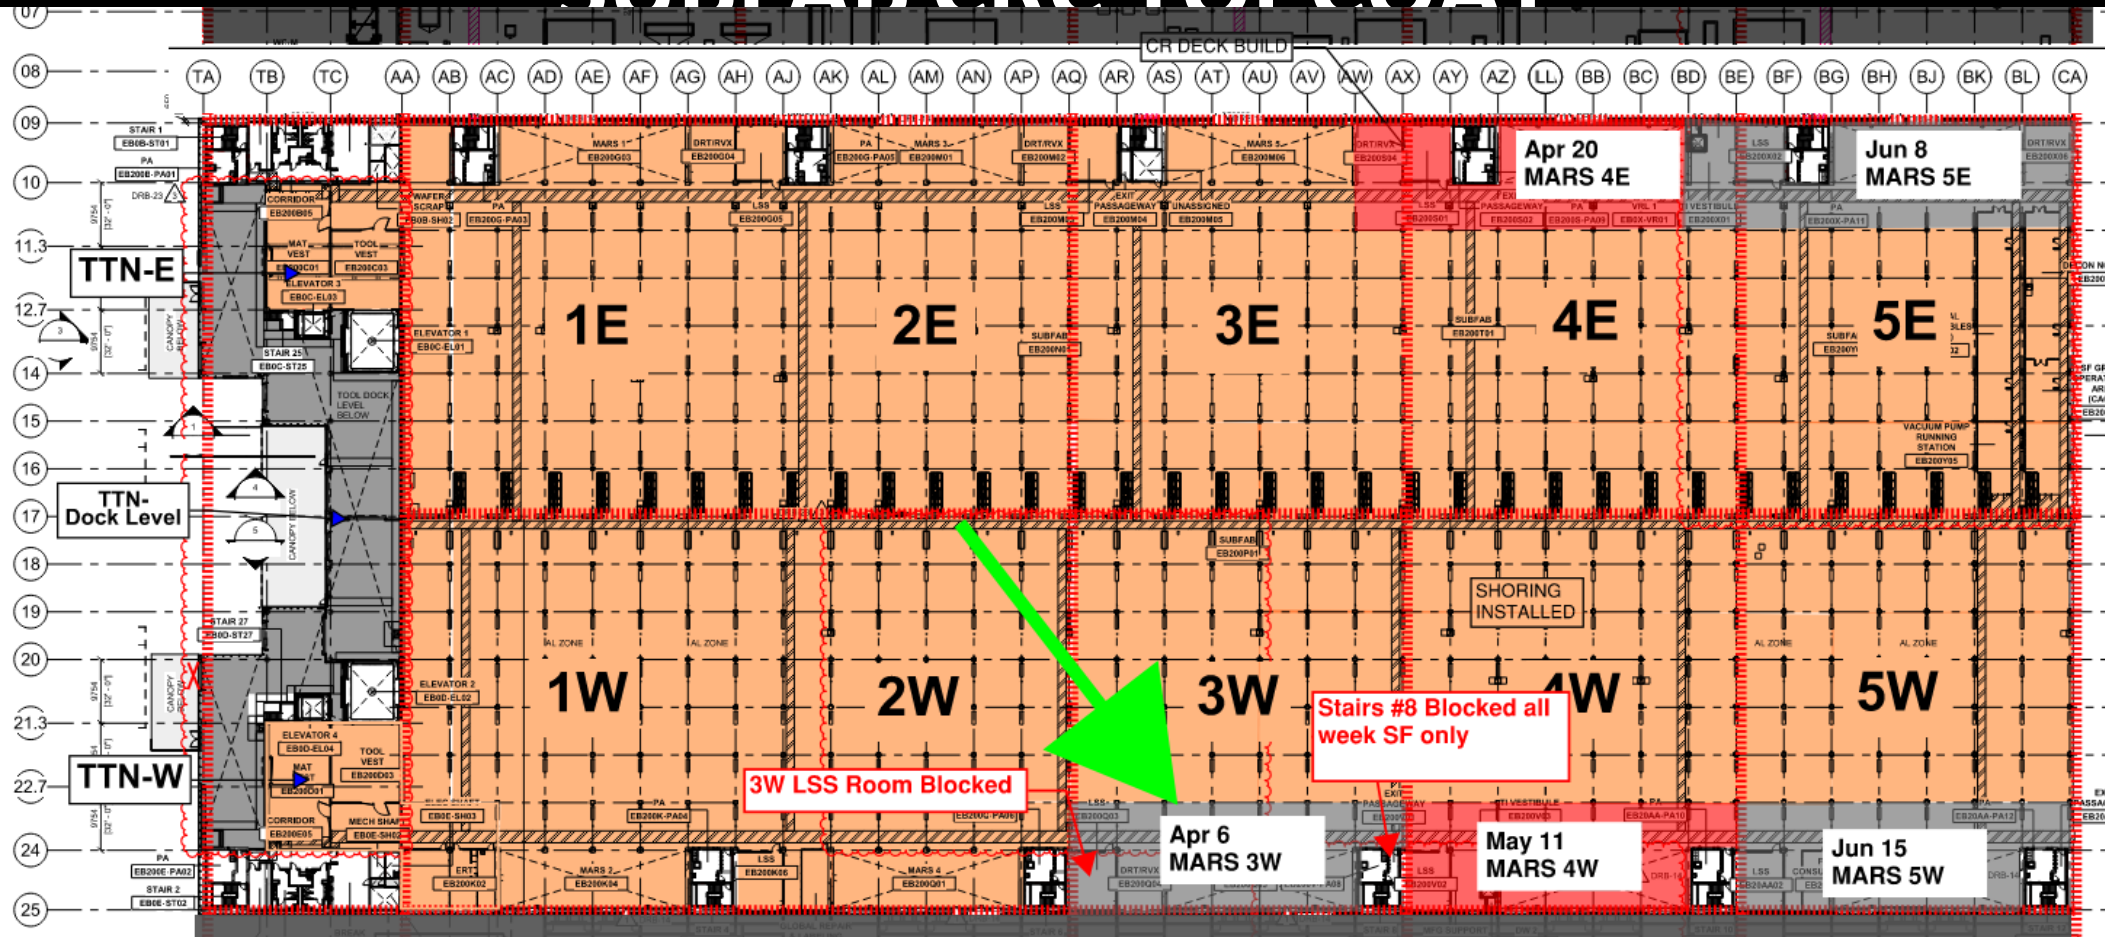



BCT Pressure Test Tomorrow

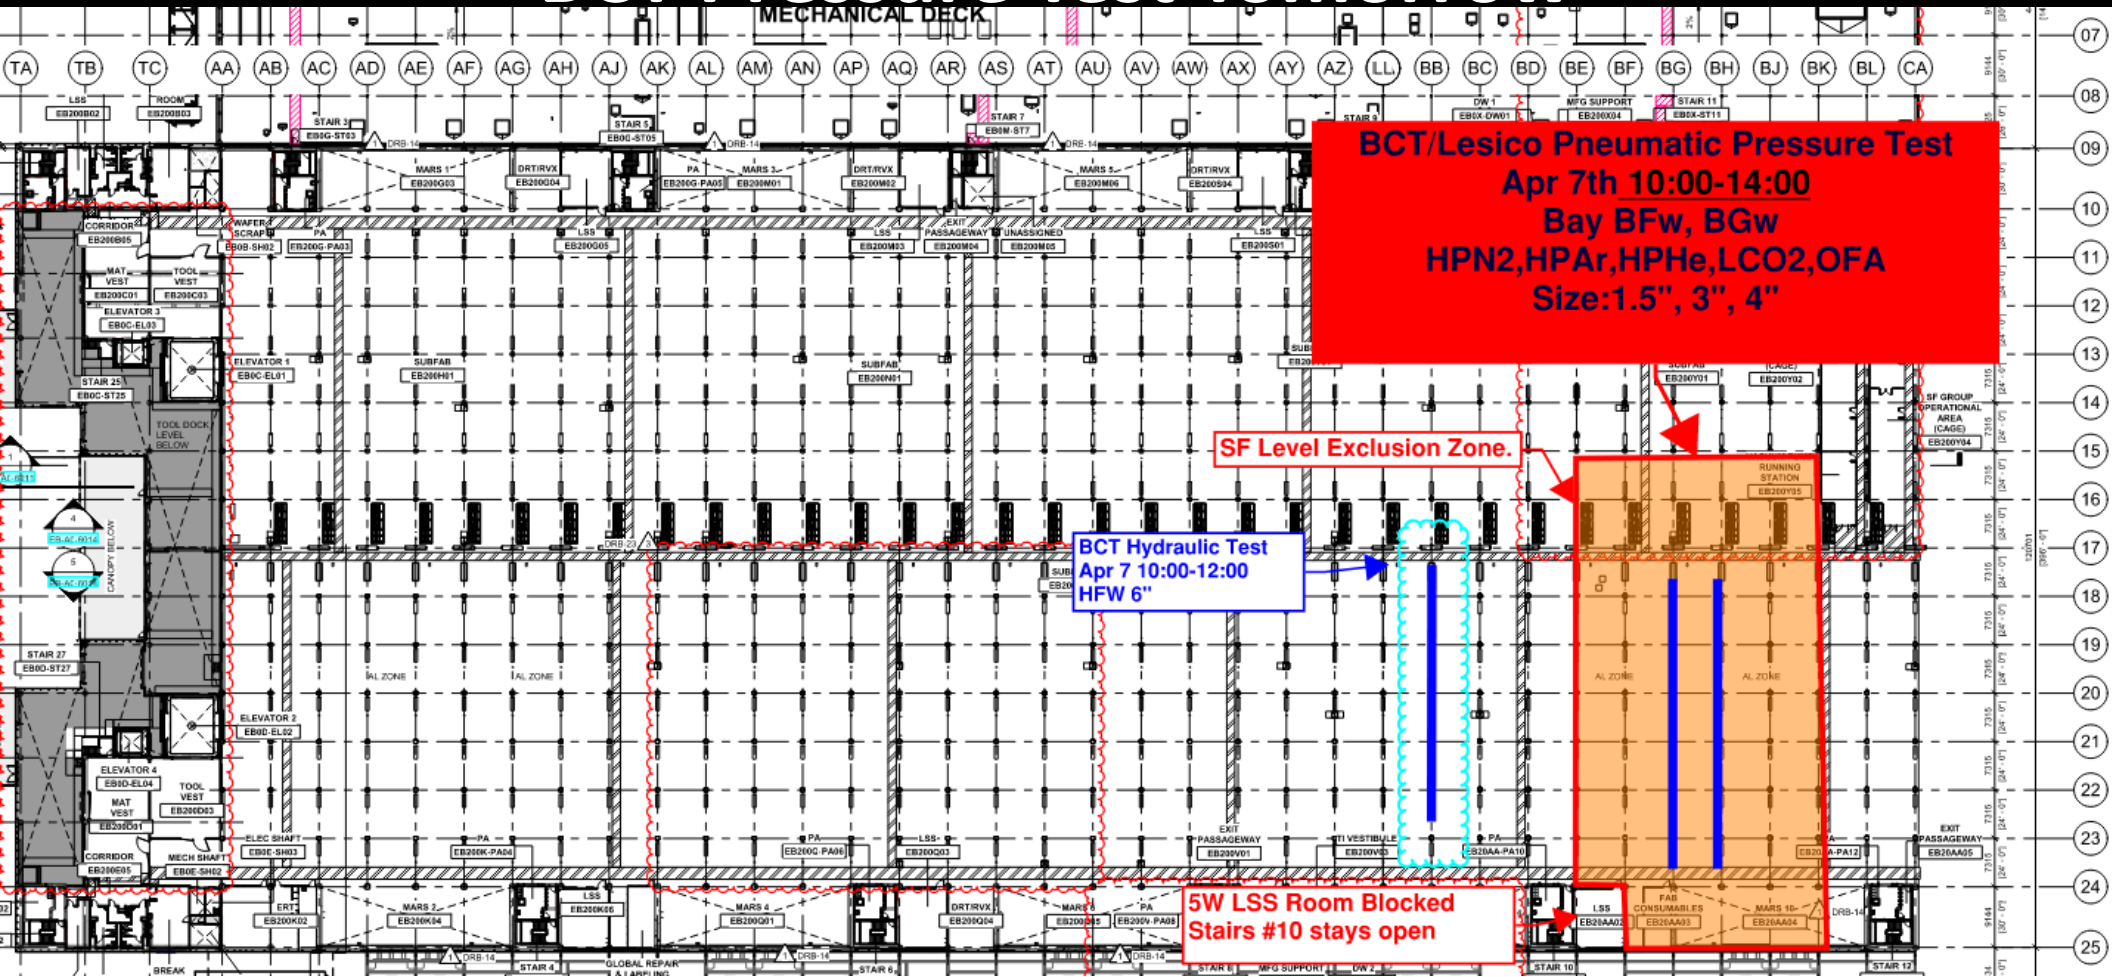


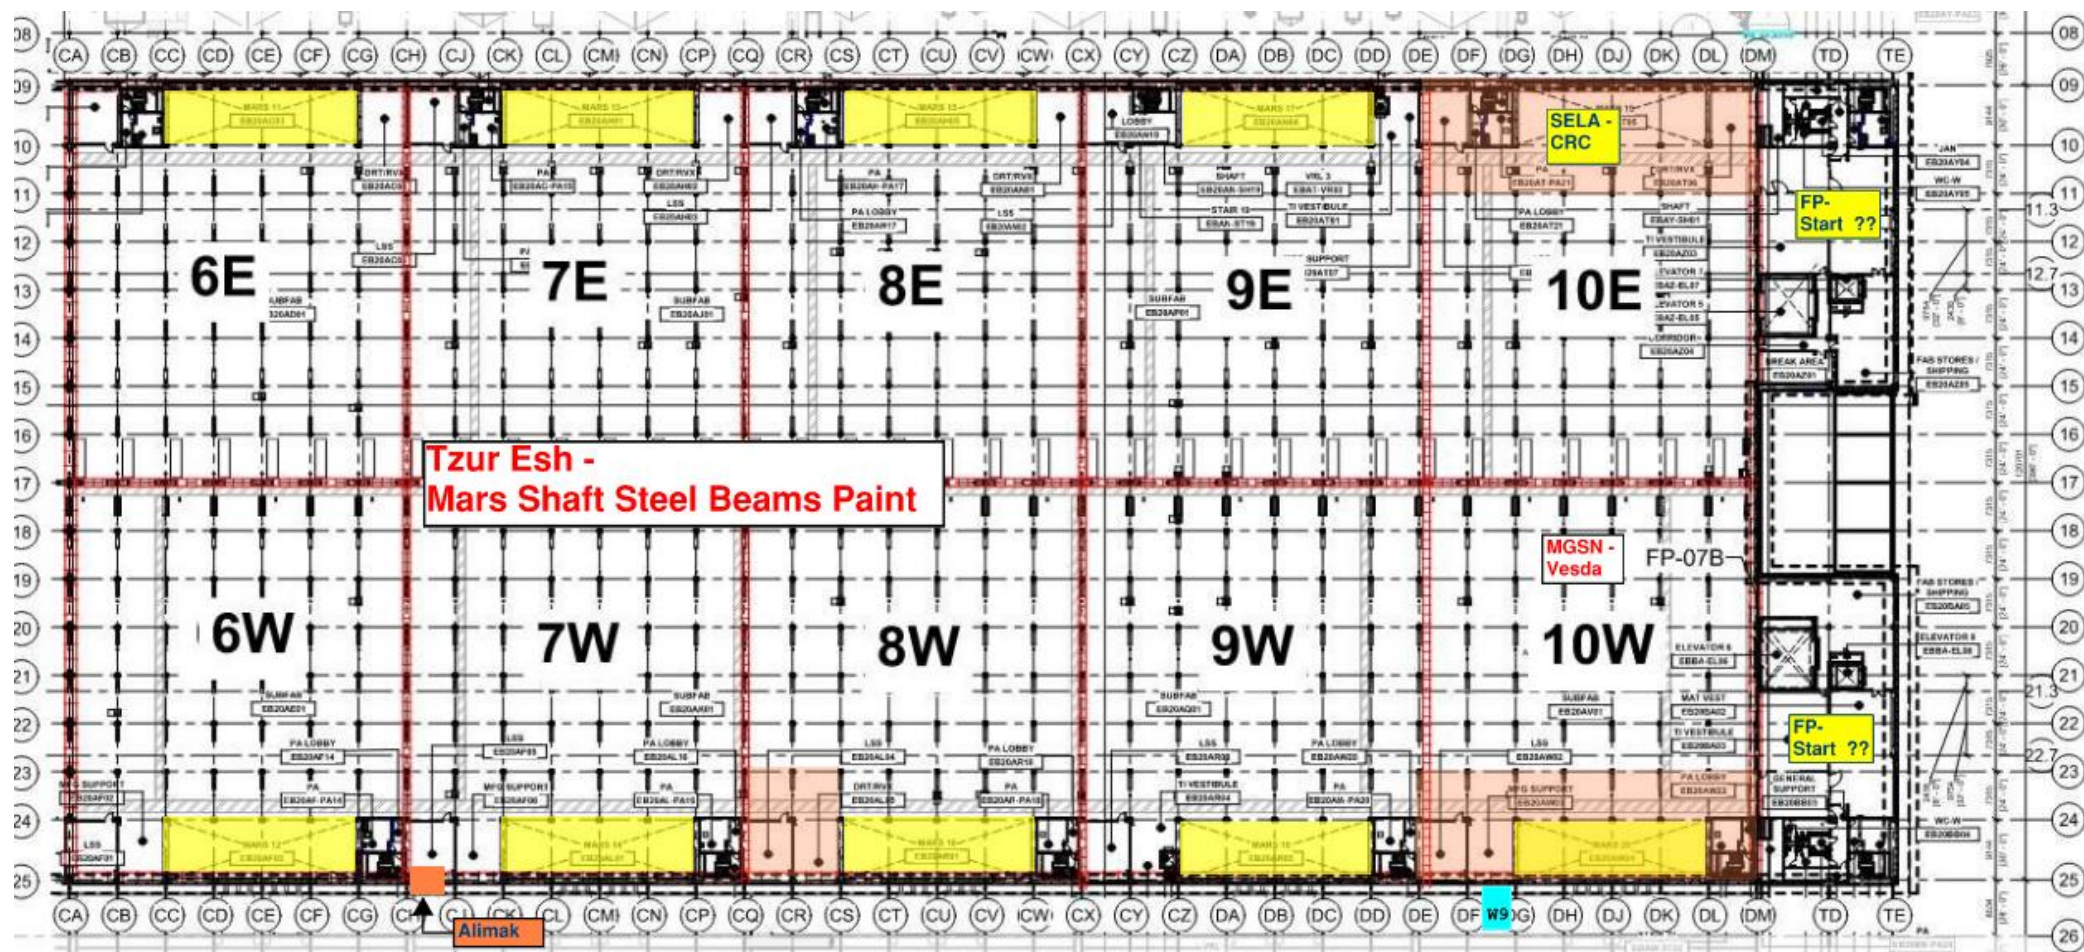


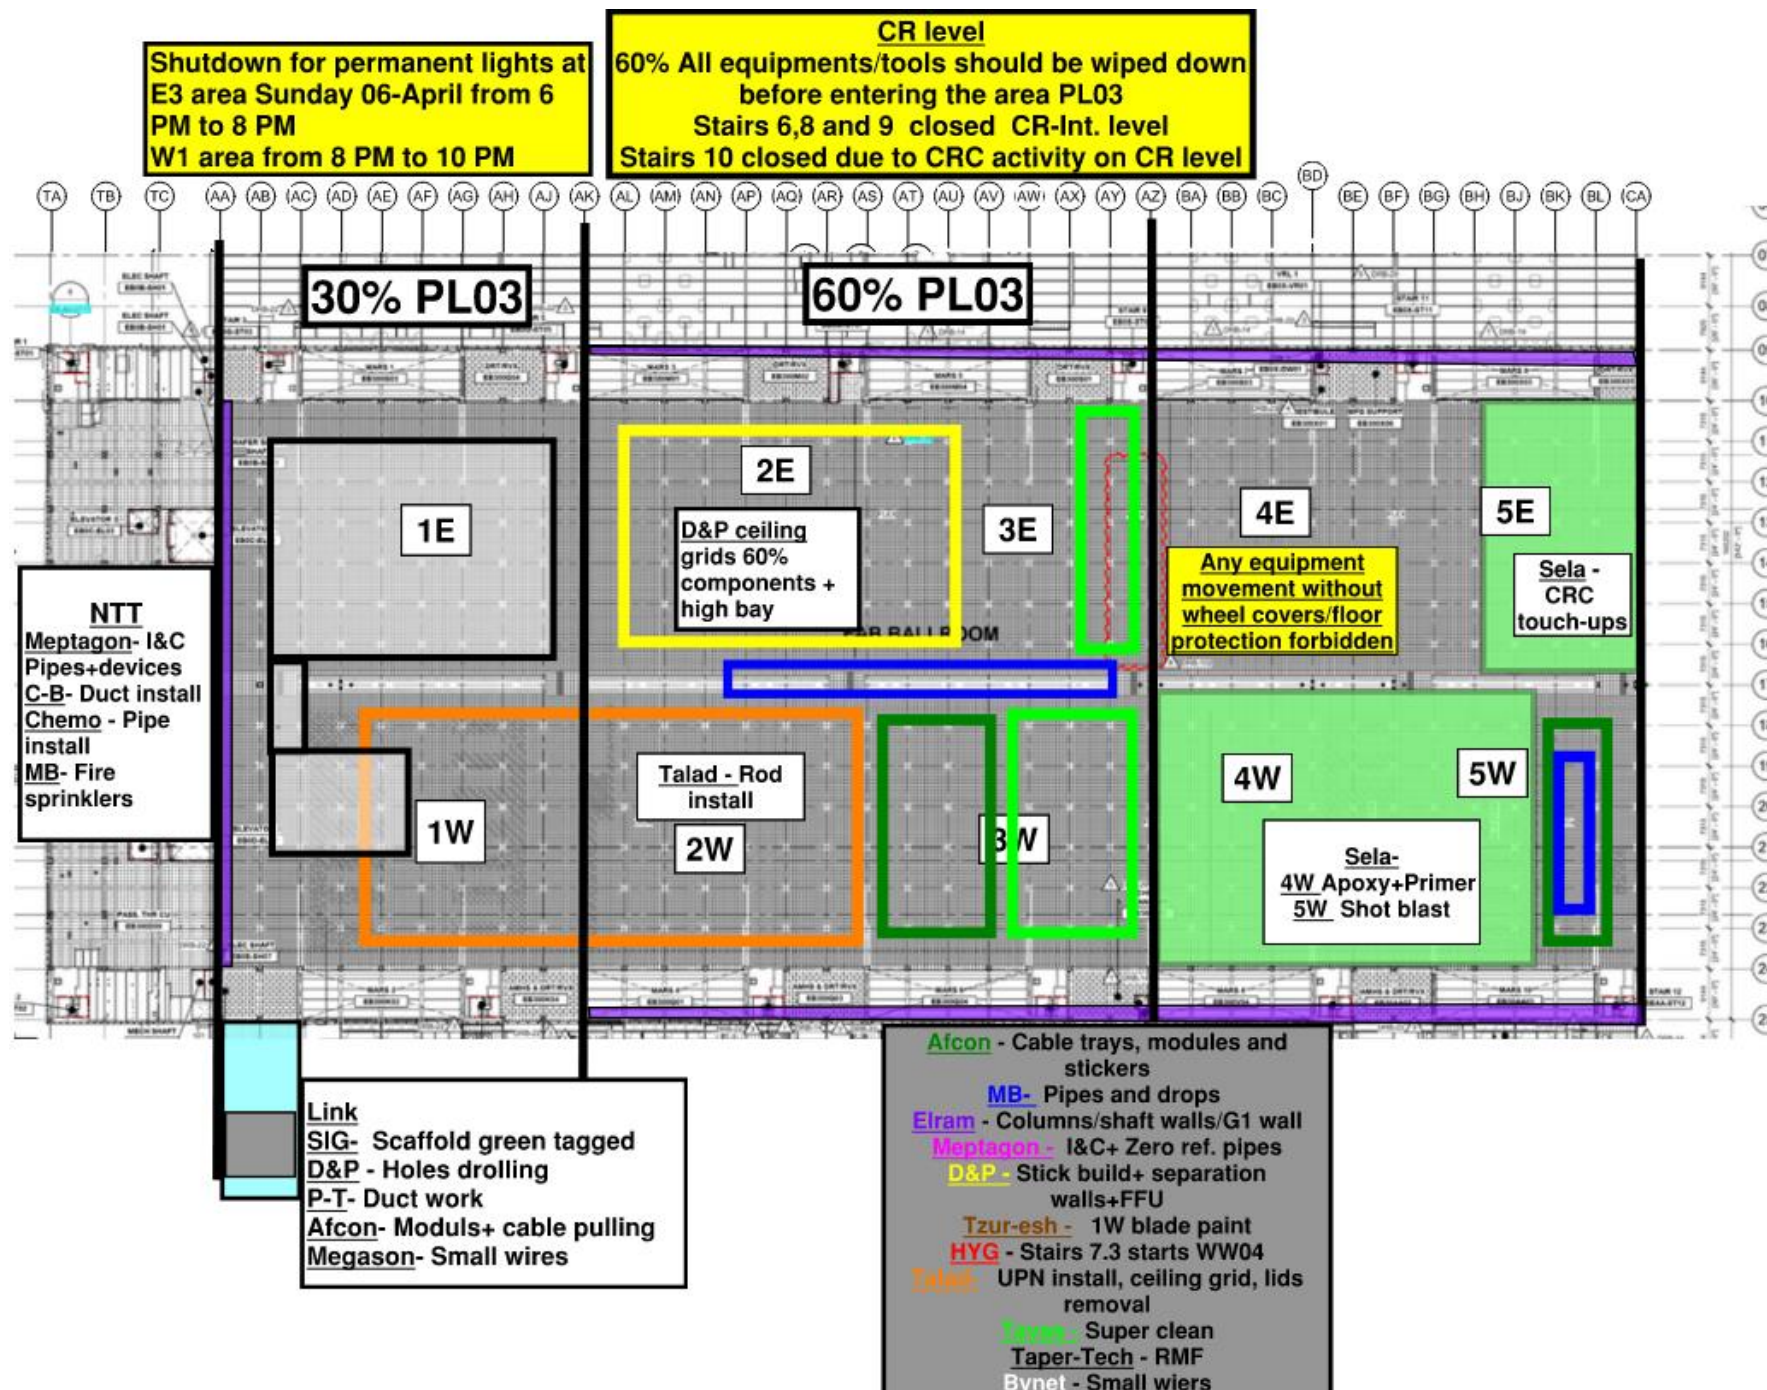

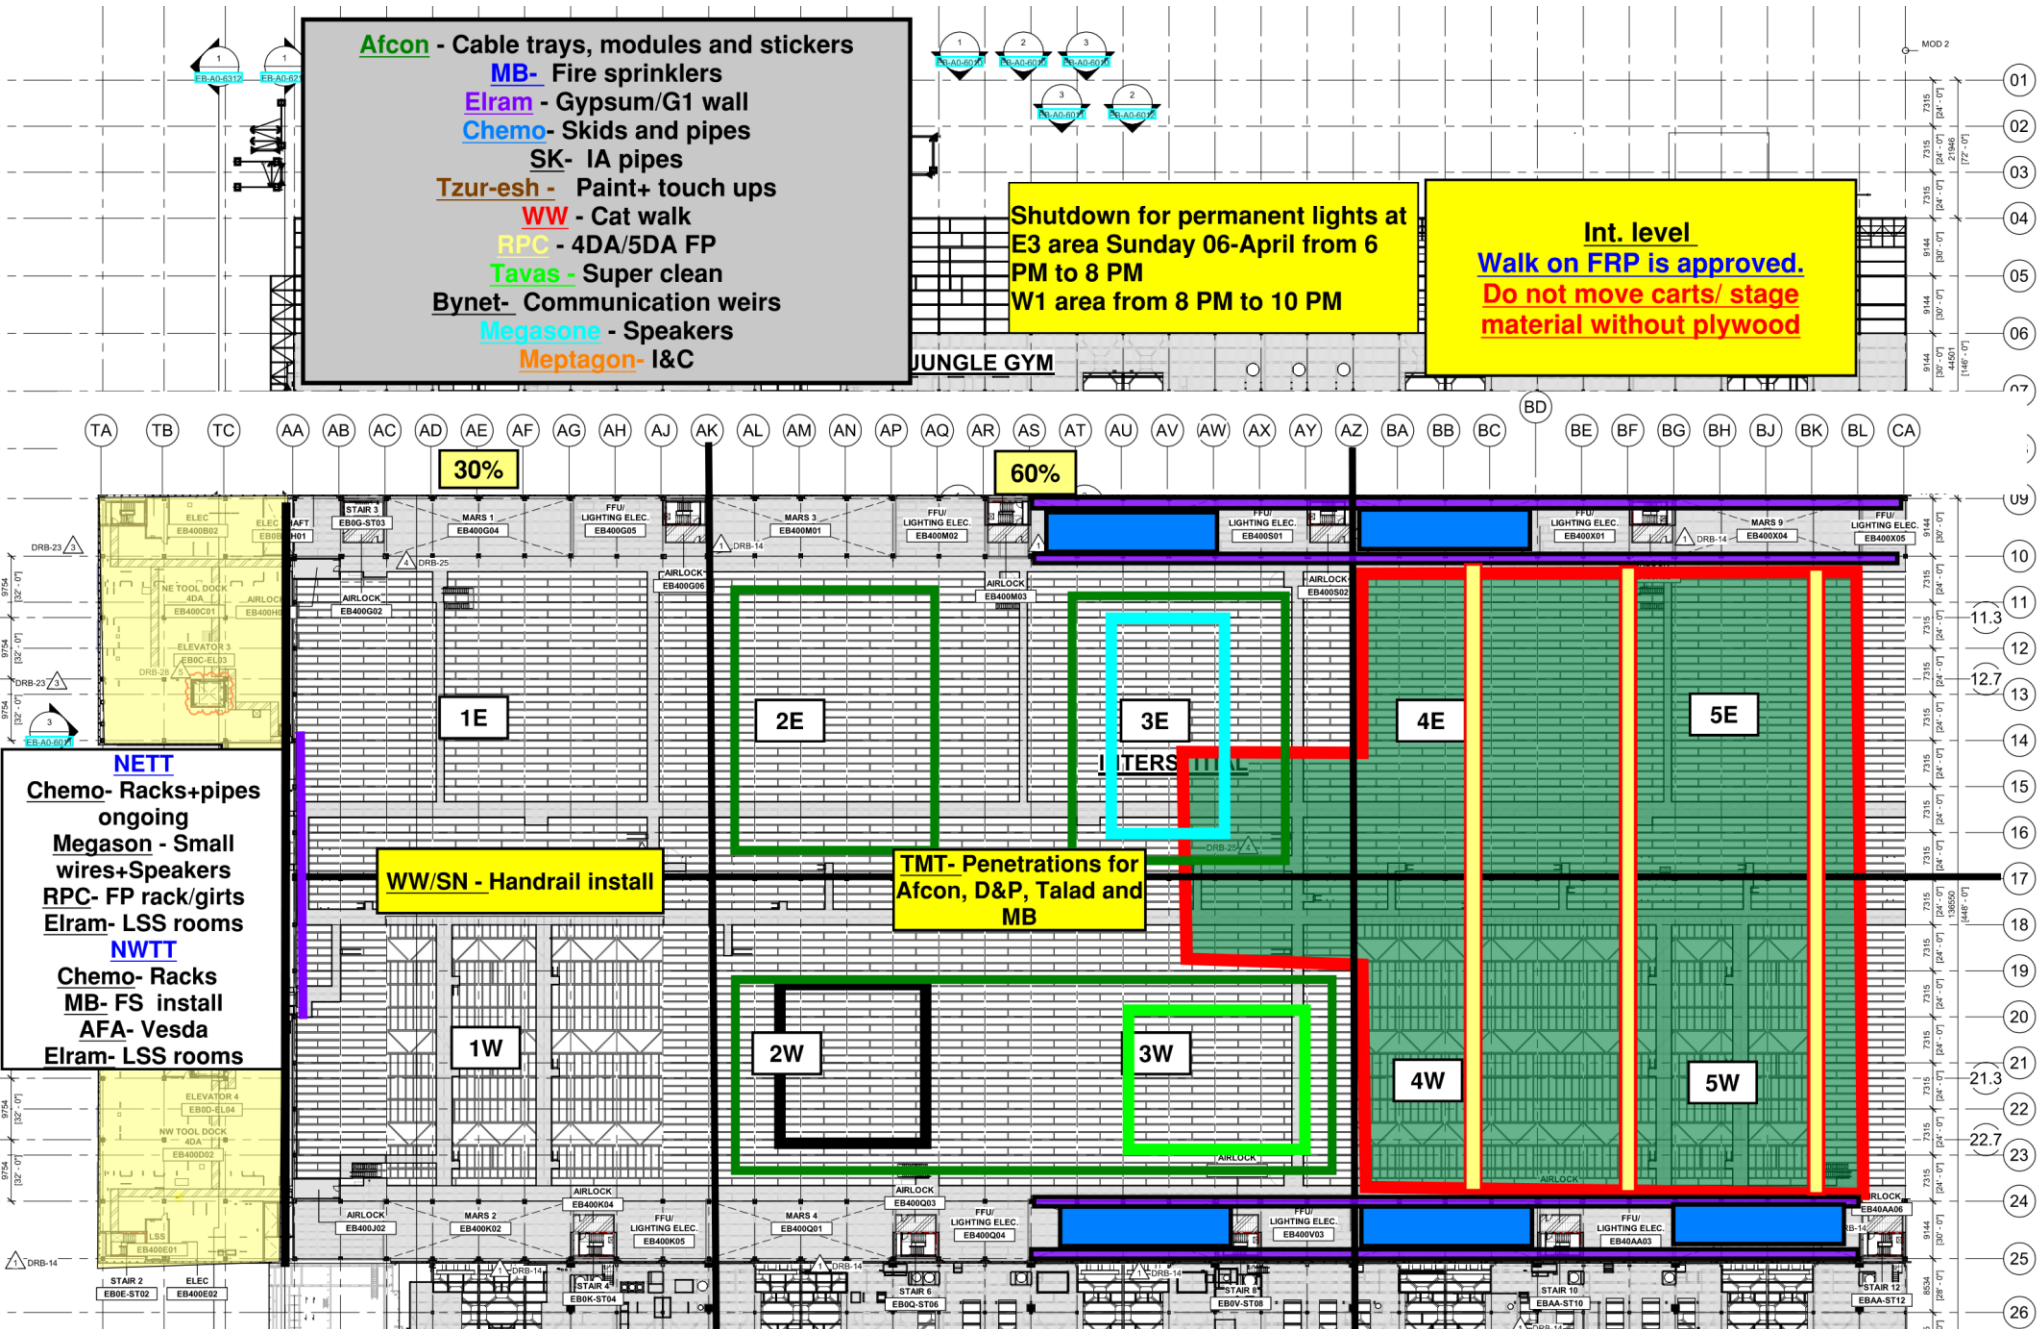

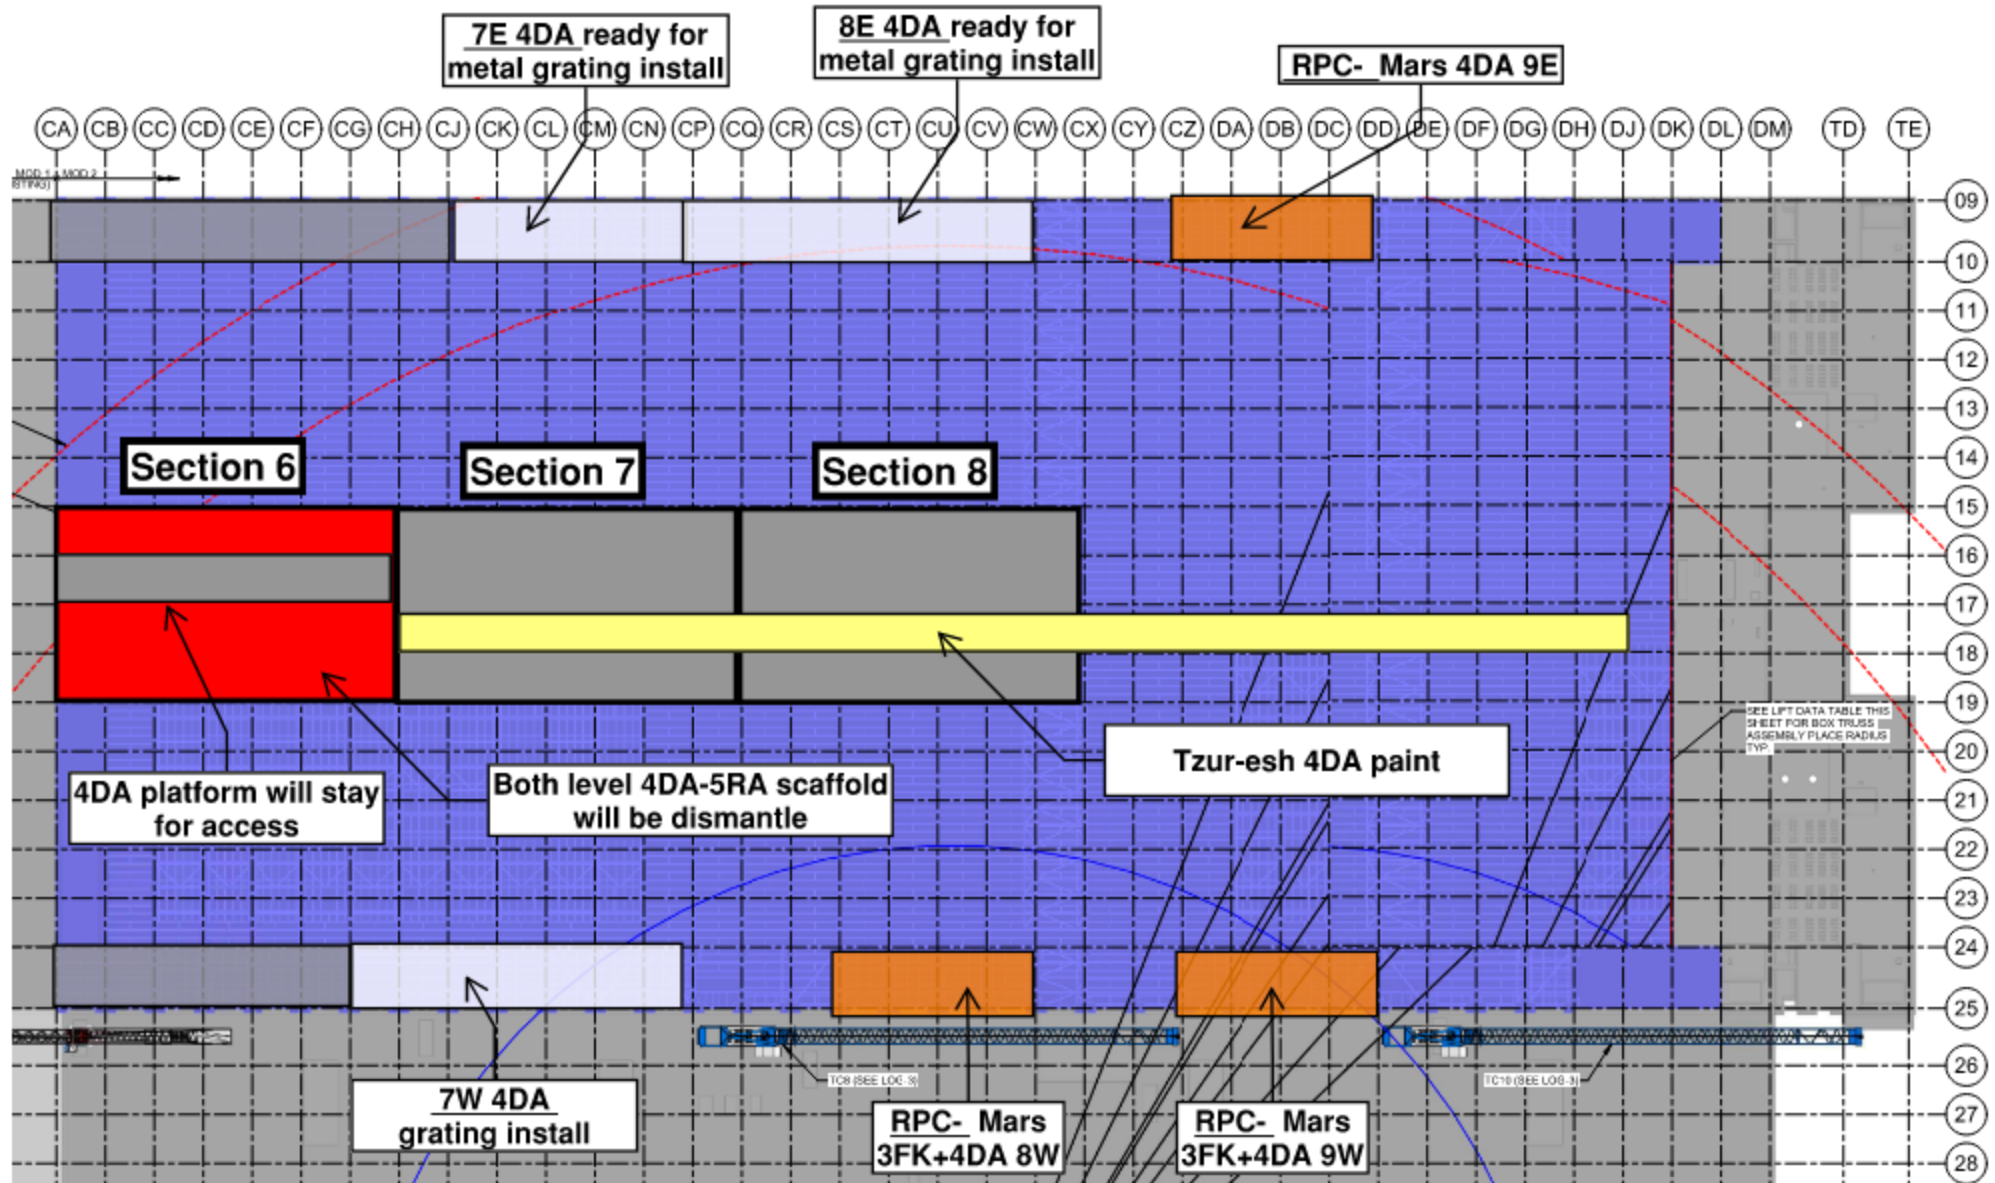

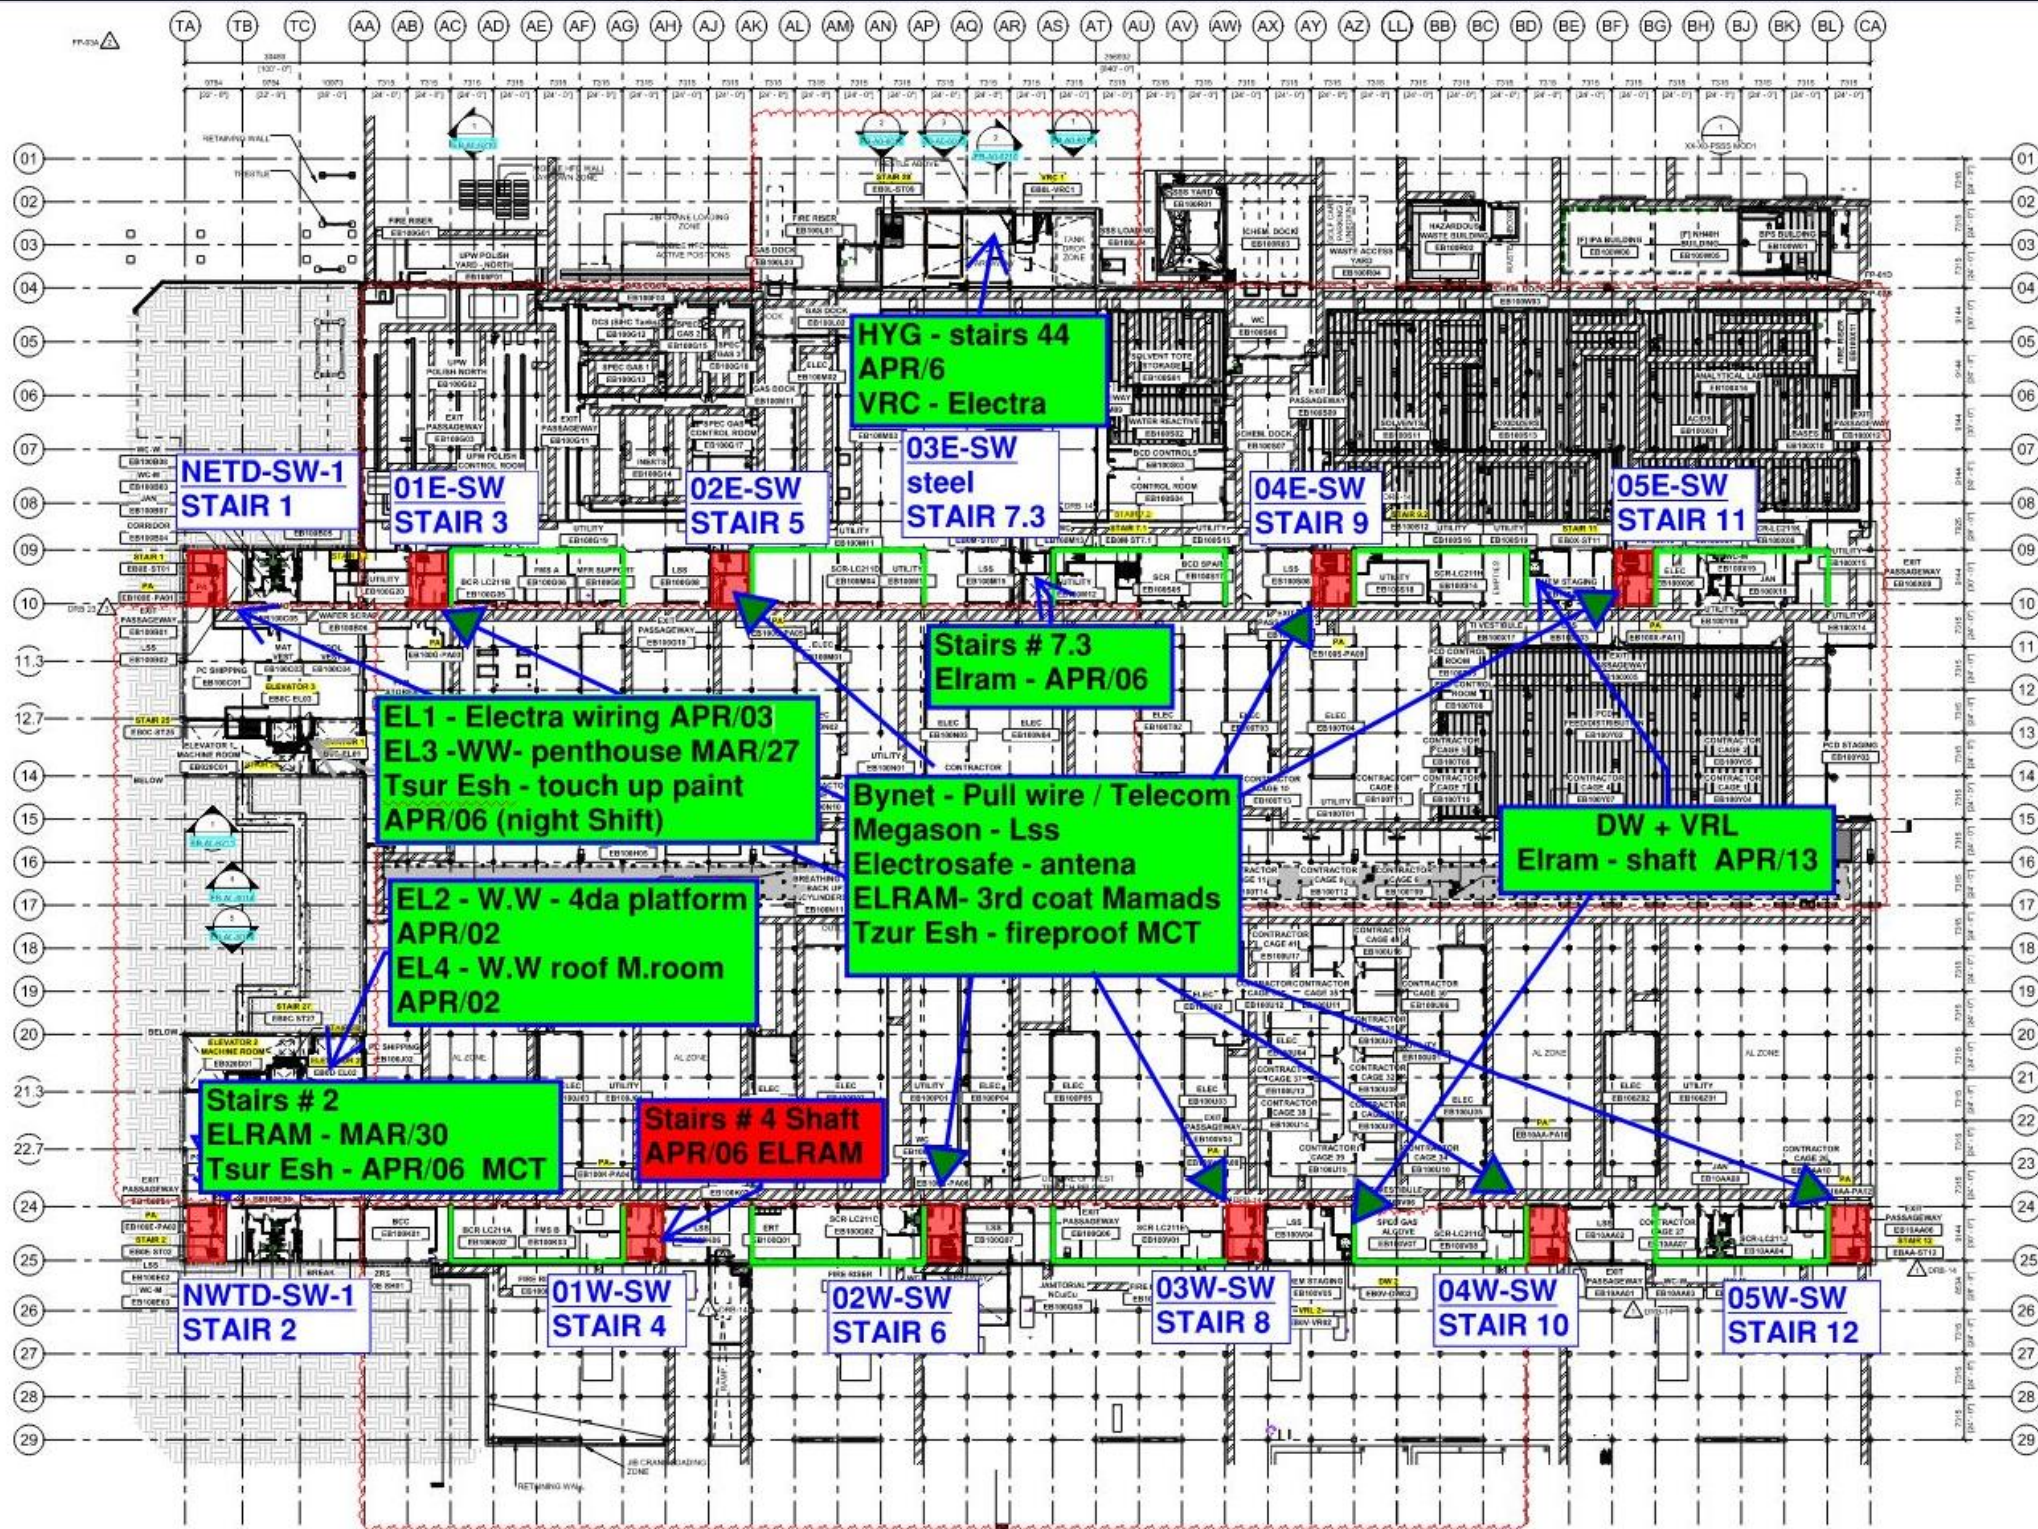


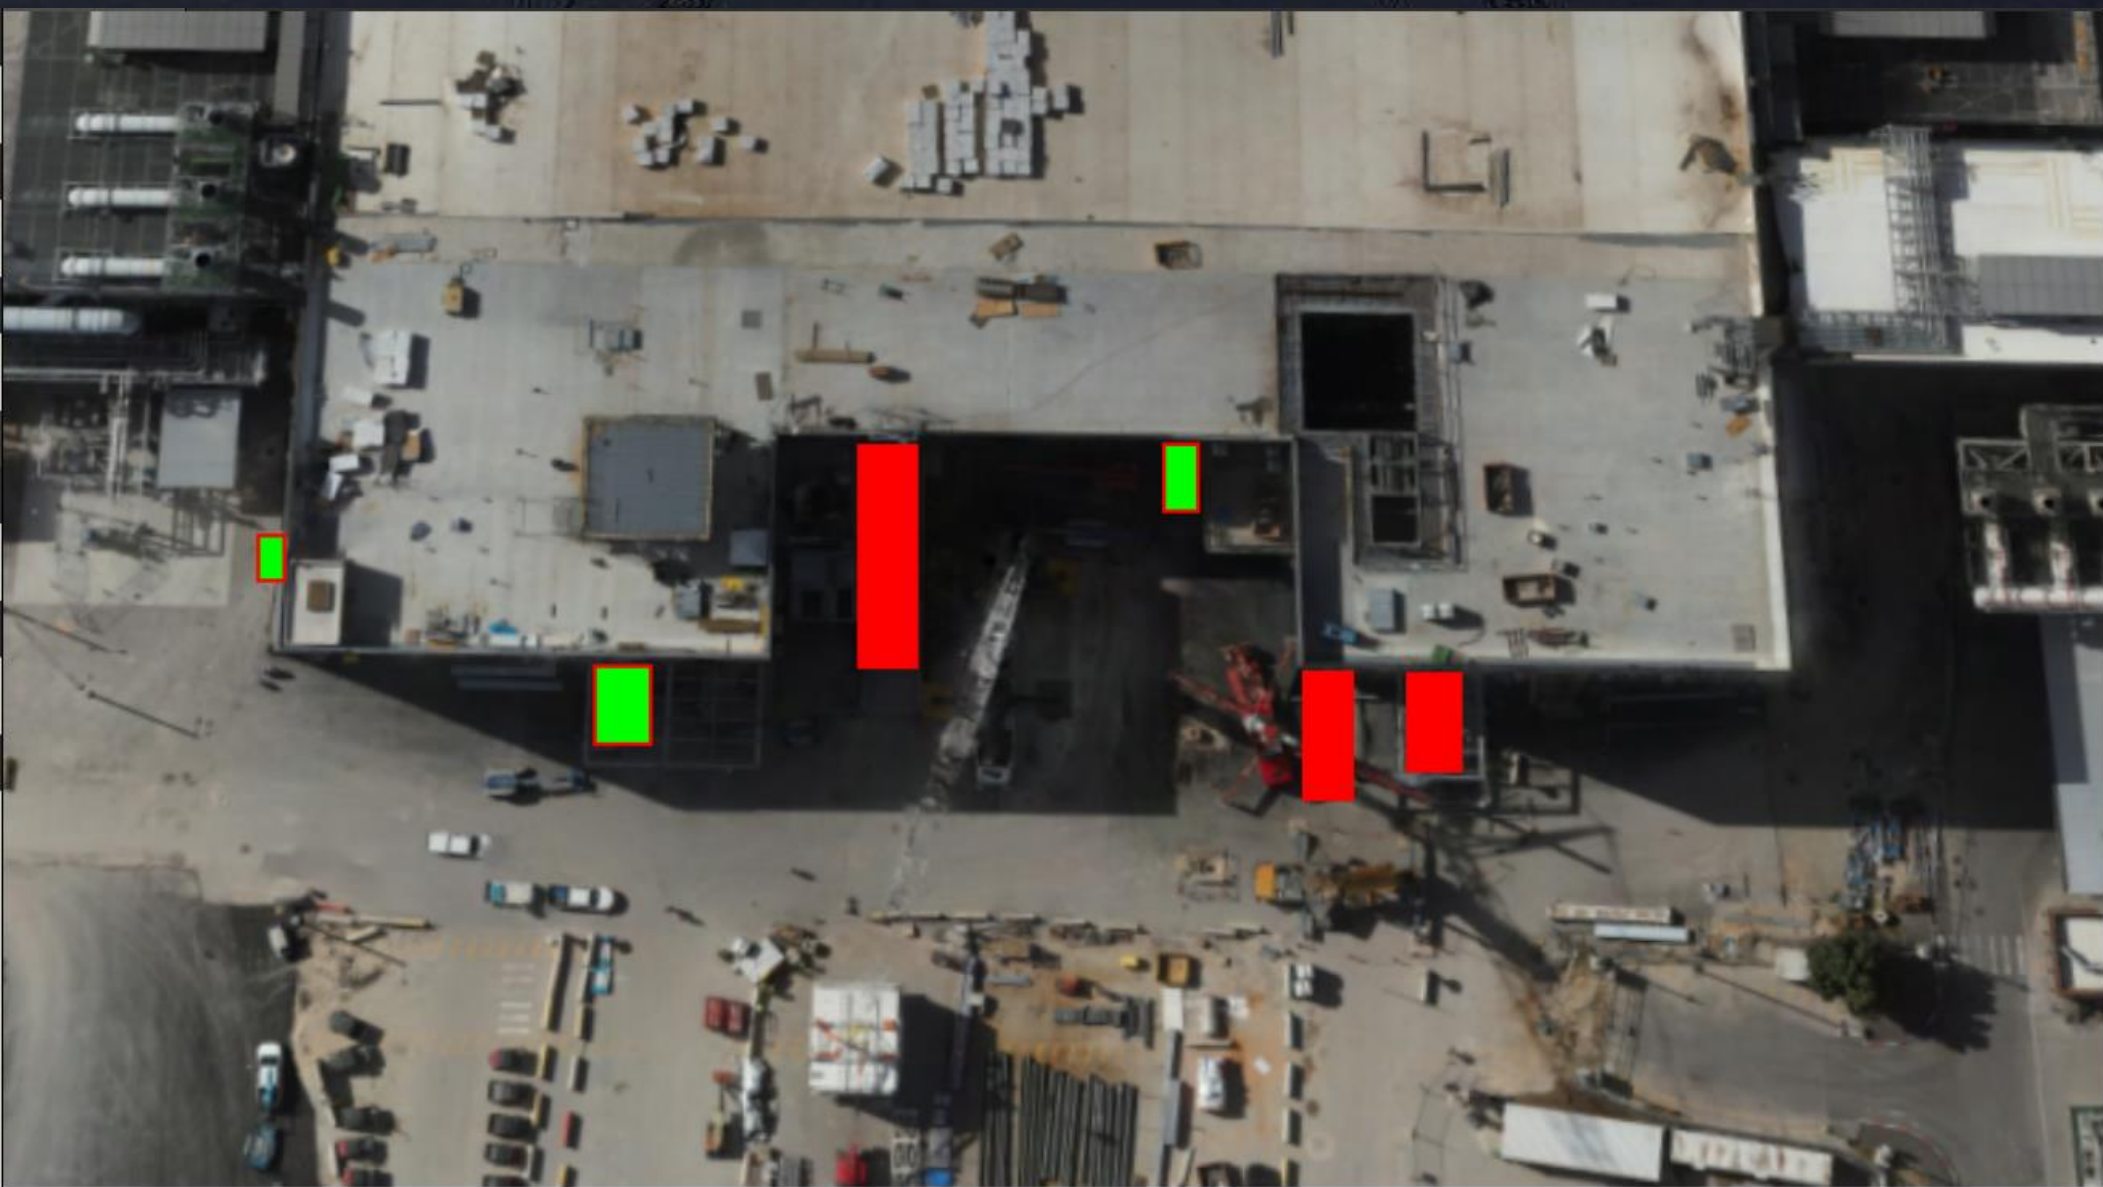




- READY FOR GIRTS
- INSTALLING GIRTS
- READY FOR PANELS
- PANELS INSTALLED

MOD 2 WESTSIDE GIRTS/SIDING

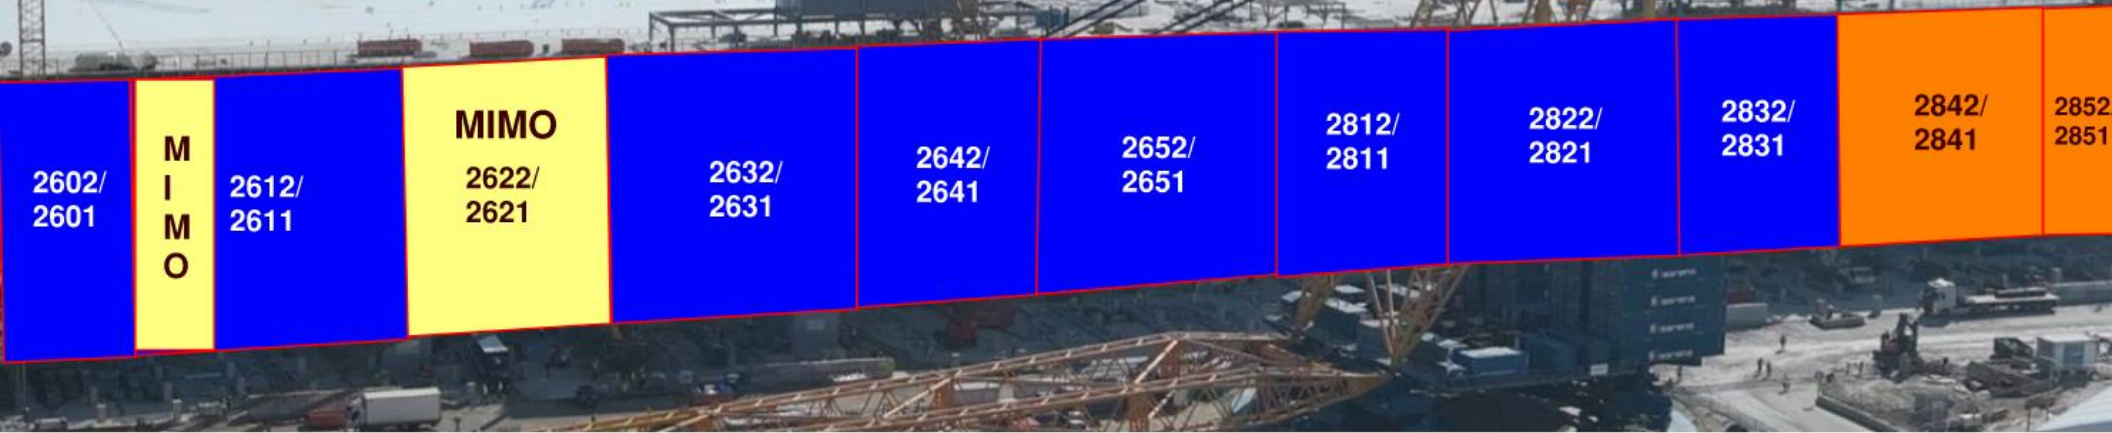


MOD 2 EASTSIDE GIRTS/SIDING

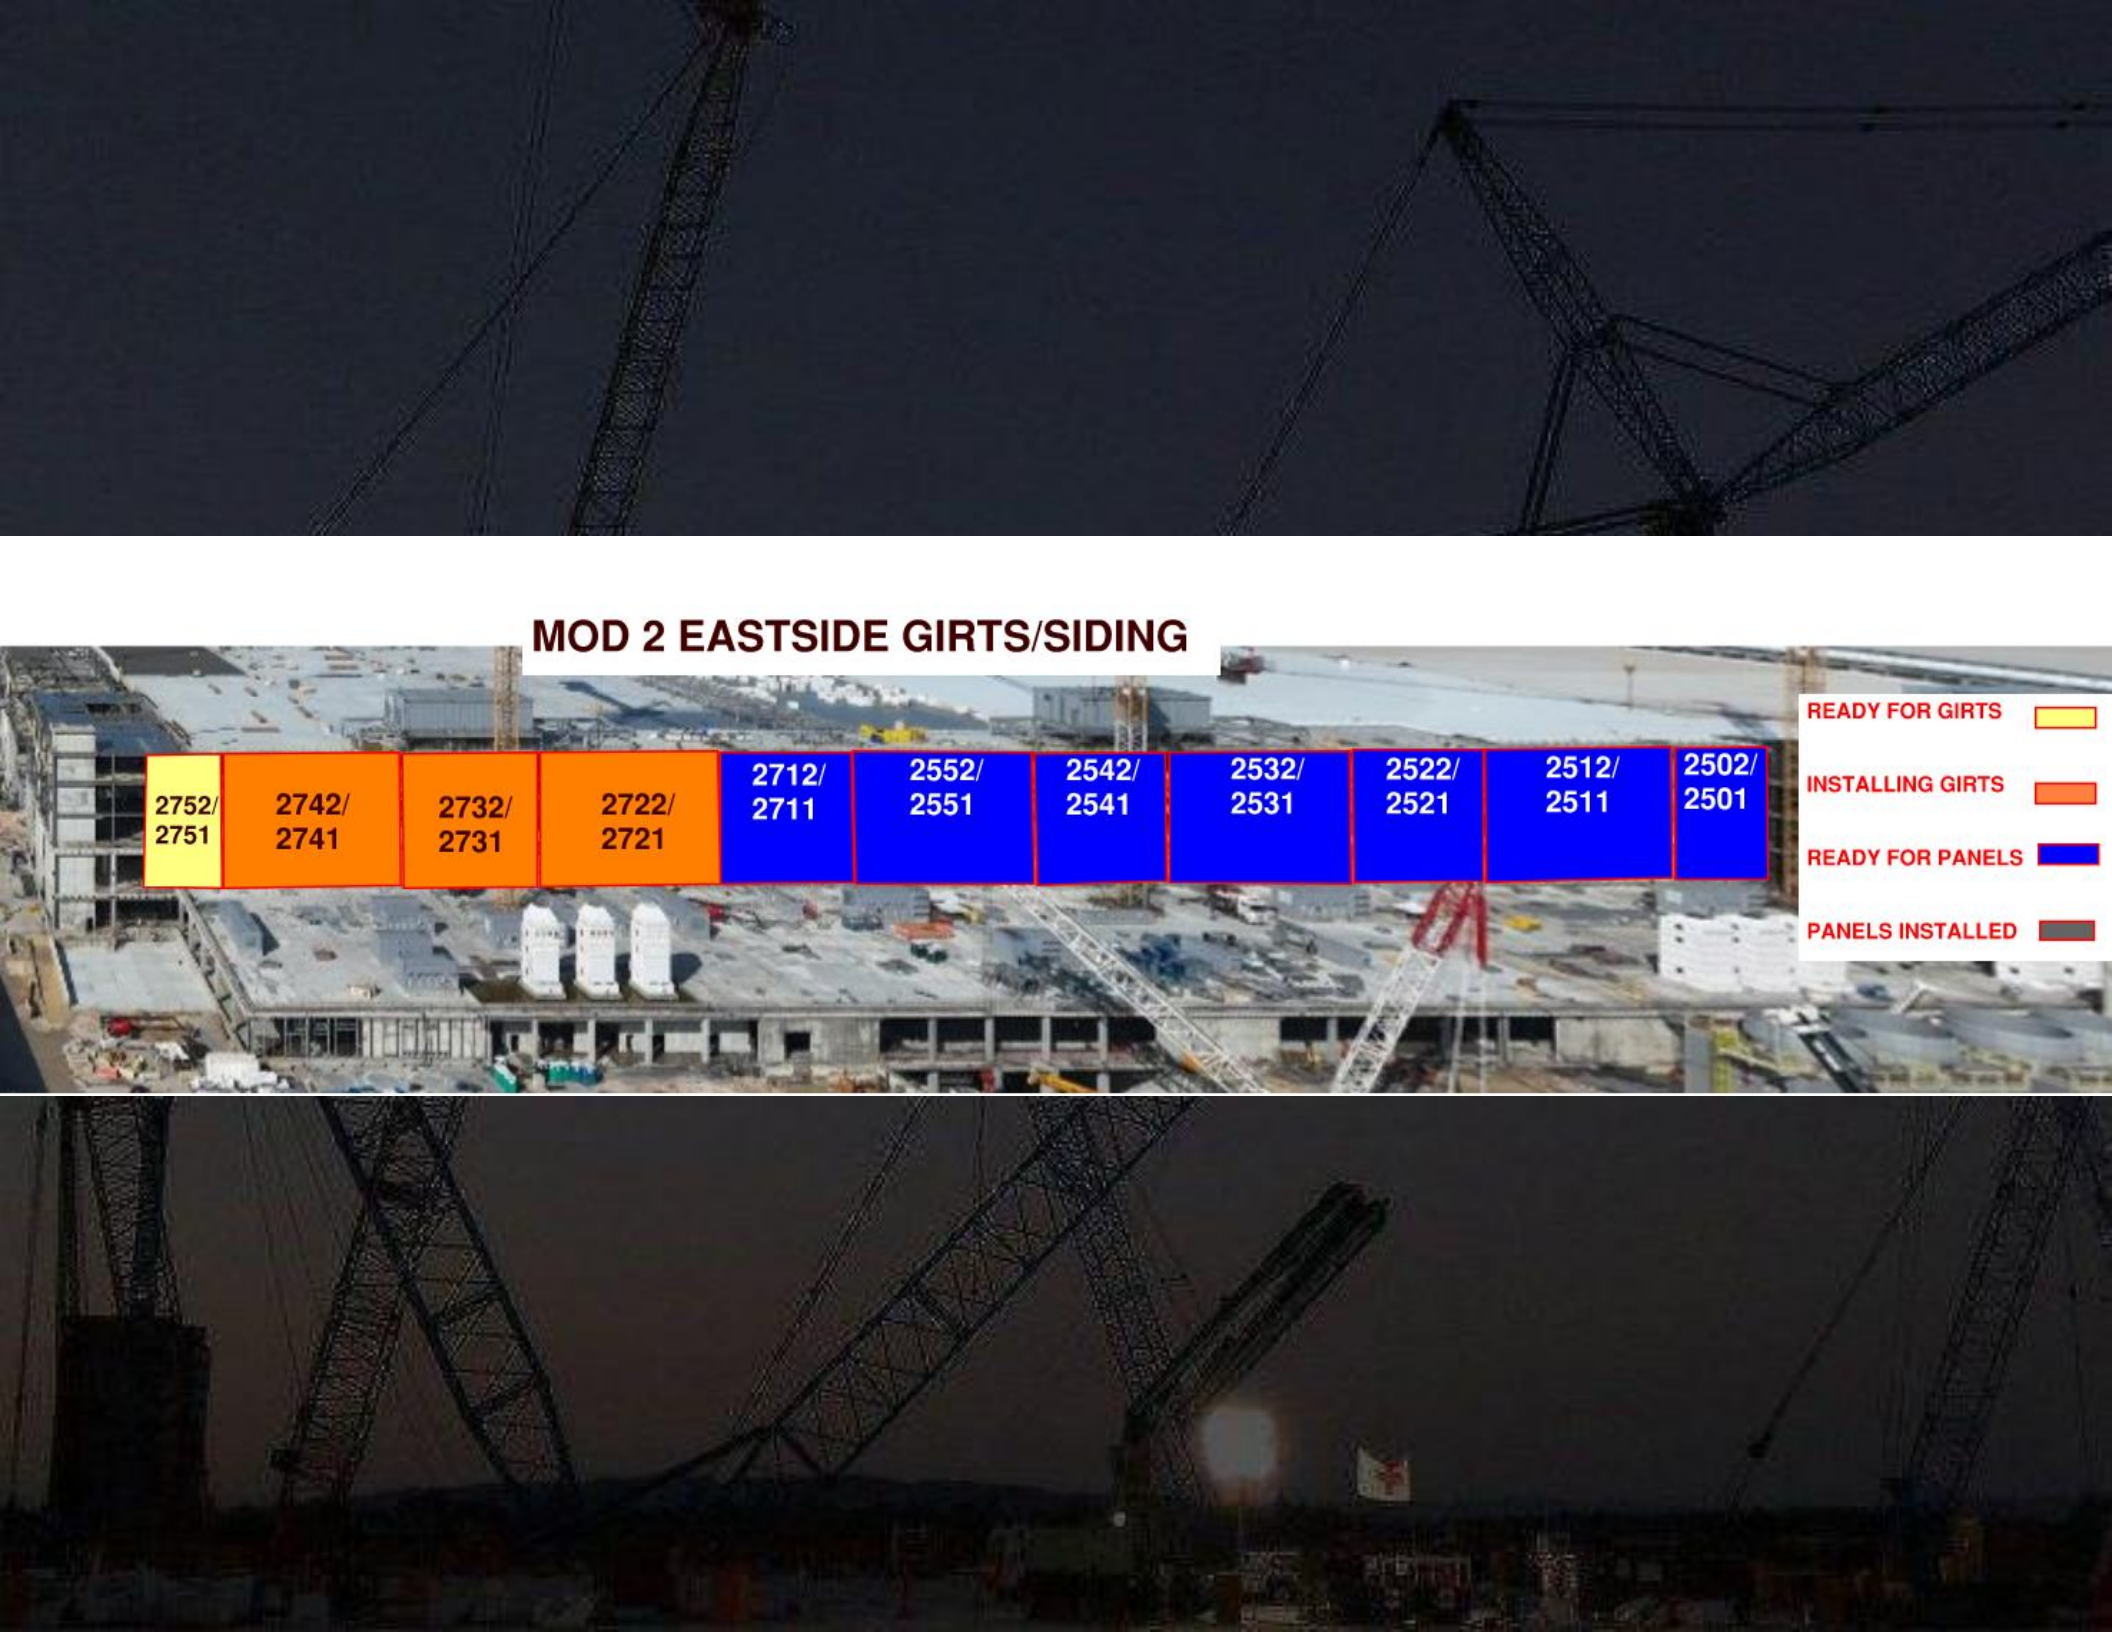


2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501
---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	


PSSS.1

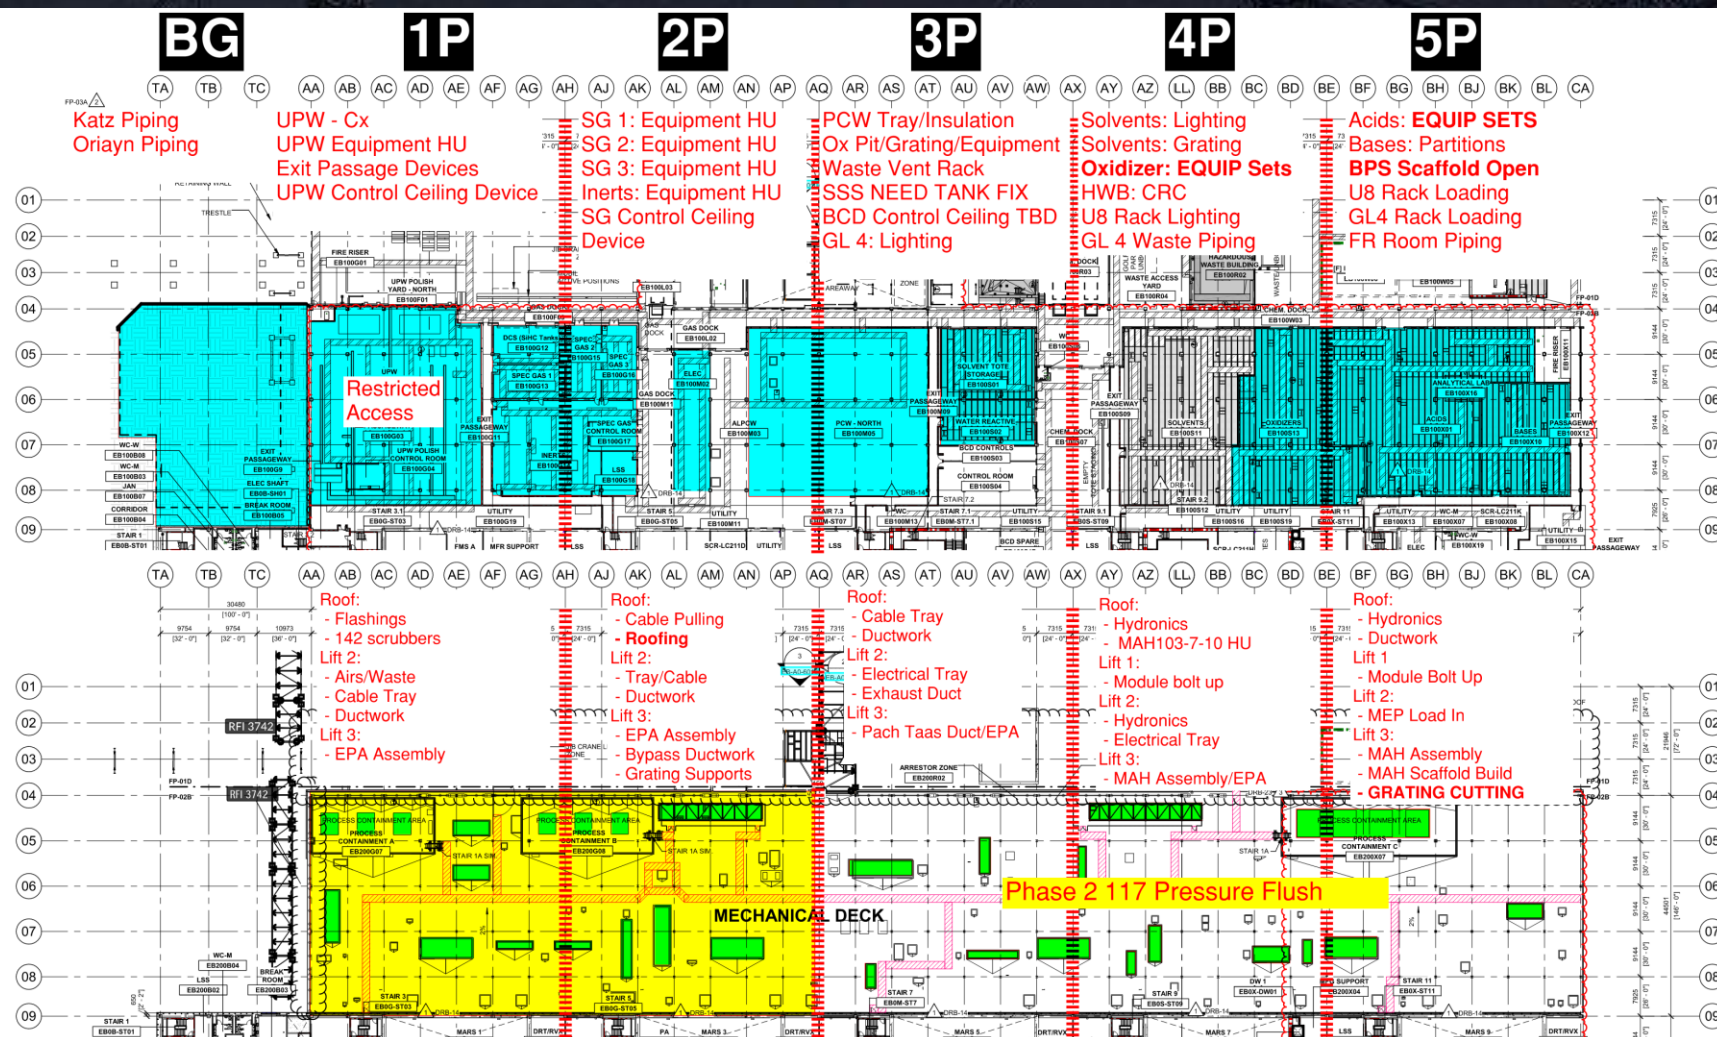

PSSS Roof
2SA

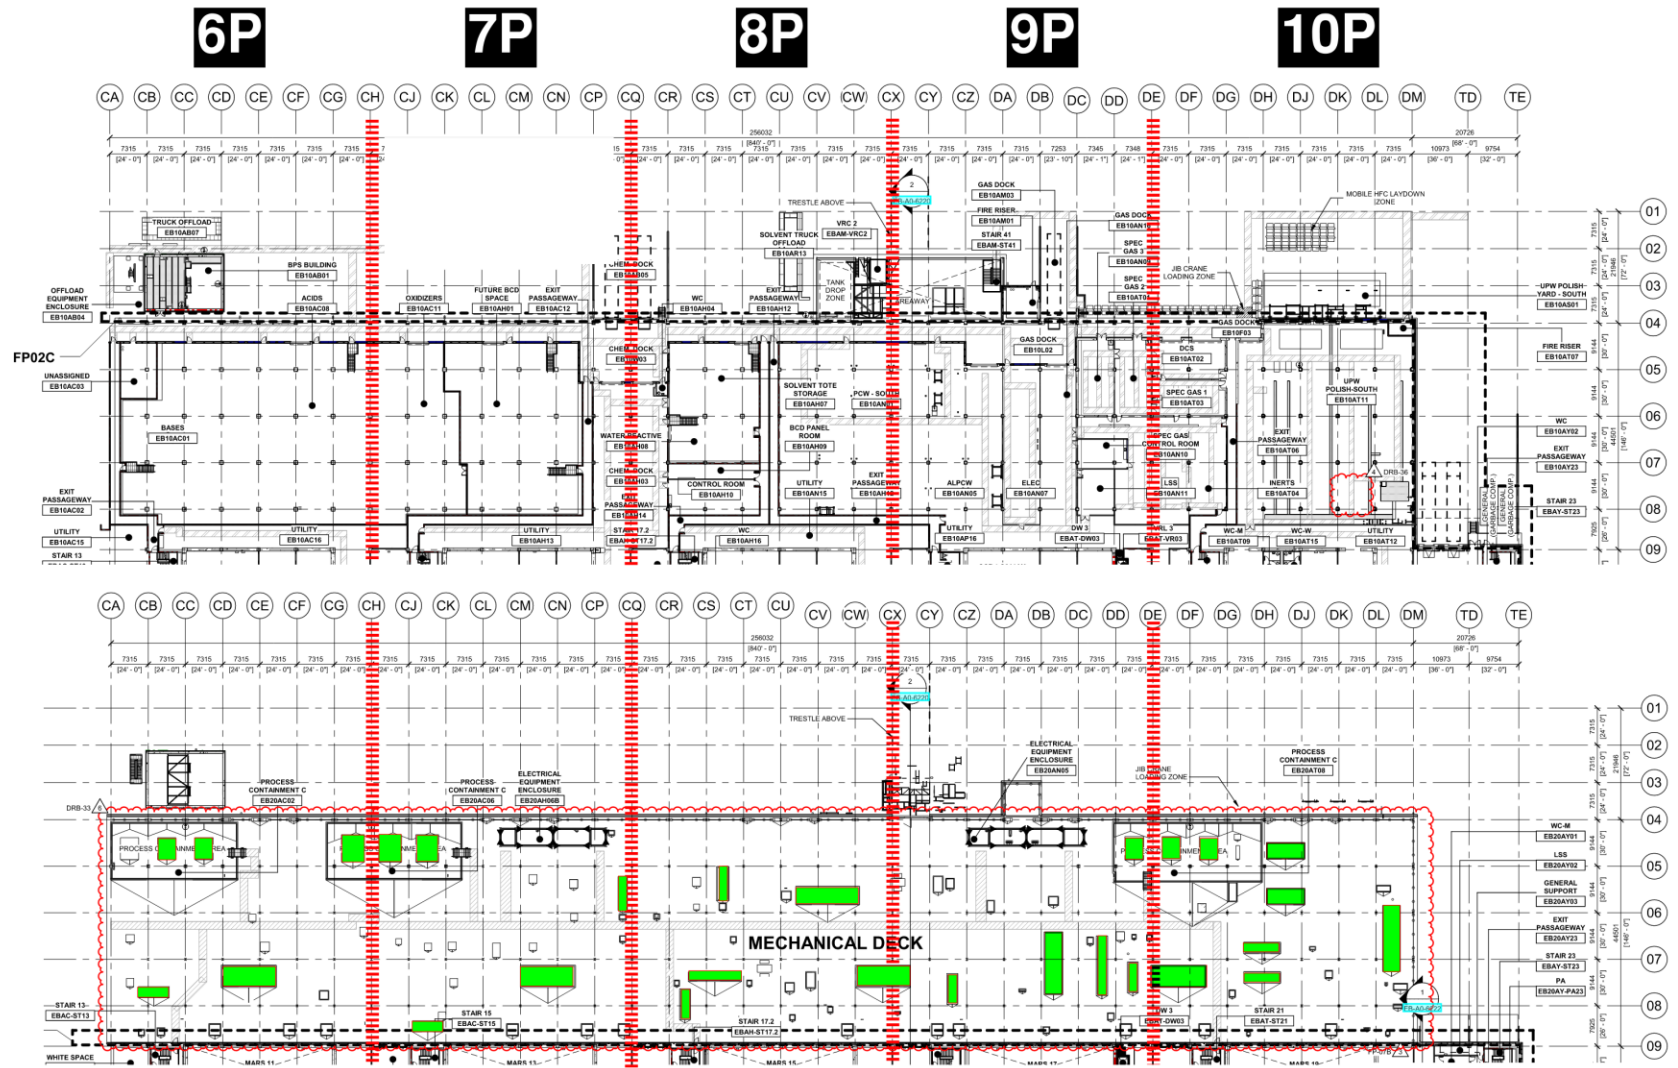


OFA PRRESURE TEST 17:00- 05:00

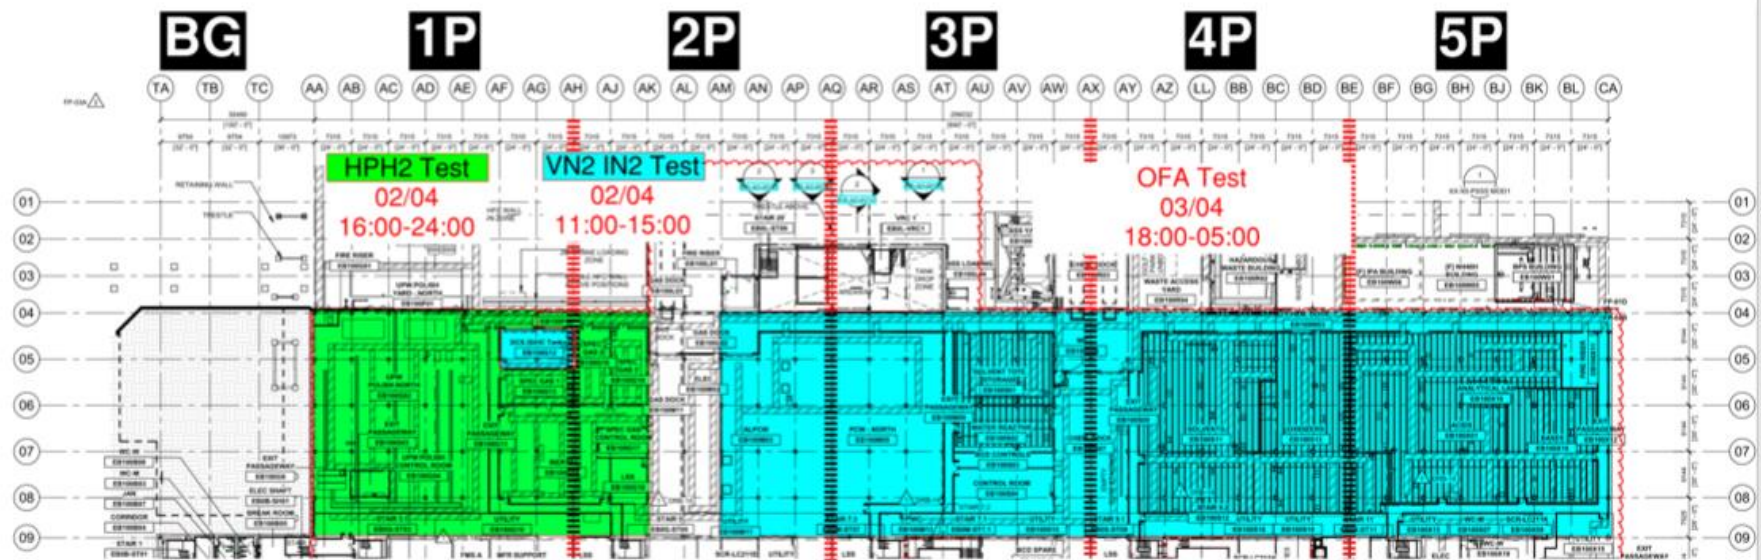

Utility Level
1YA

MODE 2 VFD - 220 TON CRANE SUN 6th - MON 7th

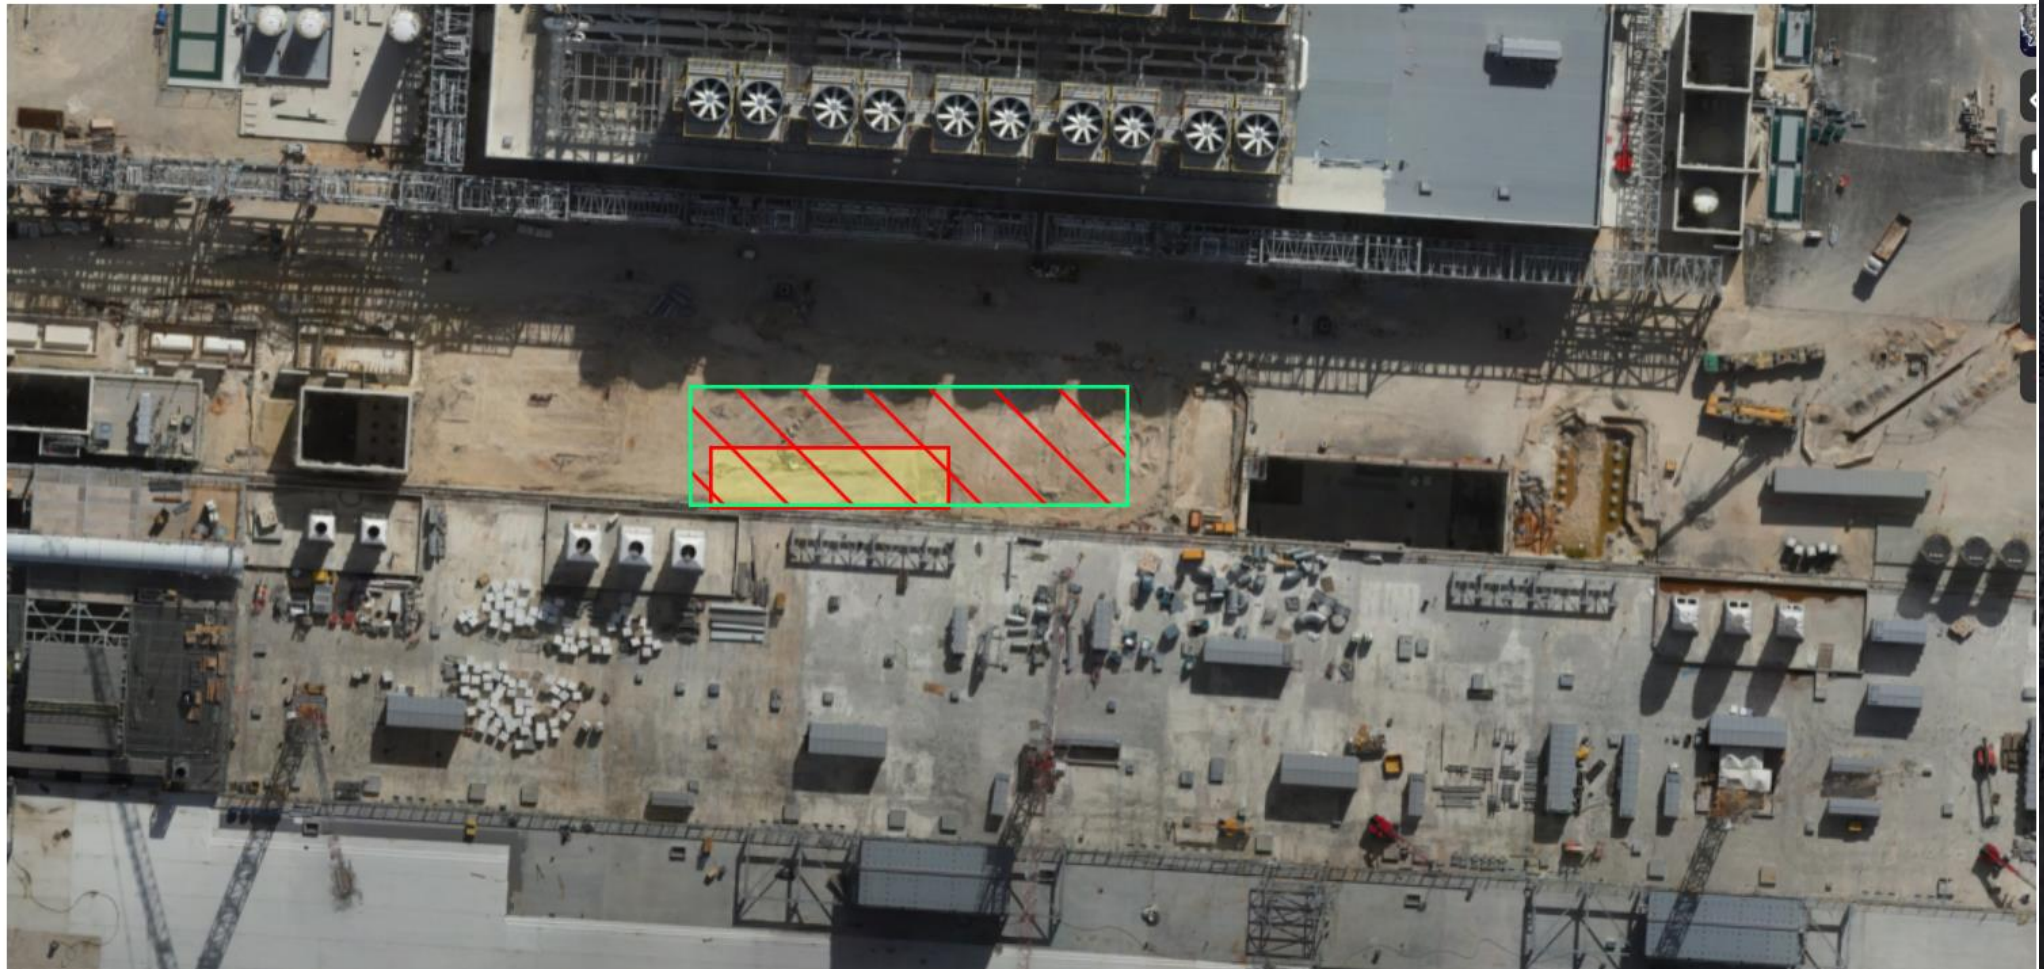


WJG – UL

* Pach Taas - completion of spools and lindapters on UPN 138
 * Pach Taas - working on connections of WP to modules

* Chemo - performing passivation on UPN 111 (UL + lift 2)

* Afcon - Installation of lighting and cable pulling

* ASD - erection of scaffold for VFD derains
 * W&W - welding connections on CA line for MOD2 steel
 * CB - working on small AH ducts.

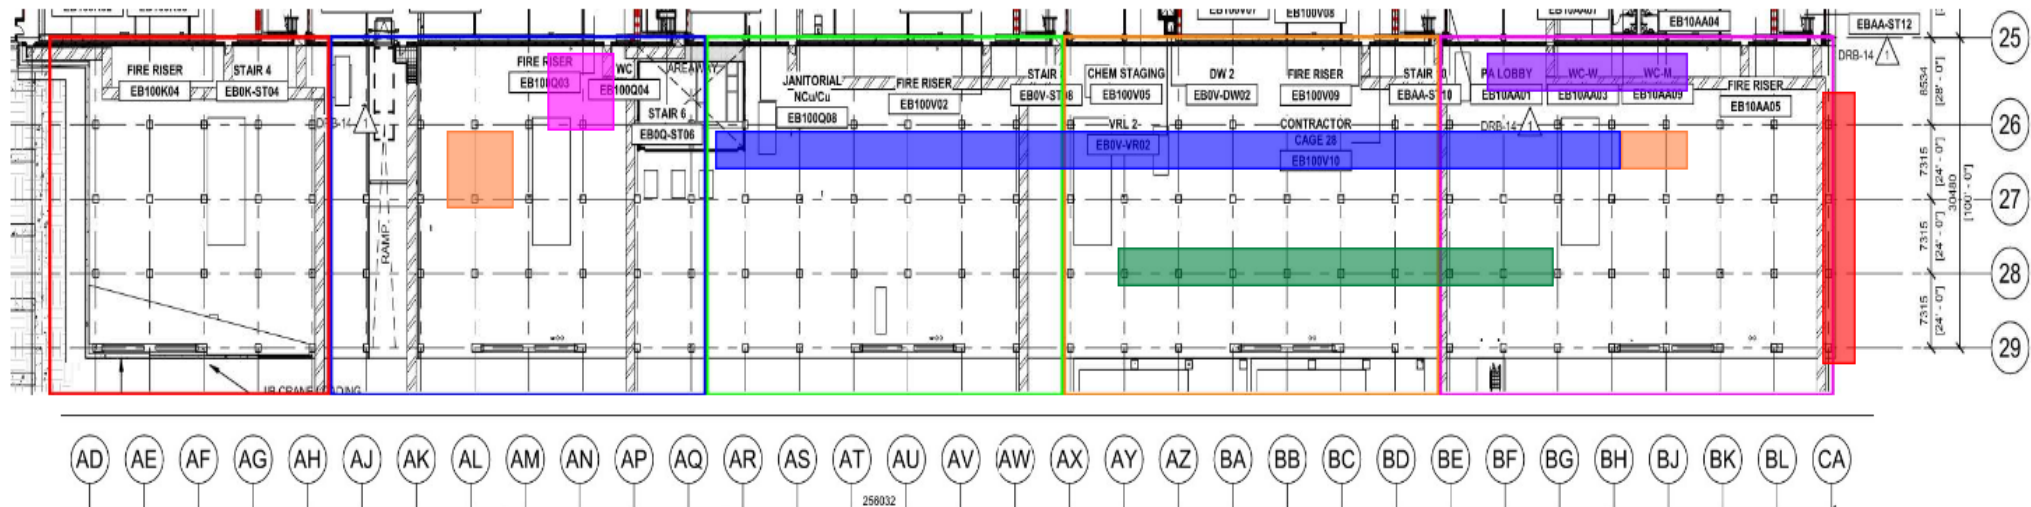


WJG – Lift 2

* Chemo - about to start restoration of UPN 113 once water test results are good
* Carmel Bidud - installing handrails to open planking for stiffeners

* Afcon - installation of trays to exhaust fans

* Chemo - continuing insulation
* SK - performing connections to MAH (later this week, scaffold will be turned to yellow tag)

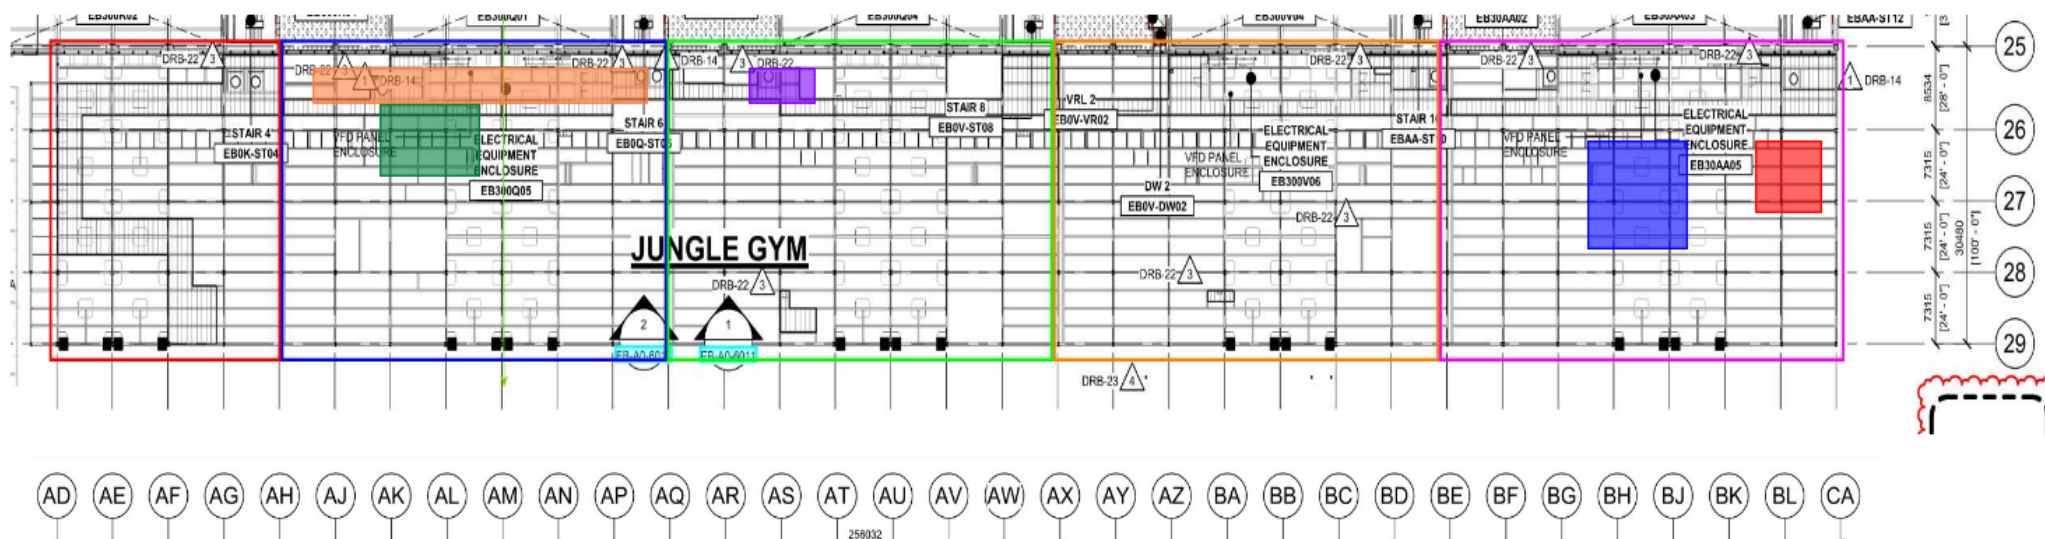

WJG – Lift 3

* Chemo - hoisting and installing 4J
MARS pipes

* SN - handrai installation and
penetrations



Crane logistics


Crane: 750 ton crane
moving south of RCTO
Tuesday 08/04/25




CUB 1 2 working days to room ready




CUB 1 Ops Ready April 24

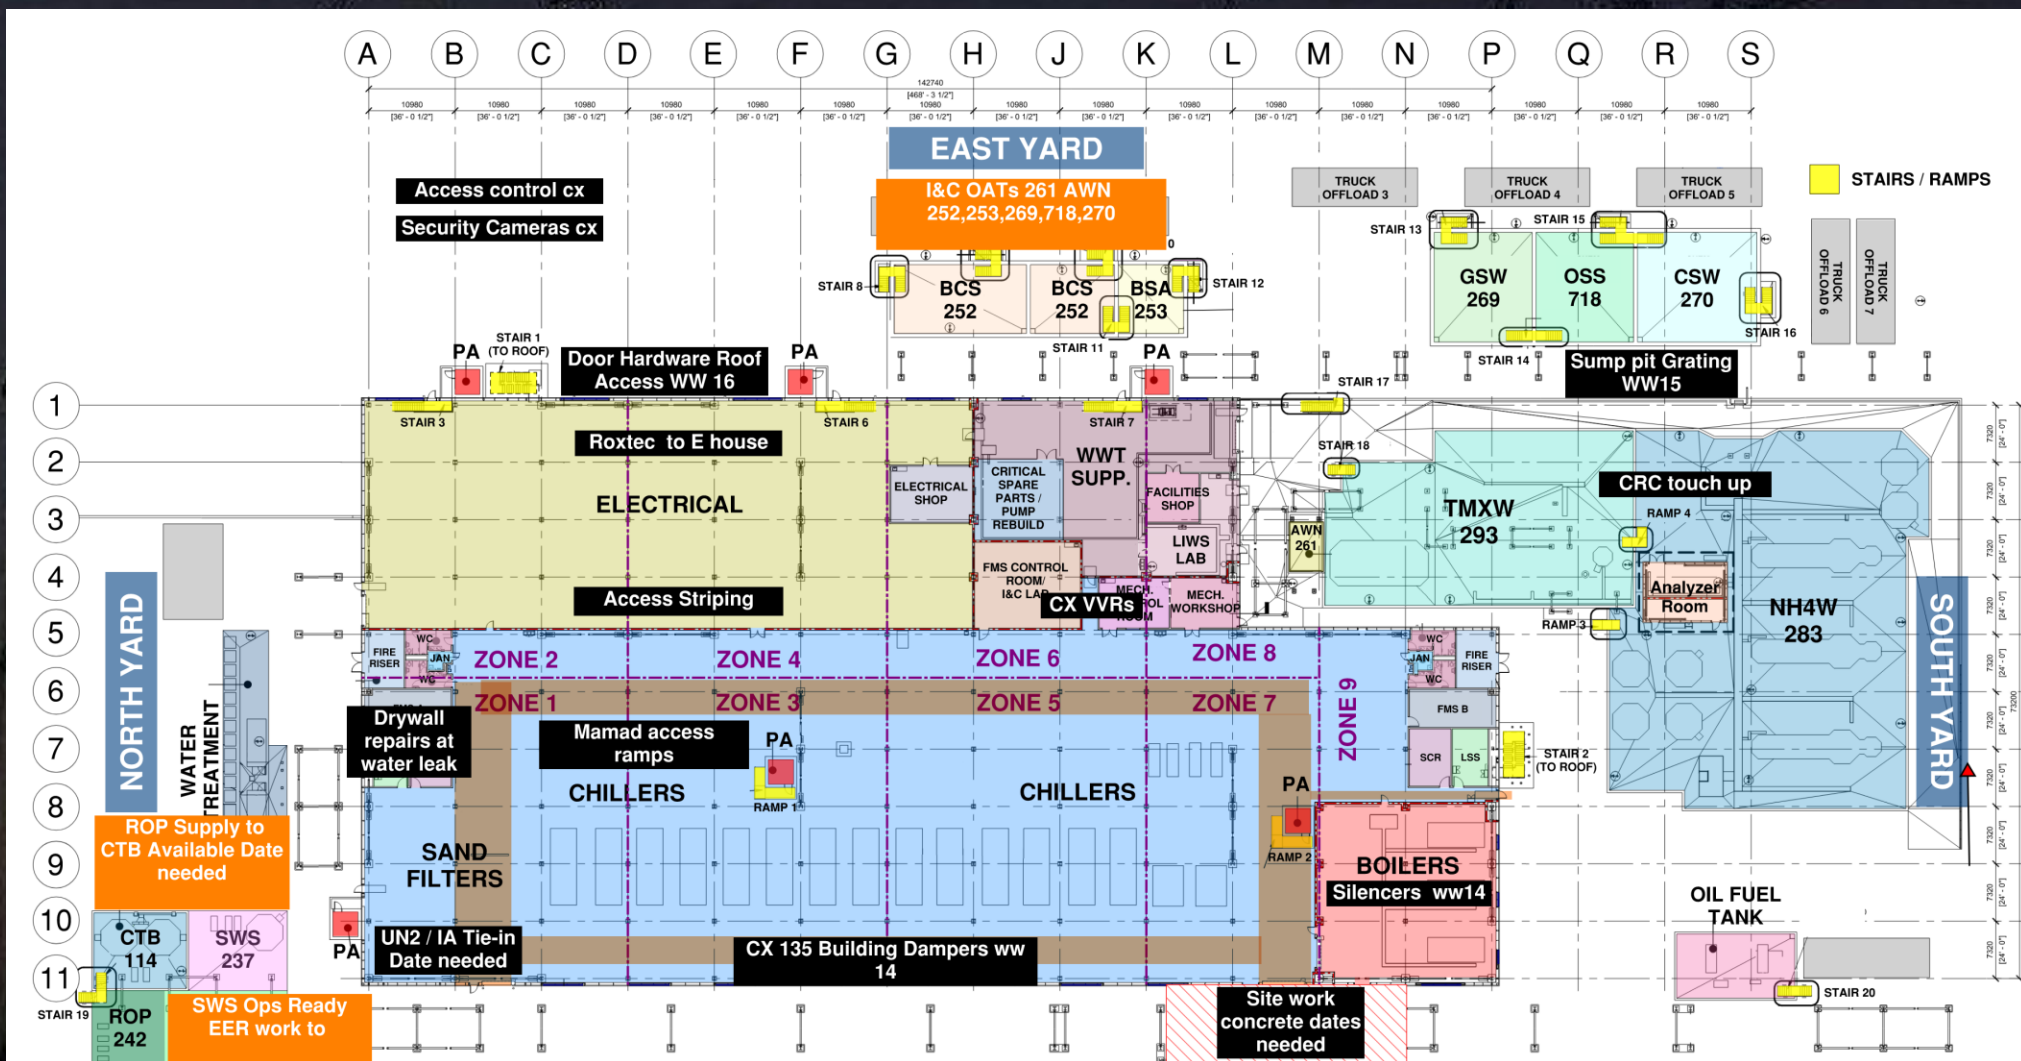


CUB 1 – EXTERIOR/ROOF

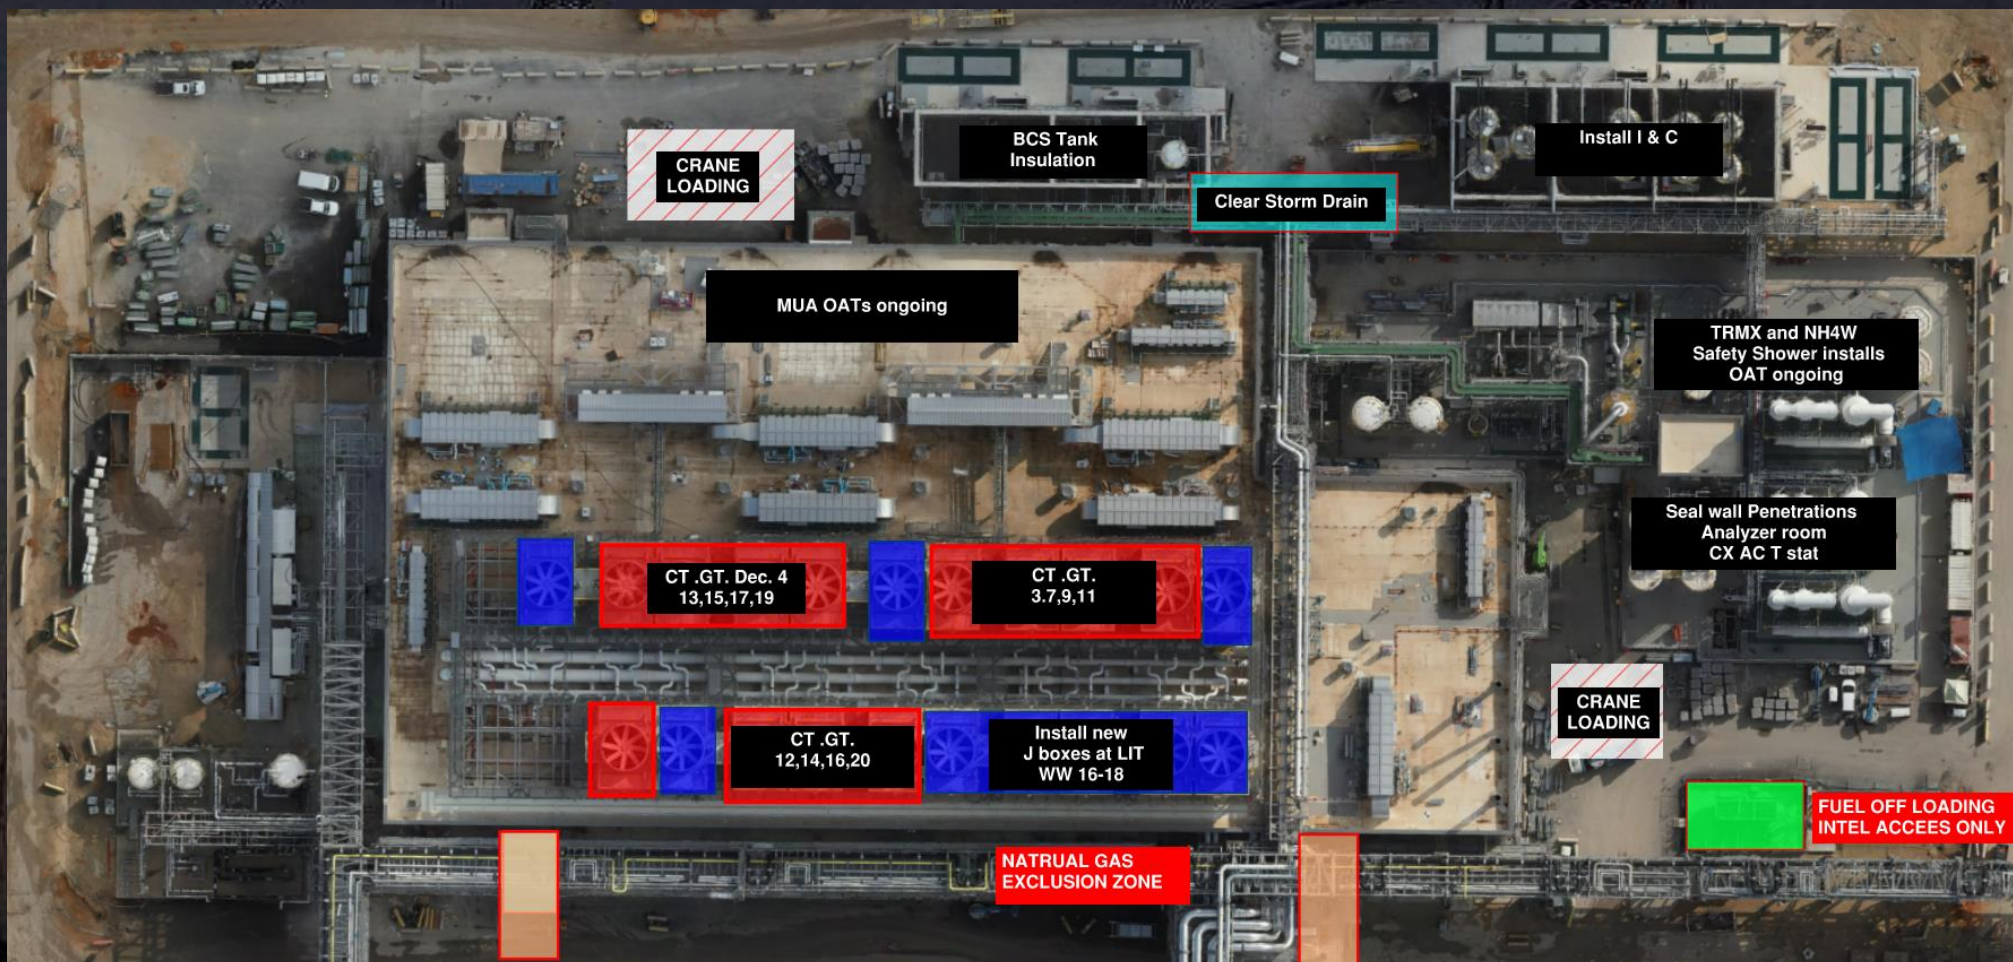

CUB 2- NDT Pipe weld testing April 6-7 1800-0200

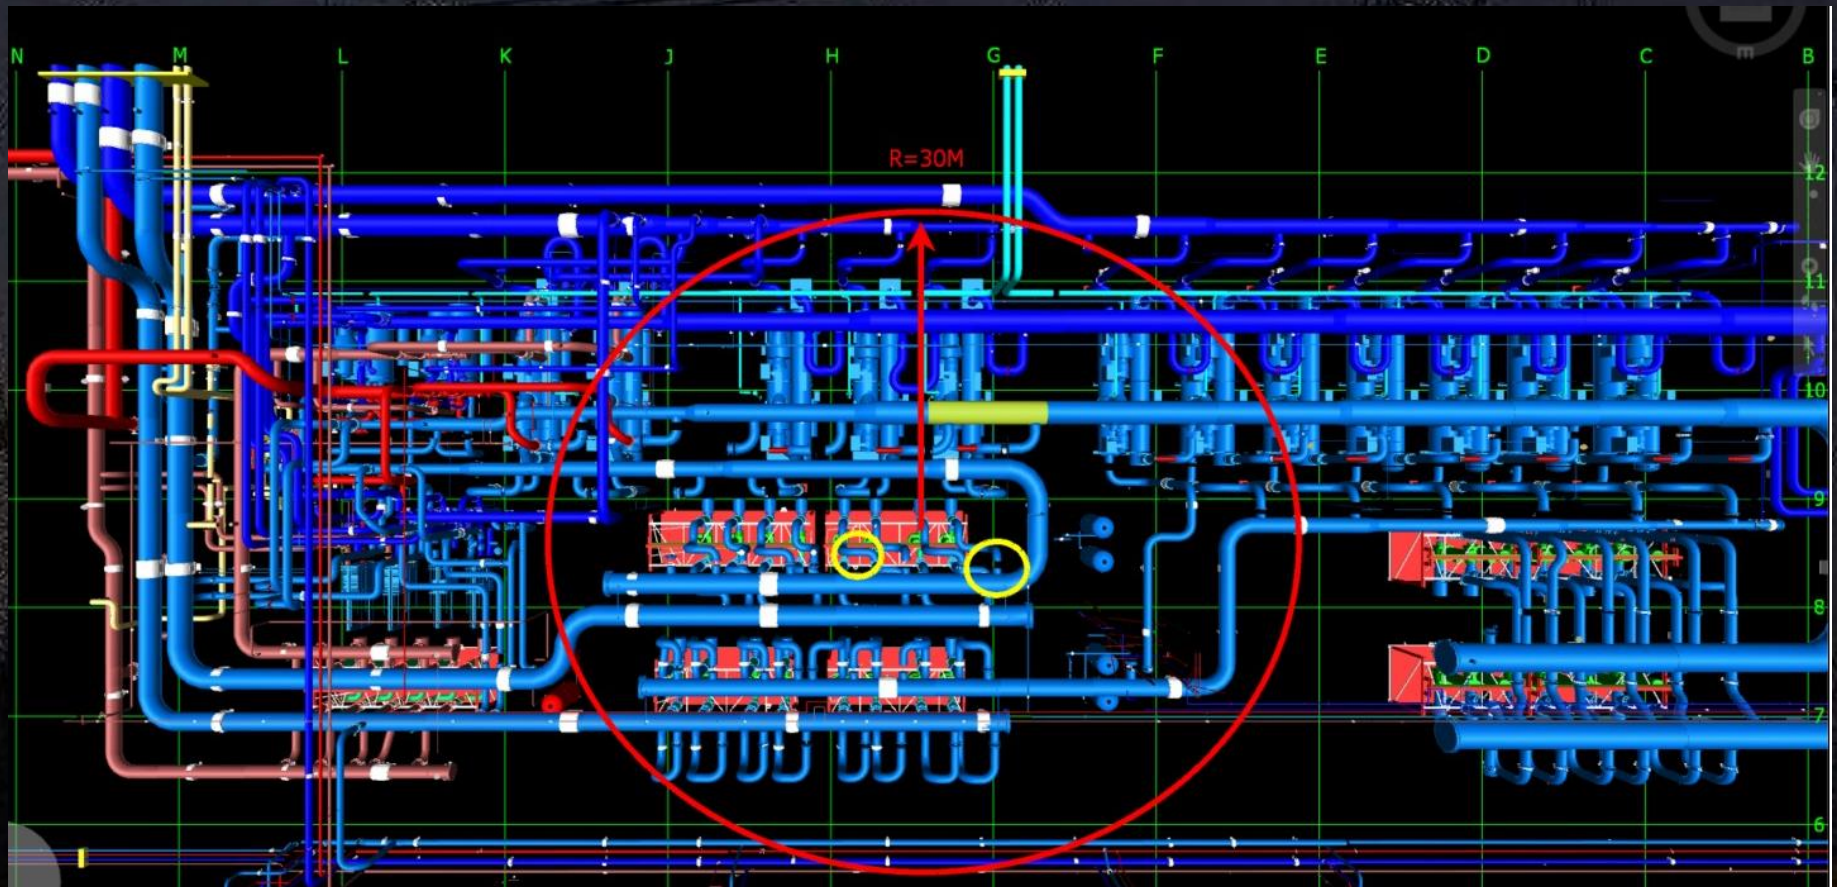

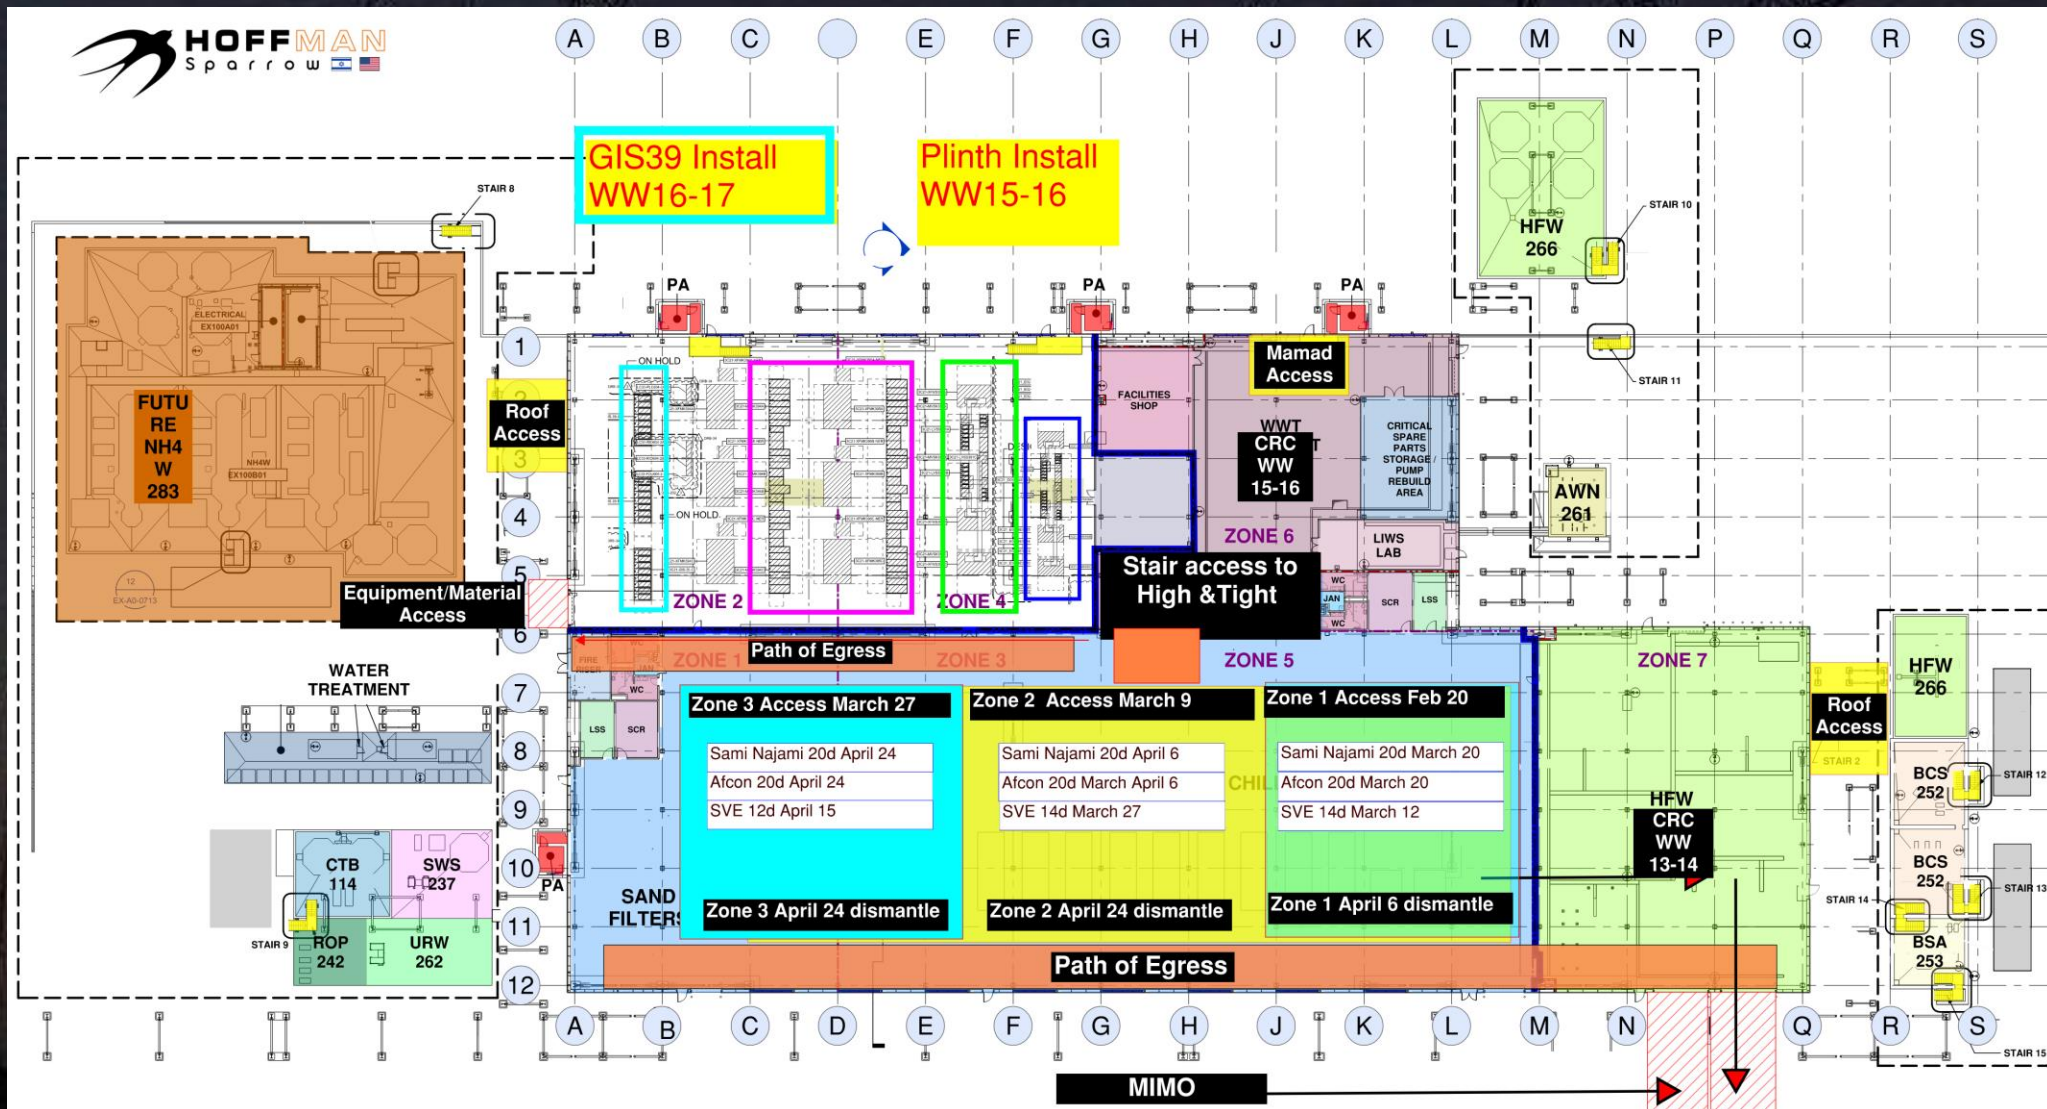


CUB 2 – EXTERIOR/ROOF








Site- temporary power

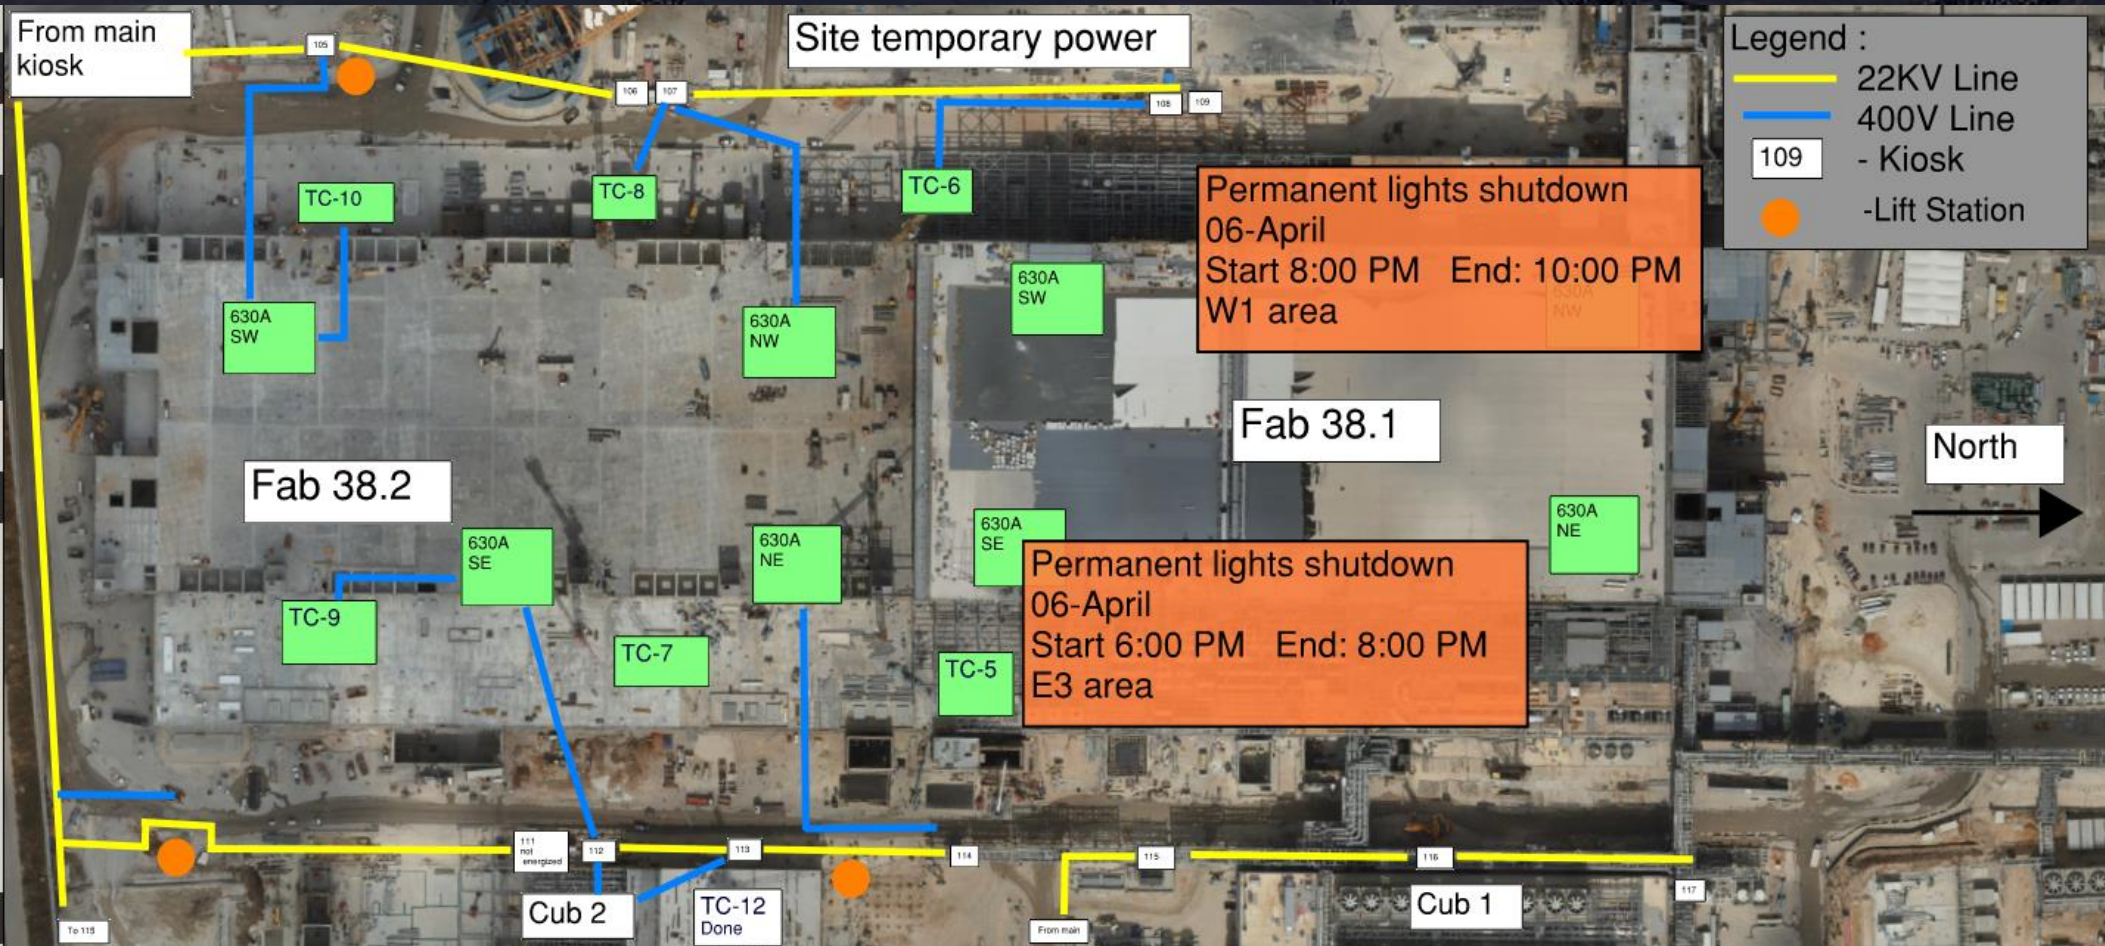

Daily Coordination Meeting


Site Logistics

North

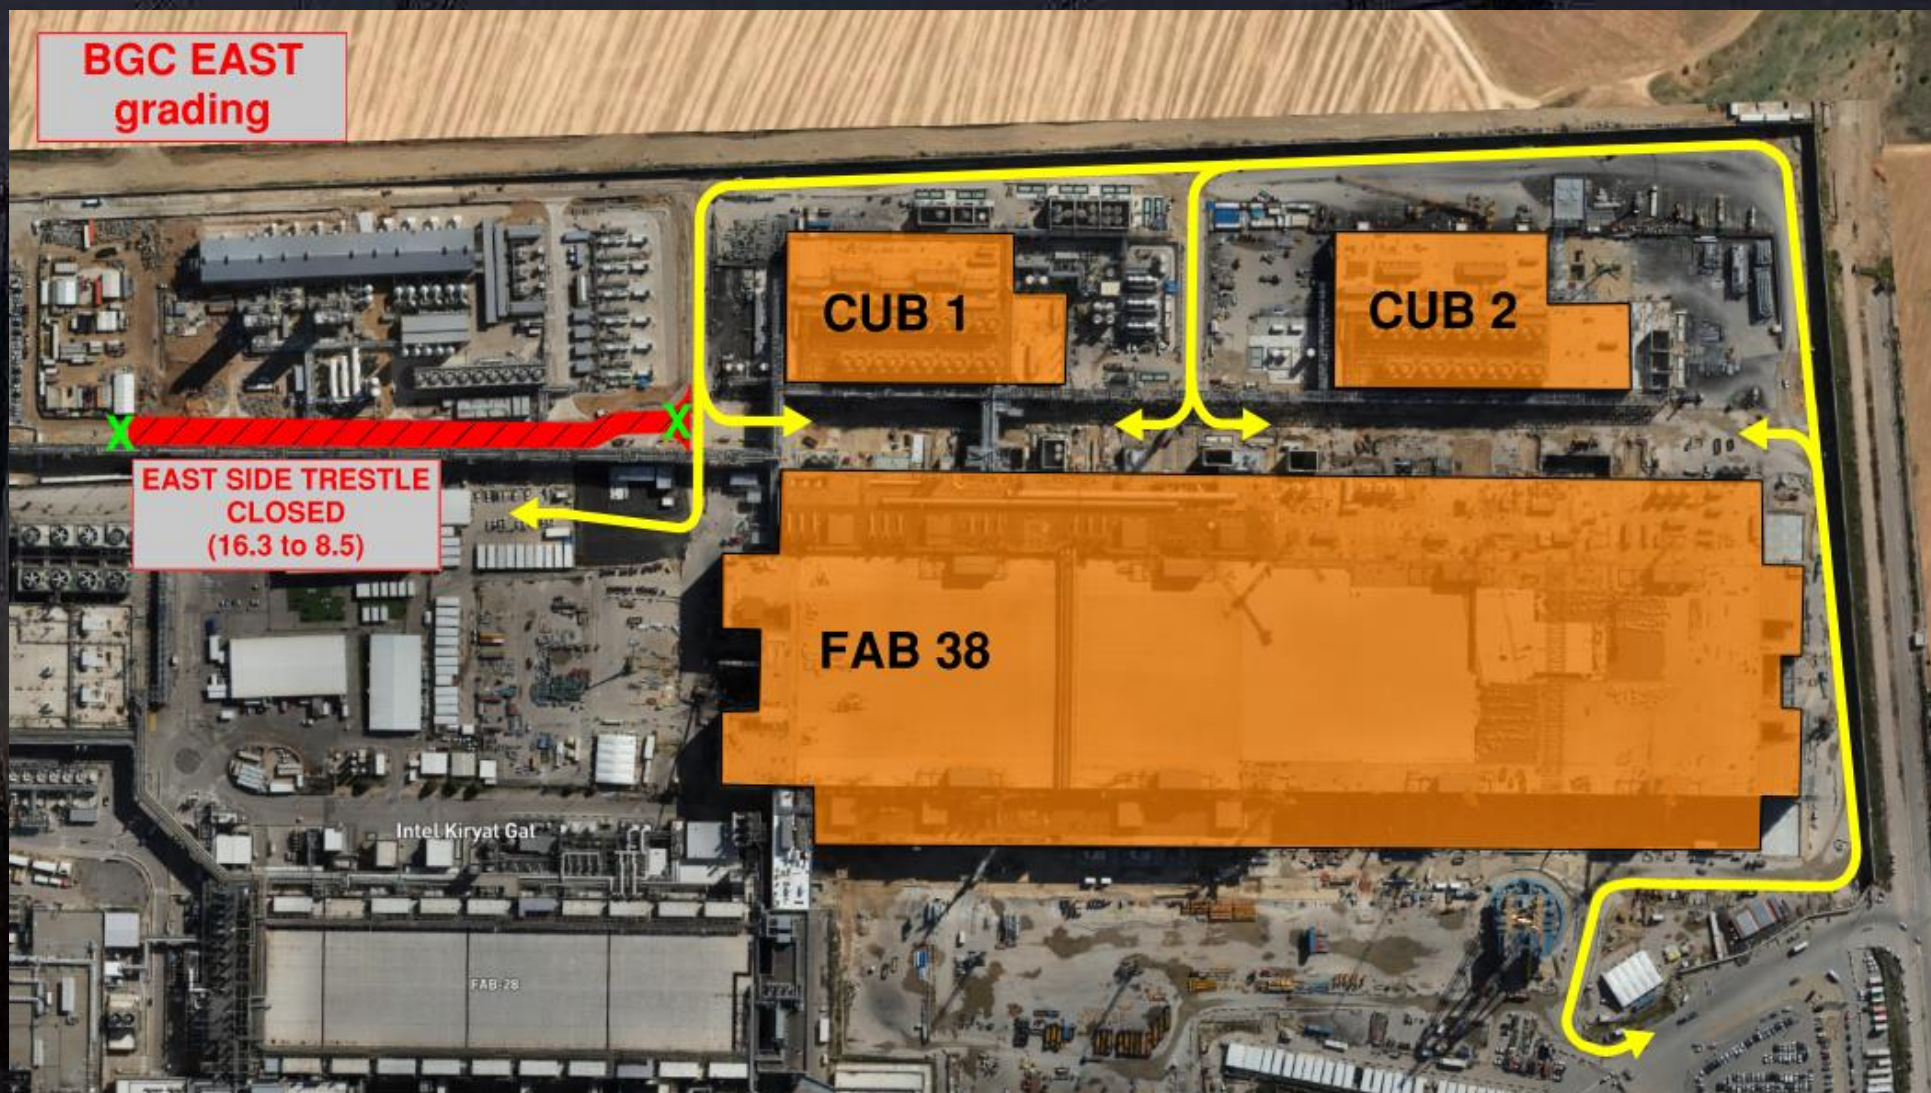


Daily Coordination Meeting

Site Logistics North

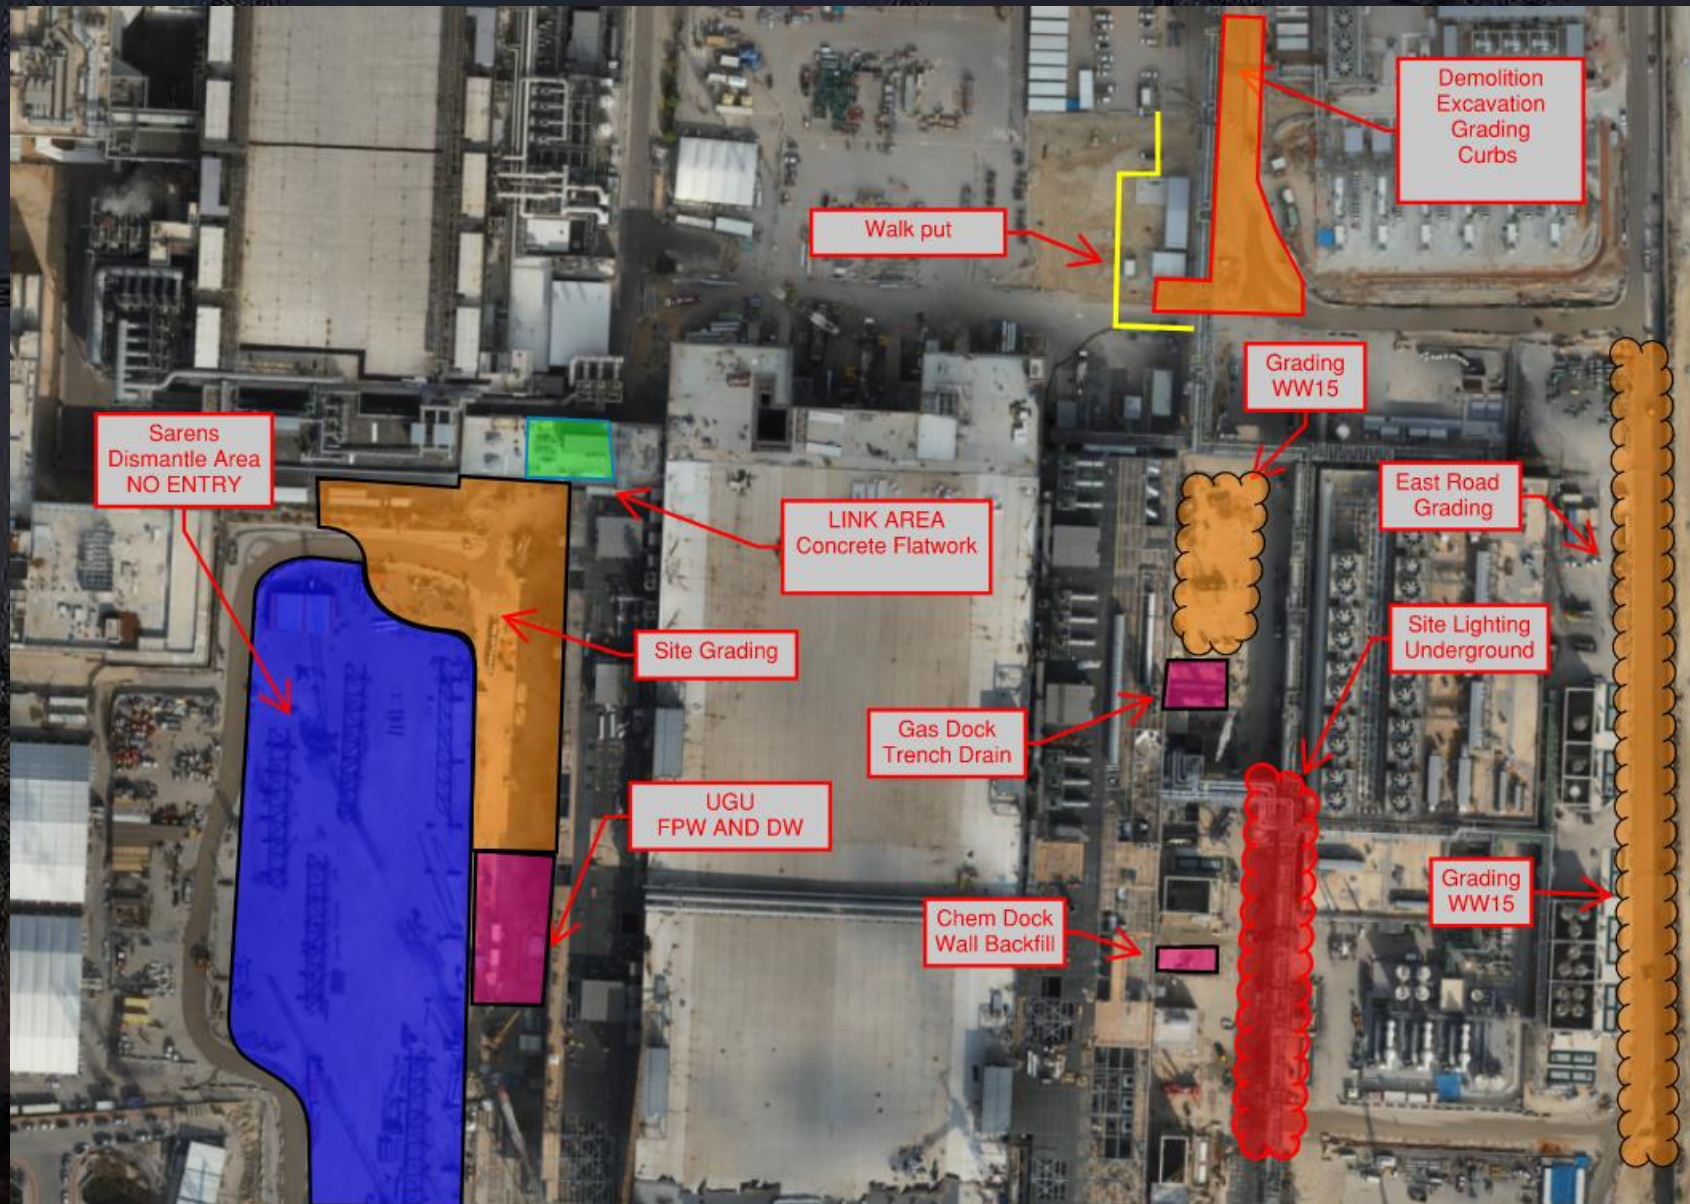

Daily Coordination Meeting


Site Logistics South

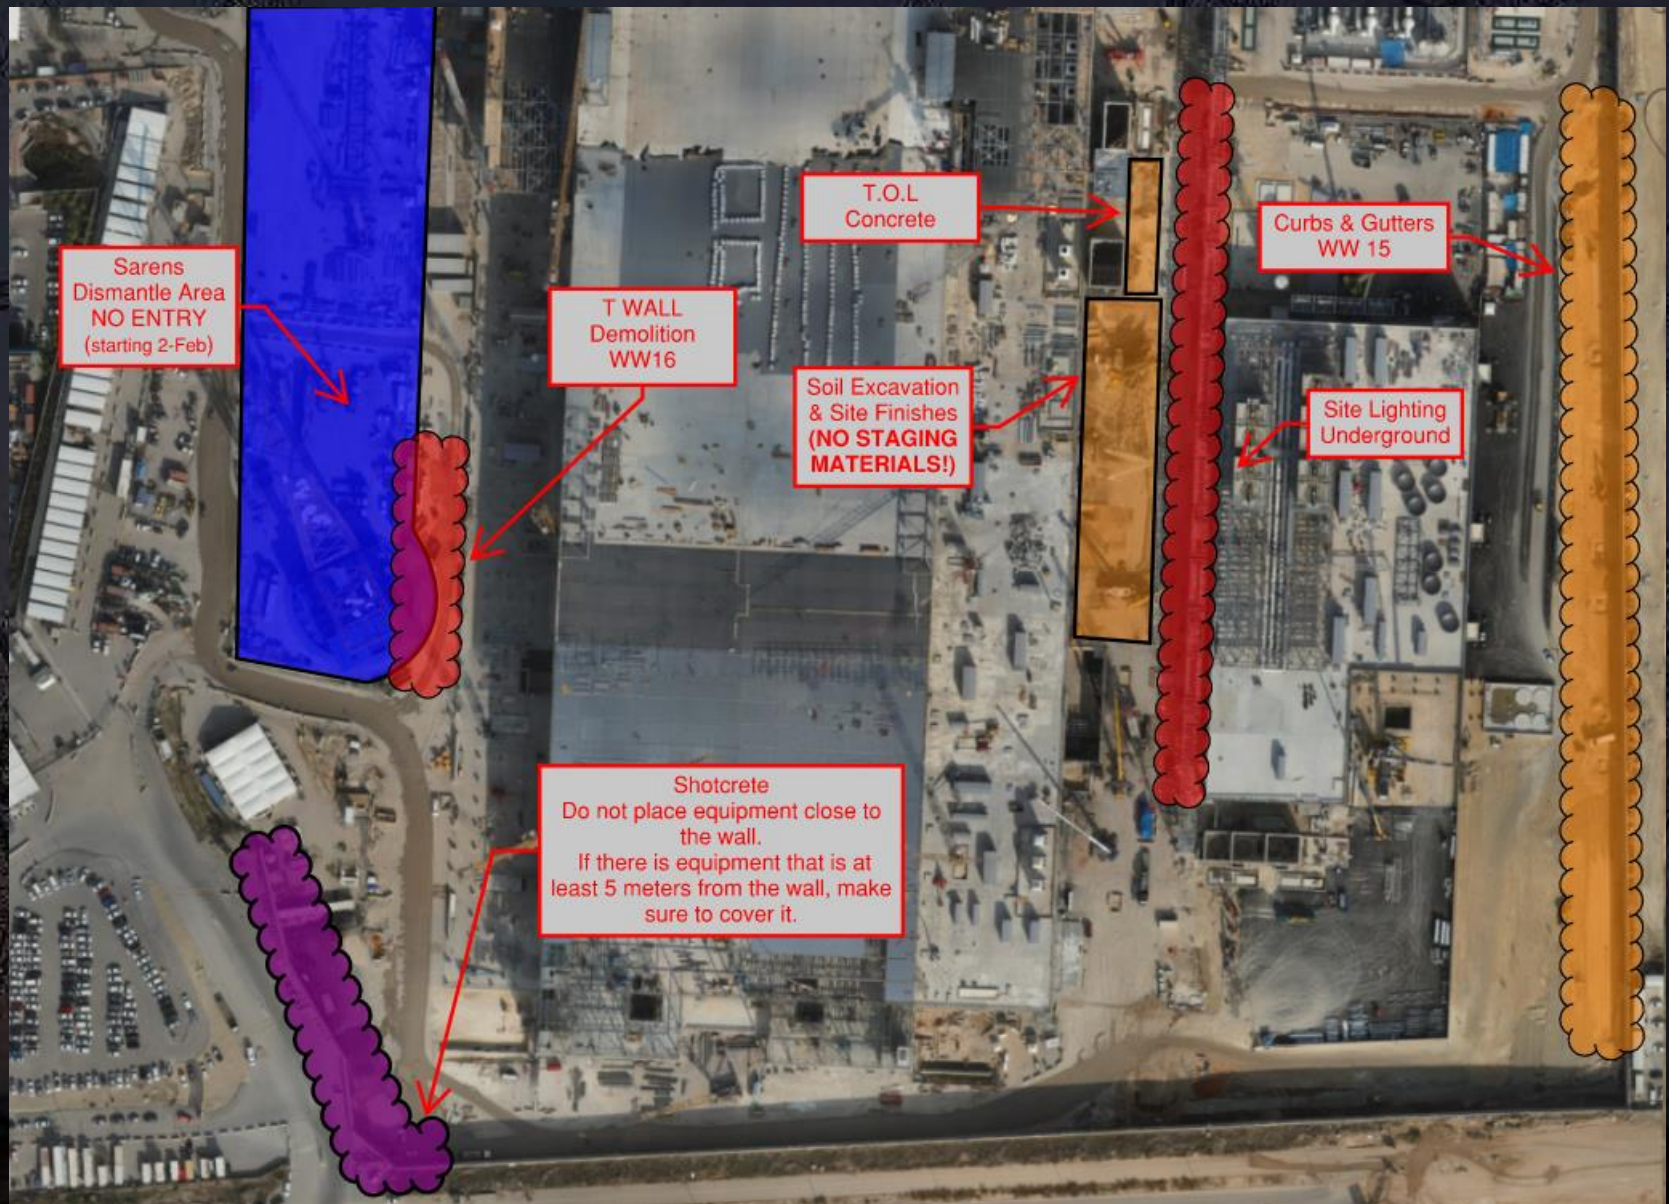

Daily Coordination Meeting

MAMAD Locations

MAMAD LOCATIONS (19-March-2025)
■ LARGE
■ SMALL
■ BUILDING

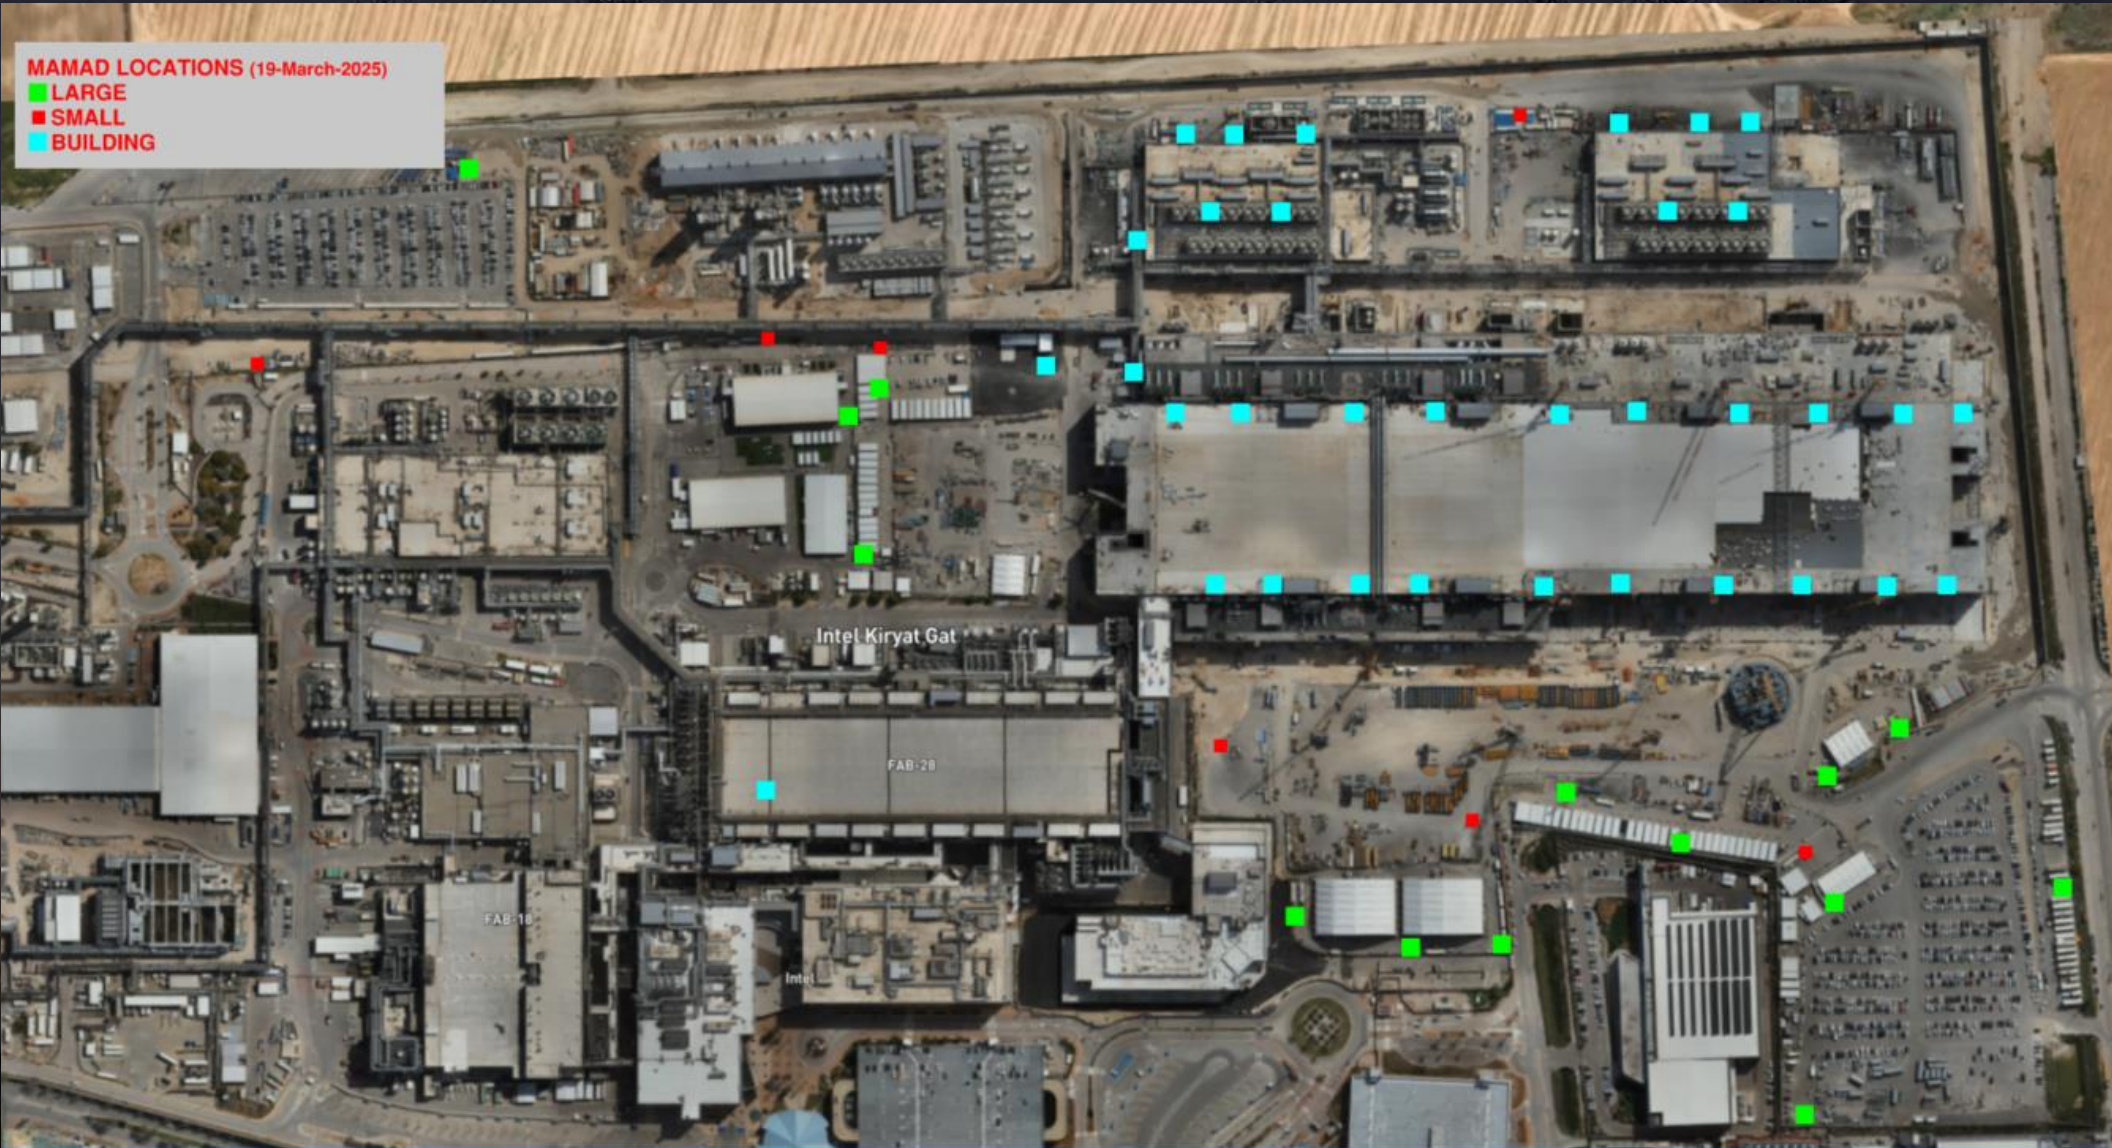

Project Sparrow Mass Safety Meeting



ATTENDANCE

Daily Coordination Meeting



14:00 Sign In
