

Daily Coordination Meeting



Daily Coordination Meeting

General Topics:


- If you don't know, ask.



KATZ


5/5

16:00 to 23:59

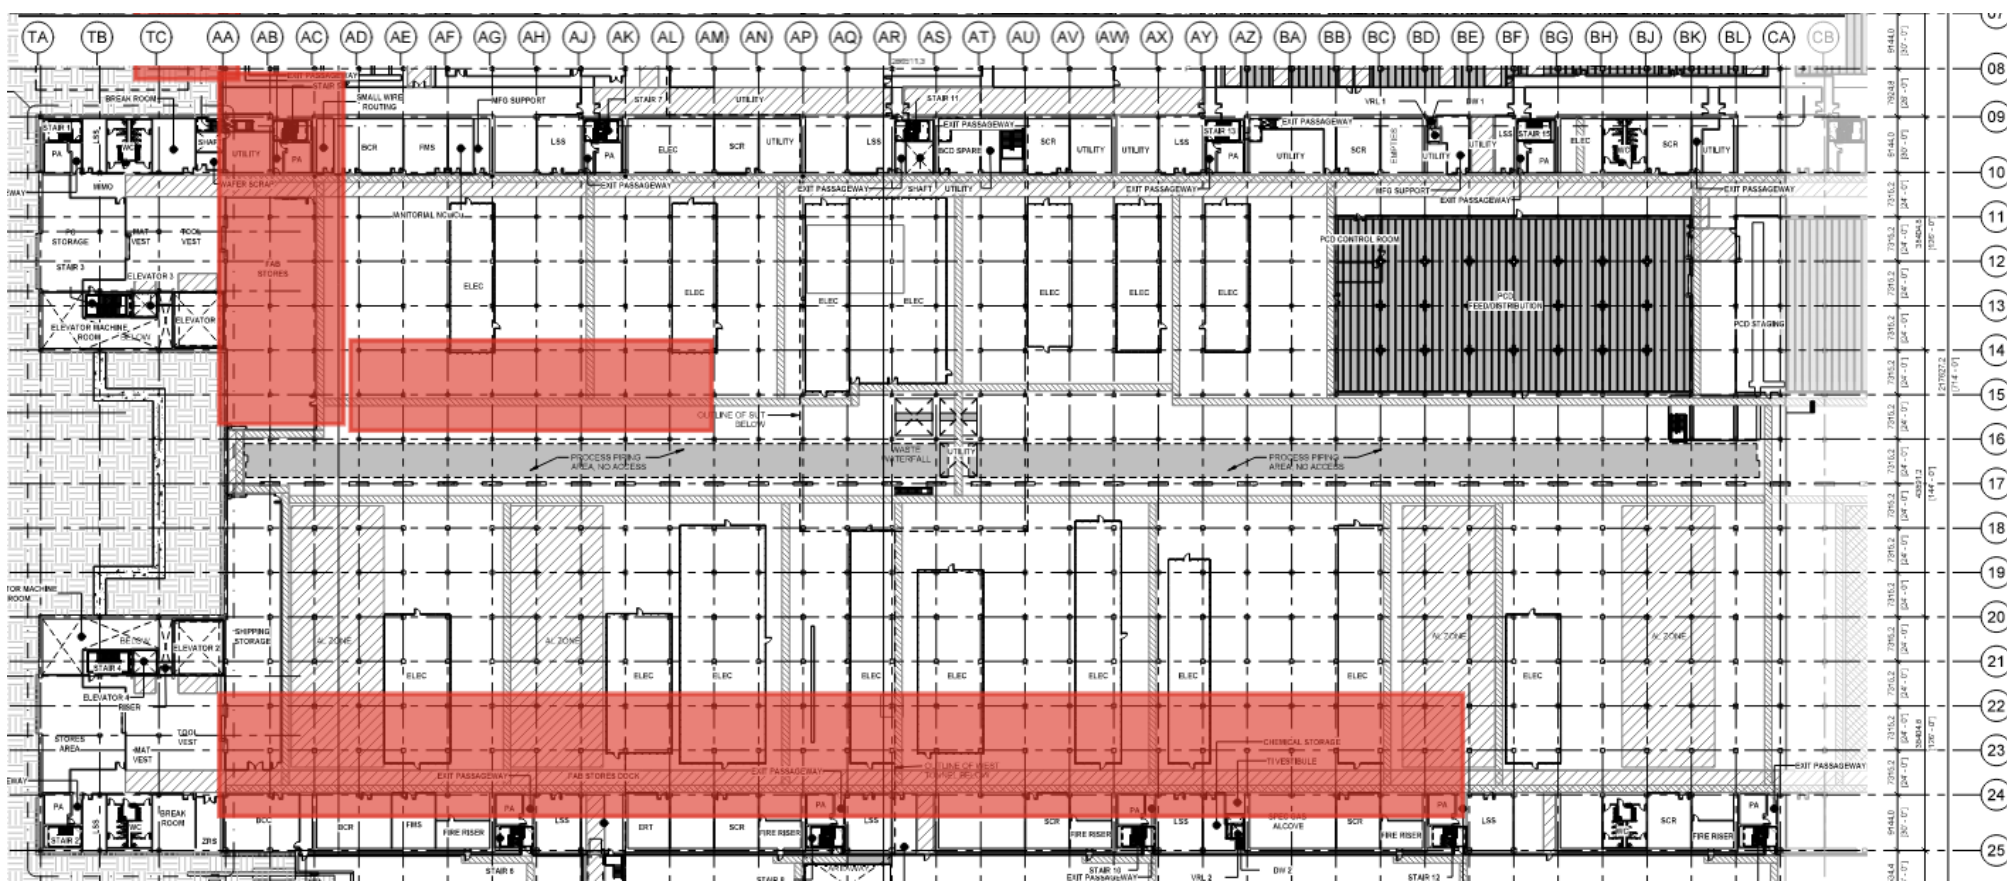




UTILITY LEVEL MOD1

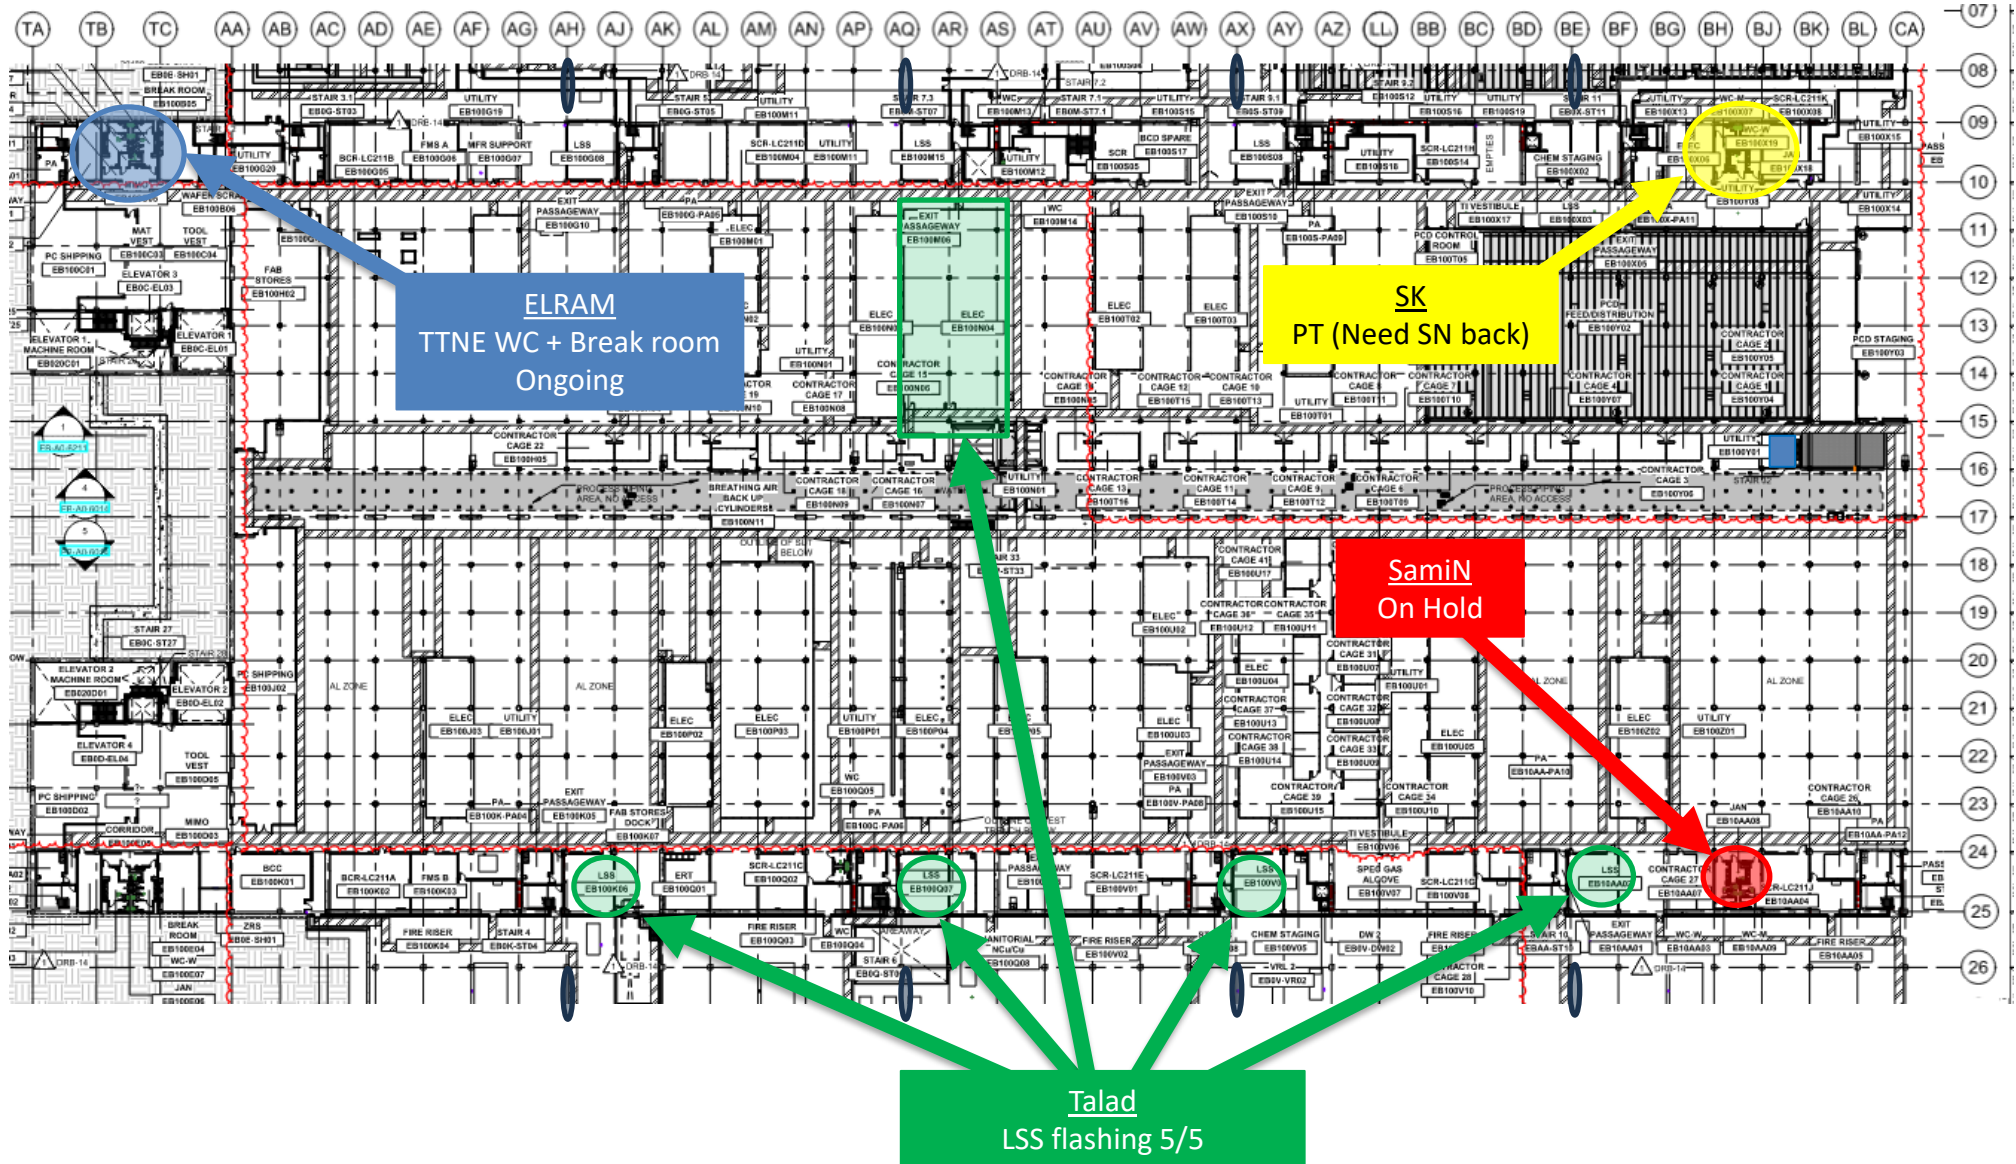


UTILITY LEVEL MOD2

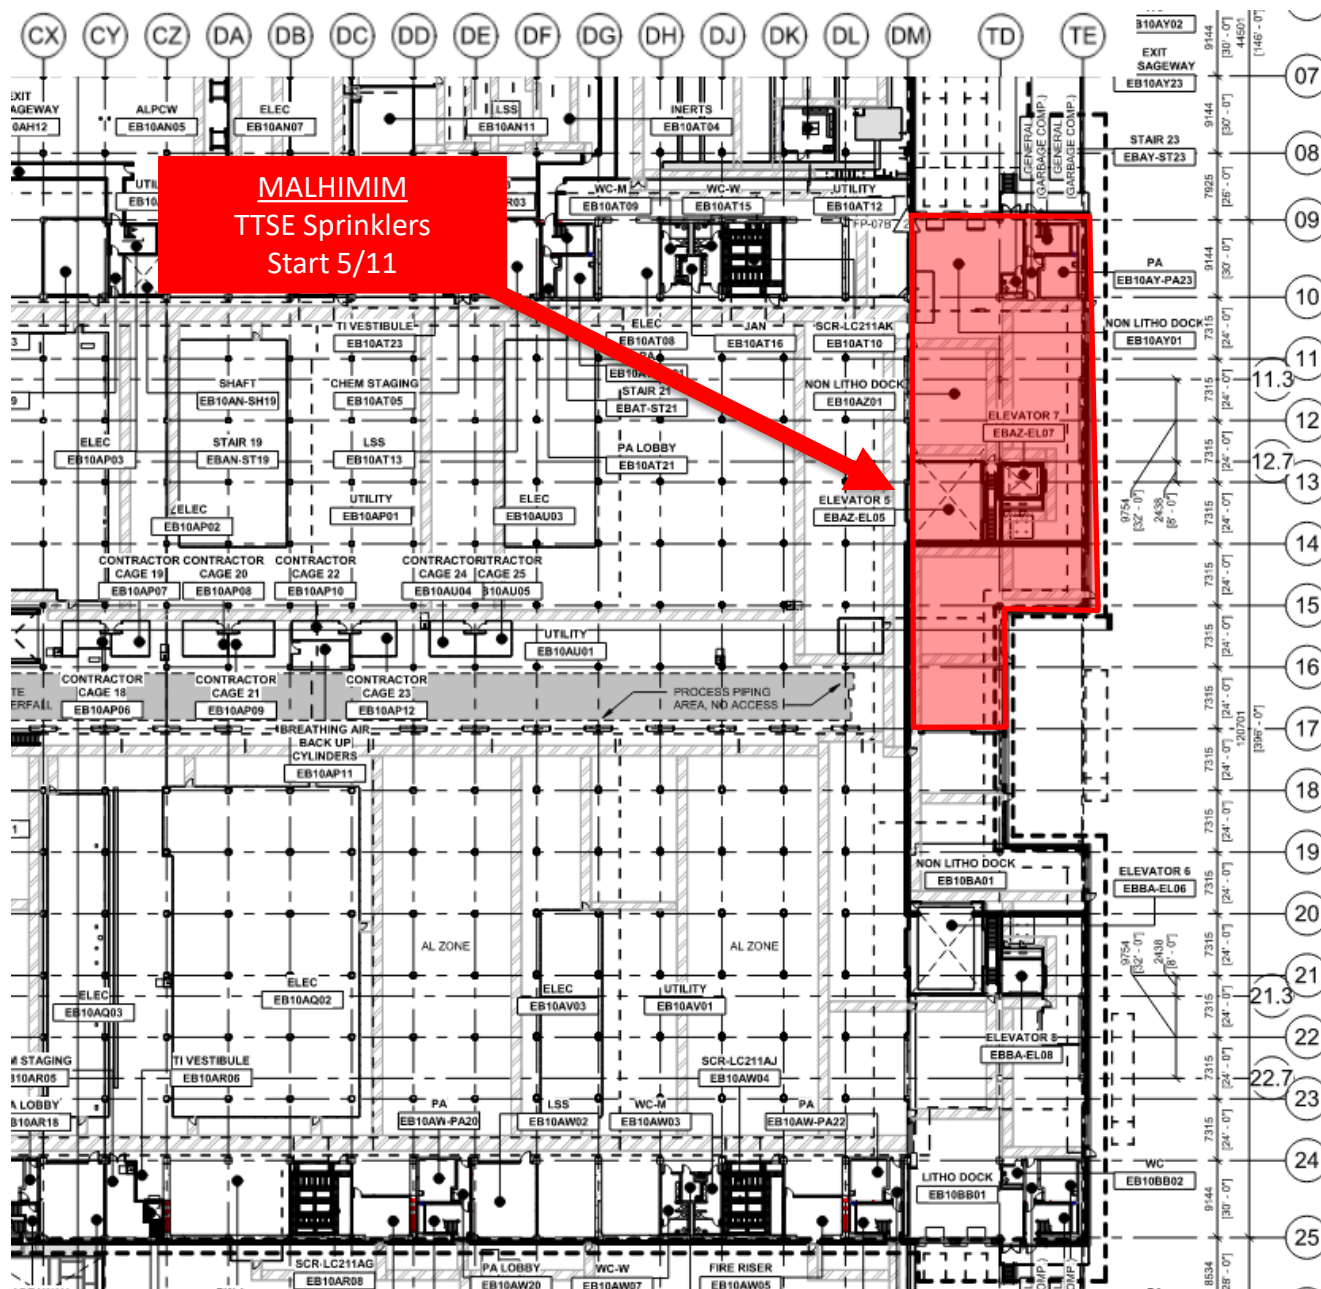




SUT 38.1 LEVEL

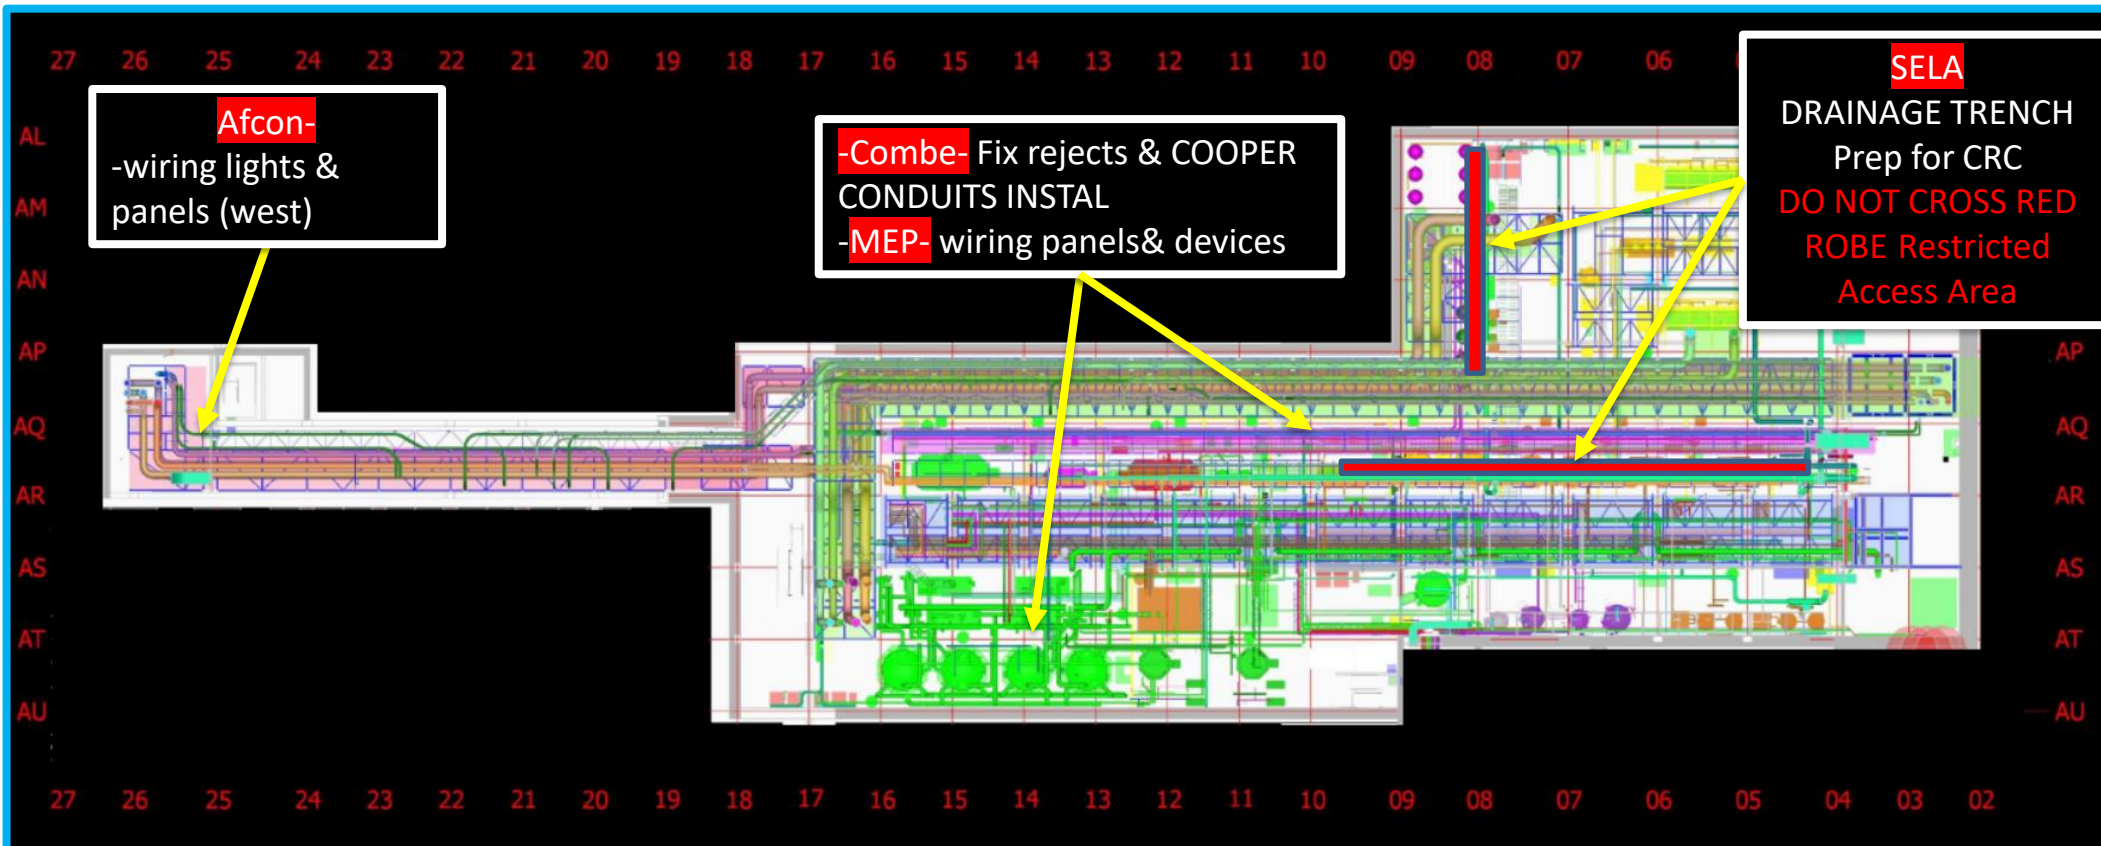

-HOUSE KEEPING

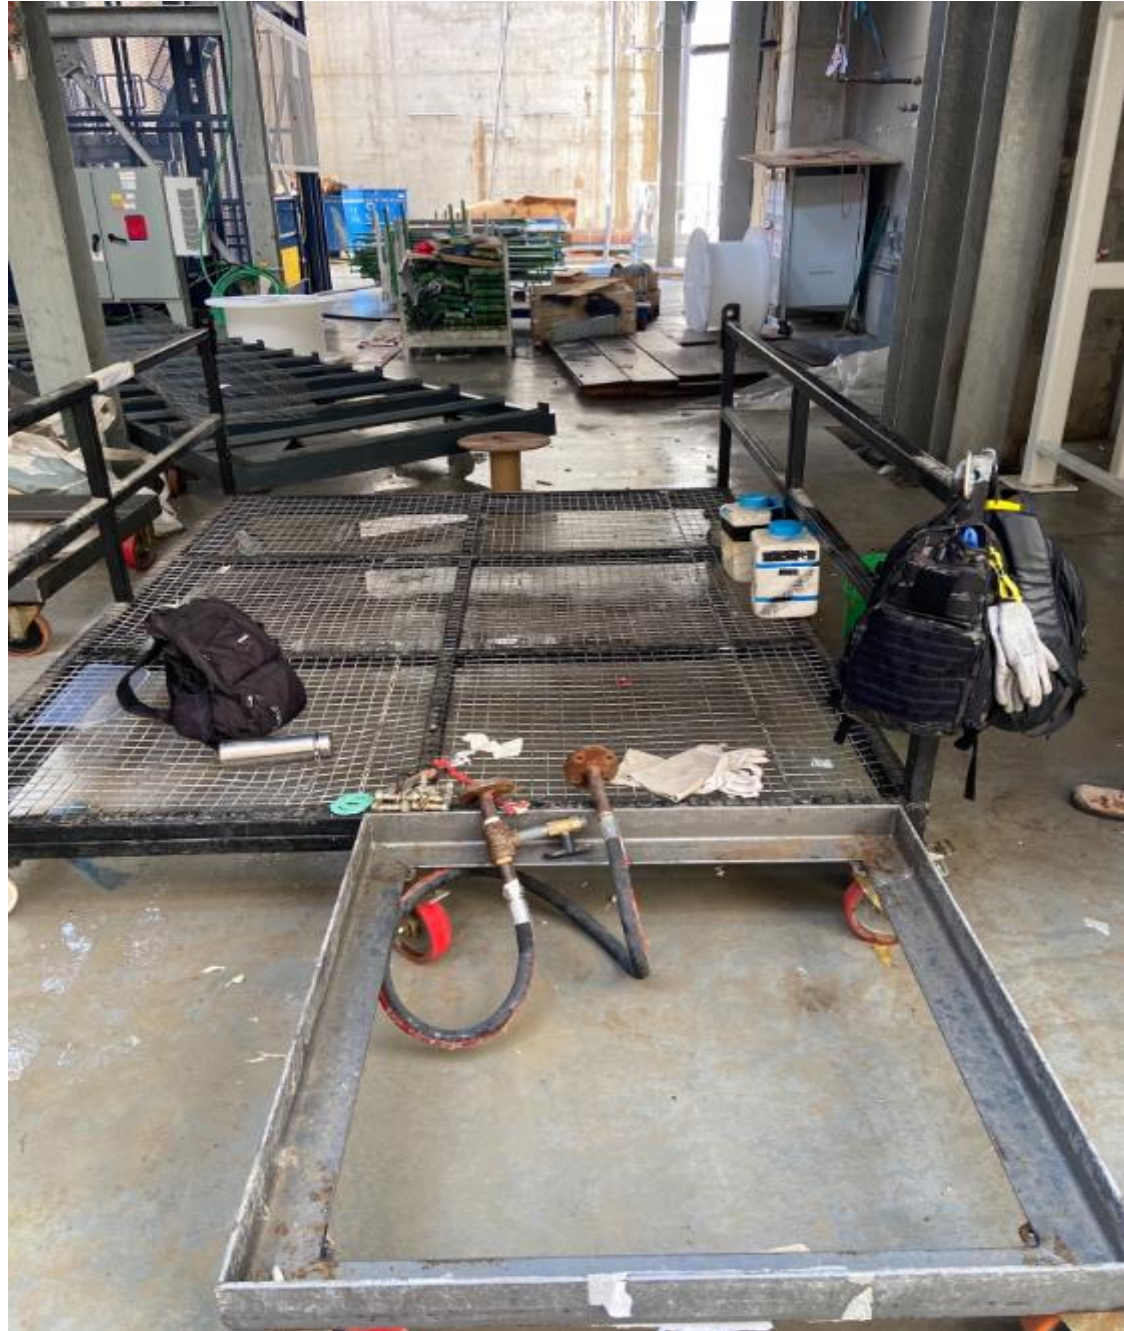






UNRECOGNIZED MATERIALS & TOOLS
PLEASE LOOK AT THESE MATERIALS& TOOLS OR GO LOOK AT
MATERIALS& TOOLS SHOUD CLEAR OUT TILL 06.05.25
AT 07.06.25 JOB SERVICE WILL THRU IT TO DUMPSTER







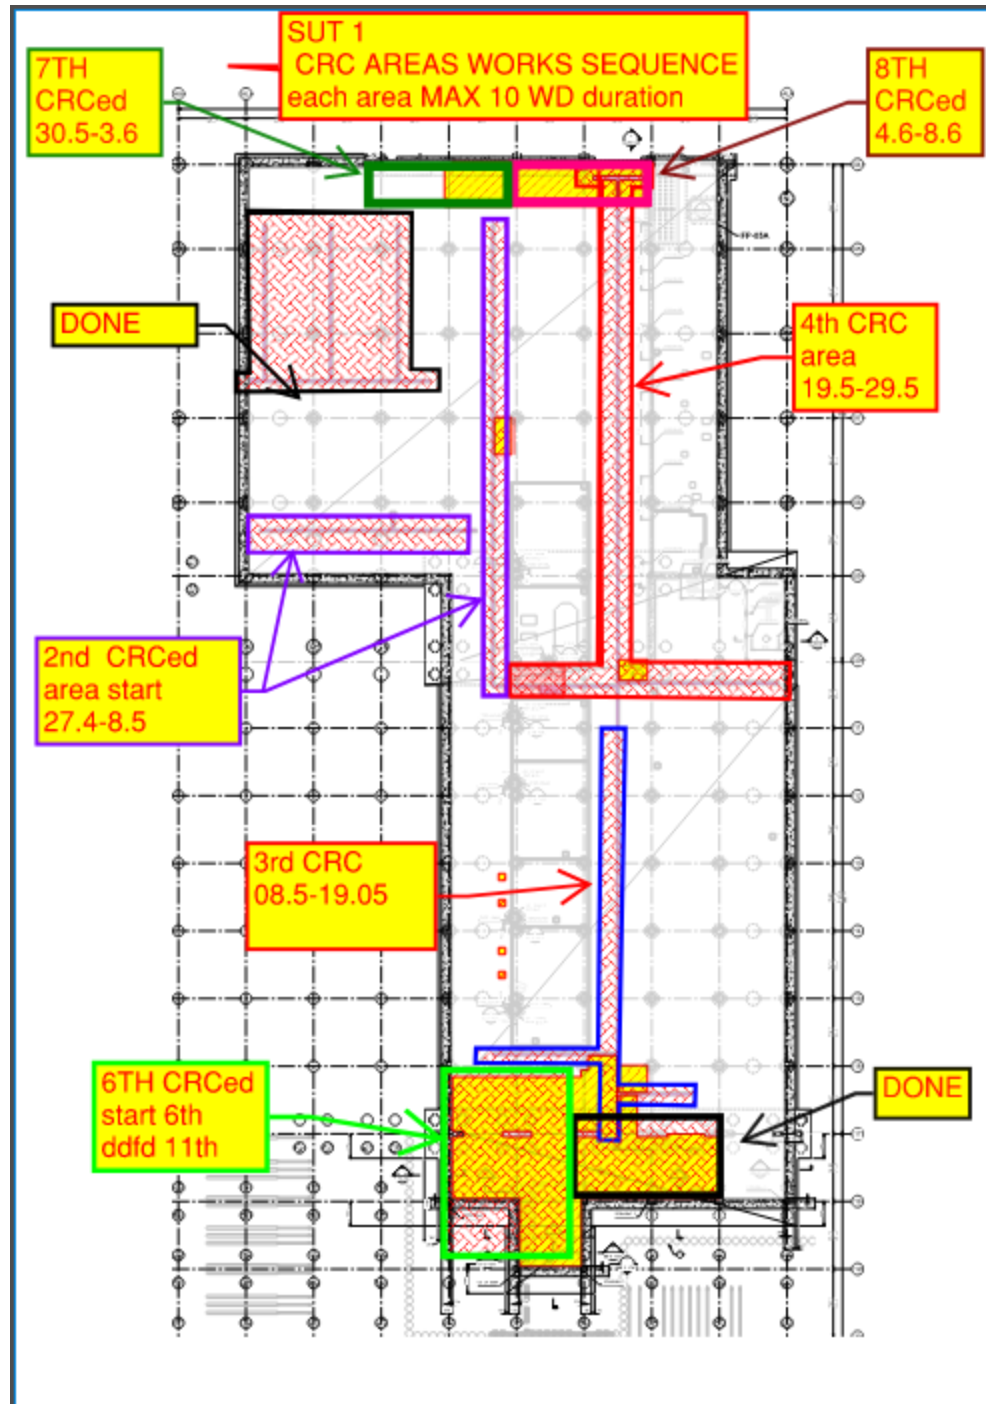

SUT 1 CRC sequence & duration

Area No	start date	completion date
1		done
2	27.4	7.5
3	8.5	19.5
4	19.5	29.5
5	23.4	27.4
6	28.4	1.5
7	1.6	3.6
8	4.6	8.6


complete all crc works at sut 1
date is 08.06.2025




HYG

**IMMEDIATELY GRID INSTALL for
each area after CRC completion**


SUT 38.2 LEVEL

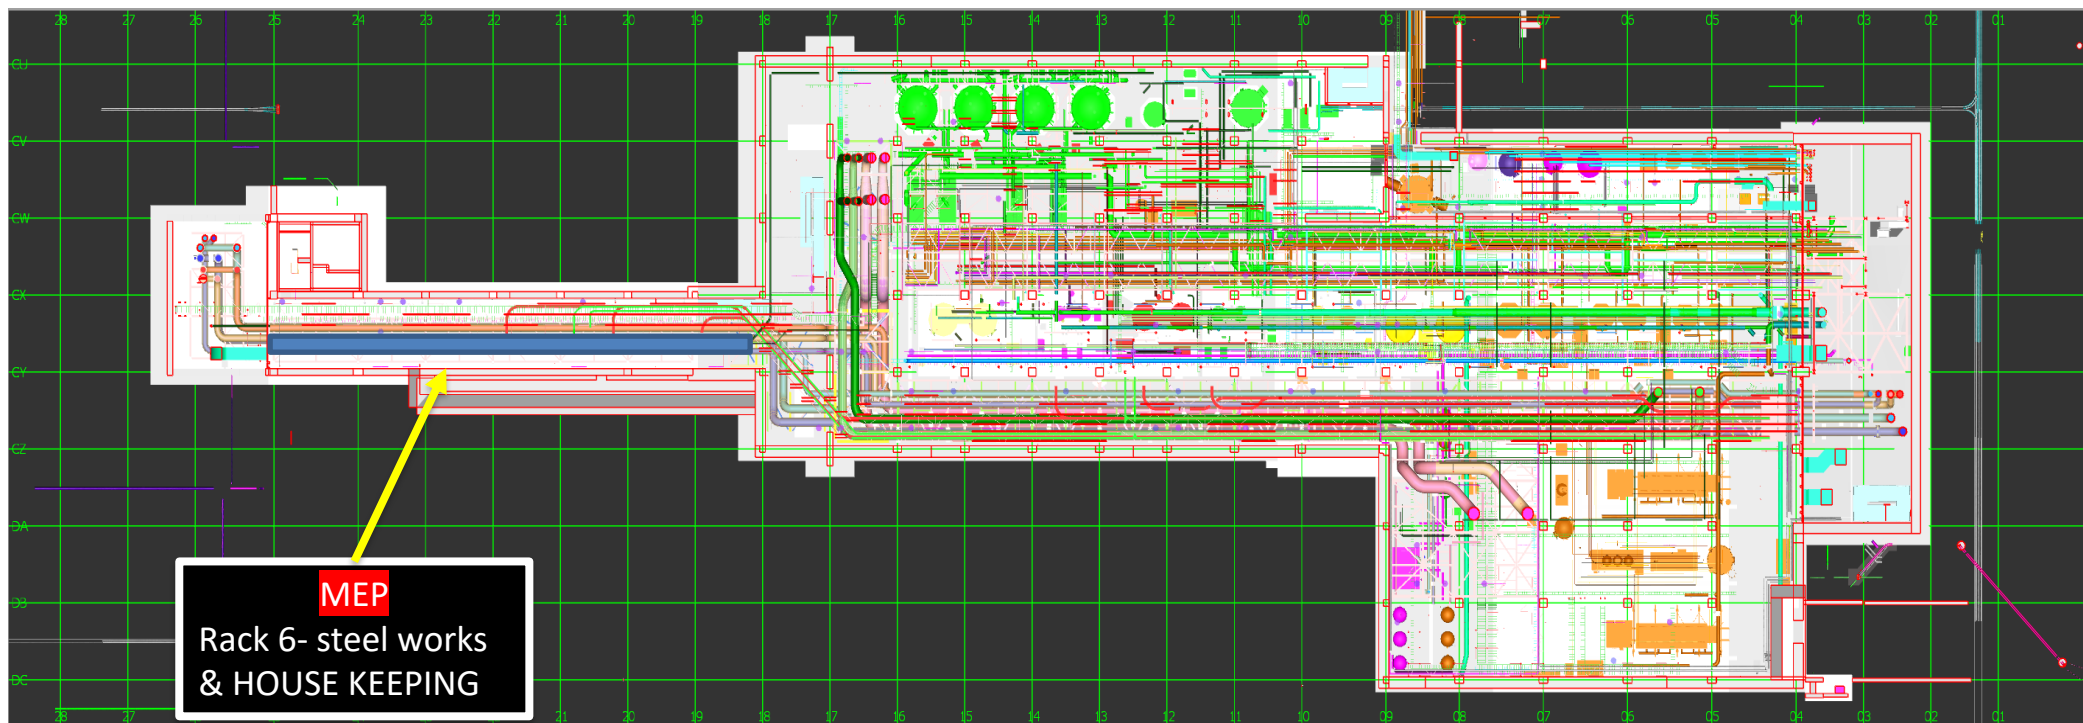

SUBFAB BUILDOUT MOD 1

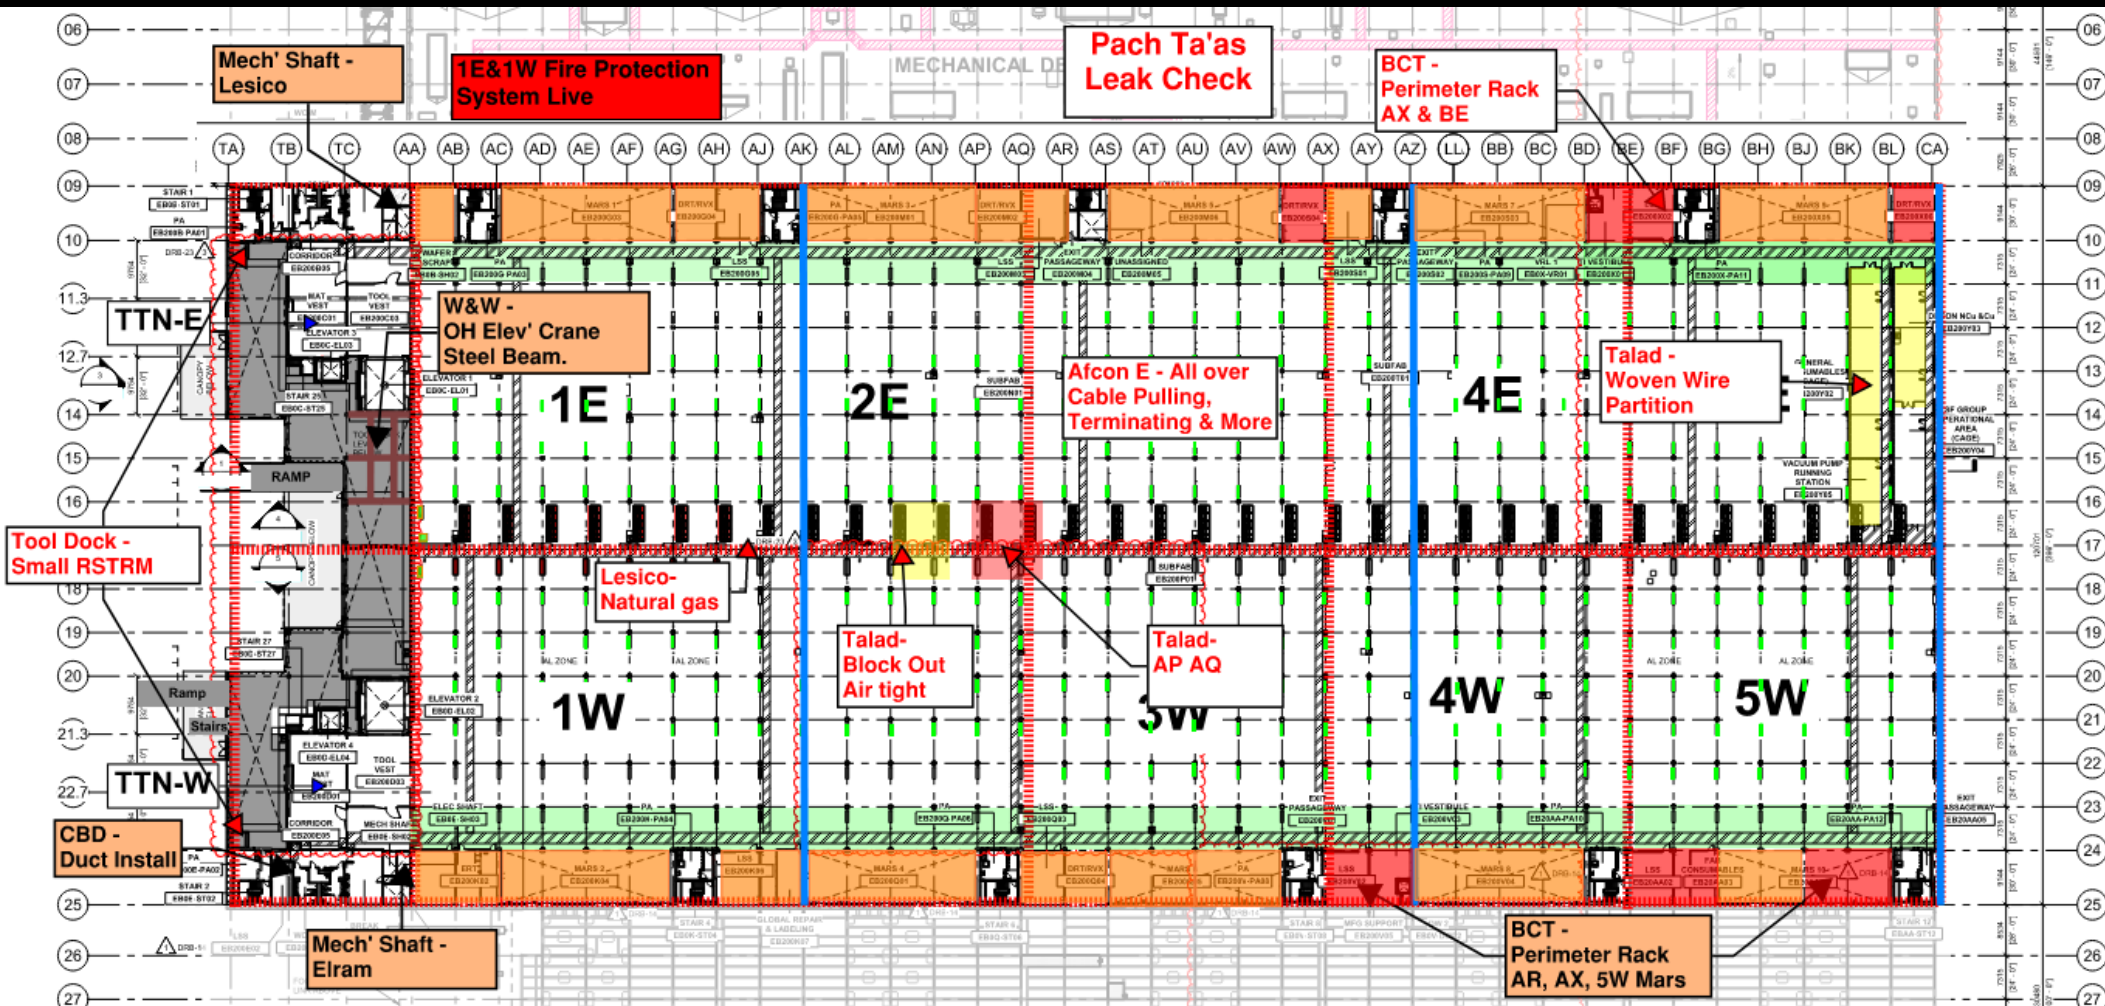

BCT Pressure Test Tomorrow

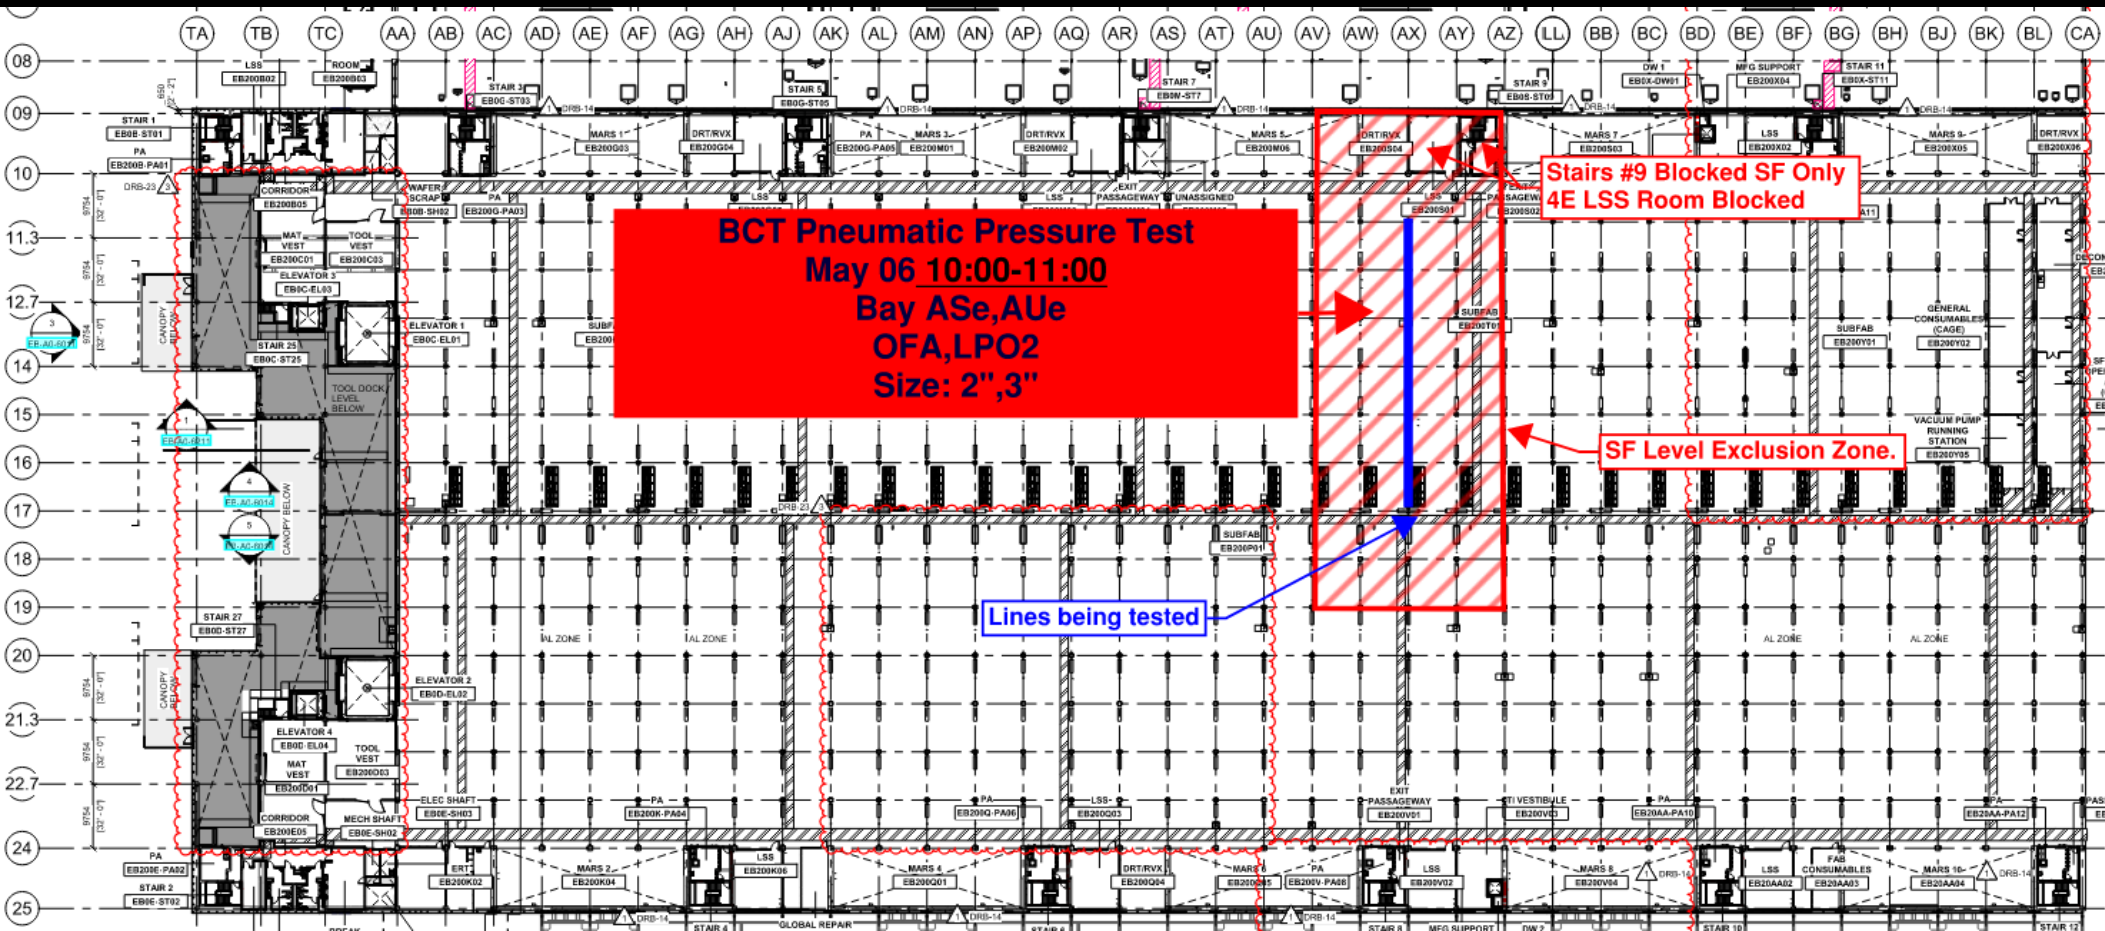


Stairs #5 Blocked SF Only
2E LSS Room Blocked


SF Level Exclusion Zone.



2W LSS Room Blocked



Stairs #6 Blocked SF Only


MLB Pressure Test
May 07 17:00-19:00
Fire Protection
2E,2W

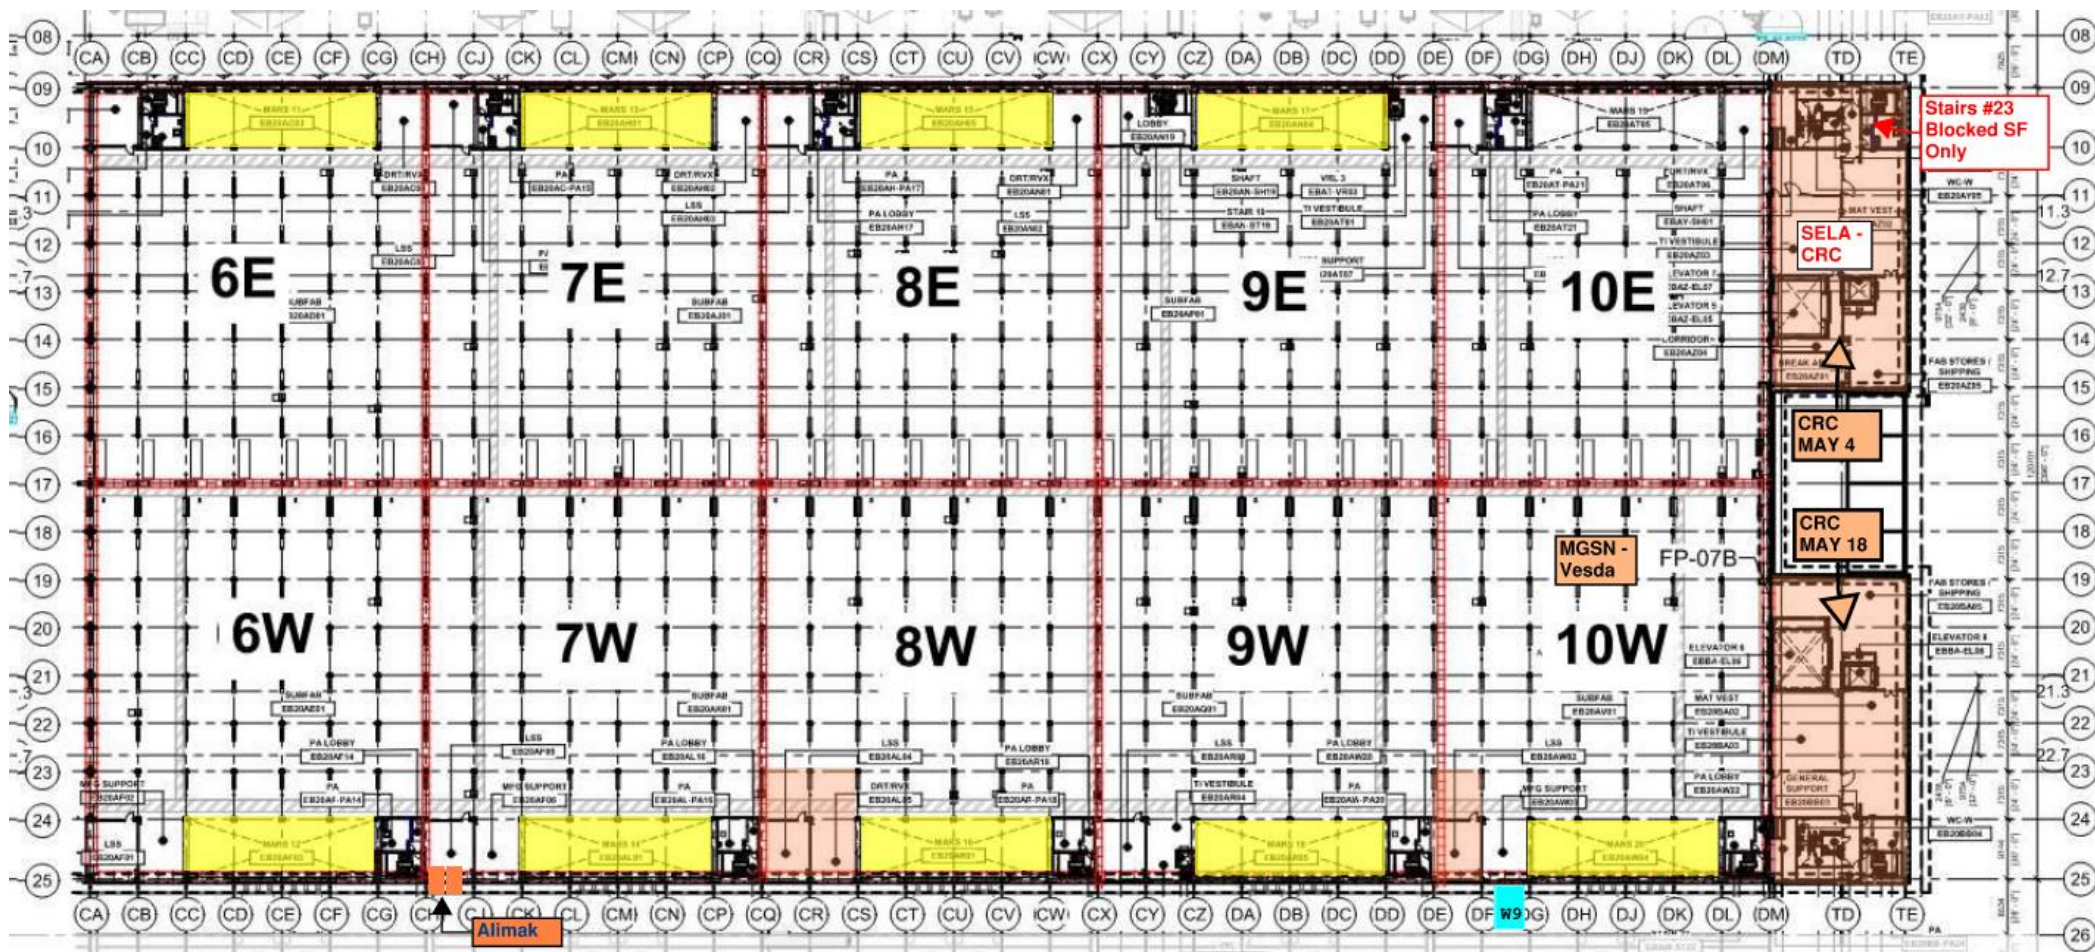

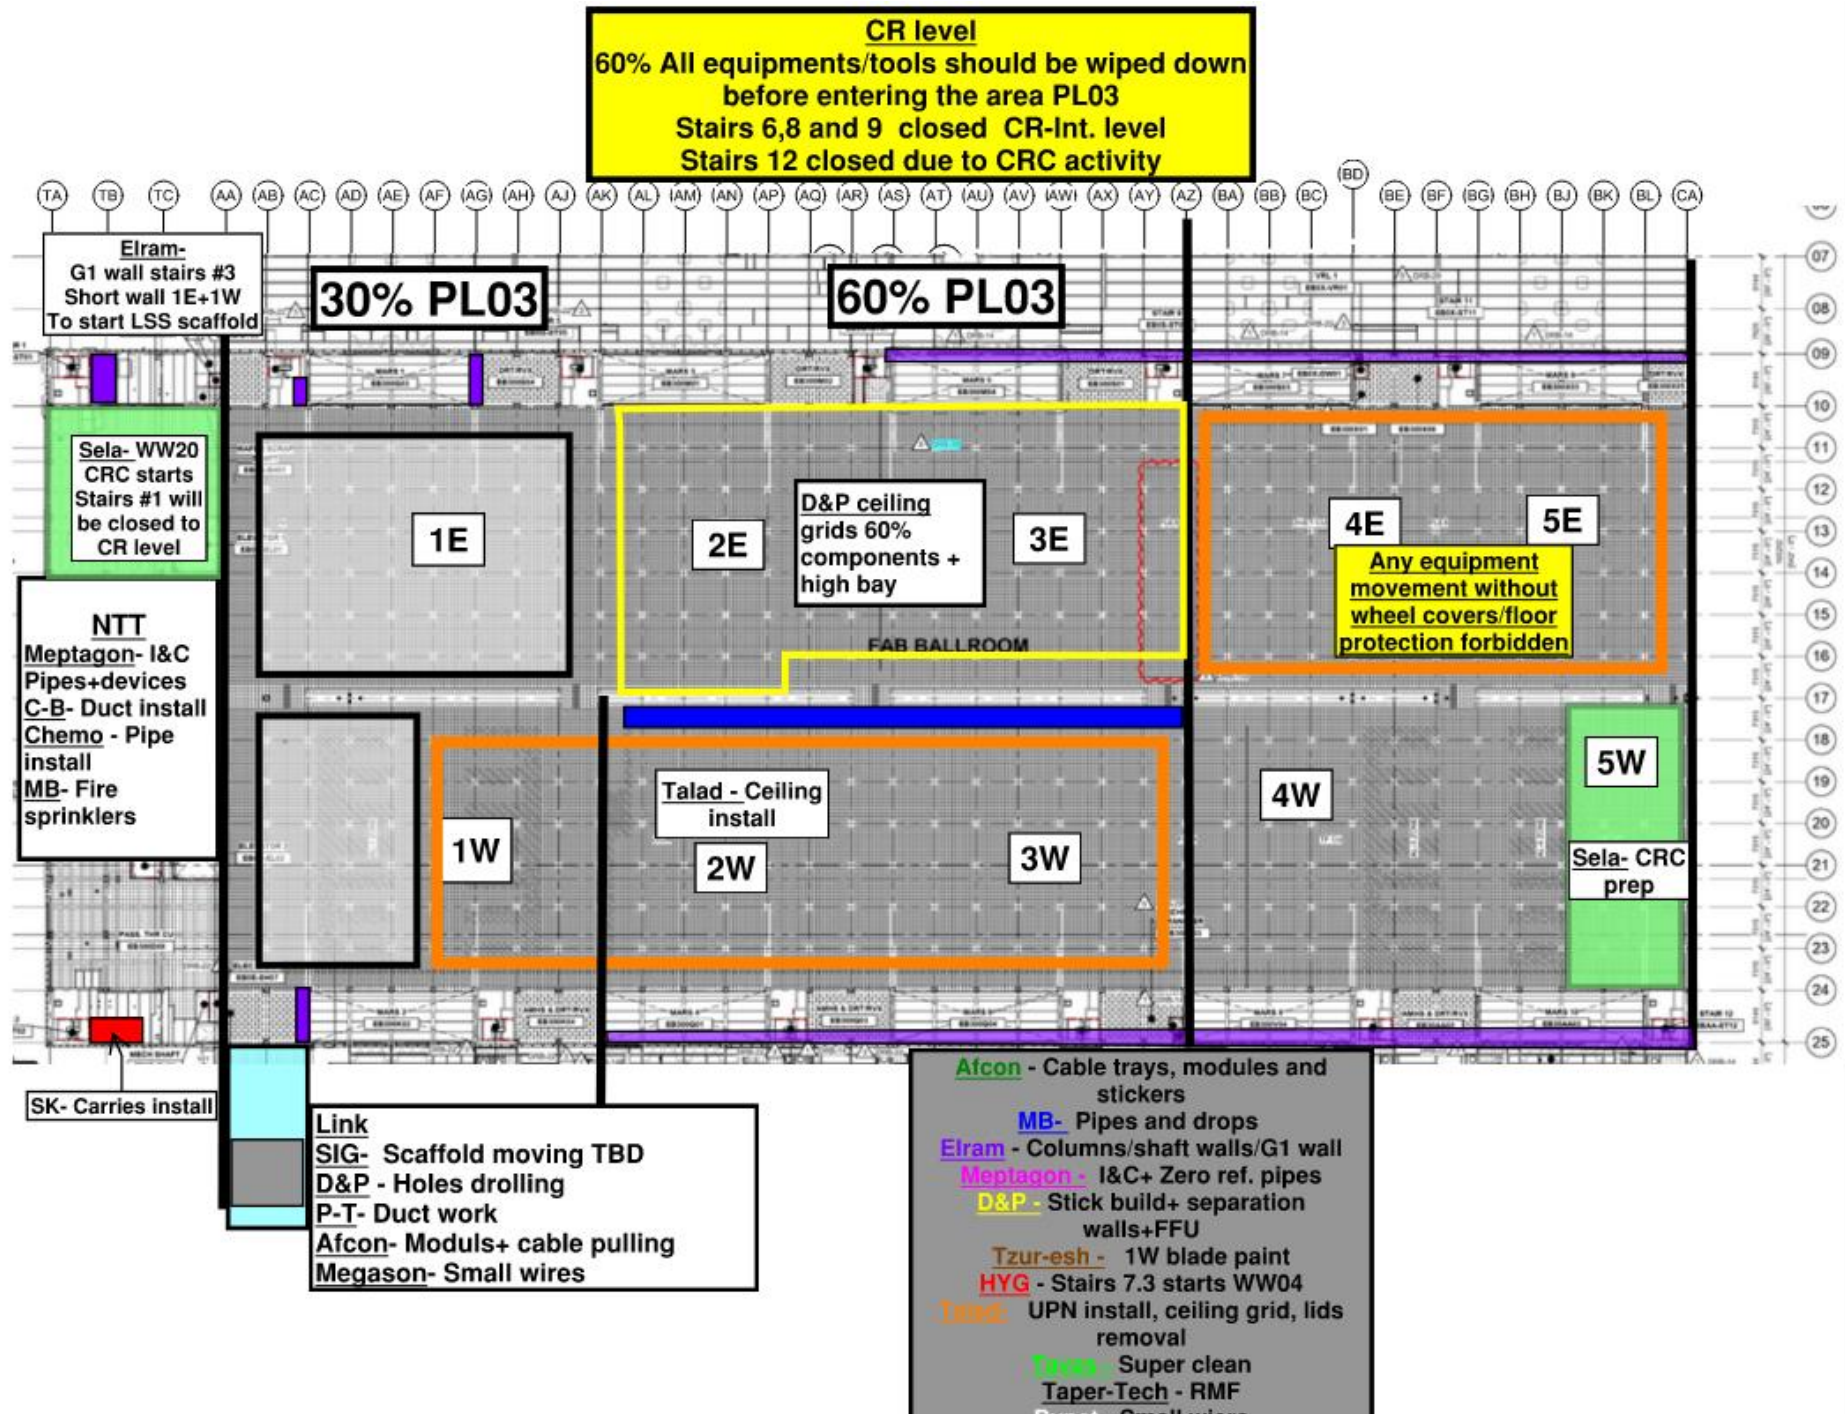


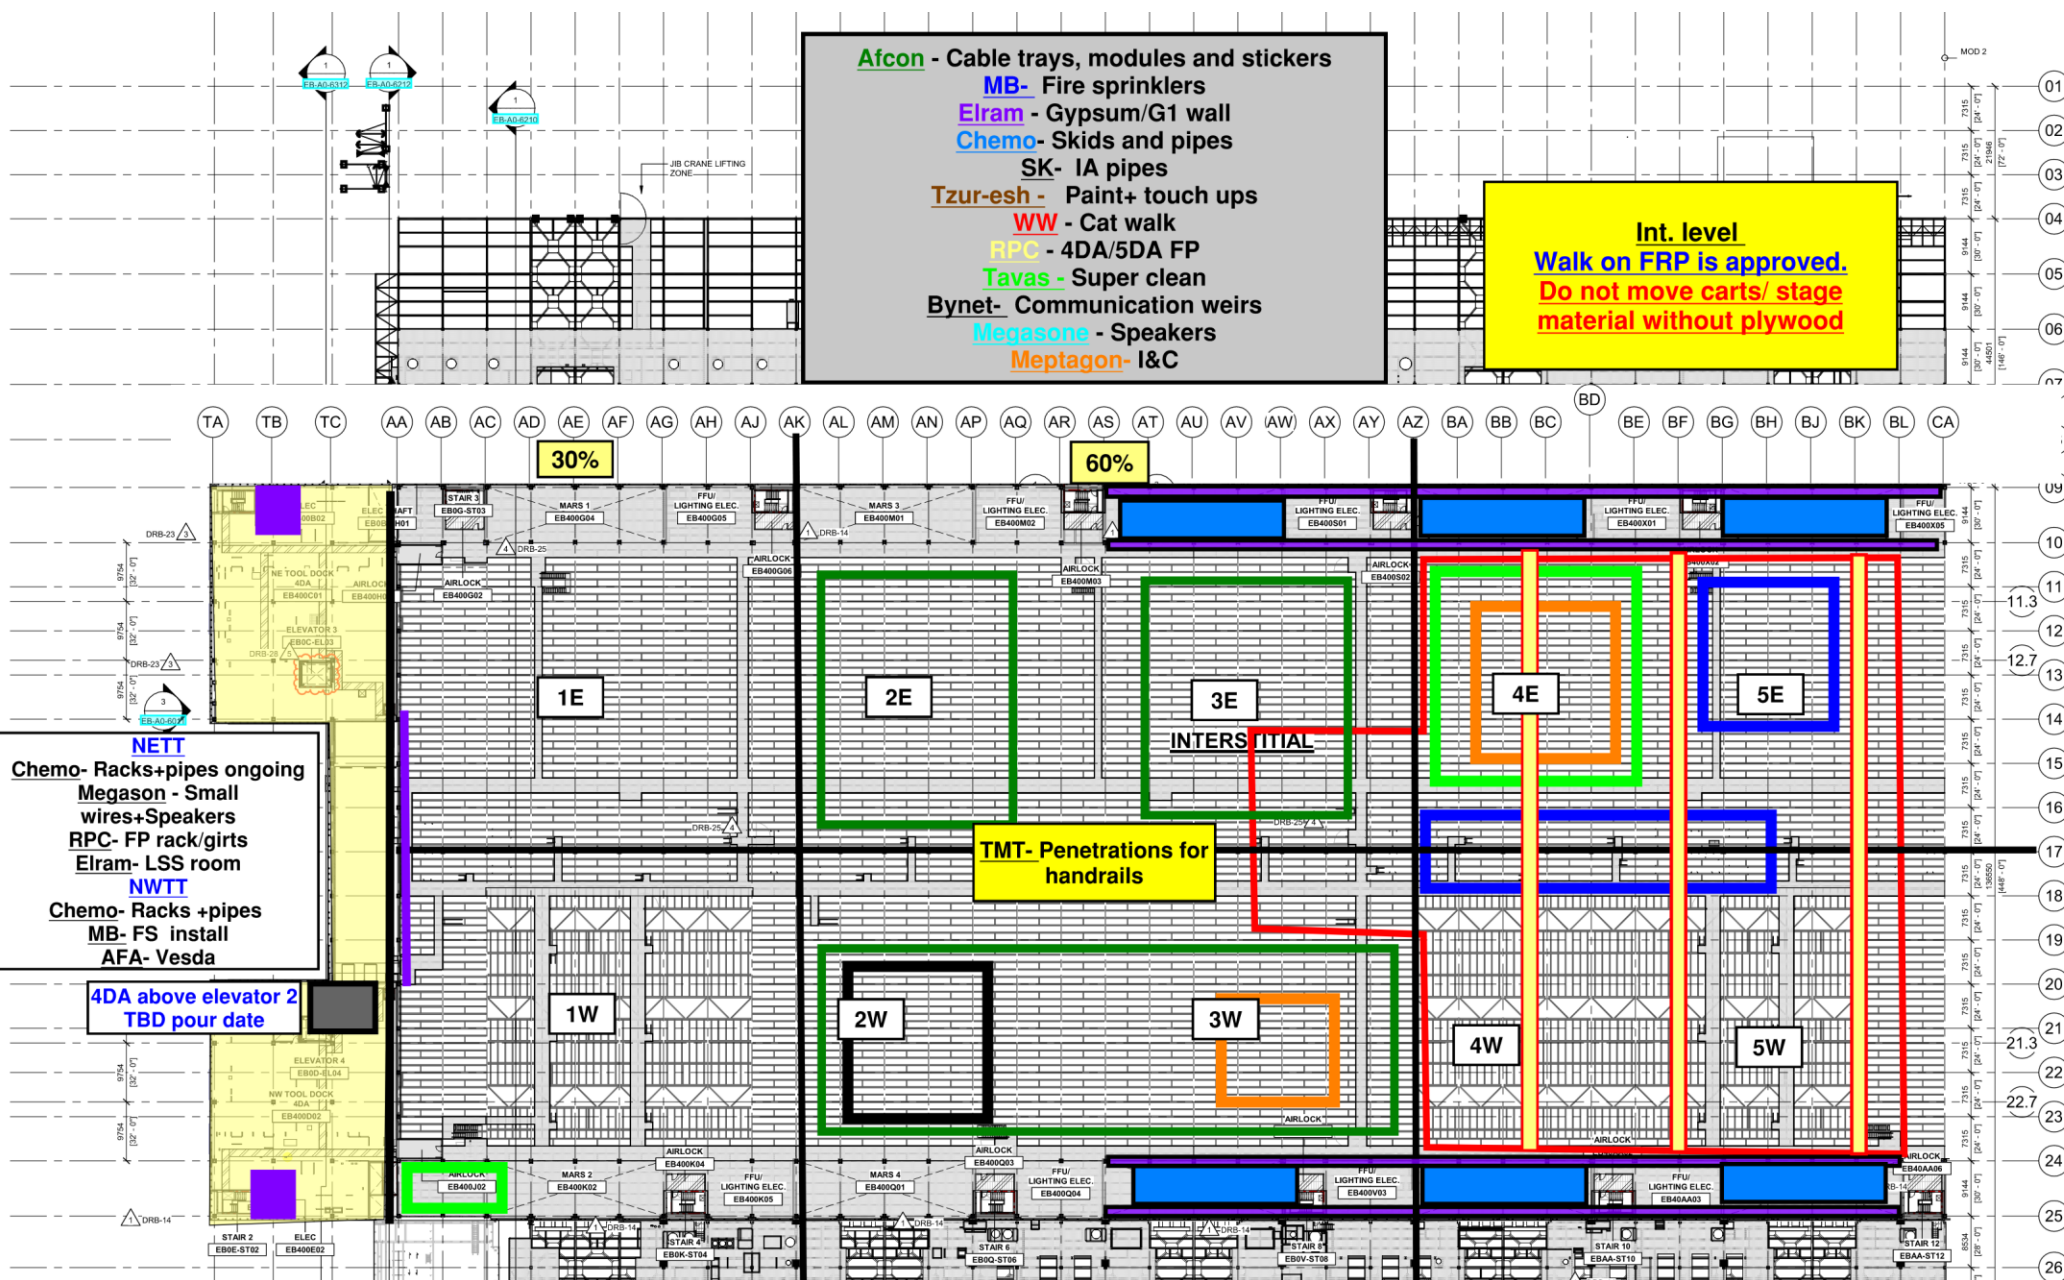

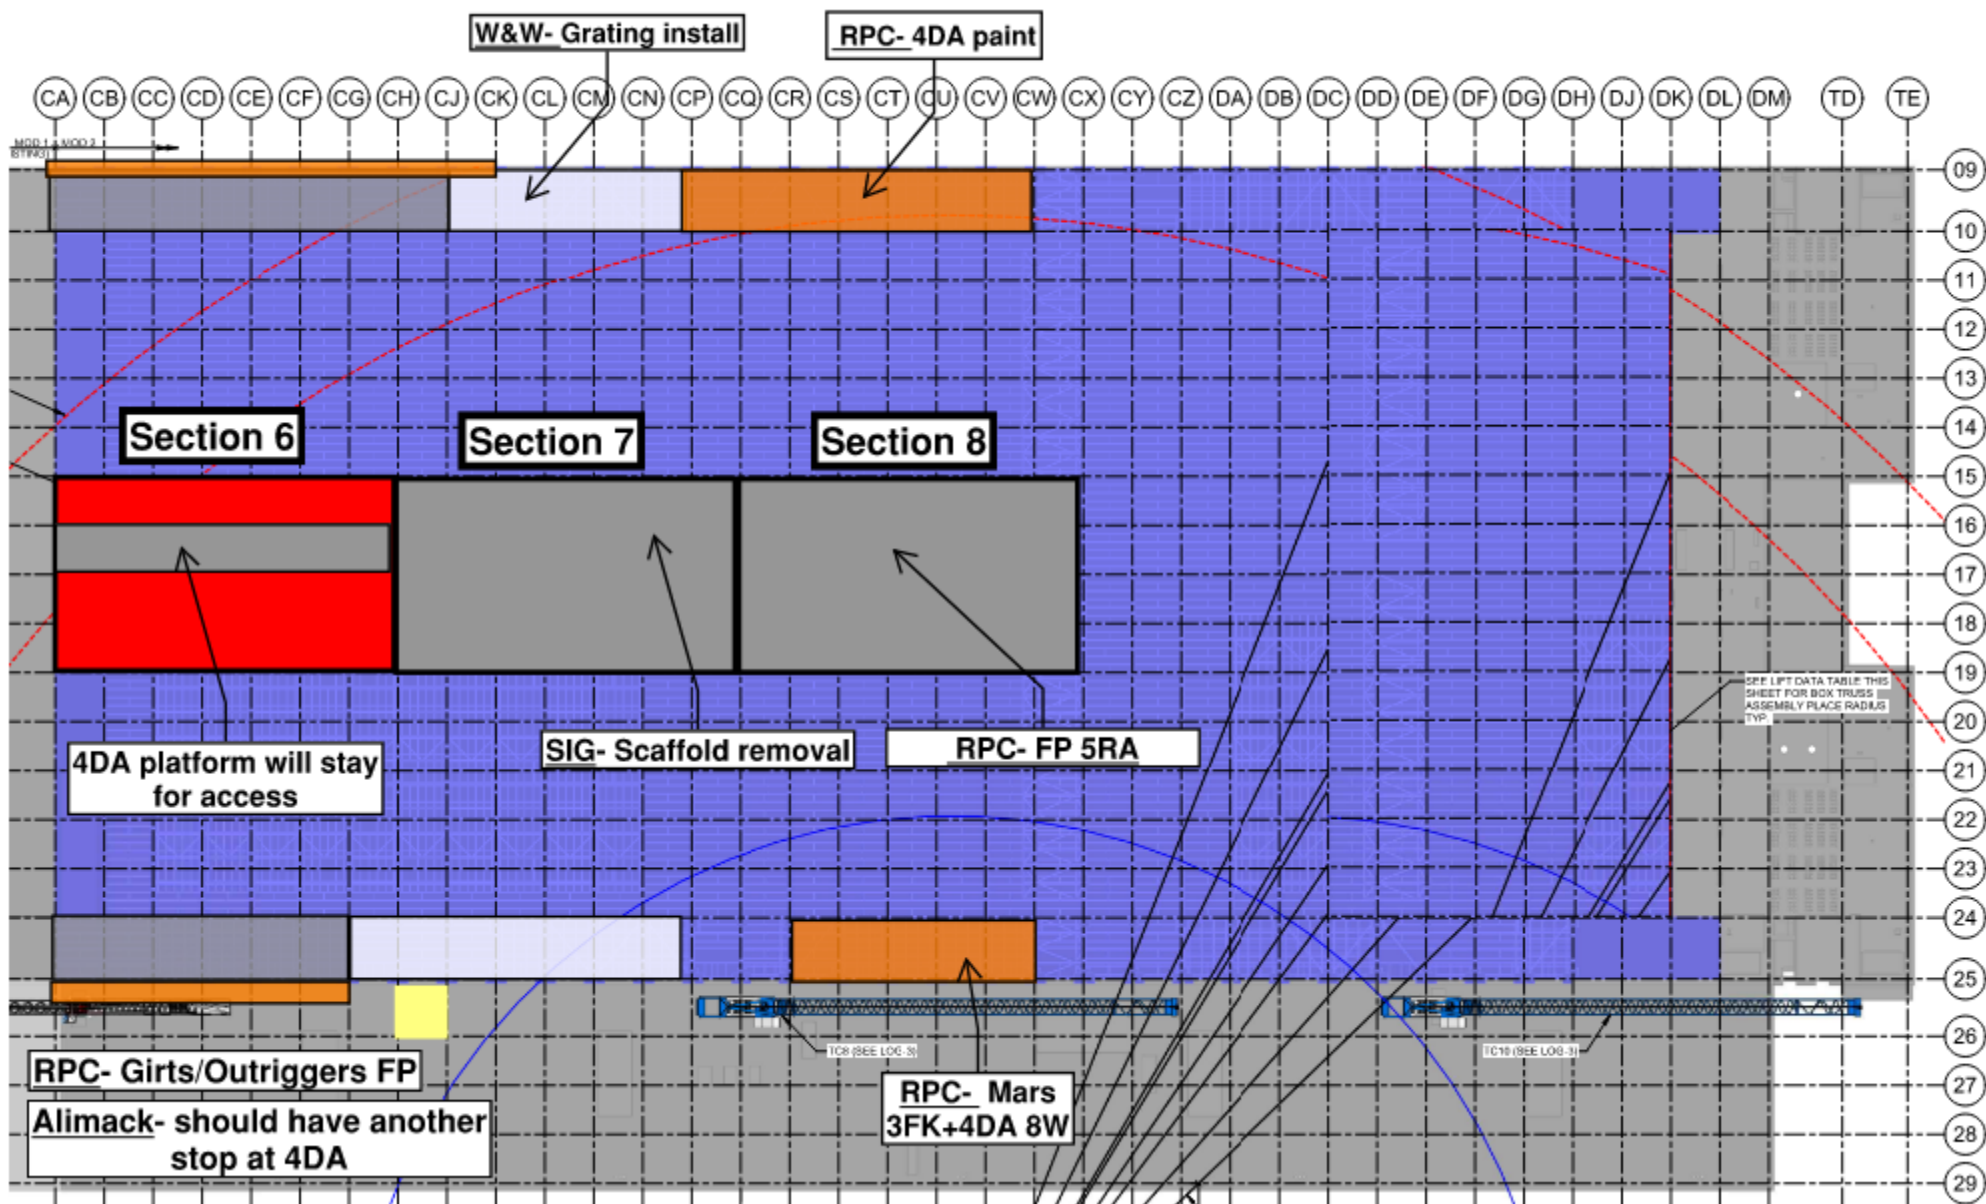


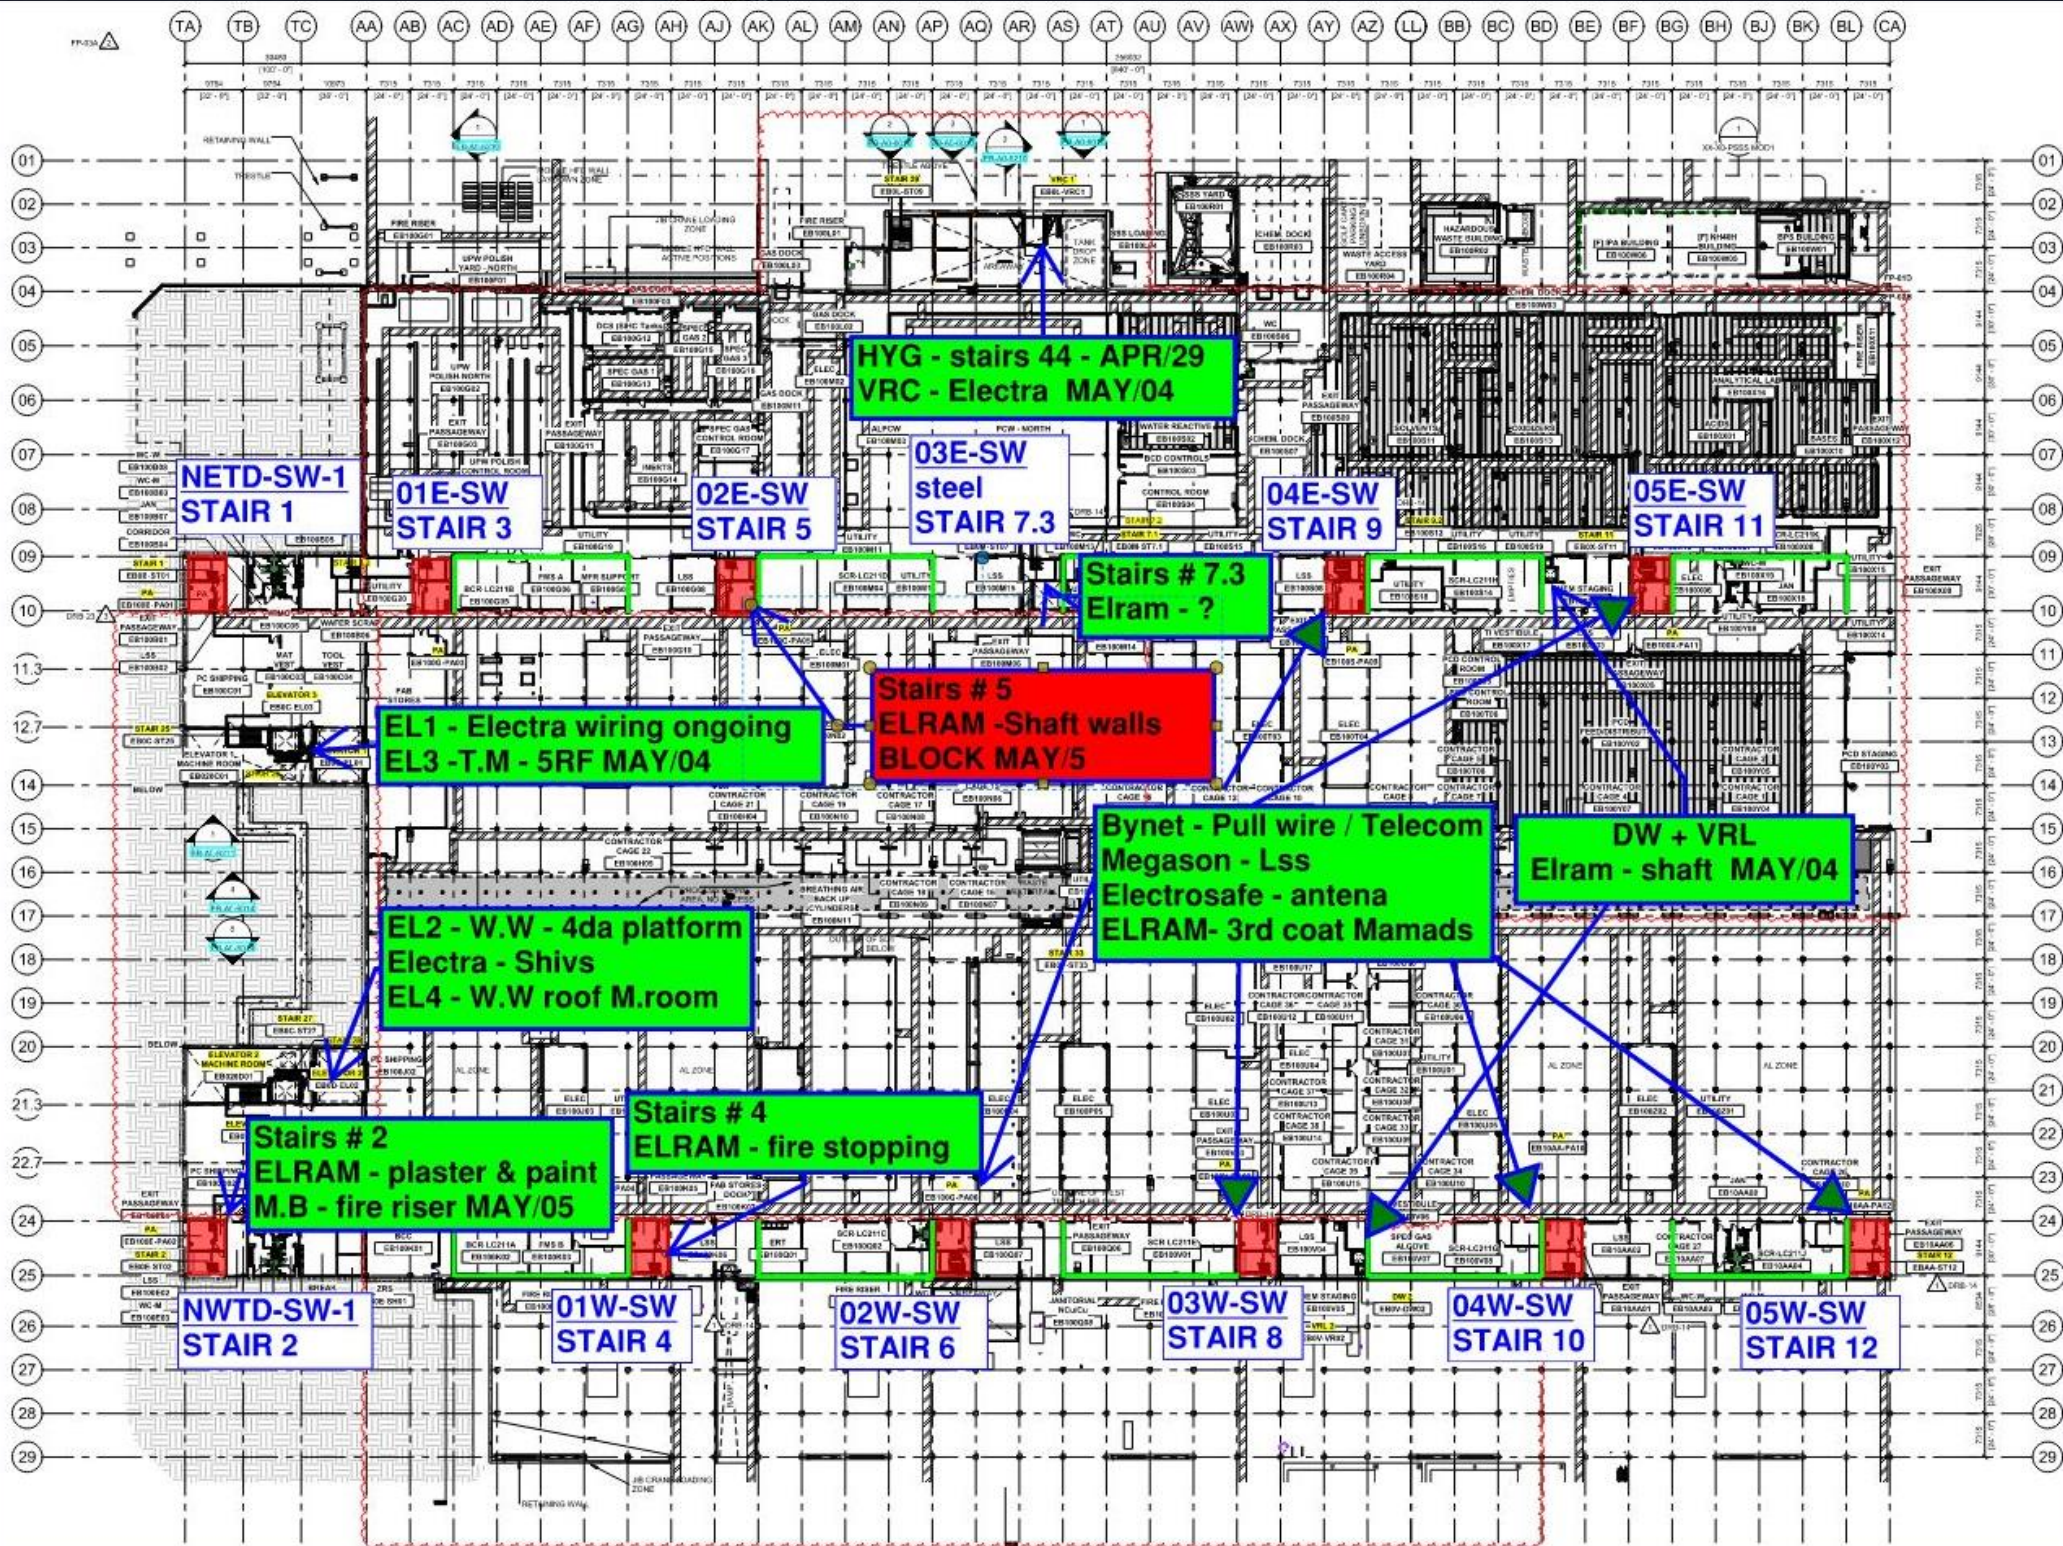


Request Form

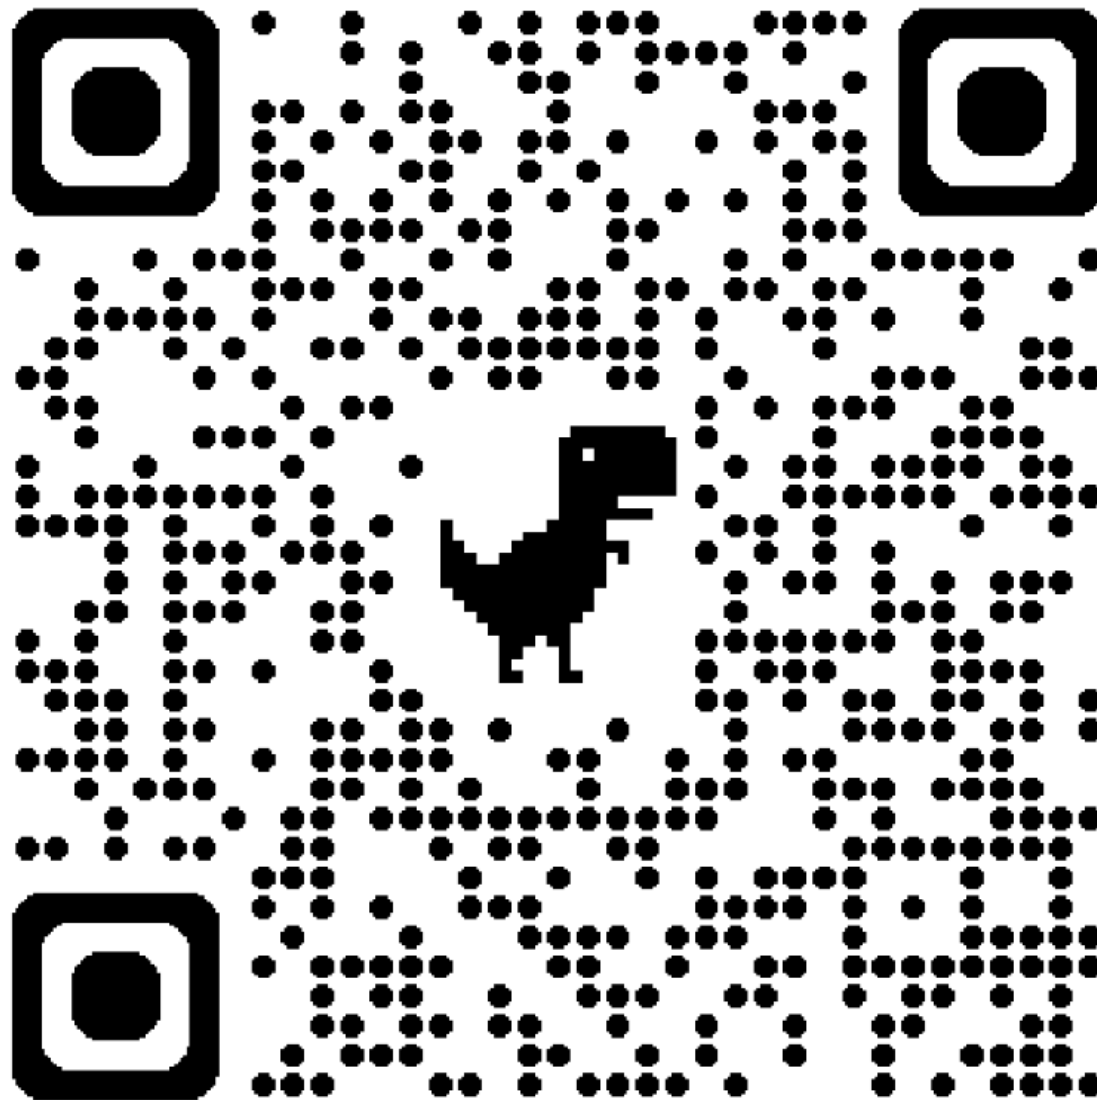

Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

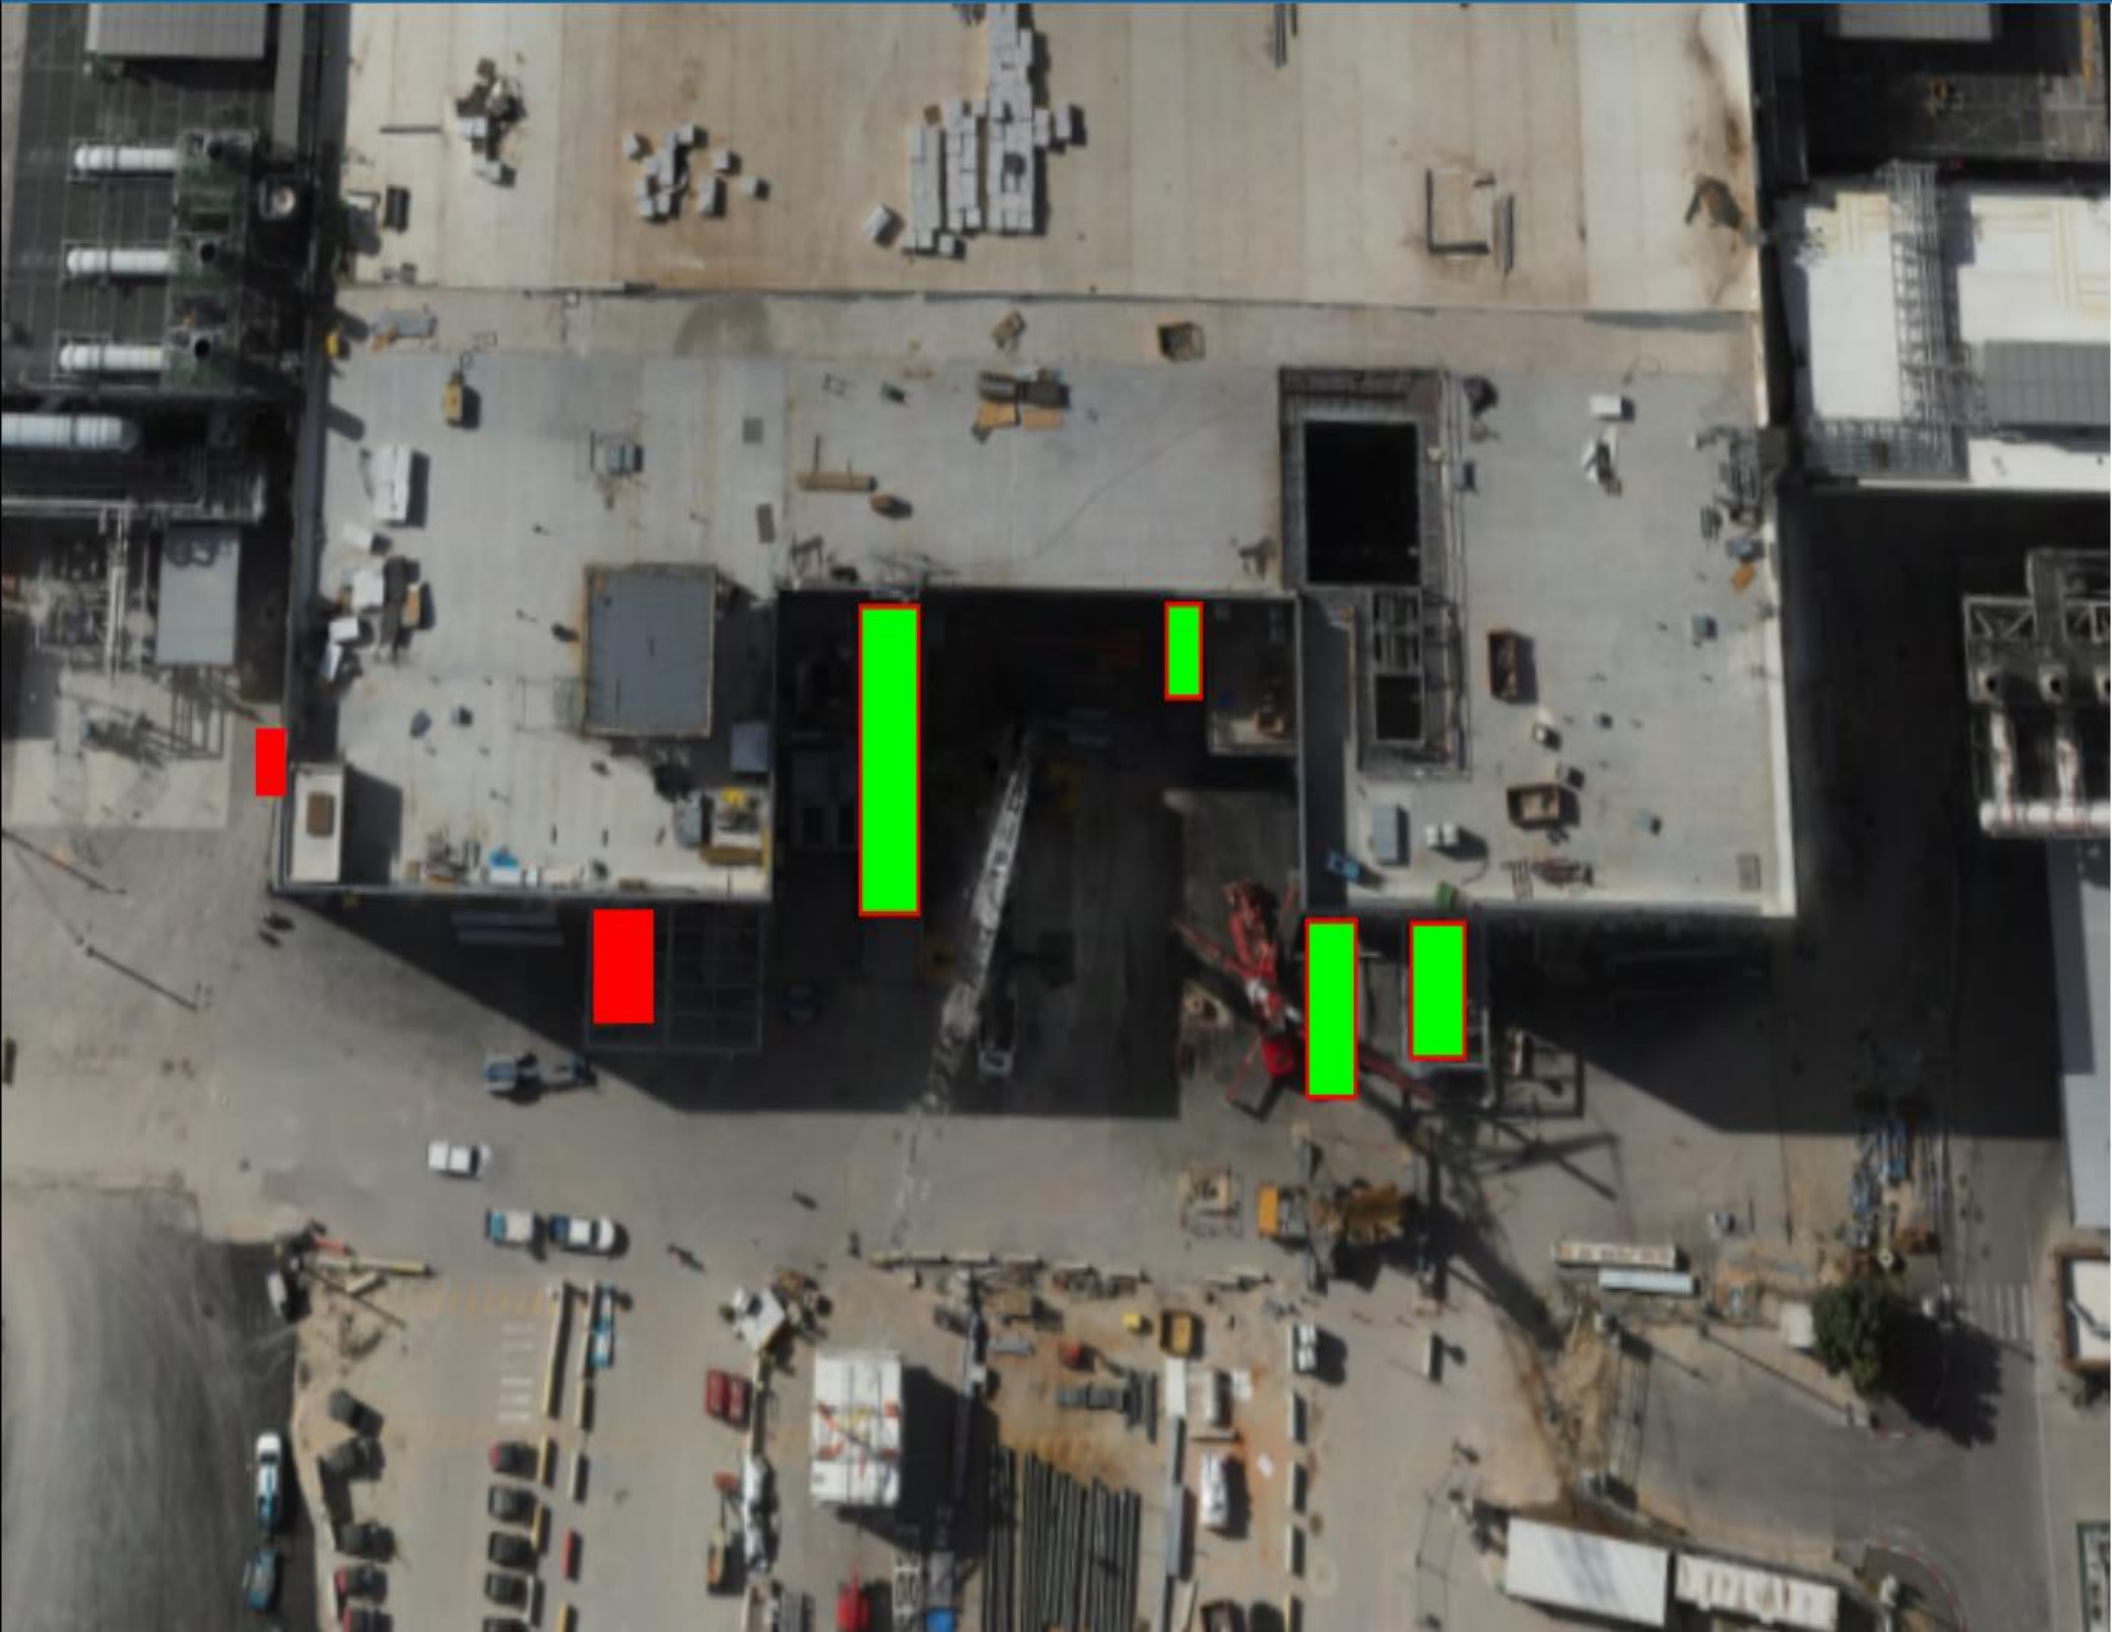


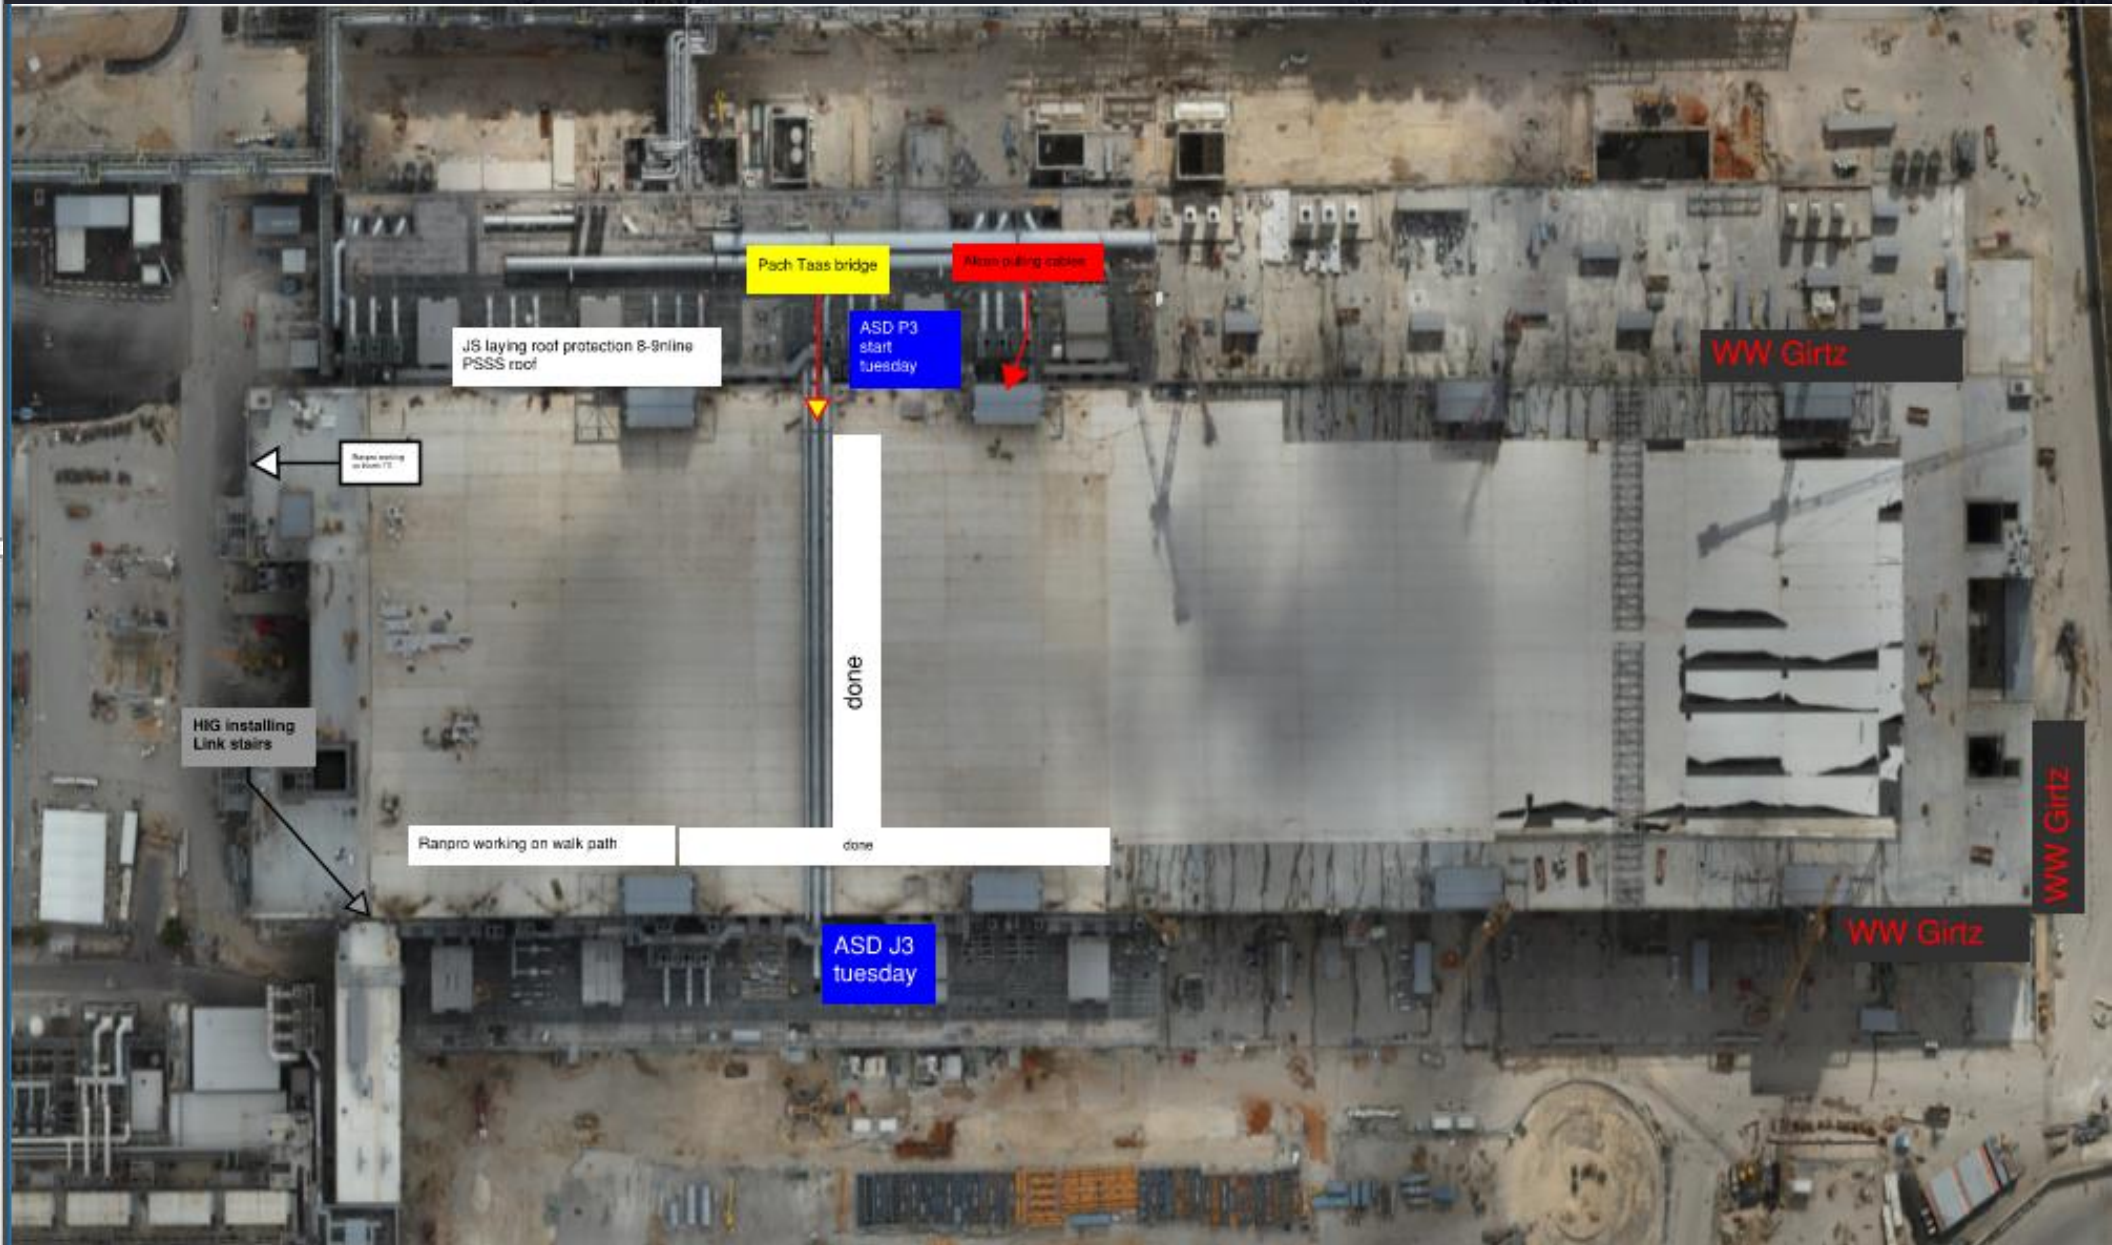



- READY FOR GIRTS 
- INSTALLING GIRTS 
- READY FOR PANELS 
- PANELS INSTALLED 

MOD 2 WESTSIDE GIRTS/SIDING

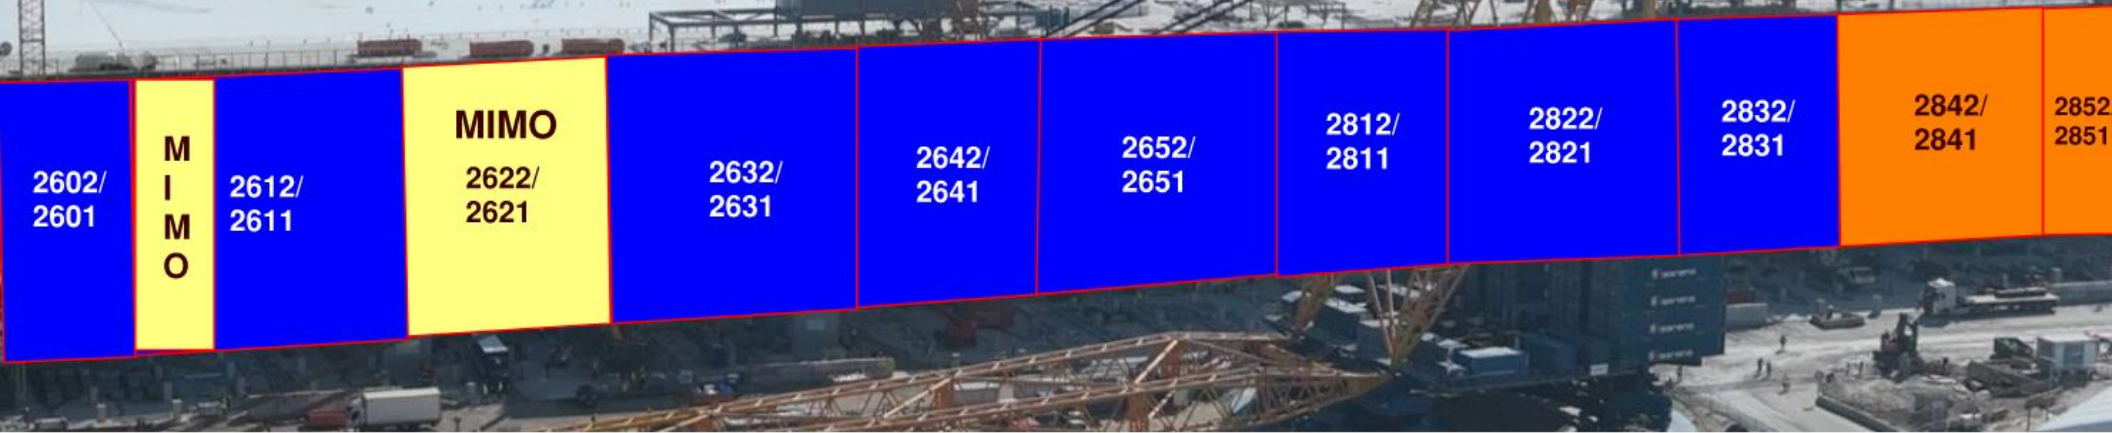

MOD 2 EASTSIDE GIRTS/SIDING




2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501
---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

PSSS.1

Utility Level 1YA


PSSS Roof 2SA

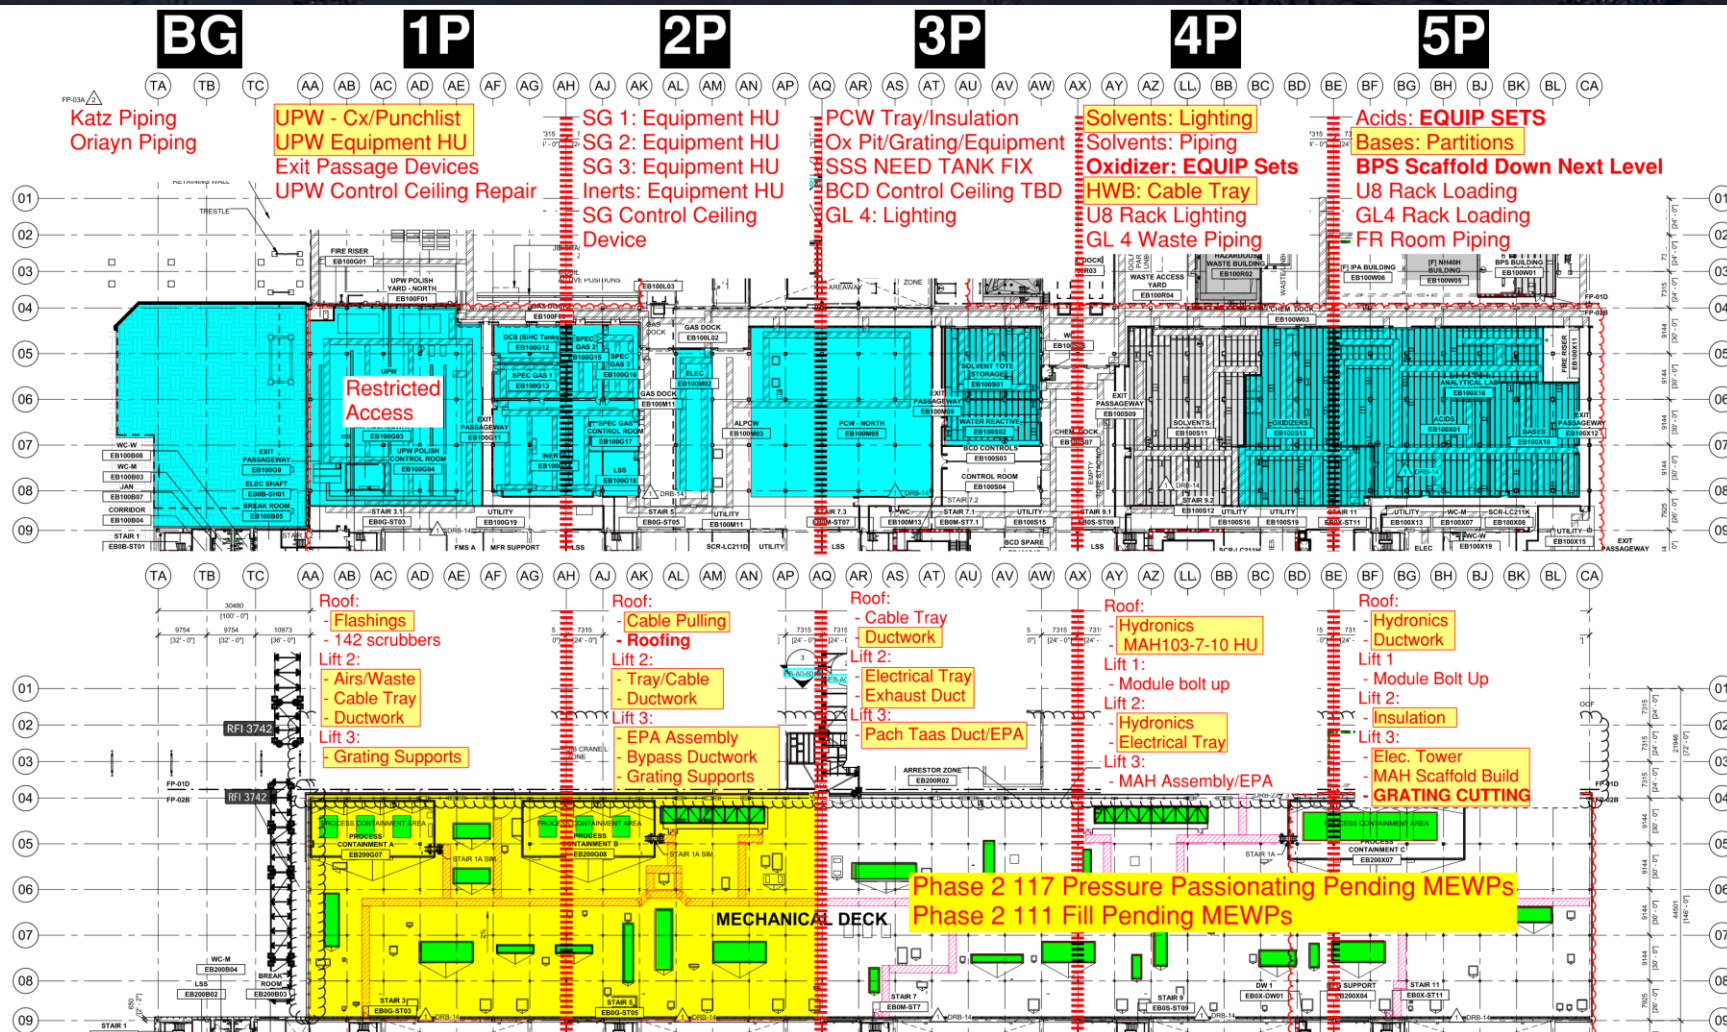

PSSS.2


Utility Level 1YA

PSSS Roof
2SA

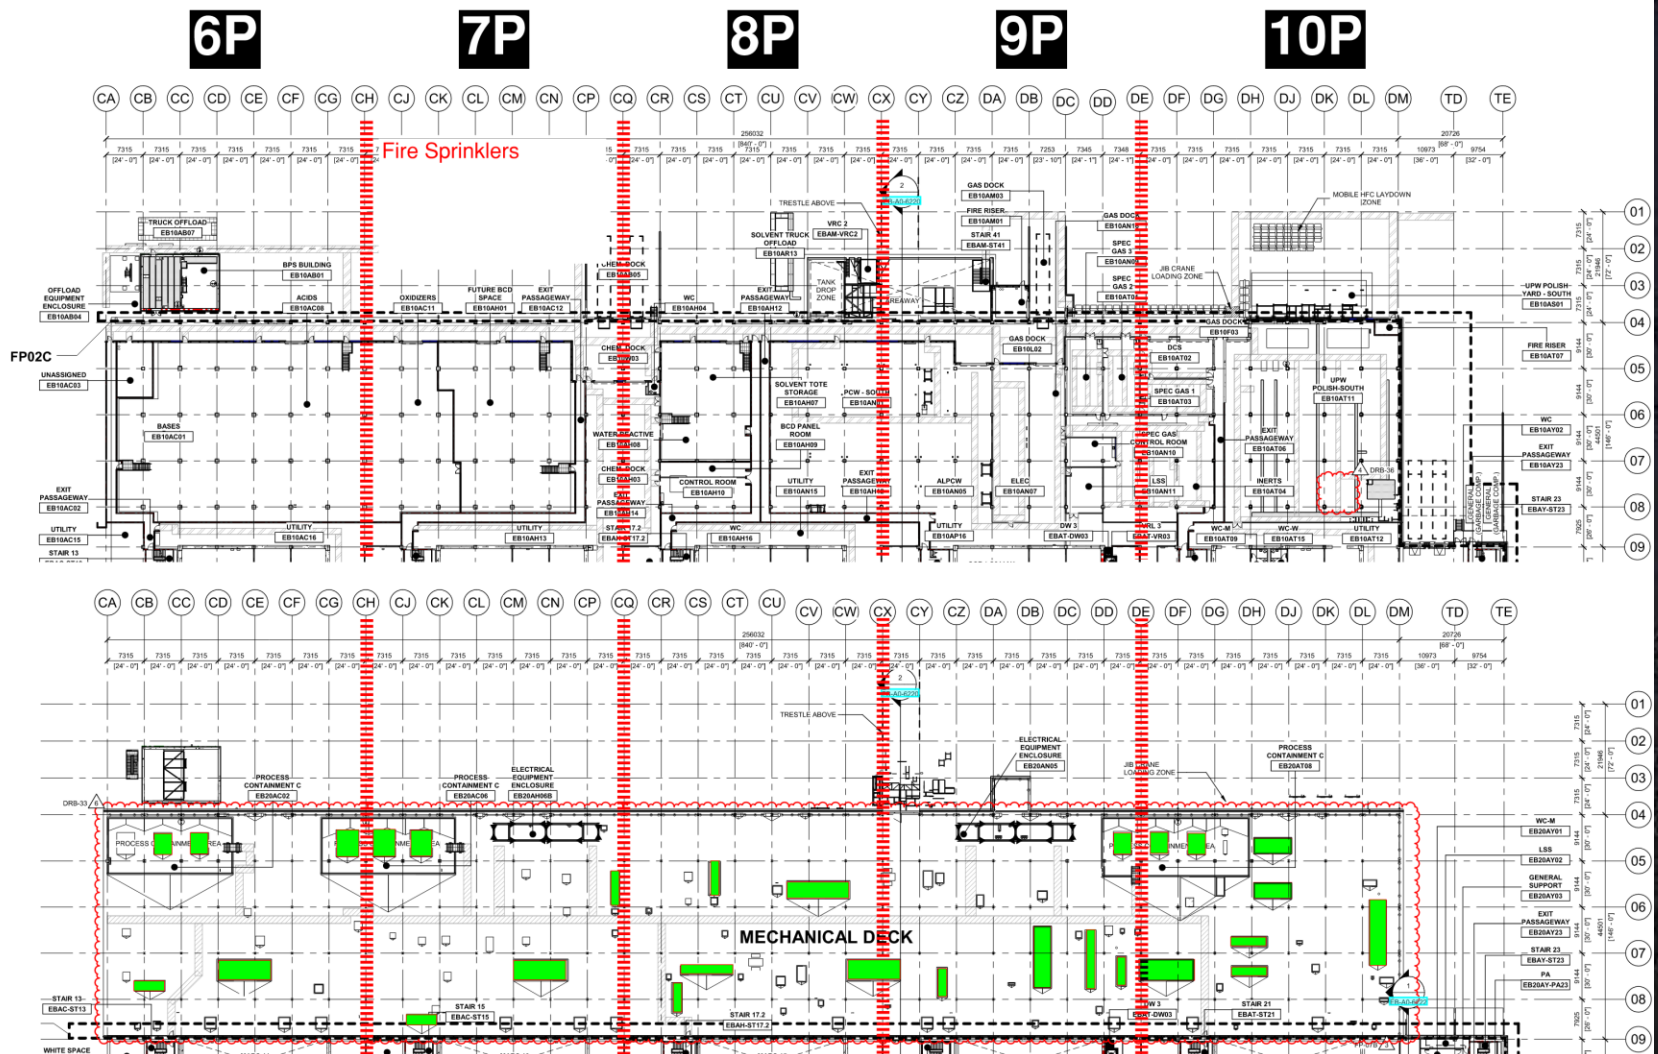

PSSS.1

KATZ - pressure test AB24- BB17
16:00 -24:00

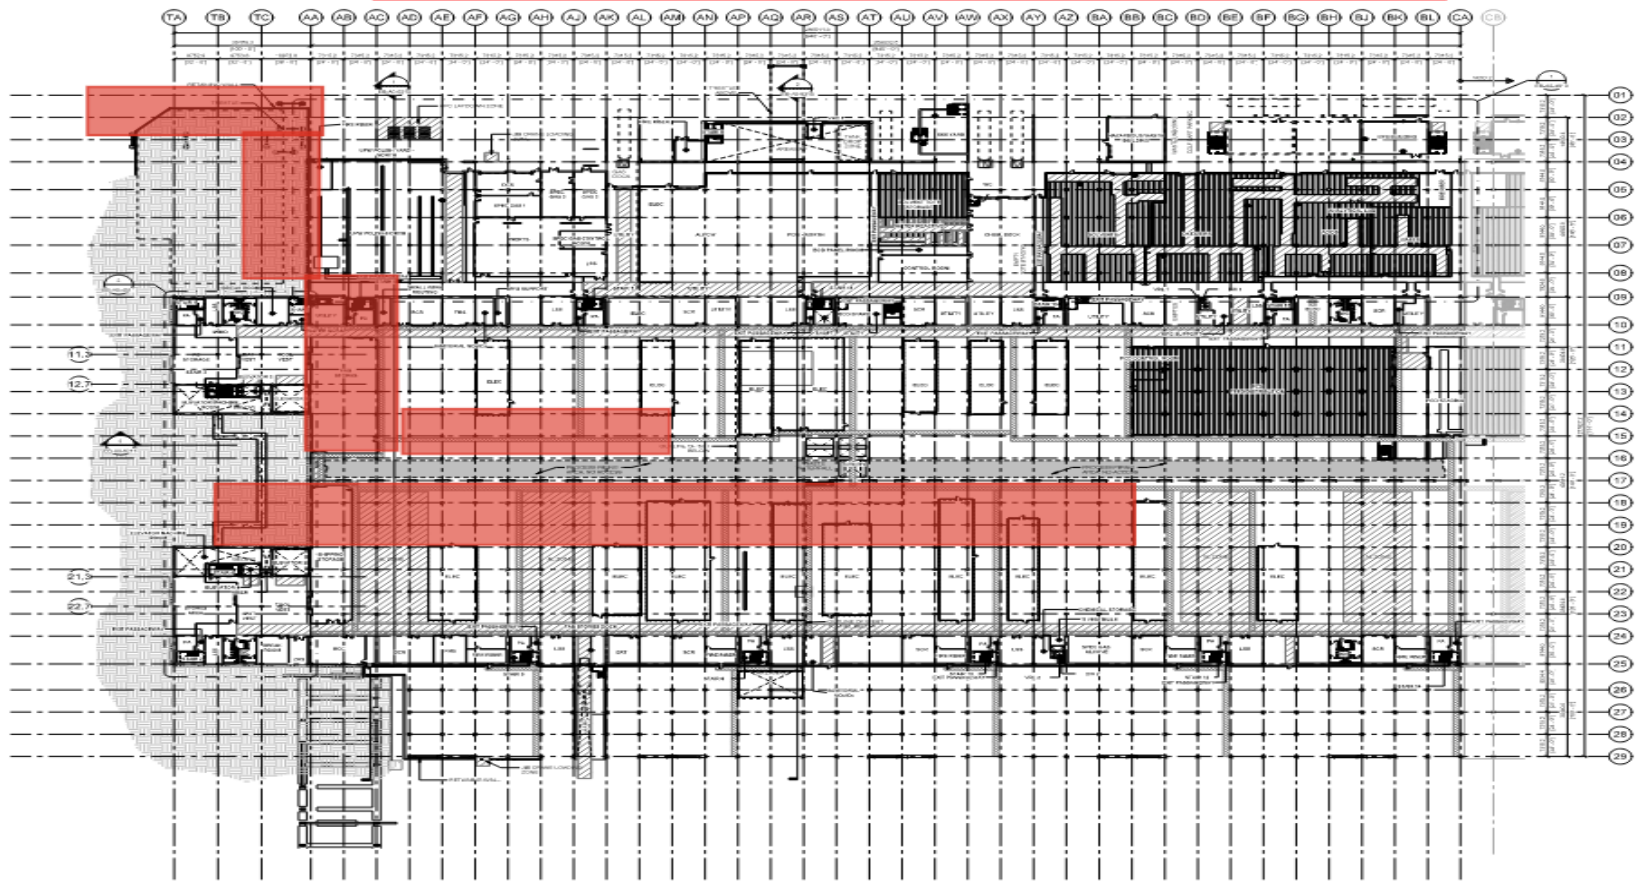




WJG – UL

PACH TAAS
install upn 135

PACH TAAS
wall penetration

CARMEL BIDUD
Measurements
and punch list

SK
punch list

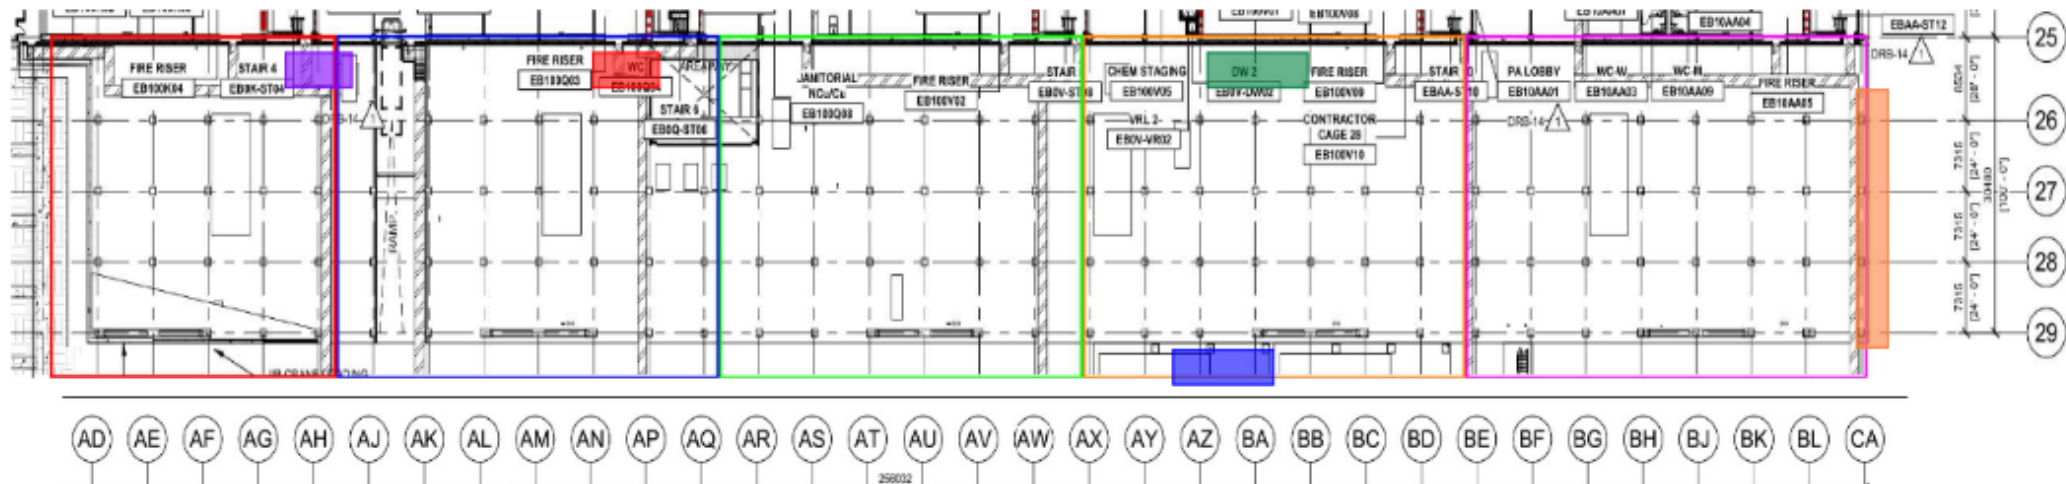




WJG – Lift 2

AHARON
installation

PACH TAAS
punch list


HYG
welding
penetration
supports


Afcon
instalation of
cable tray

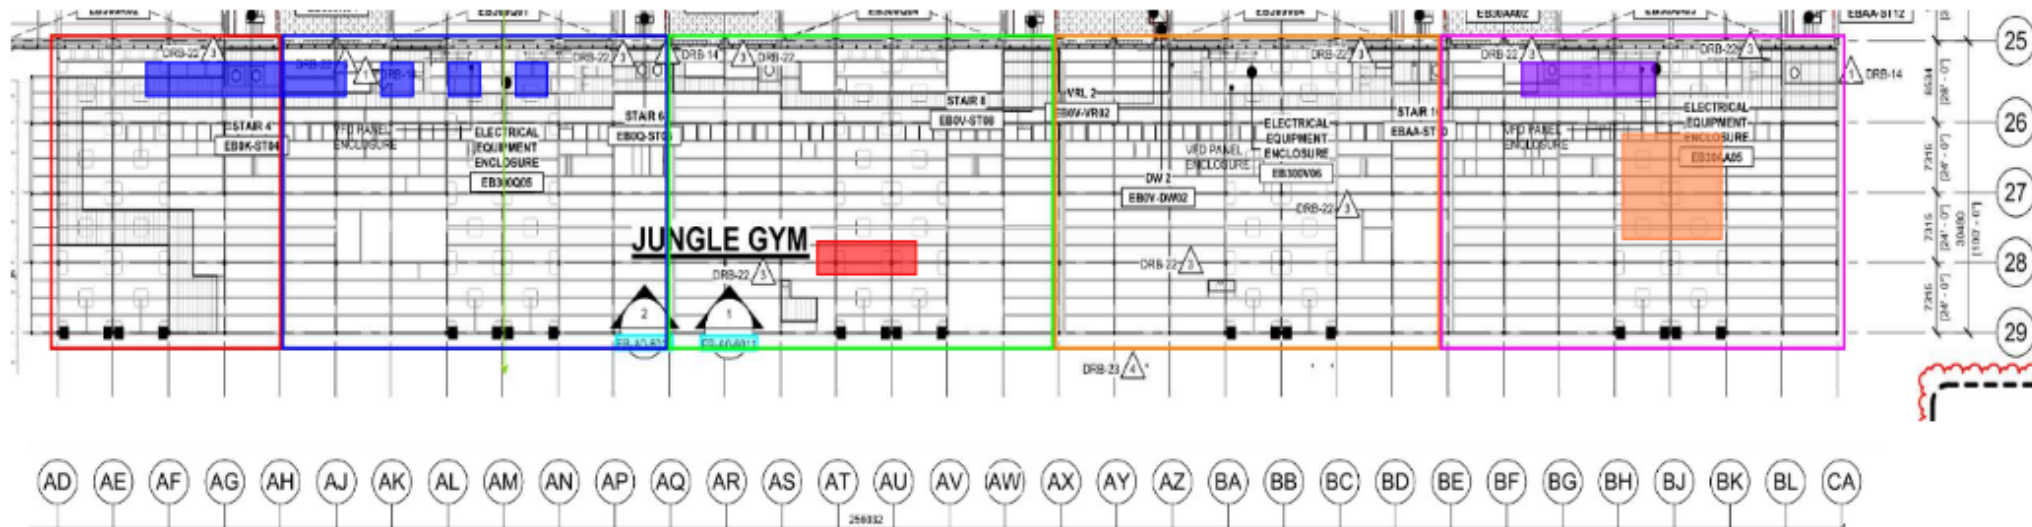

WJG – Lift 3

		AA scaffolding erections		PACH TAAS erecting EPA platform
--	--	--------------------------------	--	---------------------------------------

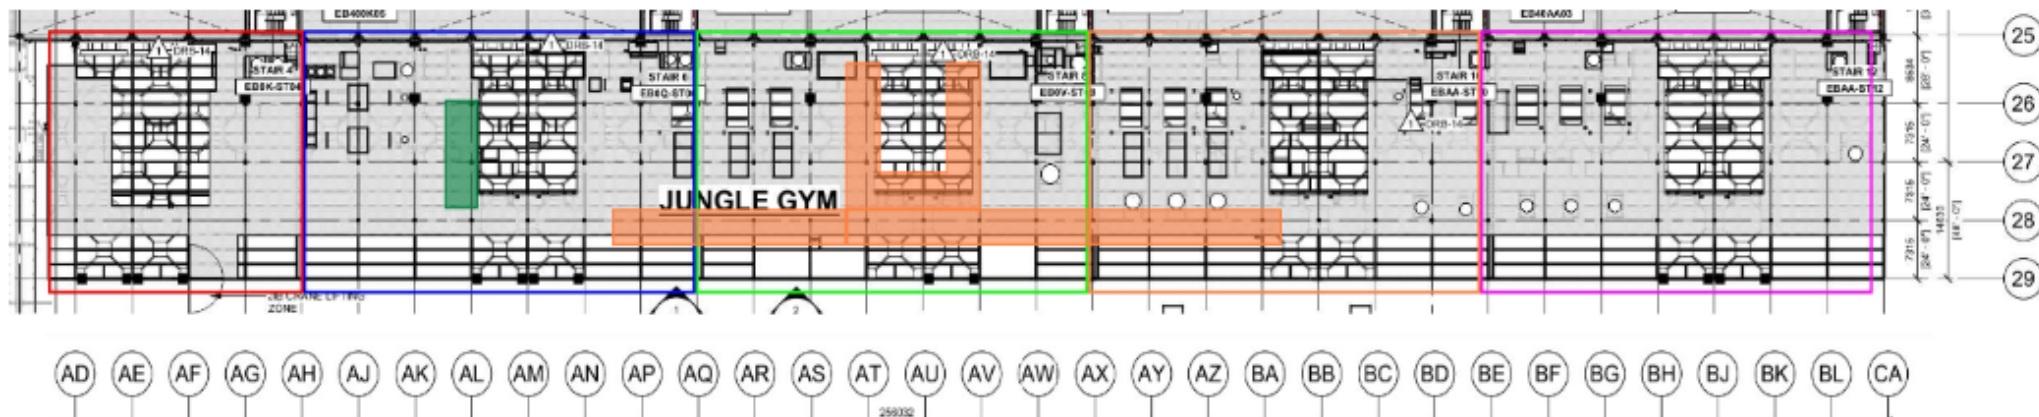

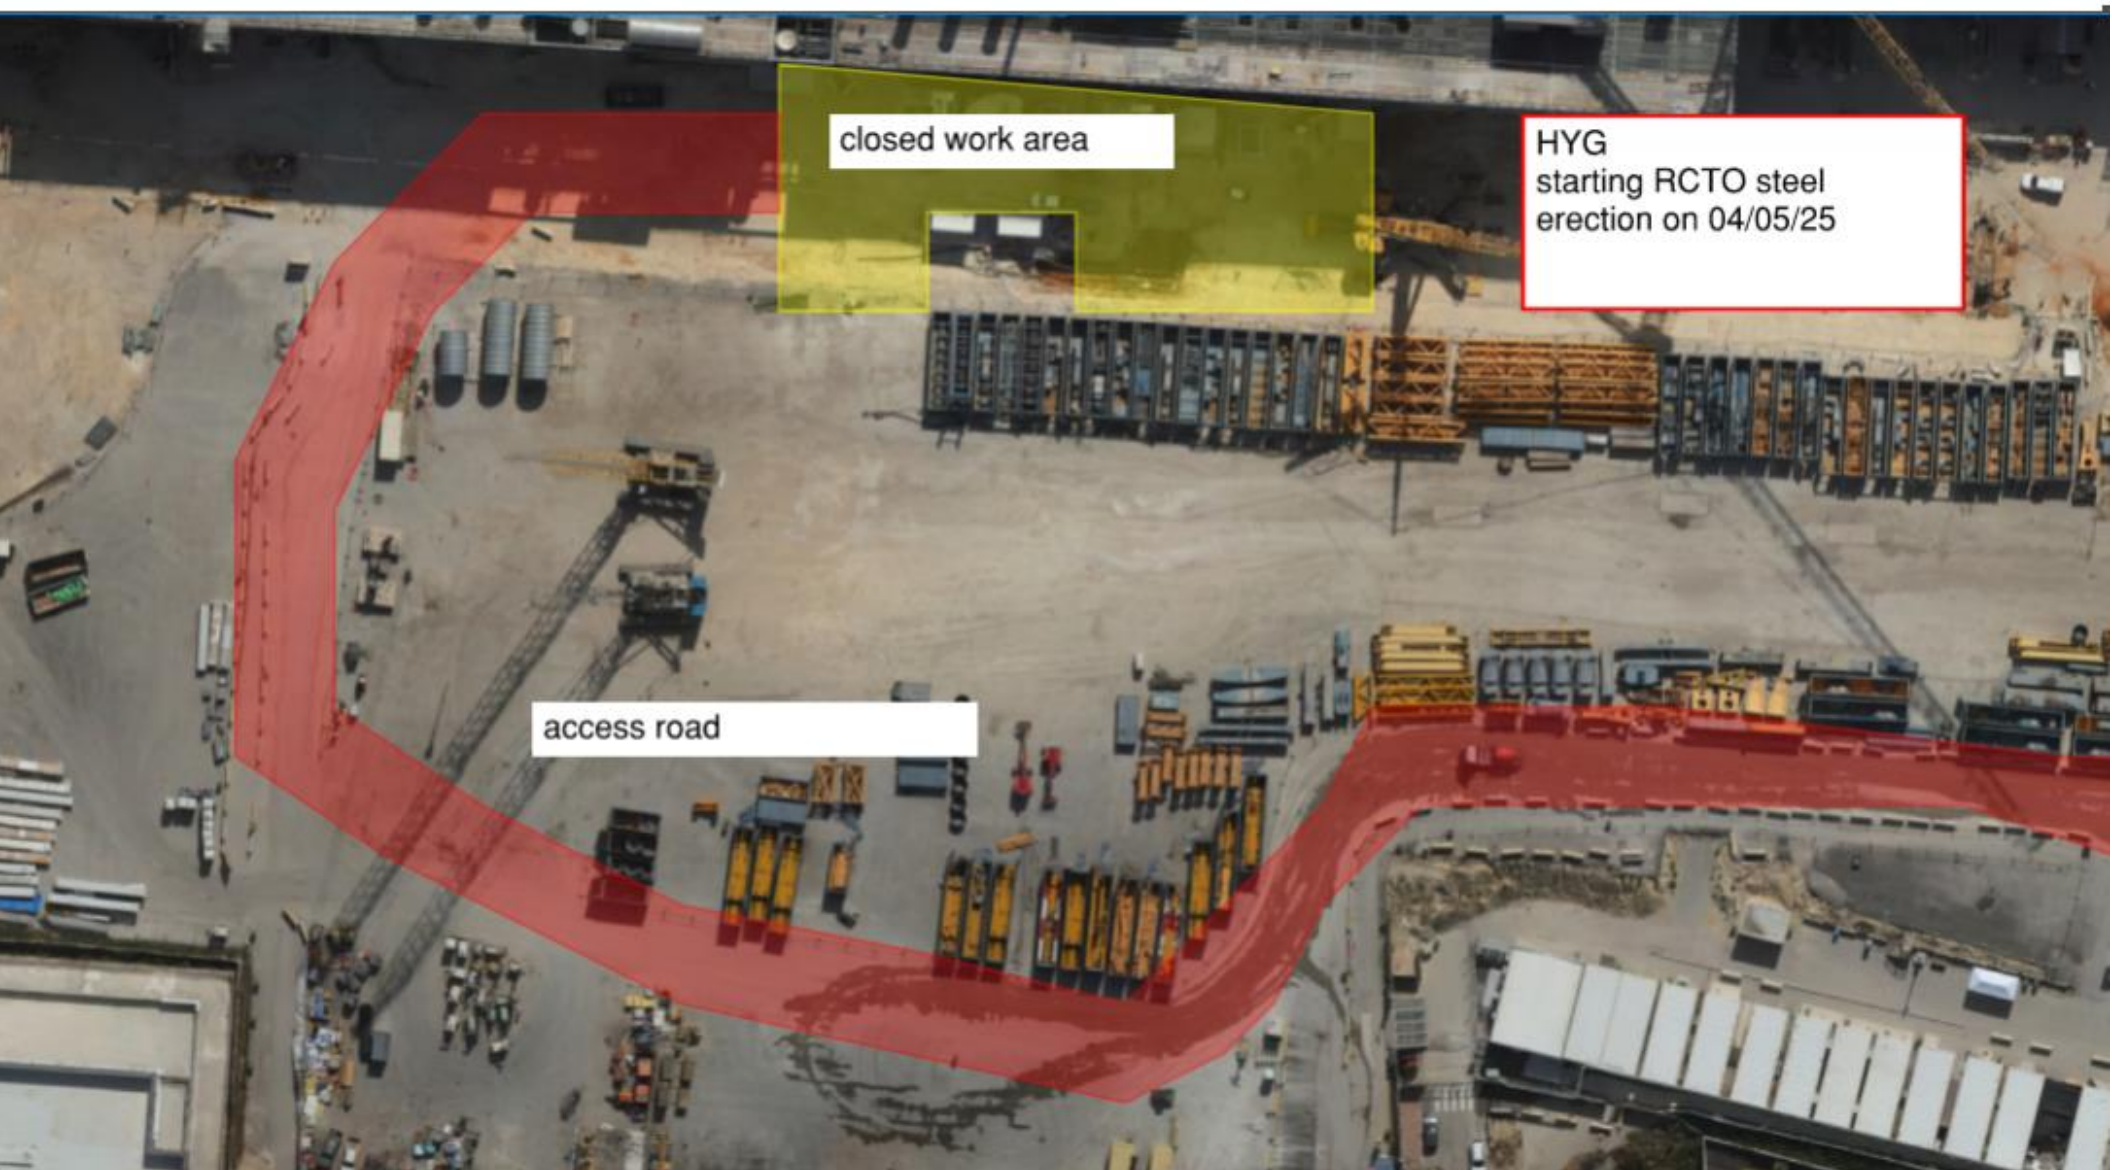


closed work area


HYG
starting RCTO steel
erection on 04/05/25

access road


[illegible]

CUB 1 – EXTERIOR/ROOF

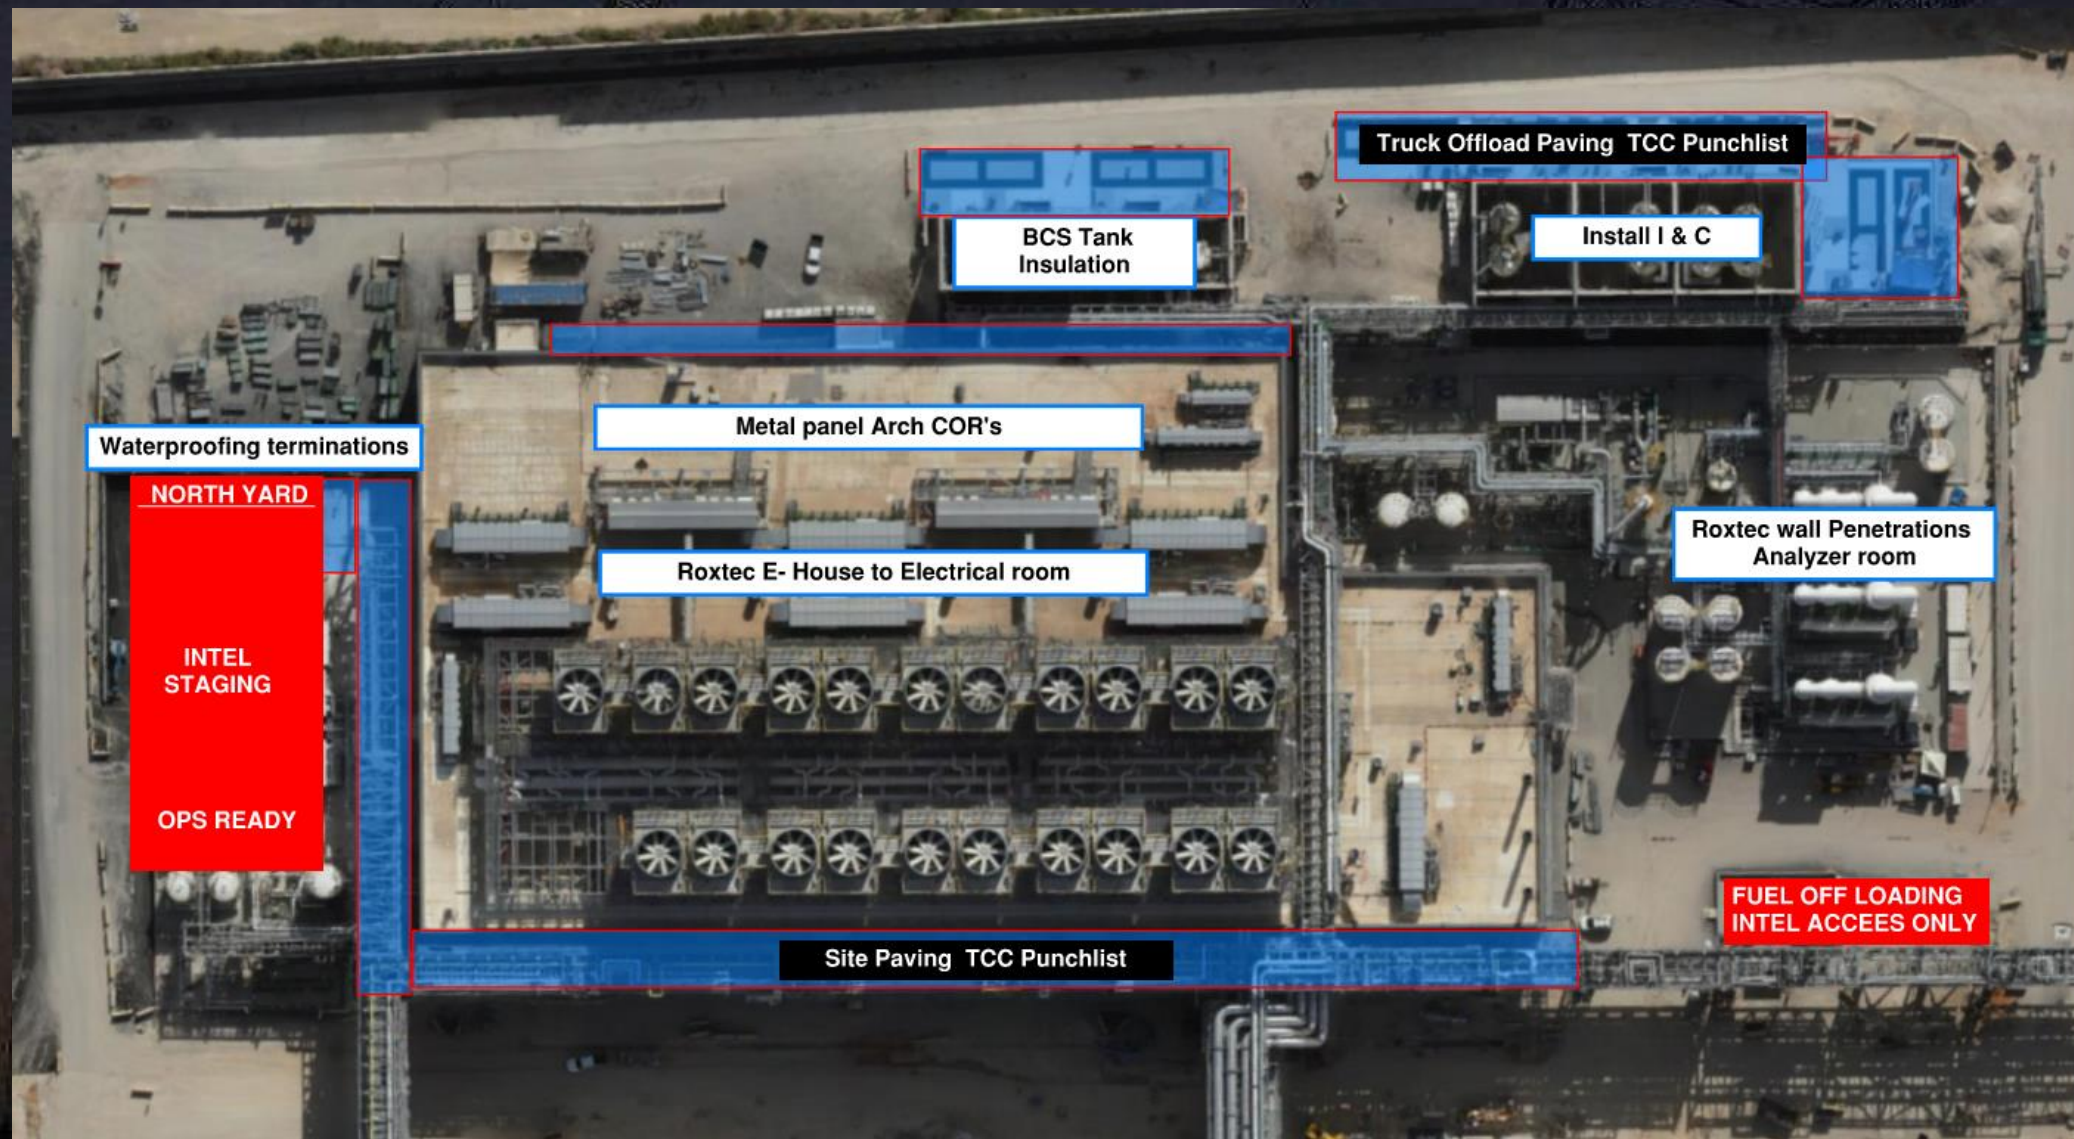

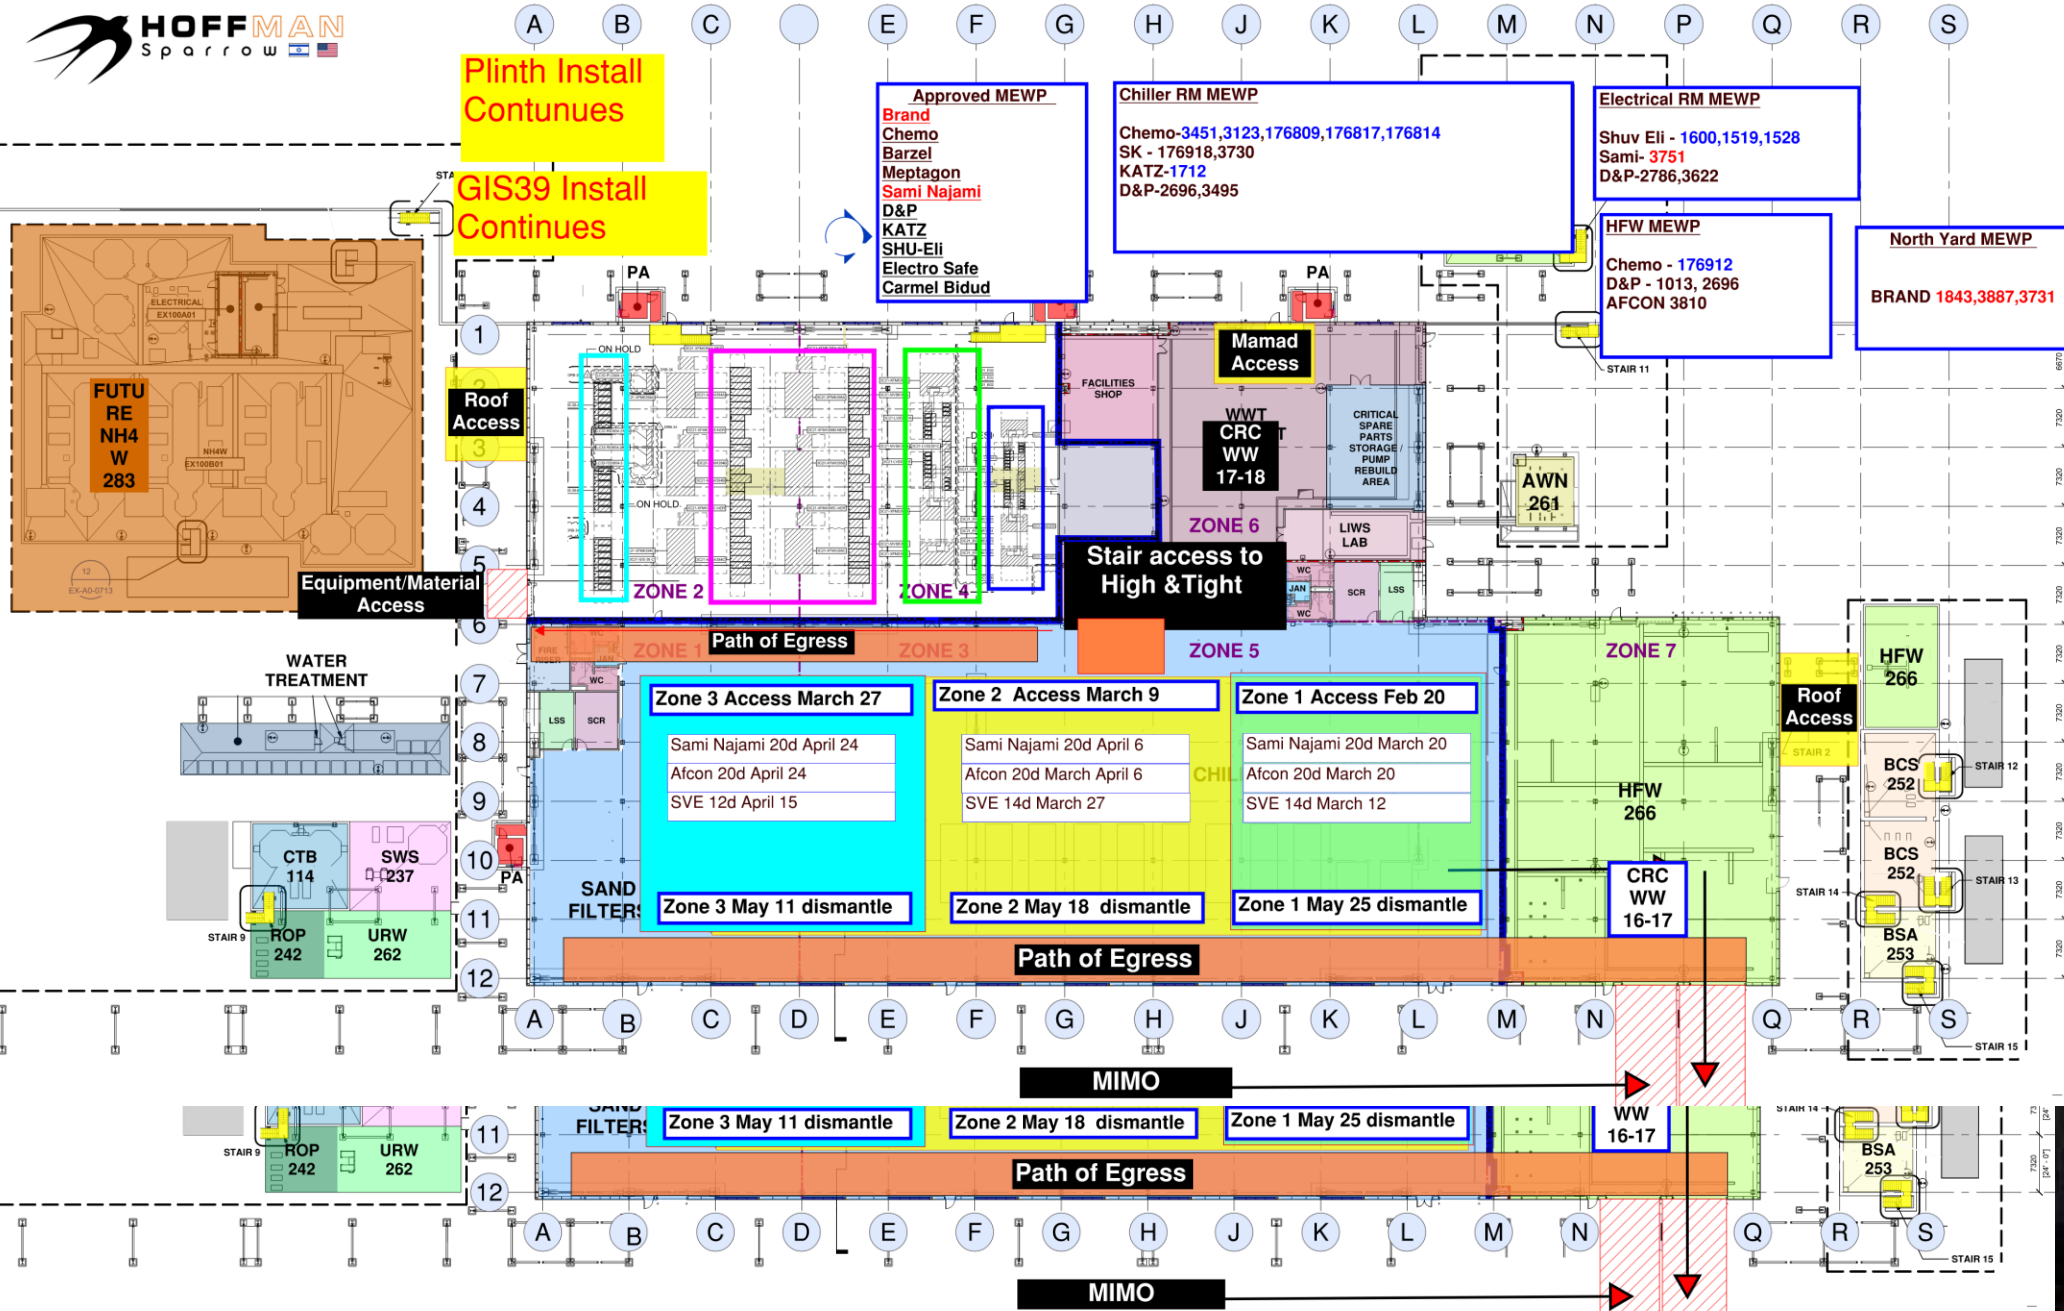

CUB 2- Trestles/Roof/Guardrails

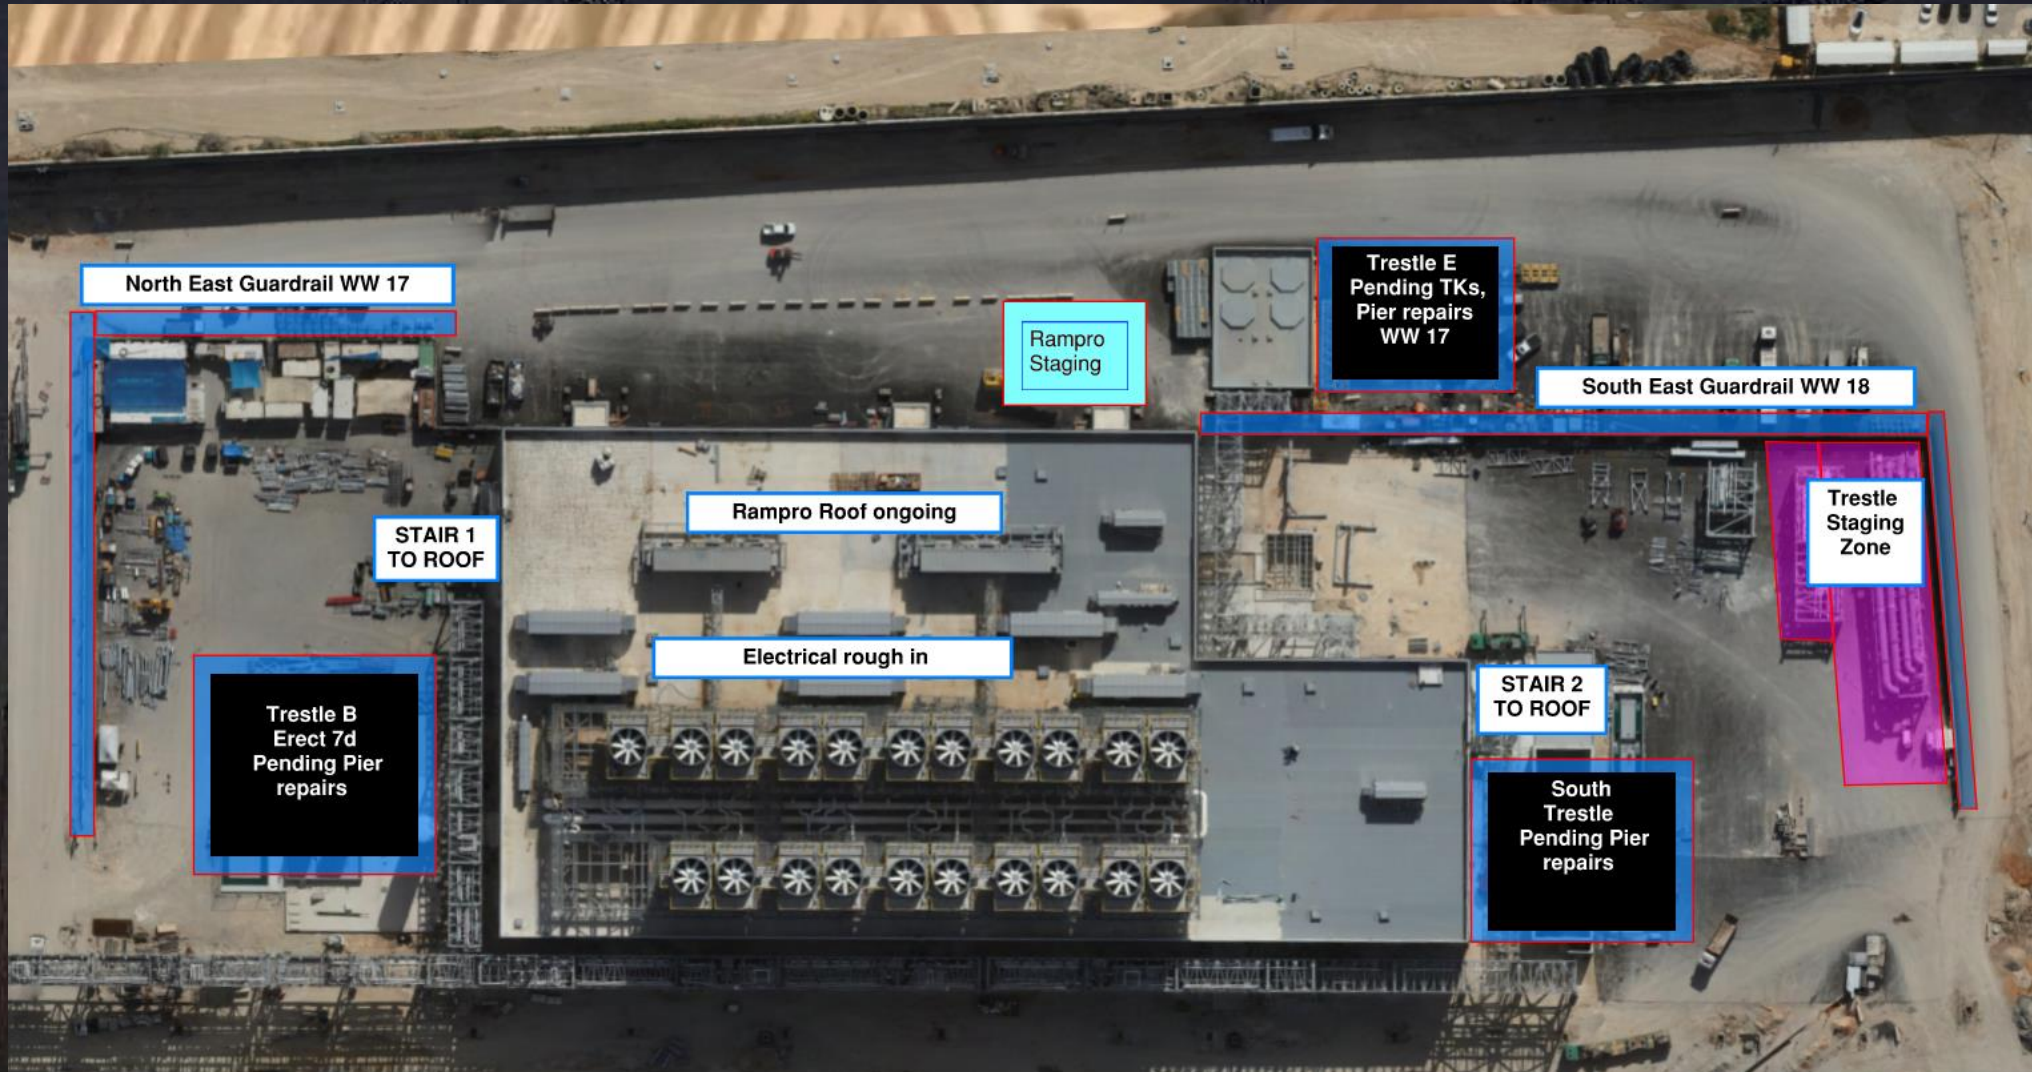



Daily Coordination Meeting

Site Logistics




Daily Coordination Meeting

Site Logistics: North



Daily Coordination Meeting

Site Logistics: South

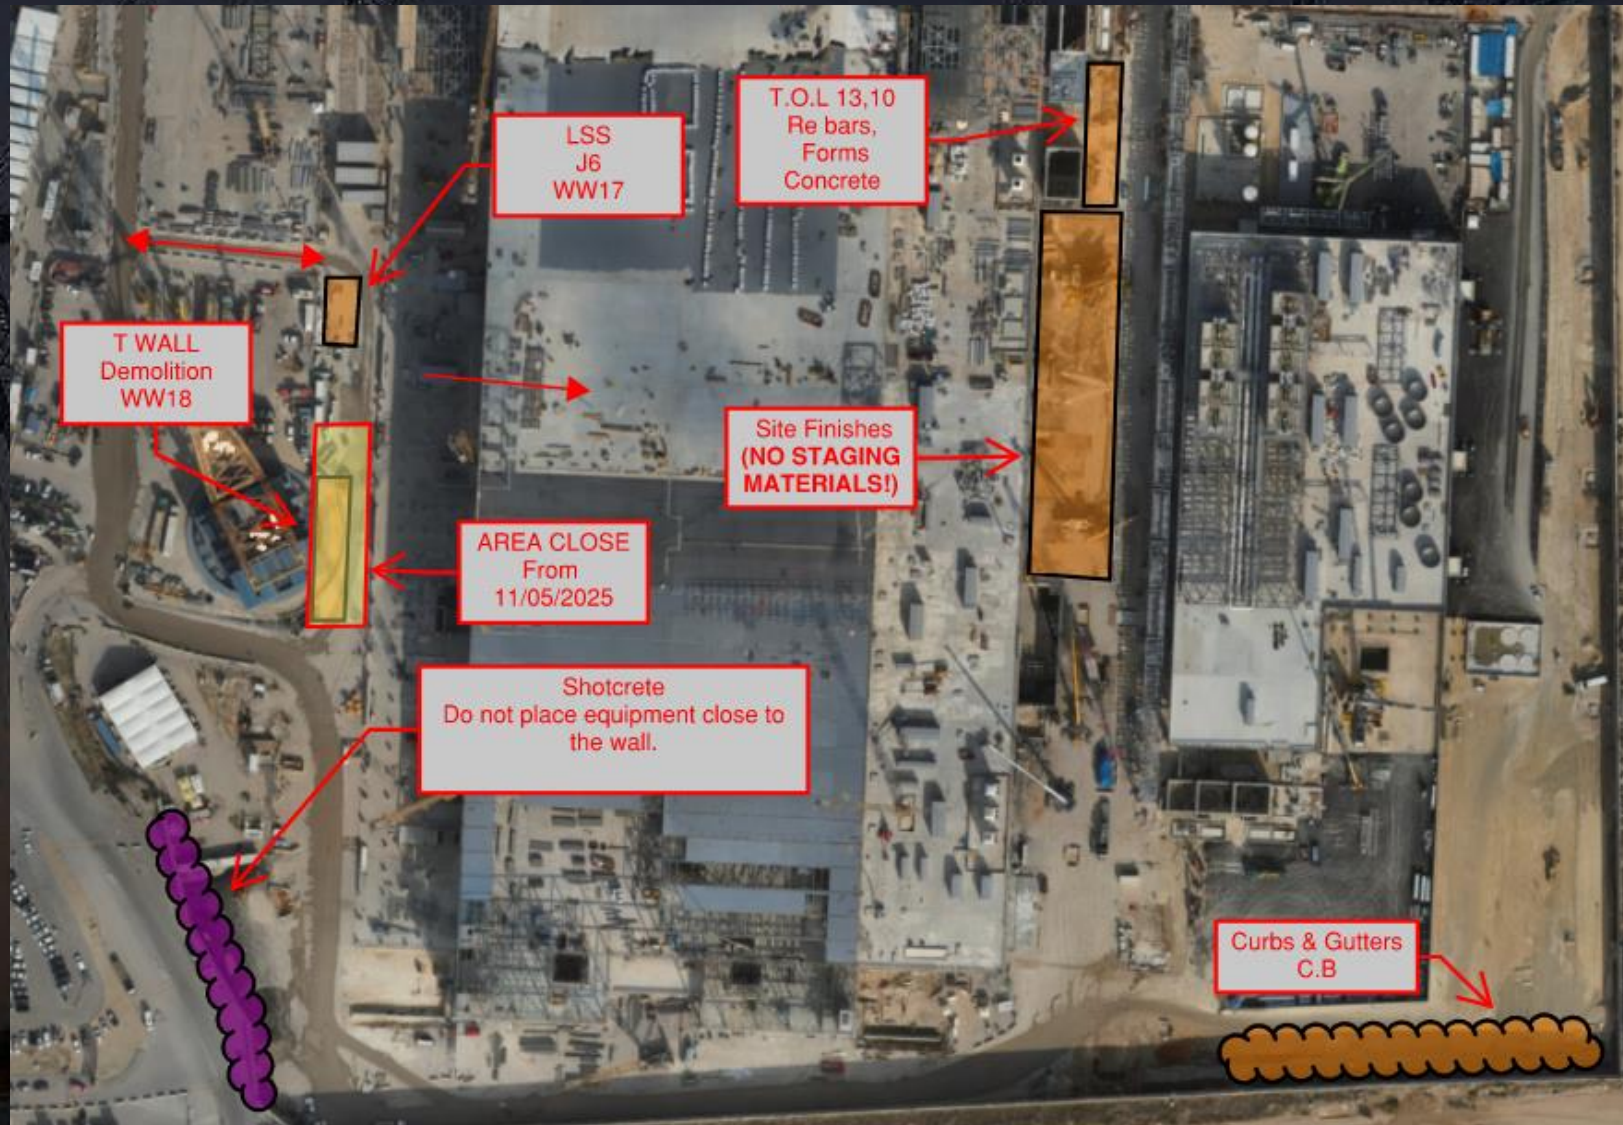


Daily Coordination Meeting

MAMAD Locations

MAMAD LOCATIONS (19-March-2025)


■ LARGE
■ SMALL
■ BUILDING

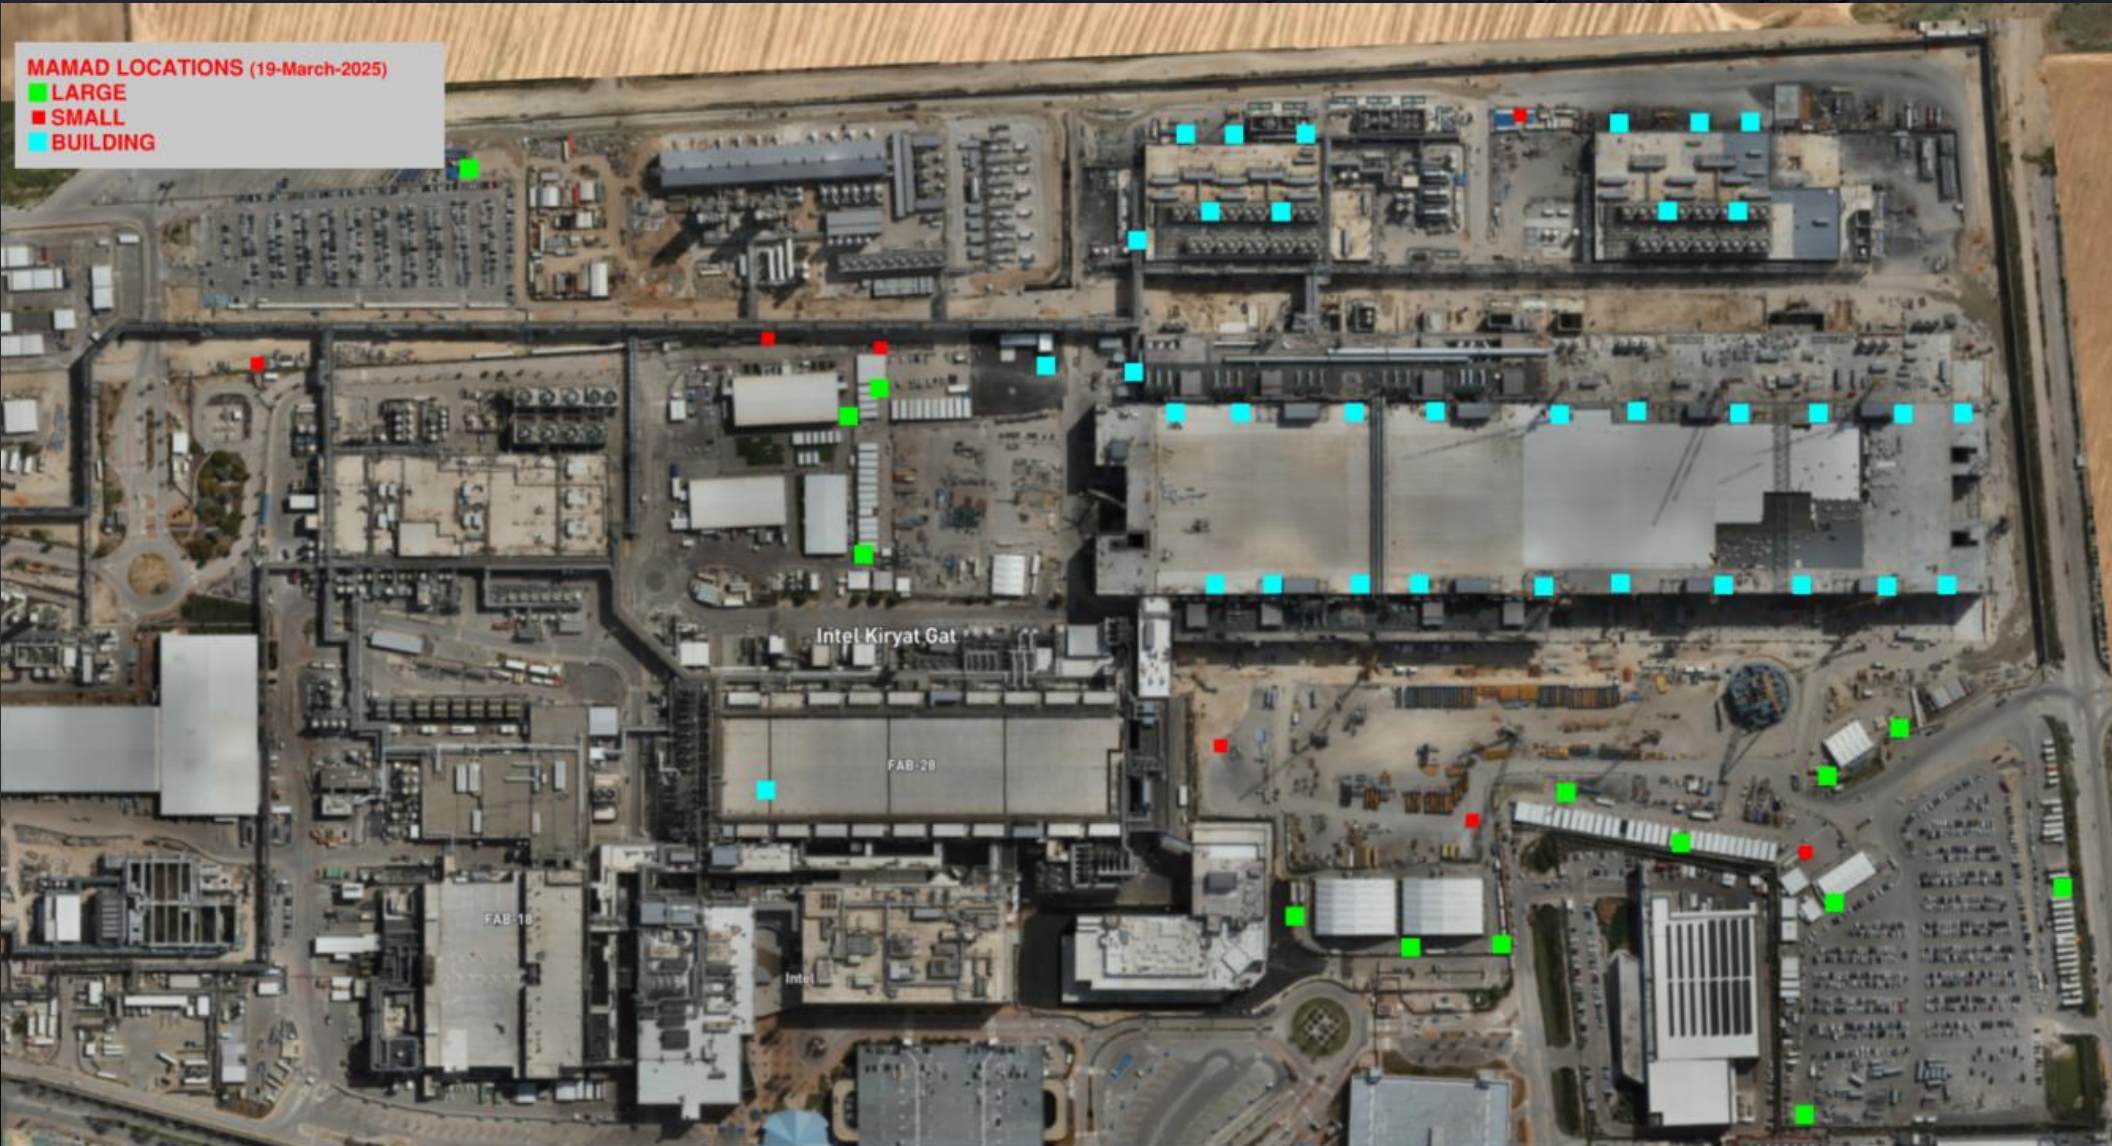

Daily Coordination Meeting

WATER BOTTLE FILLING STATIONS

WATER BOTTLE FILLING STATIONS

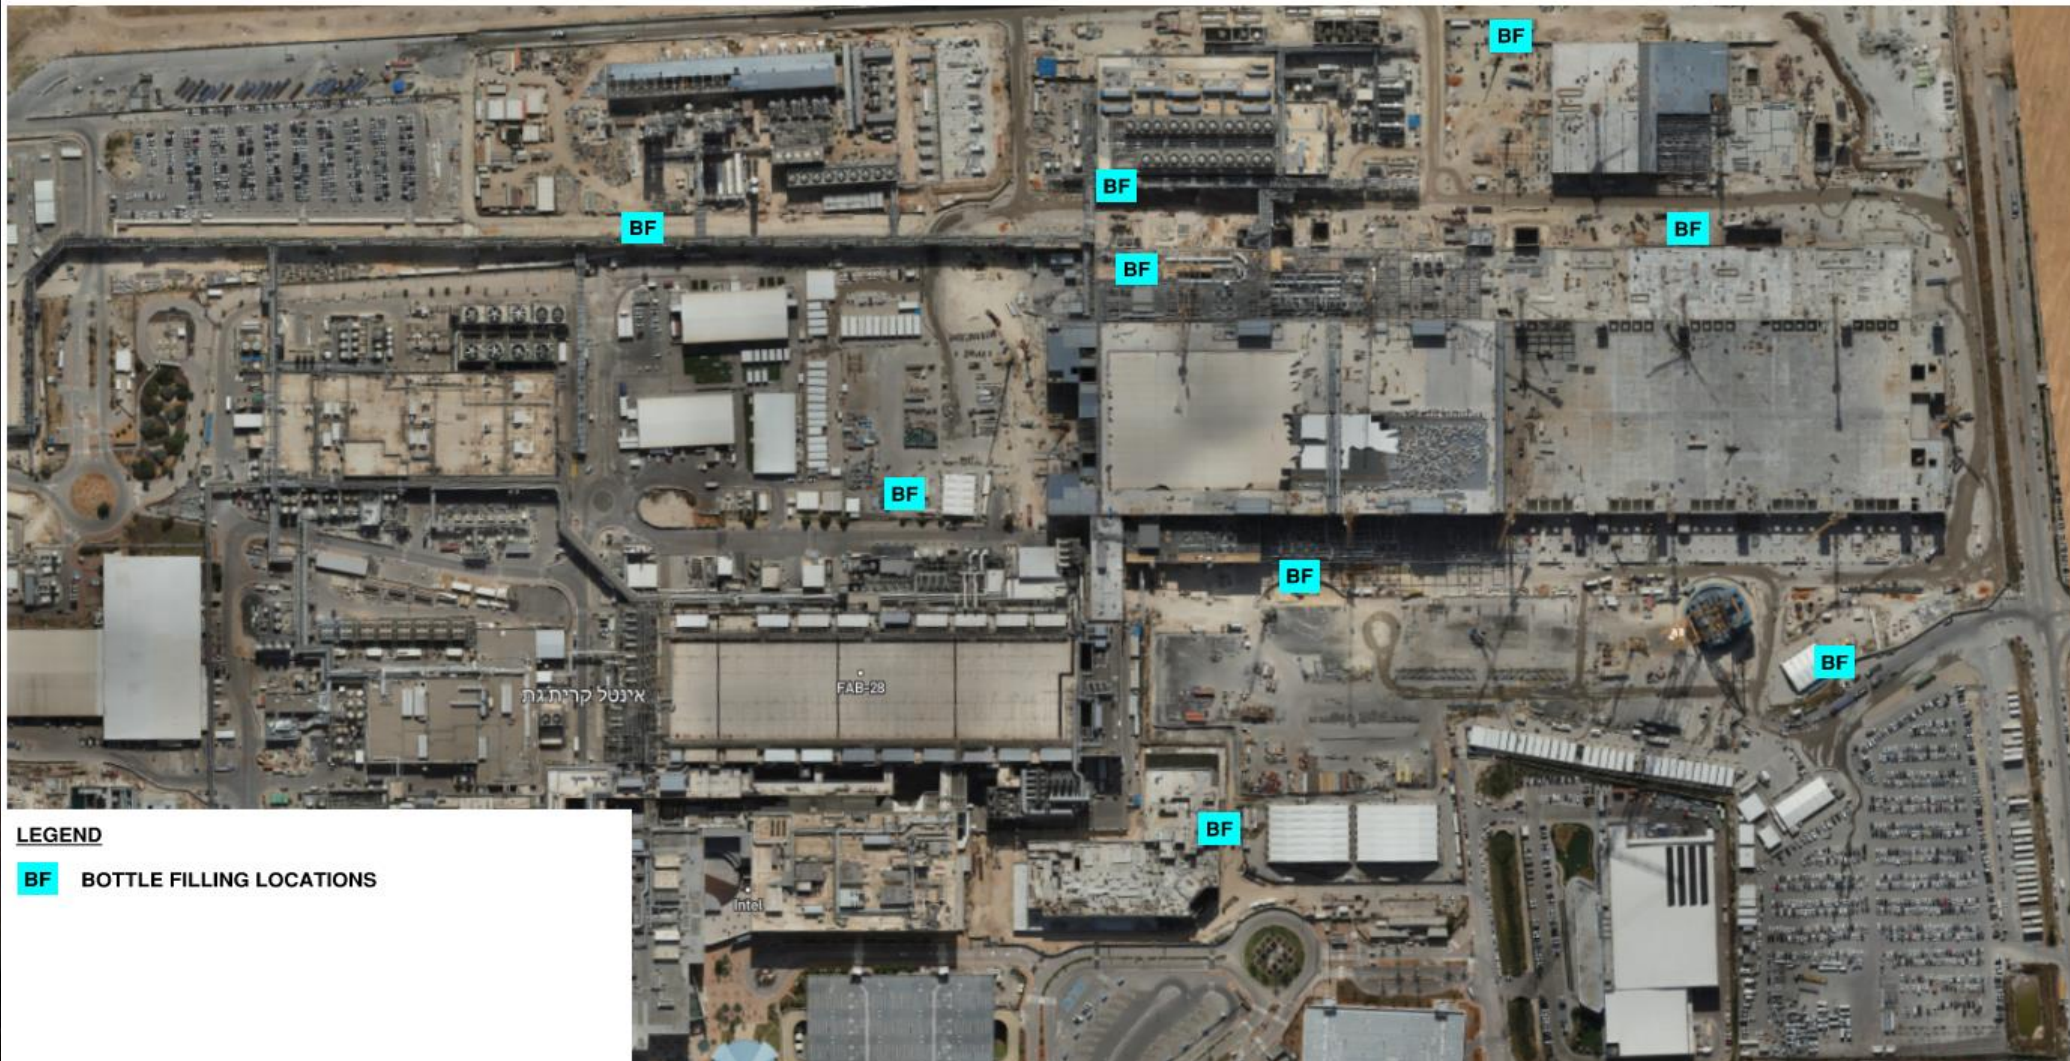

Area assessment

A worker went into an exclusion zone made by handrail. The zone contained fall hazards through openings in the floor. No area assessment was done by supervision before sending worker.

All tasks require an area assessment by supervision with findings included in the PTP.



Daily Coordination Meeting



14:00 Sign In
