

Daily Coordination Meeting




Daily Coordination Meeting


General Topics:

- **UPW Polish Op Ready L1 Milestone Claimed!!**


UTILITY LEVEL MOD1

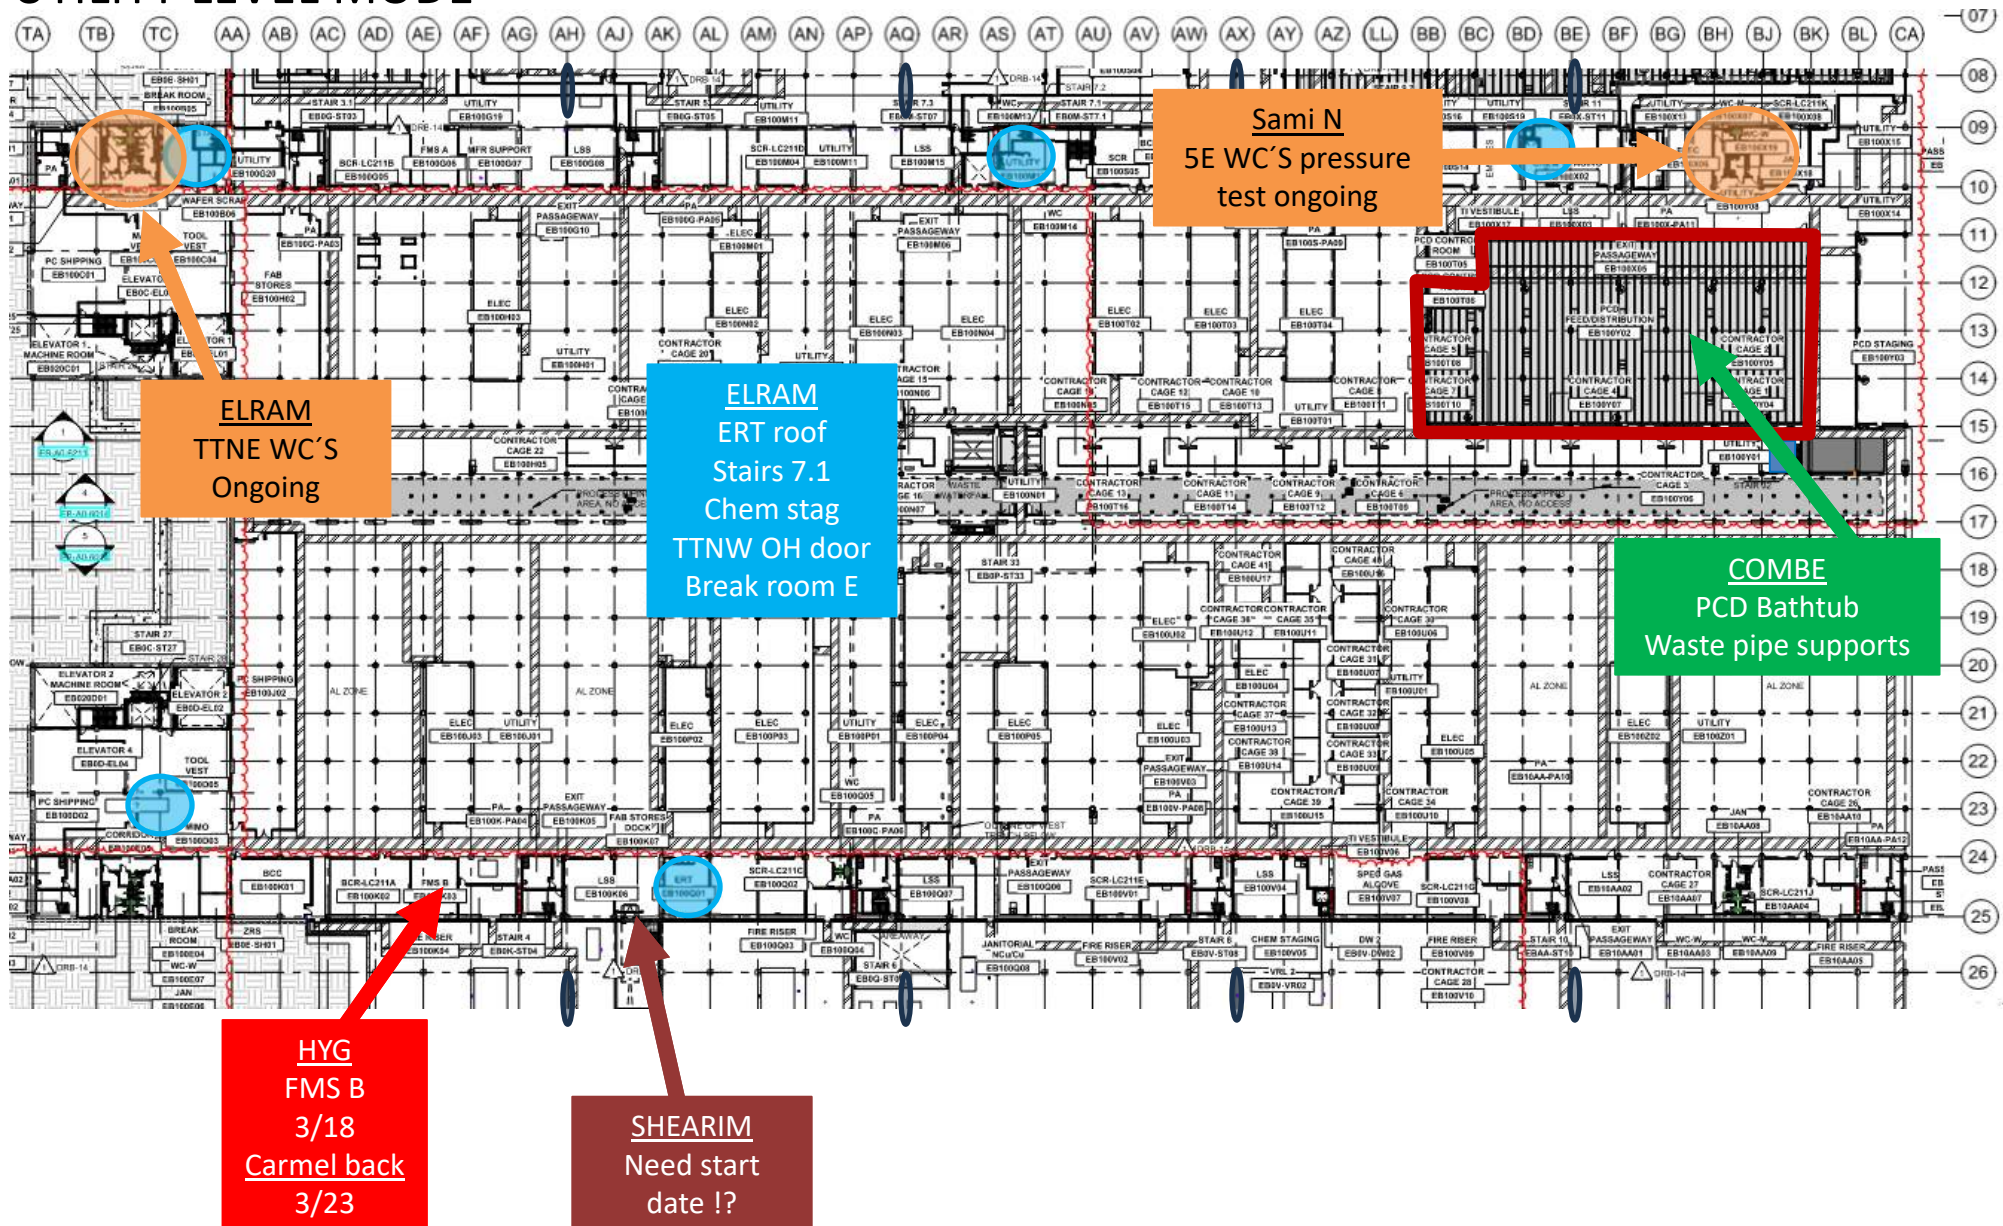


SUT 38.1 LEVEL

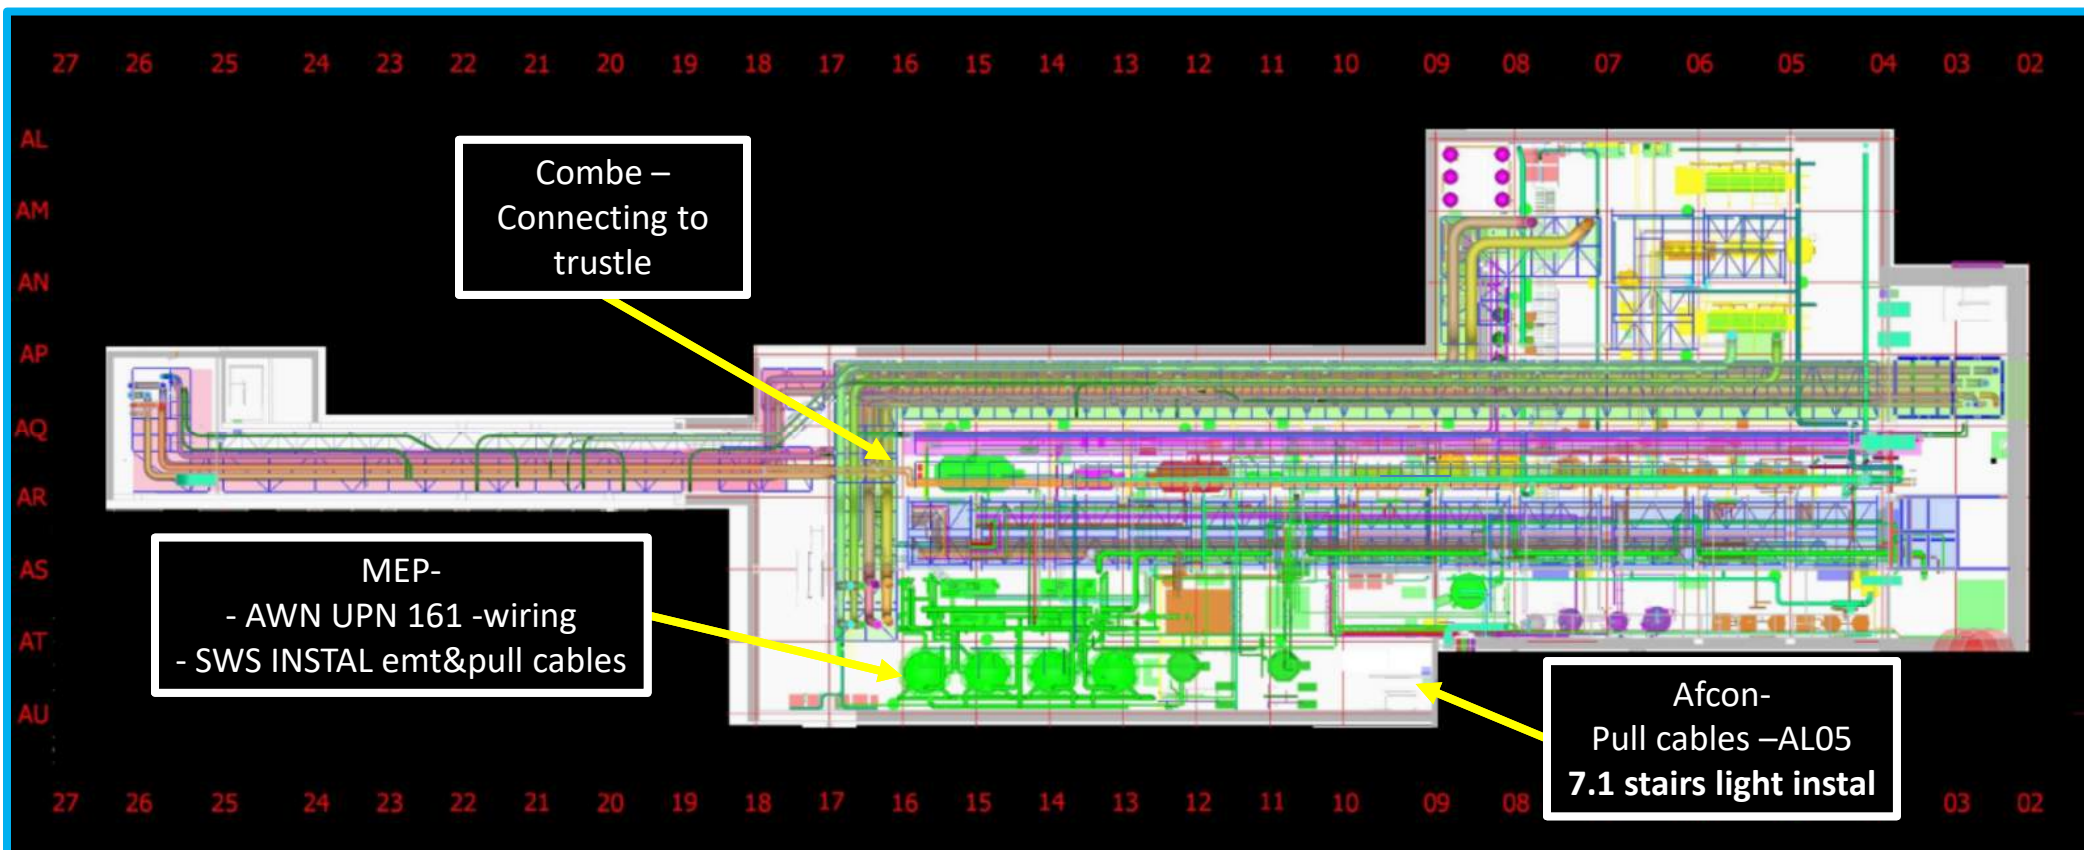


SUT 38.2 LEVEL

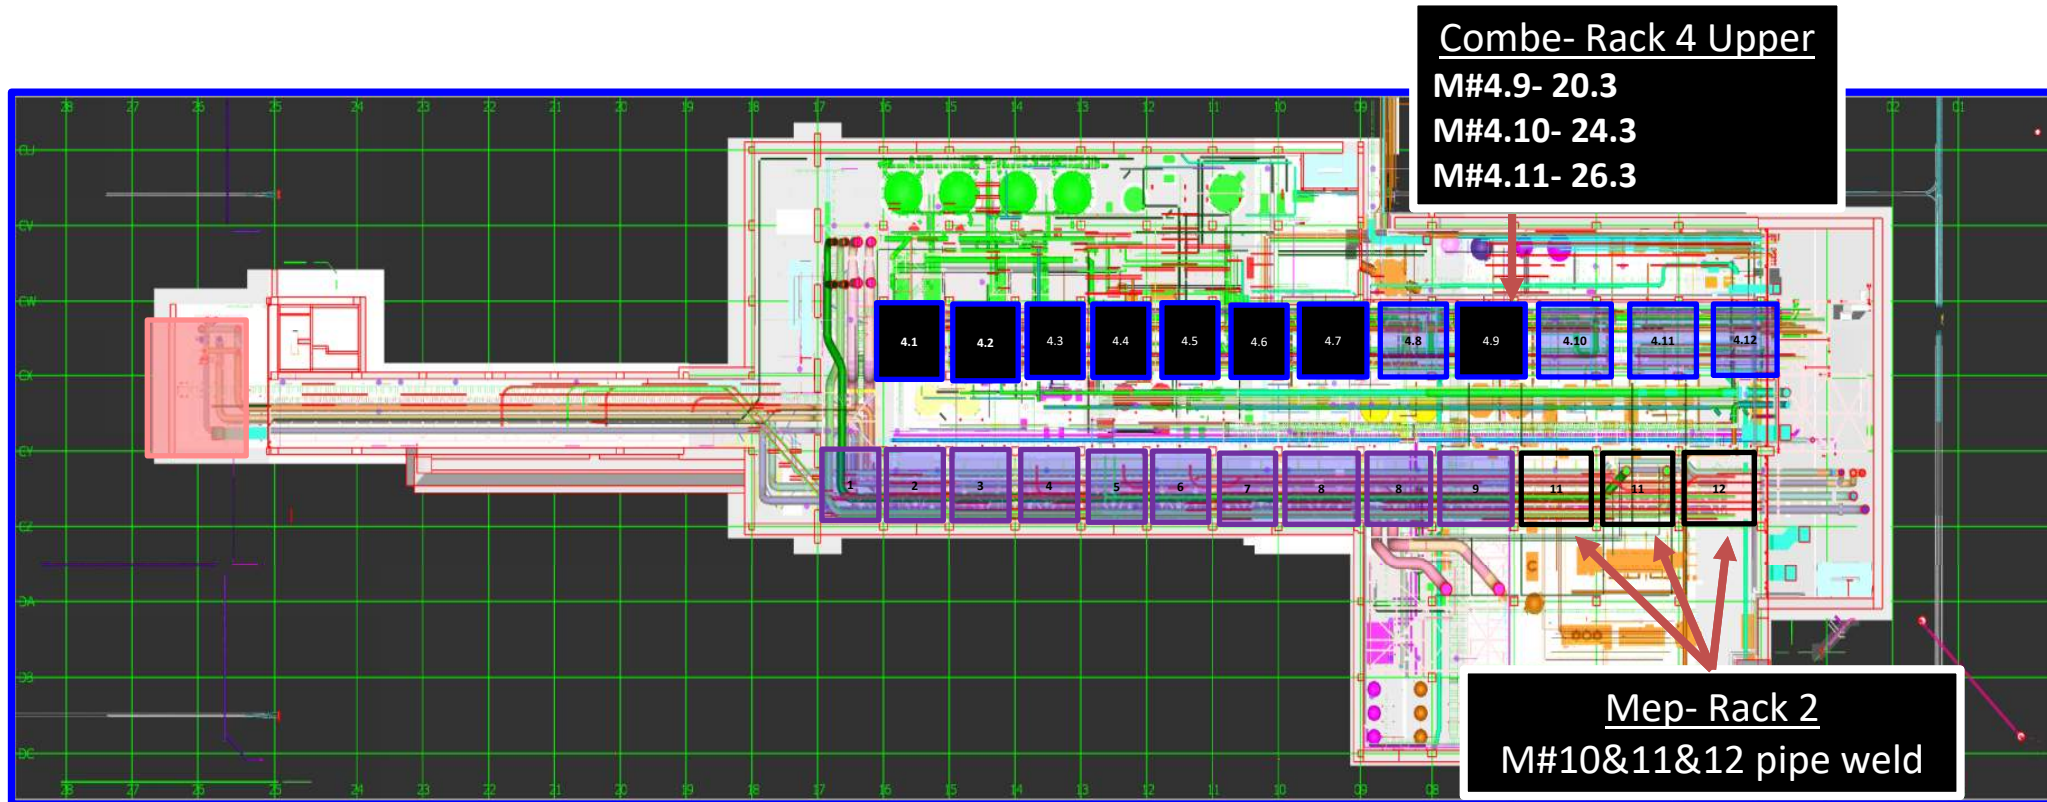


SUT 38.1 LEVEL

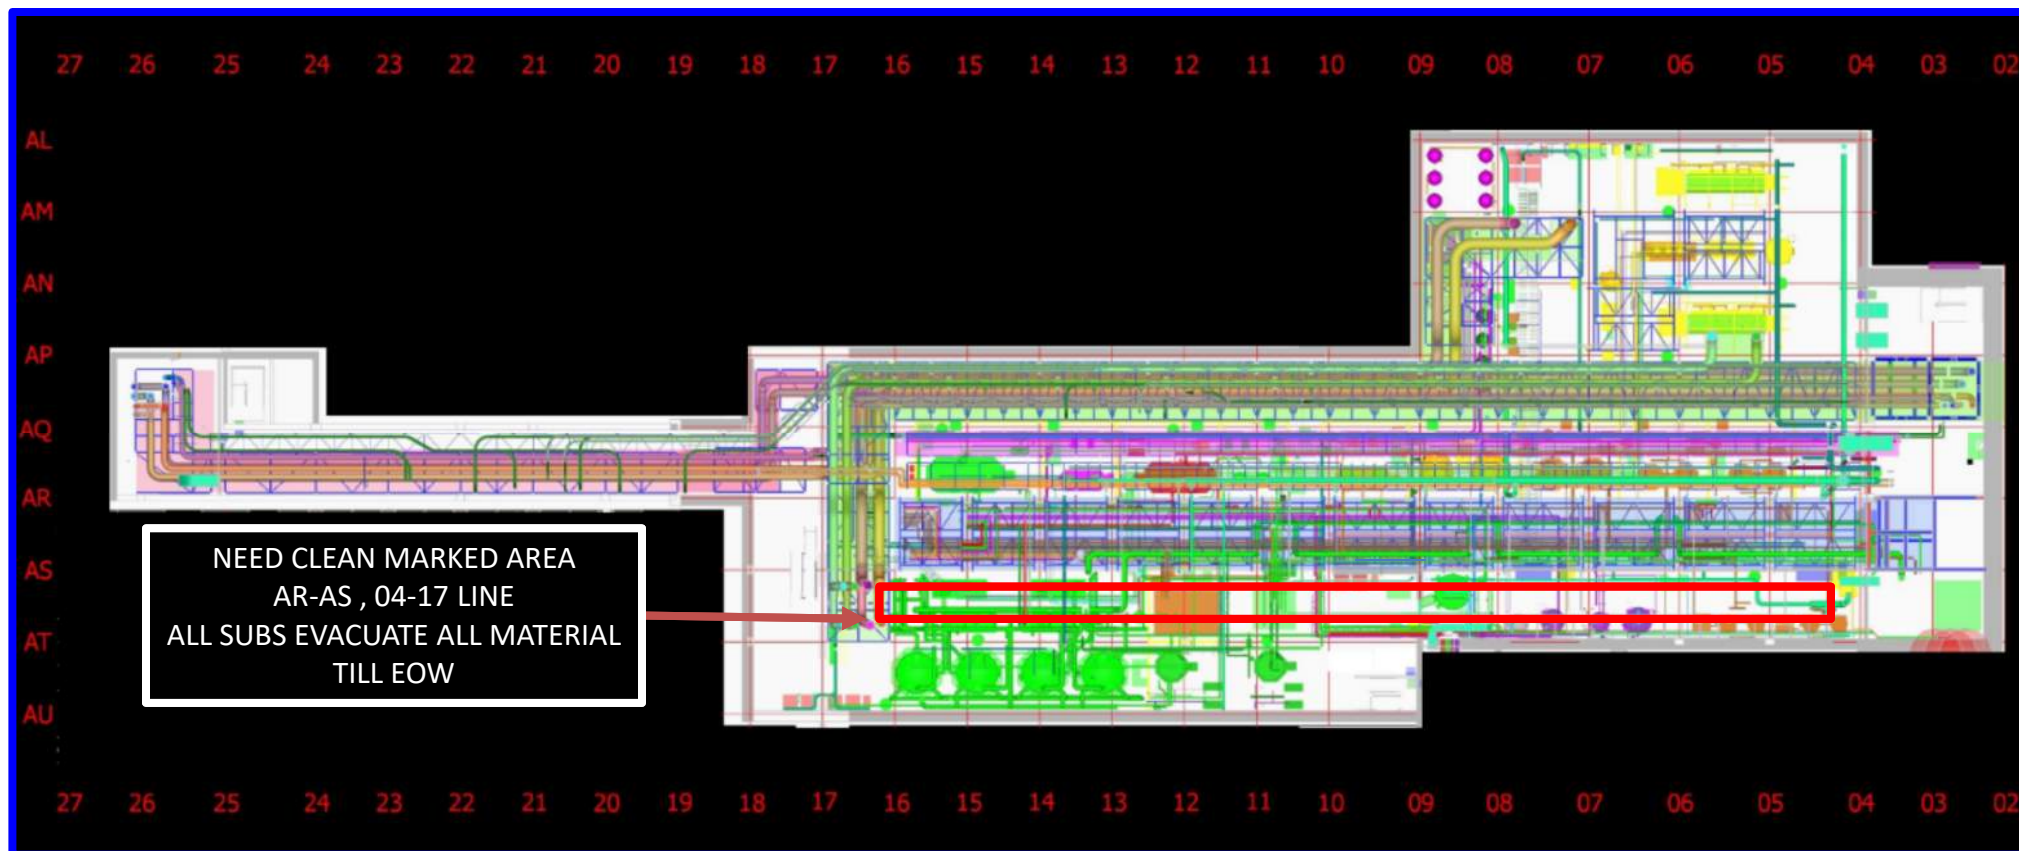

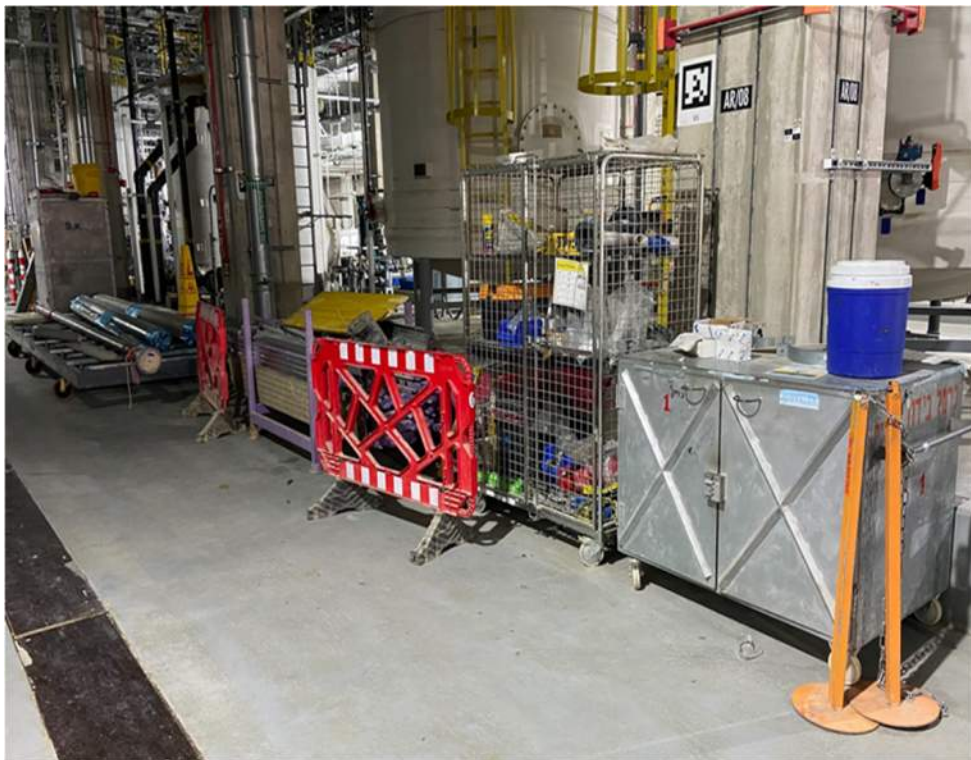





SUBFAB BUILDOUT MOD 1

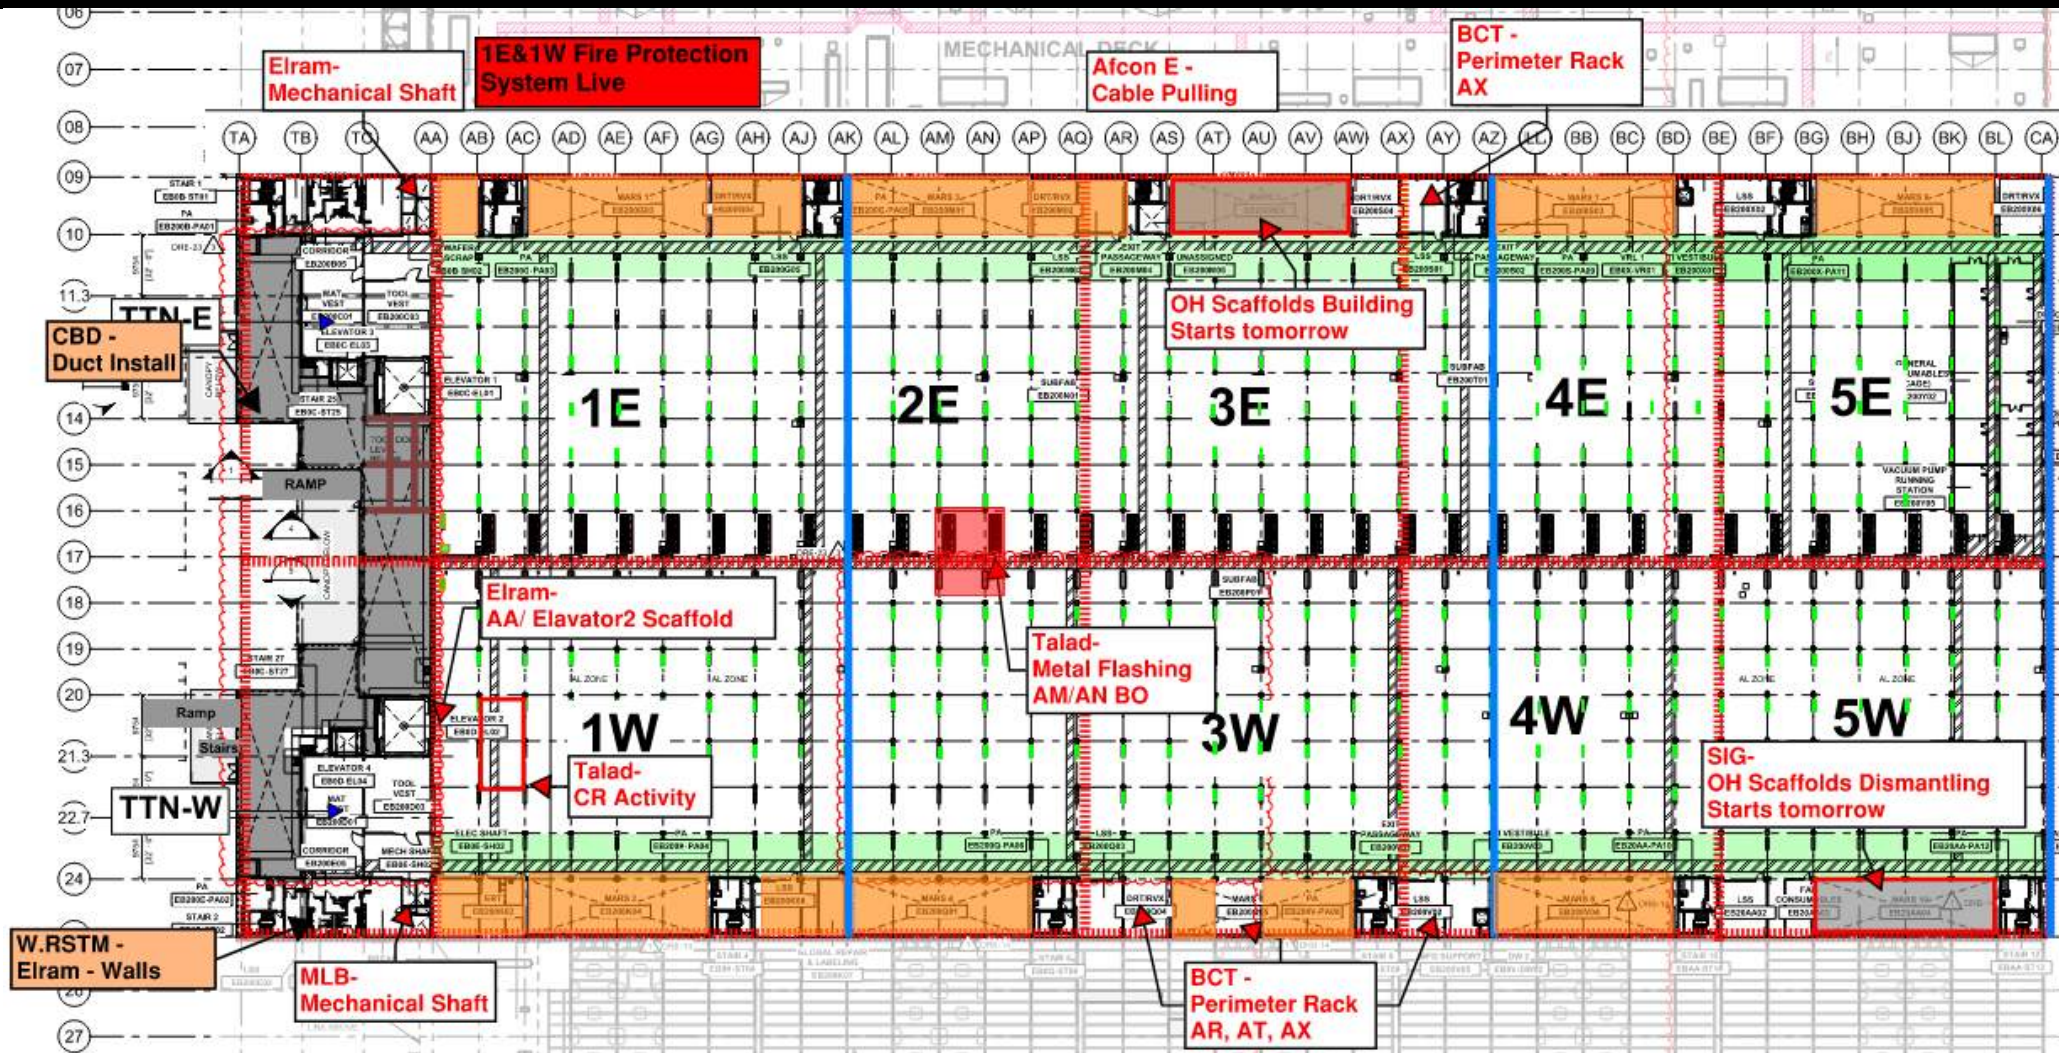


SUBFAB CRC TOPCOAT

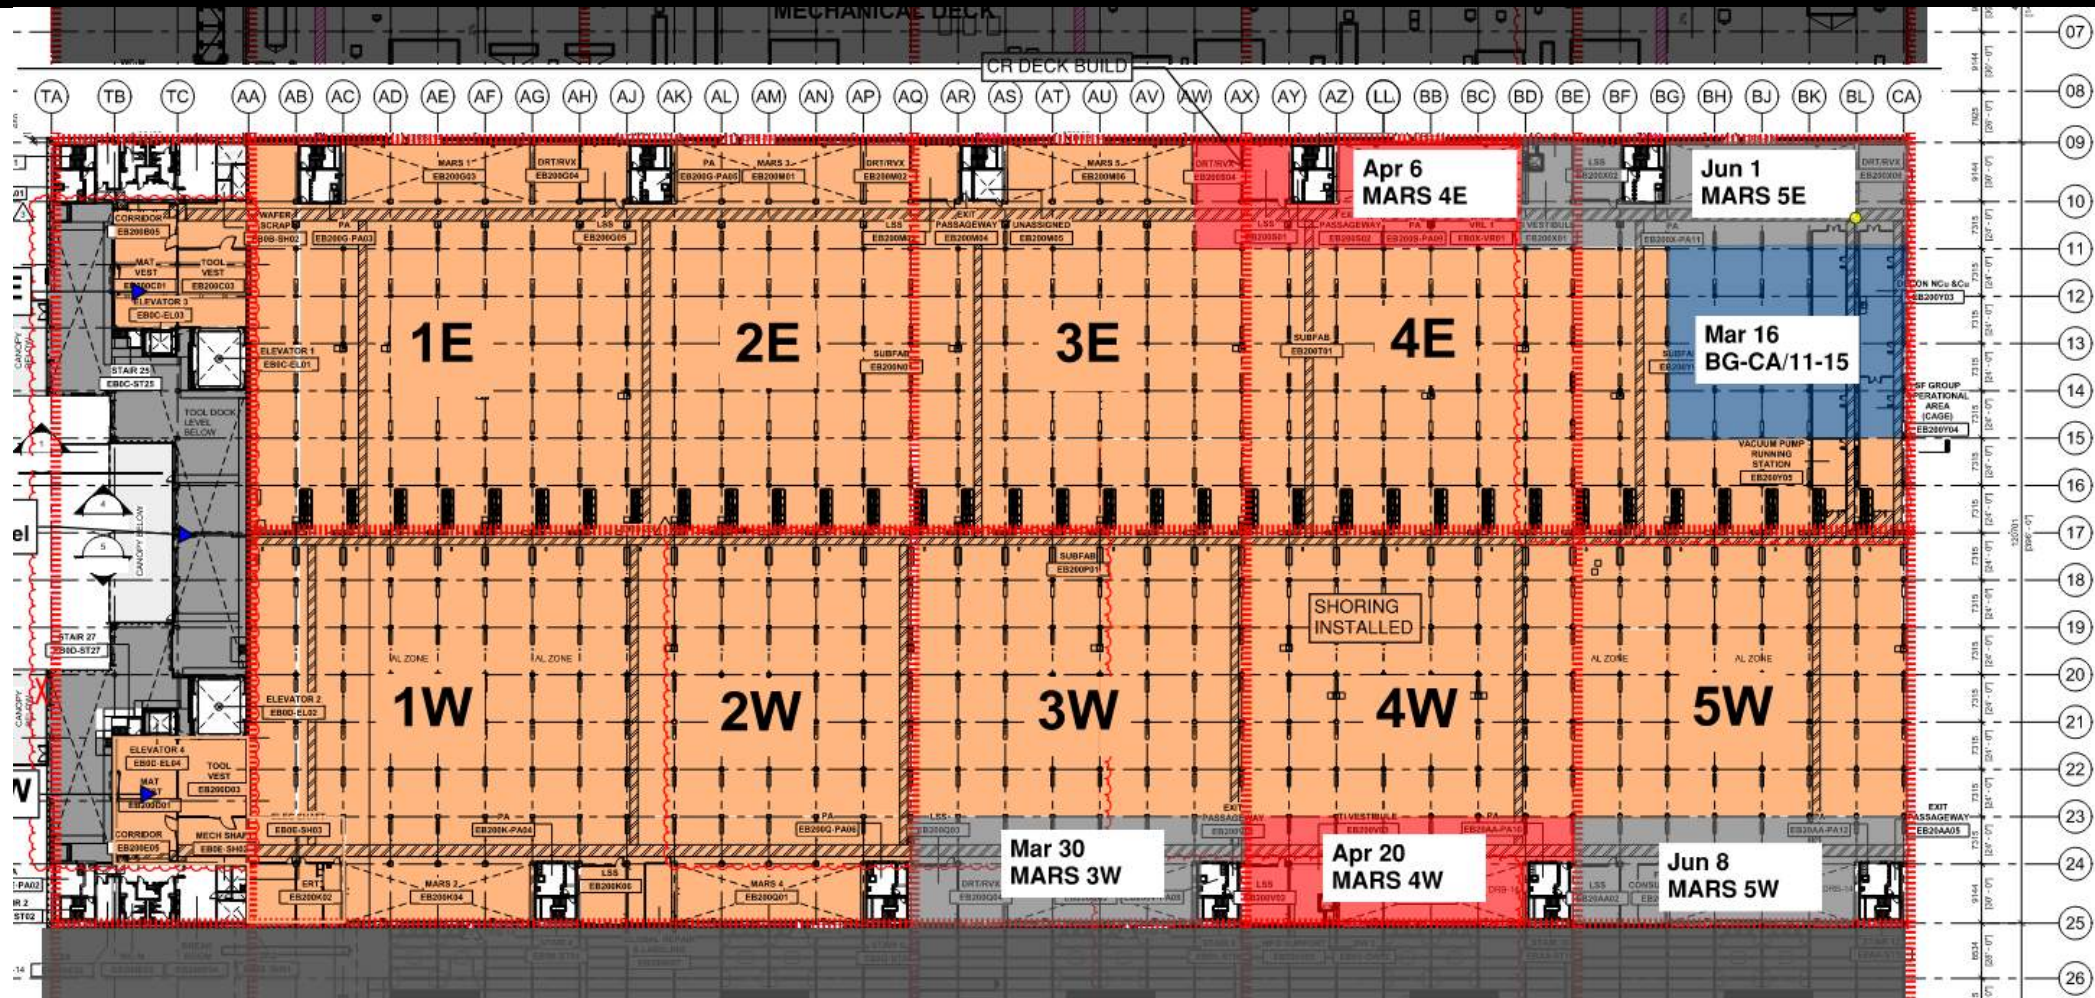

BCT Pressure Test Tomorrow

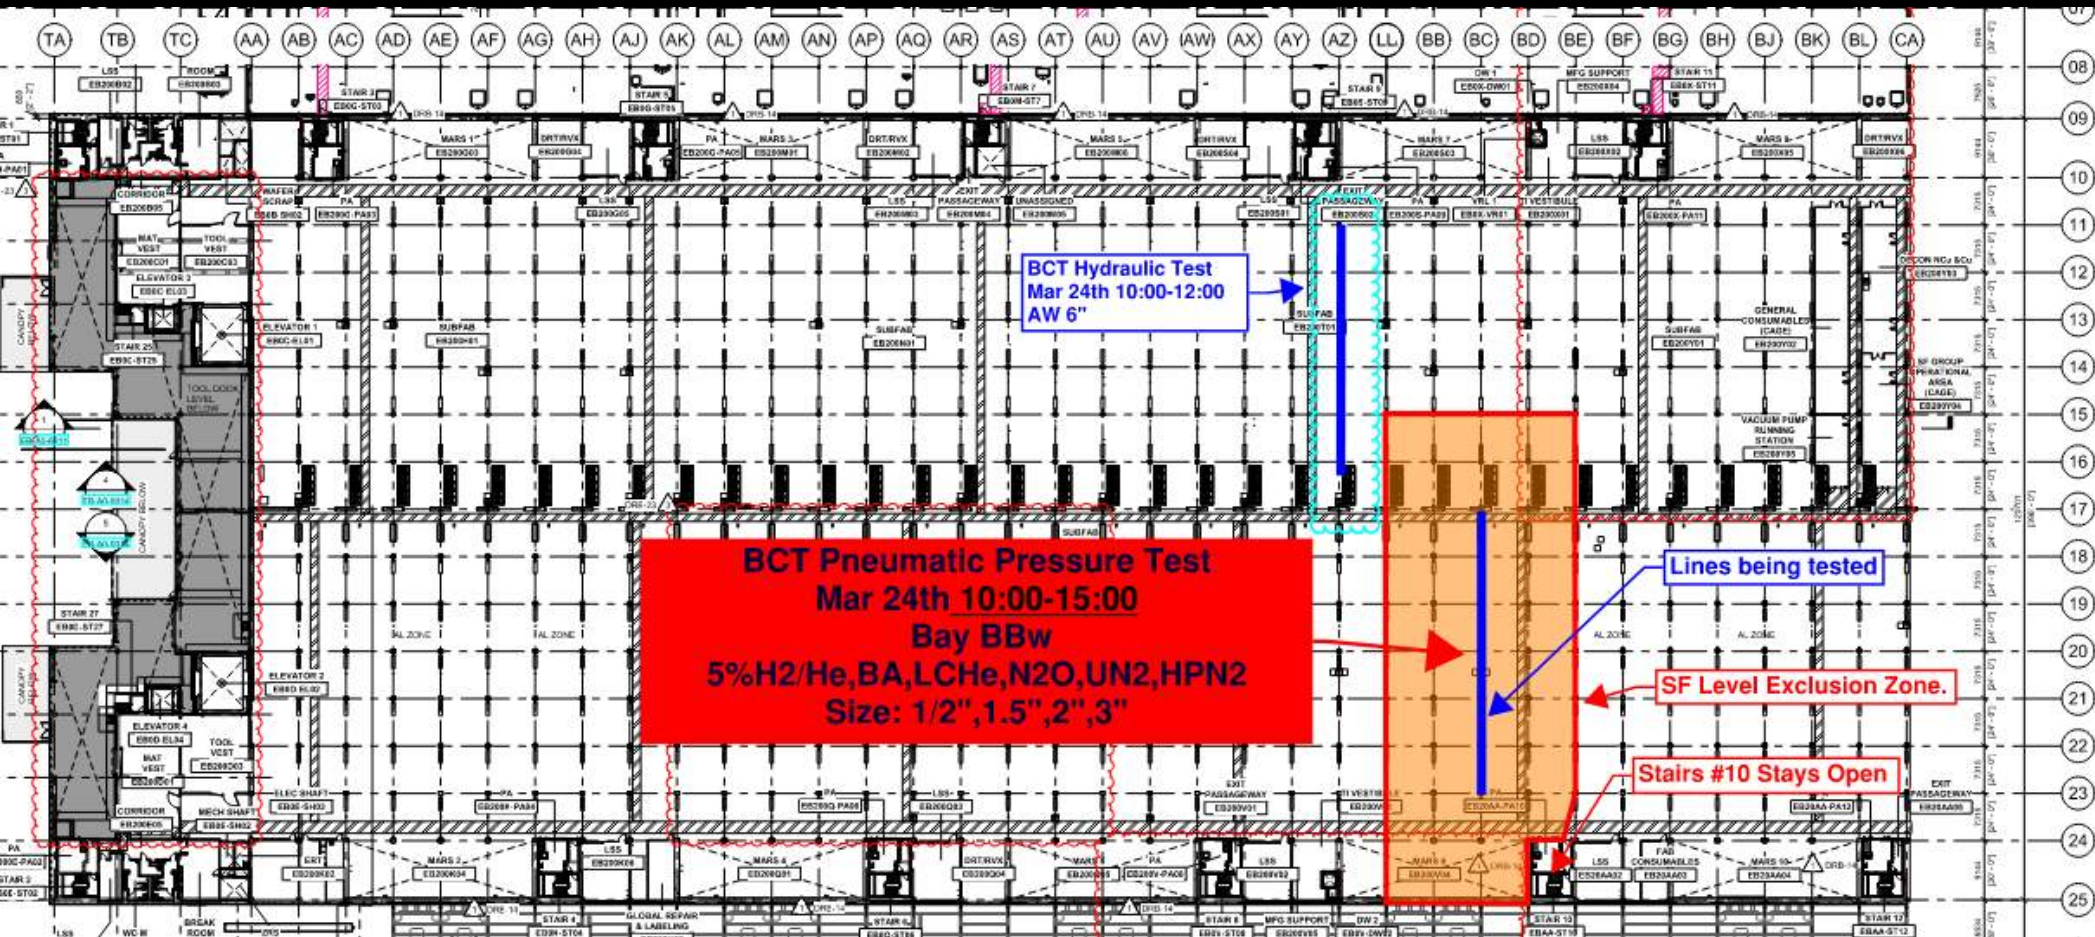

[illegible]

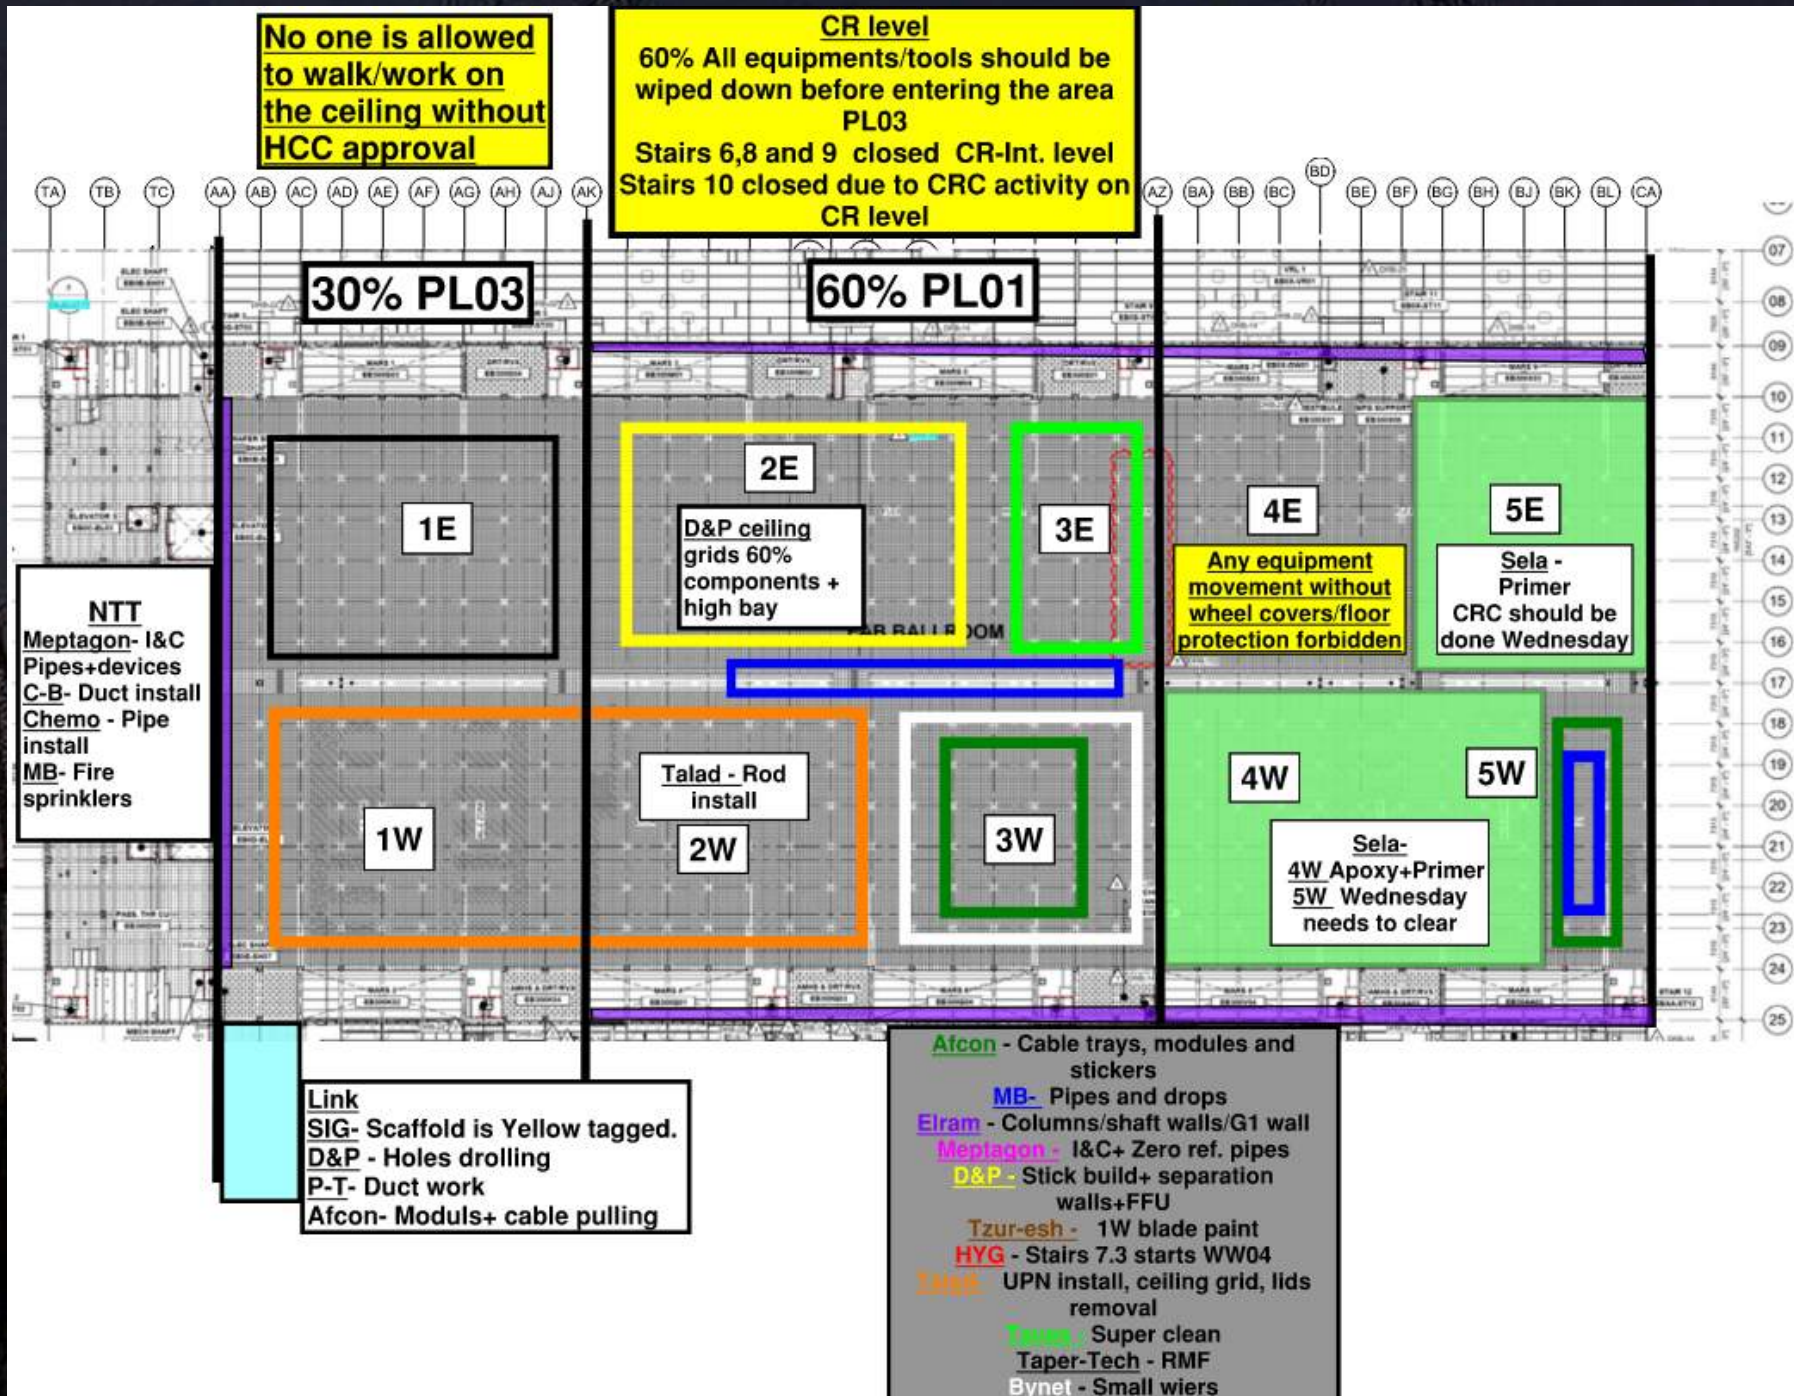



Afcon - Cable trays, modules and stickers

MB - Fire sprinklers

Eiram - Gypsum/G1 wall

Chemo - Skids and pipes

SK - IA pipes

Tzur-esh - Paint+ touch ups

WW - Cat walk

RPC - 4DA/5DA FP

Tavas - Super clean

Bynet - Communication weirs

Megasone - Speakers

Meptagon - I&C

Int. level

60% All equipments/tools should be wiped down before entering the area PL03

Electric shut down

TTNE - between 6pm and 7pm.

Affects one lighting circuit

AD-13 - between 7pm and 8pm.

No effect on lighting

AE-13 between 8pm and 9pm.

Affects one lighting circuit

30%

60%

NETT

Chemo - Racks+pipes ongoing

Megasone - Small wires+Speakers

RPC - FP rack/girts

NWTT

Chemo - Racks


MB - FS install



AFA - Vesda


RPC - started FP racks

WW/SN - Handrail install
Eiram - G1 metal sheet


TMT - Penetrations for
Afcon, **D&P**, **Talad** and
MB

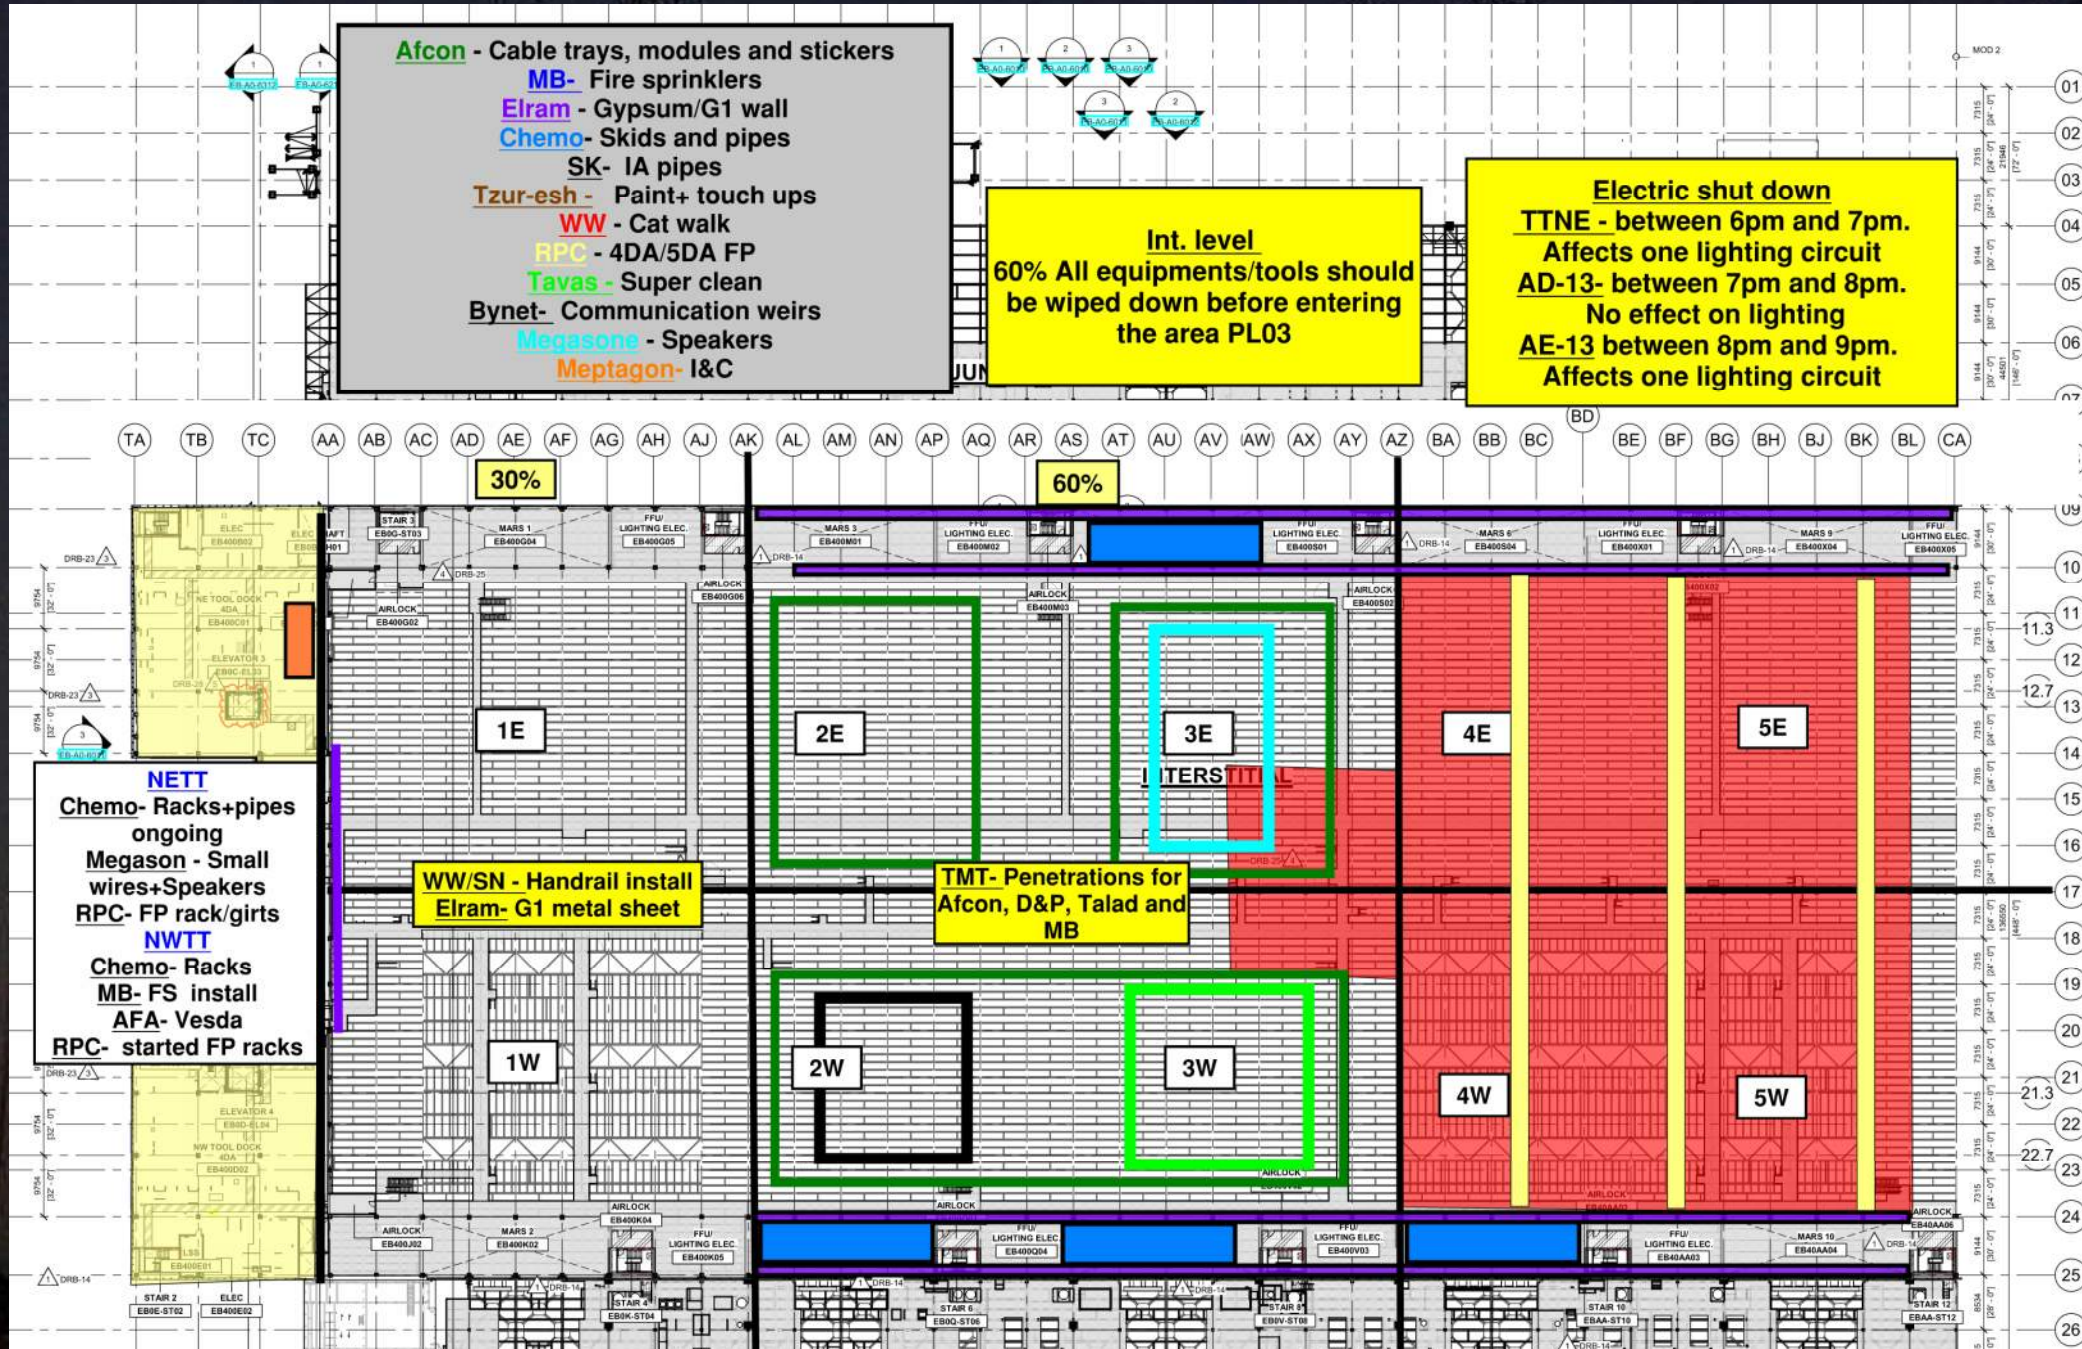

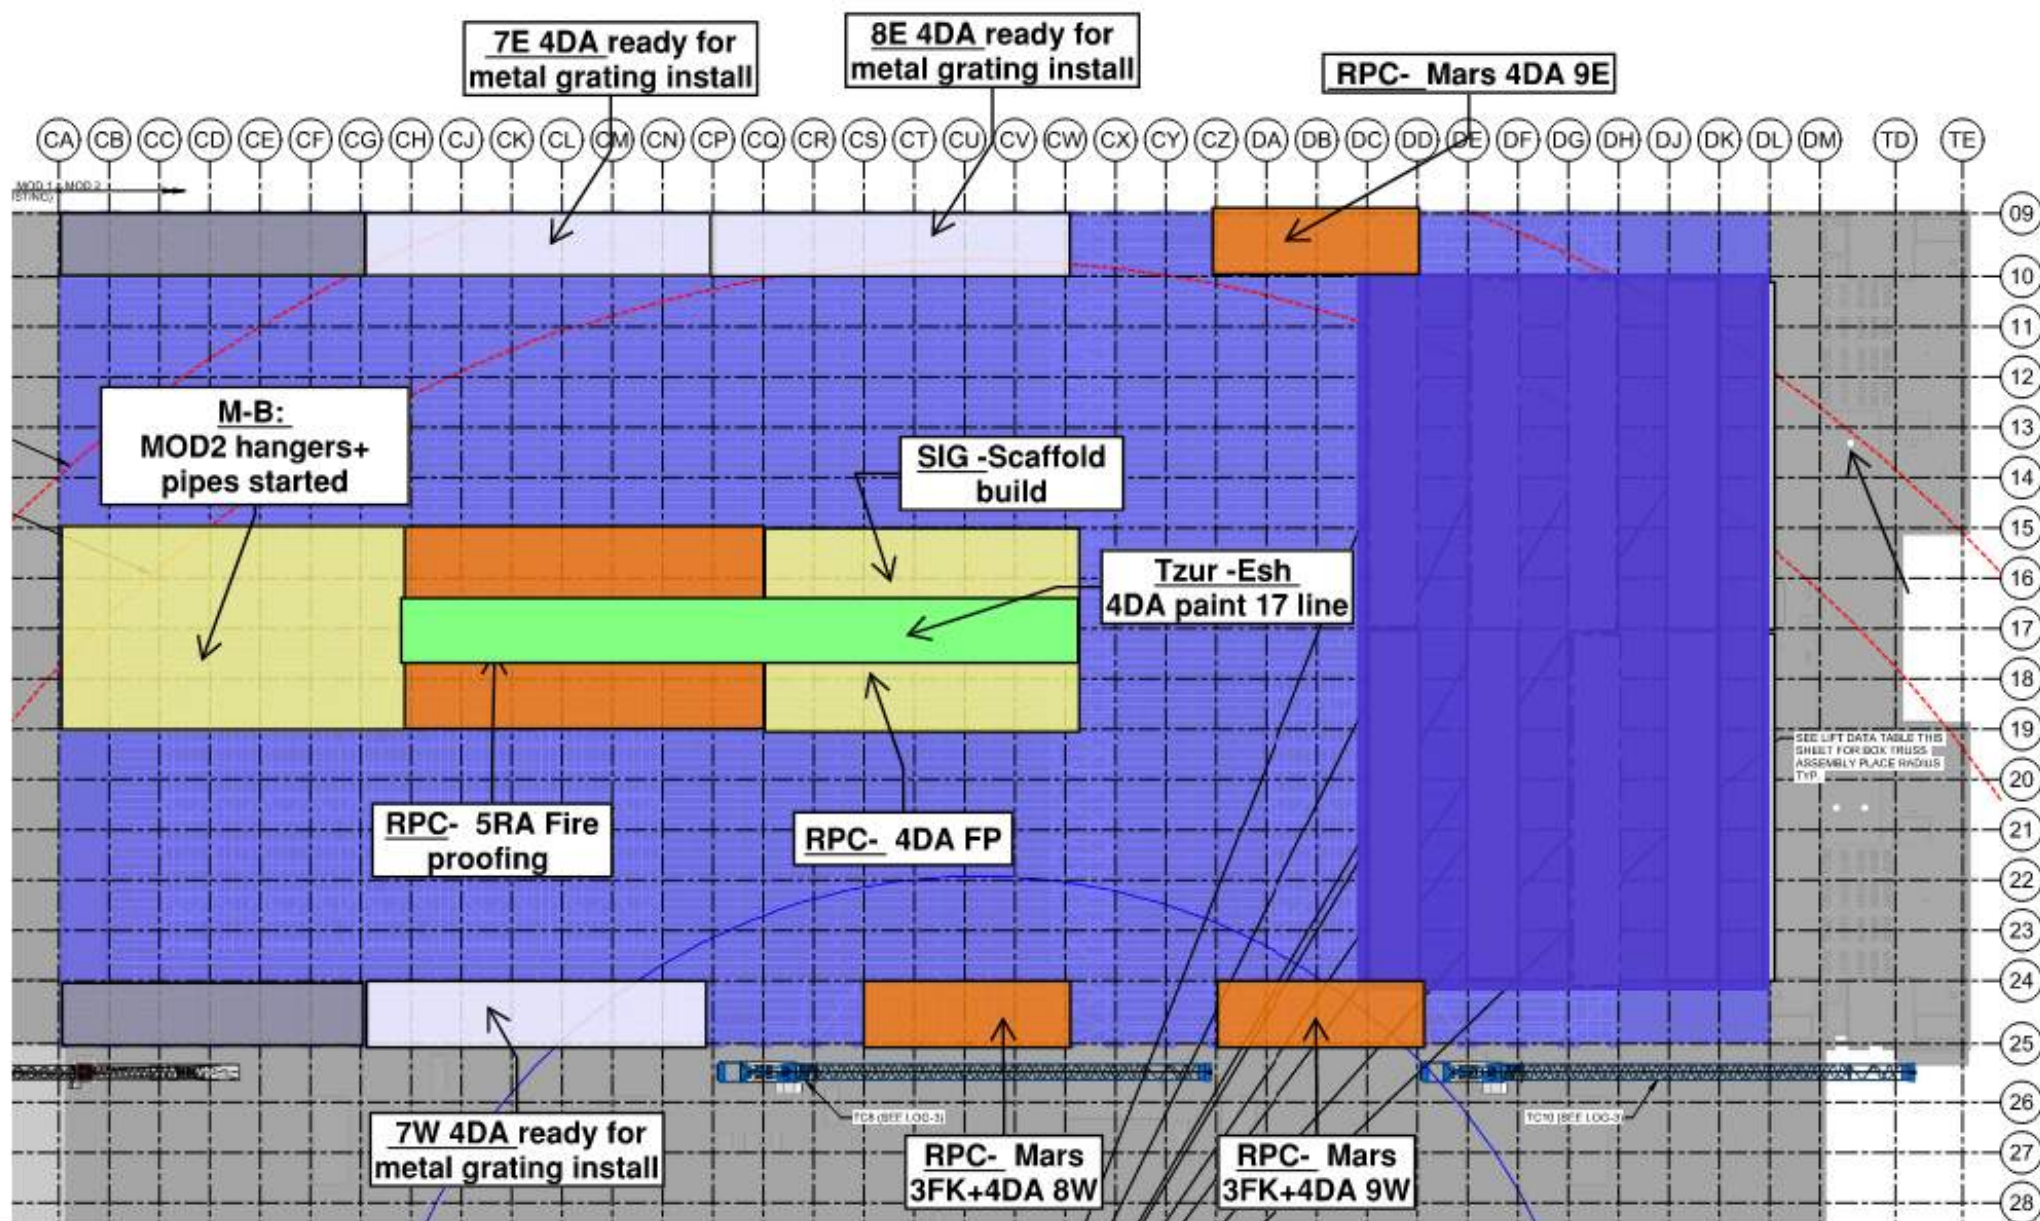


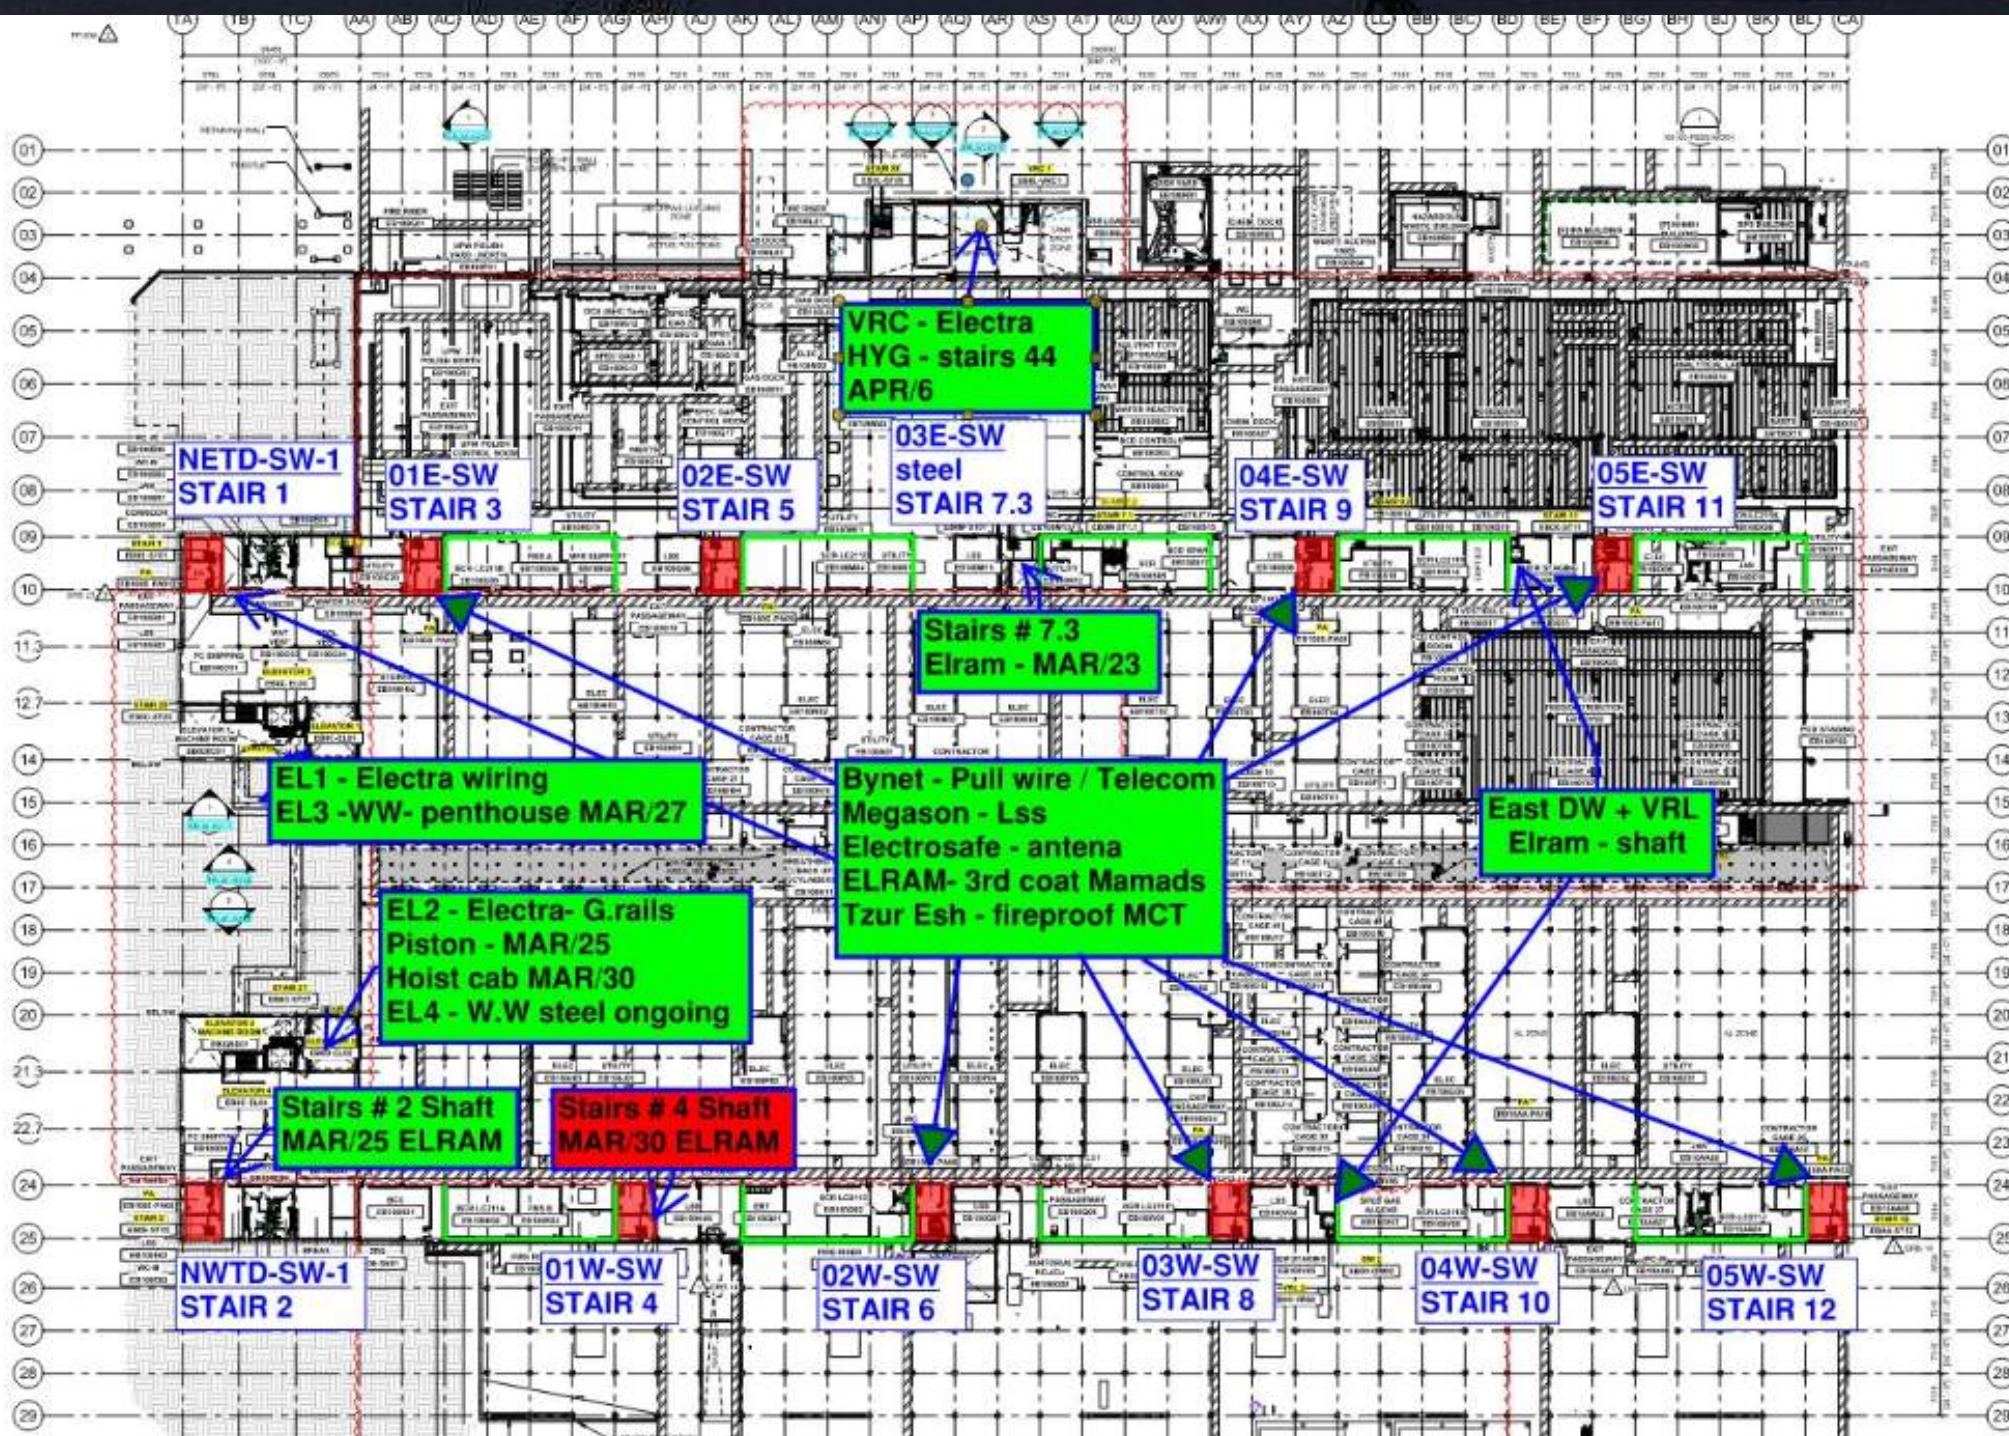

Siding Penetration Request Form

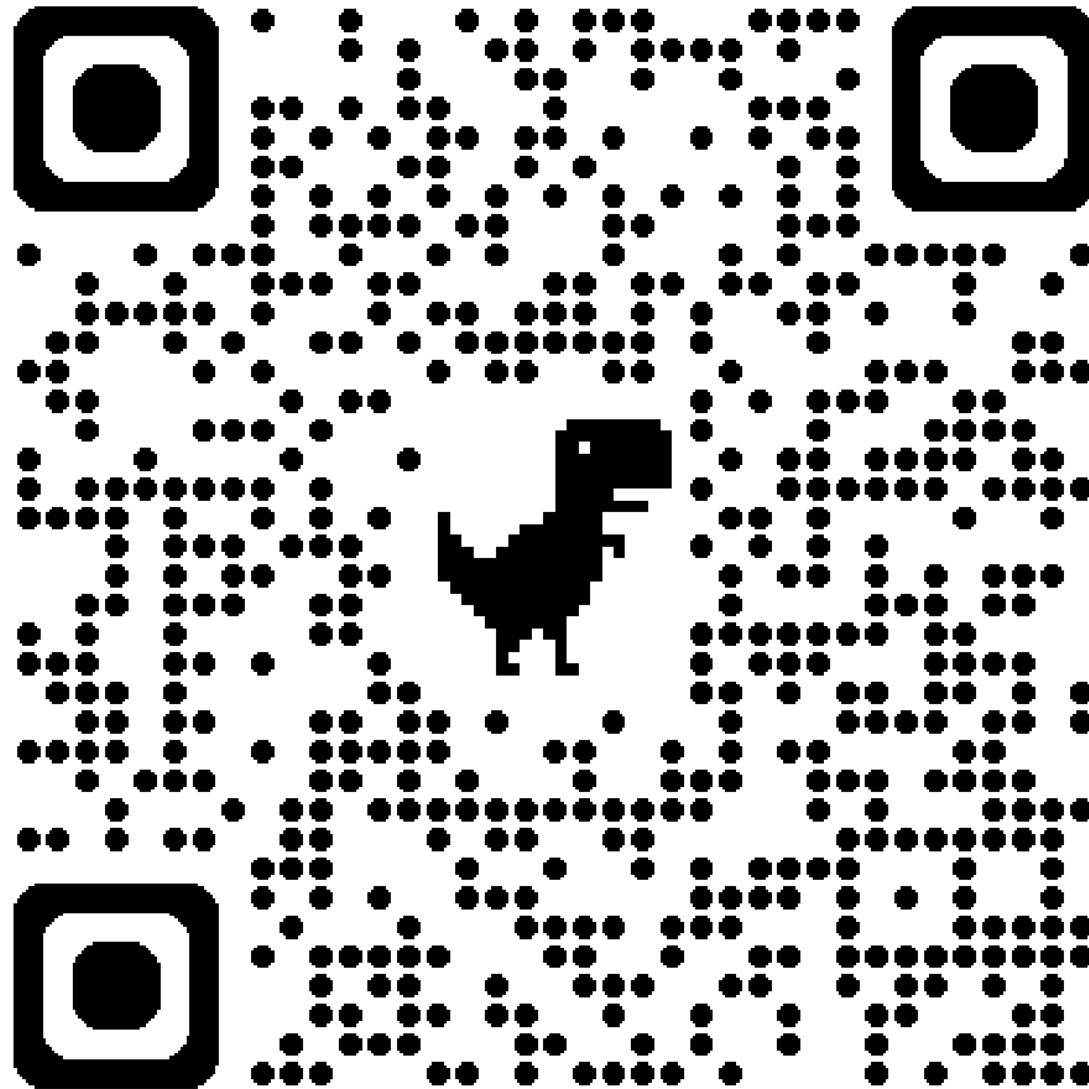


Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

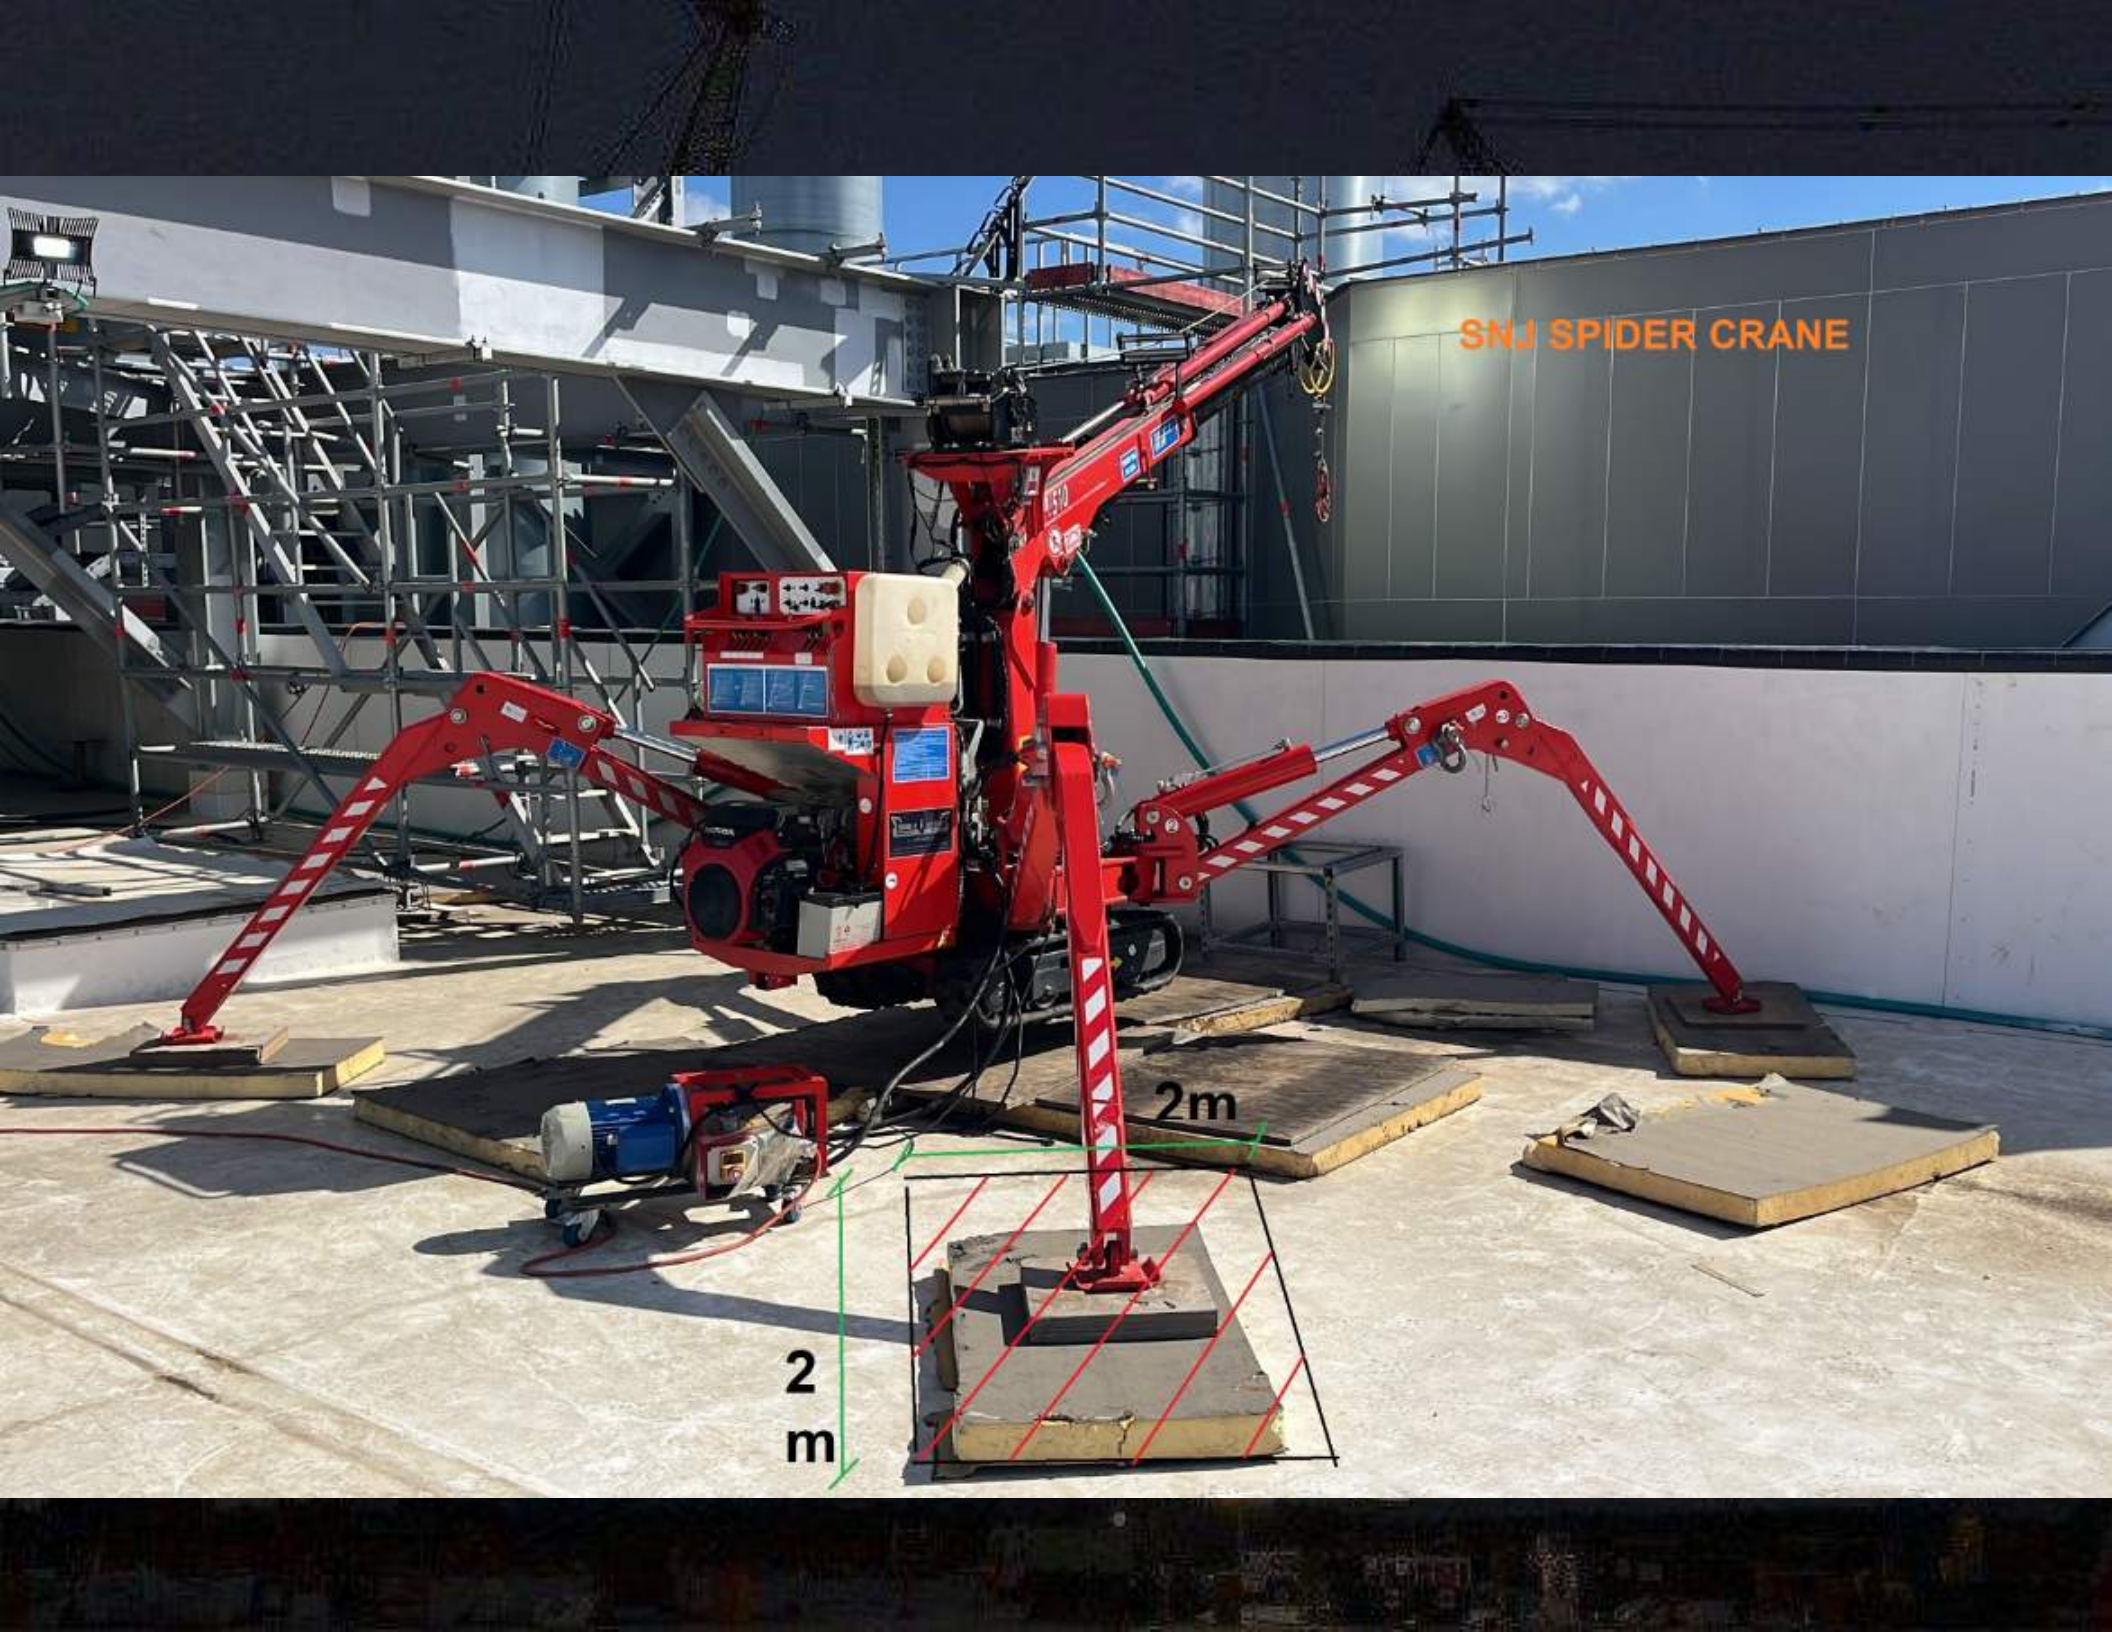

SNJ SPIDER CRANE

2m

2
m

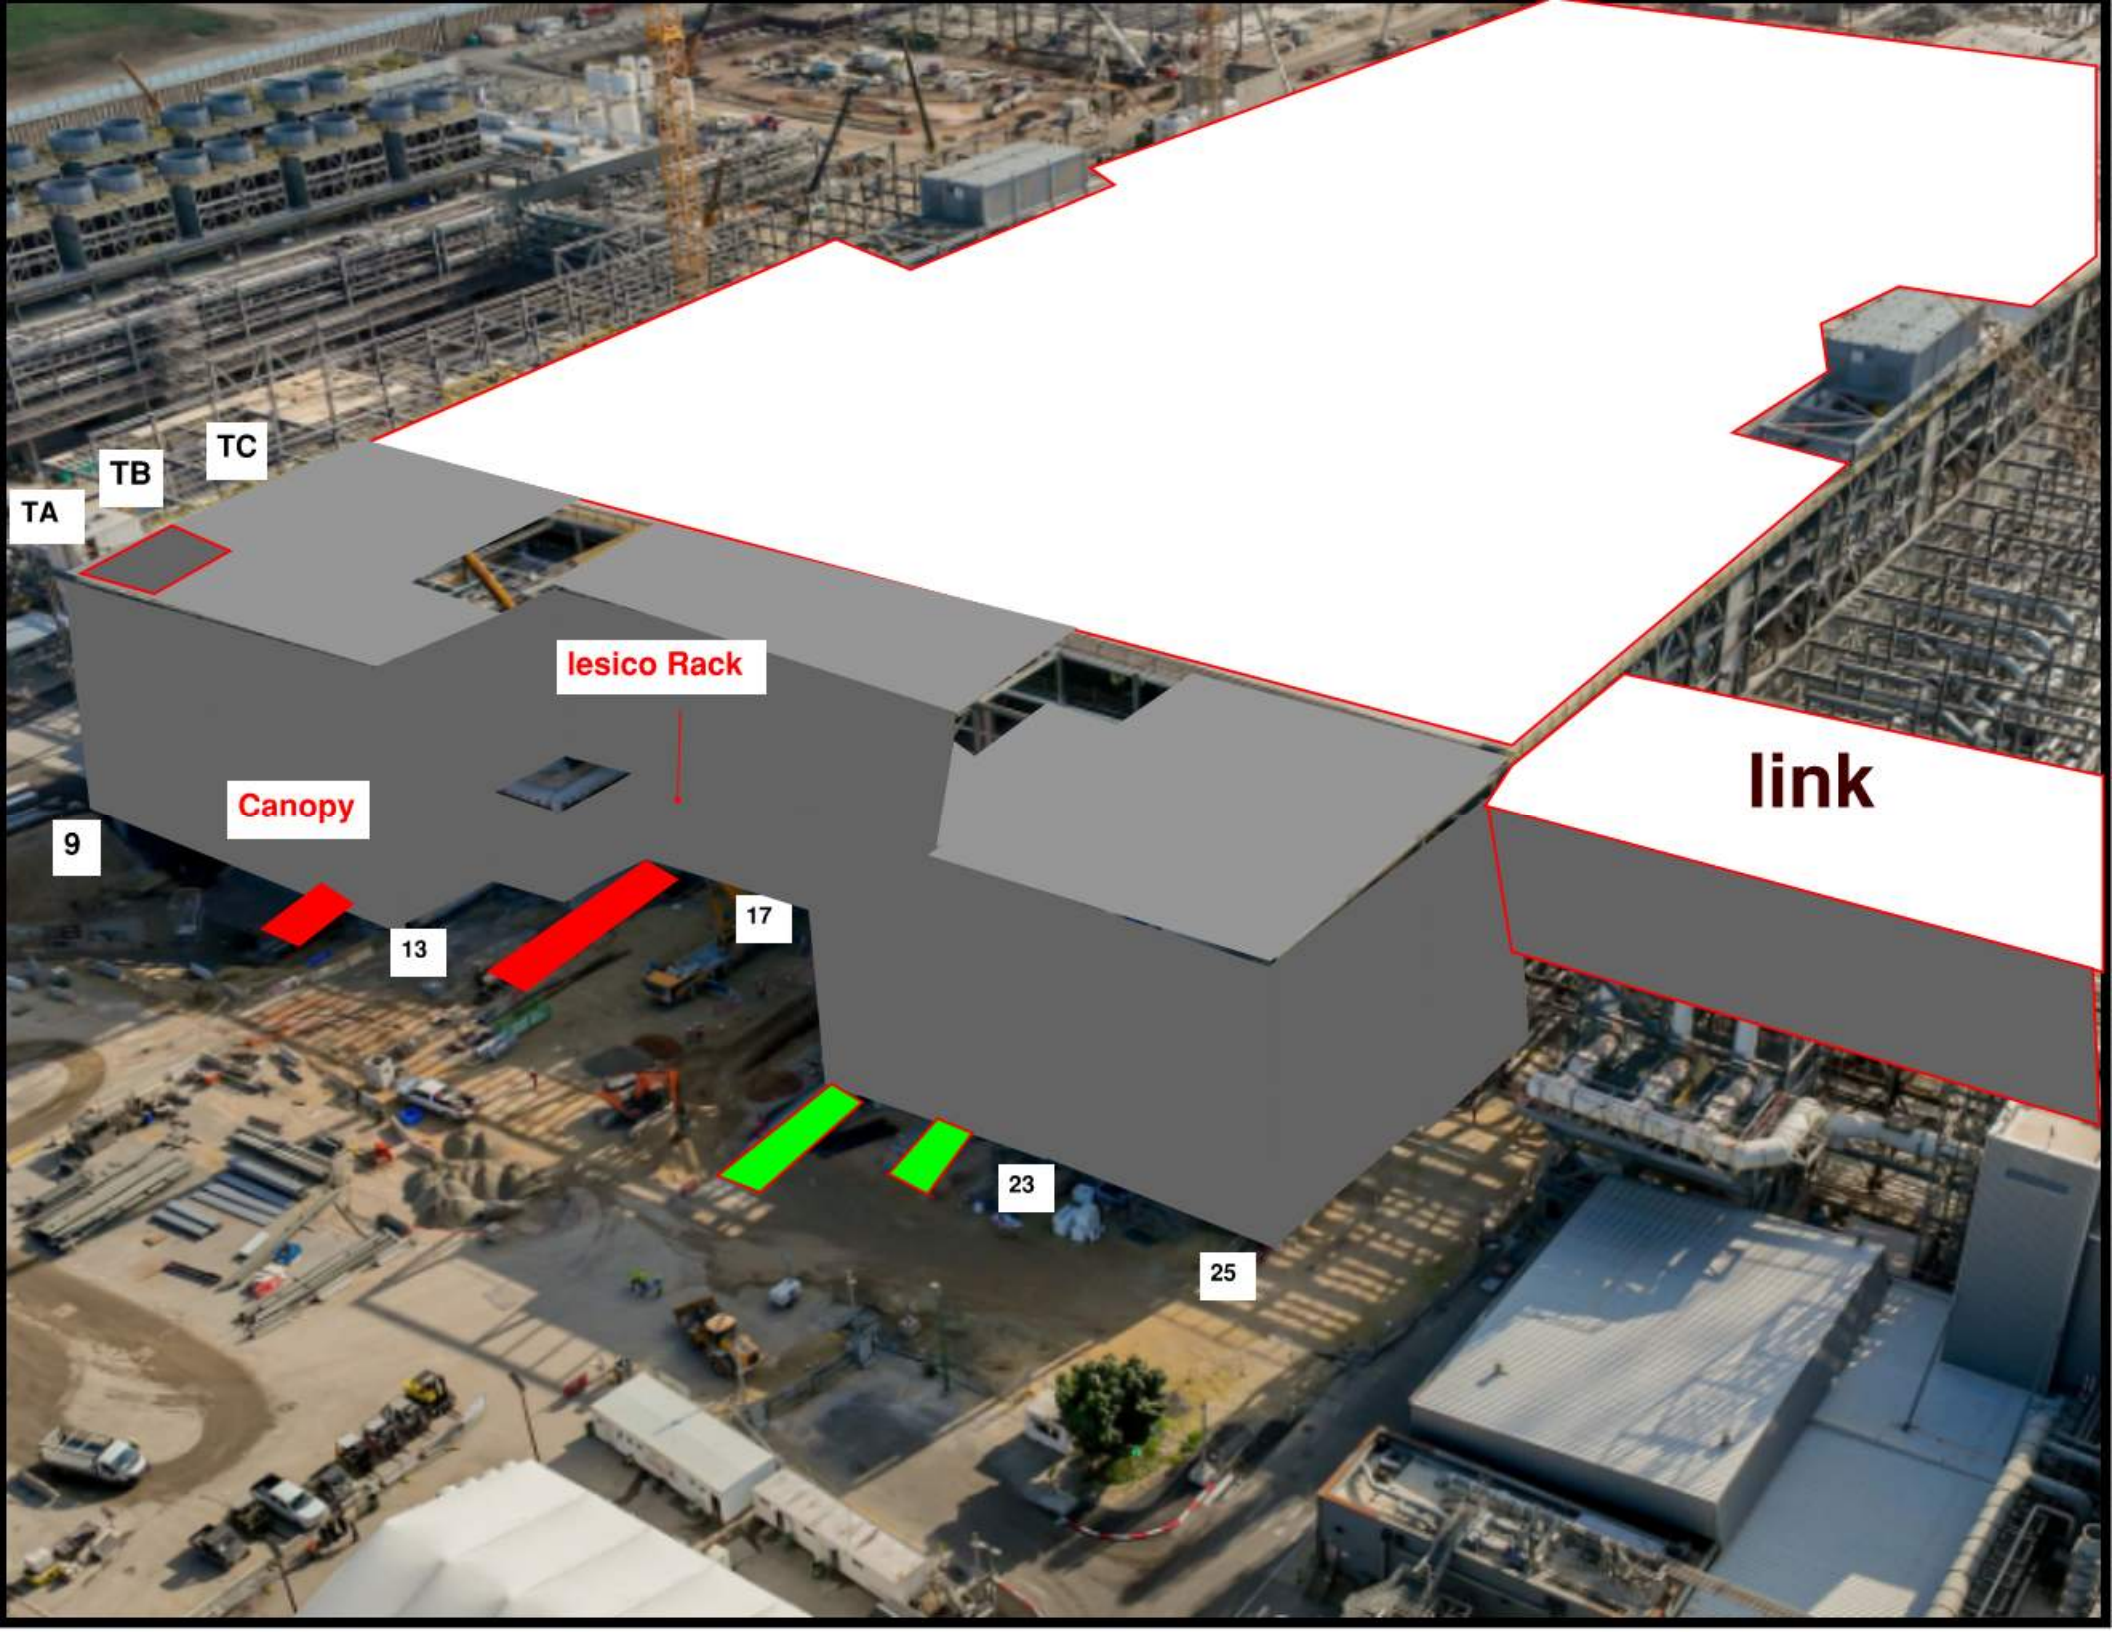

TA
TB
TC

lesico Rack

Canopy

link

9

13

17

23

25



MOD 2 EASTSIDE GIRTS/SIDING

2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

MOD 2 WESTSIDE GIRTS/SIDING

READY FOR GIRTS 

INSTALLING GIRTS 

READY FOR PANELS 


PANELS INSTALLED 



PSSS.1


Utility Level
1YA

PSSS Roof
2SA

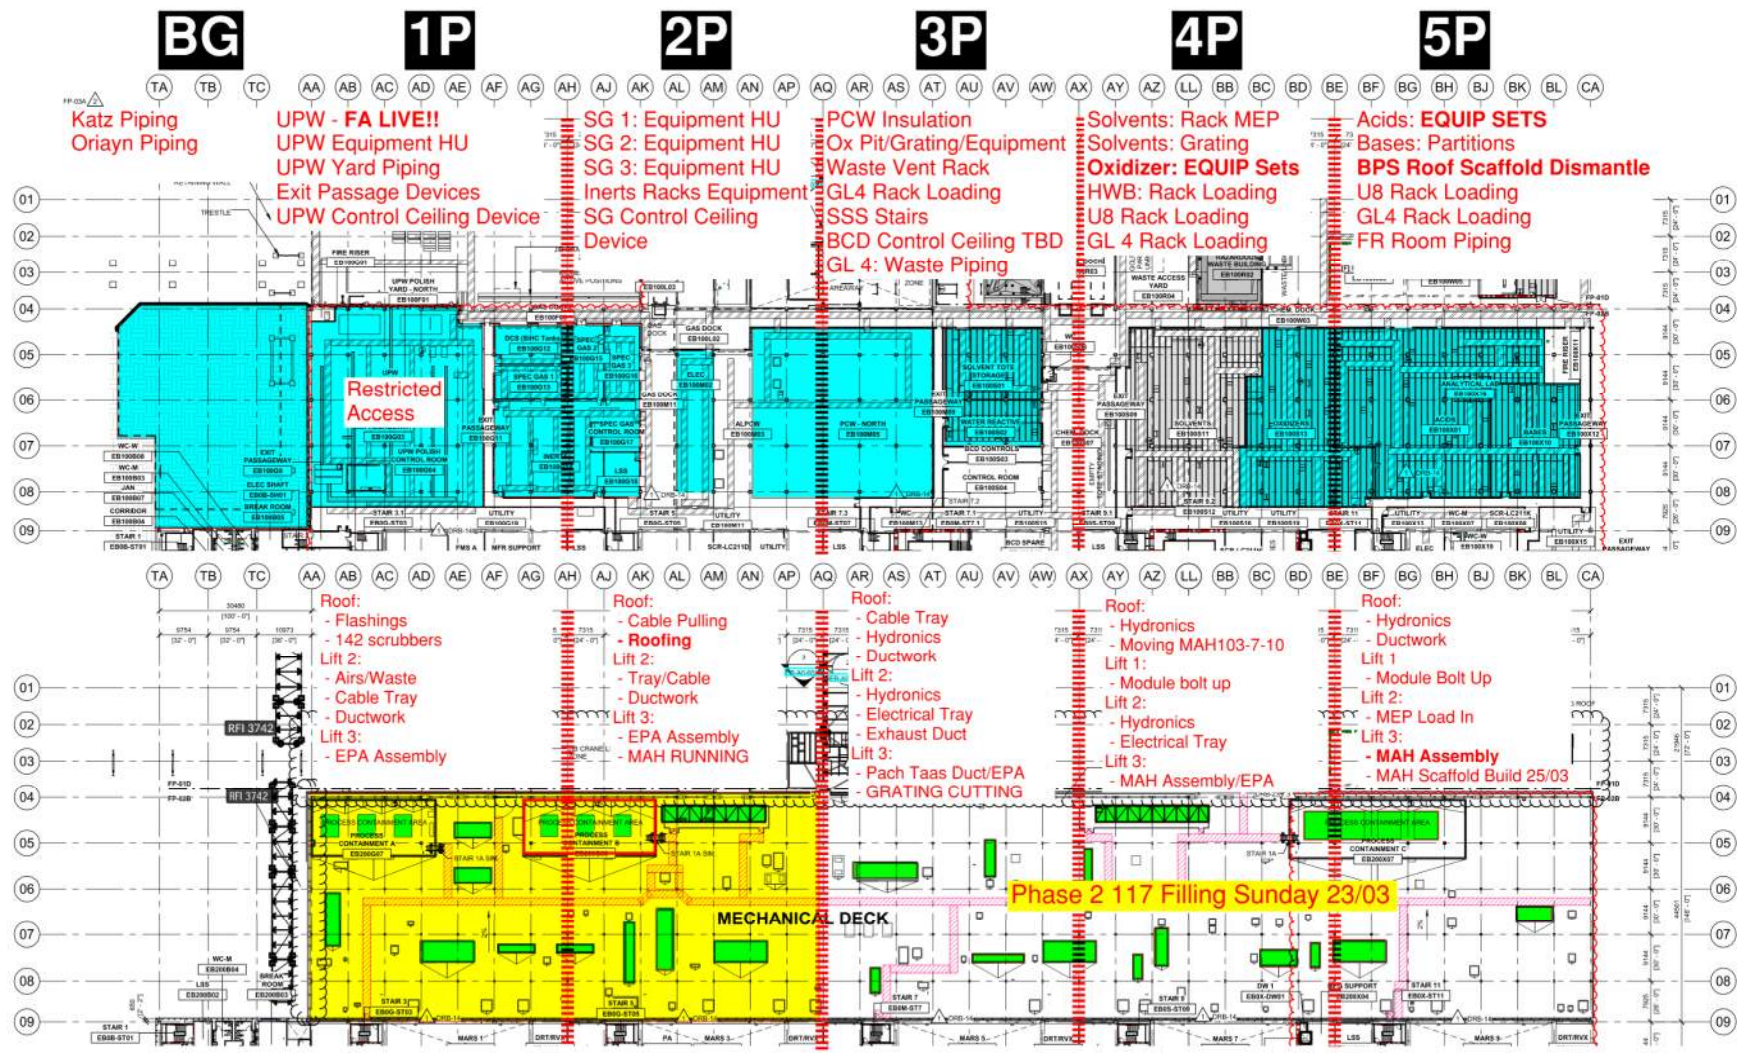


PSSS.2

Utility Level 1YA

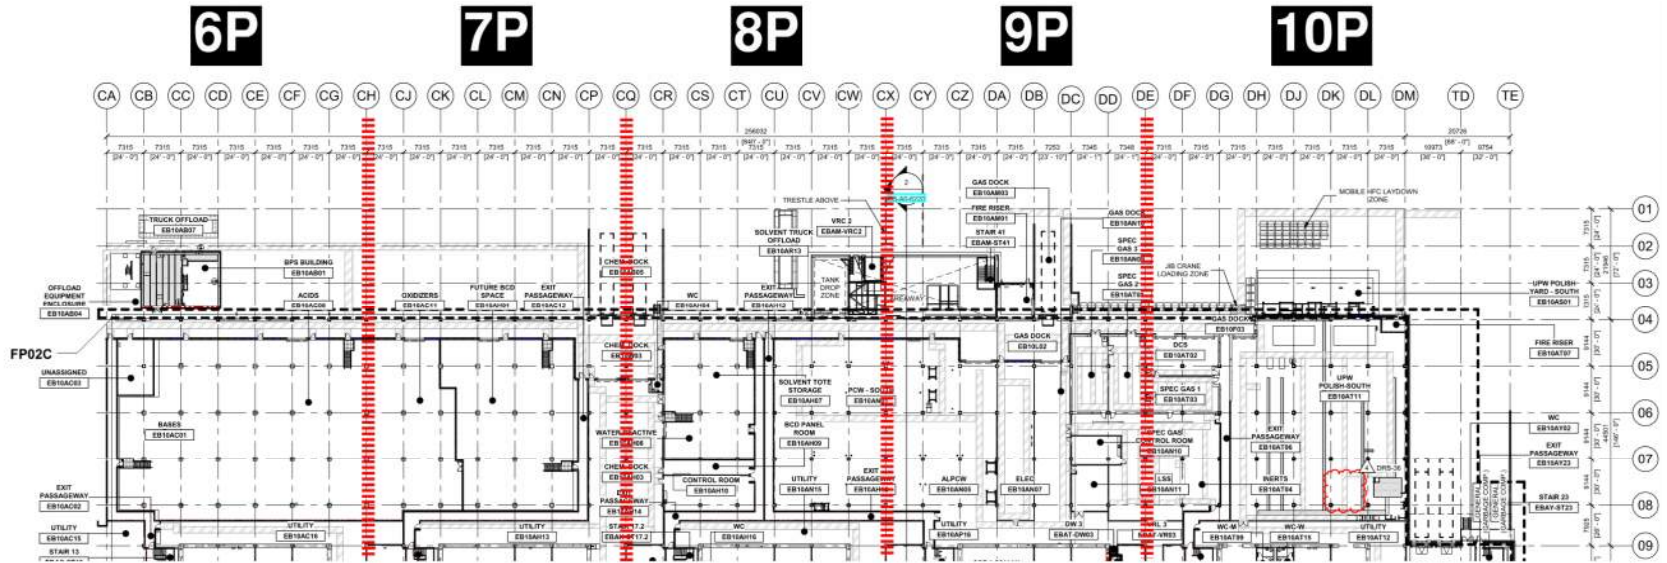


PSSS Roof
2SA

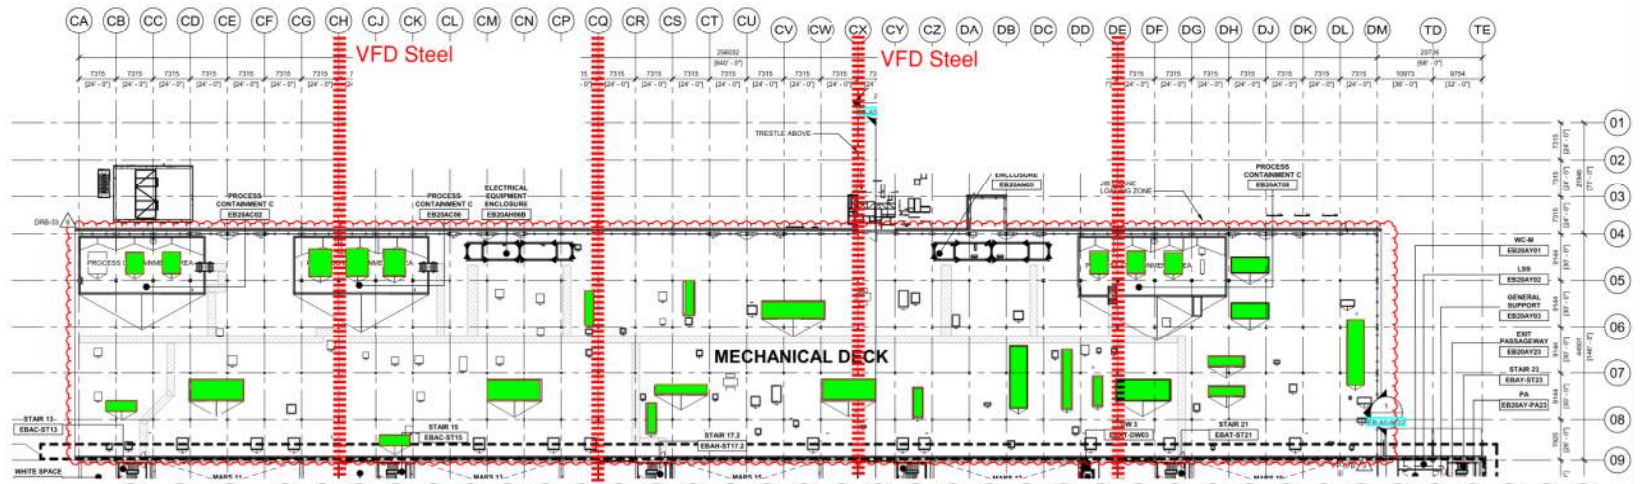


PSSS Pressure Testing

Utility Level
1YA

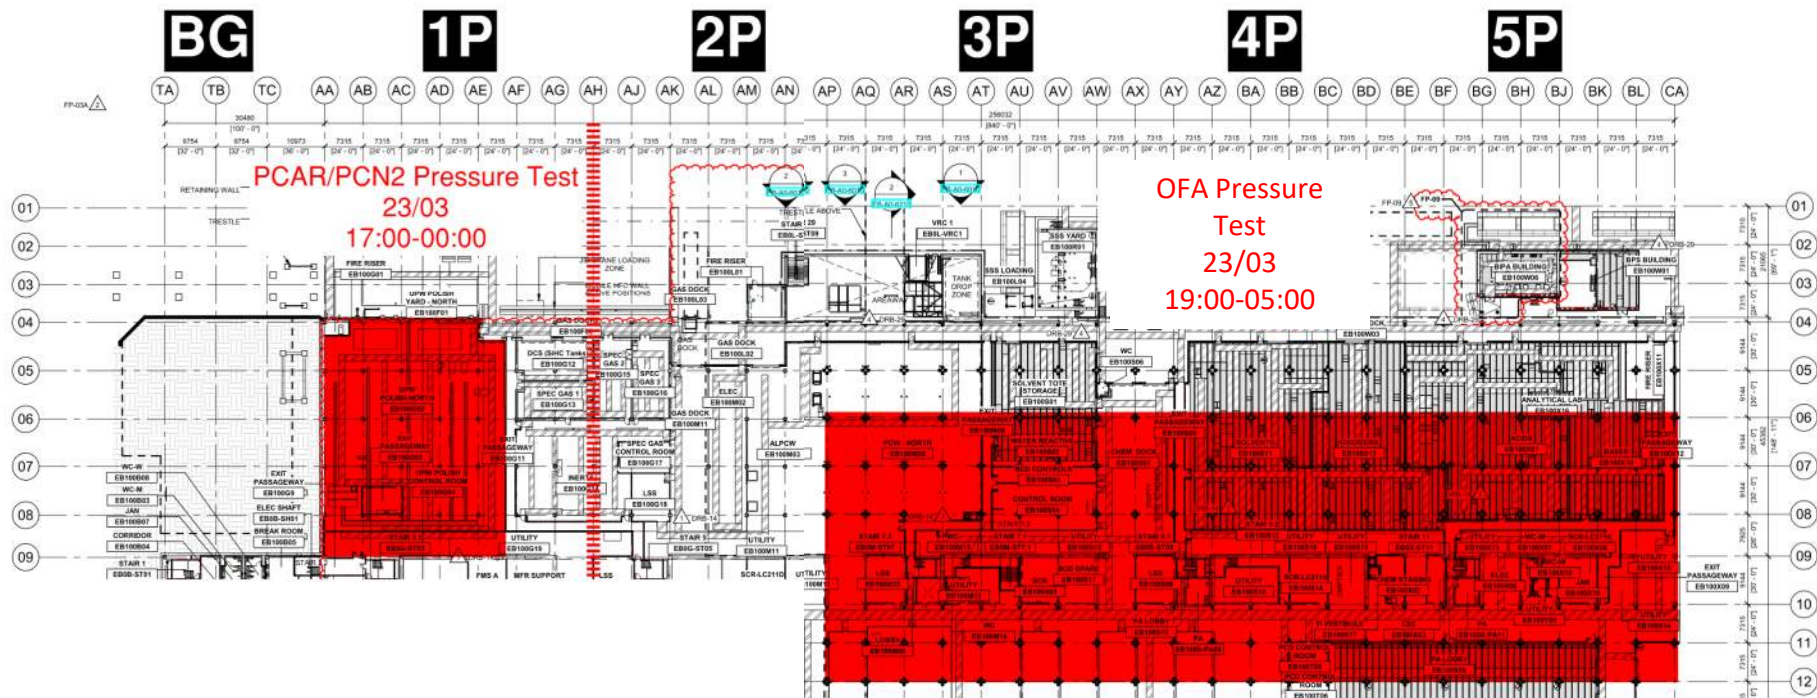


BGY GN2 Bursting Zone WW13

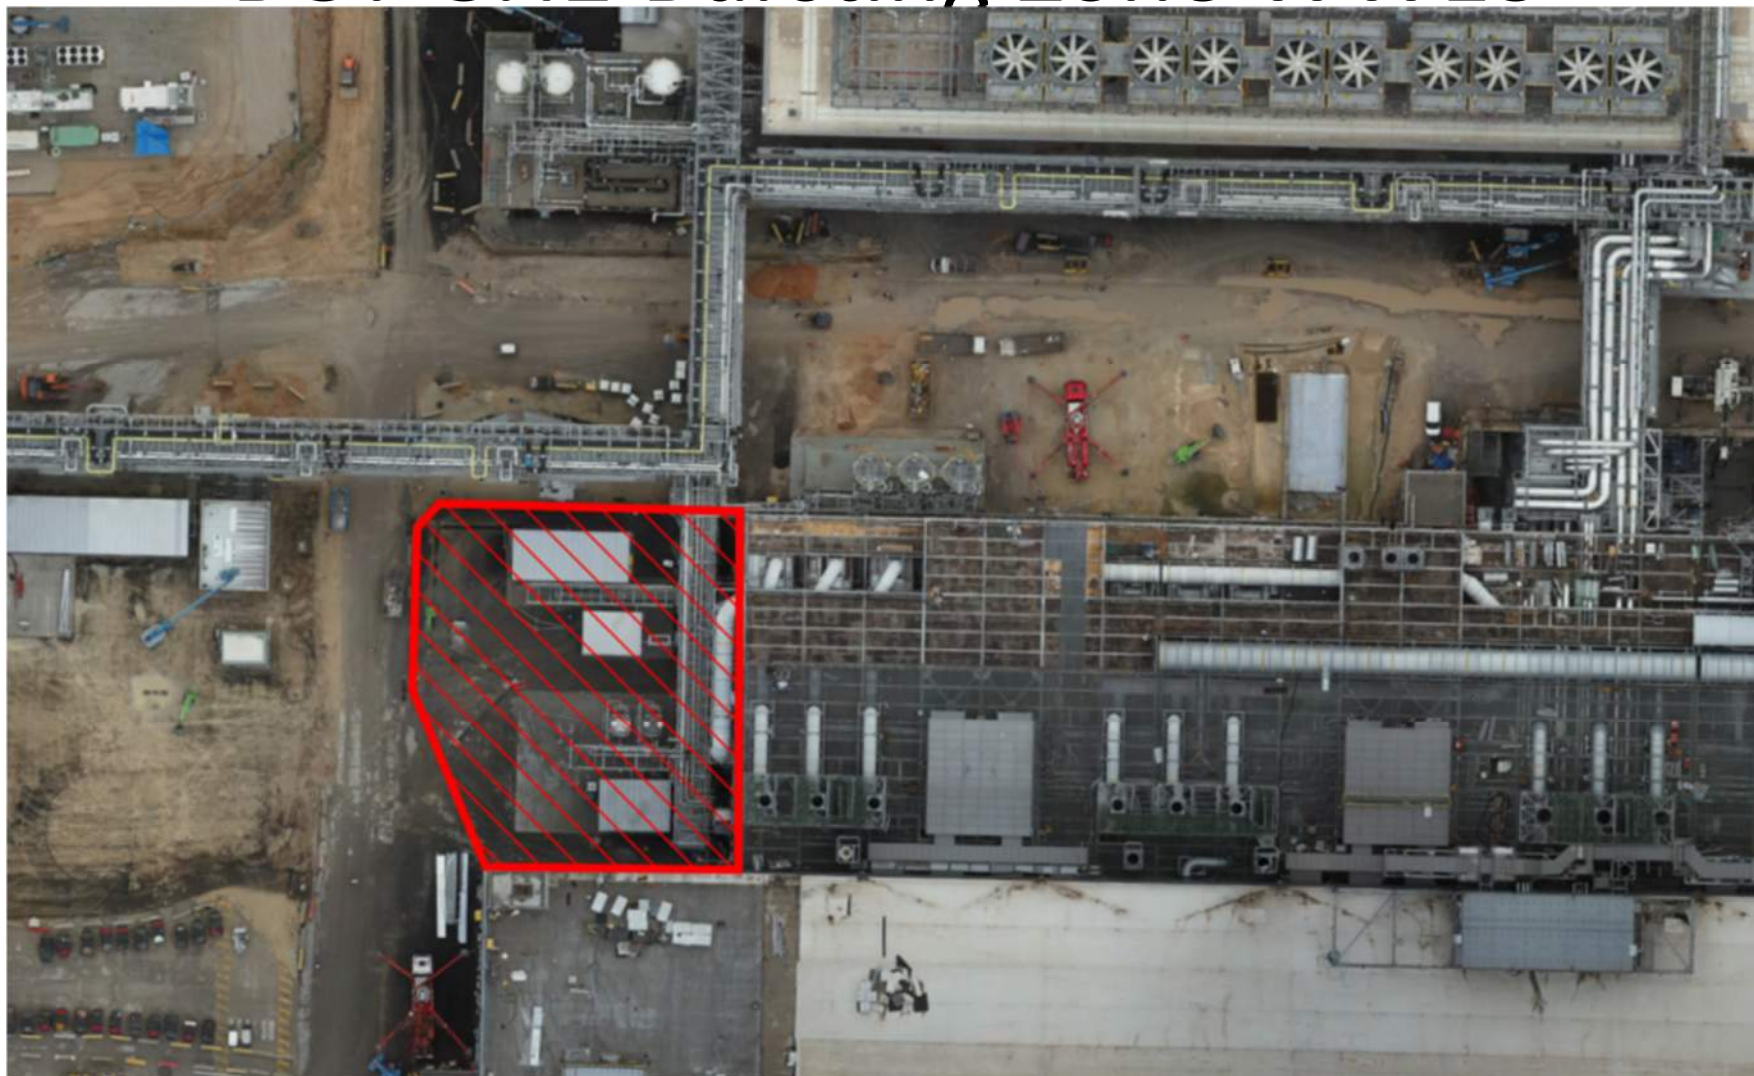




WJG – UL

	*Pach Taas - installation of modules in west SUT. * Pach Taas - completion of spools and lindapters on UPN 138	*Afcon - Installation of lighting and cable pulling	* Carmel Bidud - installation of air ducts	* BCT - installation of permanent stairs to AHU * Afcon - cacle pulling from roof to VFD and UL
--	--	---	--	---

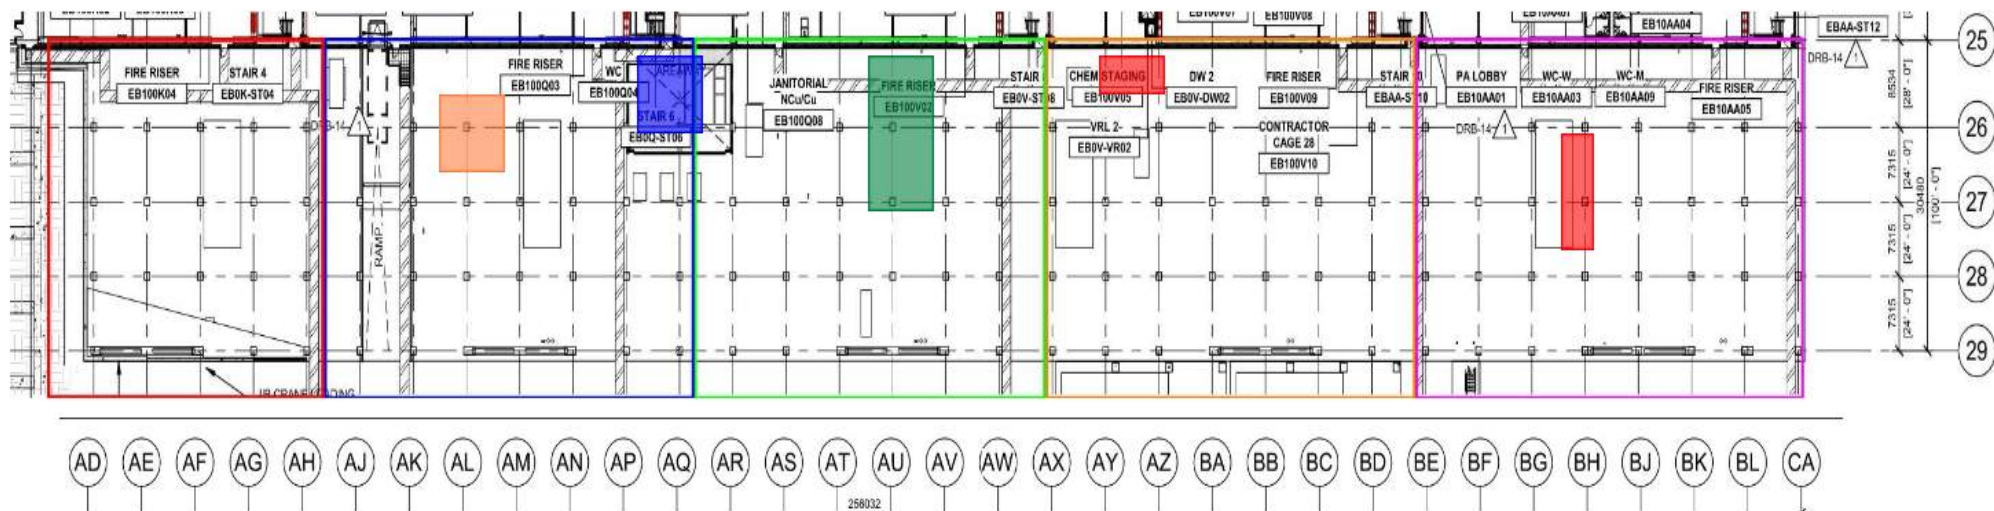

	* Chemo - performing flushing to UPN 113 MARS pipes		*SN - installing handrails on lift 1	* Carmel Bidud - MAH scaffold IS green tagged and ready to perform connections to MAH * Chemo - continuing insulation * Pach Taas - installation of air ducts and connection of single stacks to exhaust fans
--	---	--	--	---

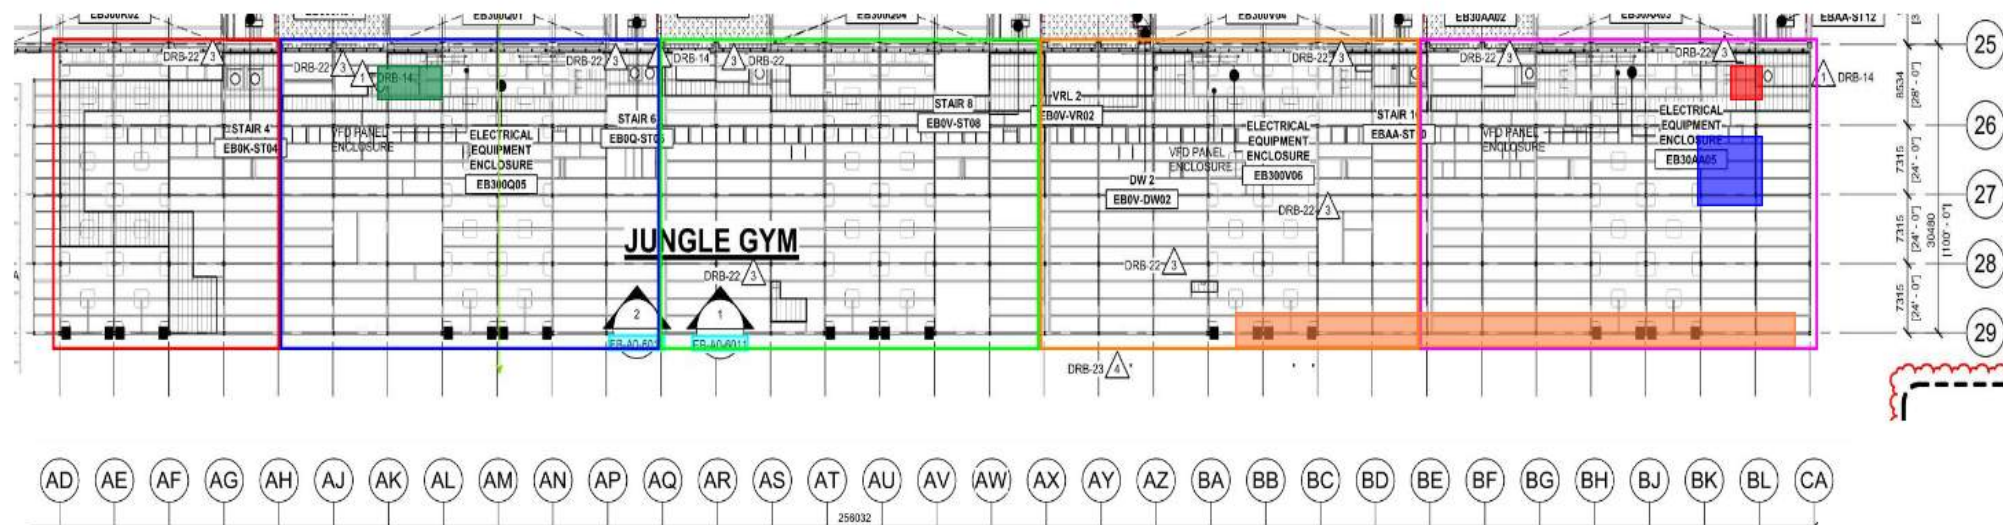

WJG – Lift 3


* Stage design - dismantle of scaffold
 ASD- erection of scaffolds for installing gutters

* Stage design - erection of scaffold for connecting stacks to outriggers

* Pach Taas - hoisting and installing EPA balcony and bypass structure

* SN -cutting grating penetrations



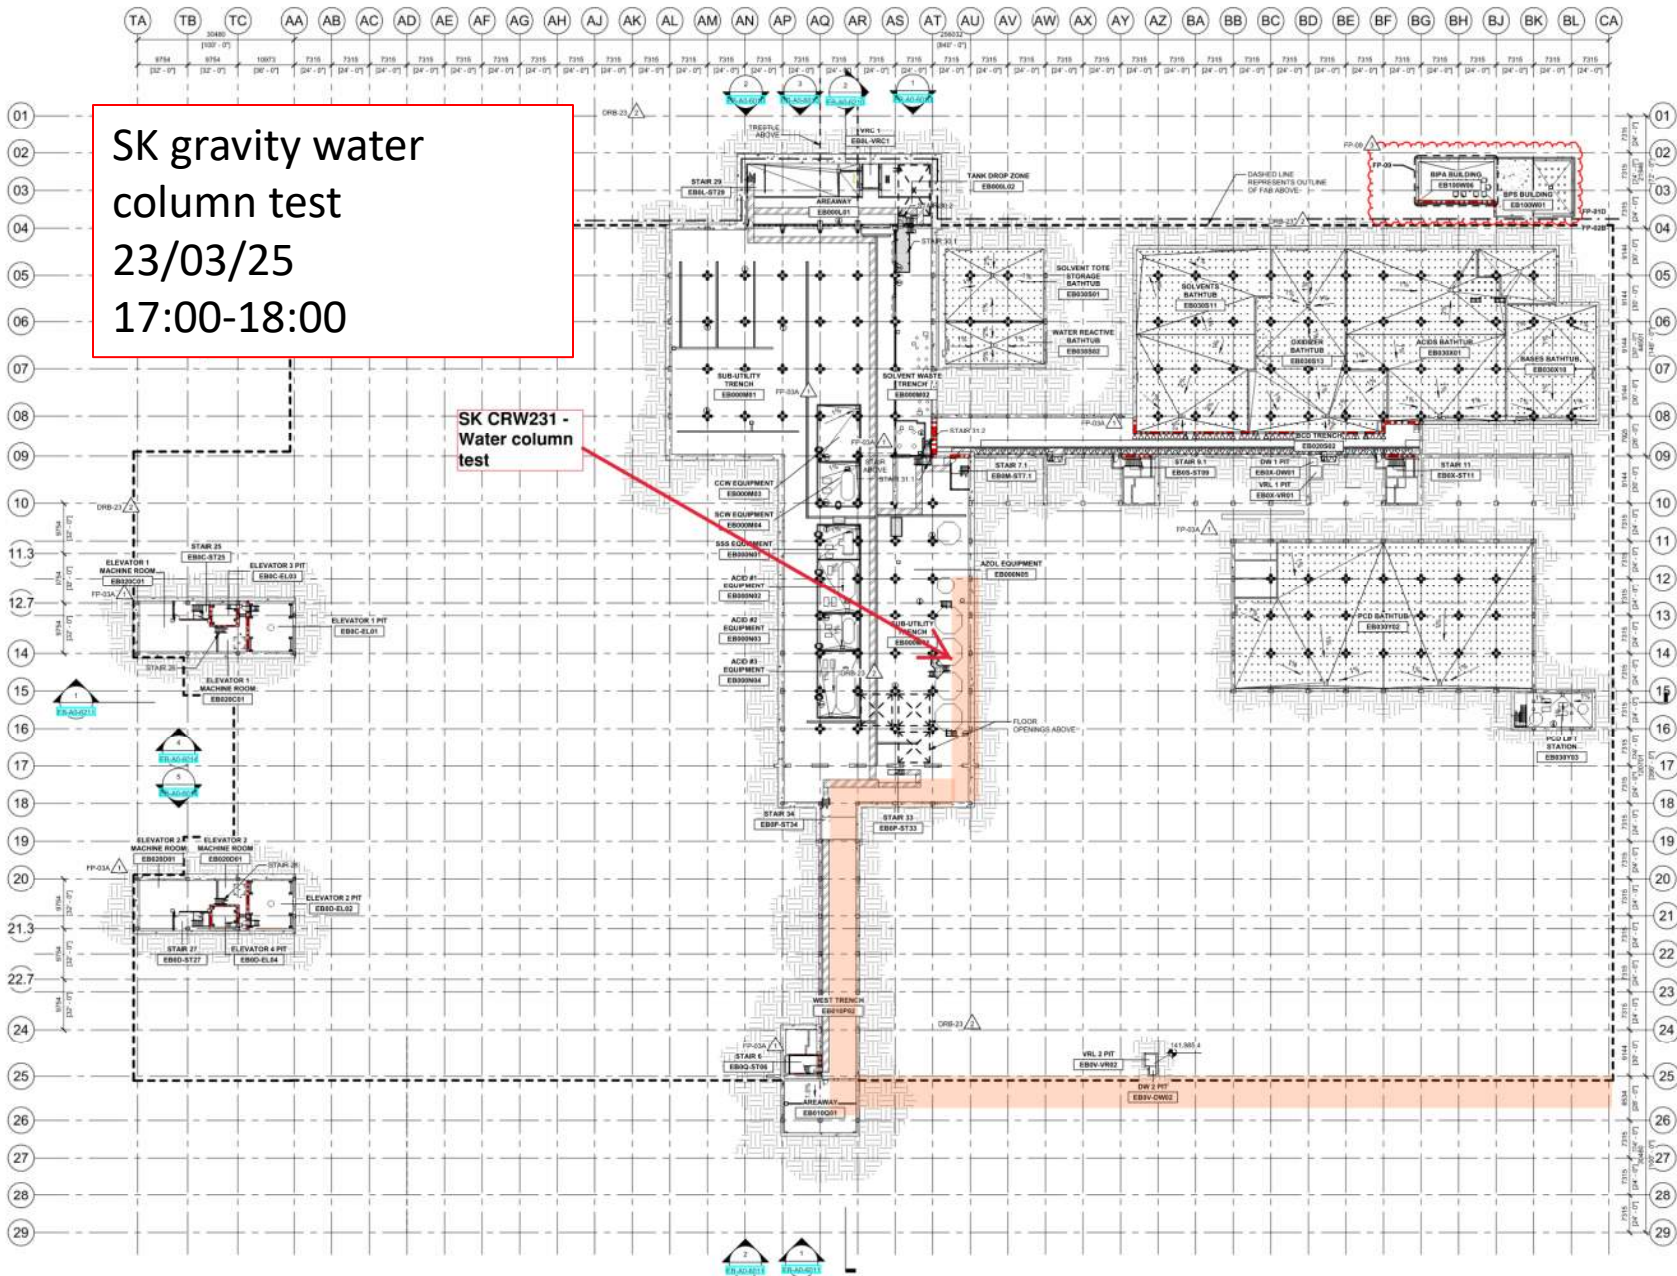

CUB 1 10 working days to room ready




CUB 1 10 Temp Utilities its time to go...




CUB 1 Closing time push to finish line




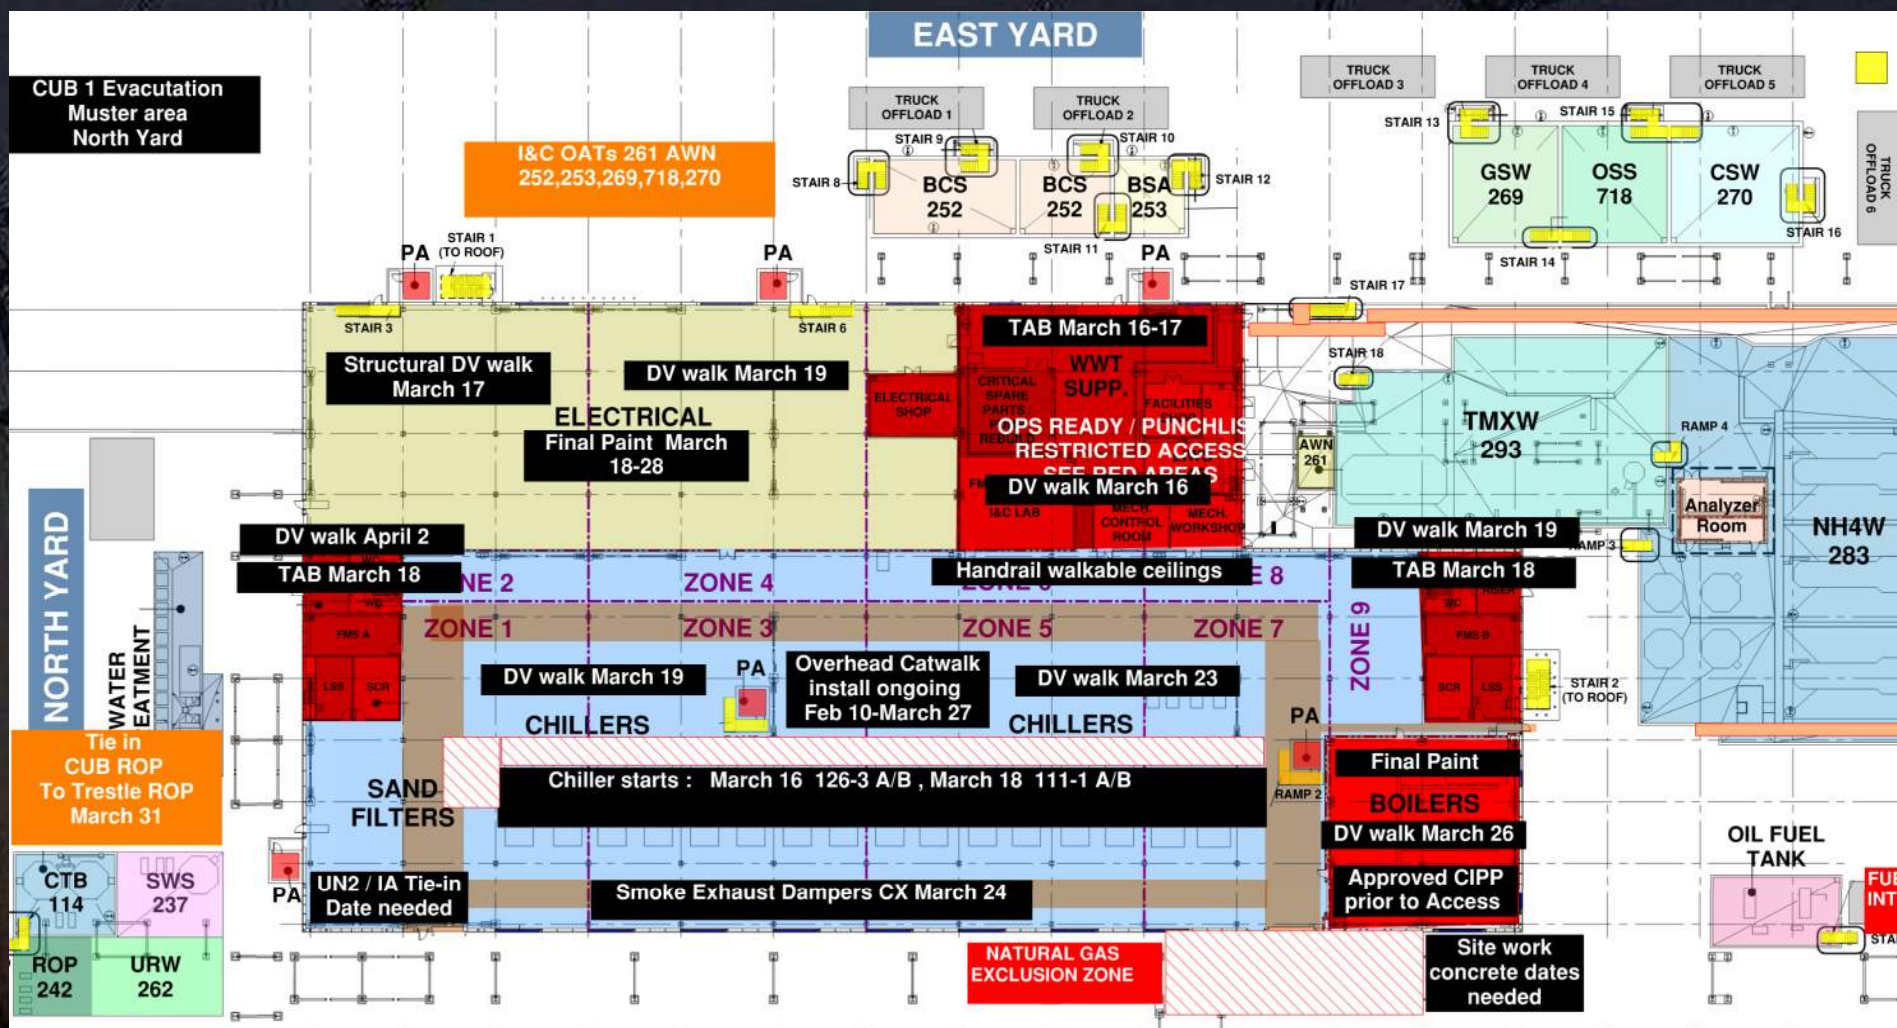

CUB 1 – EXTERIOR/ROOF

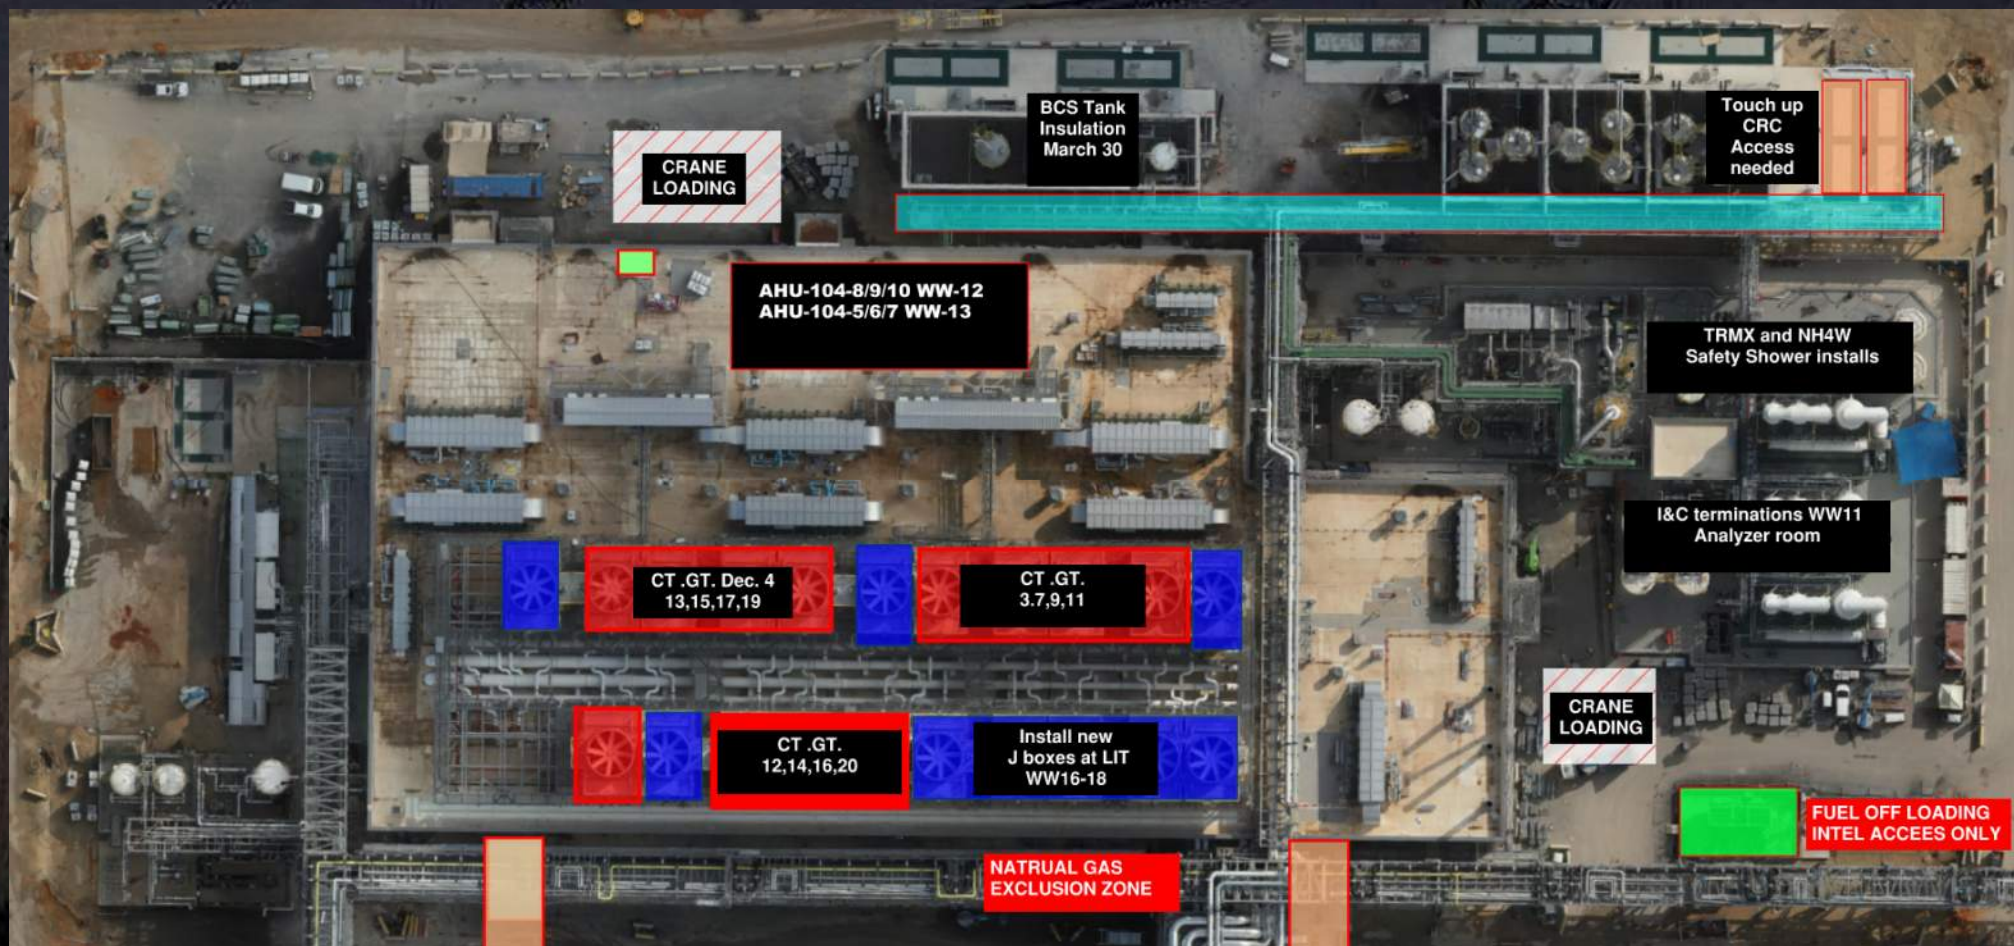


CUB 2- Load in & H&T

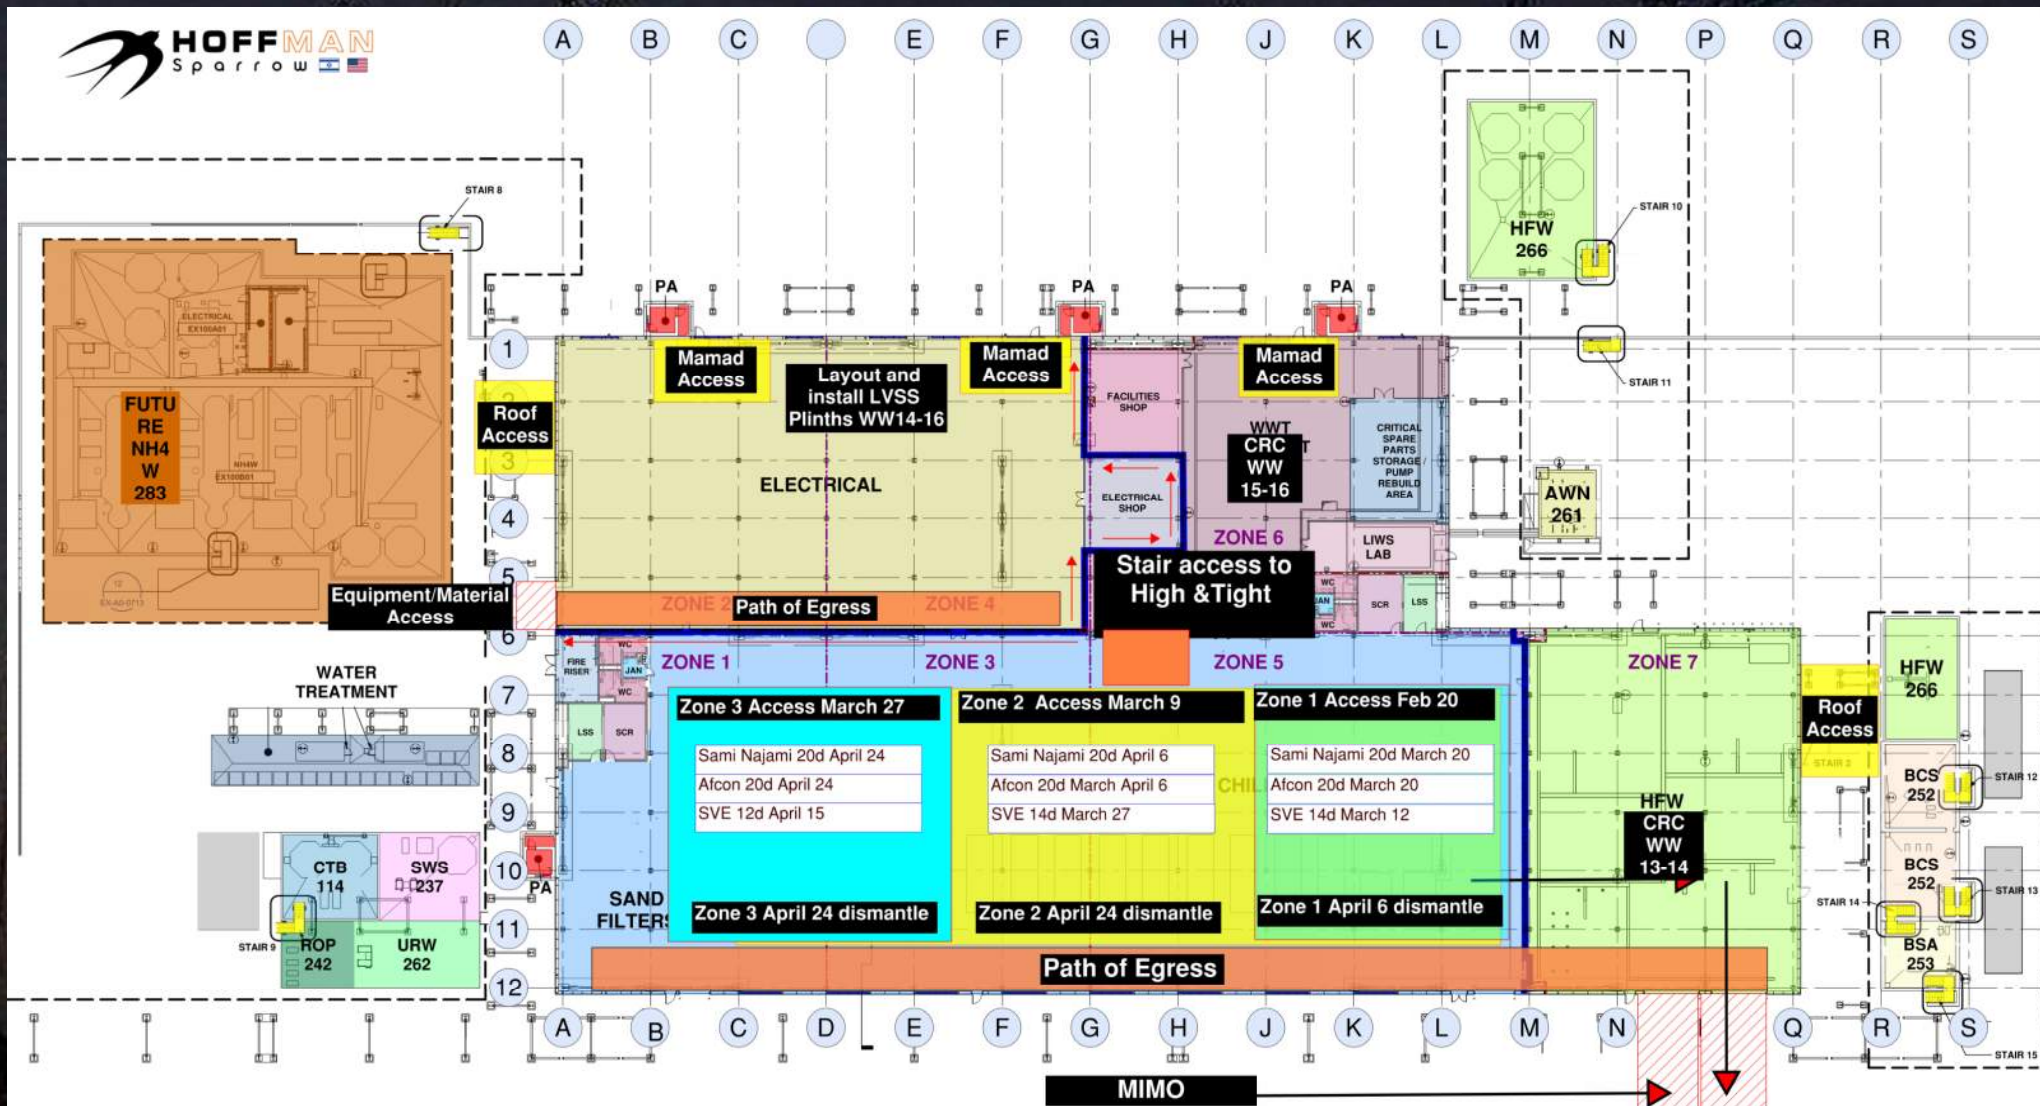


CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

LESICO RADIOGRAPHIC NDT
Sunday, Mar. 23 17:00-23:00



From main kiosk

Site temporary power

Legend :

- 22KV Line
- 400V Line
- 109 - Kiosk
- Lift Station

TC-10

TC-8

TC-6

630A SW

630A NW

630A SW

630A NW

Fab 38.1

Fab 38.2

Temp power shutdown
23-Mar-25
Start 5:00 PM End: 6:00 PM
CR and 4DA E9, E10 area
lights and spider boxes.

630A SE

630A NE

630A SE

630A NE

TC-7

TC-5

Cub 2

TC-12 Done

Cub 1

North

111 not energized

112

113

114

115

116

117

To 115

From main




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North

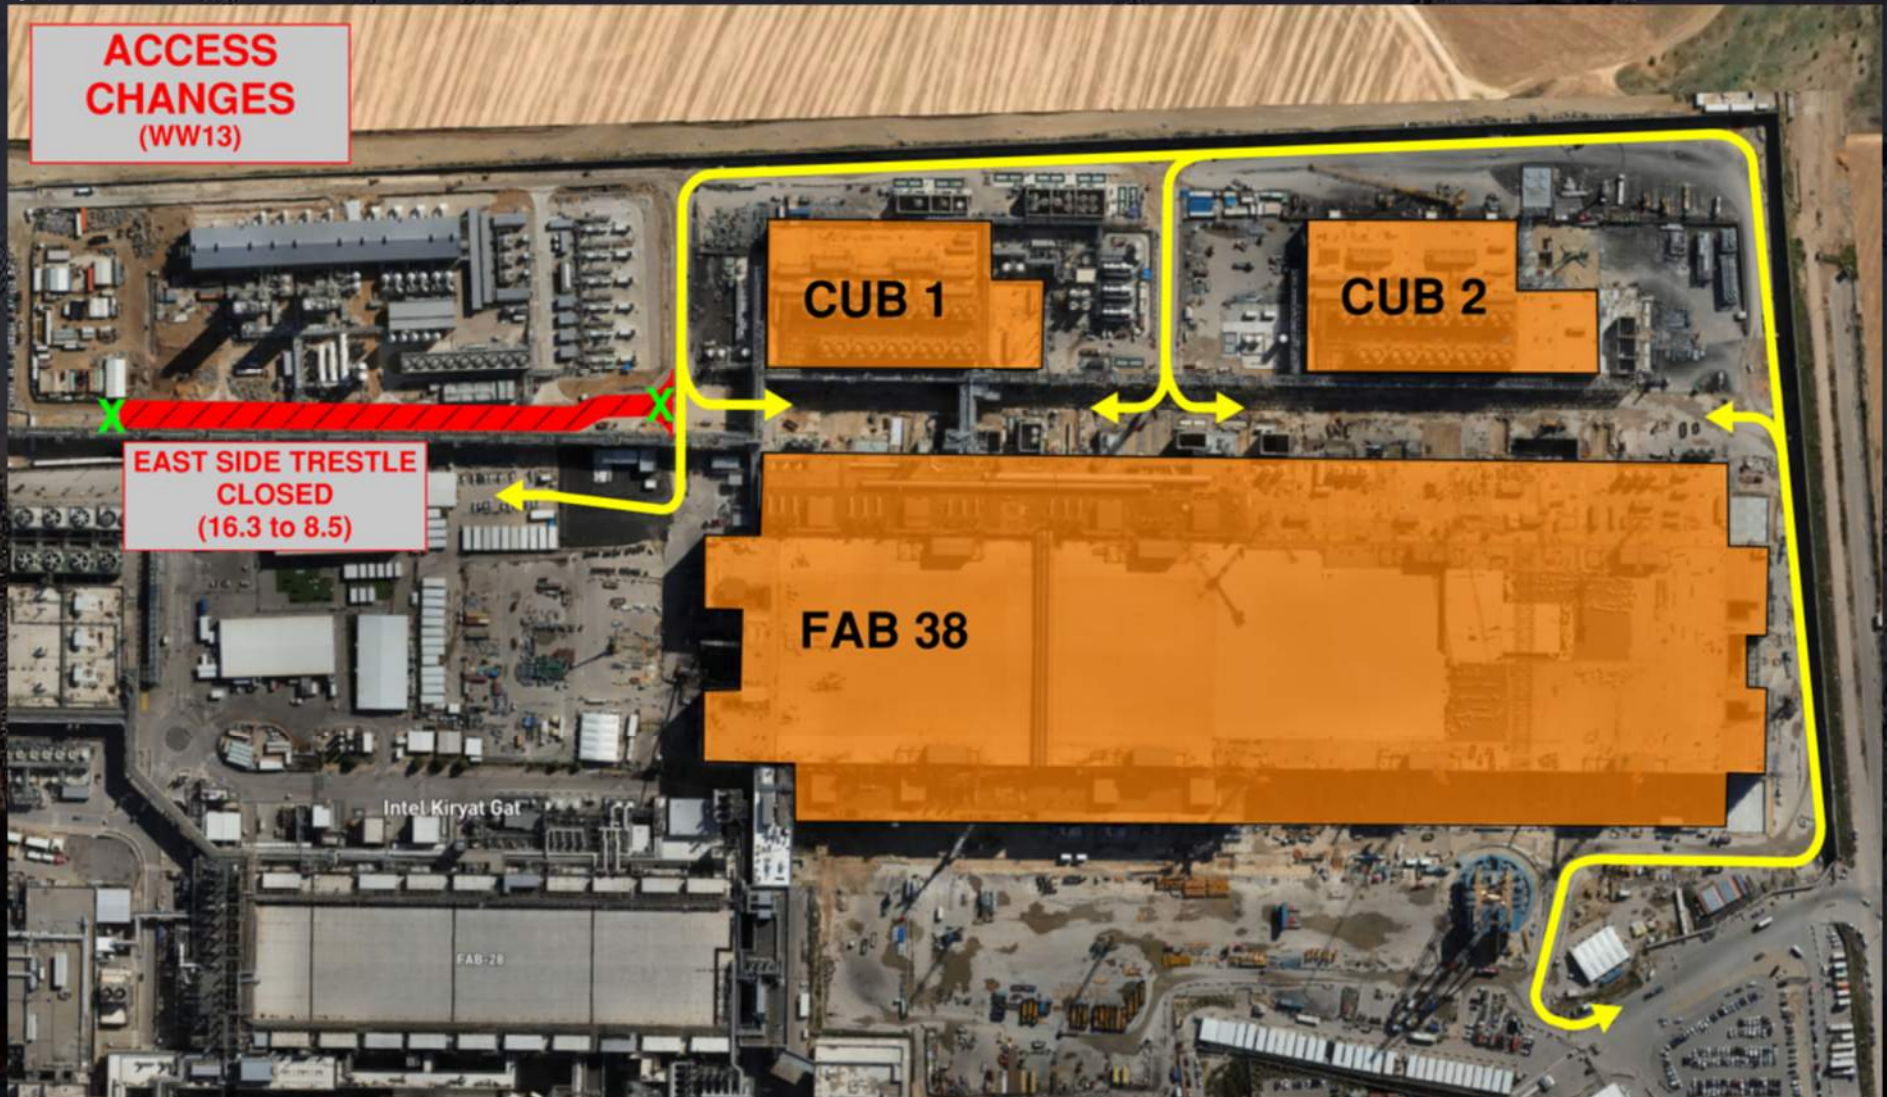




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
North

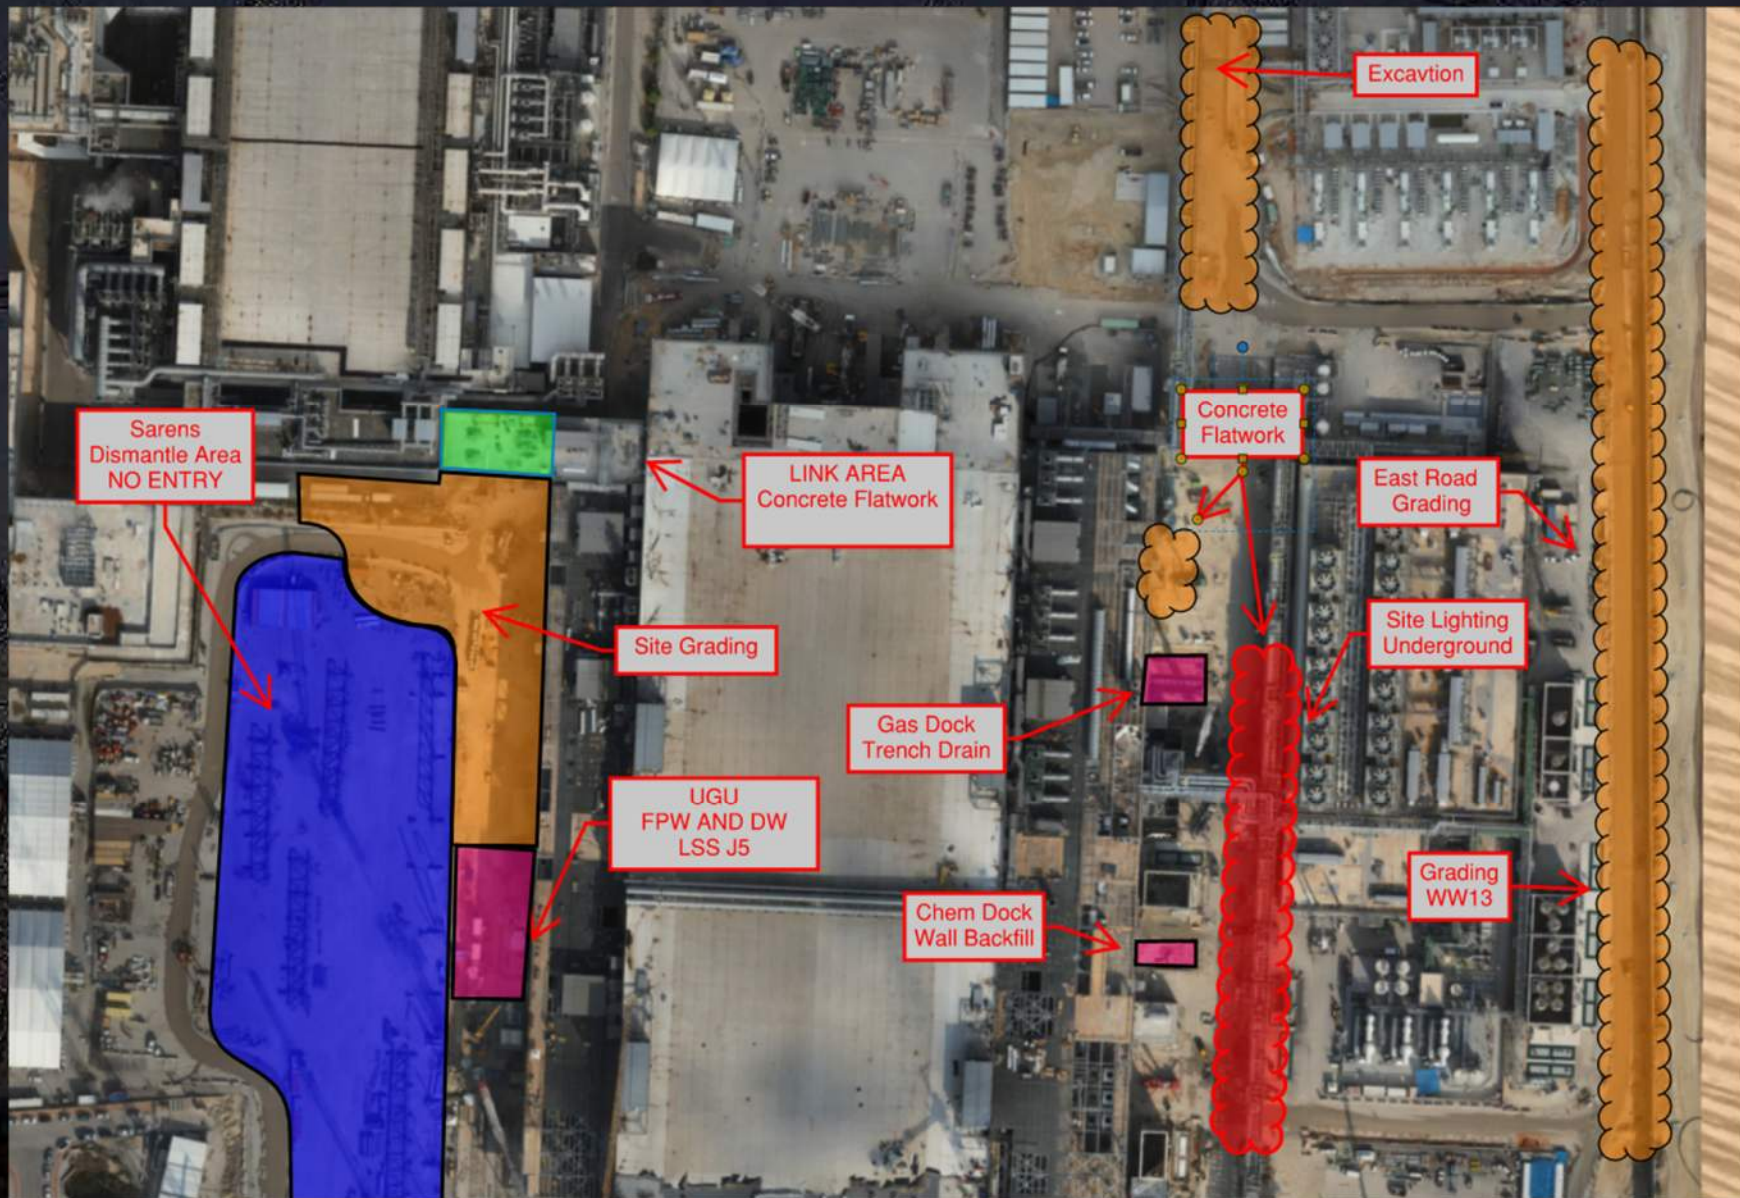



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South





HOFFMAN CONSTRUCTION COMPANY




Daily Coordination Meeting

MAMAD Locations

MAMAD LOCATIONS (19-March-2025)

■ LARGE
■ SMALL
■ BUILDING

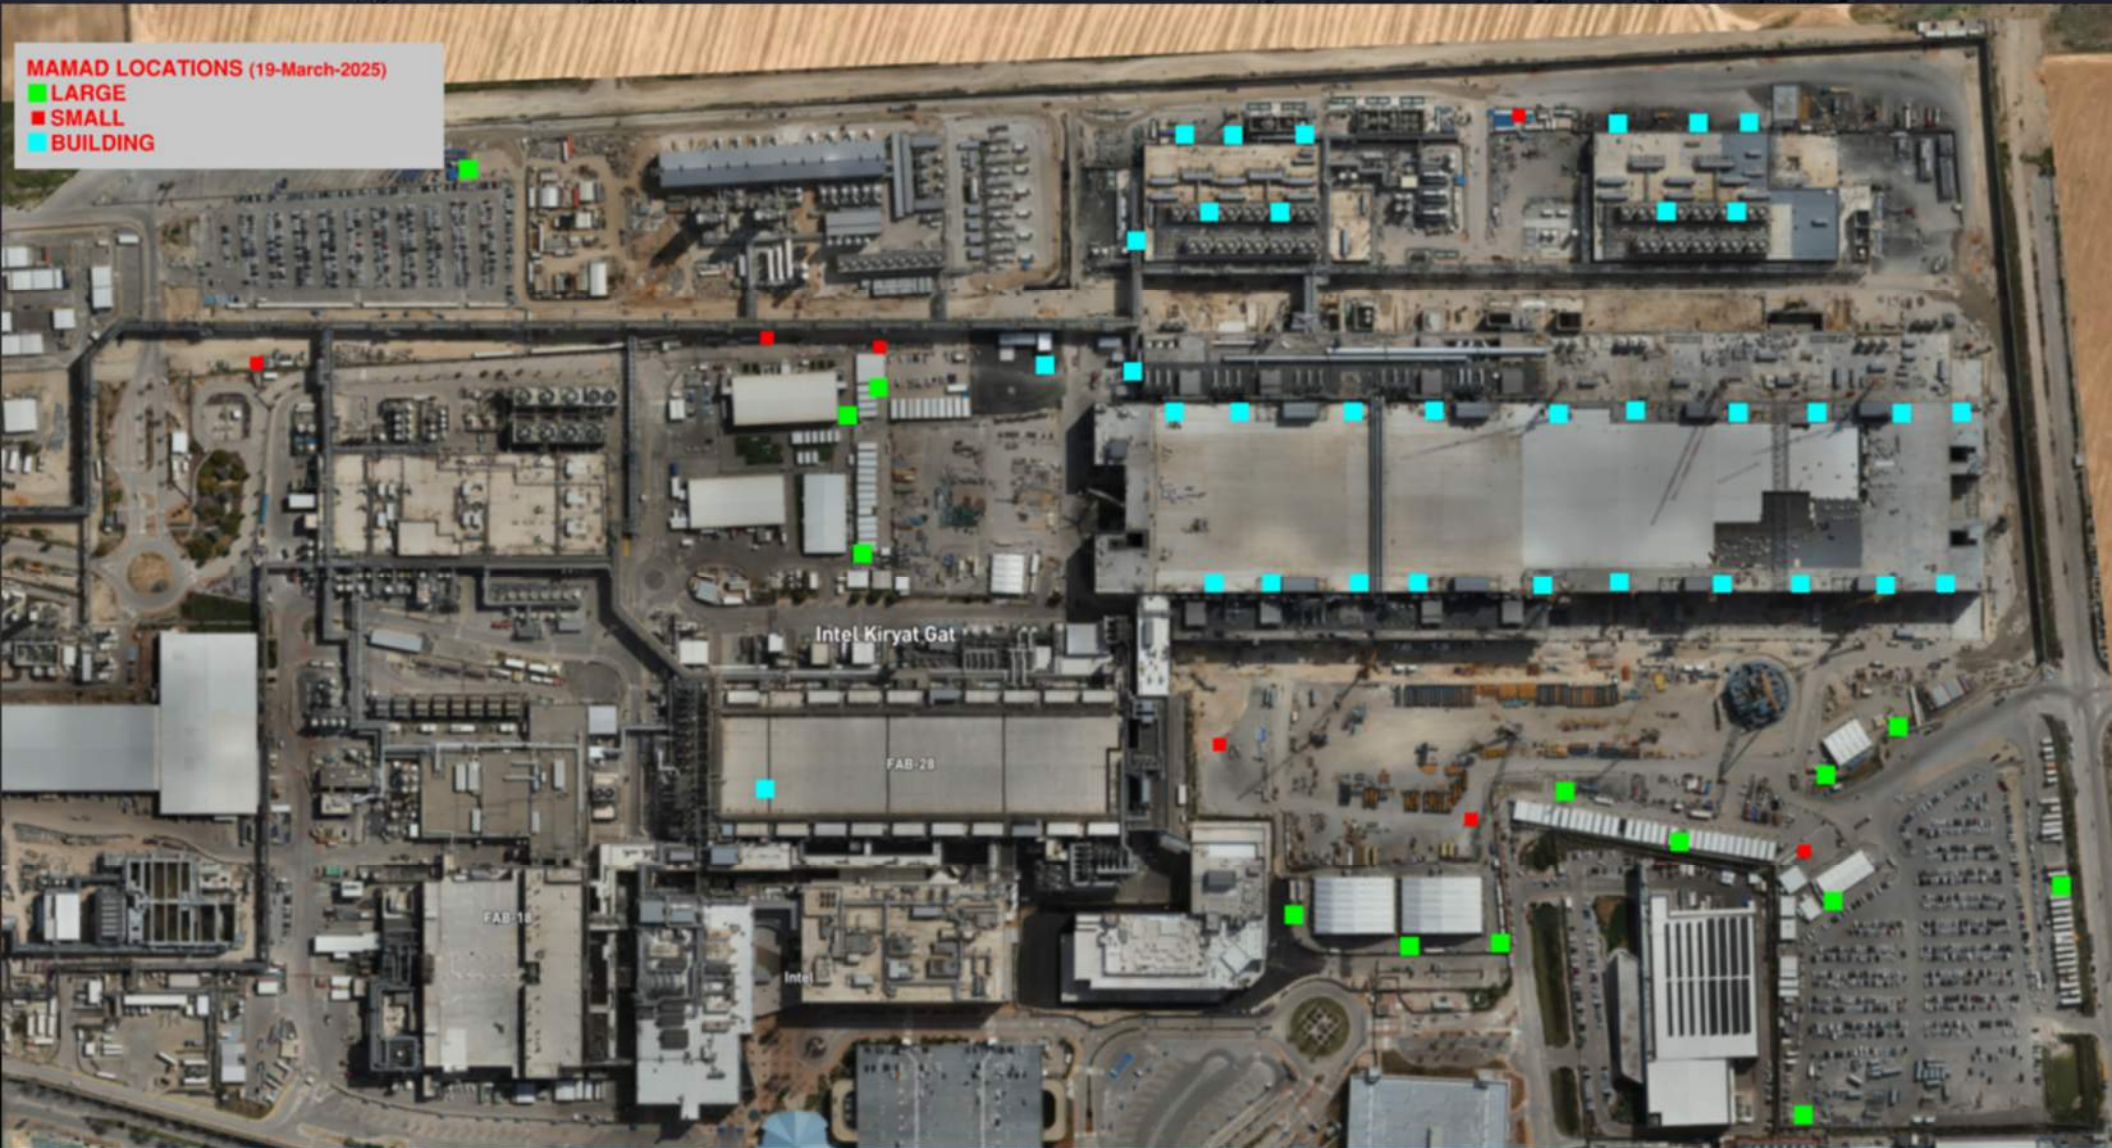

Site Requirements

- **Site Requirements:** You must adhere to and respect the site requirements. Anyone who requests to see your badge, you are obligated to show it, regardless of who is standing in front of you.
- **Personal Protective Equipment (PPE):** You are required to wear personal protective equipment at all times when it is necessary.
- **Red Barriers:** Do not cross red barriers. Respect the work area and the signs in the area. Any violation in this matter will be addressed through disciplinary procedures.
- **Speed Limit on Site:** Remember to comply with the driving rules on site. The speed limit is 16 km/h, and you must stop at every stop sign.
- **Use of Phones on Site:** The use of phones is prohibited within the work area. Do not walk and use your phone. You must stop and take calls in a safe location.

HCC/EHS Weekend Work- 21.03.2025

White Board Meeting in Beavers at 06:30

Superintendents

Brian-Grevious - 052-5394339
David Kanzevich - 052-2045446
Igor Shuster - 054-4743767
John McCrudden - 052-3756957
Michael-Ohehir - 052-4168879

CSA CM

Charles-Aitken - 052-6041443
Brandon-Britton - 052-6042828
Boris-Gruman - 054-7886568
Kenneth McGuirk - 052-5415017
Andy bJollands - 052-9659290

Crane

Craig Mowry - 052-300-2769
Yossi Atias - 052-3060790

Cx

John-Renwick - 052-3820589
Hadar-Swissa - 052-3467273

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Officer - Arkady Gerber-050-6851432 Arkady-Garber@Hoffmancorp.com

Subcontractor Weekend Work- 21.03.2025

FAB

Utility level/ SUT

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- **Megason**
 - LSS Rooms, 10E Vesda
 - Israel: 0526869393
- **Afcon E**
 - All Over SF
 - Avi Eli: 0526008487
- **Lesico**
 - 3W,3E PT
 - Gabriel 0549892929
- **Talad**
 - 1W
 - Ezat: 0543098001

Clean Room

- **Talad** – 30 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Maty 0504887477, Super Igor 0544509386)
- **Chemo** – 45 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2 guys (Liran 0532323696, Eden 0585335445)
- **Sig** – 16 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- **Rolling Plains** – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Oleg 0542689370, EHS Ovidiu 0546993648)
- **Tavas** – 18 guys , 12 cleanroom maintenance, 6 at interstitial (Super Inas 0537148630, EHS Vadia 0528412021)
- **W&W** 20 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- **Tapertech** – 13 guys CAF installation 1E/1W (EHS Amit 0549249356 Supervisor Igor 0547953798)
- **Tavas** – Cleanroom clean Maintenance 1-2E/1-2W (Supervisor Ilan 0522758886, EHS Stas)

Subcontractor Weekend Work- 21.03.2025

PSSS

- **Afcon Electrical** – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- **Chemo A.** – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- **Combe Waste** – 2P Waste Piping at GL4/Lift 2 Waste Piping
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Lesico** – Low Point Drains on PSSS Roof/OFA in Solvents
 - Foreman – Suju Pally – 052-7755967
 - Safety – Tal Madar – 052-8229109
- **SK Engineering** – Lift 2 MAH 4P/DW Punchlist
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **W&W** – Grating Cutting Lift 3 1P
 - Foreman –
 - Safety –

WJG

Chemo:

Safety: Erez Megidish - 0549716840

Foreman: Maor - 0509889071

Afcon:

Safety: Steven Shartho – 0559129333

Foreman: Mantu Singh – 0559116973

Lesico:

Safety: Michael Gisri – 0526060223

Foreman: Rajesh Francis – 0549375380

SK:

Safety: Marzouk Amor – 0548830263

Foreman: Marcelo – 0542072784

SN:

Safety: Wisam - 0509828381

Foreman: Sorov – 0552837973

Subcontractor Weekend Work- 21.03.2025

CUB

Chemo Aharon:

Dudu - 0509808846

Leonid - 054-8883878

Carmel Bidud:

Fahri - 0526105266

Moyat - 0524335060

Trestle

Site

- **Derech Afar** – Shotcrete wall
 - Supervision = Raed: 054-244203
 - EHS = Alex: 054-5403849
- **Olizki** – Offload 10, Link and East BGC road
 - Supervision = Or: 052-4917313
 - EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
