

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:


- Weather
- Fit for duty




HOFFMAN CONSTRUCTION COMPANY



UTILITY LEVEL PRESS TEST

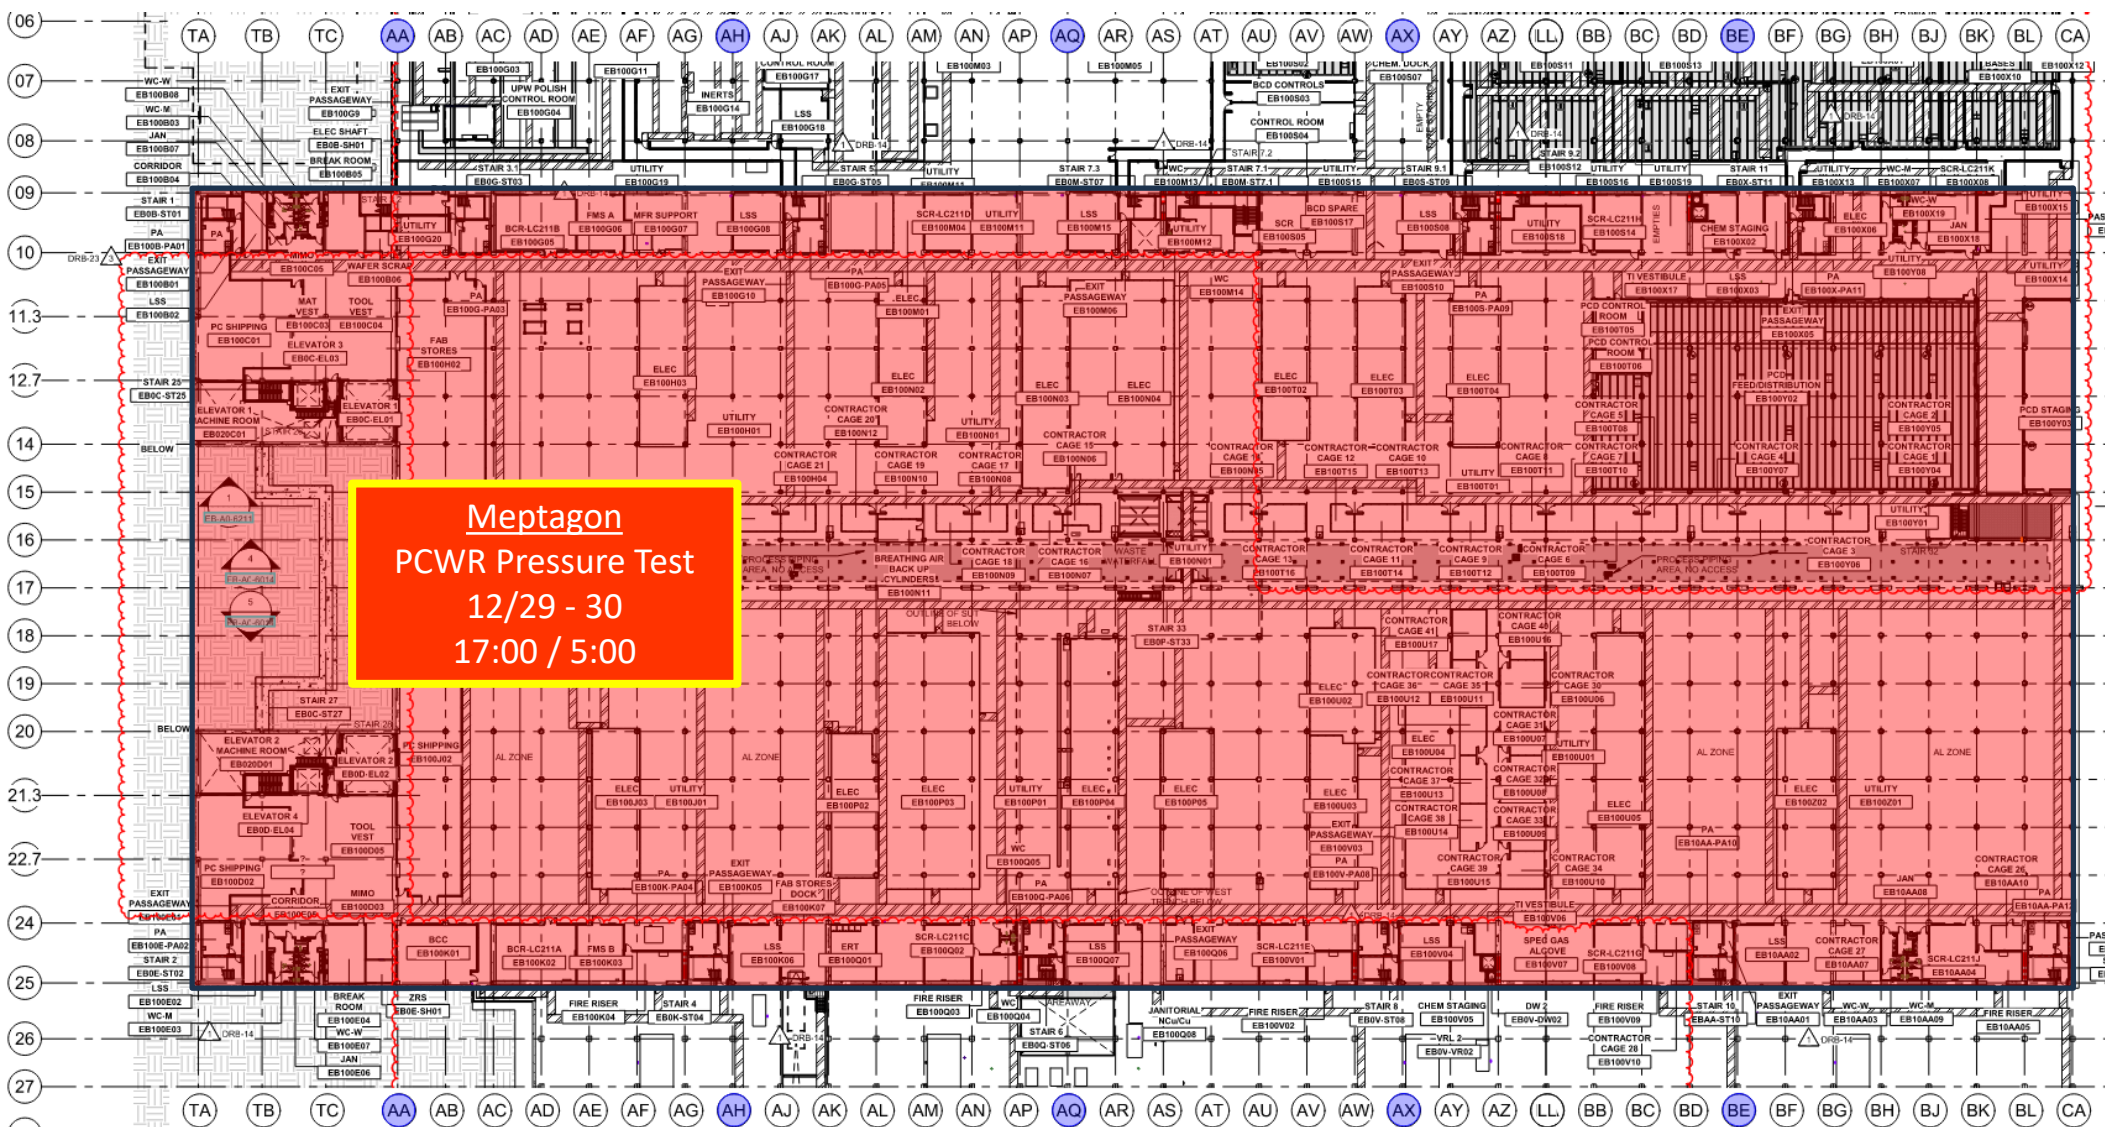

UTILITY LEVEL MOD1

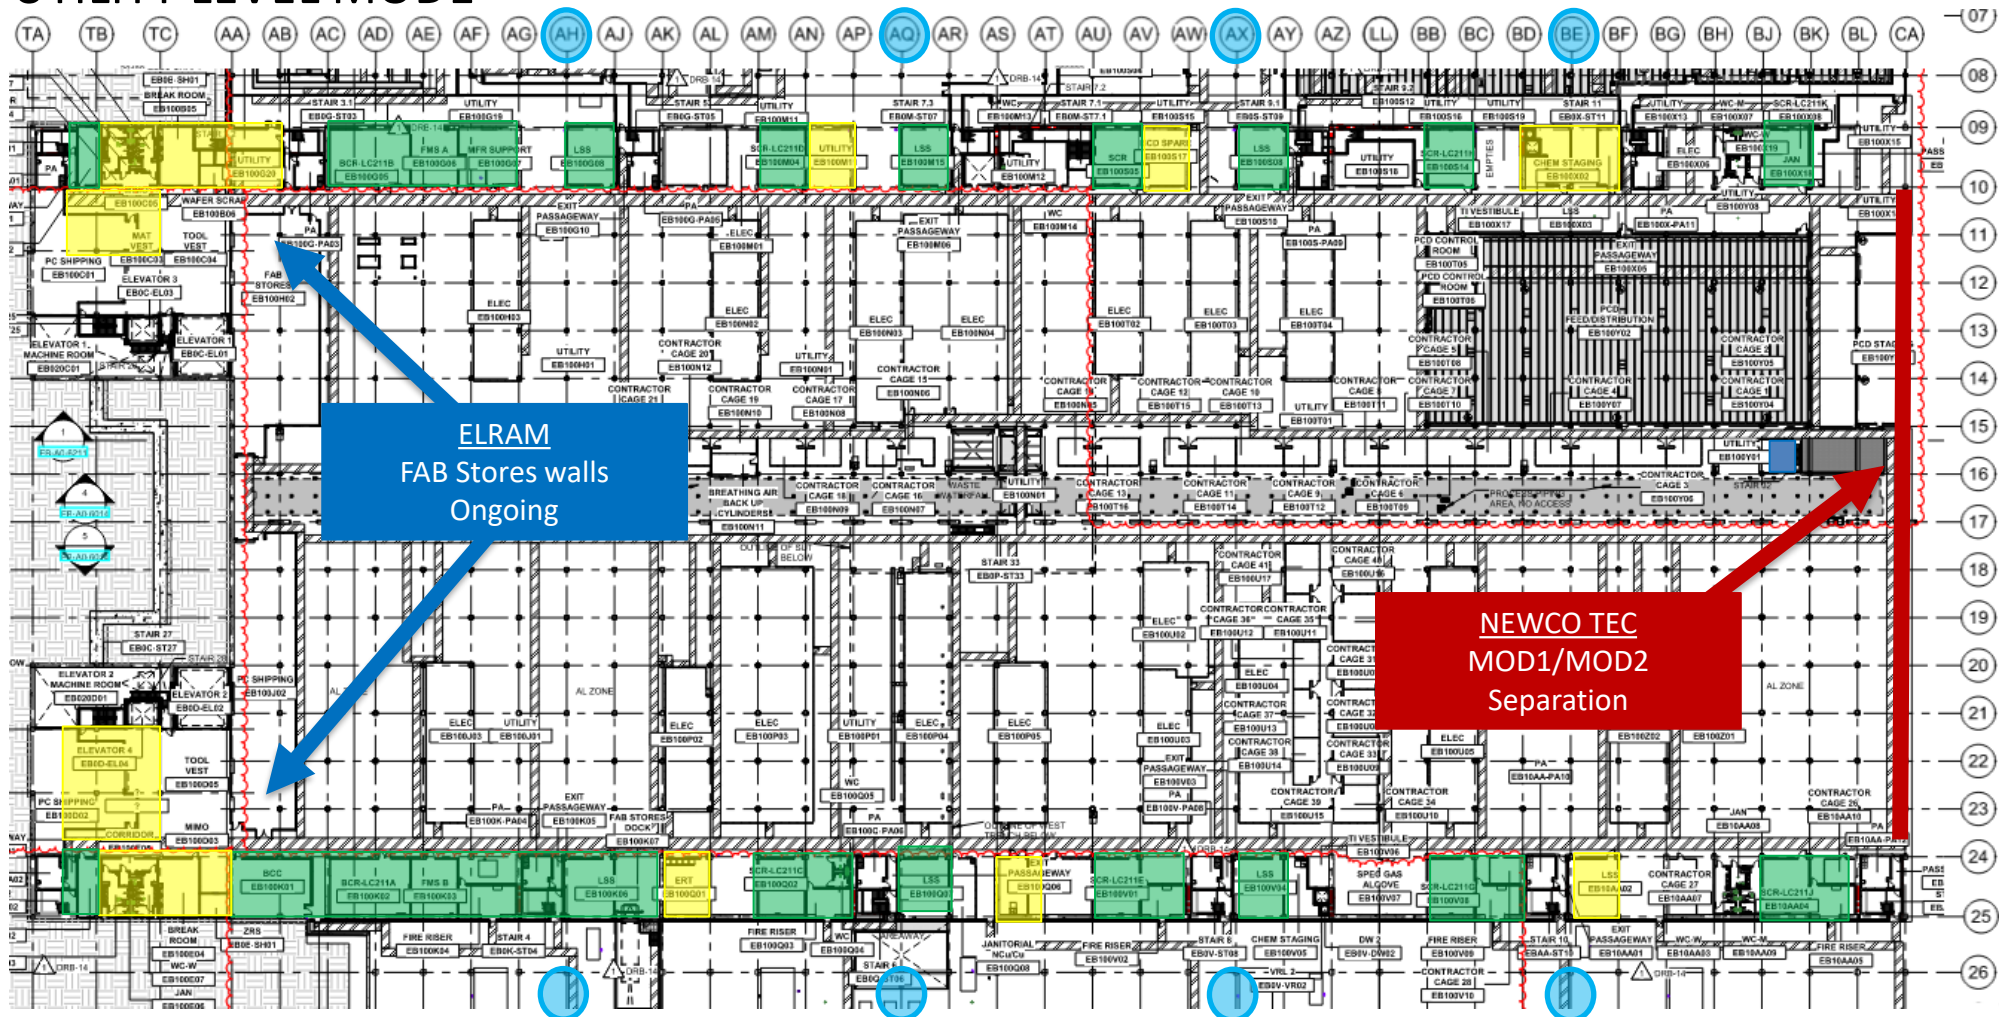


ELRAM
Drywall install

MEP+Electrical
Ready for re-install




UTILITY LEVEL MOD2

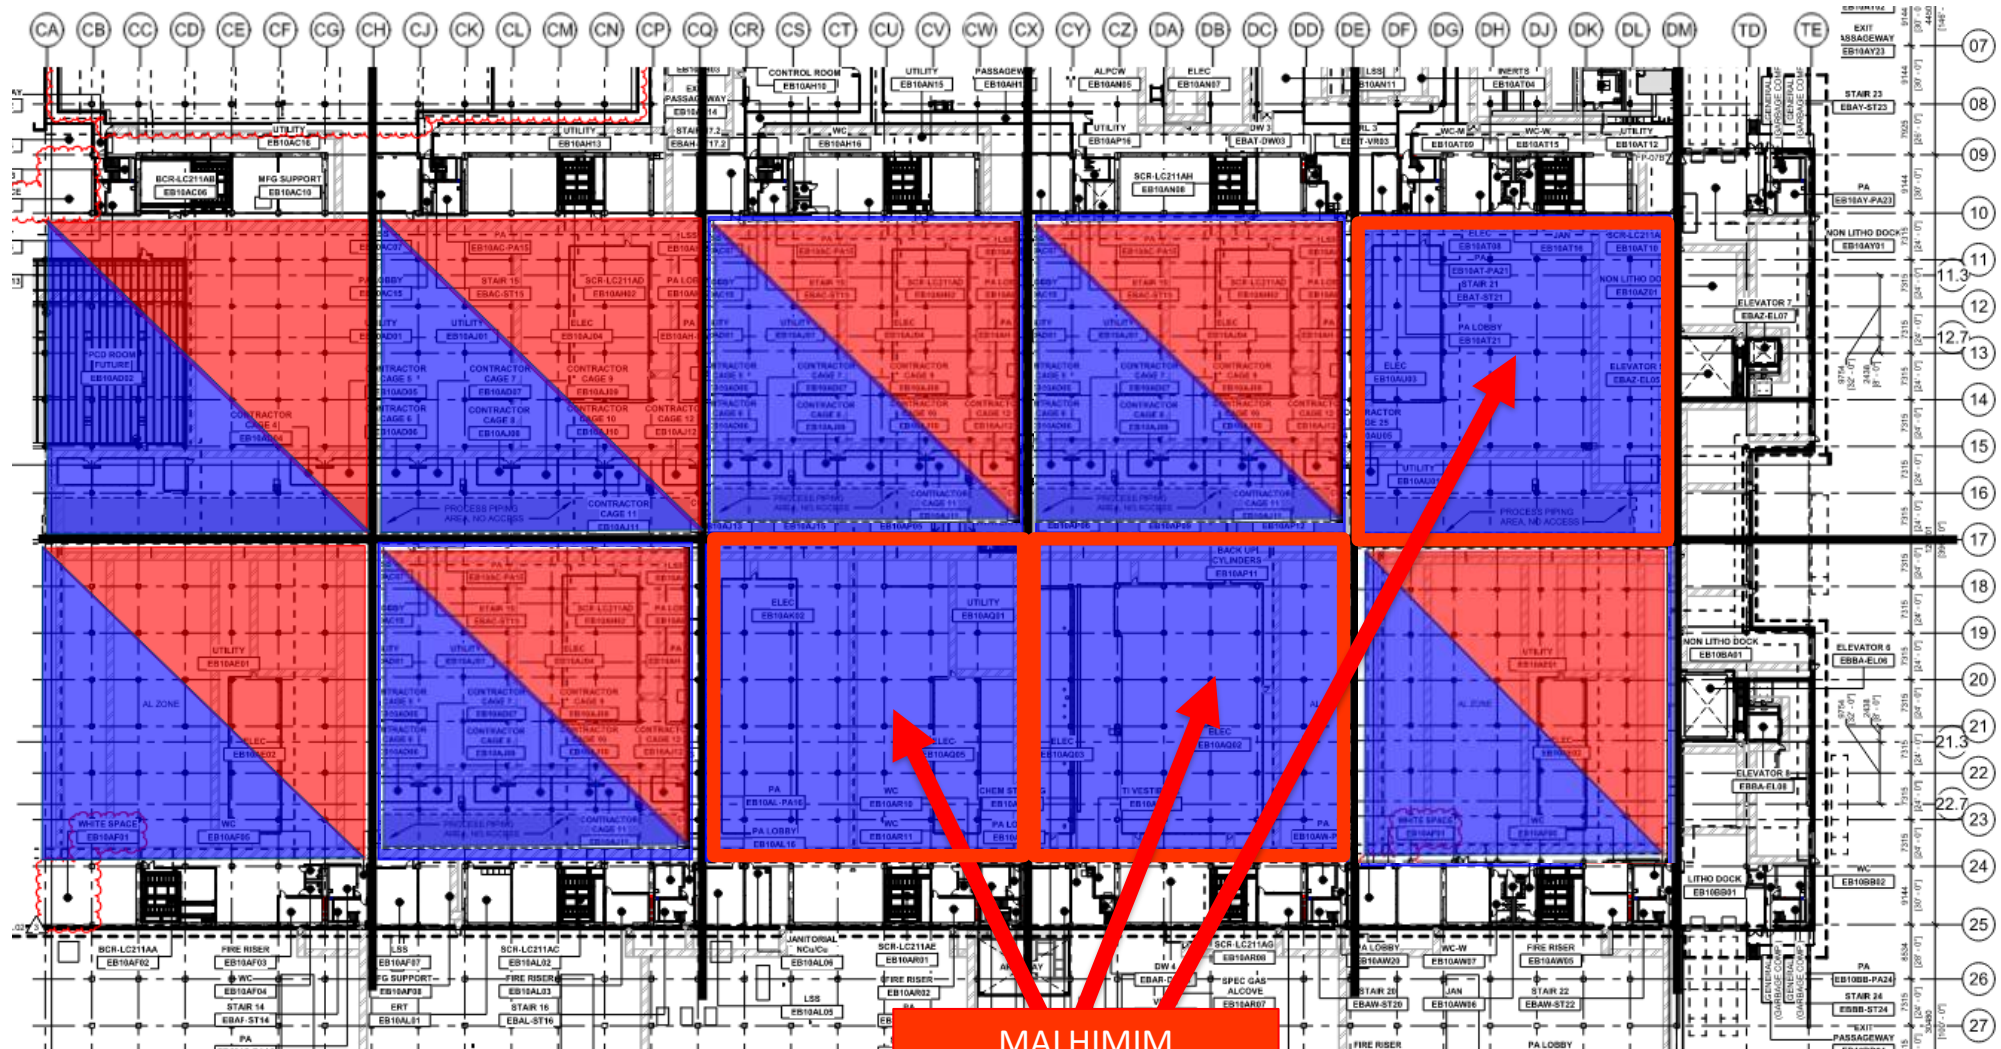

MALHIMIM
8W 9W 10E
Ongoing


SUT 38.1 LEVEL

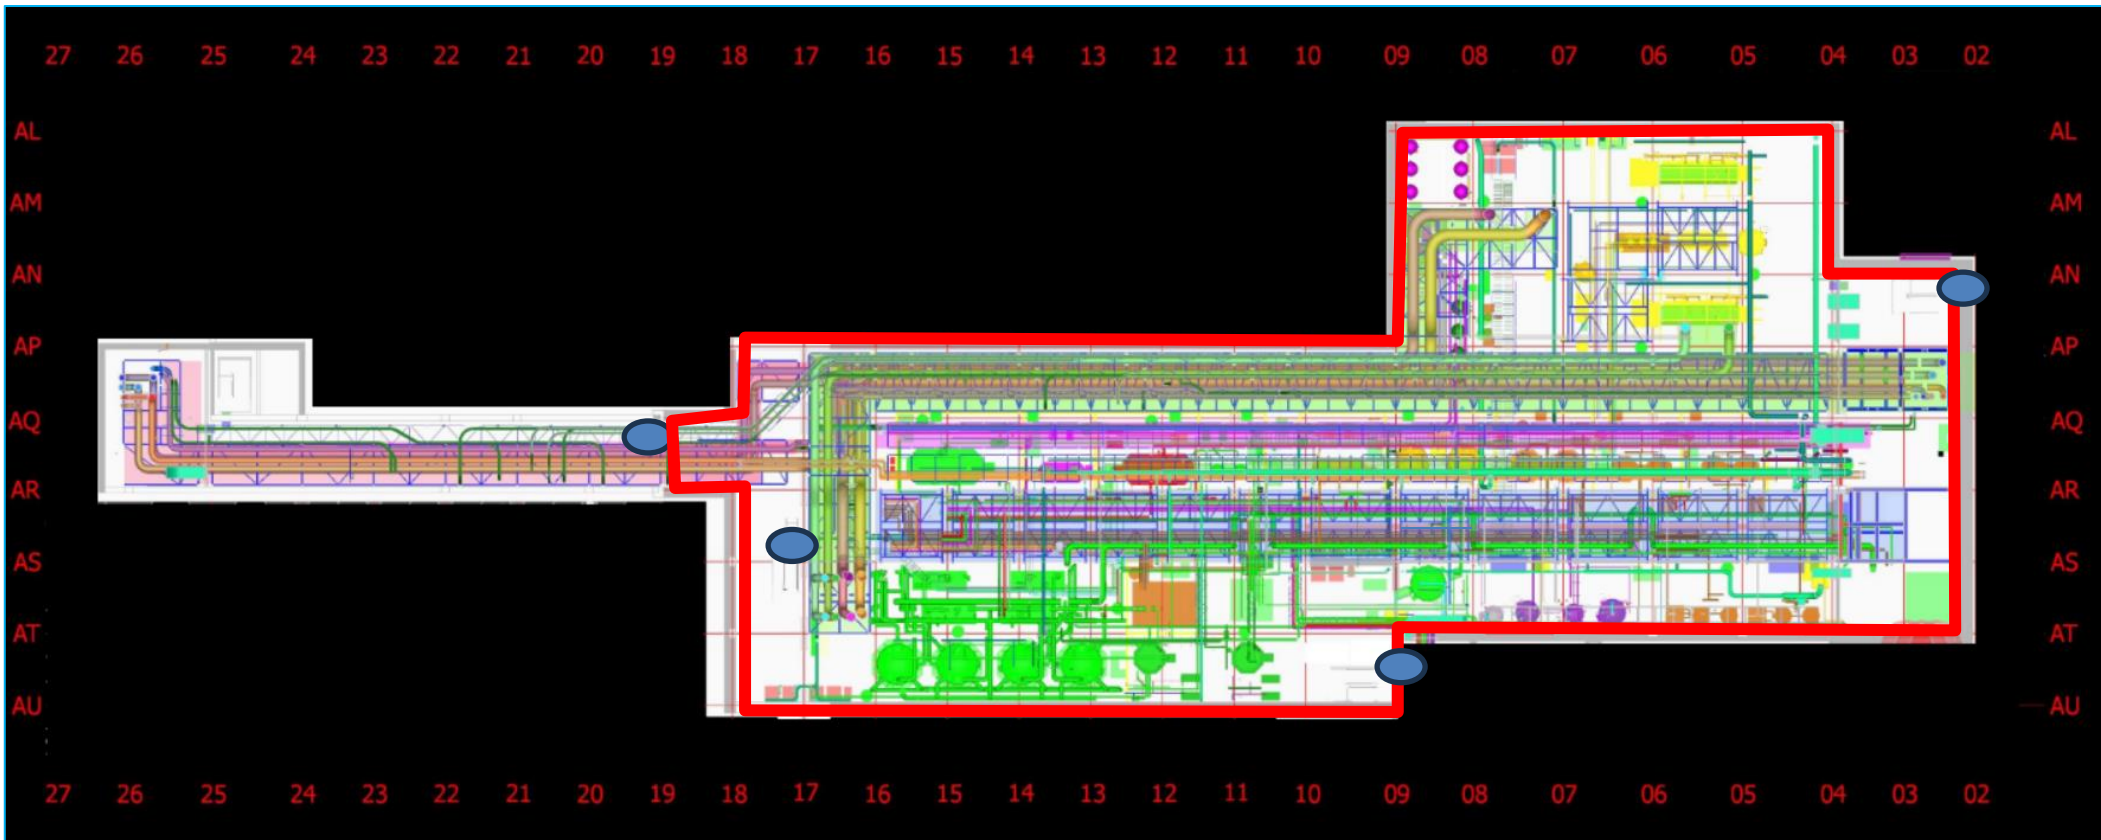

Meptgon PCW/ALPCW
pressure test
12/29 + 12/30
17:00 - 4:00




SUT 38.1 LEVEL

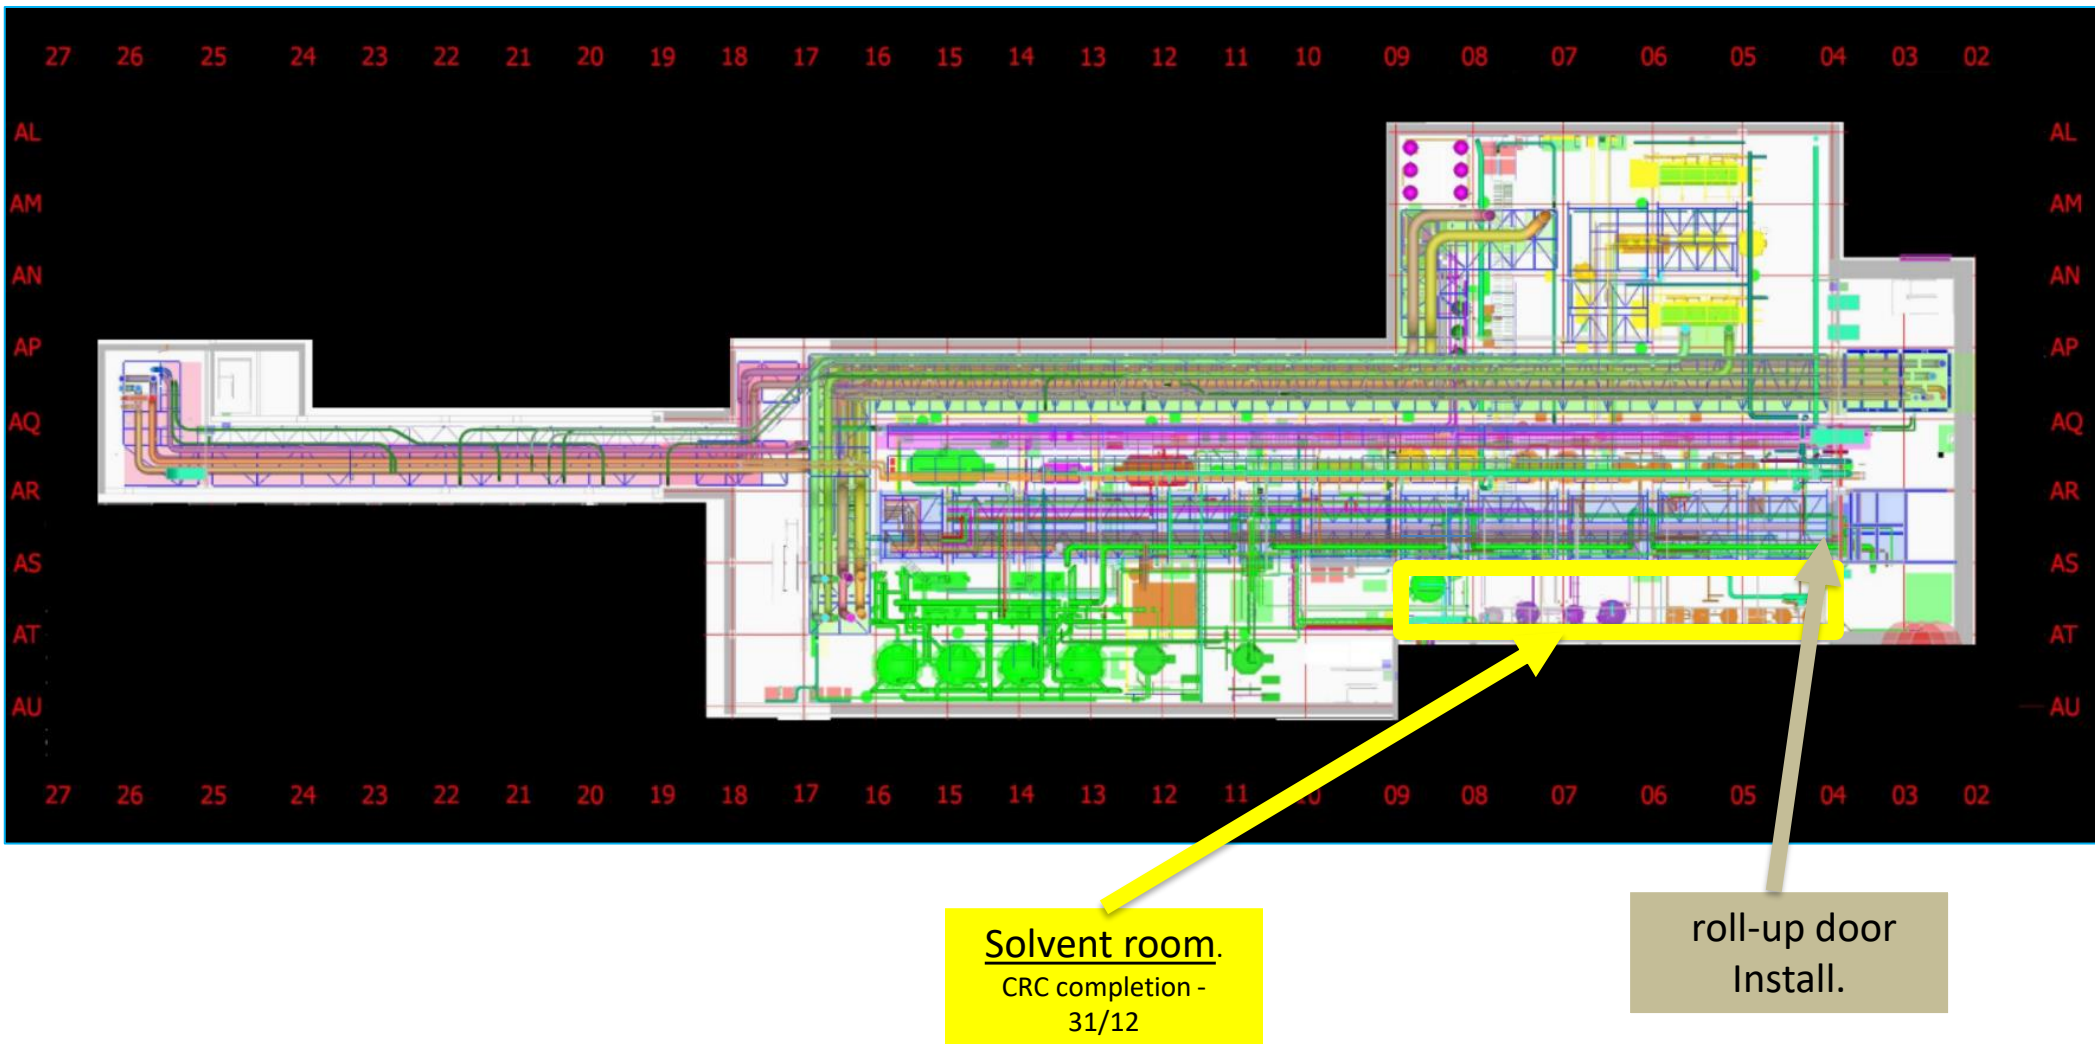

SUT 38.2 LEVEL

Rack 4b
Lifting
schedule
#6 –

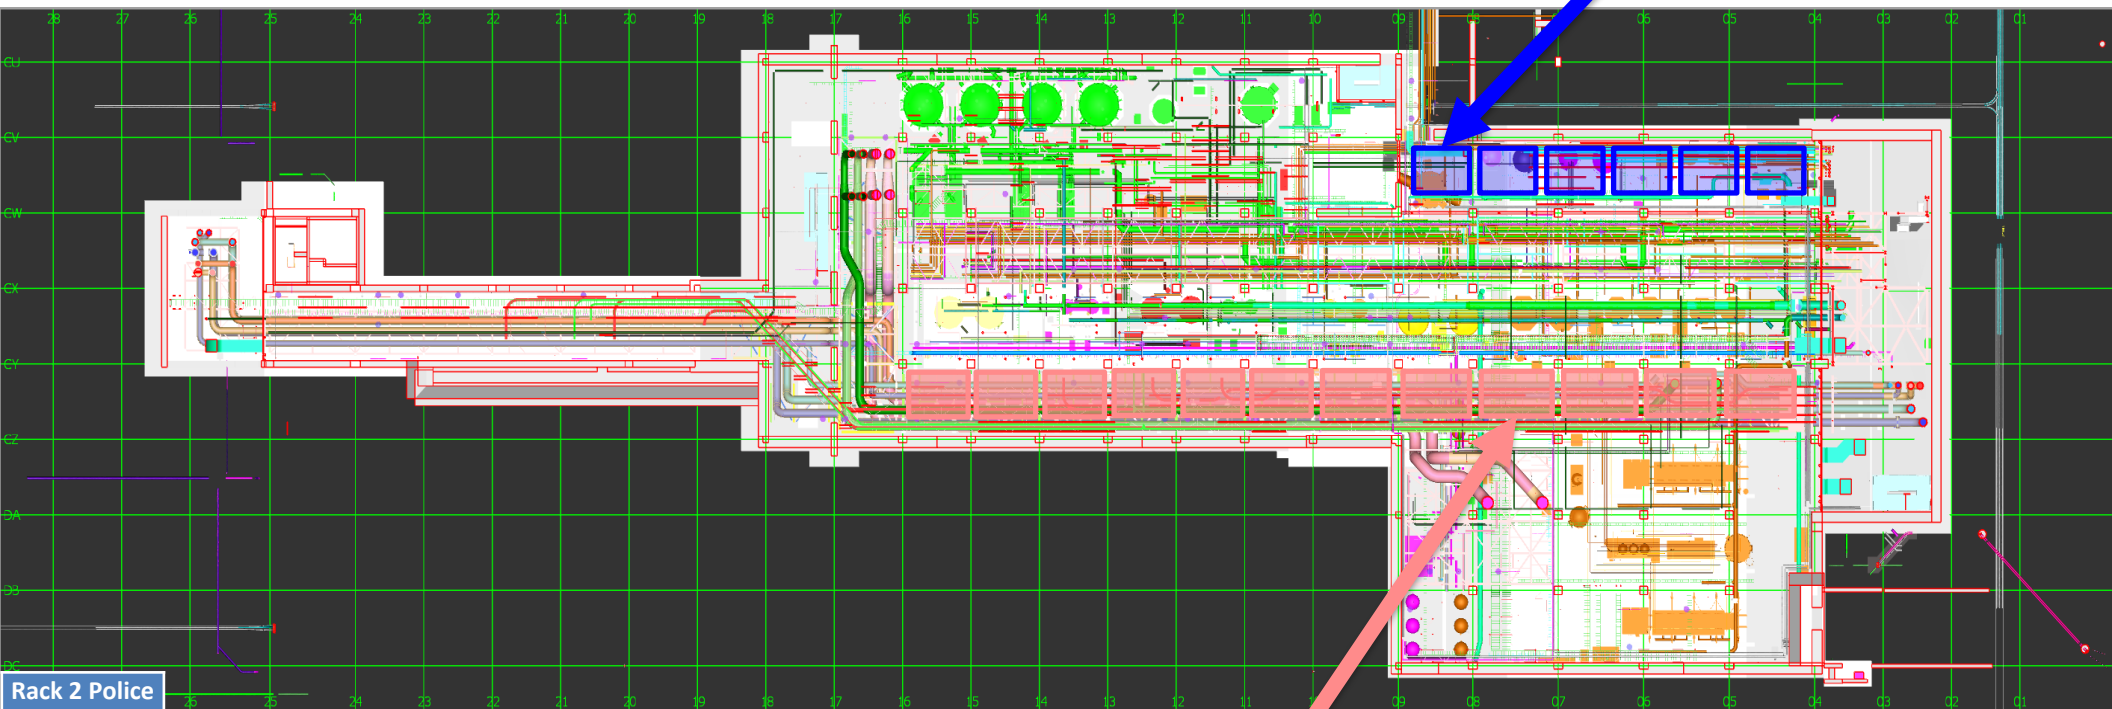


**Rack 2 Police
escort dates**


v24.11.24
v25.11.24
v3.12.24
v9.12.24
v12.12.24
v15.12.24
v17.12.24
v22.12.24
5.1.25
14.1.25
2.2.25
9.2.25

Rack 2
MIMO -
Module #9
5th of Jan


SUBFAB BUILDOUT MOD 1

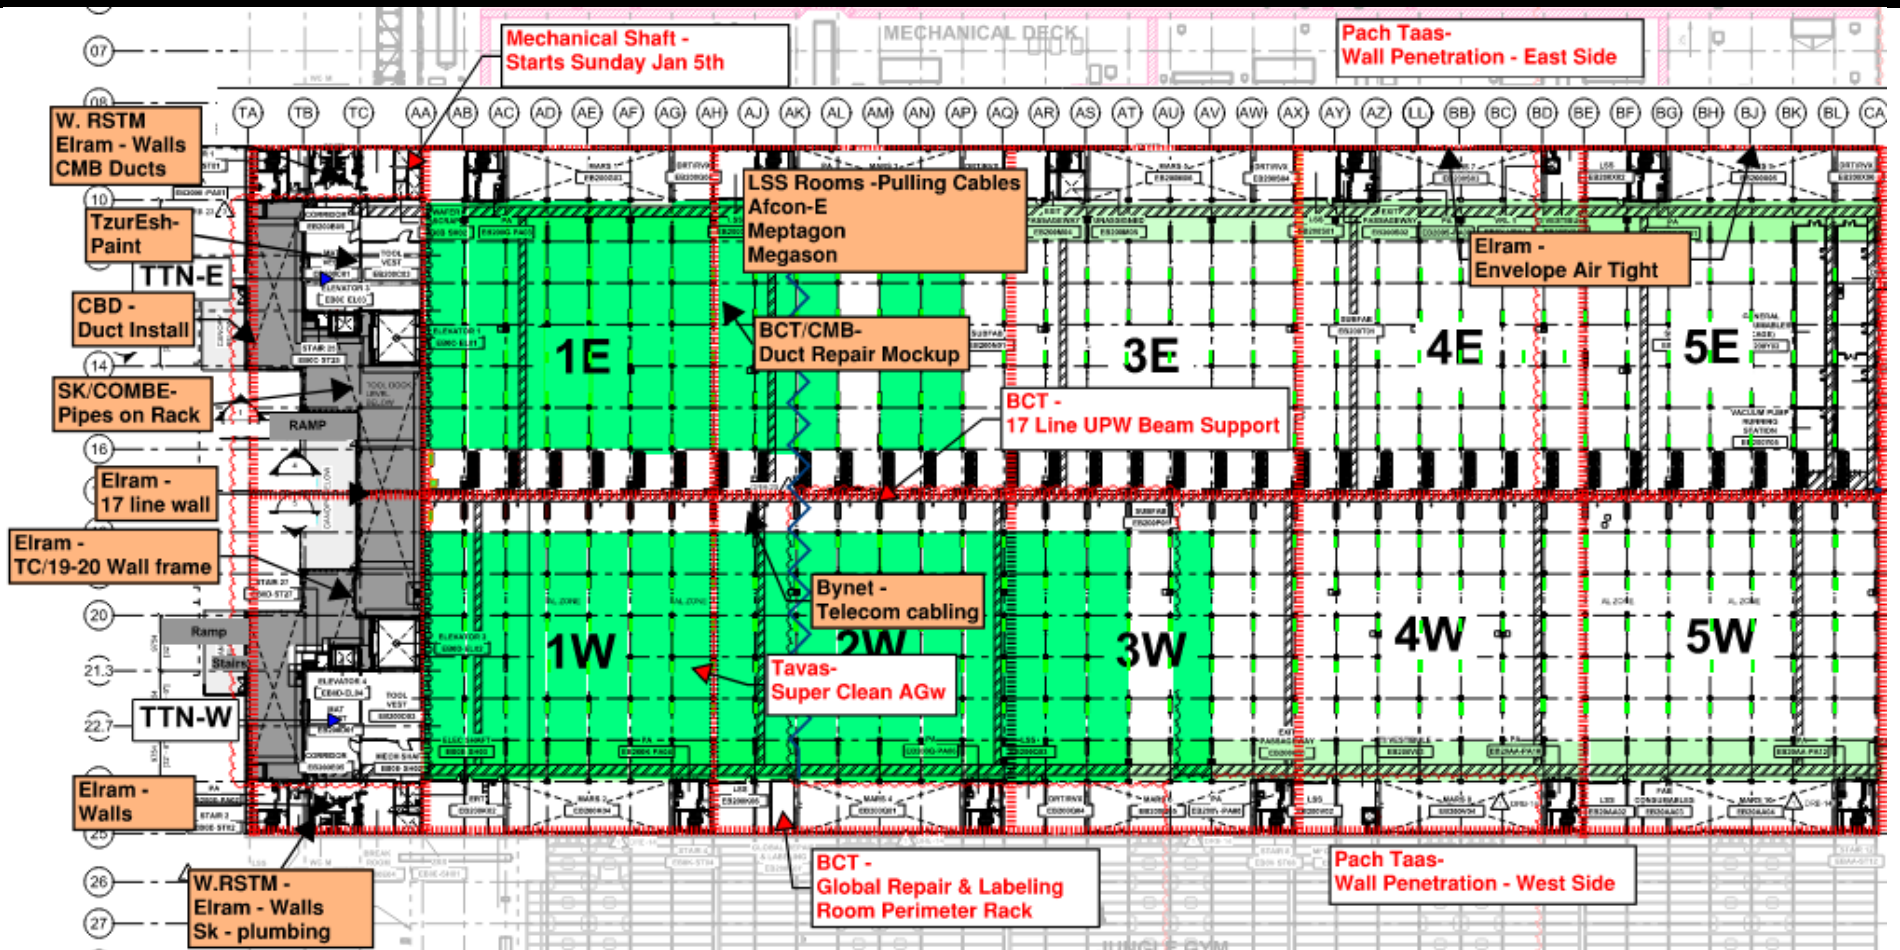


SUBFAB CRC TOPCOAT

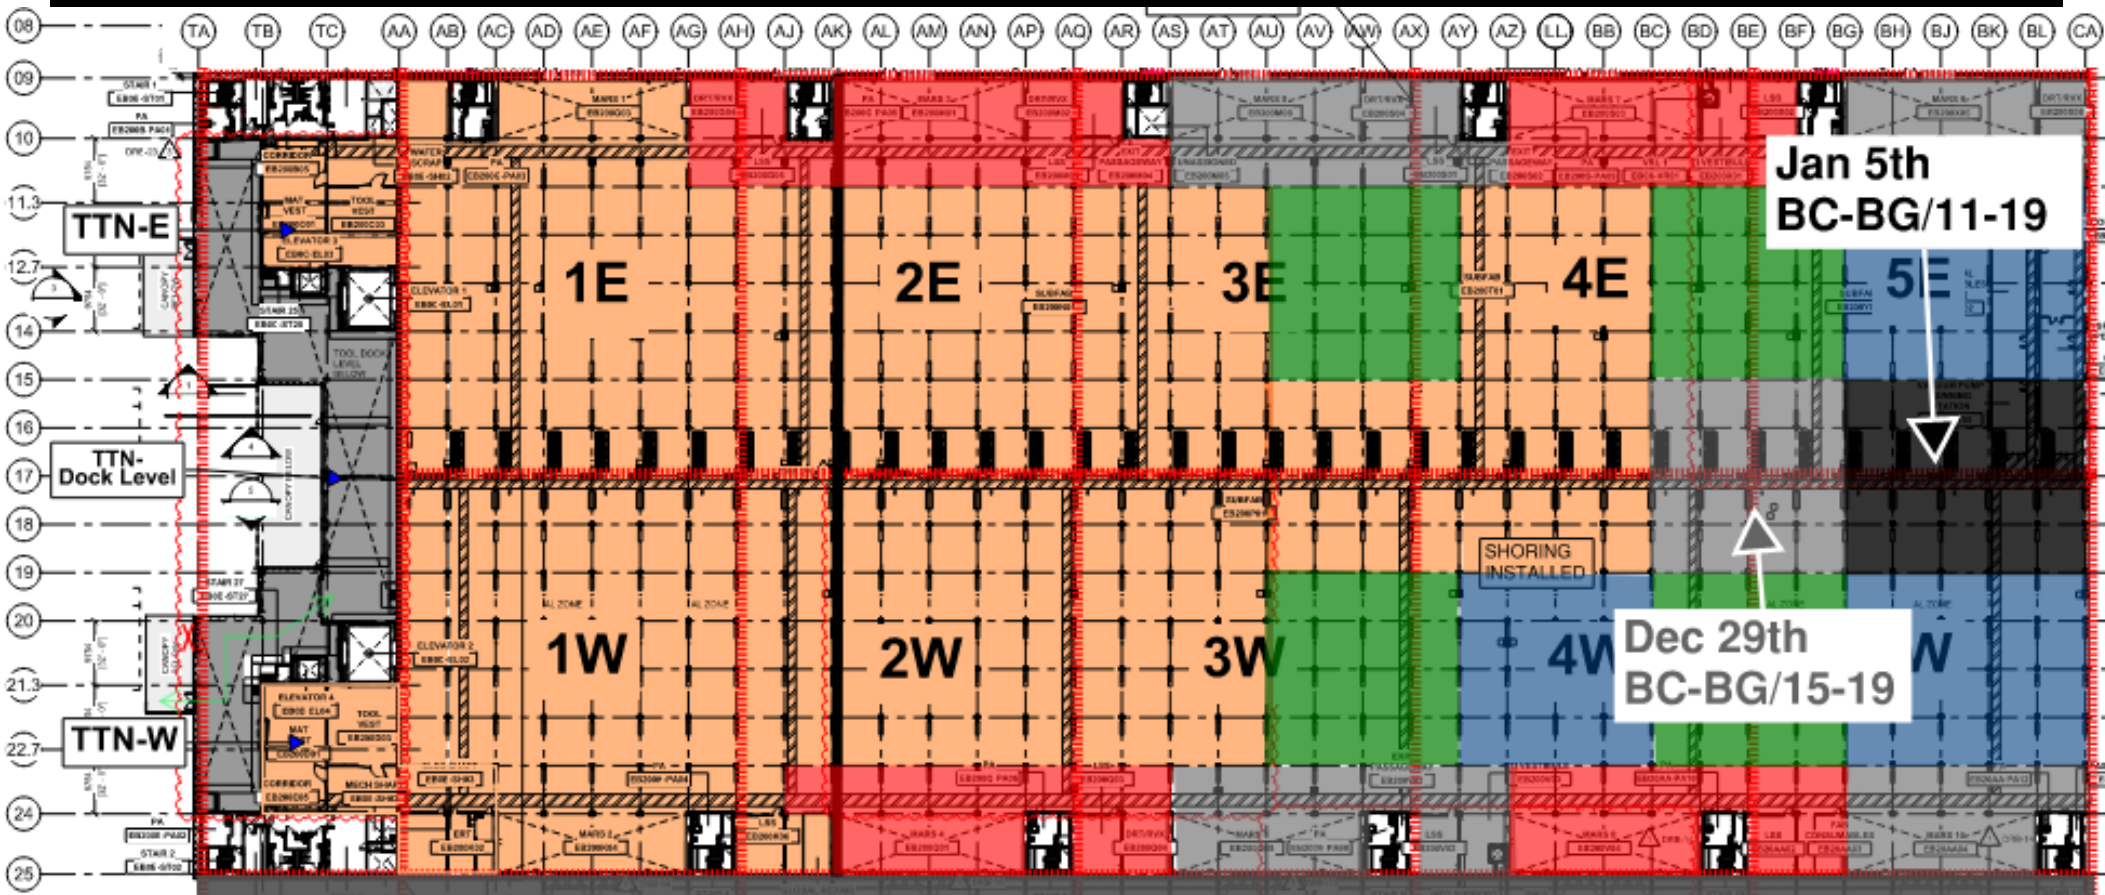


BCT Pressure Test Today

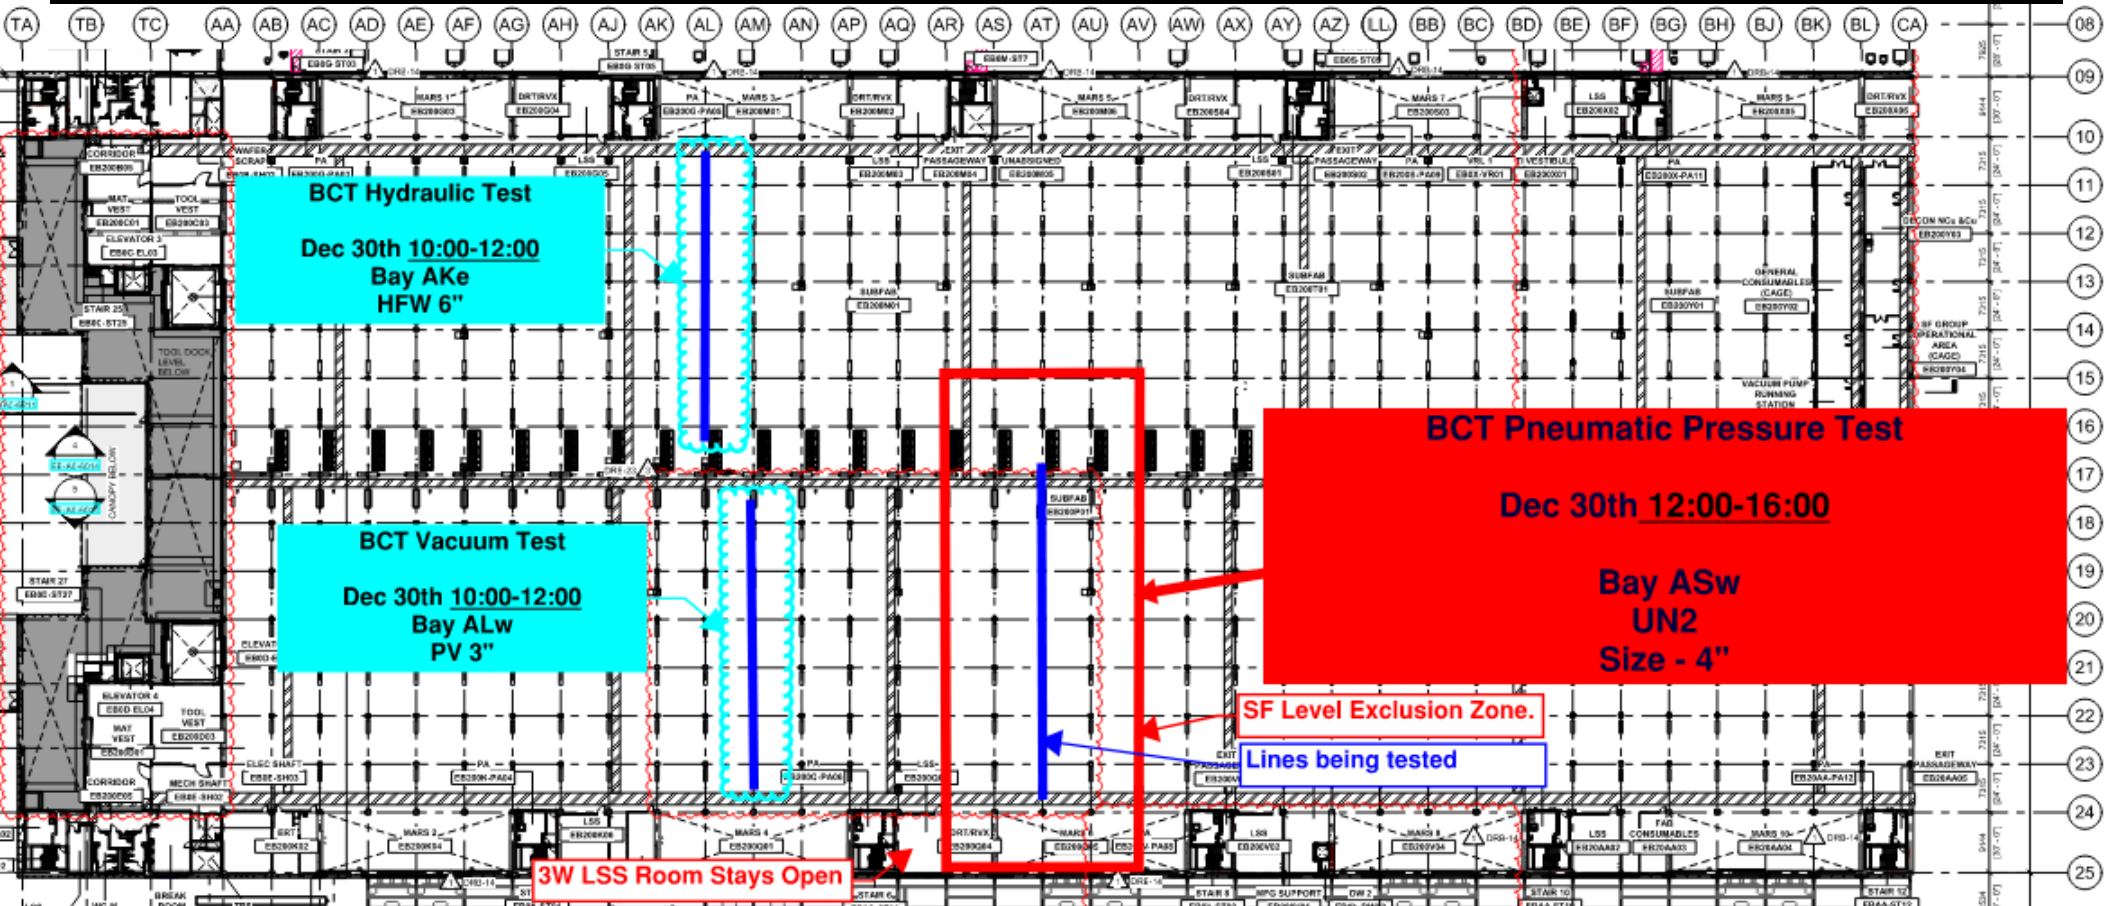


BCT Pressure Test Tomorrow


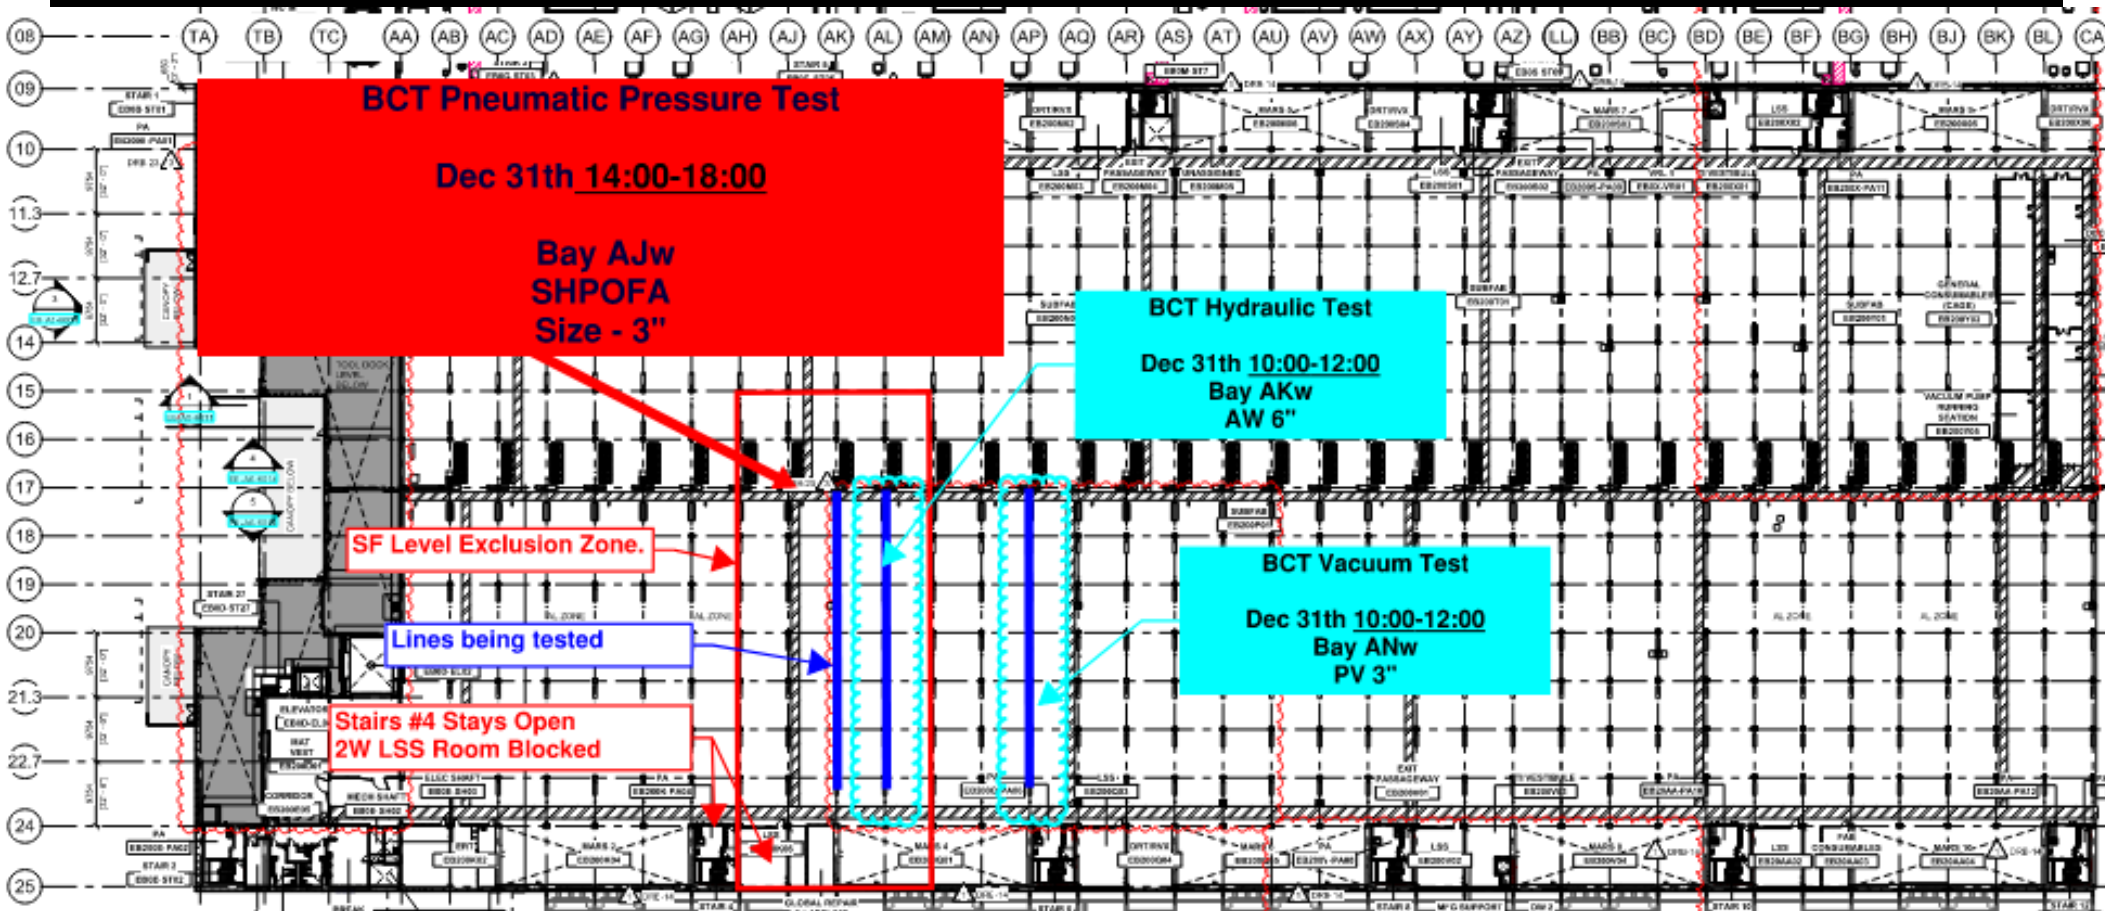




MEPTAGON Pressure Test Today


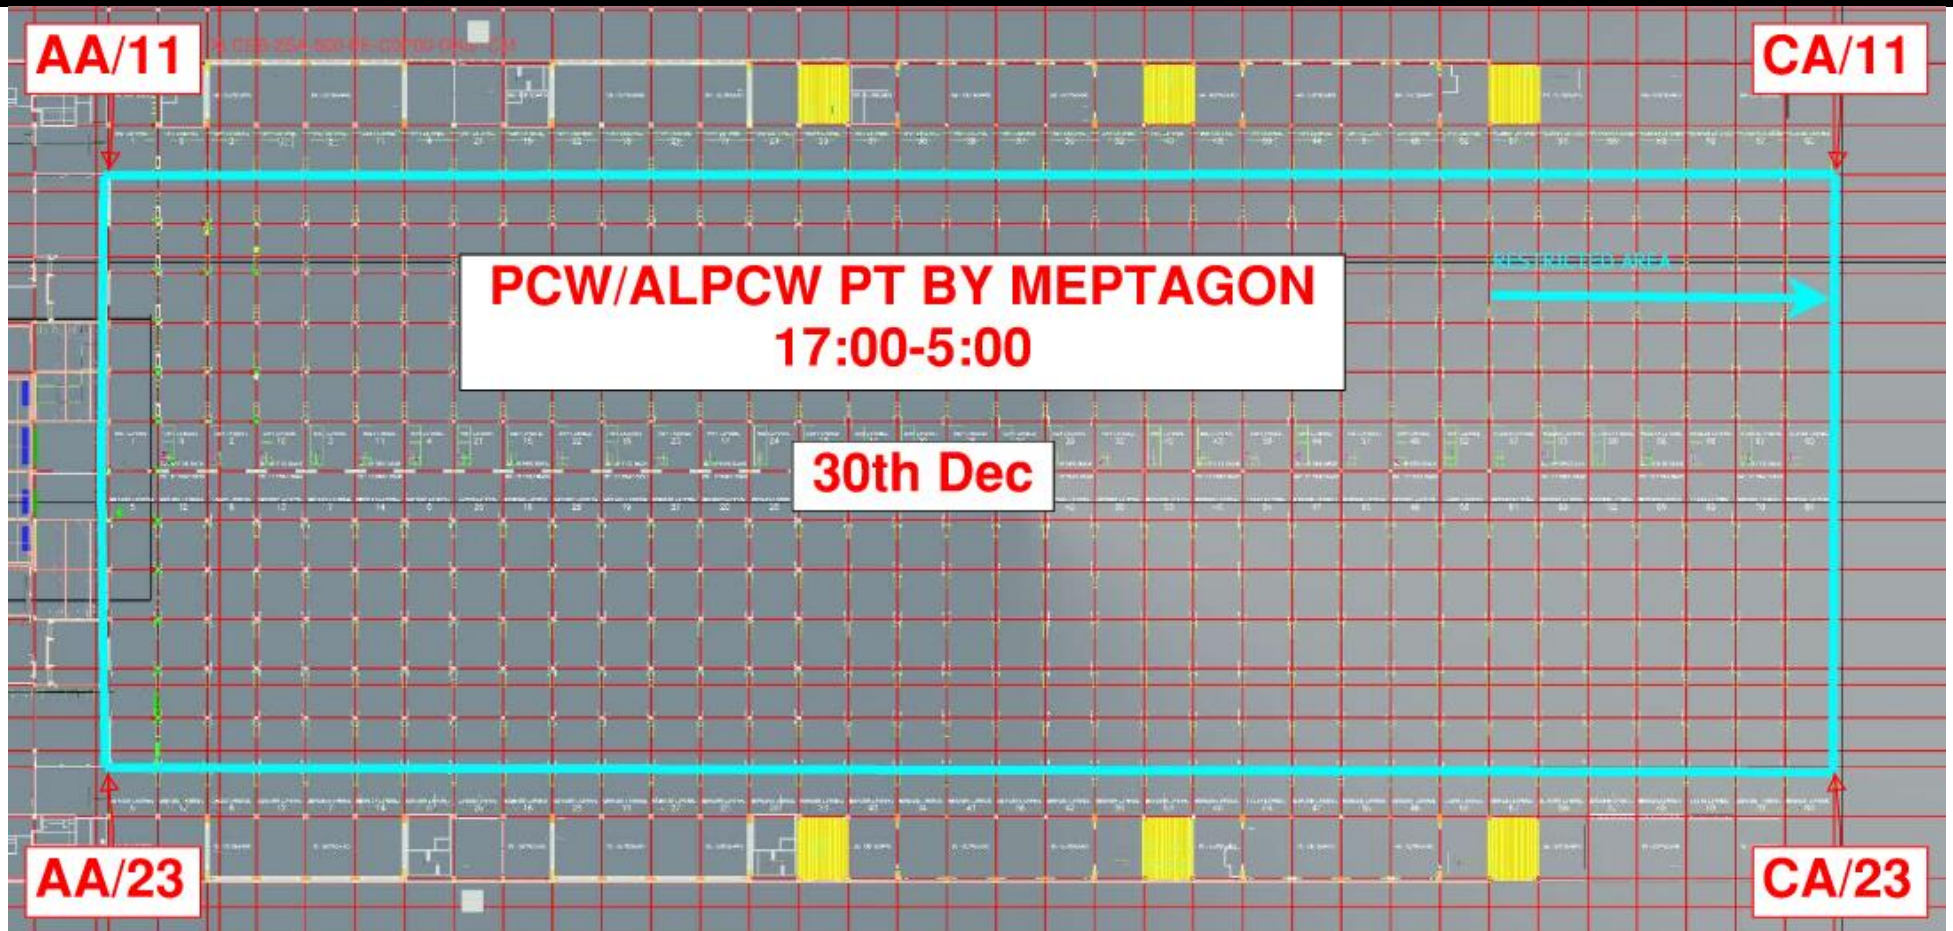



SUBFAB BUILDOUT MOD 2

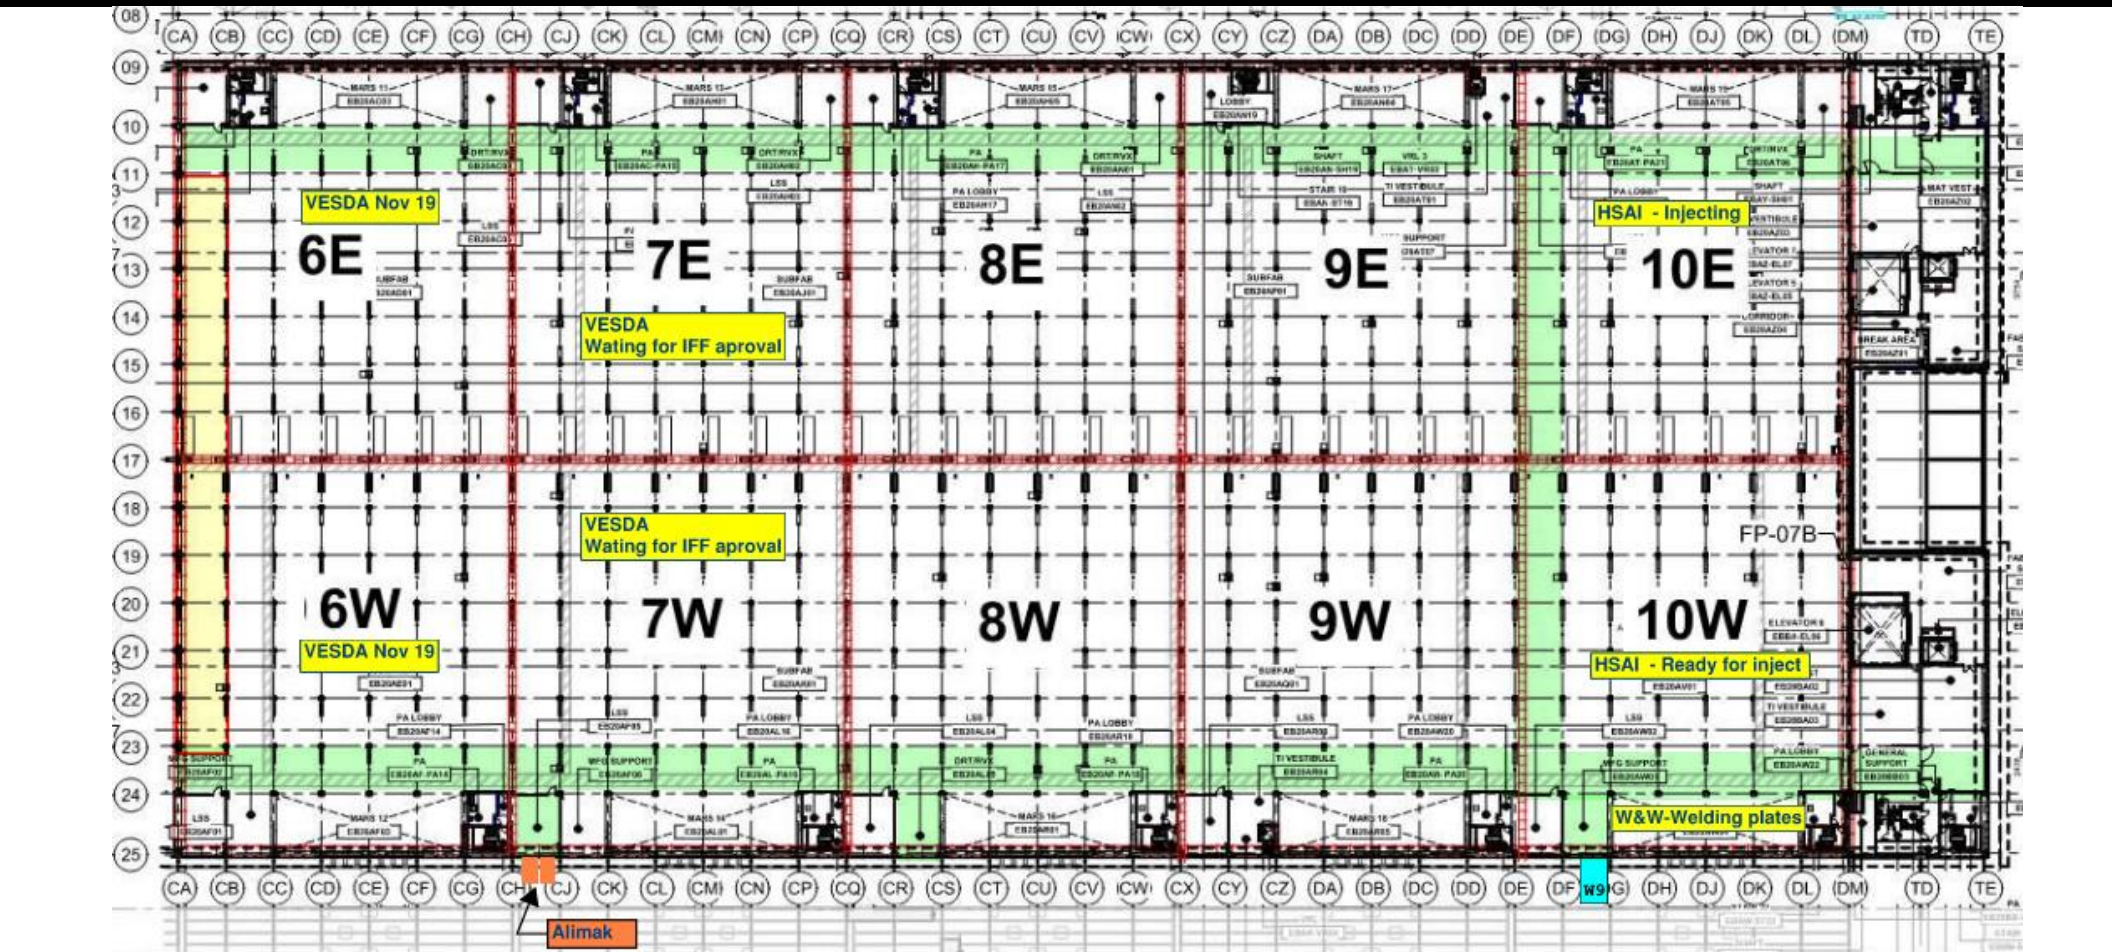

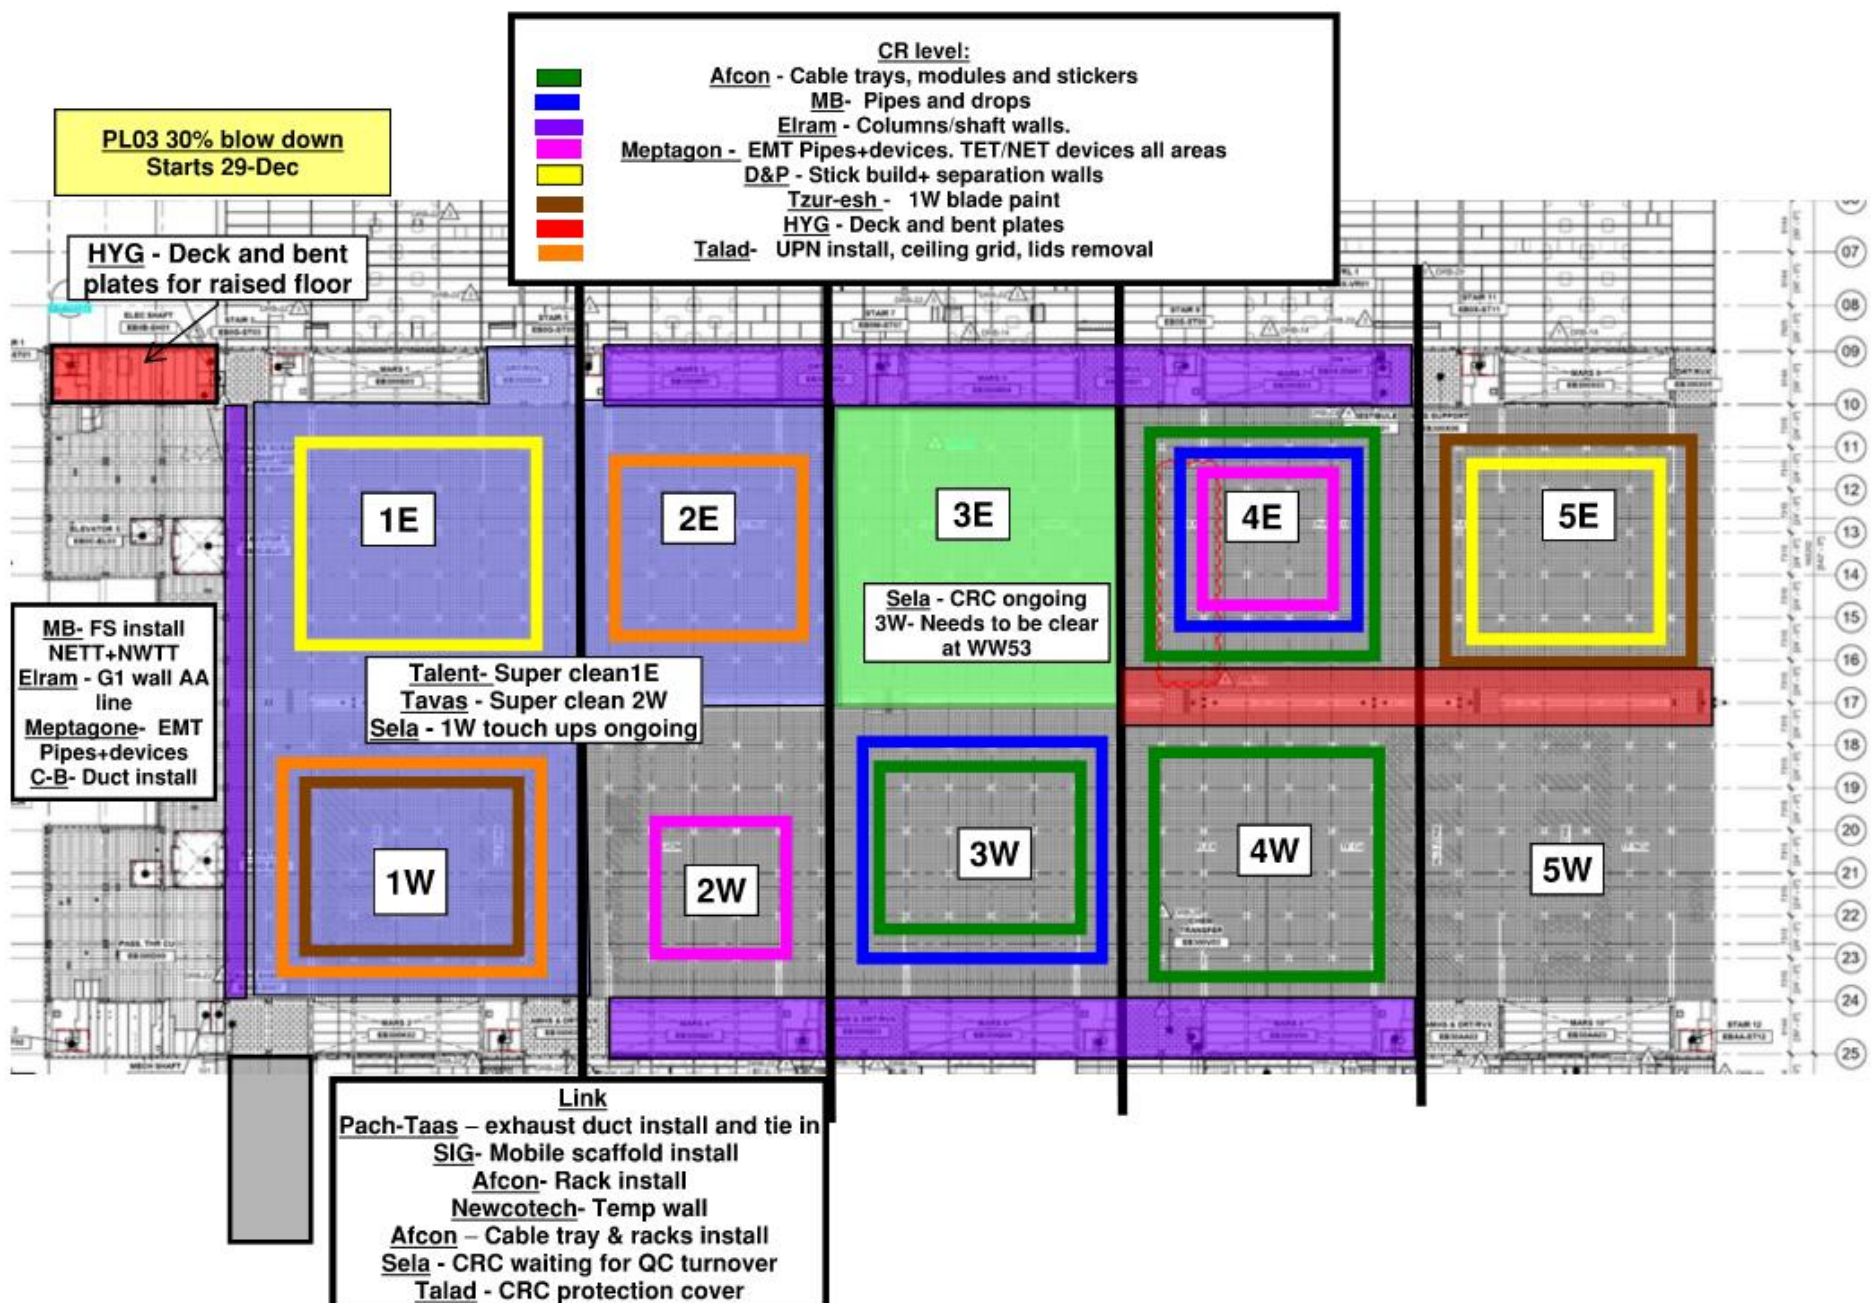

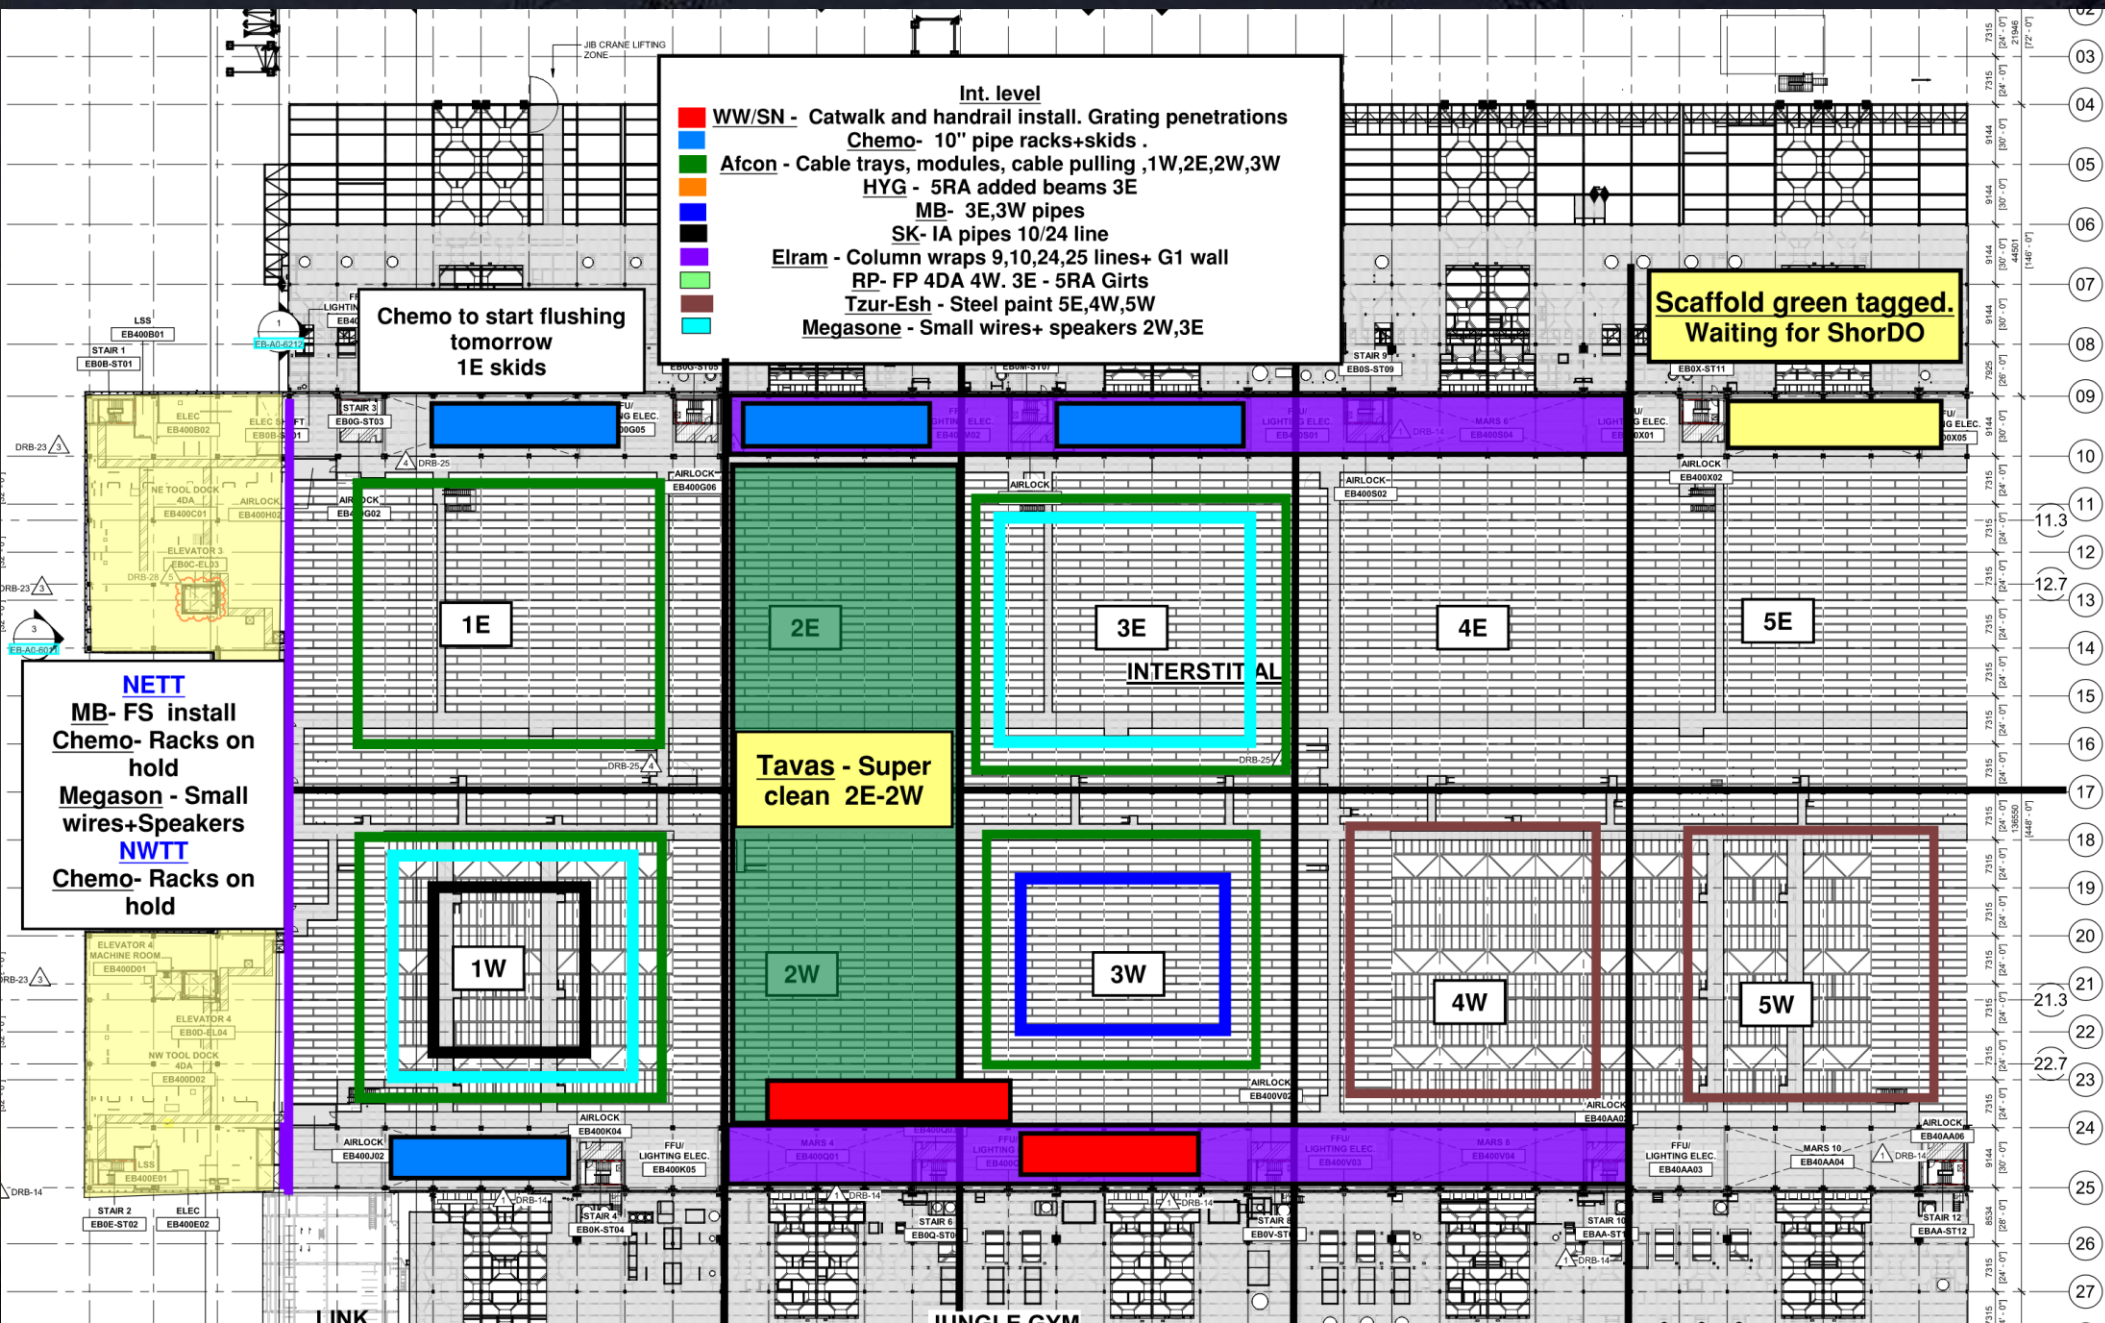

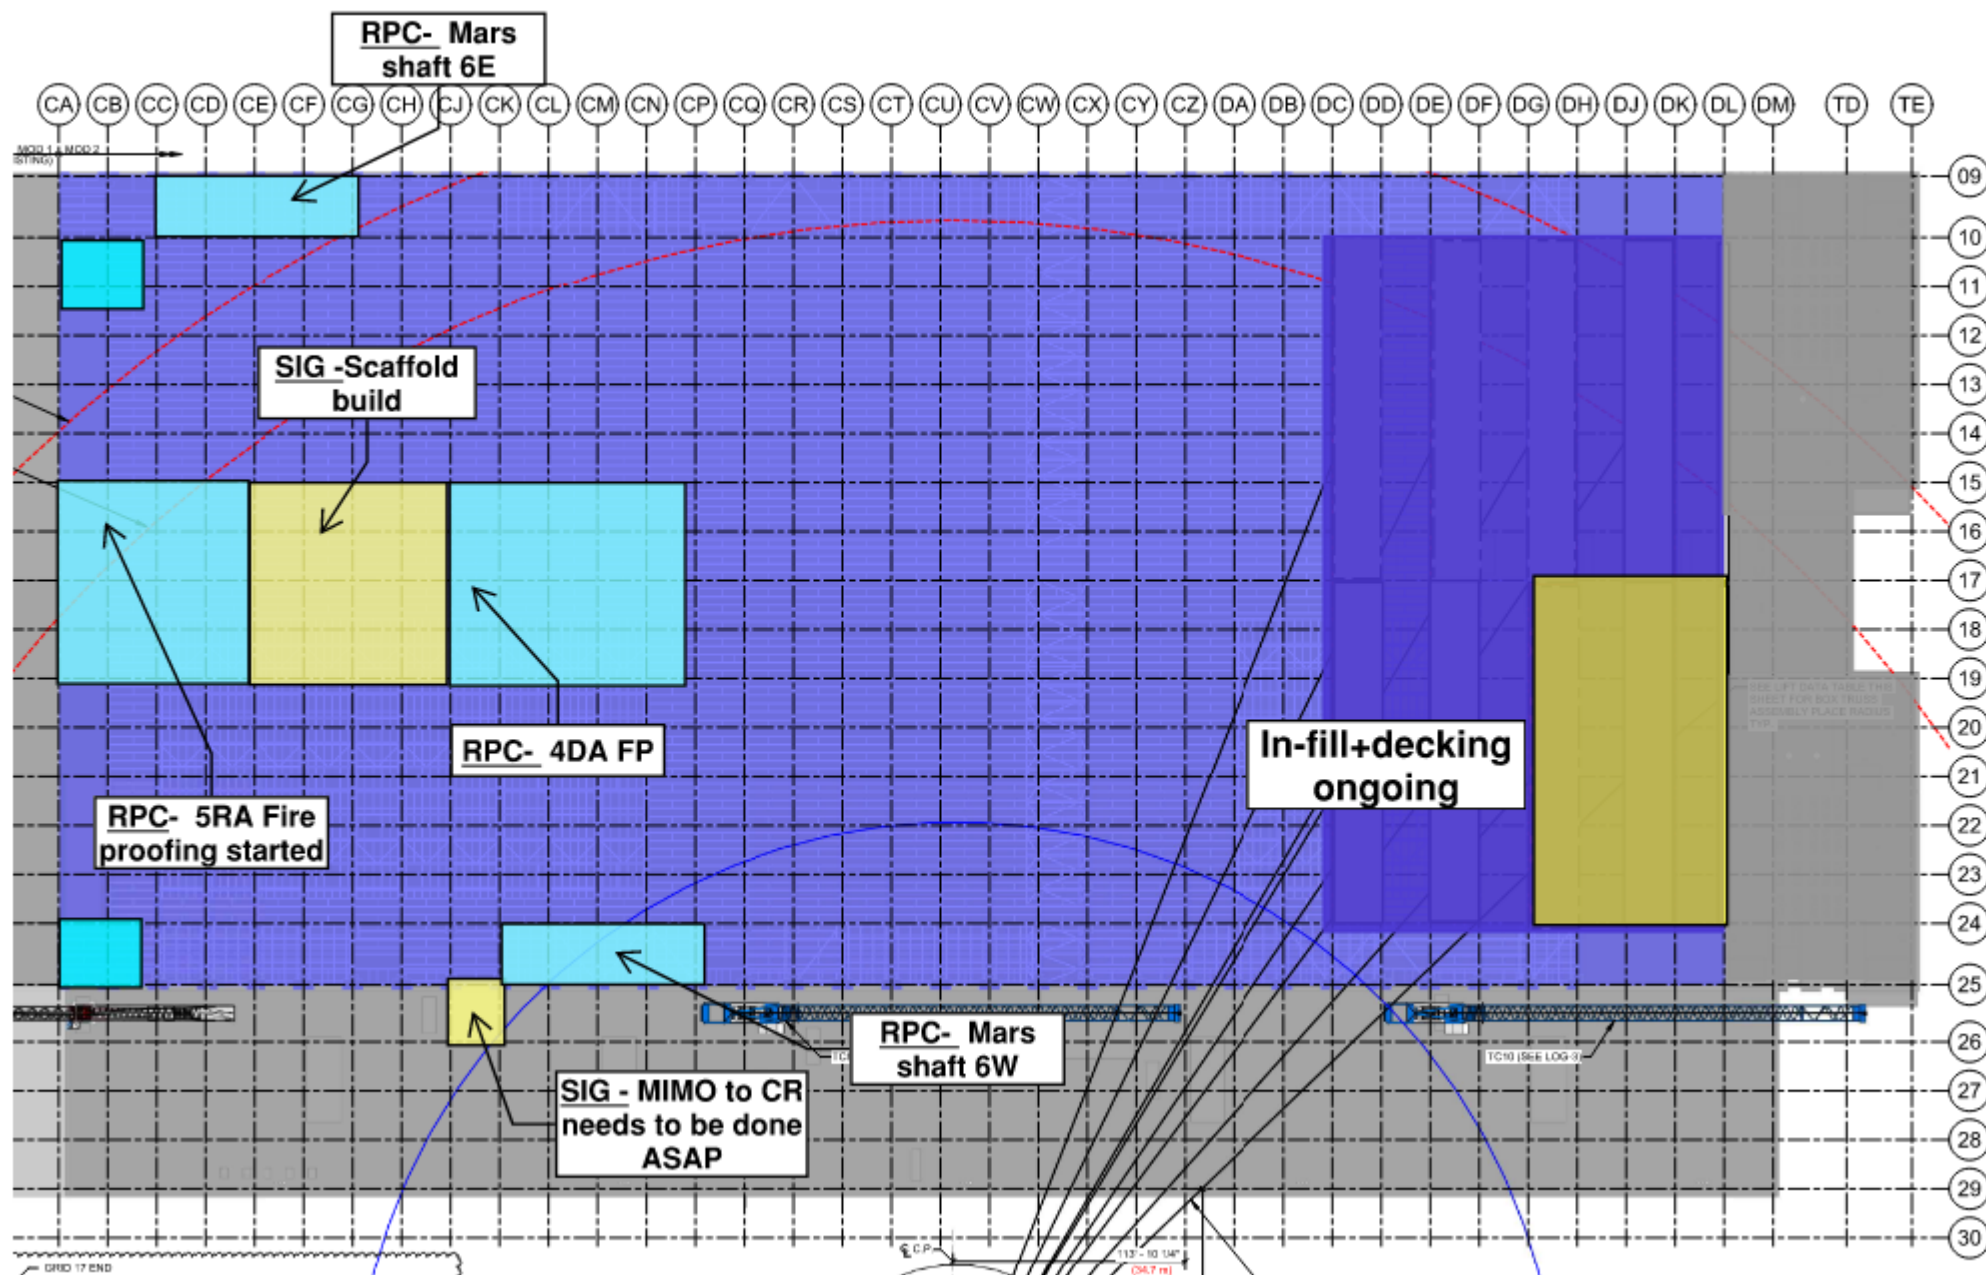

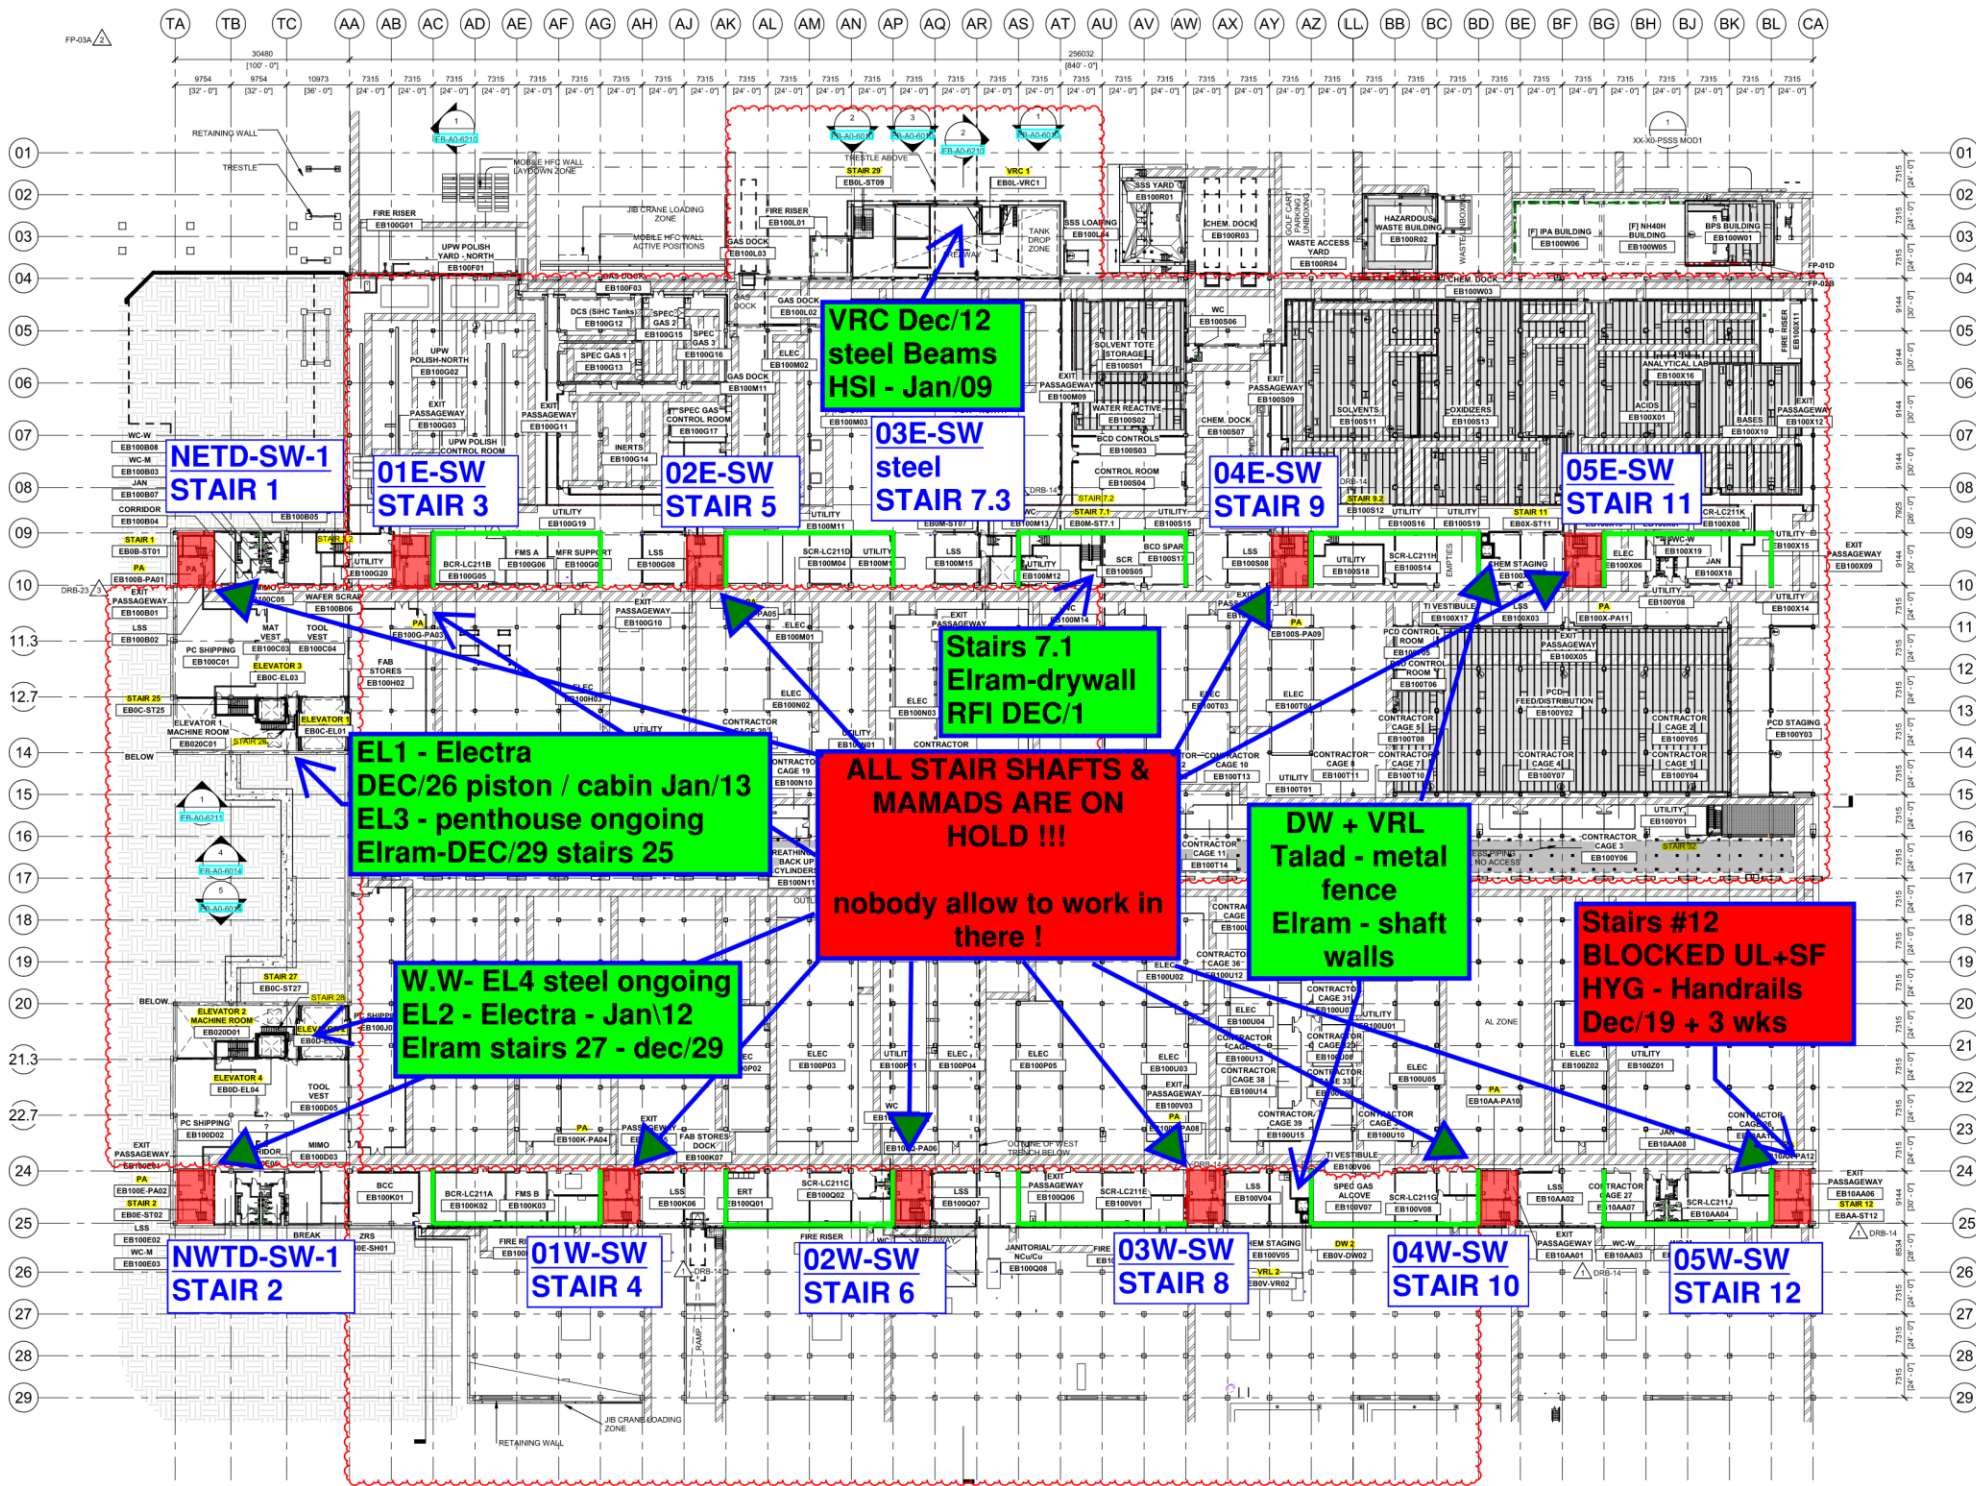

VRC Dec/12
steel Beams
HSI - Jan/09

03E-SW
steel
STAIR 7.3

NETD-SW-1
STAIR 1

01E-SW
STAIR 3

02E-SW
STAIR 5

04E-SW
STAIR 9

05E-SW
STAIR 11

Stairs 7.1
Eiram-drywall
RFI DEC/1

EL1 - Electra
DEC/26 piston / cabin Jan/13
EL3 - penthouse ongoing
Eiram-DEC/29 stairs 25

ALL STAIR SHAFTS &
MAMADS ARE ON
HOLD !!!
nobody allow to work in
there !

DW + VRL
Talad - metal
fence
Eiram - shaft
walls

Stairs #12
BLOCKED UL+SF
HYG - Handrails
Dec/19 + 3 wks

W.W- EL4 steel ongoing
EL2 - Electra - Jan/12
Eiram stairs 27 - dec/29

NWTD-SW-1
STAIR 2

01W-SW
STAIR 4

02W-SW
STAIR 6

03W-SW
STAIR 8

04W-SW
STAIR 10

05W-SW
STAIR 12

Siding - West FAB - JYG


BLOWDOWN 30%

	TA	TE	TC	RA	RE	AC	AD	AE	AF	AG	AH	AI	AK	AL	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BK	BL	CA			
		1001 / 1002			501 / 502		611 / 612				621 / 622			631 / 632						641 / 642			651 / 652				811 / 812				821 / 822			831 / 832				841 / 842			851 / 852	
Total		28	28	28	16	16	31	31	31	31	31	31	31	31	30	31	31	31	31	31	31	24	24	24	25	31	31	31	31	25	25	25	19	19	19	31	28	23	23	23	19	
Invallied		100%	100%	96%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	90%	90%	90%	100%	100%	87%	77%	77%	8%	100%	100%	100%	8%	8%	8%	6%	6%	6%	100%	90%	74%	74%	74%	6%		
SRA																0	0	0			0	0	0	0					0	0	0	0	0		0	0	0	0	0			
																0	0	0			0	0	0	0					0	0	0	0	0		0	0	0	0	0			
																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			
ADA																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			
																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			
3FK																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			
3FA																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			
																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			
2SA SF																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			
																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			
UL																					0	0	0	0					0	0	0	0	0		0	0	0	0	0			


Siding - East FAB - PSSS


BLOWDOWN 30%

[illegible]

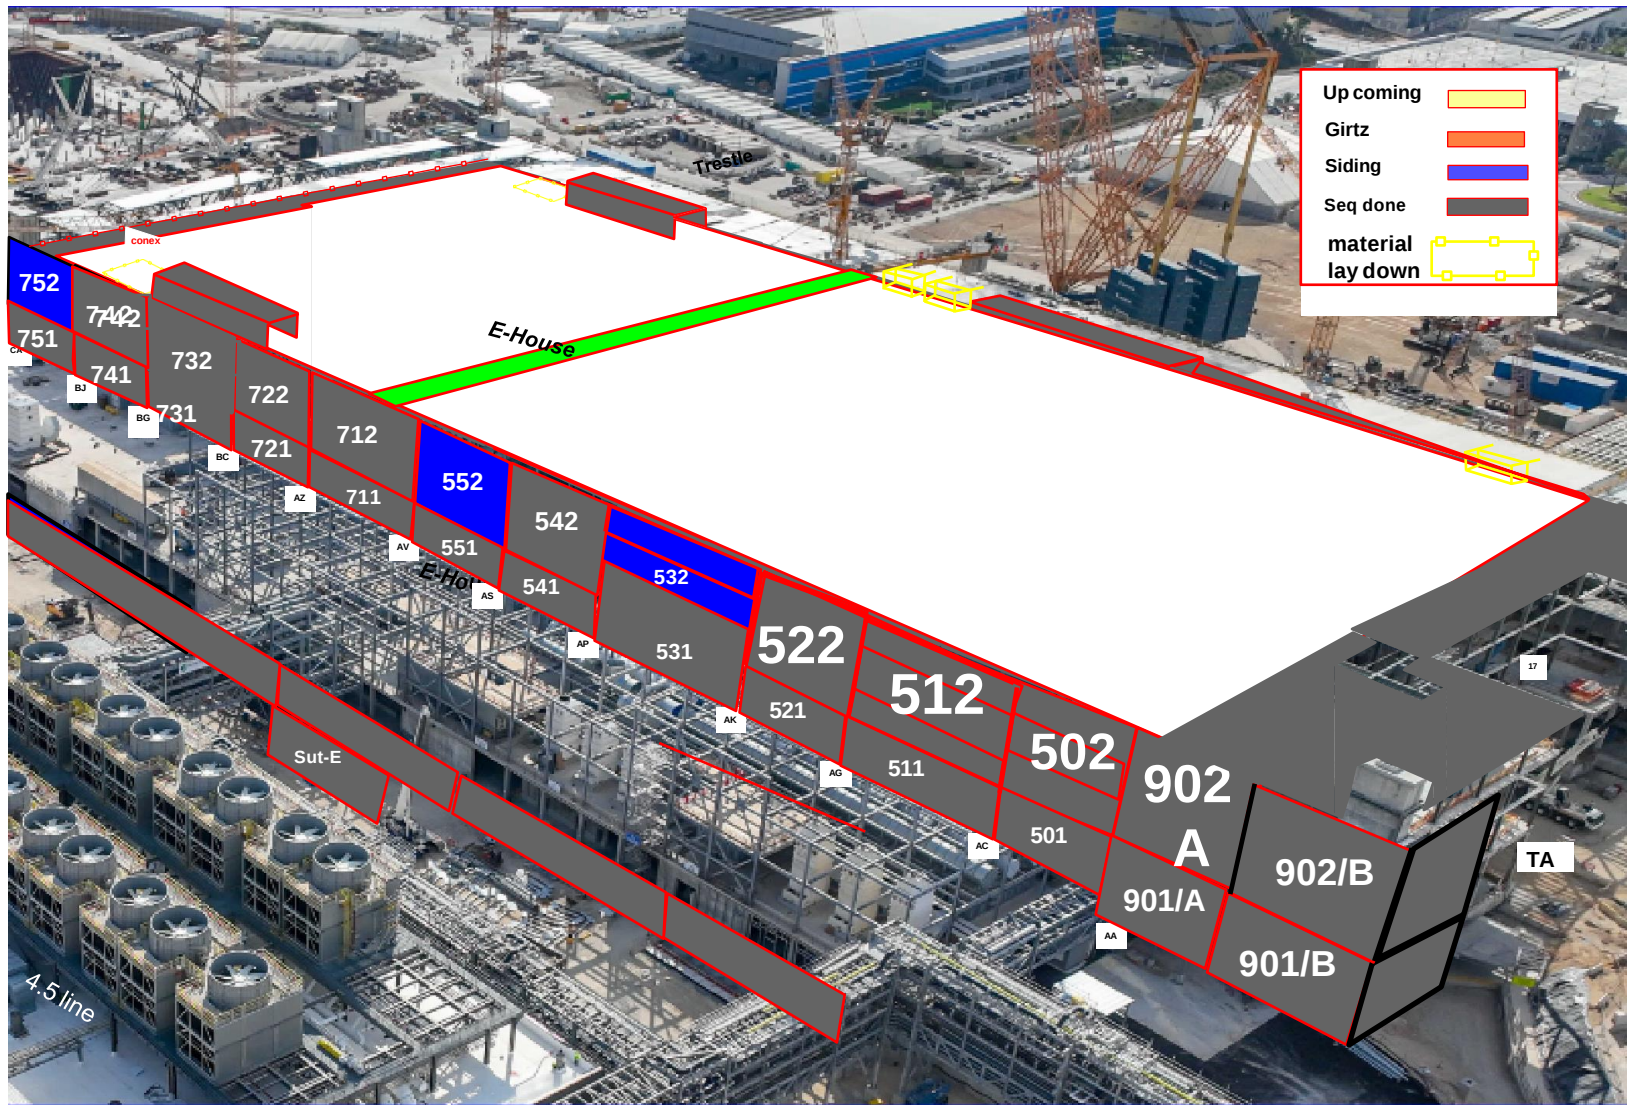

Walk path

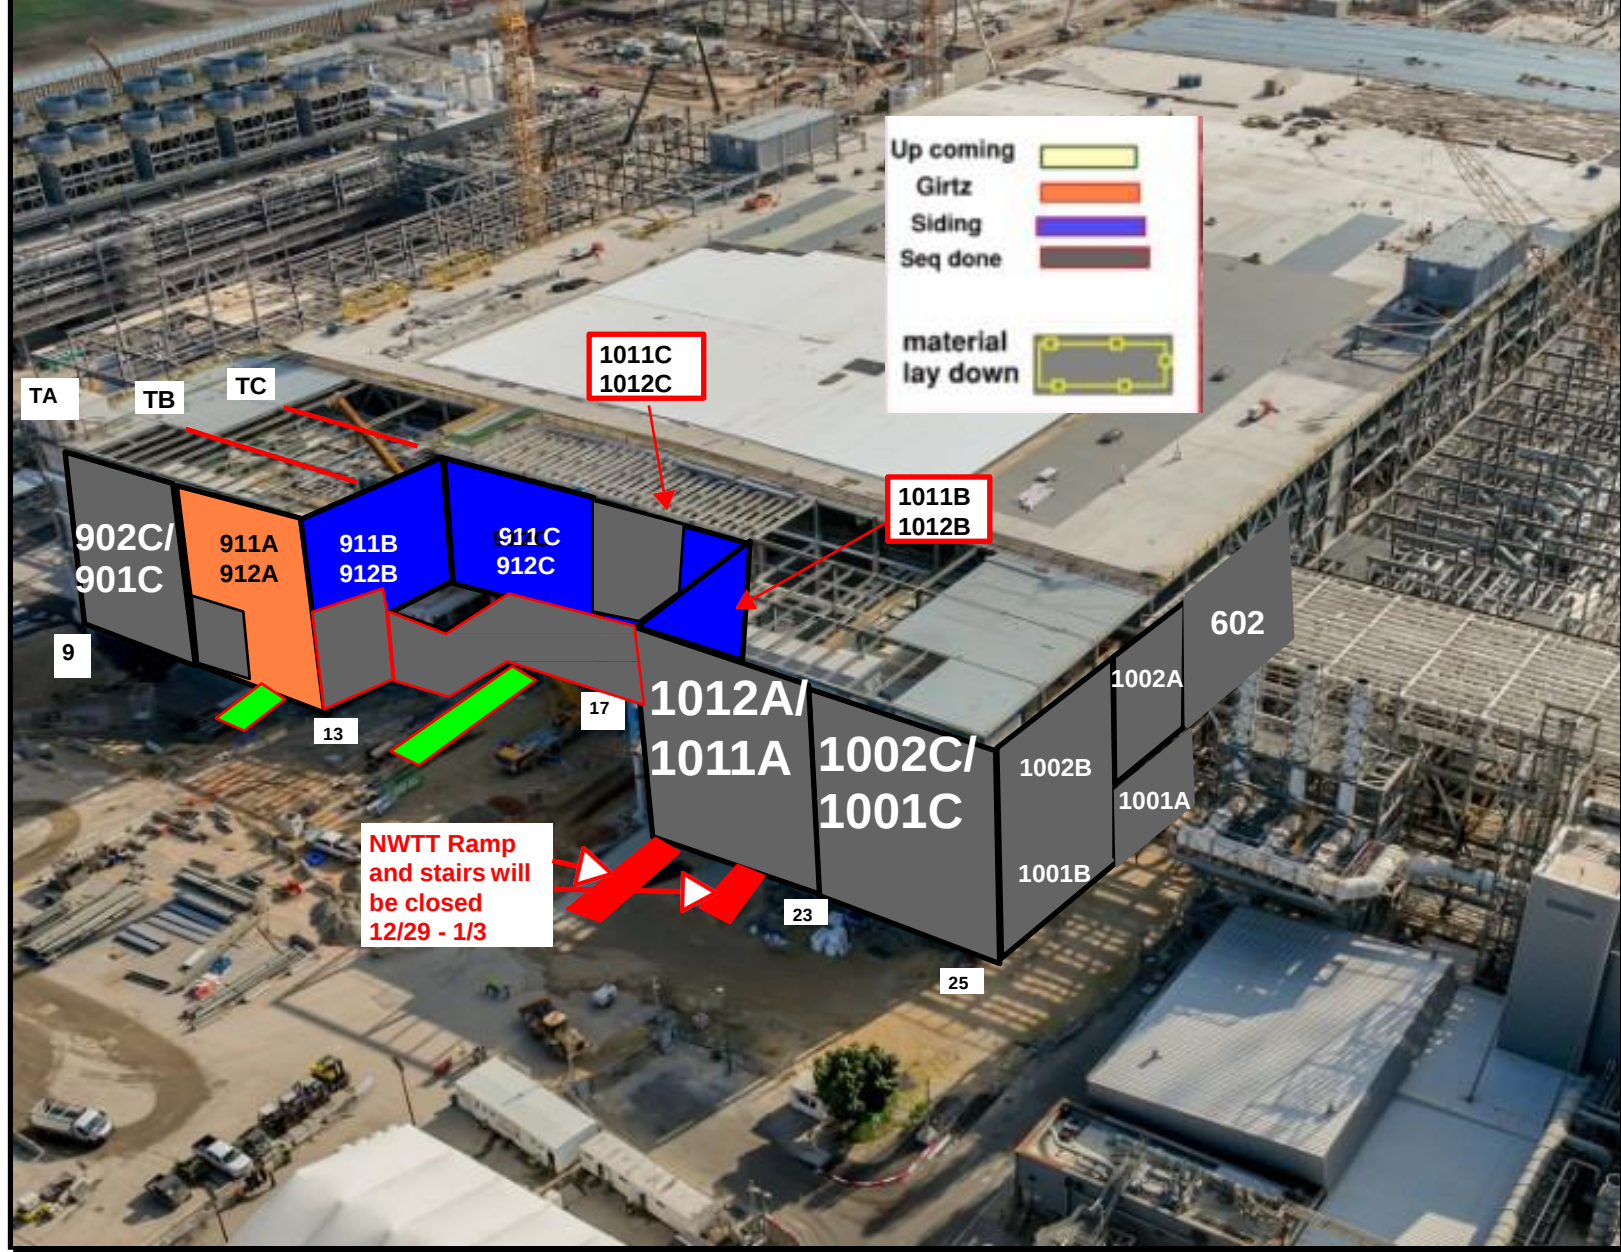


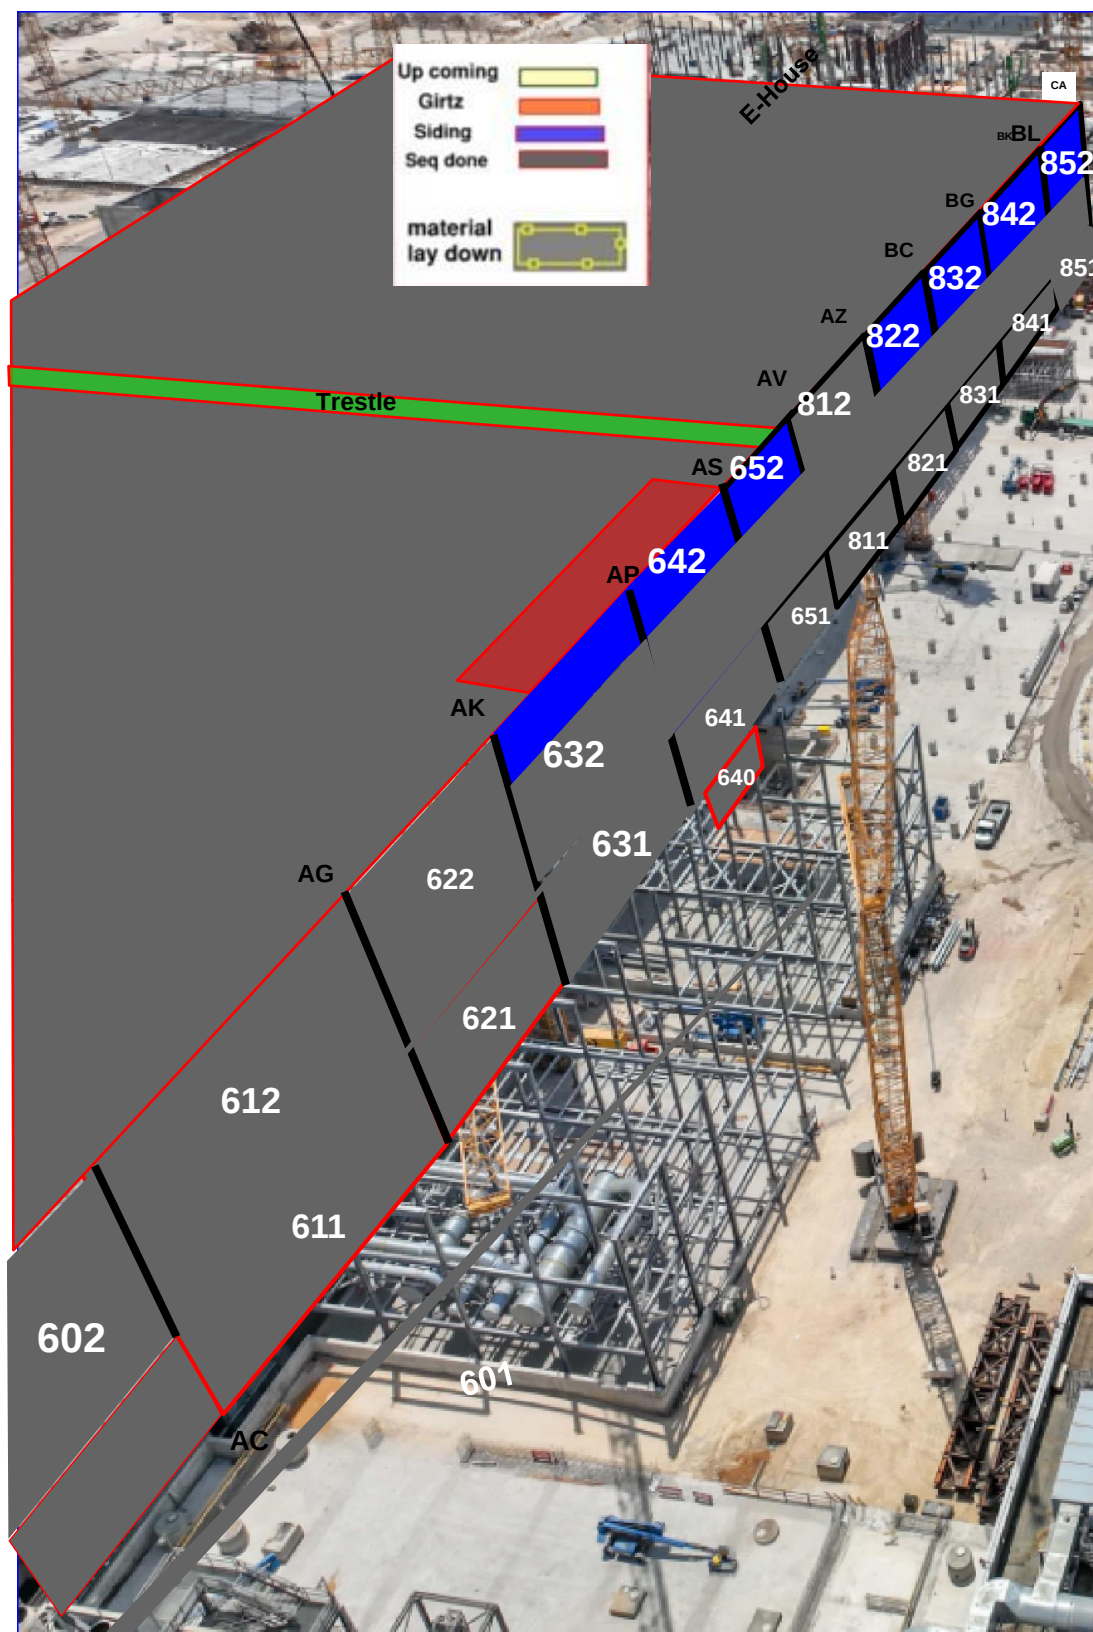

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

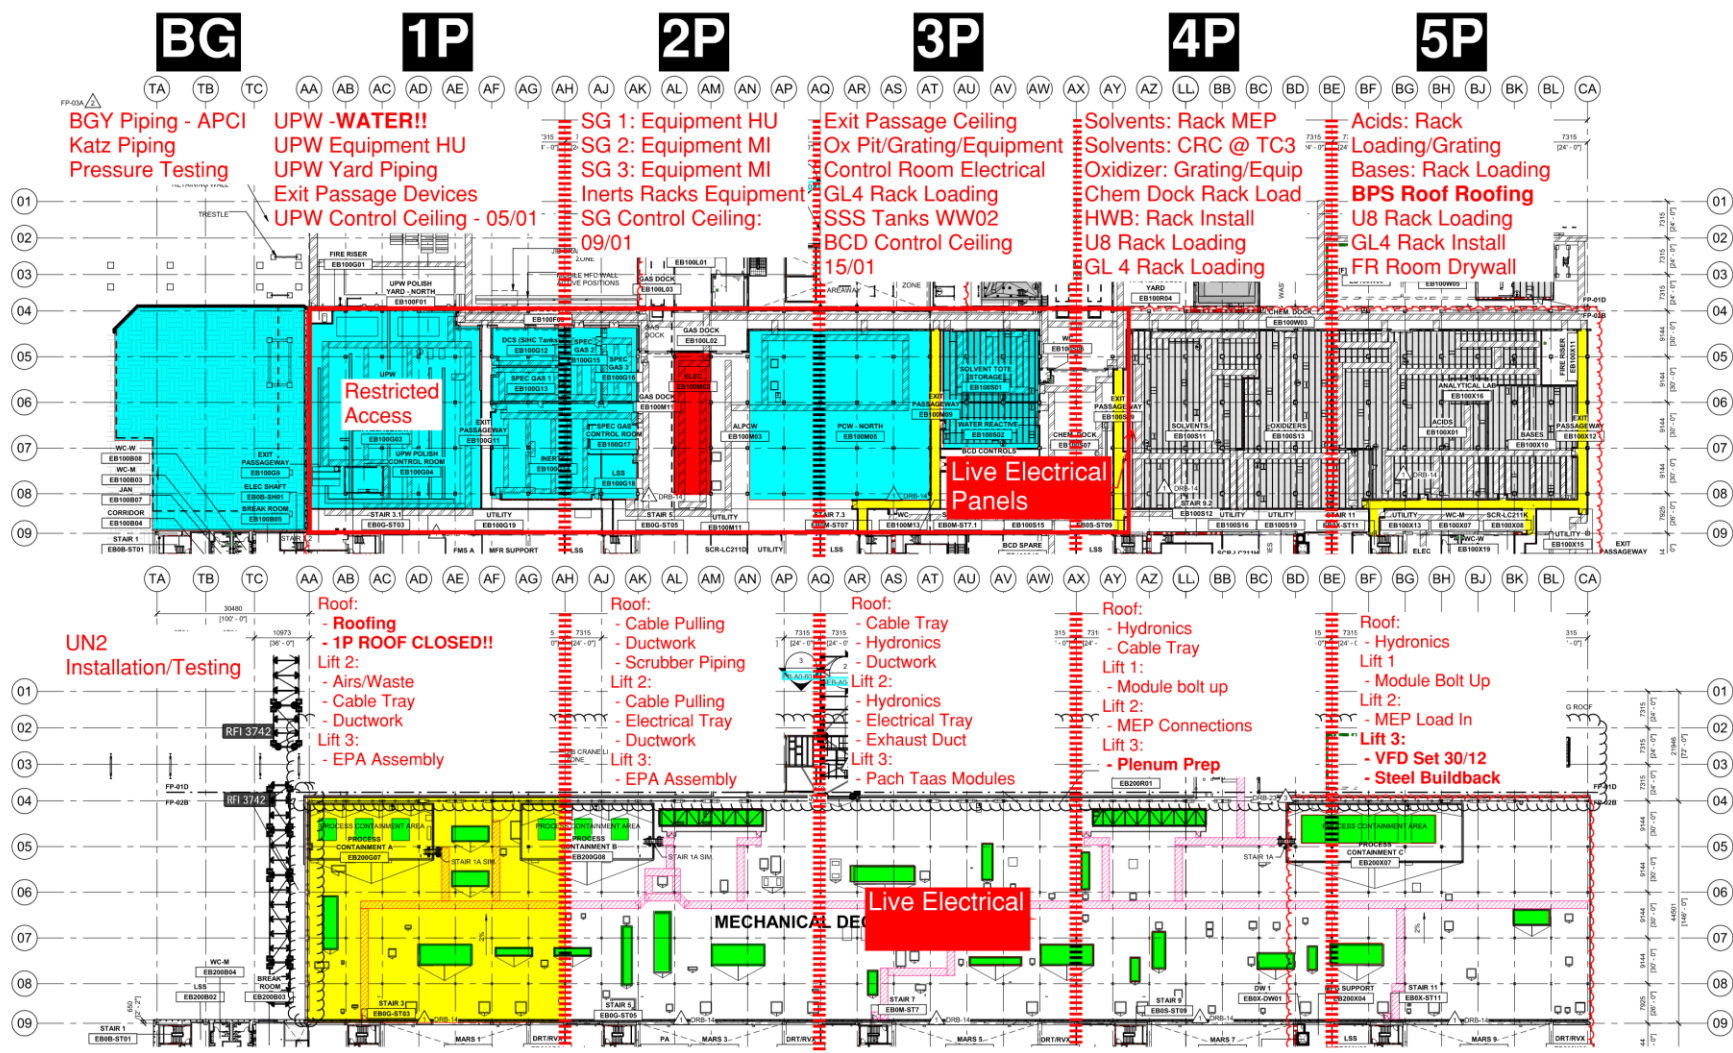


PSSS.2

Utility Level
1YA

PSSS Roof
2SA

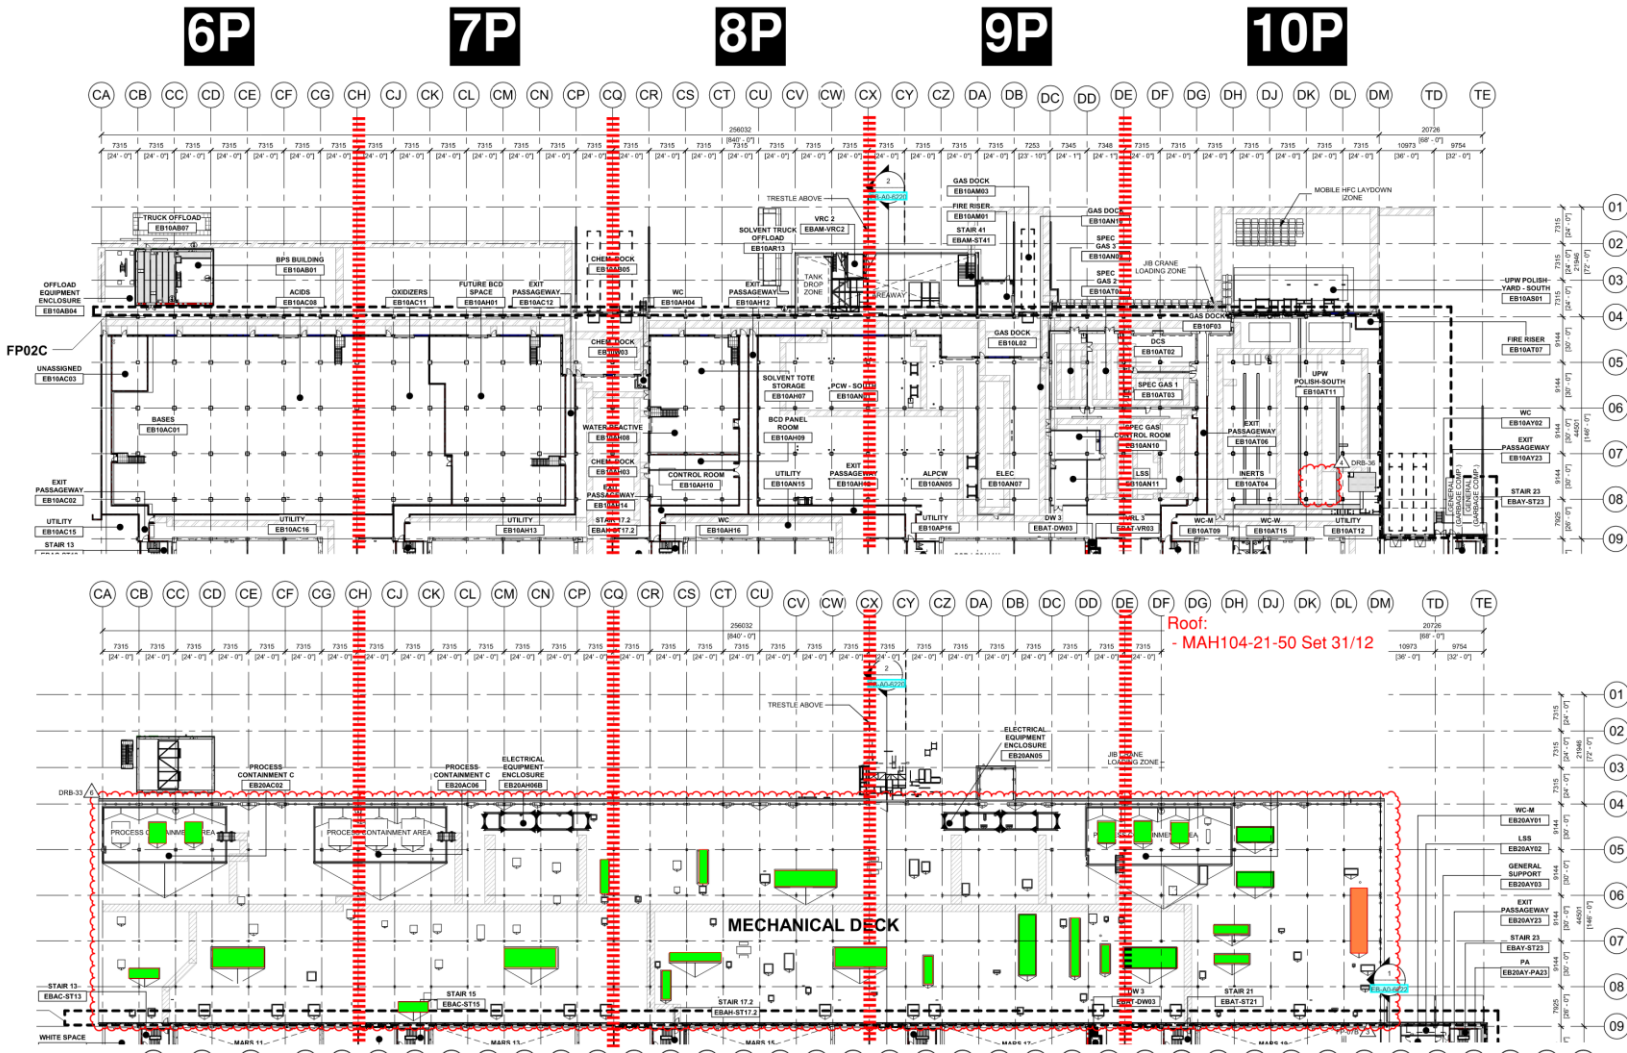


3800
Build
22nd_
30th

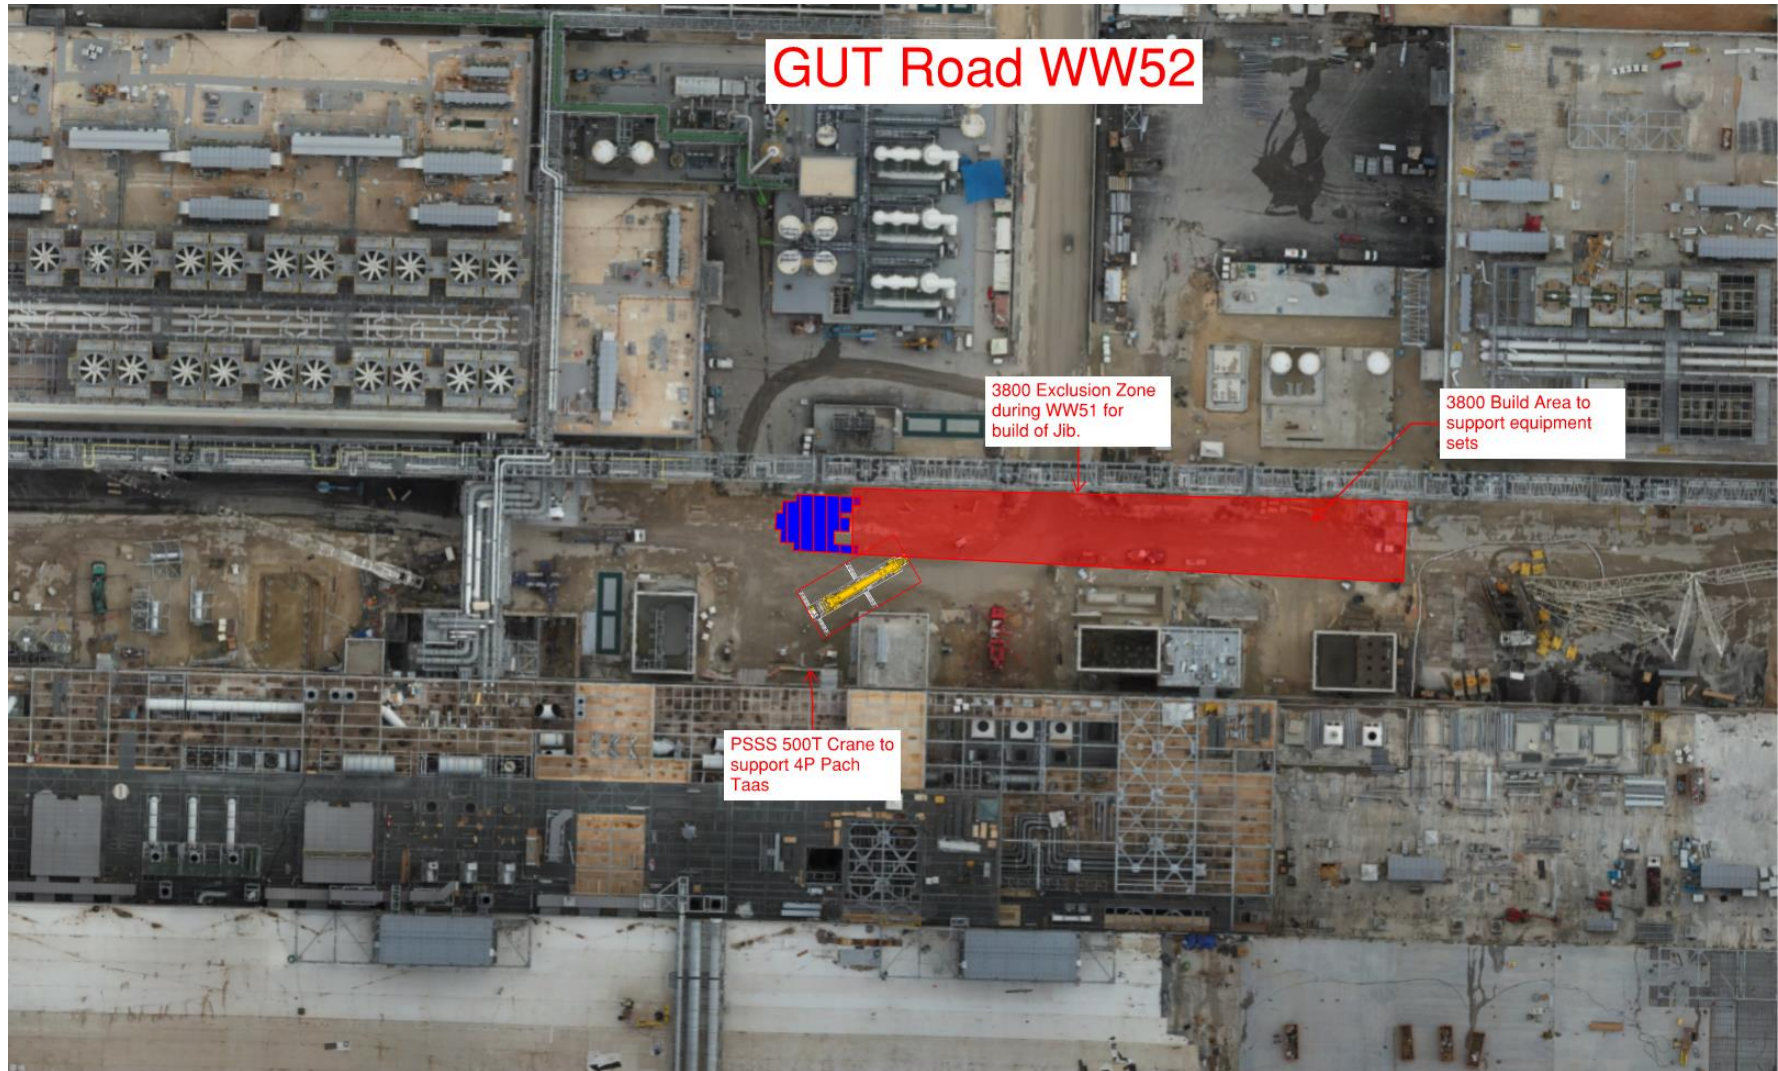

5P

PSSS Roof 2SA

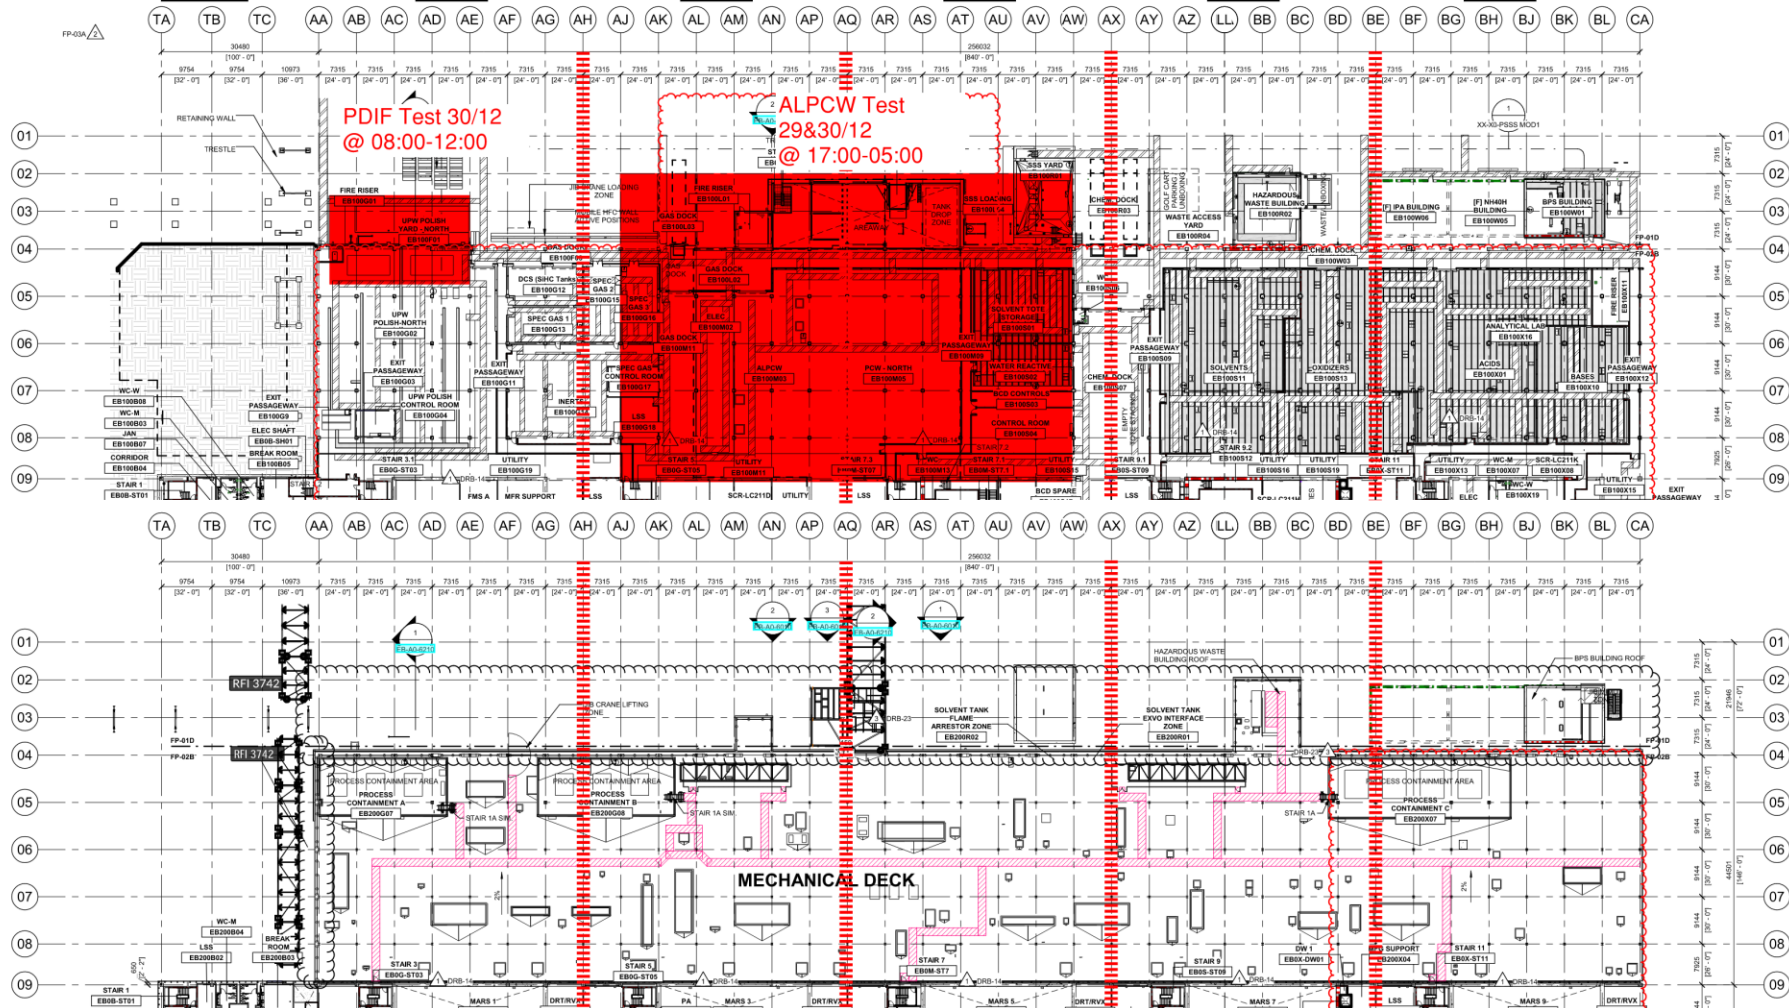





WJG 01J, 02J LIFT 2 & 3






WJG 03J, 04J, 05J LIFT 2 & 3

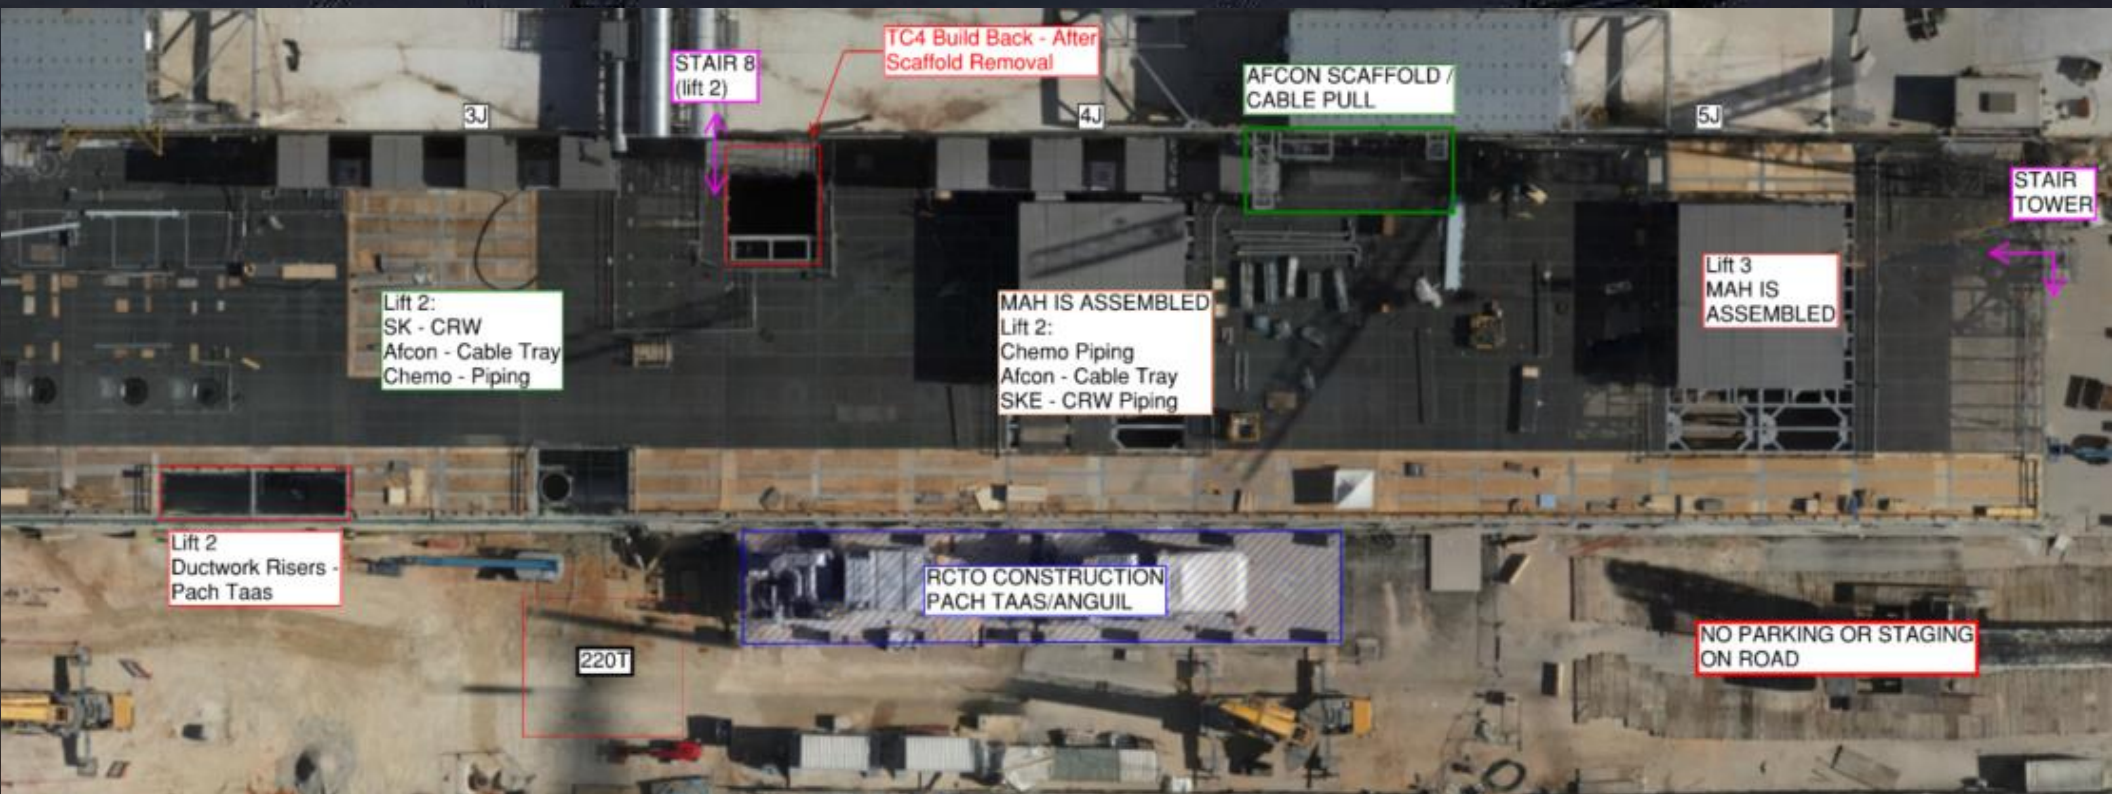


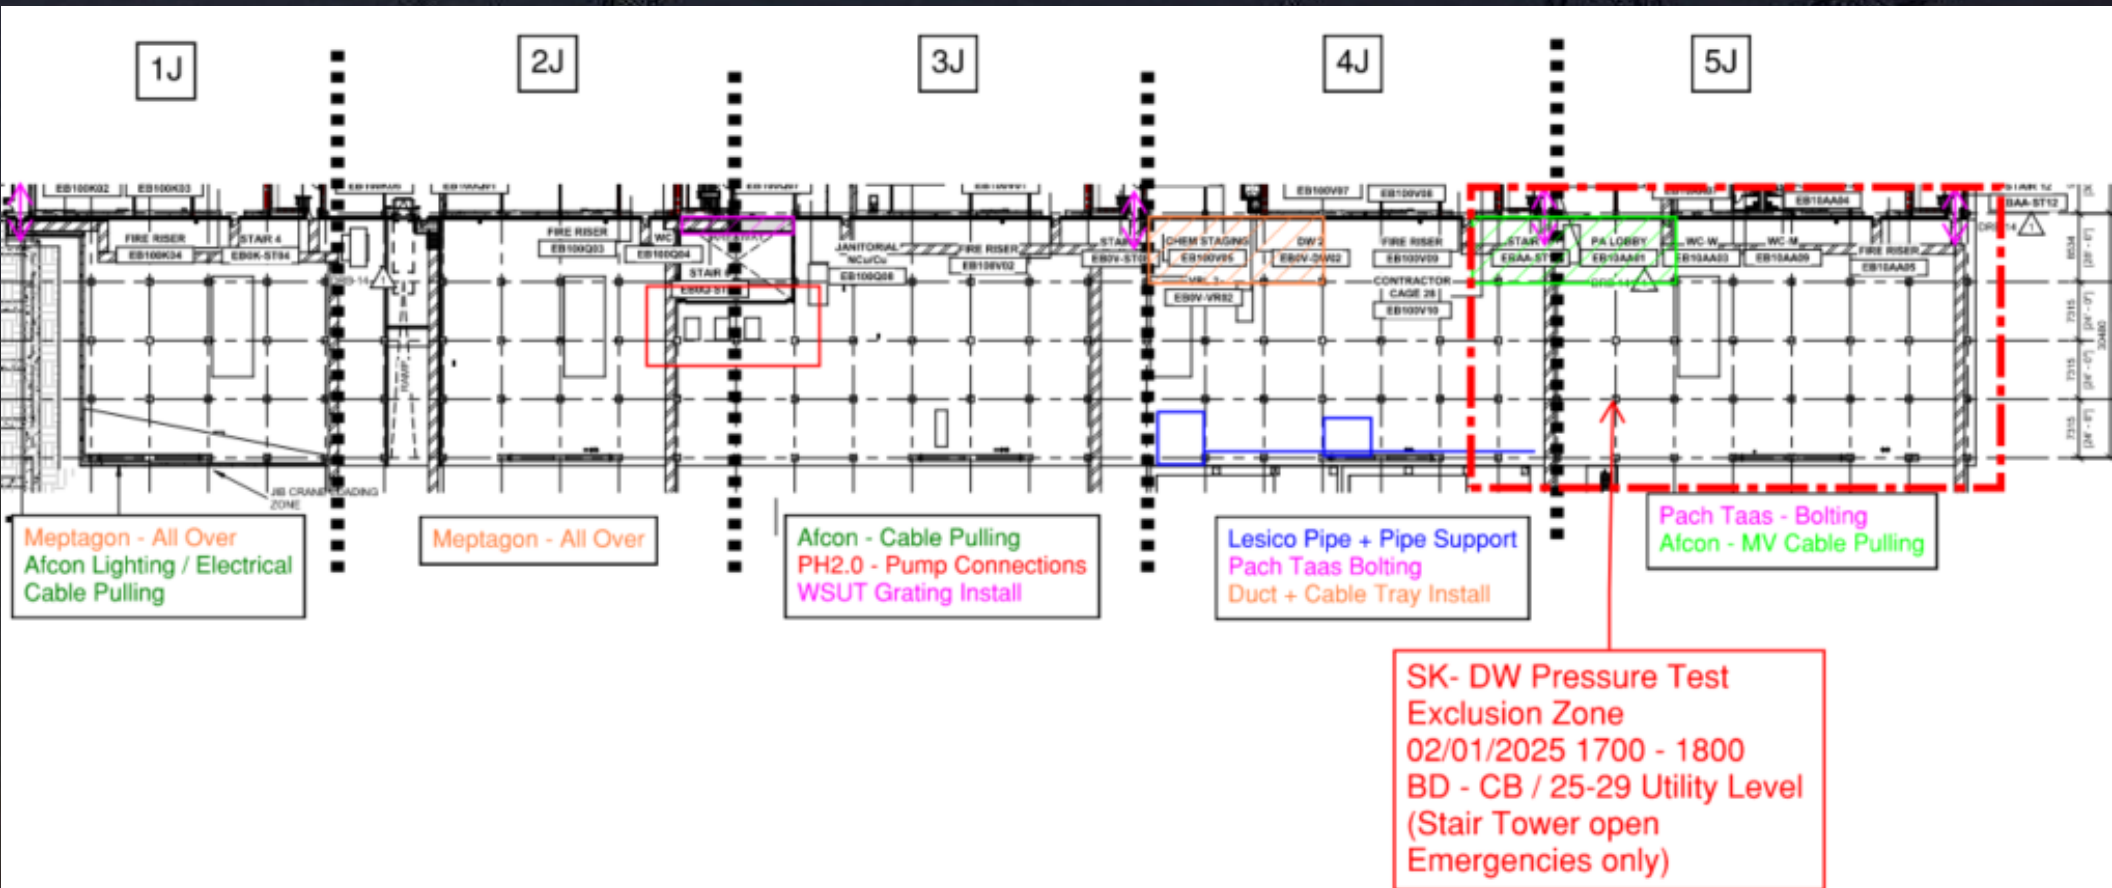

CUB 1

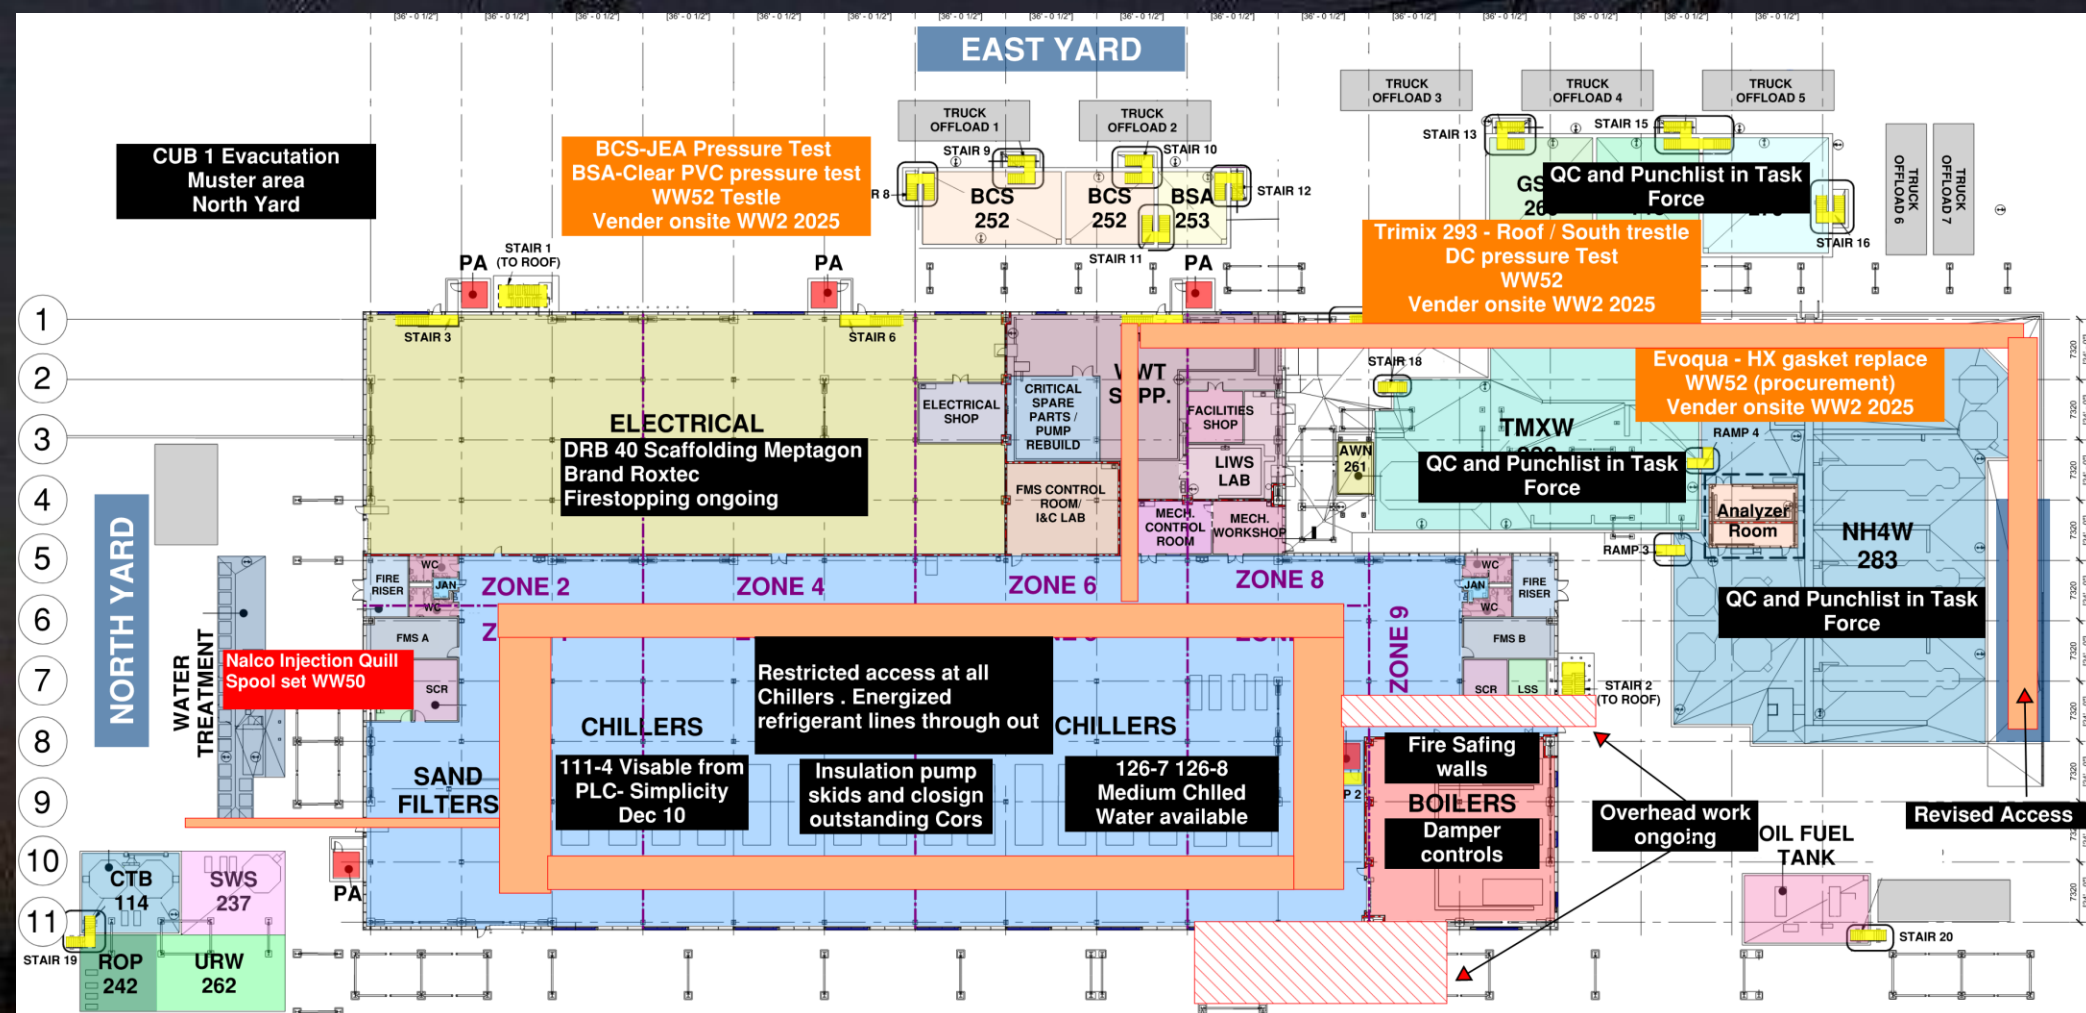

CUB 1 – EXTERIOR/ROOF

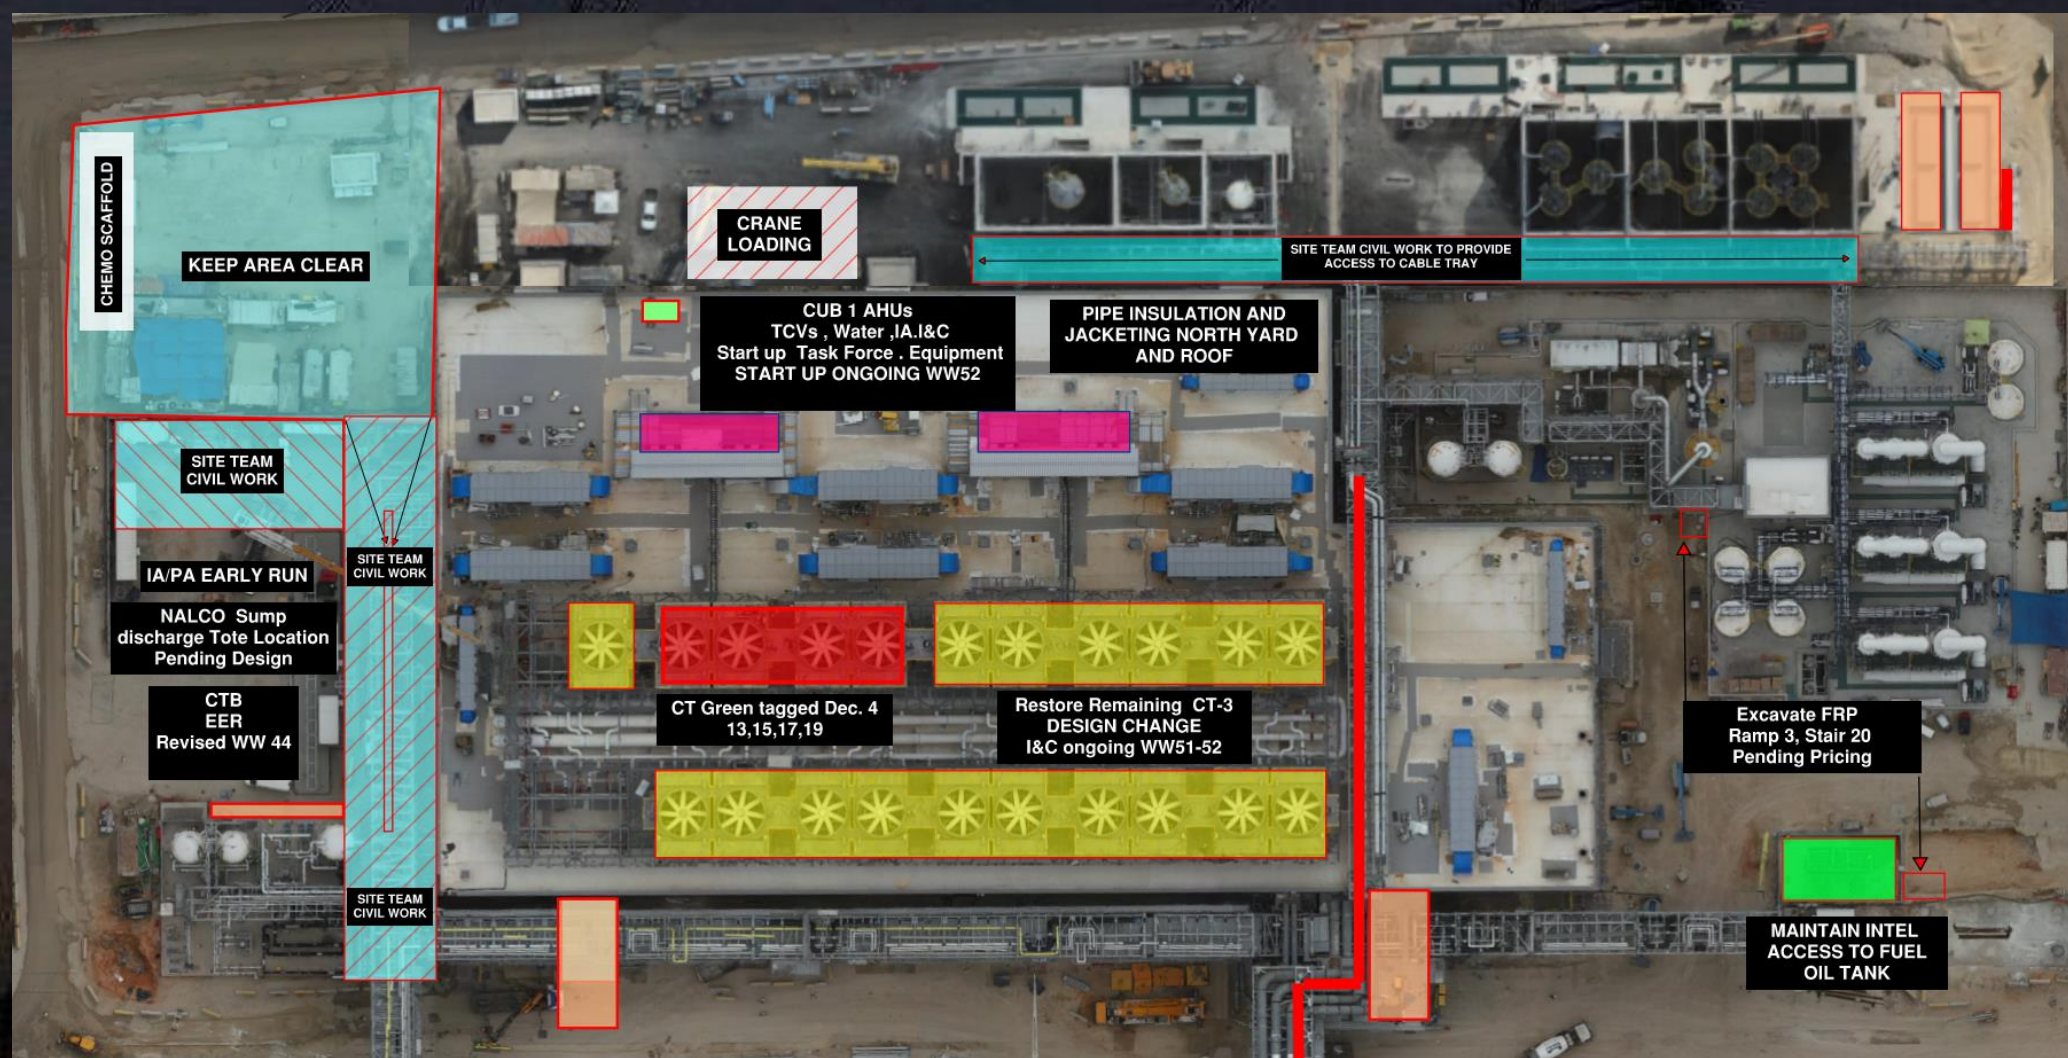

HOFFMAN Sparrow

12th Floor Plan Details:

- Grid System:** A-S (Horizontal), 1-12 (Vertical)
- Rooms and Areas:**
 - FUTURE NH4W 283 (Orange)
 - Mamad Access (Yellow)
 - Cable Tray Seismic Bracing Review ELECTRICAL (Yellow)
 - Zone 2 Path of Egress (Orange)
 - Zone 4 (Yellow)
 - Zone 5 (Blue)
 - Zone 6 (Purple)
 - Zone 7 (Green)
 - HFW 266 (Green)
 - BCS 252 (Pink)
 - BSA 253 (Pink)
 - SAND FILTERS (Blue)
 - Pump Load in (Black)
- Stairs:** STAIR 2, STAIR 8, STAIR 9, STAIR 10, STAIR 12, STAIR 13, STAIR 14, STAIR 15
- Access Points:** Roof Access, Equipment/Material Access, Mamad Access
- Other Labels:** CRCs HFW /AWN WW51, Awn 261, LIWS LAB, CRITICAL SPARE PARTS STORAGE / PUMP REBUILD AREA, WWT SUPPORT, FACILITIES SHOP, ELECTRICAL SHOP, MECHANICAL WORKSHOP, MECHANICAL CONTROL ROOM, JAN, WC, SCR, LSS, SWS, CTB 114, ROP 242, URW 262, WATER TREATMENT, STAIR 9, STAIR 10, STAIR 12, STAIR 13, STAIR 14, STAIR 15
- Directional Indicators:** Large black arrow labeled 'MIMO' pointing right.

CUB 2 – EXTERIOR/ROOF







HOFFMAN CONSTRUCTION COMPANY



CLOSED

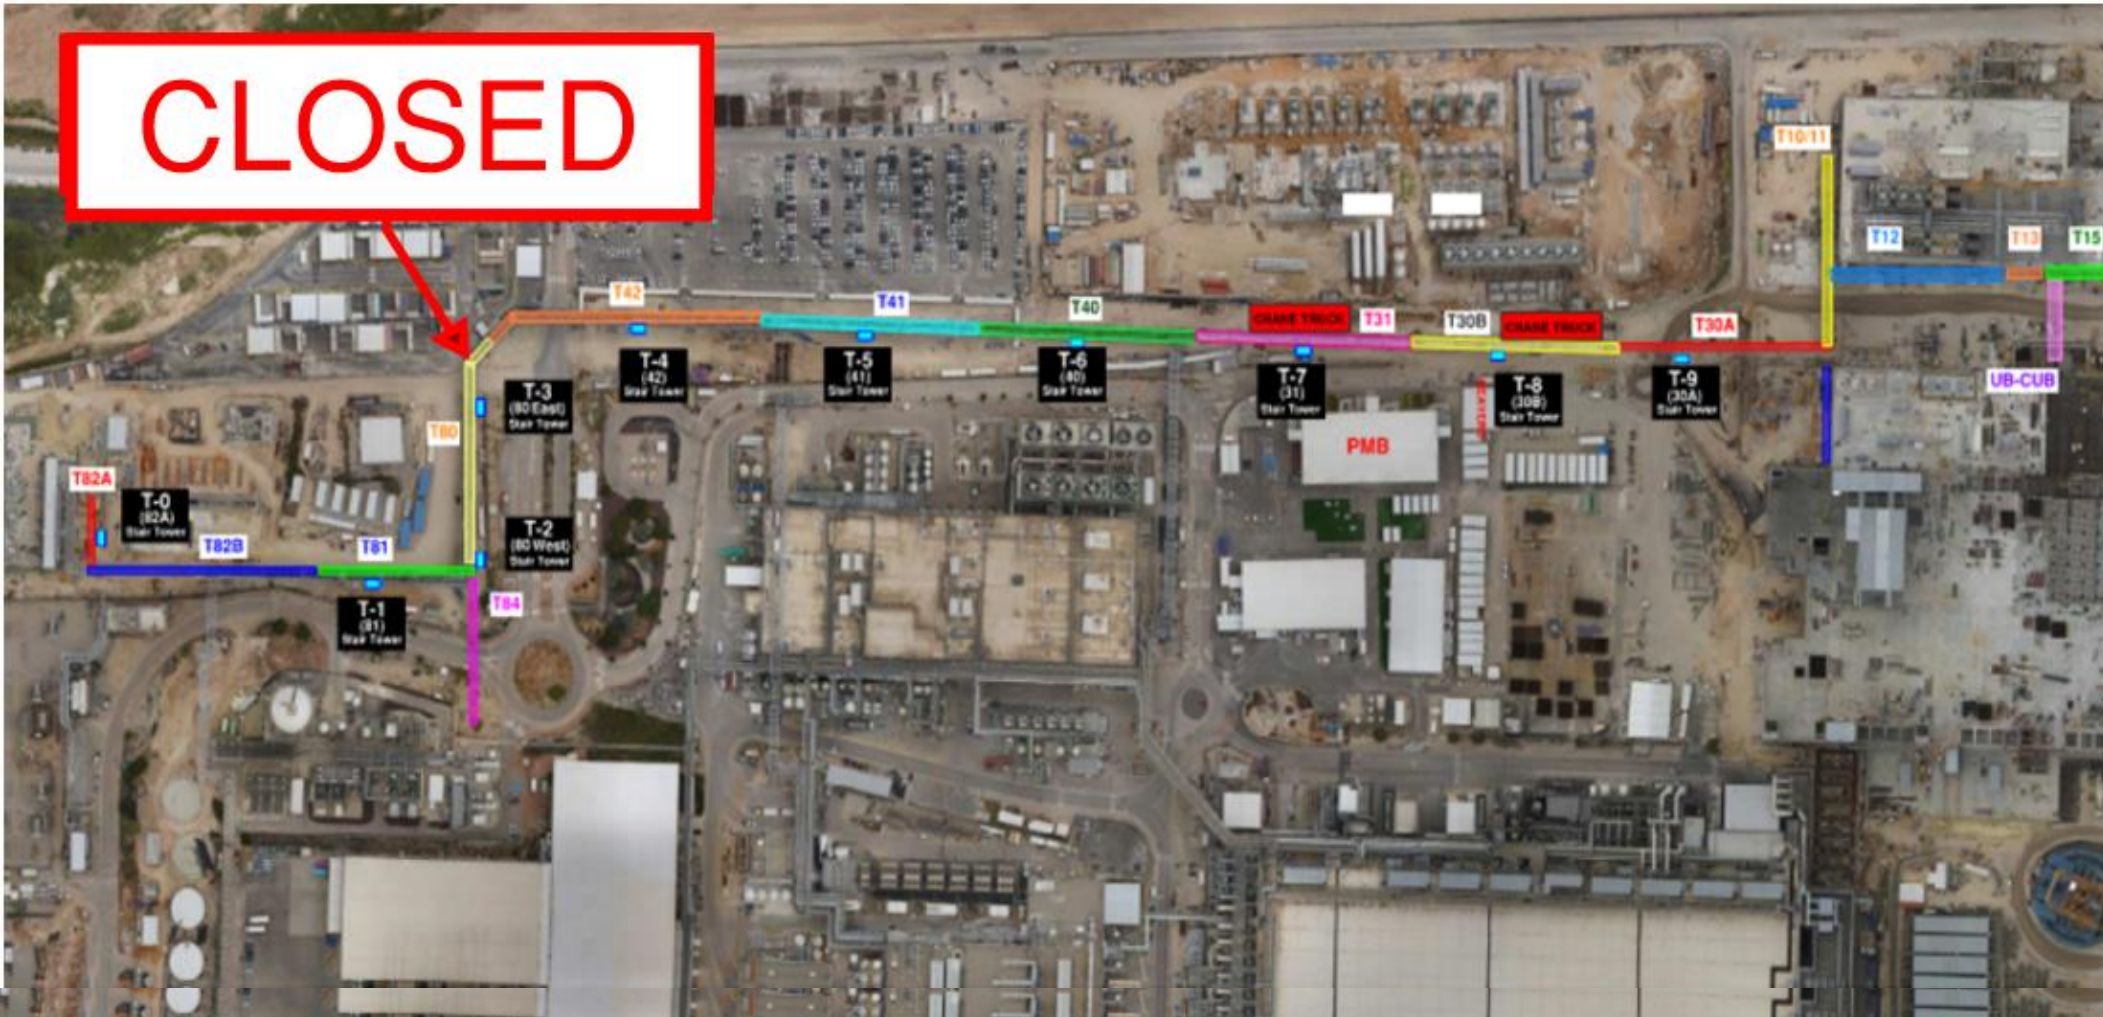

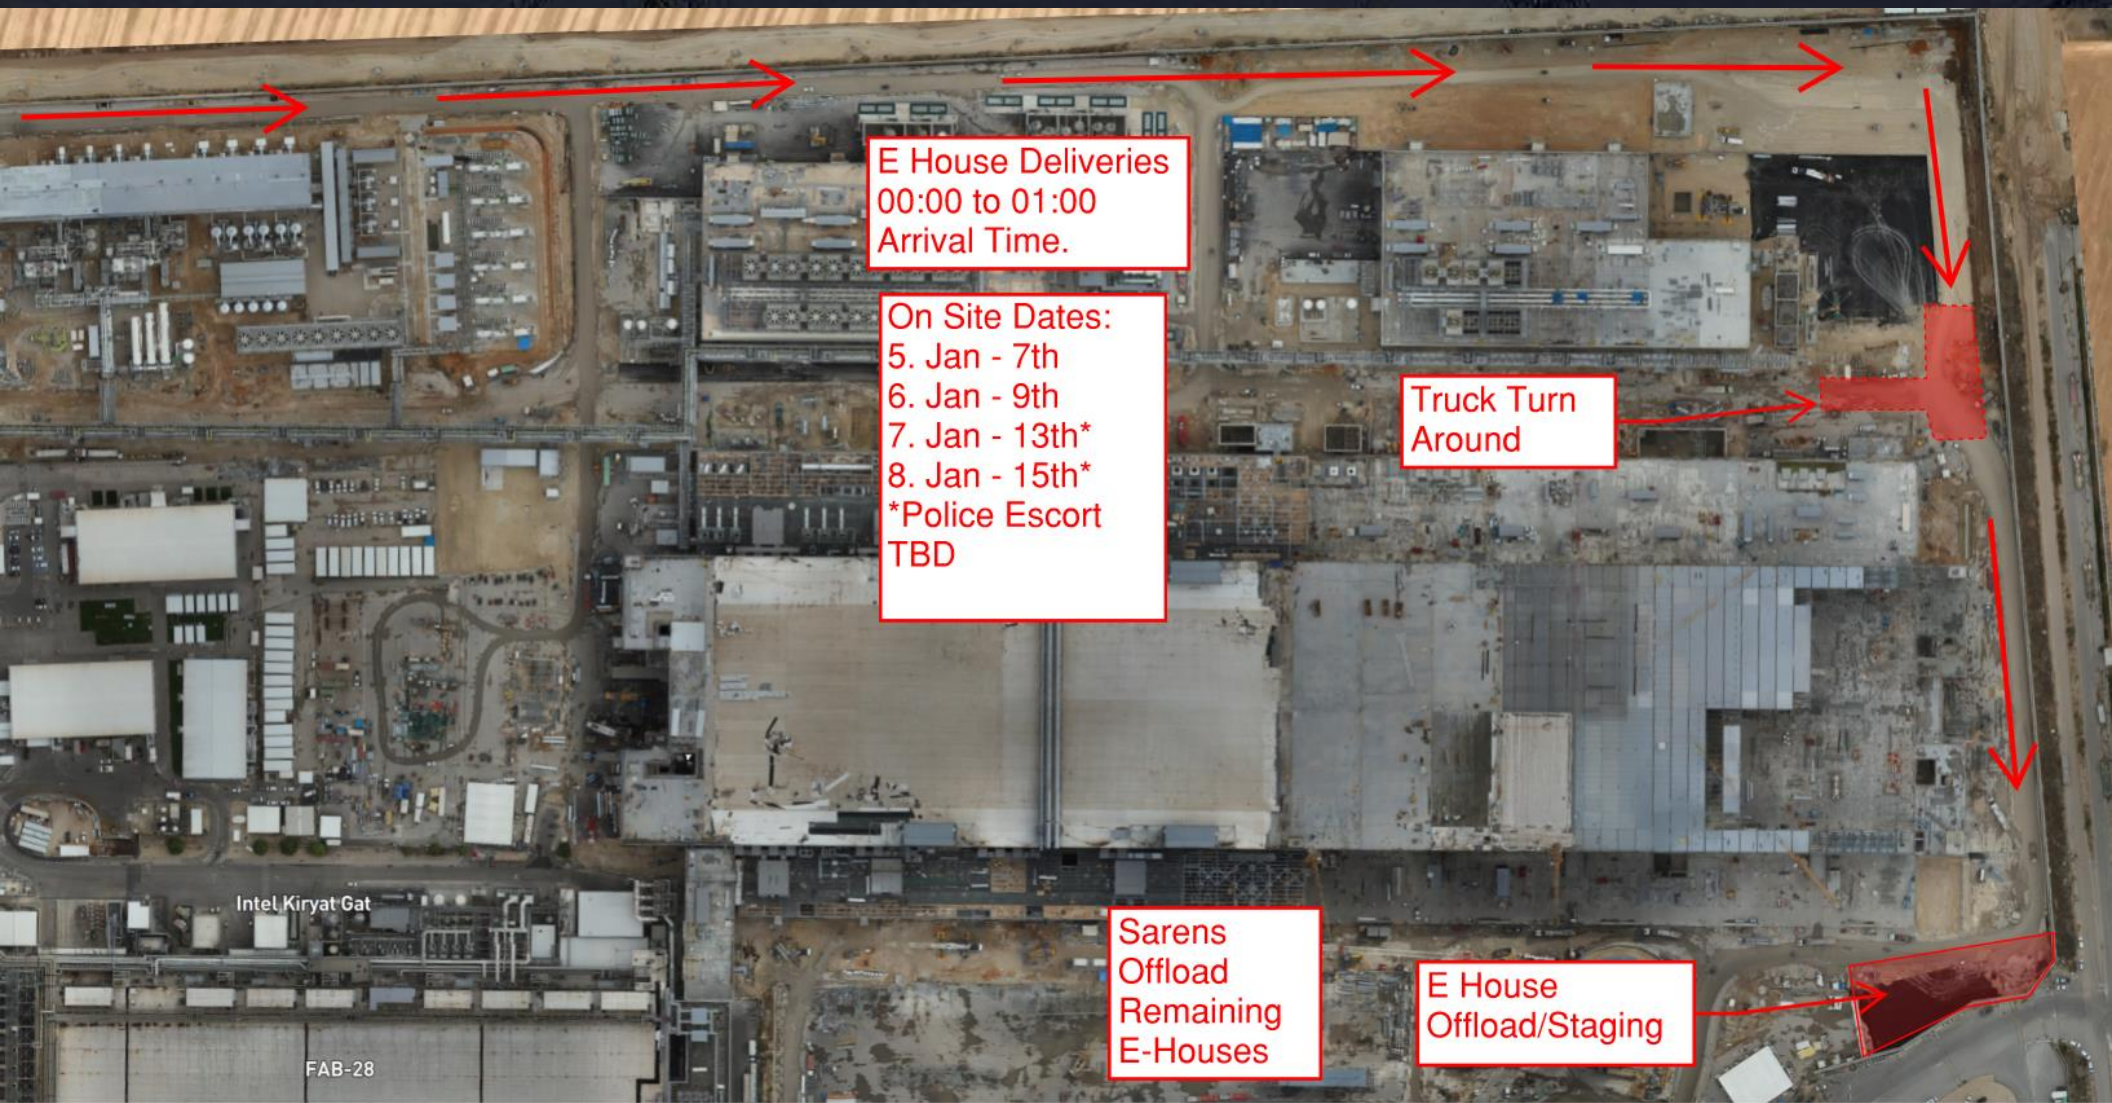

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:
5. Jan - 7th
6. Jan - 9th
7. Jan - 13th*
8. Jan - 15th*
*Police Escort
TBD

Truck Turn
Around

Sarens
Offload
Remaining
E-Houses

E House
Offload/Staging

Intel Kiryat Gat

FAB-28

From main kiosk

Site temporary power

Legend :

- 22KV Line
- 400V Line
- 109 - Kiosk
- Lift Station

Temp power shutdown
Start: 05-Jan- 00:01 AM
End: 05-Jan- 06:00 AM
From AY to CE Grid line
All the floors + JG
SB, lights, elevator
+TC-6

Fab 38.2

Fab 38.1

North

Cub 2

TC-12 Done

Cub 1

TC-10

TC-8

T

630A SW

630A NW

630A NW

TC-9

630A SE

630A NE

630A SE

630A NE

TC-7

TC-5

To 115

From main

117

105

106

107

108

109

111

112

113

114

115


116

Daily Coordination Meeting

Site Logistics


600 Car Park

Boring

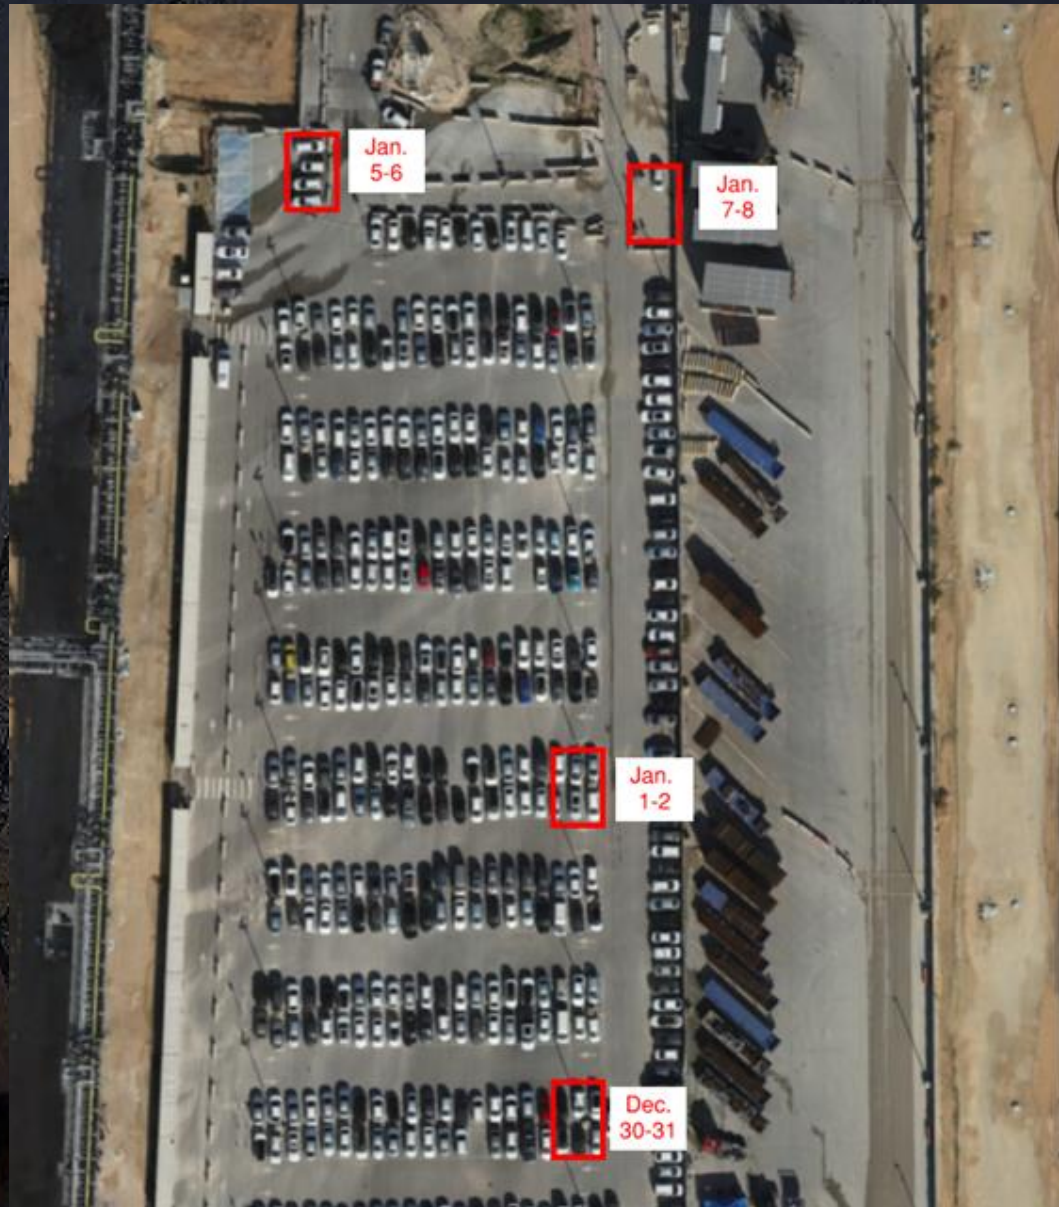

Daily Coordination Meeting

Site Logistics North

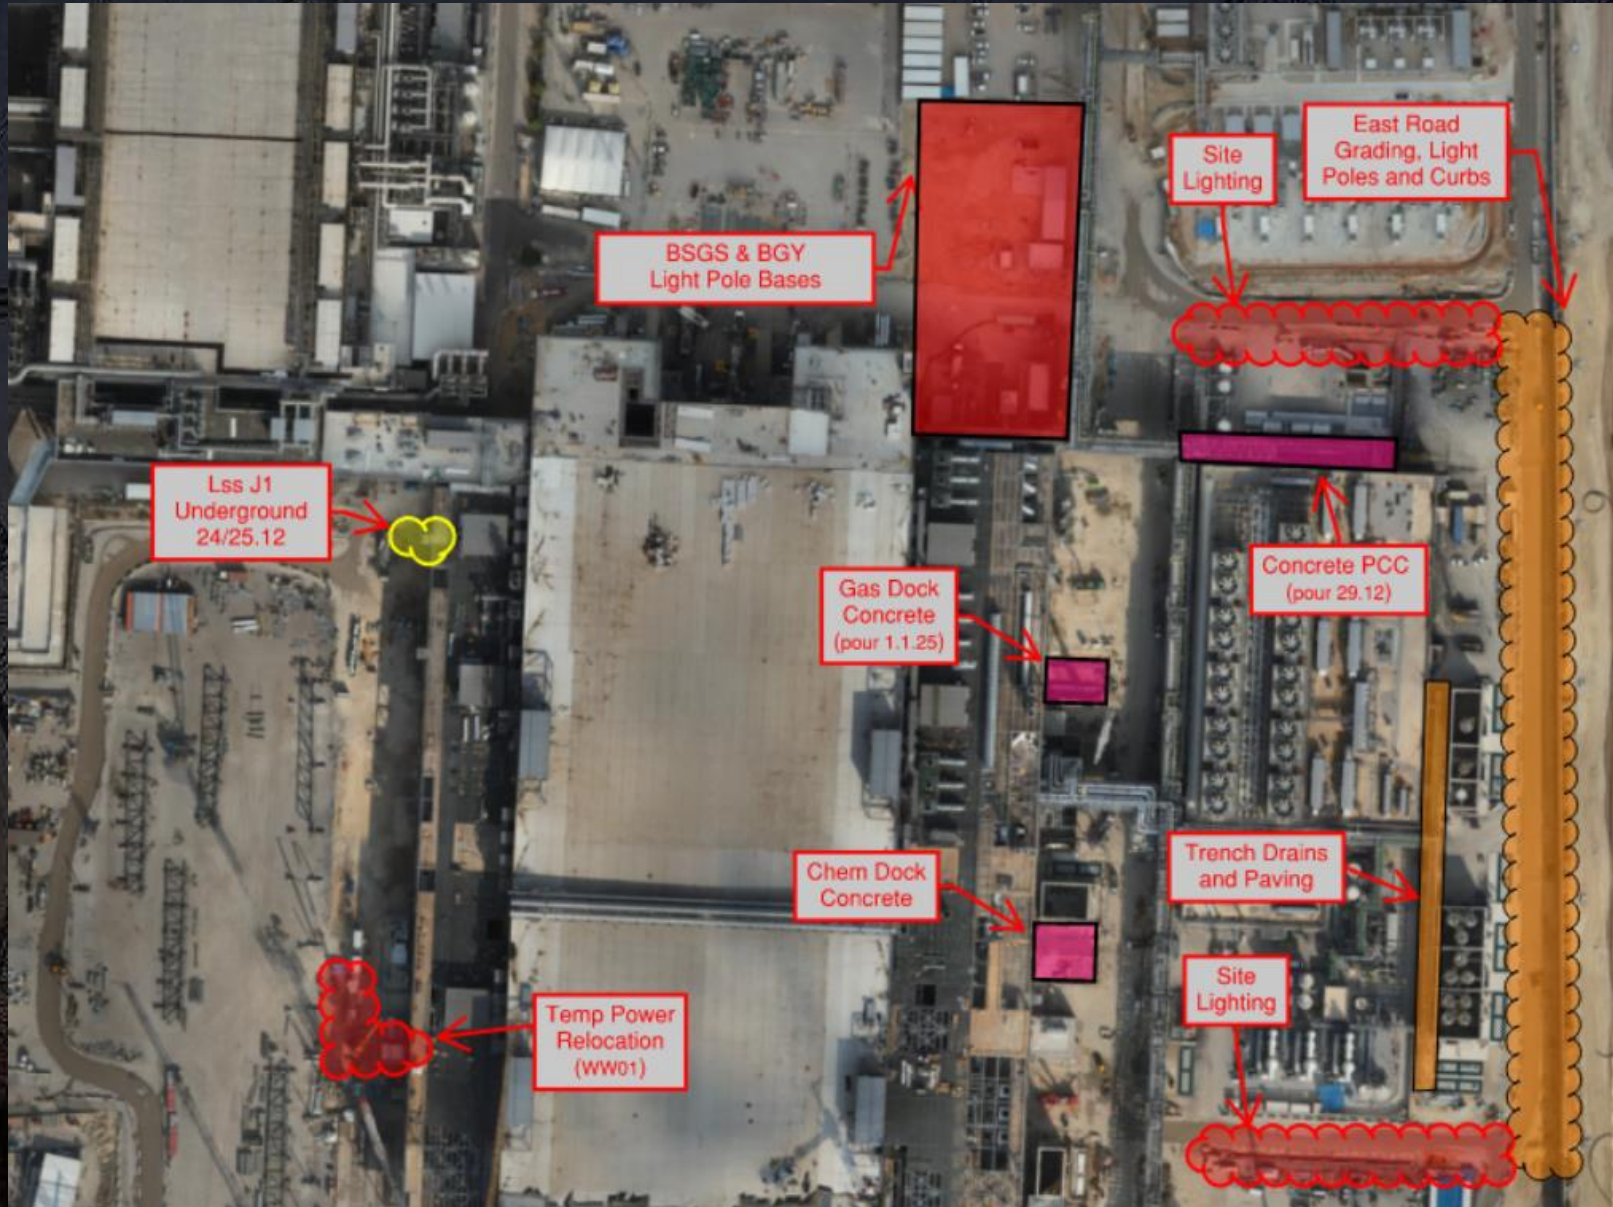

Daily Coordination Meeting

Site Logistics
South






COR Status by Subcontractor WW1

Open – 602 CORs

Overdue – 176 CORs

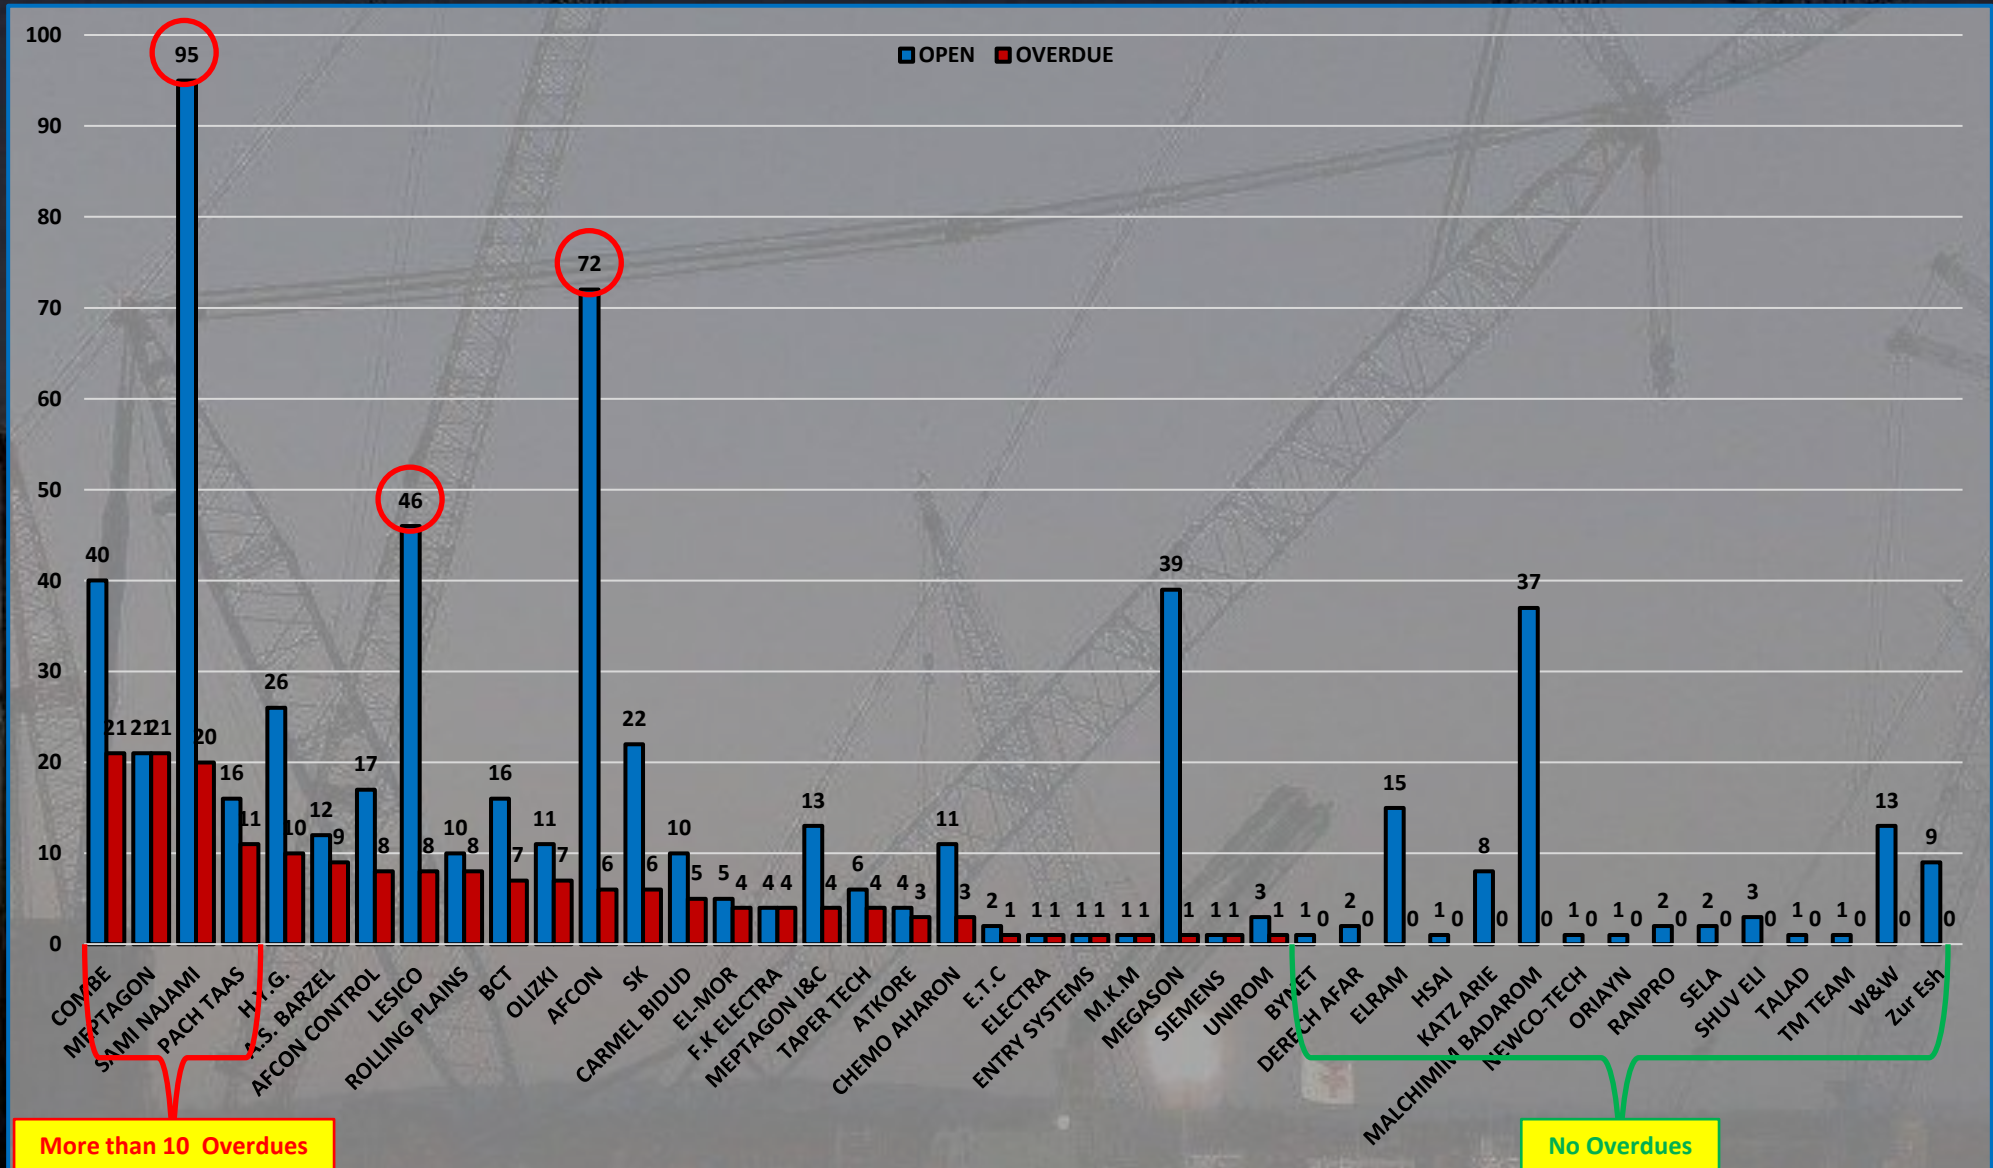

Slick Conditions

- Wet surfaces, mud, and boot covers all can increase our chances of someone slipping and falling.
- Injuries from slip and falls can range drastically from bruises to broken bones.
- All workers need to have appropriate footwear, with treads that are in good condition.
- No running on the project.
- If working on the TPO, something must be placed down when it is wet to prevent people from slipping. If you cannot make this happen, do not walk on the TPO.
- Boot covers absolutely must be removed when you leave a clean area. They cannot be worn to the chemical toilets, the break tents, or dirty parts of the building.

Daily Coordination Meeting



14:00 Sign In
