

# Daily Coordination Meeting




14:00 Sign In

# Daily Coordination Meeting

## General Topics:

- Crane incident yesterday
  - Minor injuries
  - No one goes into the area without Keylee or Abbas' ok (includes subs)
  - All cranes shut down today. Tower cranes and truss pick on for tomorrow
- No night shift Thur 07 Nov jobsite closes at 17:00, jobsite reopens 06:30 Fri 08 Nov


**UTILITY LEVEL TRUSS**

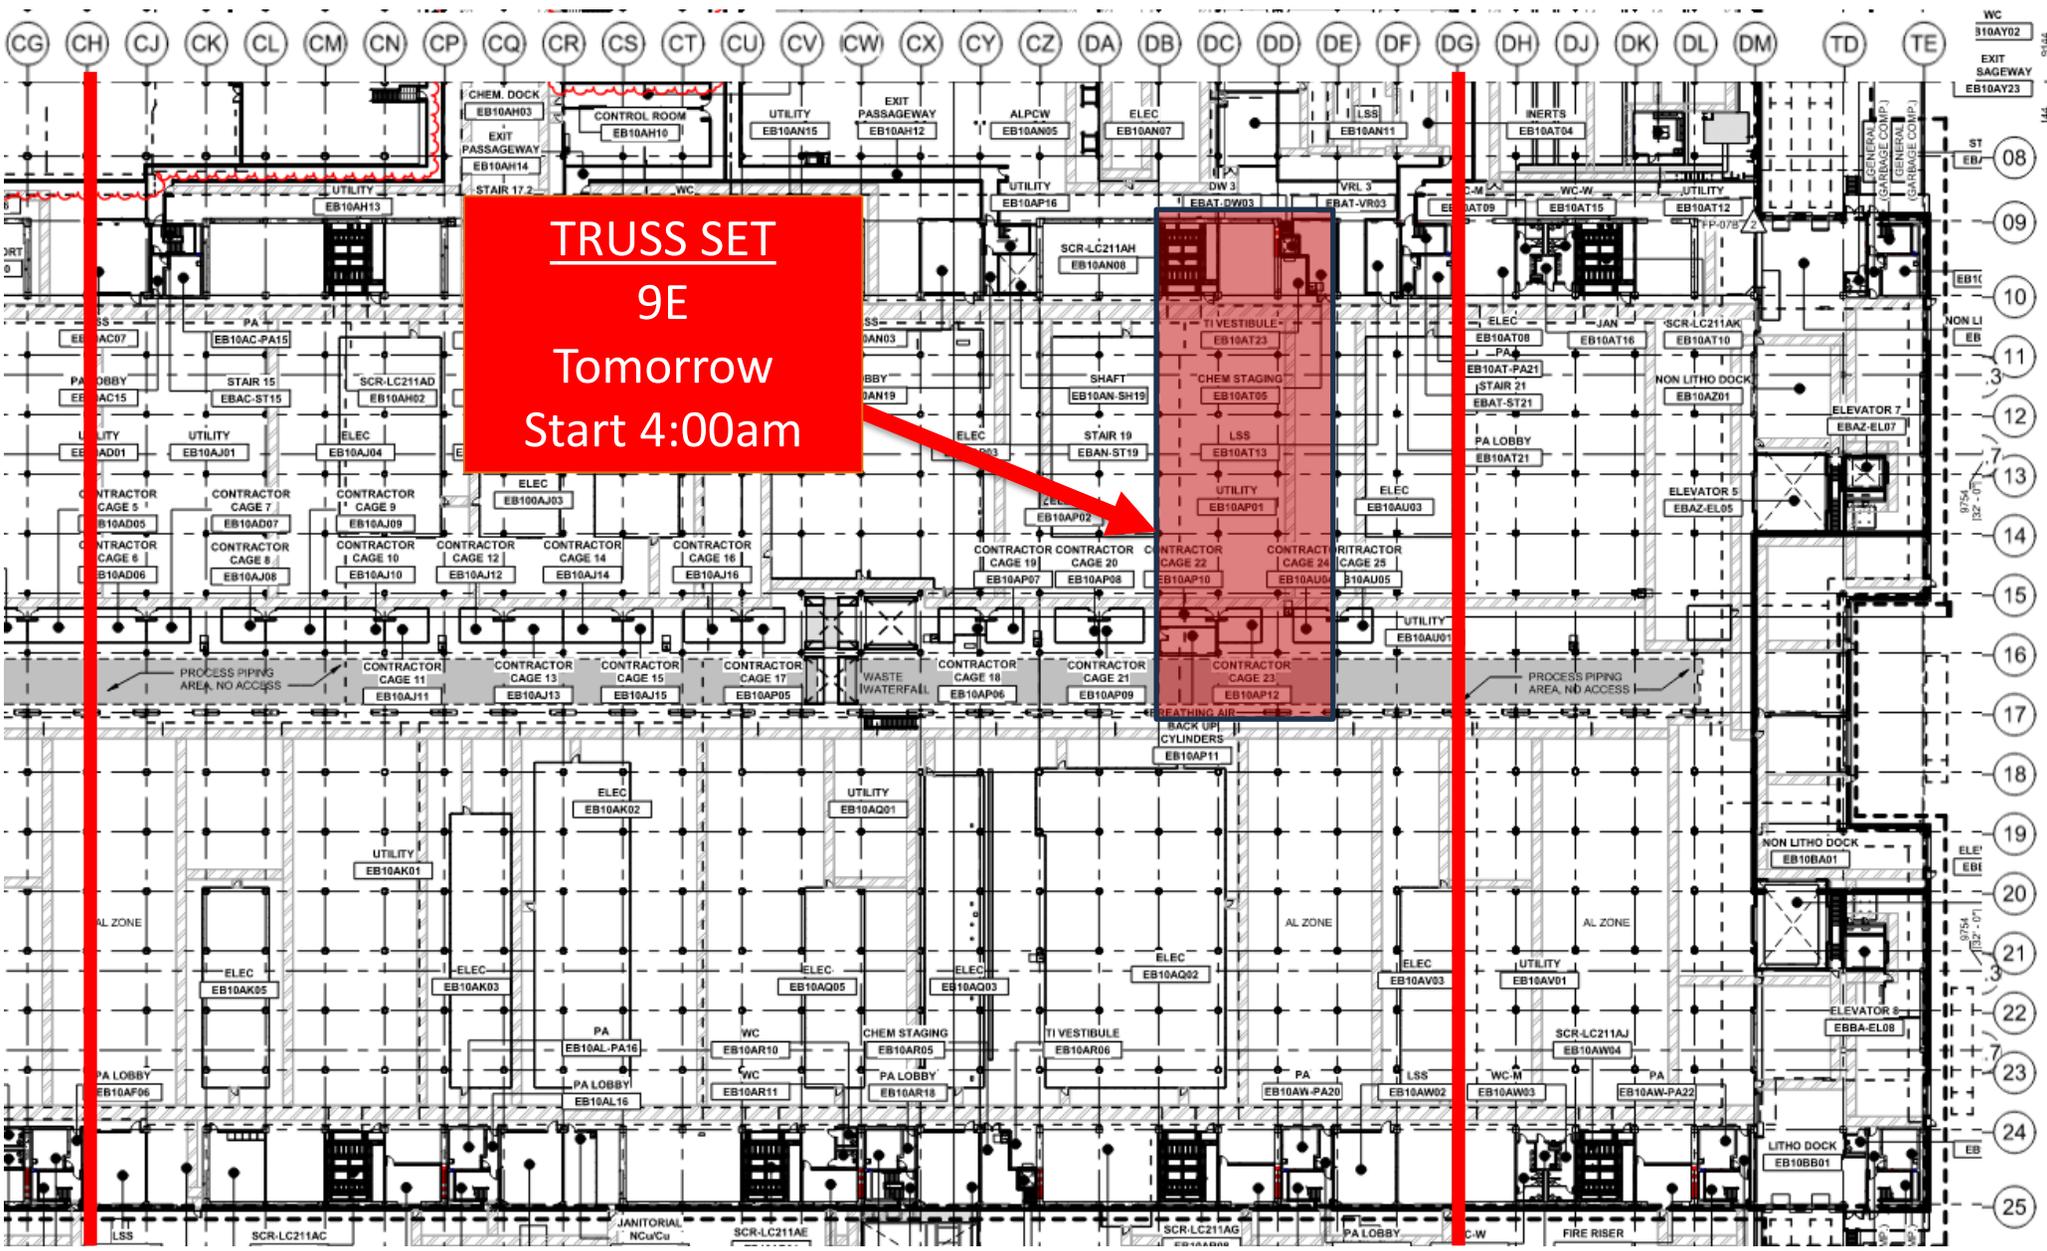

**TRUSS SET  
9E  
Tomorrow  
Start 4:00am**



UTILITY LEVEL MOD1

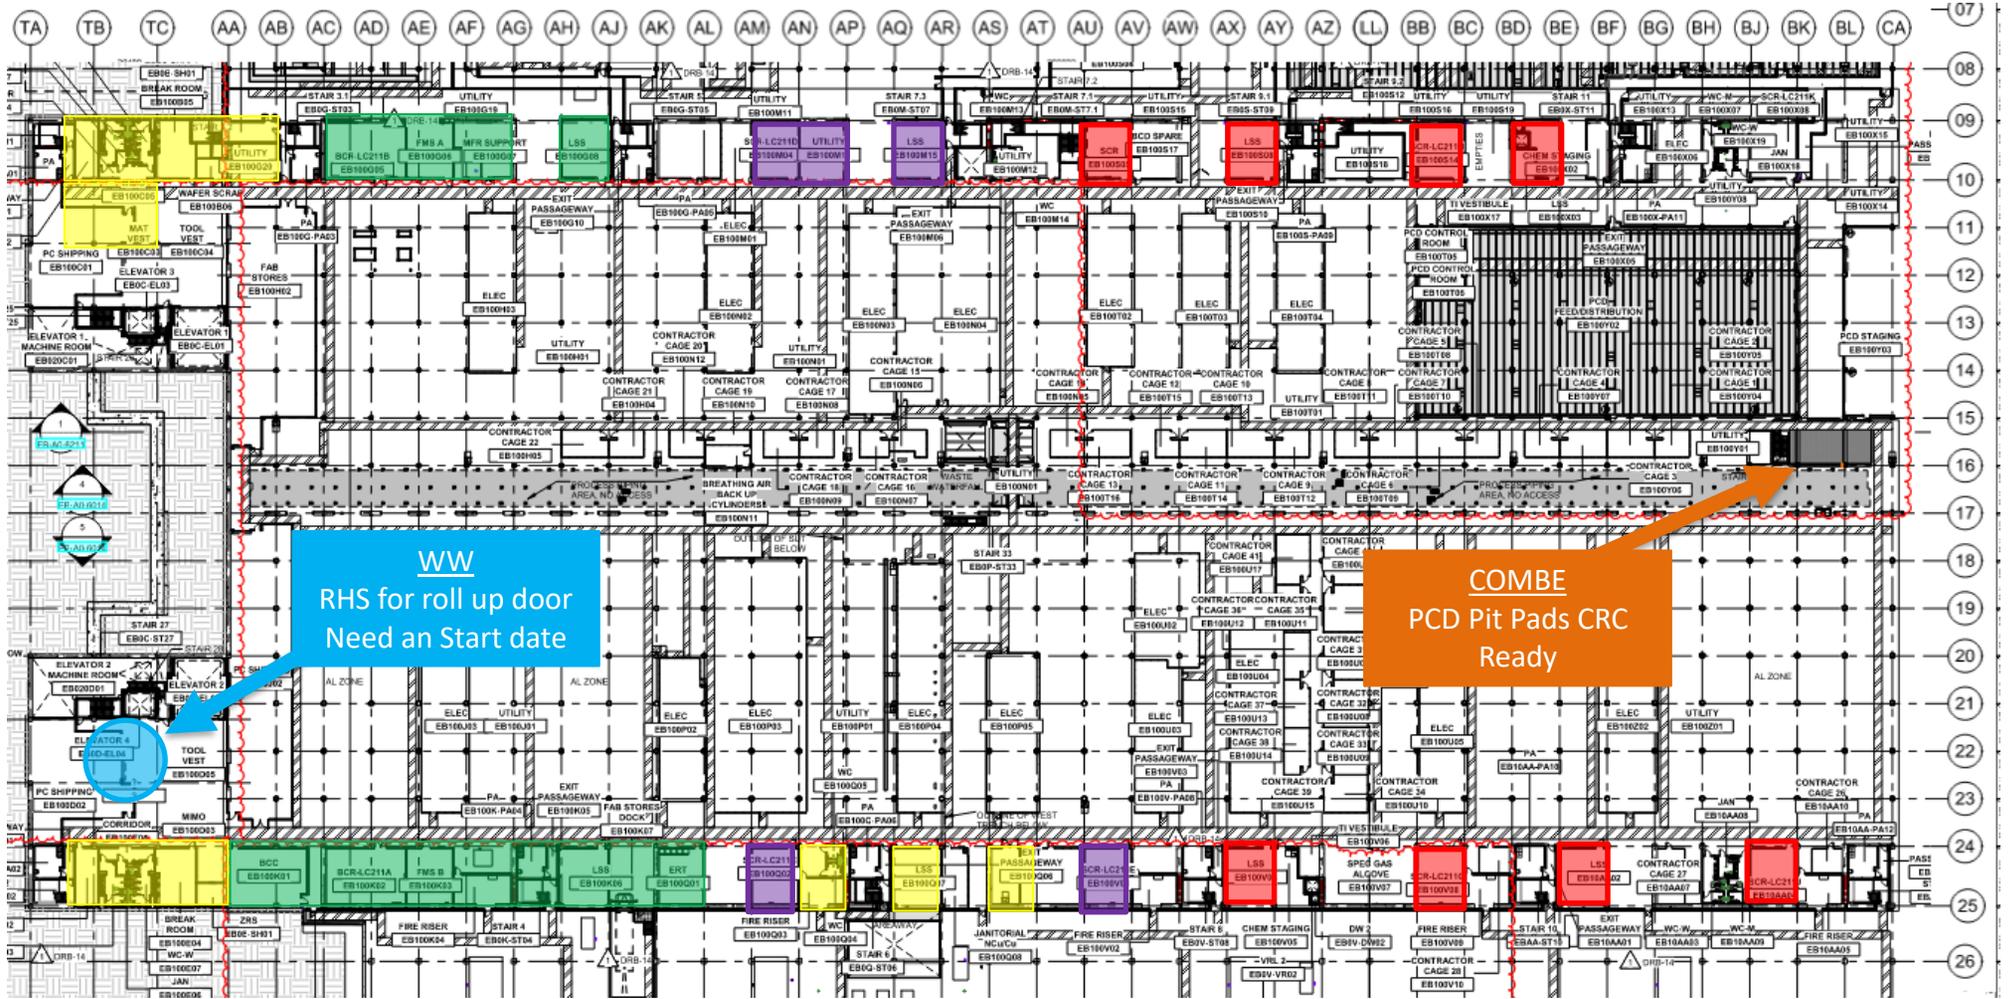


Pre-mold Rem dismantle  
Should be uninstll

BELFOR  
Mold remediation


ELRAM  
Drywall install

MEP+Elctrical  
Ready for re-install


UTILITY LEVEL MOD2

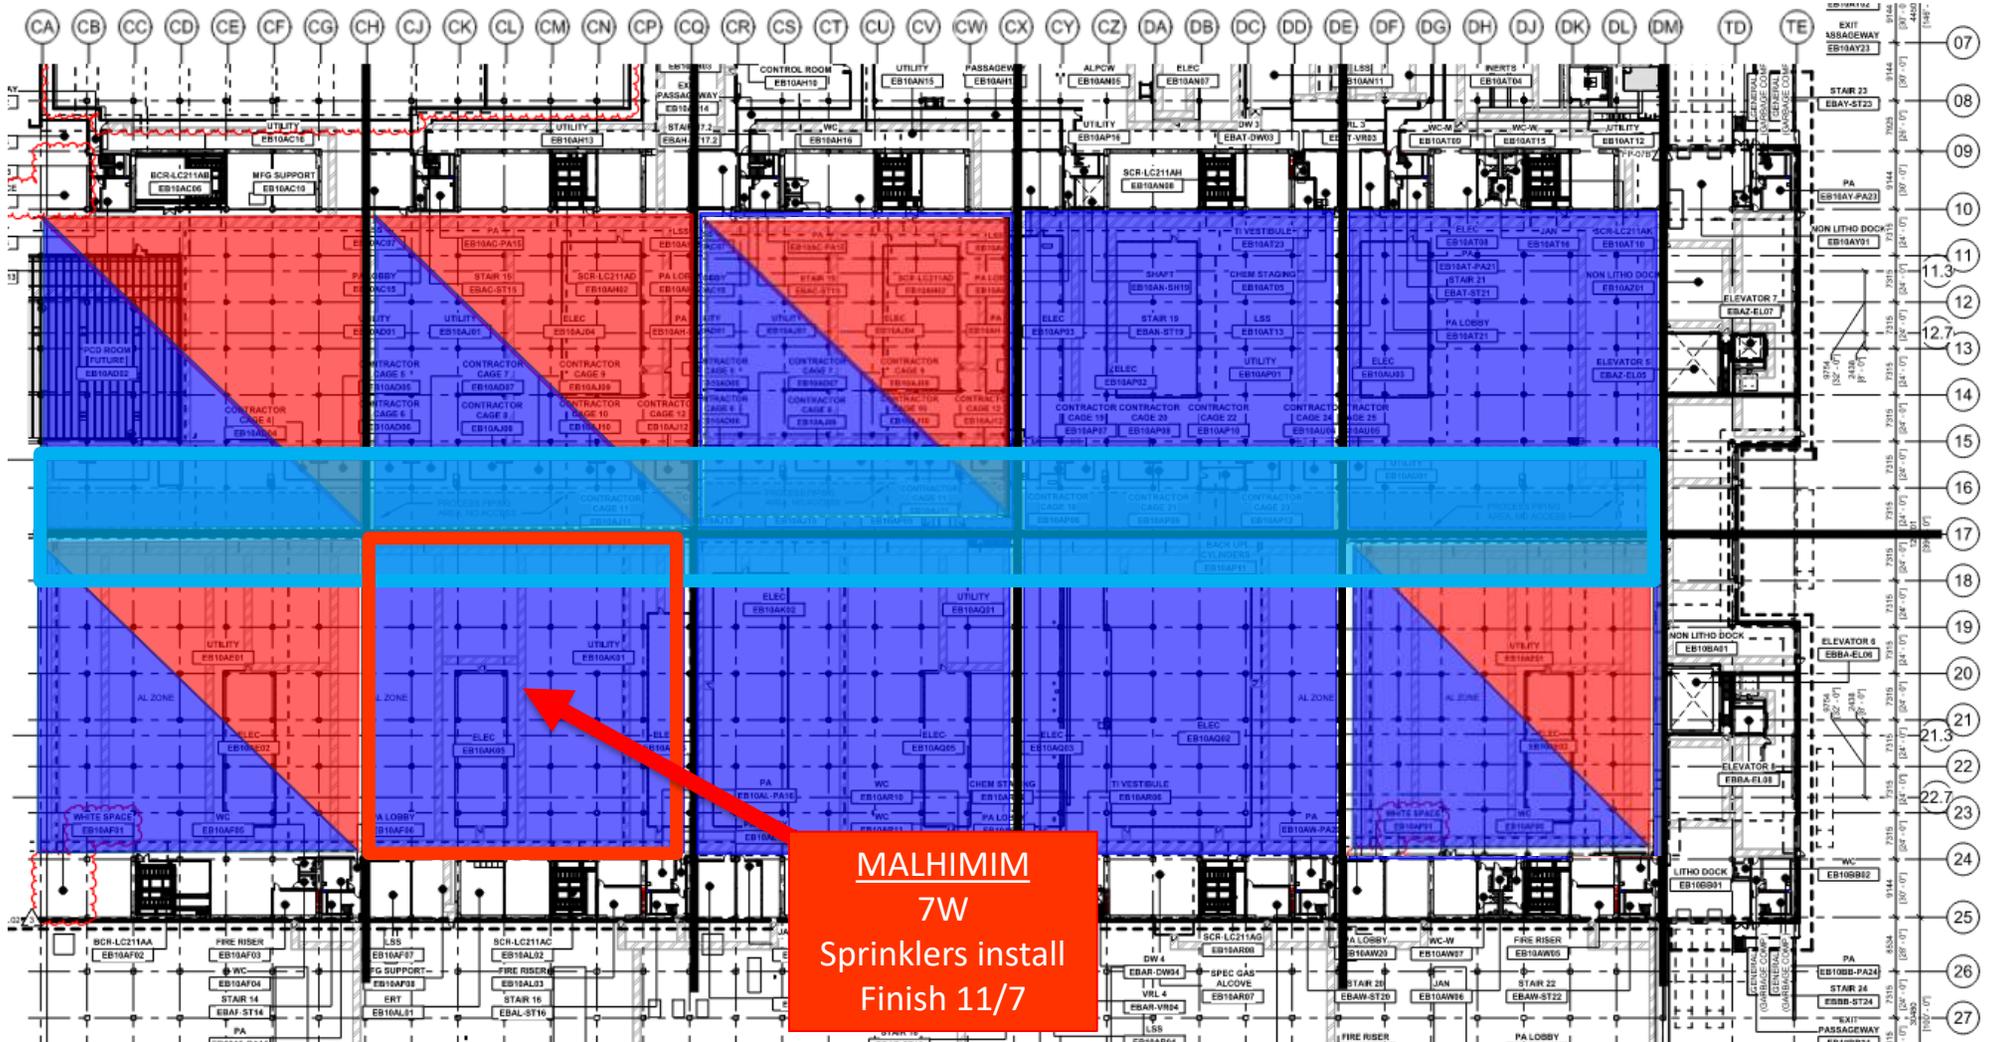


# SUT 38.1 LEVEL

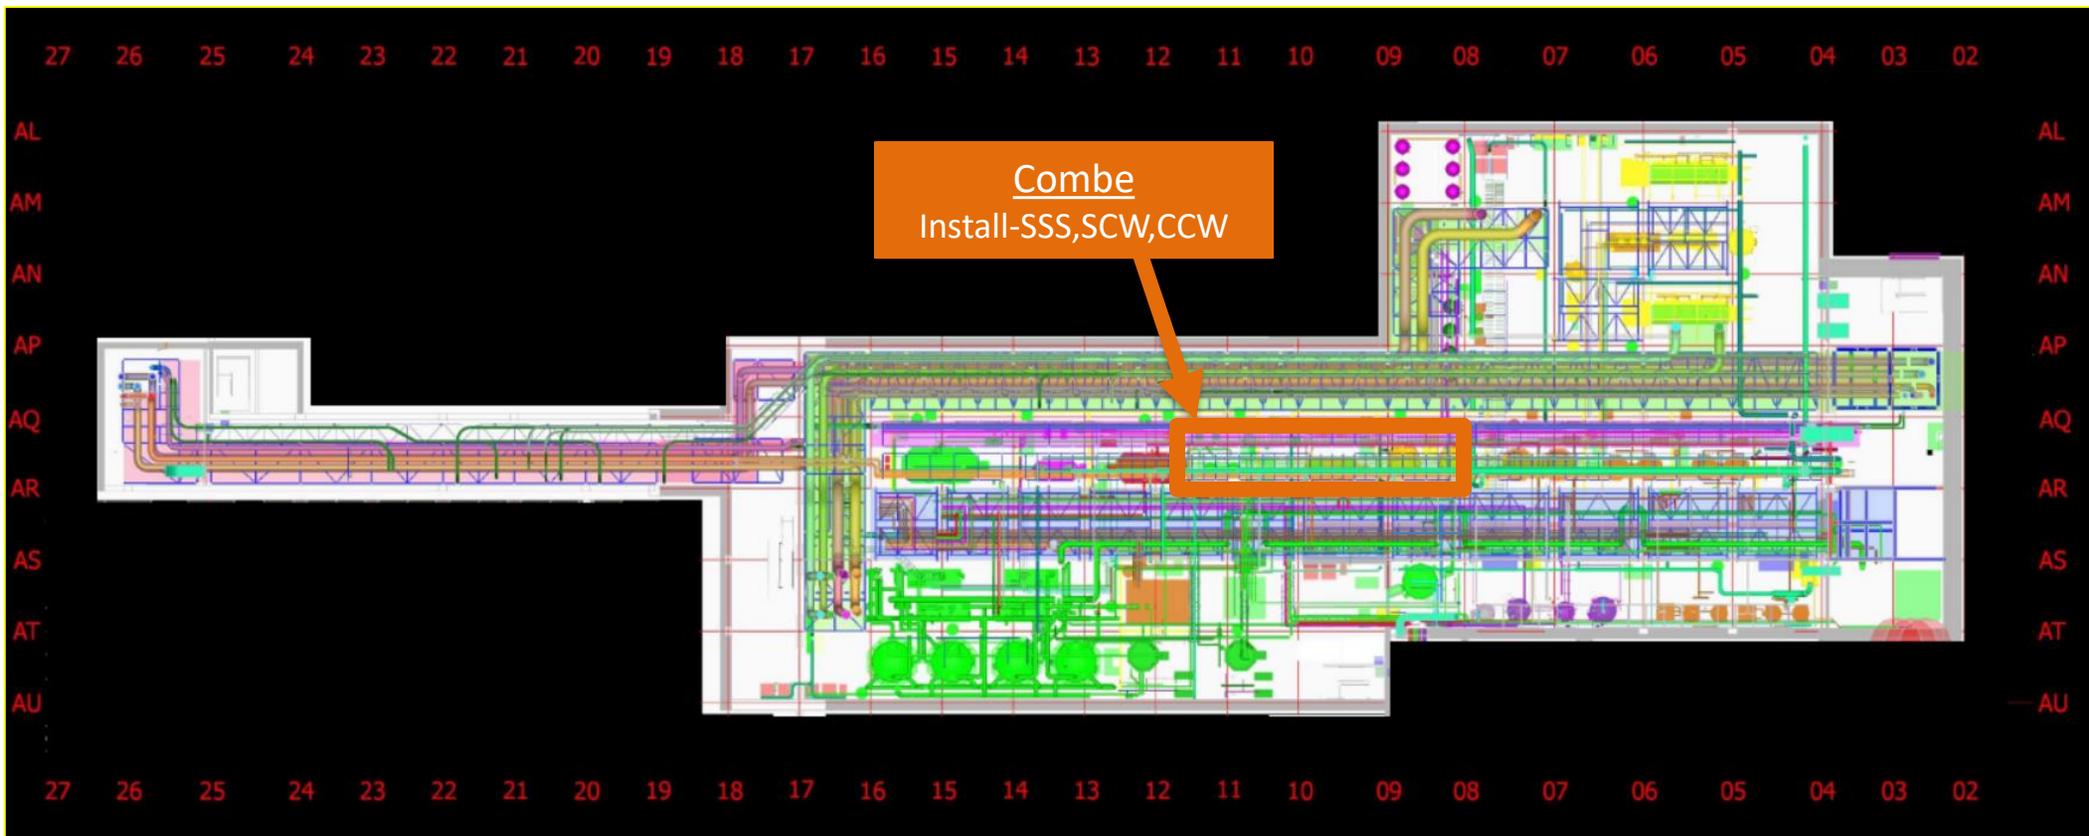


SUT 38.2 LEVEL

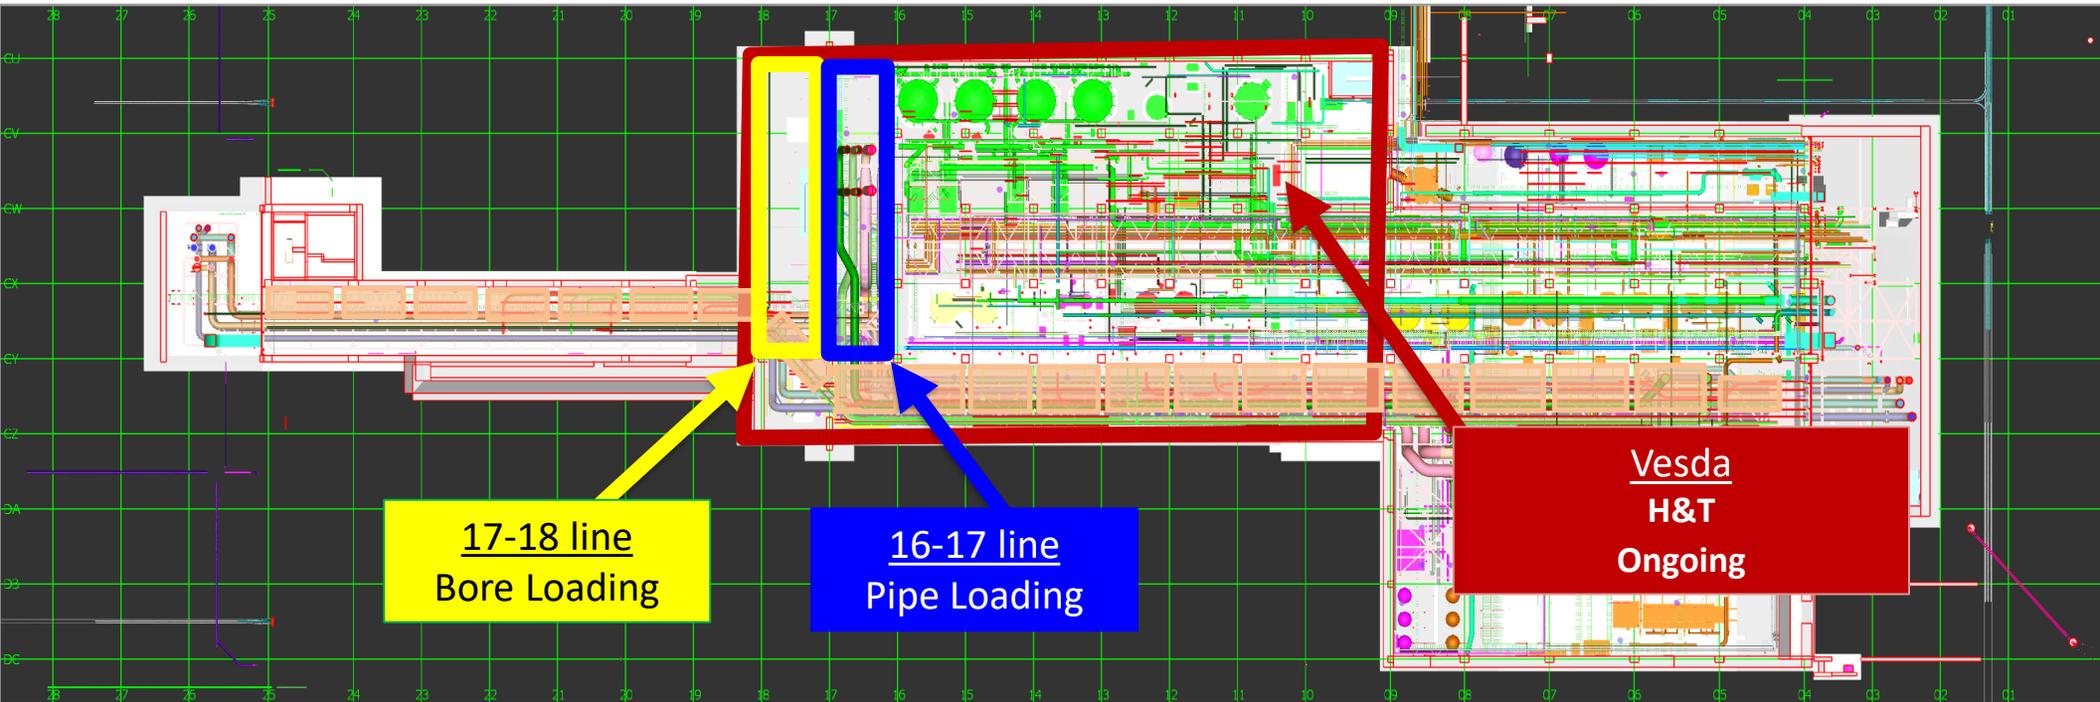

# SUBFAB BUILDOUT MOD 1

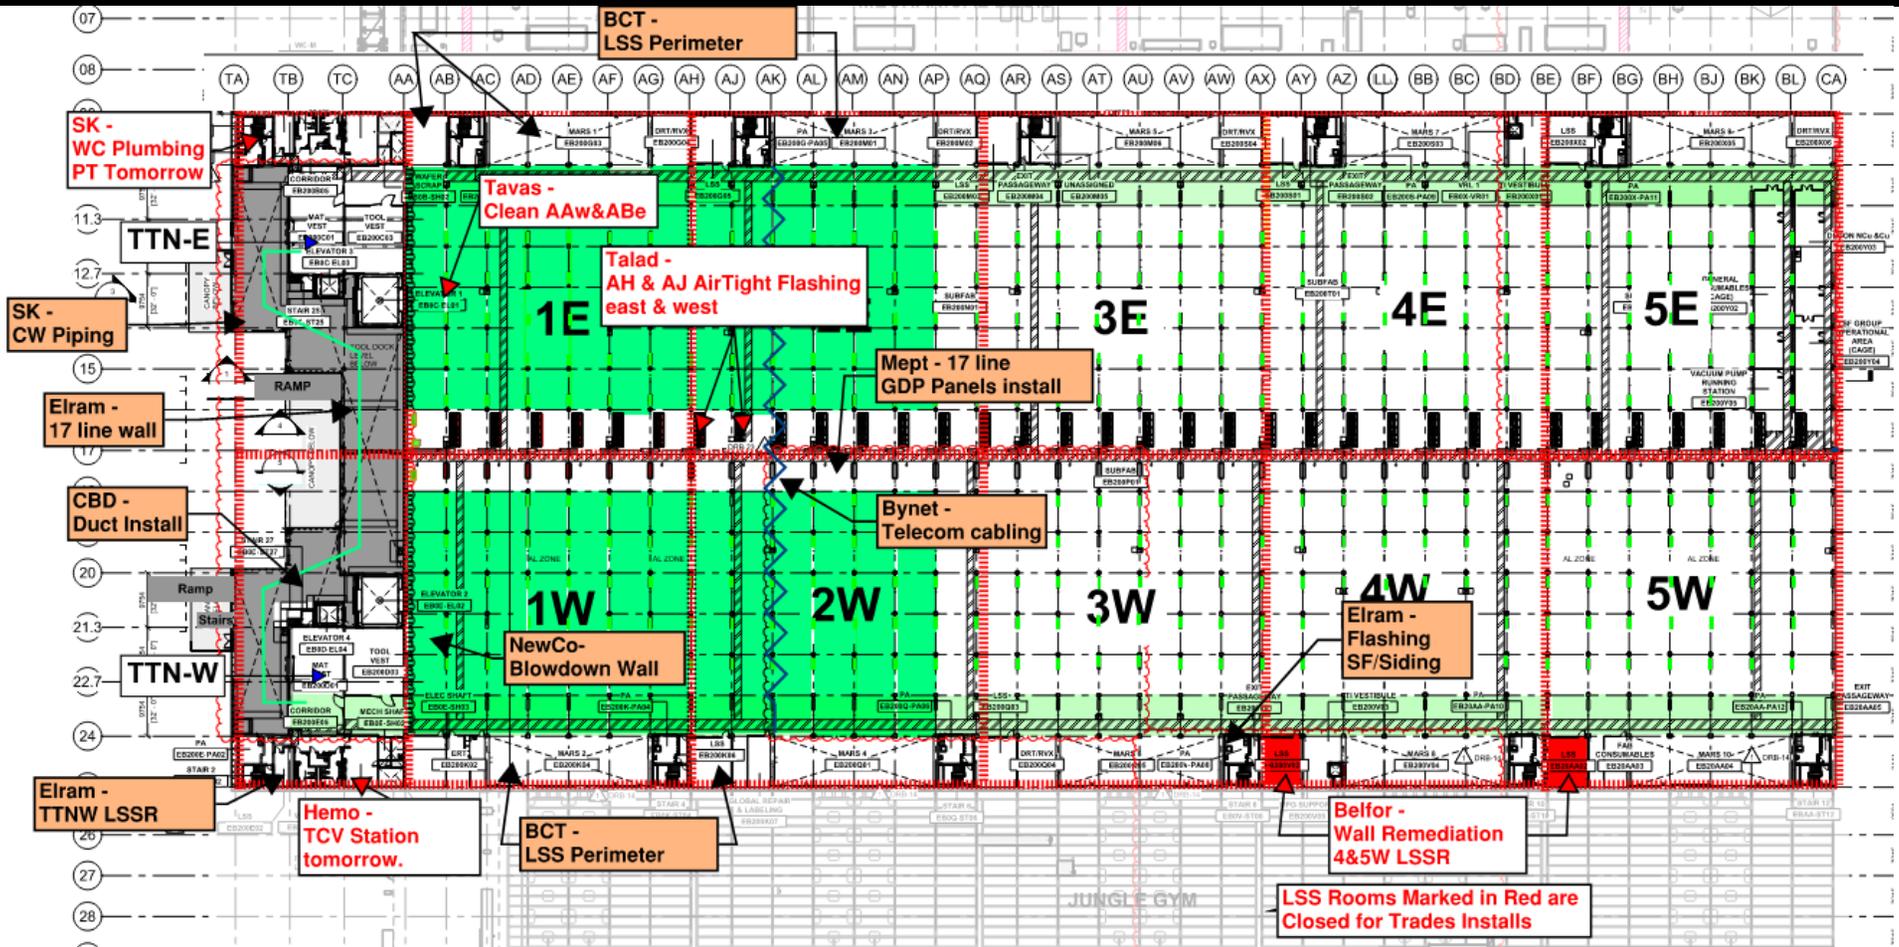

# SUBFAB CRC TOPCOAT

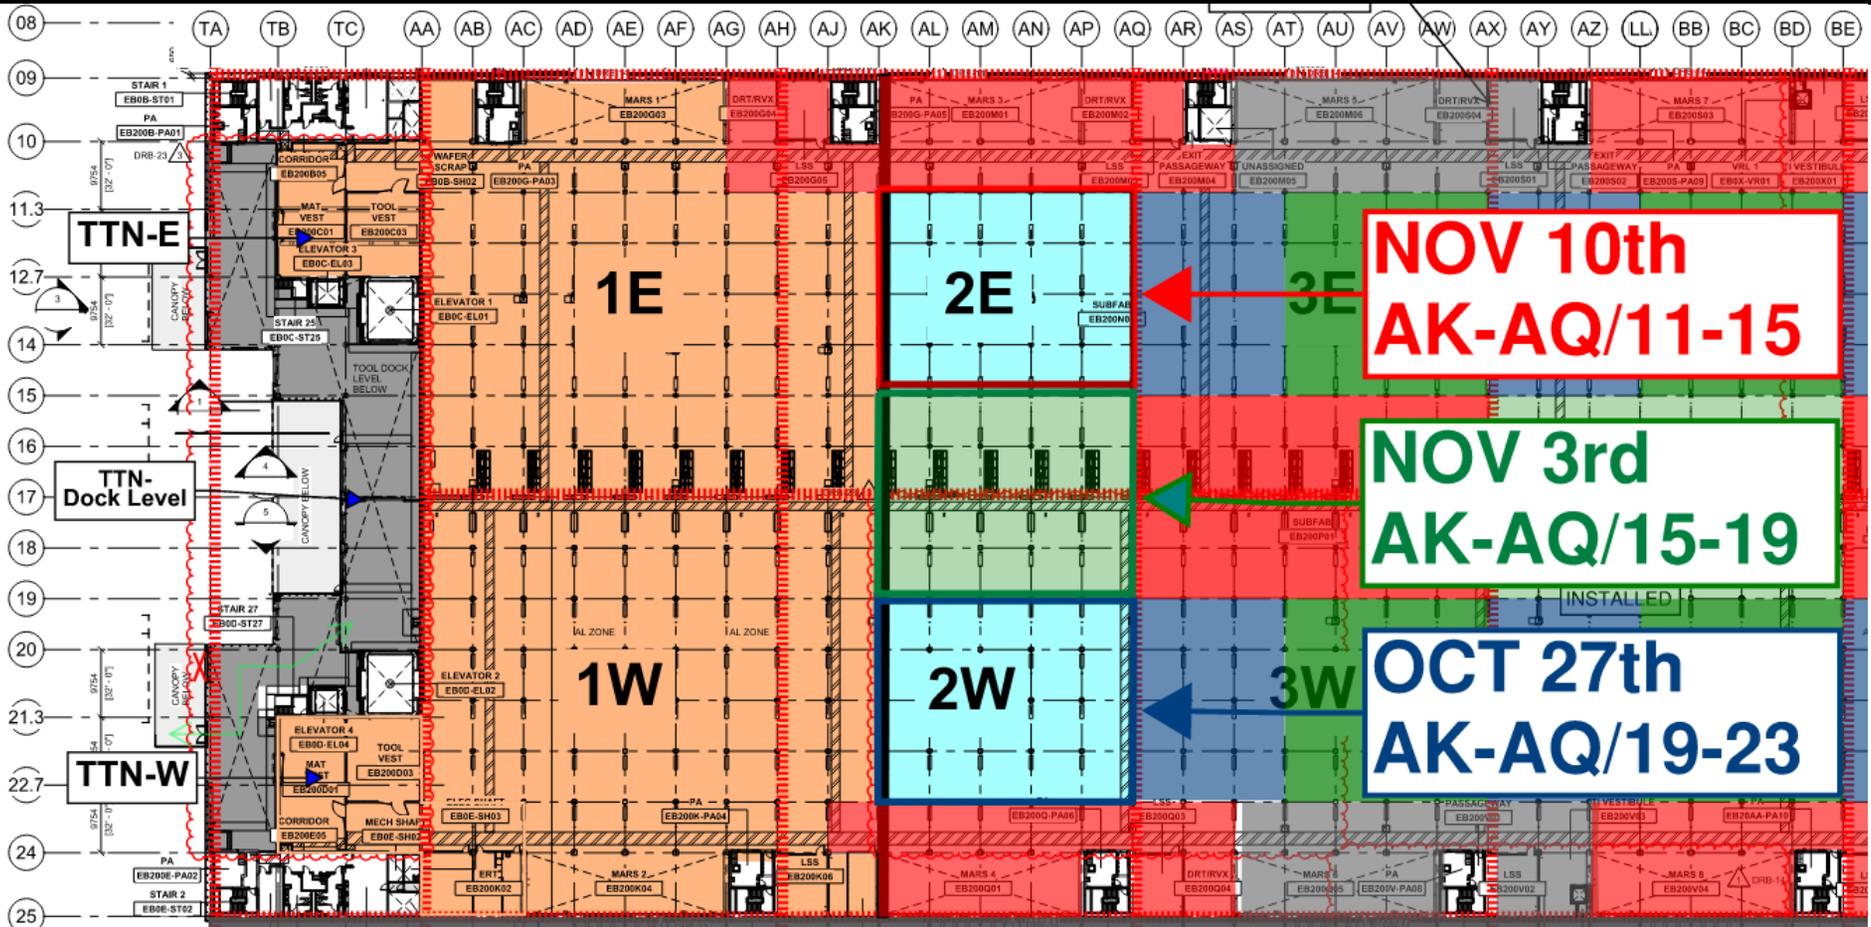

BCT Pressure Test Today

NOT TODAY

# BCT Pressure Test Tomorrow

**BCT Pneumatic Pressure Test**

**Nov 5th 13:30-18:30**


**Bay AGw -  
HPN2  
Size - 4"**

15m


SF Level Exclusion Zone.


Stair#4 - Access is blocked to the SF floor only.


LSS room is open

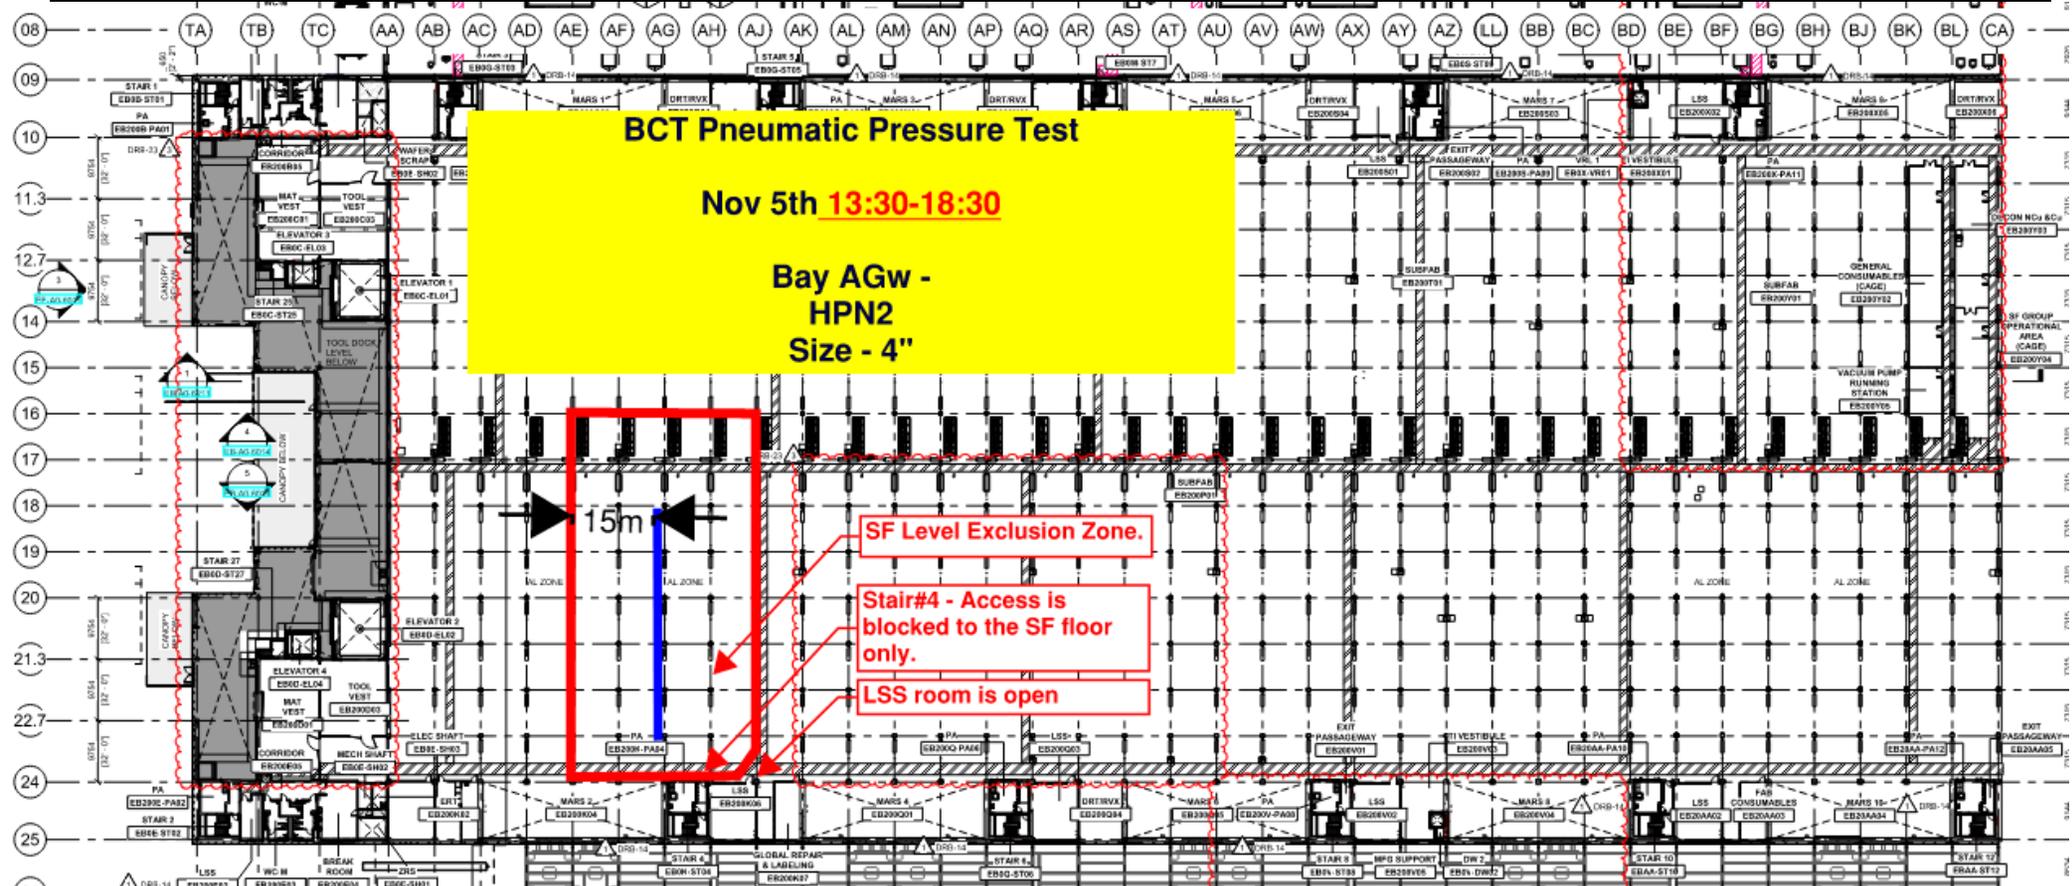

# SUBFAB BUILDOUT MOD 2

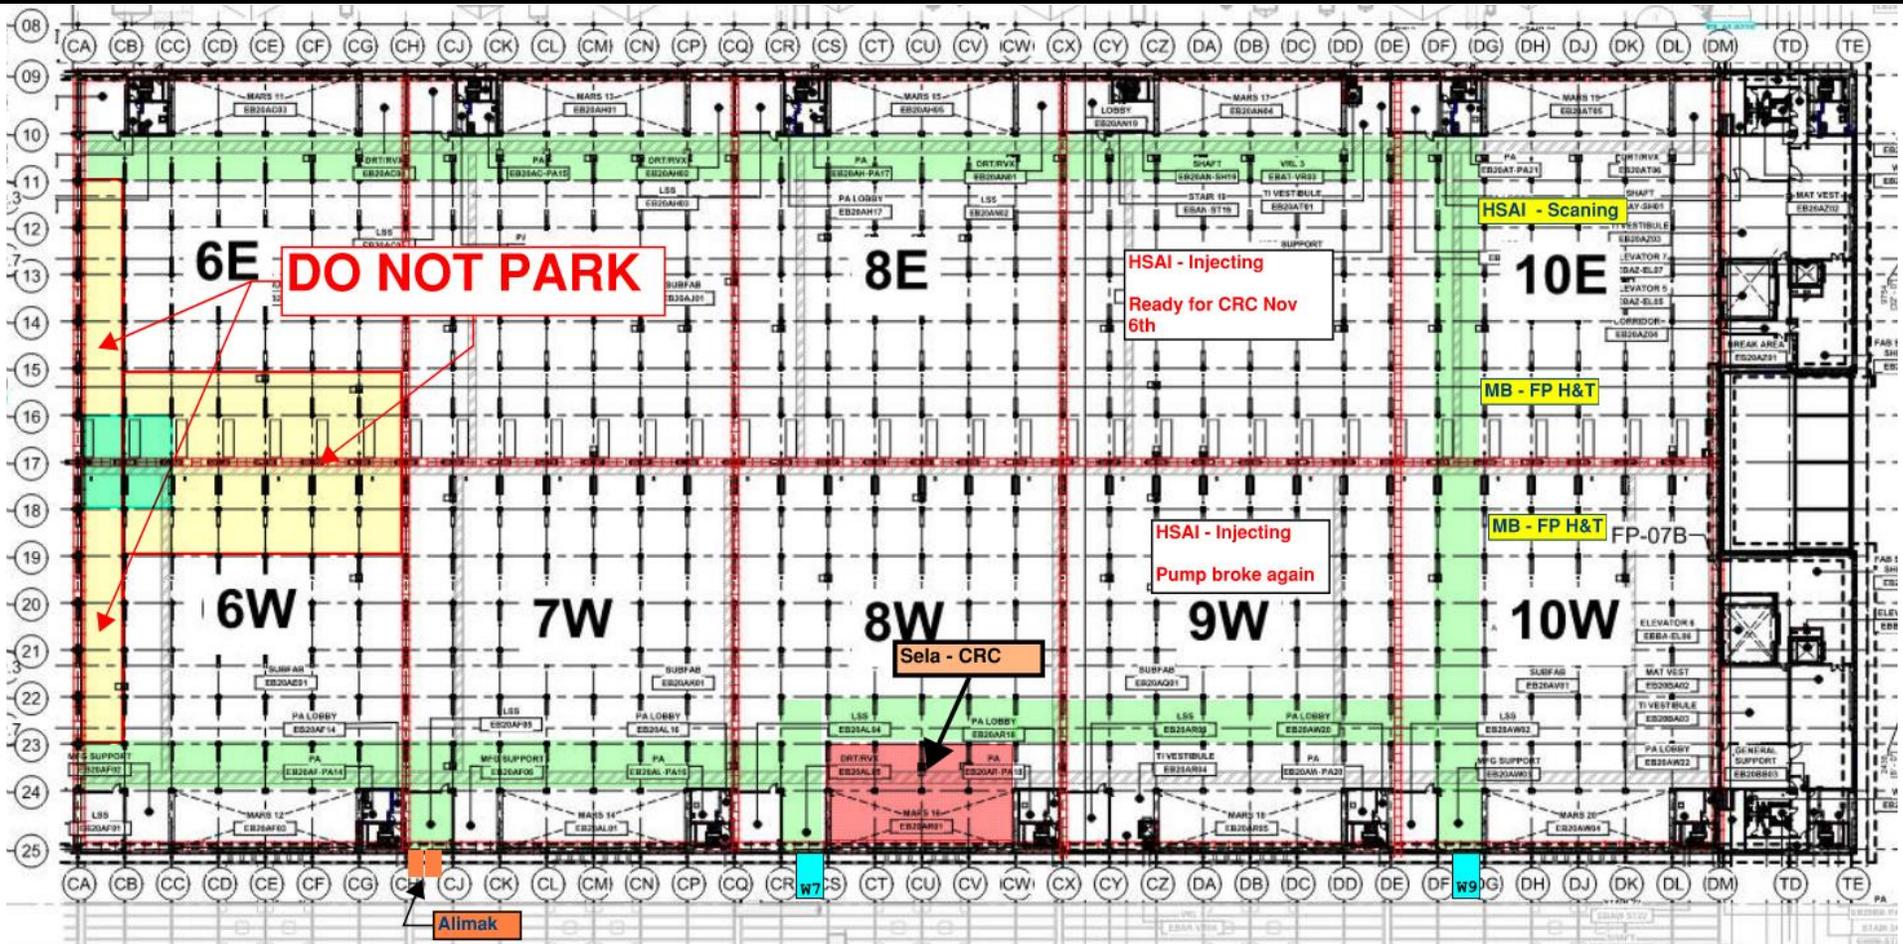

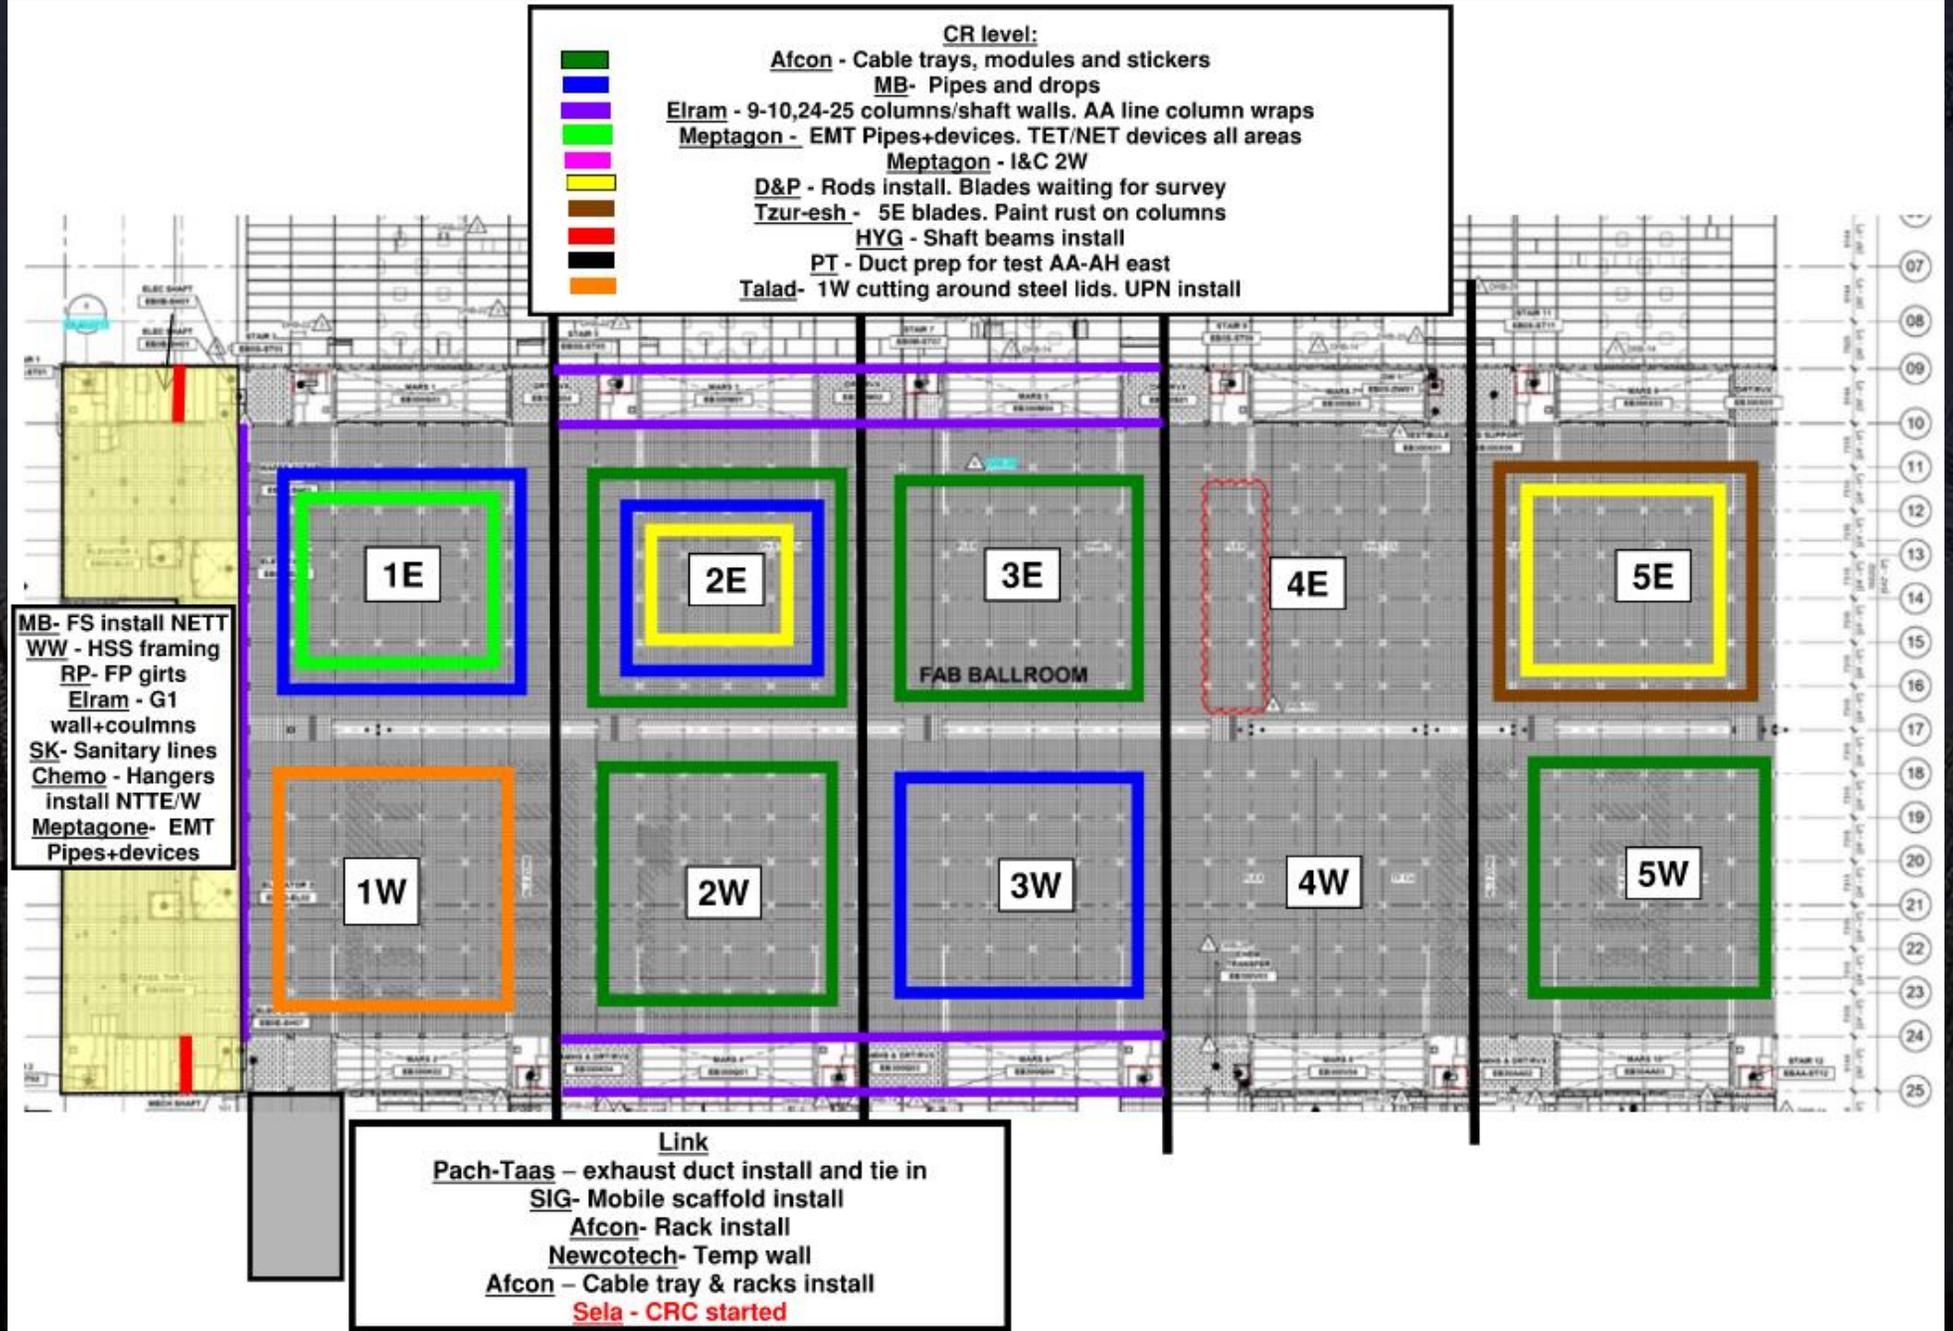

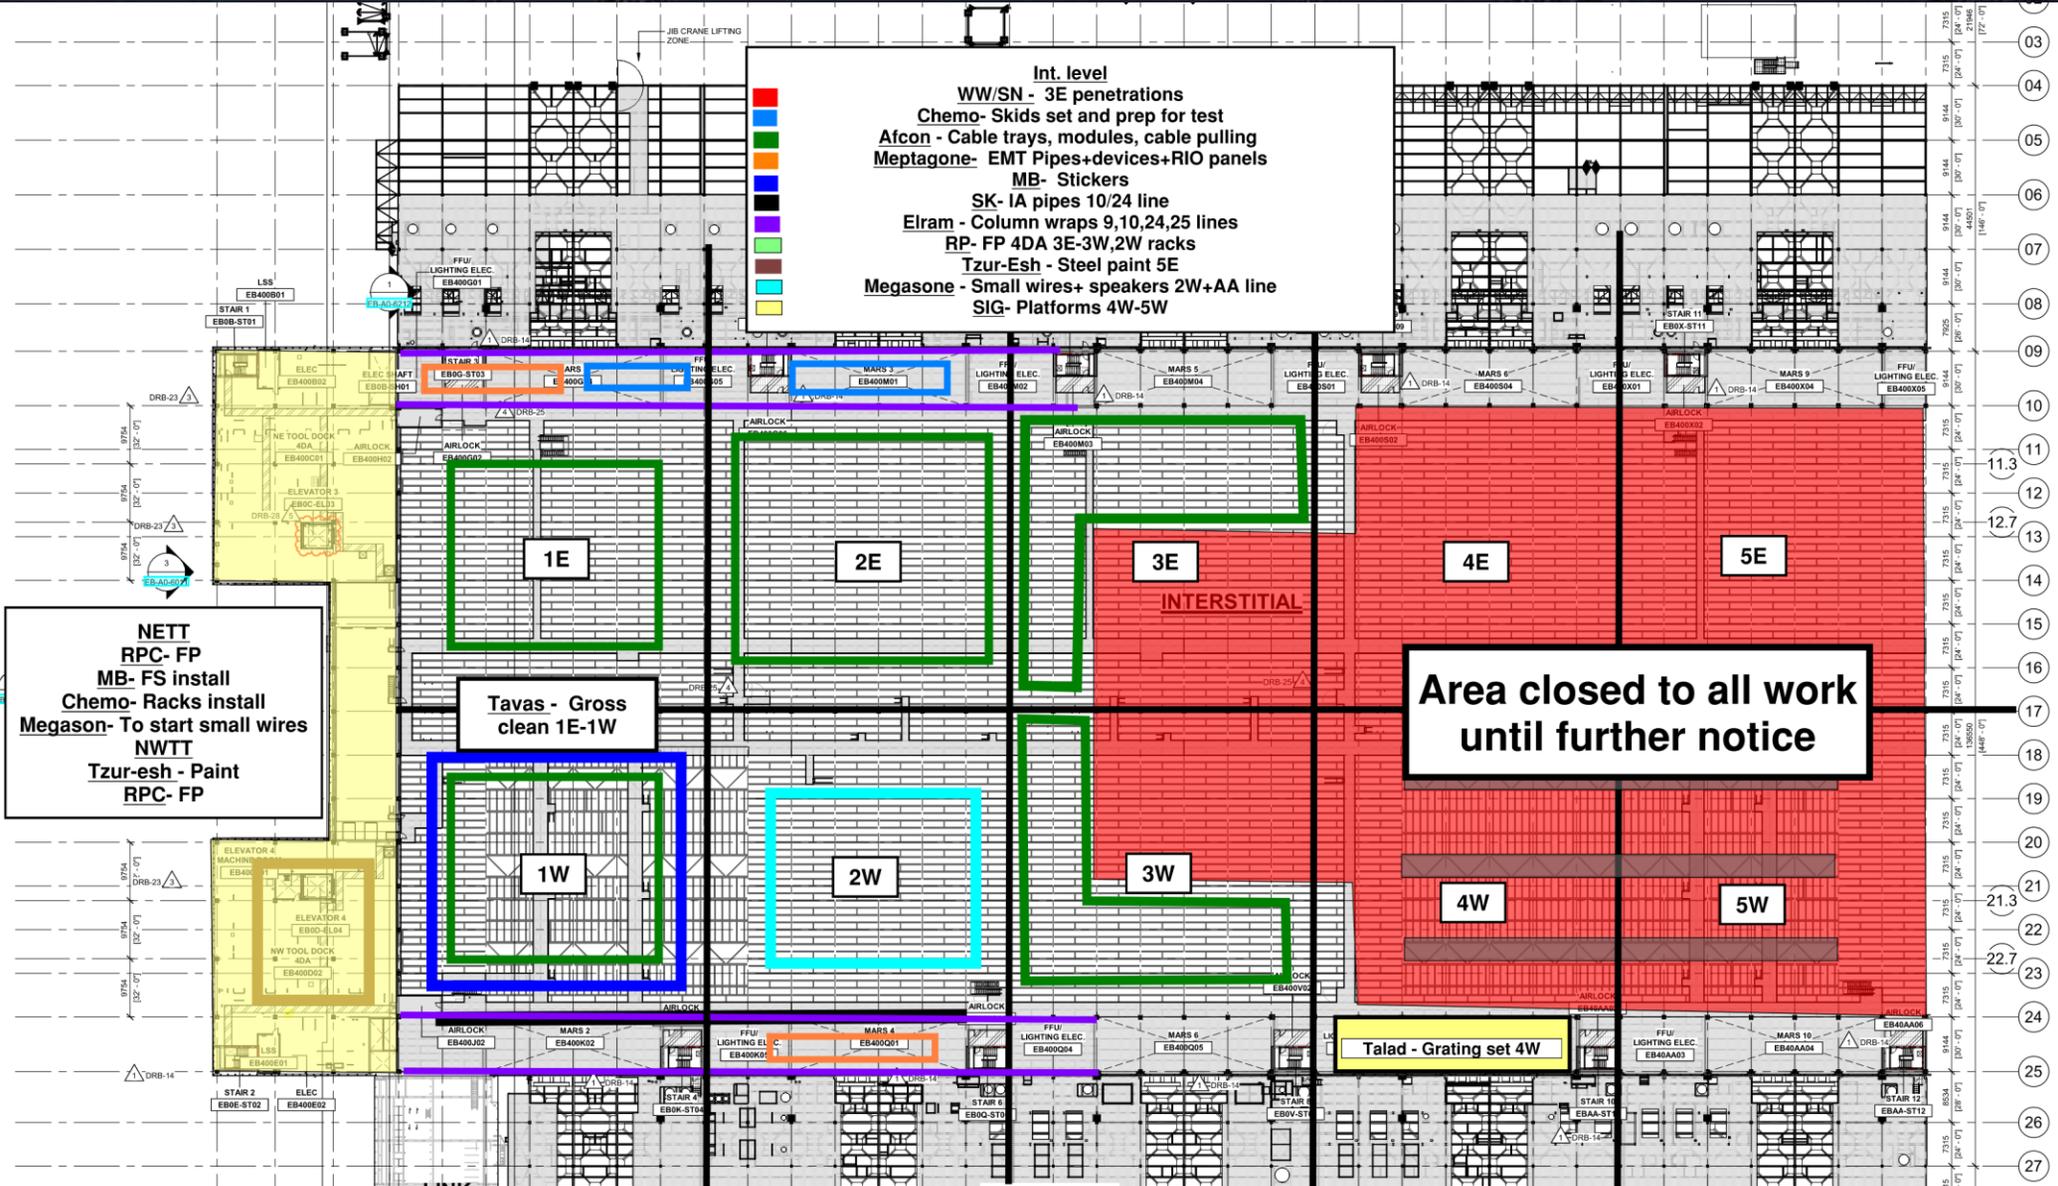

**Int. level**


- WW/SN - 3E penetrations
- Chemo- Skids set and prep for test
- Afcon - Cable trays, modules, cable pulling
- Meptagone- EMT Pipes+devices+RIO panels
- MB- Stickers
- SK- IA pipes 10/24 line
- Elram - Column wraps 9,10,24,25 lines
- RP- FP 4DA 3E-3W,2W racks
- Tzur-Esh - Steel paint 5E
- Megasone - Small wires+ speakers 2W+AA line
- SIG- Platforms 4W-5W

**NETT**  
RPC- FP  
MB- FS install  
Chemo- Racks install  
Megasone- To start small wires  
NWTT  
Tzur-esh - Paint  
RPC- FP

**Tavas - Gross clean 1E-1W**

**Area closed to all work until further notice**

**Talad - Grating set 4W**

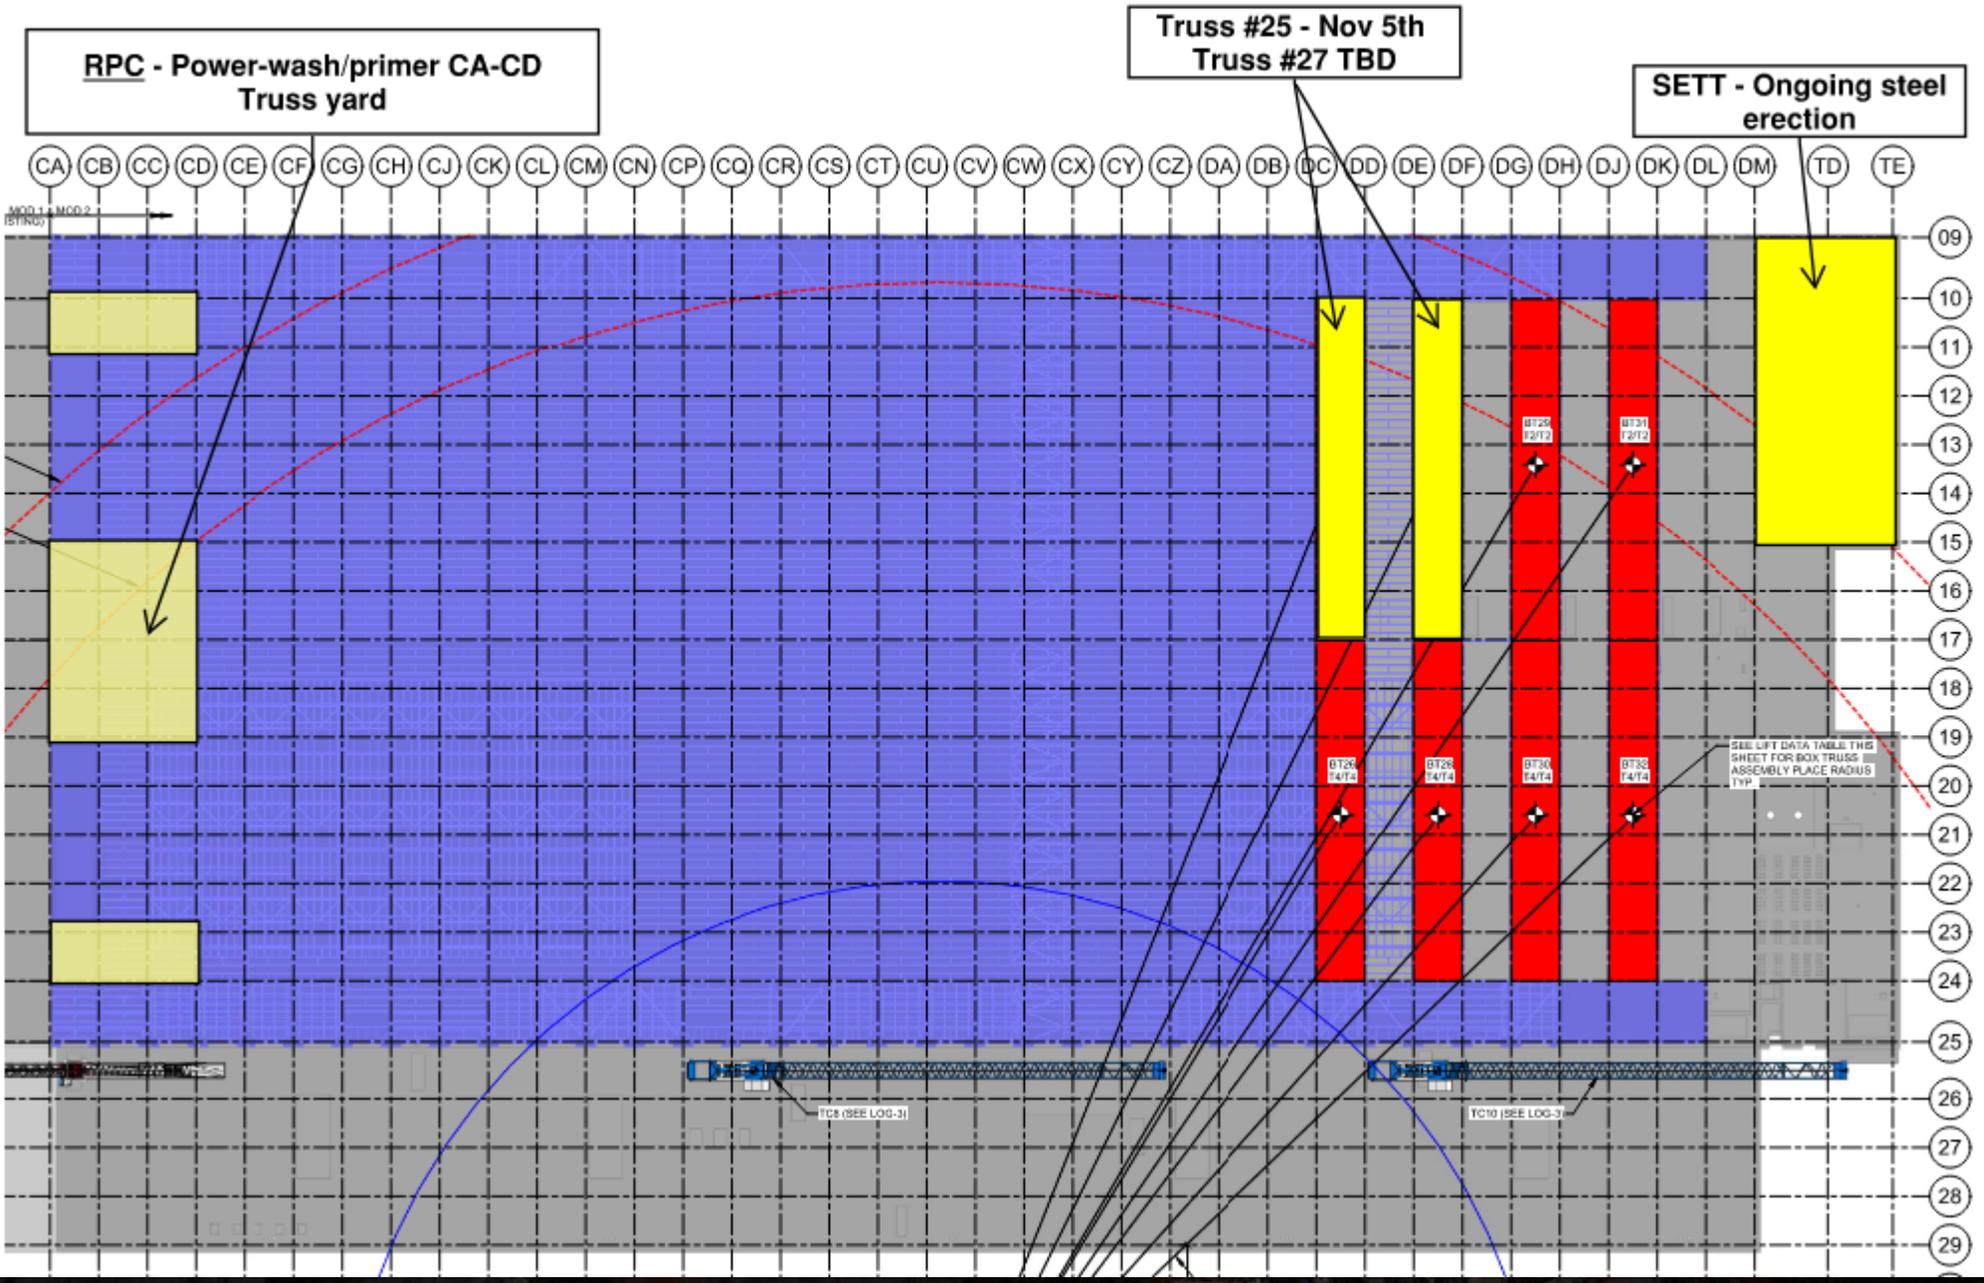

# PL1 – Envelope closure

---



## Keep small Particles levels below 1 million

(particles size 0.5 nm)

(outside air particles level usually above this level)

All we should do is:

Clean up!

Everywhere!

All times!



## Keep good housekeeping practice

All you should is making sure your equipment is properly maintained

Take trash away (to trash bin or out of Area)


All storage in order and in safe manner



## Keep infrastructure integrity

Damage prevention to CRC floor, Walls (permanent or Temporary)

If damage occurs - report immediately to your supervisor

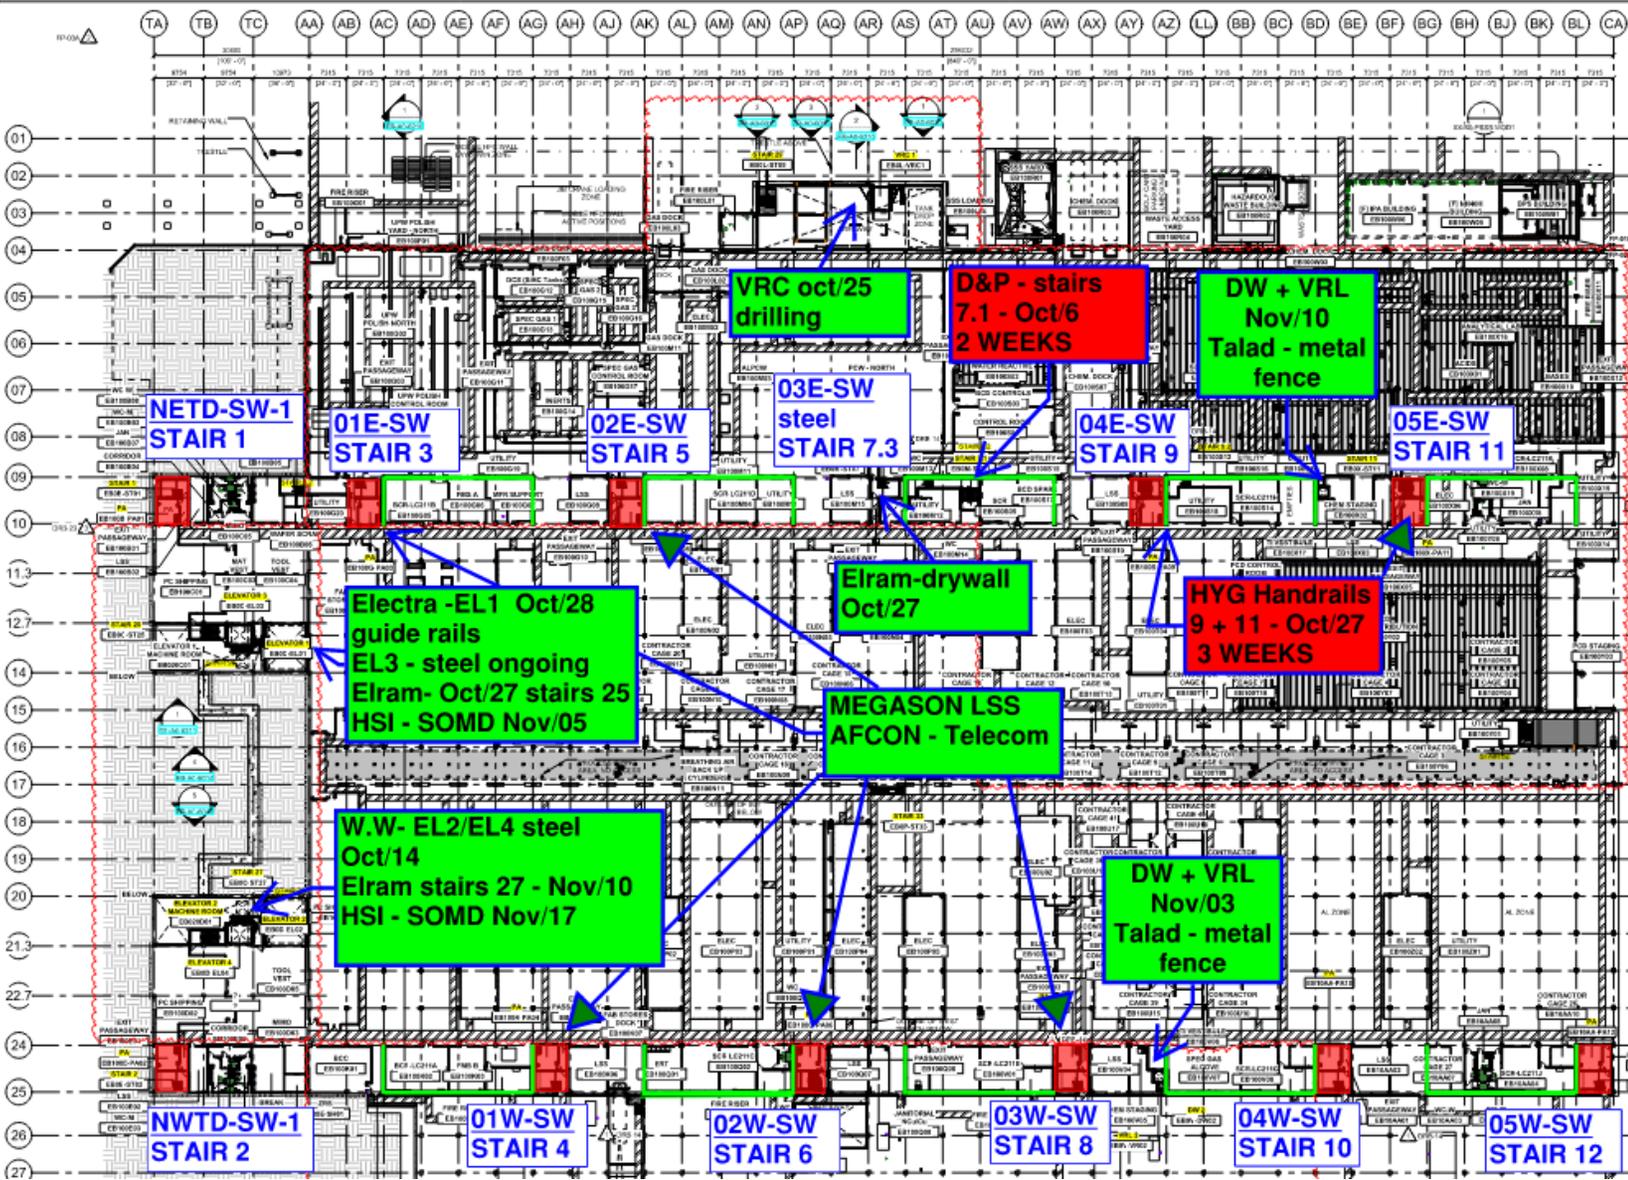




Siding - West FAB - JYG

BLOWDOWN 30%

	TA	TB	TC	AA	AB	AC	AD	AE	AF	AG	AH	AJ	AK	AL	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BJ	BK	BL	CA								
	1001/1002			601/602			611/612					621/622				631/632				641/642				651/652				611/612				621/622				631/632				641/642				651/652			
Totals	28	28	28	15	15		31	31	31	31	31	31	31	29	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31					
Invent	21	24	12	15	15		31	31	31	31	31	31	31	29	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31				
%	75%	86%	43%	99%	99%		100%	100%	99%	100%	100%	100%	100%	97%	91%	77%	71%	94%	74%	48%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%					
SRA	0	0	0	0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
ADA	0	0	0	0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
ZFC	0	0	0	0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
ZFA	0	0	0	0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
ZSA ZF	0	0	0	0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	
UL	0	0	0	0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Link

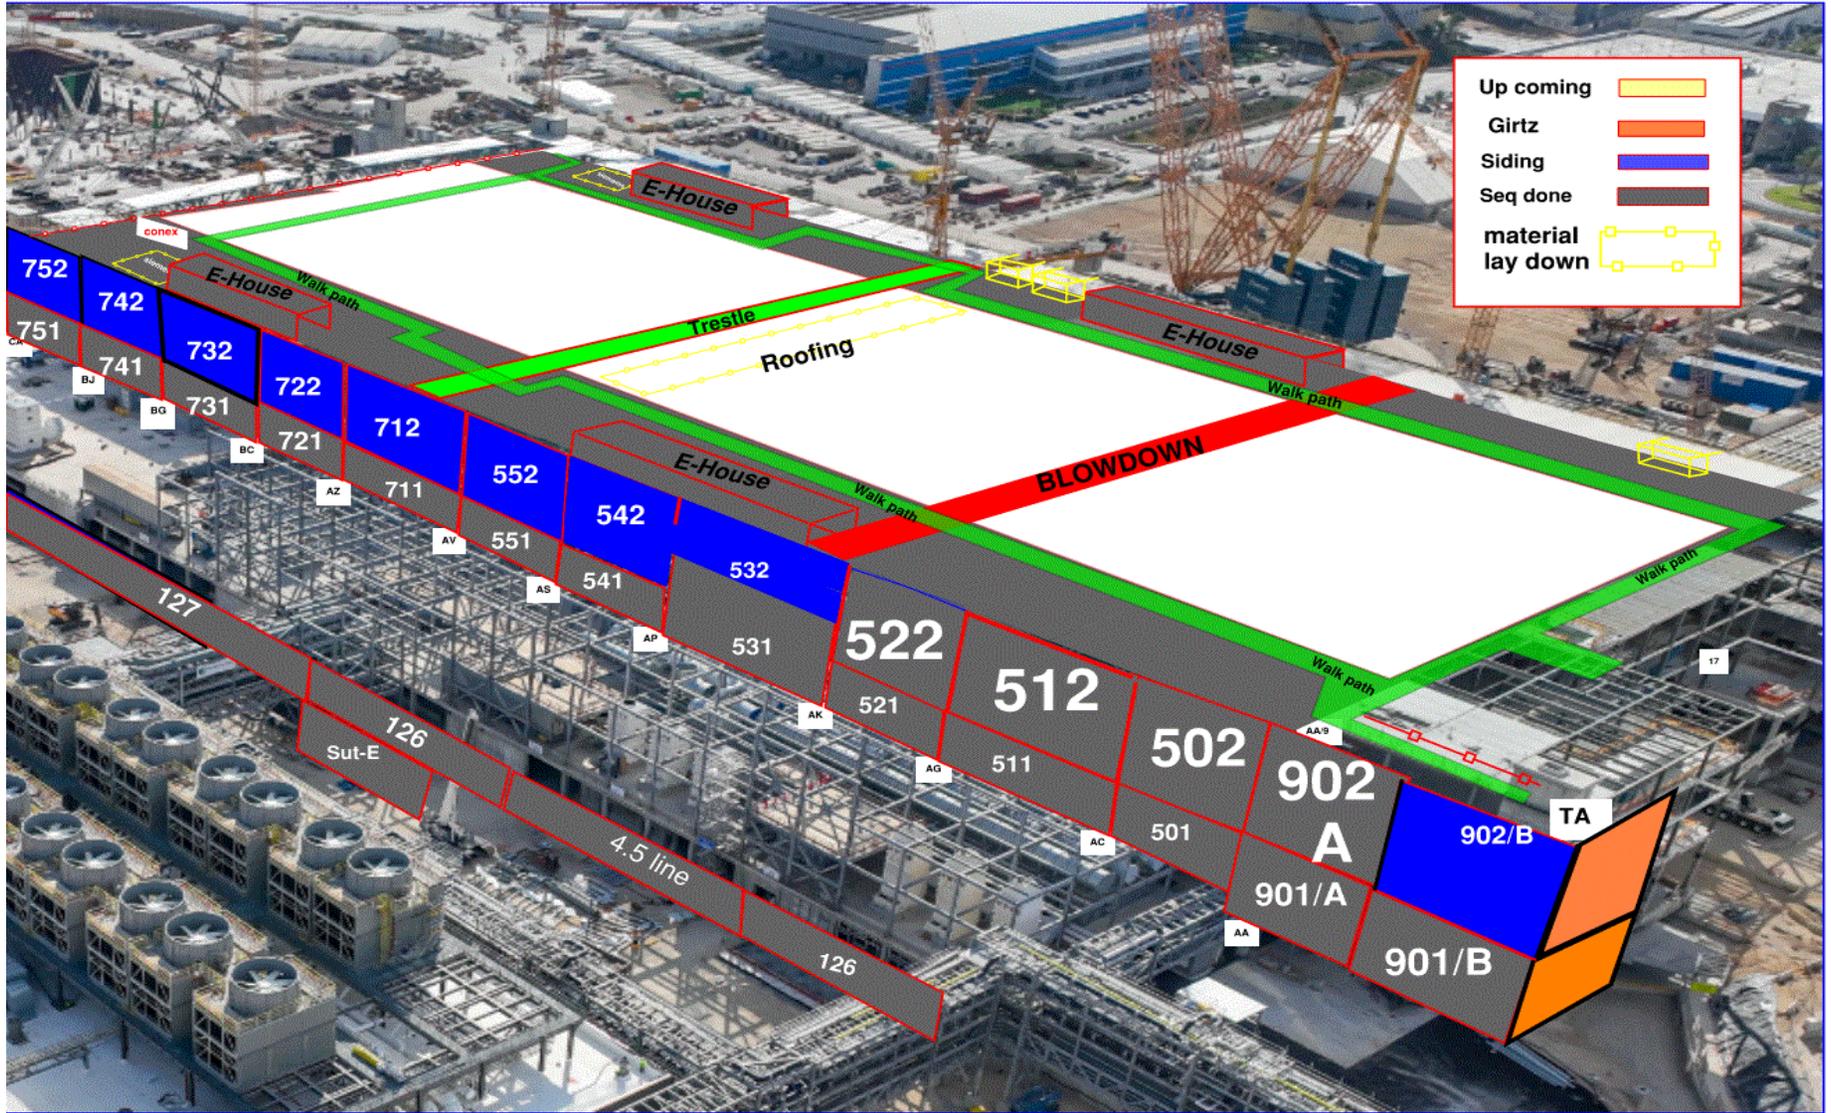

Up coming	<span style="display:inline-block; width:15px; height:10px; background-color:yellow; border:1px solid black;"></span>
Girtz	<span style="display:inline-block; width:15px; height:10px; background-color:orange; border:1px solid black;"></span>
Siding	<span style="display:inline-block; width:15px; height:10px; background-color:blue; border:1px solid black;"></span>
Seq done	<span style="display:inline-block; width:15px; height:10px; background-color:grey; border:1px solid black;"></span>
material lay down	<span style="display:inline-block; width:15px; height:10px; border:1px dashed yellow;"></span>

752

742

732

722

712

552

542

532

522

512

502

902

902/B

901/A

901/B

TA

127

126

4.5 line

126

Sut-E

conex

BJ

BG

BC

AZ

AV

AS

AP

AK

AG

AC

AA

17

AA-9

AA

E-House

E-House

E-House

E-House

BLOWDOWN

Roofing

Trestle


Walk path

Walk path

Walk path

Walk path

Walk path

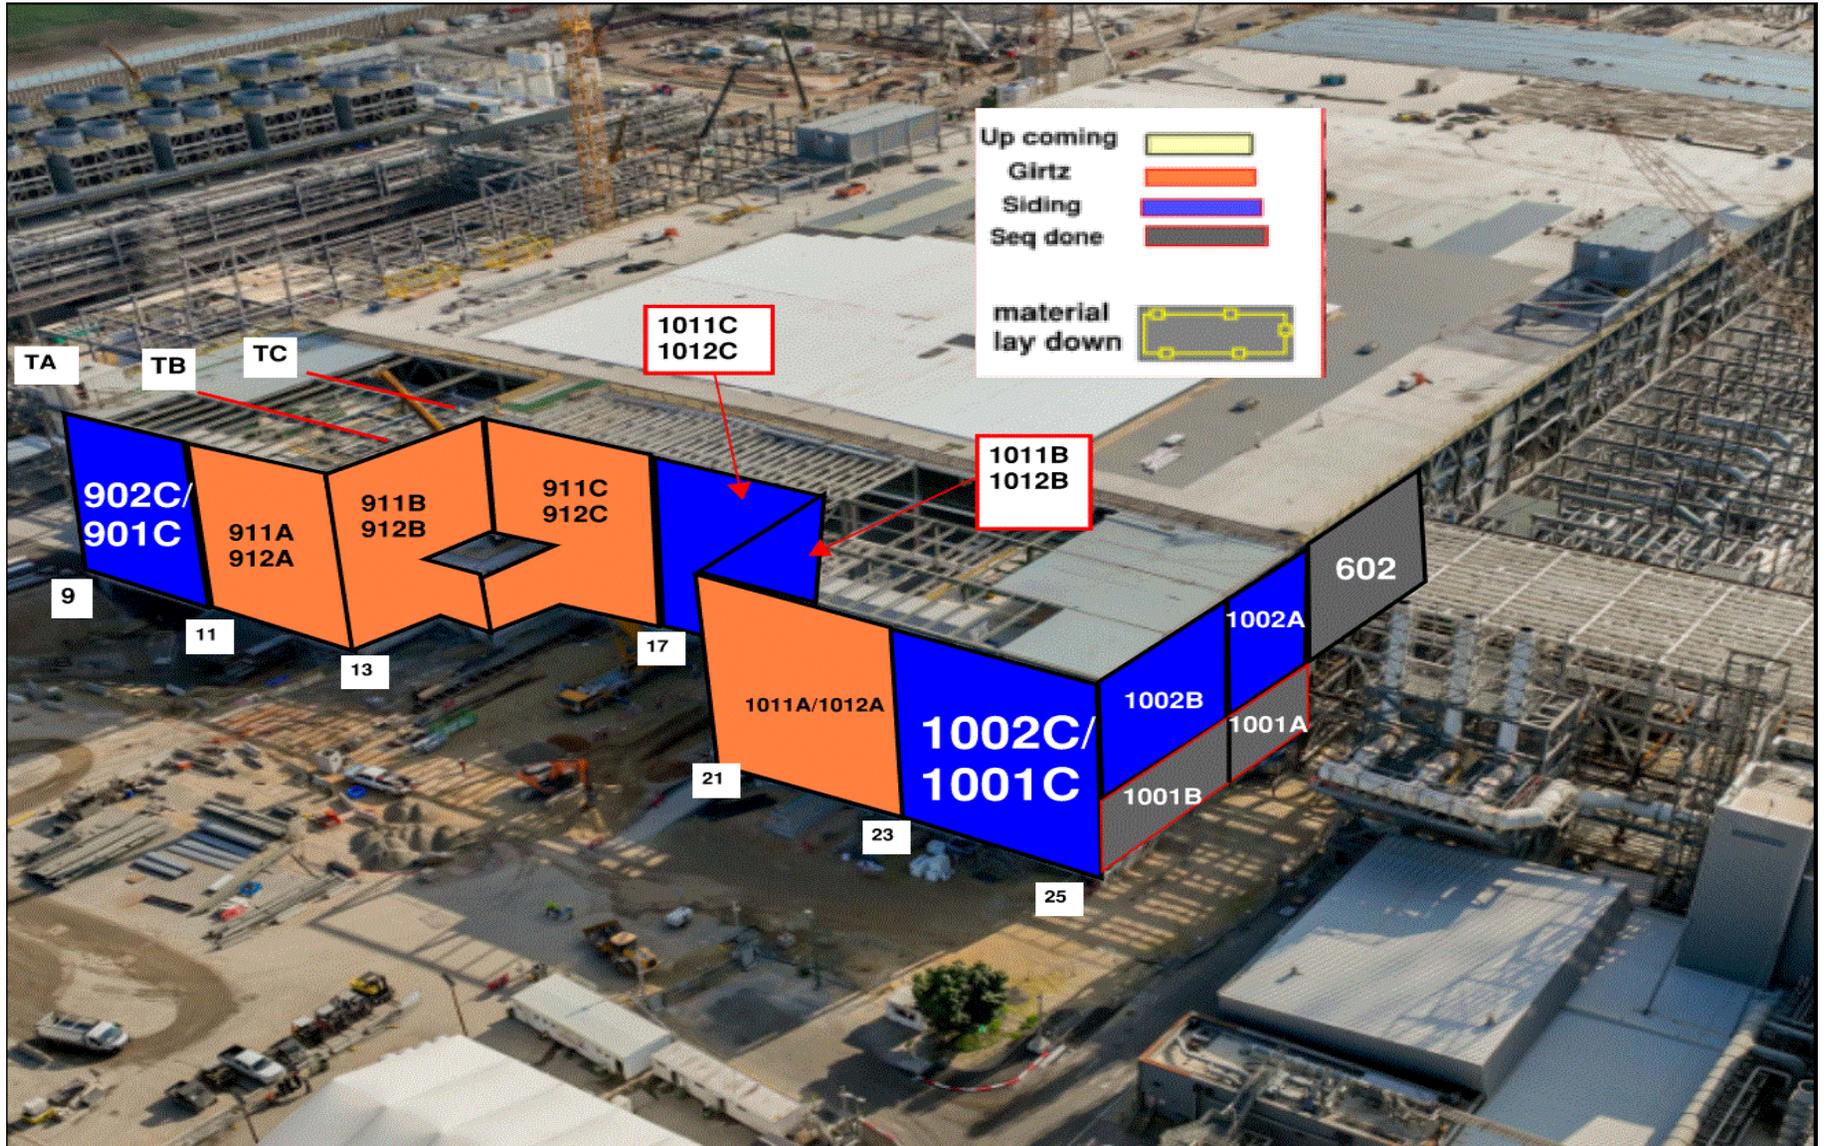

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

TA

TB

TC

1011C  
1012C

1011B  
1012B

902C/  
901C

911A  
912A

911B  
912B

911C  
912C

602

9

11

13

17

1011A/1012A

1002C/  
1001C

1002A

1002B


1001A

1001B

21

23

25

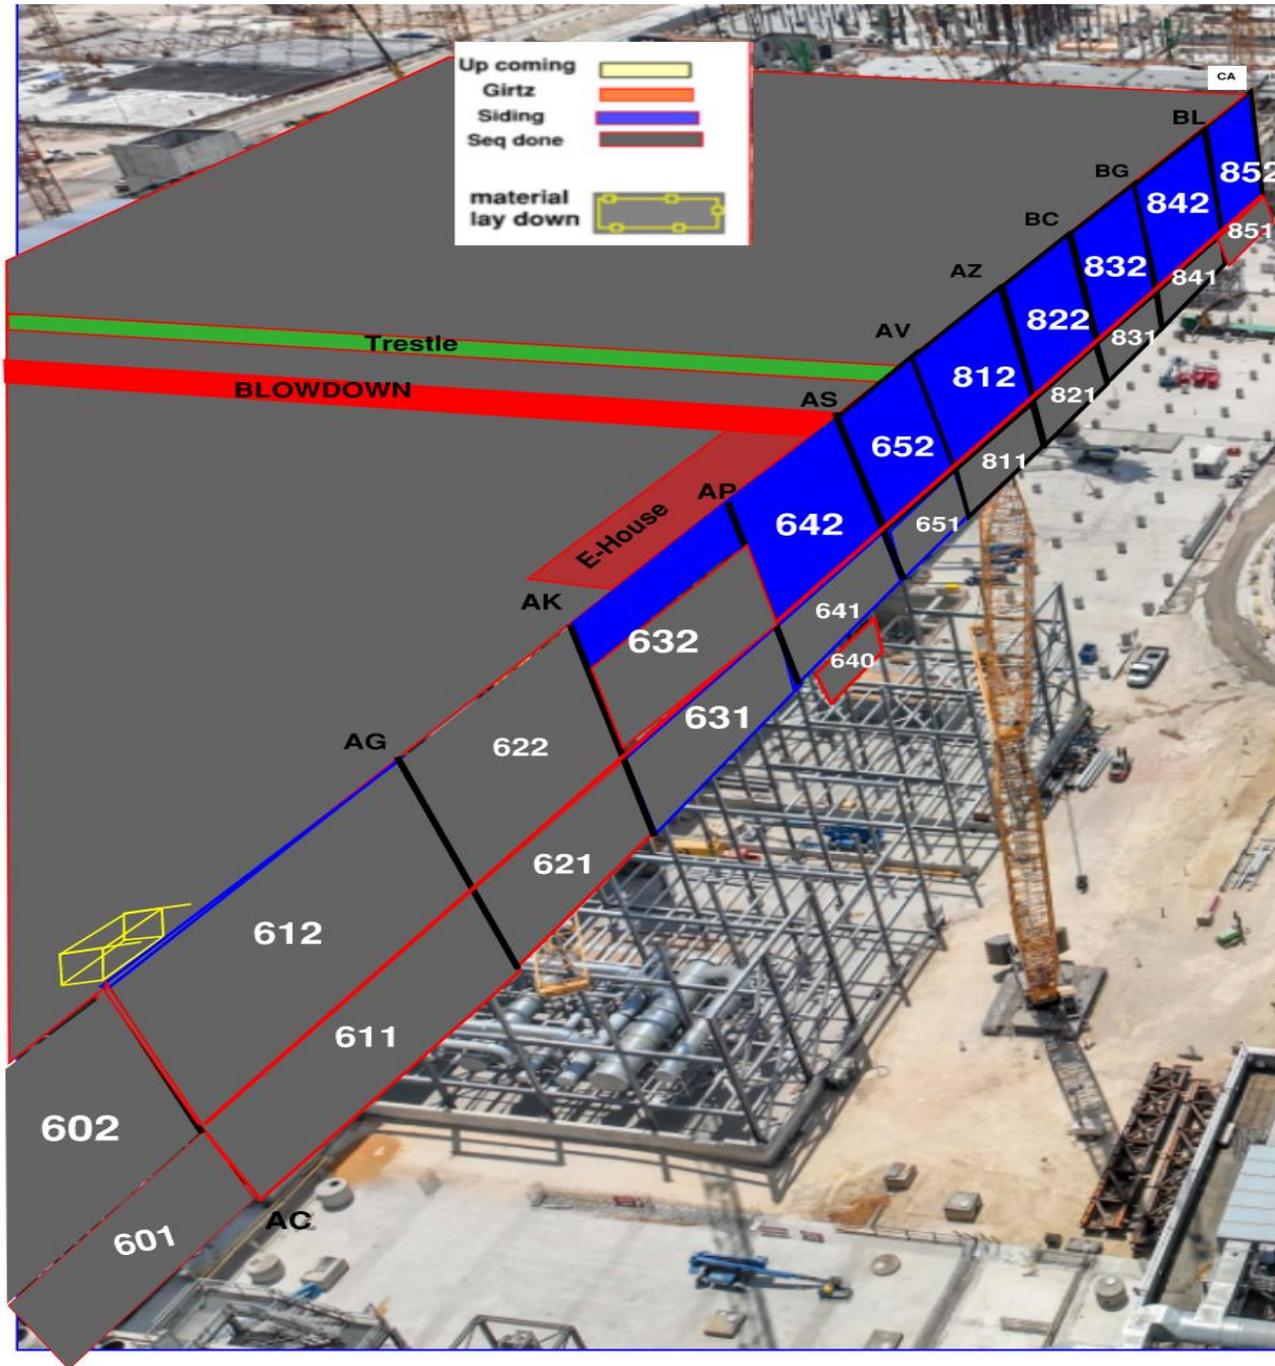


X



# PSSS.1


## Utility Level 1YA

## PSSS Roof 2SA

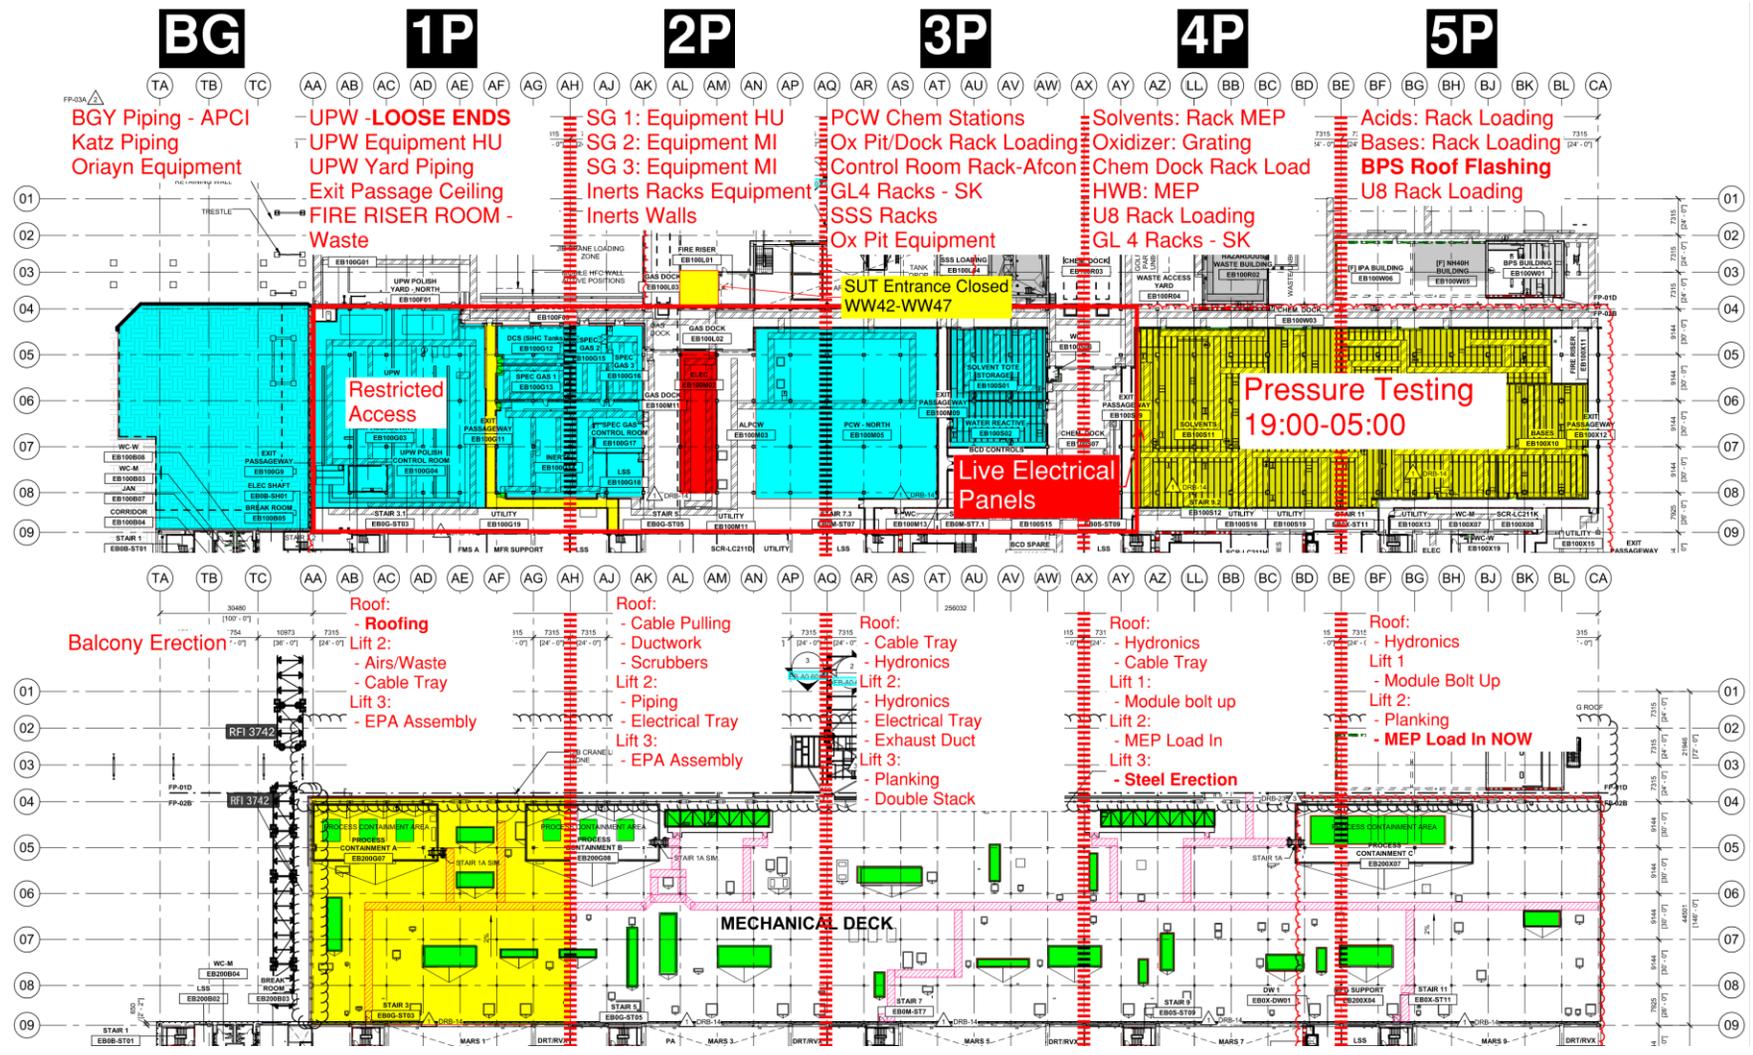



# WJG 01J, 02J LIFT 2 & 3

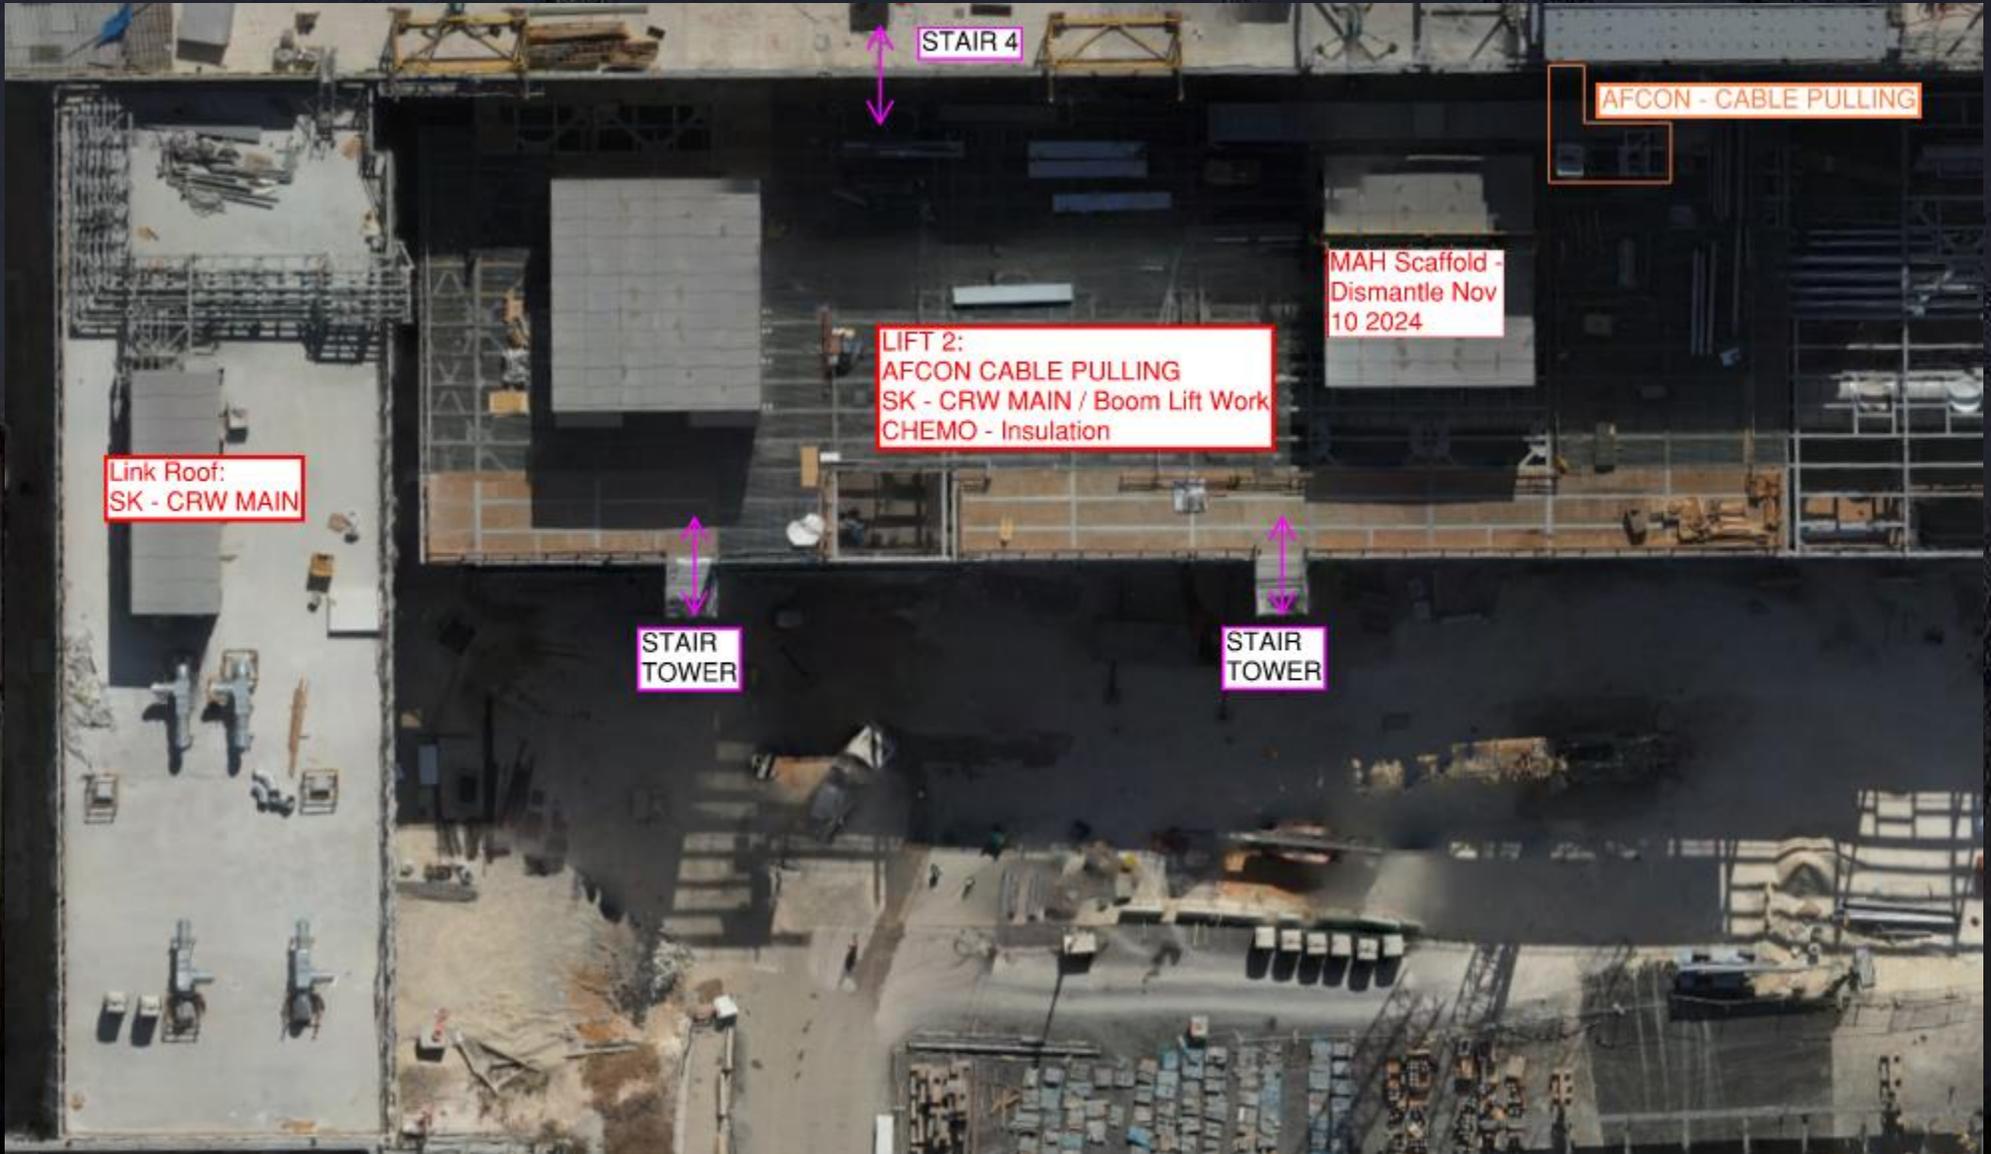


# WJG 03J, 04J, 05J LIFT 2 & 3






# MAH101-7/8-00 SET: TBD

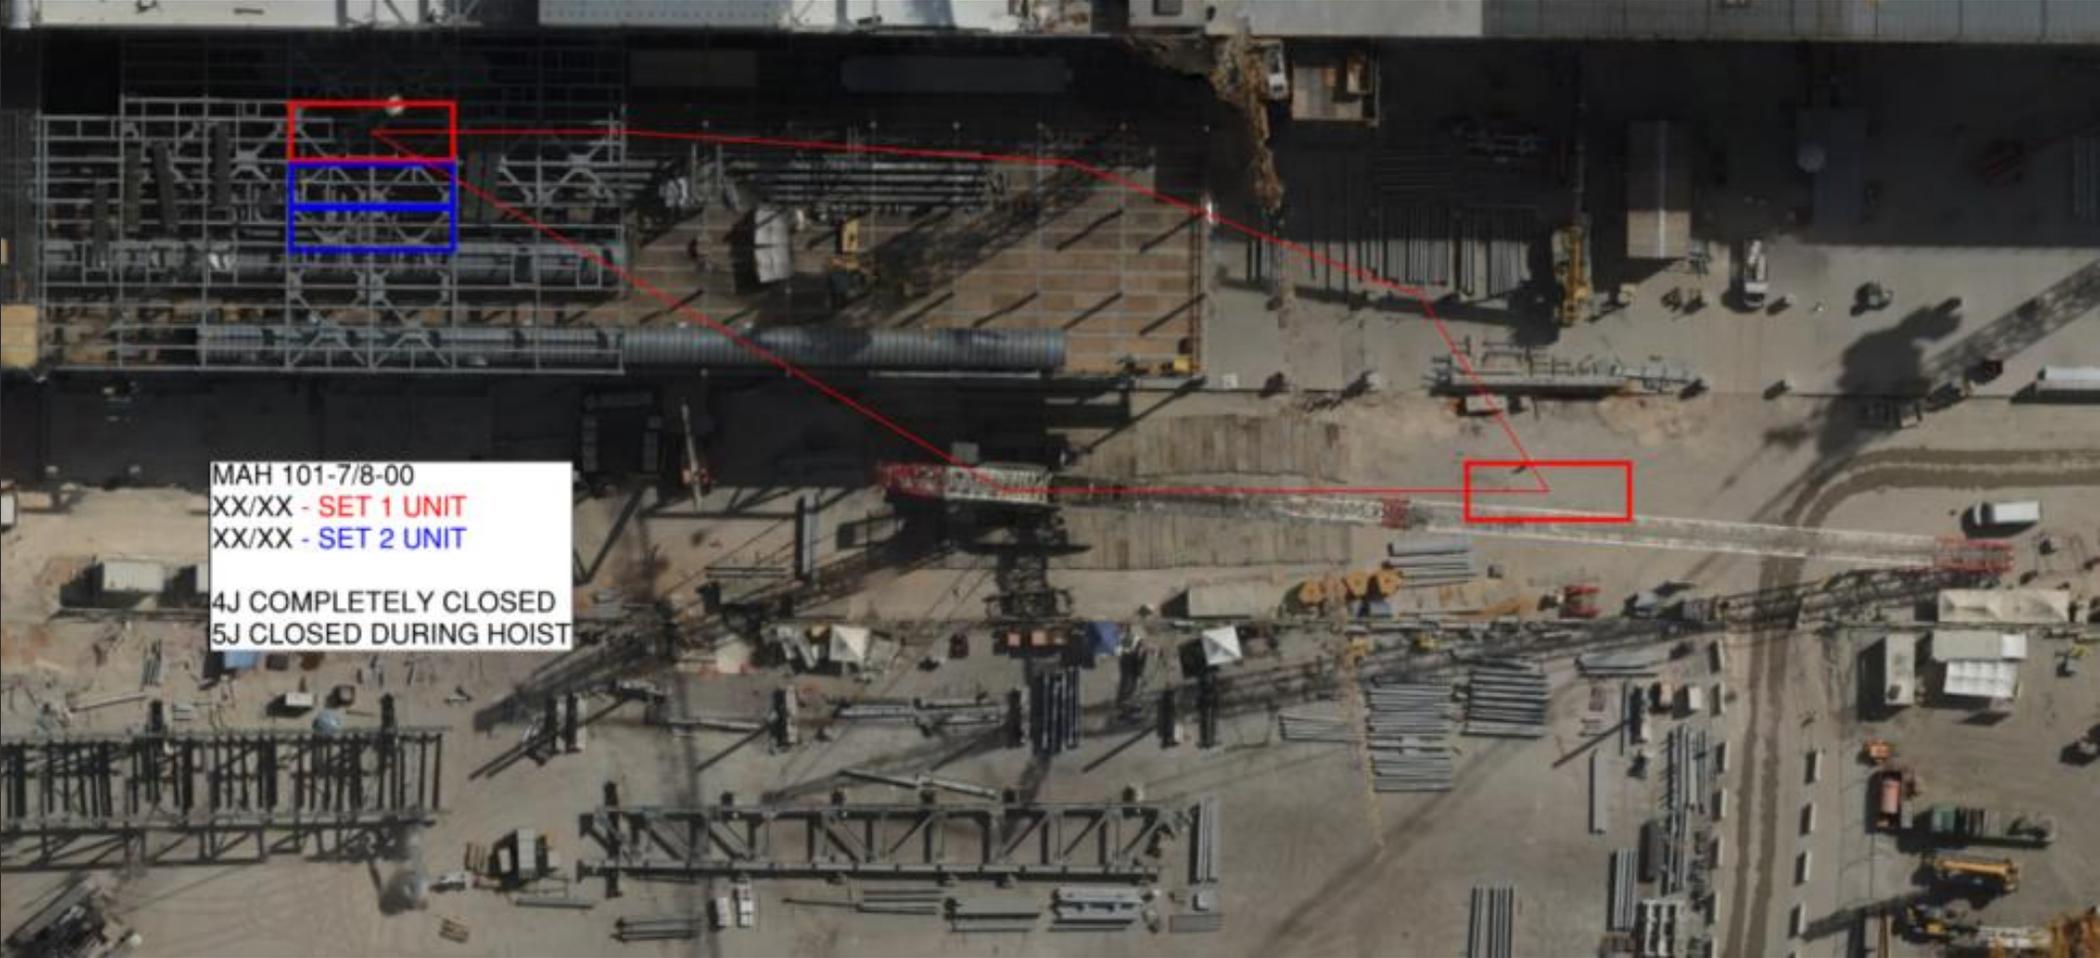


MAH 101-7/8-00  
XX/XX - SET 1 UNIT  
XX/XX - SET 2 UNIT  
4J COMPLETELY CLOSED  
5J CLOSED DURING HOIST

# WJG UTILITY LEVEL BUILD OUT

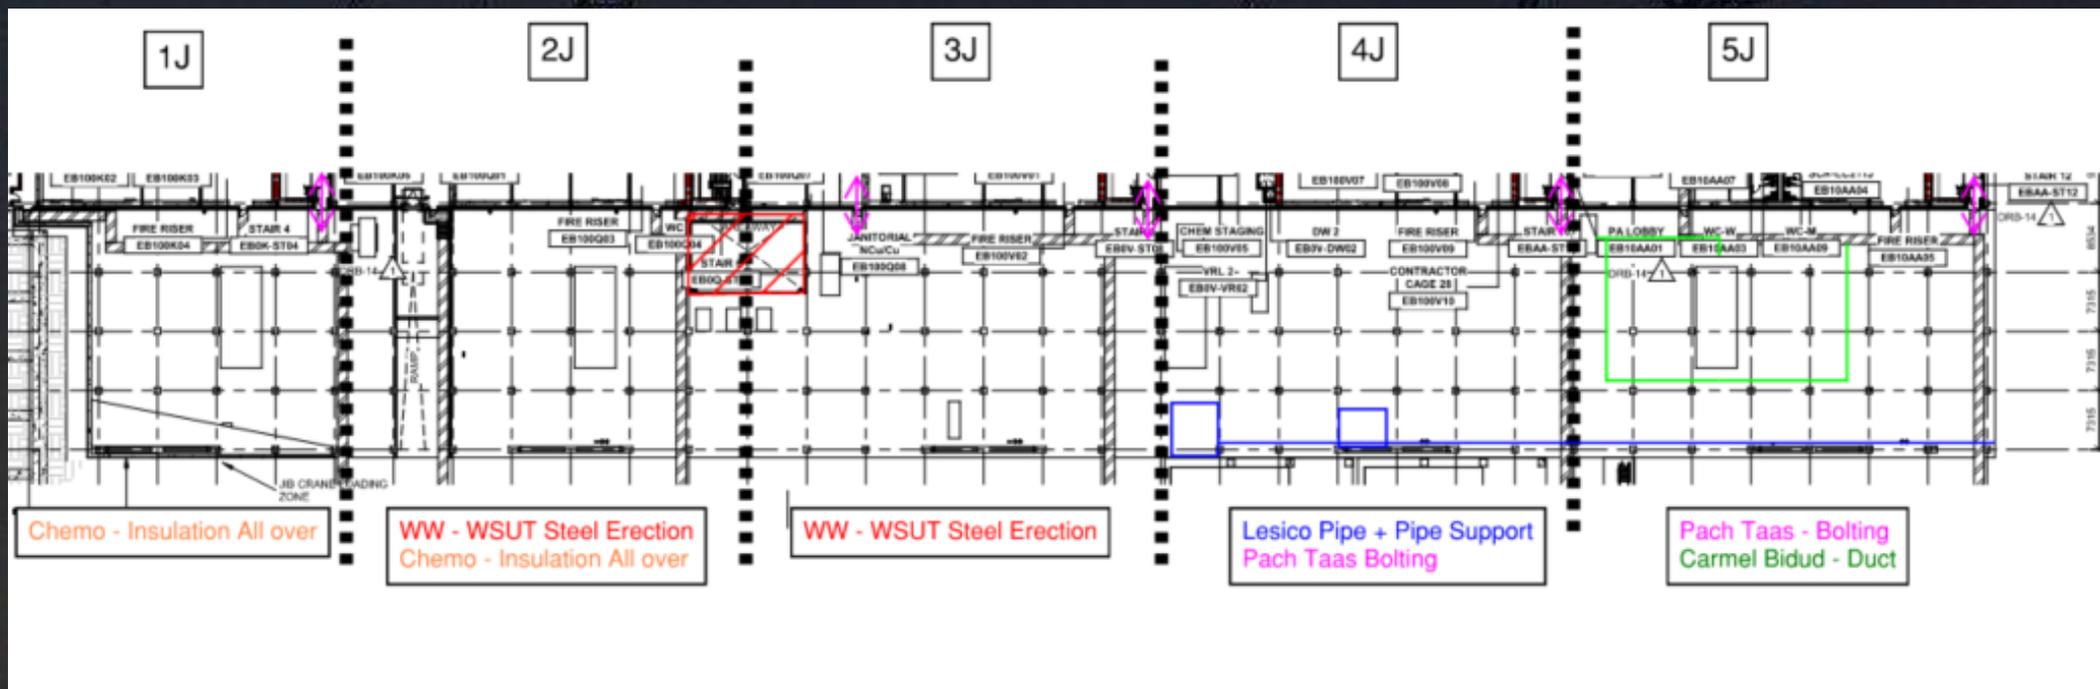

# CUB 1

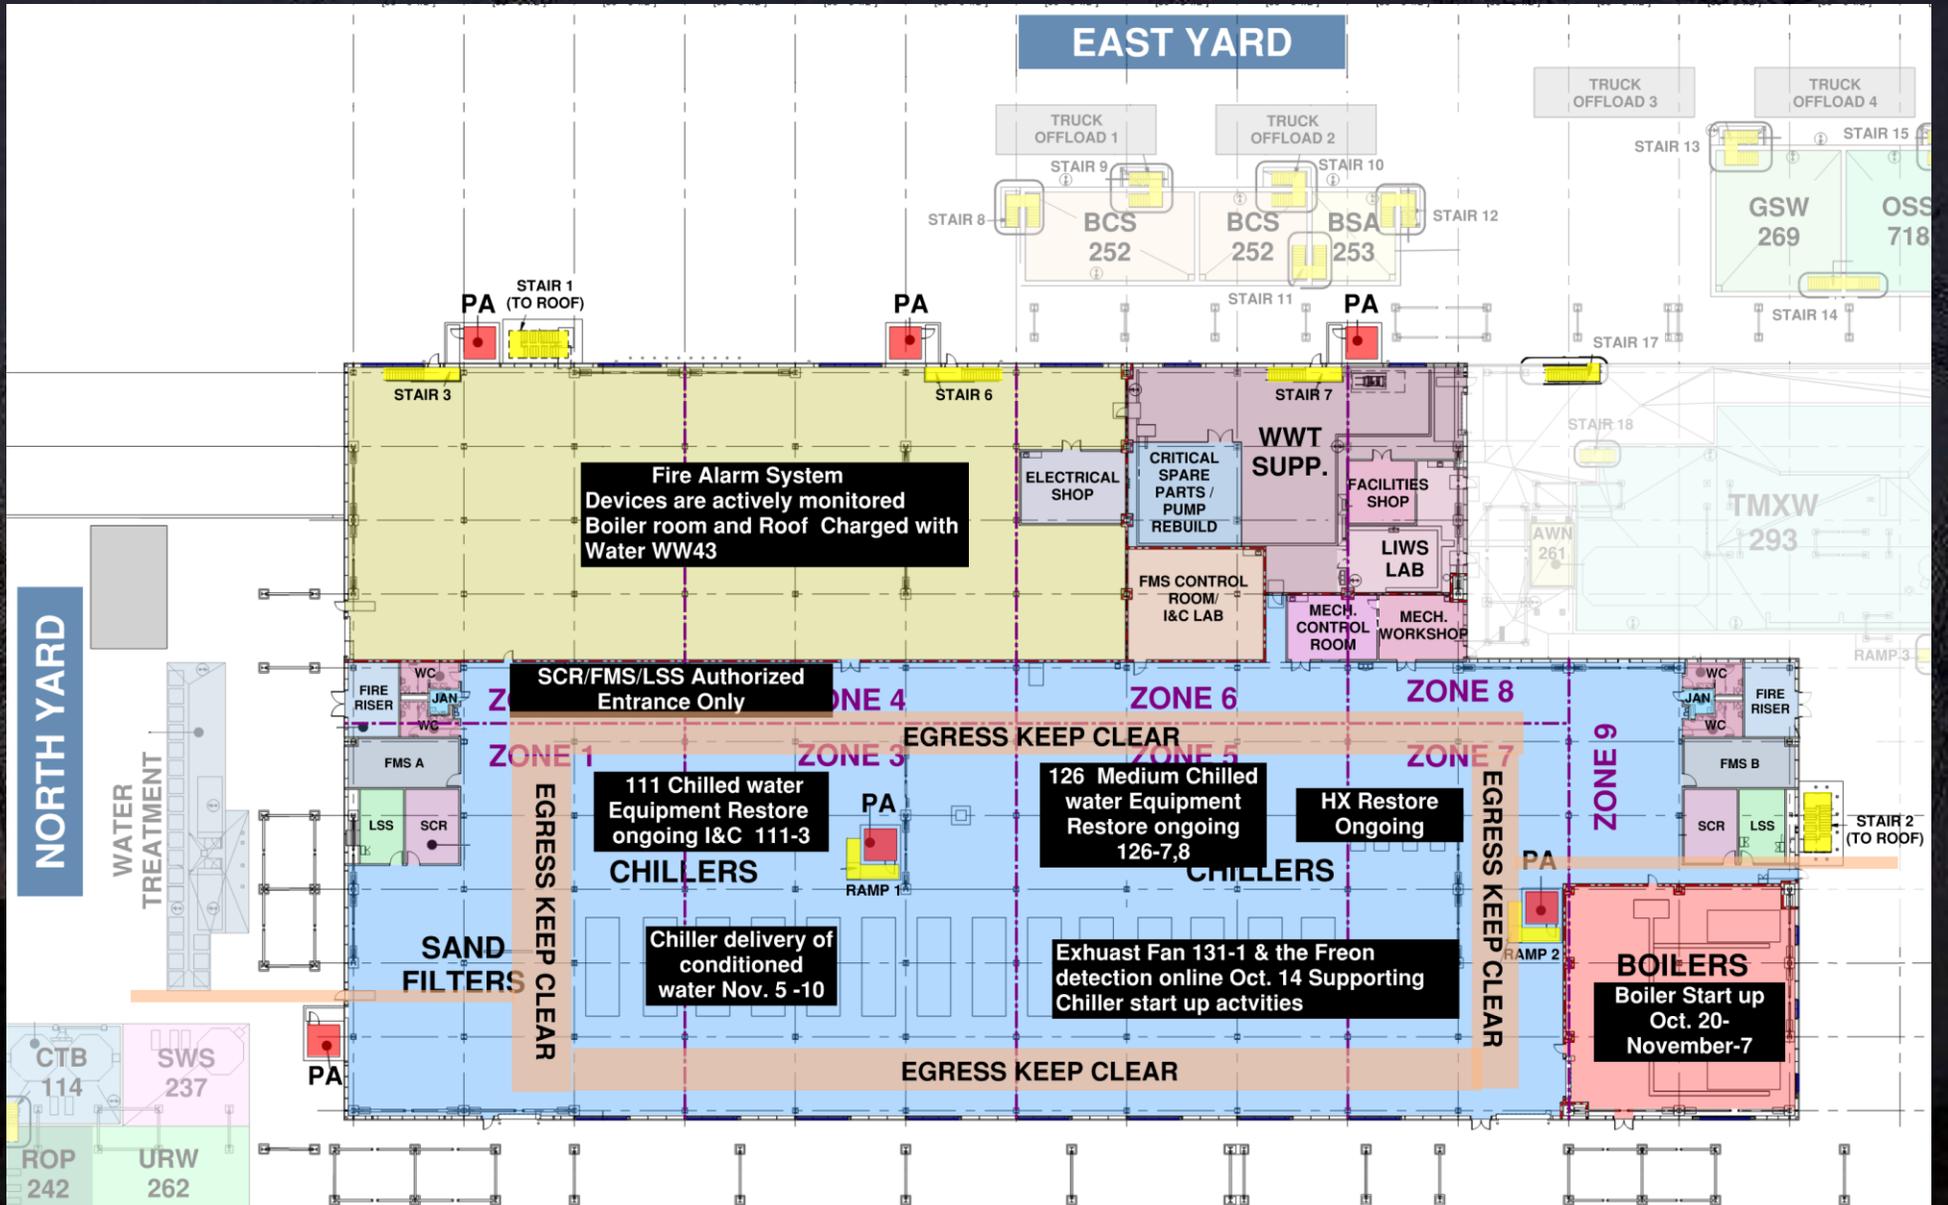


# CUB 1 – Refrigerant Loading


## CUB 1 COORDINATION MAP

A B C D E F G H J K L M N P Q R S


**NOTES:**  
 1. REFRIGERANT DETECTION SYSTEM IS LIVE.  
 2. IF ANY ALARM IS SOUNDED - ALL WORKERS MUST EVACUATE THE BUILDING. HORNS AND STROBES WILL SOUND AND INDICATE A GAS LEAK.  
 3. EVACUATION LOCATION TO BE IN NORTH YARD OF CUB 1. UNTIL AREA IS SAFE TO RETURN

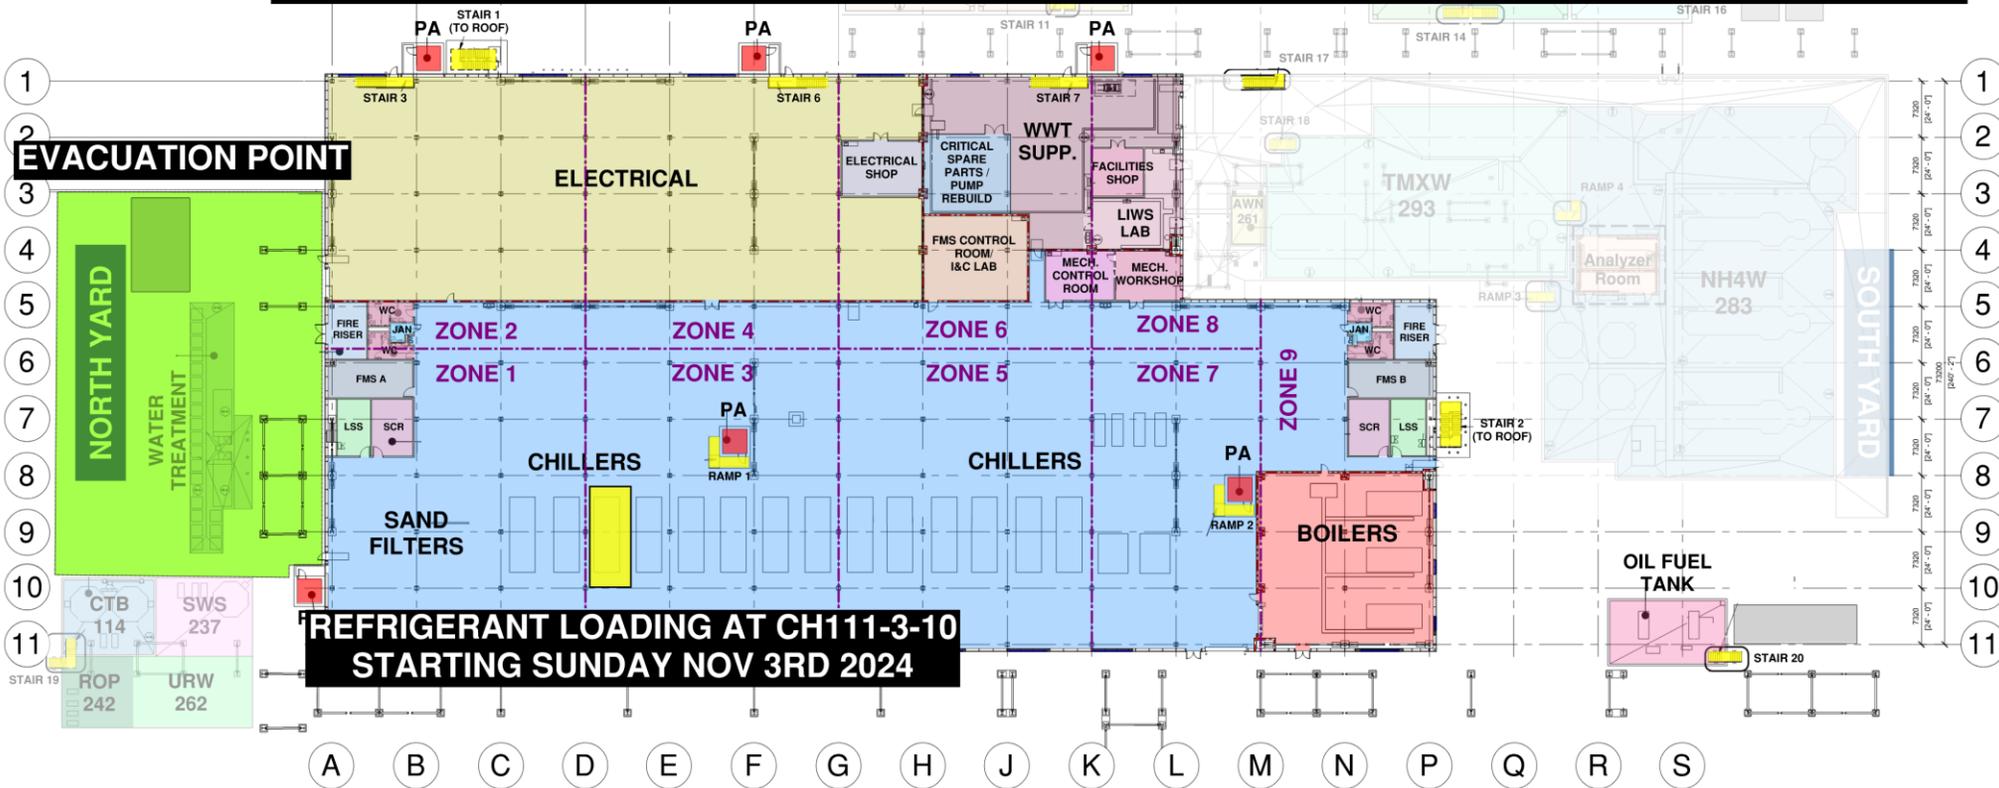


# CUB 1 – EXTERIOR/ROOF

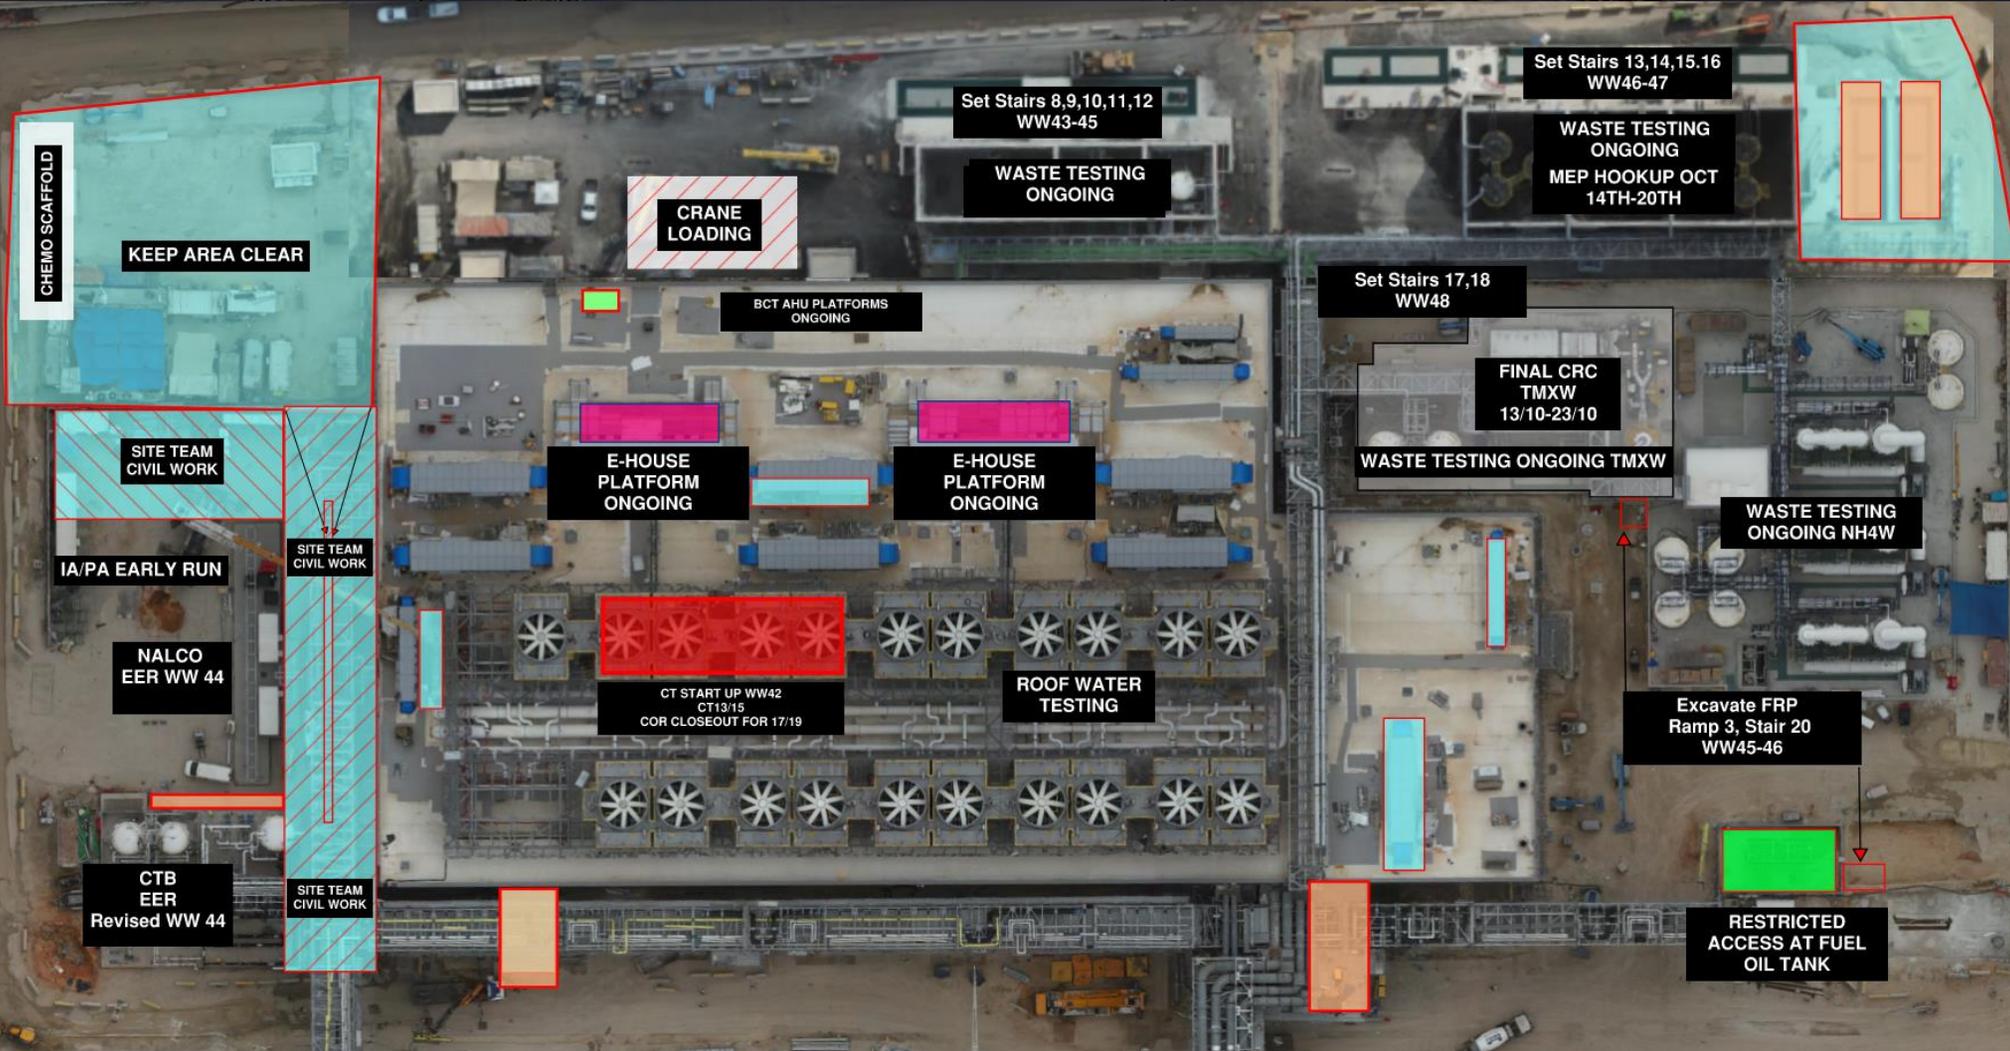

# CUB 2

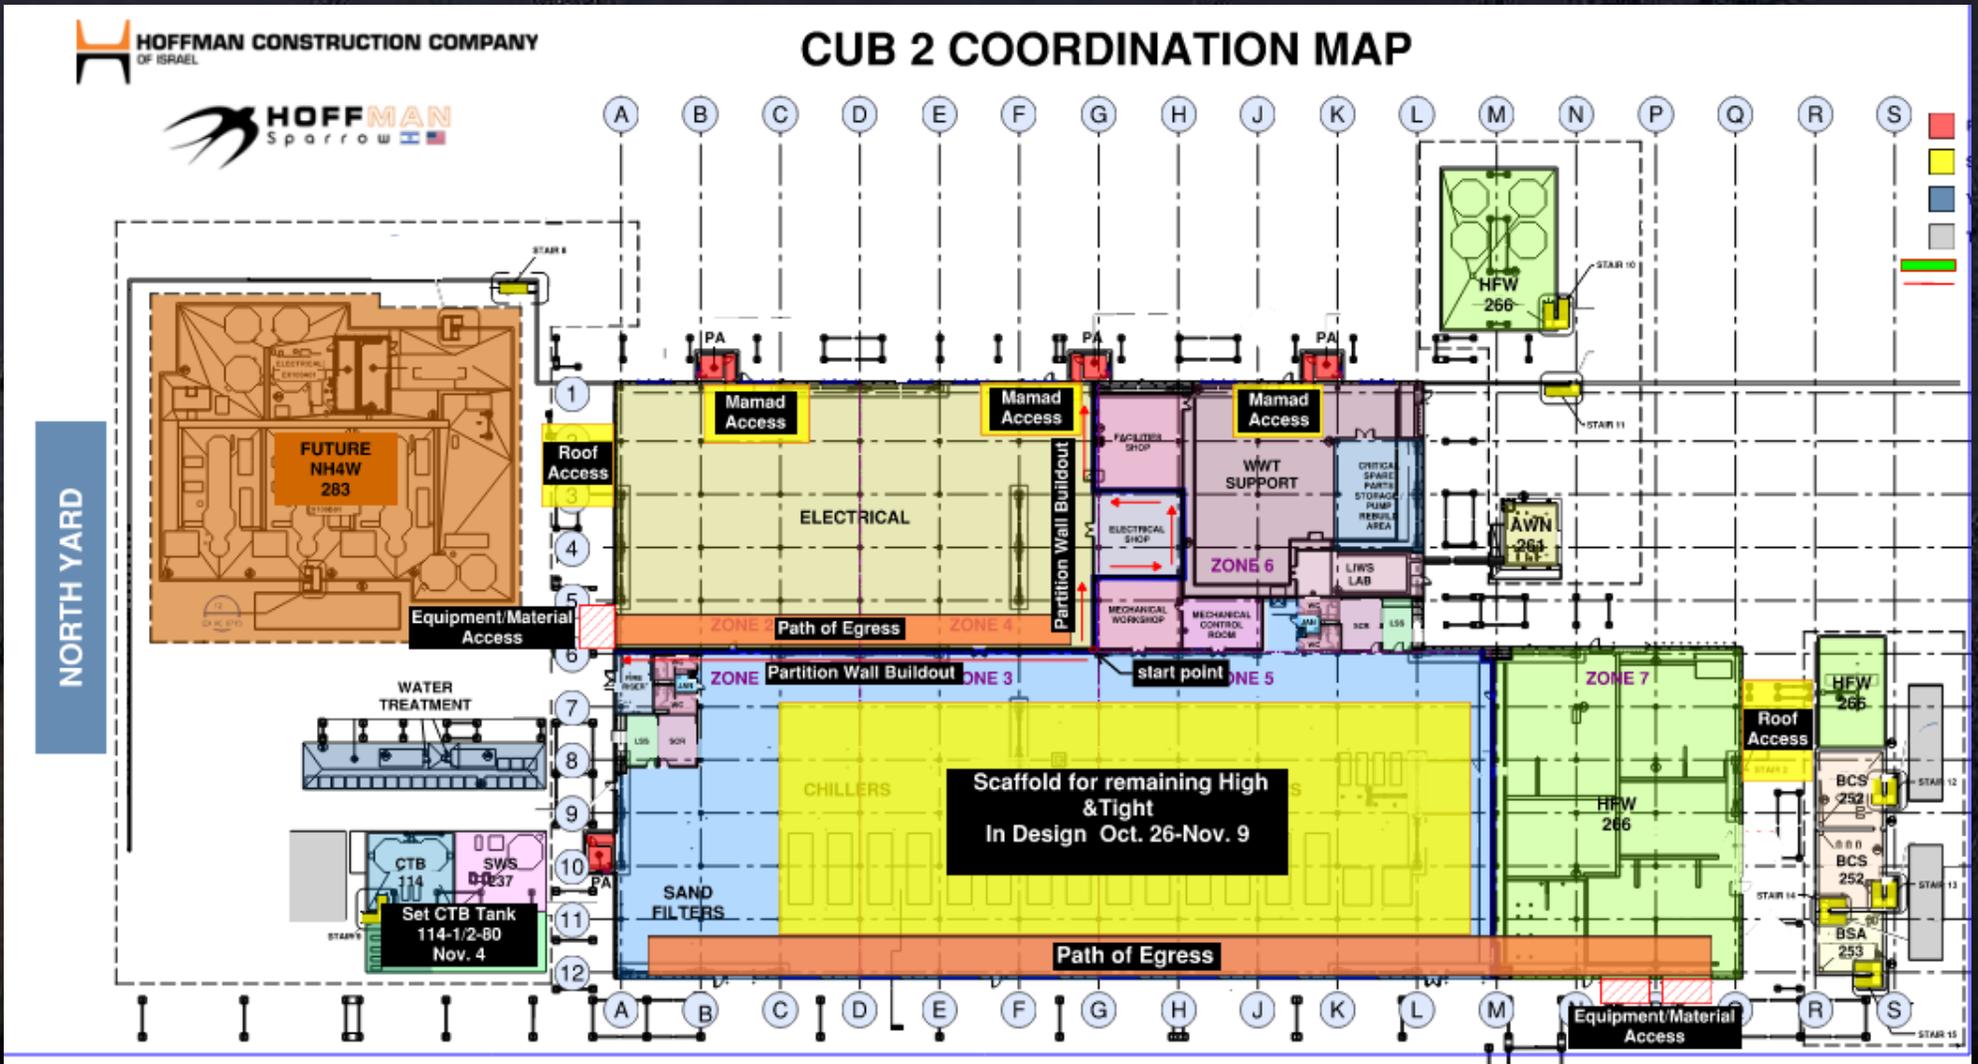

# CUB 2 – EXTERIOR/ROOF

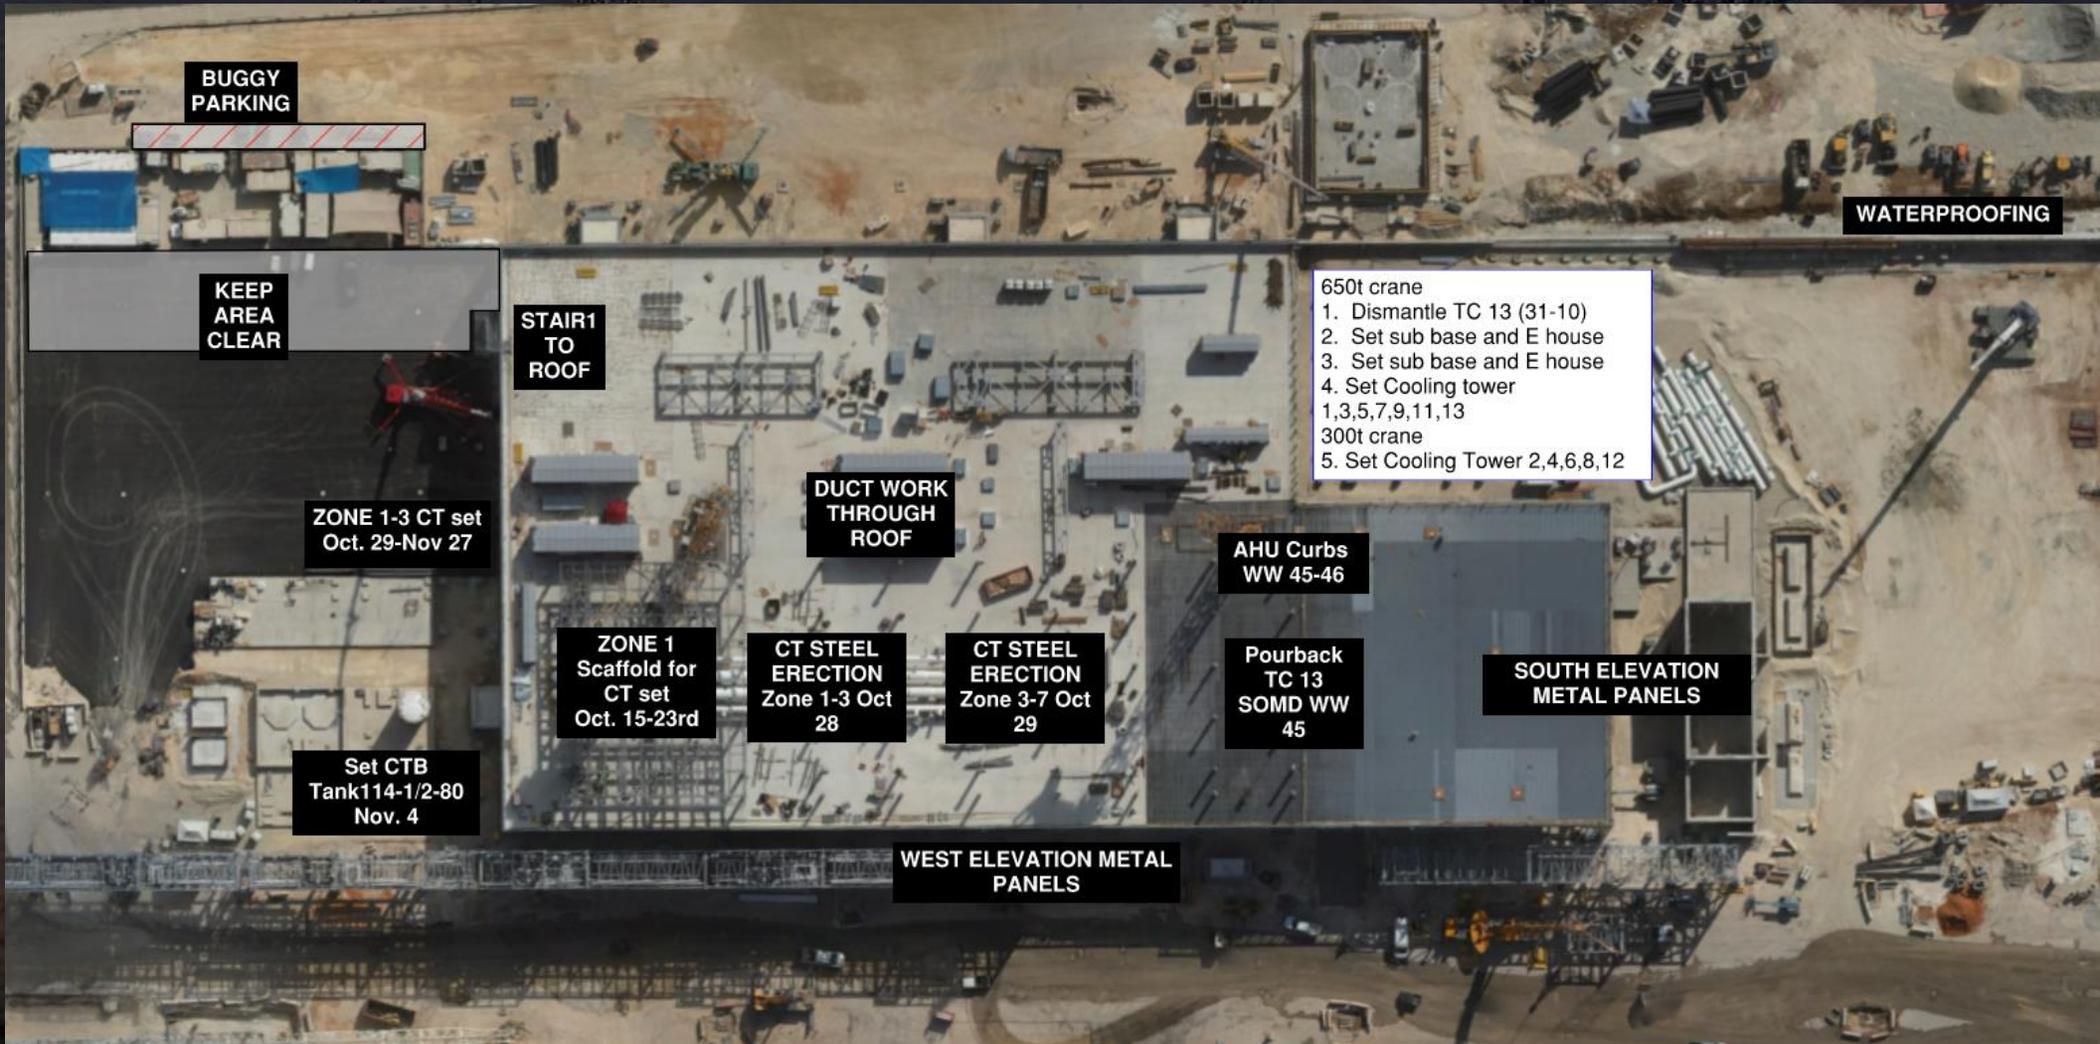

**BUGGY PARKING**

**WATERPROOFING**

**KEEP AREA CLEAR**

**STAIR1 TO ROOF**

- 650t crane
1. Dismantle TC 13 (31-10)
  2. Set sub base and E house
  3. Set sub base and E house
  4. Set Cooling tower 1,3,5,7,9,11,13
- 300t crane
5. Set Cooling Tower 2,4,6,8,12

**ZONE 1-3 CT set**  
Oct. 29-Nov 27

**DUCT WORK THROUGH ROOF**

**AHU Curbs**  
WW 45-46

**ZONE 1 Scaffold for CT set**  
Oct. 15-23rd

**CT STEEL ERECTION**  
Zone 1-3 Oct 28

**CT STEEL ERECTION**  
Zone 3-7 Oct 29


**Pourback TC 13**  
SOMD WW 45


**SOUTH ELEVATION METAL PANELS**

**Set CTB Tank114-1/2-80**  
Nov. 4

**WEST ELEVATION METAL PANELS**

# CUB 2 – Crane Logistics

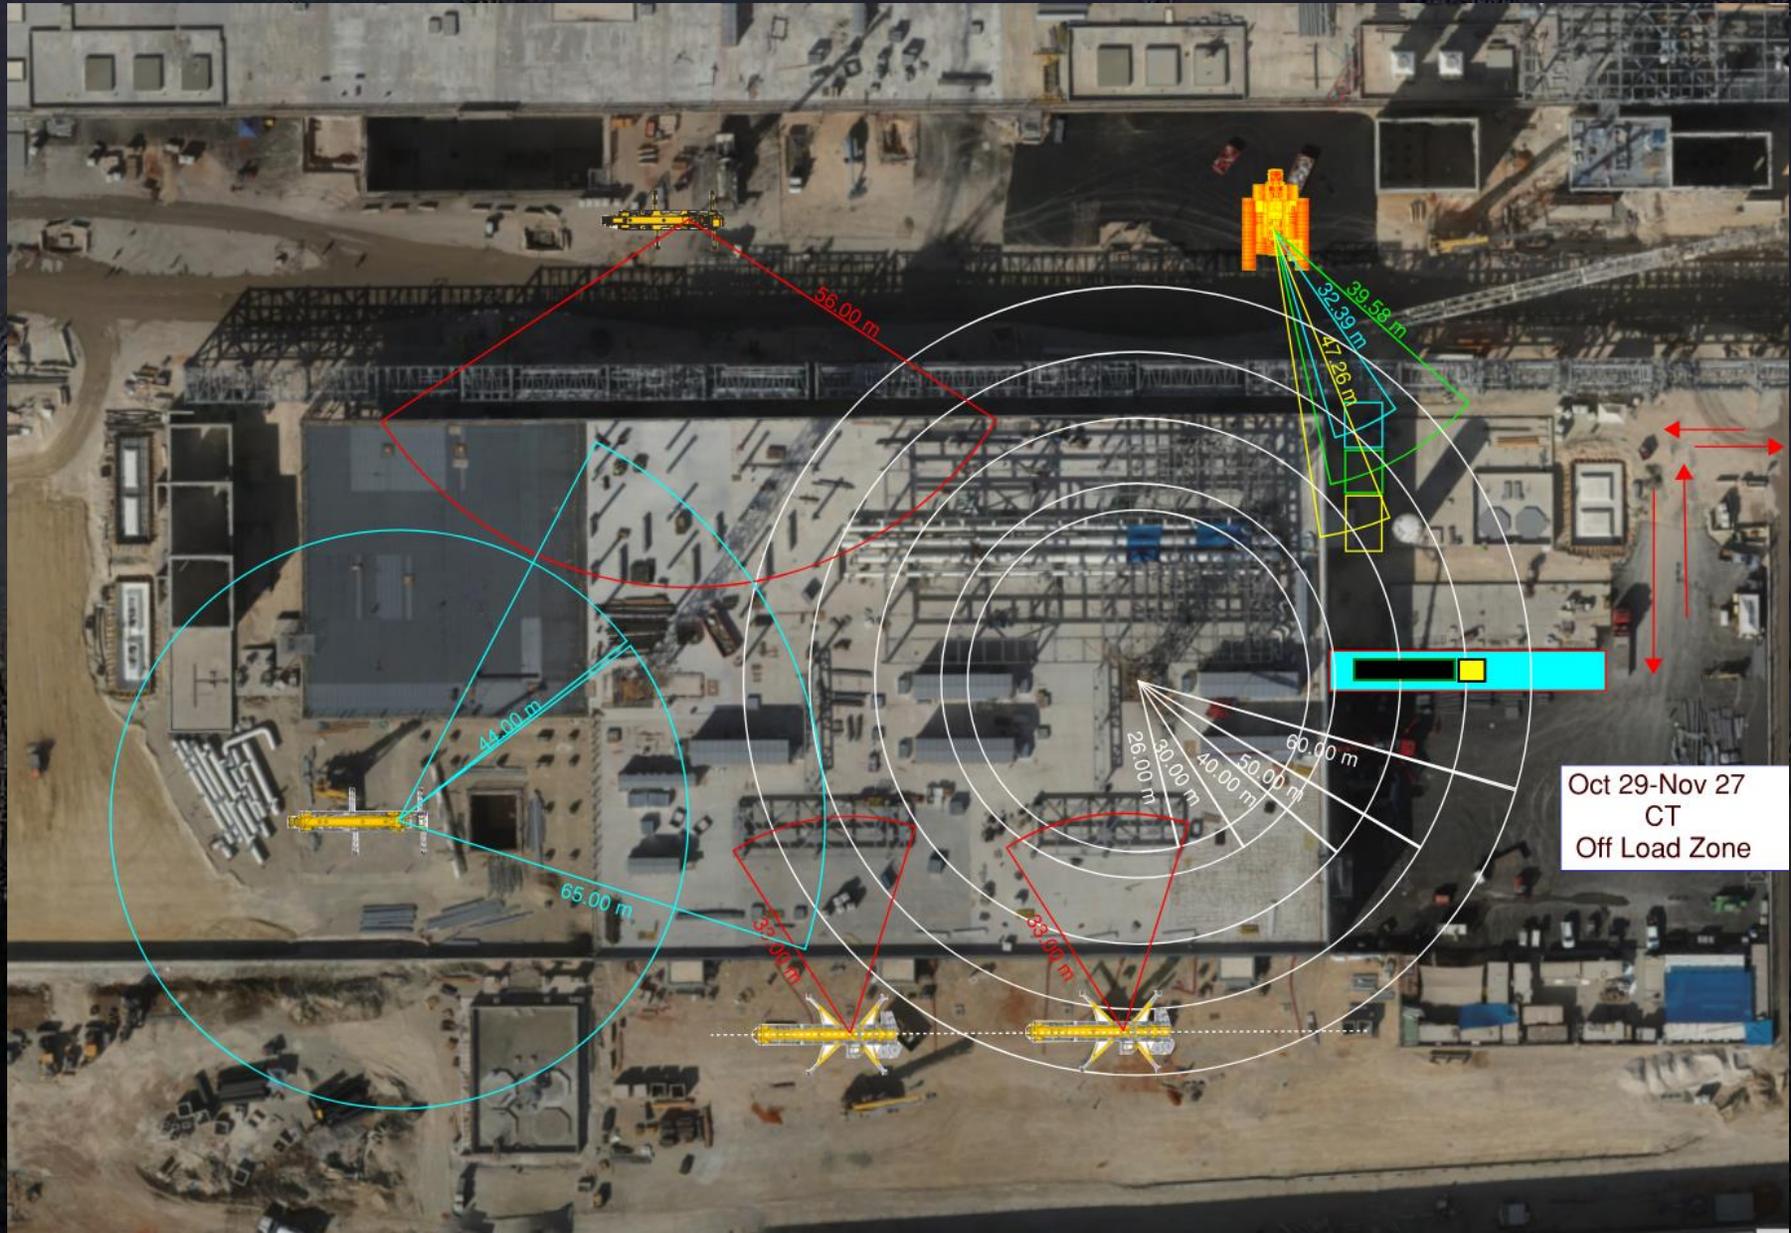


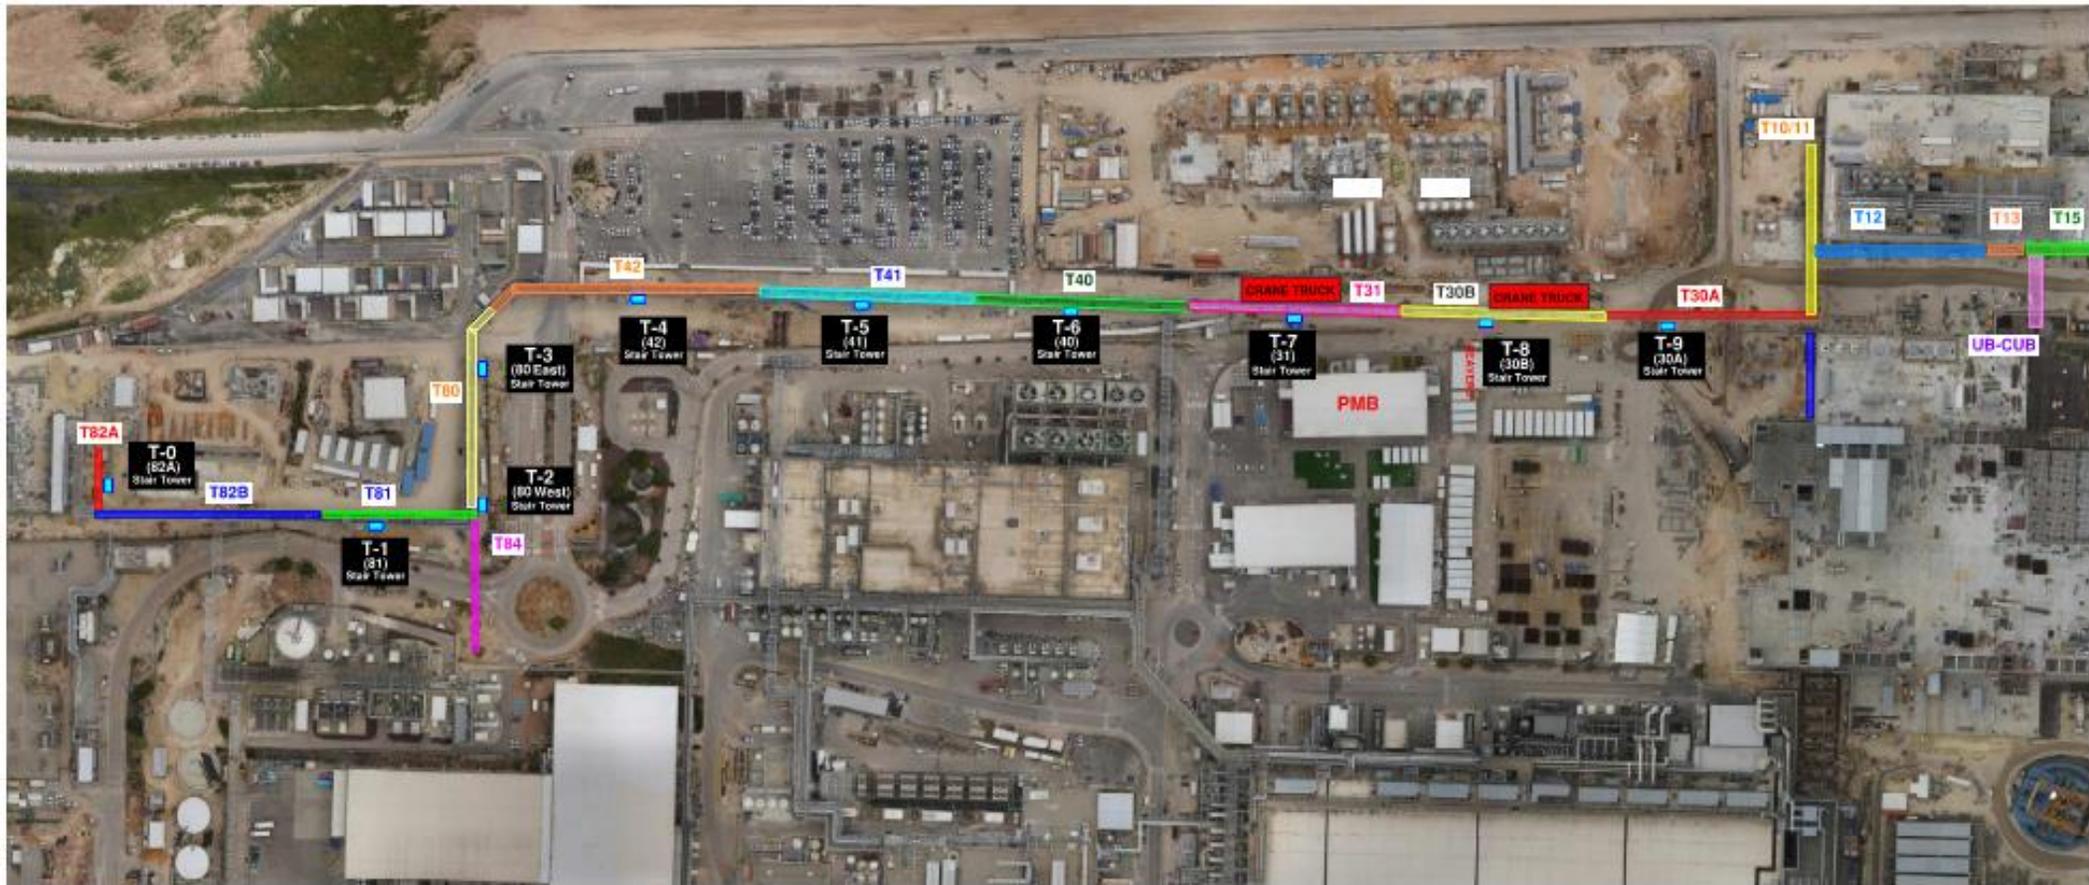

# Daily Coordination Meeting

Site Logistics


North

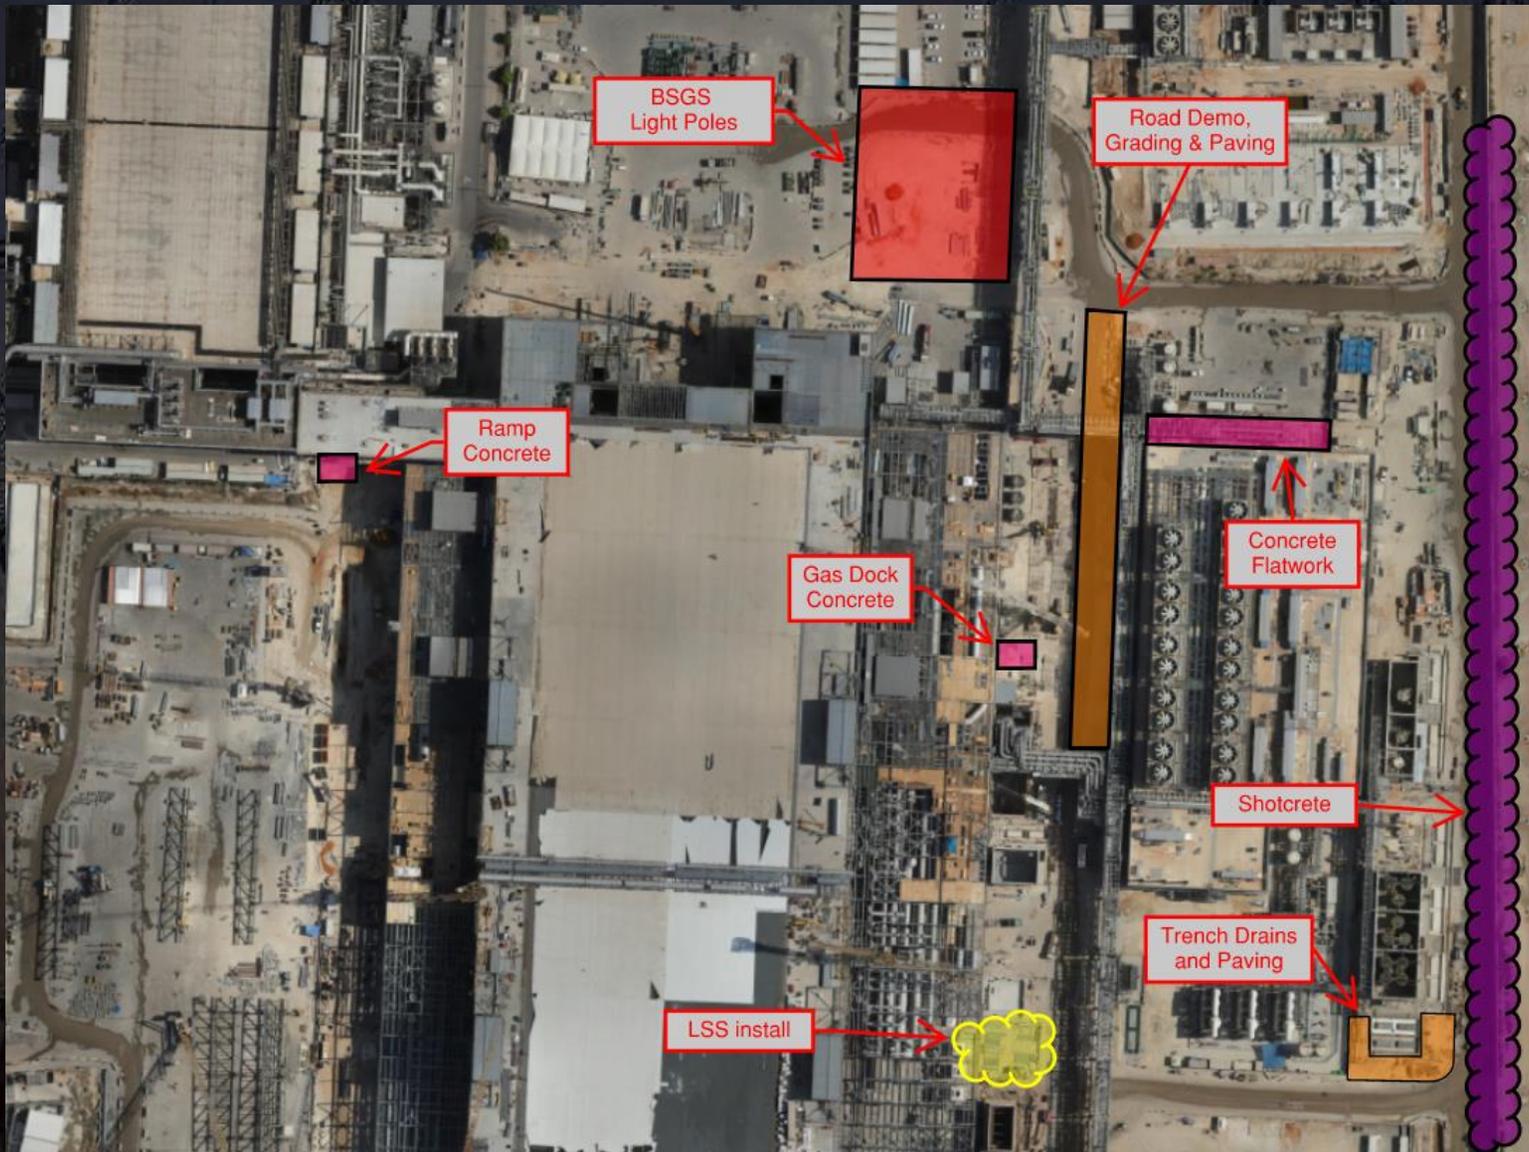

# Daily Coordination Meeting

## Site Logistics

### South

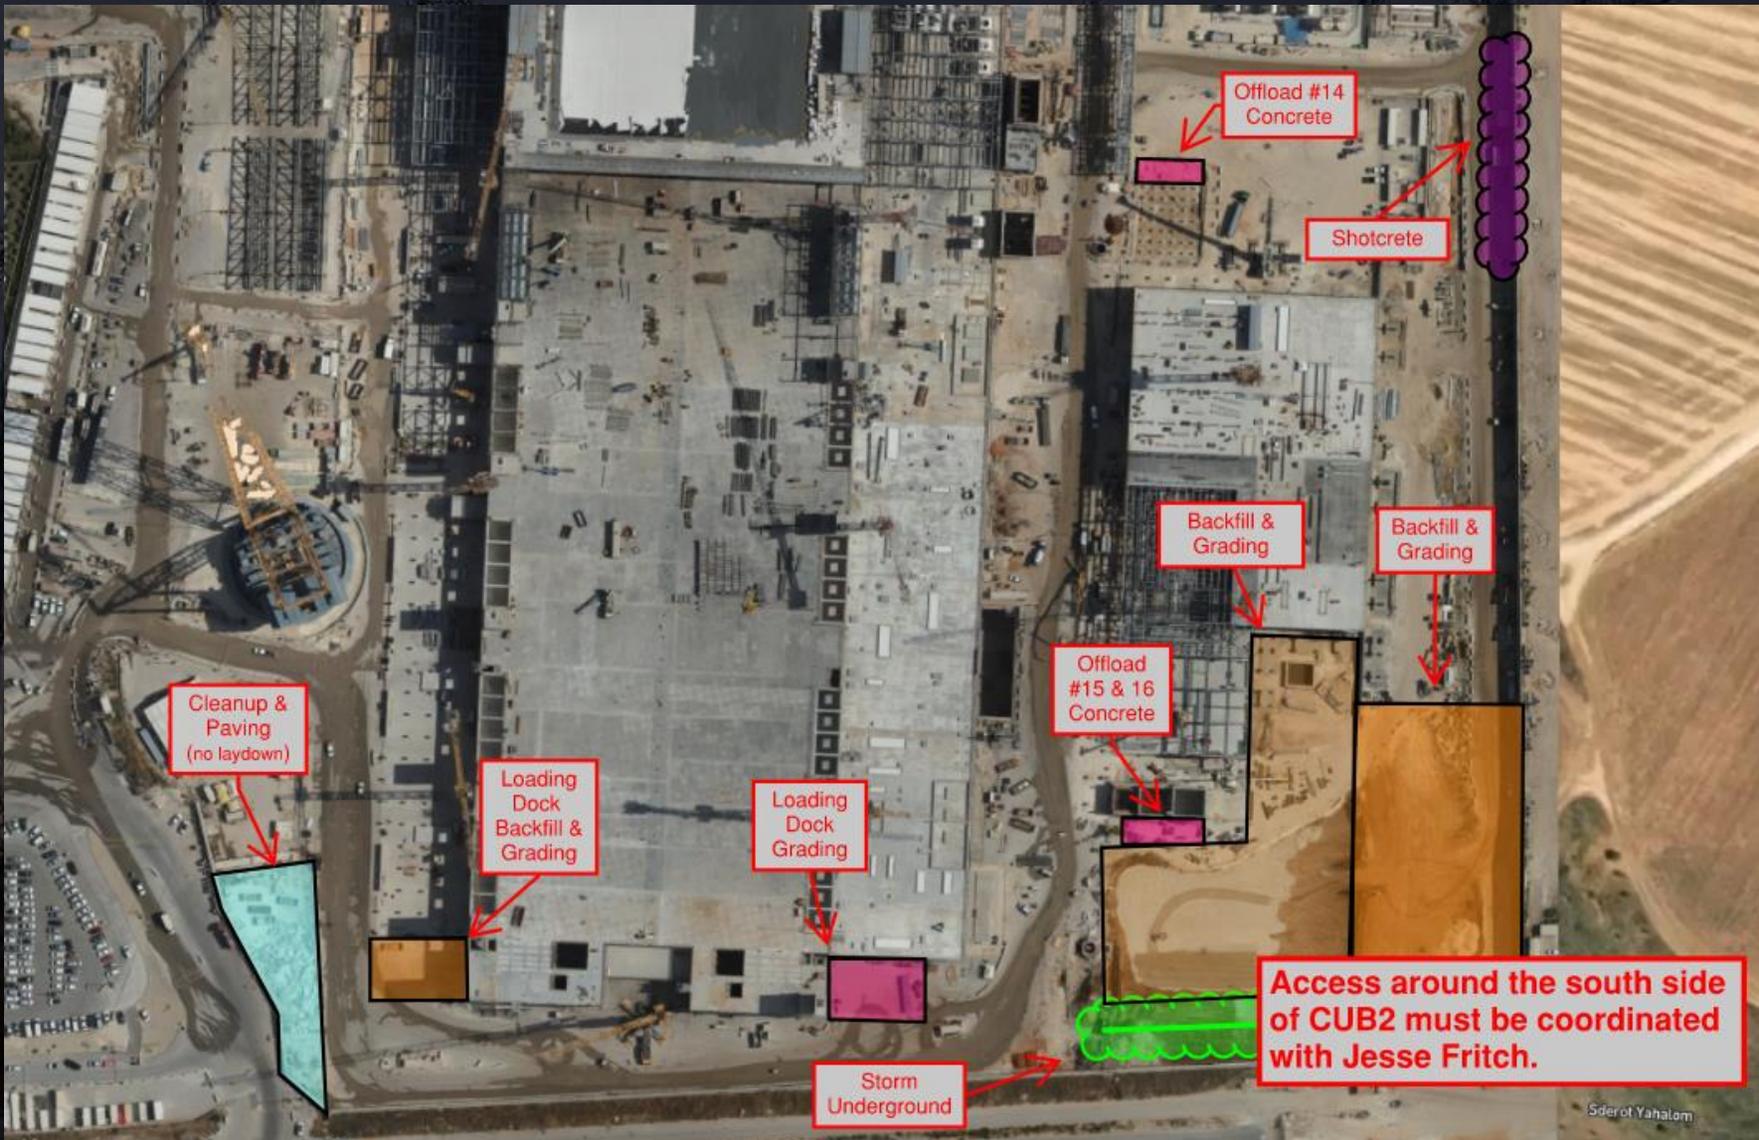

## Plan your work, Work your plan

- This phrase emphasizes the importance of thorough planning and disciplined execution in achieving successful outcomes.
- Plans are not just for HCC to review, but for your crews to understand and follow.
- If there's a change in circumstances—whether due to unexpected risks, resource availability, or scope alterations—pause work immediately.
- Once adjustments are made, recommit to the revised plan.
- Everyone should understand their roles and responsibilities moving forward.

# Daily Coordination Meeting



14:00 Sign In
