

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Drugs/Alcohol – Zero Tolerance



RES-13 Roof
pour 10 PM

Truck off load #15
6:00 am

Truck off load #15
6:00 am

RES-13 Roof pour
10:00 pm

אינטל קרית גת

FAB-28


AB-18



HOFFMAN CONSTRUCTION COMPANY




UTILITY LEVEL MOD1

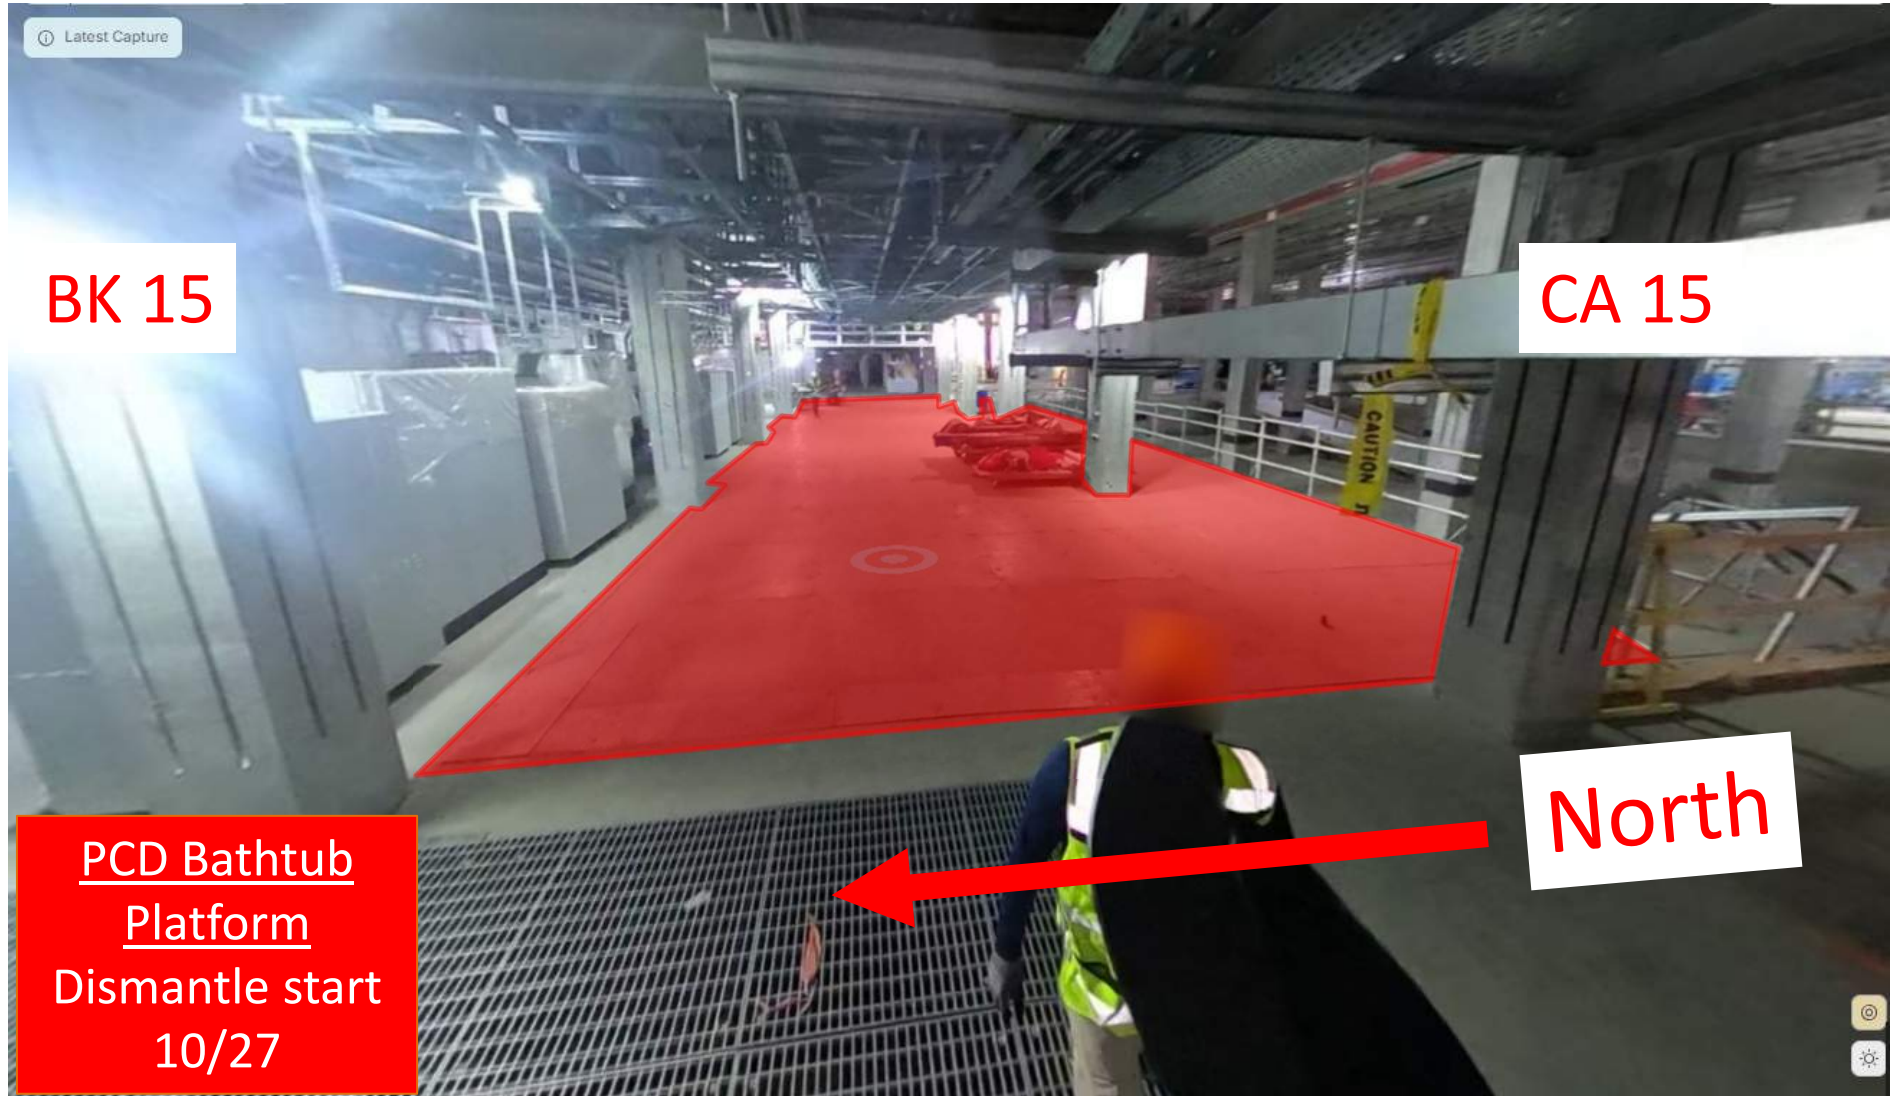



UTILITY LEVEL MOD1

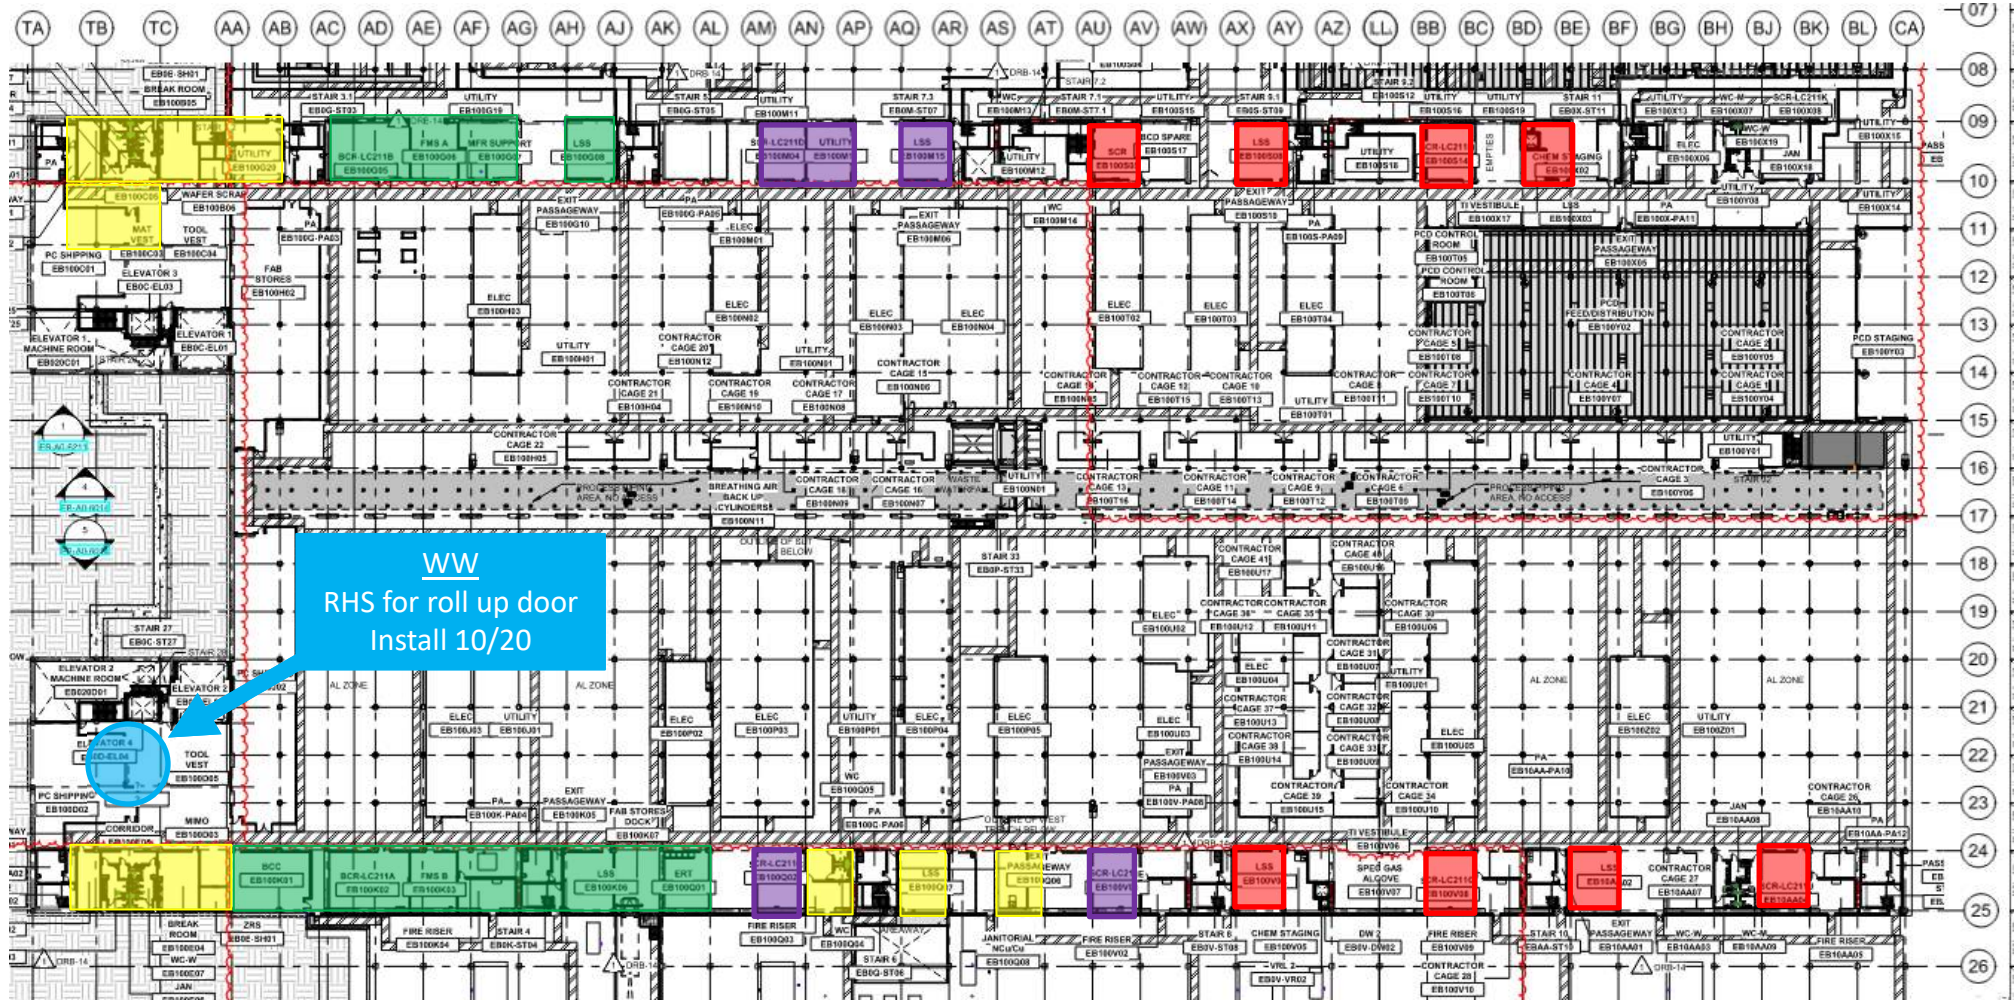

Pre-mold Rem dismantle
Should be uninstll


BELFOR
Mold remediation

ELRAM
Drywall install

MEP+Elctrical
Ready for re-install




UTILITY LEVEL MOD2

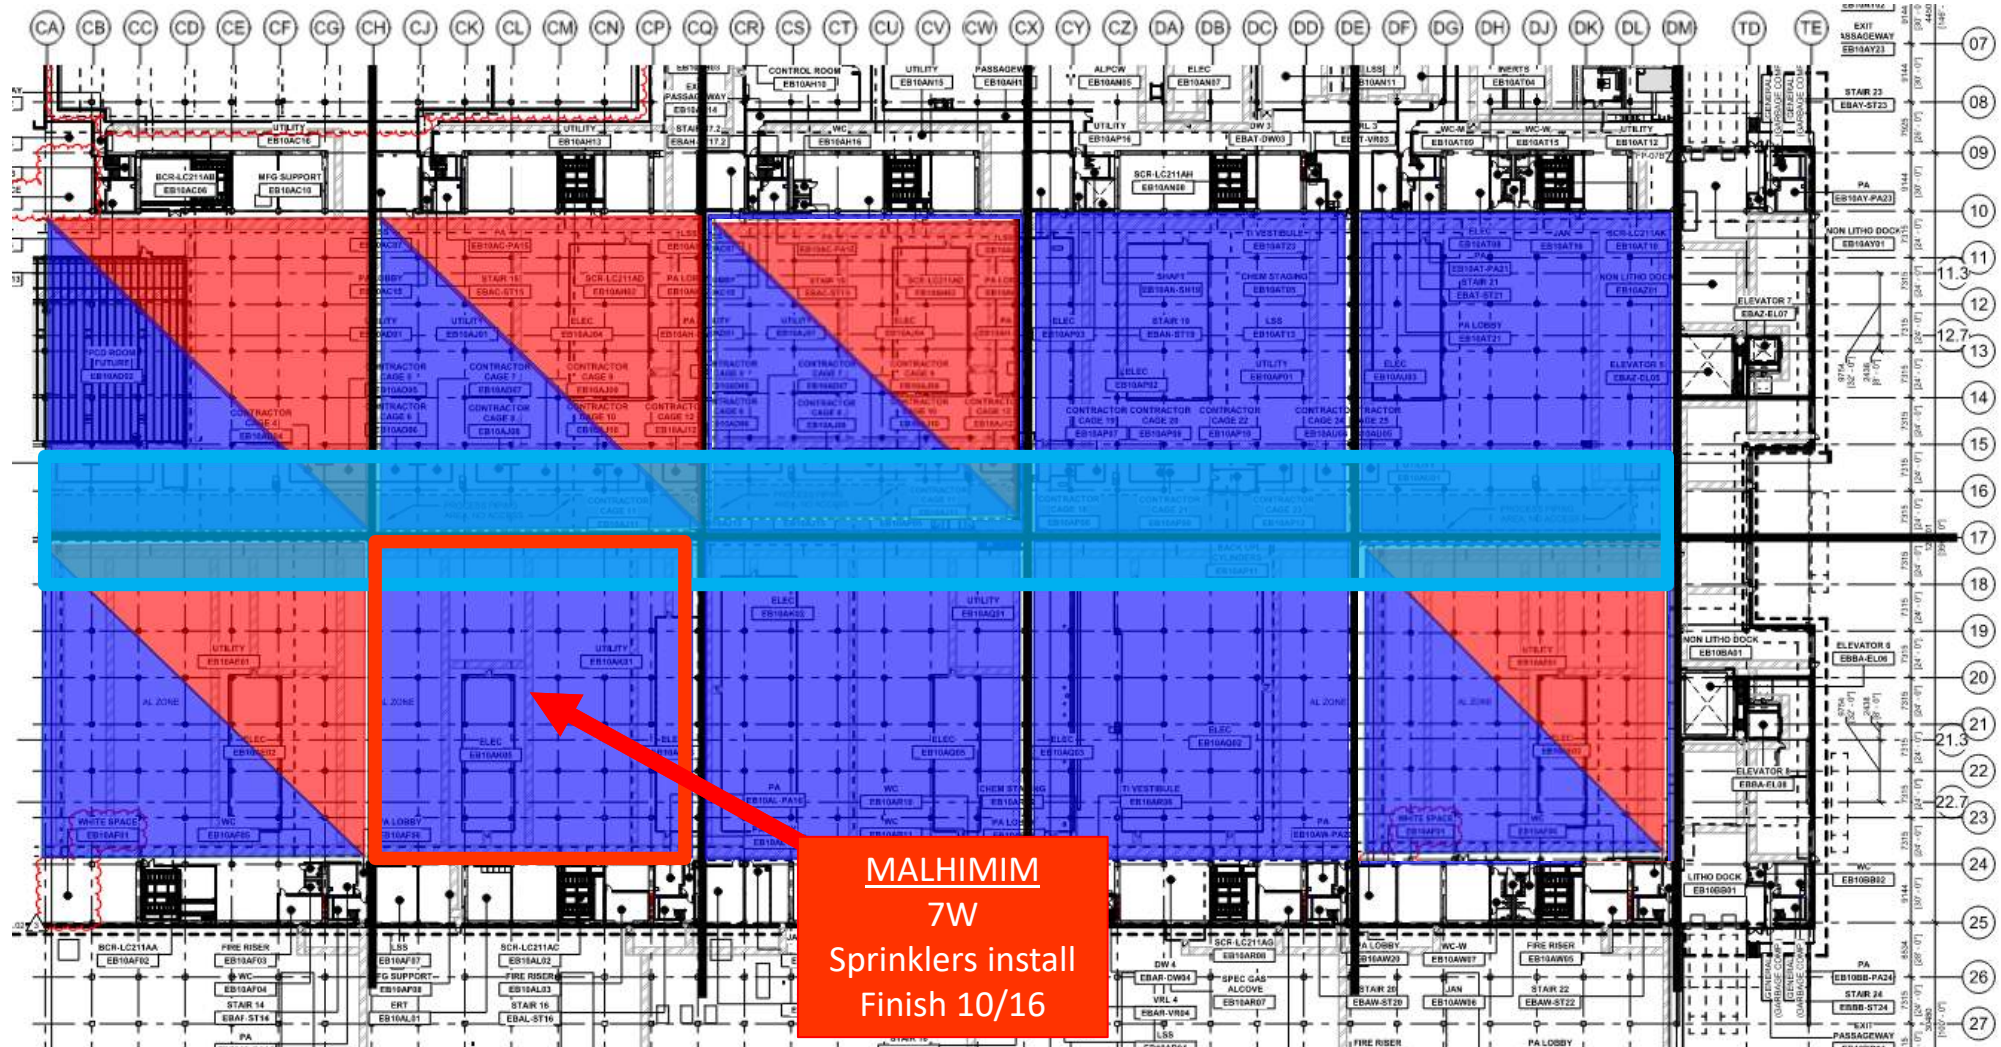




SUT 38.1 LEVEL

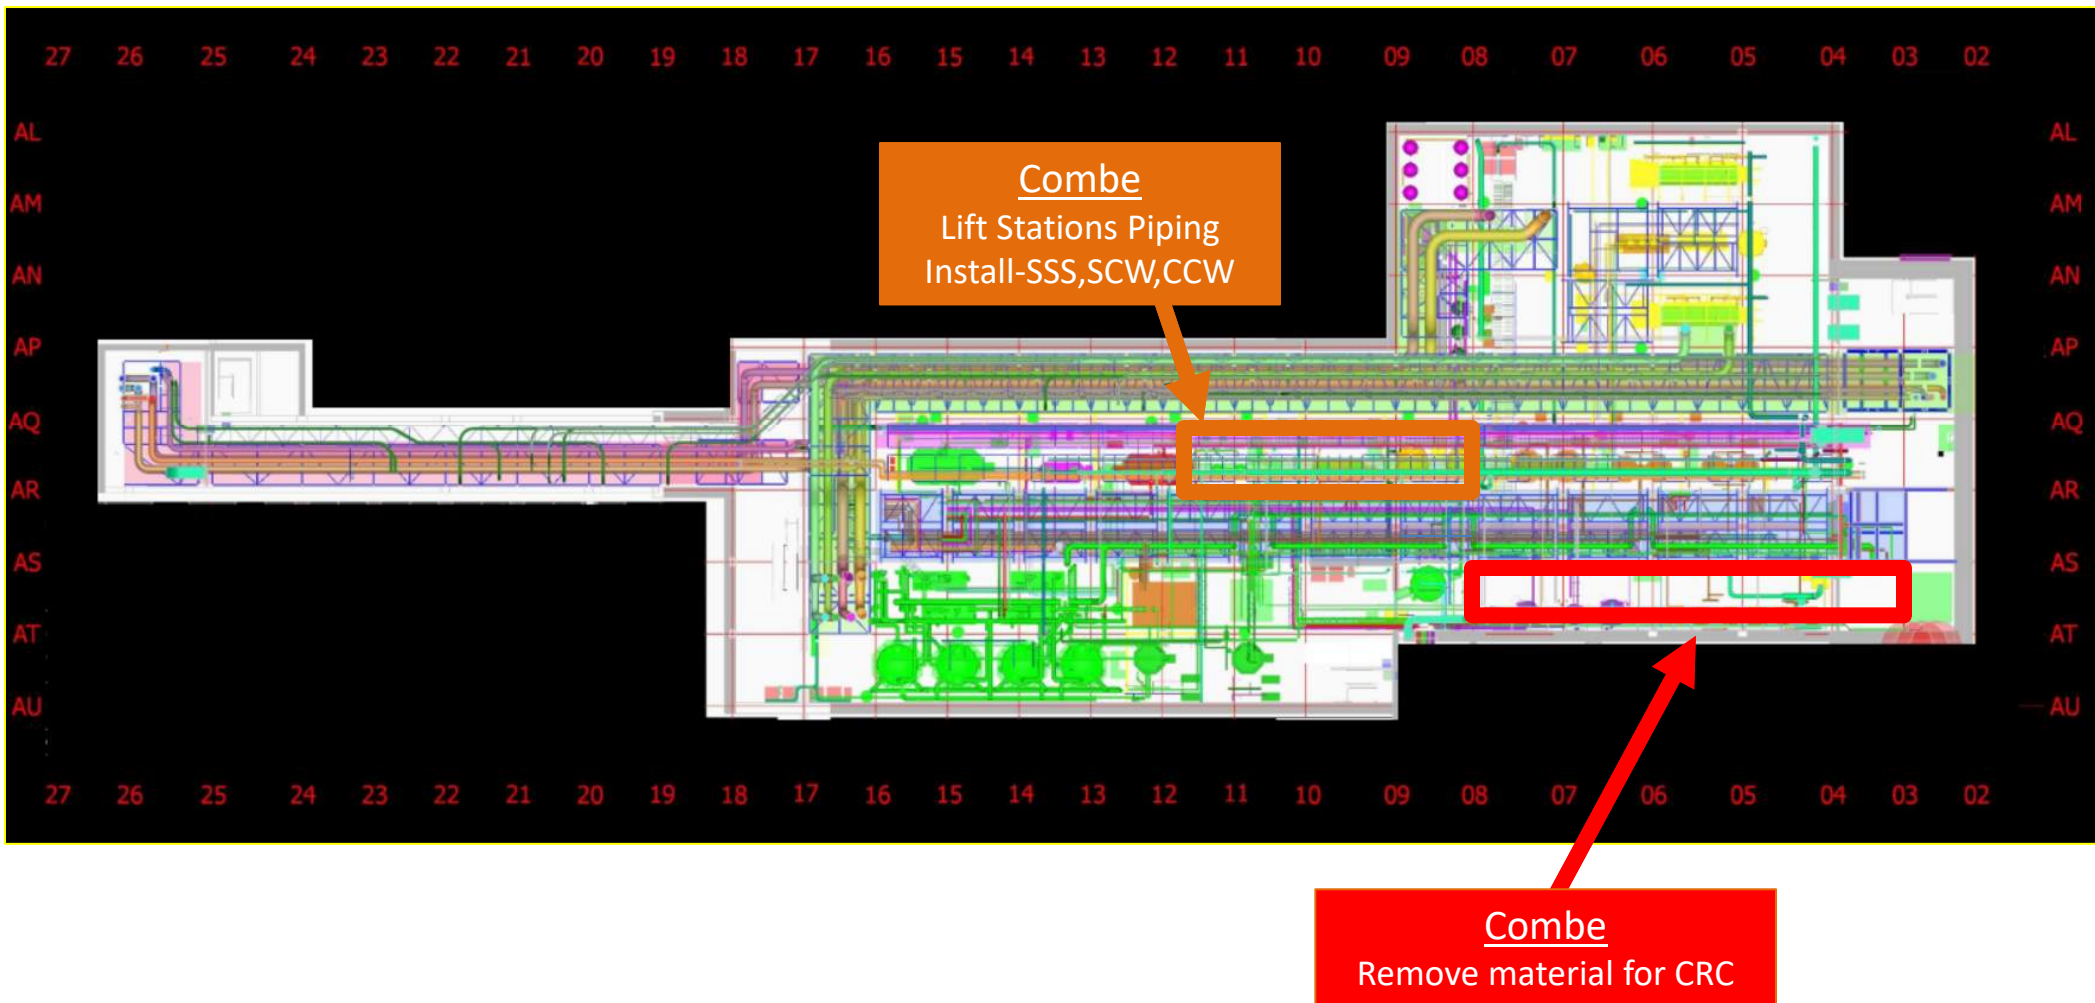

SUT 38.2 LEVEL

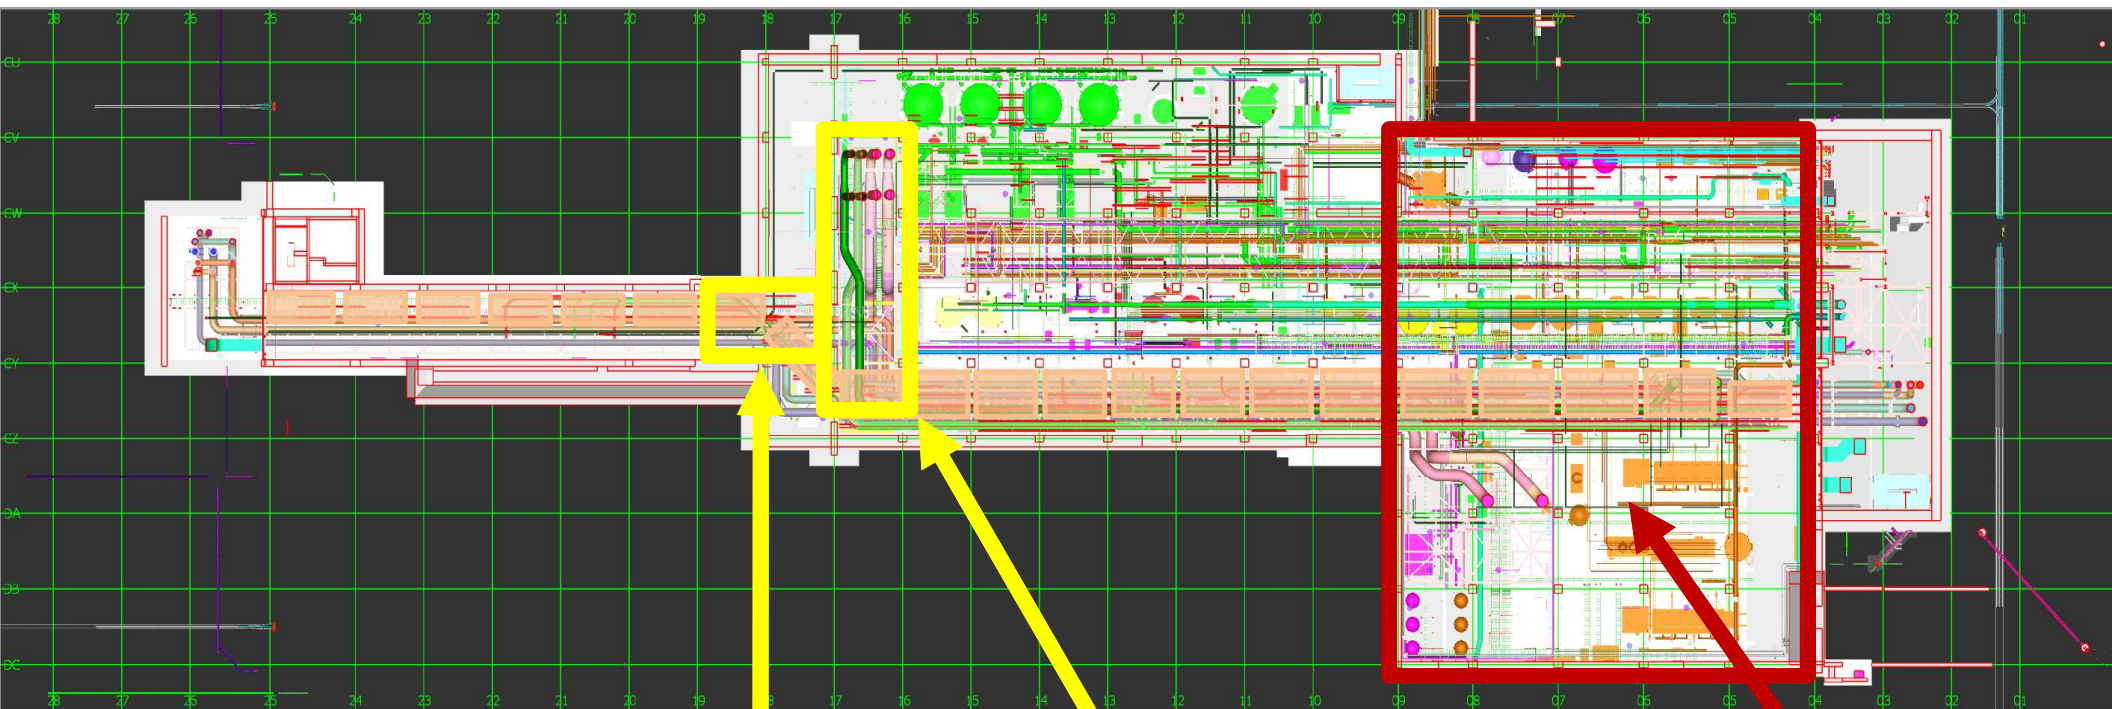


CRW
H&T
NEED PIPING


17-18 line
Bore Loading

16-17 line
lvl2+3
bed lift: Need a
Date

Vesda
H&T
Ongoing

SUBFAB BUILDOUT MOD 1

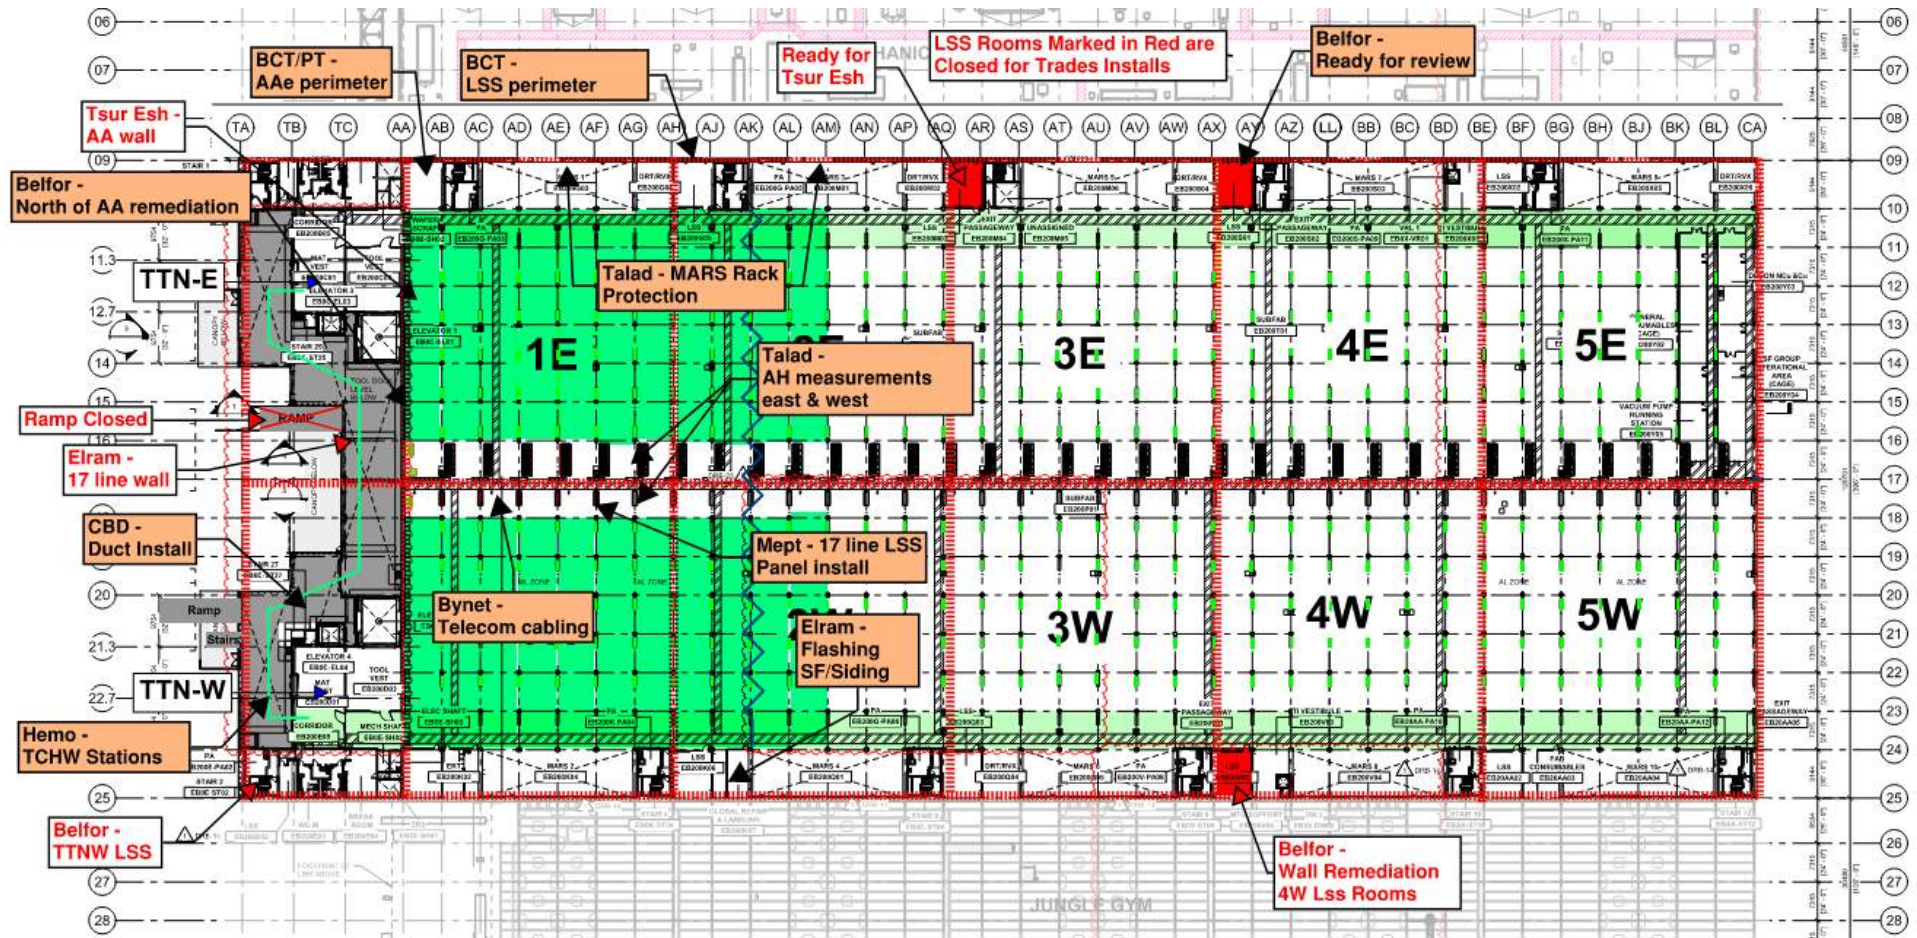

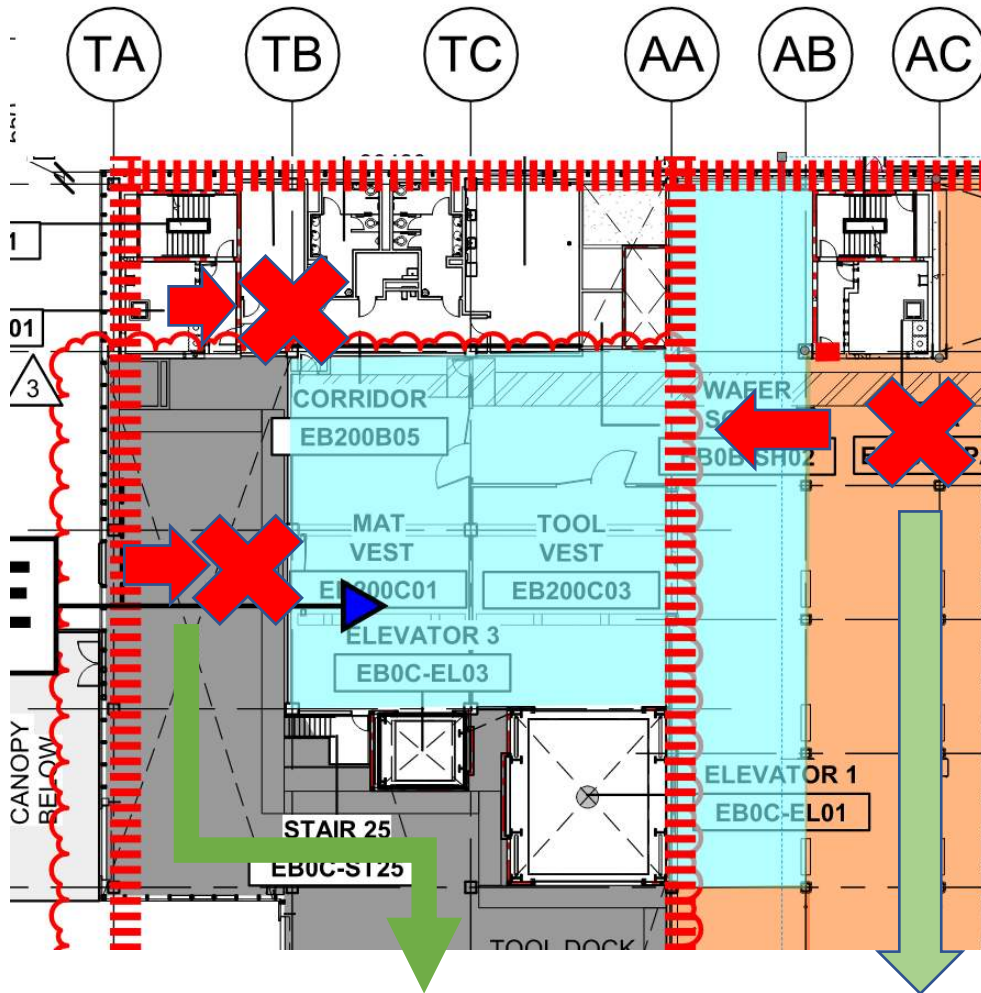


Sunday OCT 20th


CRC AAe & TTNE Upper Dock.

- Temp stairs – Access blocked.
- Stairs1 – Access blocked, SF level only.


SUBFAB CRC TOPCOAT

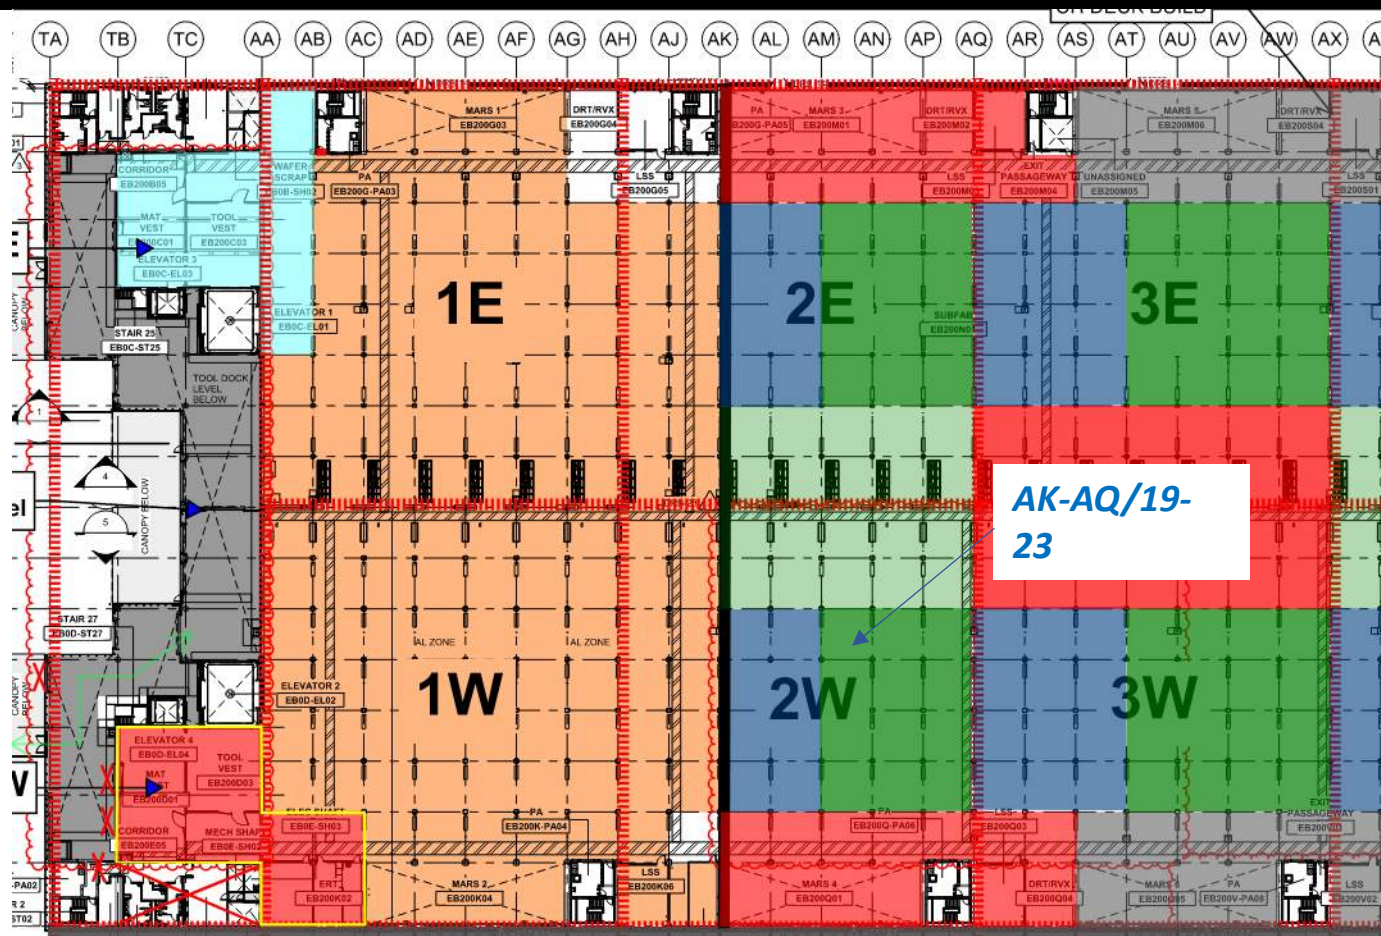

BCT Pressure Test Exclusion Zone

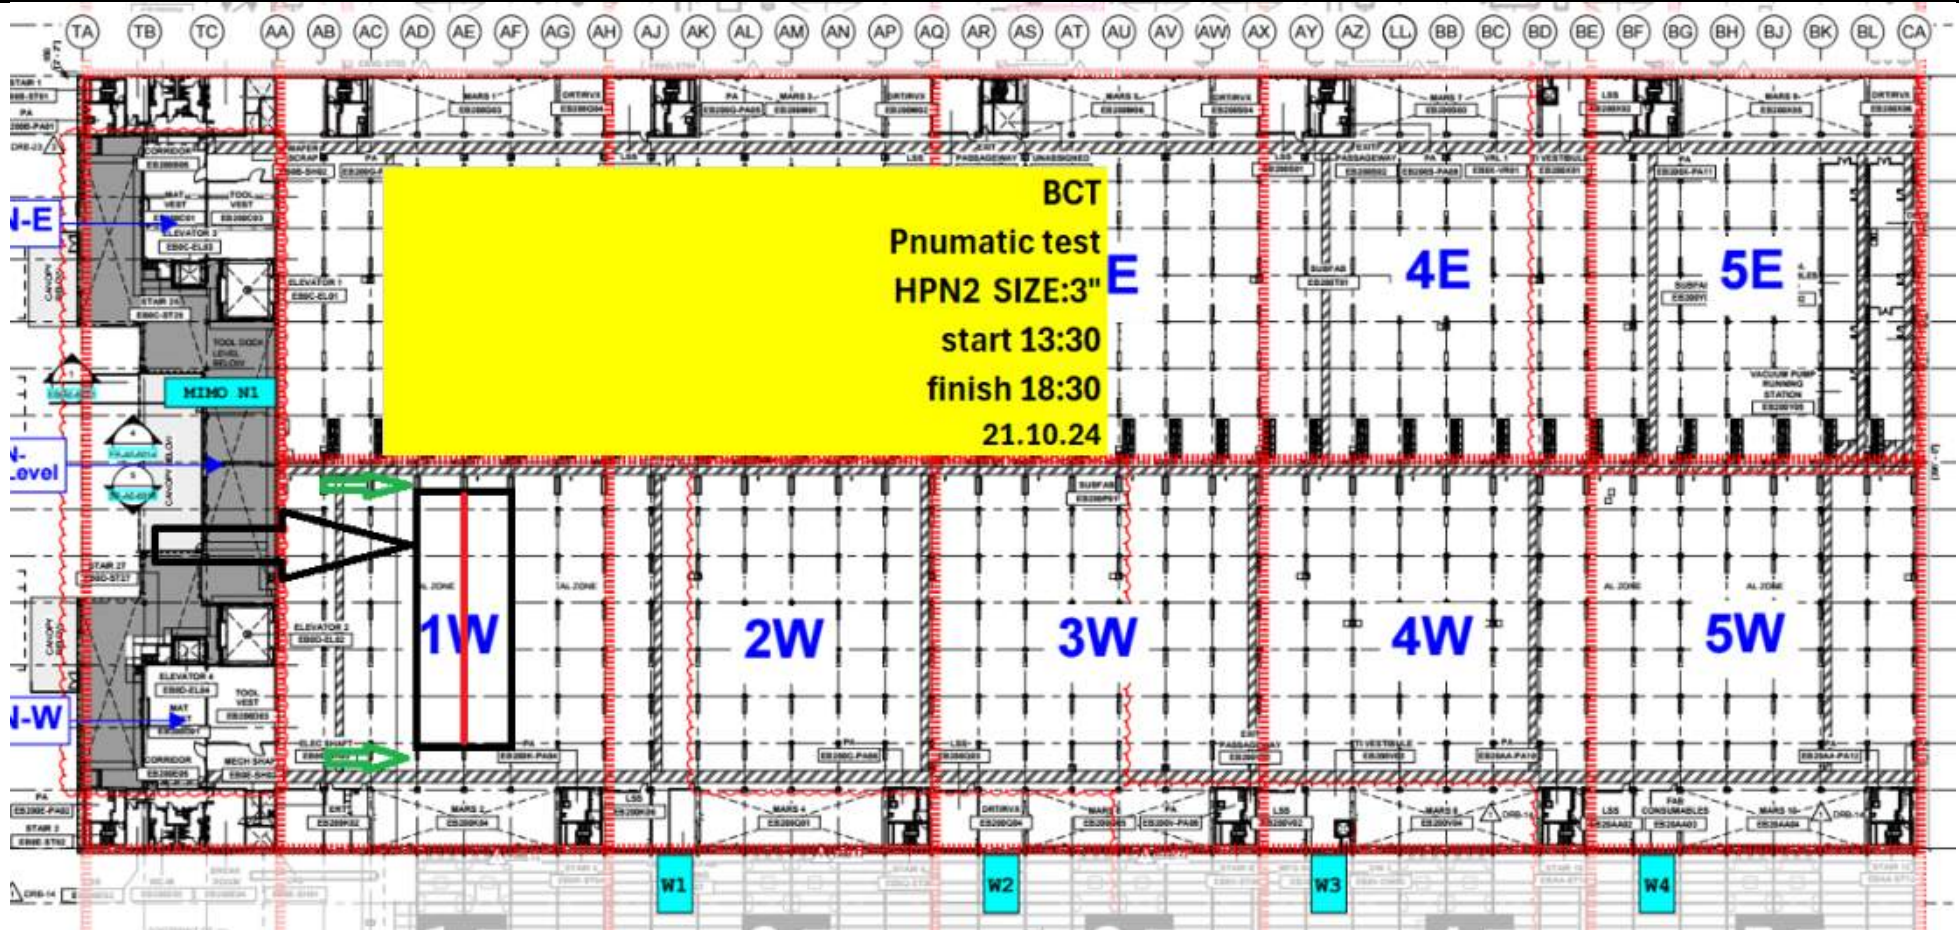

SUBFAB BUILDOUT MOD 2

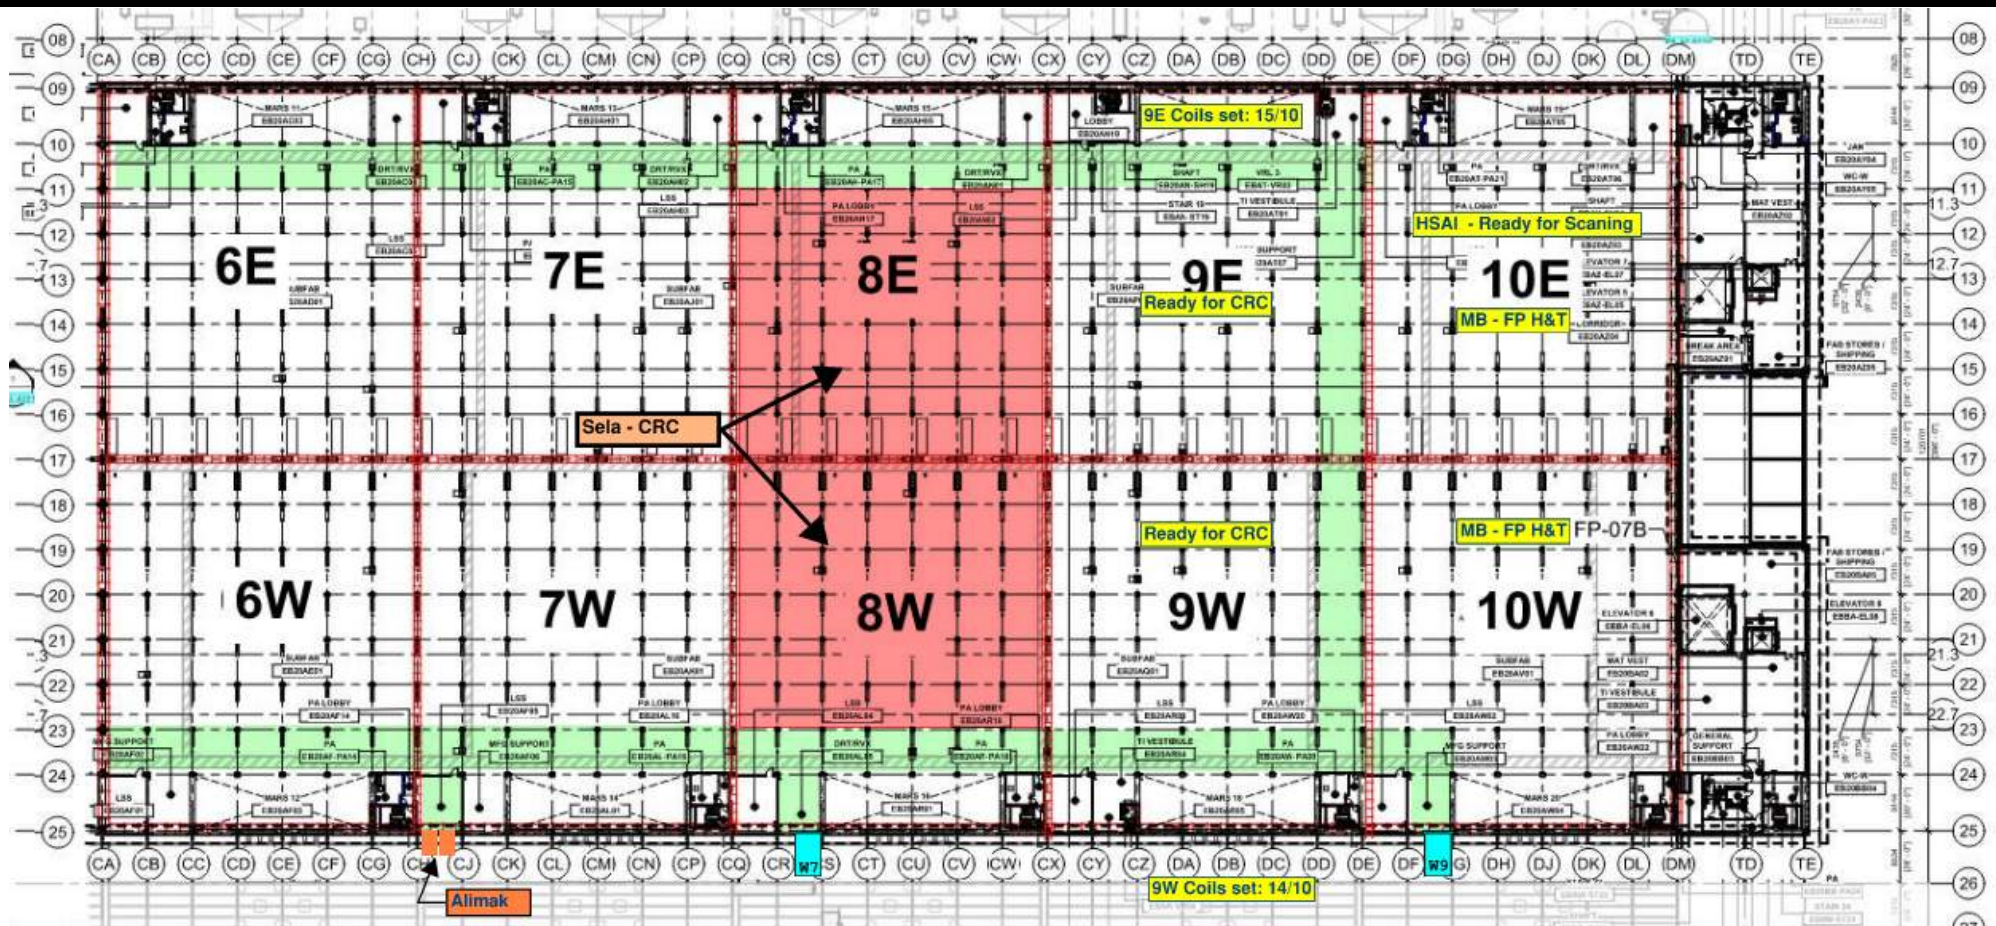

Tavas + Talent solution
P1 cleaning 1E

D&P blades
install

Elram- AA line
columns+G1 wall
mock-up
Chemo- Hangers
install
SN - Beams layout

SELA-crc spraying 17 aa-ak

CRC AA-AK/17-23

Sela: CRC Done

Talad- Cutting around lids

TALAD CRC
PREP

2

3

L
I
N
K

Link

Path-Taas - exhaust duct install and tie in
SIG- Mobile scaffold install
Afcon- Rack install
Newcotech- temp wall
Afcon - cable tray & racks install

CR level:

Afcon - Cable trays, modules and stickers, 2E, 2W, 3E, 3W, 4E
MB- 1W drops, 2E- 2W pipes and drops
Elram - 9-10, 24-25 columns/shaft walls, AA line column wraps
VW/JS - 17-18 line added beams+ AS south stocker beams
Meptagon - I&C 2W
D&P - 5E blades install.
Tavaresh - 5E blades, 1W-1E shaft walls
HYG- 5W Litho crane steel
T - Duct prep for test AA-AH east
Talad- 1W 4DA holes drilling, 1W cutting around steel, 17 line bracing
TMT - Safety net install

2E

3E

4E

5E

2W

3W

4W


5N

Talad-ongoing beam bracing across 17 line+aa/ab

Sella's next prepped
areas.



HOFFMAN CONSTRUCTION COMPANY

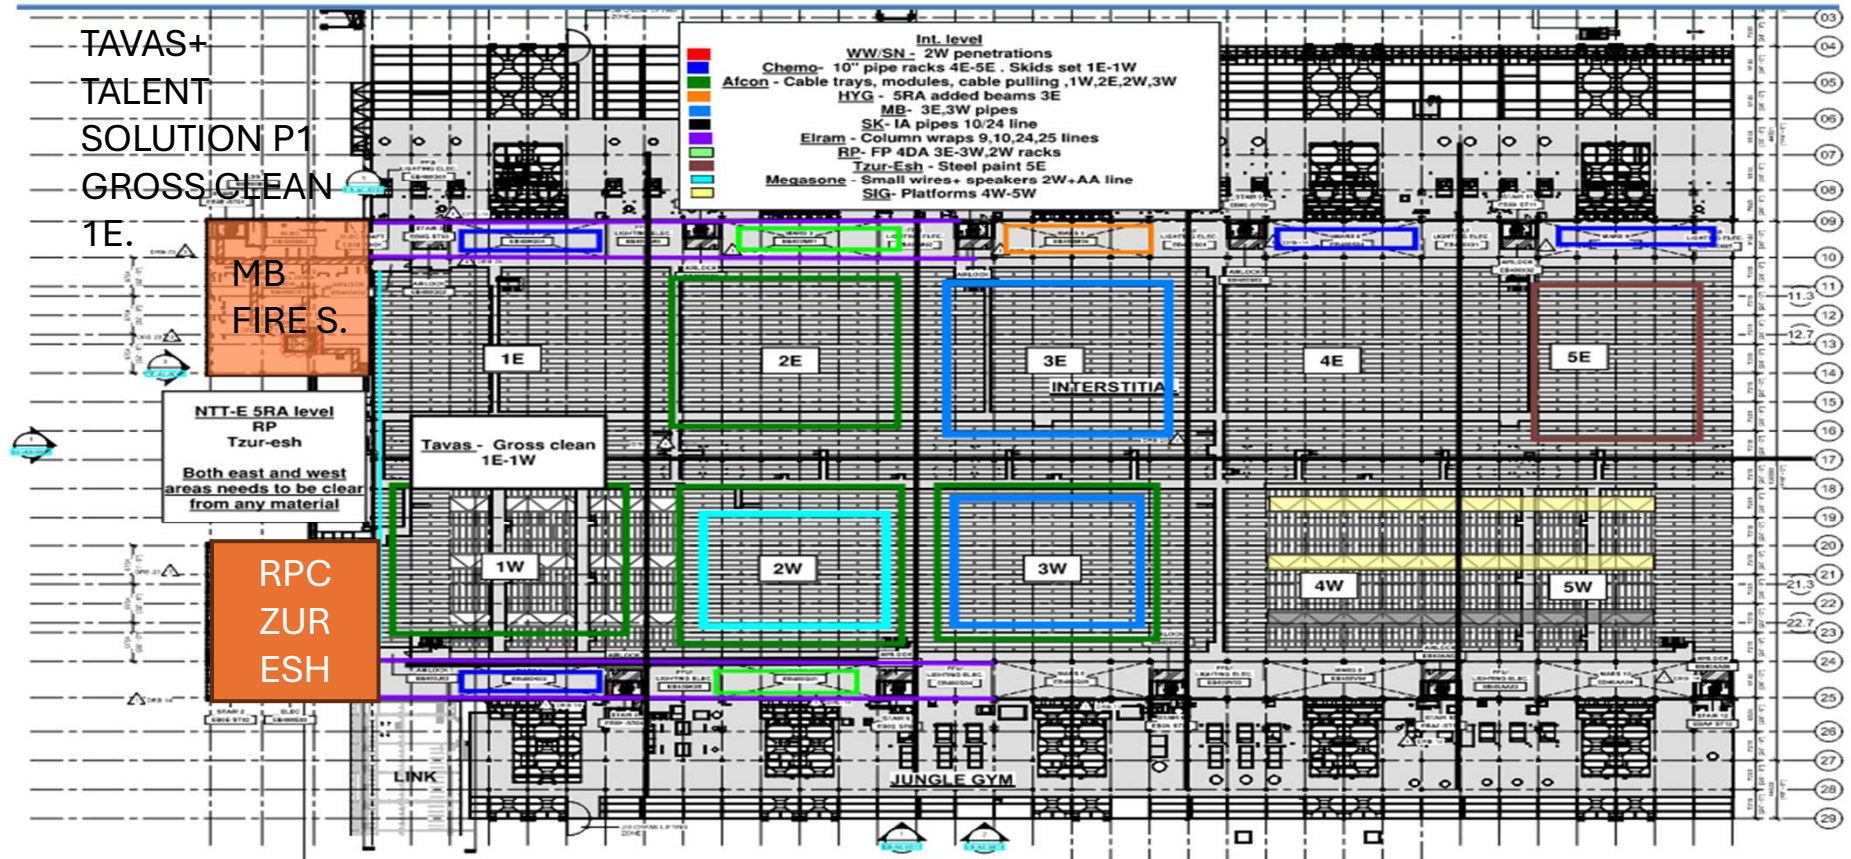



HOFFMAN CONSTRUCTION COMPANY



MOD 2 STEEL ERECTION

Truss Yard:
RP and Tzur-Esh to start FP and paint trusses on night shift

Infill ongoing

Tzur-esh
MOD2 paint

MIMO 4DA level CB-CC
SIG done

NEW DUMPSTER ON
TOP OF MIMO

TRUSS #21
EAST SIDE
TUESDAY 04:00.

SEQ 282 ongoing


07


08

ELRAM

21.10.2024

ELRAM

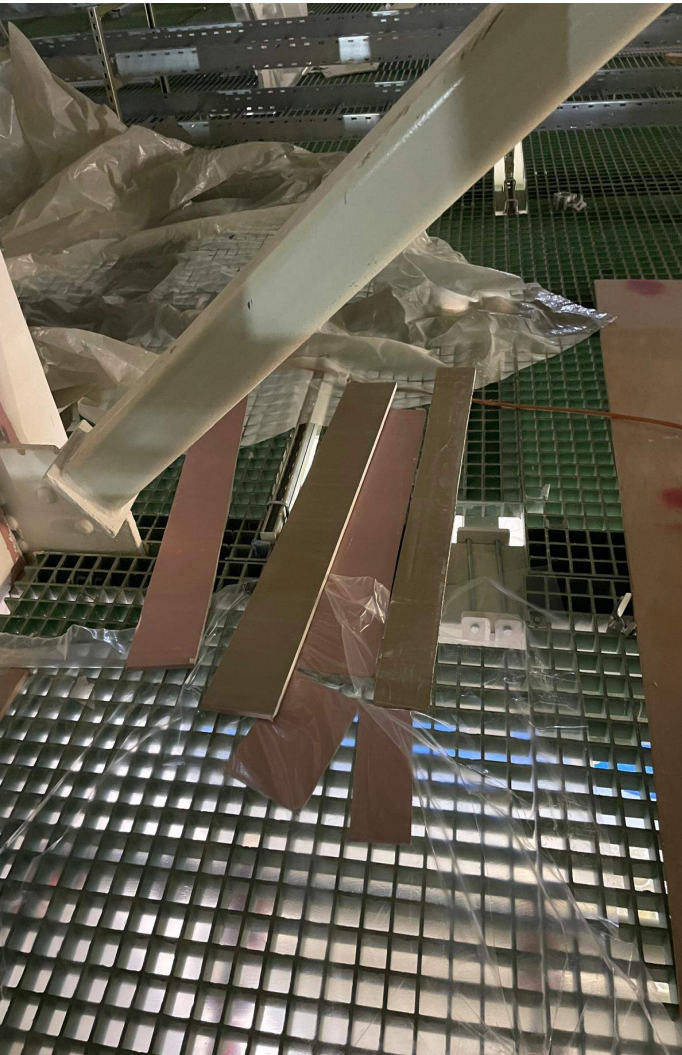

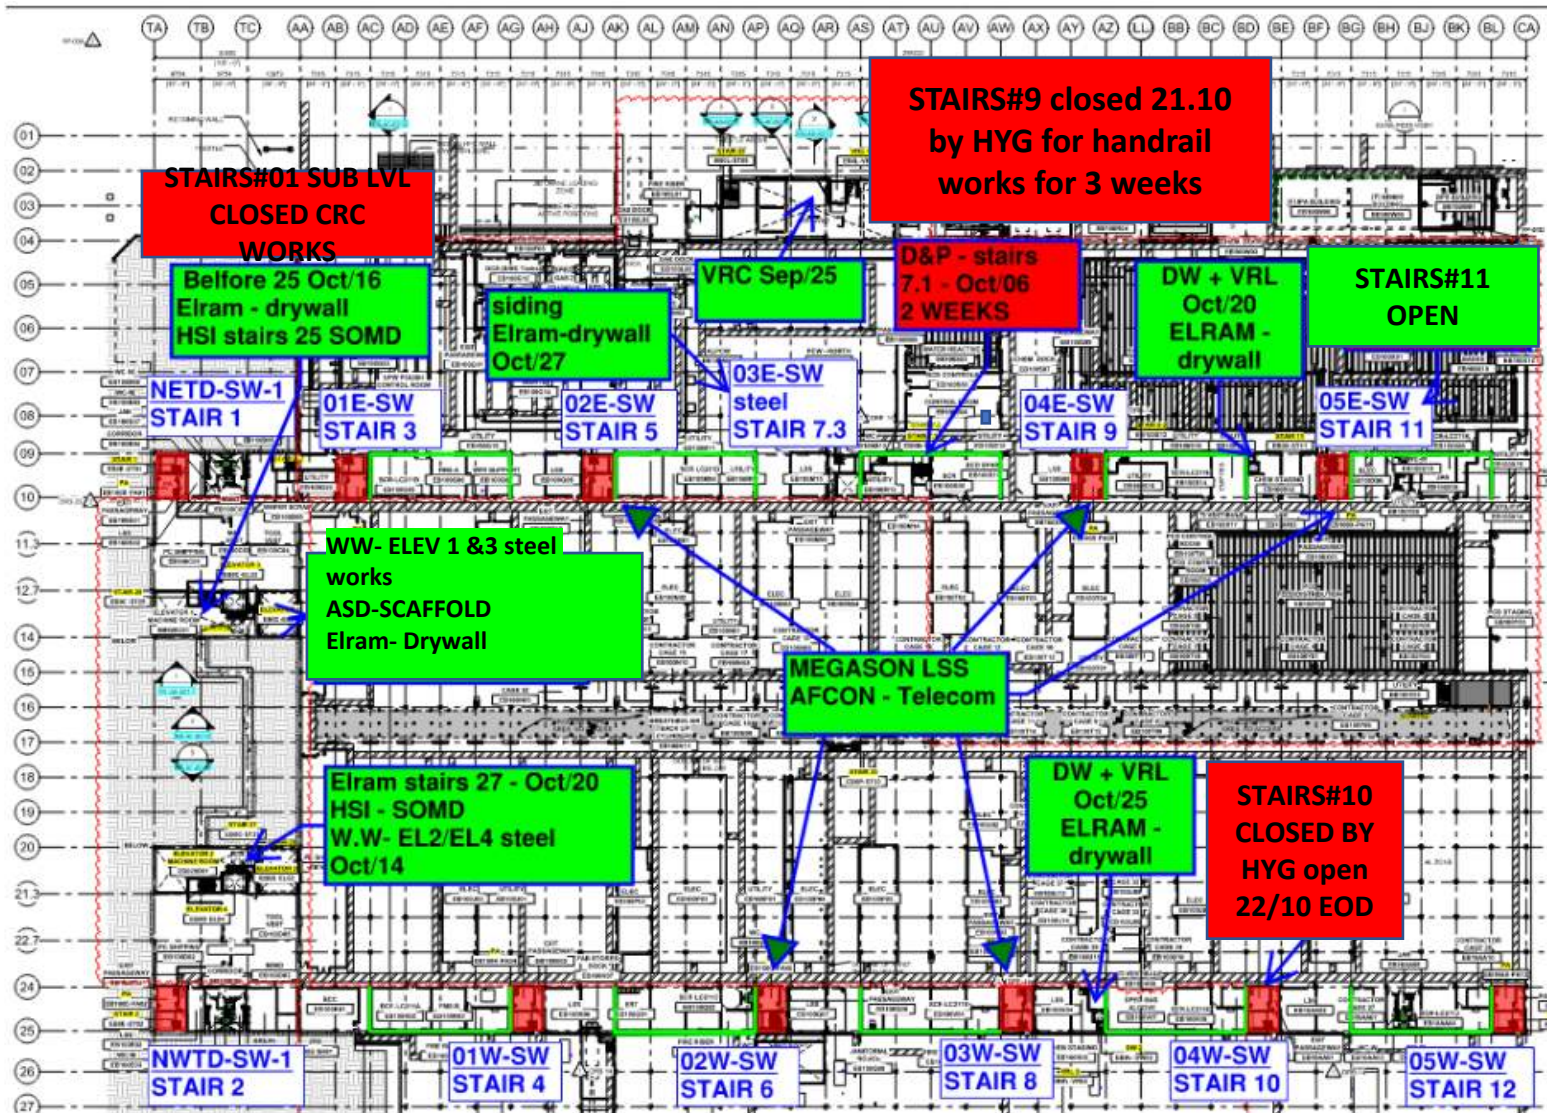

Siding - West FAB - JYG

BLOWDOWN 30%


[illegible]


Siding - East FAB -

BLOWDOWN 30%

[illegible]




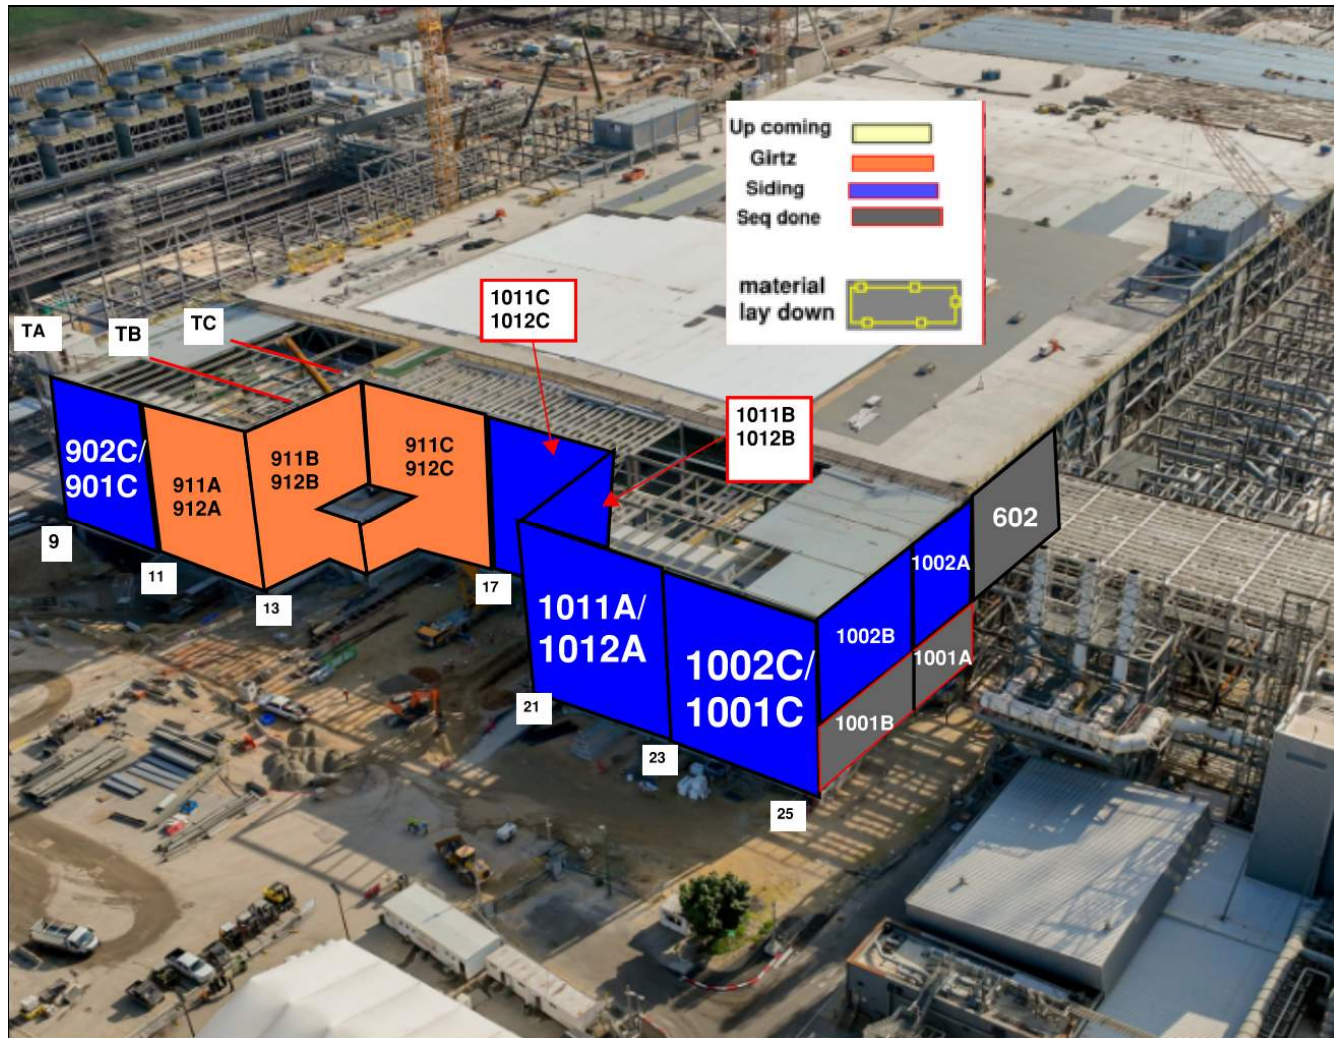

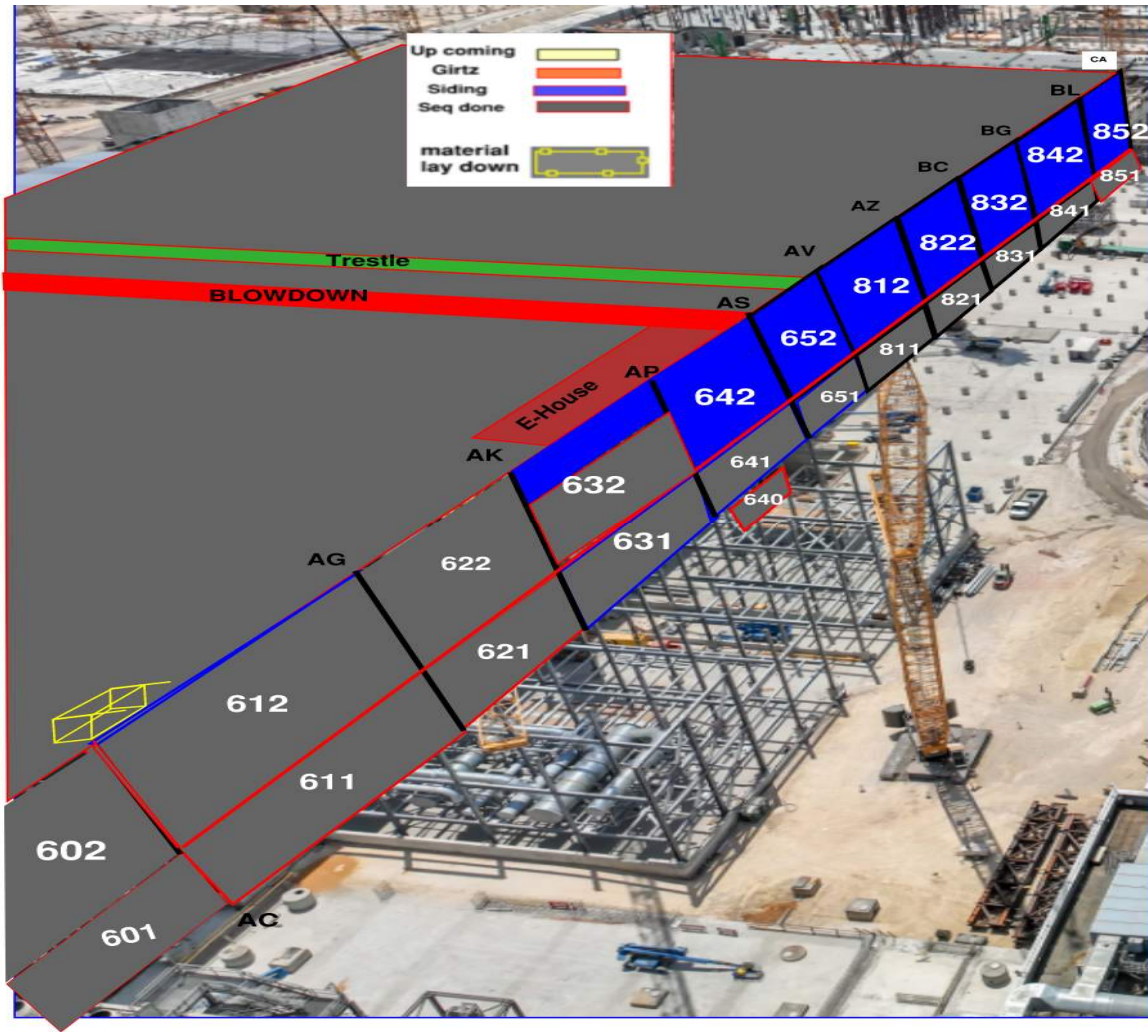


PSSS.1

Utility Level
1YA

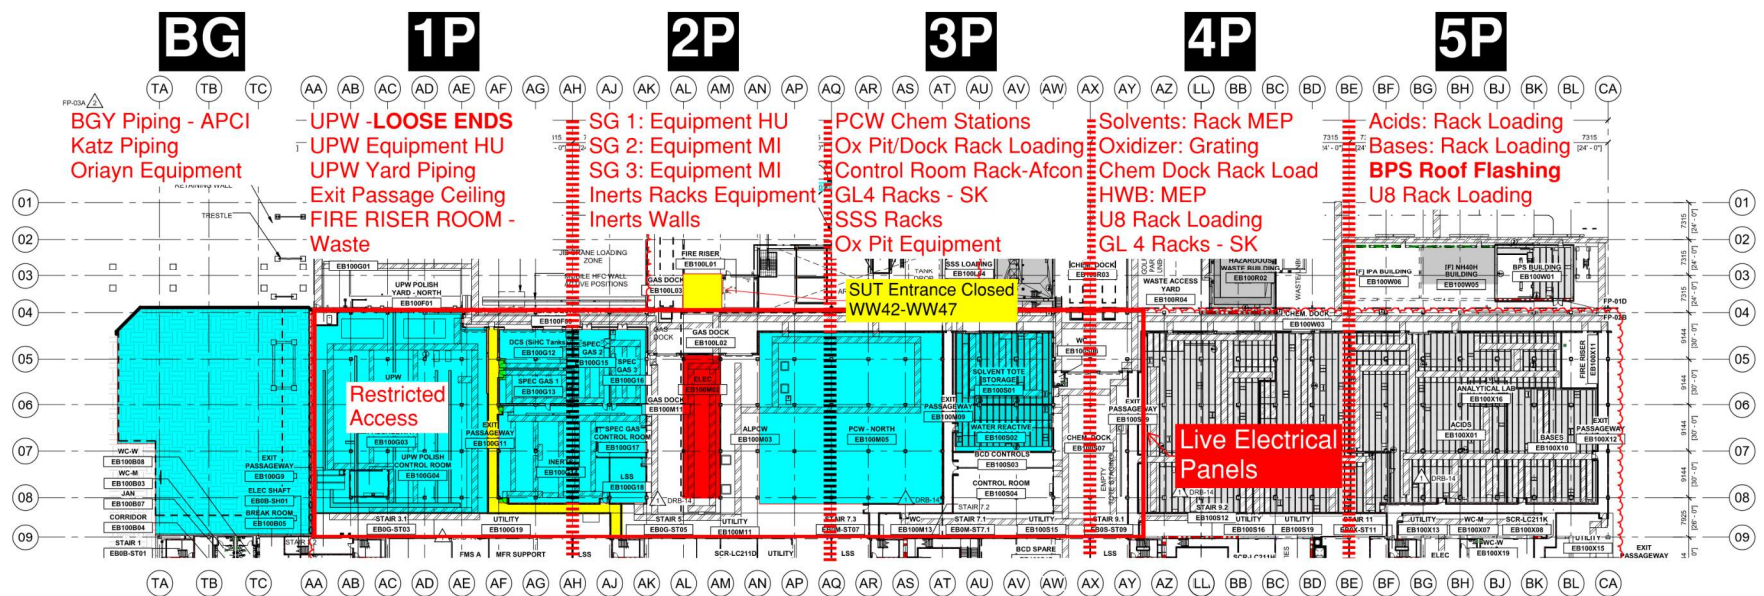


PSSS Roof
2SA

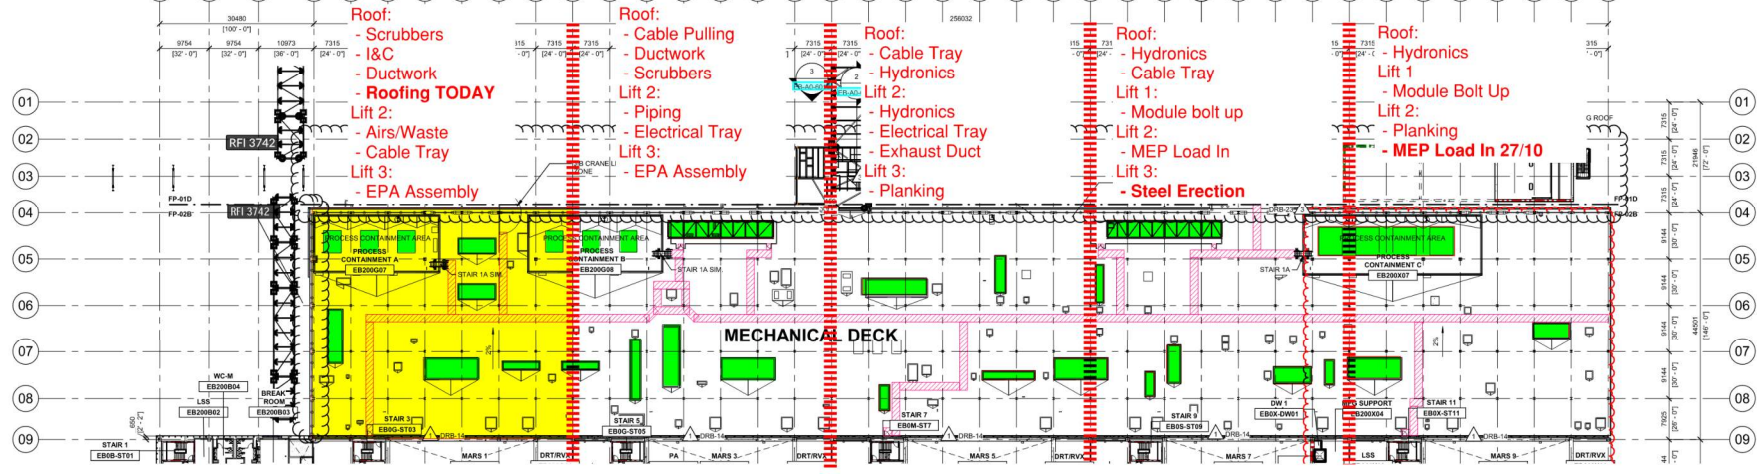

PSSS.2


Utility Level
1YA

PSSS Roof
2SA

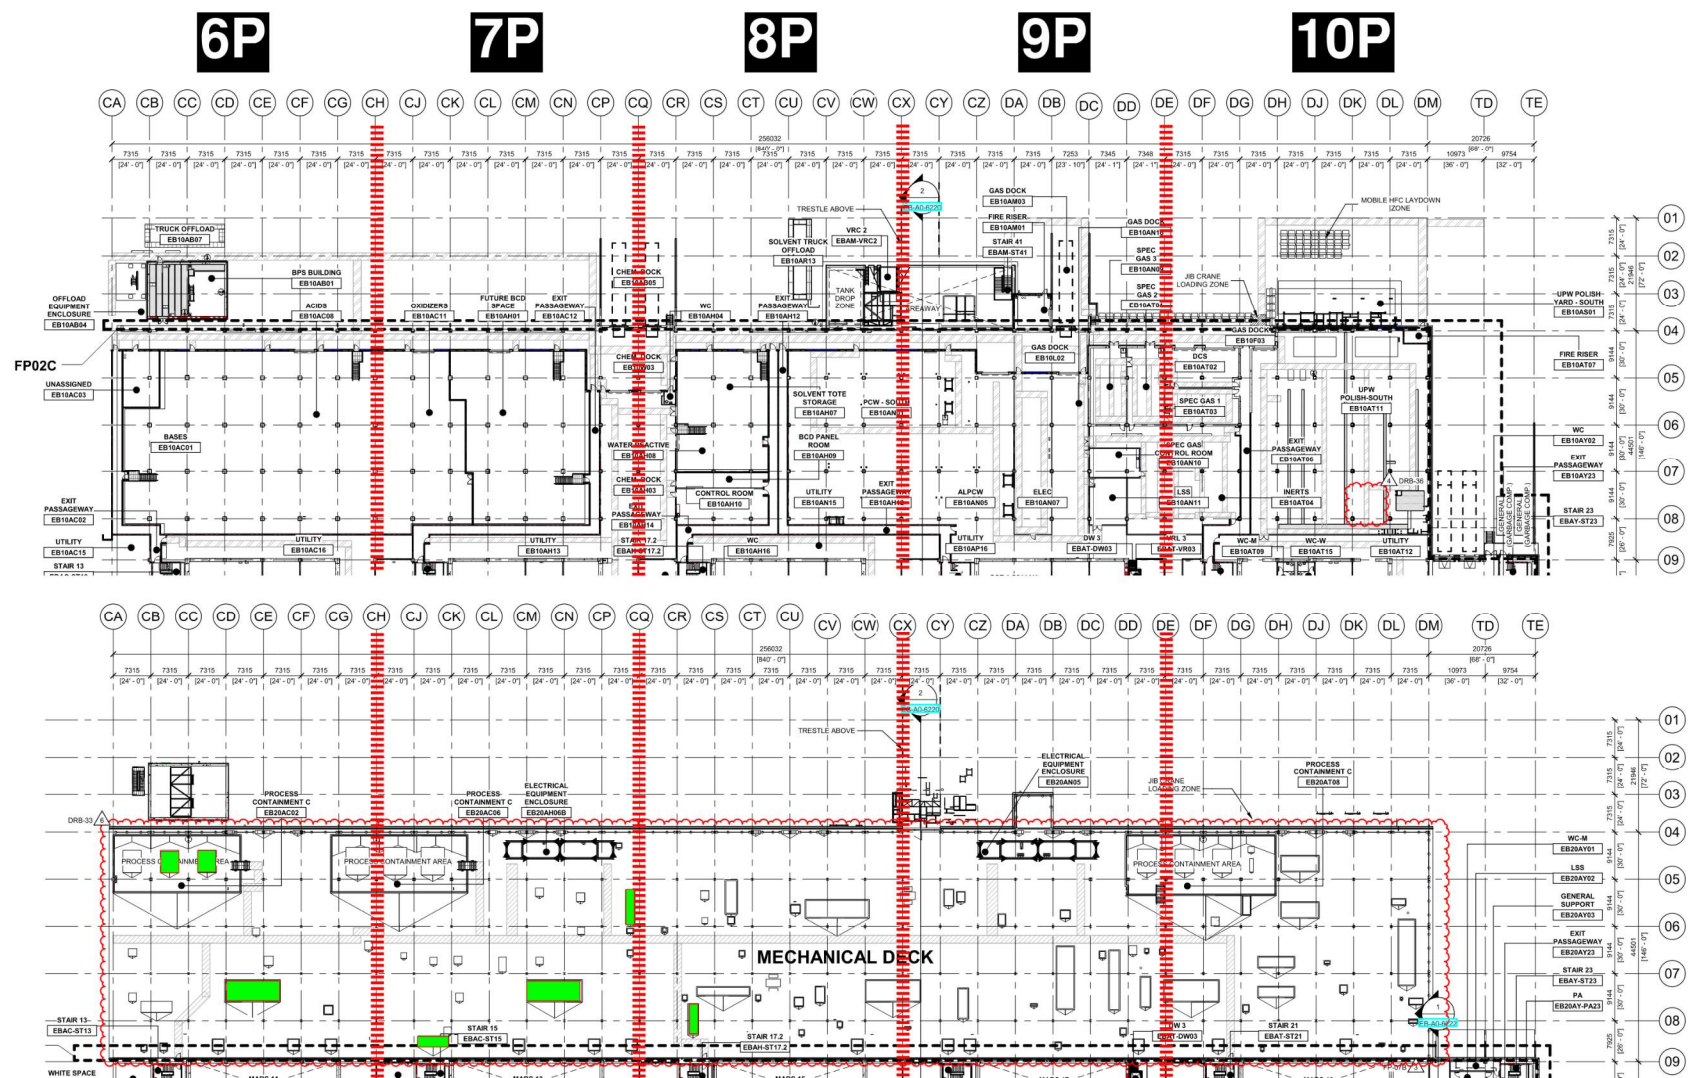


DMAG MOVE FOR Plenum Set






WJG 01J, 02J LIFT 2 & 3







WJG 03J, 04J, 05J LIFT 2 & 3






WJG 03J Plenum Set 21/10

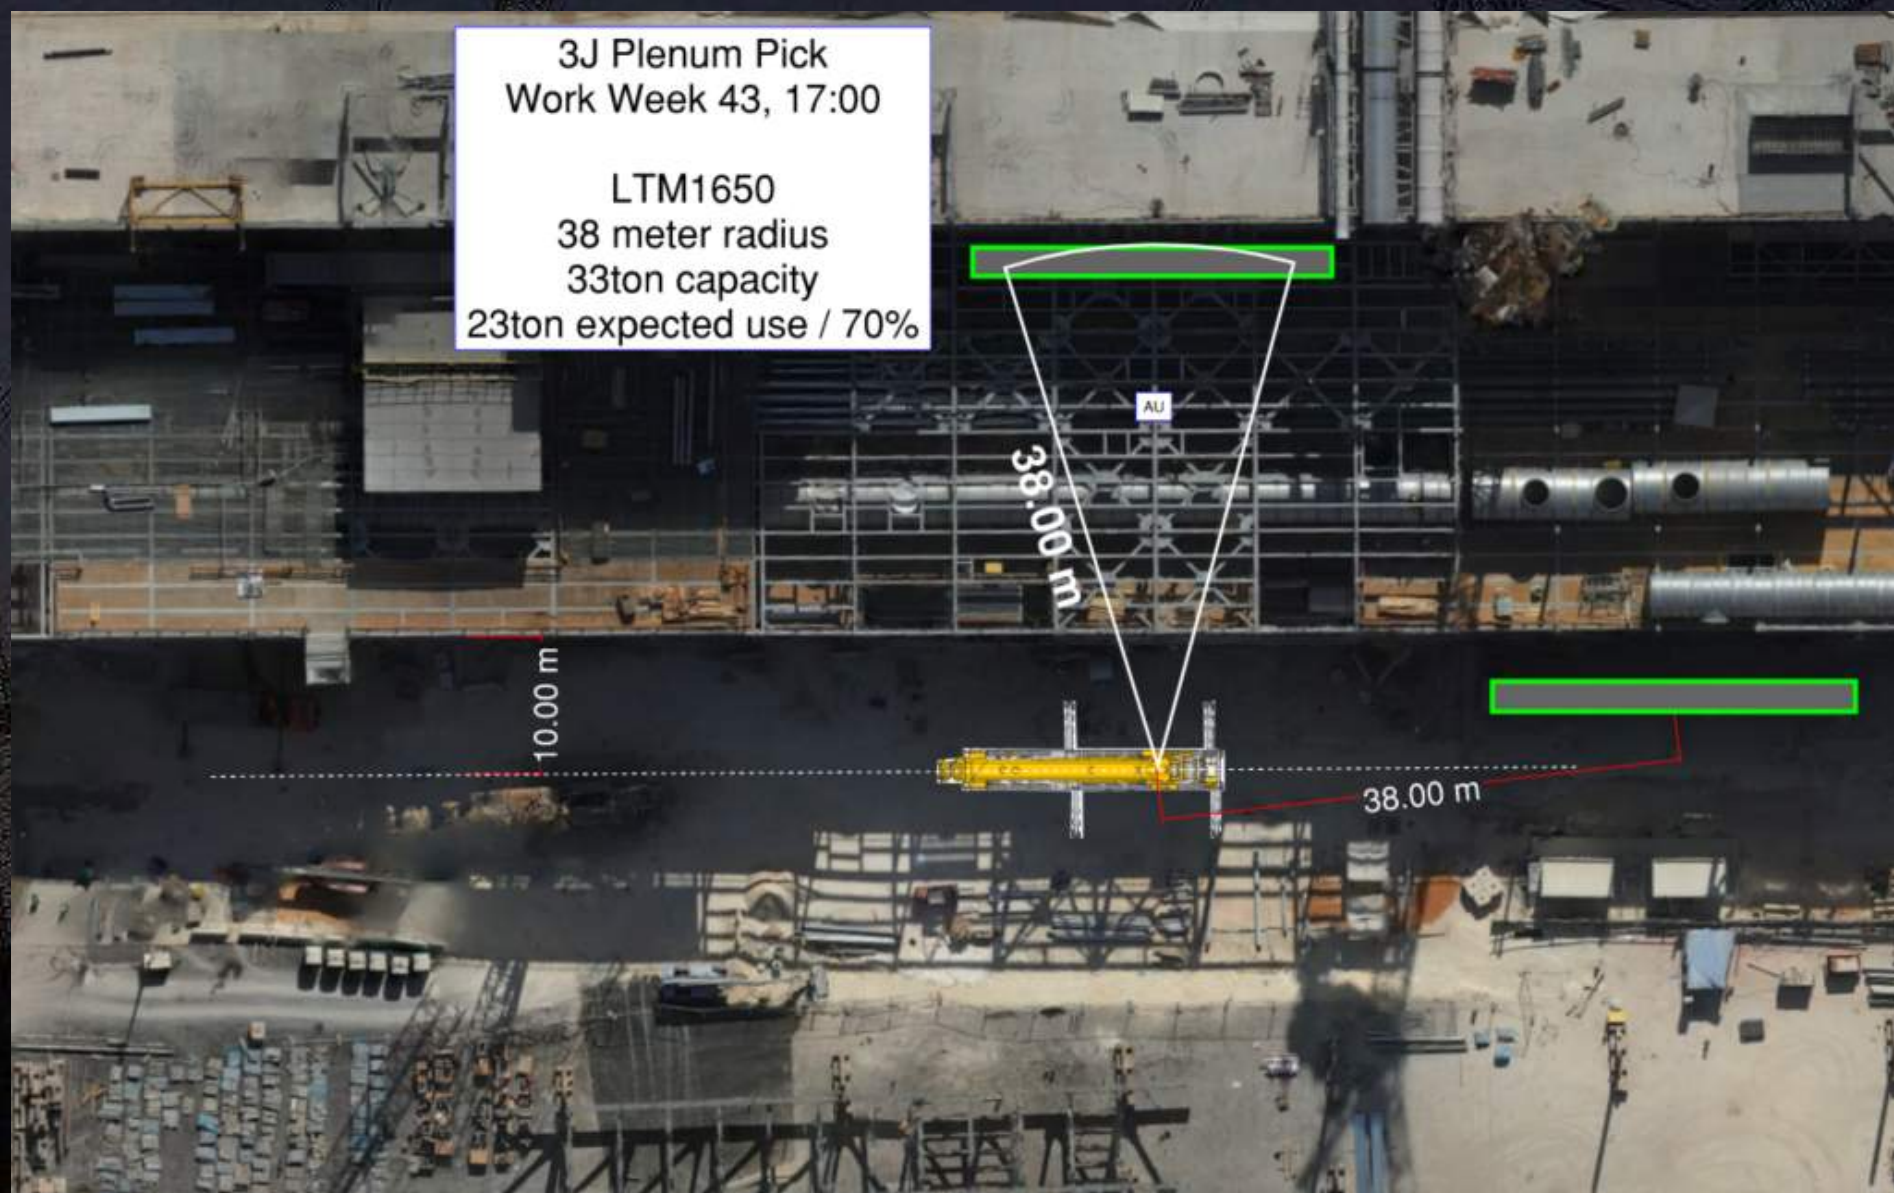





Walk Path Reroute WW43 & WW44

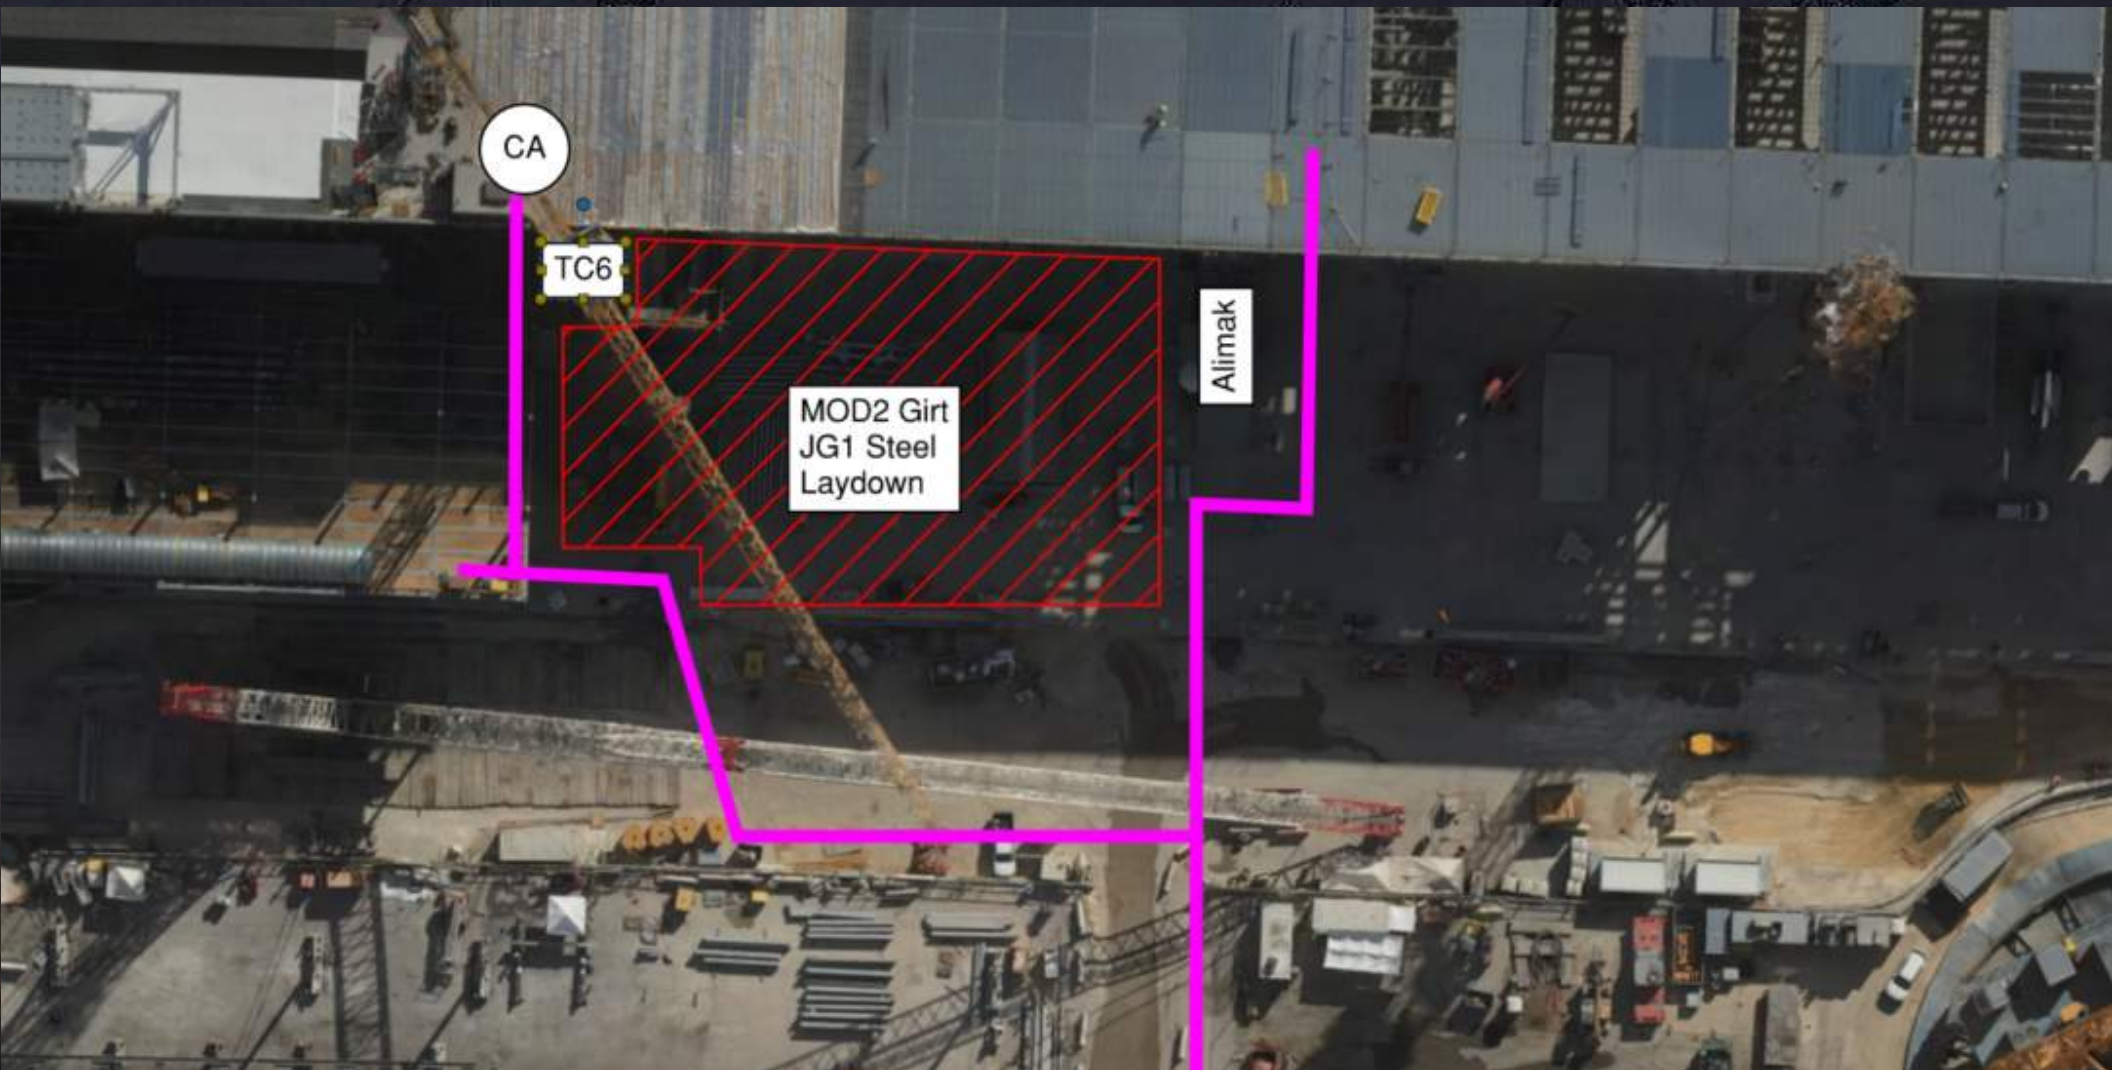

AH104-22-00 Set – 29/10

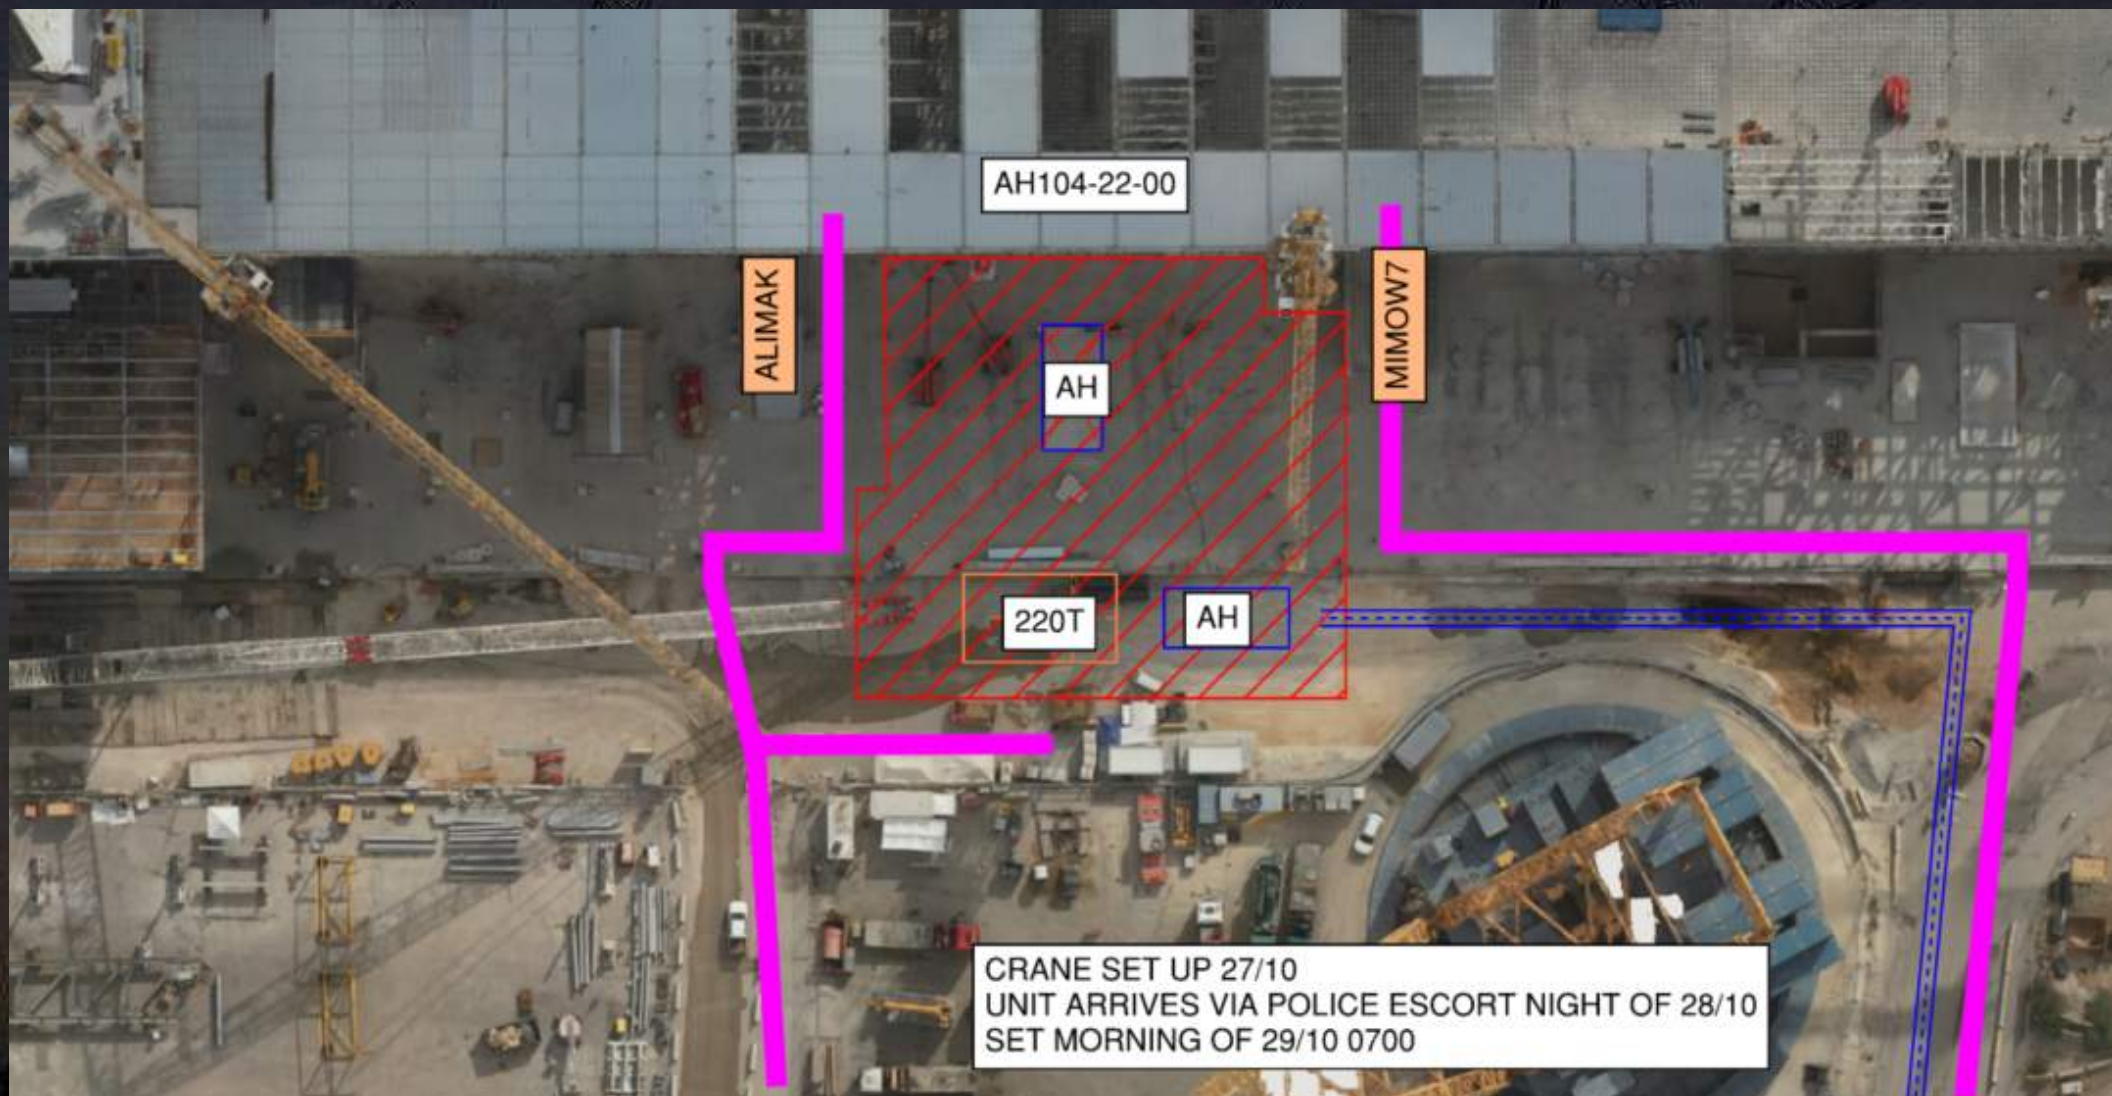

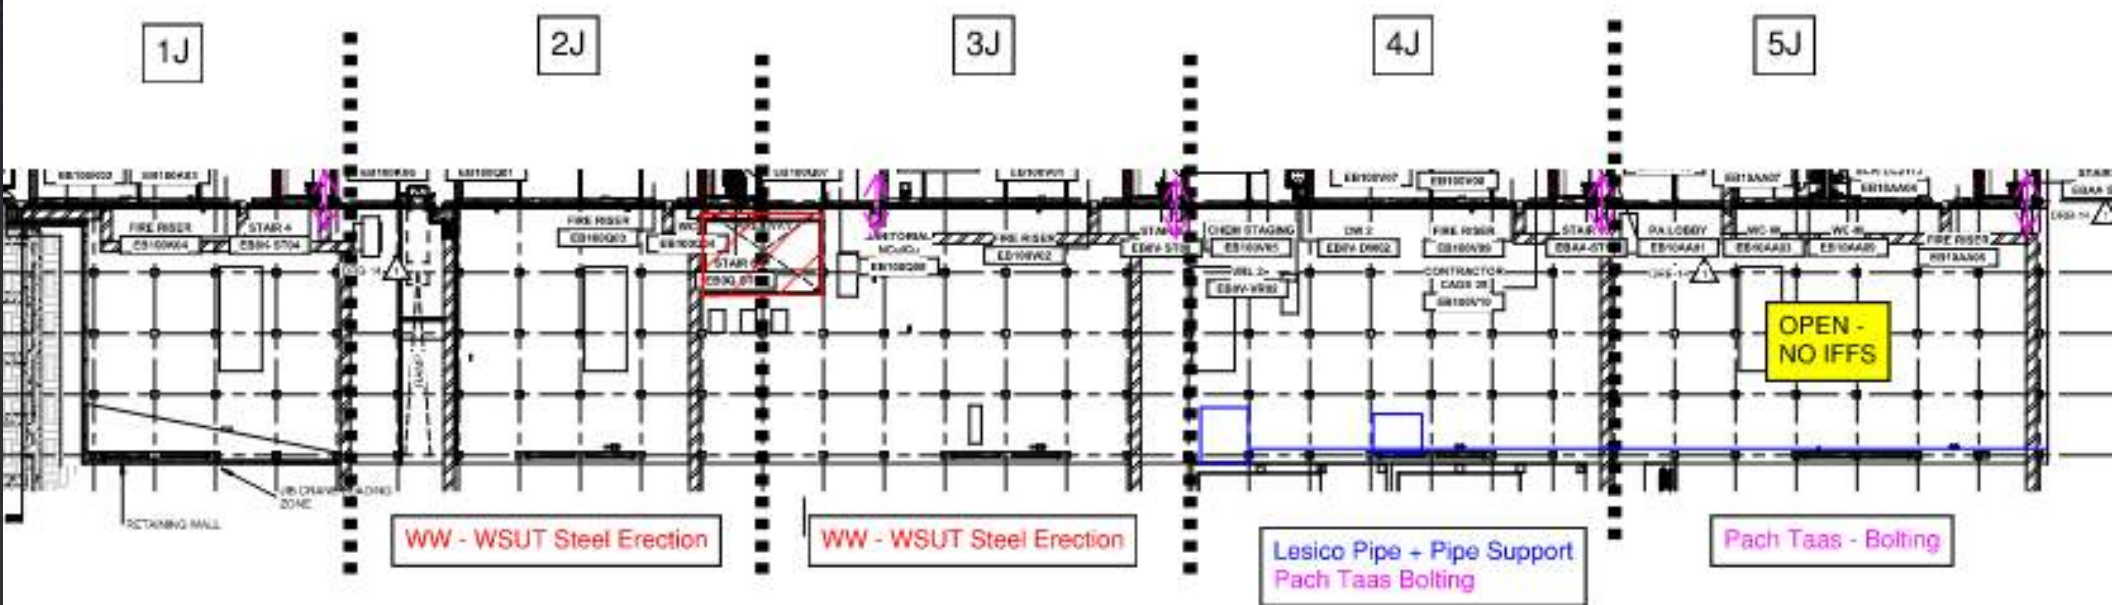




CUB 1

CUB 1 COORDINATION MAP

UPDATED

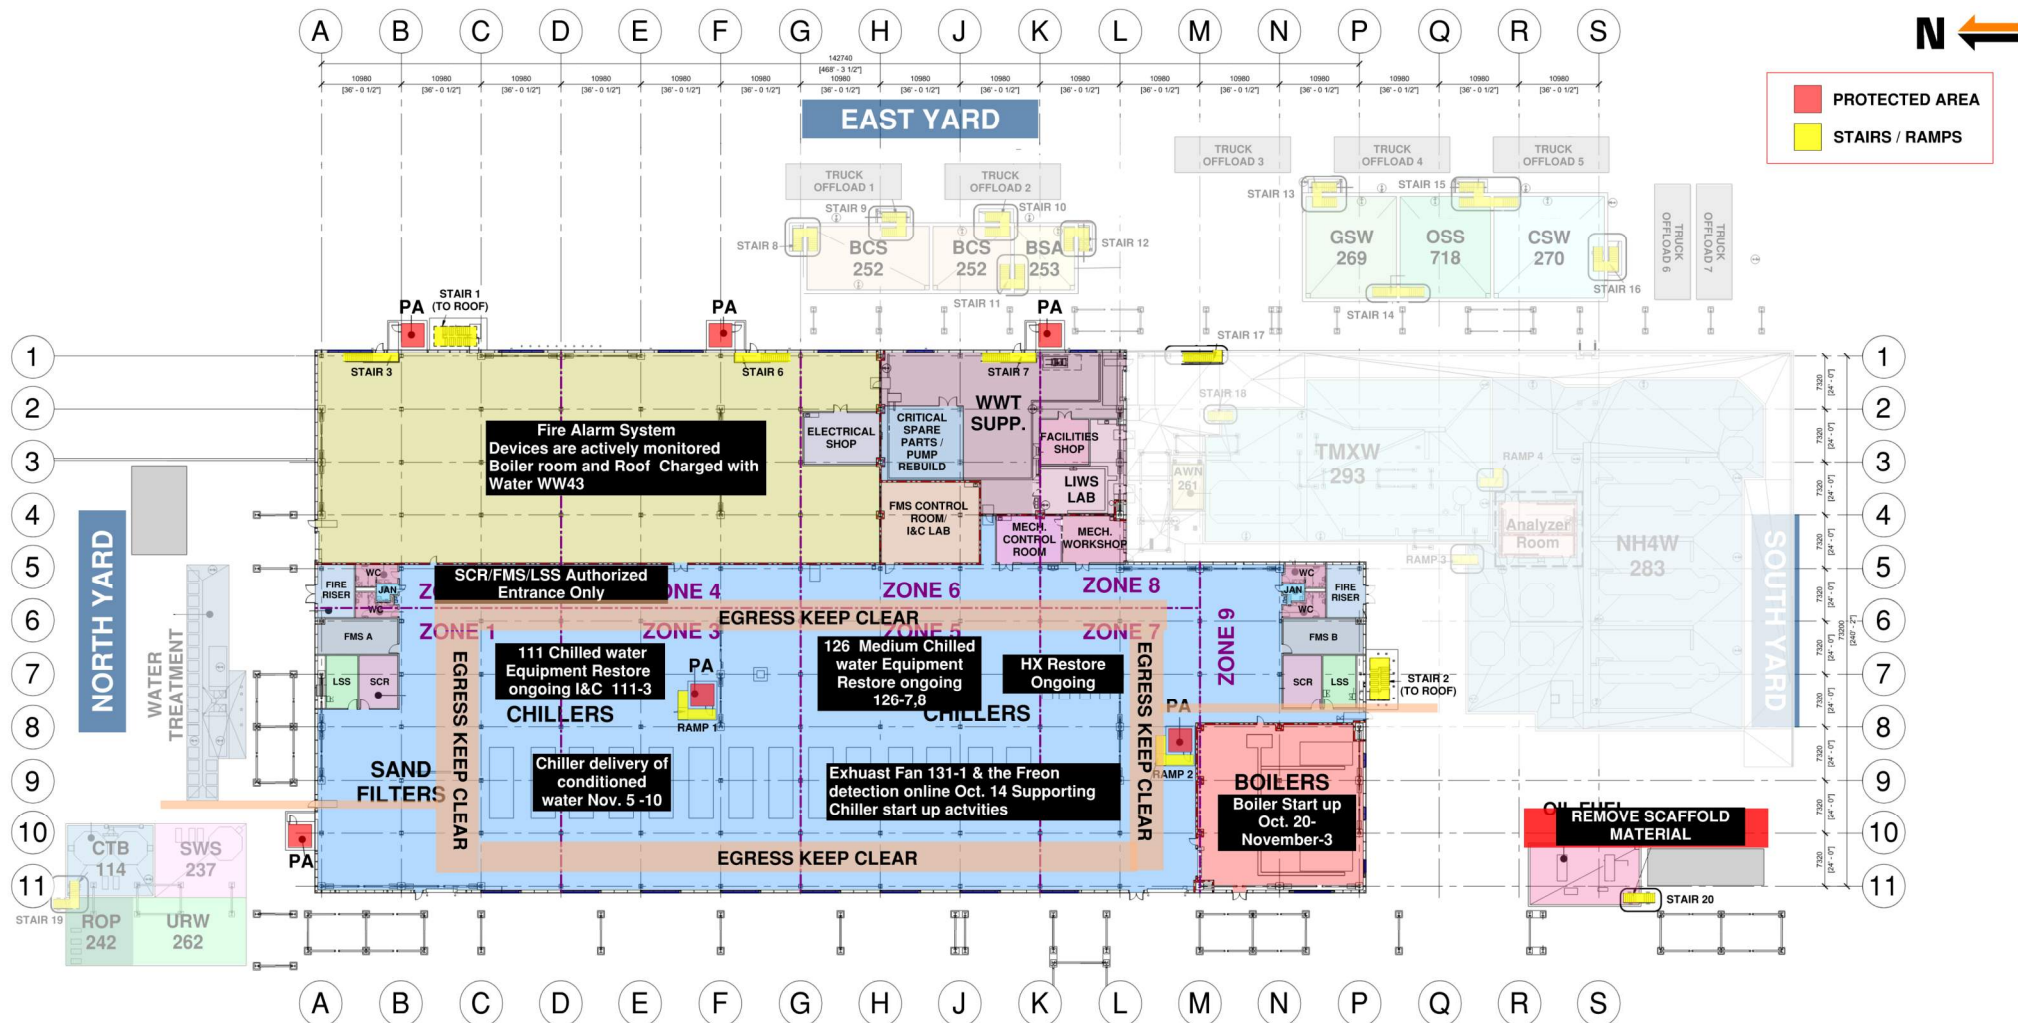

CUB 1 – EXTERIOR/ROOF






CUB 2


CUB 2 COORDINATION MAP




- PROTECTED AREA
- STAIRS / RAMPS
- YARDS
- TRUCK OFF/LOADING
- Wall Framing
- Metal Panels

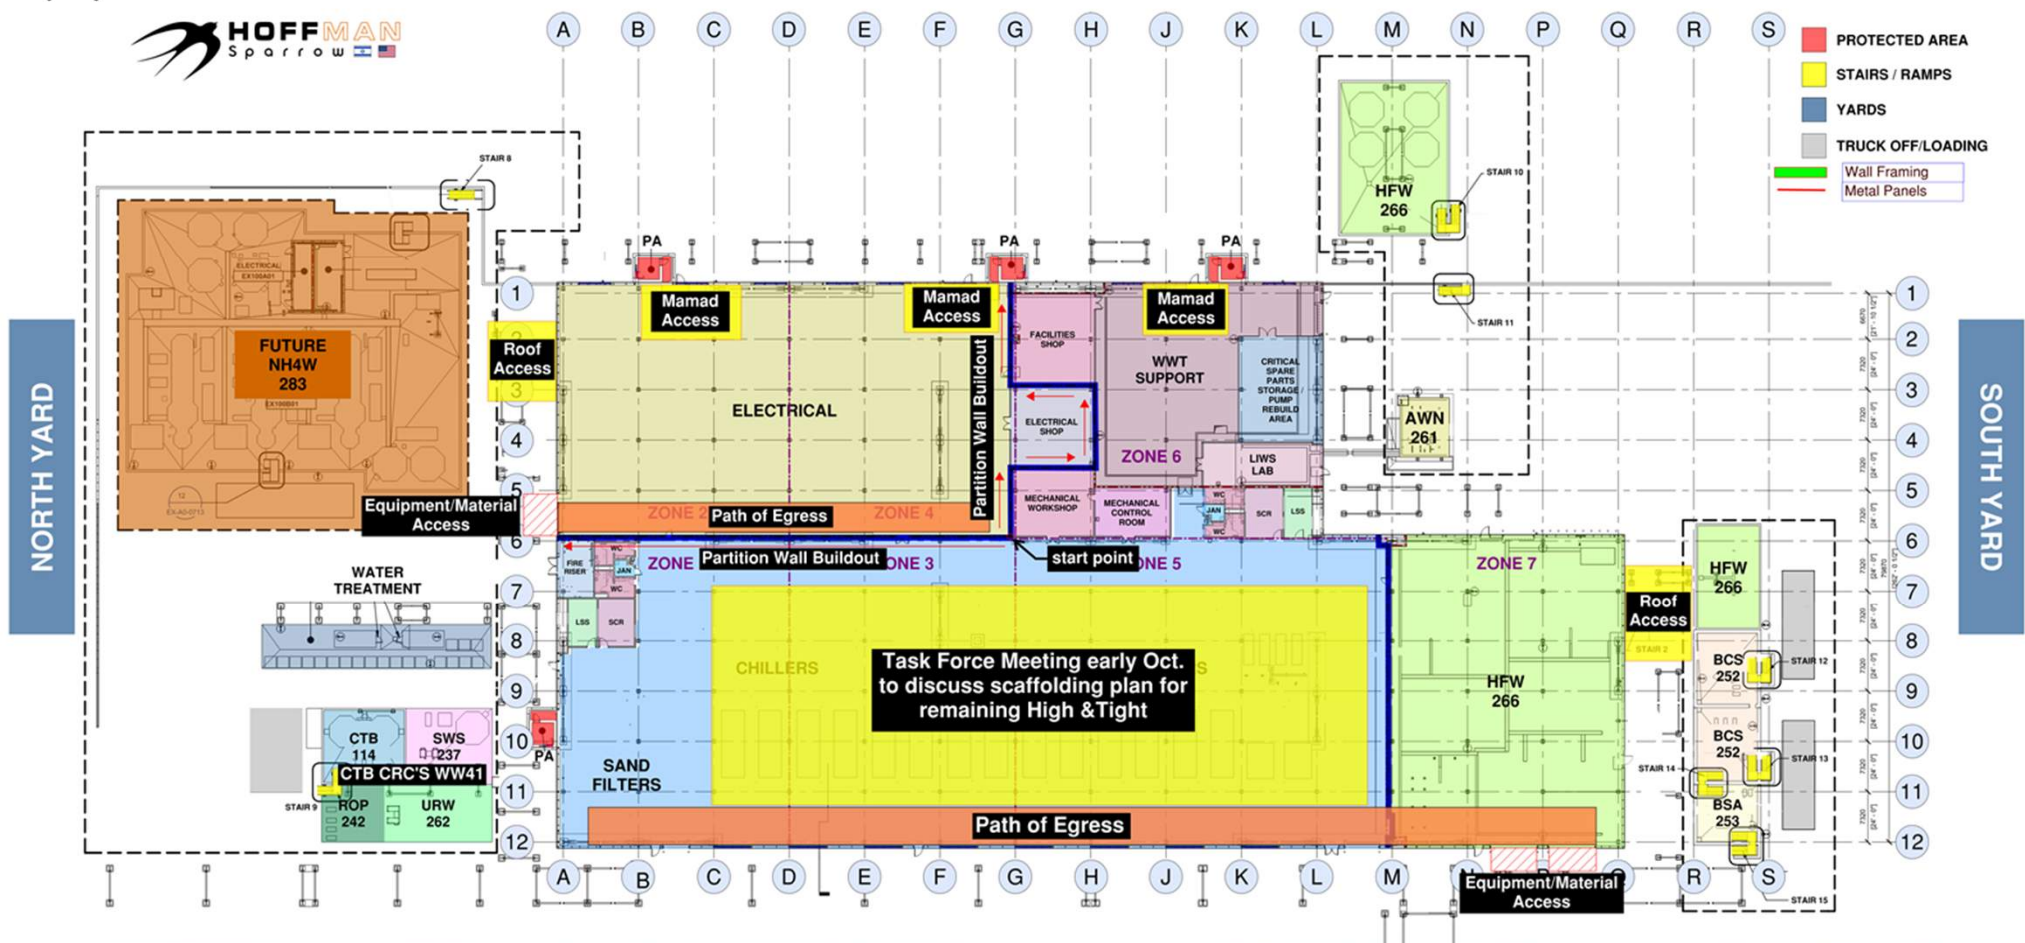


CUB 2 – EXTERIOR/ROOF

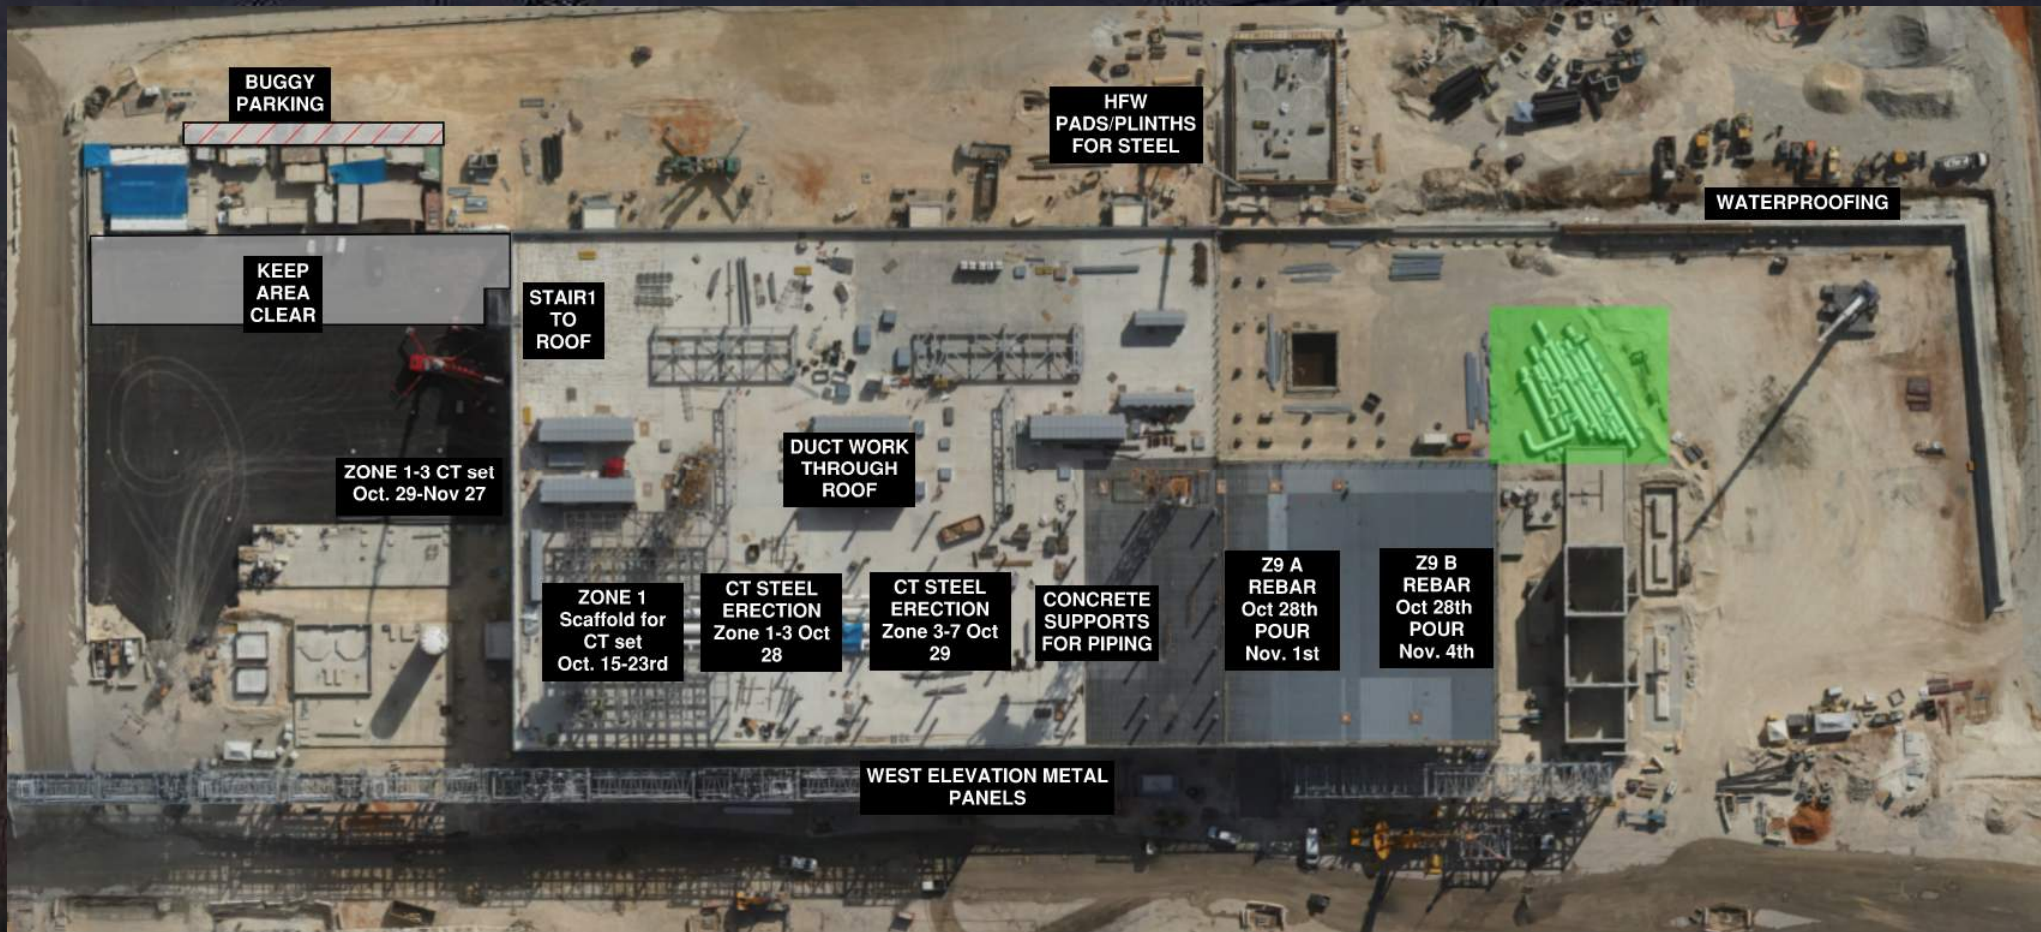



HOFFMAN CONSTRUCTION COMPANY

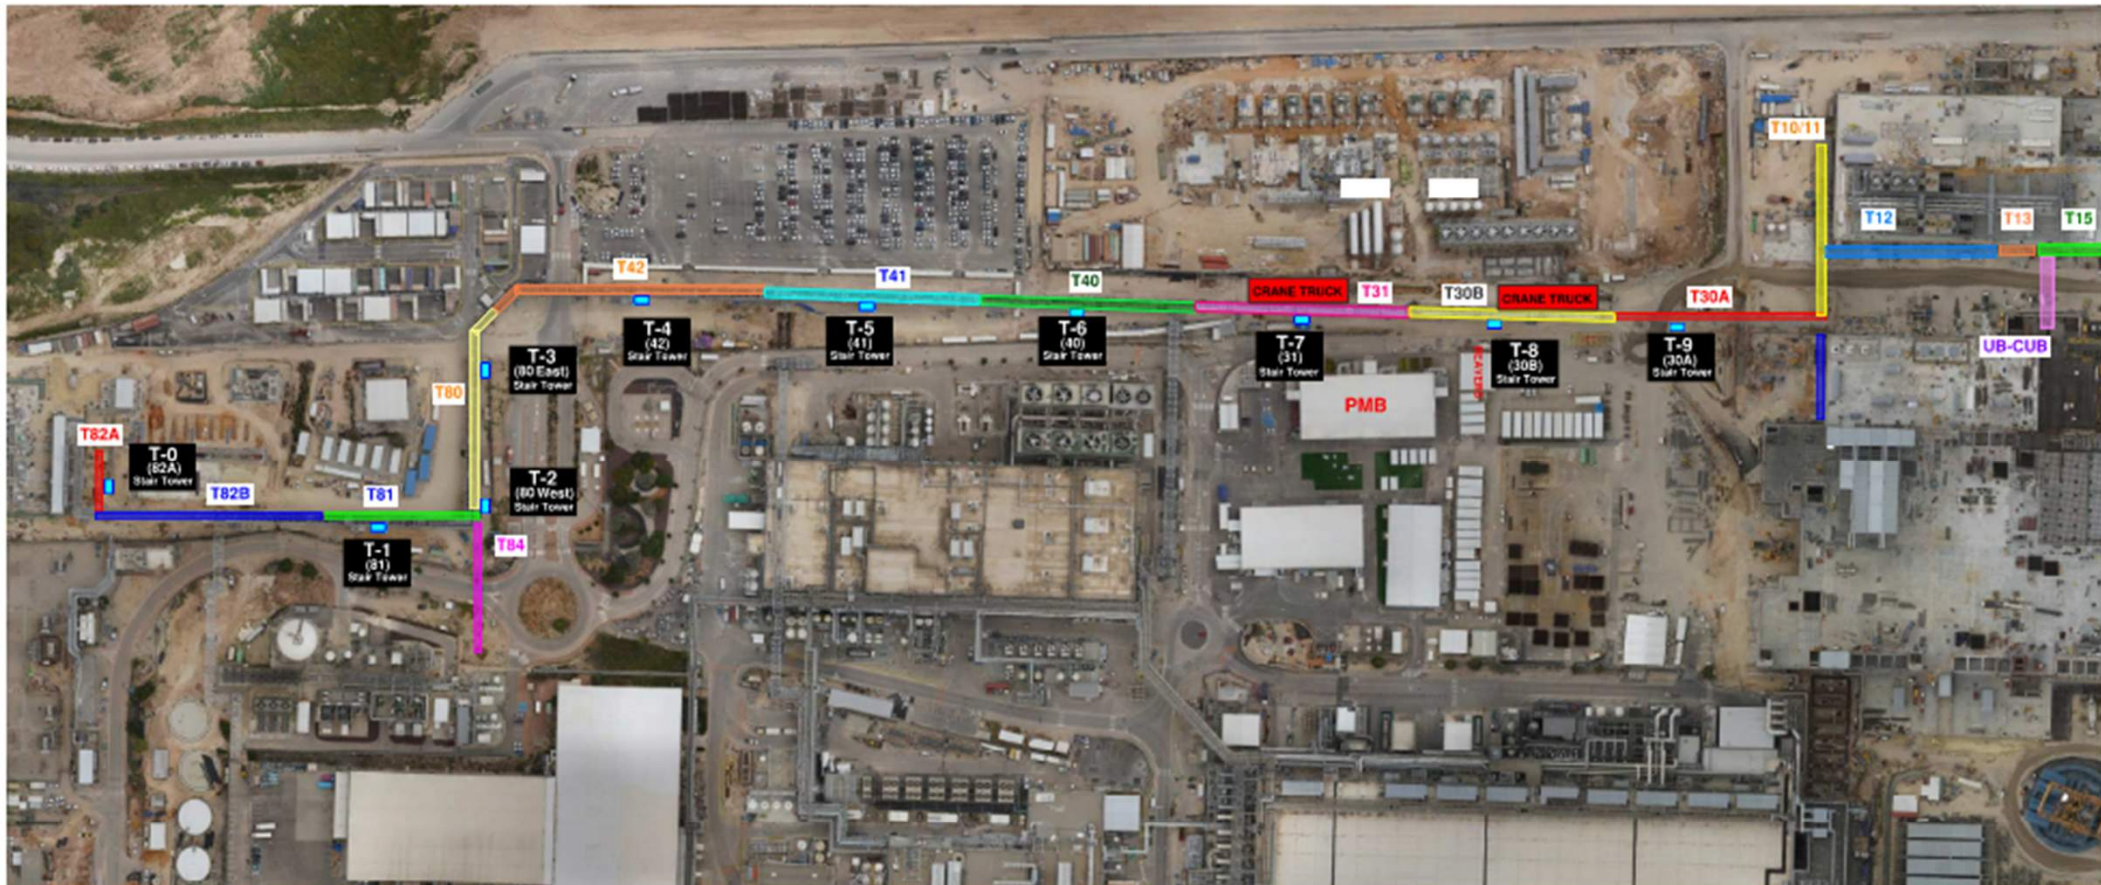

T18

CUB 2 - NOV 3th - NOV 11rh

nov 7th

nov 6th

nov 5th

nov 3th

nov 10th

nov 11th



5 m



Daily Coordination Meeting

Site Logistics

North






Daily Coordination Meeting

Site Logistics

South

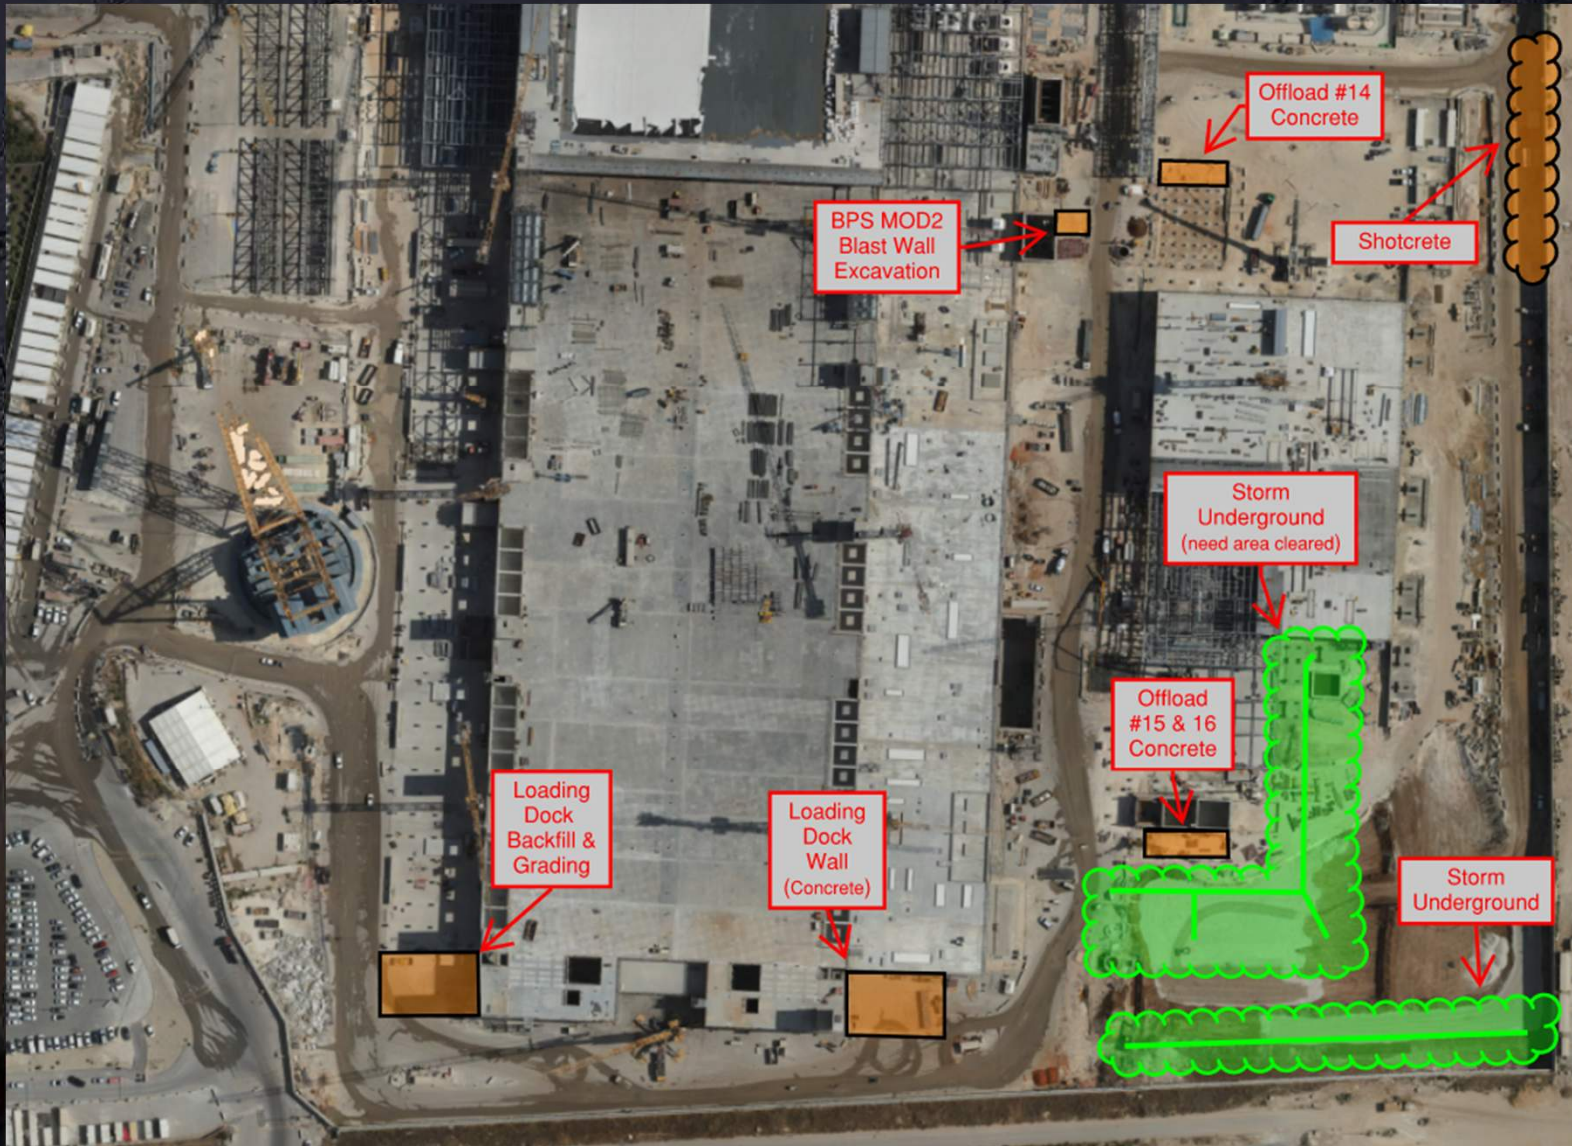

Let's Again Focus on the Basics

- With the holidays, we are seeing a slip on some basic site rules. Please ensure that all of you are reinforcing the following with your crews:
- ALL PPE is required in the construction site. This includes safety glasses, cut level 5 gloves, reflective hi-vis outer layer, S3 work boots, and a helmet (chin strap must be buckled).
- Barricades must be enclosed and have proper signage.
- The speed limit is 16 KPH, and no driving through the GUT road.
- Don't use cell phones while walking or while in an active work area.
- Clean as you go, not at the end of the week.

HCC/EHS Weekend Work- 27.09.2024

White Board Meeting in Beavers at 06:30

Superintendents

Brian Grevious 052-5394339

Igor Shuster 054-4743767

Josh Noll 052-5590653

Husein Abu Hammad 052-4106872

CSA CM

Tarek Nairoukh 052-6636782

Idan Turjeman 052-4093025

MEP

David Jollands 052-3961675

Andy Jollands 052-9659290

Paruic O'Reilly 052-3571665

OSM

CX/QA

Darryl Hicks 052-3215975

Cranes

Brady Prouty 052-6047531

Safety

Safety Foreman- Adir Elmakayes- 054-7254767 Adir-Elmakayes@Hoffmancorp.com

Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com

Safety Officer - Arkady Gerber-050-6851432 Arkady-Garber@Hoffmancorp.com

Subcontractor Weekend Work- 27.09.2024

FAB

UTILITY LEVEL

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

EIram

Foreman: Shlomo

0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

Pach Taas

Perim Rack Aae

Team Lead : Nuriel 0549012324

Afcon E

PA/Stairs

Team Lead : Avi Eli 0526008487

Chemo

TTNW

Team lead: Tommy 0523759408

Safety: Lilah 0547886704

Belfor

TTNE / TTNC

Team Lead: Salame 0546651886

HYG

SF Zones 3- White steel touchups/Mamad plates weld/

Stair # 8

Salah 0507773119

WW Steel

Elevator 3

Teddy 0522392473

Clean Room

W&W 17-18 Line added the beams 10-24 line – catwalks, MOD2: steel fan deck east west, infill ongoing (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

Talad – CR 1W – Drilling holes, 1 metal lids removal (EHS Guy 0544915407, Super Igor 0544509386)

Sig – 5W INT Platforms MIMO CB-CC/25 (EHS Beni 0506232032, Super Nodar 0546313261)

EIram – CR Level 9,25 line, AA line 2W shafts walls INT level 9,10,17,24 column wrap (EHS Royi 0538312234, Super Bonio 0544236899)

Afcon – CR – 2E-5E, 2W-5W, INT- 2E-3E, 3E-3W ,LINK Rack install (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Sela – 1E-AB-AK/10-12 CRC (EHS Shmuel – 0506306031, Supervisor Yuval 0502649246)

Subcontractor Weekend Work- 27.09.2024

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2, and EPA Platform
1&2P

Foreman – Vadim – 052-6229005

Safety – Offek – 050-7838486

Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-
2P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-4P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

W&W – SEQ 135, 137

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Elram – 5P Corridor, UPW Ceiling

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Lesico – 5P UN2 Welding

Foreman – Selvin – 052-4787370

Safety – Itay – 054-2336103

Combe UPW – UPW Room Piping and Yard

Foreman – Boris – 054-8346412

Safety – Abed – 052-5148747

SNJ Flashing – BPS Roof

HSAl – BPS Blast Walls

Foreman – Dave – 052-4121028

Safety – Sam – 052-5259268

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

WJG

Pach Taas

Adiv Pereg- EHS

Netanel Ivgi – Forman

Siding

SAMI NAJAMI -ROOF METAL

SAMI NAJAMI -PANTRETION

SAMI NAJAMI -GERTZ

Victor 0549220163

Subcontractor Weekend Work- 27.09.2024

CUB

Sami Najami CUB 2:

Husein - 0526917461

Alon - 0509895008

Meptagon I+C:

Raziel - 0584360845

Netanel - 0538398999

Pach Taas:

Adiv - 0506909390

Nati - 0543301880

ETC south yard:

Yosef - 0506708990

Leonid - 0545991846

S.K.E:

Reynato - 0548991623

HSAI

Chemo Aharon:

Dudu - 0509808846

Leonid – 0548883878

Date: 27 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.SARAWUT KHRUEASING, AC5094850, TEL 052-3628607 (Leader)

Date: 28 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.YOTSAWAT

Trestle

SNJ:

PIPES –UB CUB

ISOLATION –UB CUB

STEEL

FORMAN- BASHIR YONES - tel. 05273649963

SAFETY TRESTLE-Alon Matan tel. +972 50-989-5008

Site

Derech Afar – Shotcrete, Storm water bypass at Sarens & Fire protection water

Supervision = Raed: 054-2442030

EHS = Alex: 054-5403849

Olizki – Sweepers and water trucks

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

TM Team – LSS underground

Supervision = Nadav: 052-5893171

EHS = Alon: 054-7711469

GIS/NEY

Daily Coordination Meeting



14:00 Sign In
