

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:


- Contractors who are still missing dailies for last week:
 - AS Barzel
 - Afcon Construction
 - Electra Elevators
 - Olizki
 - Siemens
 - SK Engineering
- Contractors that have not collected their water bottles:

○ Afcon Controls ○ Brand ○ Bynet ○ Carmel Bidud ○ Dvir ○ EL Fireproof ○ ES Entry Systems ○ Globus ○ HYG ○ Katz	○ NewcoTech ○ Ranpro ○ Sela ○ Skyline ○ Stage Design ○ Talad ○ Tavas ○ TM Teams ○ Tzur-Esh ○ YWCT
--	---


UTILITY LEVEL MOD1

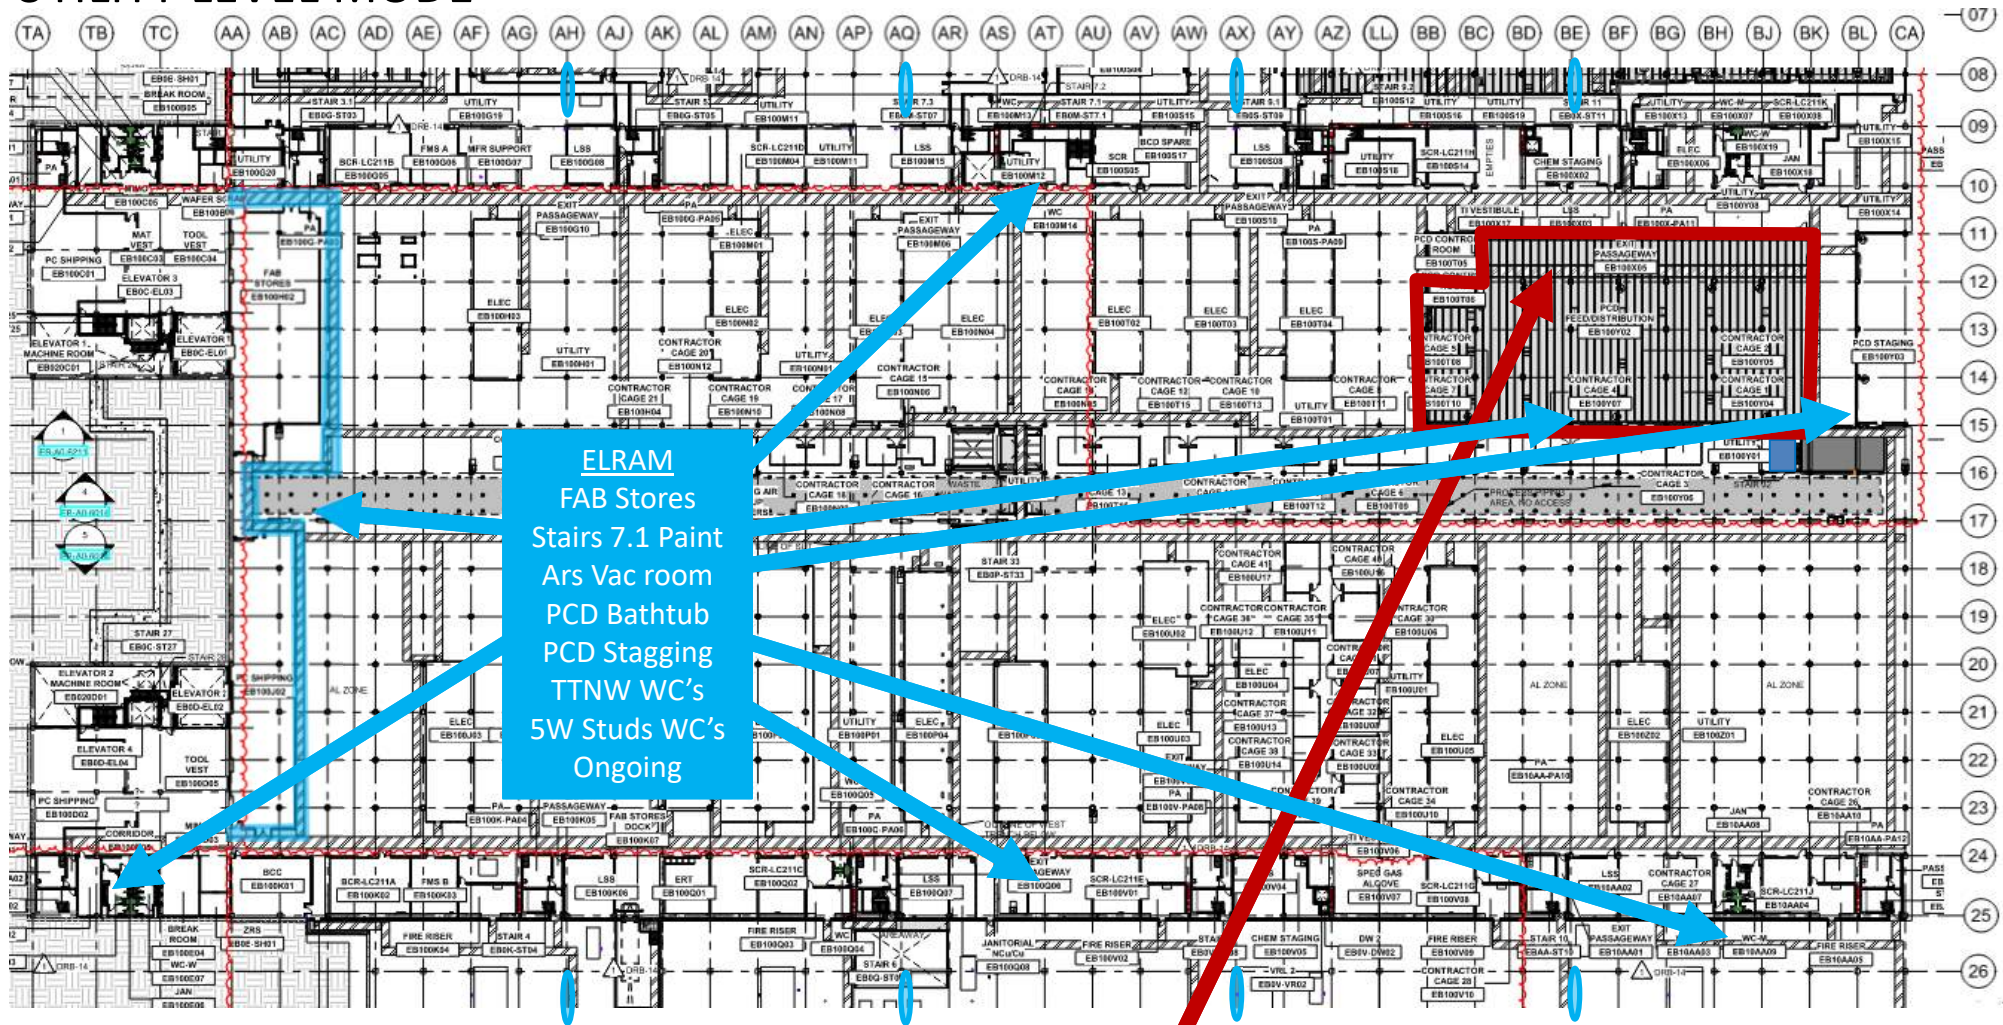

UTILITY LEVEL MOD2

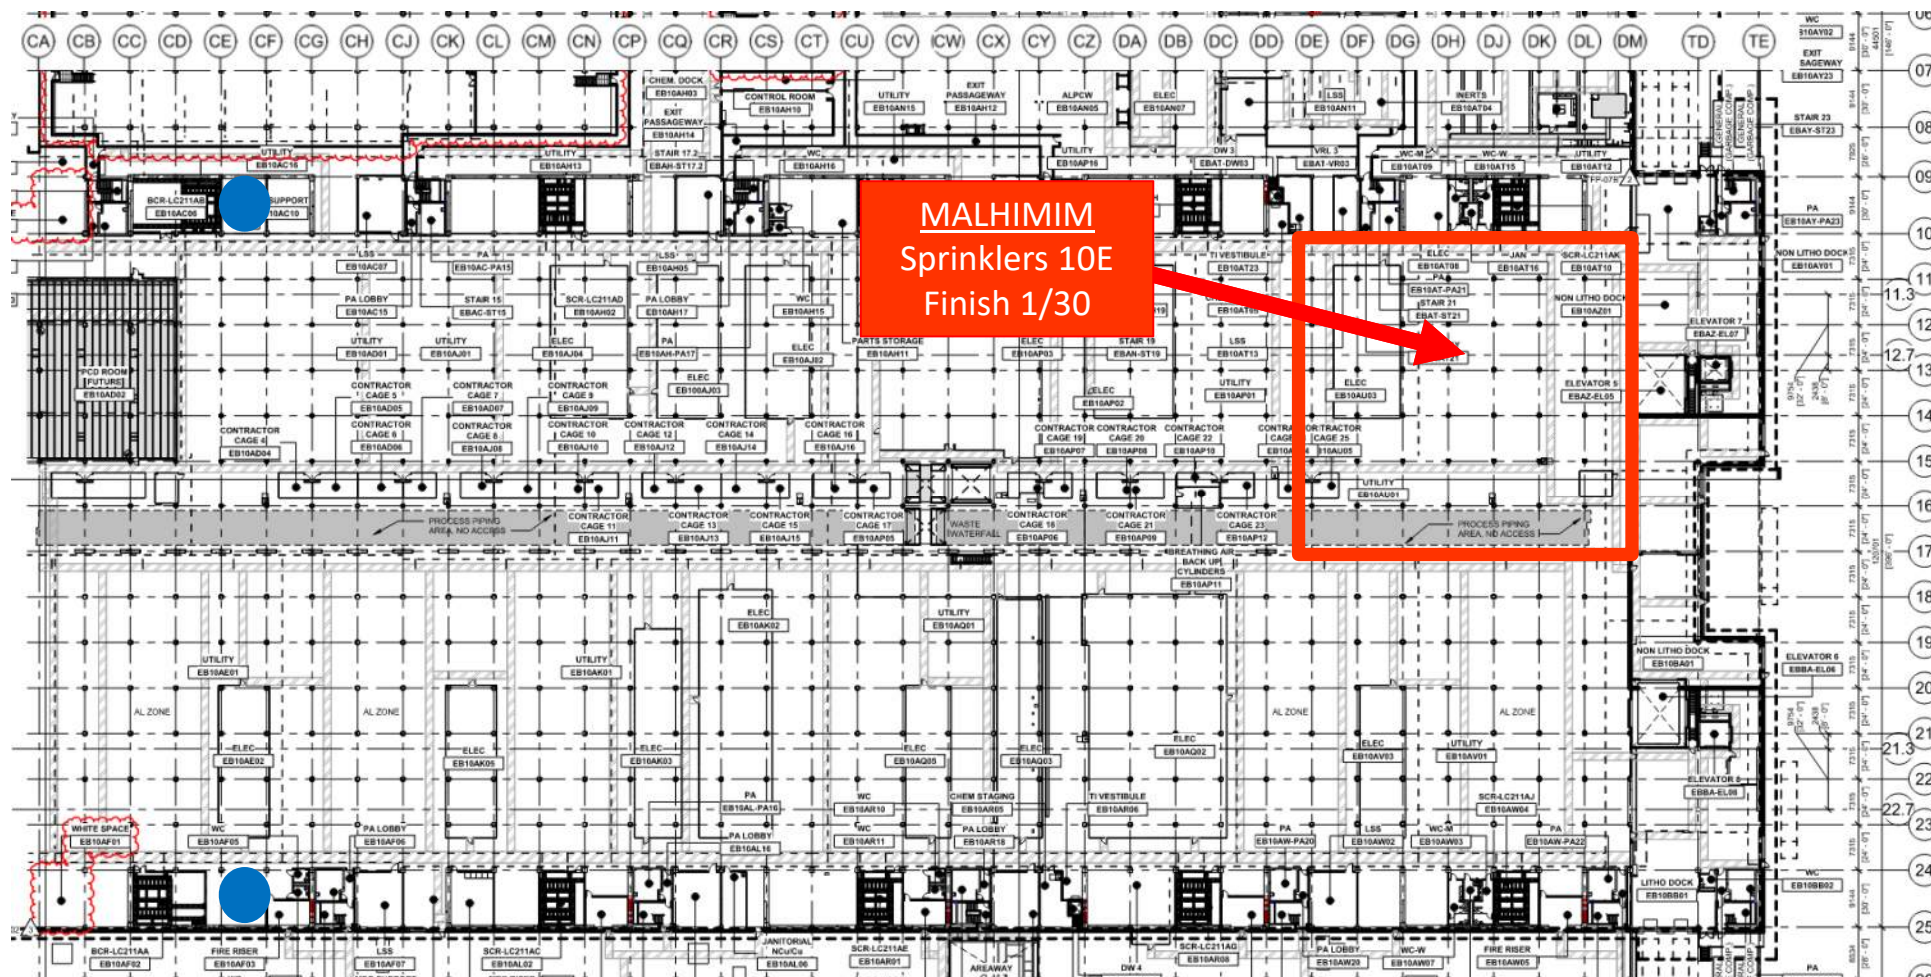

SUT 38.1 LEVEL

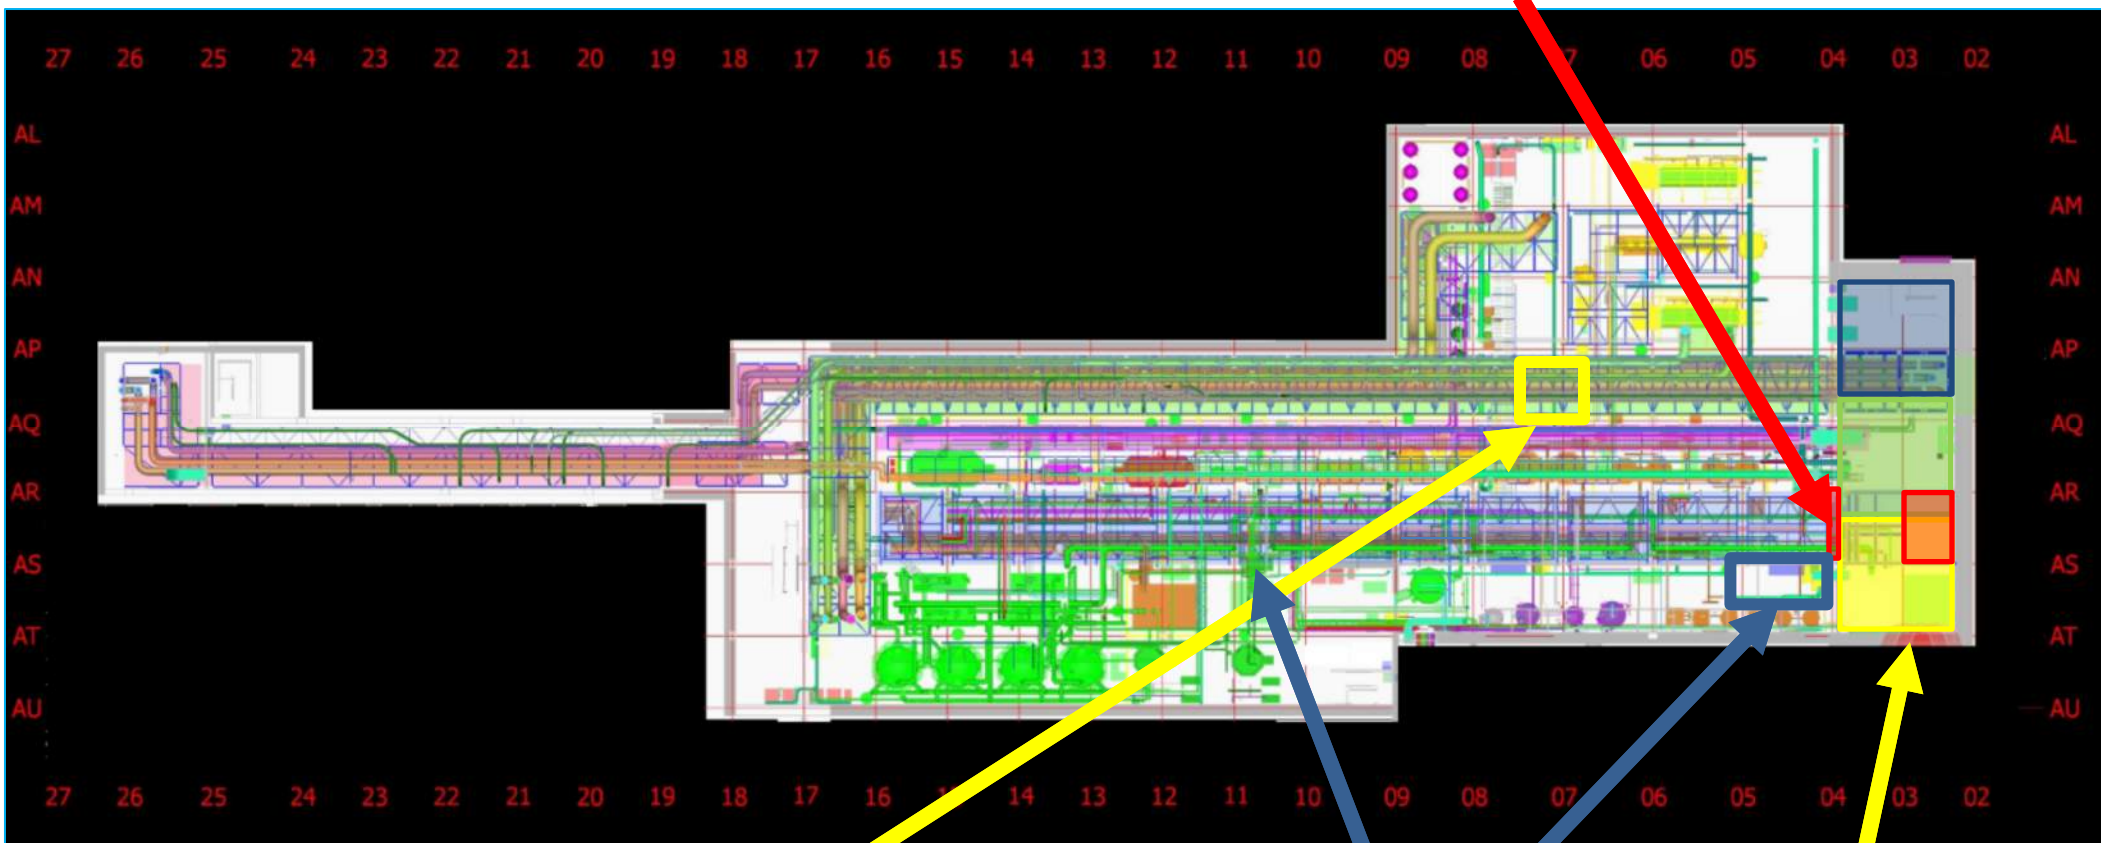

OH roll-up door
Install 30/1

CRC

HYG
Need to install SOG platform +
Bodice Grating ASAP

Topping slab Schedule


Pour 1 – 1/9 – 1/15 V
Pour 2 – 1/15 – 1/22 V
Pour 3 -1/22-1/27 V
Pour 4 – 1/28-2/4




HOFFMAN CONSTRUCTION COMPANY




SUT 38.2 LEVEL

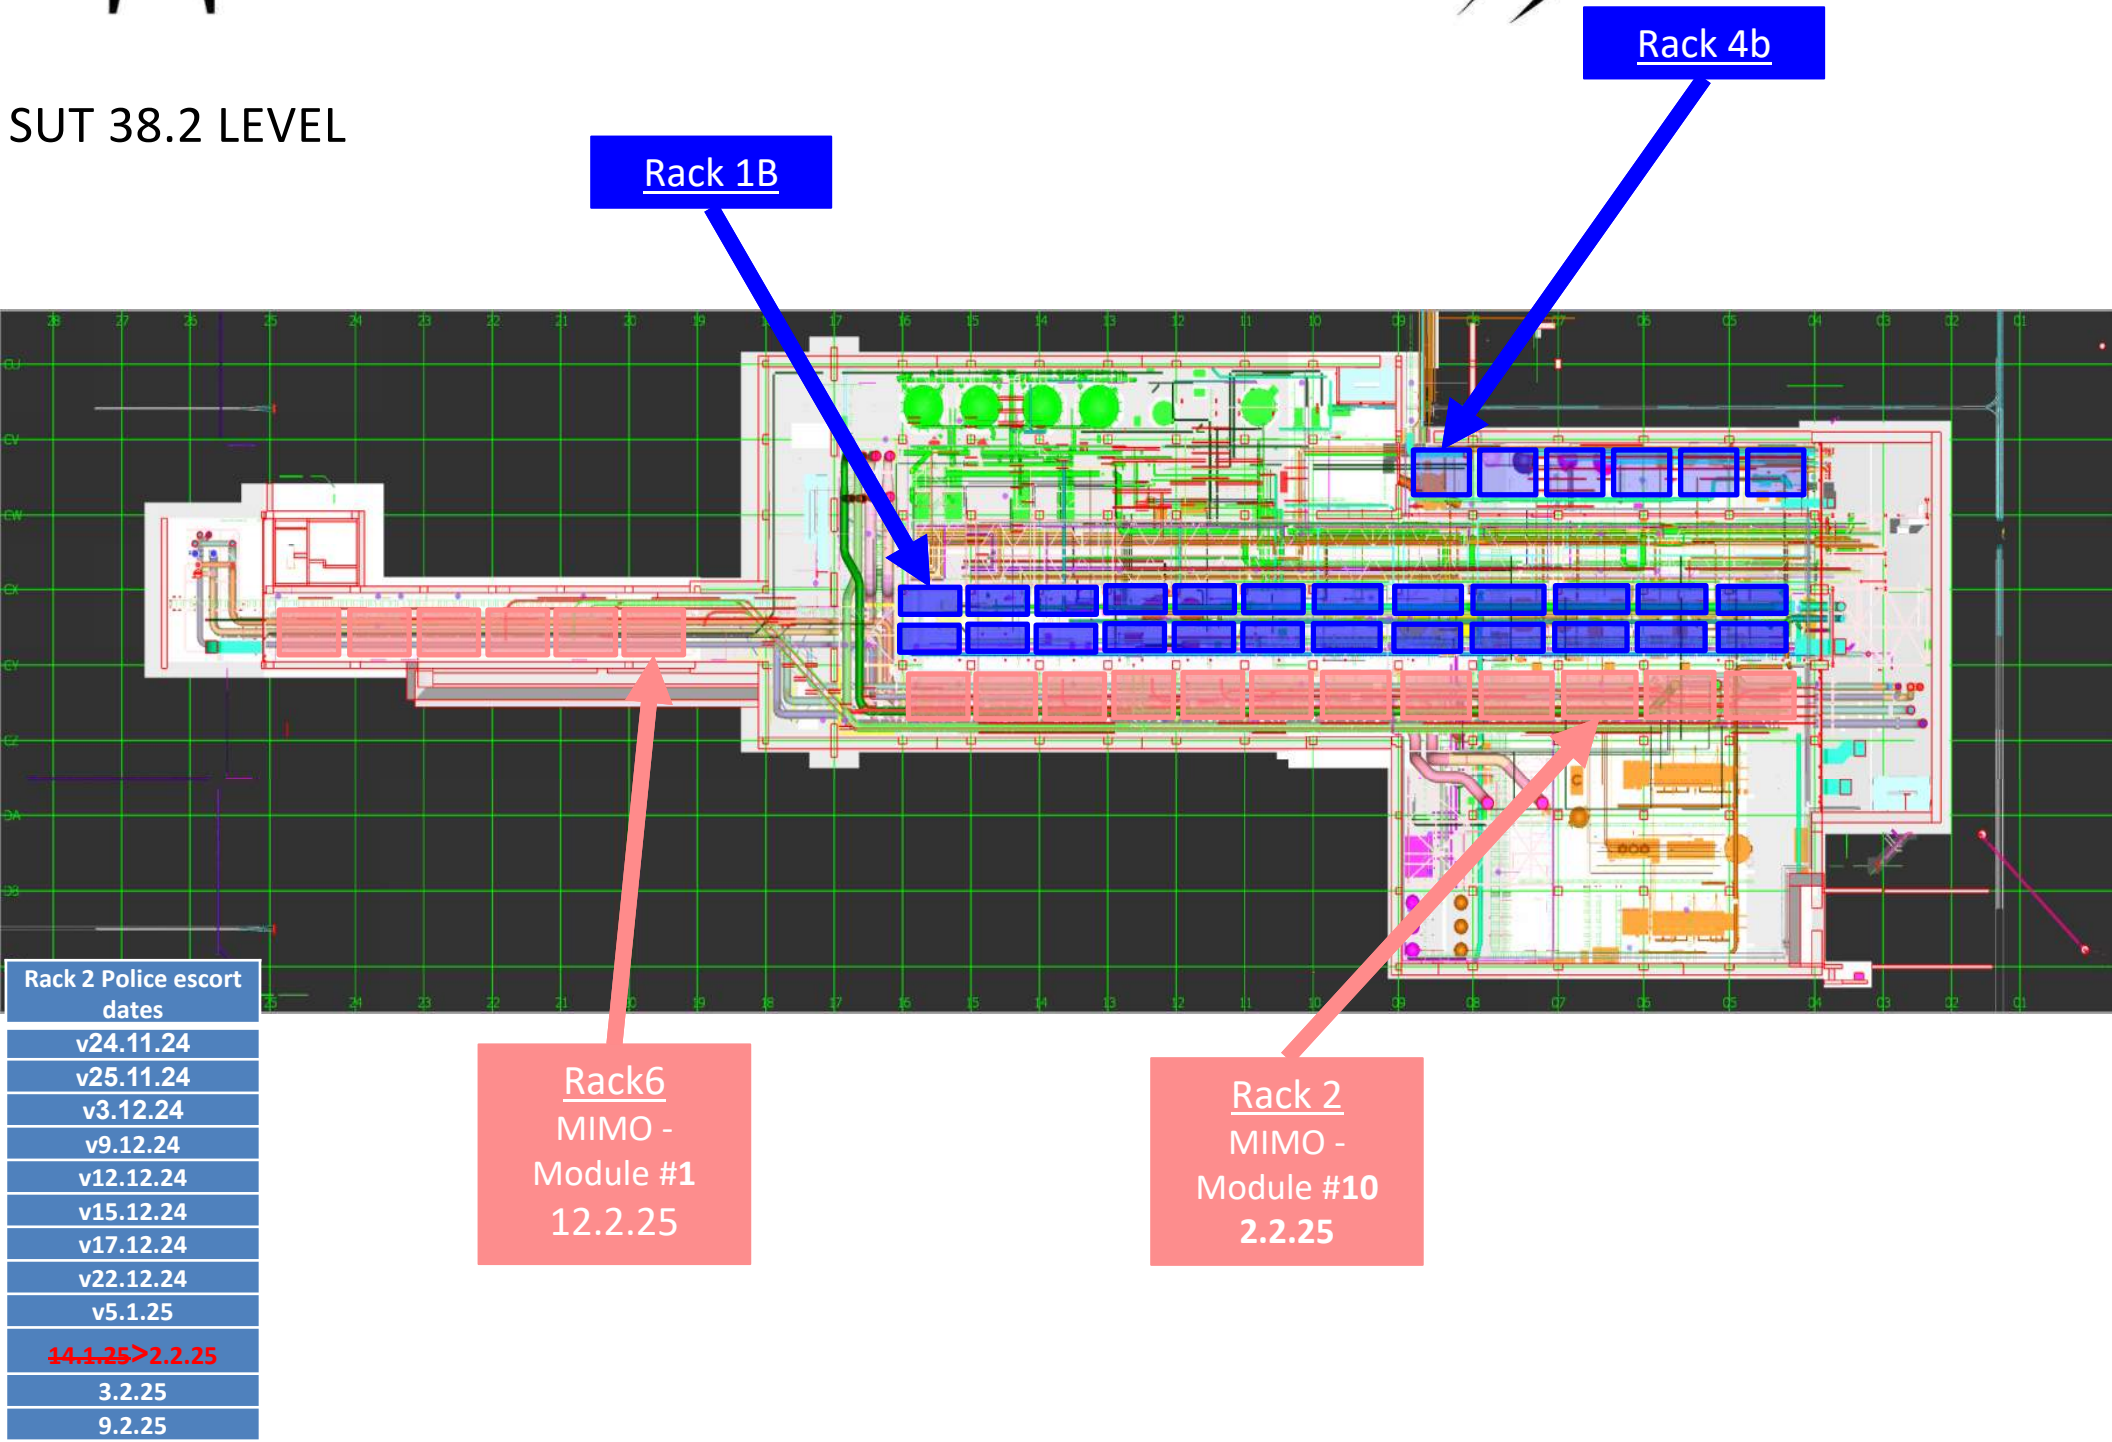


SUBFAB BUILDOUT MOD 1

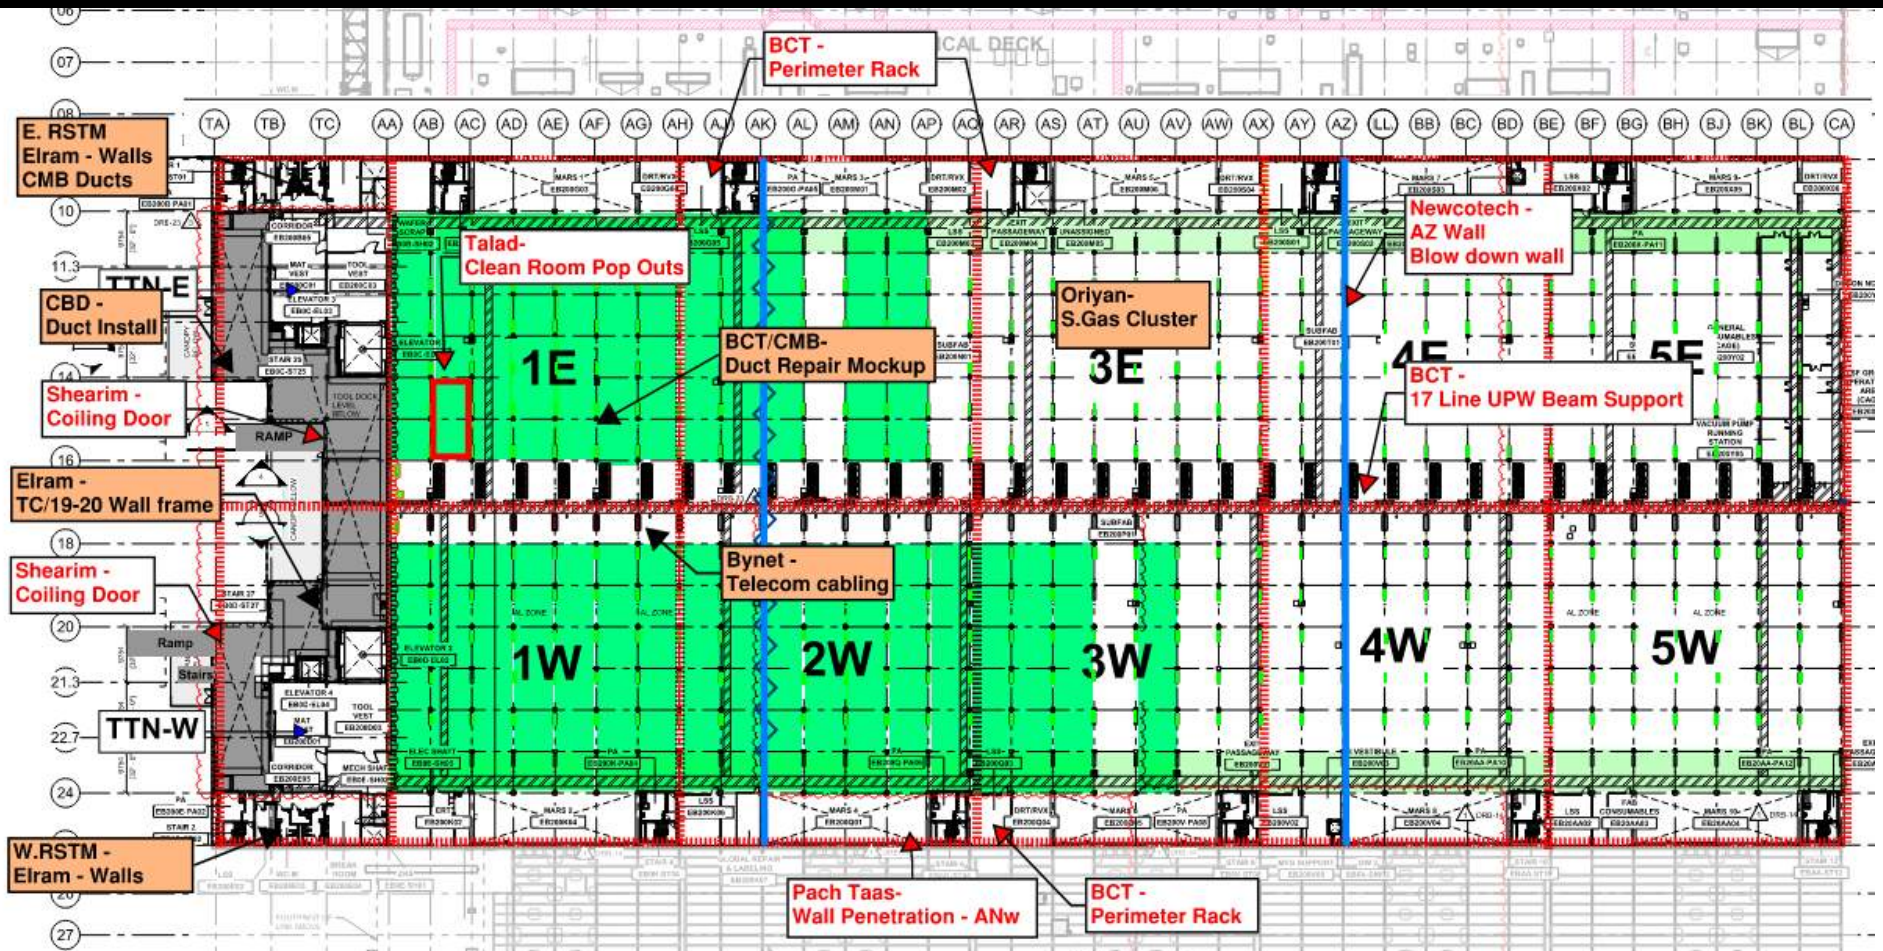


SUBFAB CRC TOPCOAT

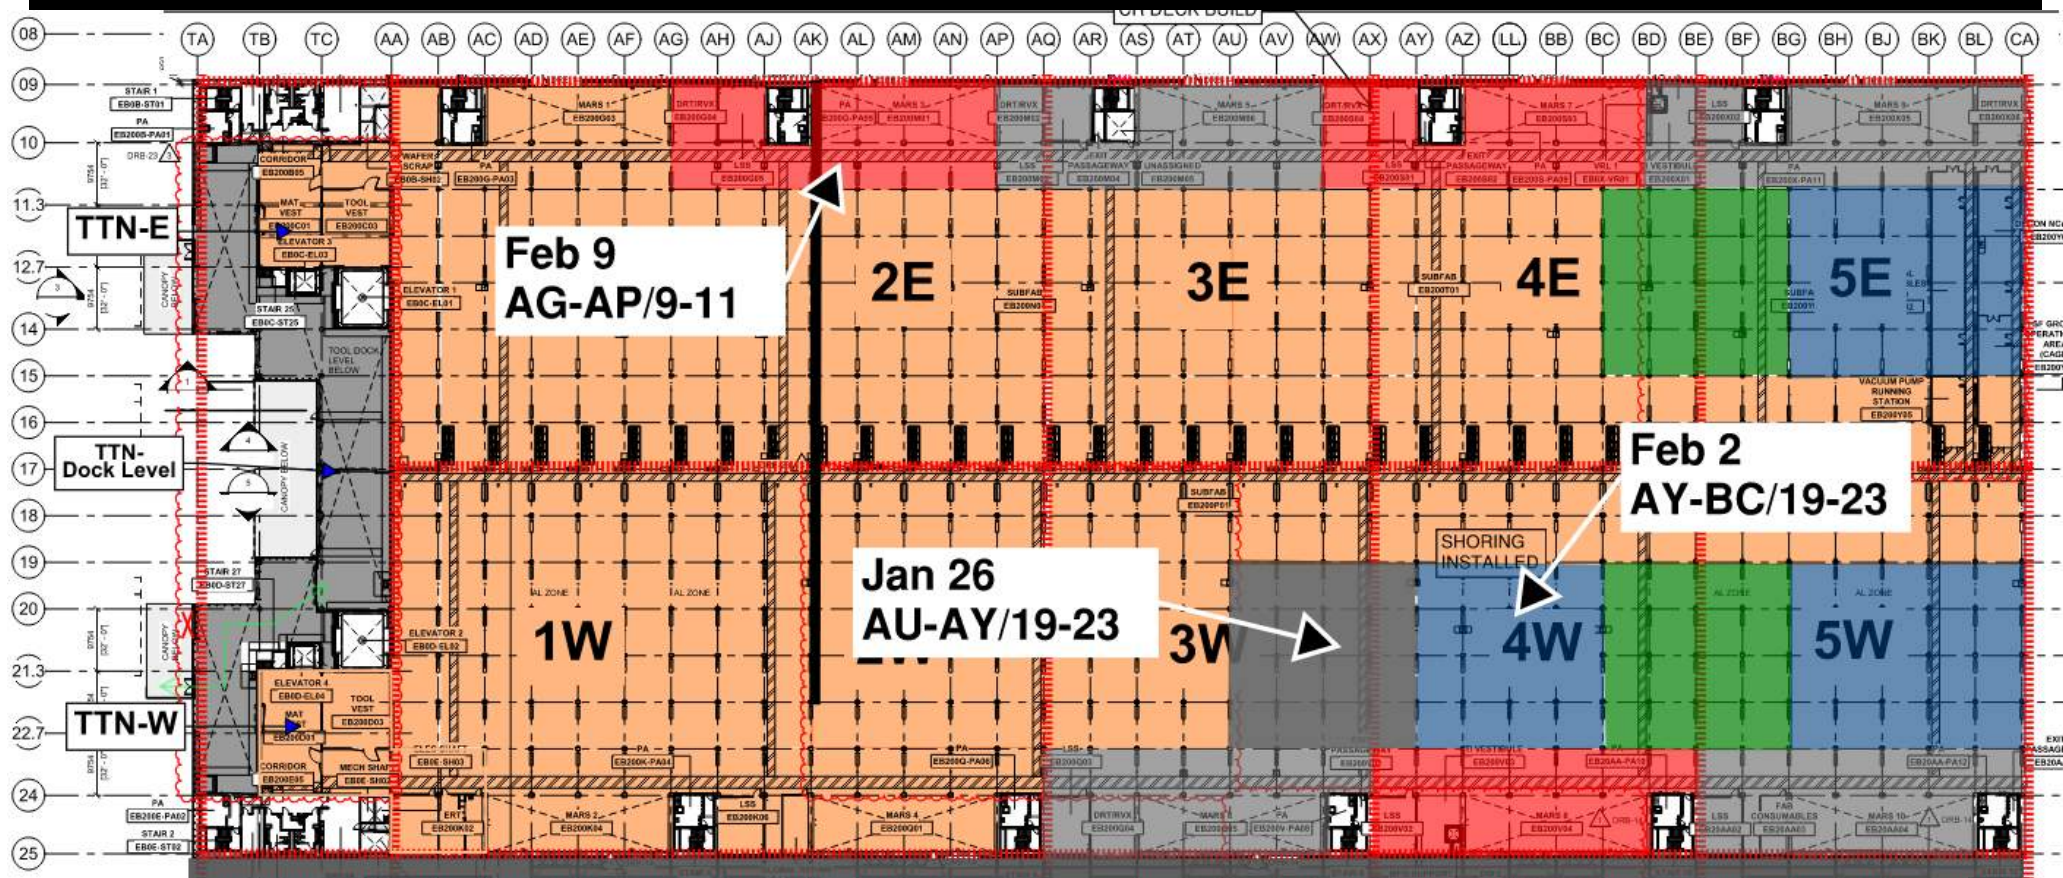


BCT Pressure Test Today

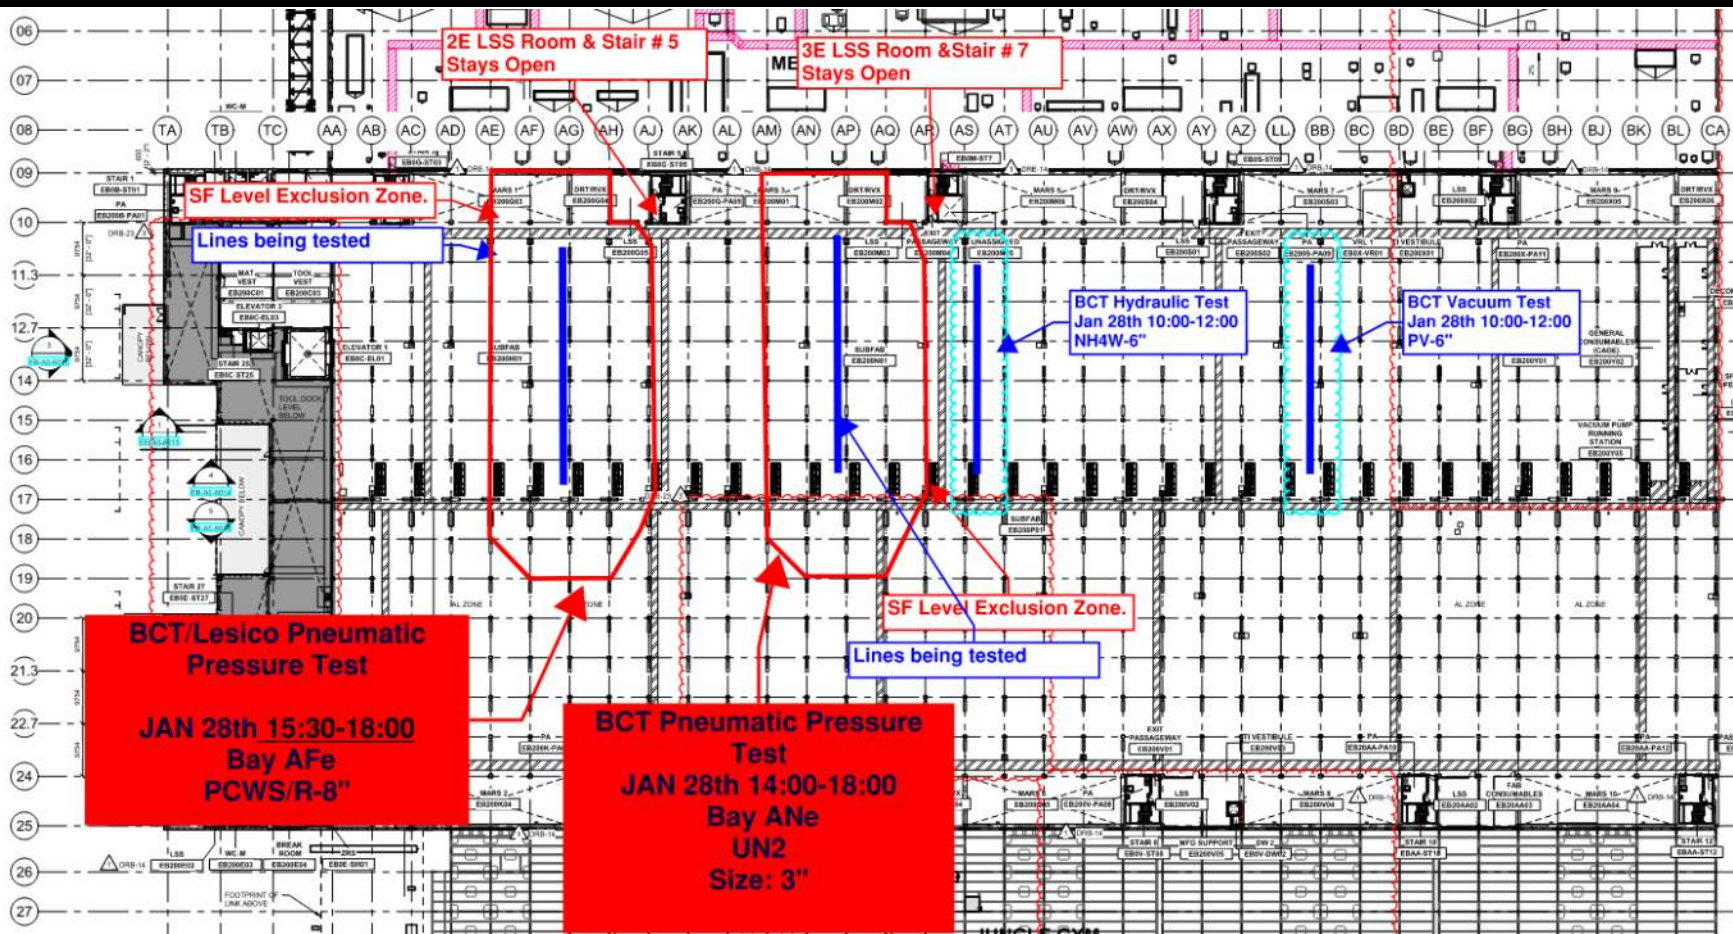



BCT Pressure Test Tomorrow

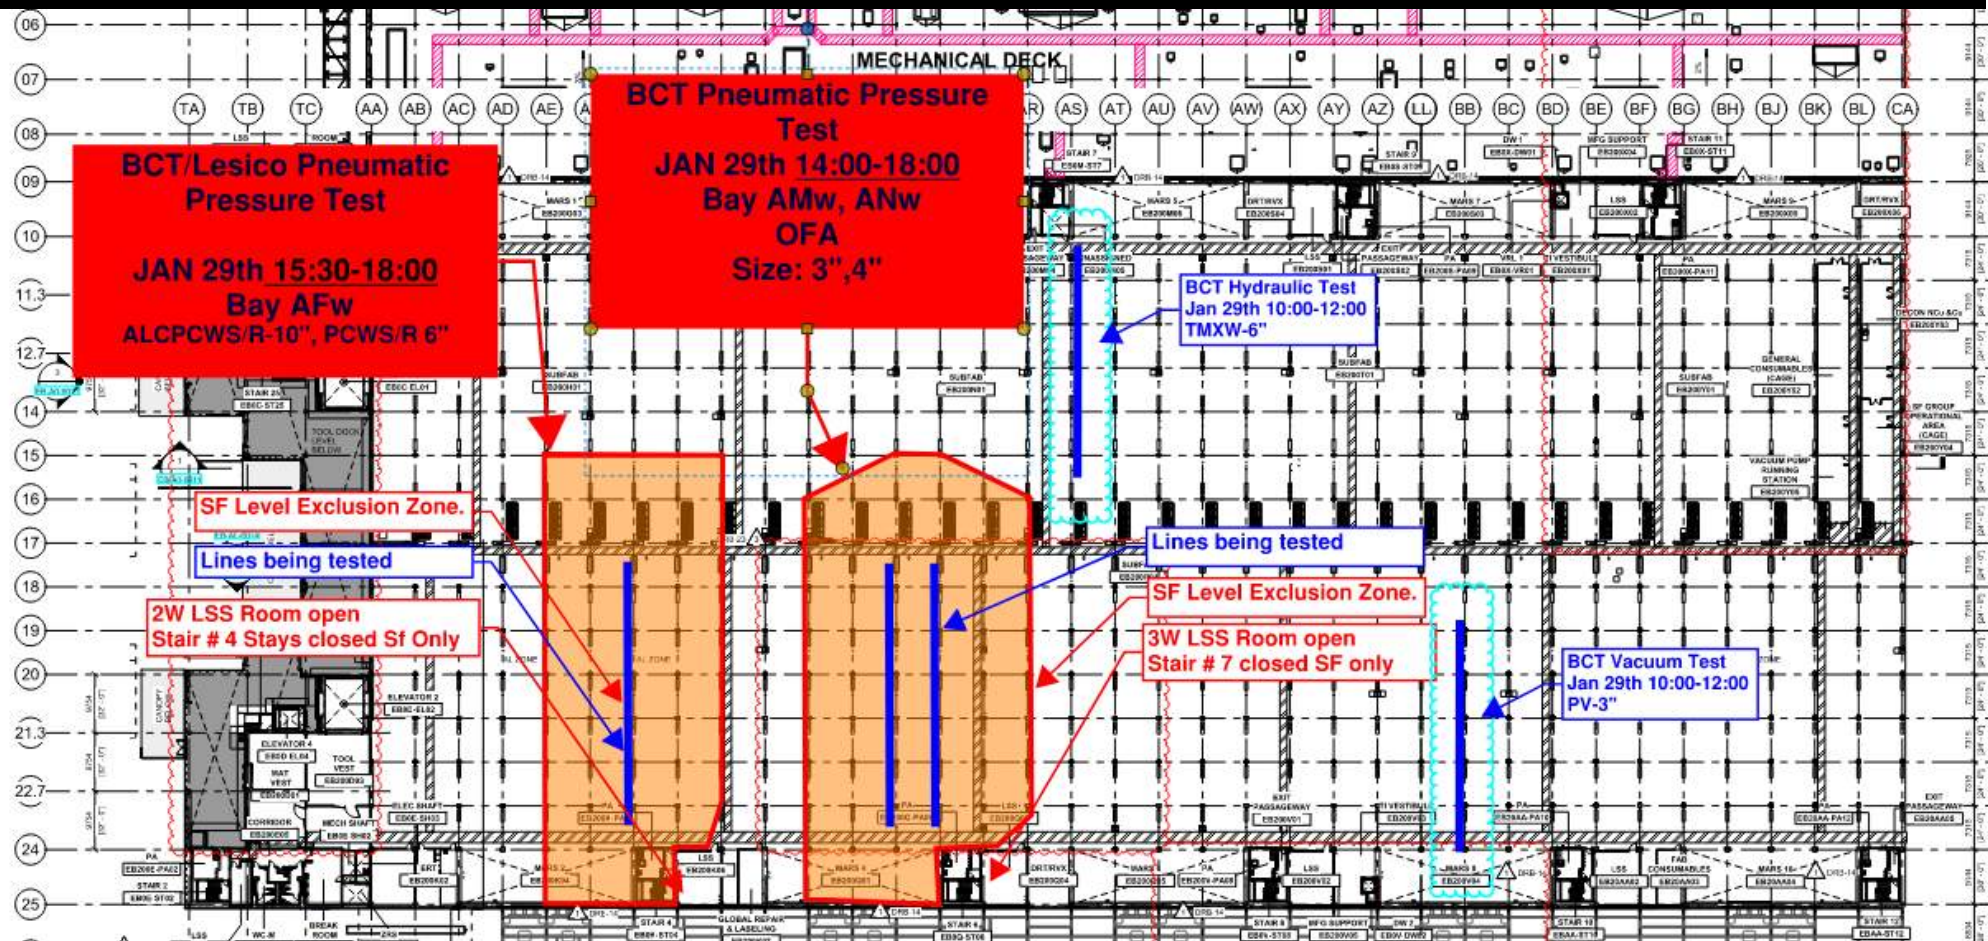


SUBFAB BUILDOUT MOD 2

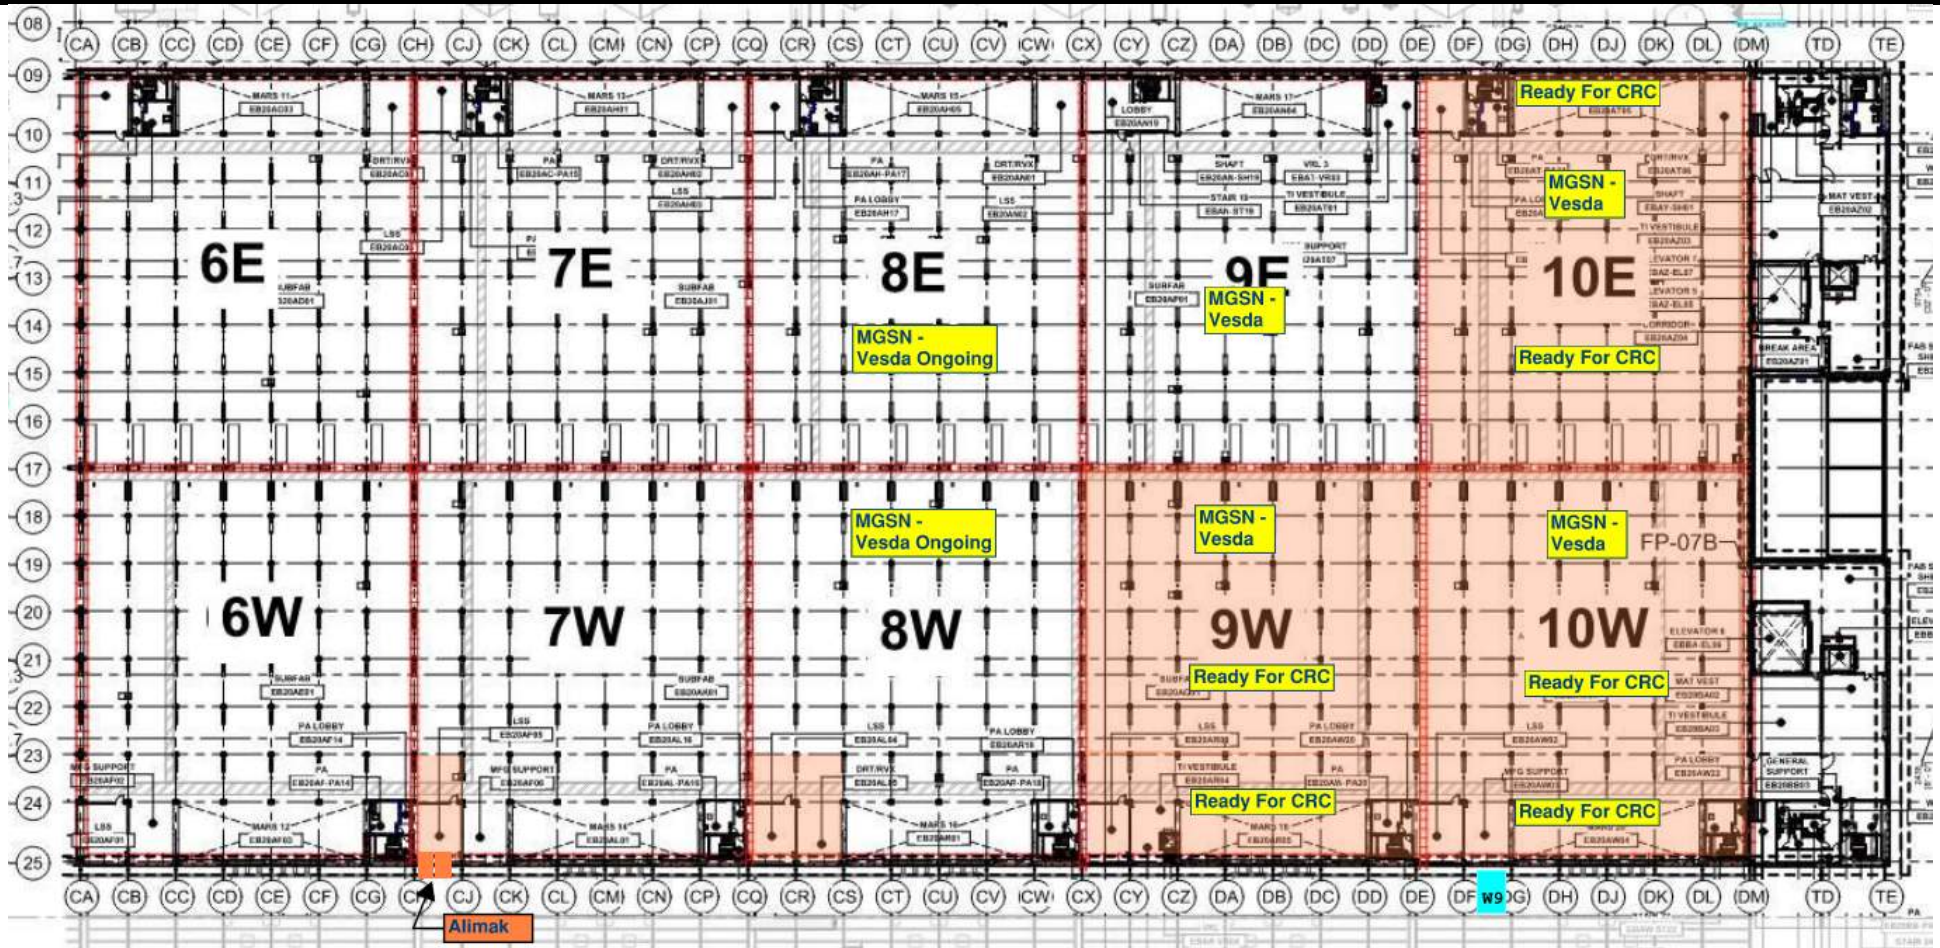

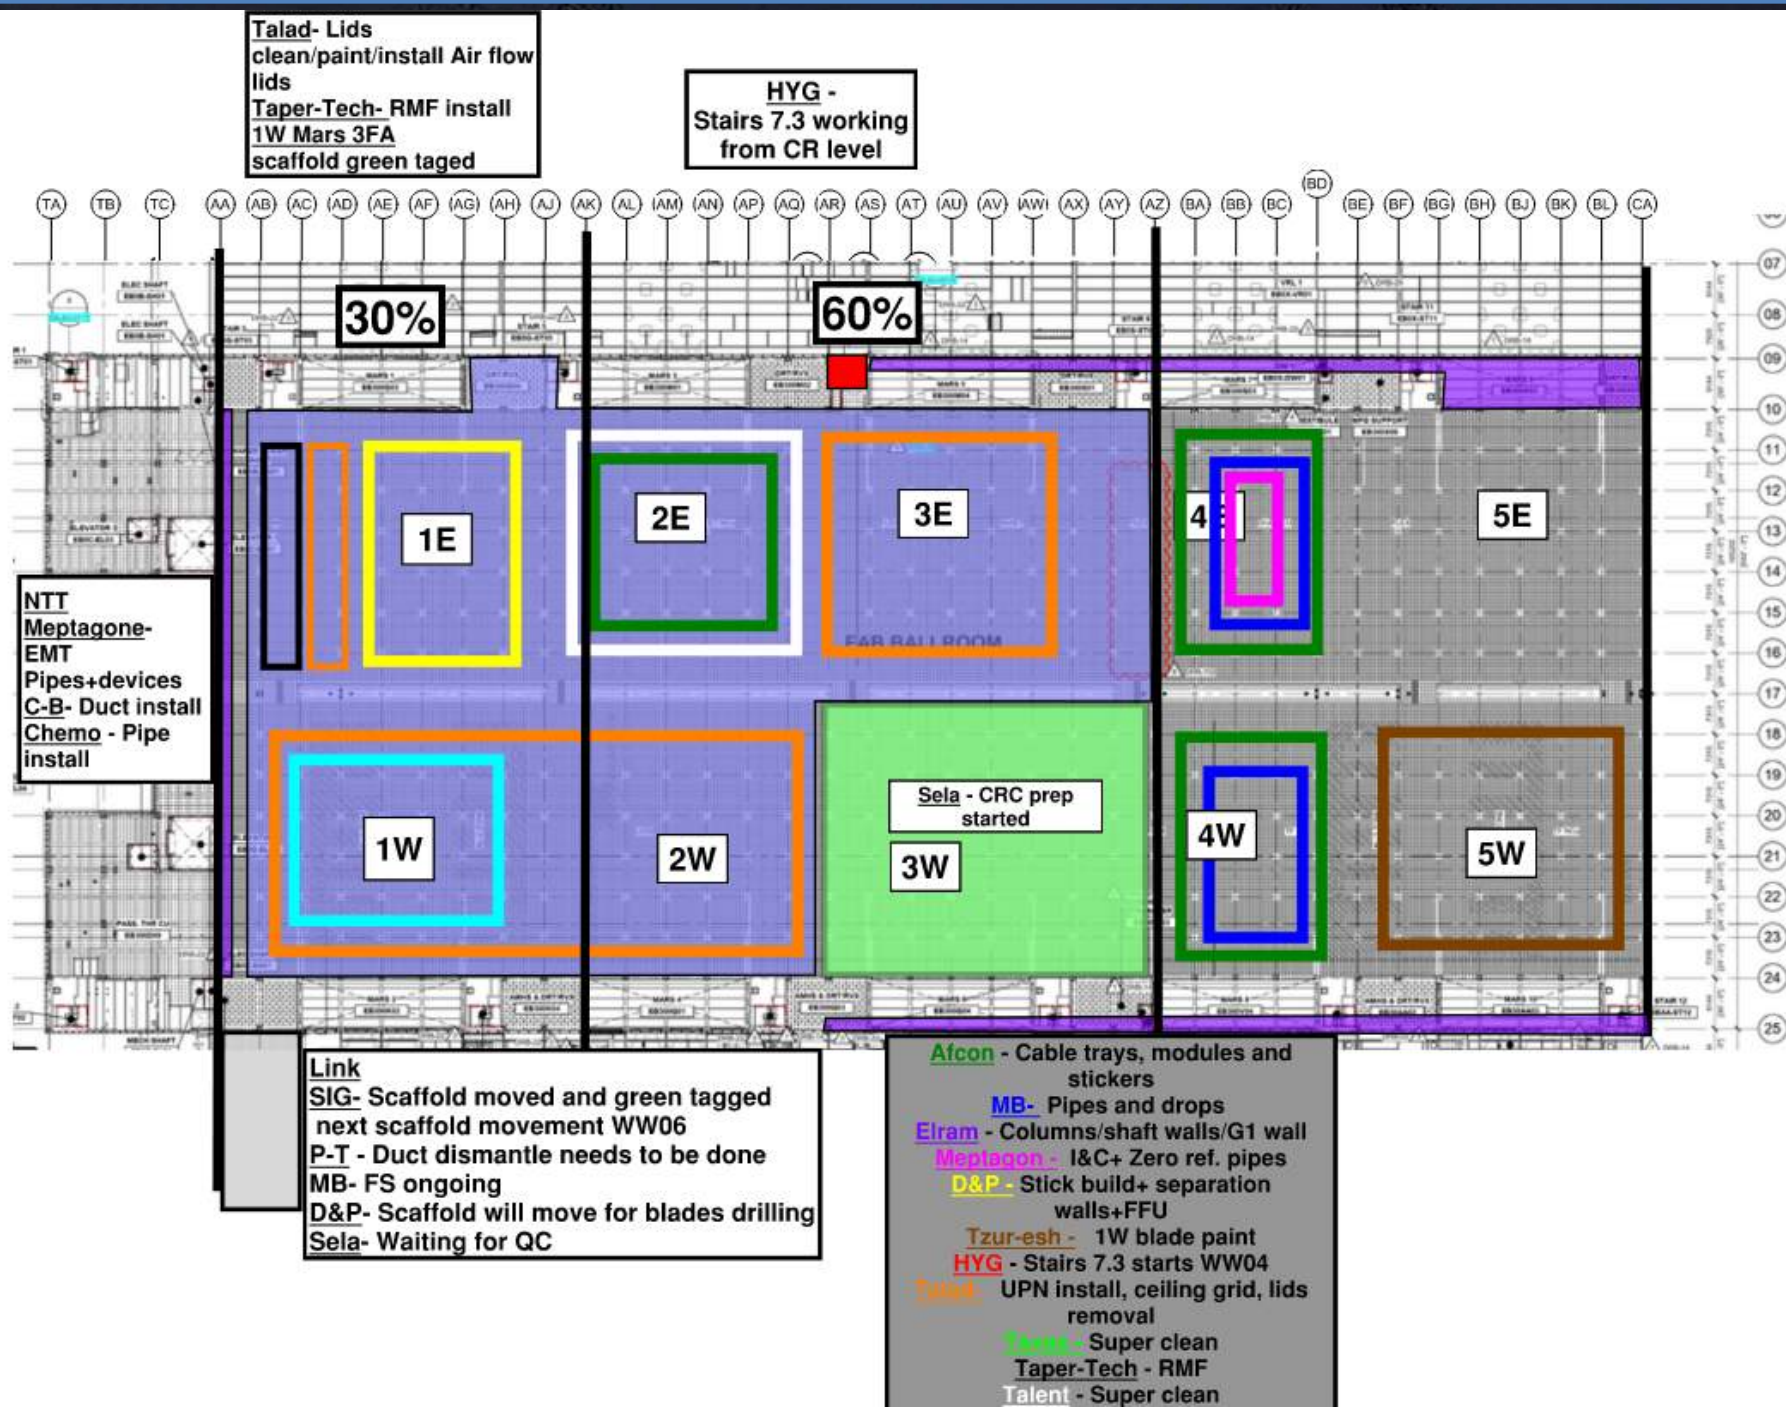

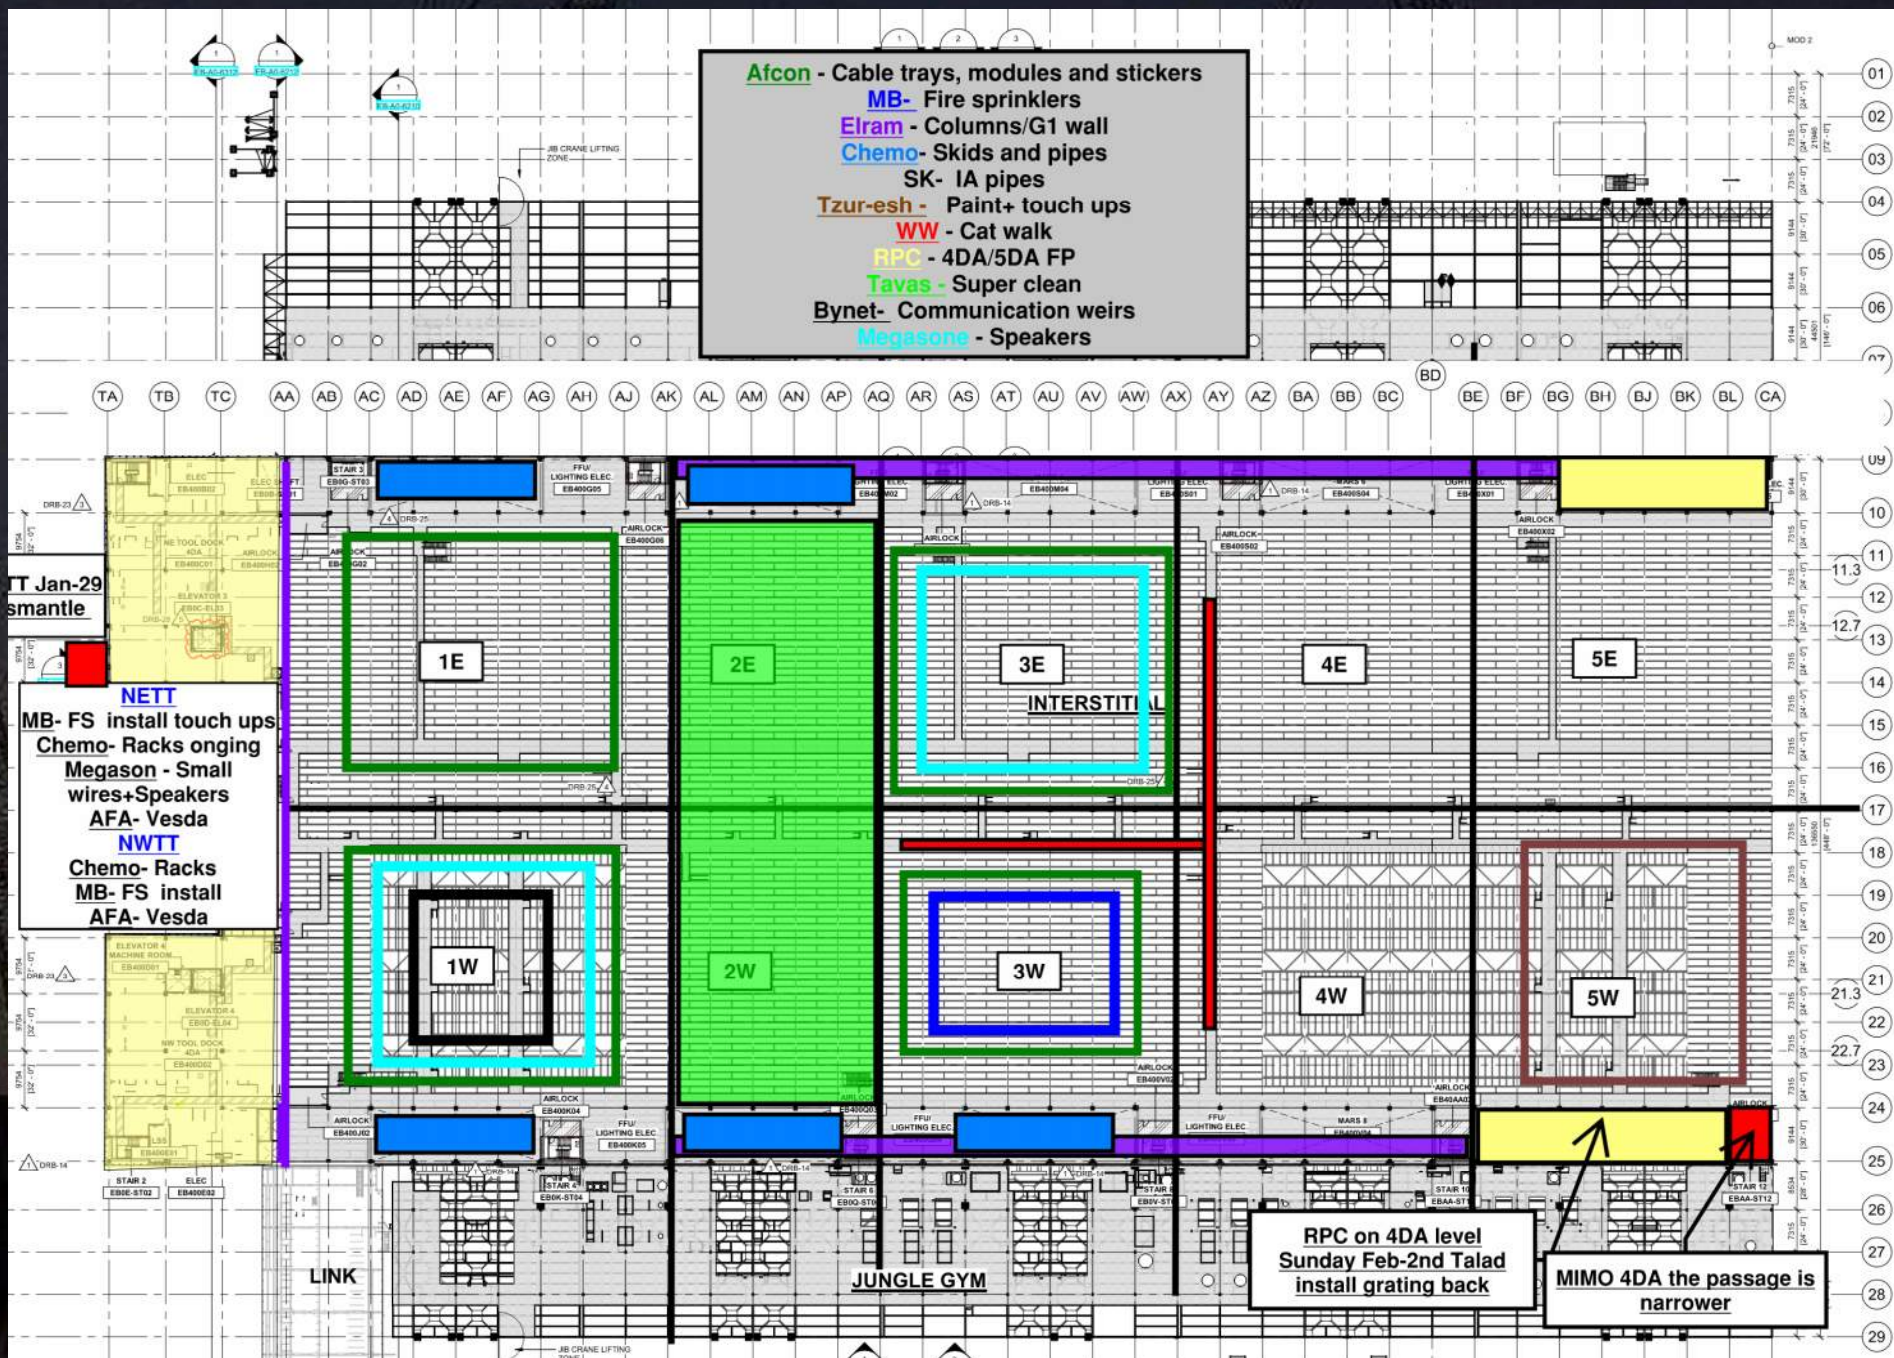


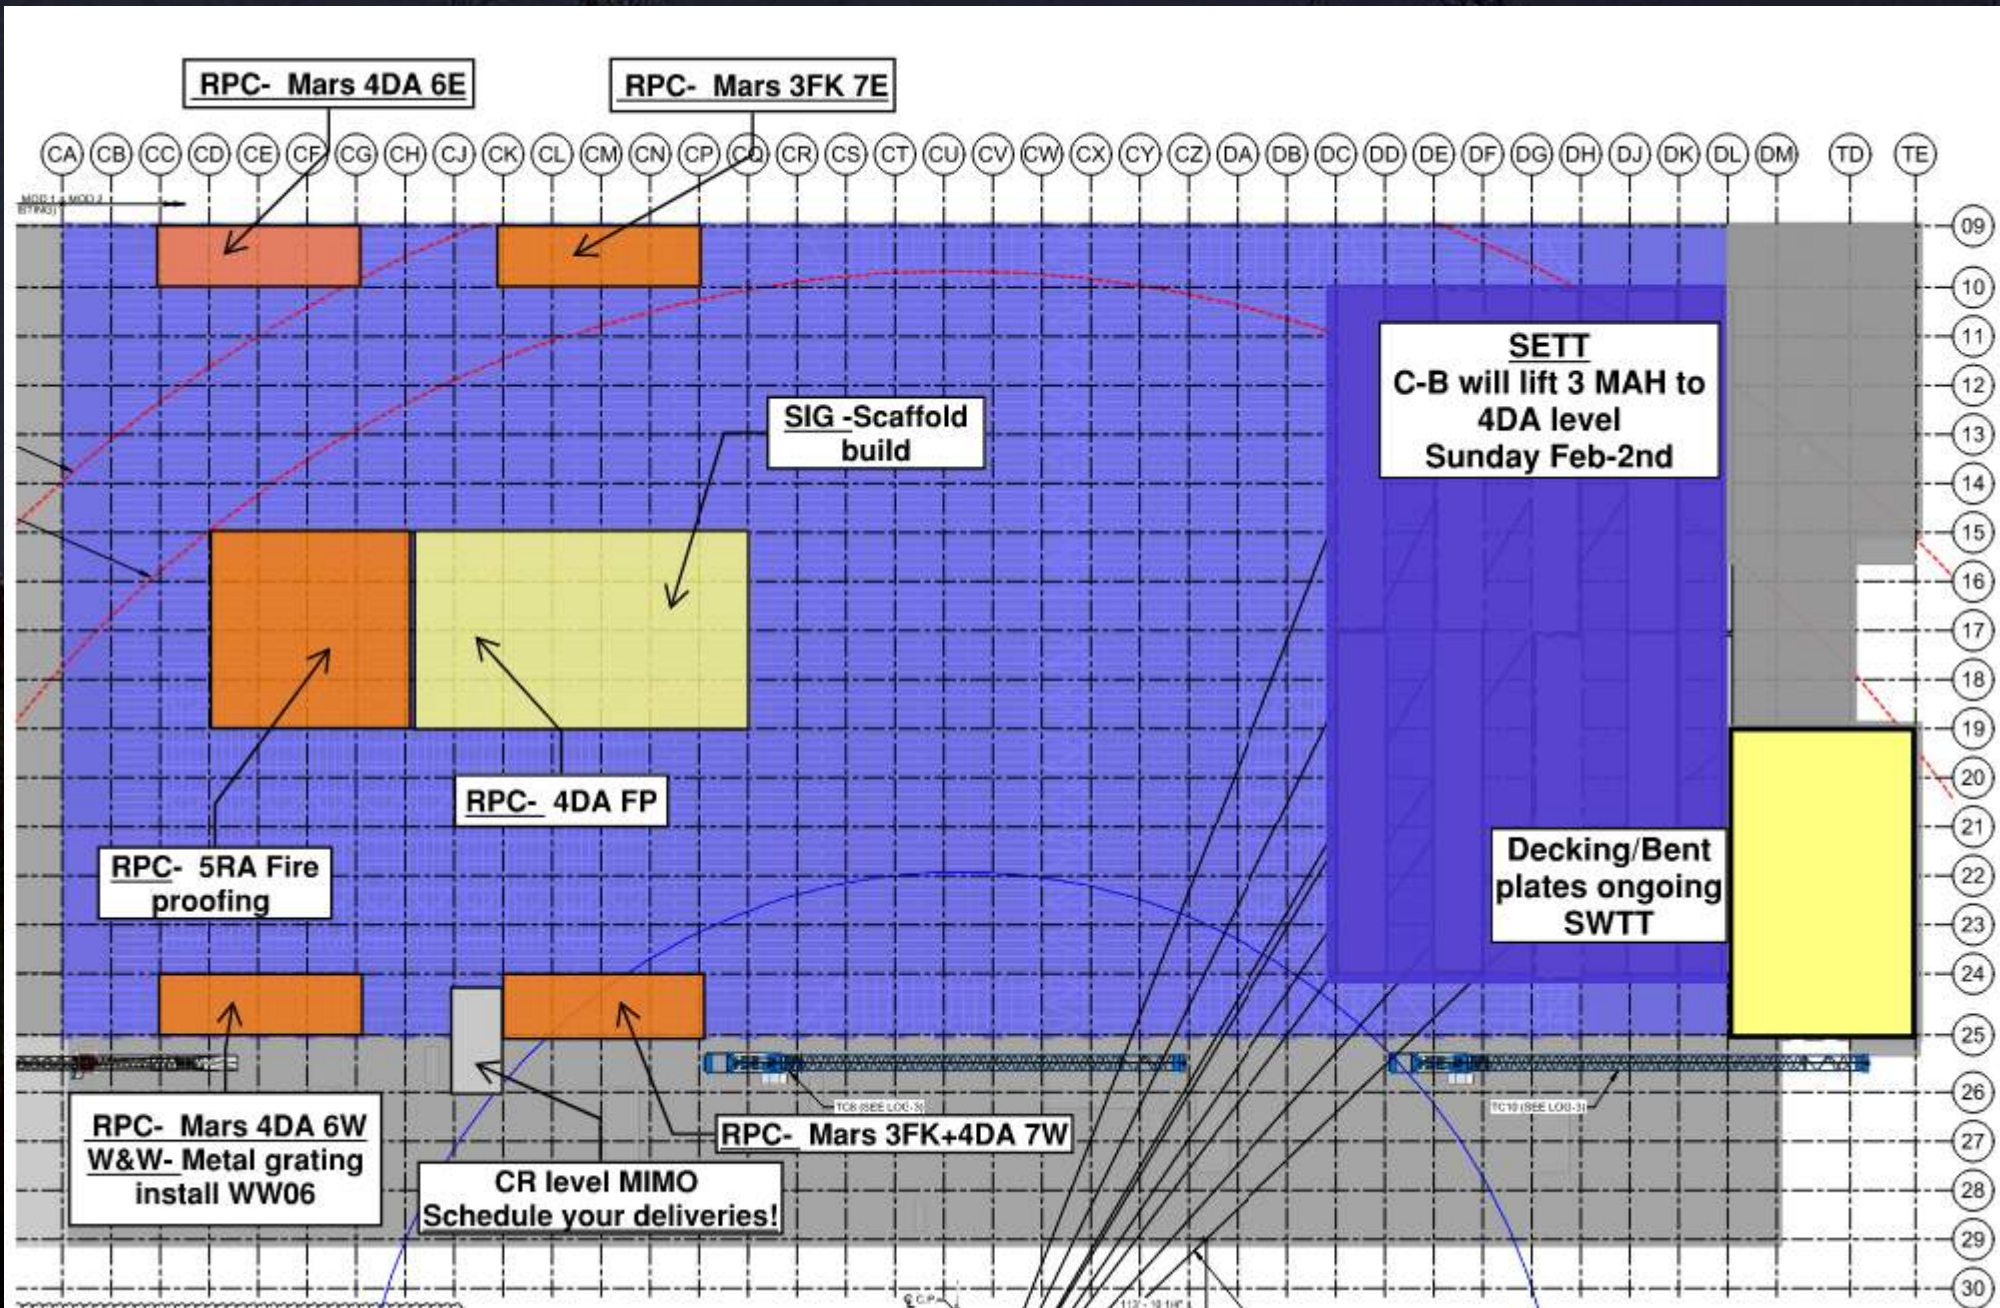



HOFFMAN CONSTRUCTION COMPANY



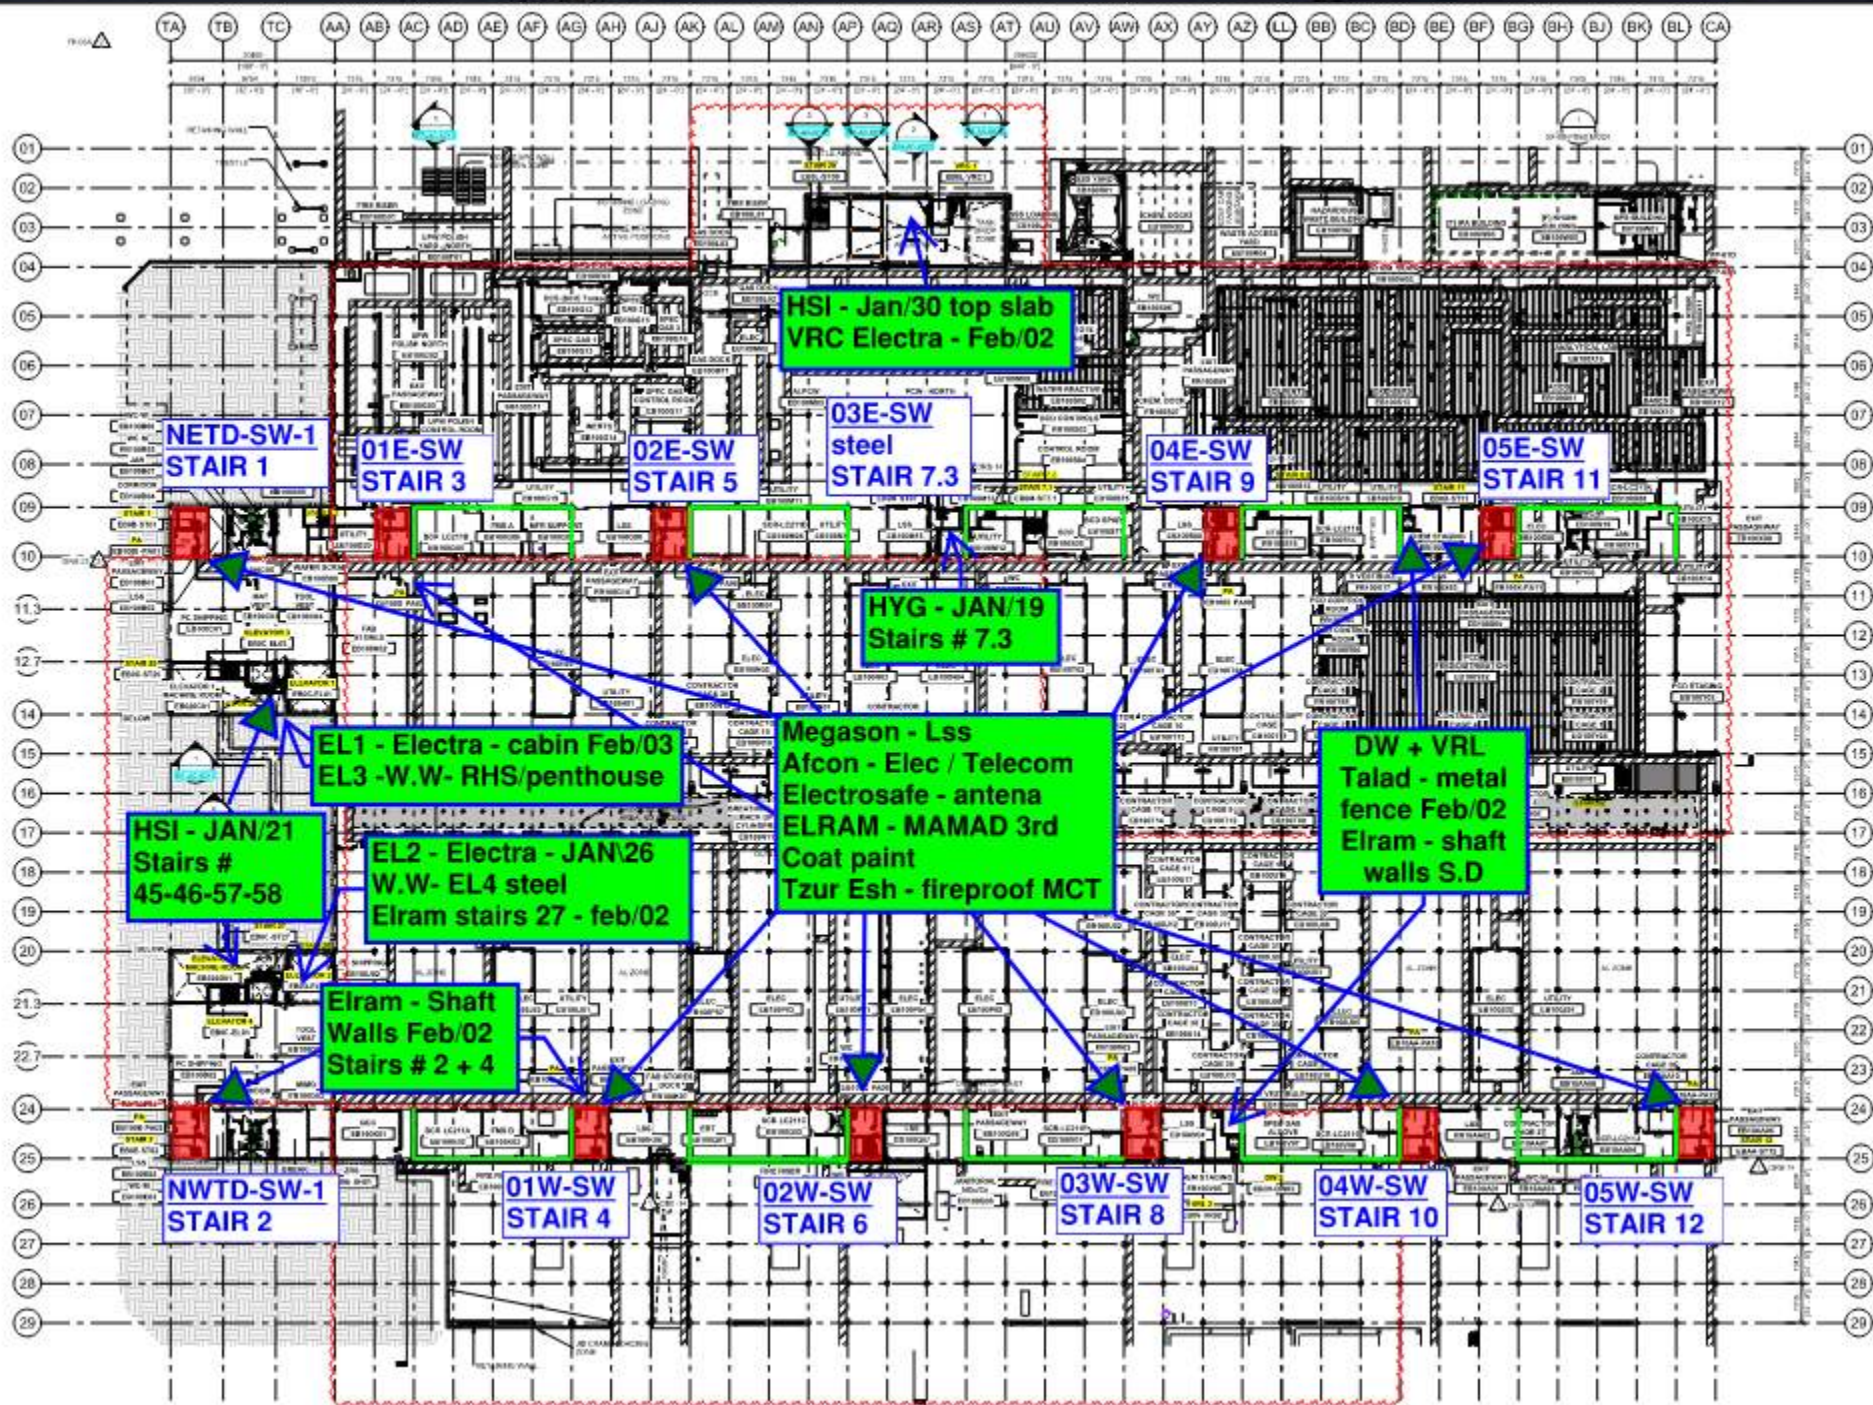

Siding - West FAB - JYG

BLOWDOWN 30%

	TA	TB	TC	AA	AB	AC	AD	AE	AF	AG	AH	AI	AK	AL	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BJ	BK	BL	CA																																					
	1001 / 1002			601 / 602		611 / 612			621 / 622			631 / 632			641 / 642			651 / 652			611 / 612			621 / 622			631 / 632			641 / 642			651 / 652																																												
	20	20	20	15	10	21	31	31	31	31	31	31	31	30	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31																																				
	20	20	27	15	10	21	31	31	31	31	31	31	31	30	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31																																				
	100%	100%	96%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%																																				
	Link																																								0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
0																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0					
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0				
																																									0	0	0	0	0	0	0	0	0	0	0	0	0	0																							

Link

LM BL BT BO BV BW BX BY BZ CA CB CC CD CE CF CG CH CI CJ CK CL CM CN CO CP CQ CR CS CT CU CV CW CX CY CZ DA DB DC DD DE DF DG DH DI DJ DK DL DM DN DO DP DQ DR DS DT DU DV DW DX DY DZ EA EB EC ED EE EF EG EH EI EJ EK EL EM EN EO EP EQ ER ES ET EU EV EW EX EY EZ FA FB FC FD FE FF FG FH FI FJ FK FL FM FN FO FP FQ FR FS FT FU FV FW FX FY FZ GA GB GC GD GE GF GH GI GJ GK GL GM GN GO GP GQ GR GS GT GU GV GW GX GY GZ HA HB HC HD HE HF HG HH HI HJ HK HL HM HN HO HP HQ HR HS HT HU HV HW HX HY HZ IA IB IC ID IE IF IG IH II IJ IK IL IM IN IO IP IQ IR IS IT IU IV IW IX IY IZ JA JB JC JD JE JF JG JH JI JJ JK JL JM JN JO JP JQ JR JS JT JU JV JW JX JY JZ KA KB KC KD KE KF KH KI KJ KL KM KN KO KP KQ KR KS KT KU KV KW KX KY KZ LA LB LC LD LE LF LH LI LJ LK LL LM LN LO LP LQ LR LS LT LU LV LW LX LY LZ MA MB MC MD ME MF MH MI MJ MK ML MN MO MP MQ MR MS MT MU MV MW MX MY MZ NA NB NC ND NE NF NH NI NJ NK NL NM NO NP NQ NR NS NT NU NV NW NX NY NZ OA OB OC OD OE OF OH OI OJ OK OL OM ON OP OQ OR OS OT OU OV OW OX OY OZ PA PB PC PD PE PF PH PI PJ PK PL PM PN PO PP PQ PR PS PT PU PV PW PX PY PZ QA QB QC QD QE QF QH QI QJ QK QL QM QN QO QQ QR QS QT QU QV QW QX QY QZ RA RB RC RD RE RF RH RI RJ RK RL RM RN RO RP RQ RR RS RT RU RV RW RX RY RZ SA SB SC SD SE SF SH SI SJ SK SL SM SN SO SP SQ SR SS ST SU SV SW SX SY SZ TA TB TC TD TE TF TH TI TJ TK TL TM TN TO TP TQ TR TS TT TU TV TW TX TY TZ UA UB UC UD UE UF UH UI UJ UK UL UM UN UO UQ UR US UT UV UW UX UY UZ VA VB VC VD VE VF VH VI VJ VK VL VM VN VO VQ VR VS VT VU VW VX VY VZ WA WB WC WD WE WF WH WI WJ WK WL WM WN WO WP WQ WR WS WT WU WV WW WX WY WZ XA XB XC XD XE XF XH XI XJ XK XL XM XN XO XP XQ XR XS XT XU XV XW XX XY XZ YA YB YC YD YE YF YH YI YJ YK YL YM YN YO YQ YR YS YT YU YV YW YX YY YZ ZA ZB ZC ZD ZE ZF ZH ZI ZJ ZK ZL ZM ZN ZO ZP ZQ ZR ZS ZT ZU ZV ZW ZX ZY ZZ

Siding - East FAB - PSSS

BLOWDOWN 30%

OF - 172166.0

CK - 167798.0

Q 16'-1" - 162,037.0

1 - 156,825.2


150,349.064

B - 143,433.6

CK - 147,700.0

T - 145,647.2

DEMO

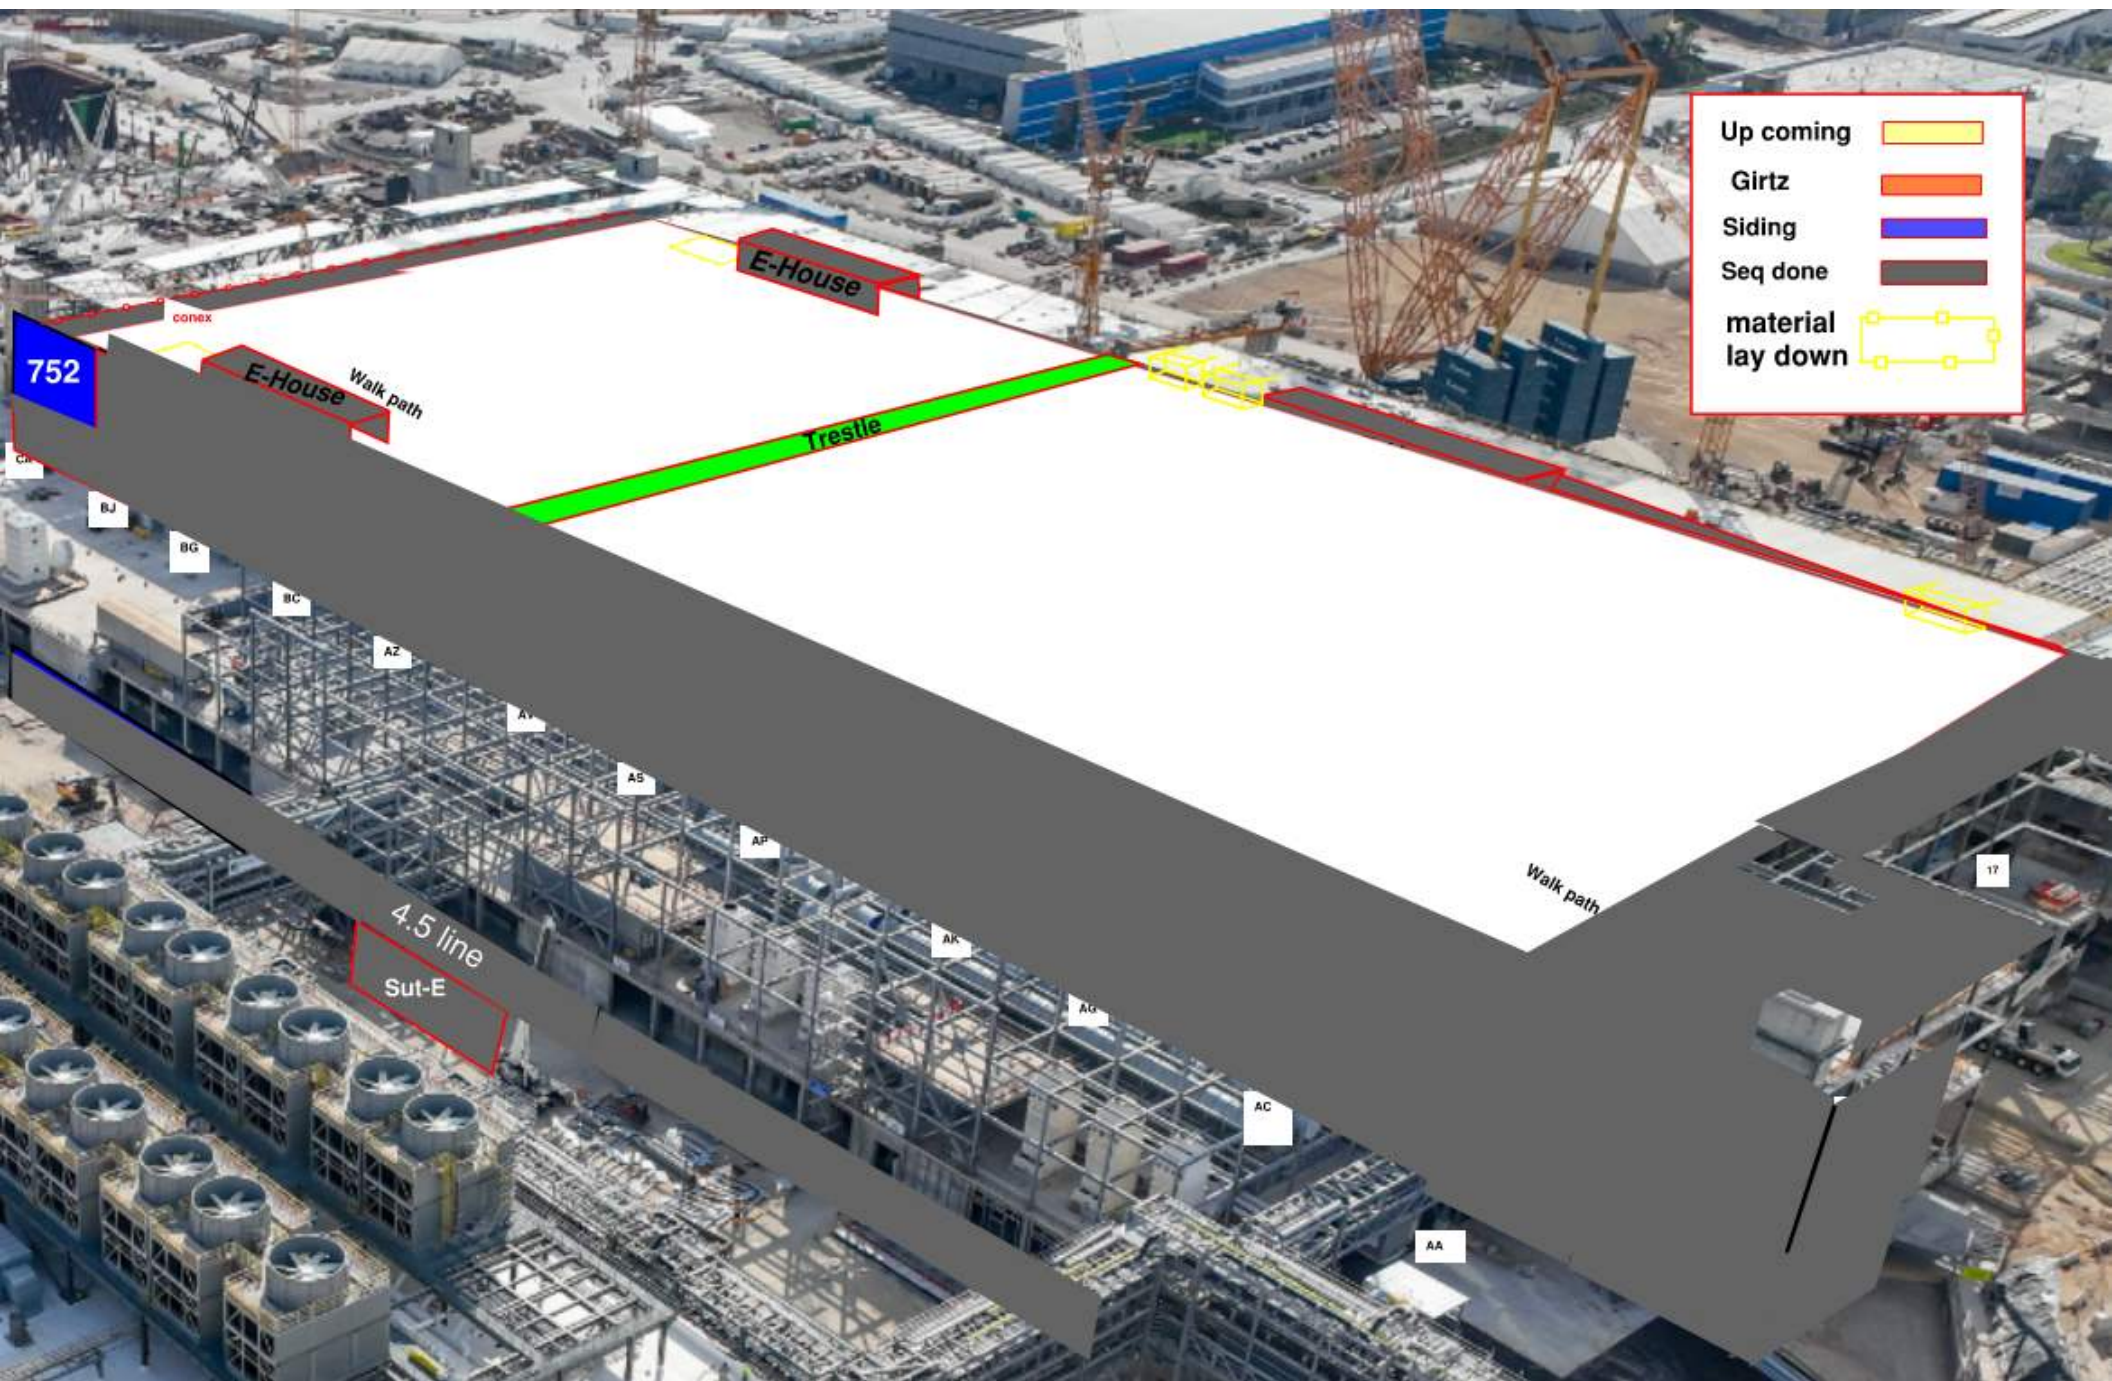

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

752

E-House

E-House

Trestle

Walk path

Walk path

4.5 line
Sut-E

BJ

BG

BC

AZ

AV

AS

AP


AK

AG

AC

AA

17

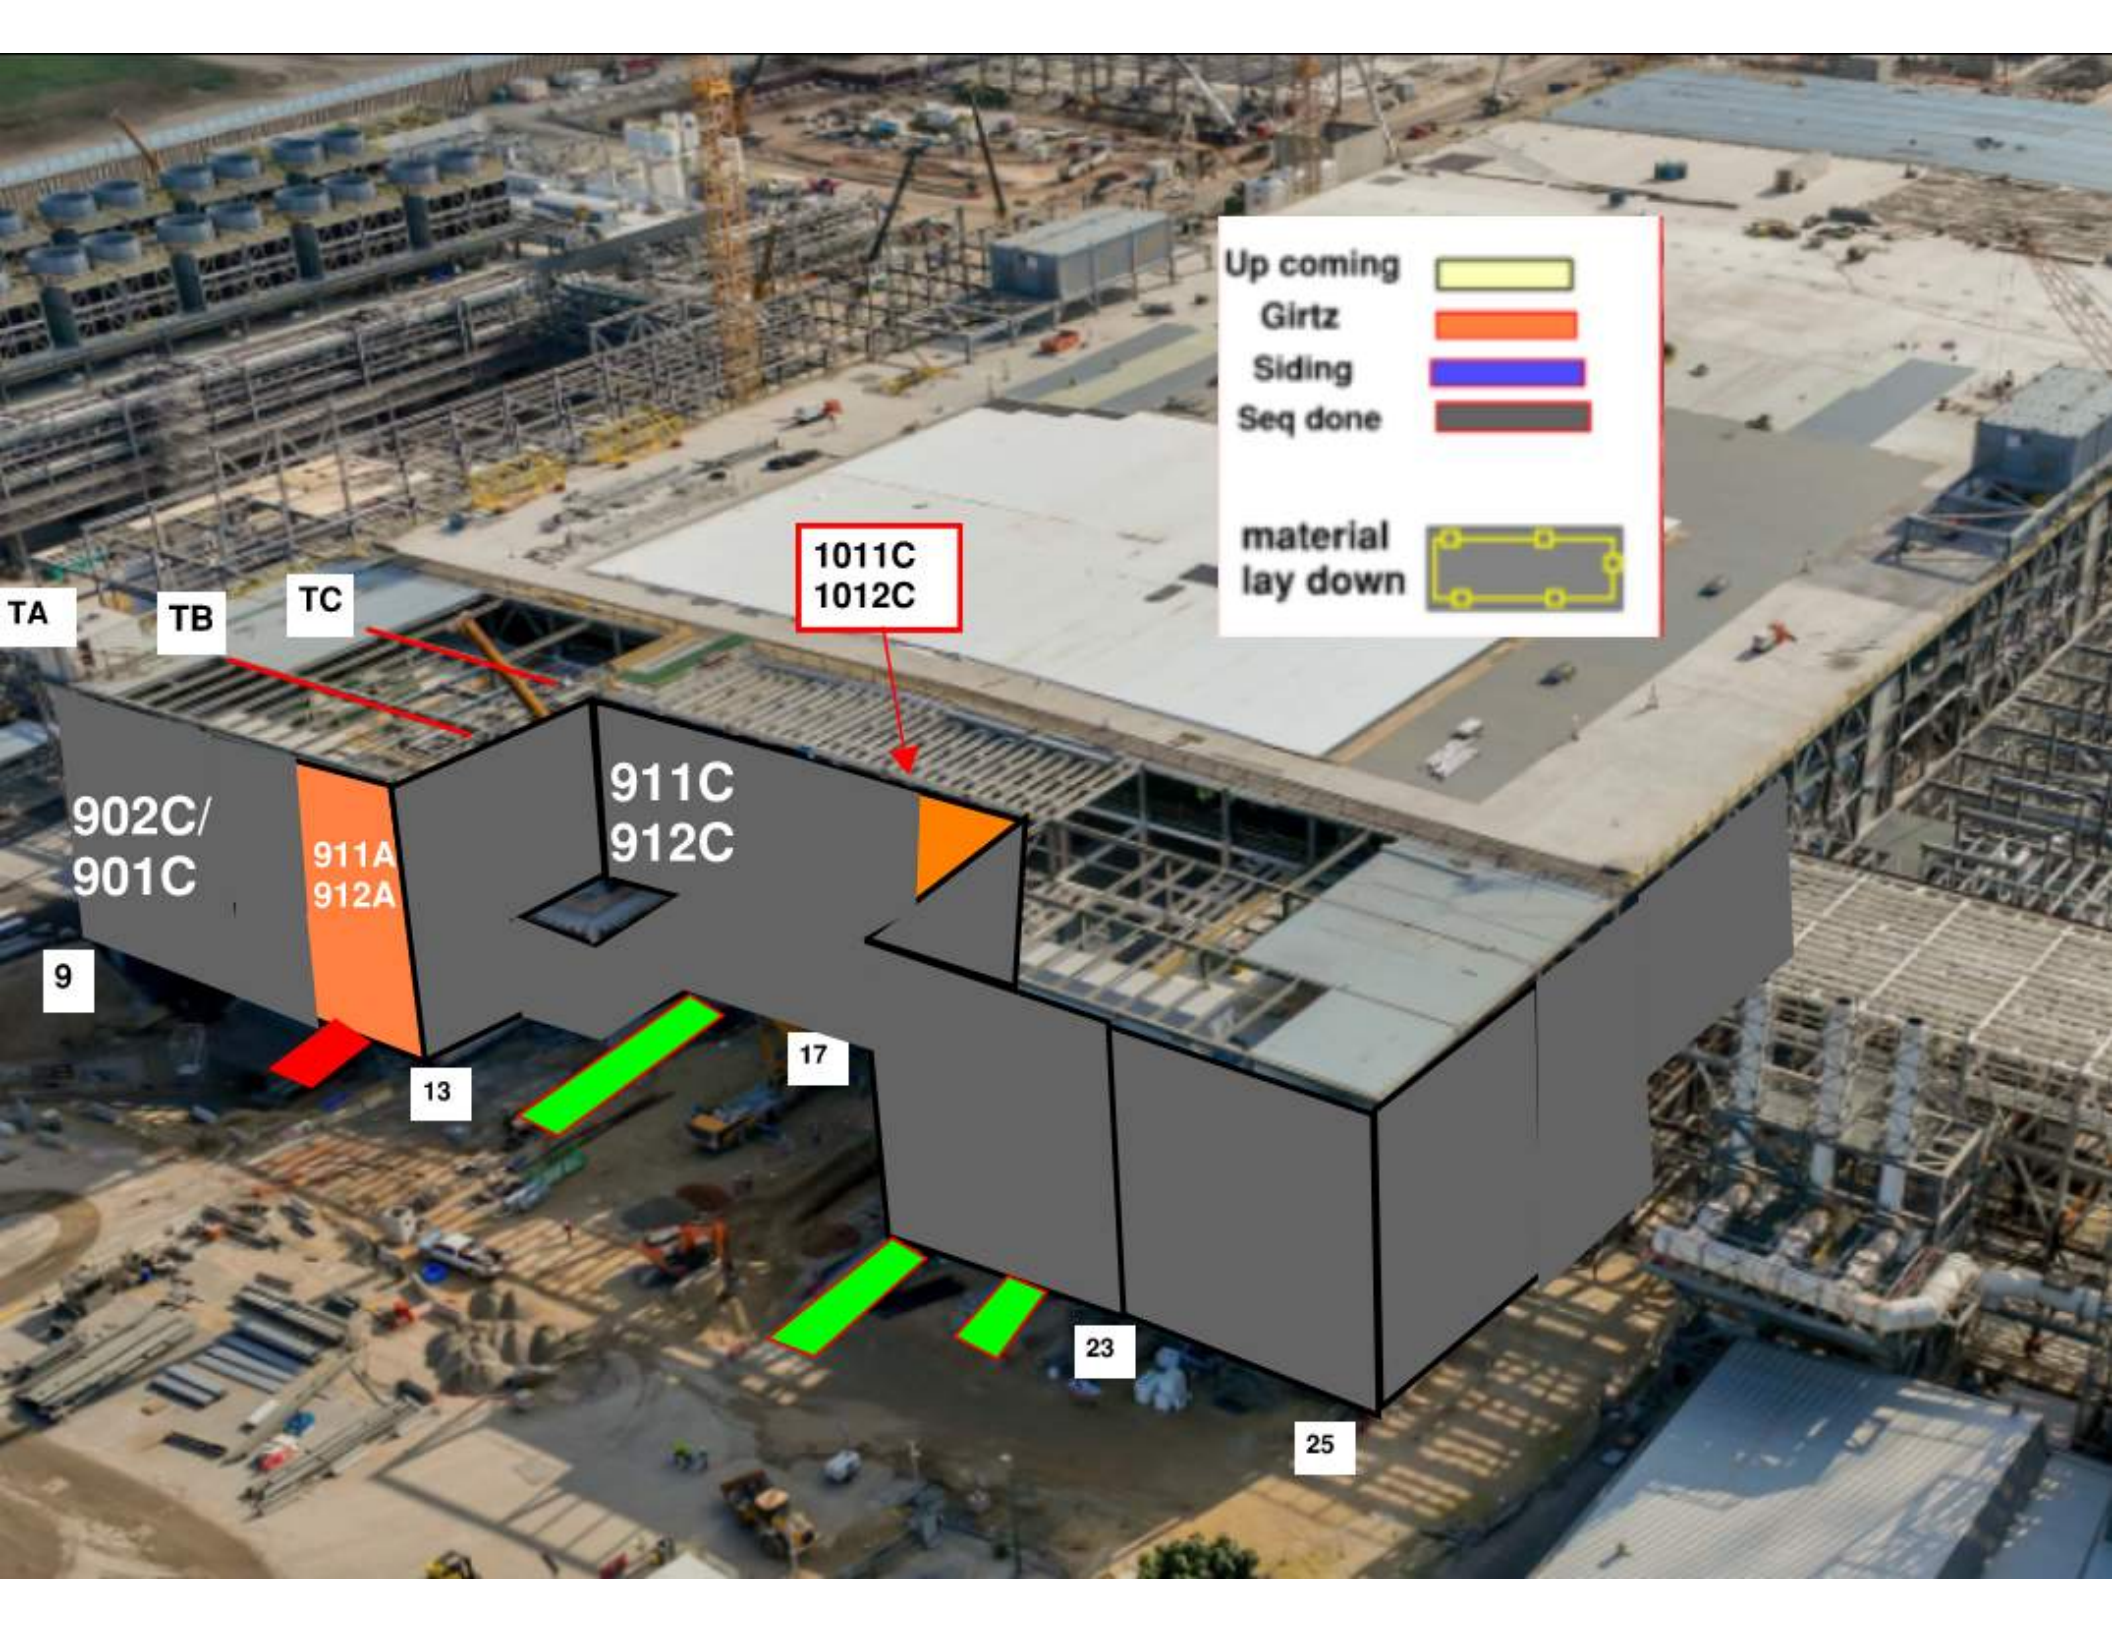

Up coming



Girtz



Siding



Seq done



material
lay down



TA

TB

TC

1011C
1012C

902C/
901C

911A
912A

911C
912C


9

13

17

23


25

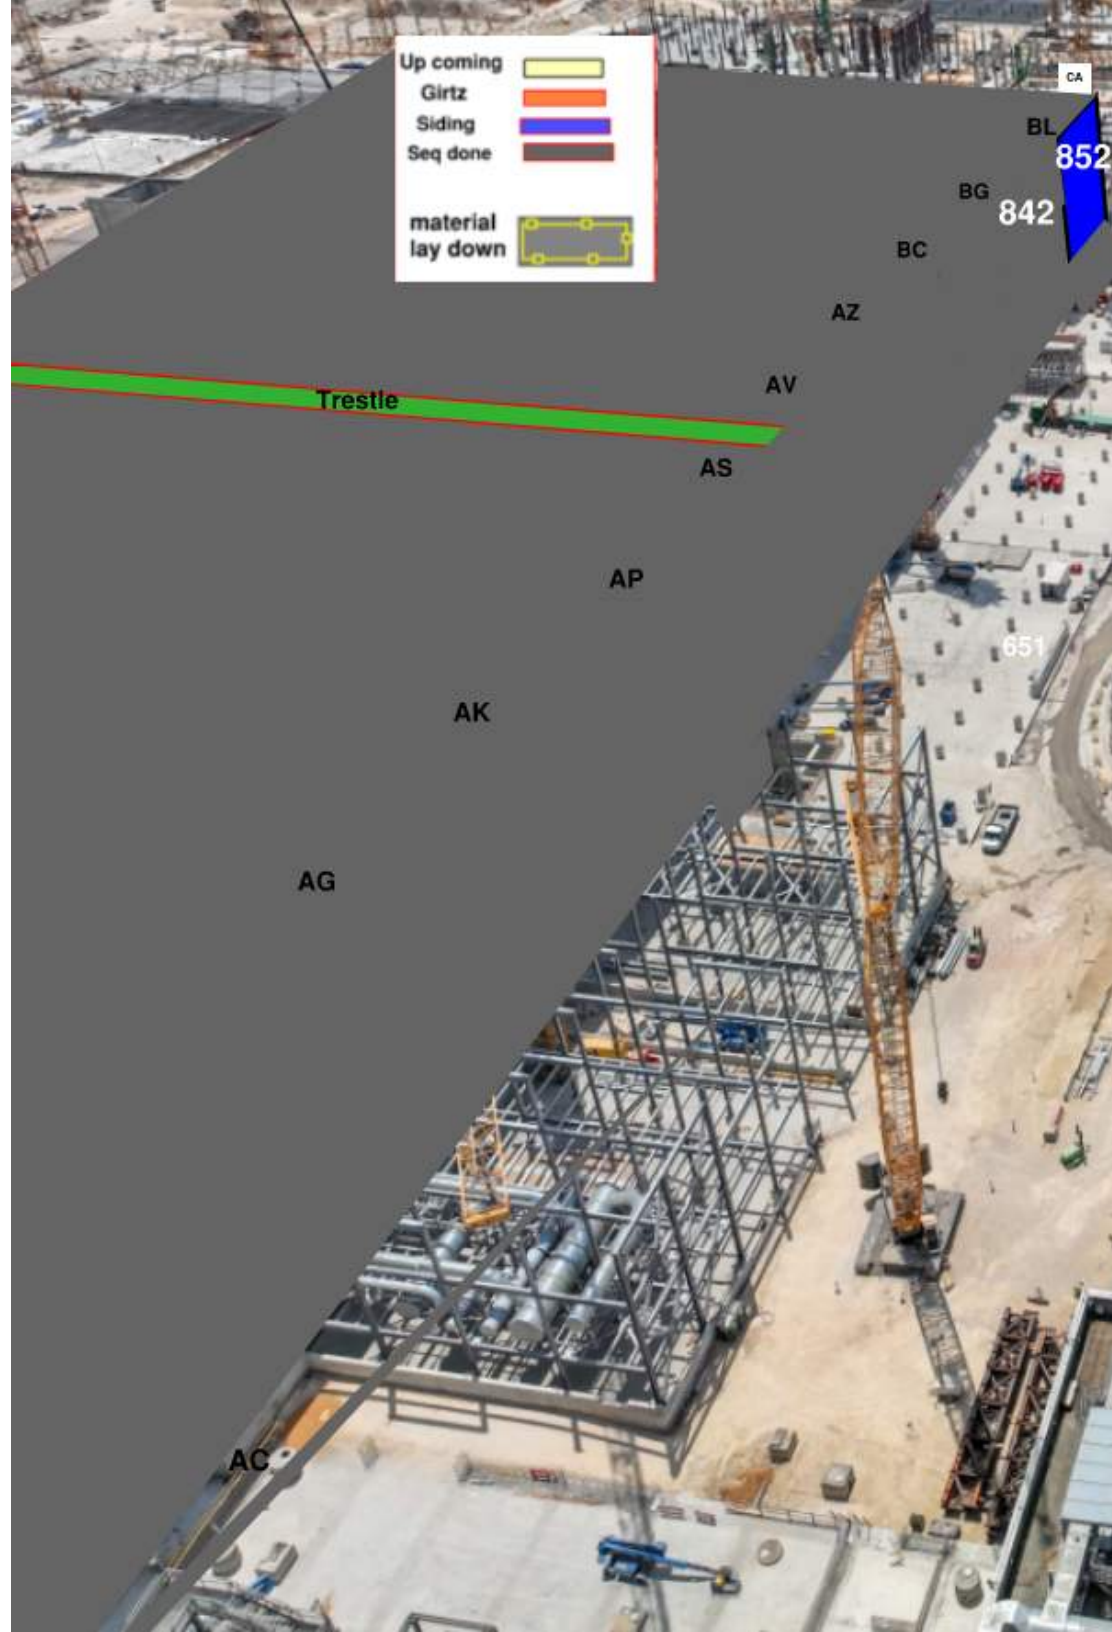

PSSS.1


Utility Level
1YA

PSSS Roof
2SA

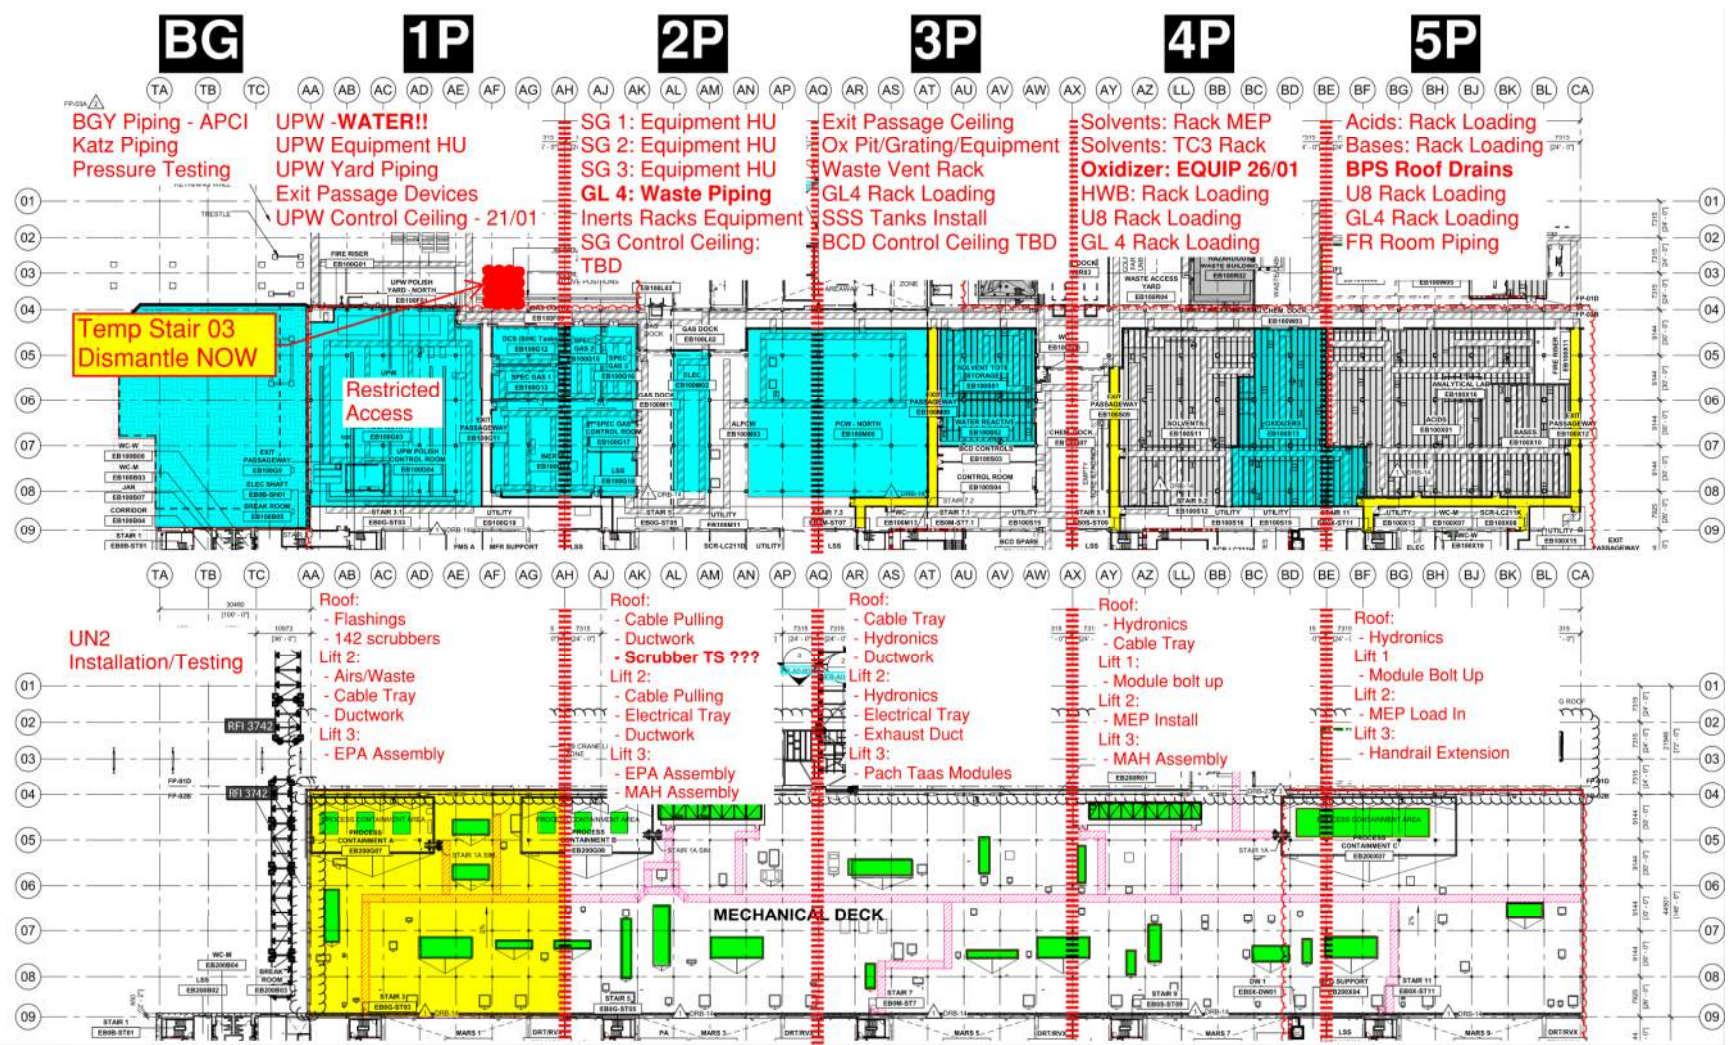


PSSS.2

Utility Level
1YA

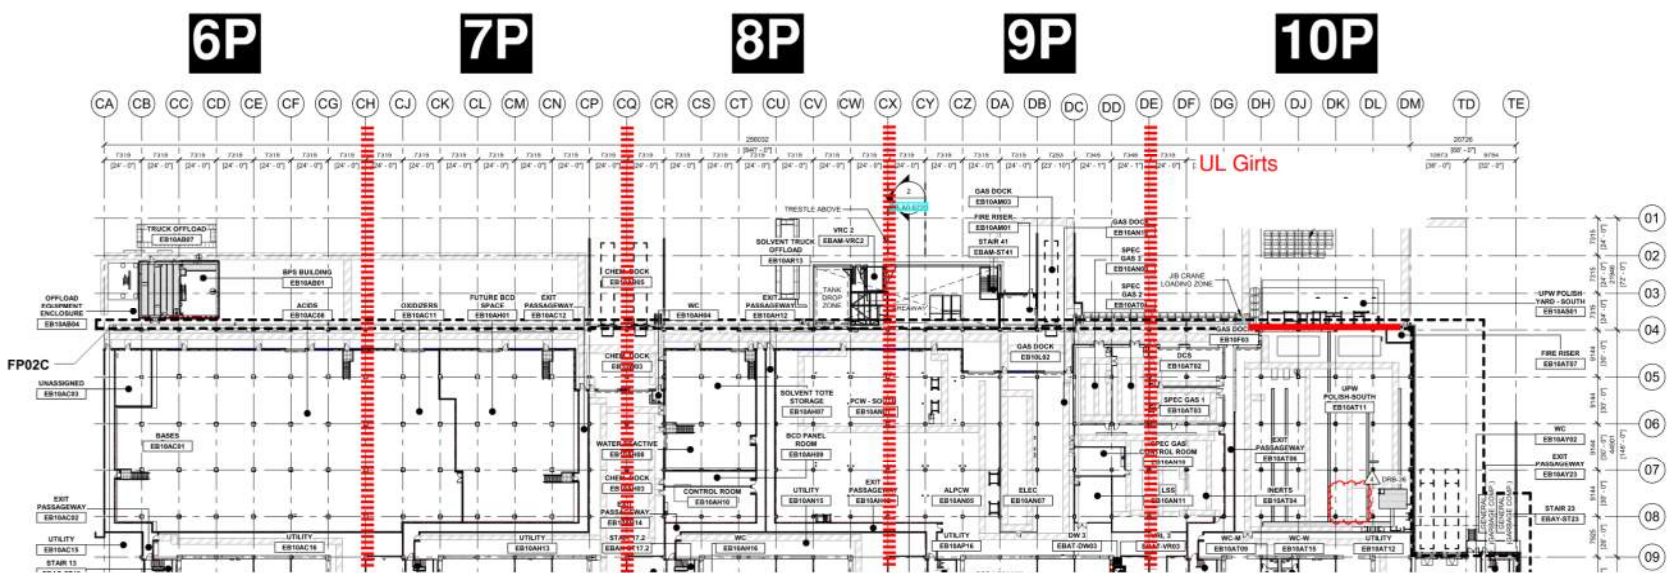

PSSS Roof
2SA

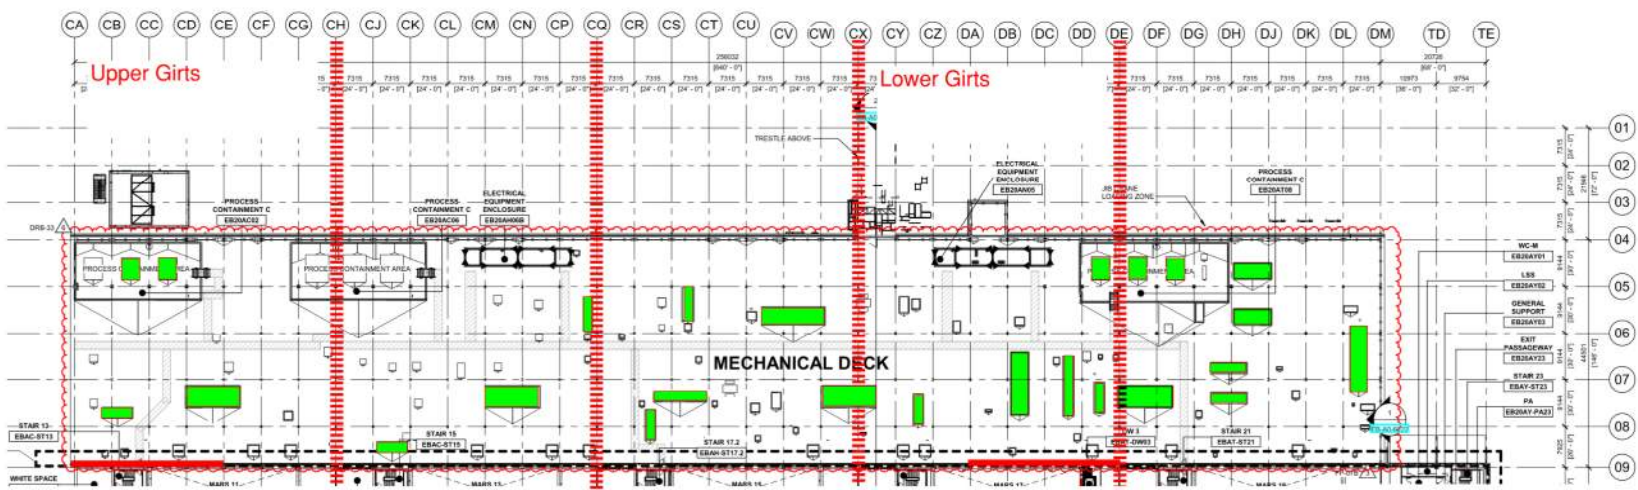


PSSS.1 Pressure Tests 28/01

BGY PCAR
Pressure
Test
17:00-05:00



UN2 U8
Pressure
Test
17:00-
05:00

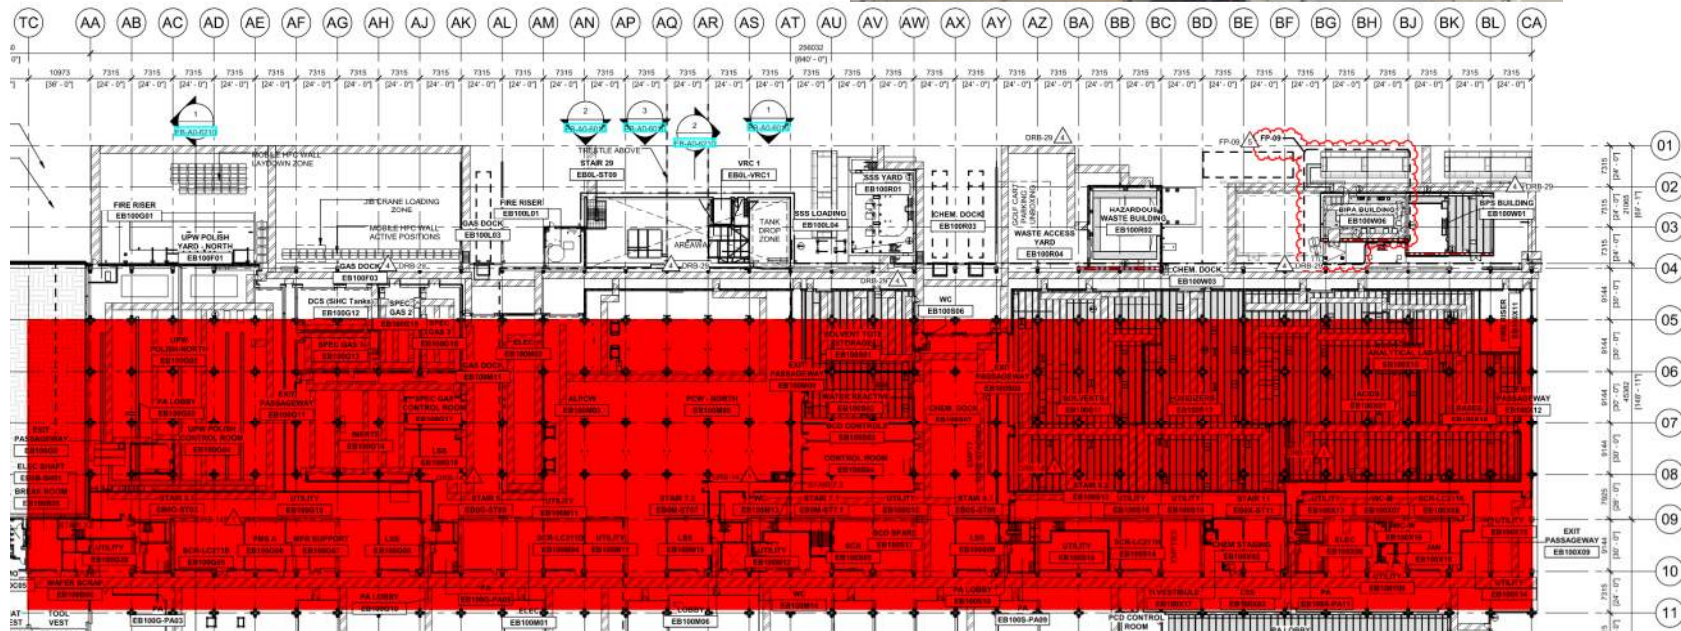

PSSS.1 Pressure Tests 29/01

BG


1P

2P

3P

4P


5P

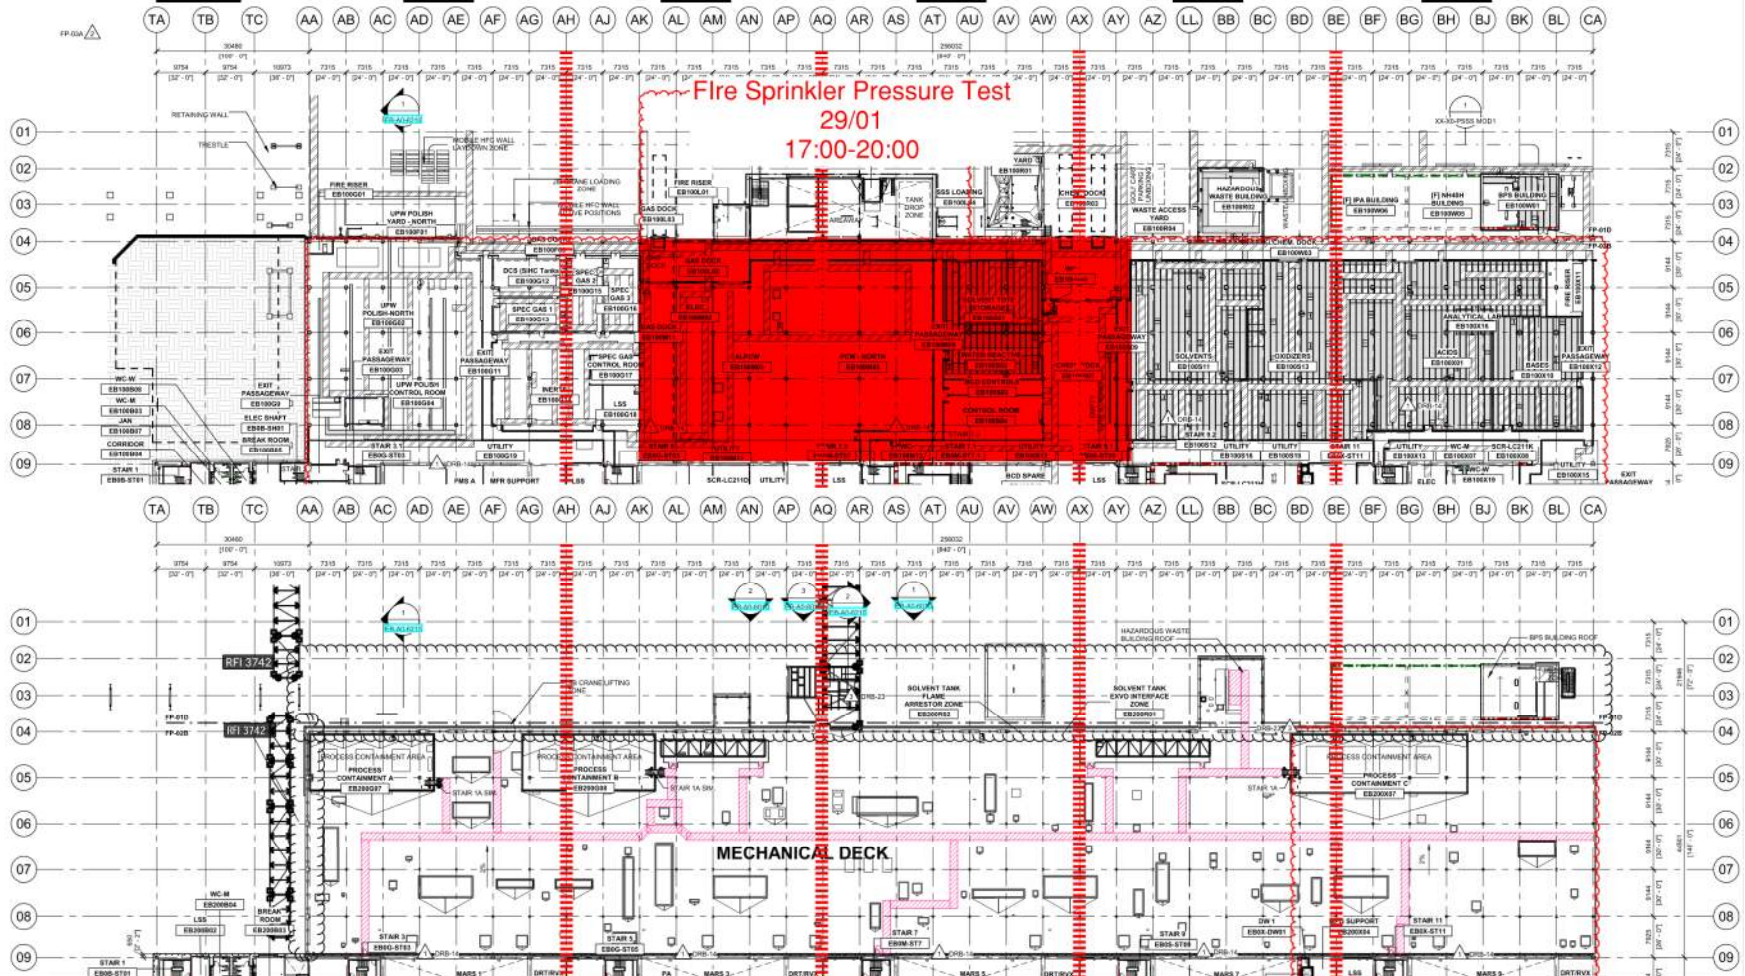


Utility Level
1YA

PSSS Roof
2SA

H2 Vent
Radiographic
Test
29/01
17:00-01:00

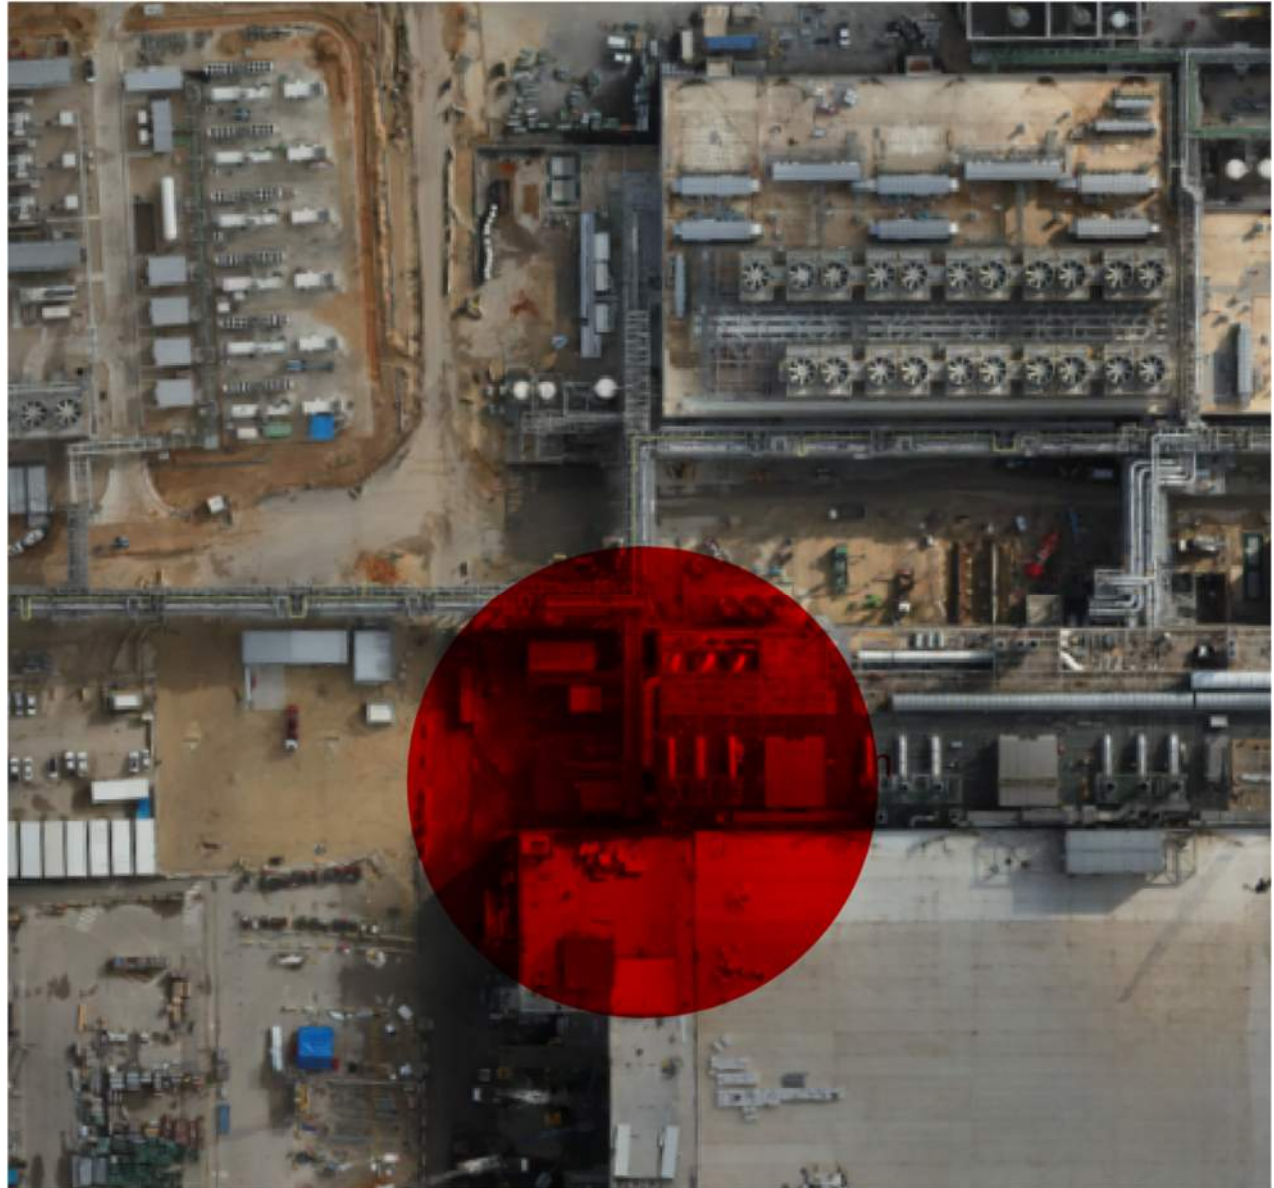


WJG 01J, 02J LIFT 2 & 3

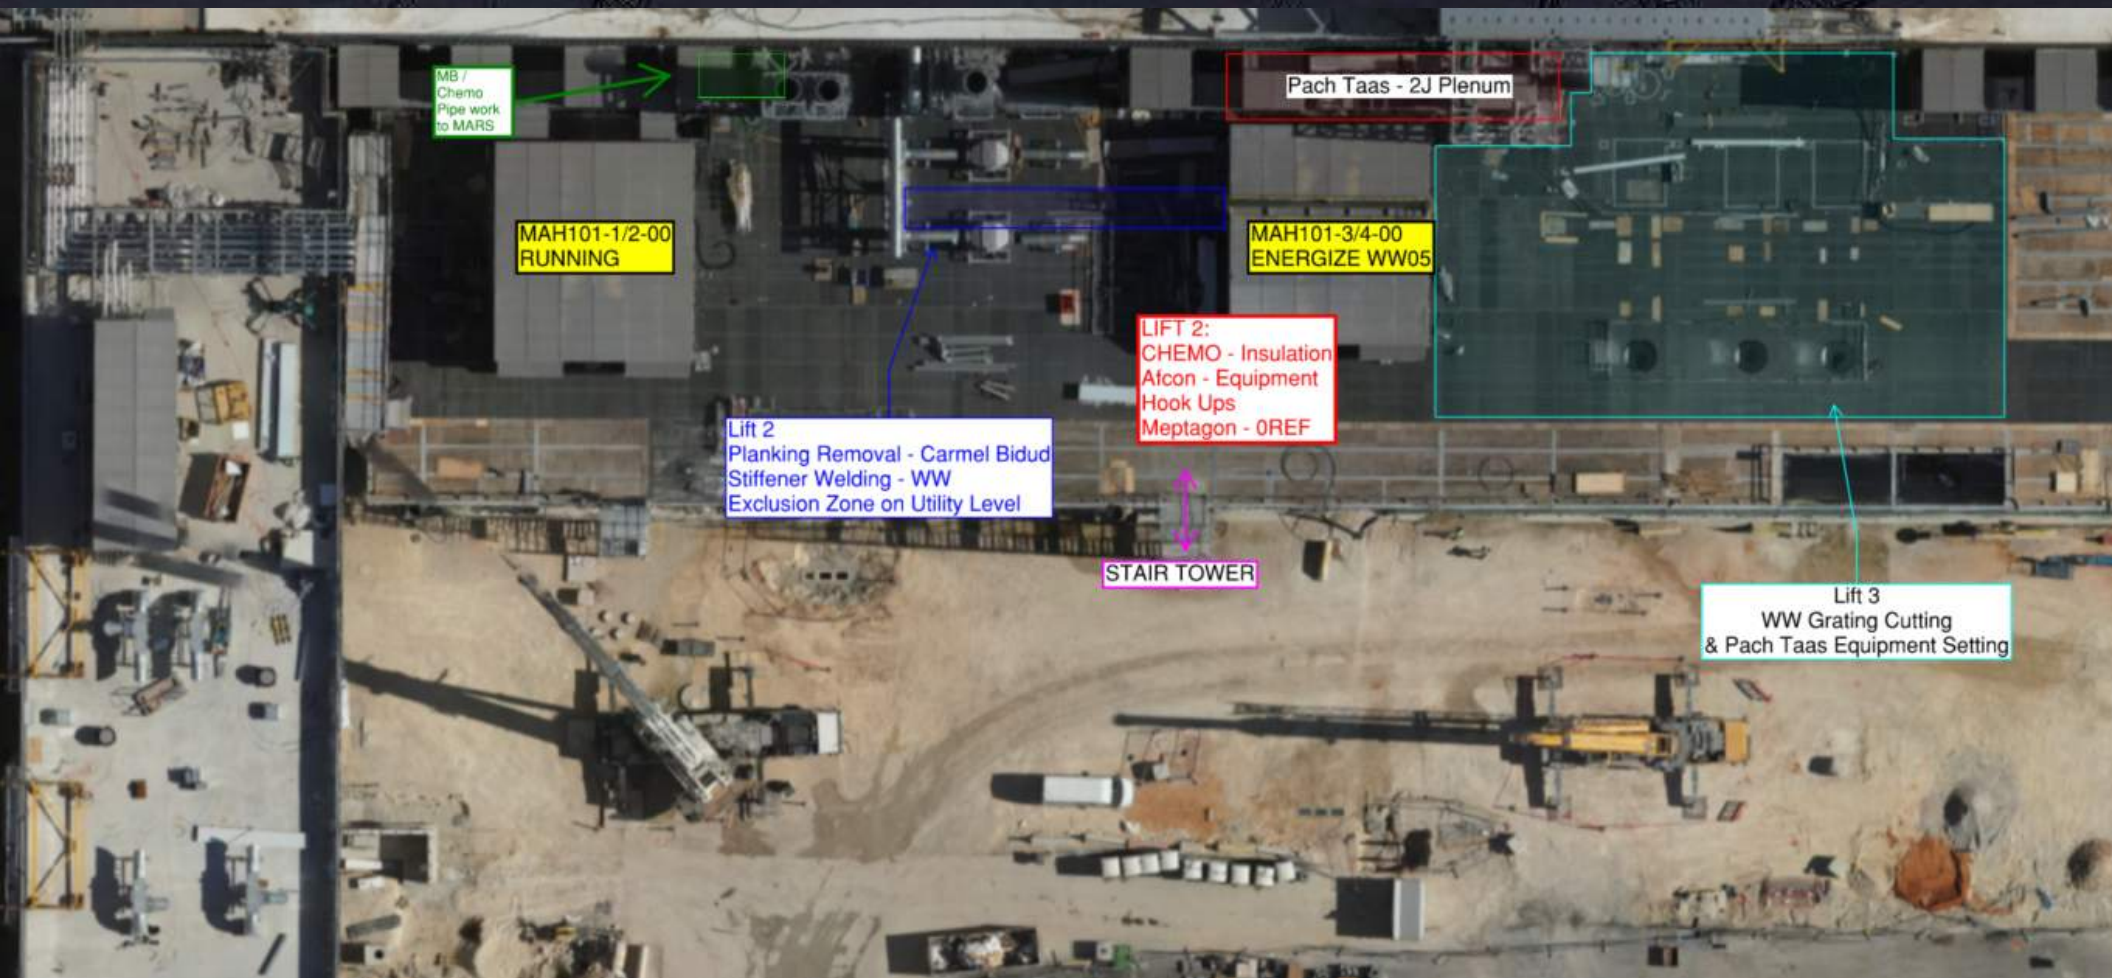





WJG 03J, 04J, 05J LIFT 2 & 3

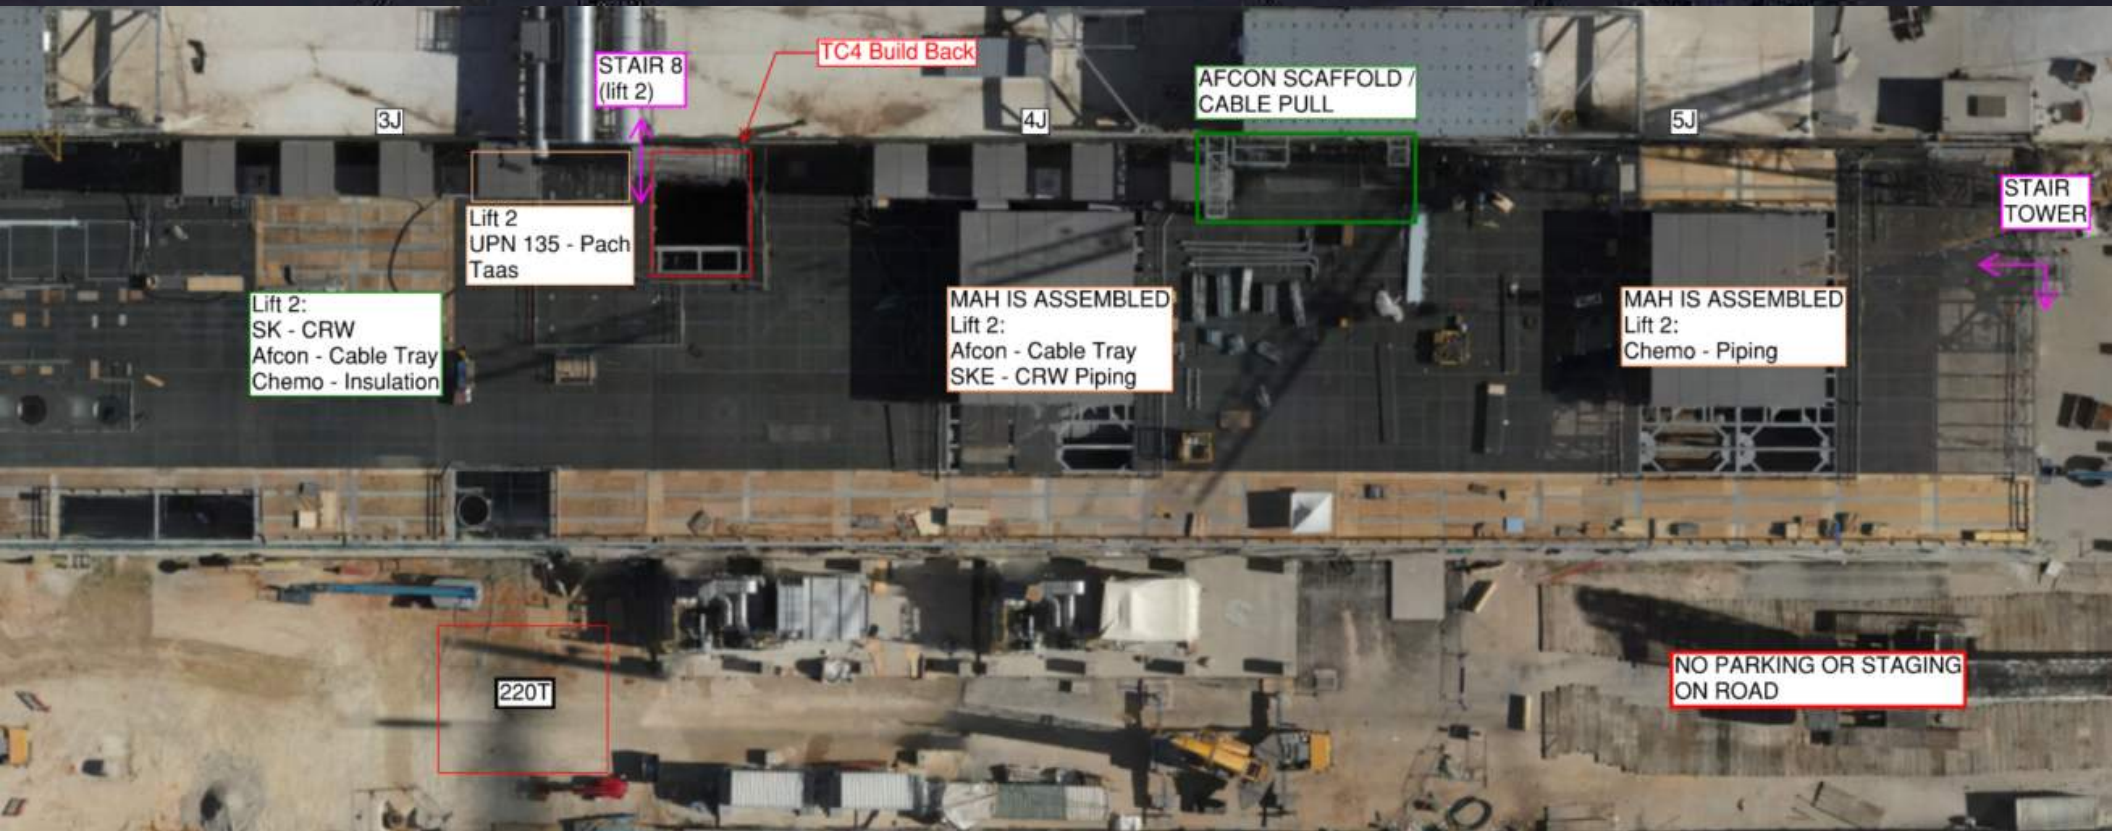




WJG UTILITY LEVEL BUILD OUT

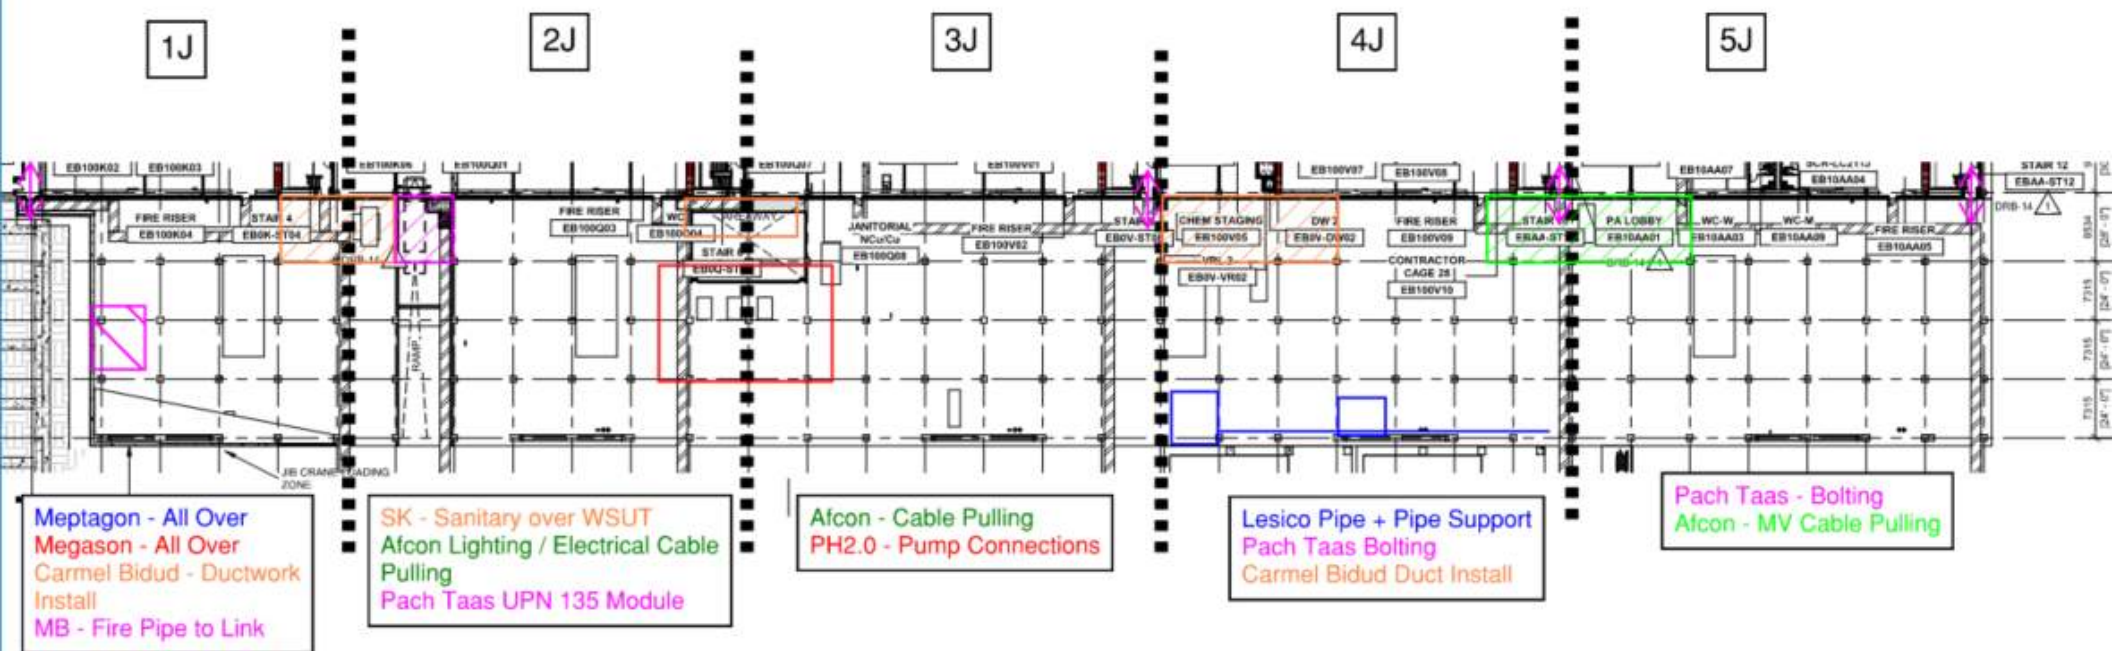

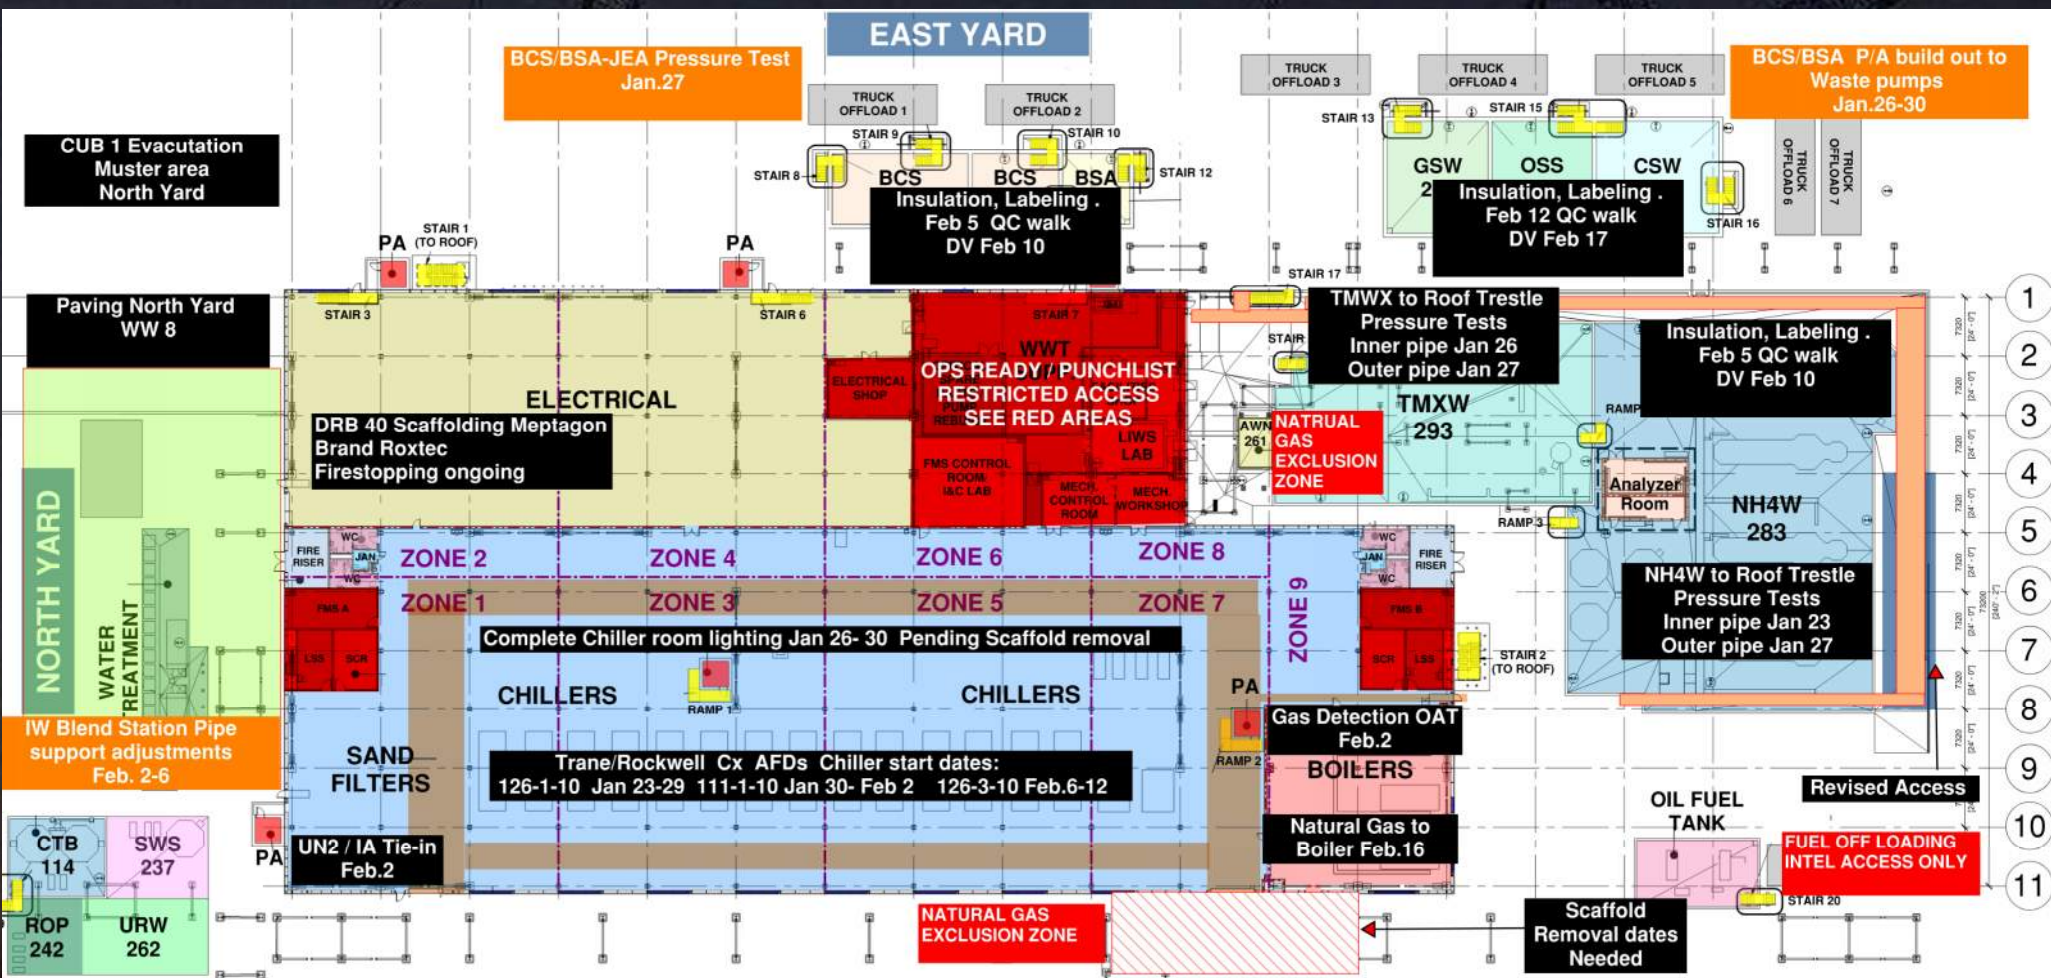


CUB 1 – EXTERIOR/ROOF

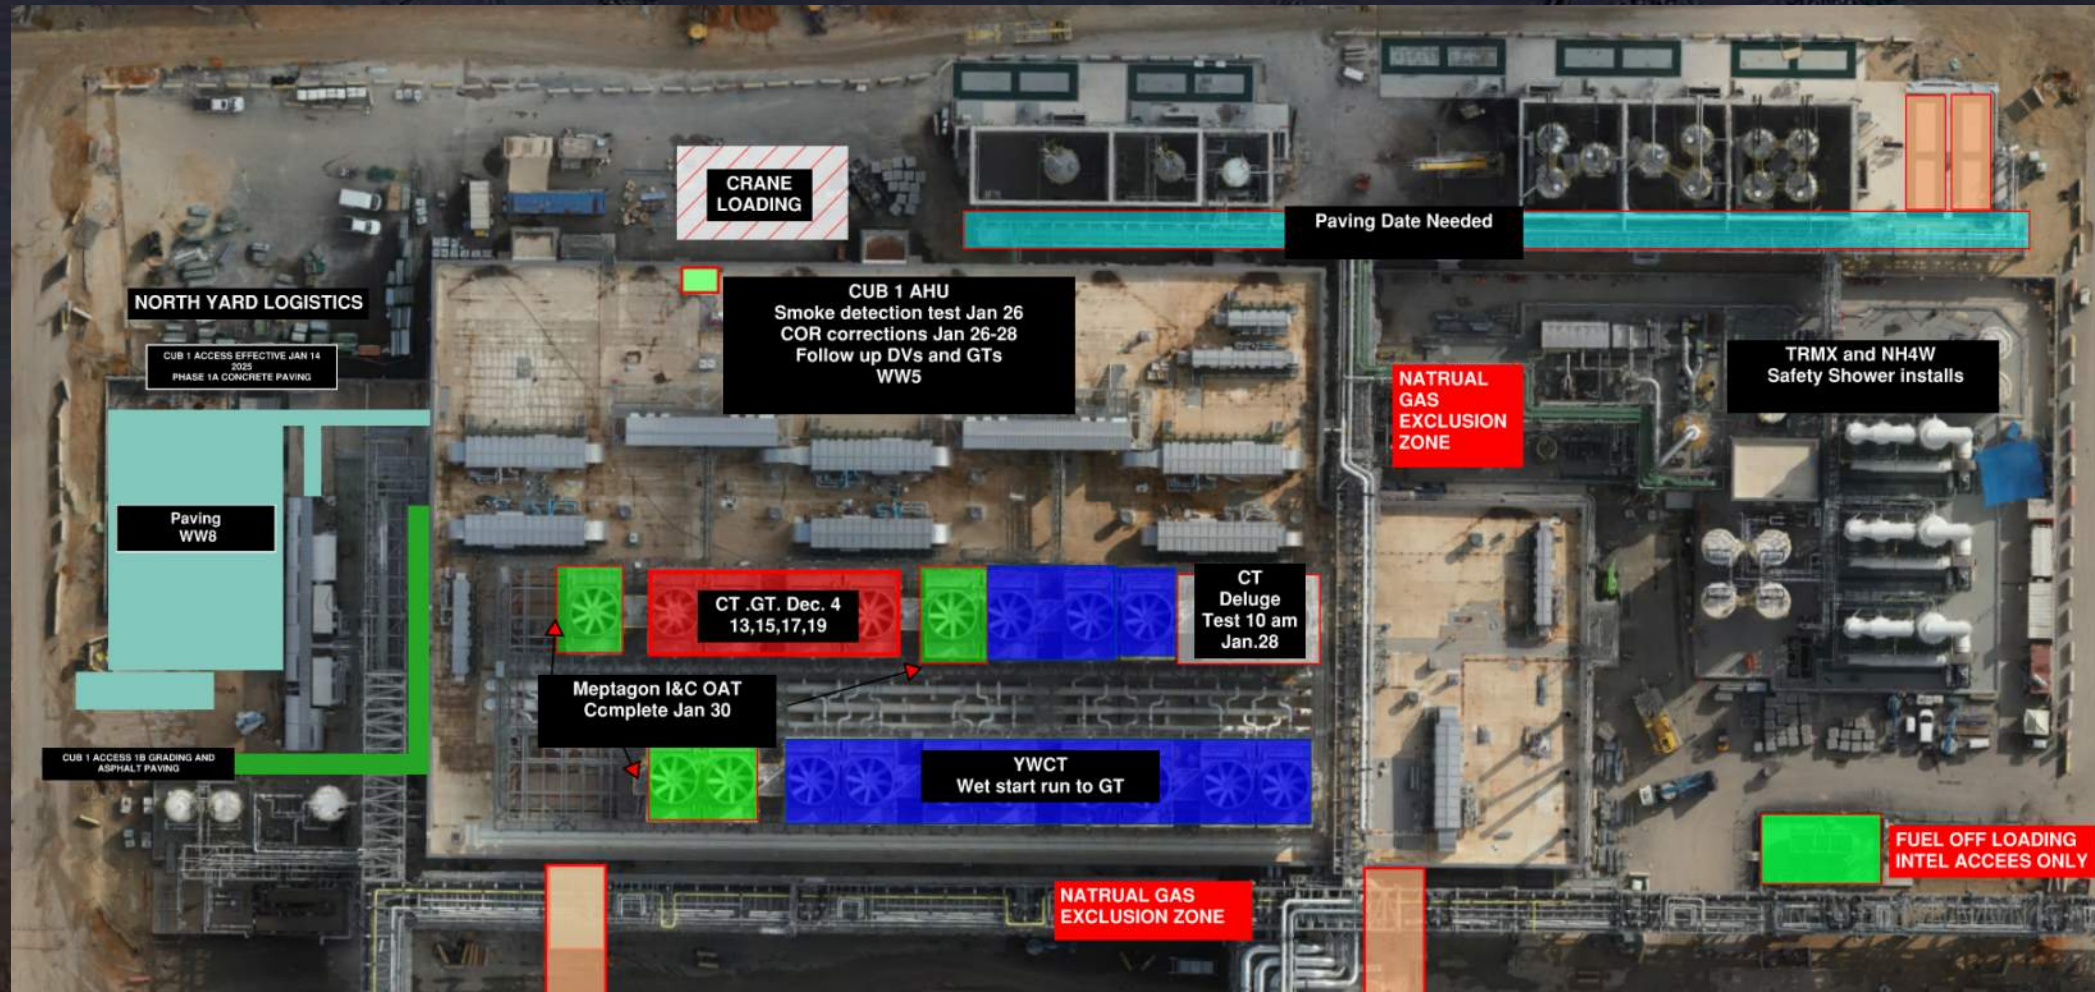




N 

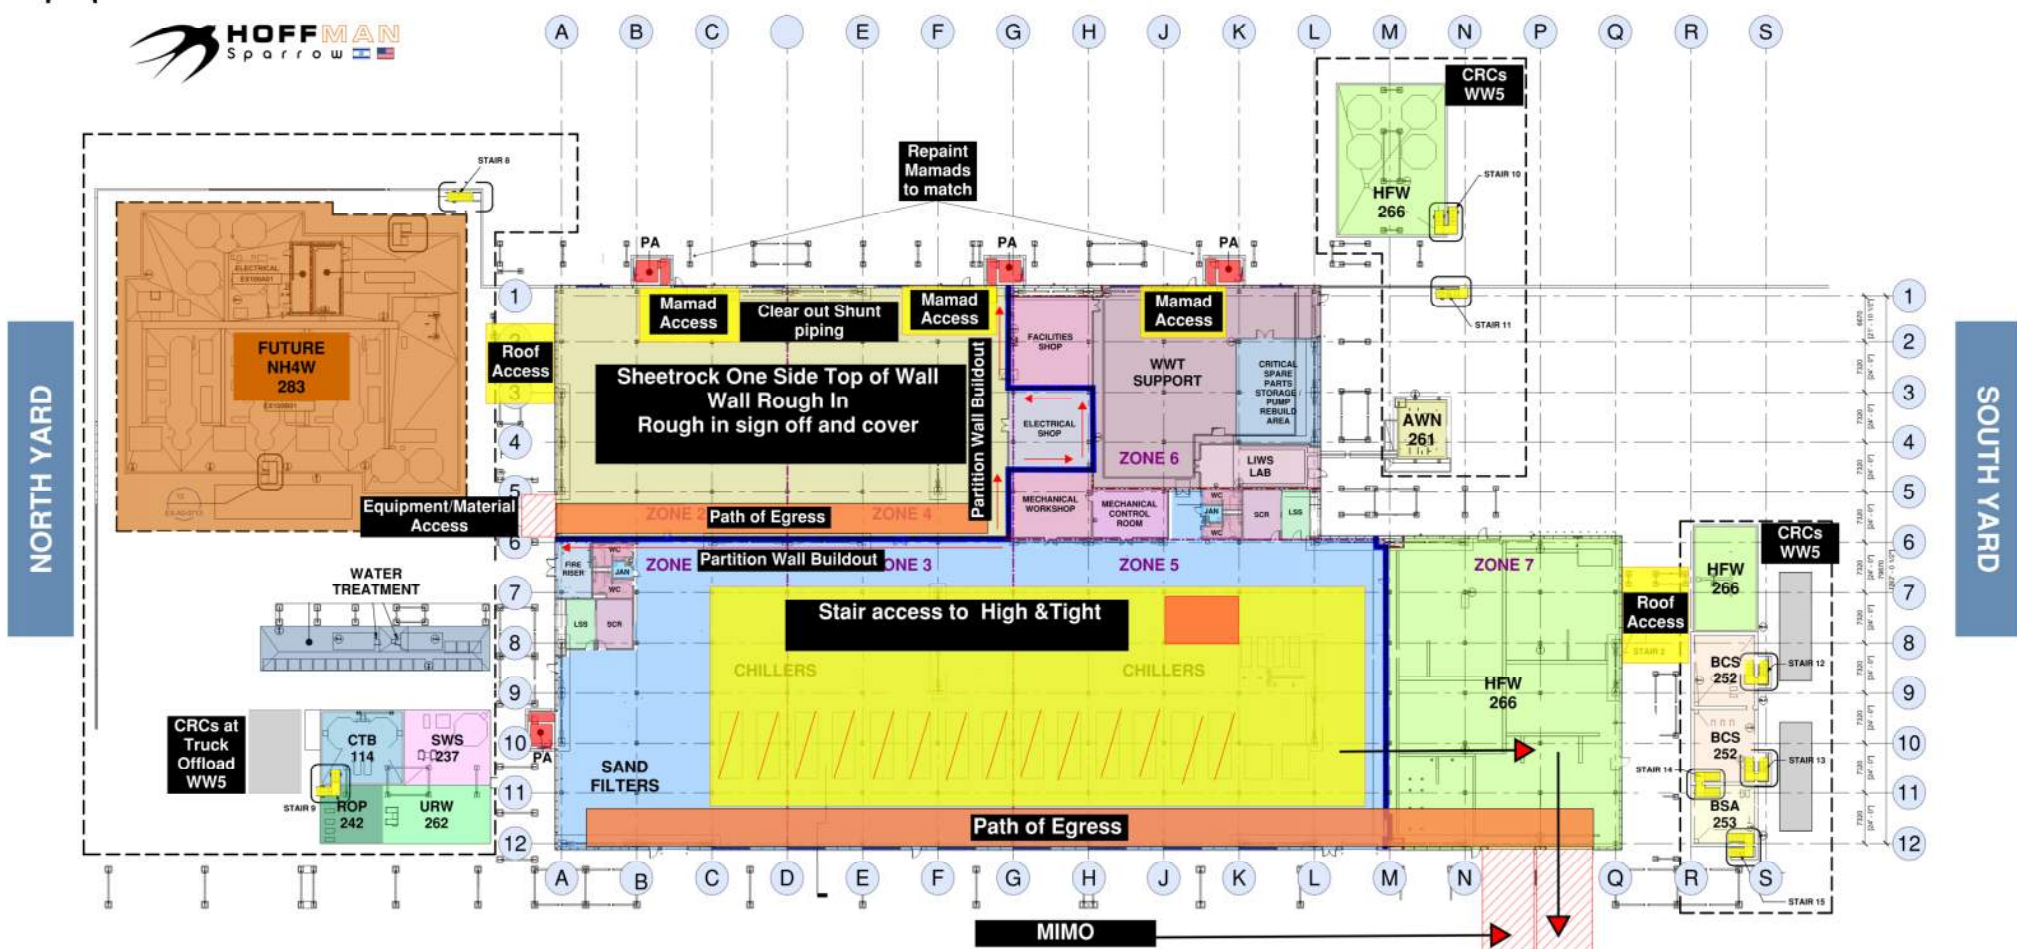

CUB 2 – EXTERIOR/ROOF

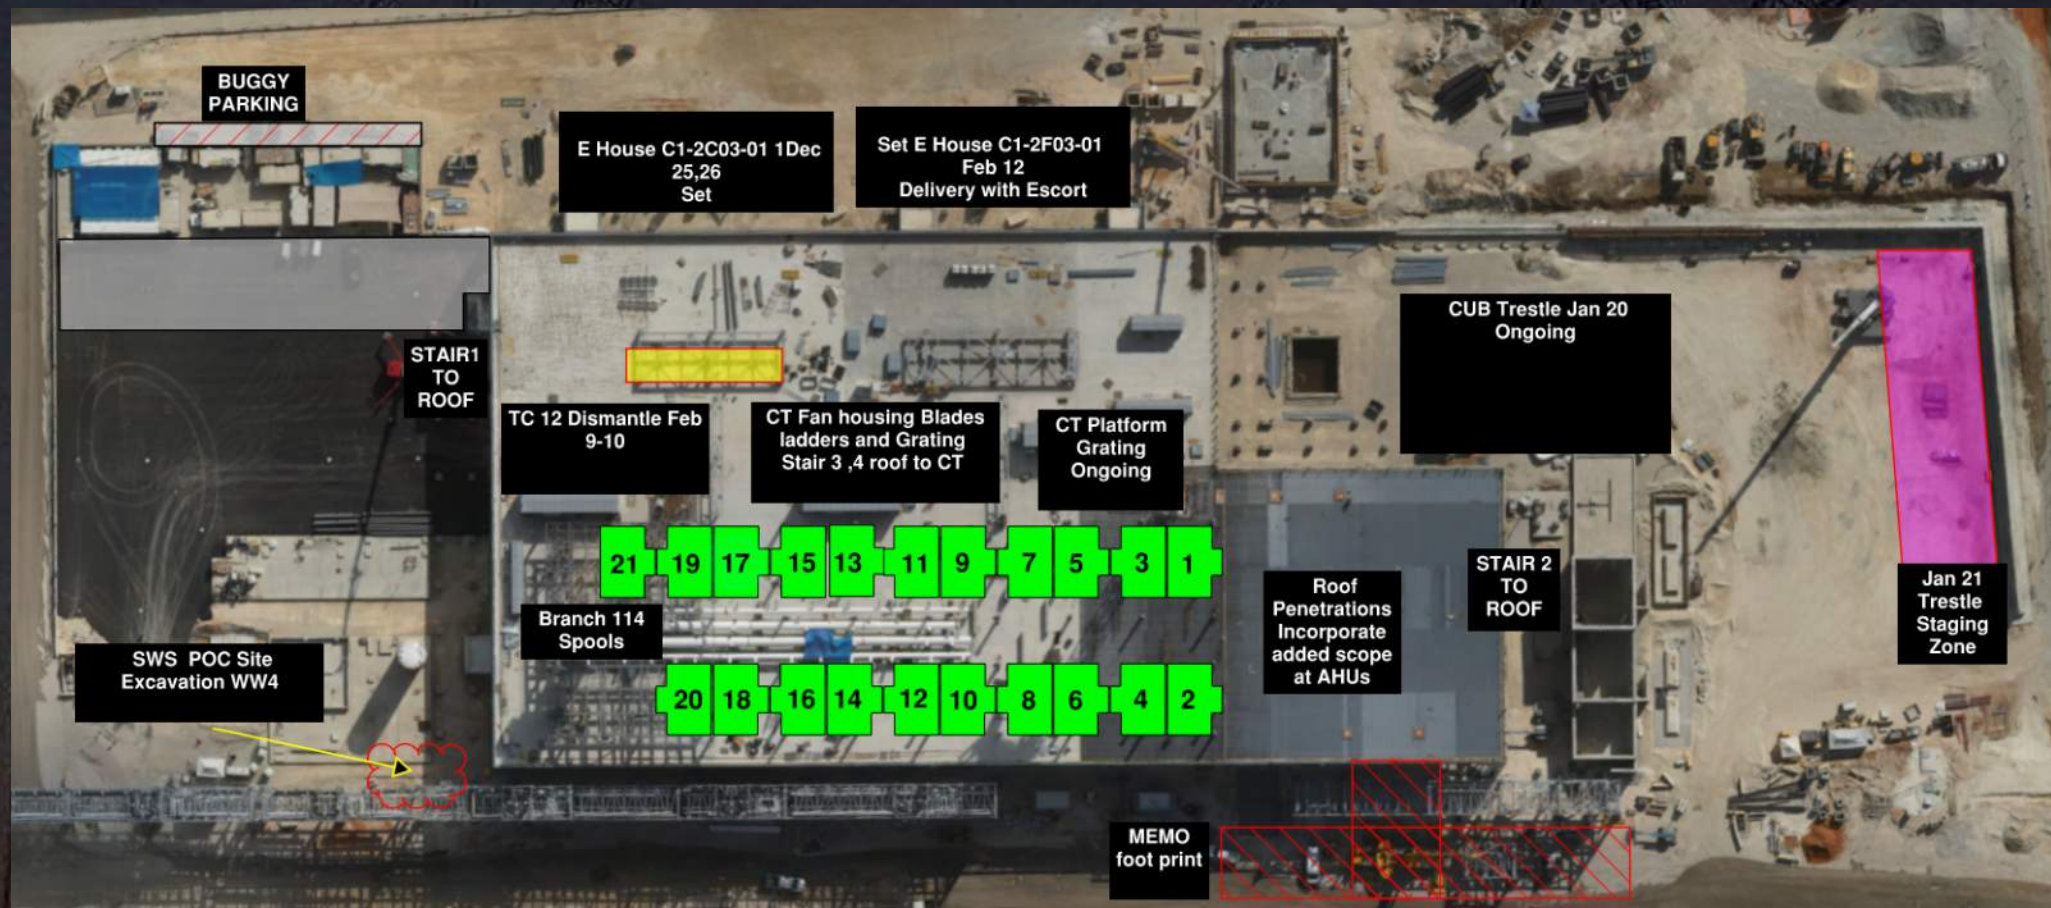



HOFFMAN CONSTRUCTION COMPANY





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Entry





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South



Assume Systems are Live Until Proven Otherwise

- All team members in the field need to be aware of the potential hazard of live systems in their area.
- Part of the area assessment must identify possible live systems AND what the employees must do to protect themselves from the energy within.
- Bullet-proofing is one way to protect workers from hazardous energies (water, air, electricity, etc.) within systems, and is required when our work MIGHT damage those systems.
- Bullet-proofing IS each contractors responsibility. It is in your contract. Continued failure to protect the finished installations and causing damage to them will result in work being stopped to protect workers, and if damage occurs back charges will occur.


Bullet-Proofing Examples



Bullet-Proofing Examples



Bullet-Proofing Examples

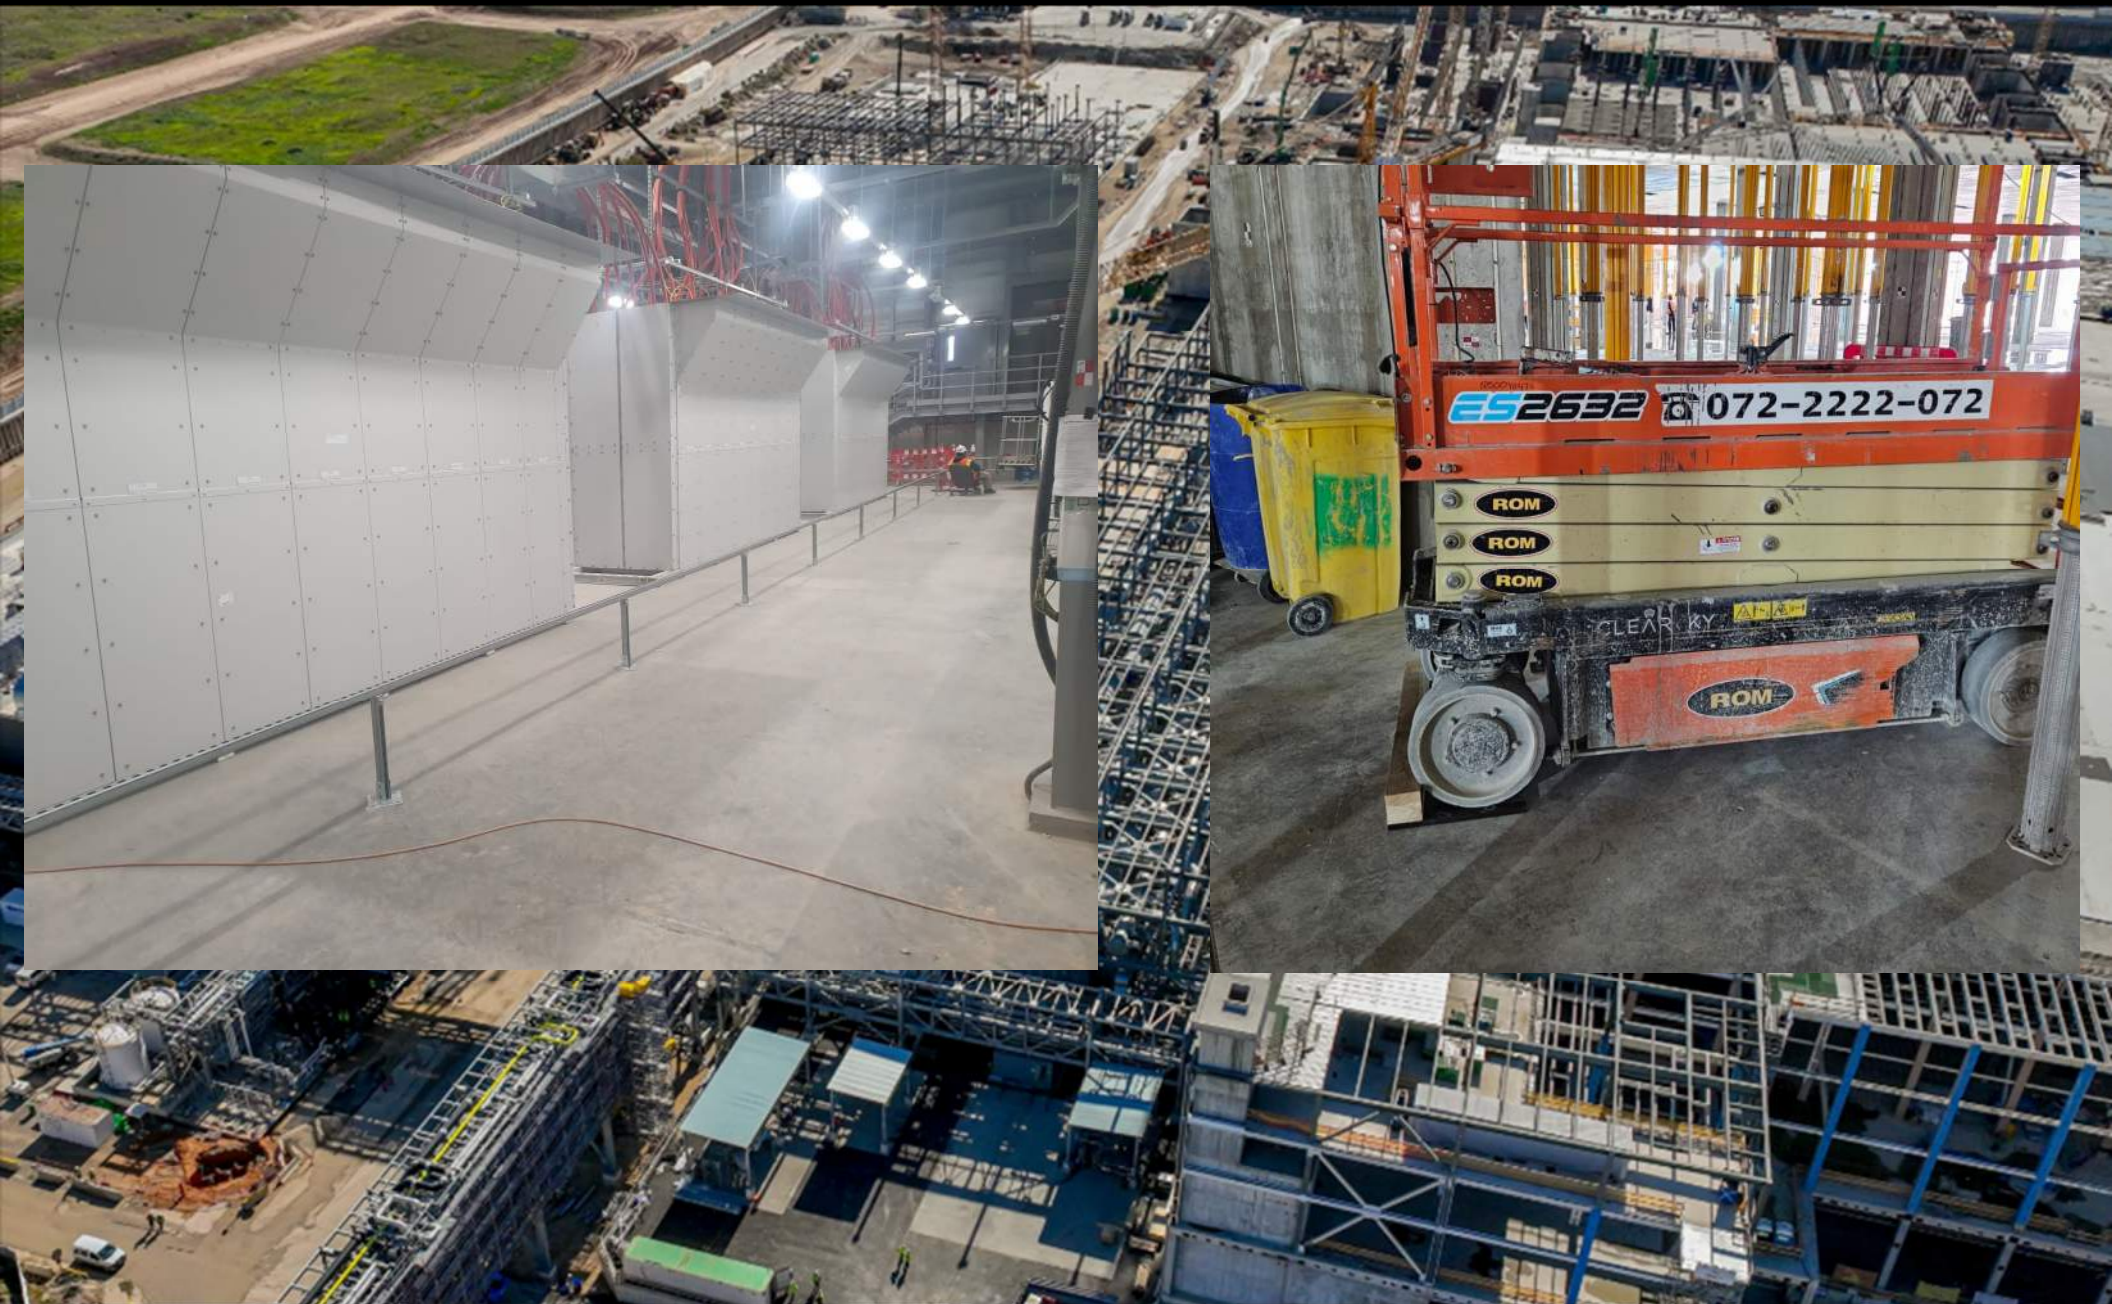

HCC/EHS Weekend Work- 24.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Jesse Fritch - 052-3697329

Ibrahim A

Or Yaakov - 052-4268250

CSA CM

Cody Baumann - 052-7582613

Eyal Ben Shabat - 052-2239767

Brandon Feerer - 052-878-4285

Mark Santiano - 052-6937203

Shmuel Rosenberg - 052-3878052

Abhilash Parameswaran - 052-6938827

Eden I

Max P

MEP

Cx

Cranes

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional - Or Pitusi- 054-812-4788 Or-Pitusi@Hoffmancorp.com

Subcontractor Weekend Work- 24.01.2025

FAB

Utility Level / Roof / Stair Shaft

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

HYG

Ehs Salah 0507773119

Foreman Avishai 0503303939

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- **Pach Taas**
 - W-E MARSes
 - Ilya: 0505771907
- **Afcon E**
 - All over SF
 - RAZ: 0526008487
- **Combe**
 - TTNE
 - Ali: 0526767936
- **MEGASON**
 - MOD 2
 - Israel: 0526869393
- **SELA**
 - 9E
 - Yoav: 0548076339

Clean Room

- **Talad** – 20 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Igor 0544509386)
- Sig – 14 GUYS Mod1 – MOD2- 17 line, 7E above coils (EHS Beni 0506232032, Super Shmulik 0549205966)
- **Afcon** – 20 guys CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- **Chemo** –26 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- **Sela** – 10 1E, 2W CRC (Supervisor Yoav 0548076339, EHS Sergey 0526650046)
- **Pach Taas** 3 guys, BF-CA 17 Line (EHS Avigdor 0542010393, Super Netanel 0543301880)
- Protocol 2 guys (Roni 0542496363, Lidia 05072148)
- Talent solution 11 guys CR 2E 1E/W maintenance cleaning (EHS 0508777611, Super Faraz 0547139706)
- W&W 15 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

Subcontractor Weekend Work- 24.01.2025

PSSS

- Pach Taas** – Module bolting PSSS Roof, Lift 2 3-5P
 - Foreman – Vadim – 053-5552472
 - Safety – Offek – 050-2161429
- **Afcon Electrical** – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- **Chemo A.** – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- **SK Engineering** – GL4 UL Piping, 3P roof/Lift 2 Piping
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Carmel Bidud Duct** – Spec Gas, BCD, and 2P Roof
 - Foreman –
 - Safety –
- **Combe Waste** – 2P Waste Piping at GL4/SSS Building
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Combe UPW** – BCD/UPW Rooms
 - Foreman – Boris – 054-8346412
 - Safety – Shimon – 054-5348843
- **Lesico** – UN2/Waste Vent Rack
 - Foreman – Selvin – 052-4787370
 - Safety – Oskar – 052-5221474

WJG

- **Afcon** – Lift 2 and Utility Level Cable Tray
 - Foreman: Montu 055 911 6973
 - Safety: Pradeep 055 274 2935
- **Chemo:** 2J Utility Level, 4J/5J Lift 2 Piping (Hot Work)
 - Foreman: Maor 050 988 9071
 - Safety: Erez 054 971 6840
- **Pach Taas:** All over (HRA)
 - Foreman: Ilya 050 577 1907
 - Safety: Eran 054 770 6233
- **Lesico:** Natural Gas Piping Utility Level
 - Foreman: Anoop 058 691 1748
- **SK** – (pressure test G water column 4J MAH)
 - Tufik 54-9433592

Subcontractor Weekend Work- 24.01.2025

CUB

Meptagon: CUB1

Foreman: Serghei – 0548038554

Safety: Haym – 0552728807

D&P: CUB1/2

Foreman: Konstantin - 0545501602

Safety: David – 0548894447

Sela: CUB1/2

Foreman: Yoav Yossi - 0548076339

Safety: Sergey Koharchok - 0526650046

Megason: CUB1

Foreman: Israel – 052686939

Safety: Guy Ishbit – 0544915409

Chemo: CUB1/2

Foreman: Dude Cohen – 0509808846

Safety: Daniel Lackford - 0525217434

Trestle

SNJ:

PIPES –T40 - UB CUB - 15 workers (3 teams)

STEEL –Galvanized paint + T30 A+B - 8 workers (2 teams)

Steel adjustment - 10 workers (3 teams)

FORMAN-

Mucles- 0526017477

SAFETY TRESTLE-

Aviram shrike - 0509059920

Siding

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Olizki – Offload 18 & CUB1 trench drains, Southeast CUB1 grading

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Sut

Sela

EHS 052-6650046

Foreman 054-8076339

Daily Coordination Meeting



14:00 Sign In
