

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Weekend work




Chem dock VB/RS
5:00 am

SE loading dock ramp
2:00 am

Mimo 7 curb and equip. pad
4:00 am

SW loading dock ramp
3:00 am

UTILITY LEVEL MOD1

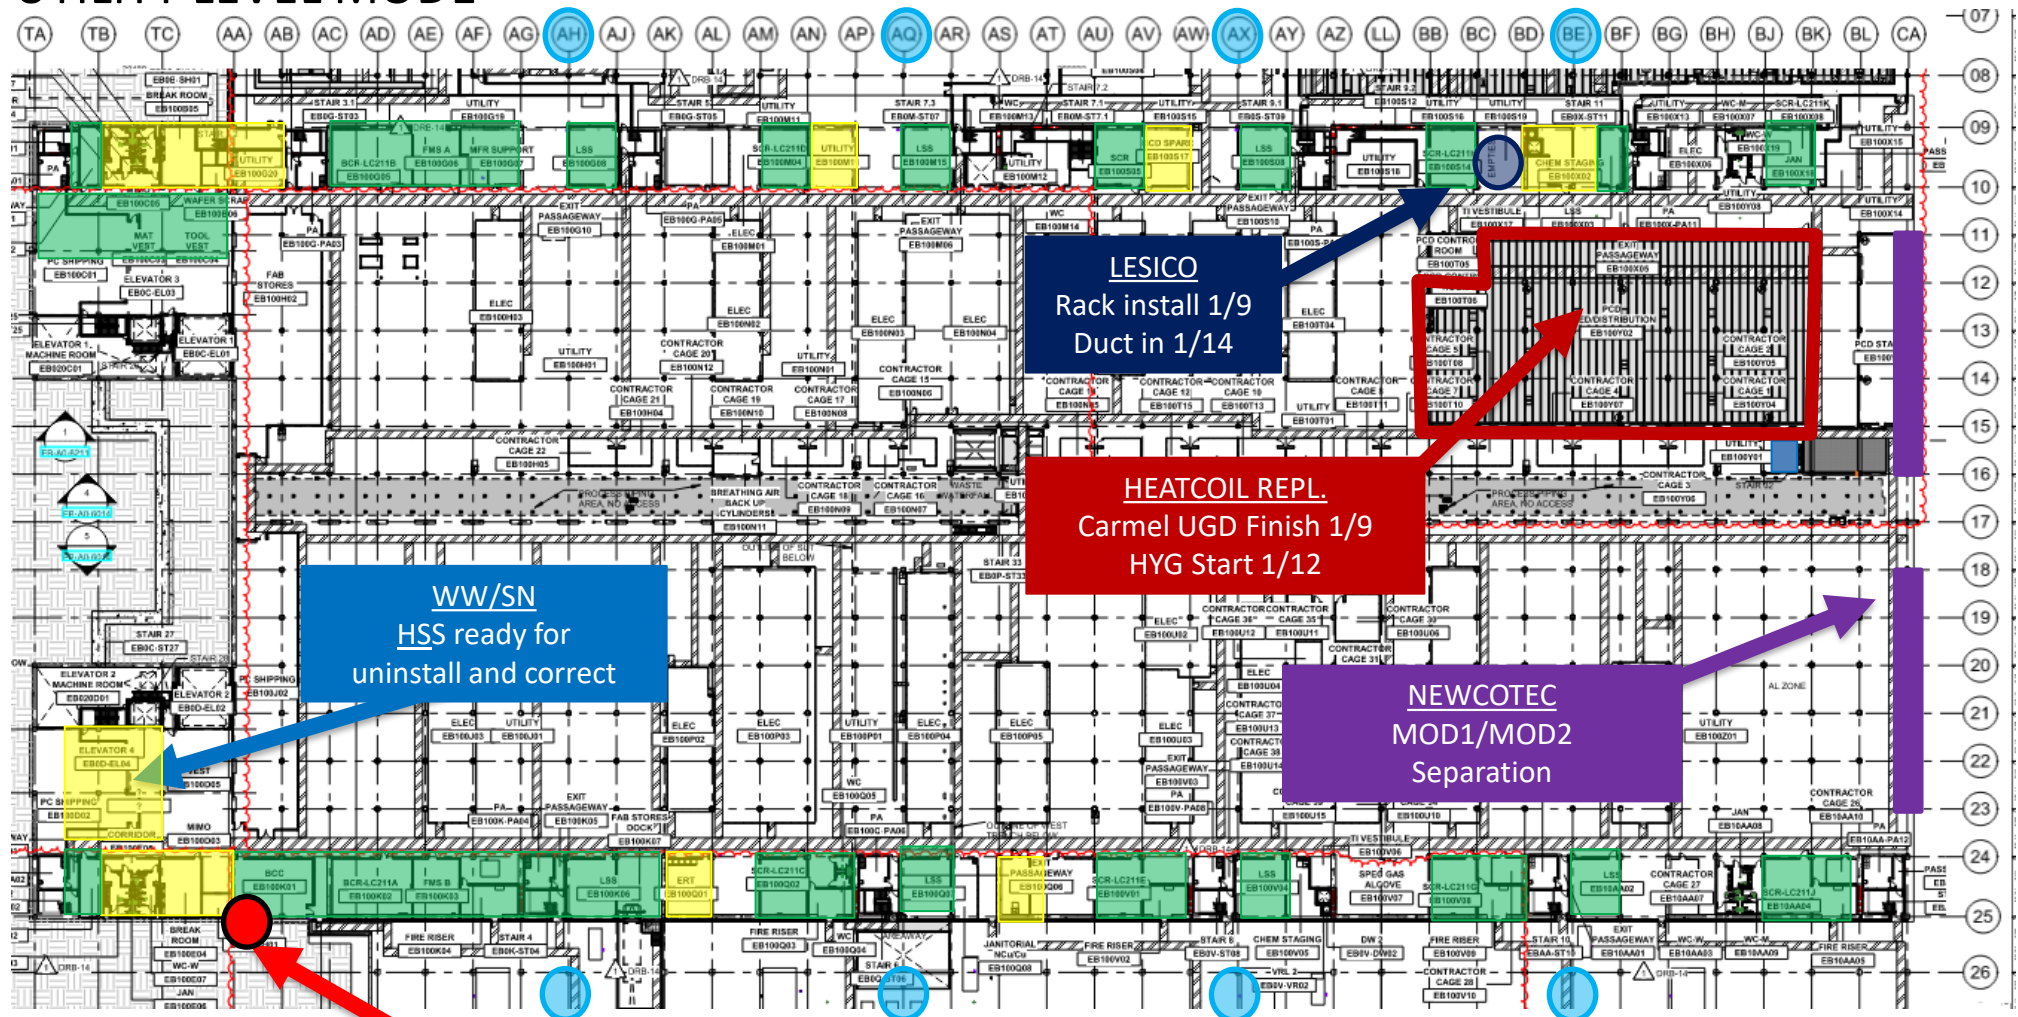


ELRAM
Drywall install


MEP+Elctrical
Ready for re-install



UTILITY LEVEL MOD2

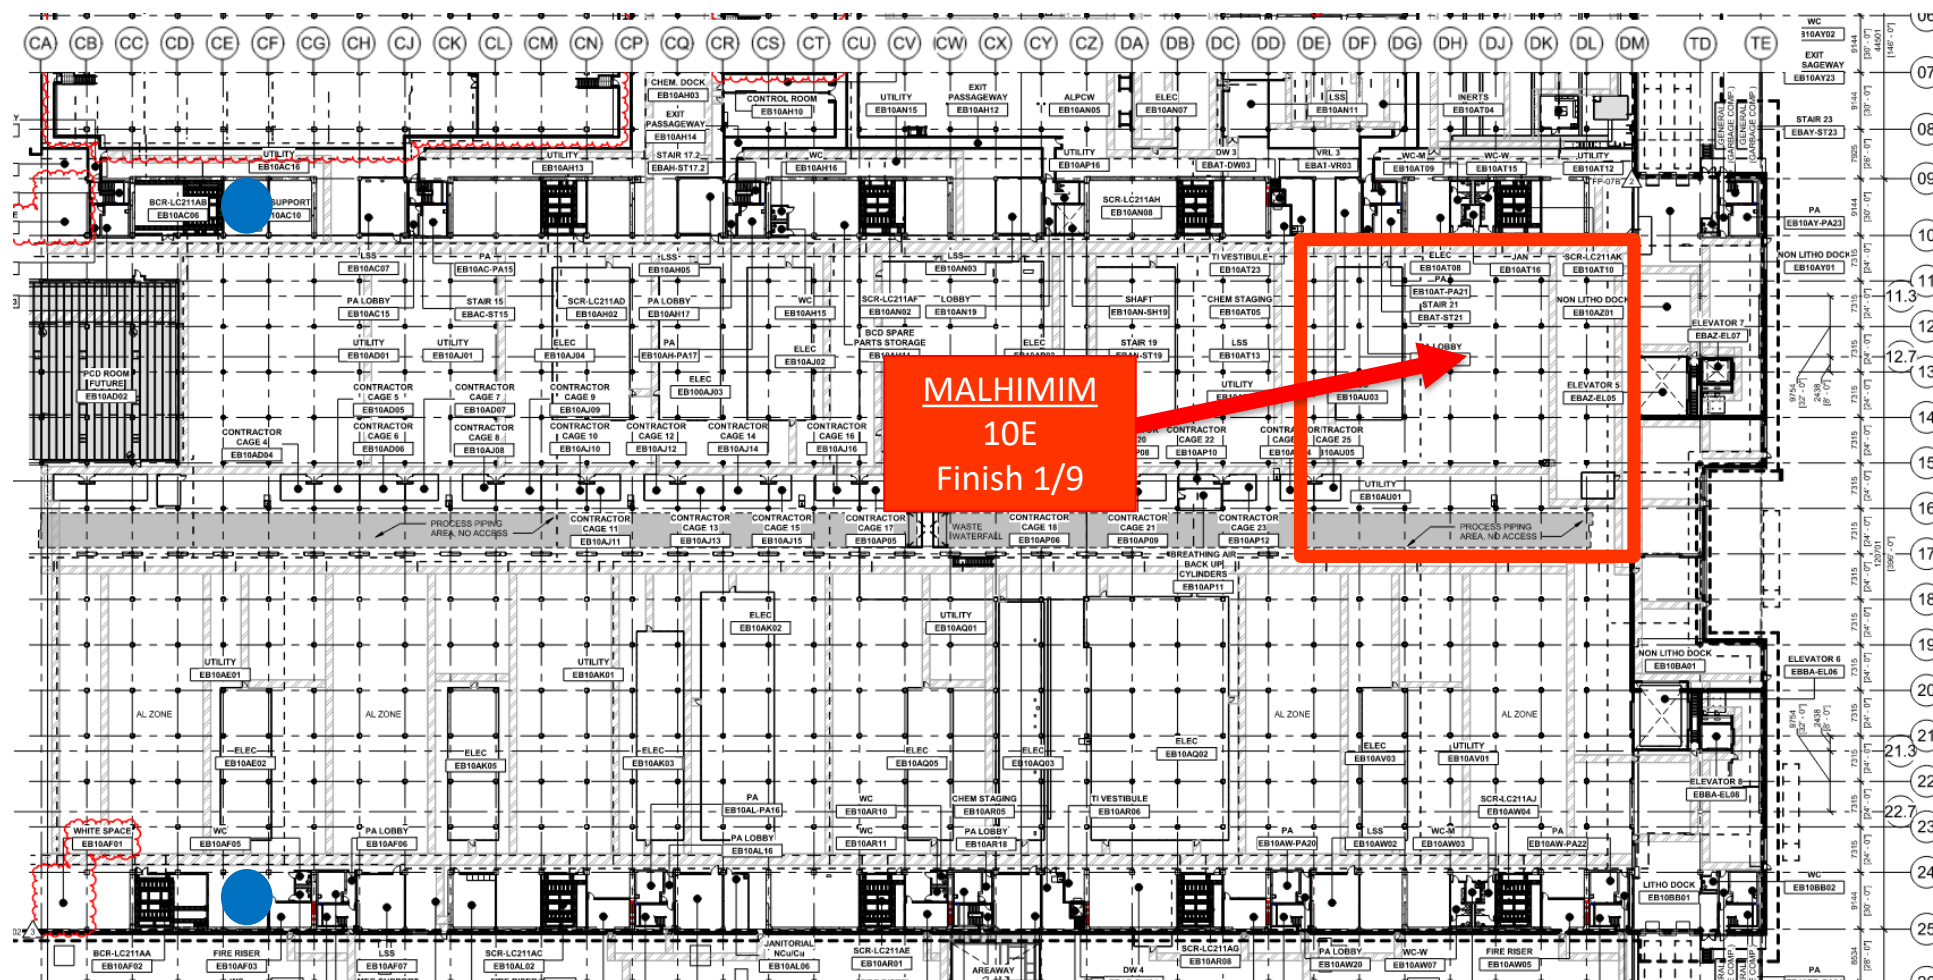


SUT 38.1 Accesses & Egress

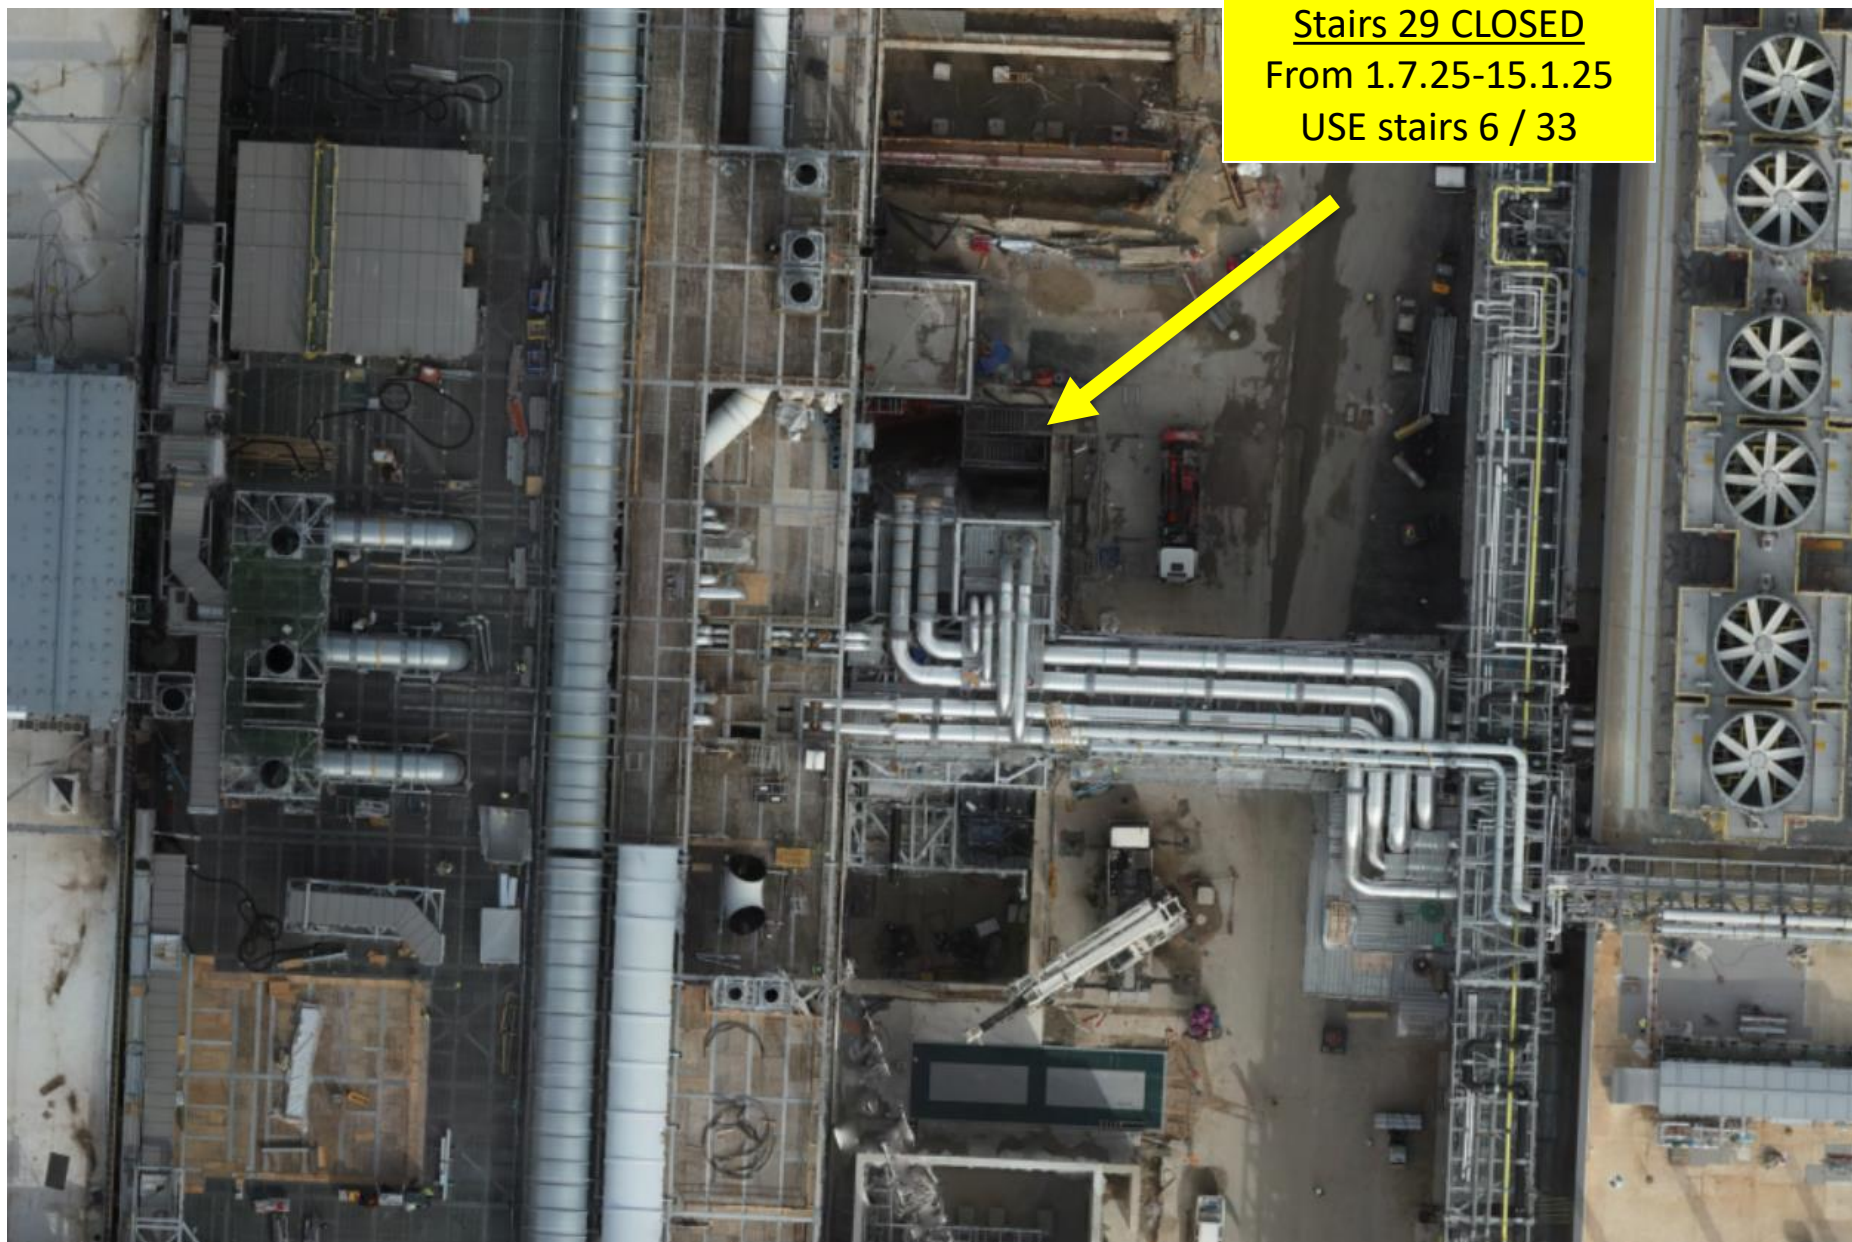

Stairs 29 CLOSED
From 1.7.25-15.1.25
USE stairs 6 / 33



SUT 38.1 LEVEL

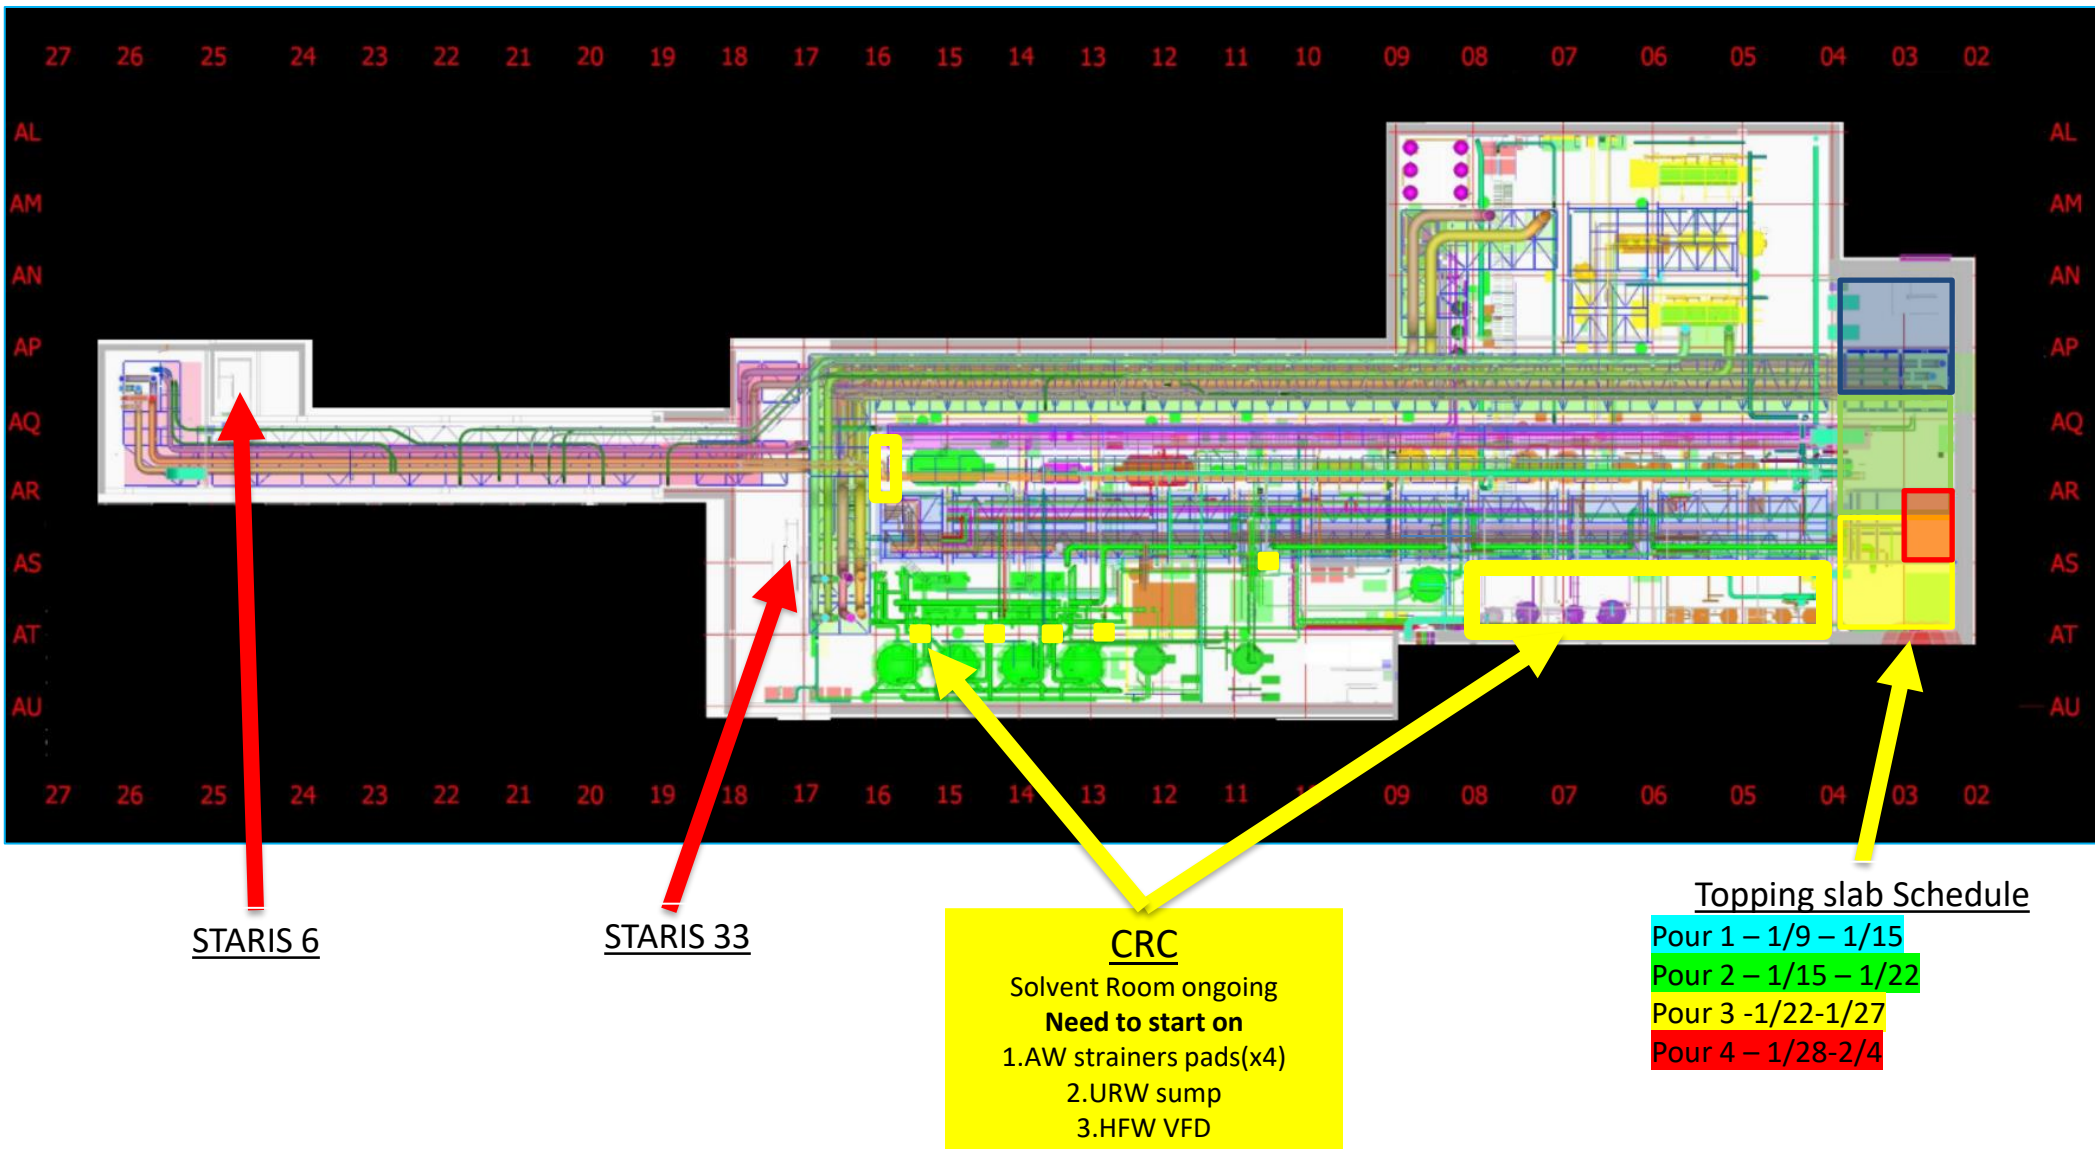




HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL

Rack 4b
Lifting
schedule
#6 –

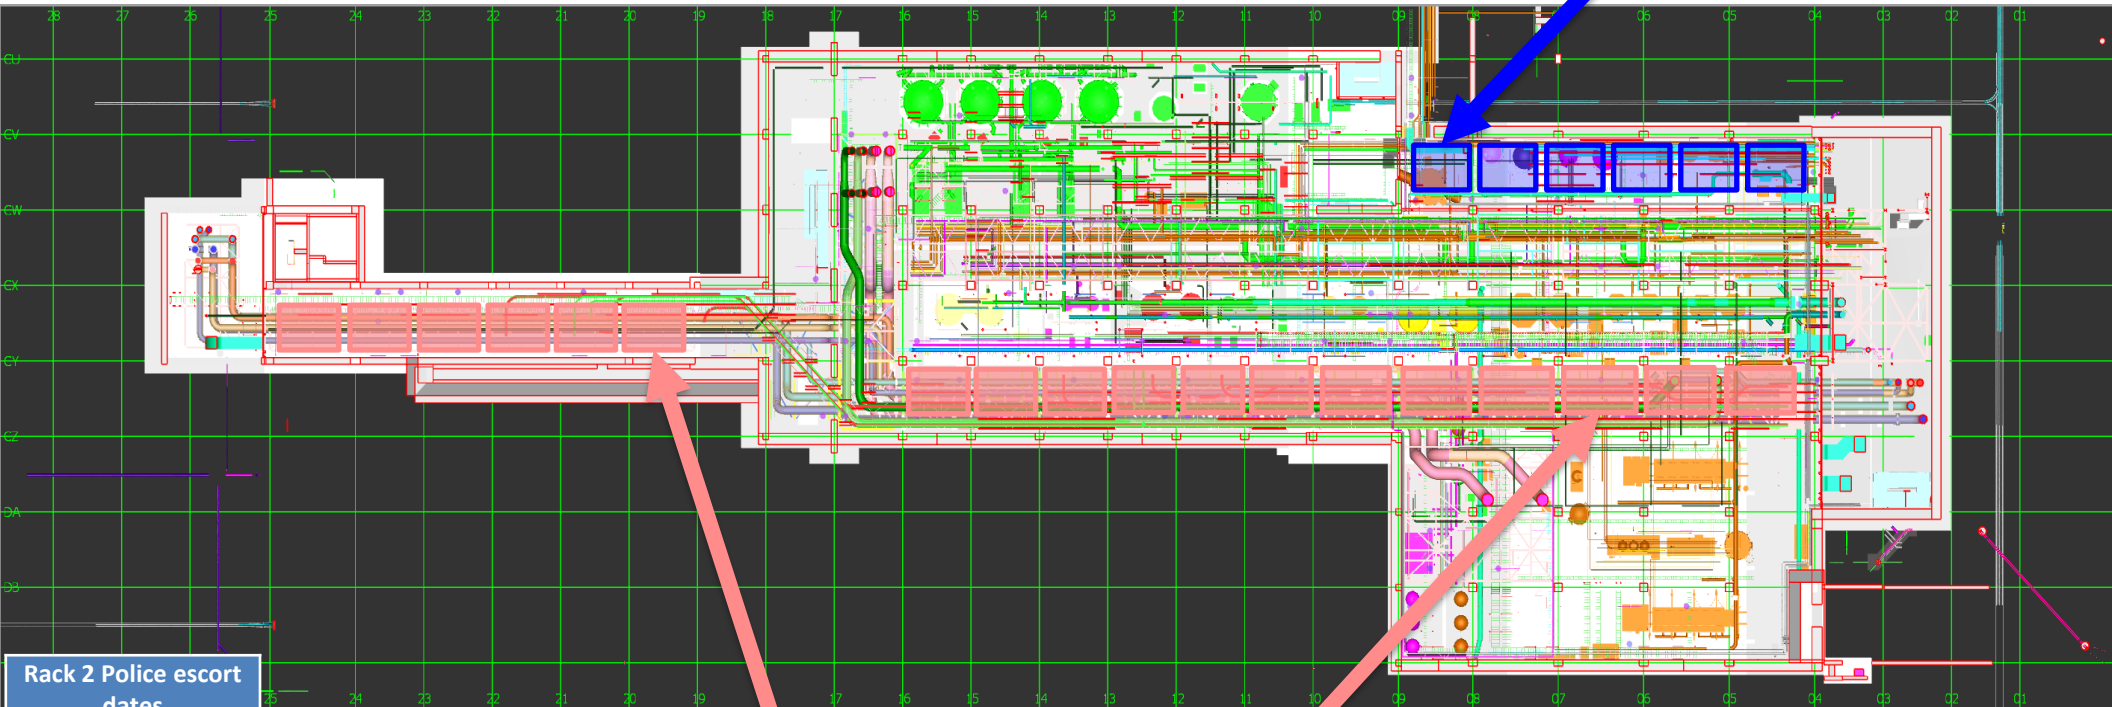

Rack6
MIMO -
Module #1
12.2.25

Rack 2
MIMO -
Module #10
2.2.25

Rack 2 Police escort
dates

v24.11.24

v25.11.24

v3.12.24

v9.12.24

v12.12.24

v15.12.24

v17.12.24

v22.12.24


5.1.25

14.1.25 > 2.2.25


3.2.25

9.2.25


SUBFAB BUILDOUT MOD 1

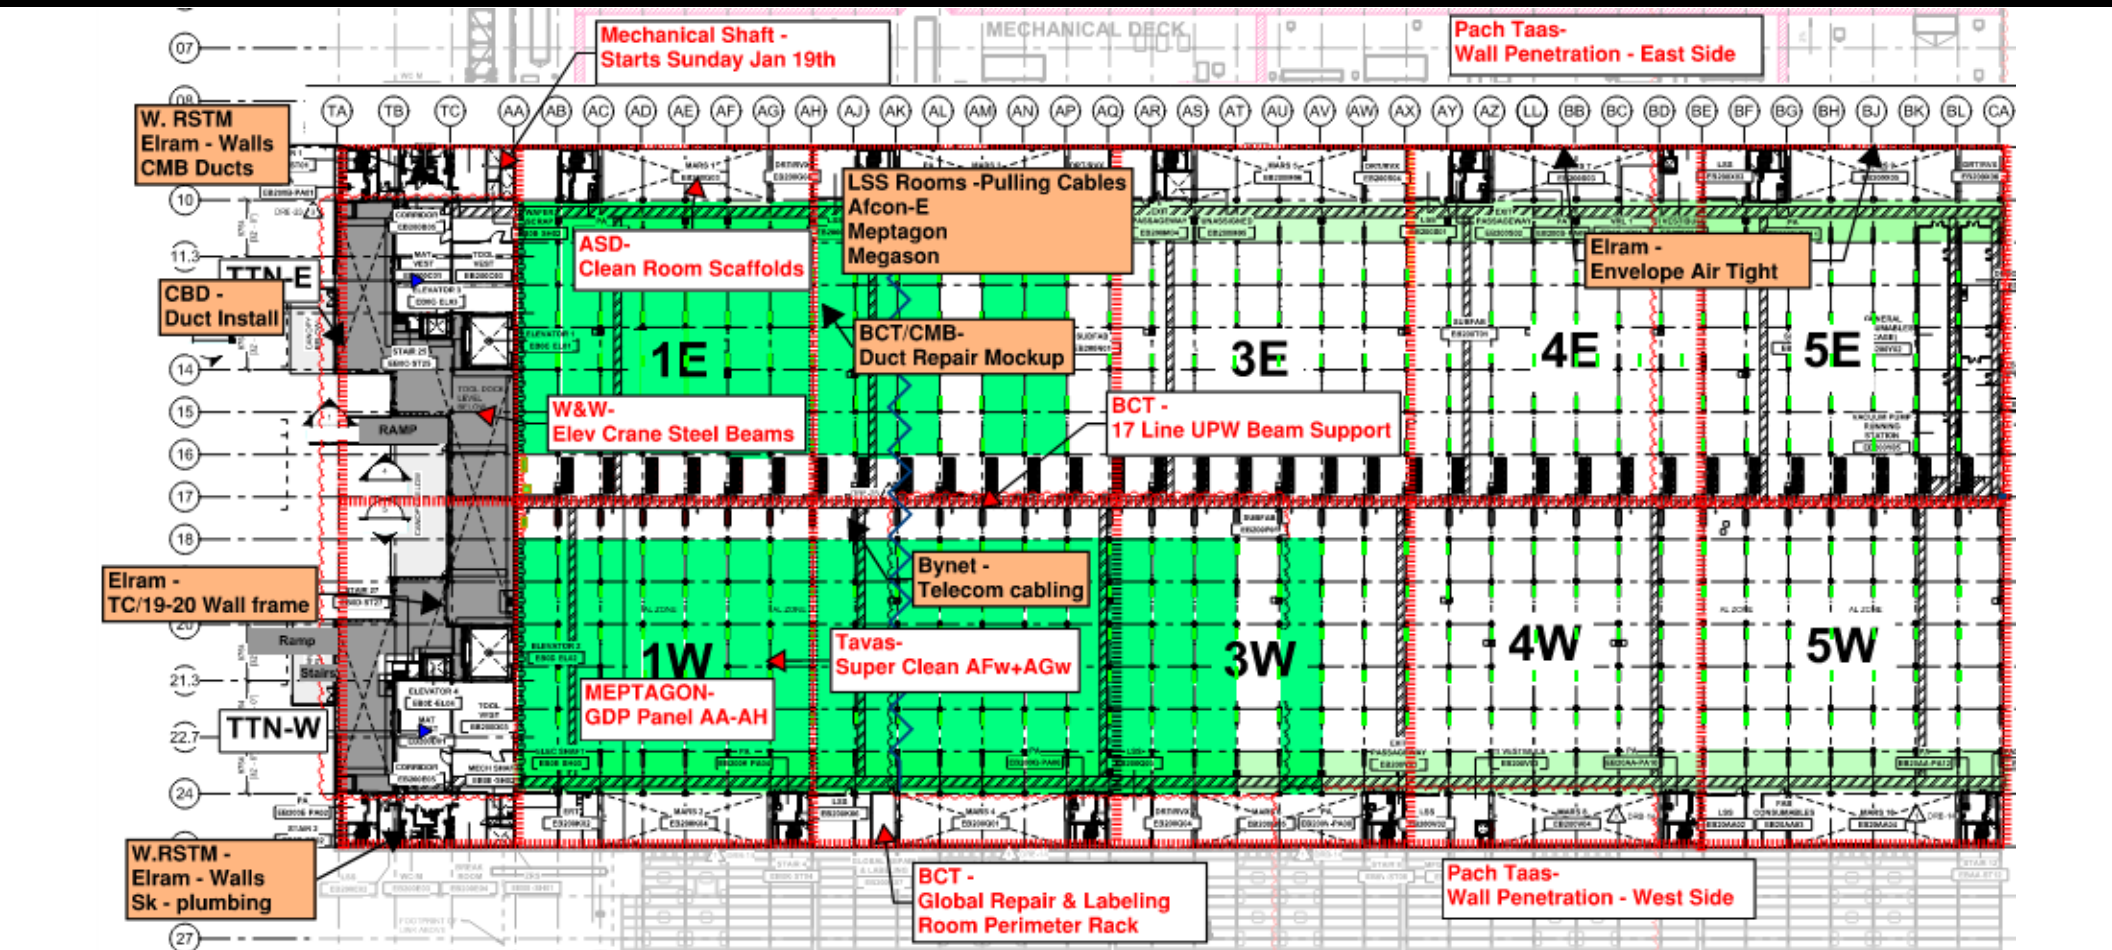


SUBFAB CRC TOPCOAT

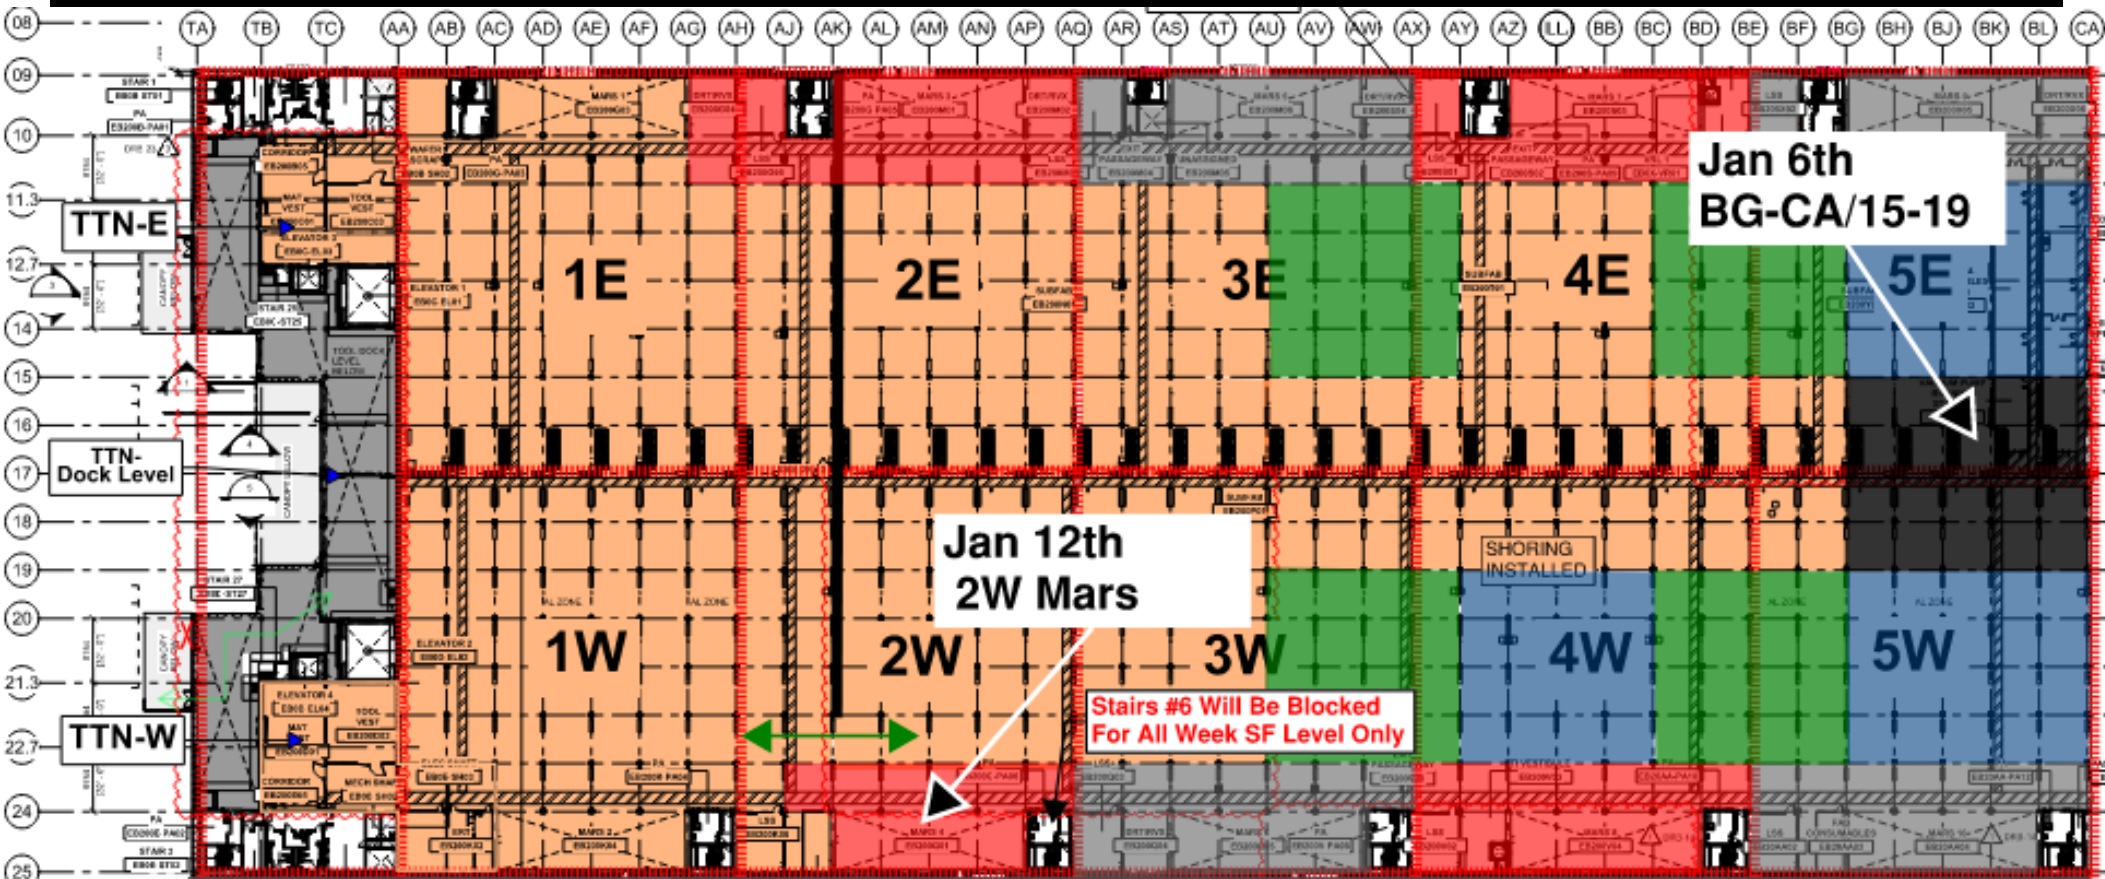


BCT Pressure Test Today

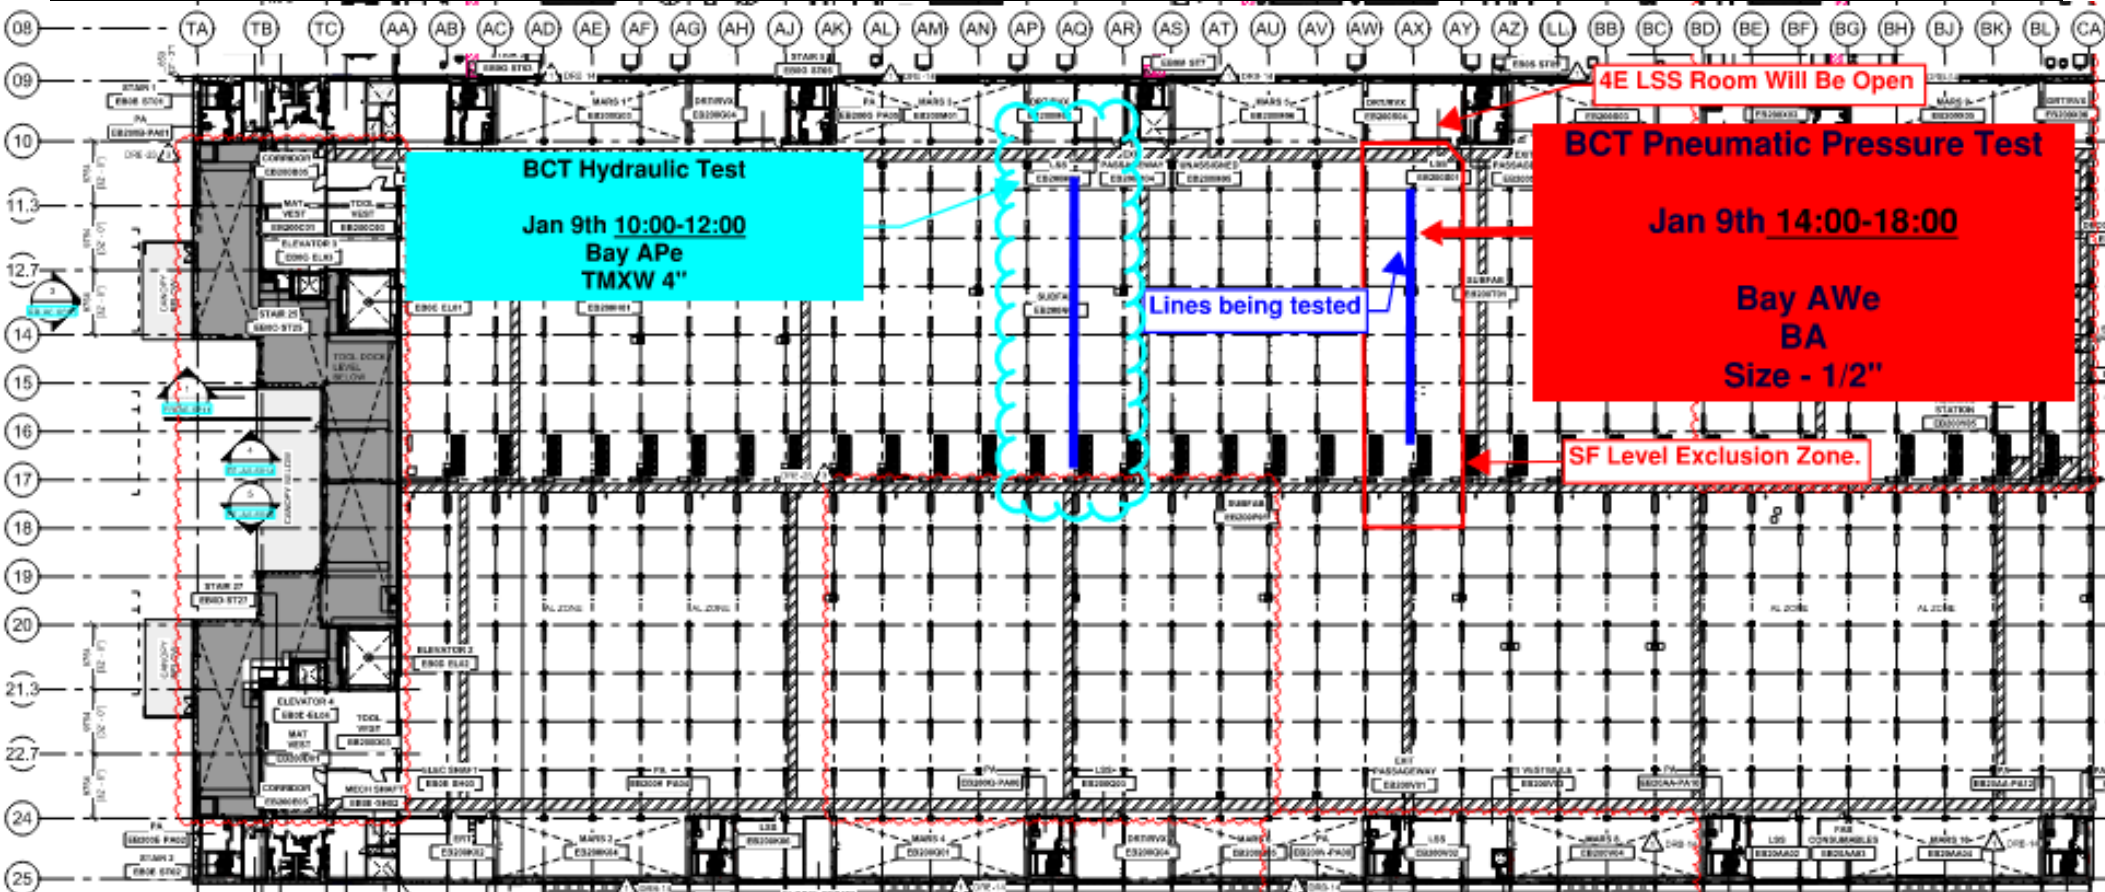


BCT Pressure Test Sunday

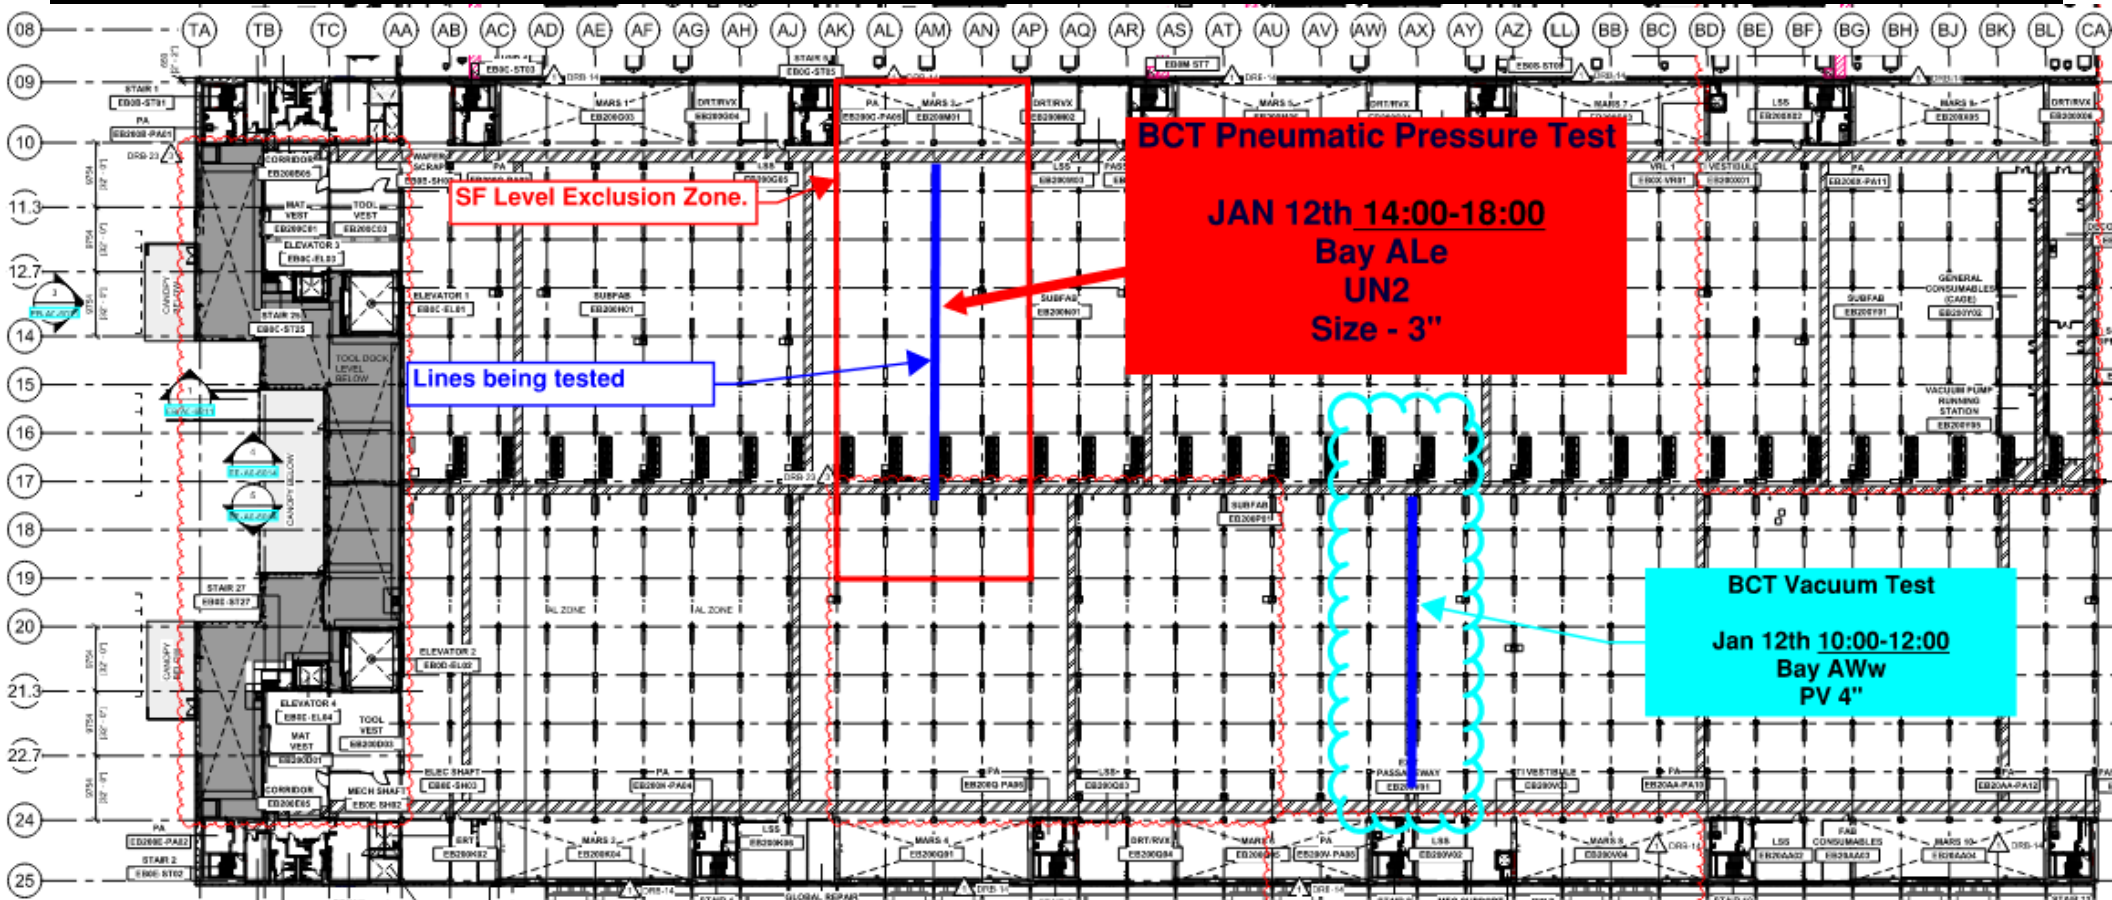

SUBFAB BUILDOUT MOD 2

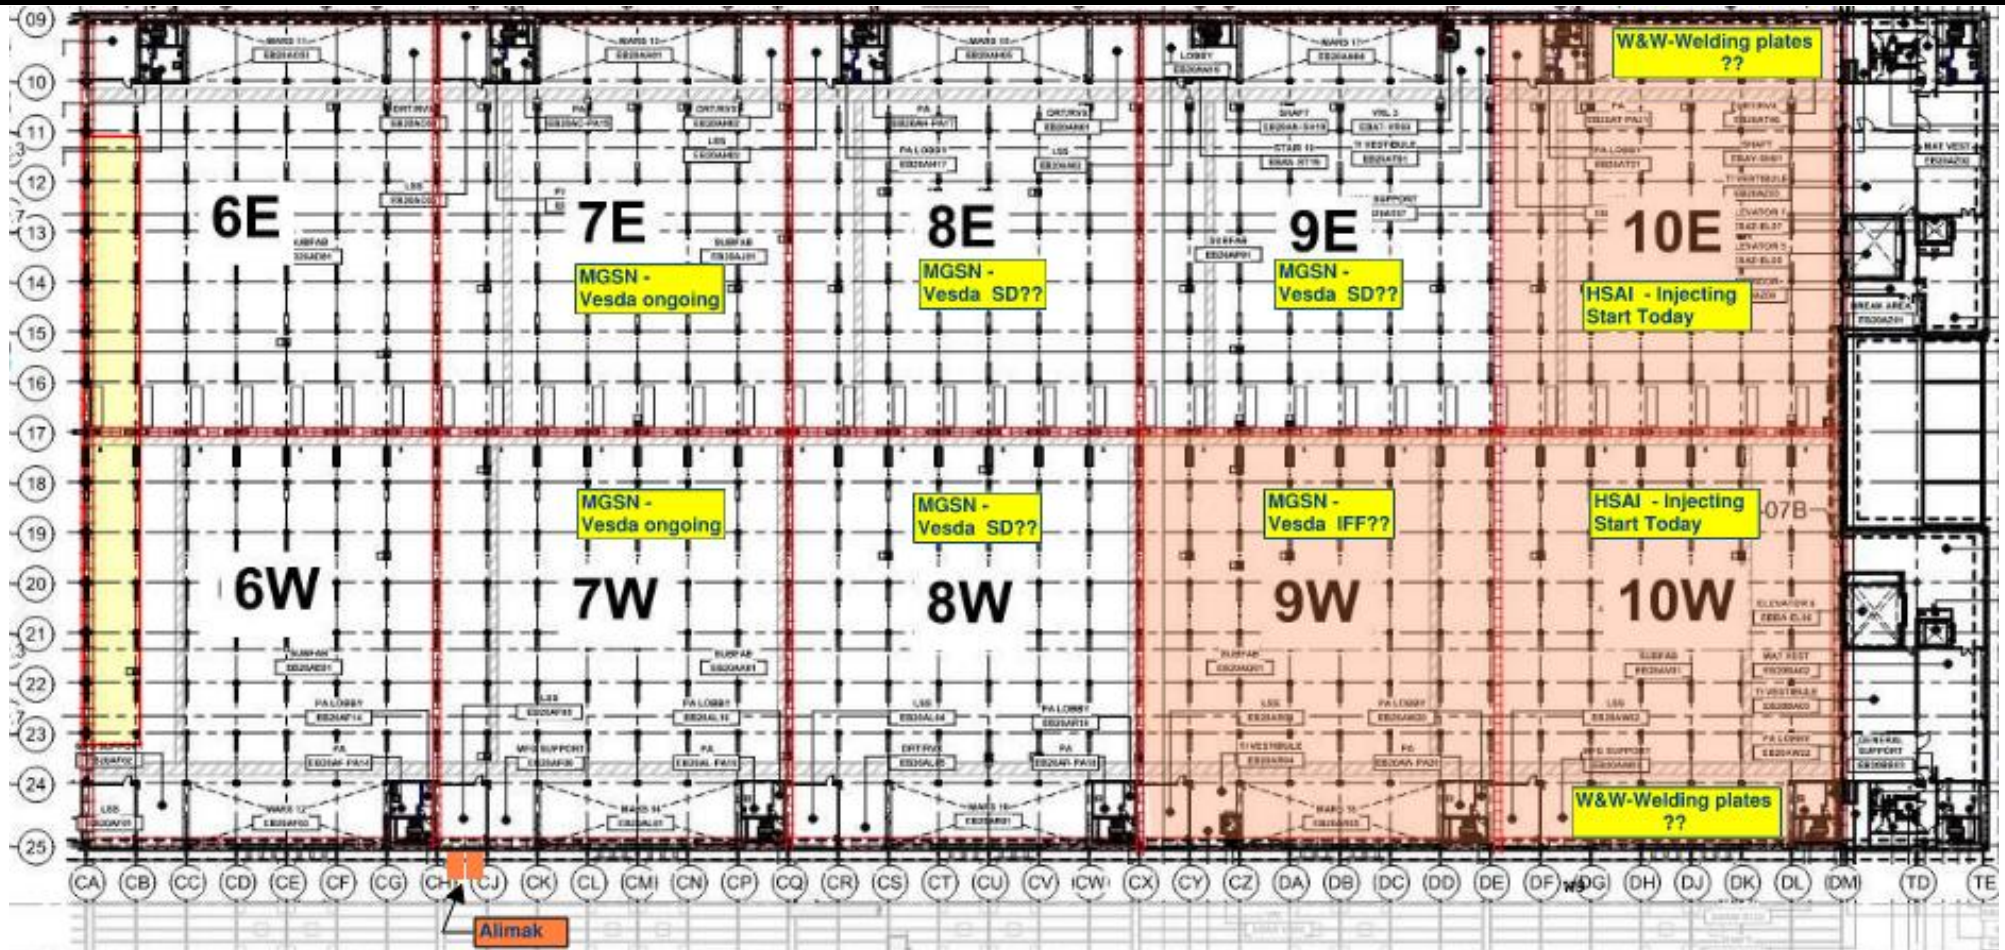




HSOI IS POURING ON
SUNDAY 12.1 NETT
SOMD NO EXIT TO CR
LEVEL ONLY


CR level:


- **Afcon** - Cable trays, modules and stickers
- **MB** - Pipes and drops
- **Elram** - Columns/shaft walls.
- **Meptagon** - EMT Pipes+devices. TET/NET devices all areas
- **D&P** - Stick build+ separation walls
- **Tzur-esh** - 1W blade paint
- **HYG** - Deck and bent plates
- **Talad** - UPN install, ceiling grid, lids removal

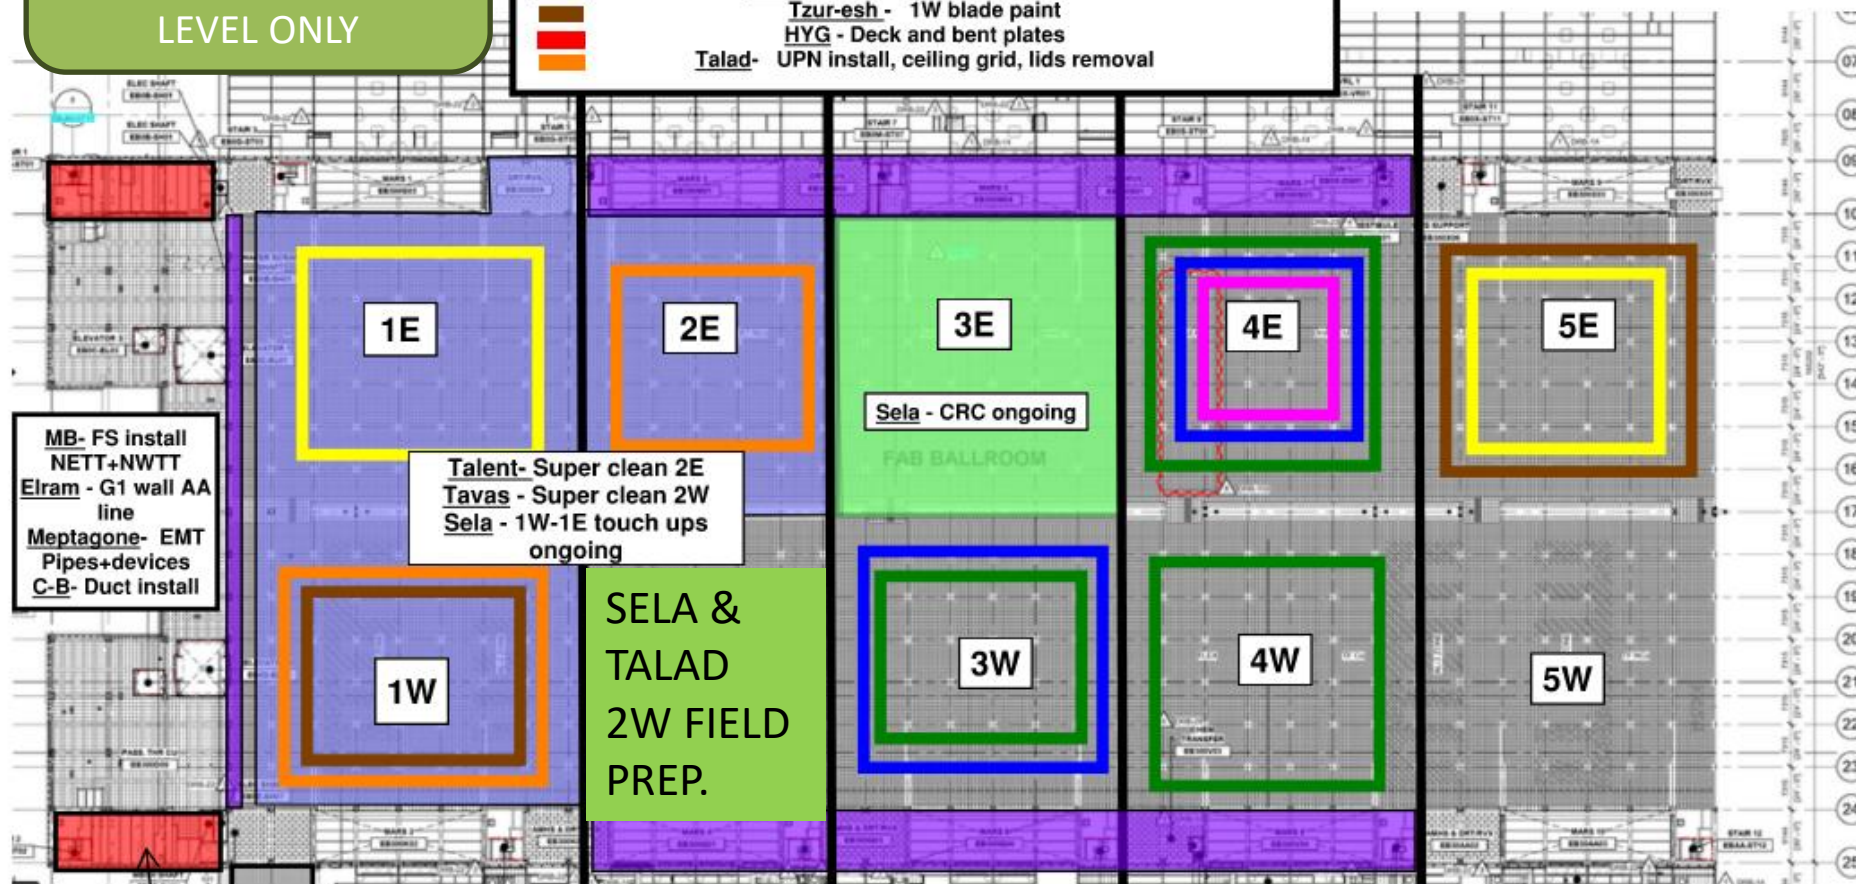


LINK-SELA
STARTED
FIELD PREP


LINK MOBILE SCAFFOLD
CHEMO WELDING
PACH TAAS FINISHING DUCT
INSTALATION

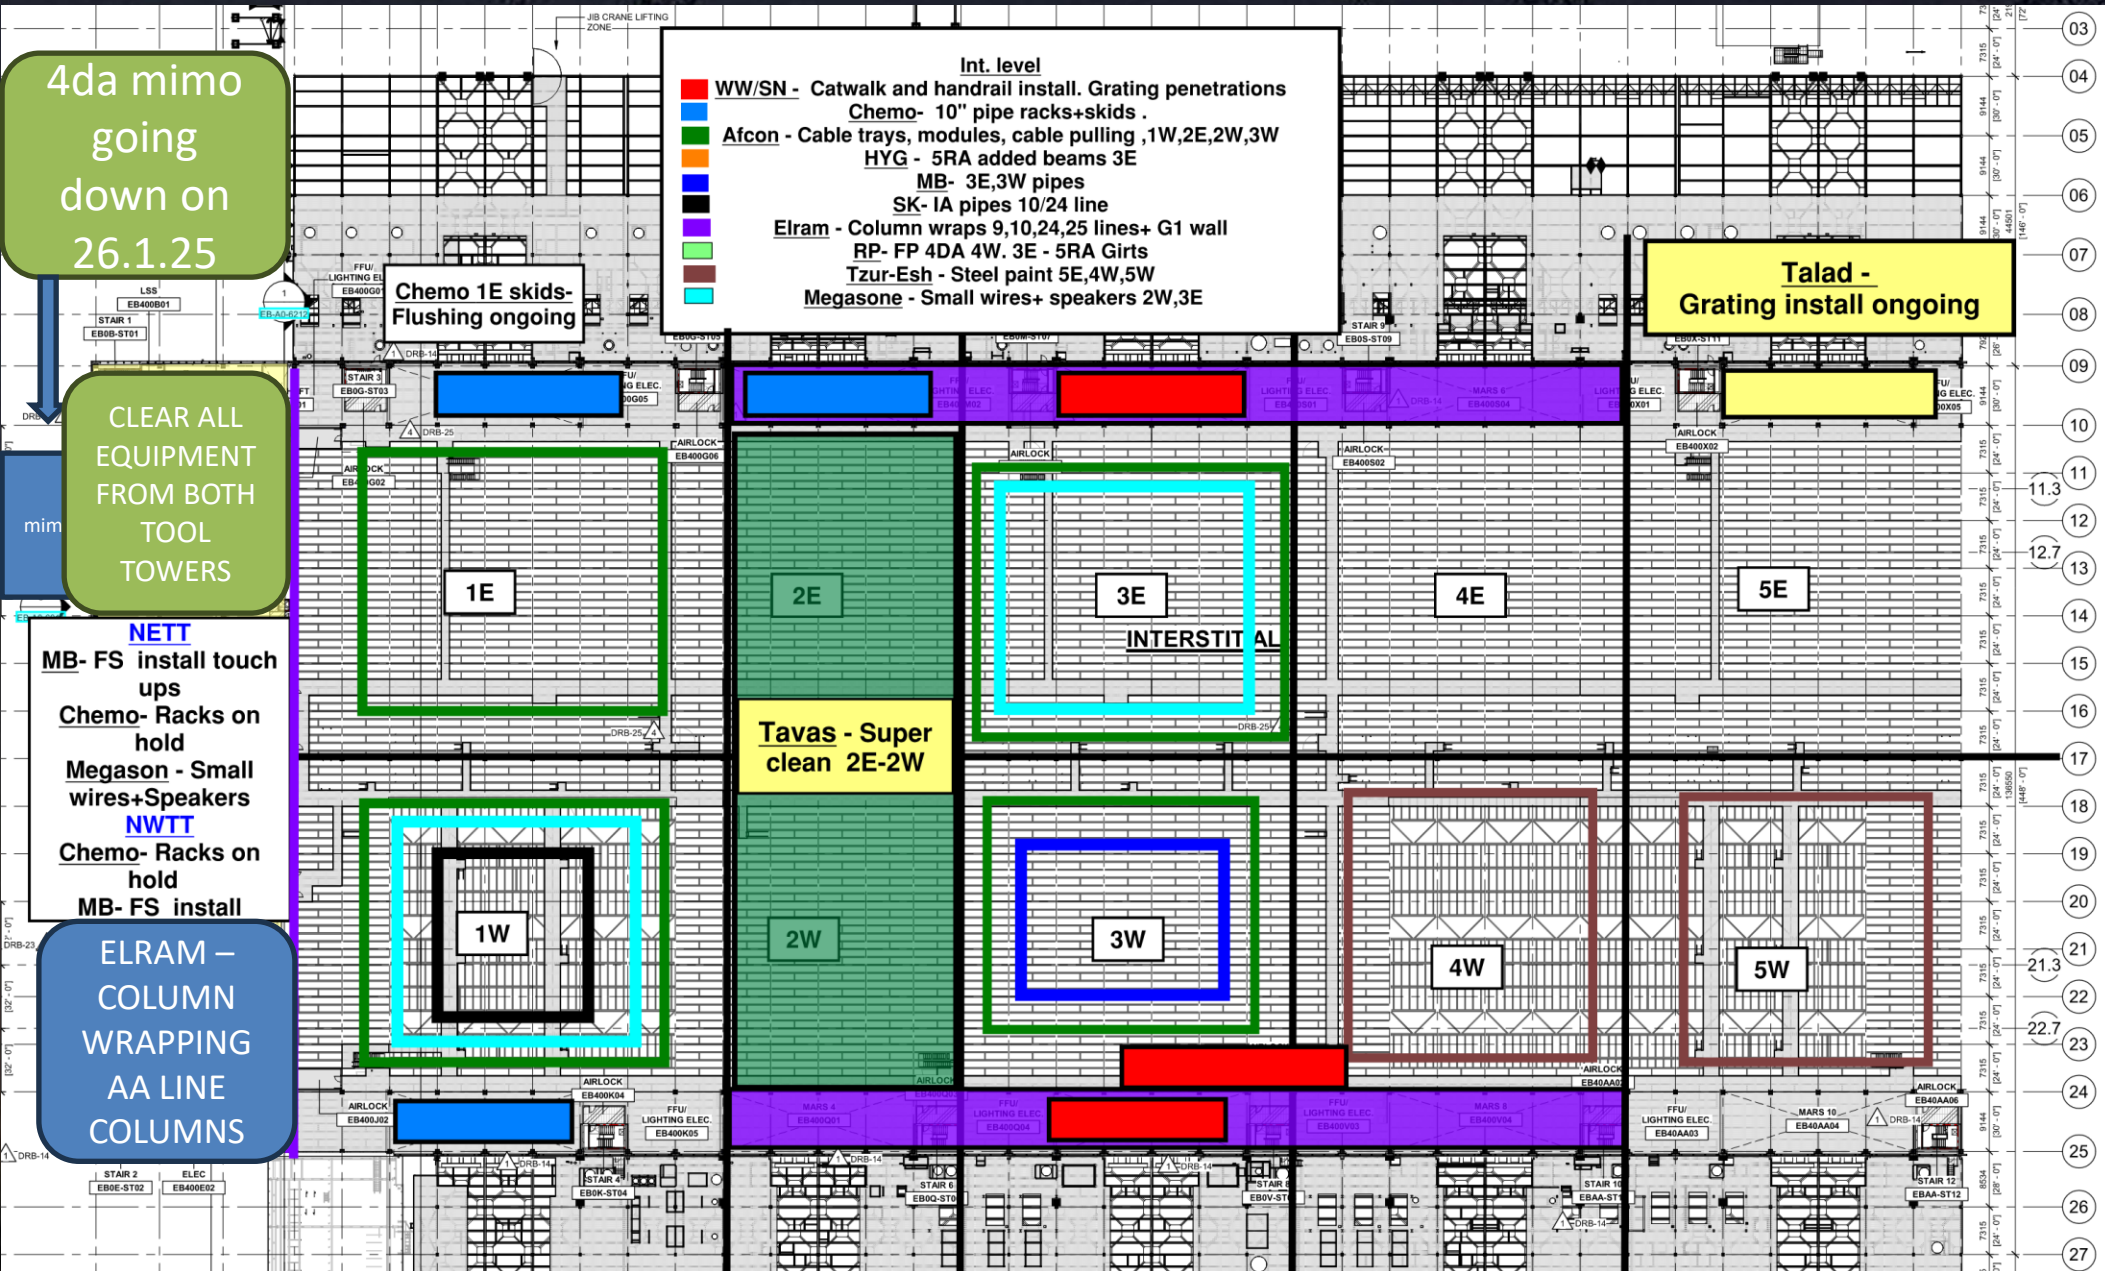



ROOF IS CLOSING THIS WEEK.

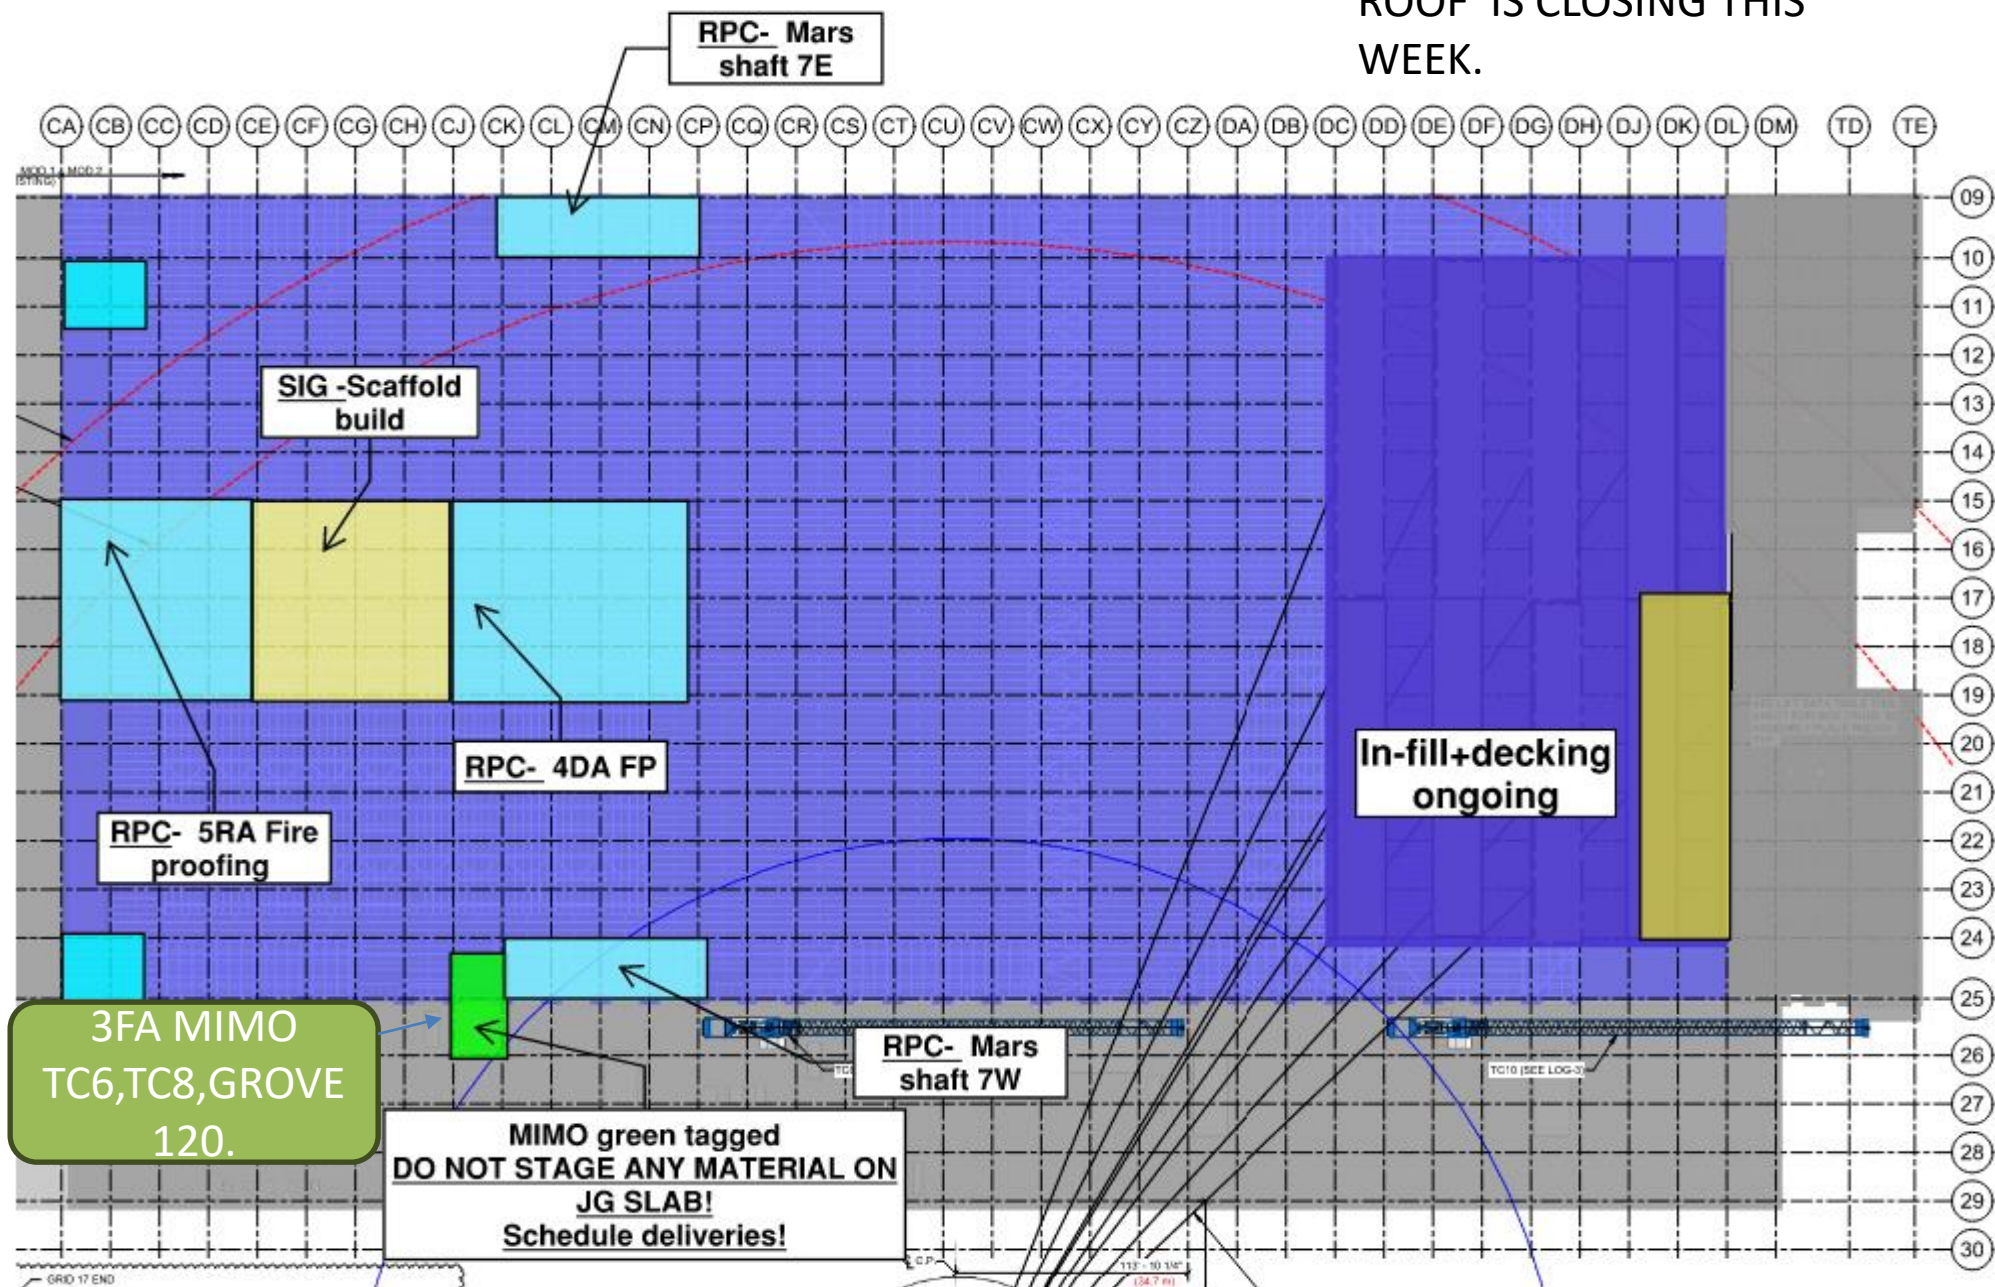


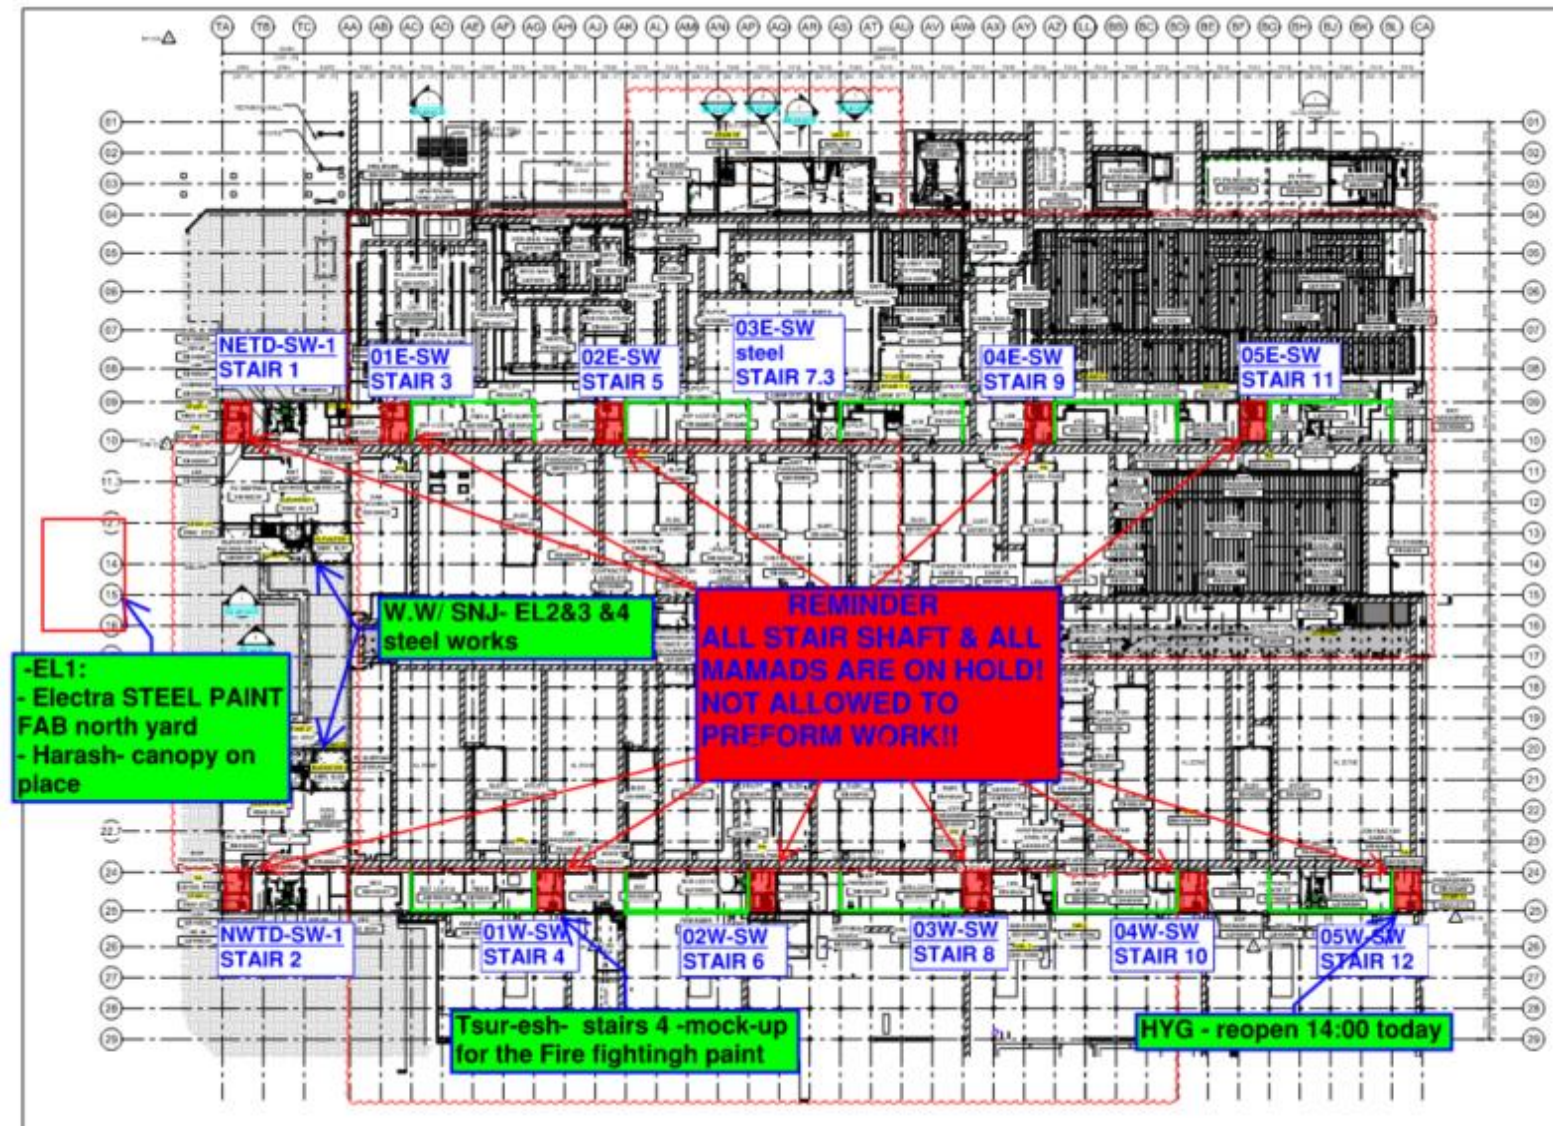

Mod 2 E House Roof
Picks.
Jan 14th @ 4:00 AM
Jan 16th @ 4:00 AM

Area to be
Closed for
Swing

Condensed
Barricade
for Bolting.

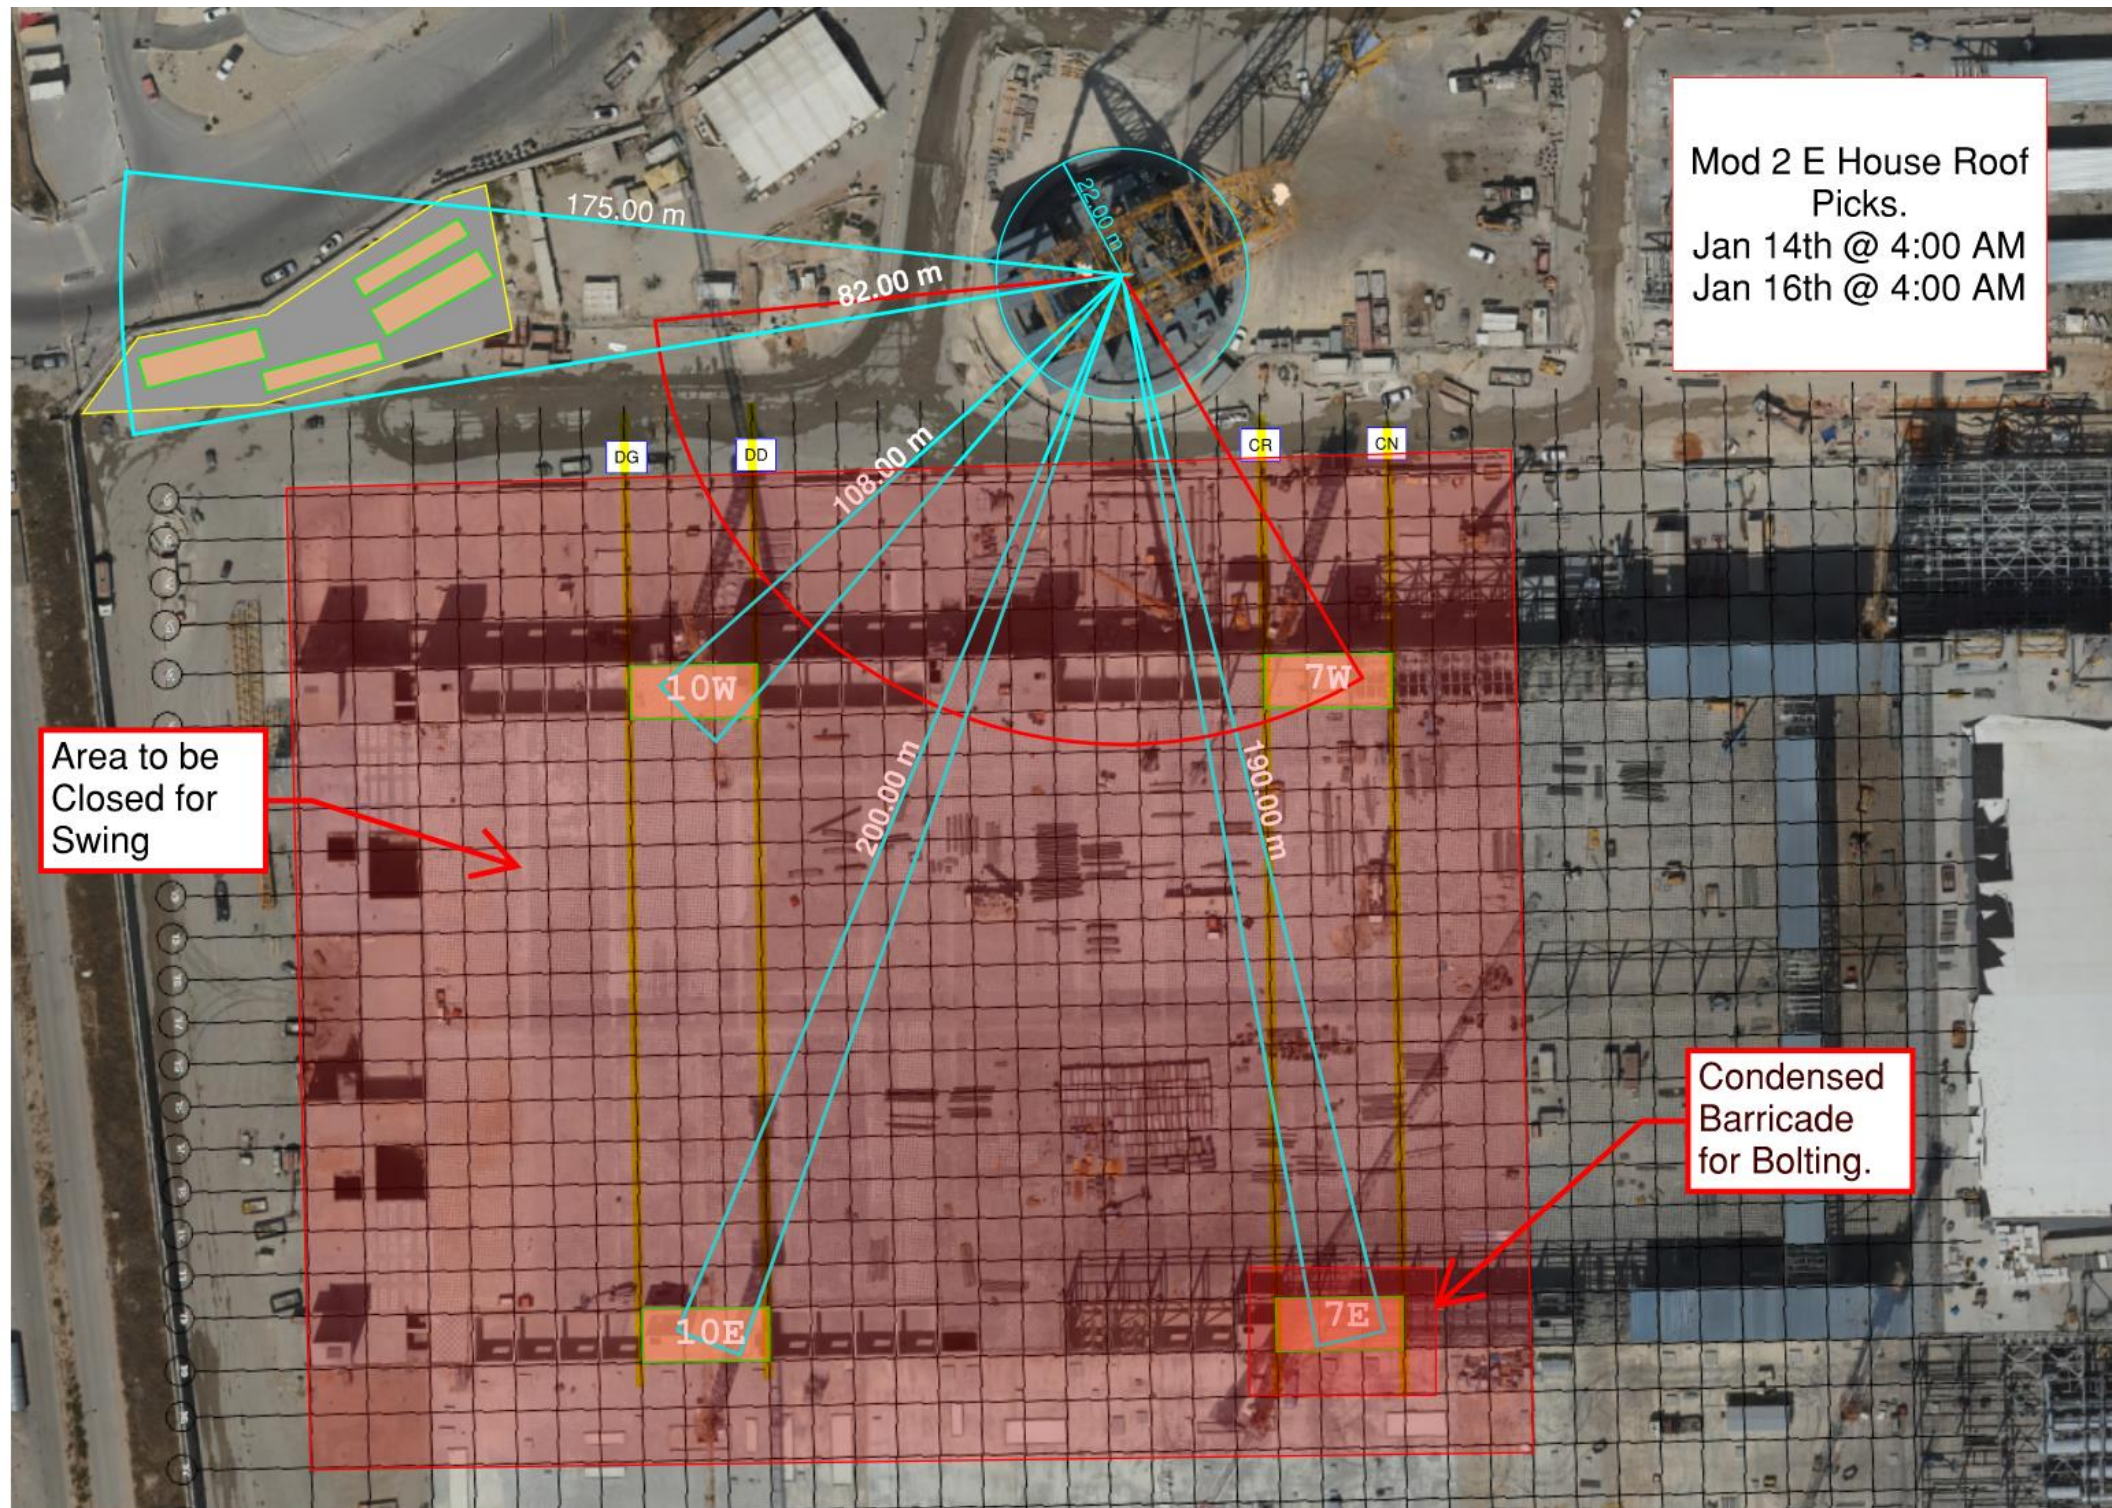



Siding - West FAB - JYG


BLOWDOWN 30%

Link

[illegible]

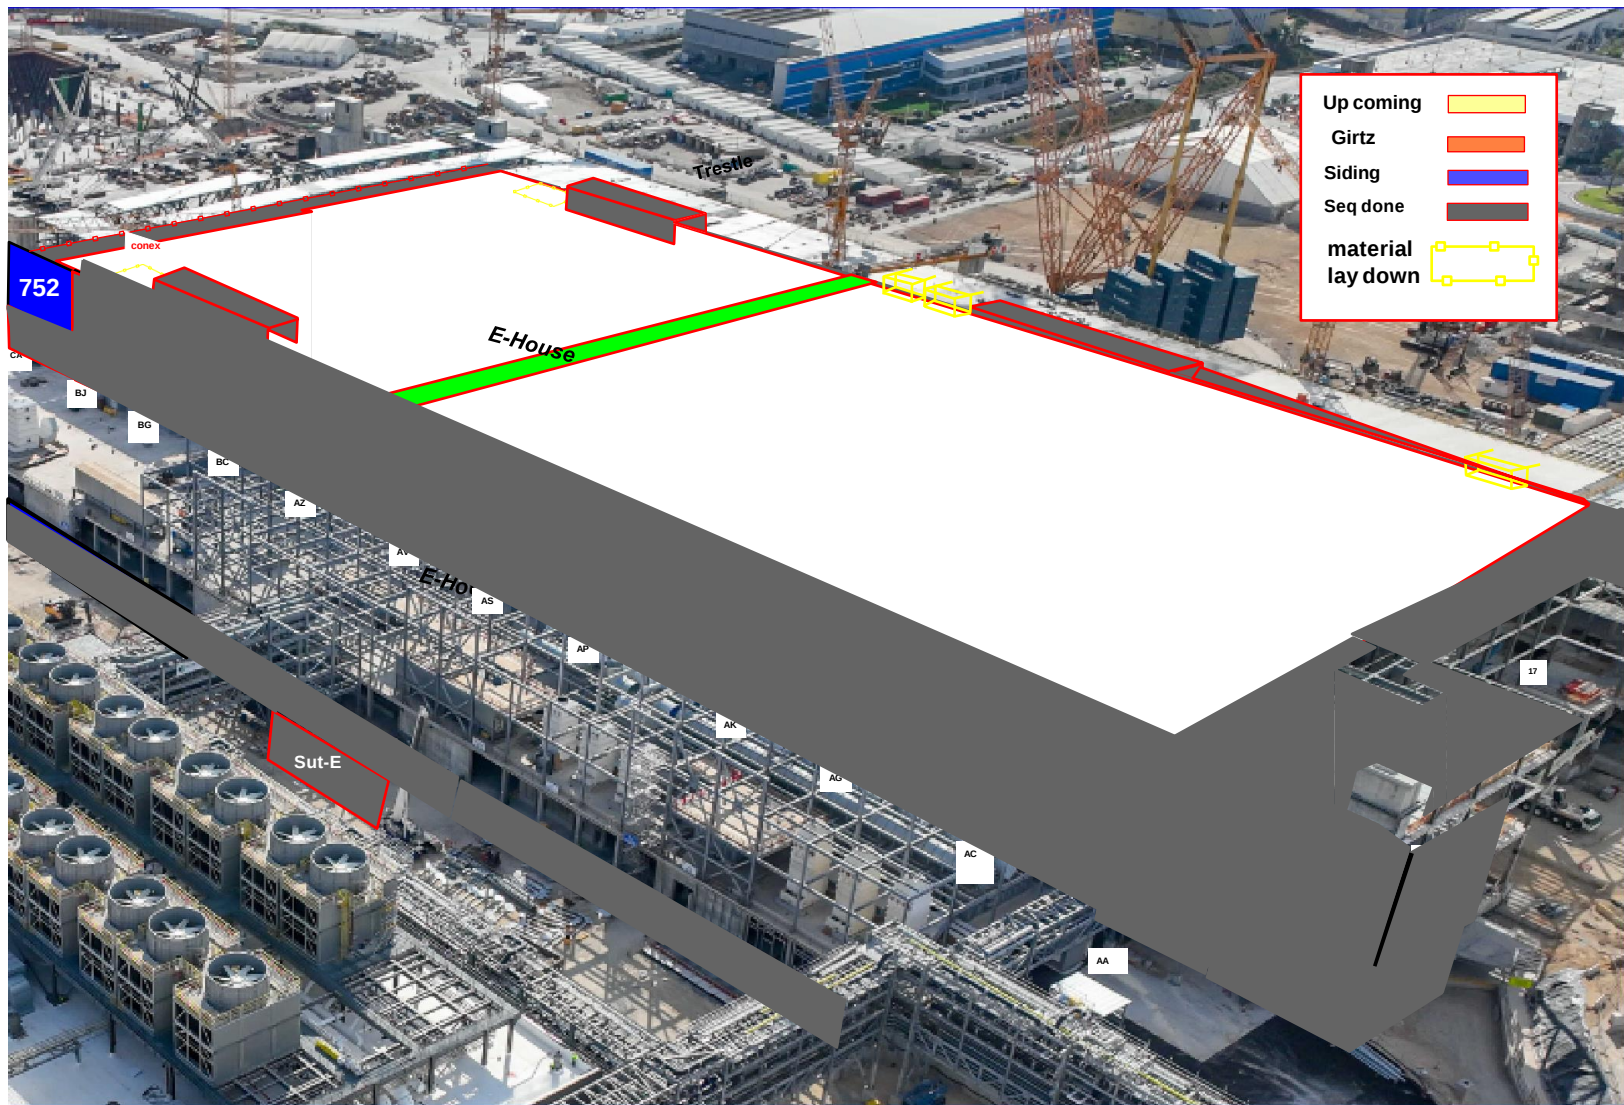

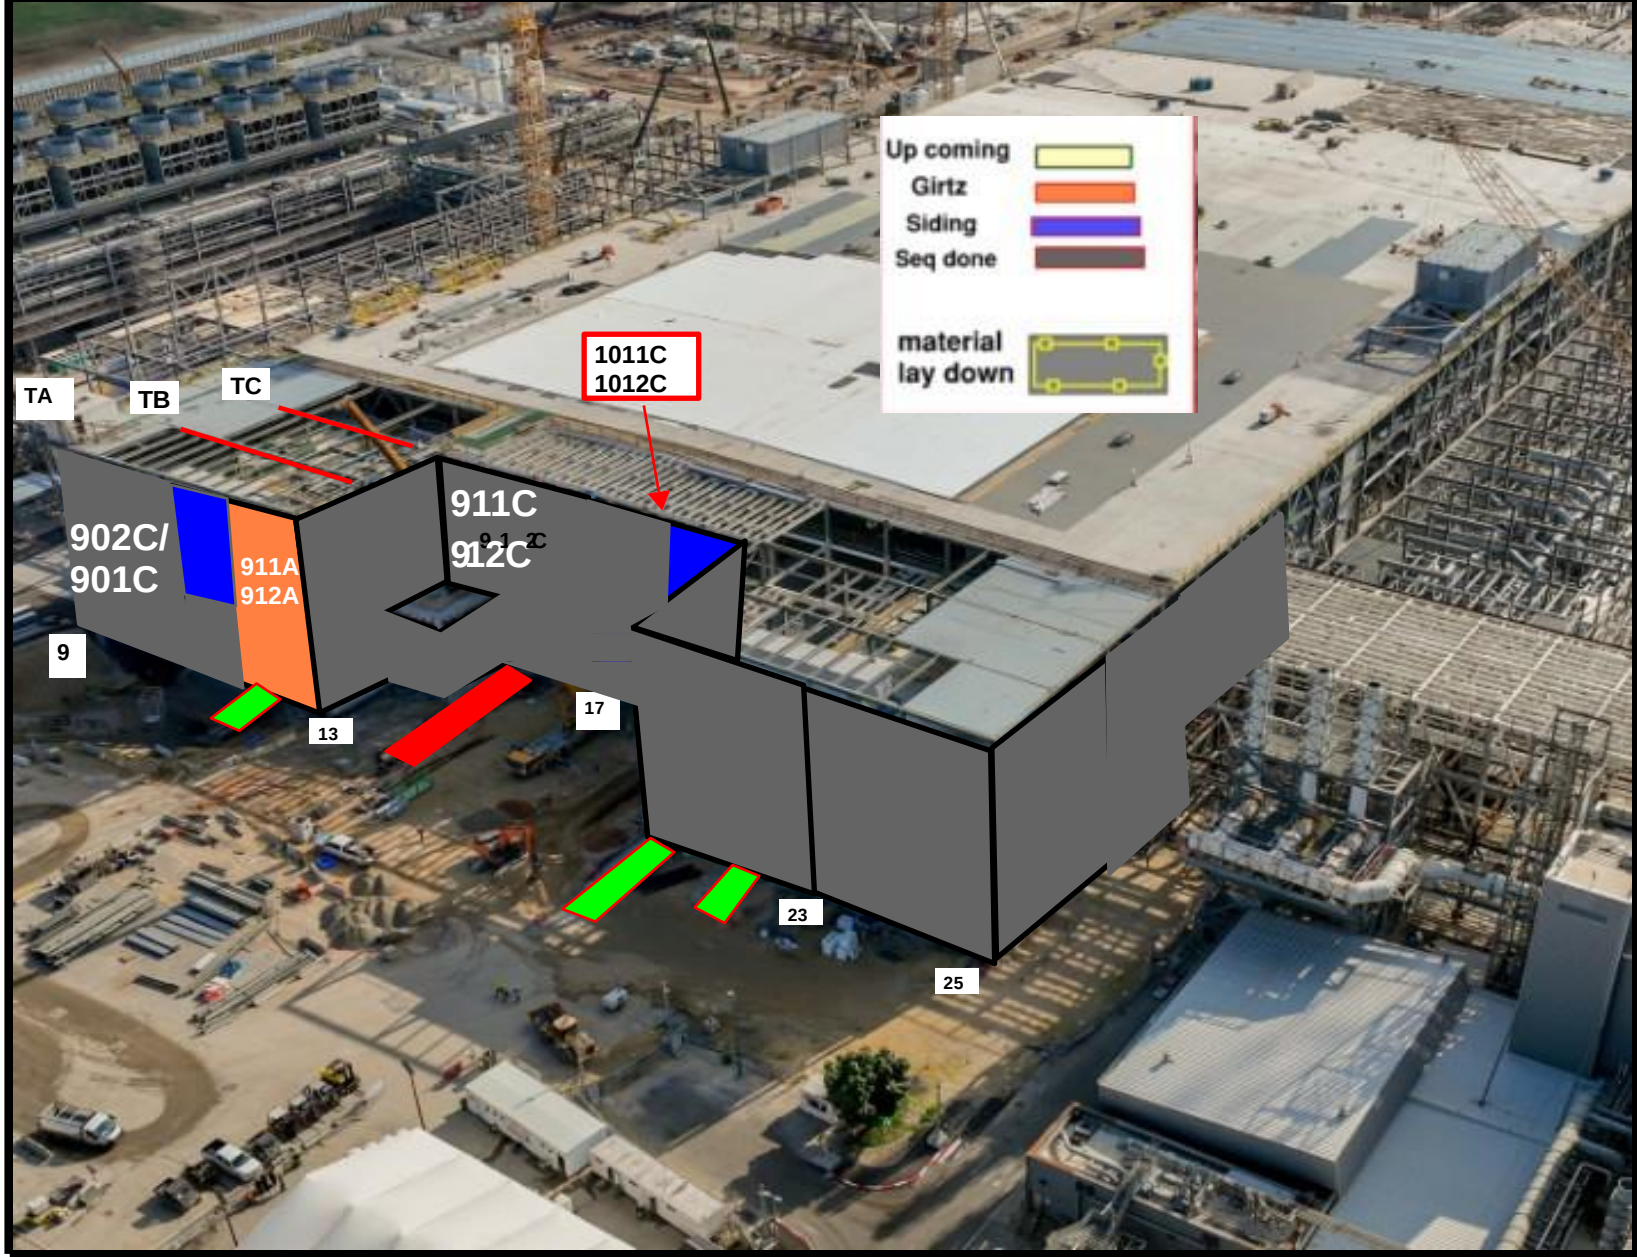

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

TA

TB

TC

1011C
1012C

902C/
901C

911A
912A

911C
912C


9

13

17

23


25

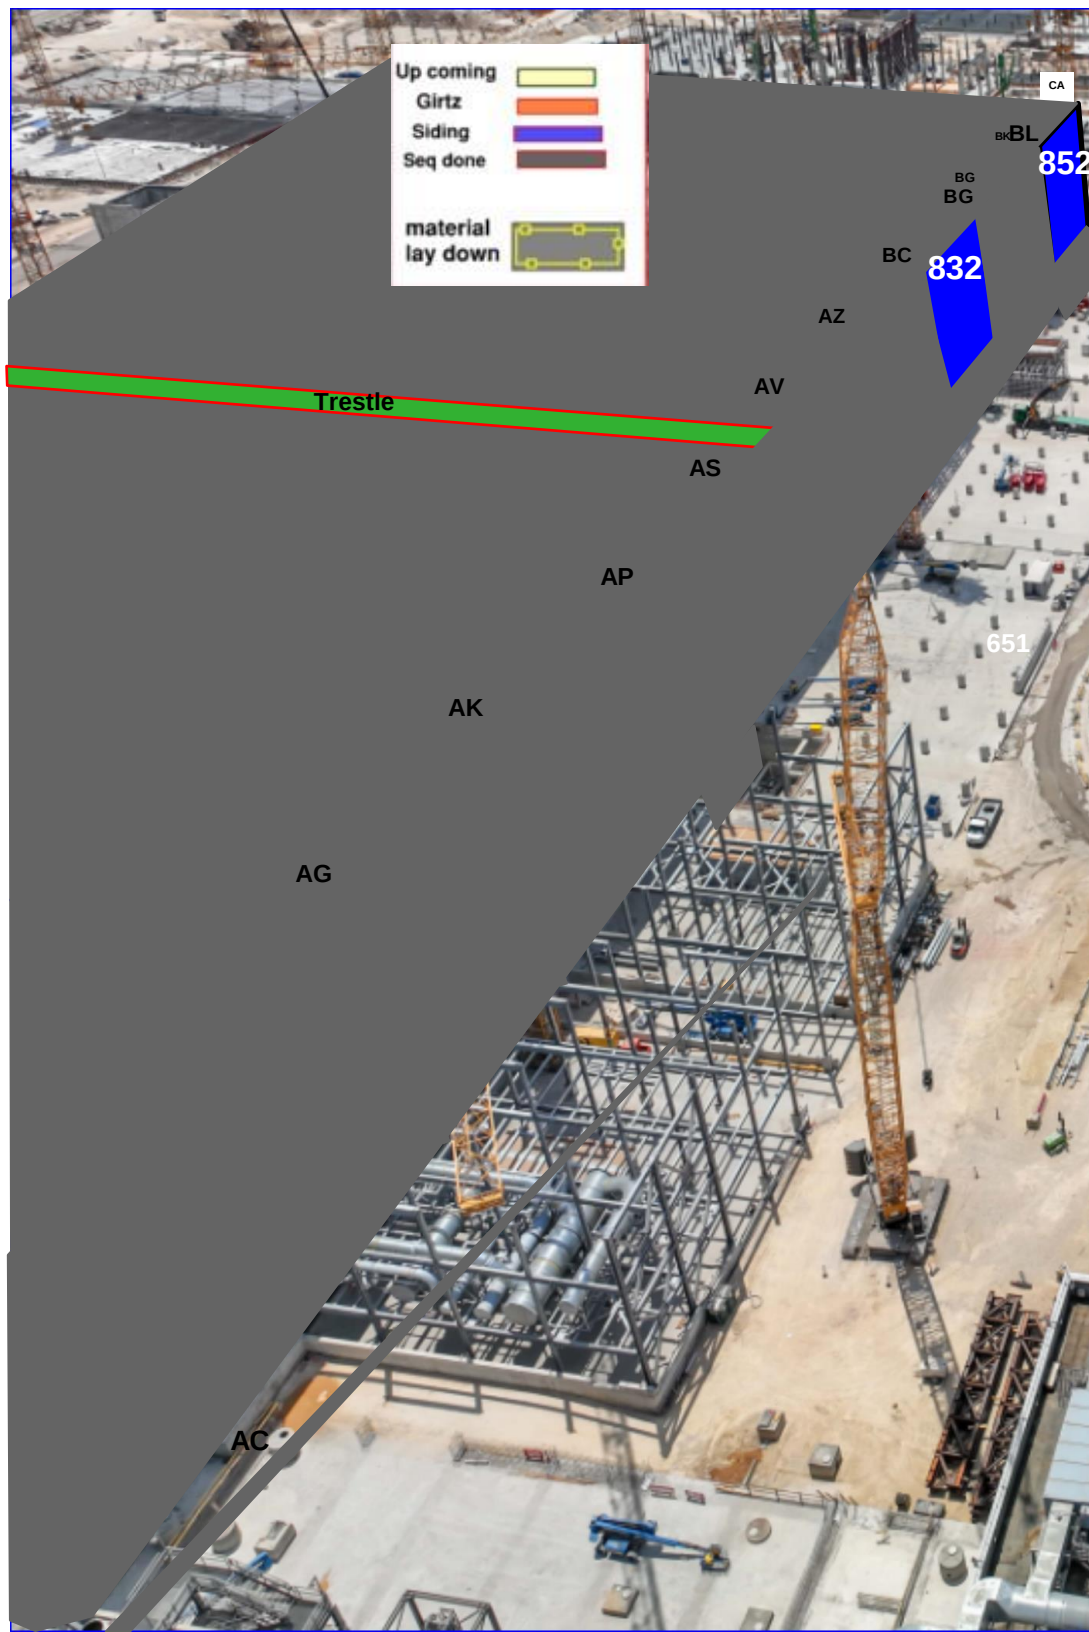

PSSS.1

Utility Level
1YA

PSSS Roof
2SA

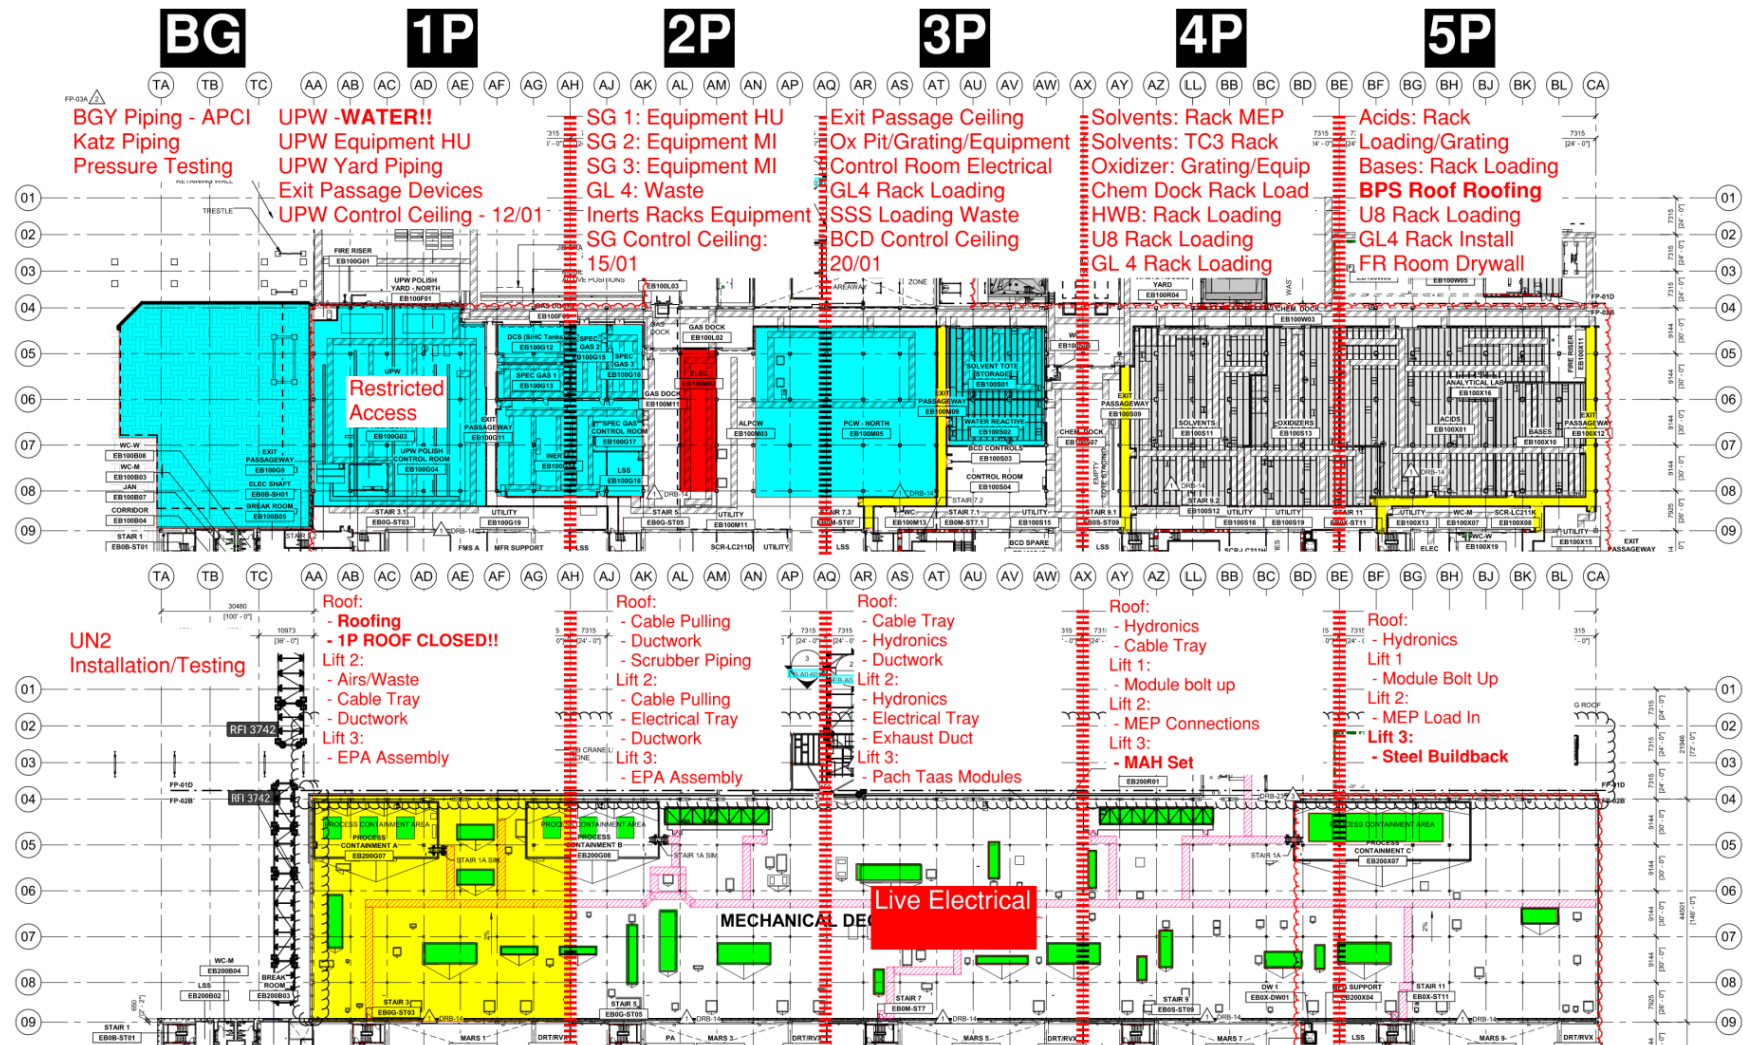

PSSS.2

6P


7P

8P


9P

10P


Utility Level
1YA

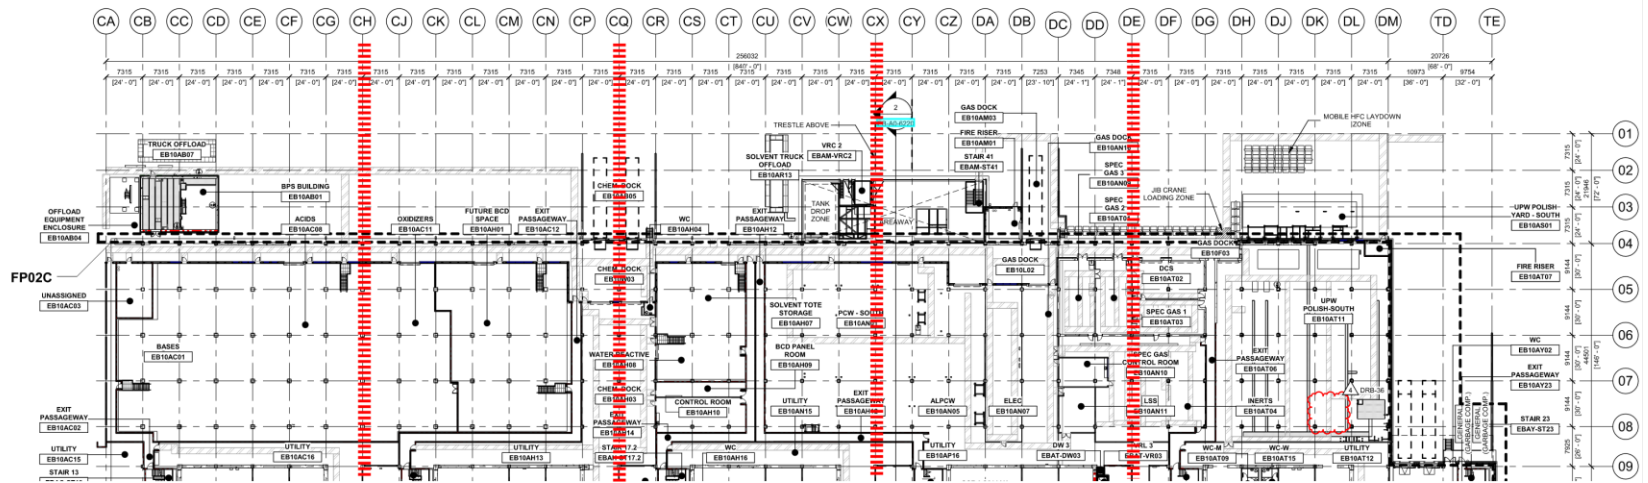


PSSS Roof
2SA

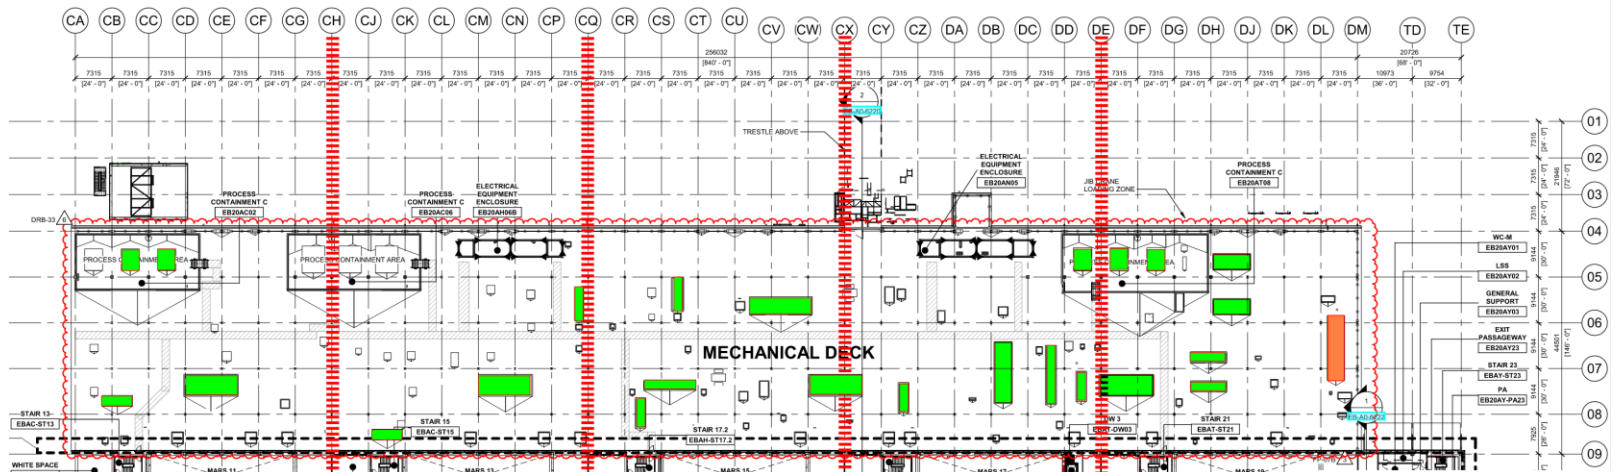

PSSS Pressure Tests

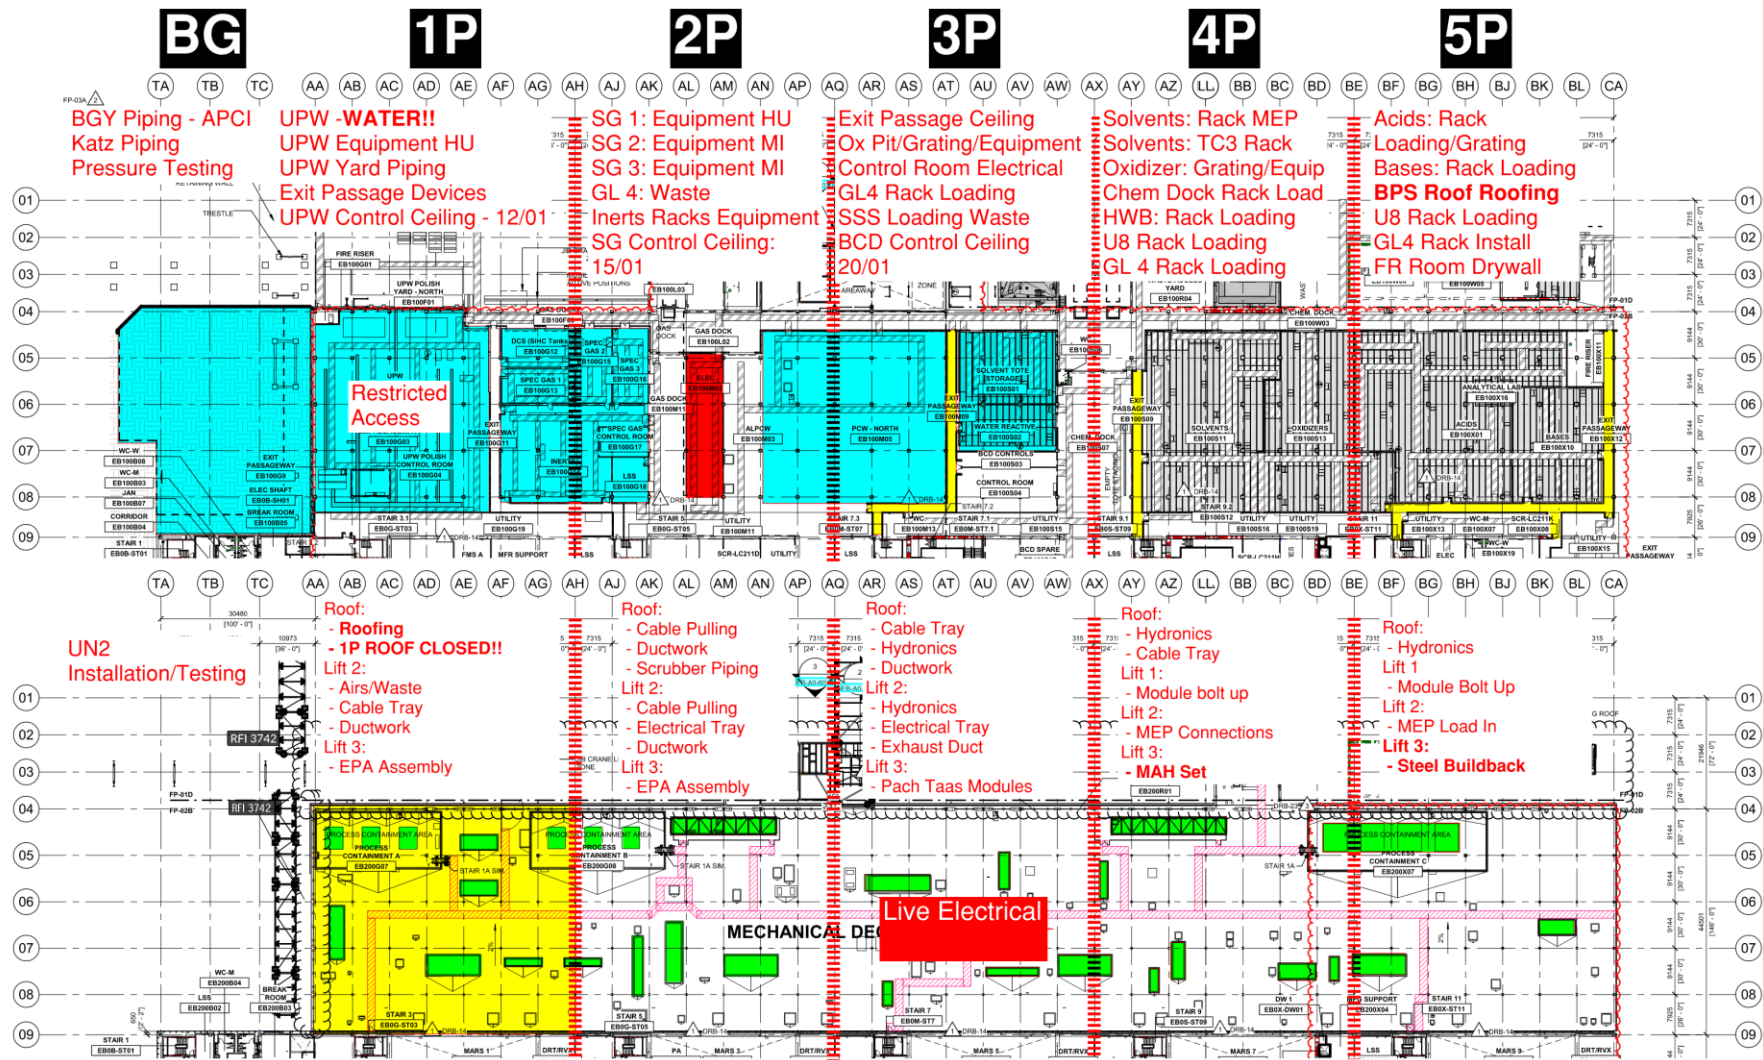


3800 Hoisting WW02

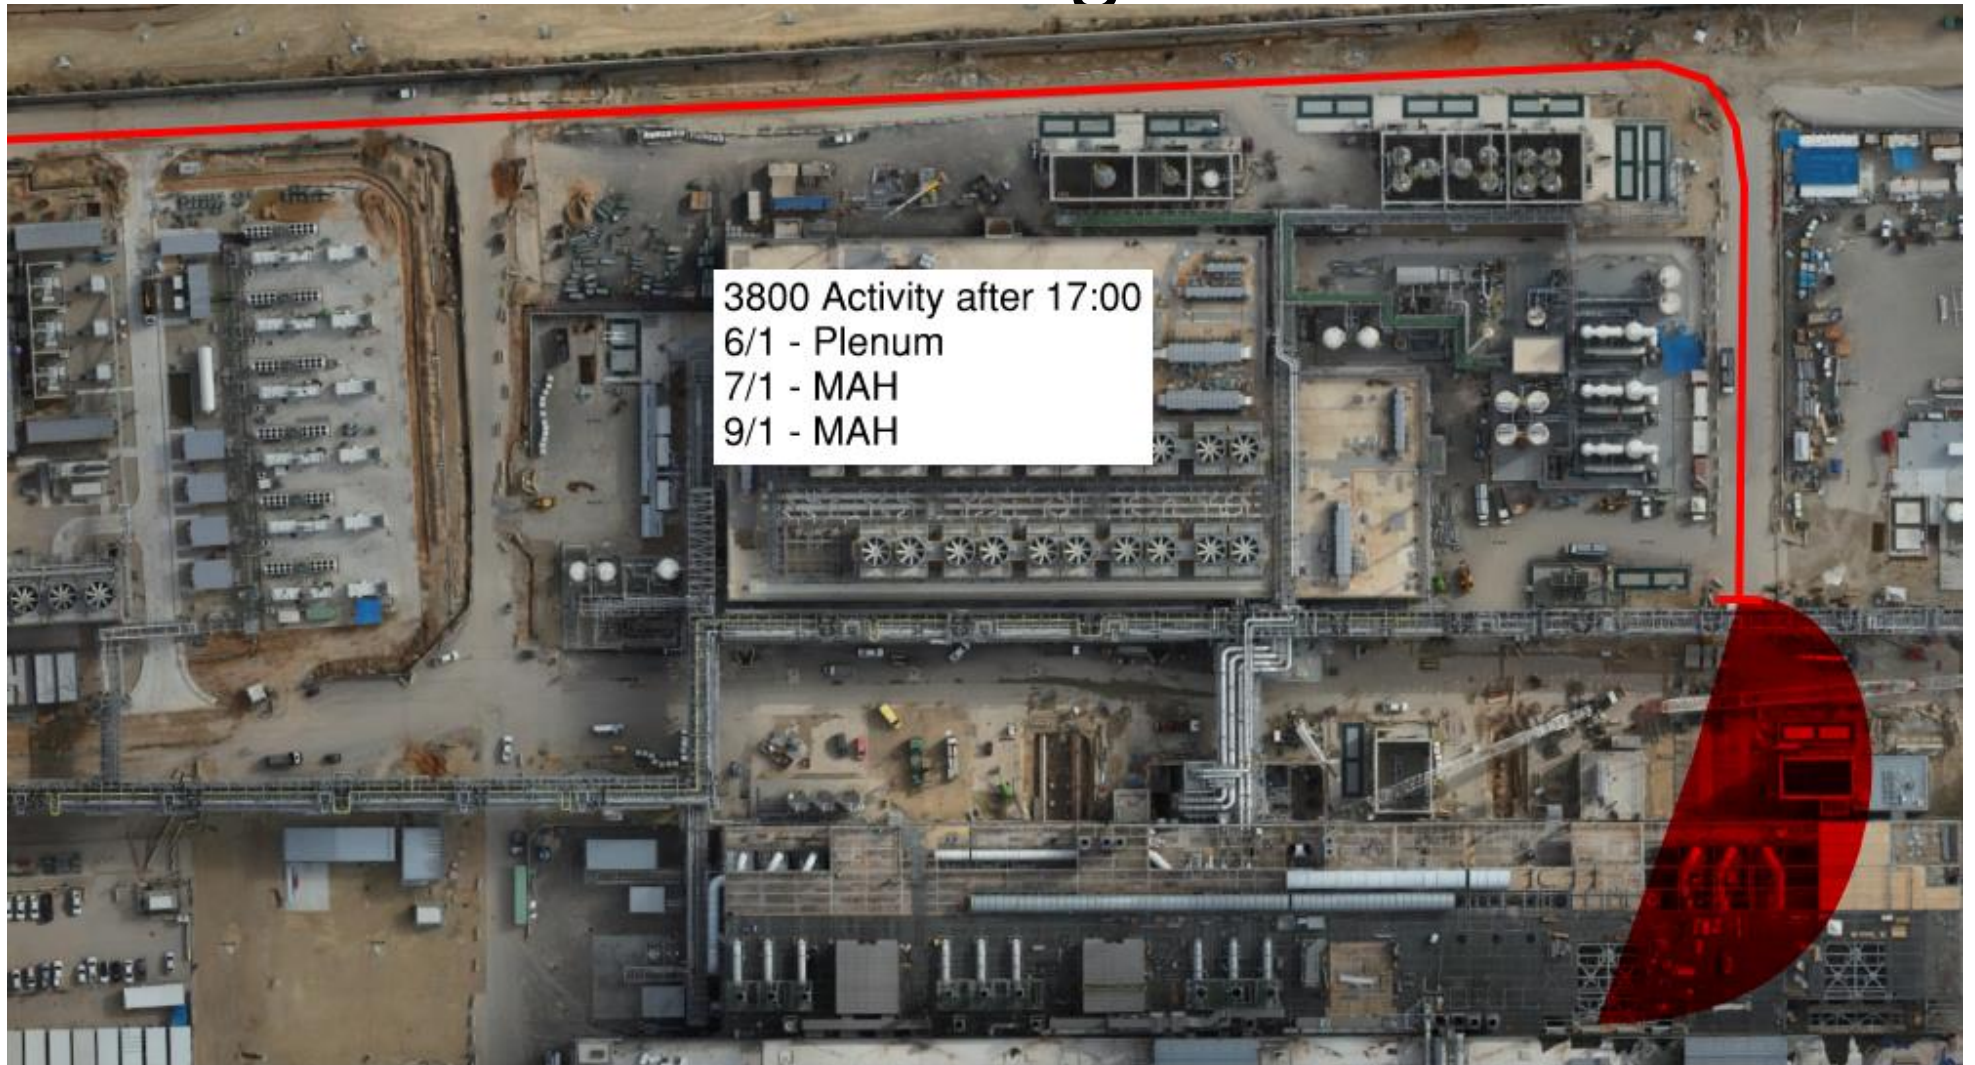





WJG 01J, 02J LIFT 2 & 3

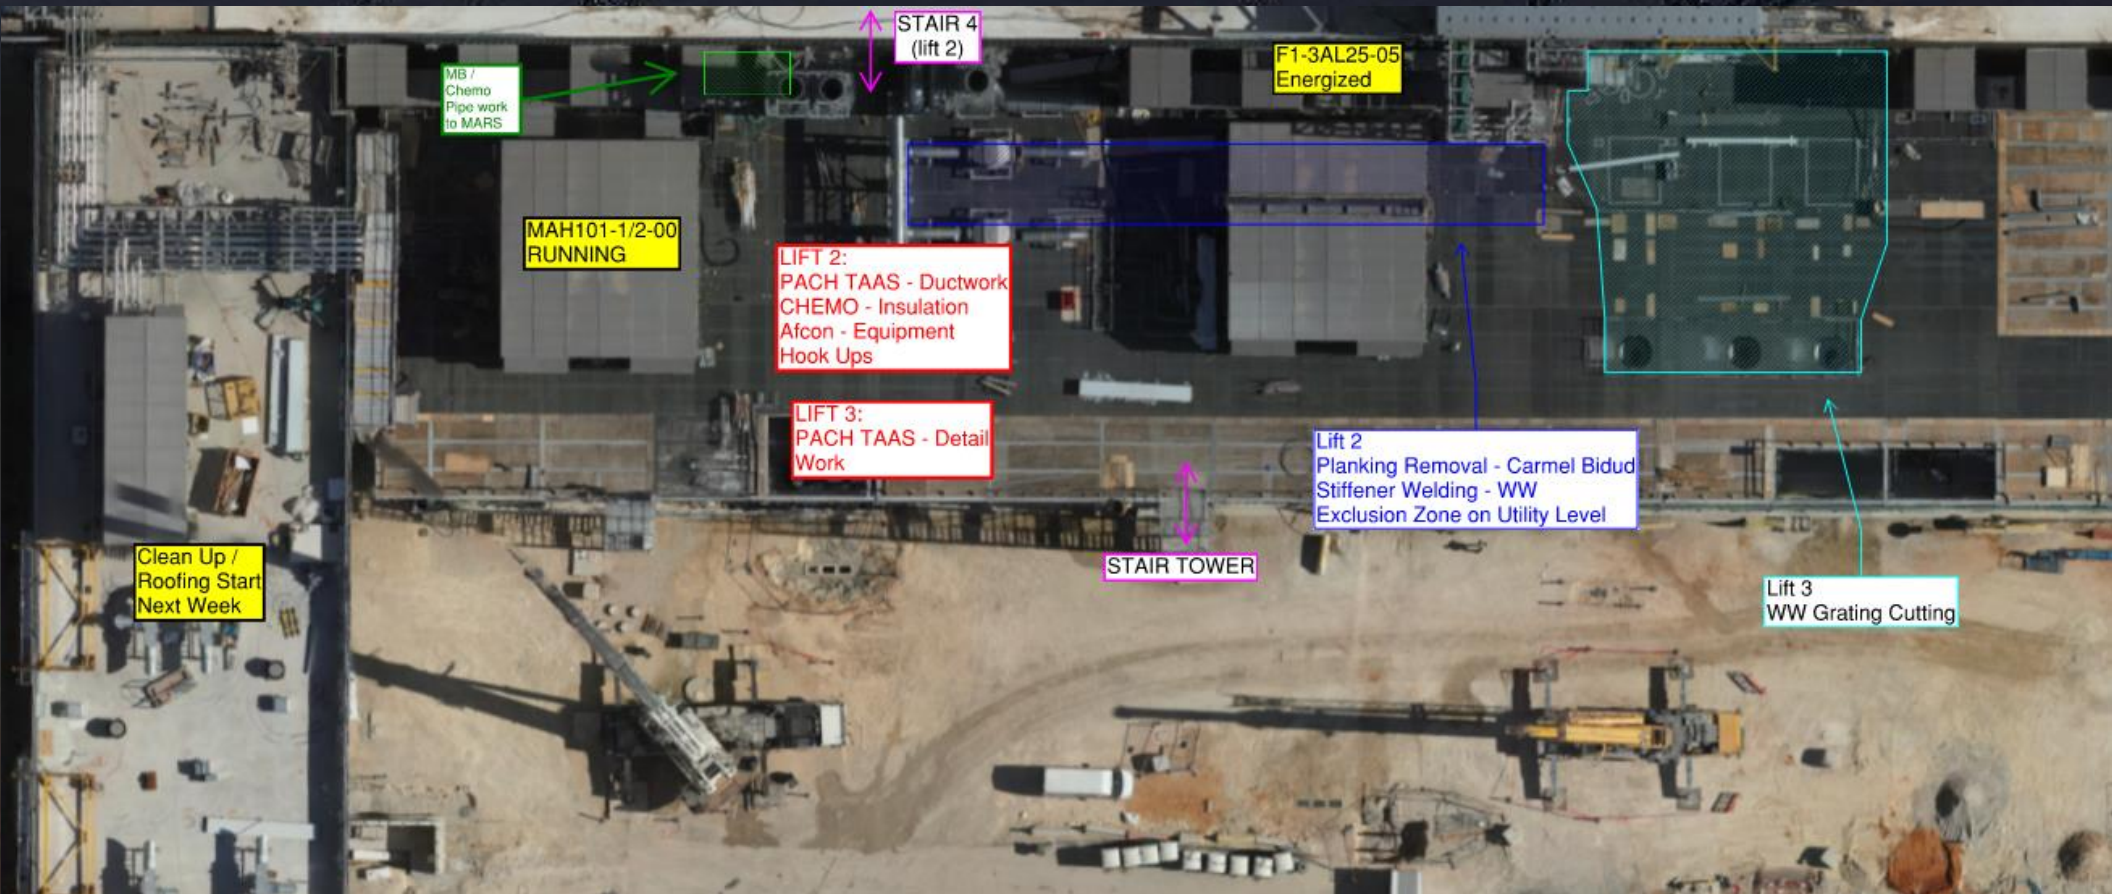


WJG 03J, 04J, 05J LIFT 2 & 3

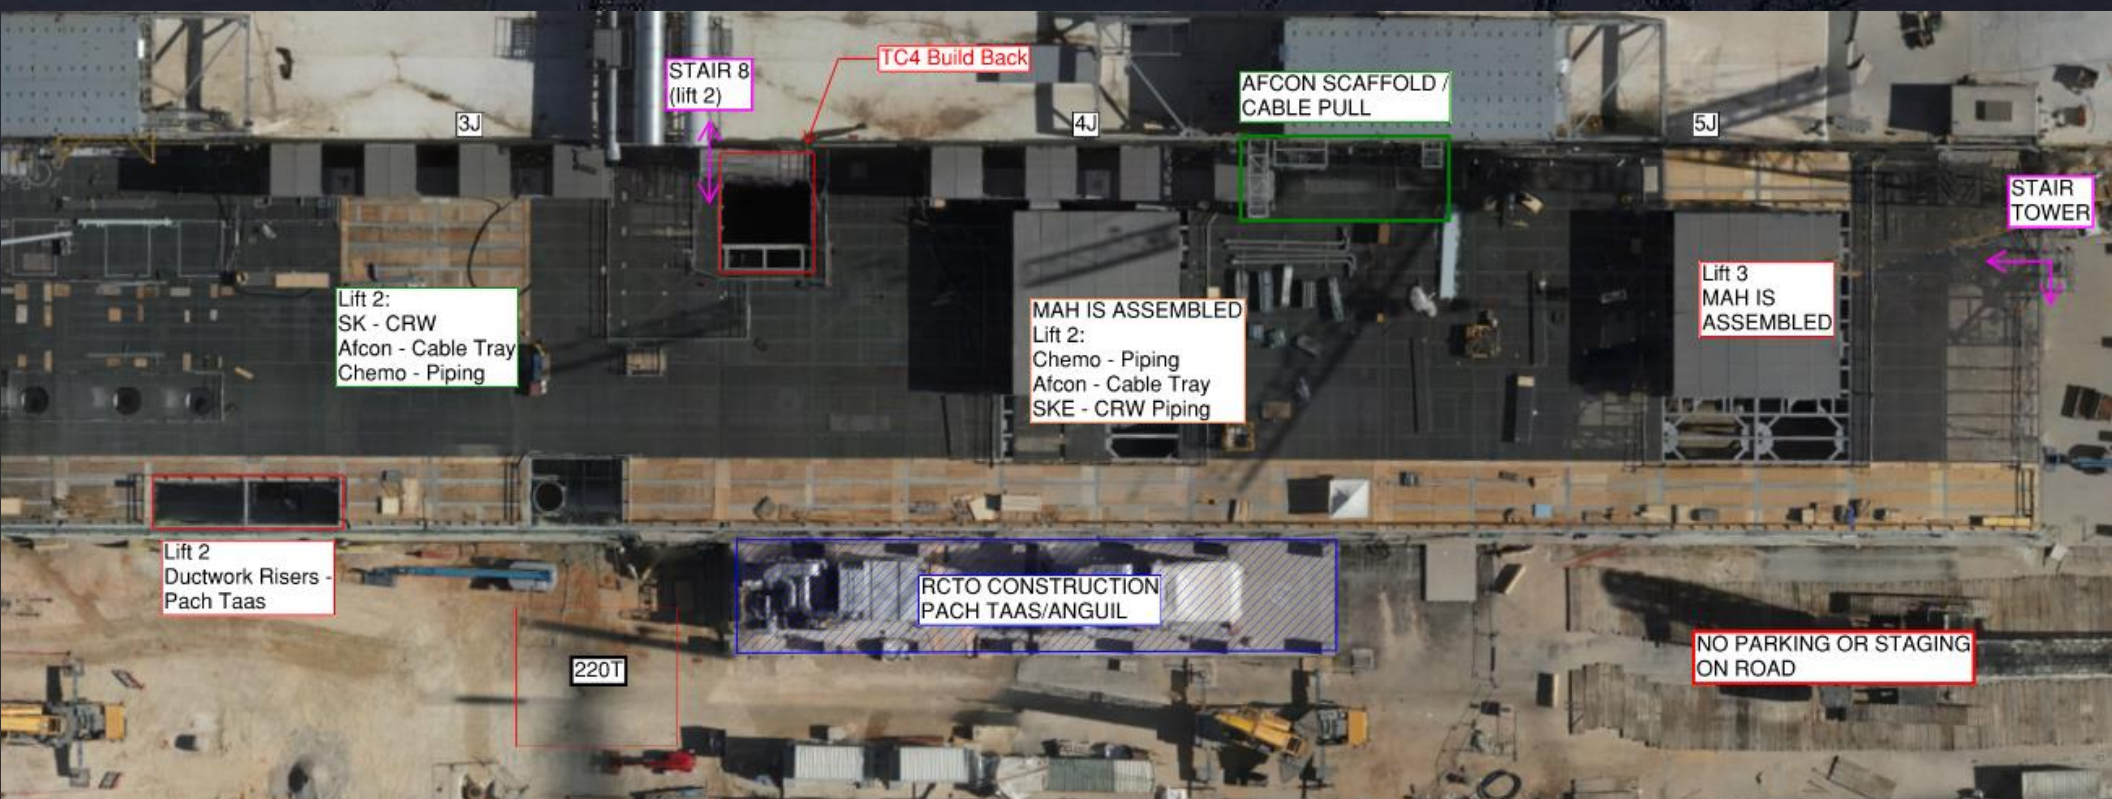

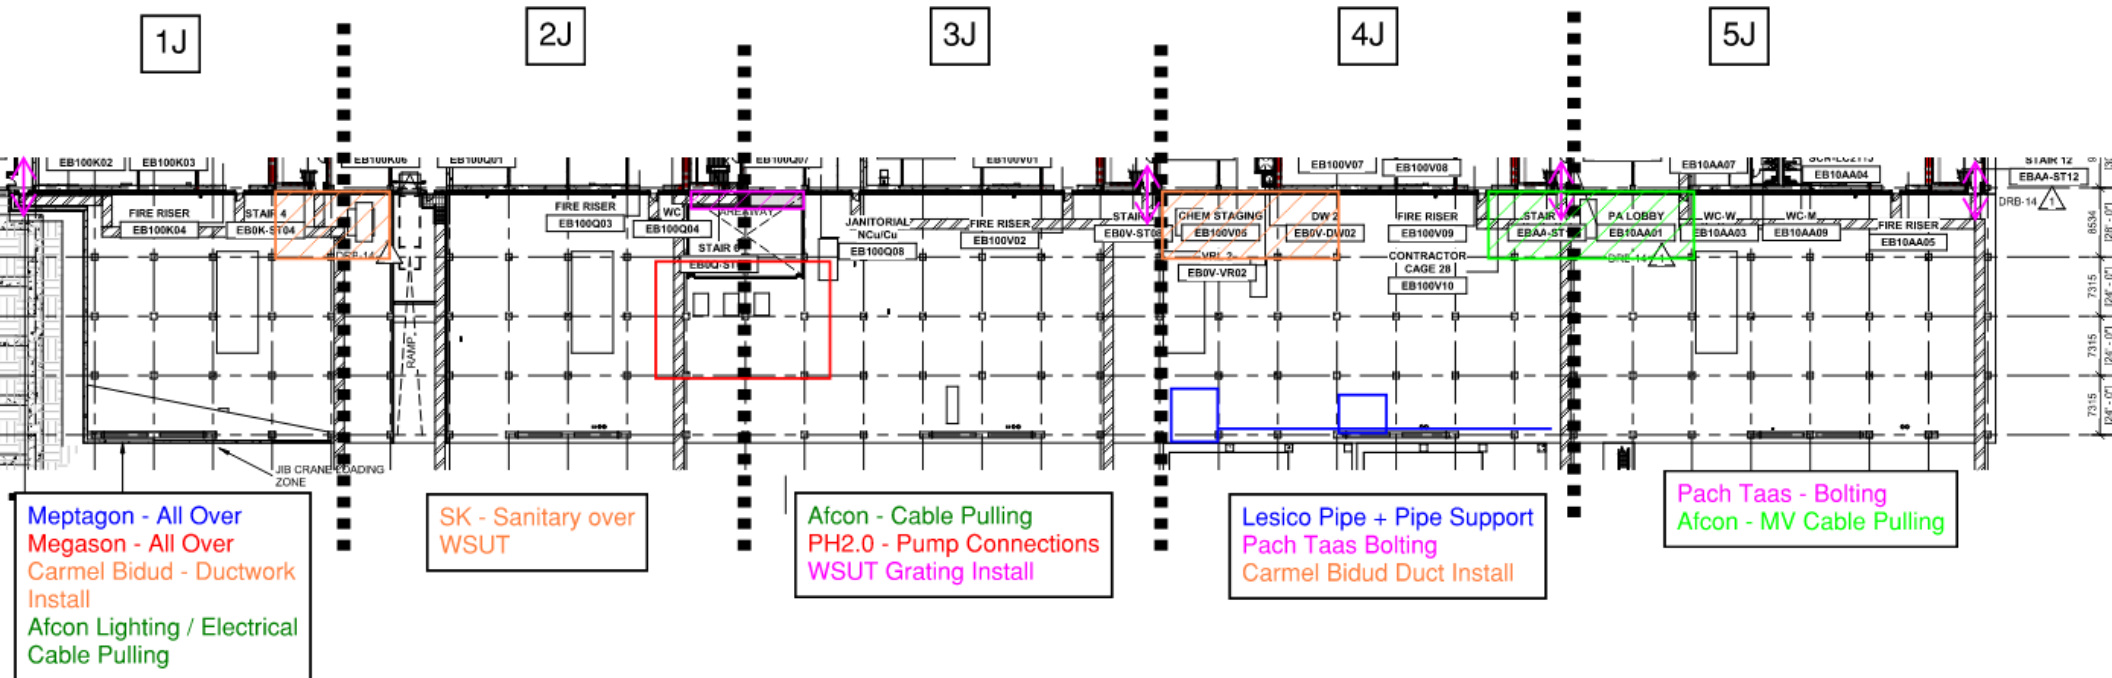



CUB 1

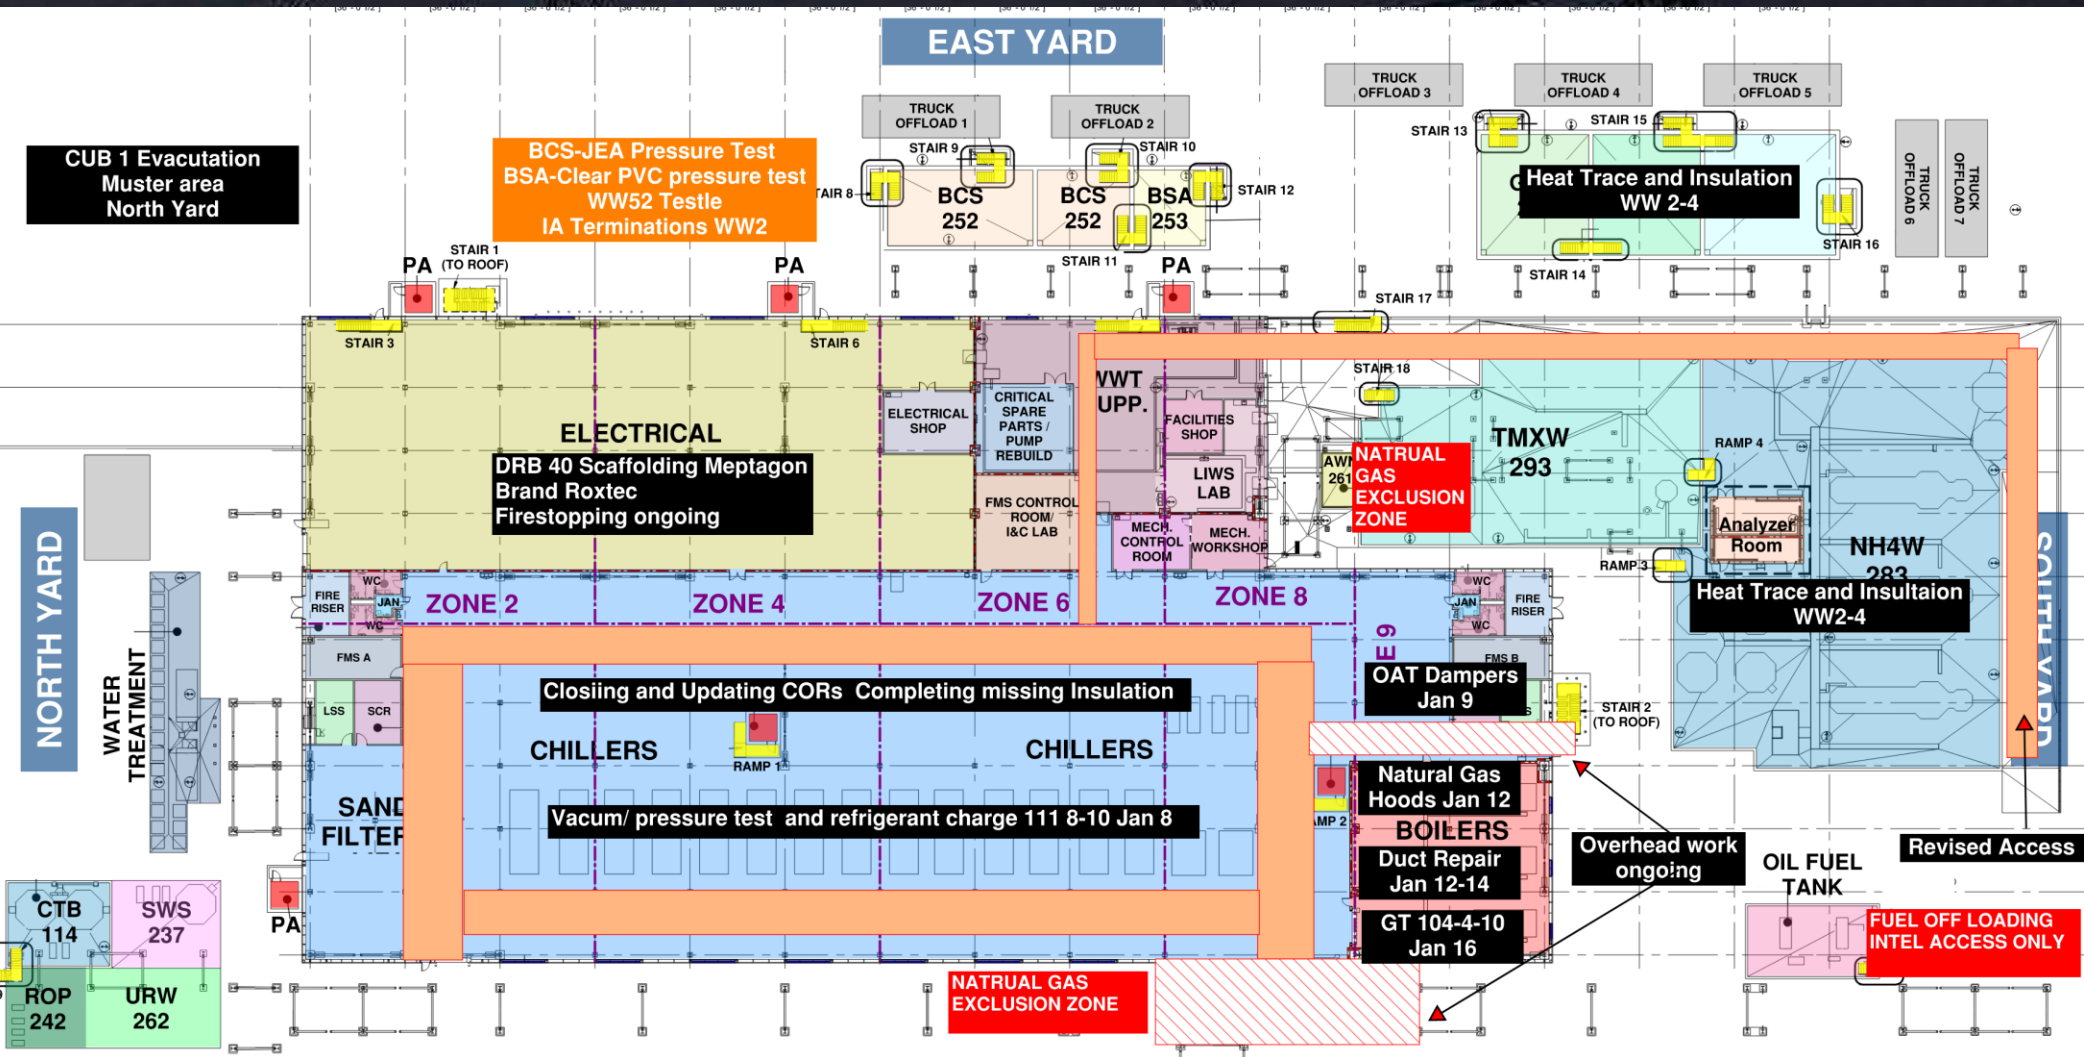


CUB 1 – EXTERIOR/ROOF







CUB 2- Load in ,H&T, Framing and Sheetrock

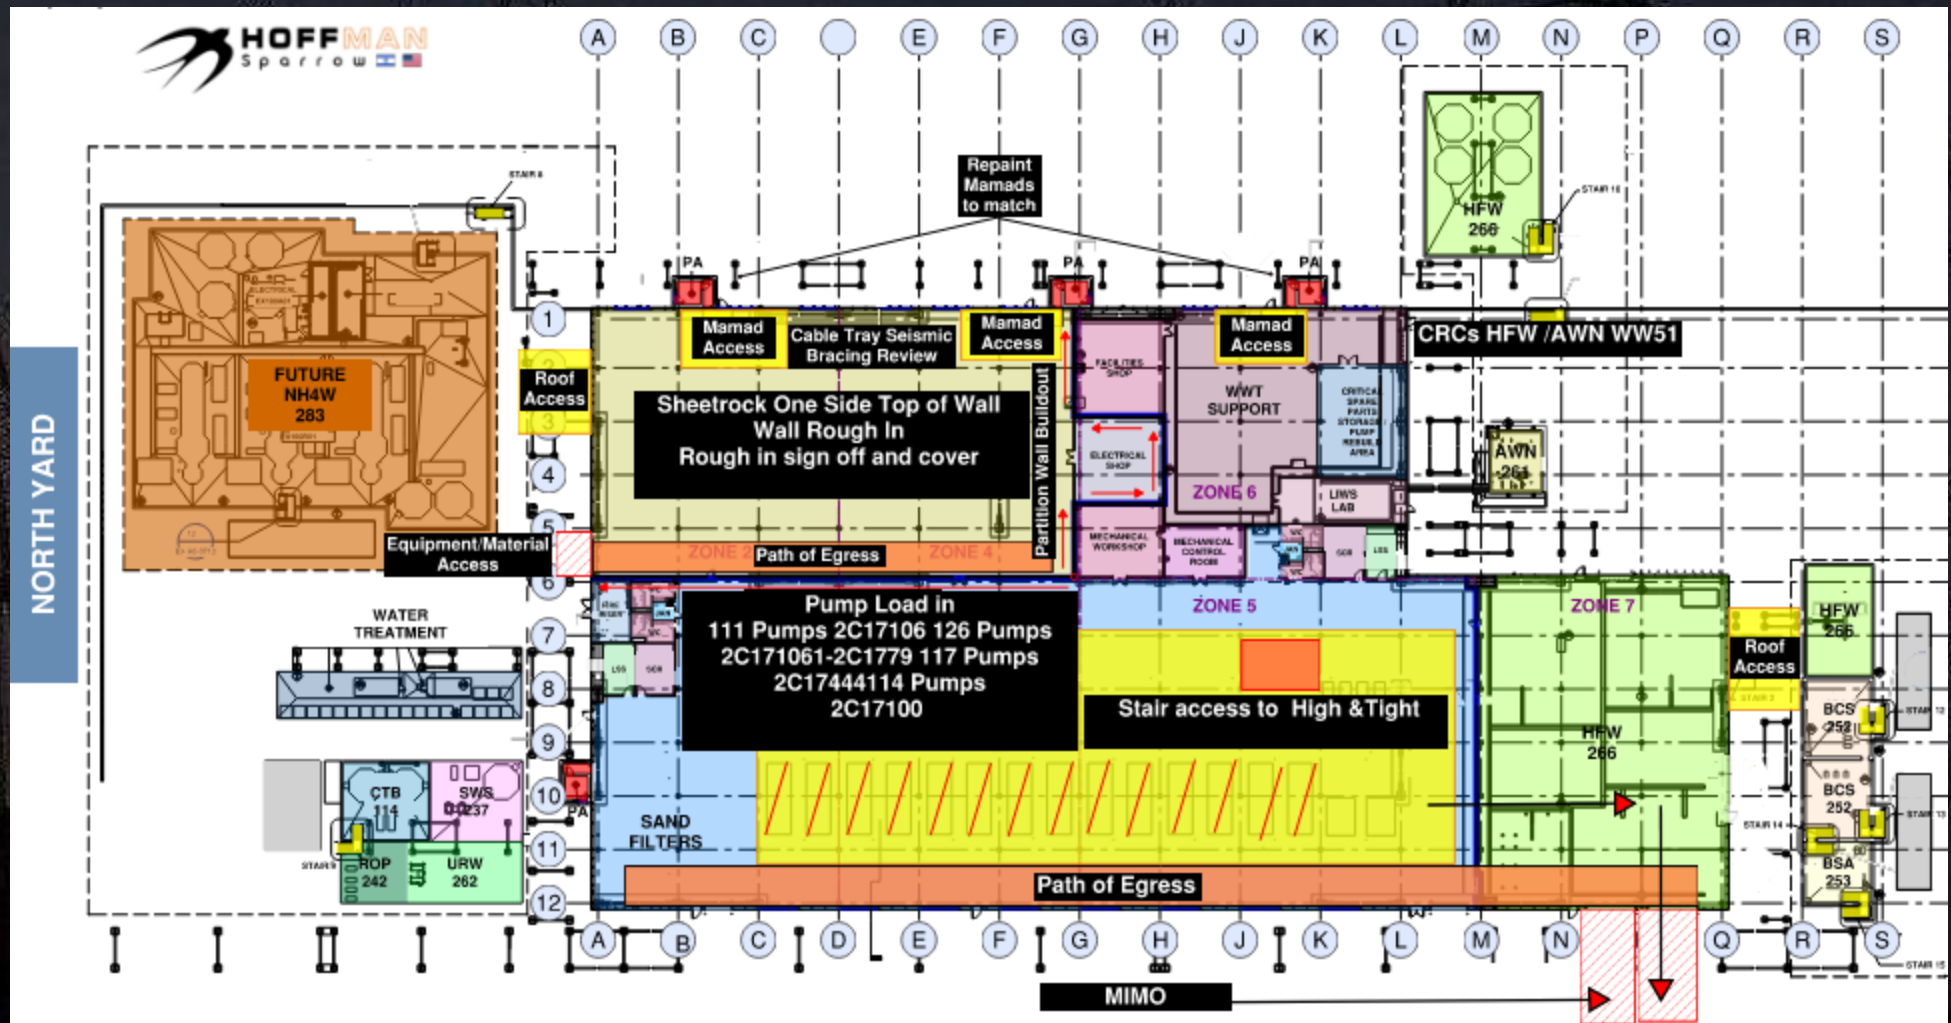

CUB 2 – EXTERIOR/ROOF

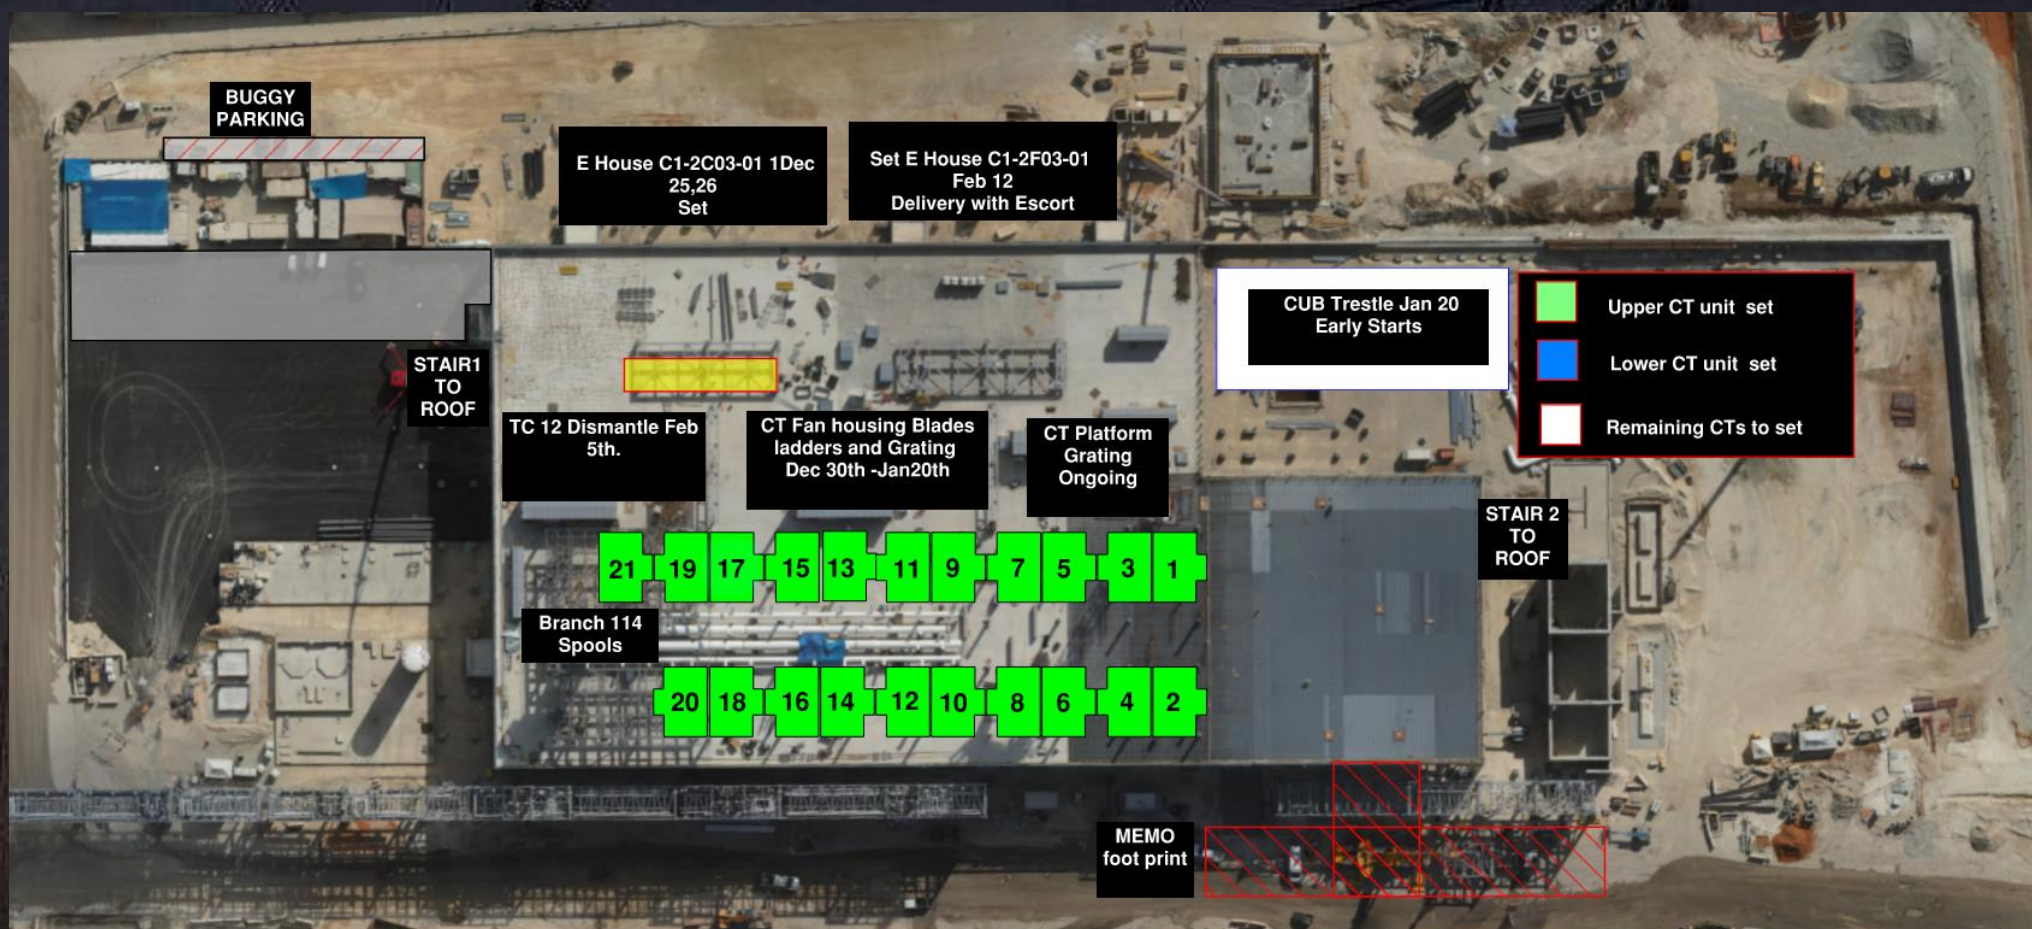





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow



G.I.S- scaffolding
dismantling
start - January 15th 2025

T82A+B
complete dissemble

T81-80
disassembling cable trays
Internal catwalks

T82A


T82B

T81

T80

T84

T84 complete dissemble

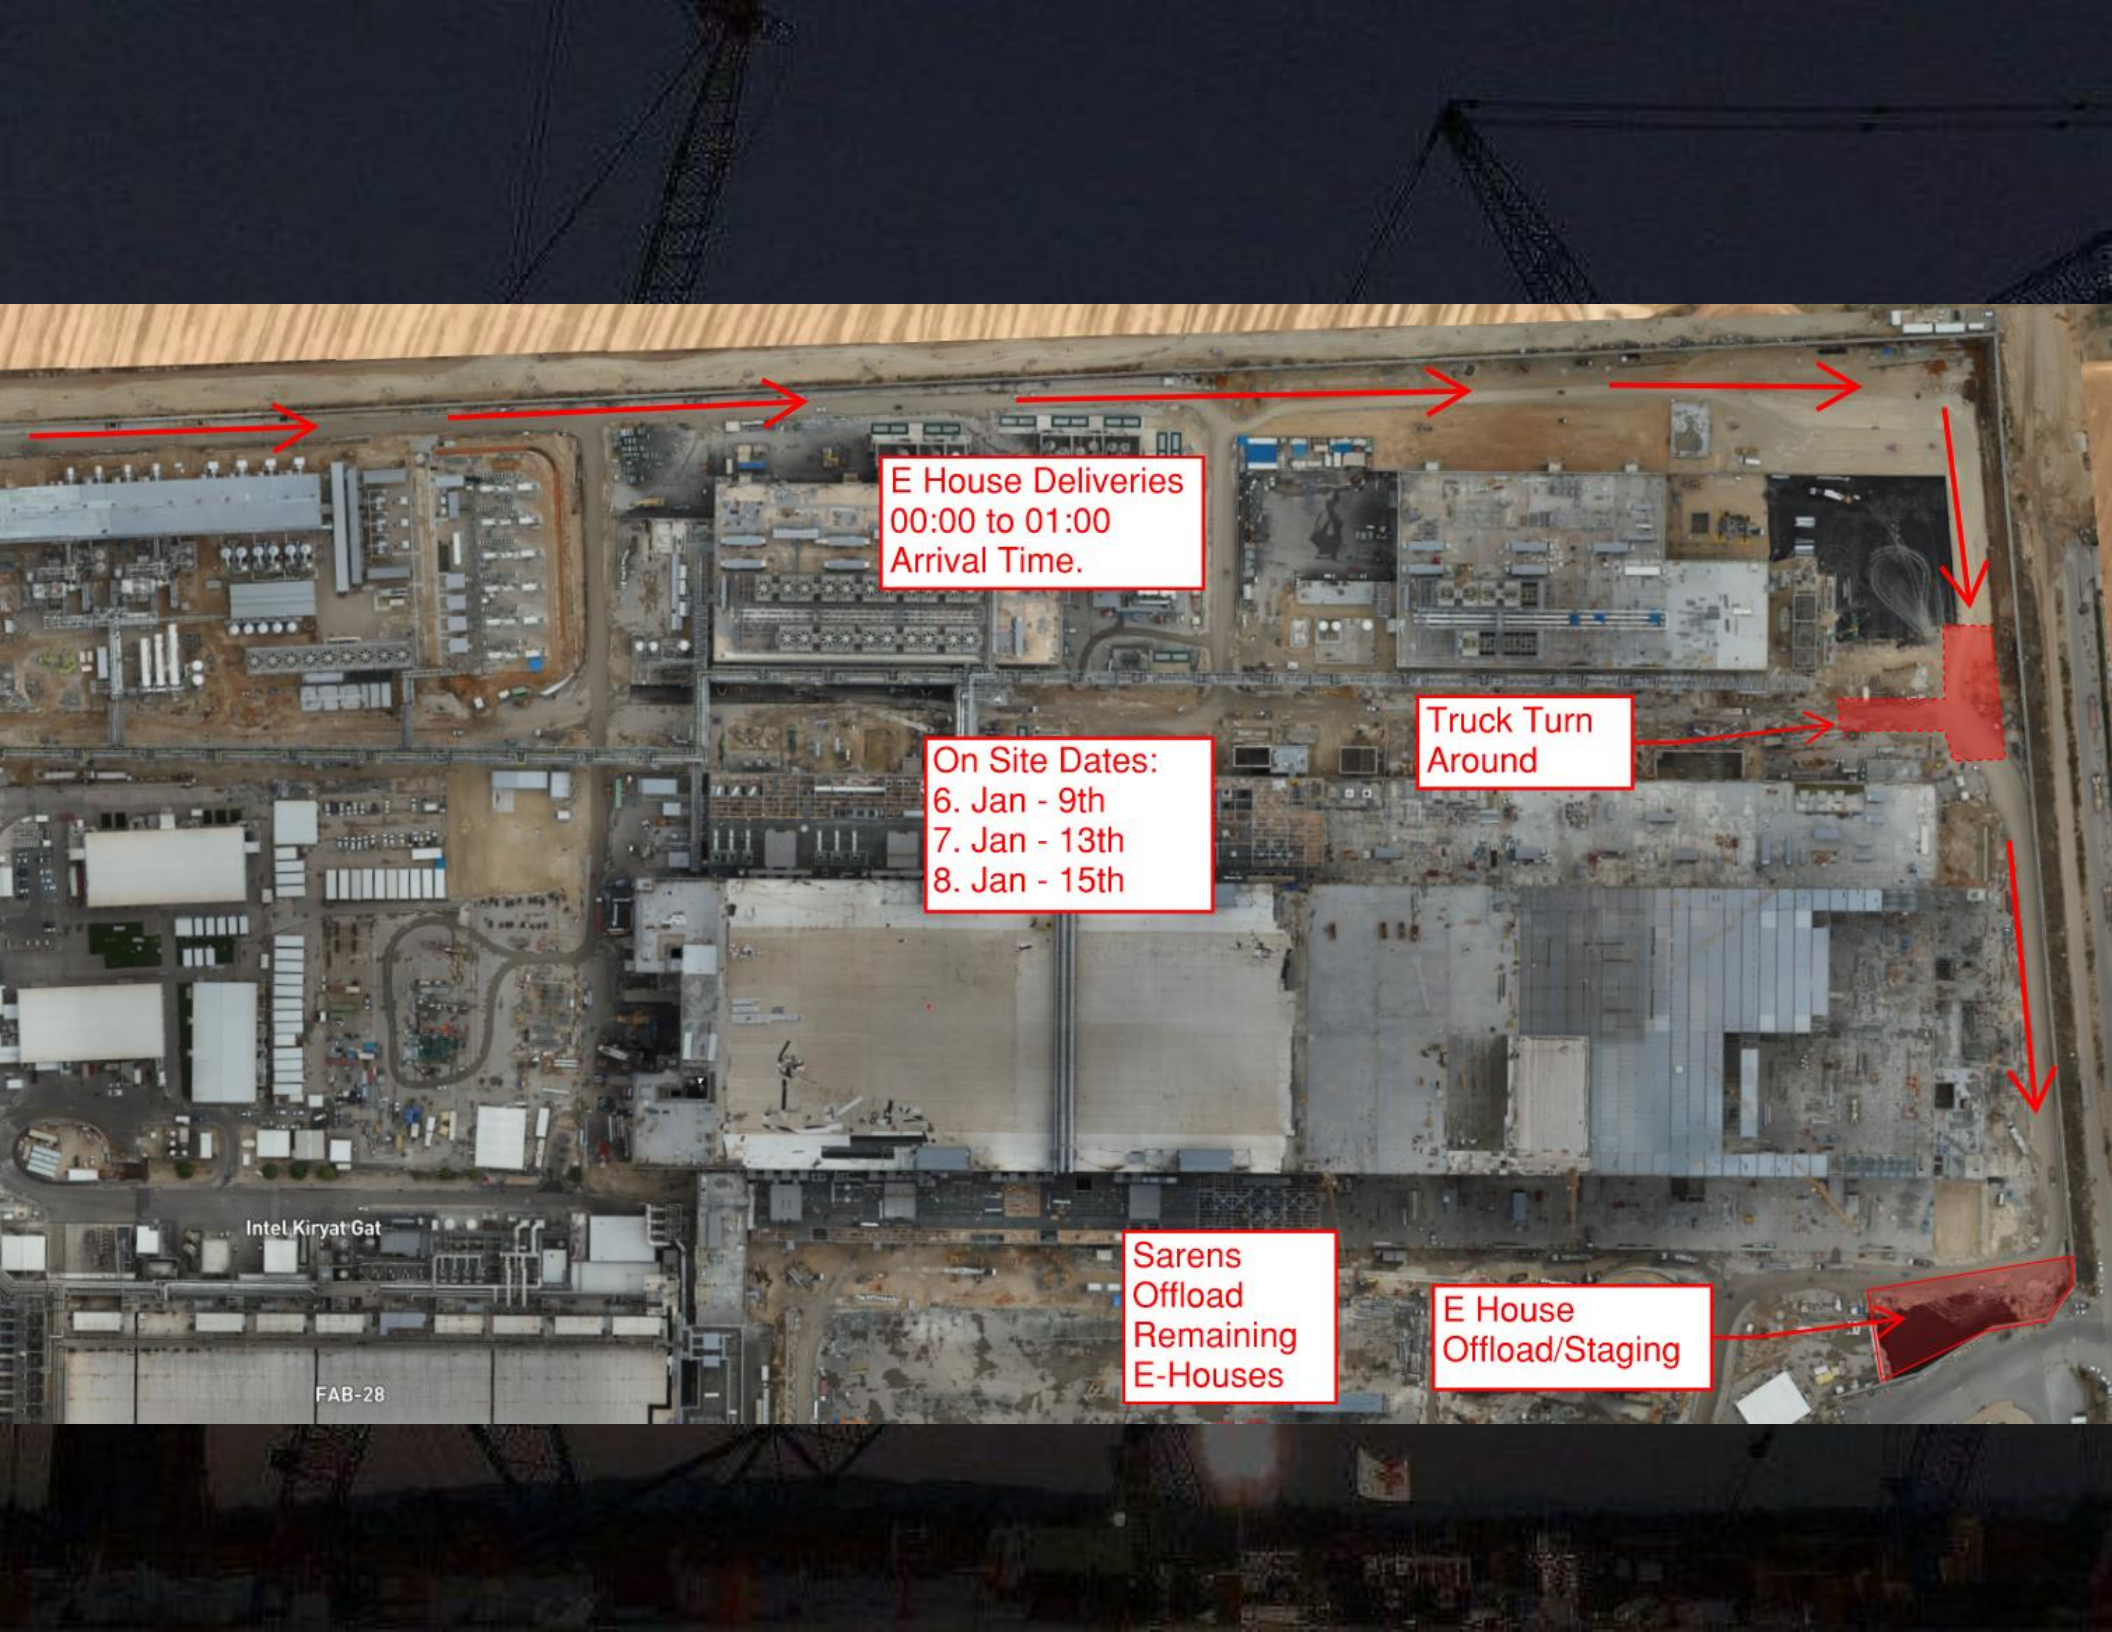

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:
6. Jan - 9th
7. Jan - 13th
8. Jan - 15th

Truck Turn
Around

Intel Kiryat Gat

FAB-28

Sarens
Offload
Remaining
E-Houses


E House
Offload/Staging

Daily Coordination Meeting

Site Logistics


600 Car Park

Boring

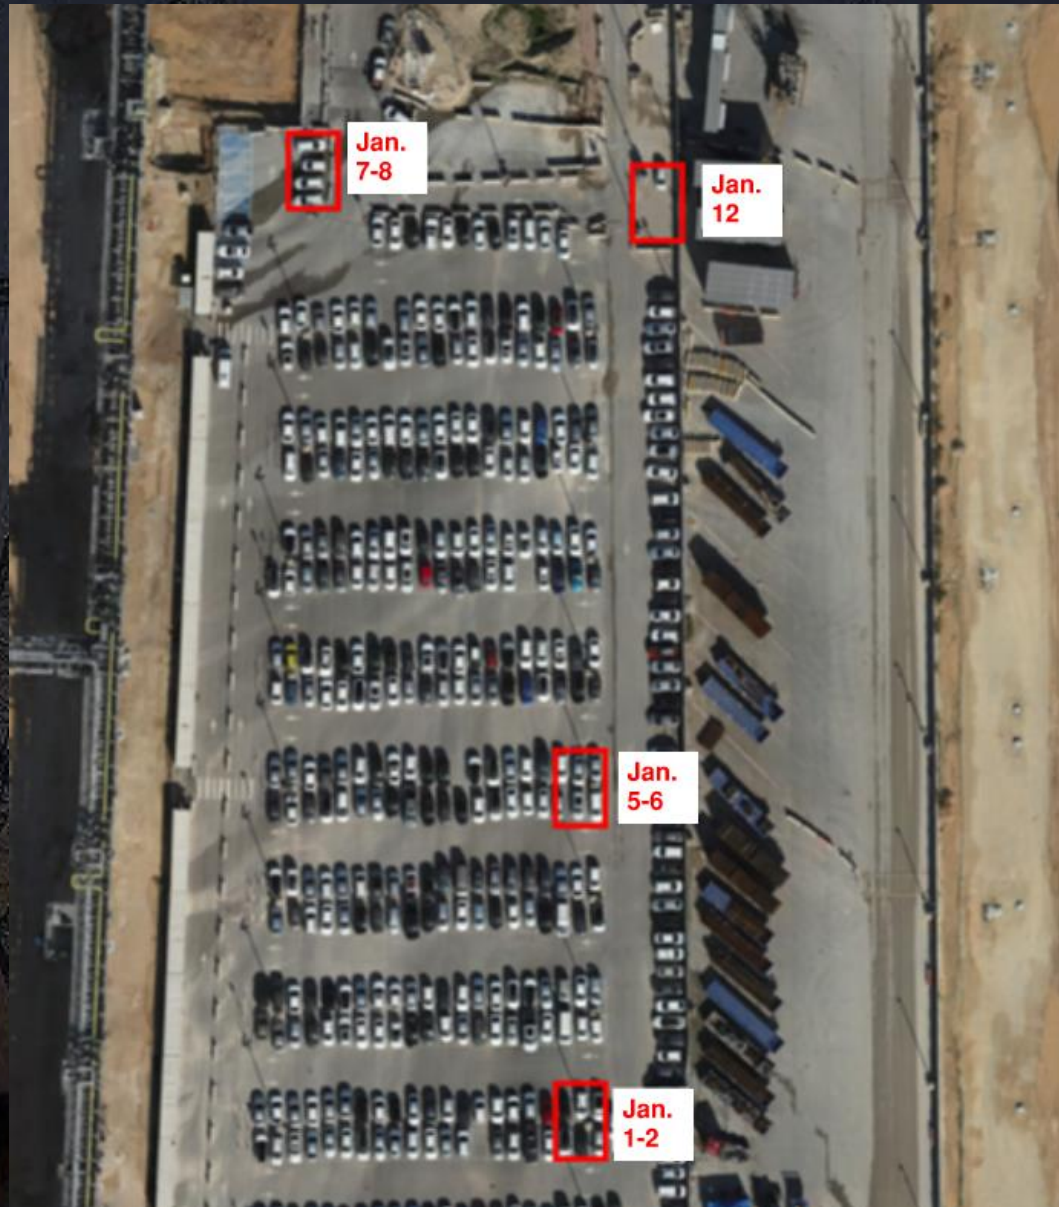

Daily Coordination Meeting


Site Logistics North

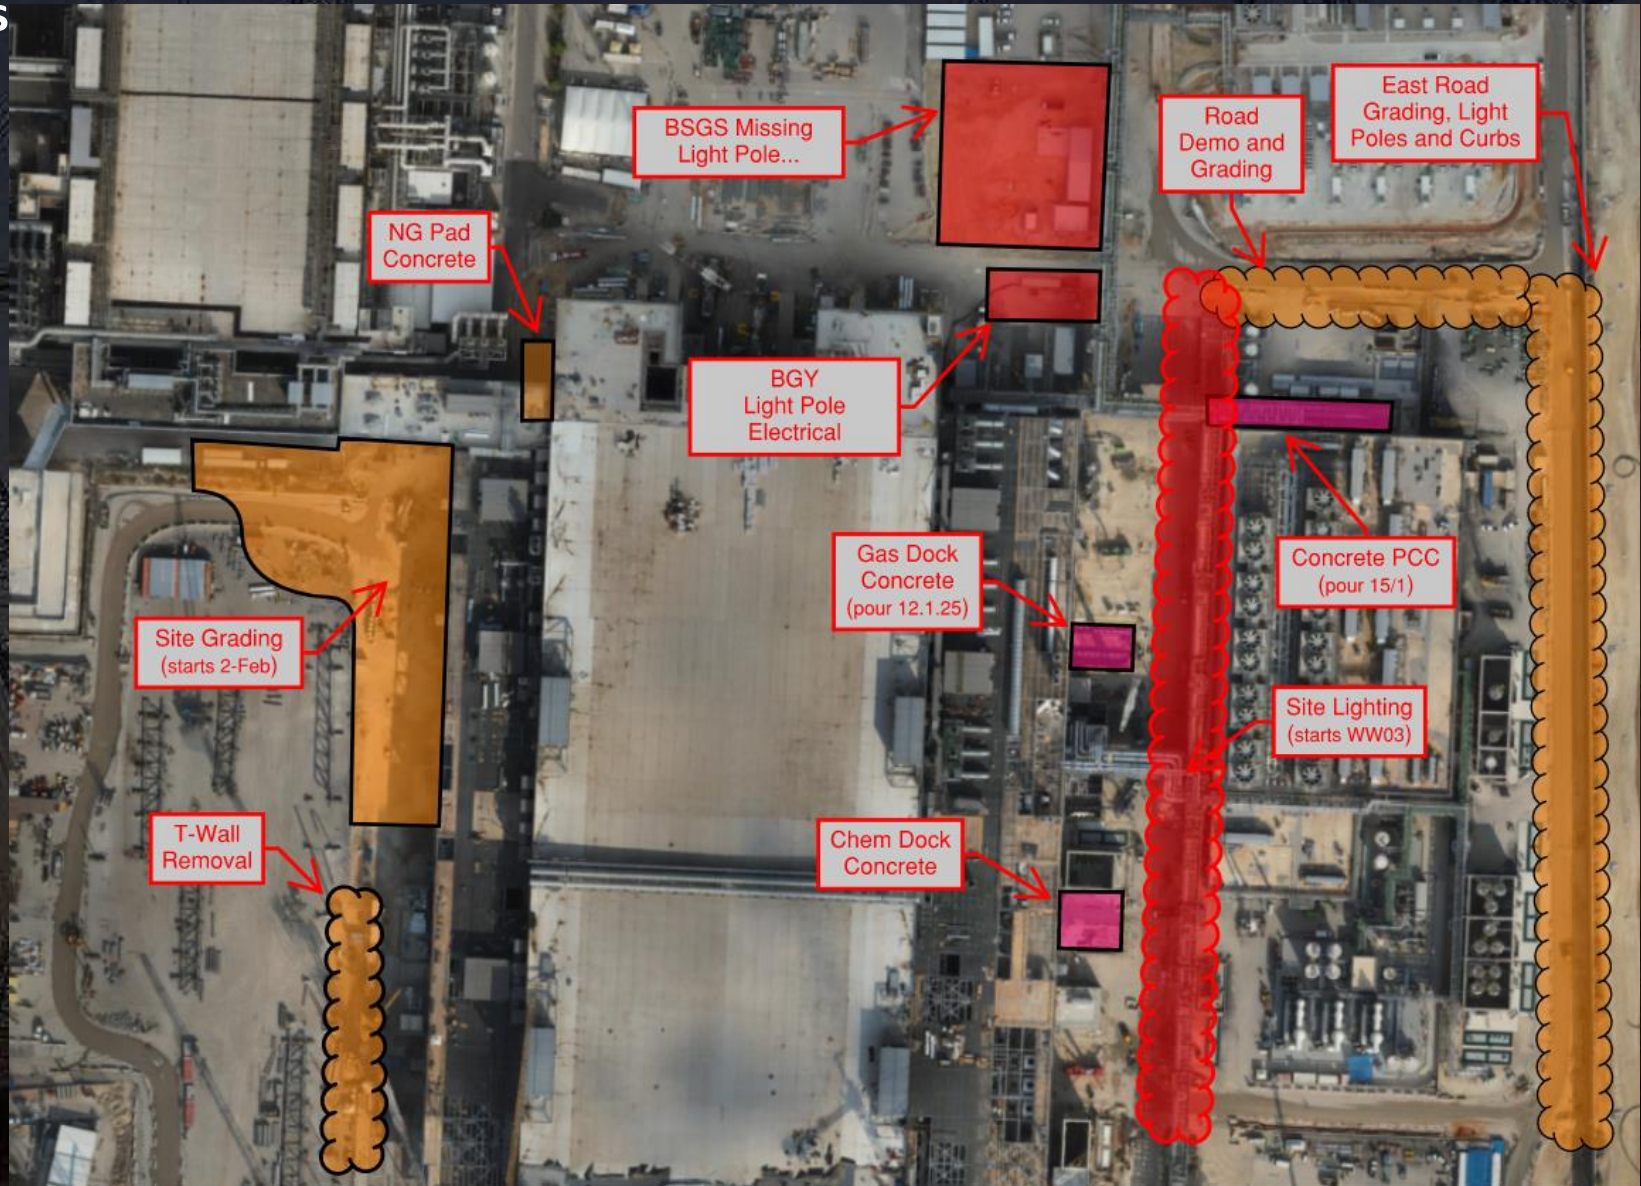

Daily Coordination Meeting

Site Logistics


South

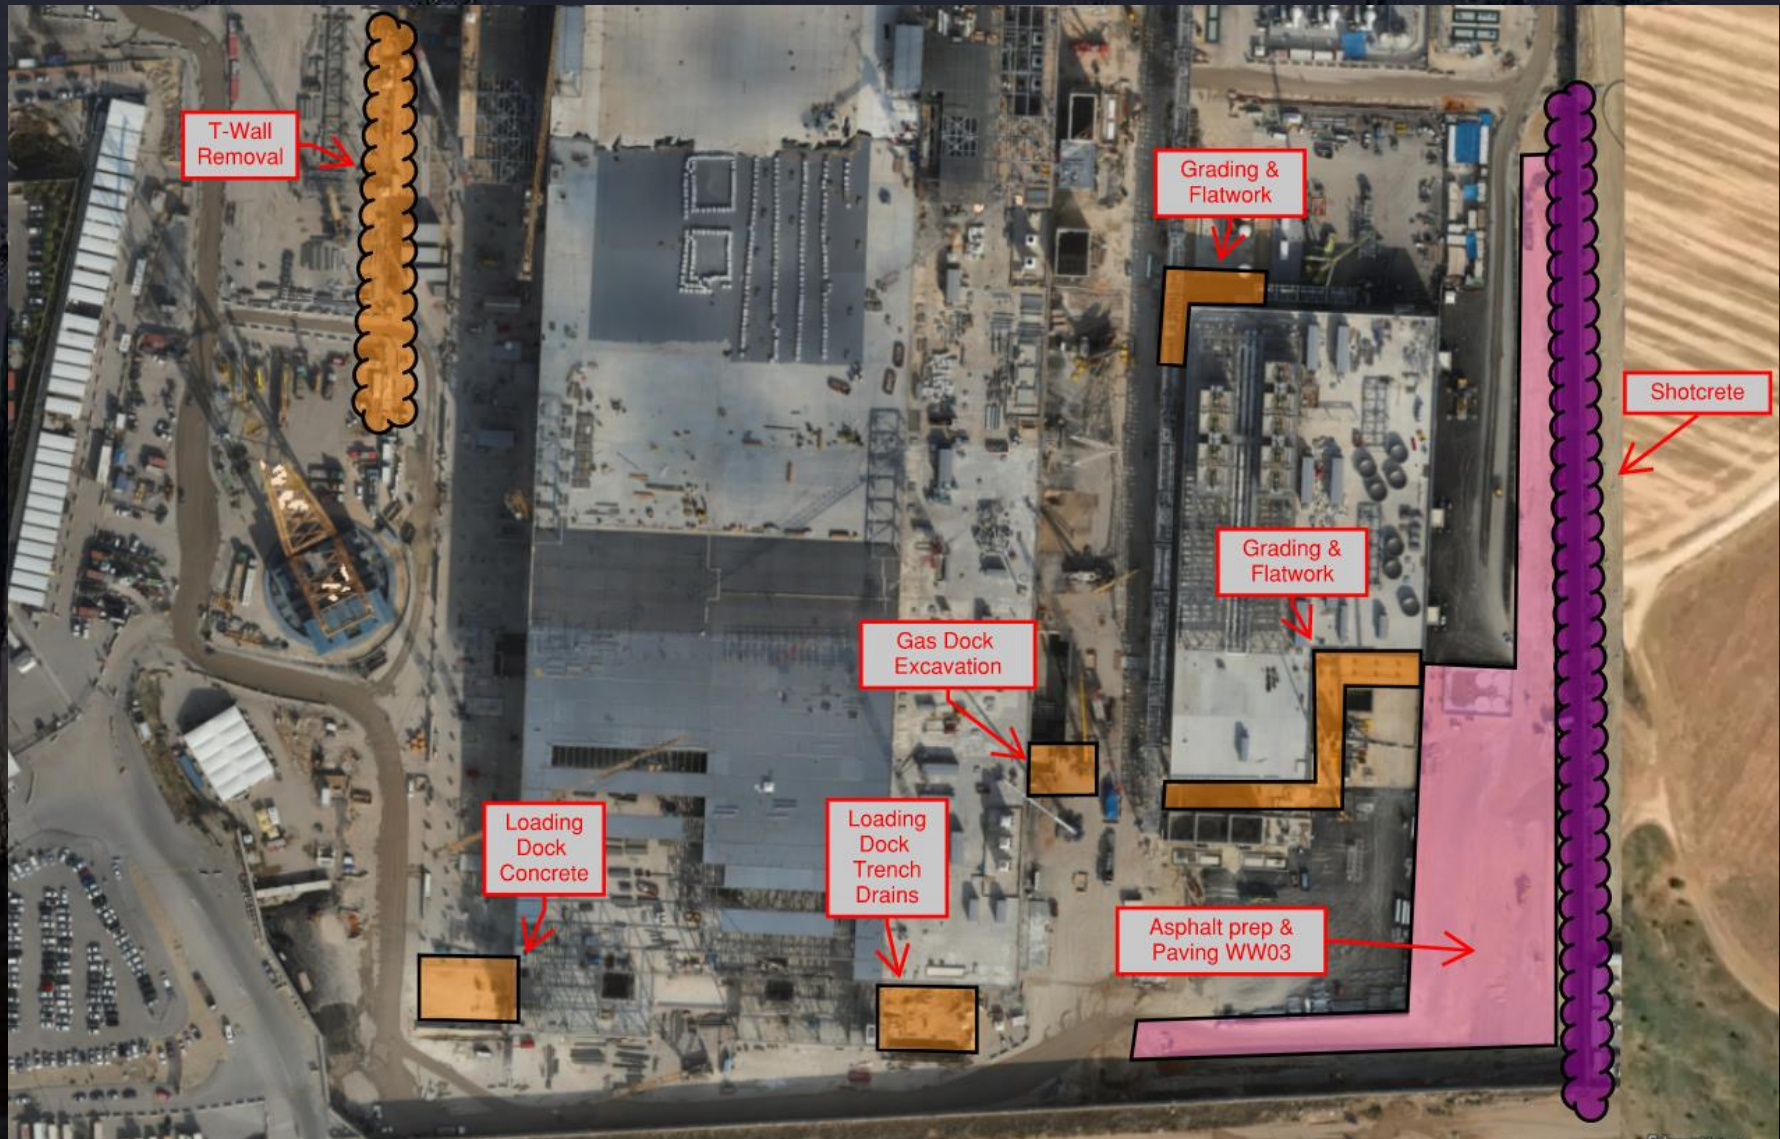

Failing Safely

- Our plans are to have nothing go wrong with our activities, and that is how we should strive to complete our work.
- However, we need to also plan for things to go wrong, and we need to leave room to fail safely.
- This means staying out of the line of fire, barricading our areas, and bullet-proofing.
- Make sure that this is your team leader's focus when they are performing their PTPs.
- What could go wrong?
- How can we protect people if that does occur?

JANUARY 13TH
10:30 - 12:00

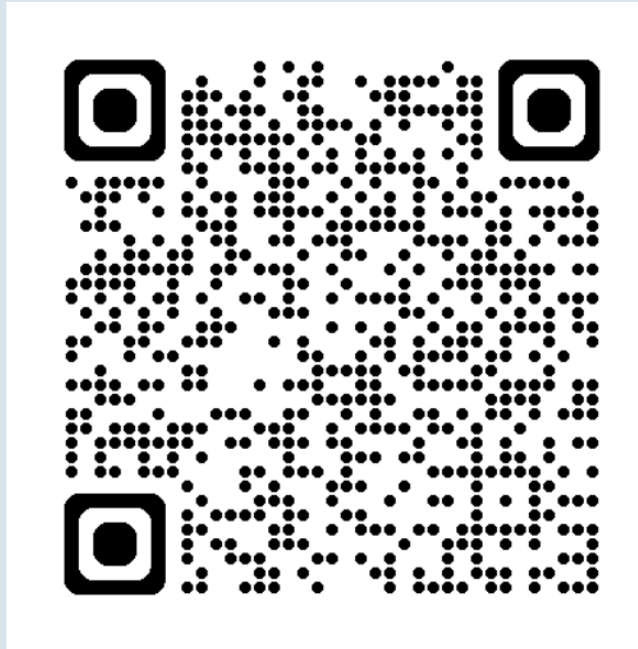

KADIMA
BUM

PLEASE SIGN UP HERE TO
RECEIVE THE CALENDAR INVITE



HCC/EHS Weekend Work- 10.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Jeremy Lee 052-6042279
Oscar Macias 052-4845469
Shimon Simo Ben Shetrit 052-5952059

CSA CM

Joe Nicpon 052-2962036
Nick Dailey 052-3308928
Andy Jollands 052-9659290

MEP

Ken Power 052-2531428
Abhilash Parameswaran 052-6938827

Cx

Calum Martin 052-4372208

Cranes

Hadar Shem Tov 054-6693626

Safety

Safety Foreman- Mohammad Zakakti- 054-8121212 Mohammad-Zakakti@Hoffmancorp.com
Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 10.01.2025

FAB

Utility Level / Roof / Stair Shaft

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

Pach Taas

3W-4W-5W Wall Penetration,1W-4E

Perimeter

Tomer 0507670575

Afcon E

MARSes, E LSS Rooms

Avi Eli: 0526008487

Chemo

TTNW

Tomi: 0523759408

MEGASON

7E

Israel 0526869393

Clean Room

Talad – 10 guys CR 2 E – UPN Install, 4E Grating (EHS Marcelo 0523540242, Super Igor 0544509386)

Sig – 7 GUYS 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)

Afcon – 22 guys CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)

Chemo –15 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)

Megason - 9 GUYS INT LEVEL + 7 GUYS ON UTILITY LEVEL FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT

Sela – 8 2E CRC (Supervisor yoav 0548076339 , EHS SERGEY 0526650046)

D&p - 16 guys freddie hazan 0503827885

Subcontractor Weekend Work- 10.01.2025

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P

Foreman – Vadim – 053-5552472

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

HSAI – 3P Roof Curb Stripping

Foreman – Dave – 052-4121028

Safety – Hiam

SK Engineering – GL4 UL Piping, 3P roof/Lift 2 Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

Carmel Bidud– Spec Gas, BCD, and 2P Roof

Foreman –

Safety –

Combe Waste – 2P Waste Piping at GL4

Foreman – Chaim – 054-5210133

Safety – Marzuke – 054-447-7112

Combe UPW – 2P & 5P Scrubbers

Foreman – Boris – 054-8346412

Safety – Shimon – 054-5348843

WJG

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 2J Utility Level, 4J/5J Lift 2 Piping (Hot Work)

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

Pach Taas: All over (HRA)

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

SK:

Foreman: Tufik 054 943 3592

Subcontractor Weekend Work- 10.01.2025

CUB

D&P:

Constantin - 0545501602

David - 0548894447

Sami Najami:

Husein - 0526917461

Alon - 0509895008

SK:

Renato- 0548991623

Marzuk - 0548830263

Chemo:

Dudu - 0509808846

Leonid - 0548883878

Trestle

SNJ:

PIPES –T40 UB CUB - 8 workers

STEEL –Galvanized paint + – T30 A+B - 8 workers

Steel adjustment - 12 workers

FORMAN

Adiv asaly- 0526017477

SAFETY TRESTLE

Aviram shriki tel. 0509059920

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Elmor – Site Lighting Underground

Supervision = Shlomi: 050-9182260

EHS = Daniel: 052-2584171

Olizki – Offload 18, CUB1 flatwork, Link NG pad formwork Supervision = Or: 052-4917313 EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
