

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:


- *Red Flags a Flying with Reduced Supervision
- * Weekend Work



SK
Press. Test
PA iA
Today
From 17:00

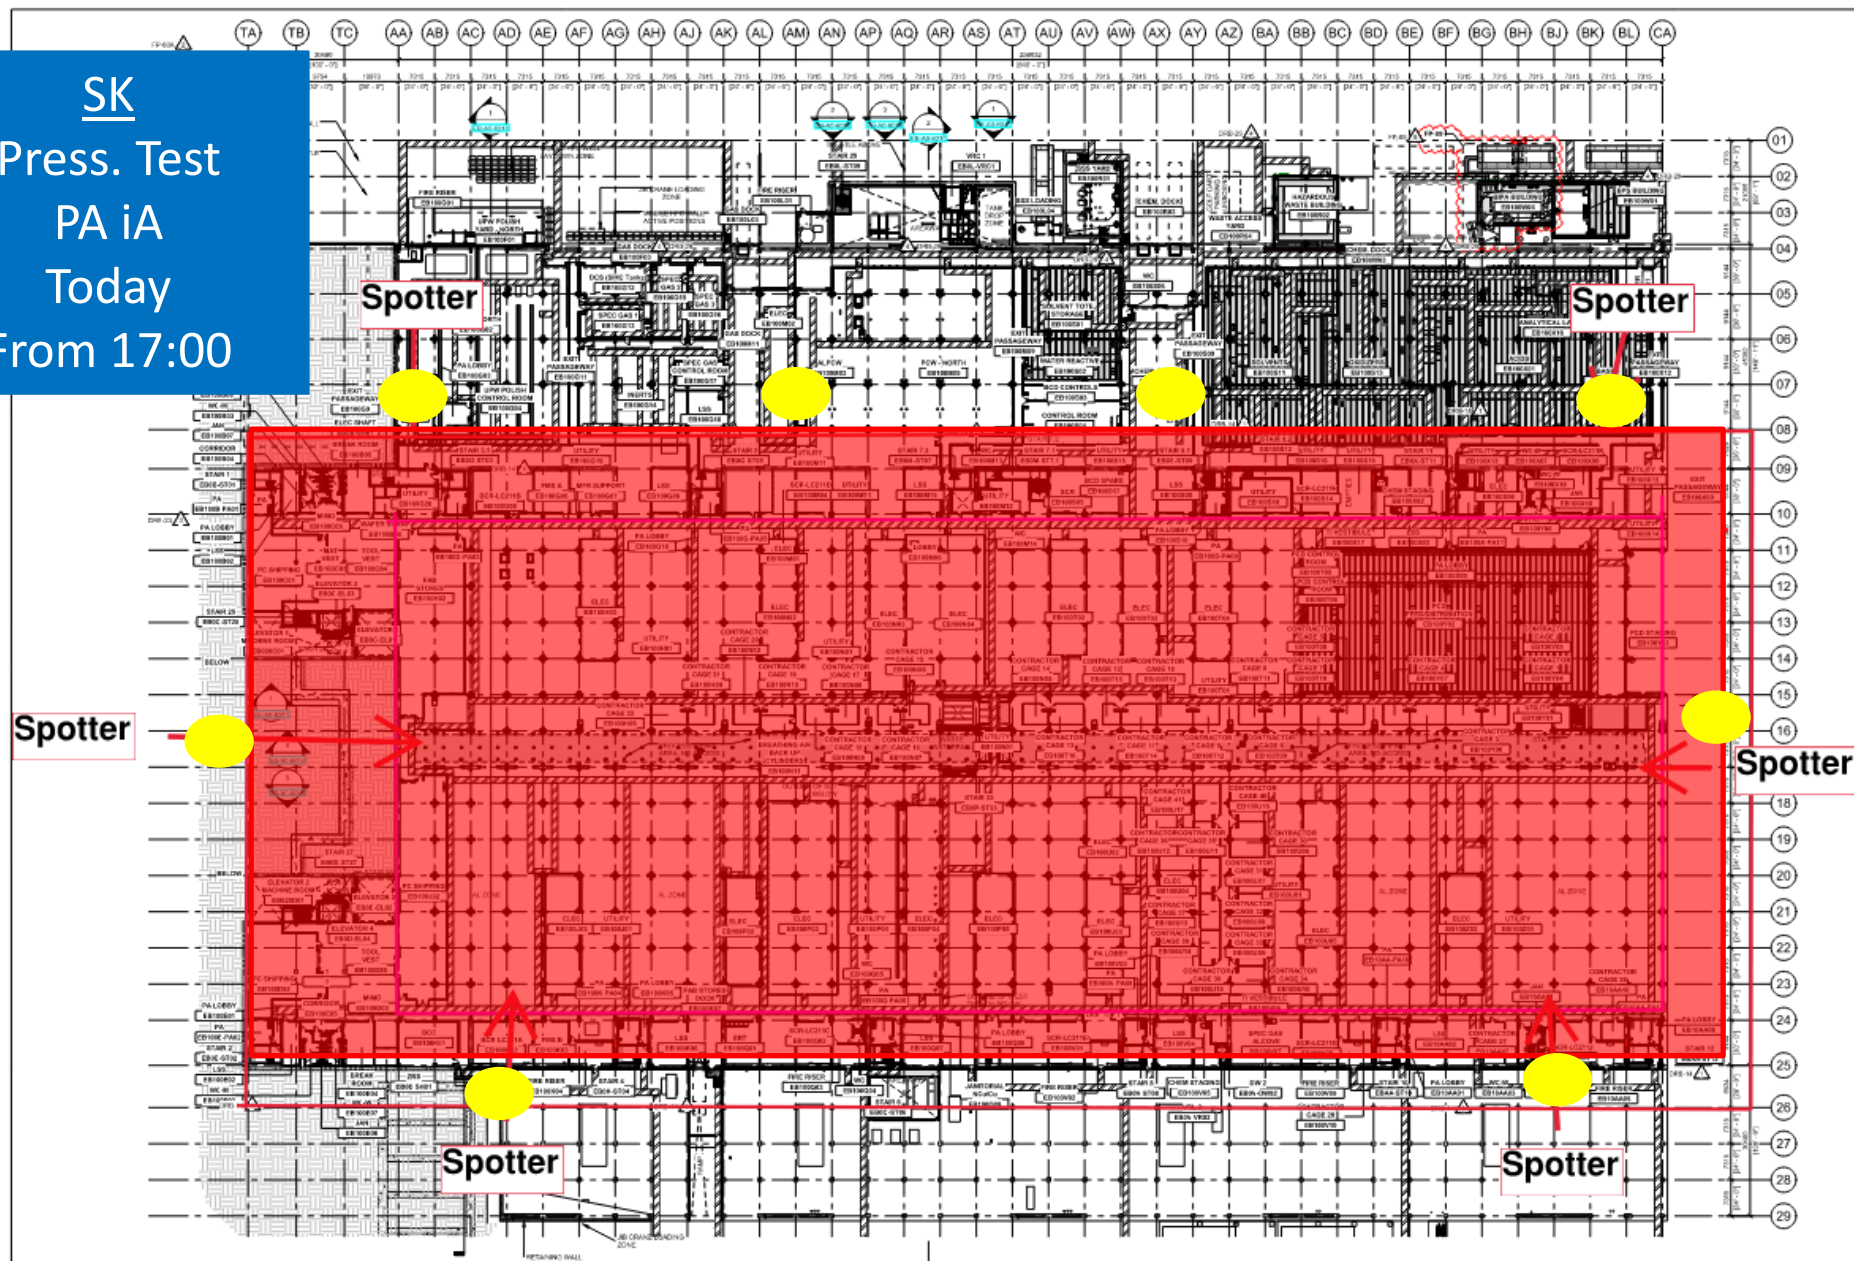

UTILITY LEVEL MOD1

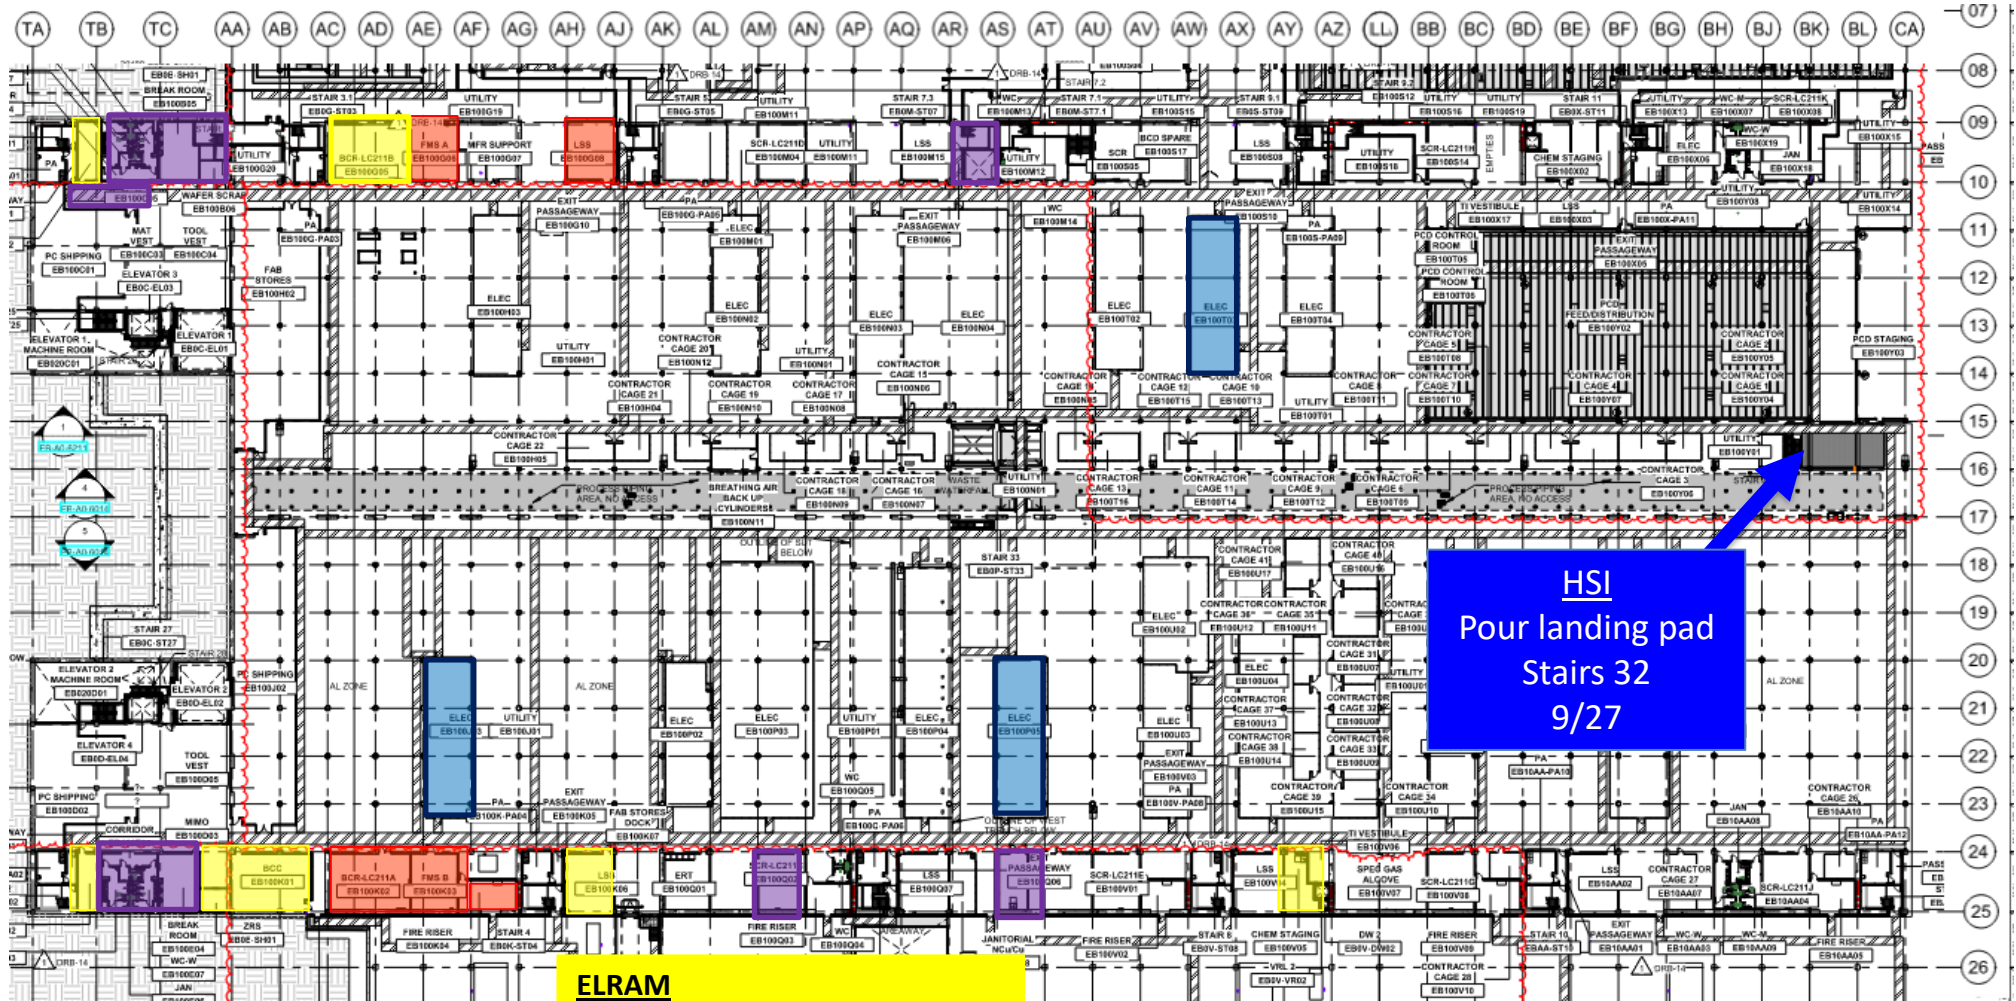

HSI
Pour landing pad
Stairs 32
9/27

BELFOR

TTNE - Corridor + Toilets + Break R
Stairs 7.3
Wafer scrap
TTNW - Toilets + Break R
SCR 2W
Exit pass 3W

ELRAM

Ongoing
LSS TTNW + TTNE
BCR 1E
CHEN STAGING
LSS 2W
Chem staging
BACKING
BCR 1E+1W – Pending funding
LSS's


MEP+Elctrical

Ready for re-install
FMS A 1E
FMS B 1W
Fire Risers 1W
BCC

[illegible]




SUT 38.1 LEVEL

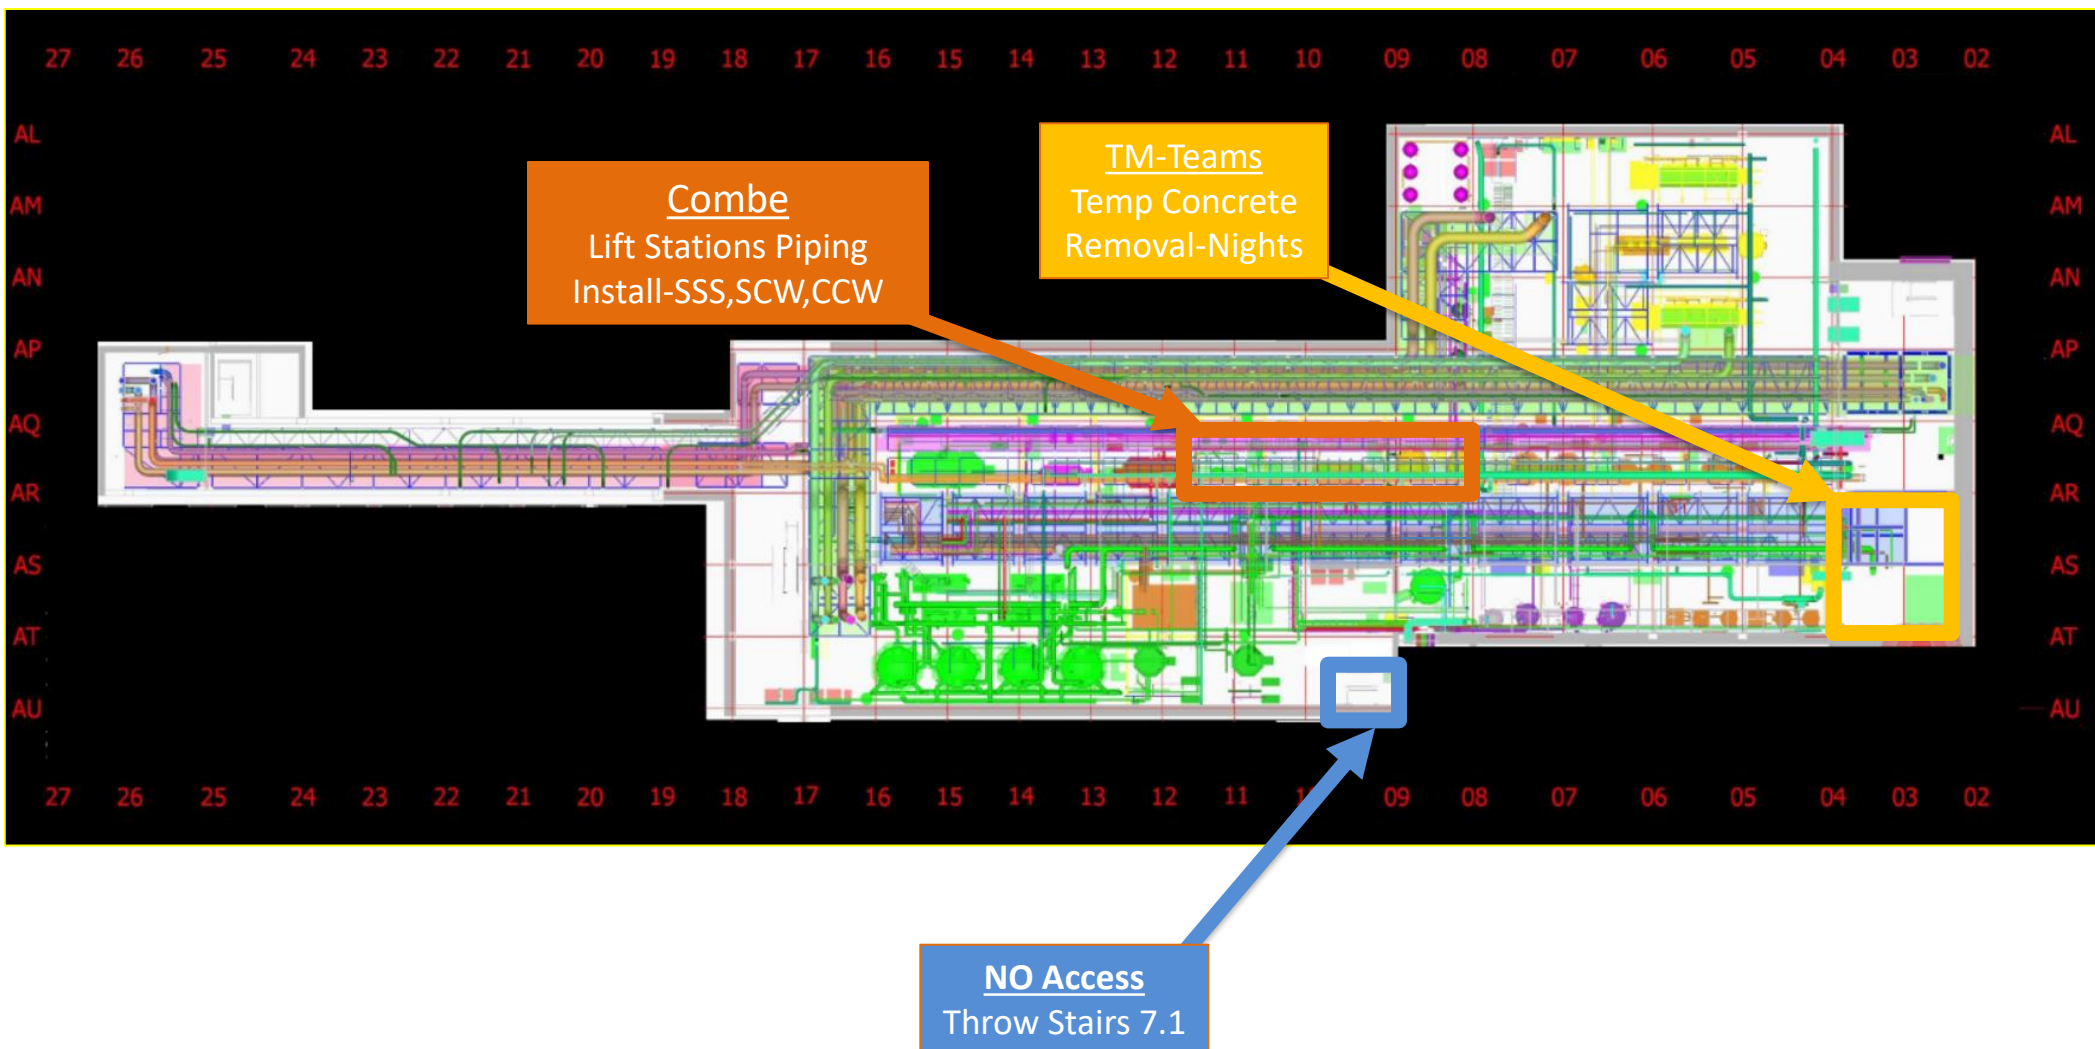



SUT 38.2 LEVEL

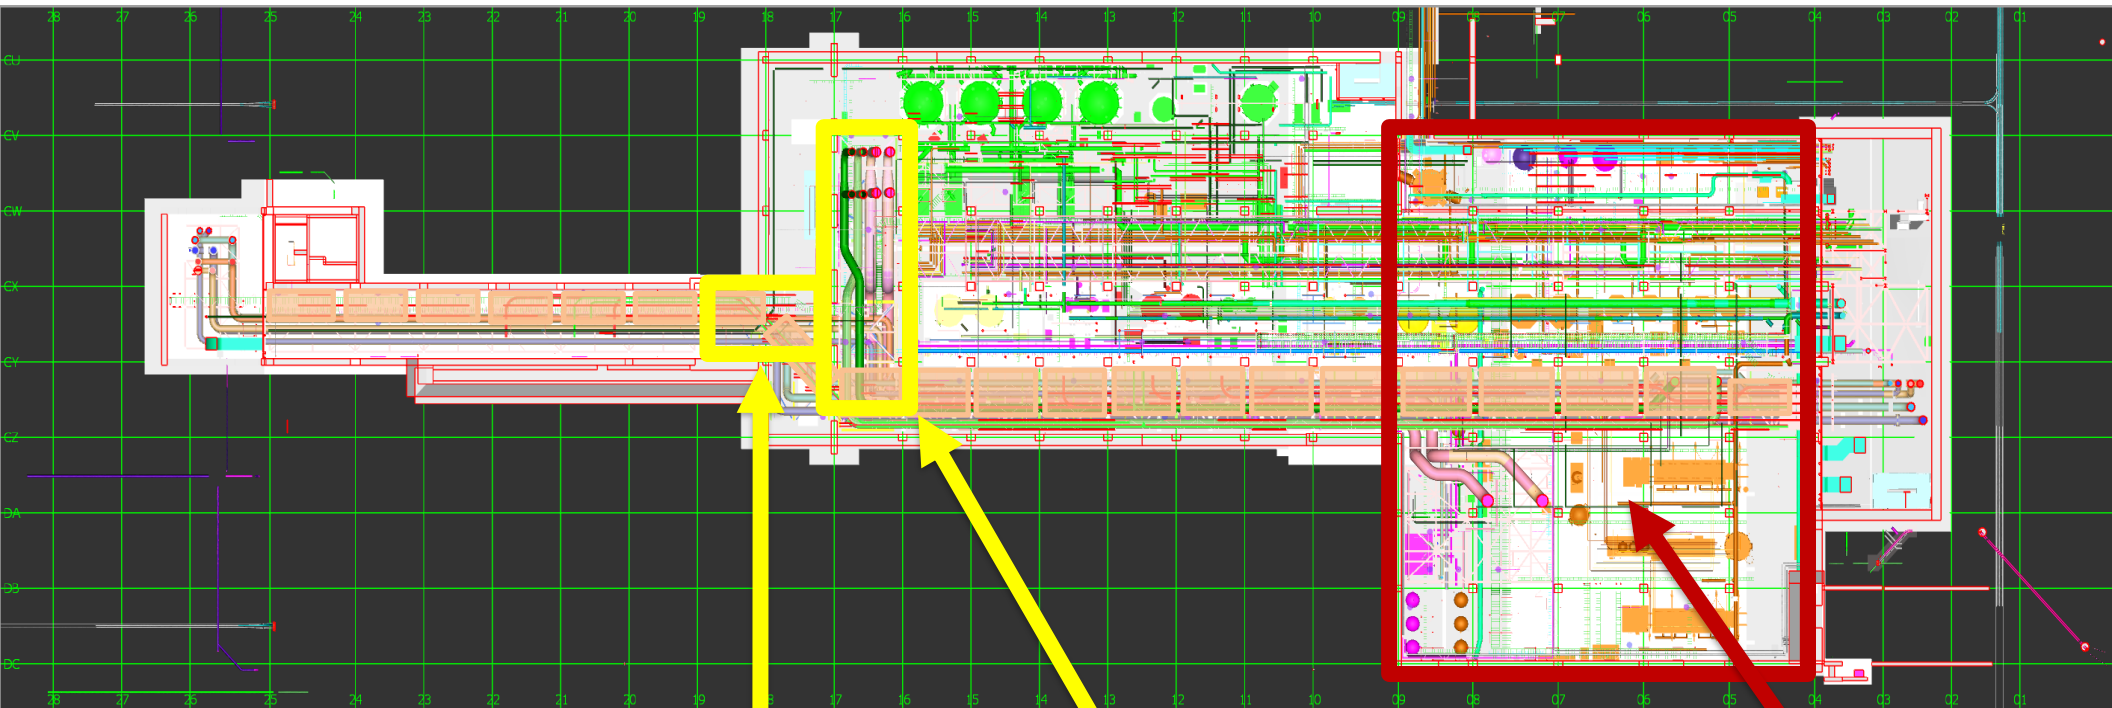


CRW
H&T
NEED PIPING

17-18 line
Bore Loading


16-17 line
lvl2+3
bed lift: Need a
Date

Vesda
H&T
Ongoing

SUBFAB BUILDOUT MOD 1

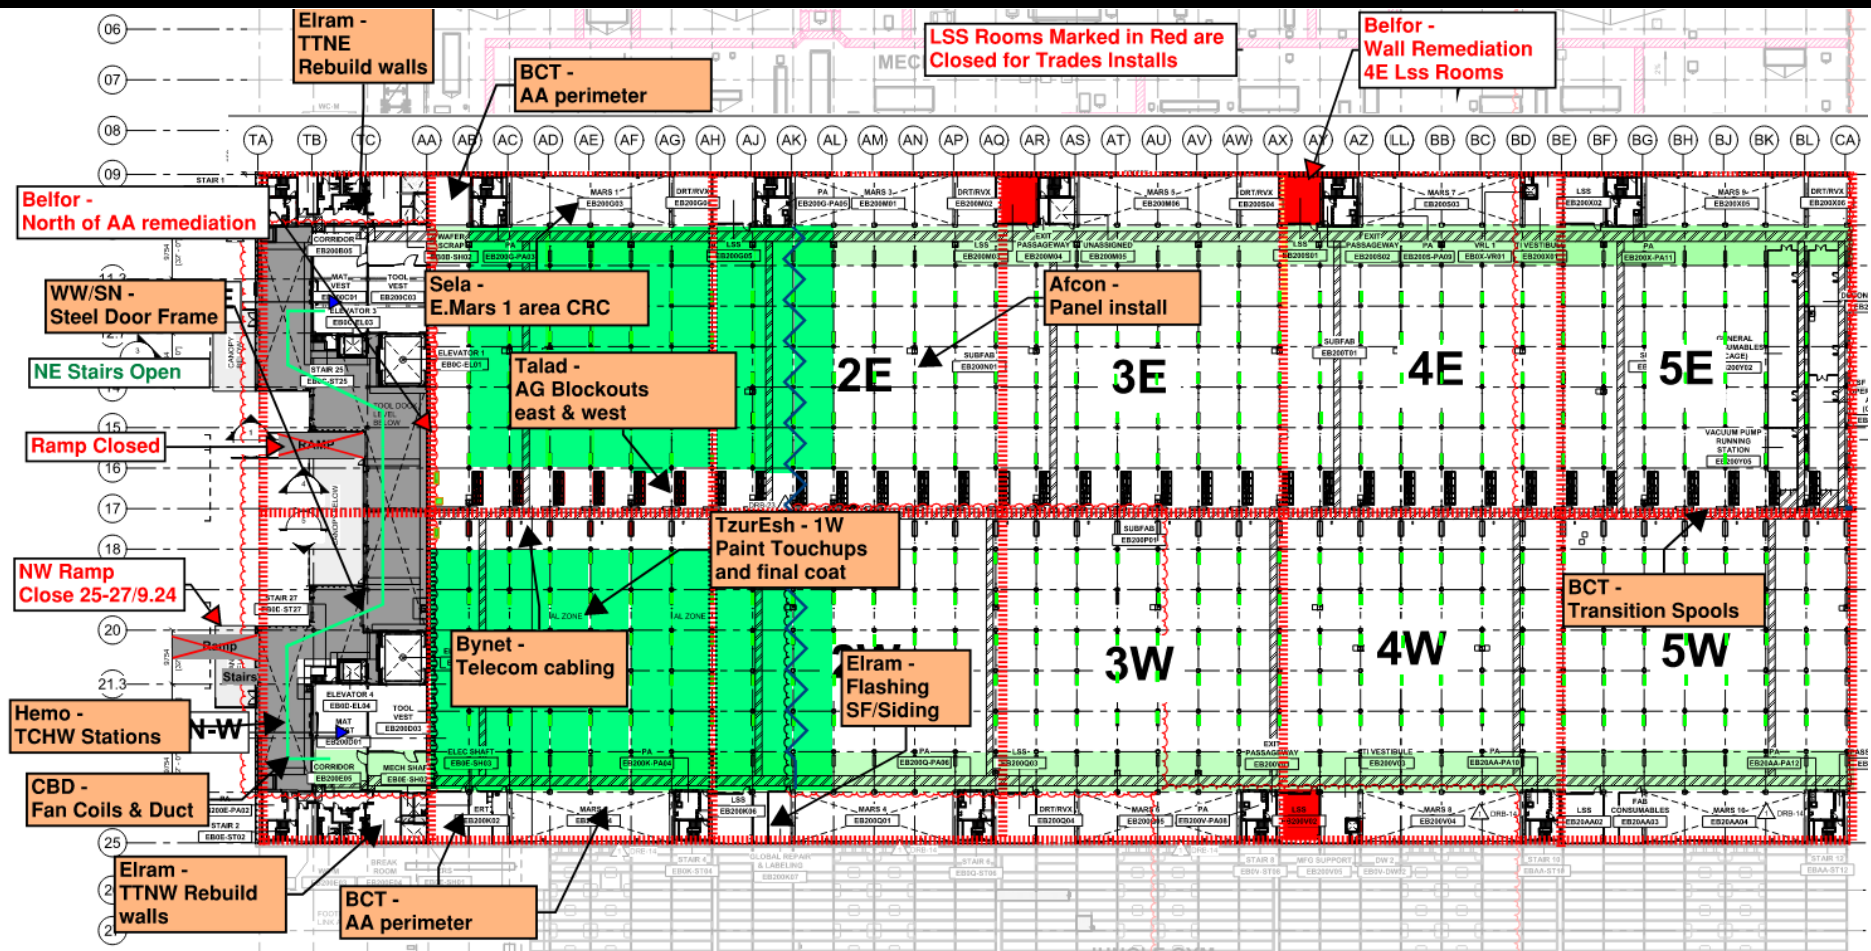

SUBFAB CRC TOPCOAT

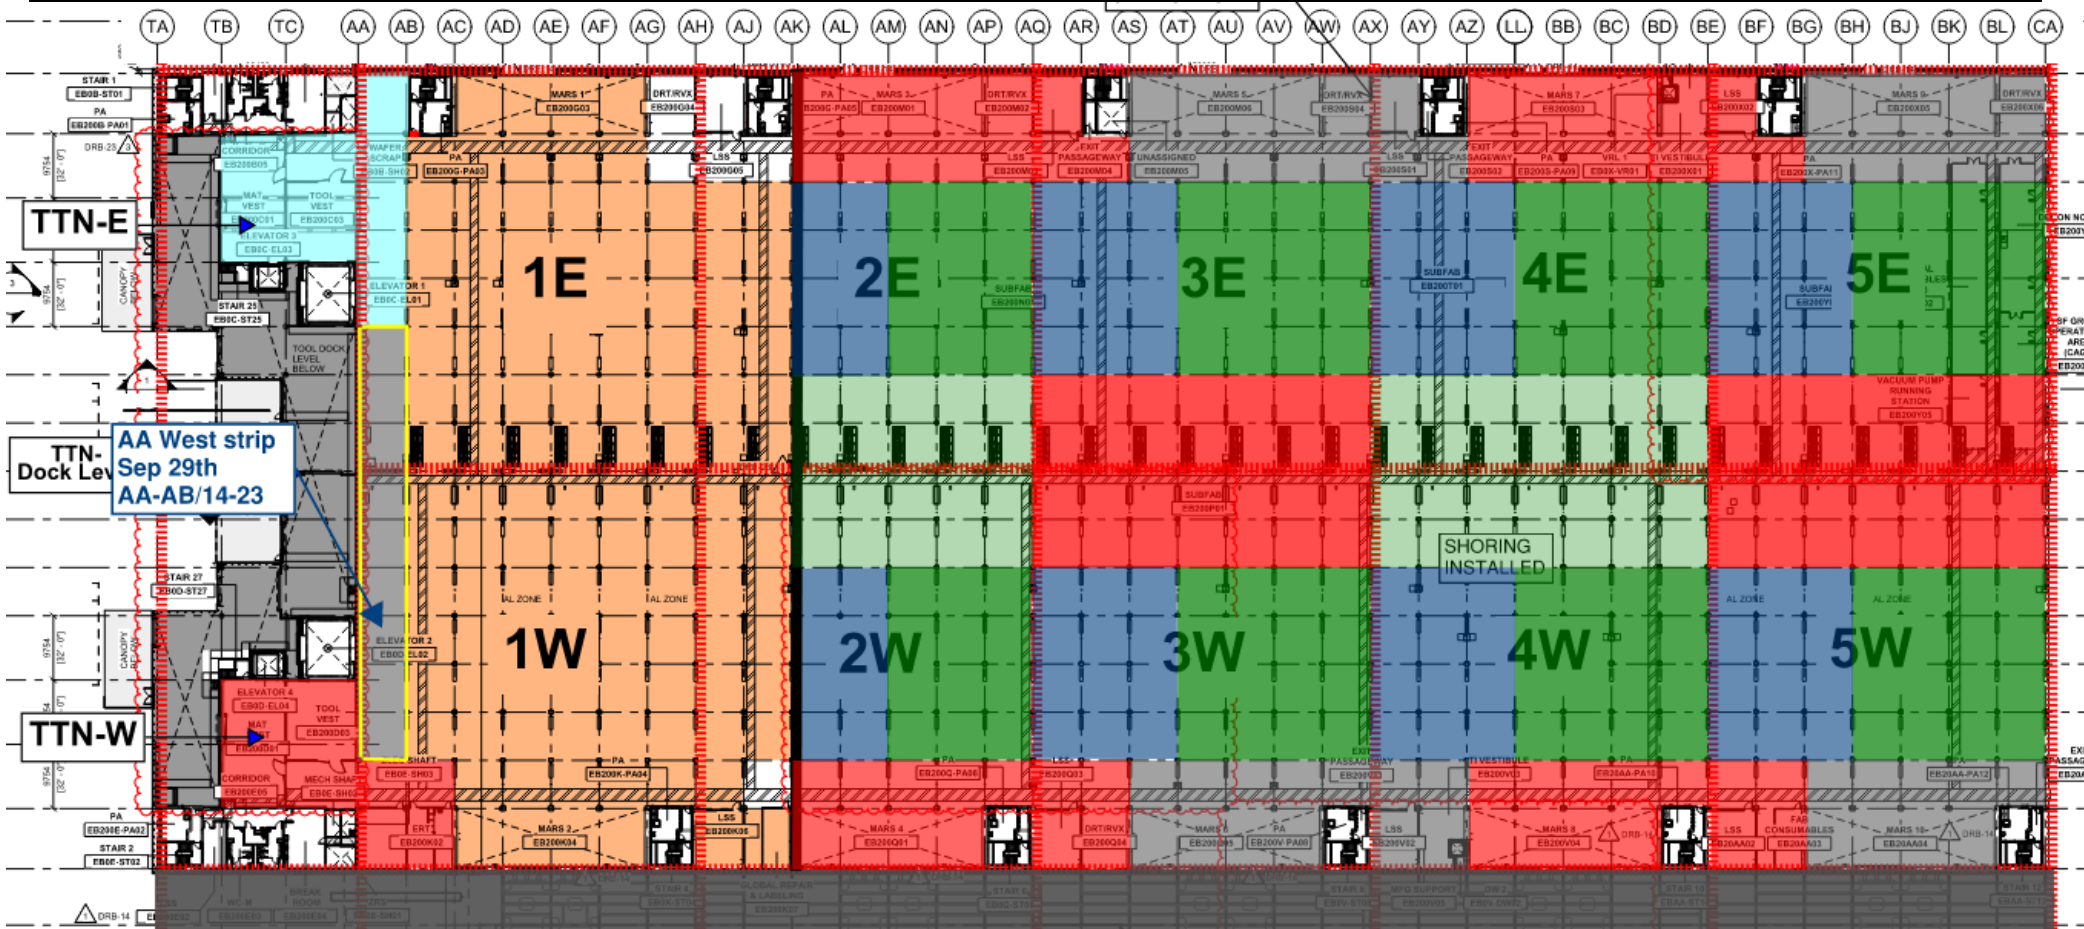

SUBFAB CRC TOPCOAT




SUBFAB CRC TOPCOAT




SUBFAB CRC TOPCOAT






BCT Pressure Test Exclusion Zone

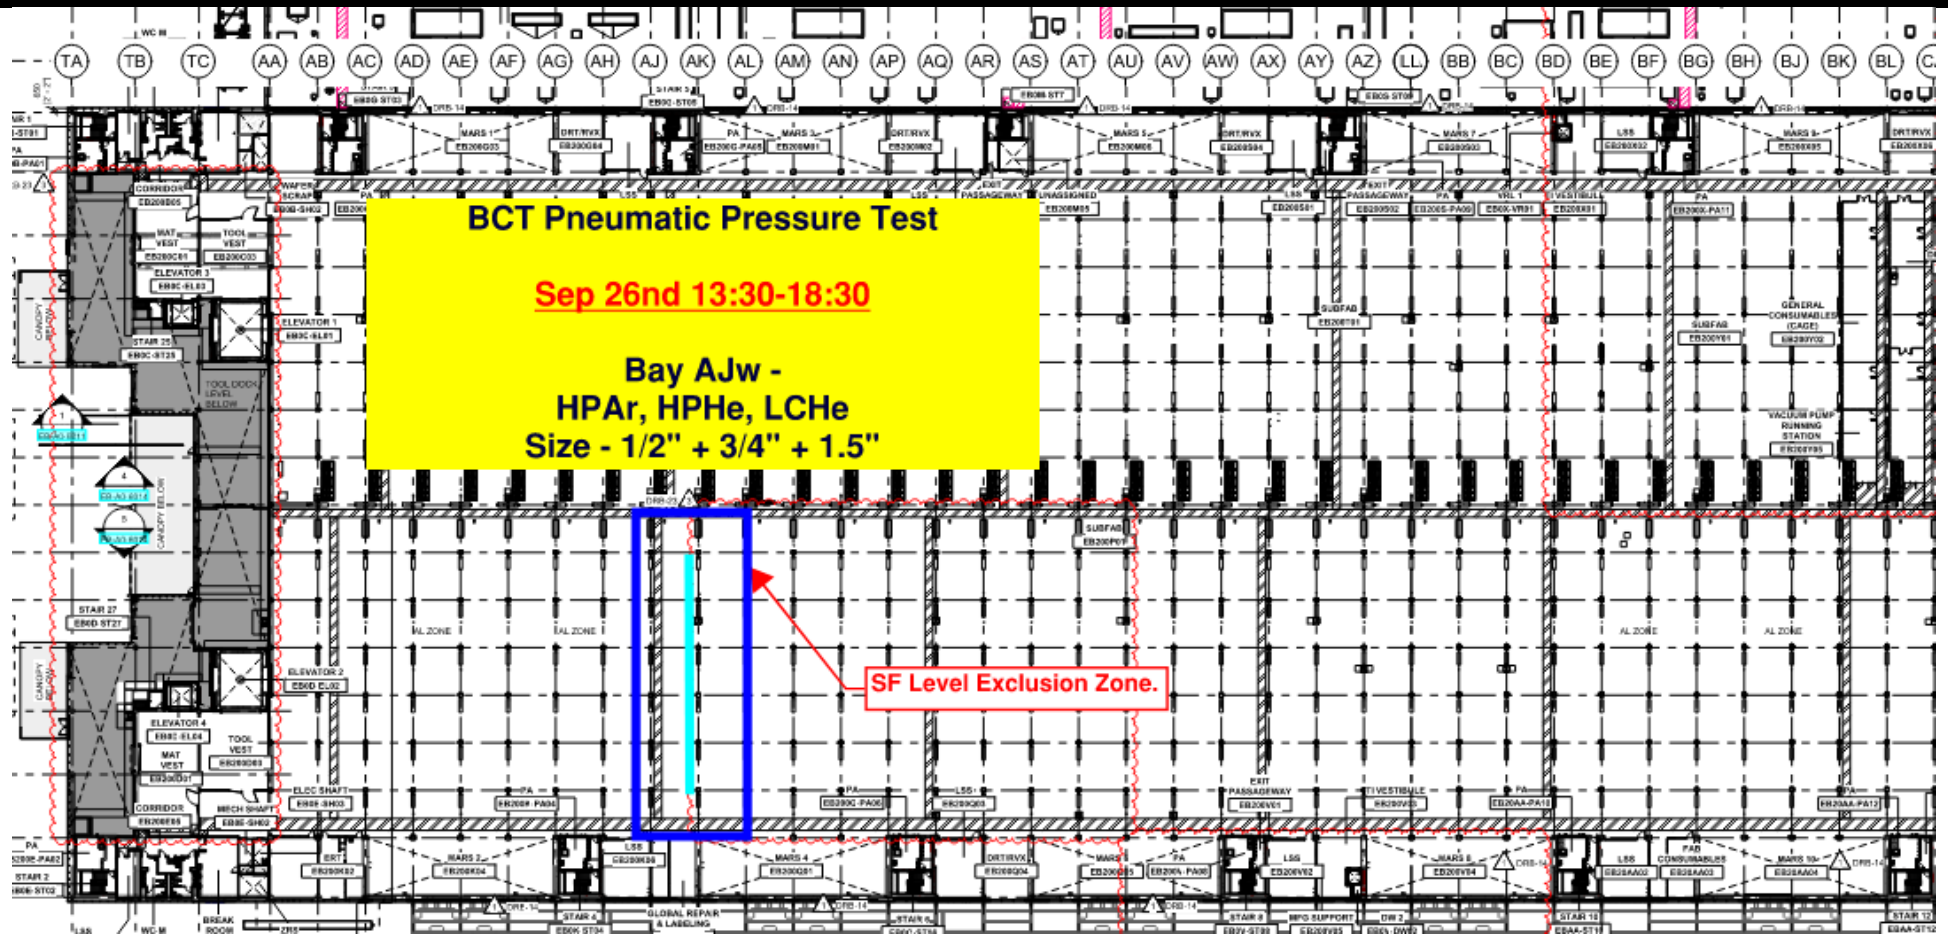



SUBFAB BUILDOUT MOD 2

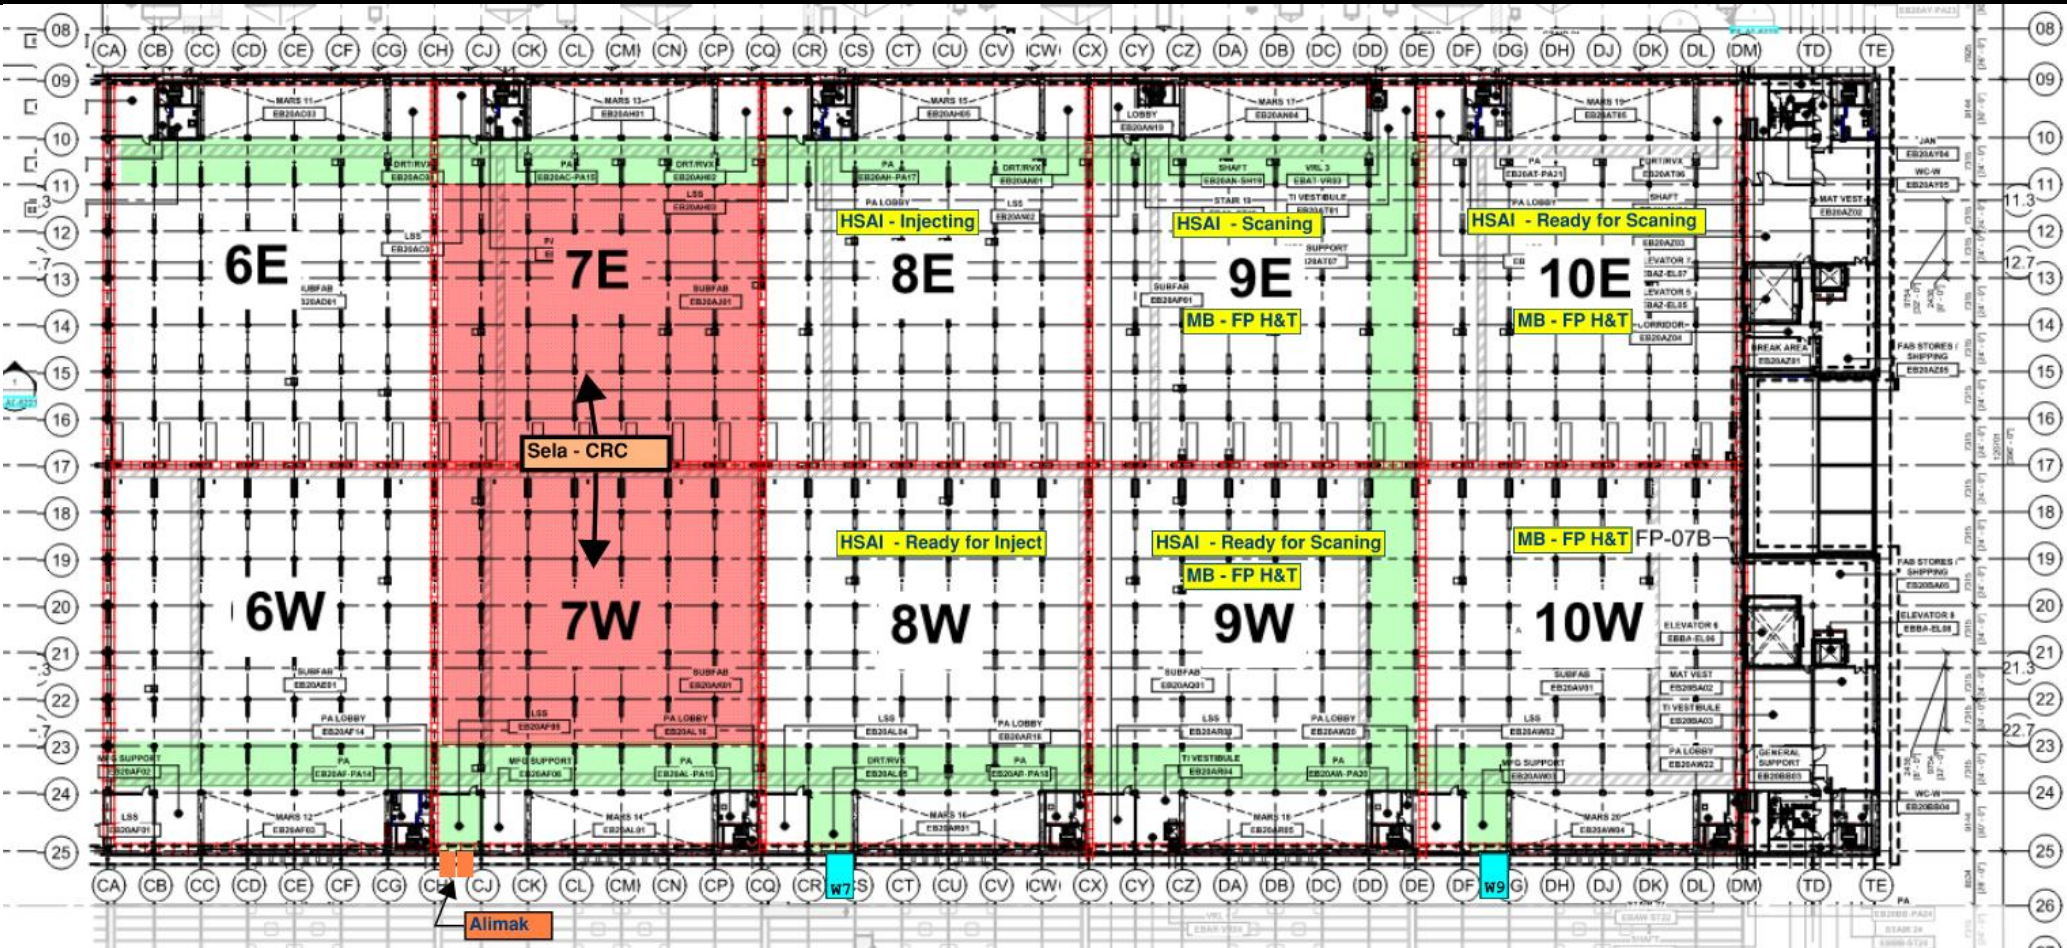

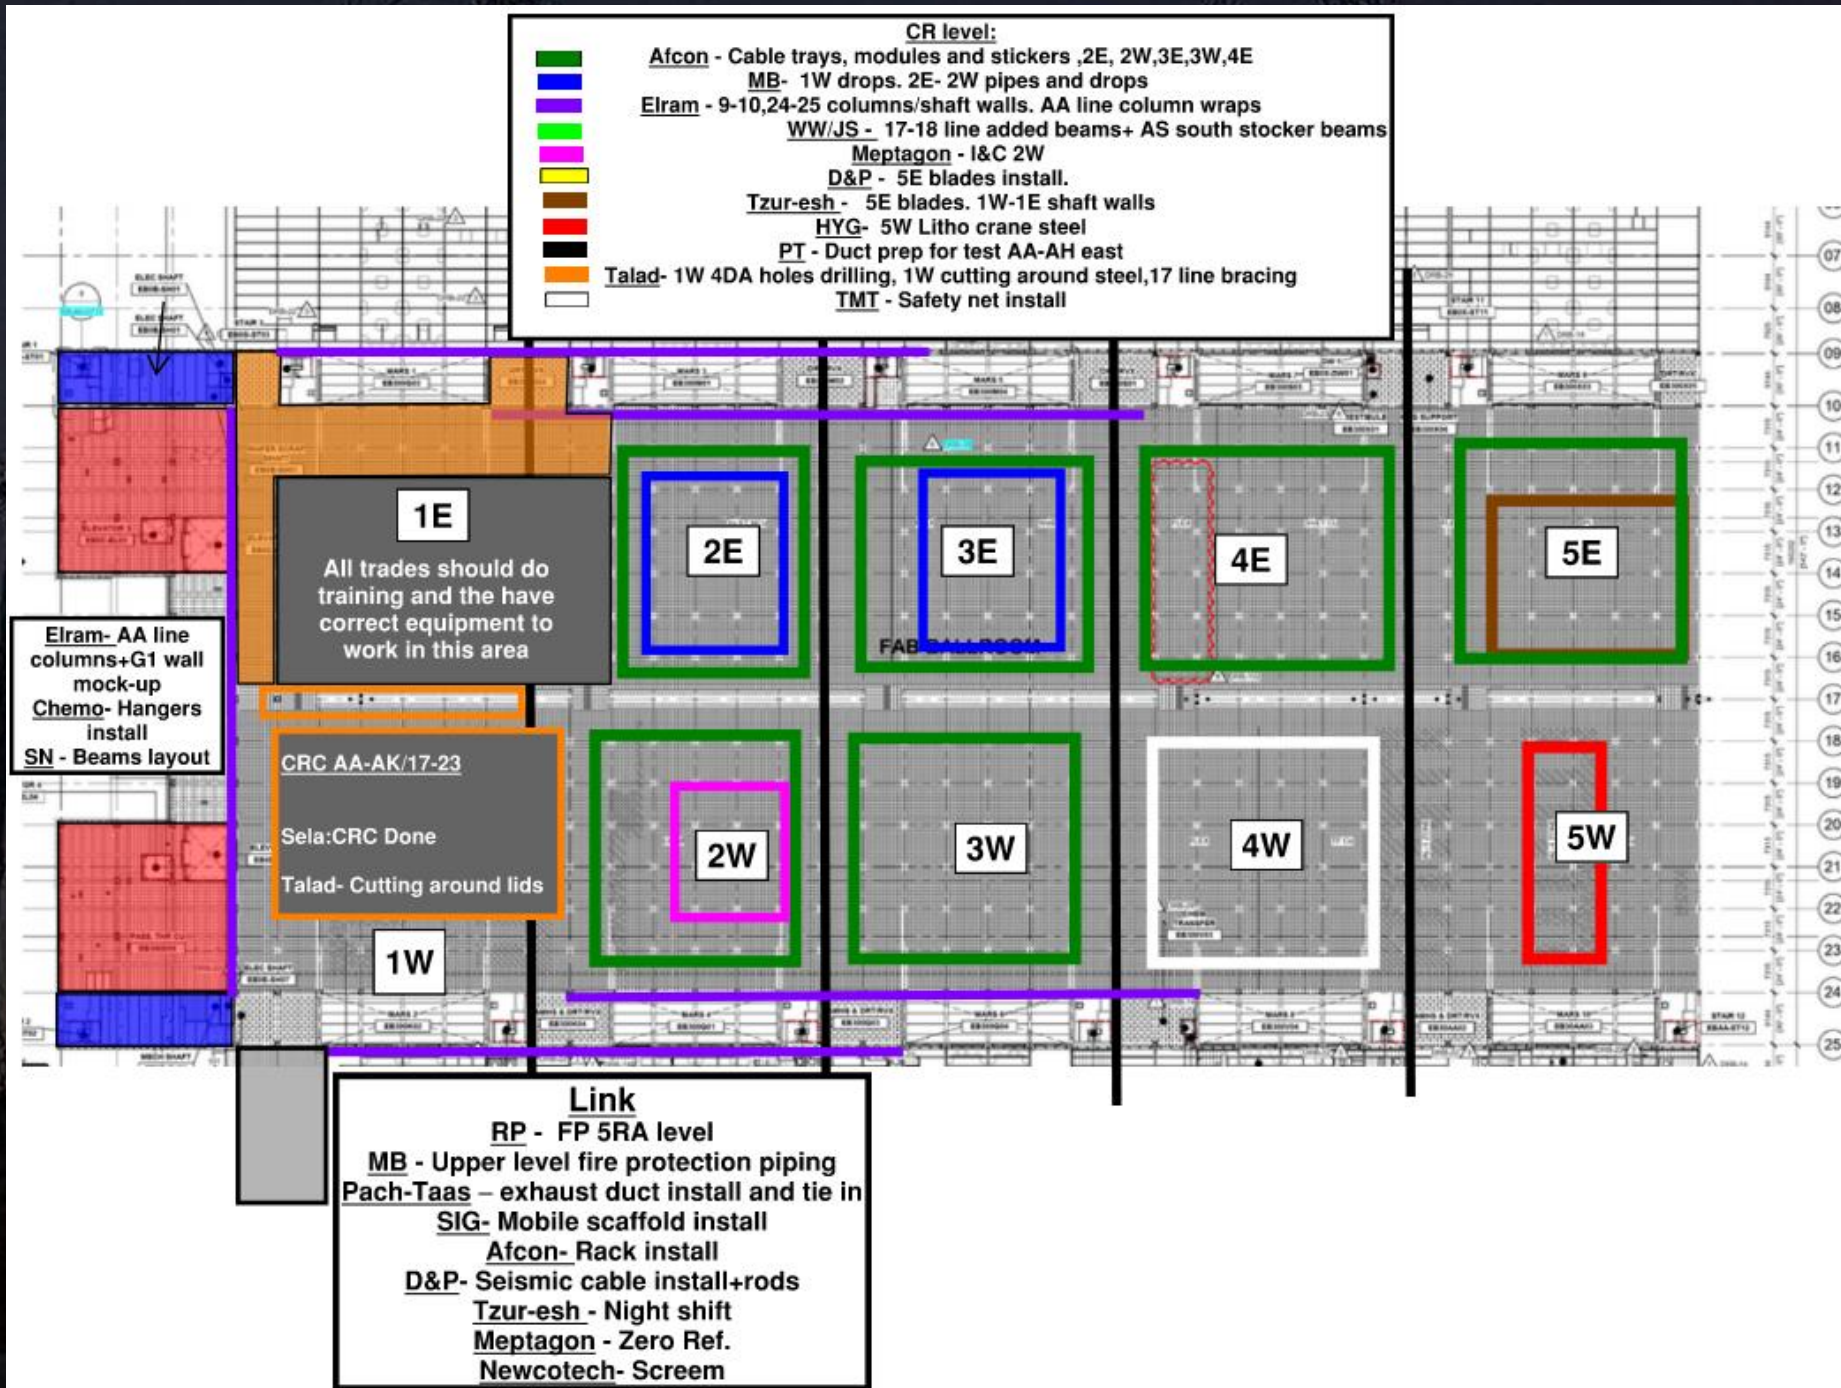


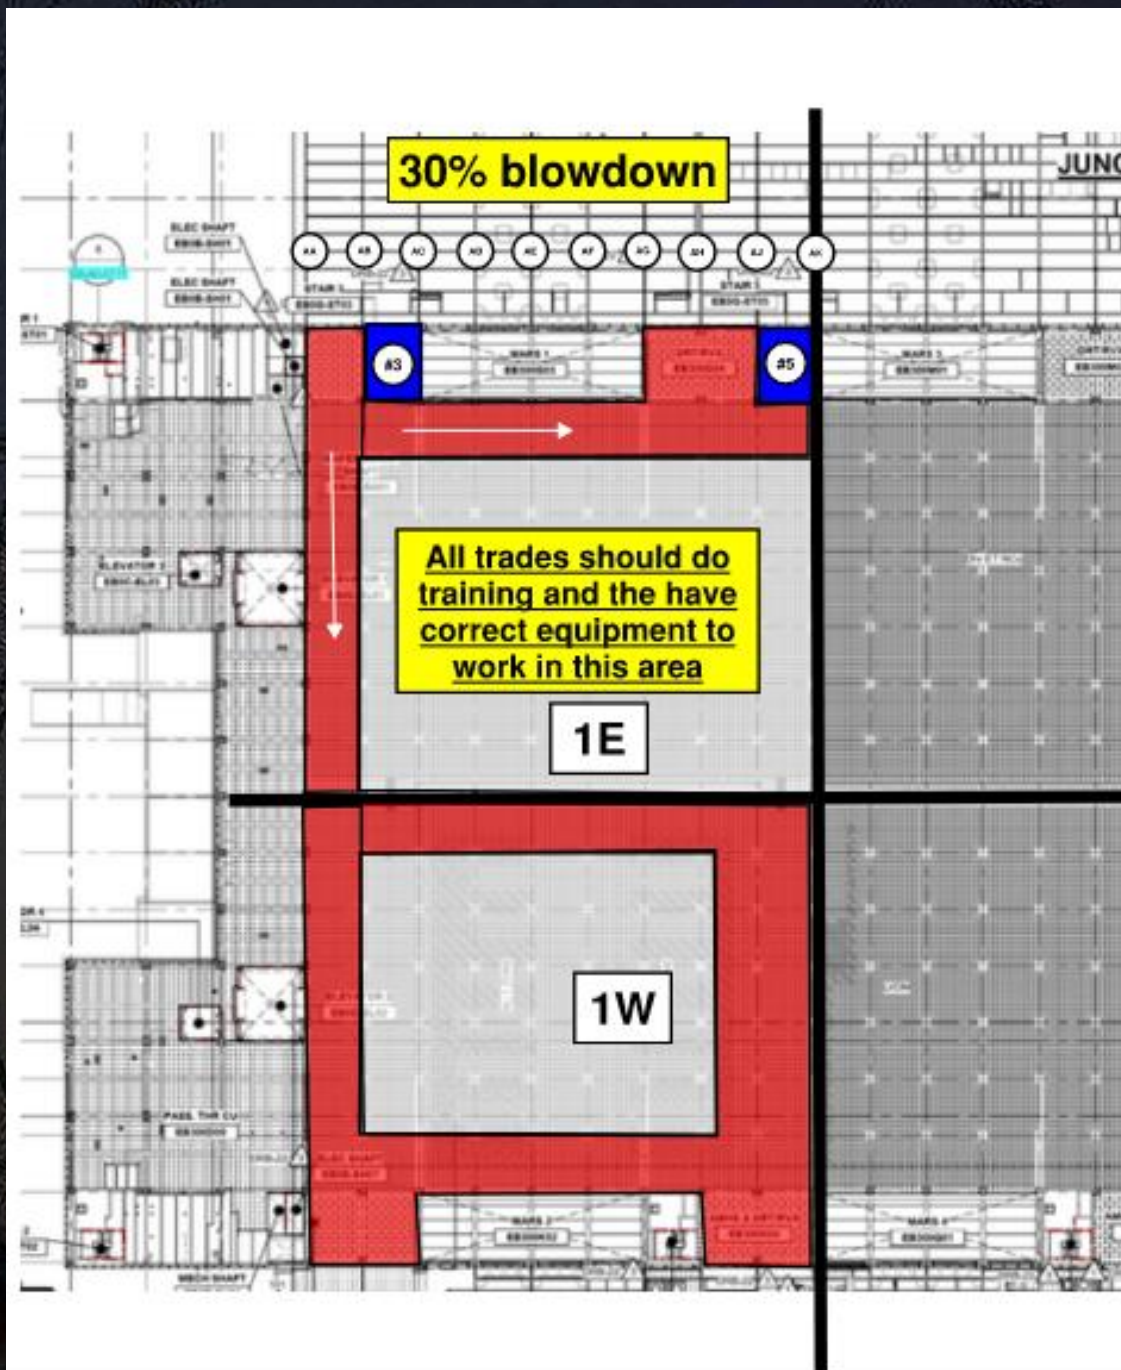

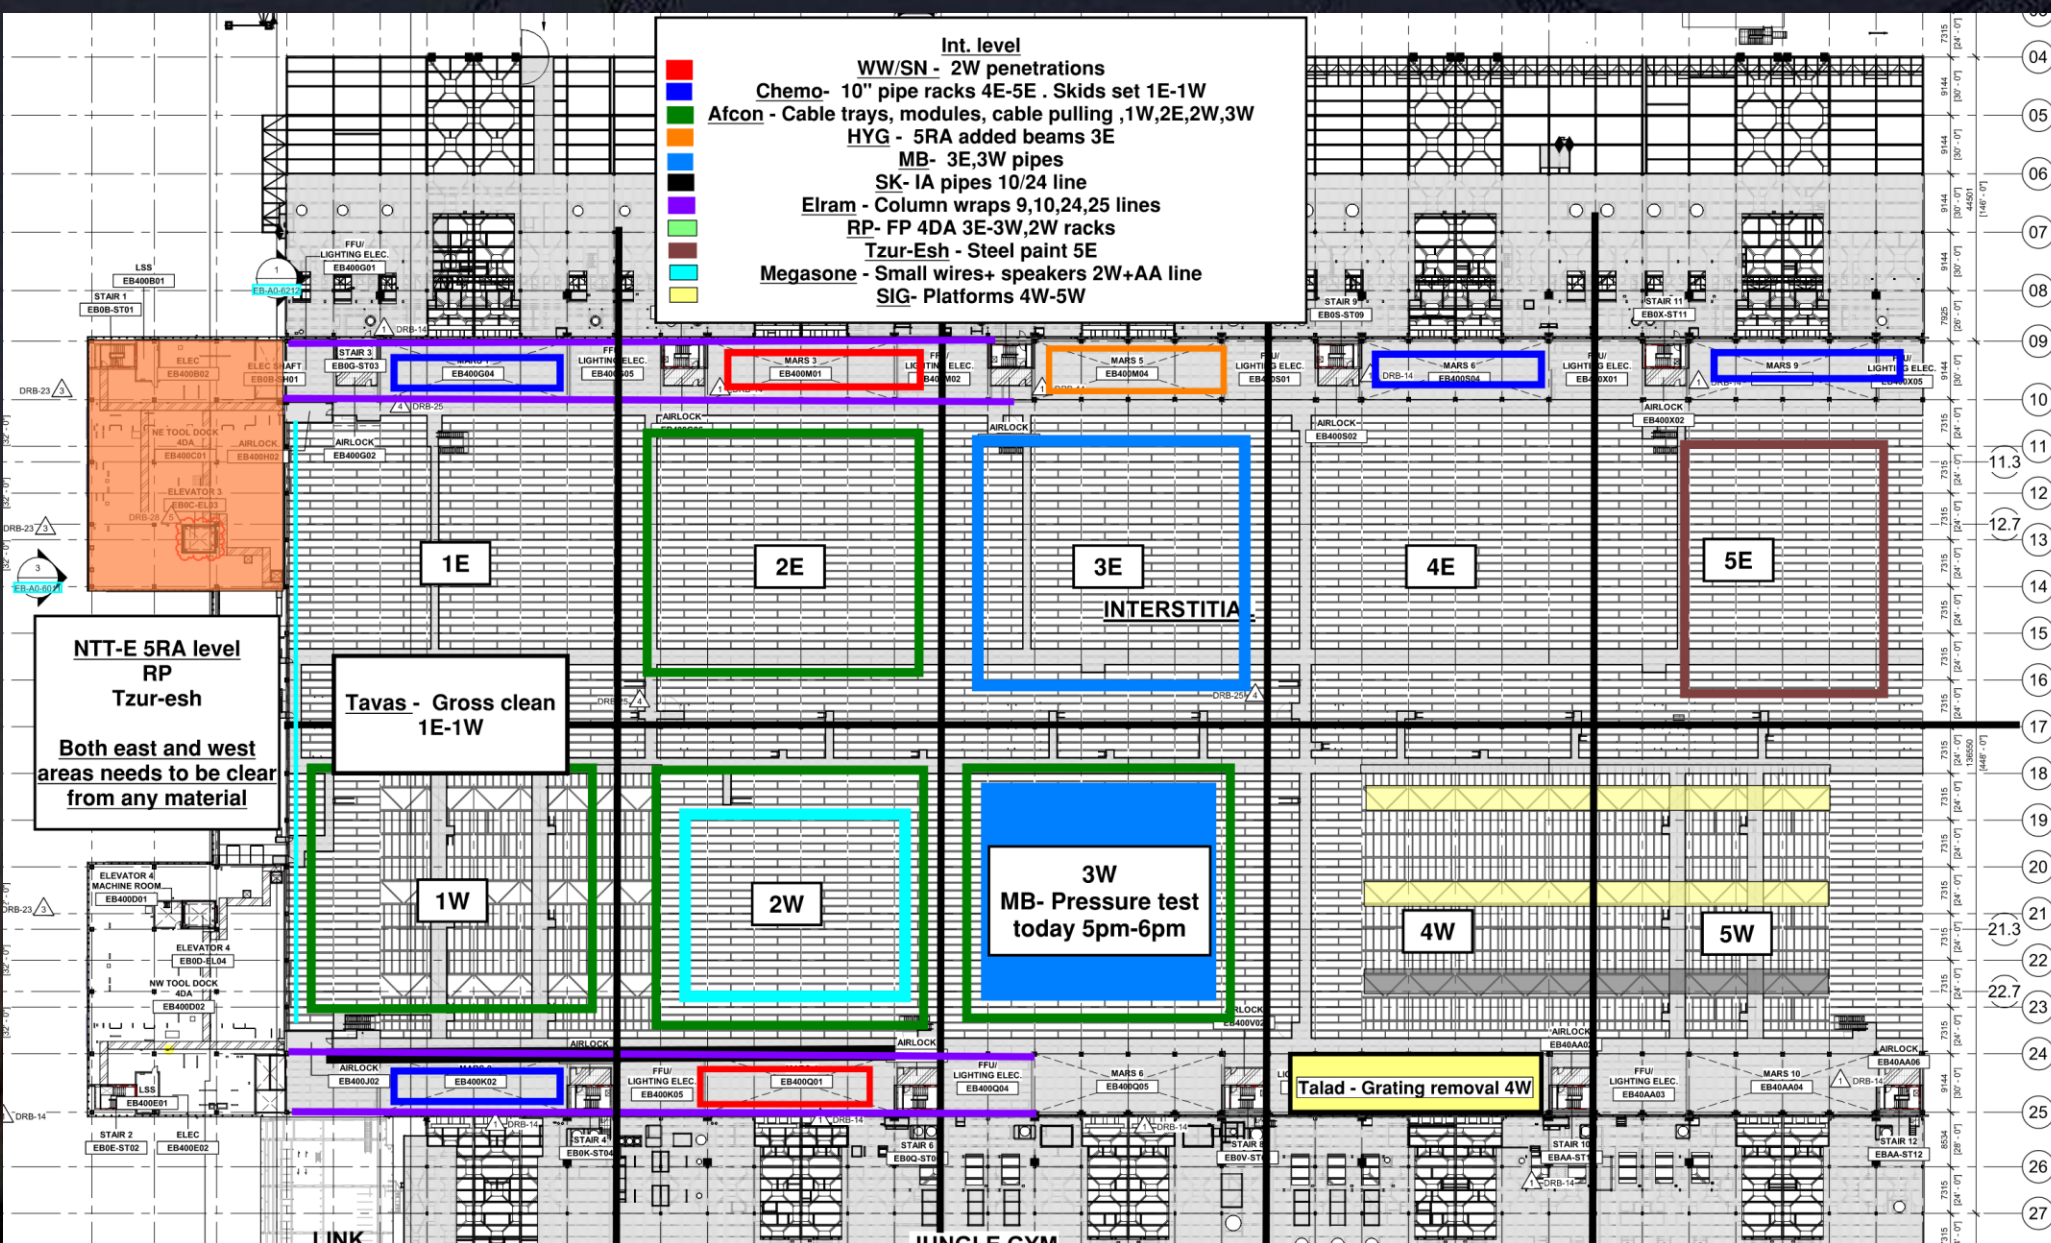



11D 17 SUPPORT STEEL PER ERECTION PROCEDURE SHOWN ON SHEET 114P.000.3.1

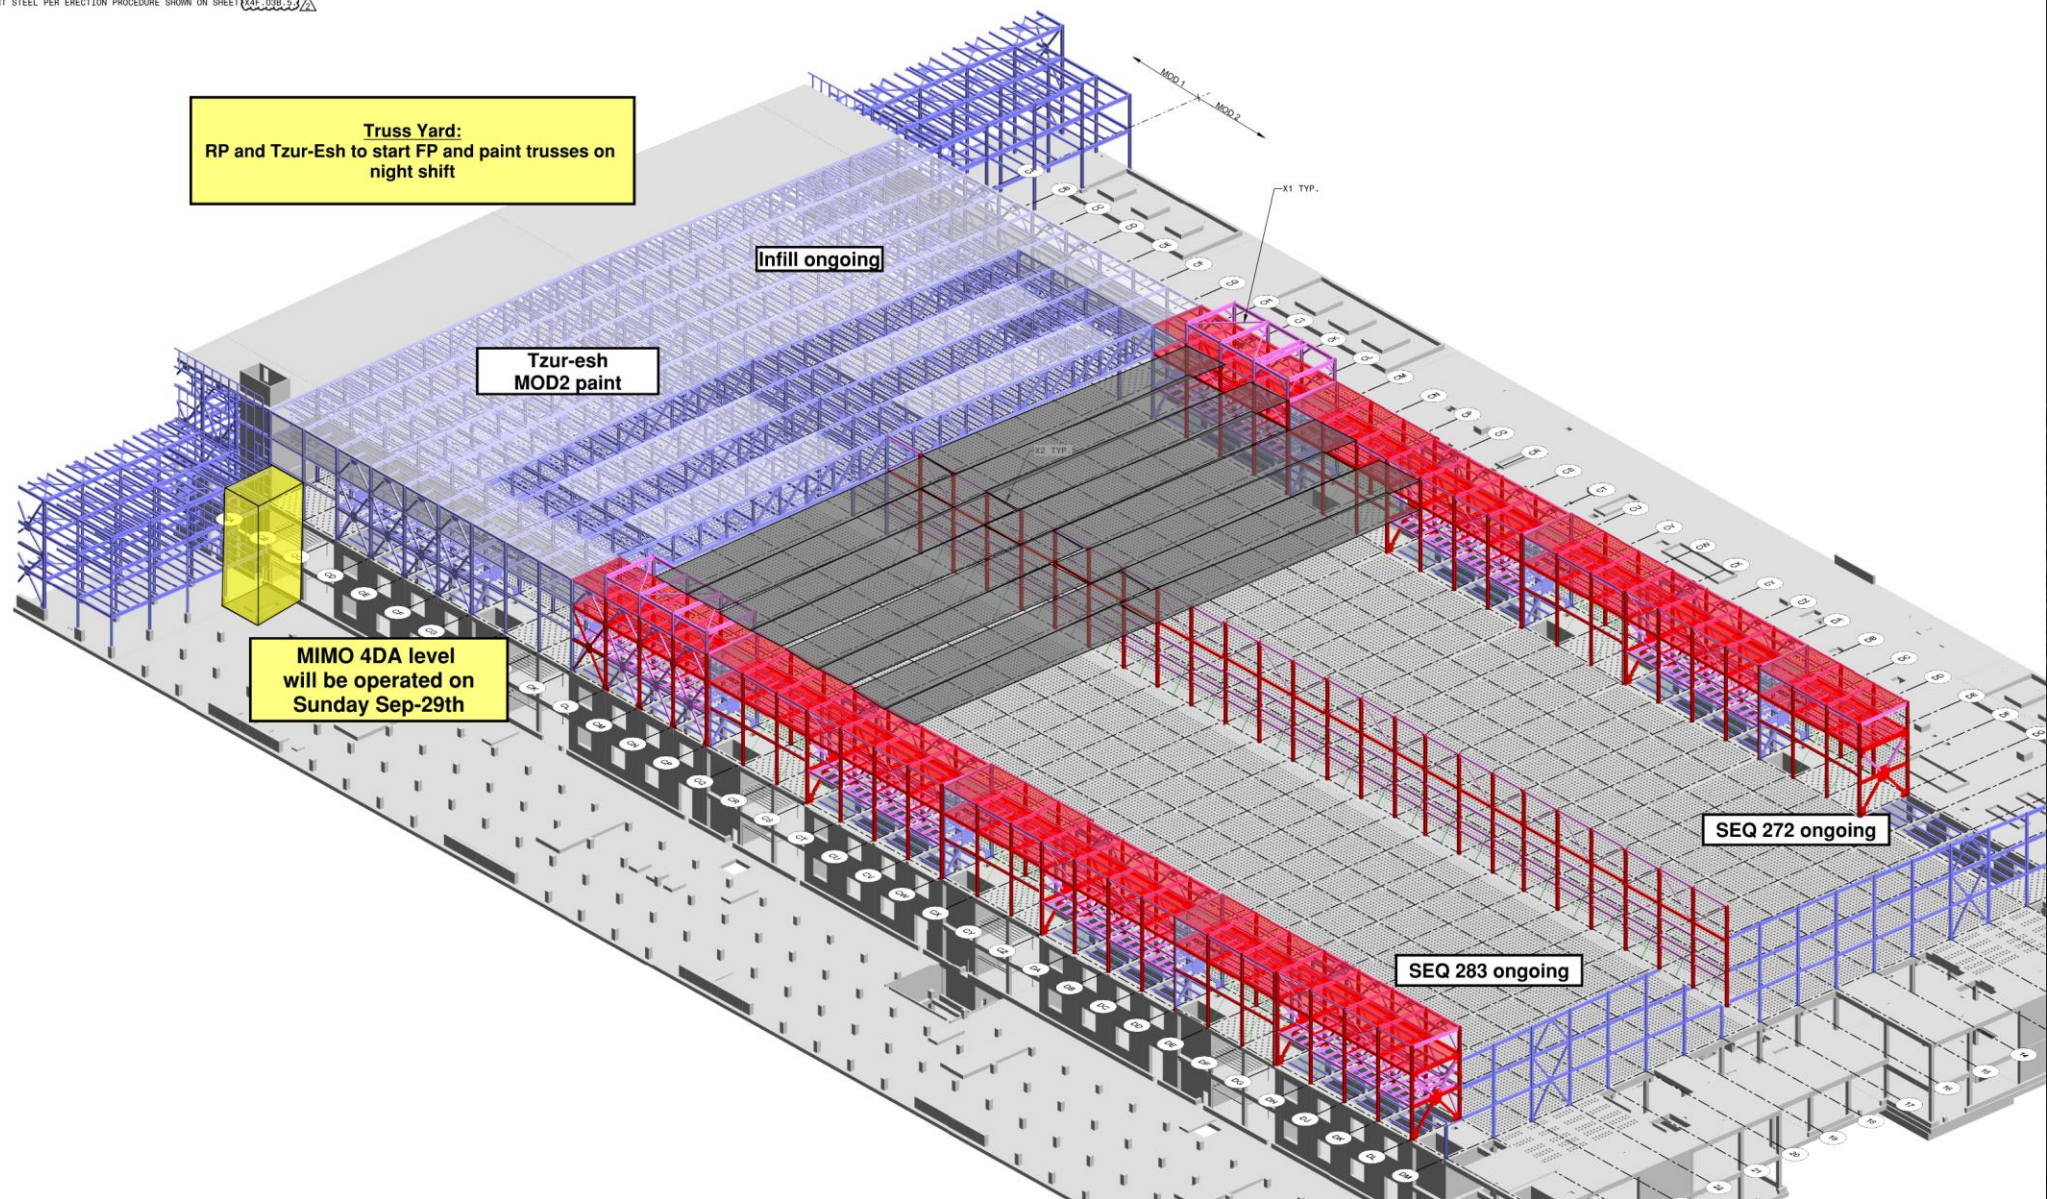



Keep Up with the good work!



HYG stairs
Sep/22
Before 2 & 25 &
7.1
Sep/22

NETD-SW-1
STAIR 1

01E-SW
STAIR 3

02E-SW
STAIR 5

03E-SW
steel
STAIR 7.3

04E-SW
STAIR 9

05E-SW
STAIR 11

Electra -EL1 Sep/22
ASD - scaffold sep/22
Elram - Aug/29 AA
EL3 - steel ongoing

HSI-SOMD Sep/22
W.W EL2 - plates
Sep/23

NWTD-SW-1
STAIR 2

01W-SW
STAIR 4

02W-SW
STAIR 6

03W-SW
STAIR 8

04W-SW
STAIR 10

05W-SW
STAIR 12


T.M chipping Sep/18
VRC Sep/25


DW + VRL
Sep/29
ELRAM - drywall


MEGASON LSS
AFCON - Telecom

DW + VRL
Sep/25
ELRAM - drywall

HYG Handrails
#8 - Sep/24
3 WEEKS

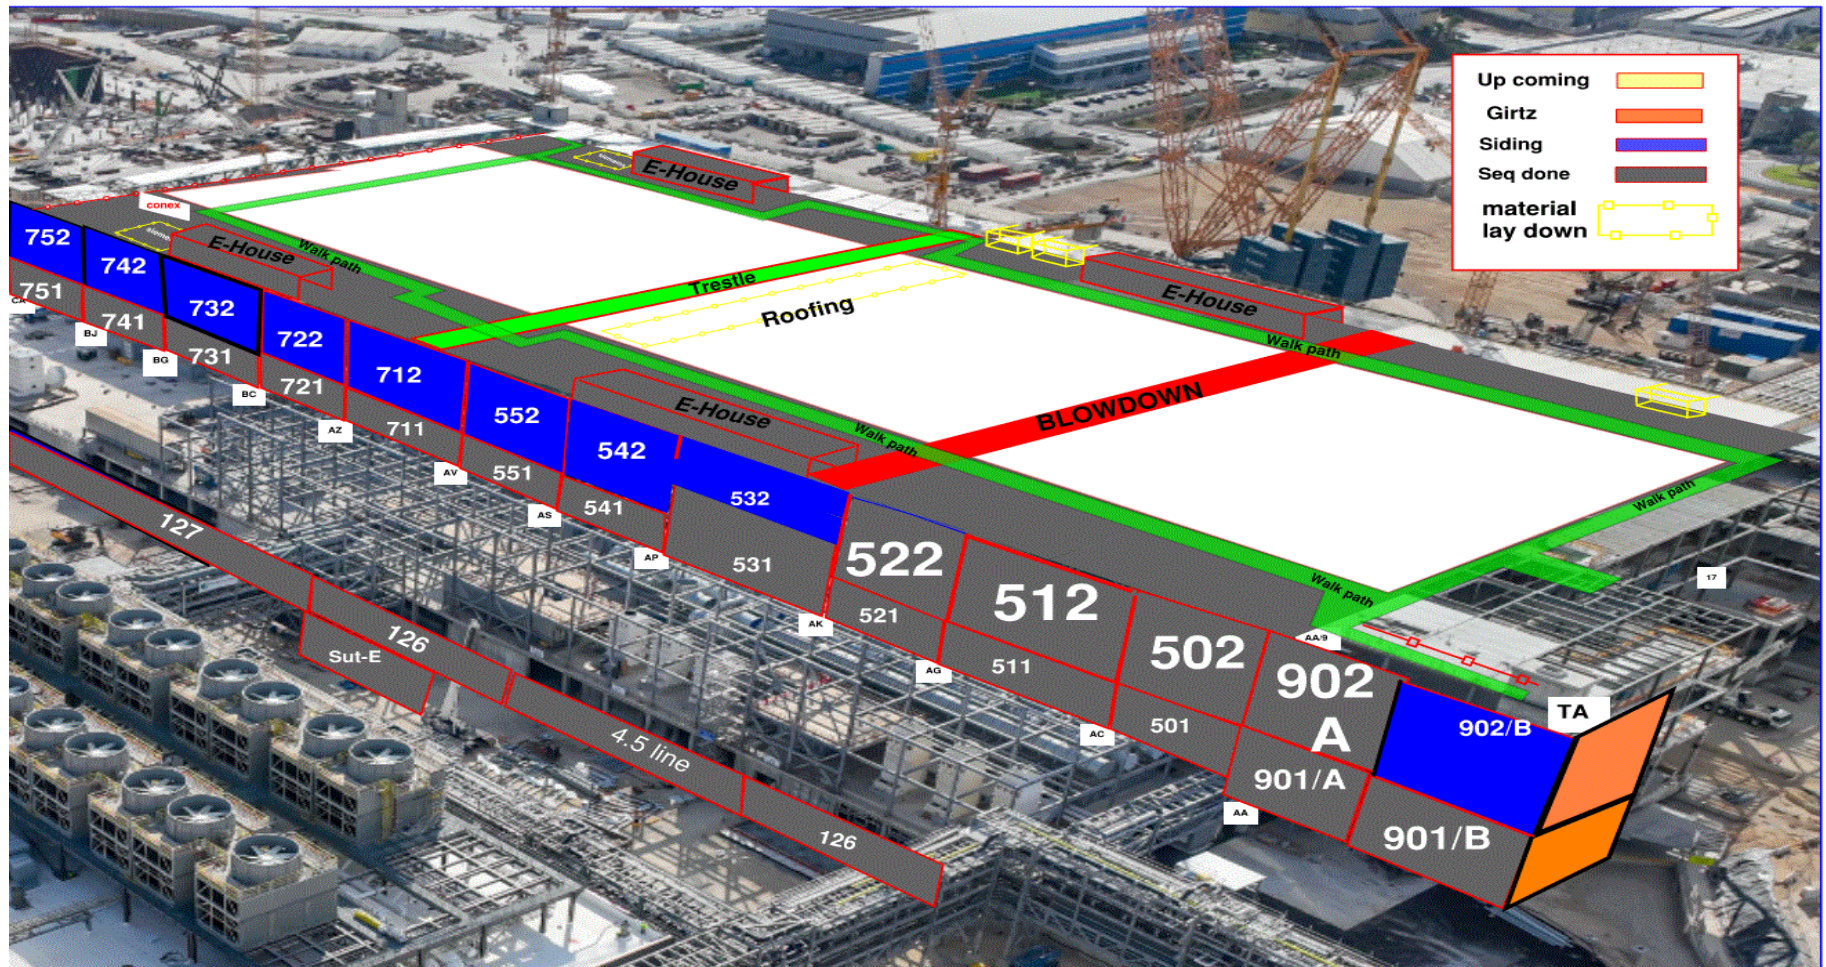

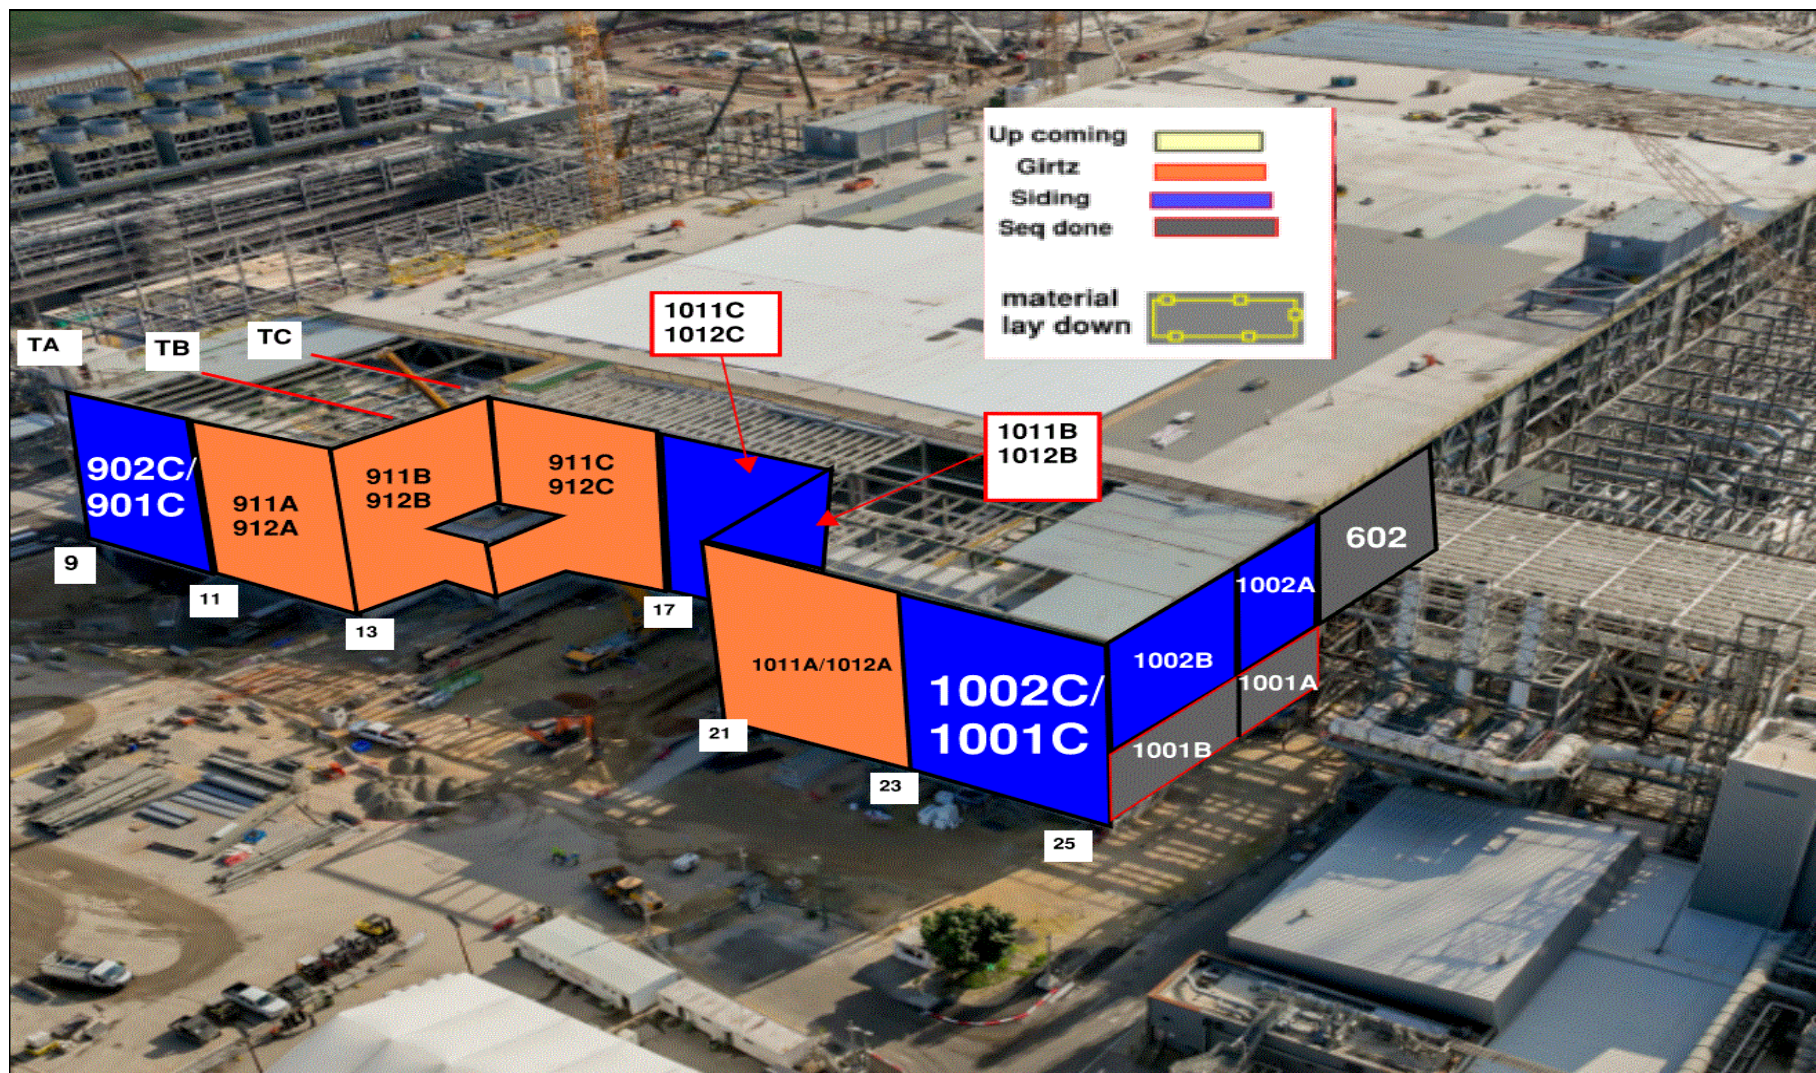

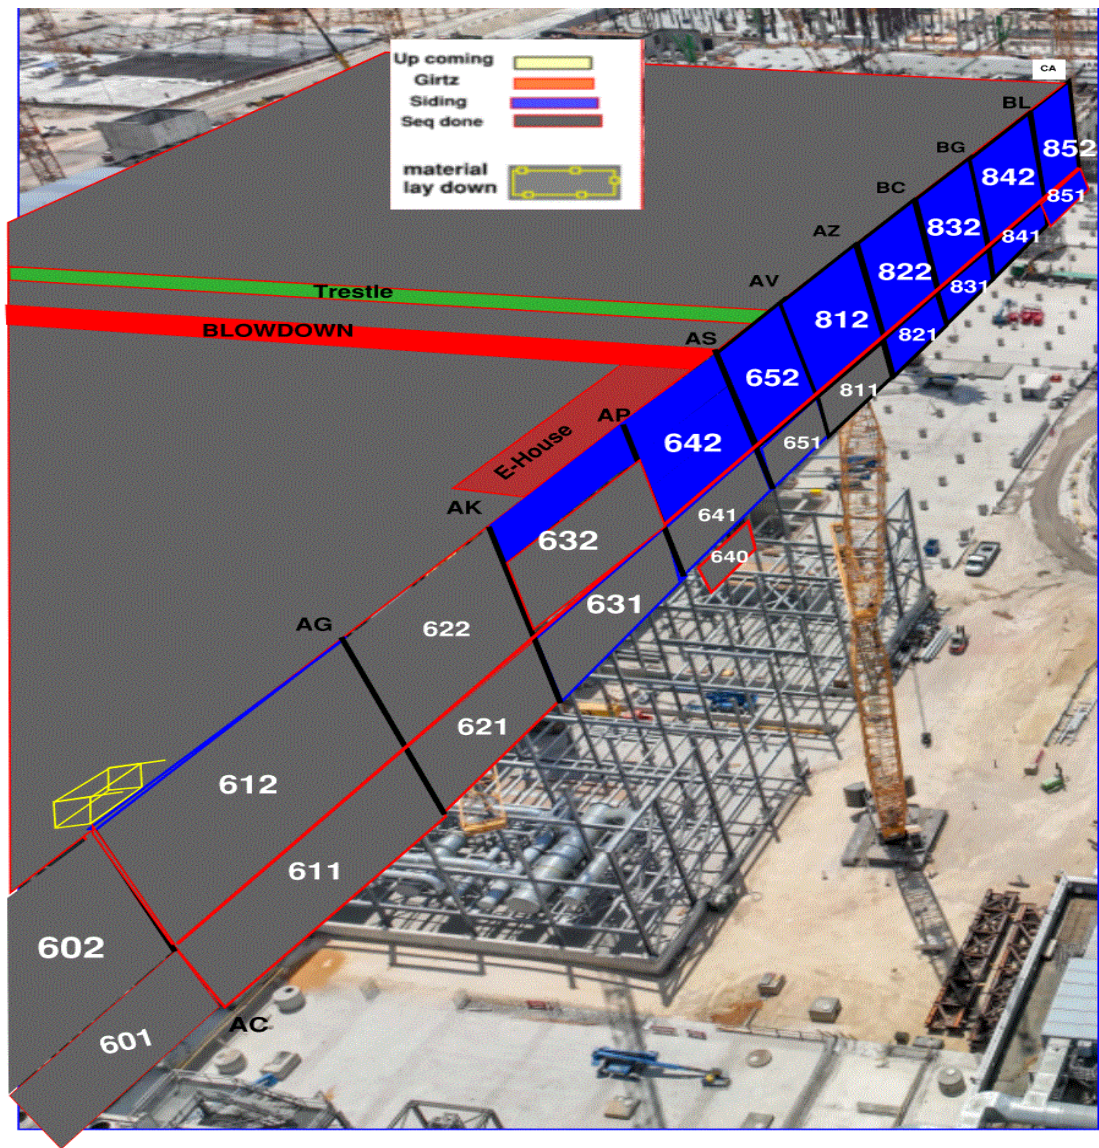

Siding - East FAB - PSSS

[illegible]

Siding - West FAB - JYG


Link

1
2
3
4
5

PSSS.1

Utility Level 1YA


PSSS Roof 2SA

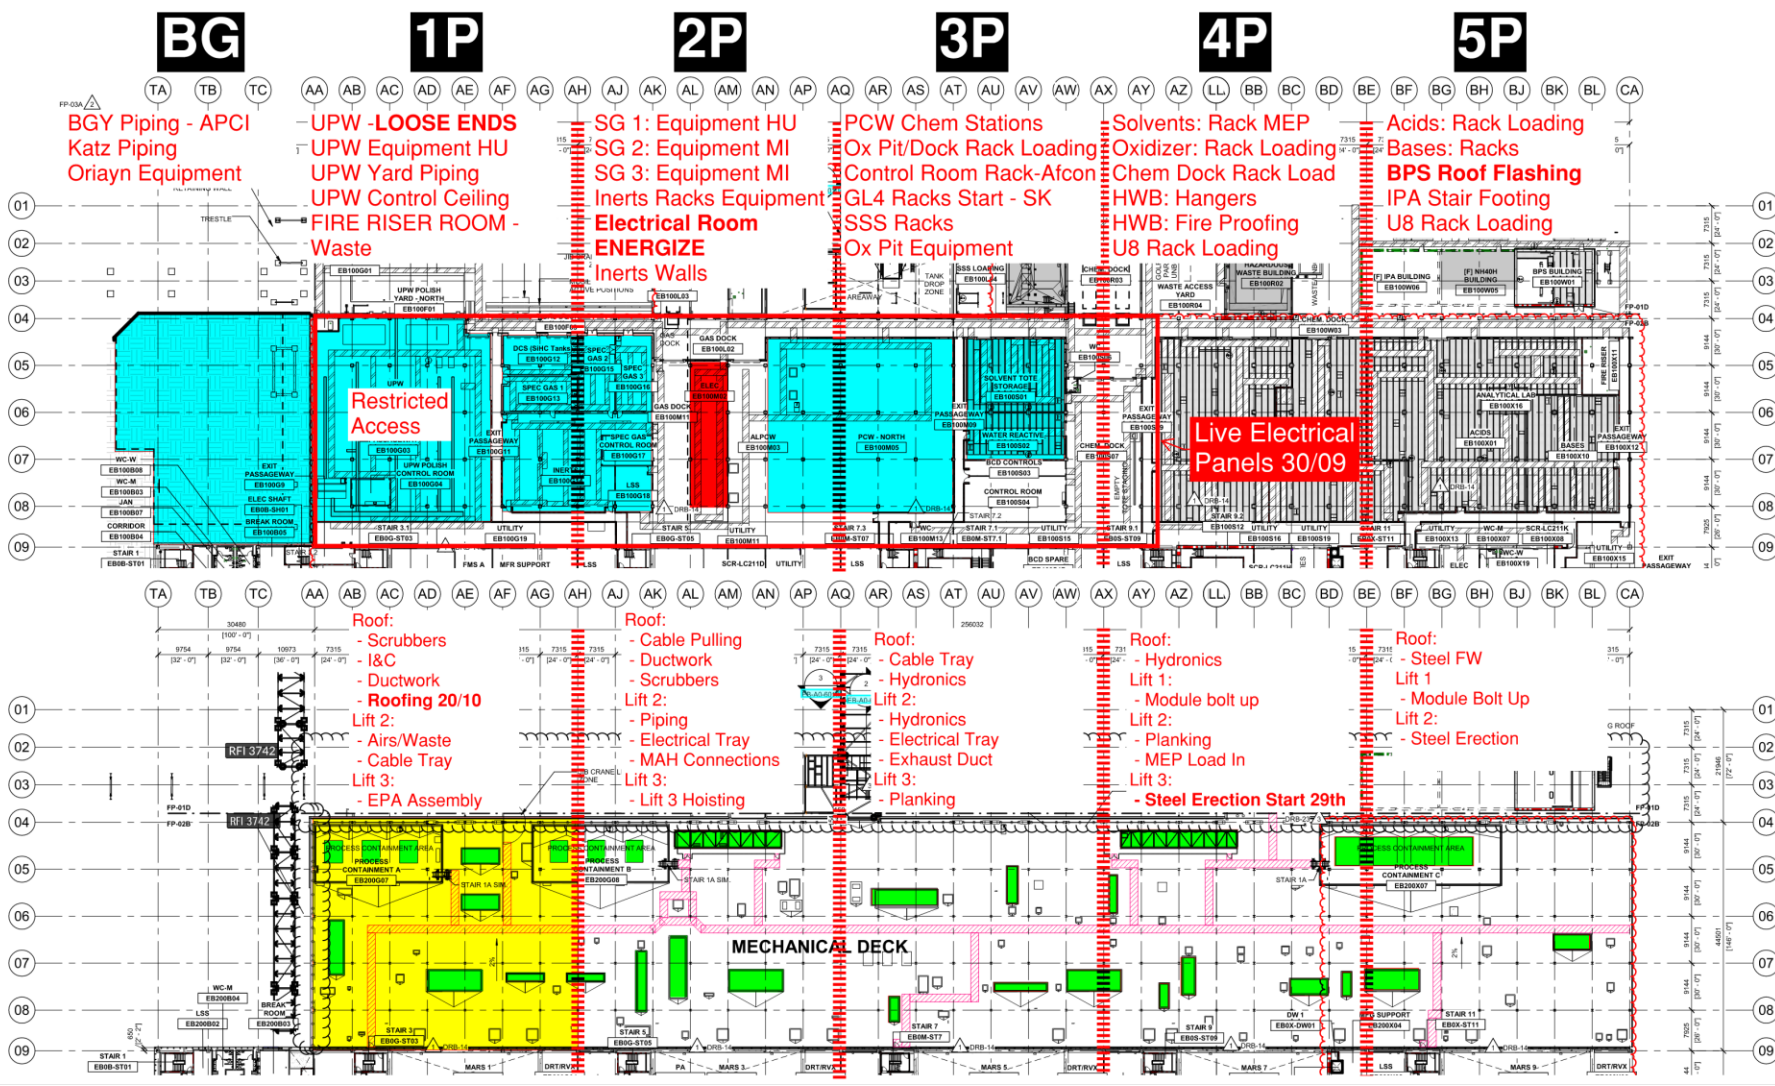

PSSS.2

Utility Level
1YA

PSSS Roof
2SA

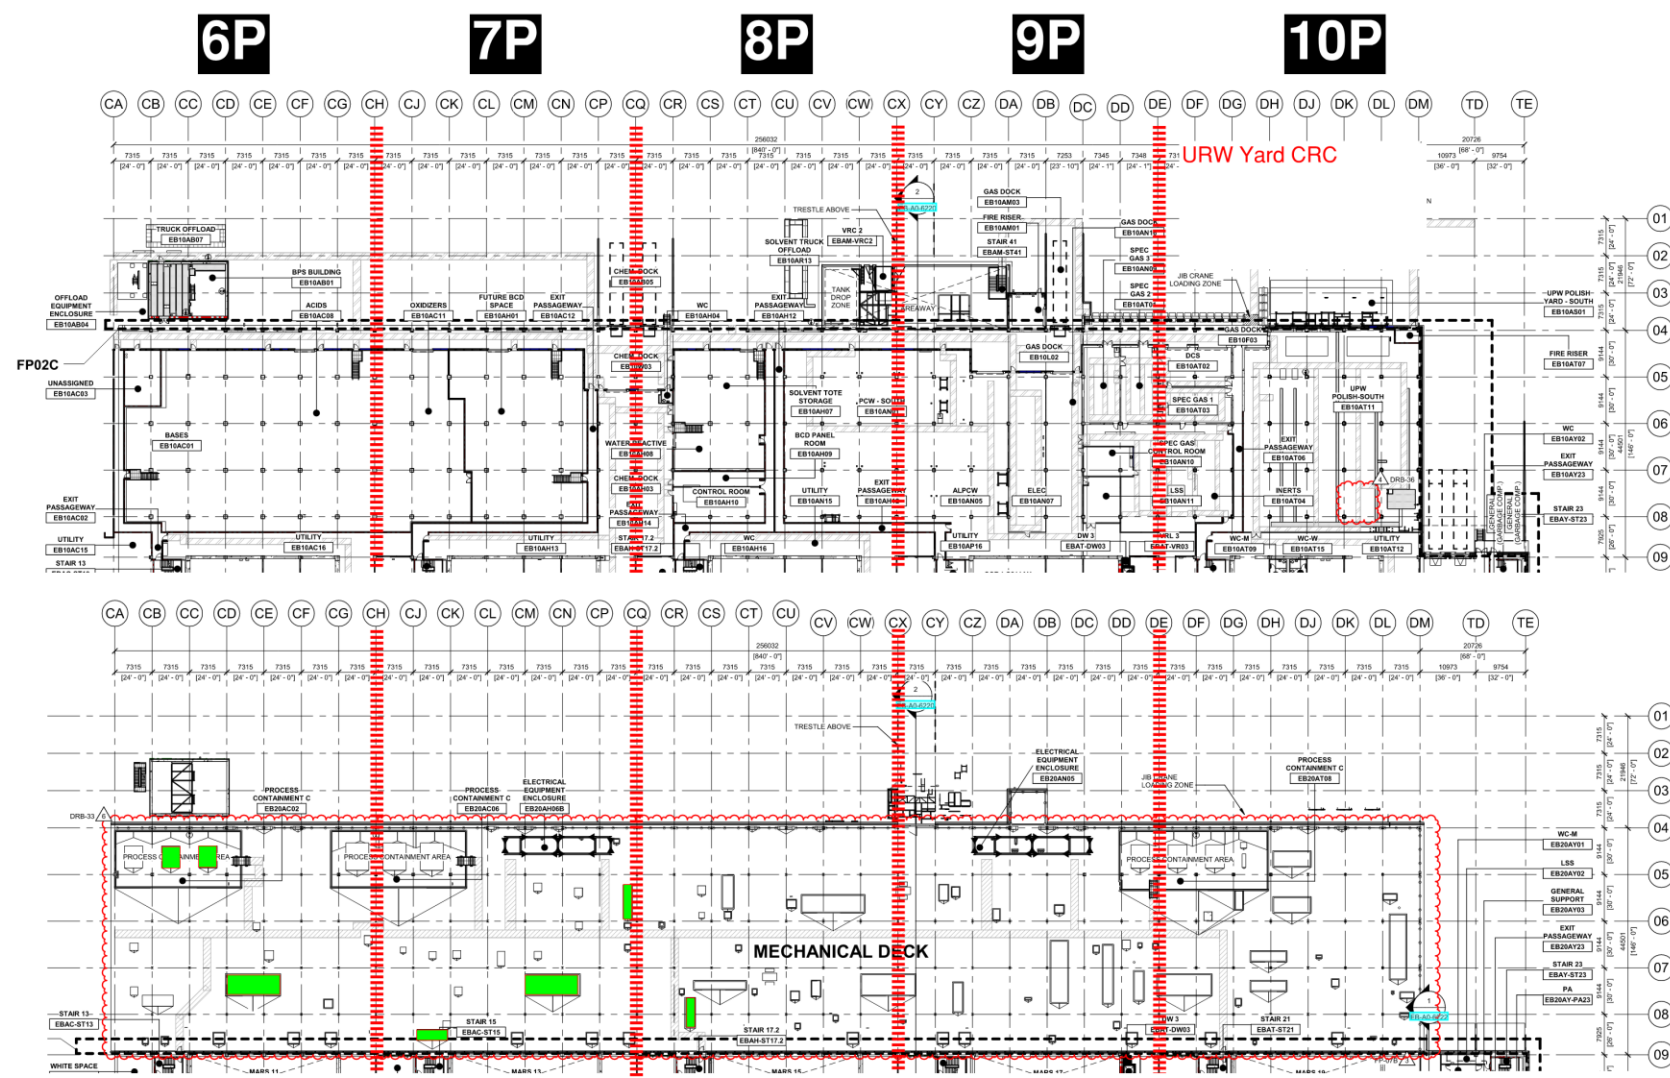











HOFFMAN CONSTRUCTION COMPANY

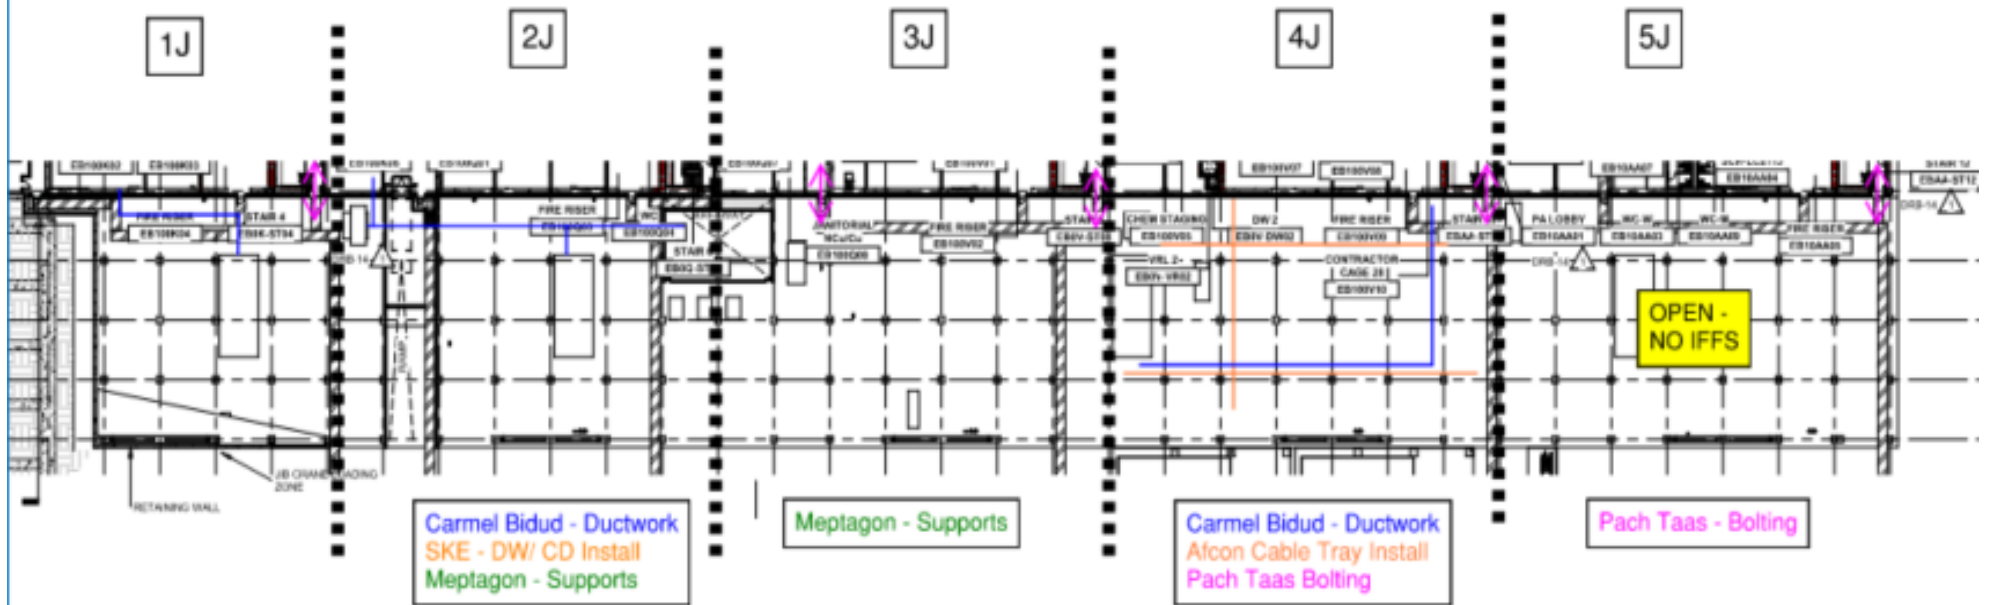


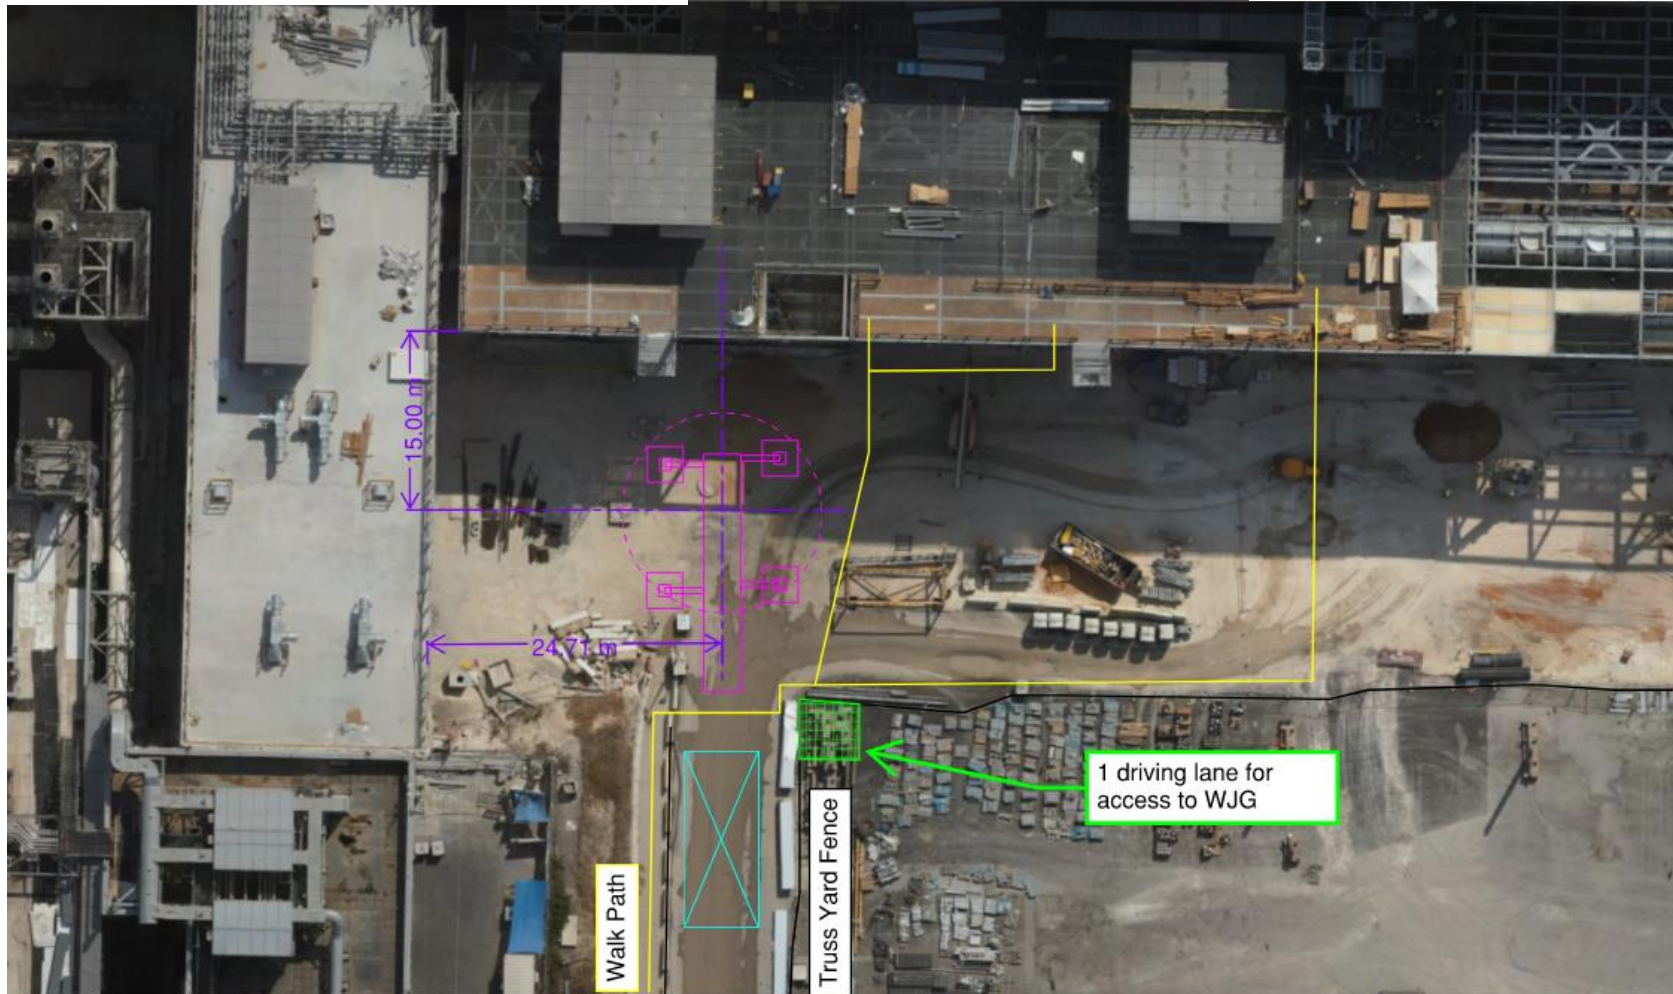


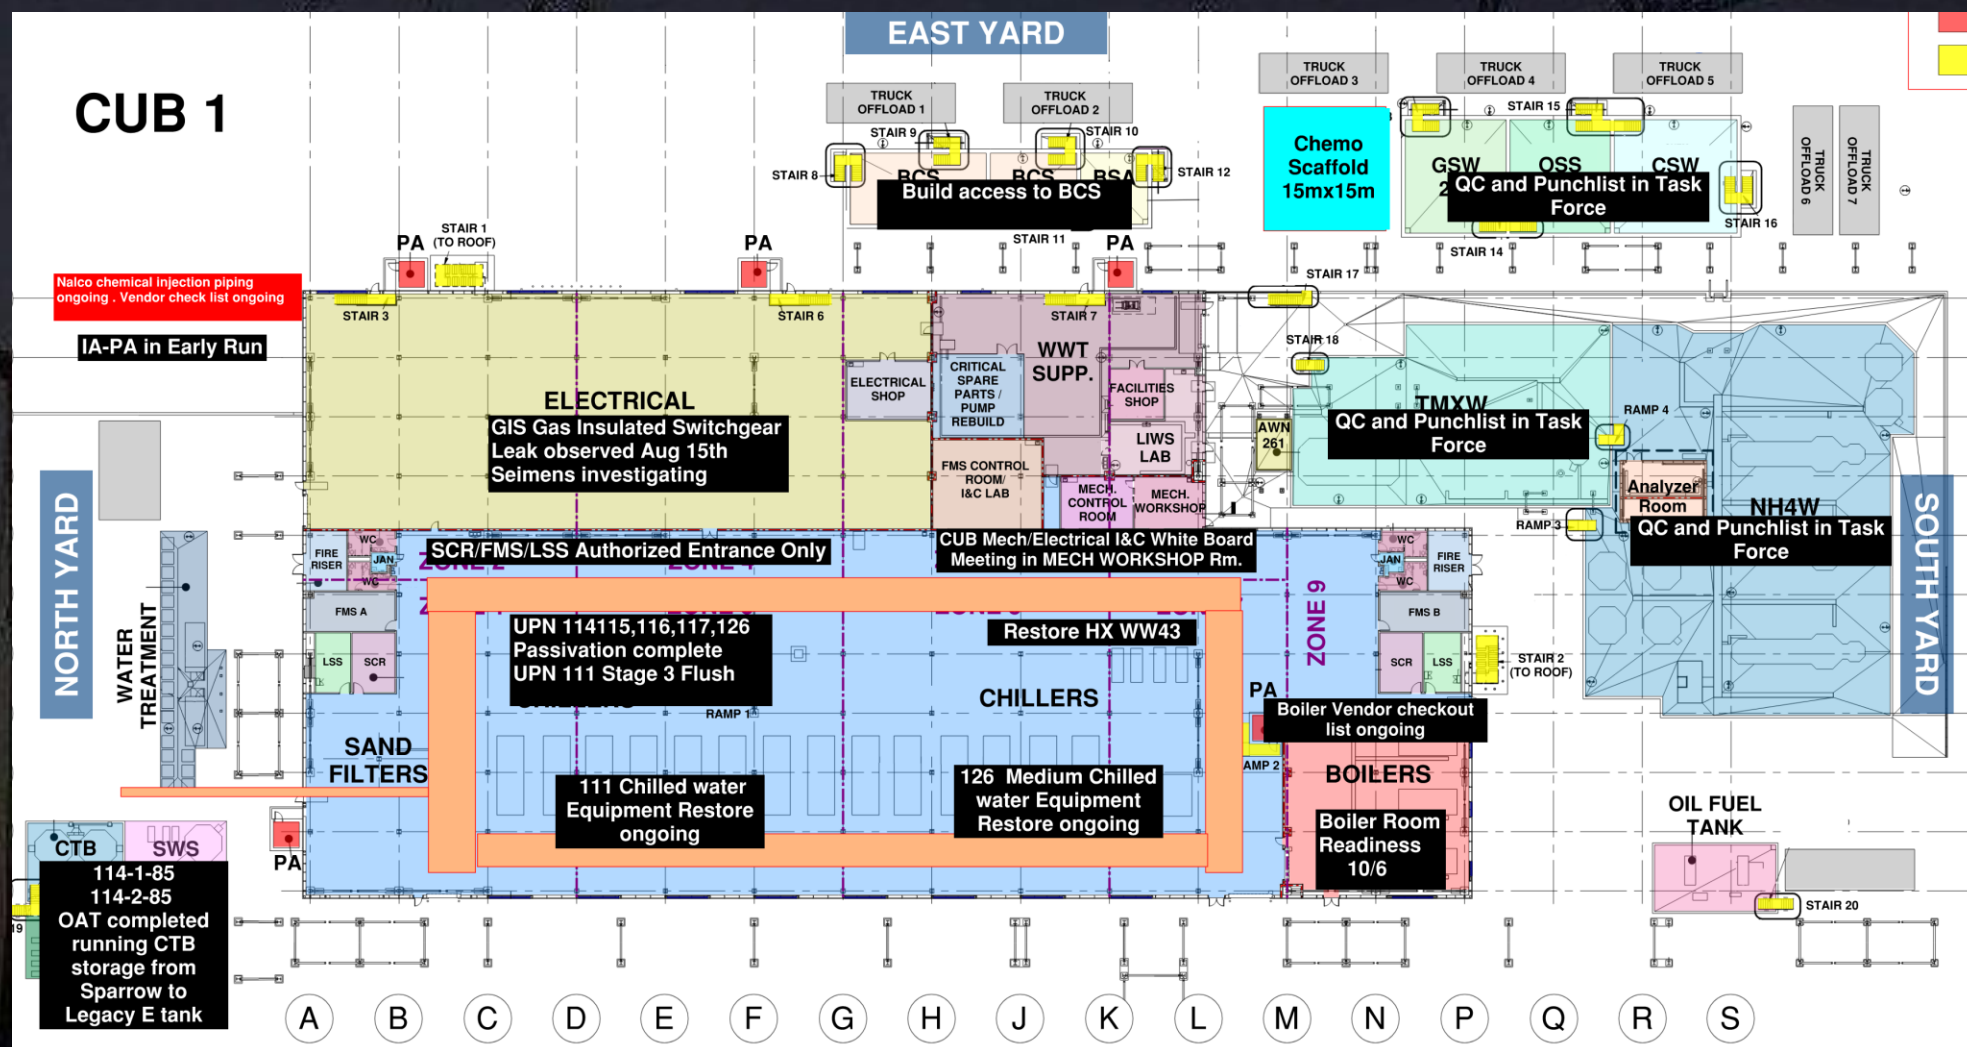


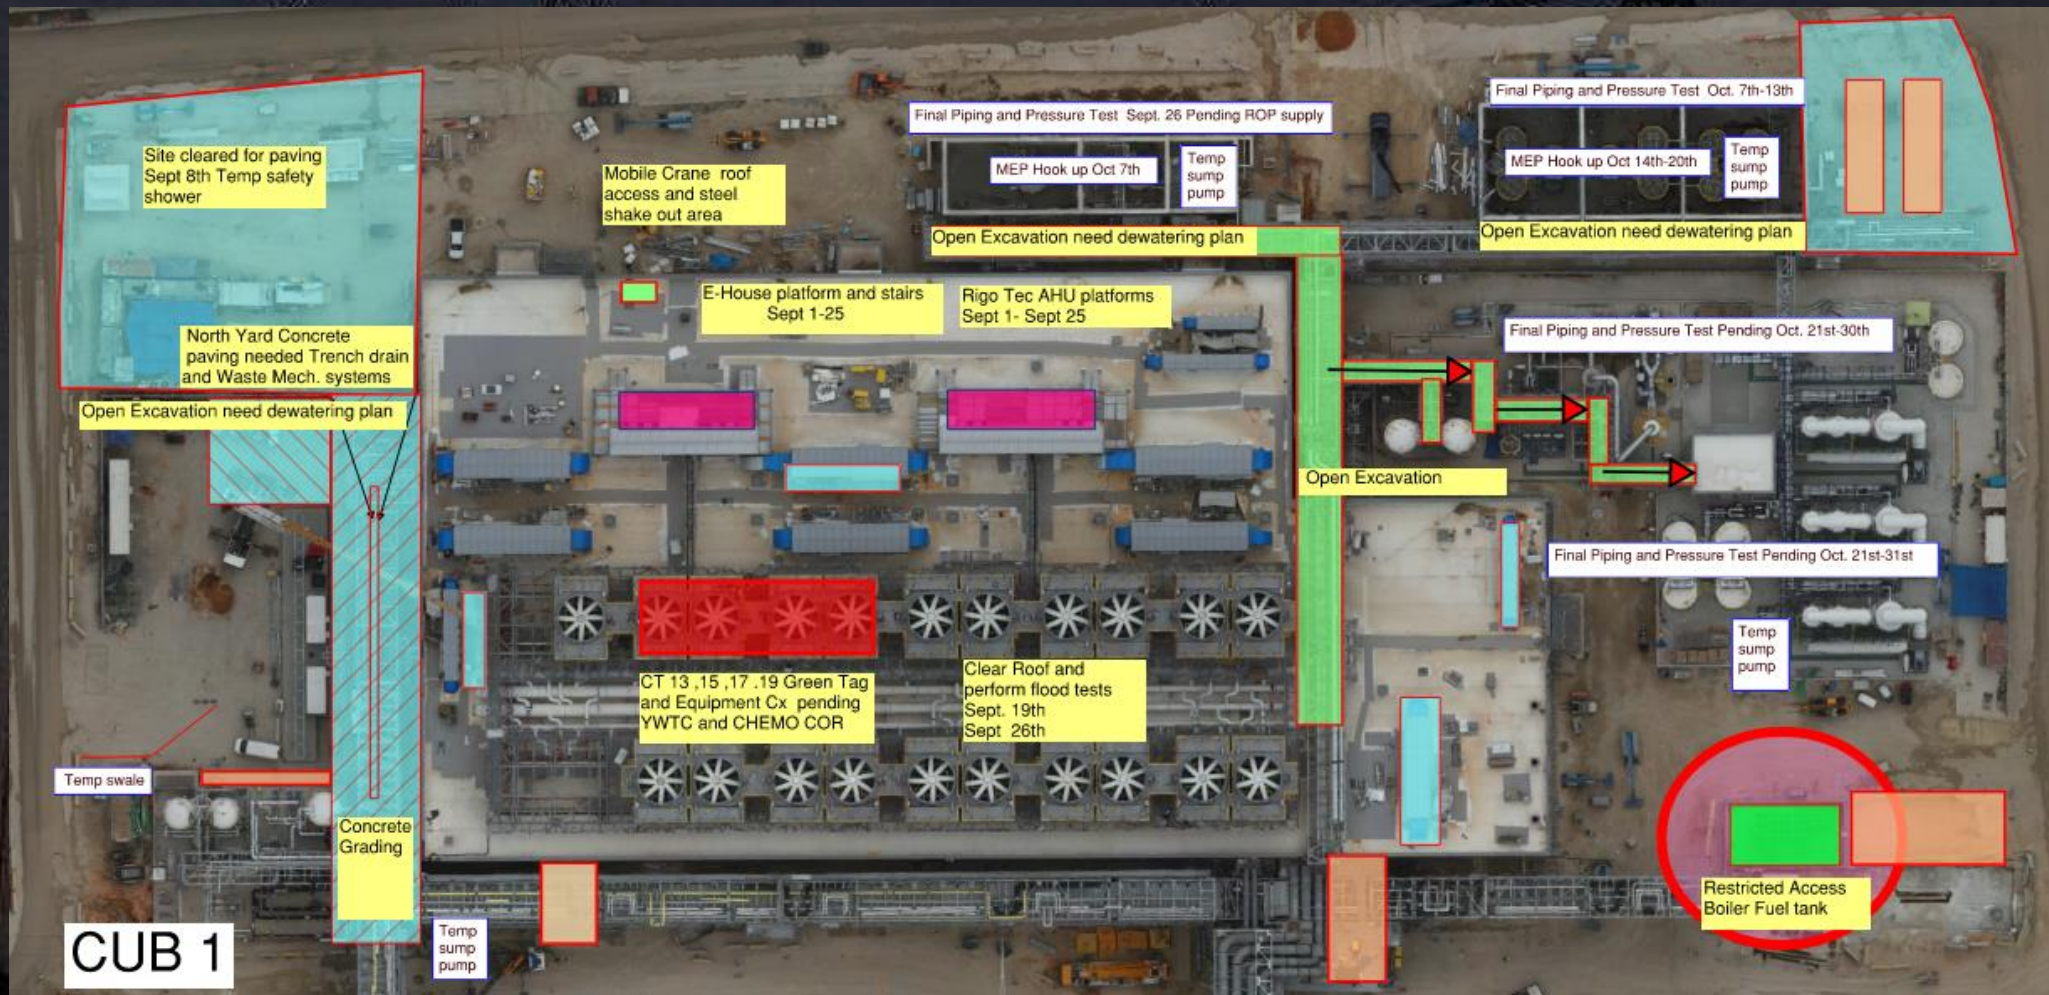

NORTH YARD

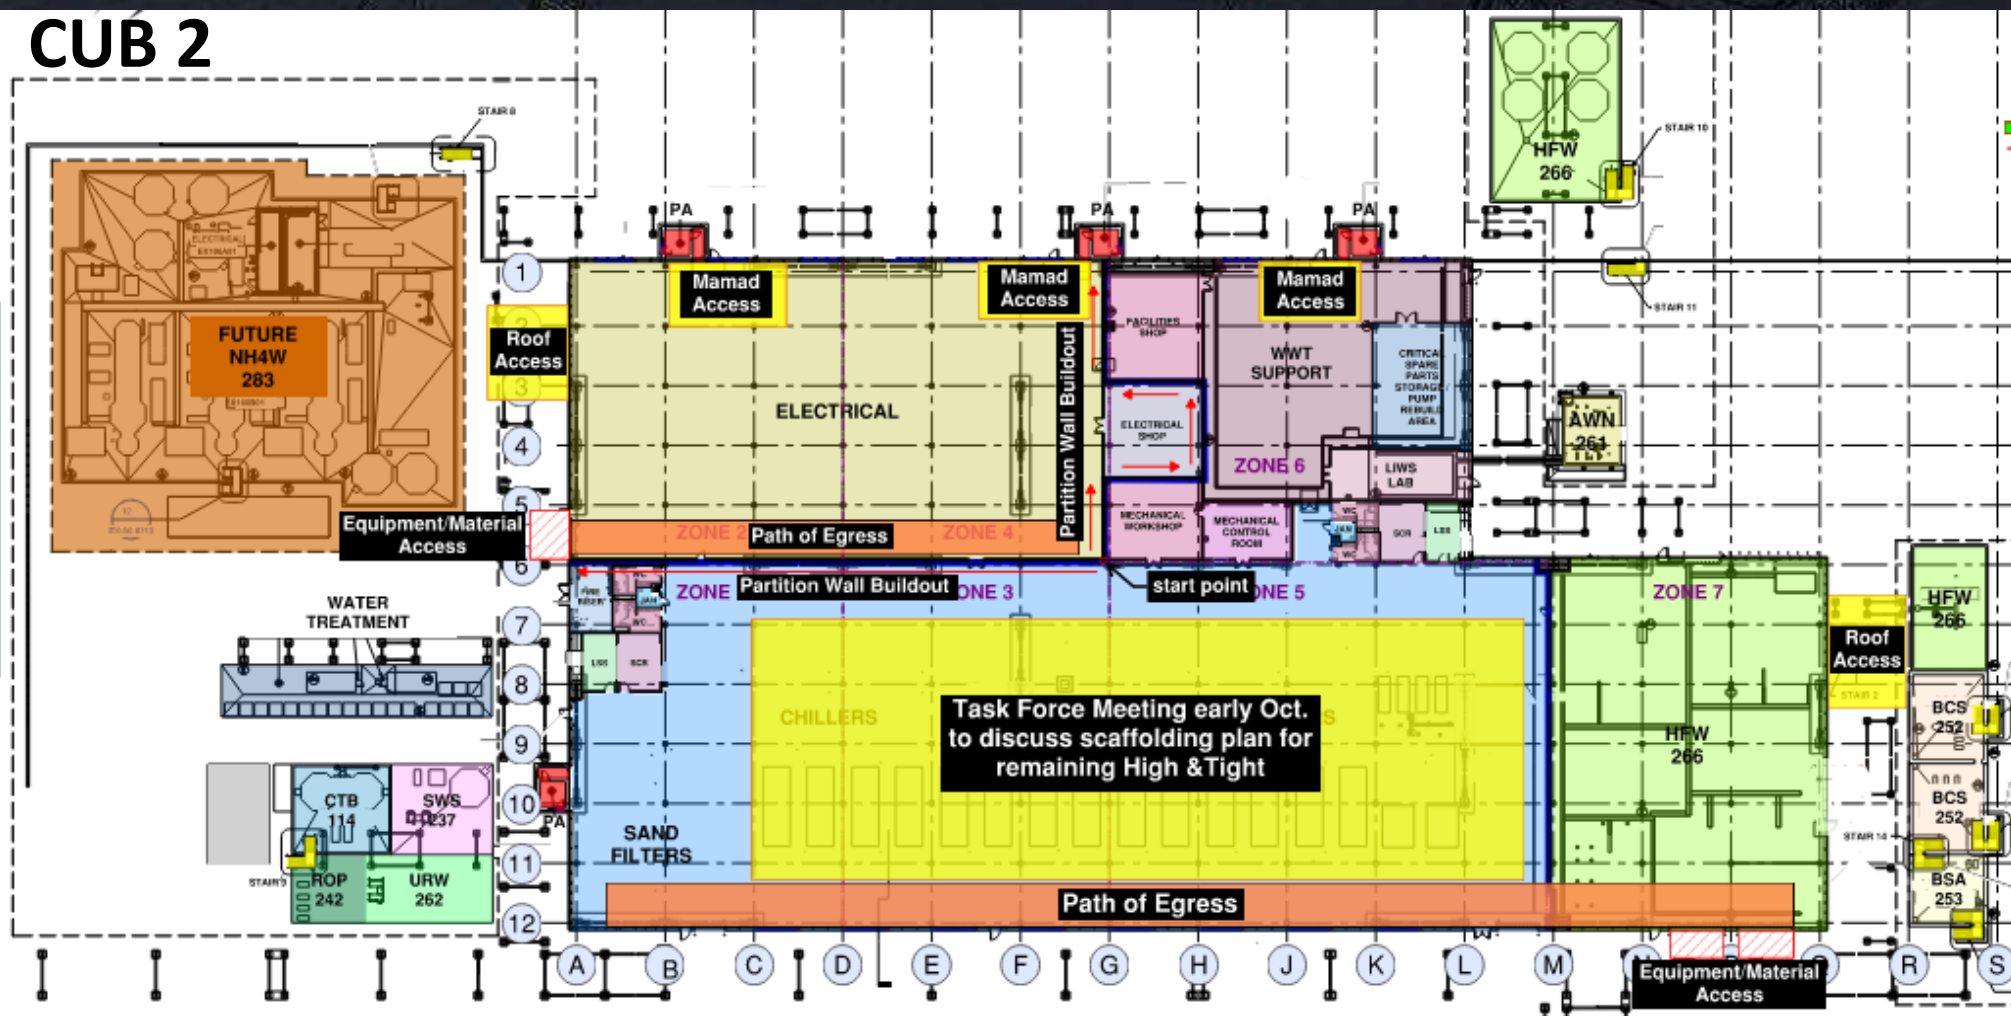

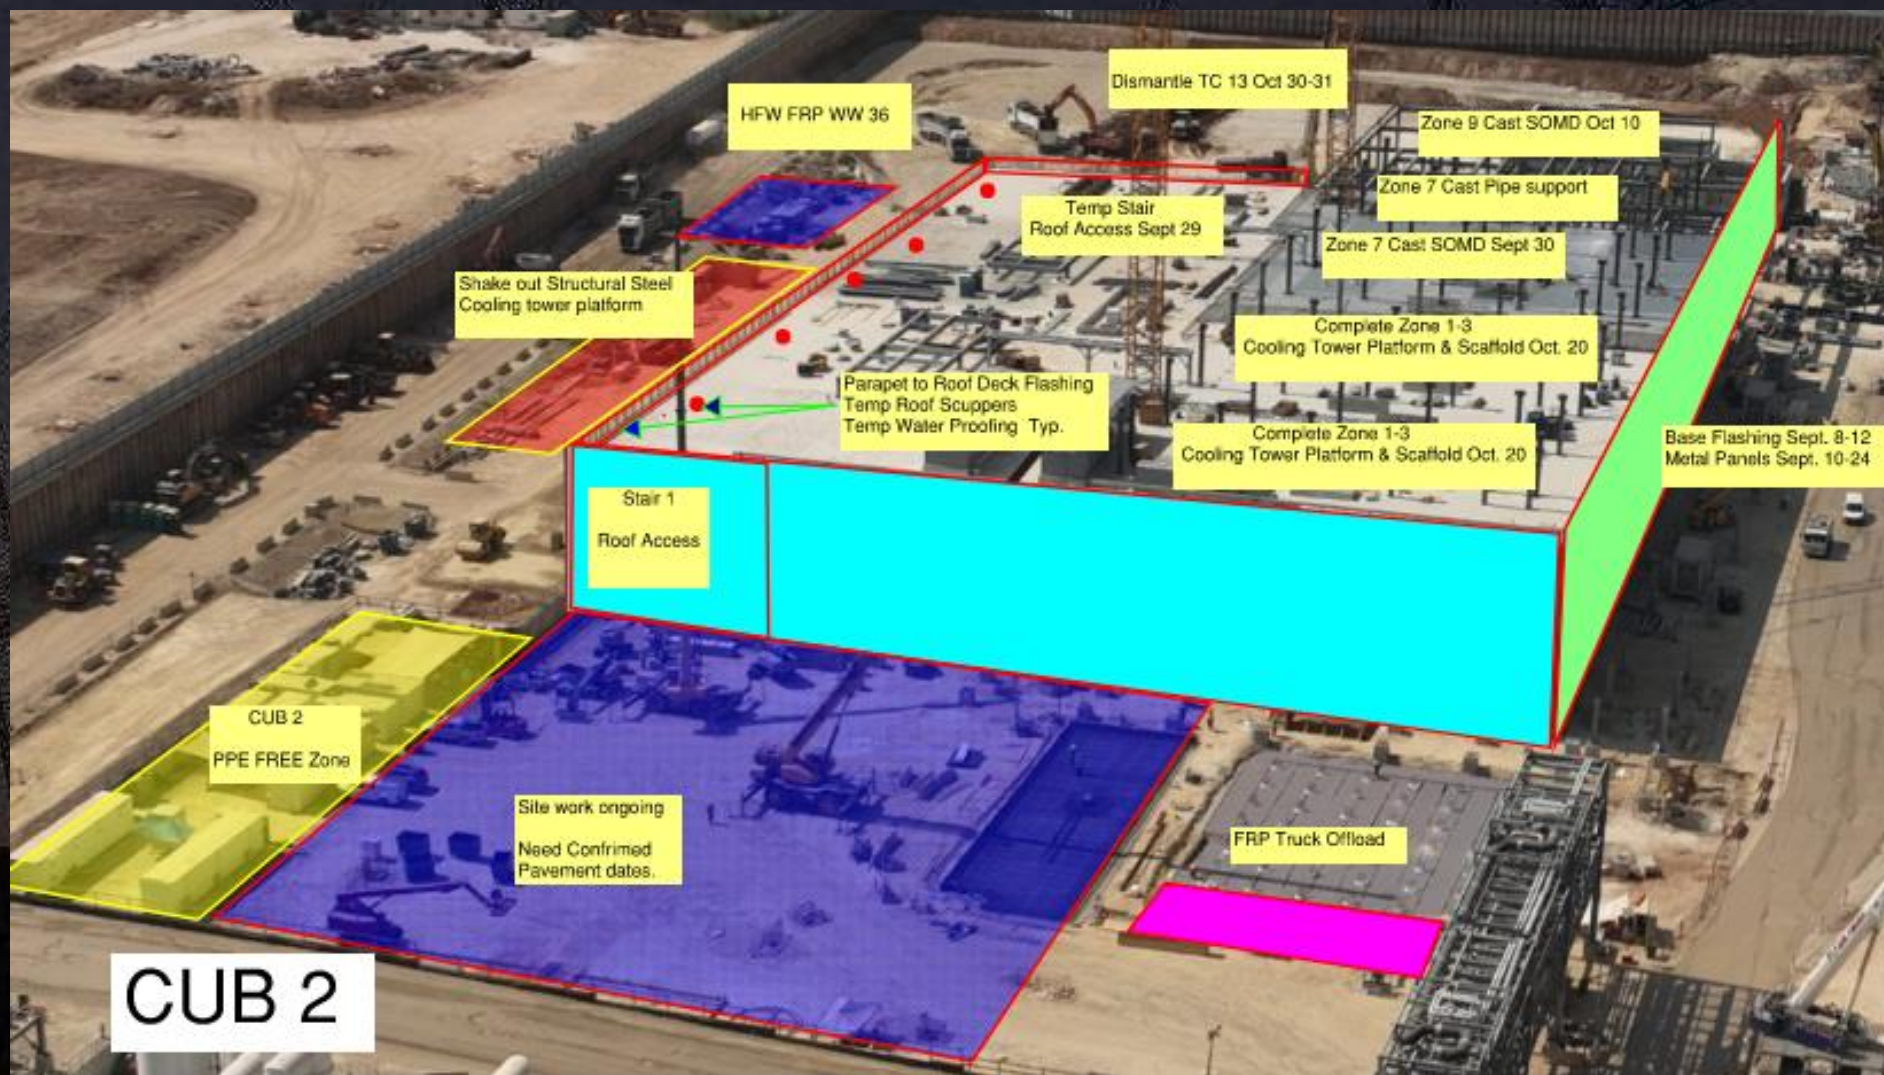

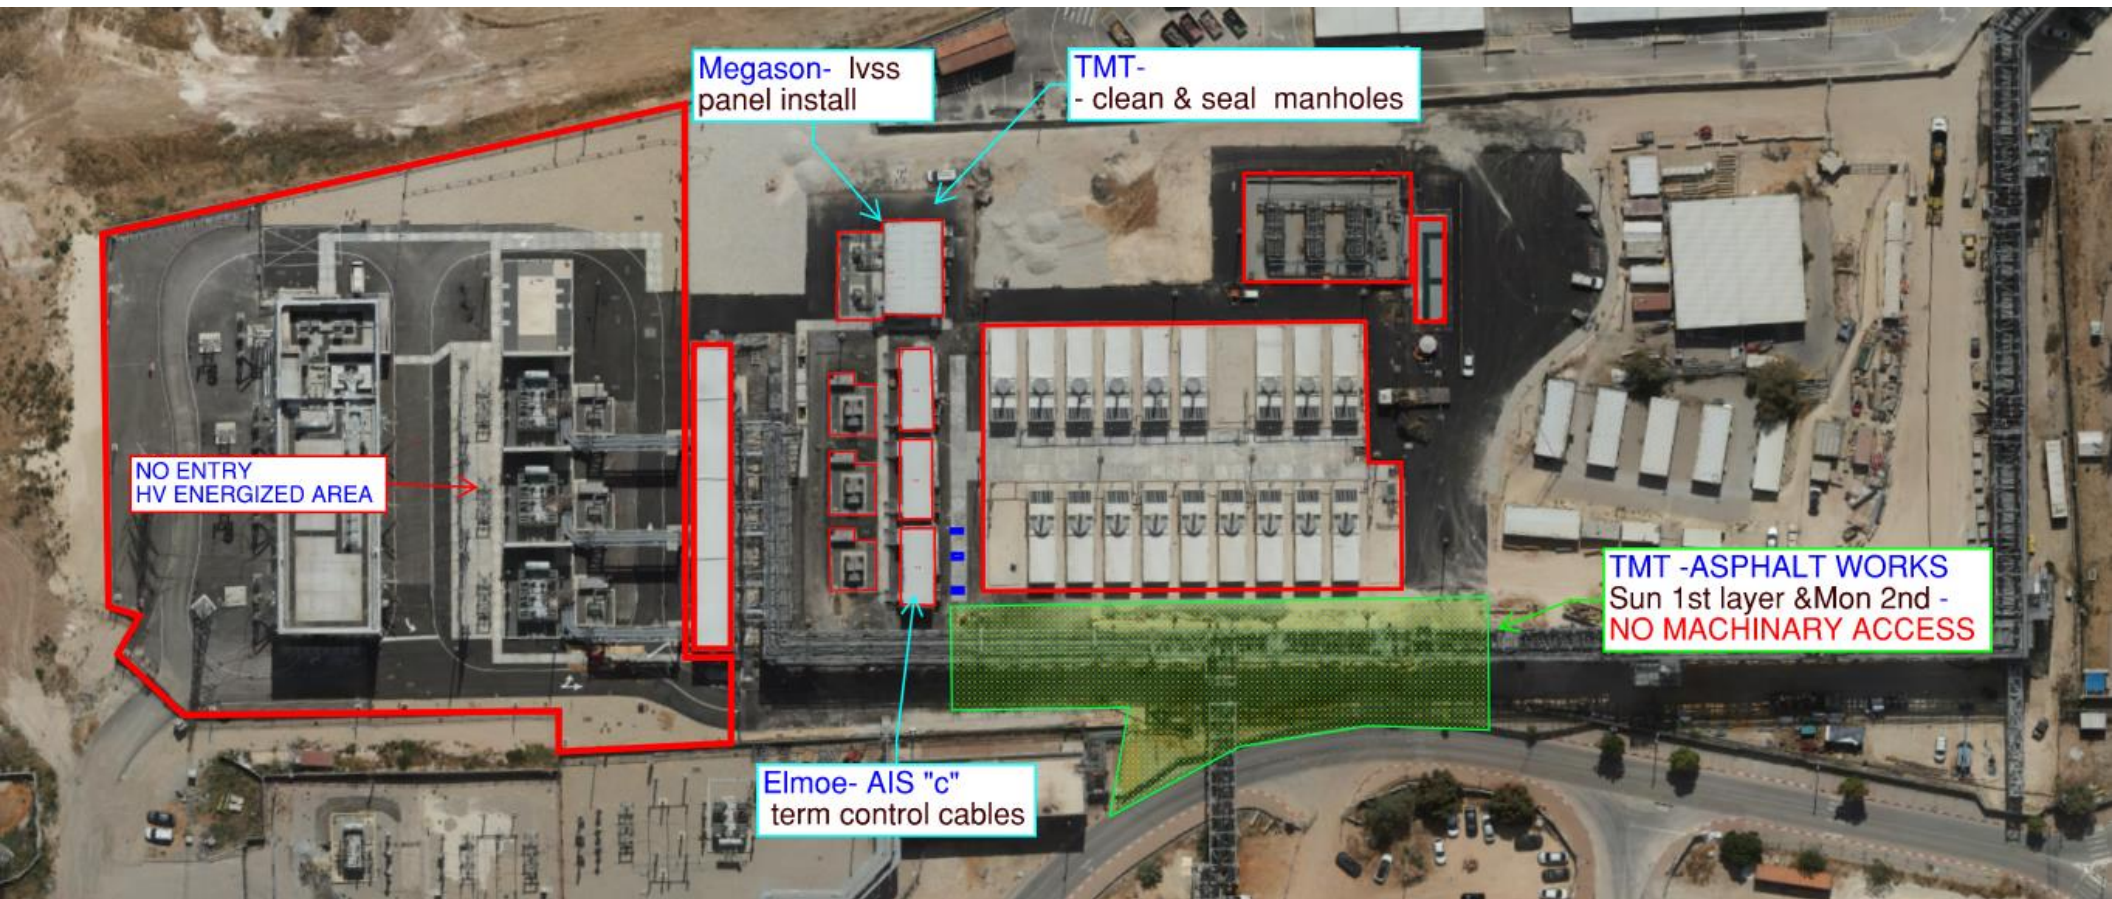

Megason- lvss
panel install

TMT-
- clean & seal manholes

NO ENTRY
HV ENERGIZED AREA

TMT -ASPHALT WORKS
Sun 1st layer & Mon 2nd -
NO MACHINERY ACCESS

Elmoe- AIS "c"
term control cables



HOFFMAN CONSTRUCTION COMPANY





HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

NO PARKING OR MATERIAL STORAGE

BSGS

T19 -ERECTION SEQUENCE

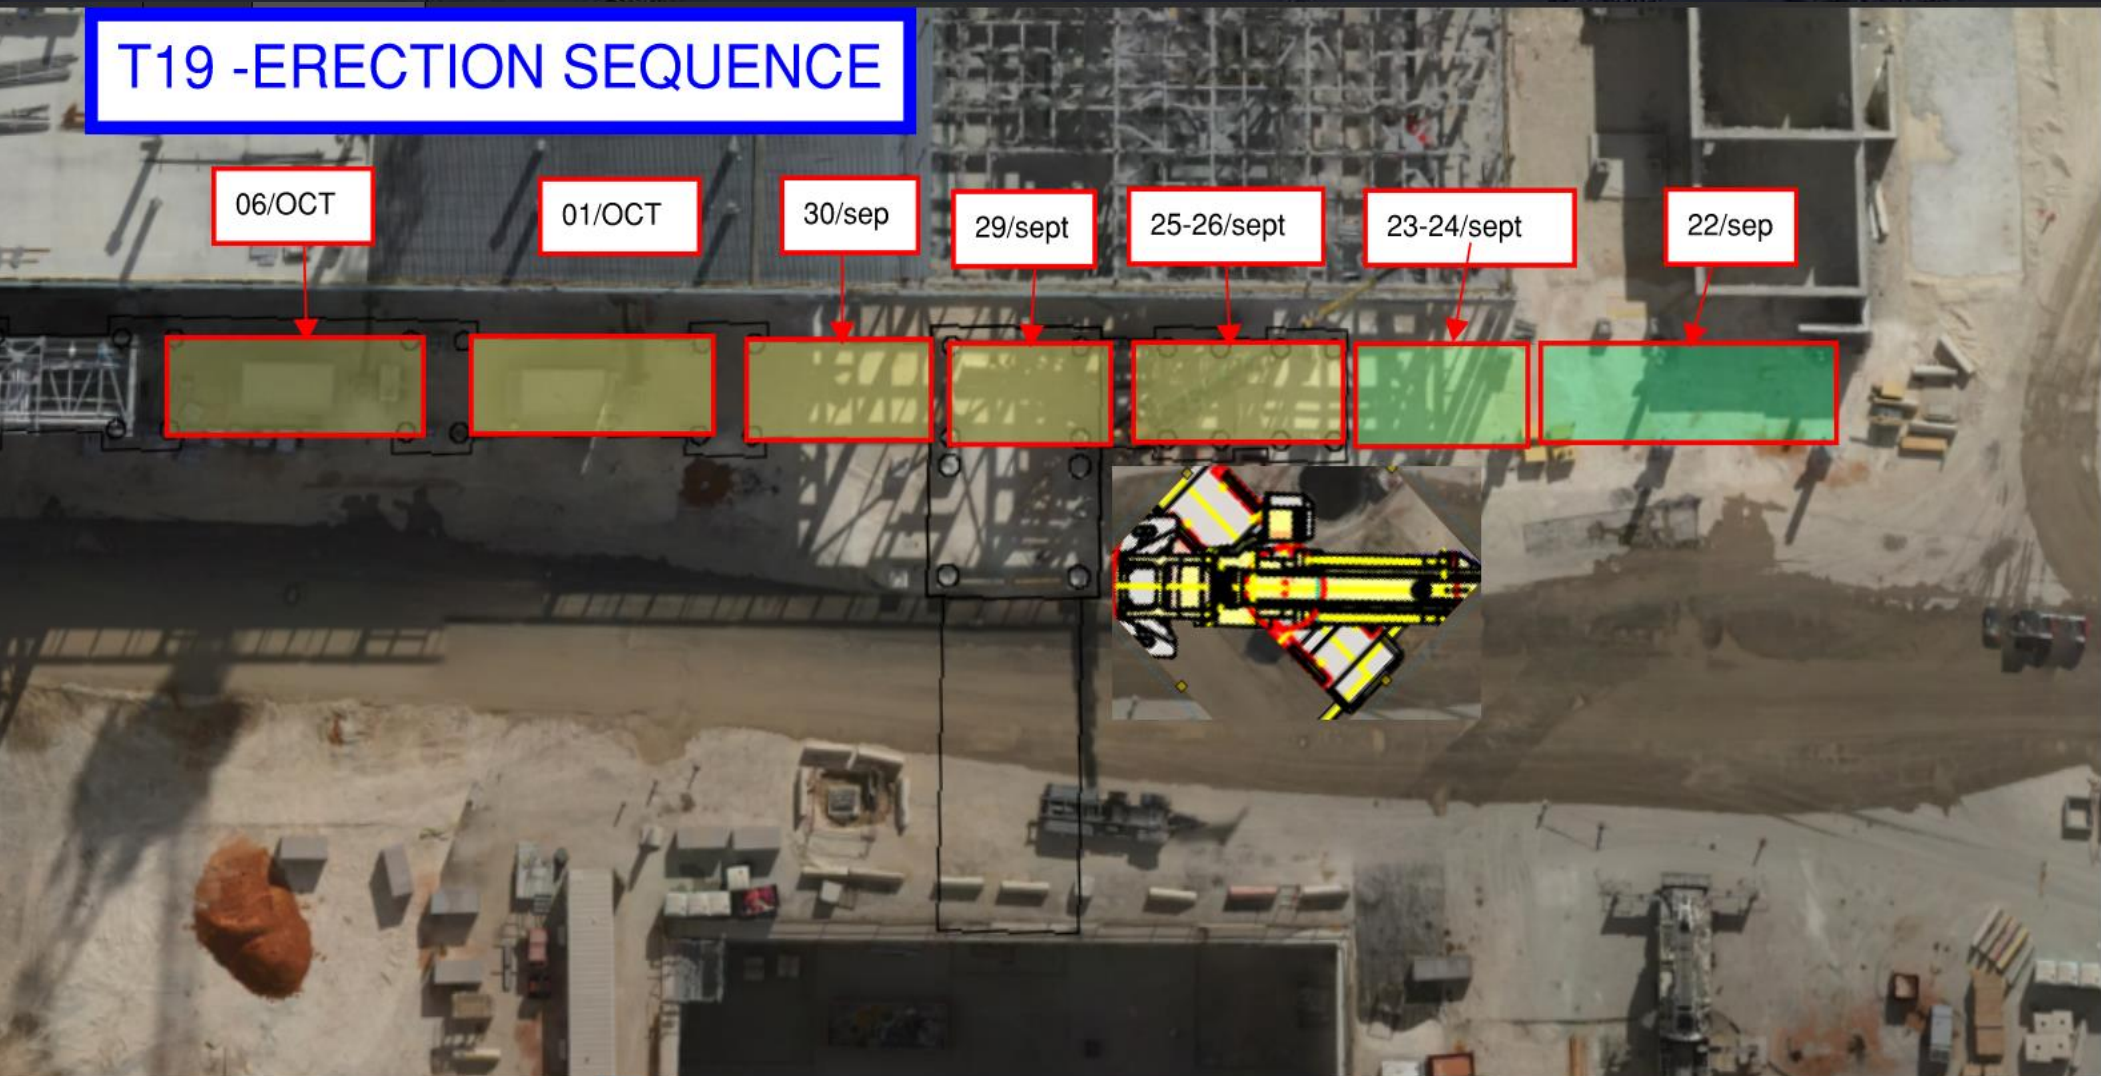

From main kiosk

Site temporary power

Legend :

— 22KV Line

— 400V Line

109 - Kiosk

● - Lift Station

Fab 38.2

Upcoming shutdown
Fab(all floors); JG; PSSS
29.Sep 00:00 to 05:00
W1;W2;W3
E1;E2;E3
Sunday morning

Cub 2

Cub 1

TC-10
Done

TC-8
Done

TC-6
Done

TC-4
Done

630A
SW
Done

630A
NW
Done

630A
SE
Done

630A
NE
Done

TC-9
On Gen
power
10.09

TC-7
On Gen power
Done

TC-5
Done

TC-3
Done

TC-13
Done

TC-12
Done

To 115

From main

117

105

106

107

108

109

111

112

113

114

115

116

Daily Coordination Meeting

Site Logistics

Underground Utilities

ALL UNDERGROUND UTILITIES ARE LIVE!


- Temp water
- Temp power (22kv)
- Storm
- Sewer
- Domestic Water
- Fire Protection Water (Intel fire pumps and alarms!)

Systems are connected to buildings and cannot be damaged or used without HCC approval.

Daily Coordination Meeting

Site Logistics

North

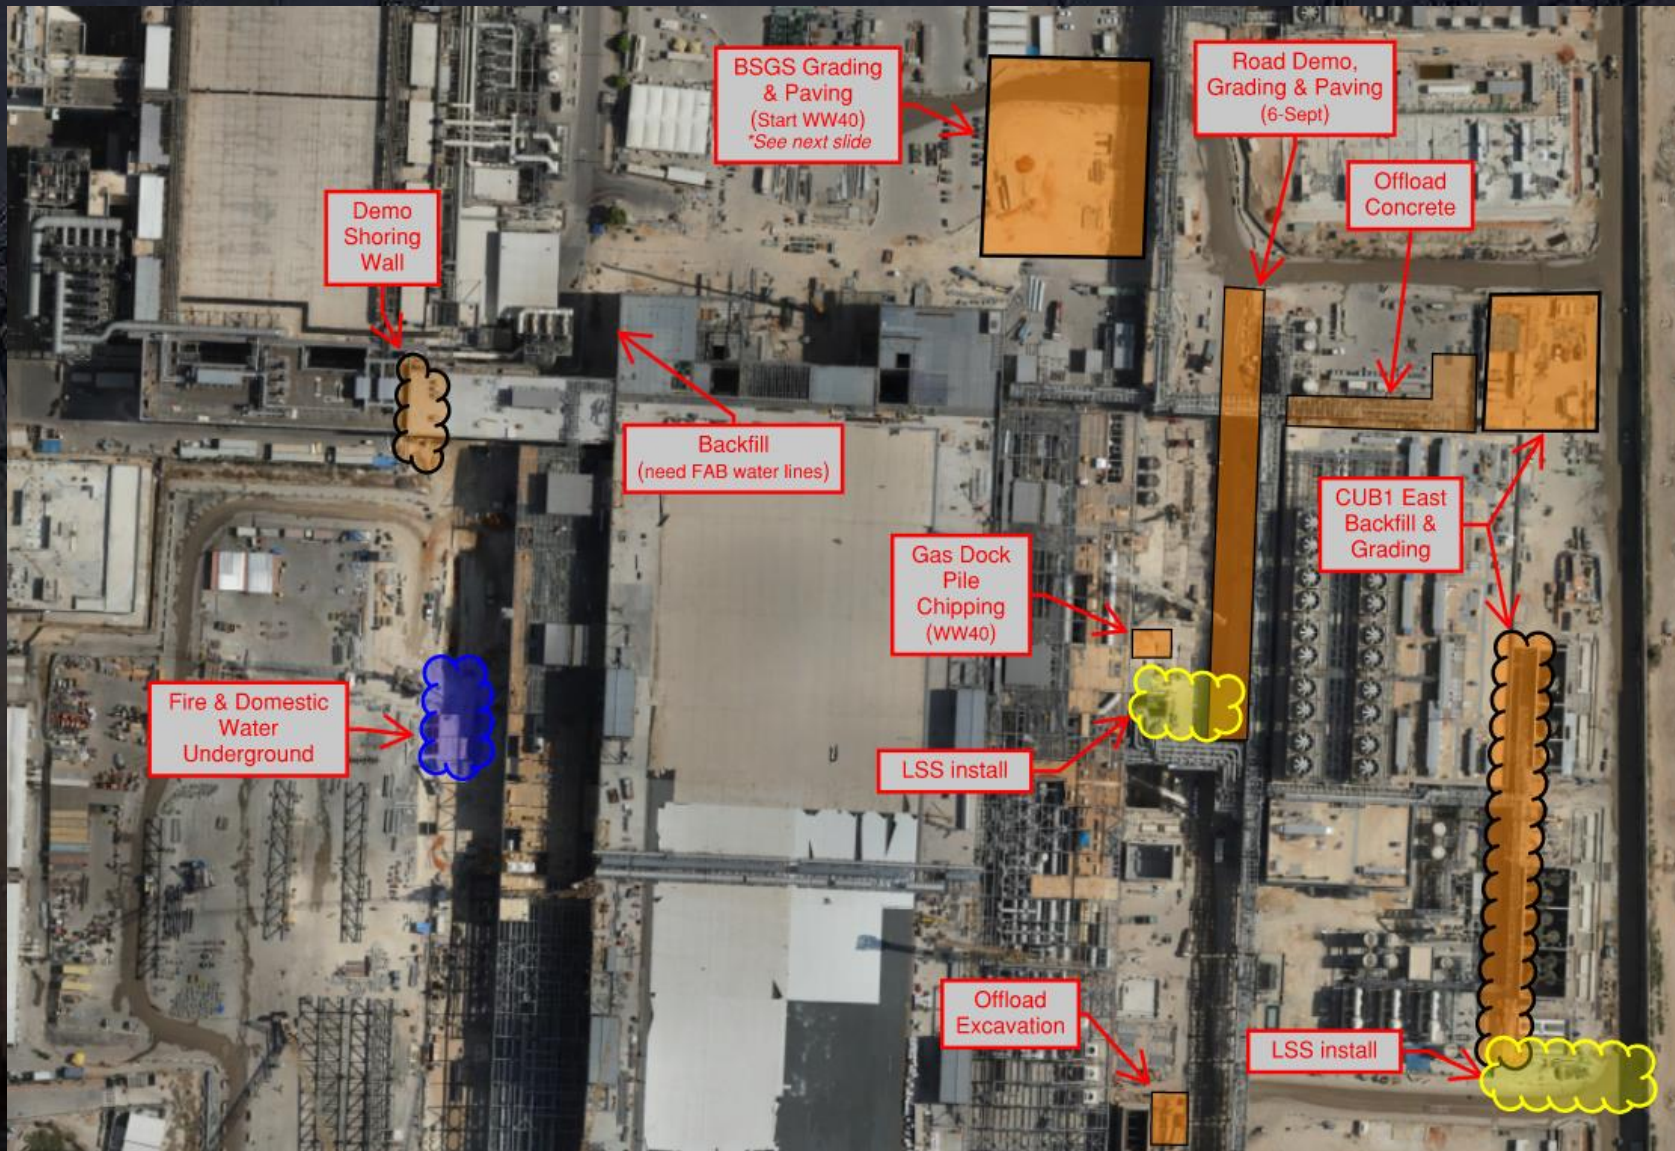




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics


North IQ Staging Access

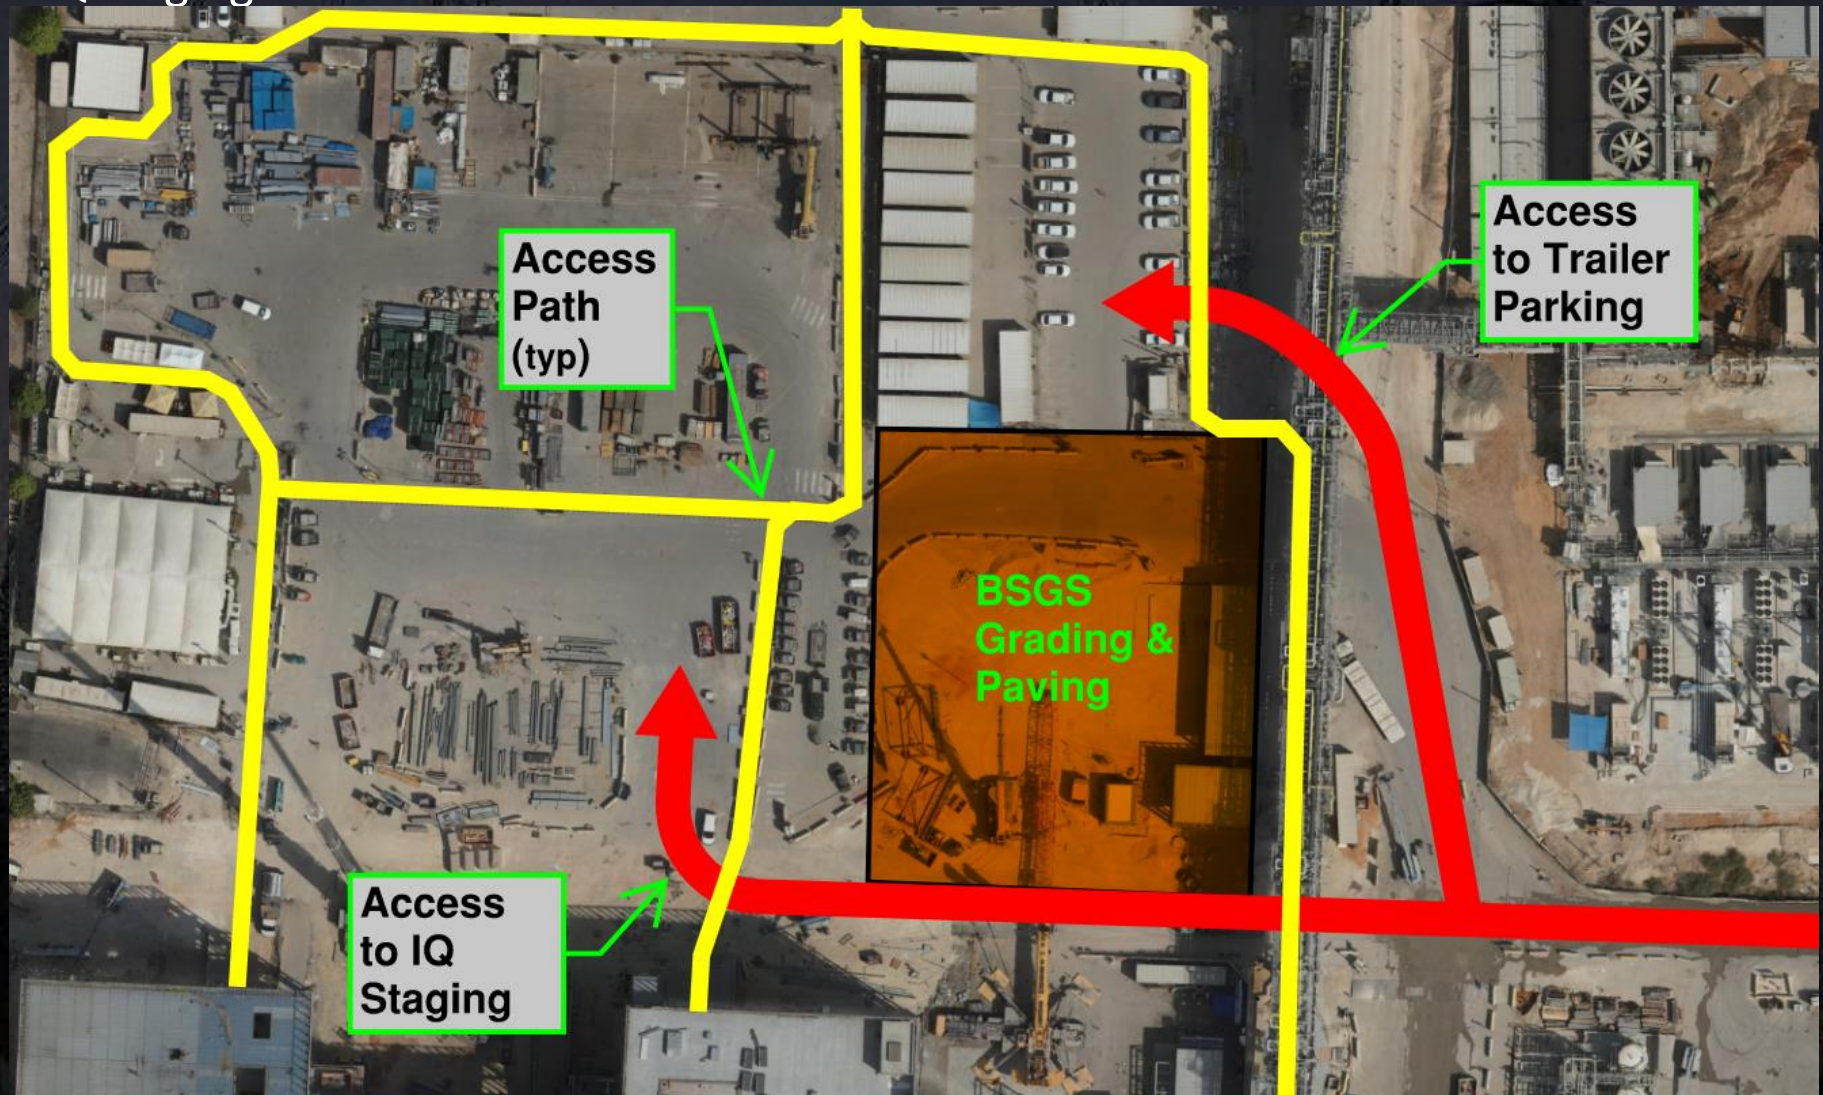

Daily Coordination Meeting

Site Logistics

South

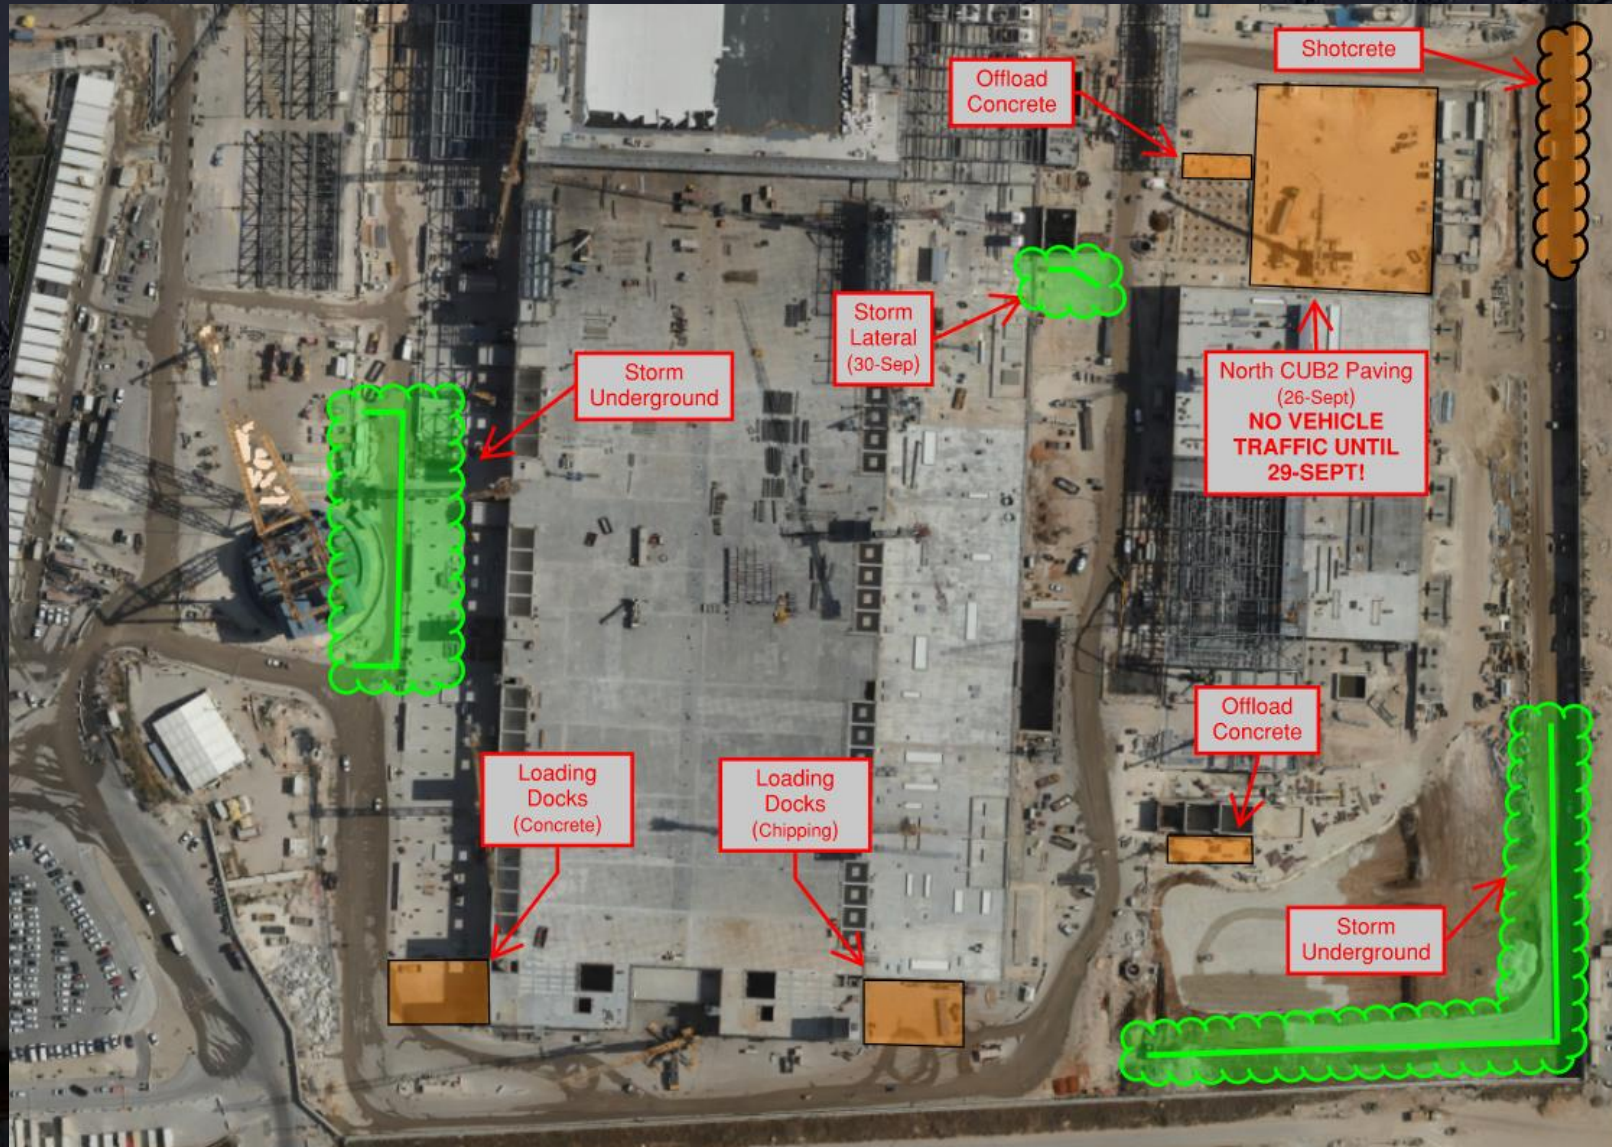

PPE Must Fit Employees

- Not all PPE works in a one size fits all situation.
- Please ensure that you are providing workers with PPE that actually fits them.
- Sometimes, helmets will need different suspension systems to fit someone's head.
- Gloves, are definitely not adjustable and should be the best size for the worker to not have too much extra fabric.
- Boots must fit your workers' feet.
- And one of the most important pieces of PPE that must fit your workers are fall protection harnesses. These can be adjusted, but only so much. You must have harnesses that fit all of your workers.

HCC/EHS Weekend Work- 27.09.2024

White Board Meeting in Beavers at 06:30

Superintendents

Brian Grevious 052-5394339

Igor Shuster 054-4743767

Josh Noll 052-5590653

Husein Abu Hammad 052-4106872

CSA CM

Tarek Nairoukh 052-6636782

MEP

David Jollands 052-3961675

Andy Jollands 052-9659290

Paruic O'Reilly 052-3571665

OSM

CX/QA

Brandon Britton 052-6042828

Darryl Hicks 052-3215975

Cranes

Brady Prouty 052-6047531

Safety

- Safety Foreman- Adir Elmakayes- 054-7254767 Adir-Elmakayes@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Officer - Arkady Gerber-050-6851432 Arkady-Garber@Hoffmancorp.com

Subcontractor Weekend Work- 27.09.2024

FAB

UTILITY LEVEL

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

Elram

Foreman: Shlomo

0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

Pach Taas

Perim Rack Aae

Team Lead : Nuriel 0549012324

Afcon E

PA/Stairs

Team Lead : Avi Eli 0526008487

Chemo

TTNW

Team lead: Tommy 0523759408

Safety: Lilah 0547886704

Belfor

TTNE / TTNC

Team Lead: Salame 0546651886

HYG

SF Zones 3- White steel touchups/Mamad plates weld/

Stair # 8

Salah 0507773119

WW Steel

Elevator 3

Teddy 0522392473

Clean Room

W&W 17-18 Line added the beams 10-24 line – catwalks, MOD2: steel fan deck east west, infill ongoing (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

Talad – CR 1W – Drilling holes, 1 metal lids removal (EHS Guy 0544915407, Super Igor 0544509386)

Sig – 5W INT Platforms MIMO CB-CC/25 (EHS Beni 0506232032, Super Nodar 0546313261)

Elram – CR Level 9,25 line, AA line 2W shafts walls INT level 9,10,17,24 column wrap (EHS Royi 0538312234, Super Bonio 0544236899)

Afcon – CR – 2E-5E, 2W-5W, INT- 2E-3E, 3E-3W ,LINK Rack install (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Sela – 1E-AB-AK/10-12 CRC (EHS Shmuel – 0506306031, Supervisor Yuval 0502649246)

Subcontractor Weekend Work- 27.09.2024

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2, and EPA Platform 1&2P

Foreman – Vadim – 052-6229005

Safety – Offek – 050-7838486

Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-4P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

W&W – SEQ 135, 137

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Elram – 5P Corridor, UPW Ceiling

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Lesico – 5P UN2 Welding

Foreman – Selvin – 052-4787370

Safety – Itay – 054-2336103

Combe UPW – UPW Room Piping and Yard

Foreman – Boris – 054-8346412

Safety – Abed – 052-5148747

SNJ Flashing – BPS Roof

HSAI – BPS Blast Walls

Foreman – Dave – 052-4121028

Safety – Sam – 052-5259268

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

WJG

Pach Taas

Adiv Pereg- EHS

Netanel Ivgi – Forman

Siding

SAMI NAJAMI -ROOF METAL

SAMI NAJAMI -PANTRETION

SAMI NAJAMI -GERTZ

Victor 0549220163

Subcontractor Weekend Work- 27.09.2024

CUB

Sami Najami CUB 2:

Husein - 0526917461

Alon - 0509895008

Meptagon I+C:

Raziel - 0584360845

Netanel - 0538398999

Pach Taas:

Adiv - 0506909390

Nati - 0543301880

ETC south yard:

Yosef - 0506708990

Leonid - 0545991846

S.K.E:

Reynato - 0548991623

HSAI

Chemo Aharon:

Dudu - 0509808846

Leonid – 0548883878

Date: 27 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.SARAWUT KHRUEASING, AC5094850, TEL 052-3628607 (Leader)

Date: 28 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.YOTSAWAT

Trestle

SNJ:

PIPES –UB CUB

ISOLATION –UB CUB

STEEL

FORMAN- BASHIR YONES - tel. 05273649963

SAFETY TRESTLE-Alon Matan tel. +972 50-989-5008

Site

Derech Afar – Shotcrete, Storm water bypass at Sarens & Fire protection water

Supervision = Raed: 054-2442030

EHS = Alex: 054-5403849

Olizki – Sweepers and water trucks

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

TM Team – LSS underground

Supervision = Nadav: 052-5893171

EHS = Alon: 054-7711469

GIS/NEY

Daily Coordination Meeting



14:00 Sign In
