

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting


General Topics:

- Weekend work



UTILITY LEVEL P.Test

LESICO
Press. Test
GN2
8/29
From 17:00

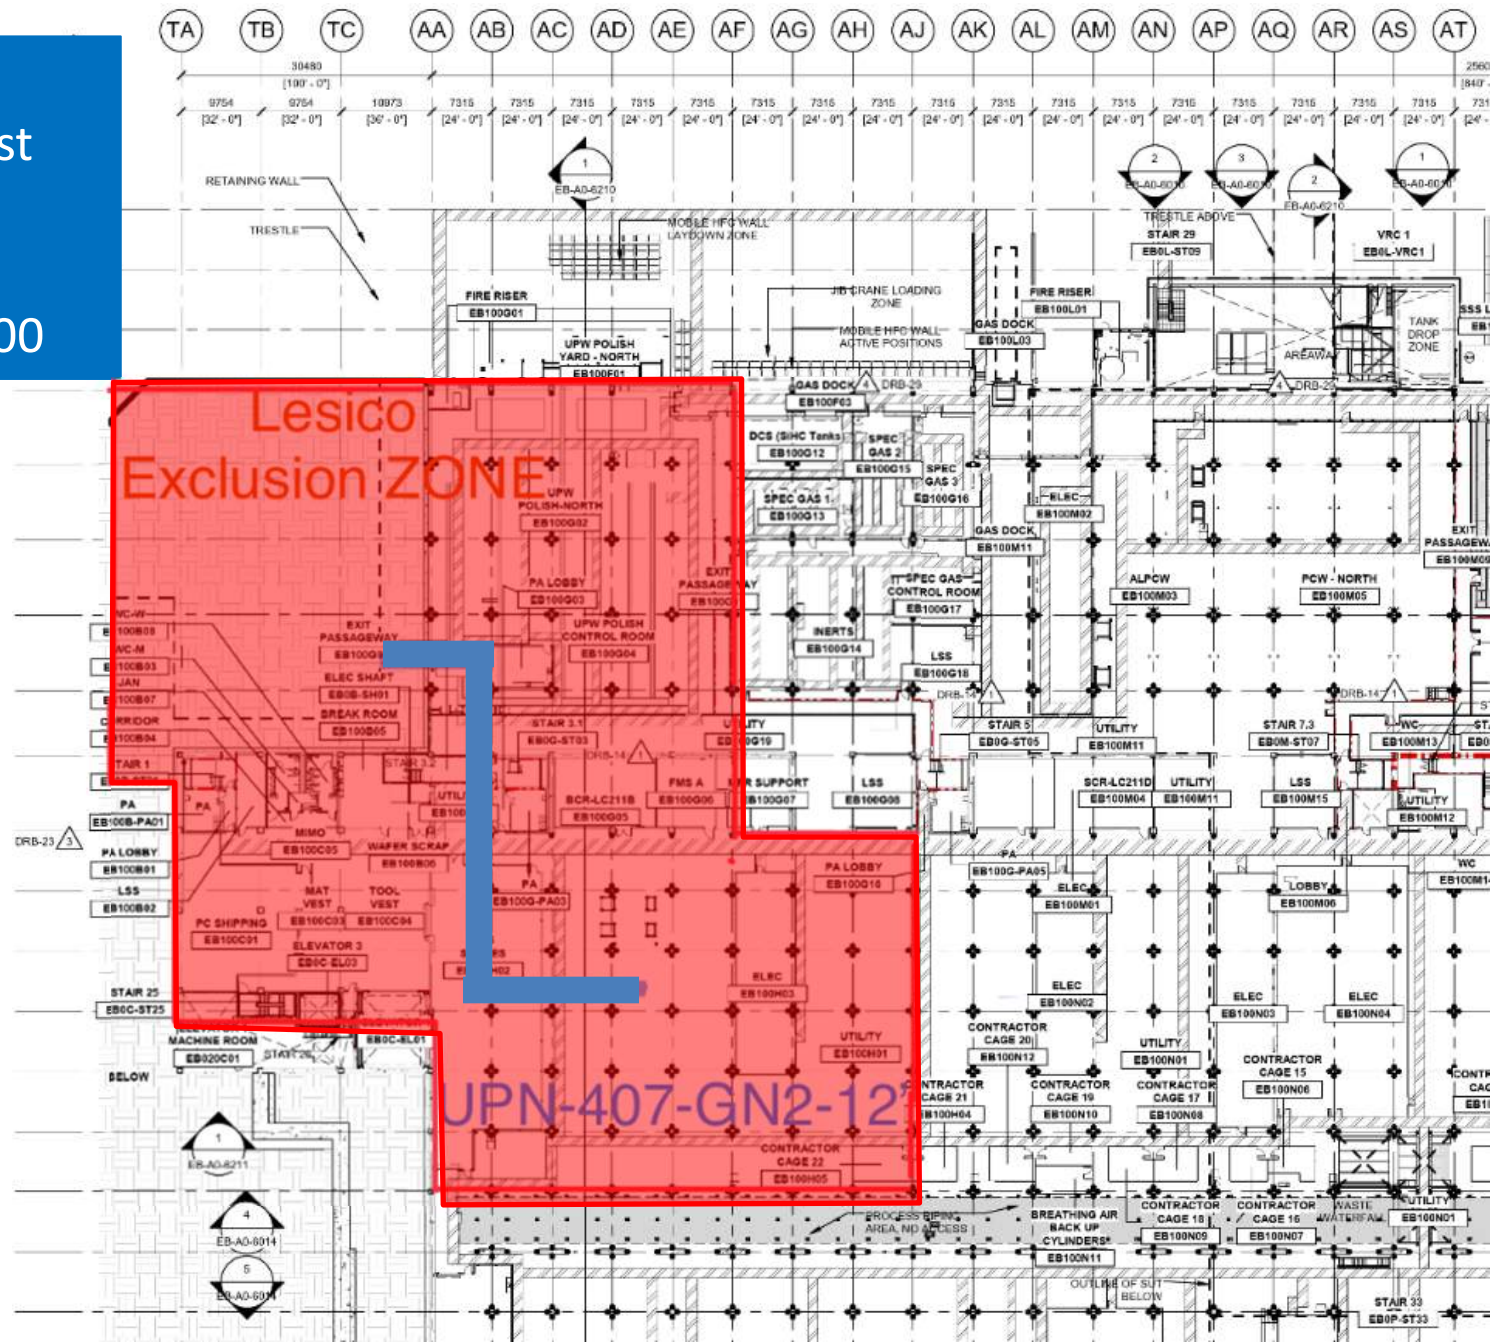

UTILITY LEVEL MOD1

LESICO

Pneumatic test


PA 8/29

Start 17:00

Finish 22:00

AA

CD

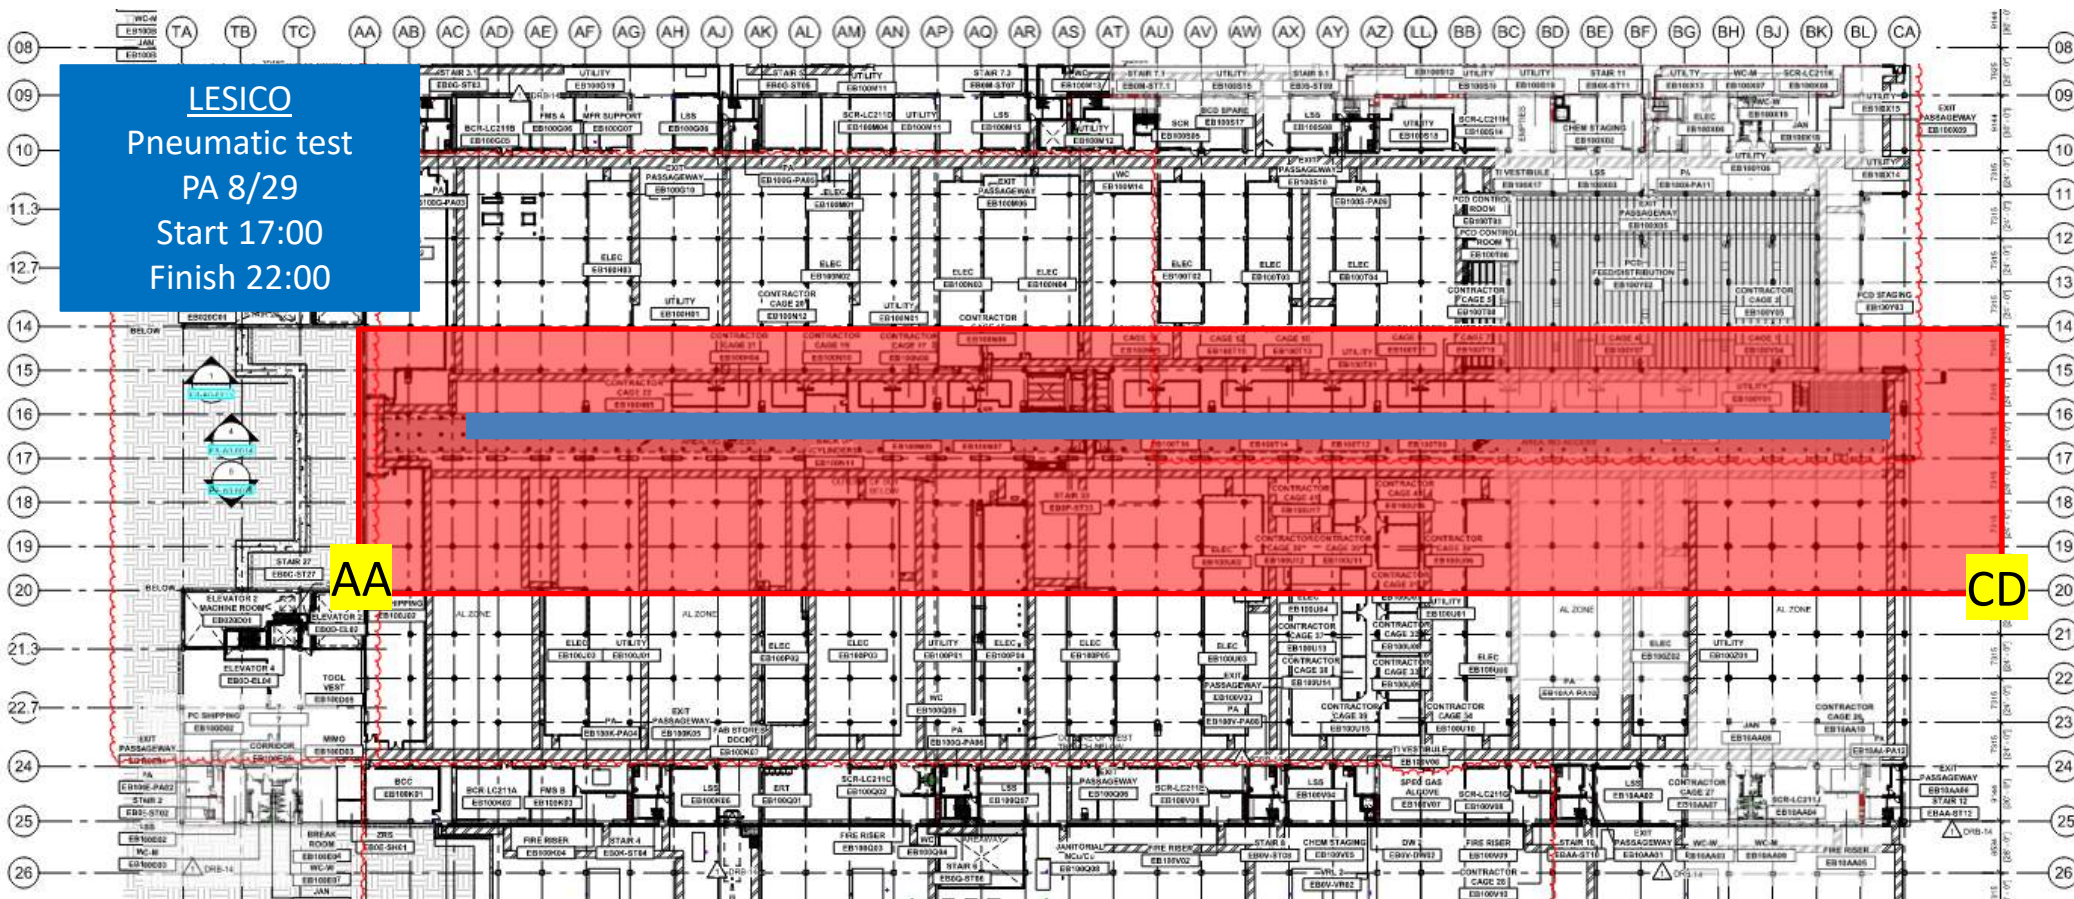




HOFFMAN CONSTRUCTION COMPANY




SUT LEVEL

LESICO
Pneumatic test
PA 8/29
Start 17:00
Finish 22:00

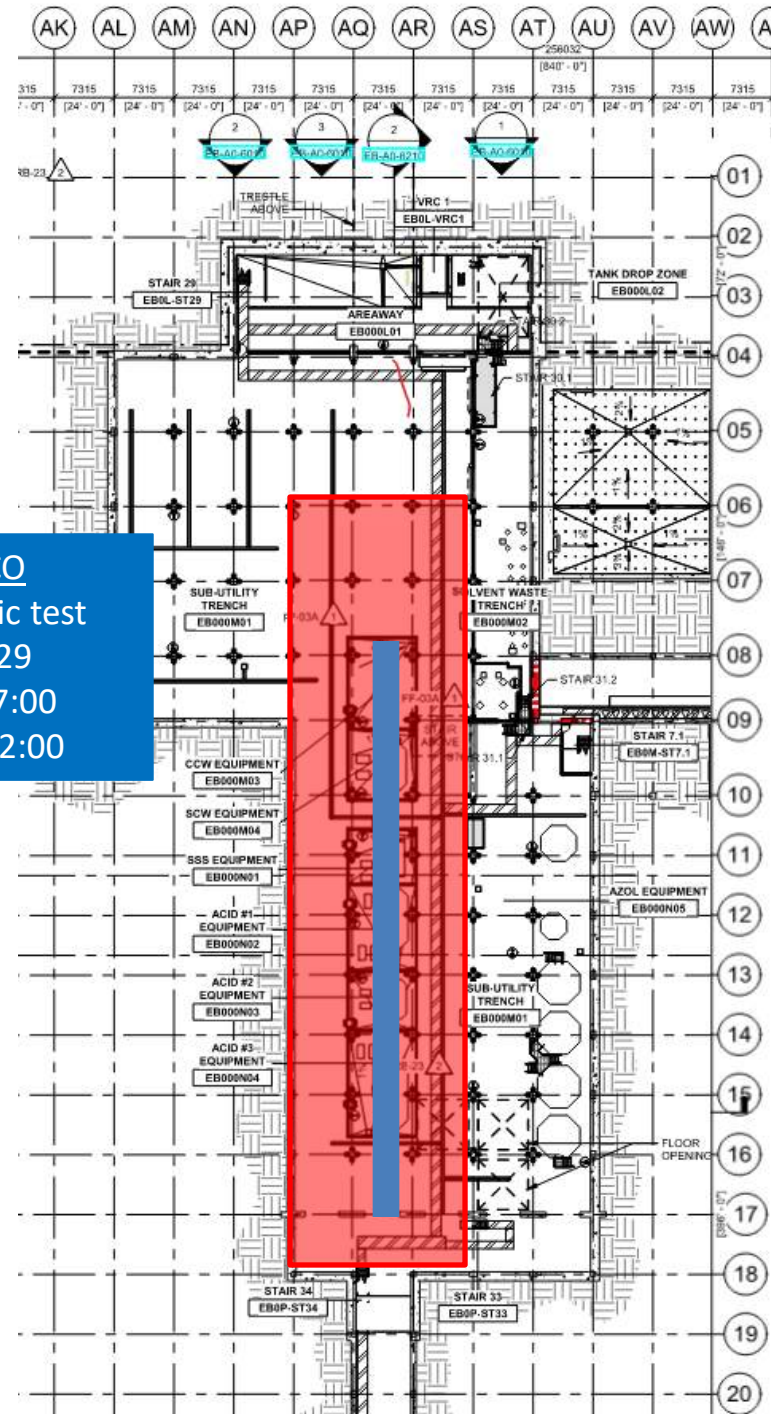



UTILITY LEVEL MOD1

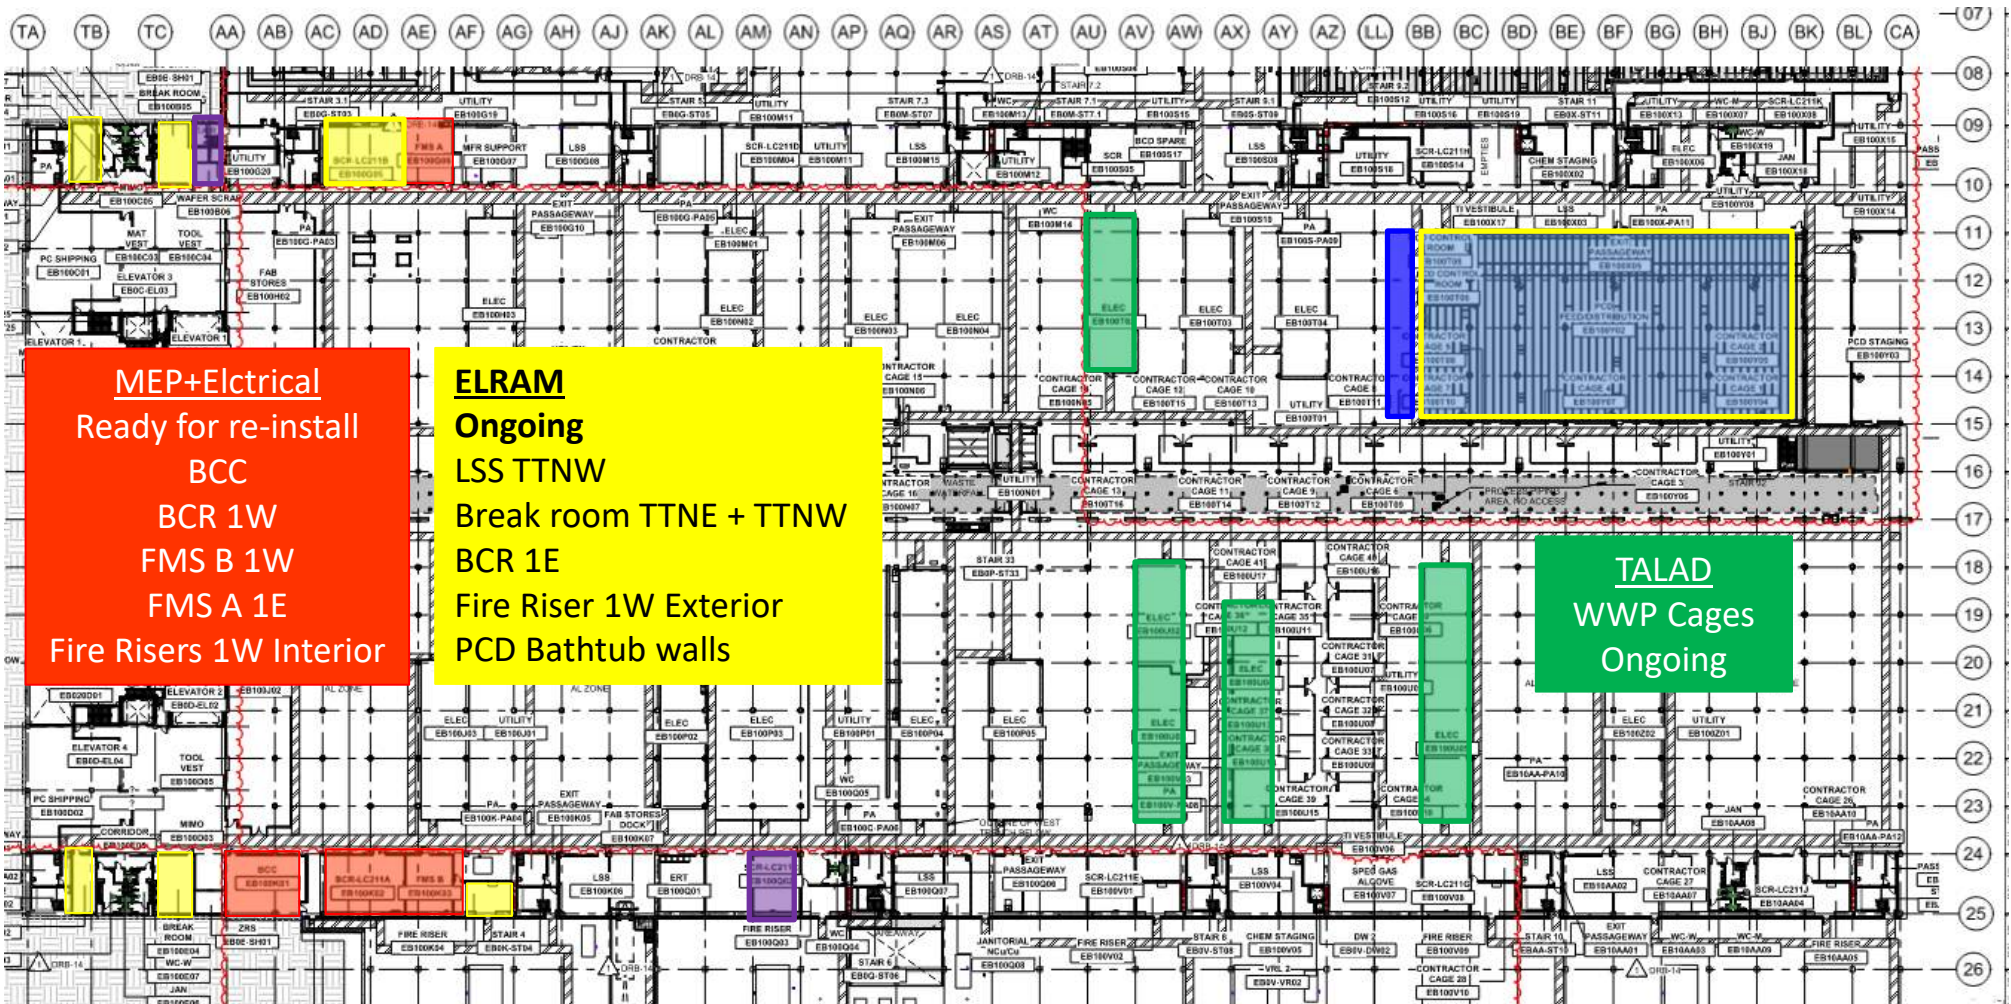

MEP+Electrical
Ready for re-install
BCC
BCR 1W
FMS B 1W
FMS A 1E
Fire Risers 1W Interior


ELRAM
Ongoing
LSS TTNW
Break room TTNE + TTNW
BCR 1E
Fire Riser 1W Exterior
PCD Bathtub walls

TALAD
WWP Cages
Ongoing




A detailed architectural floor plan of a building's upper levels, showing various rooms like CONTRACTOR CAGE, MECHANICAL ROOM, and ELEVATOR SHAFTS. A large blue rectangular area covers the central part of the plan, indicating ongoing work. A red arrow points from the bottom right towards the center of this blue area. The text "MEPTAGON 10E Bridge strut install Ongoing" is written in white on a blue background at the top left.

SUT 38.1 LEVEL

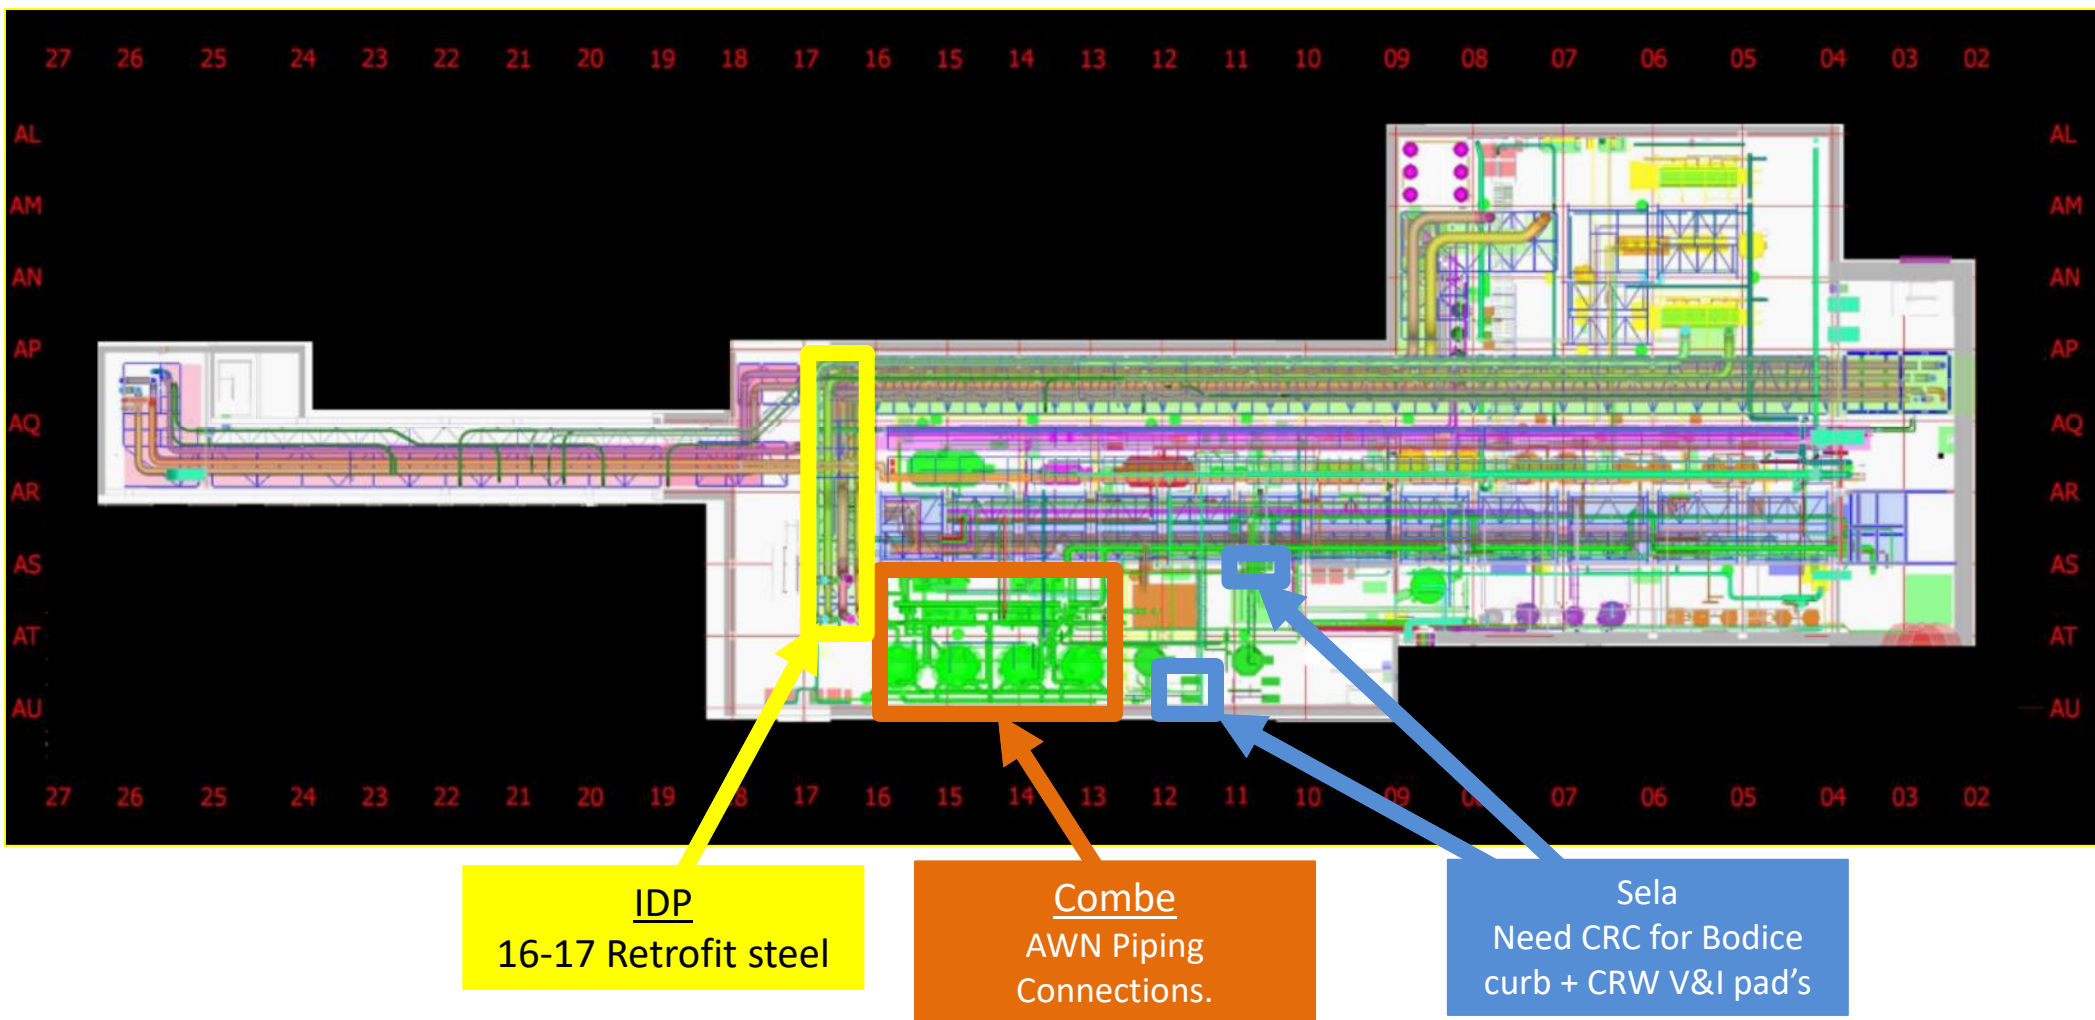



SUT 38.2 LEVEL

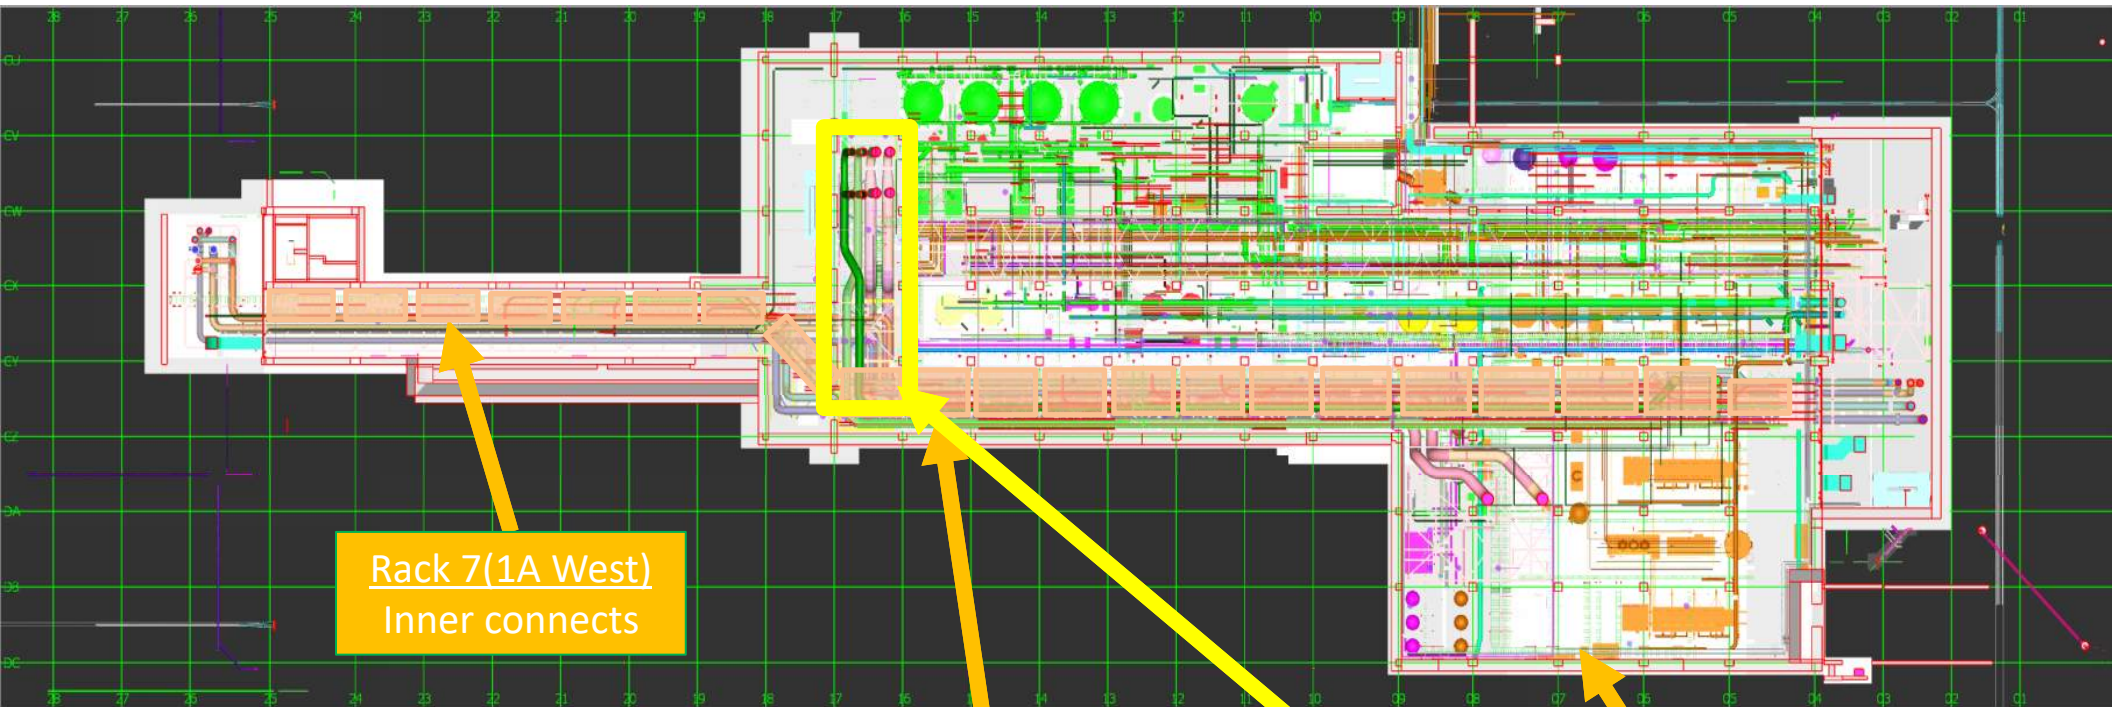

Rack 7(1A West)
Inner connects

1A Rack
Inner connects


16-17 line
Upper Steel Bed
build

8 Rack
Lifting


CRW
H&T
Installing supports

Vesda
H&T
Not actively installing


SUBFAB BUILDOUT MOD 1

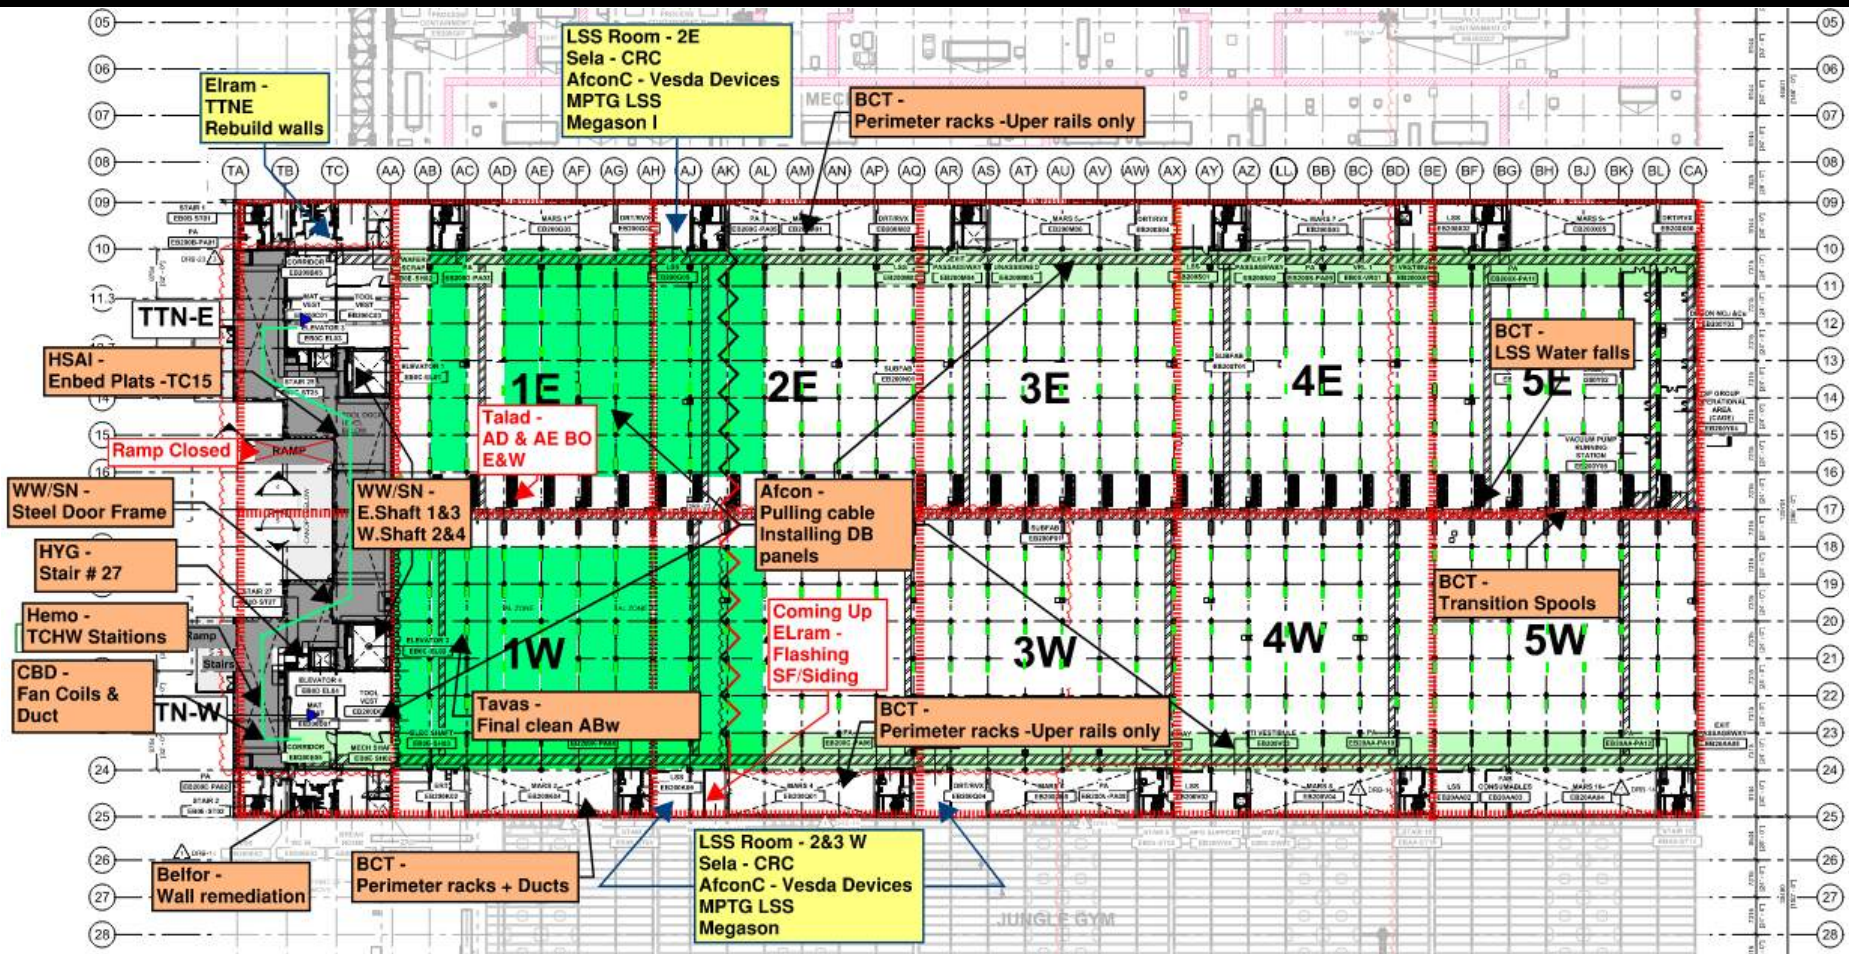



SUBFAB BUILDOUT MOD 2

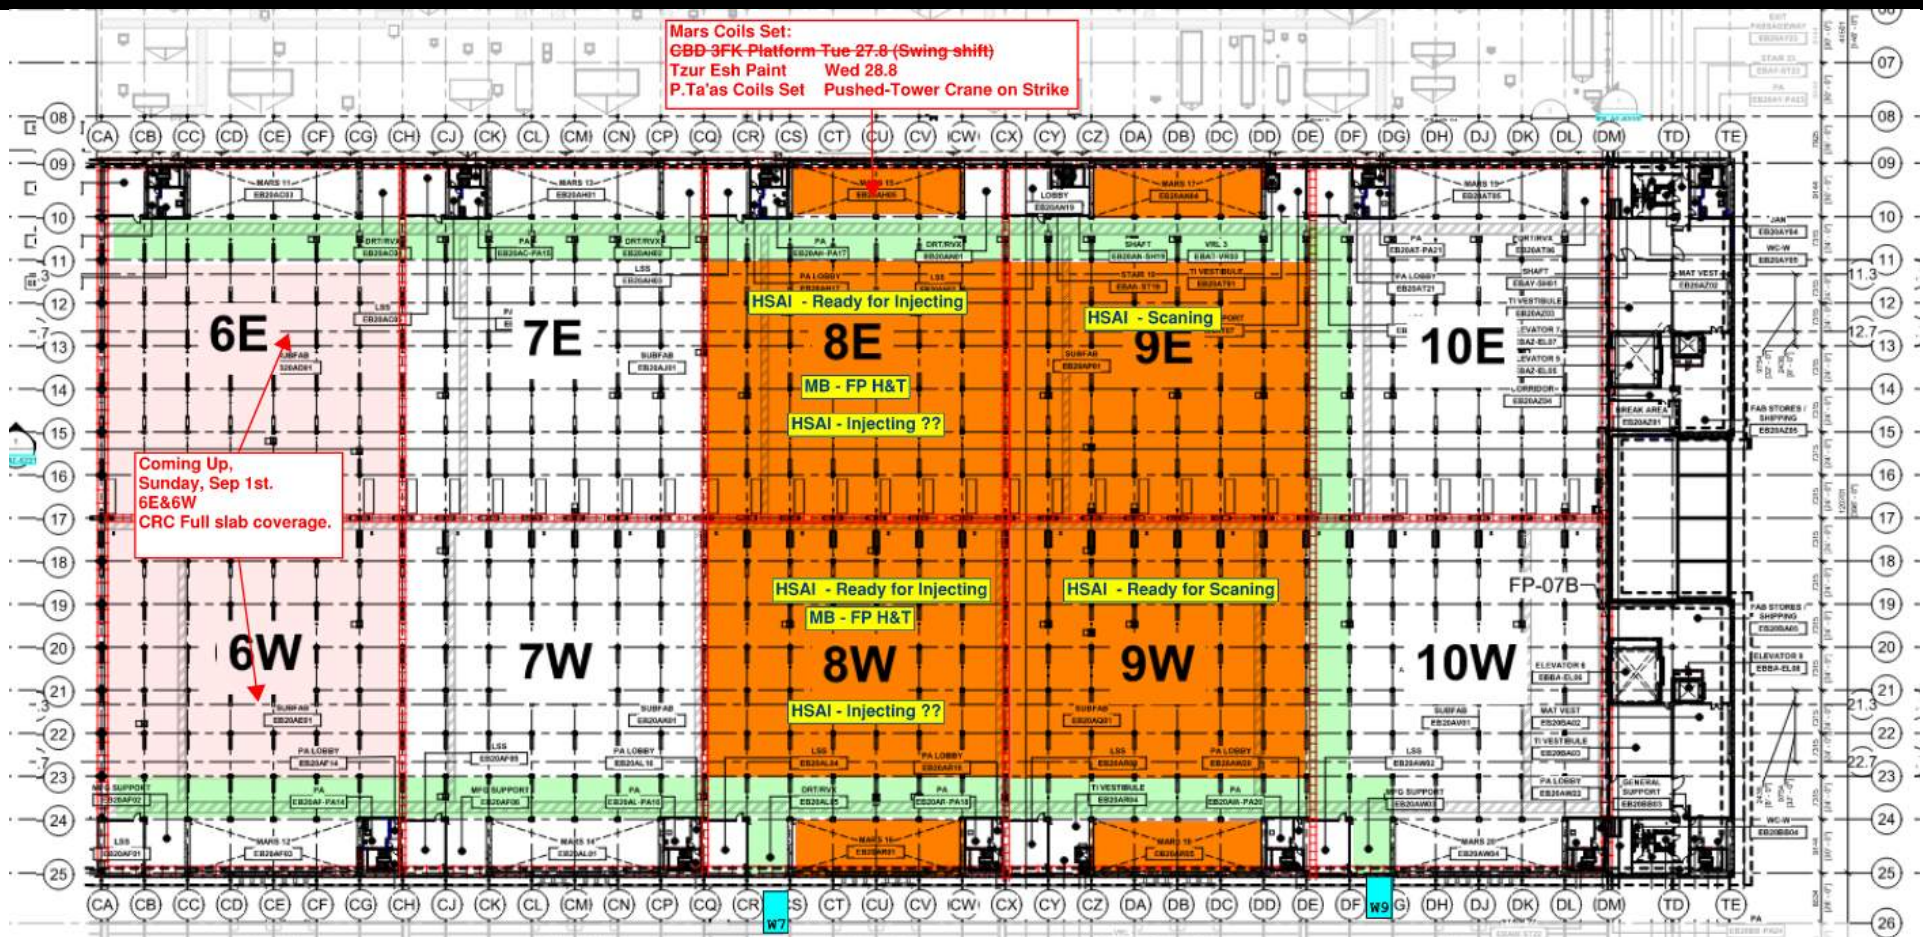

SUBFAB CRC TOPCOAT

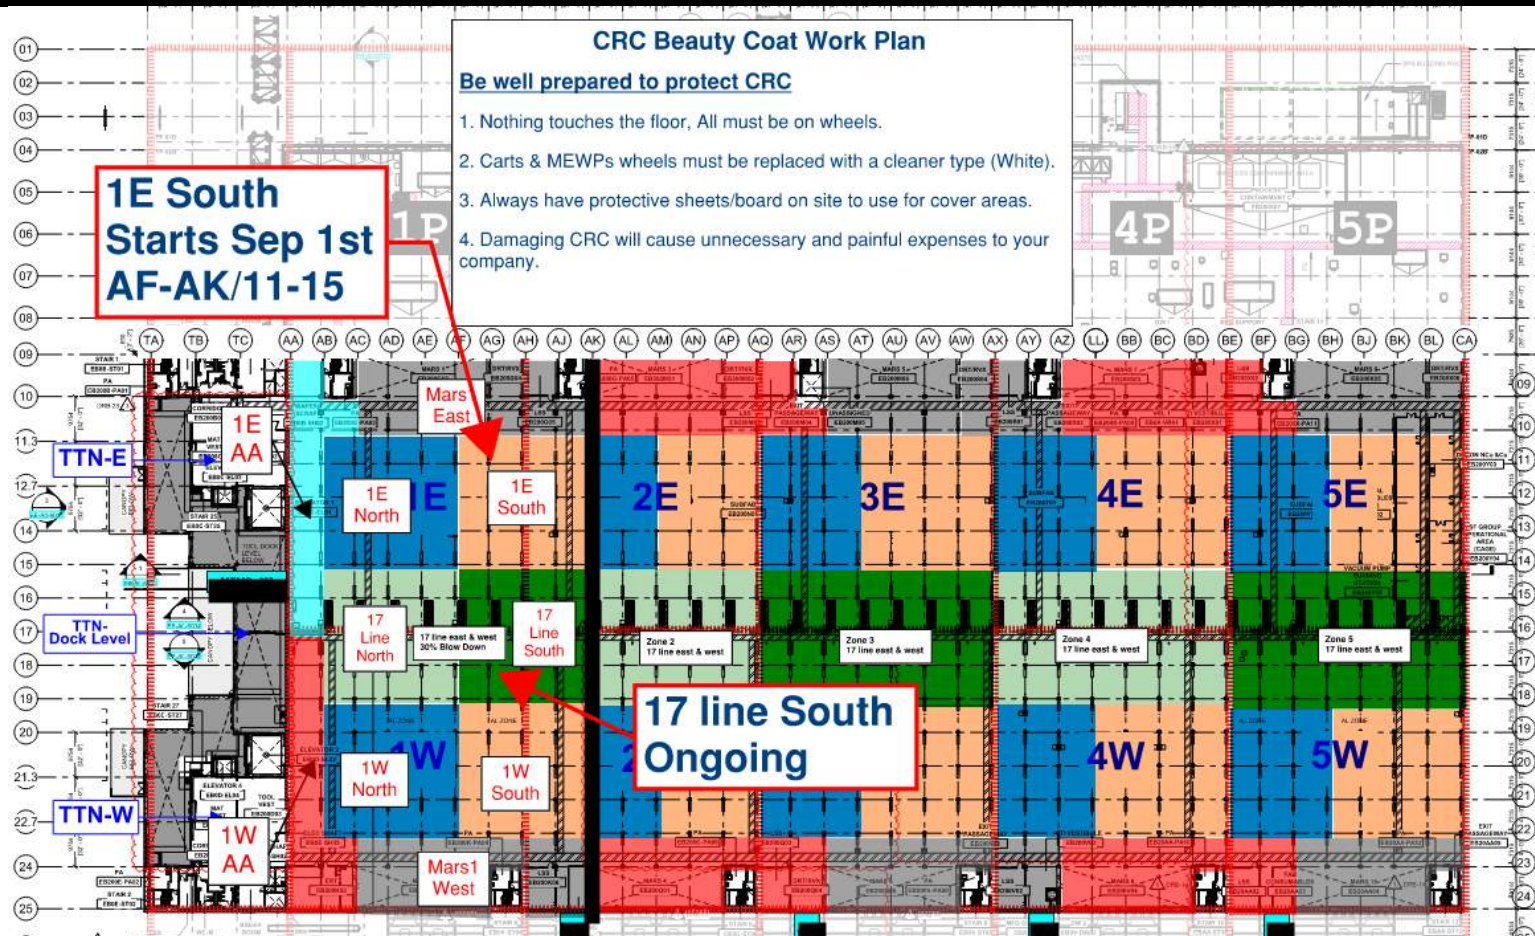


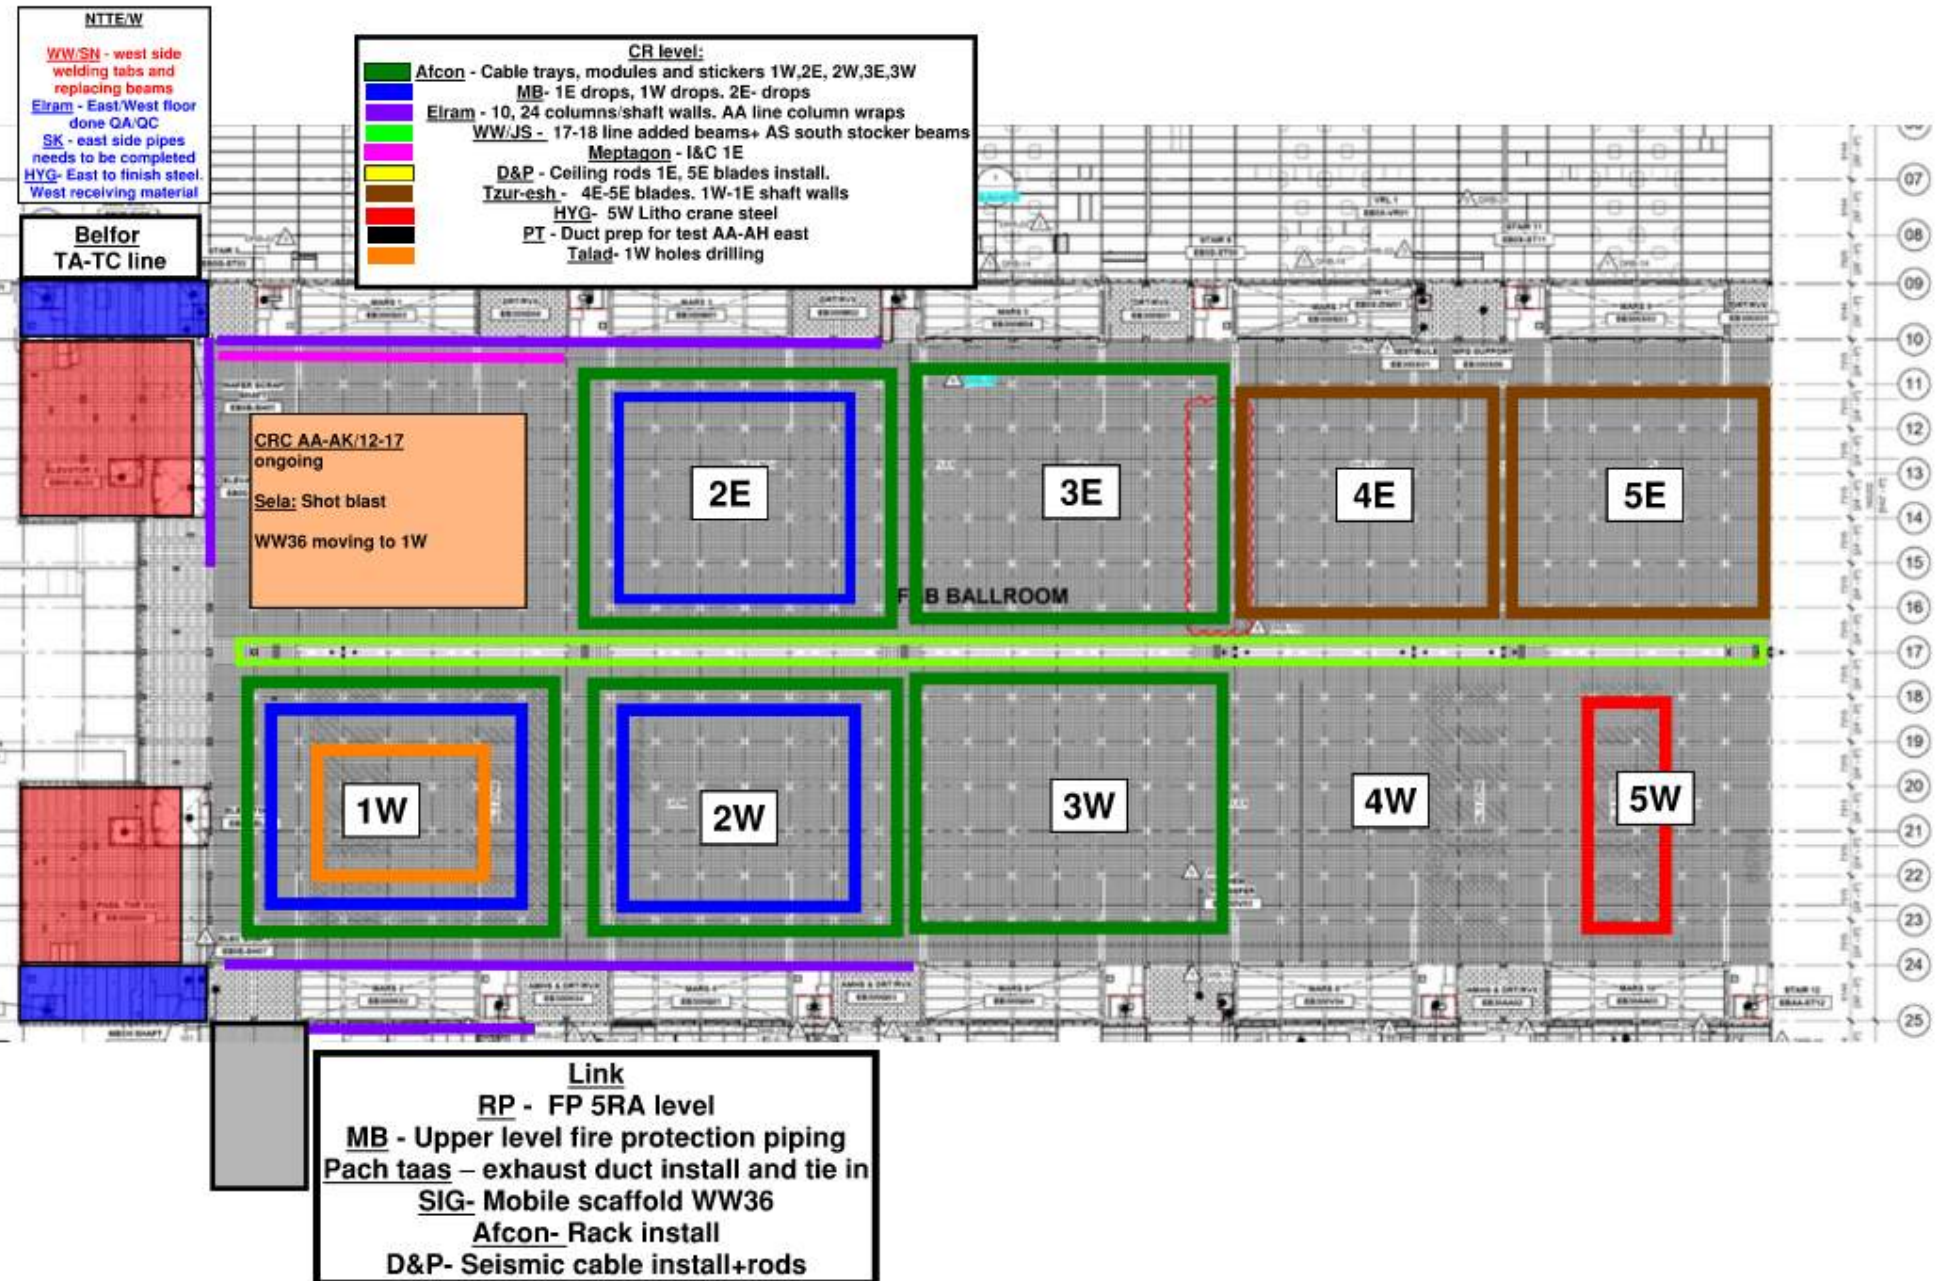


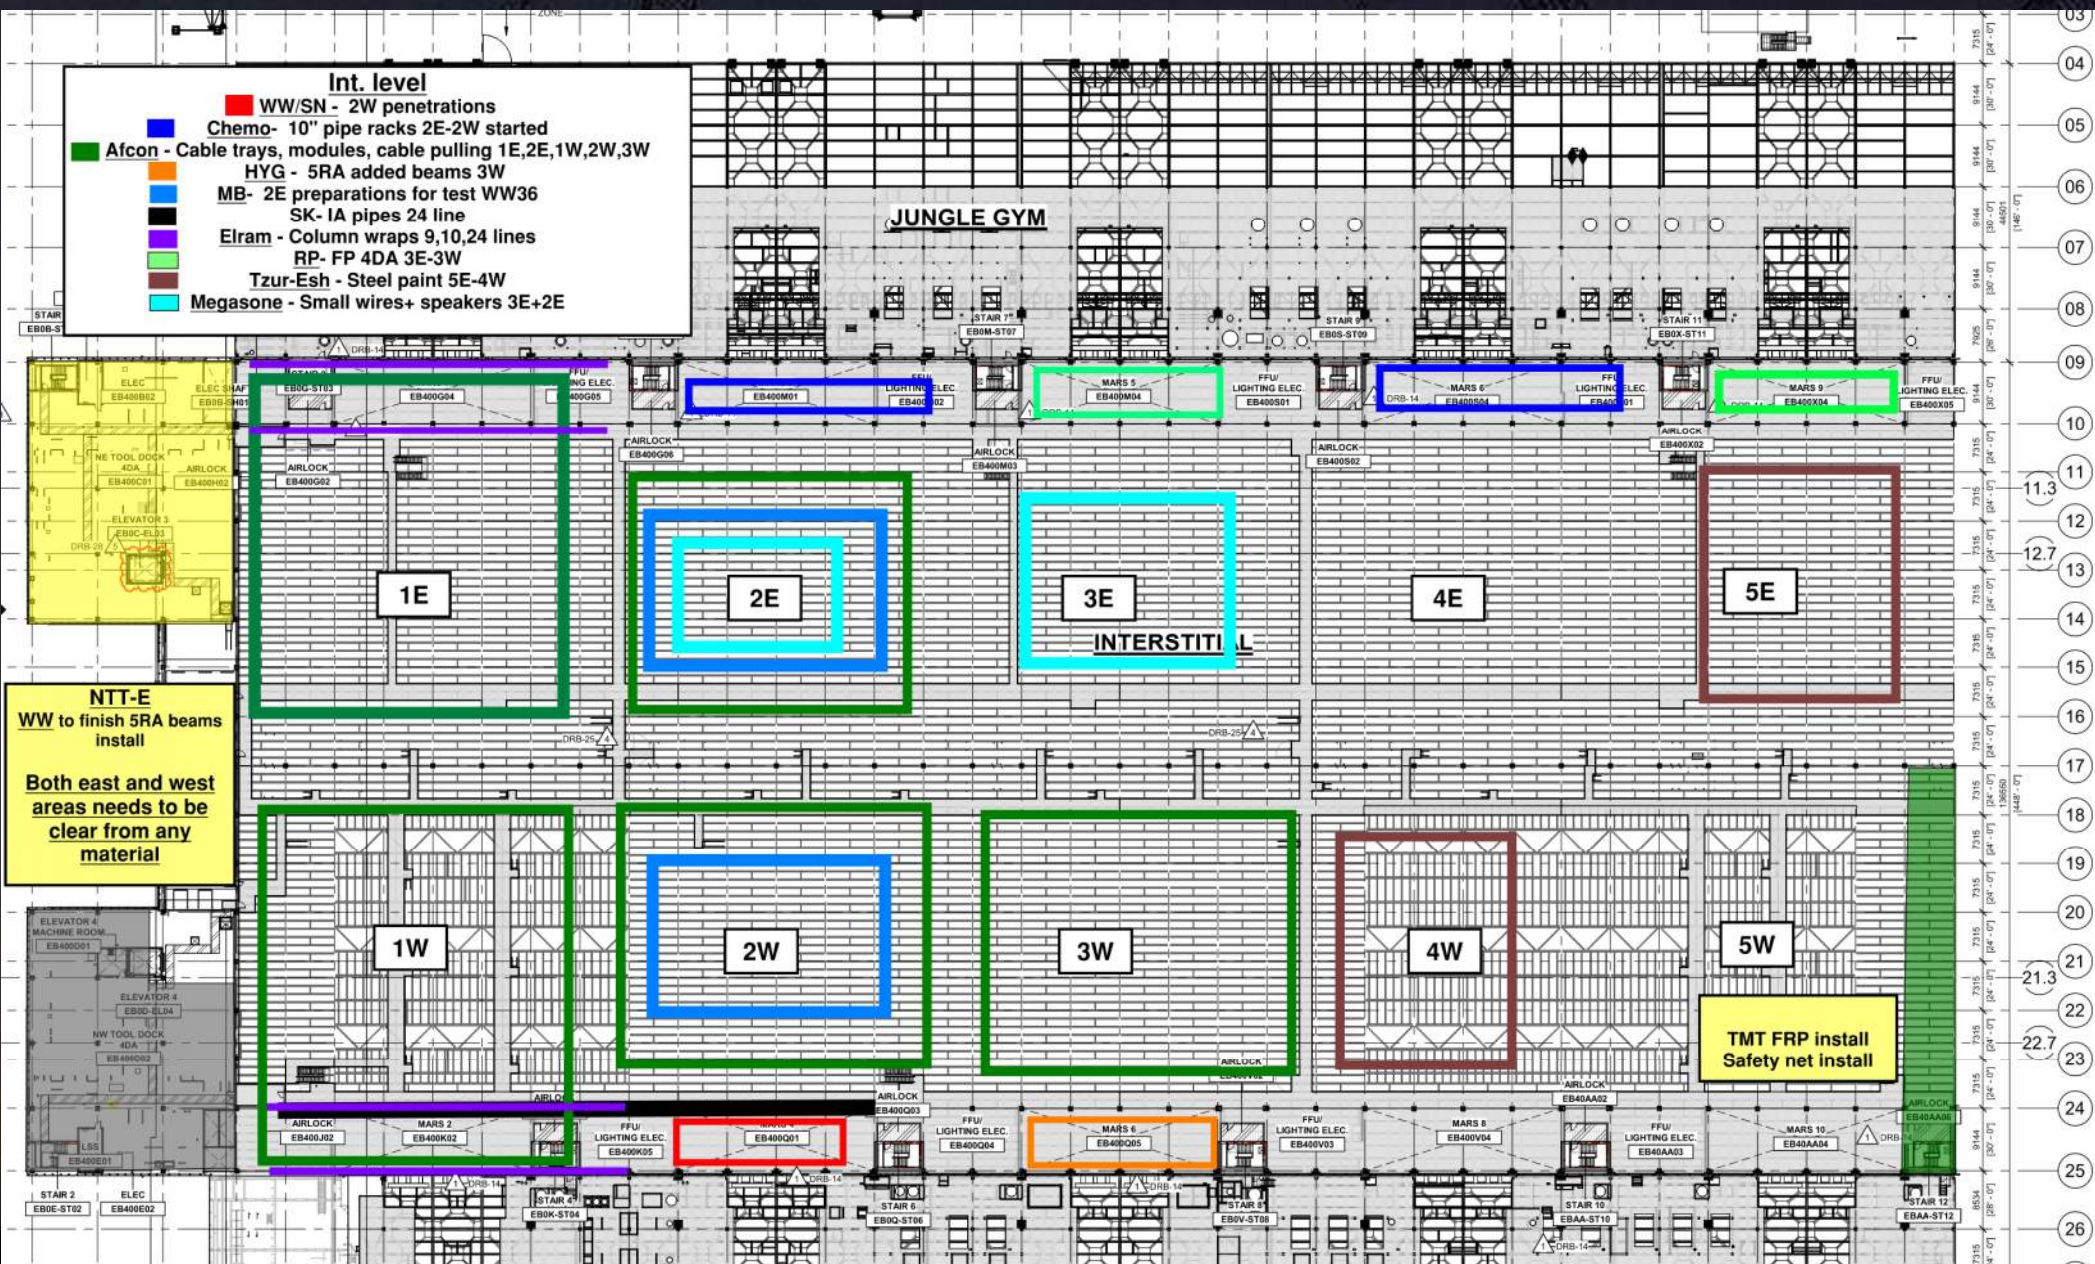





Truss Yard:
RP and Tzur-Esh to start FP and paint trusses on night shift

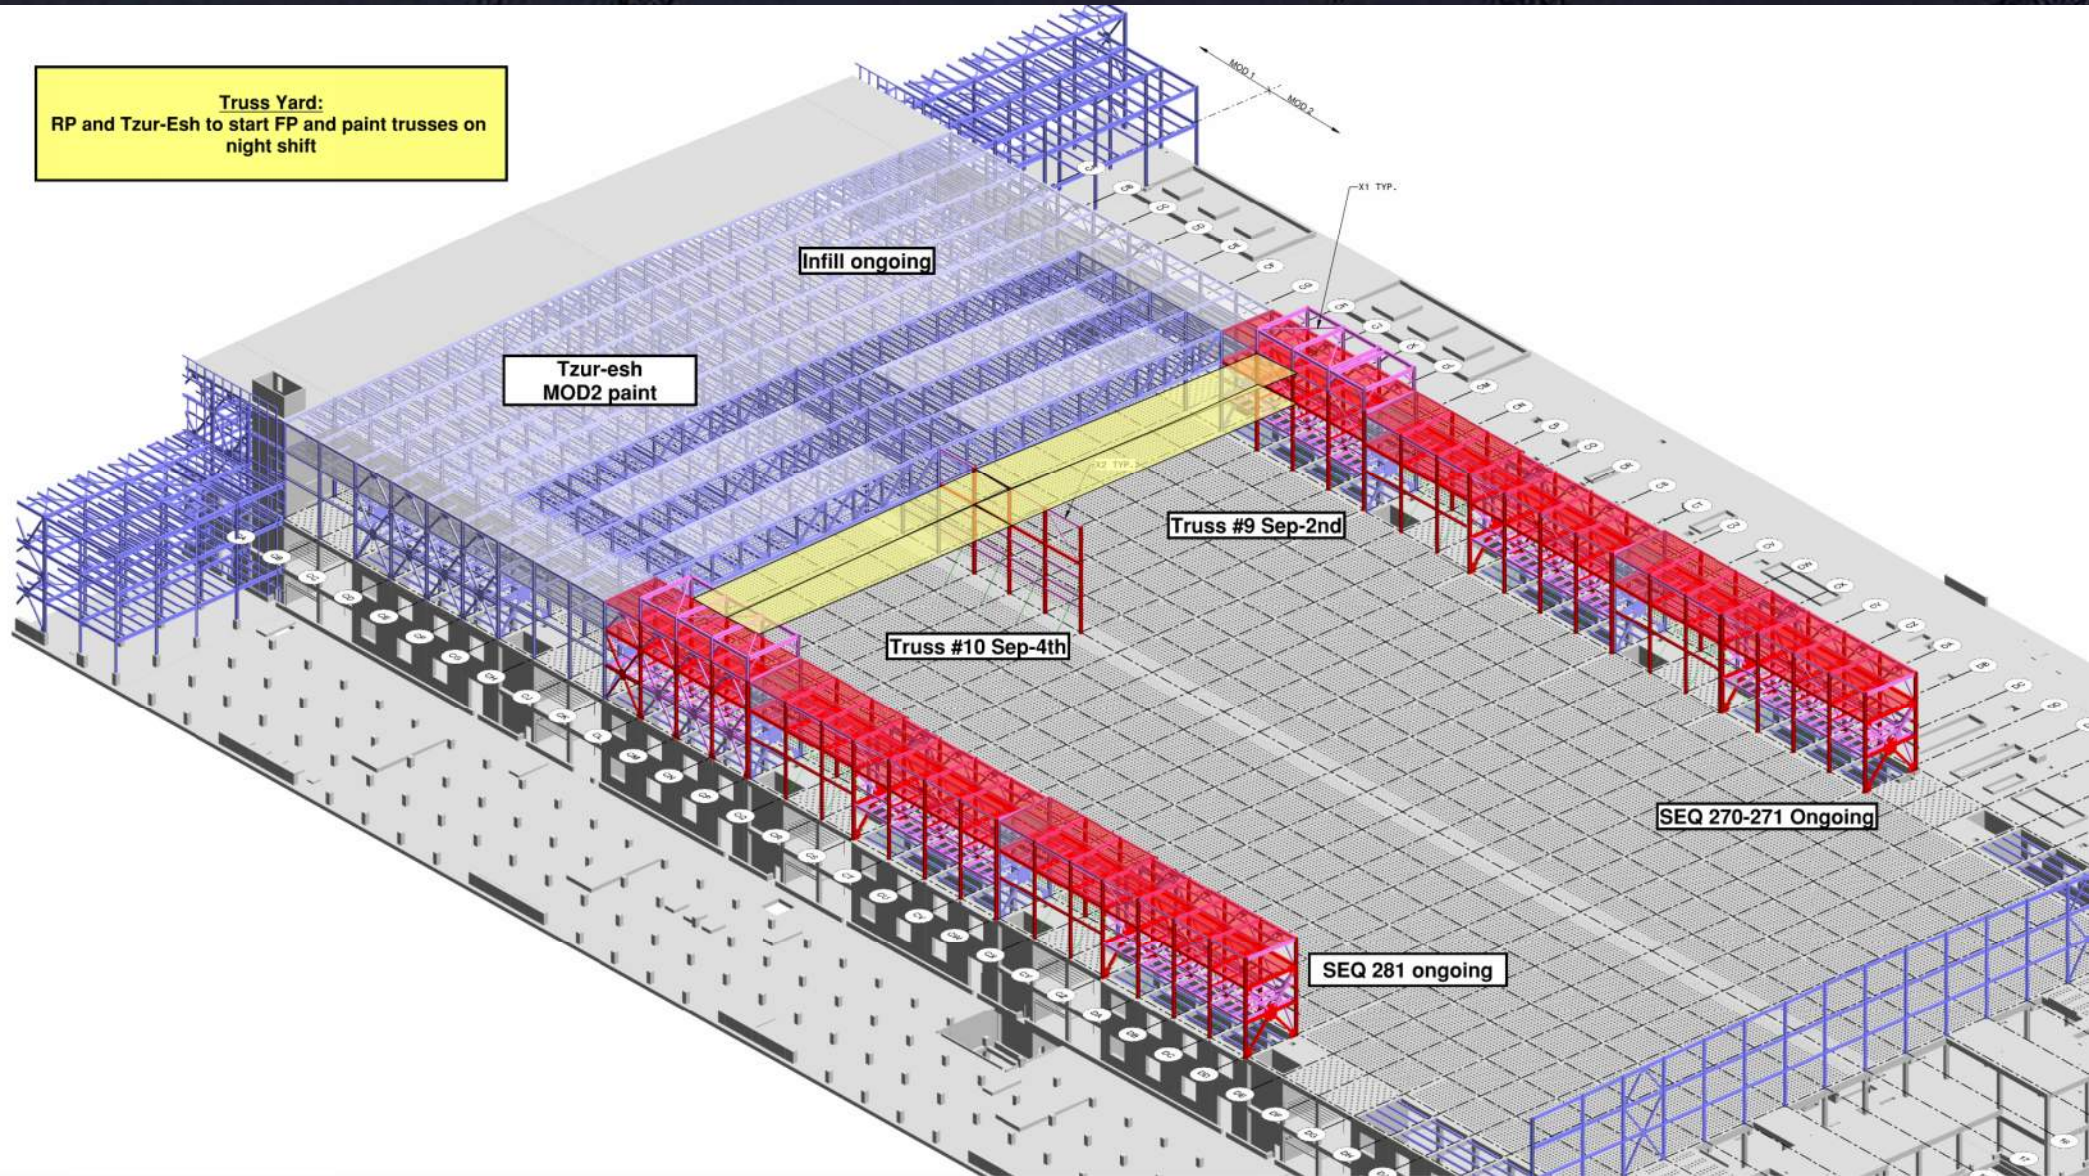


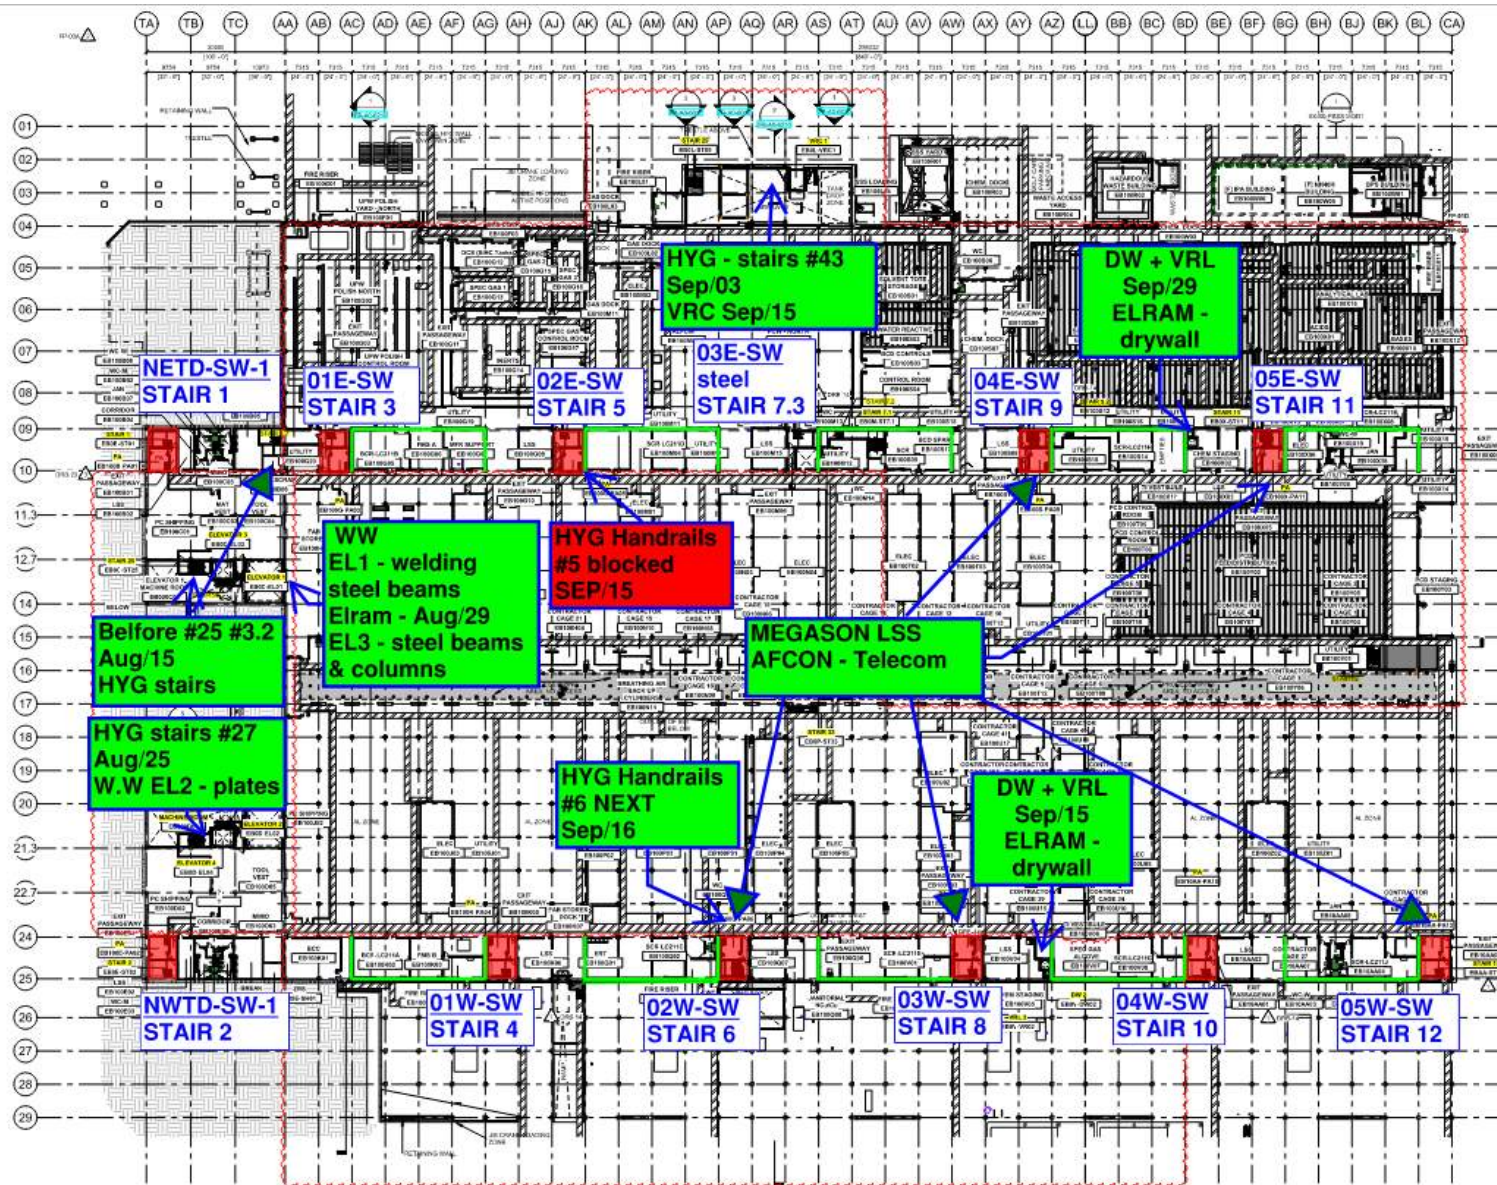

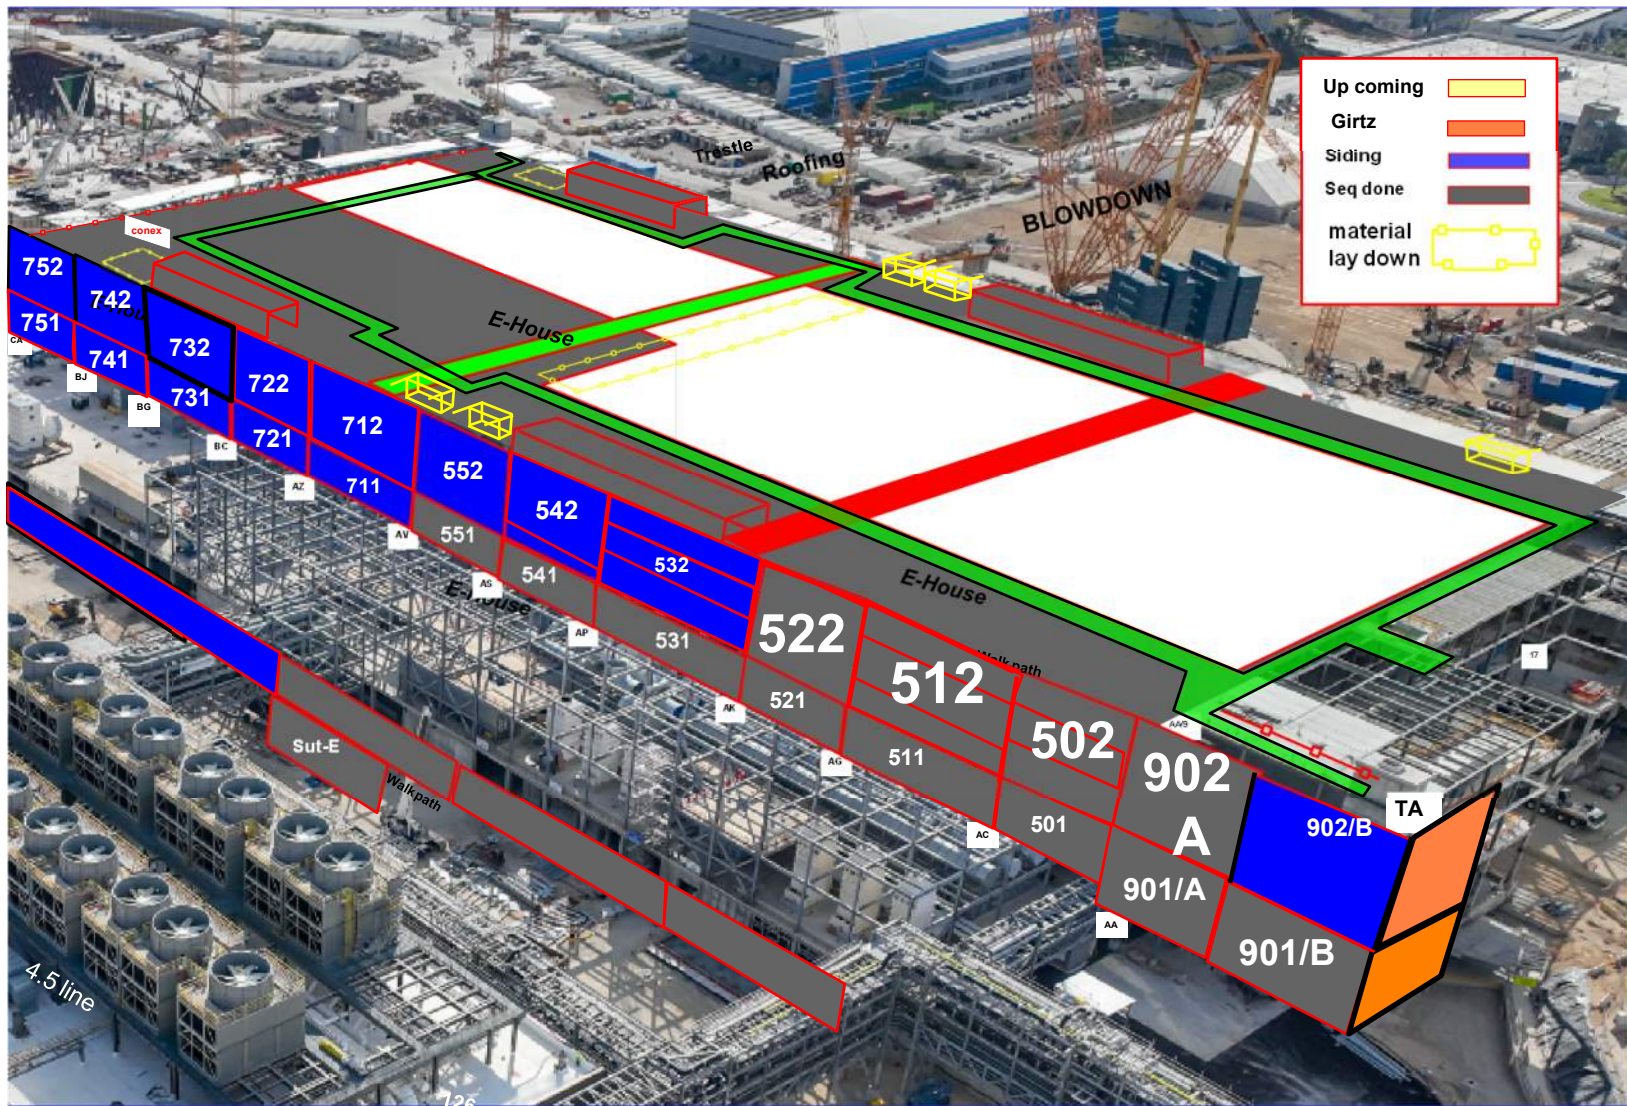

Walkpath

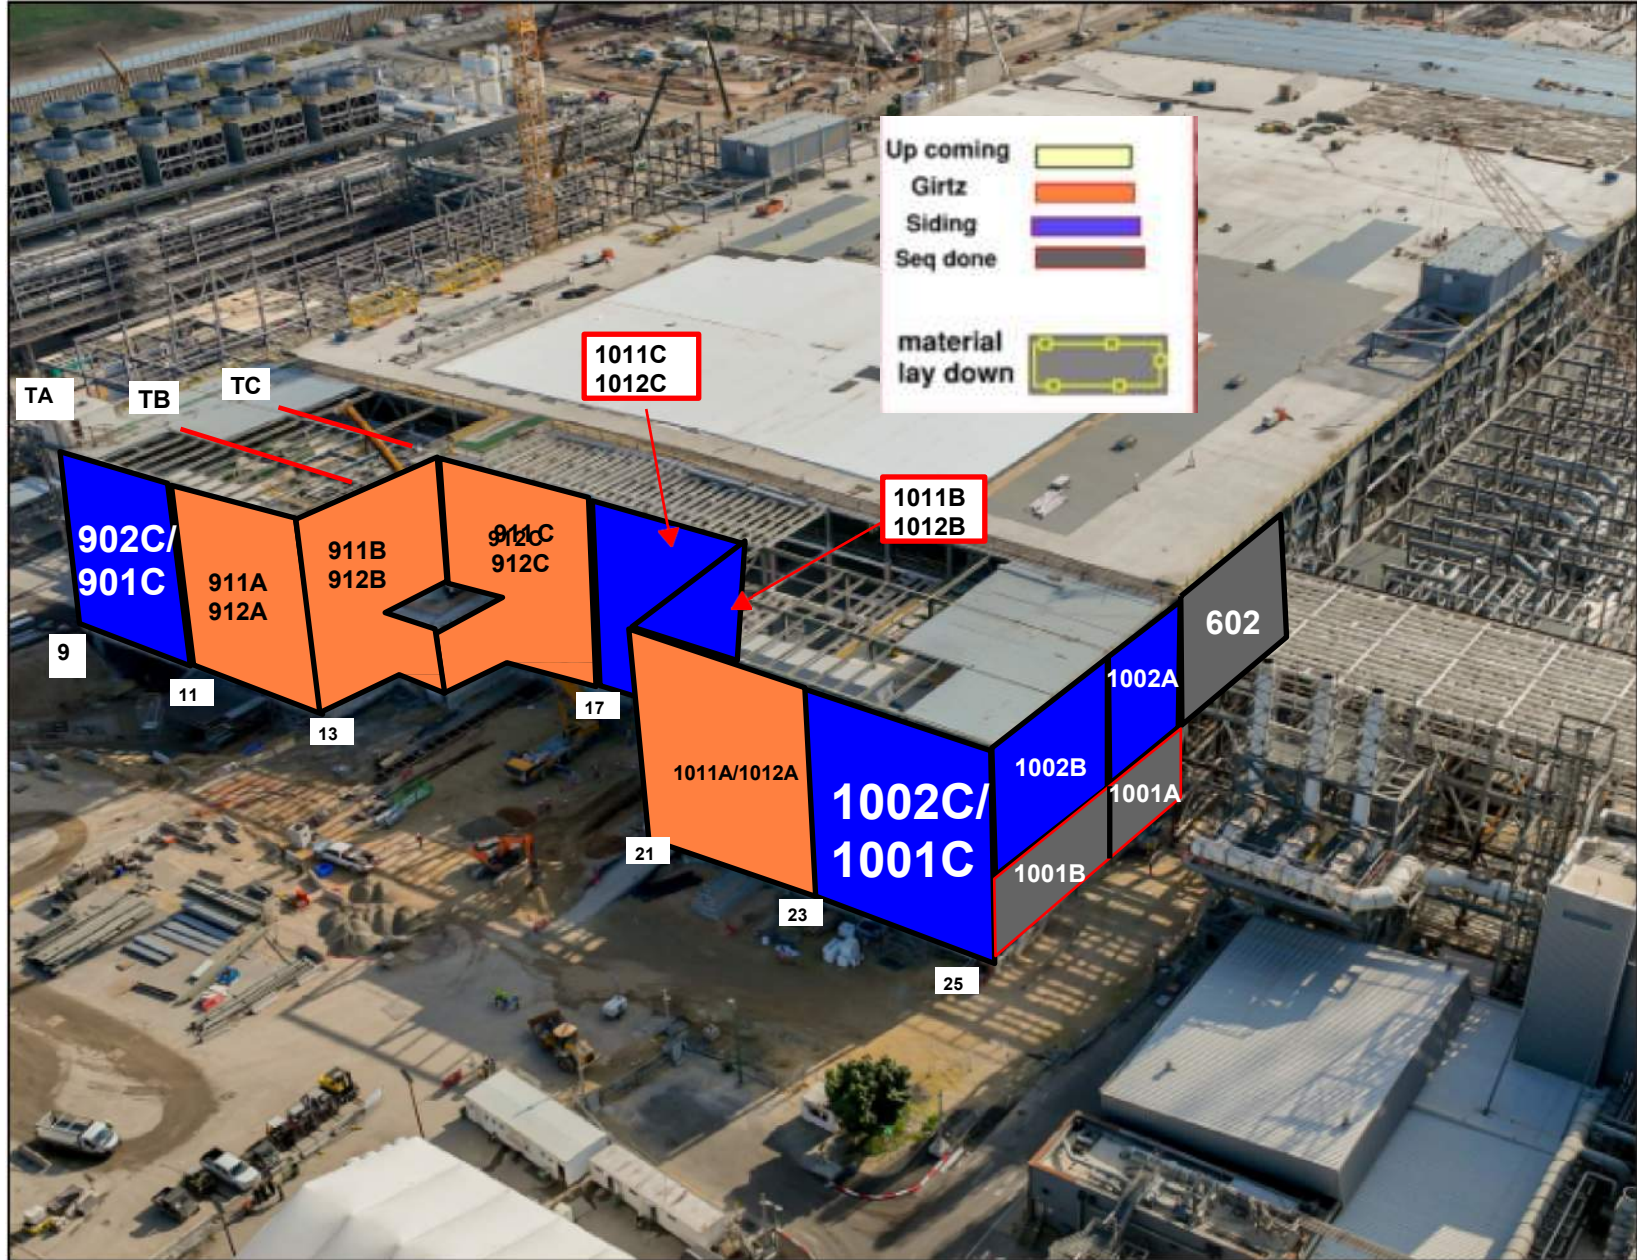

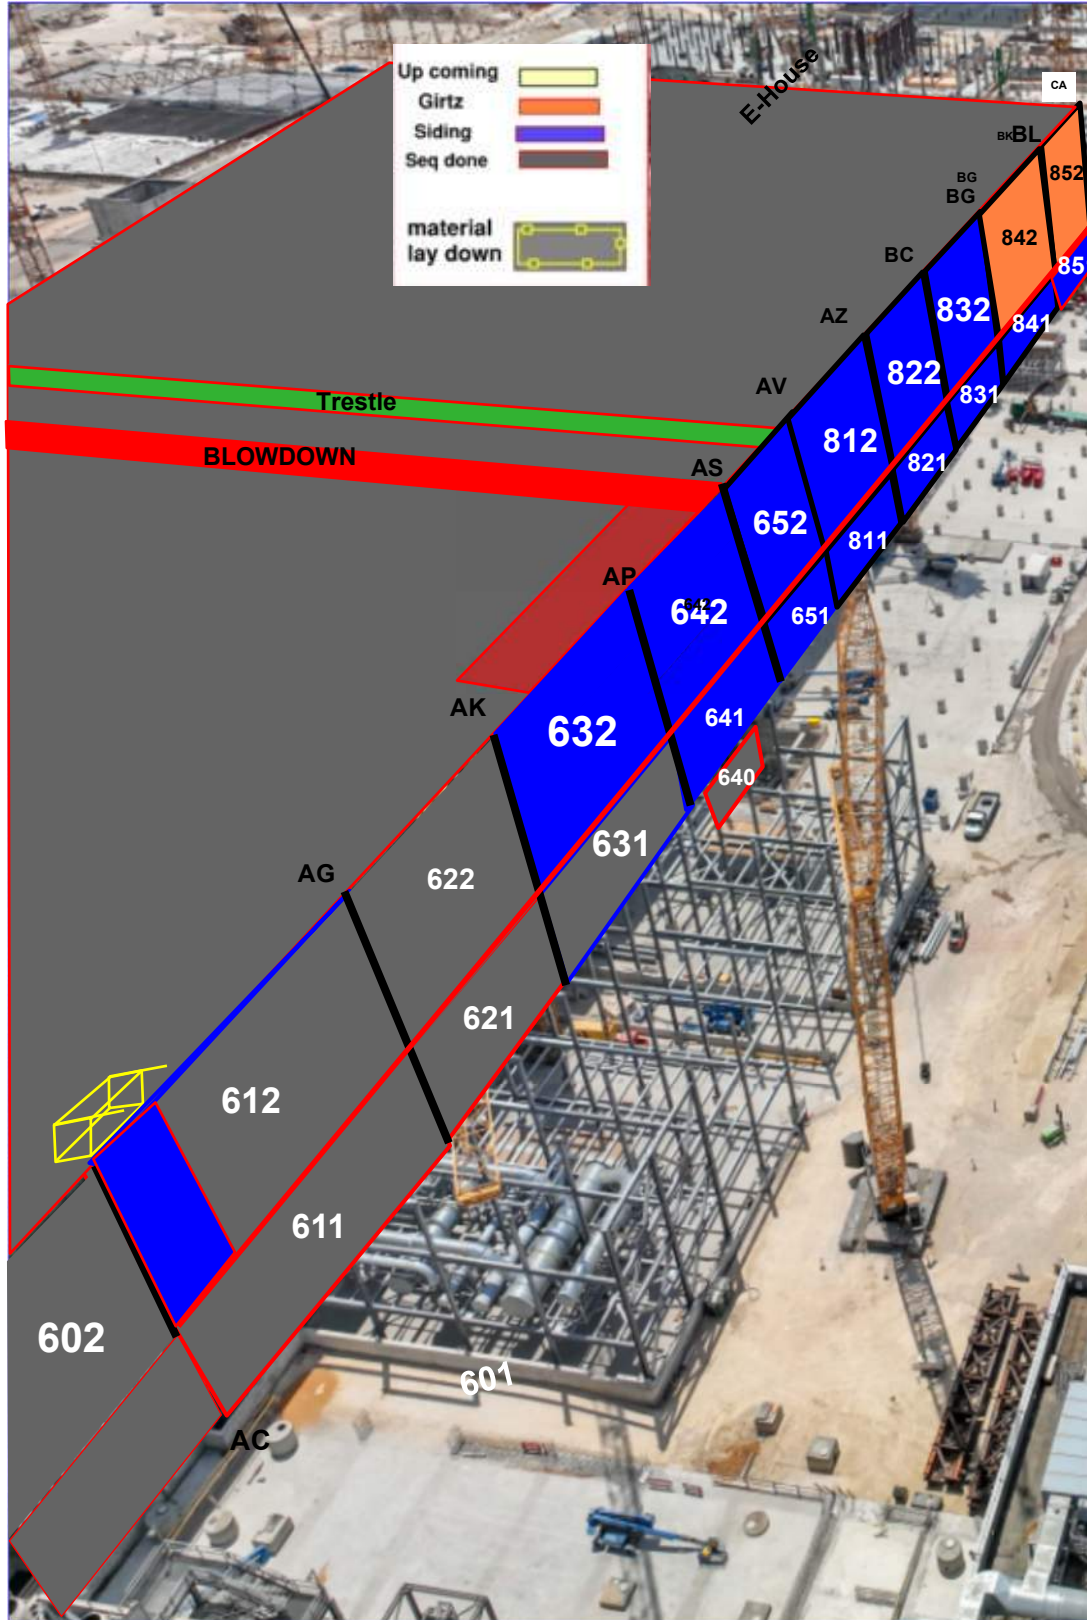


[illegible]


Siding - West FAB - JYG

		BLOWDOWN 30%																																																									
		TA	TB		TC	AA	AB		AC	AD		AE	AF	AG	AH		AJ	AK	AL		AM	AN	AP	AQ		AR	AS	AT		AU	AV	AW		AX	AY	AZ	BA		BB																				
		1001 / 1002				601 / 602				611 / 612						621 / 622						631 / 632								641 / 642								651 / 652								811 / 812								821 / 822					
Total		28	28	28	28	15	15	18	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31																
Installed		8	14	10		15	18		20	31	31	31	31	31	31	31	31	31	27	24	24	13		6	6	14		6	6	6		6	6	6	6	6	6	6	6	6	6	6	6	6	6	6													
%		29%	50%	36%		100%	100%		65%	100%	100%	100%	100%	100%	100%	100%	100%	100%	87%	77%	77%	42%		19%	19%	45%		19%	19%	19%		19%	19%	19%	19%	19%	19%	19%	19%	19%	19%	19%	19%	19%	19%	19%	19%	19%											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
5RA		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
4DA		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
3FK		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
3FA		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0											
		0	0	0		0	0		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0																										

PSSS-UL

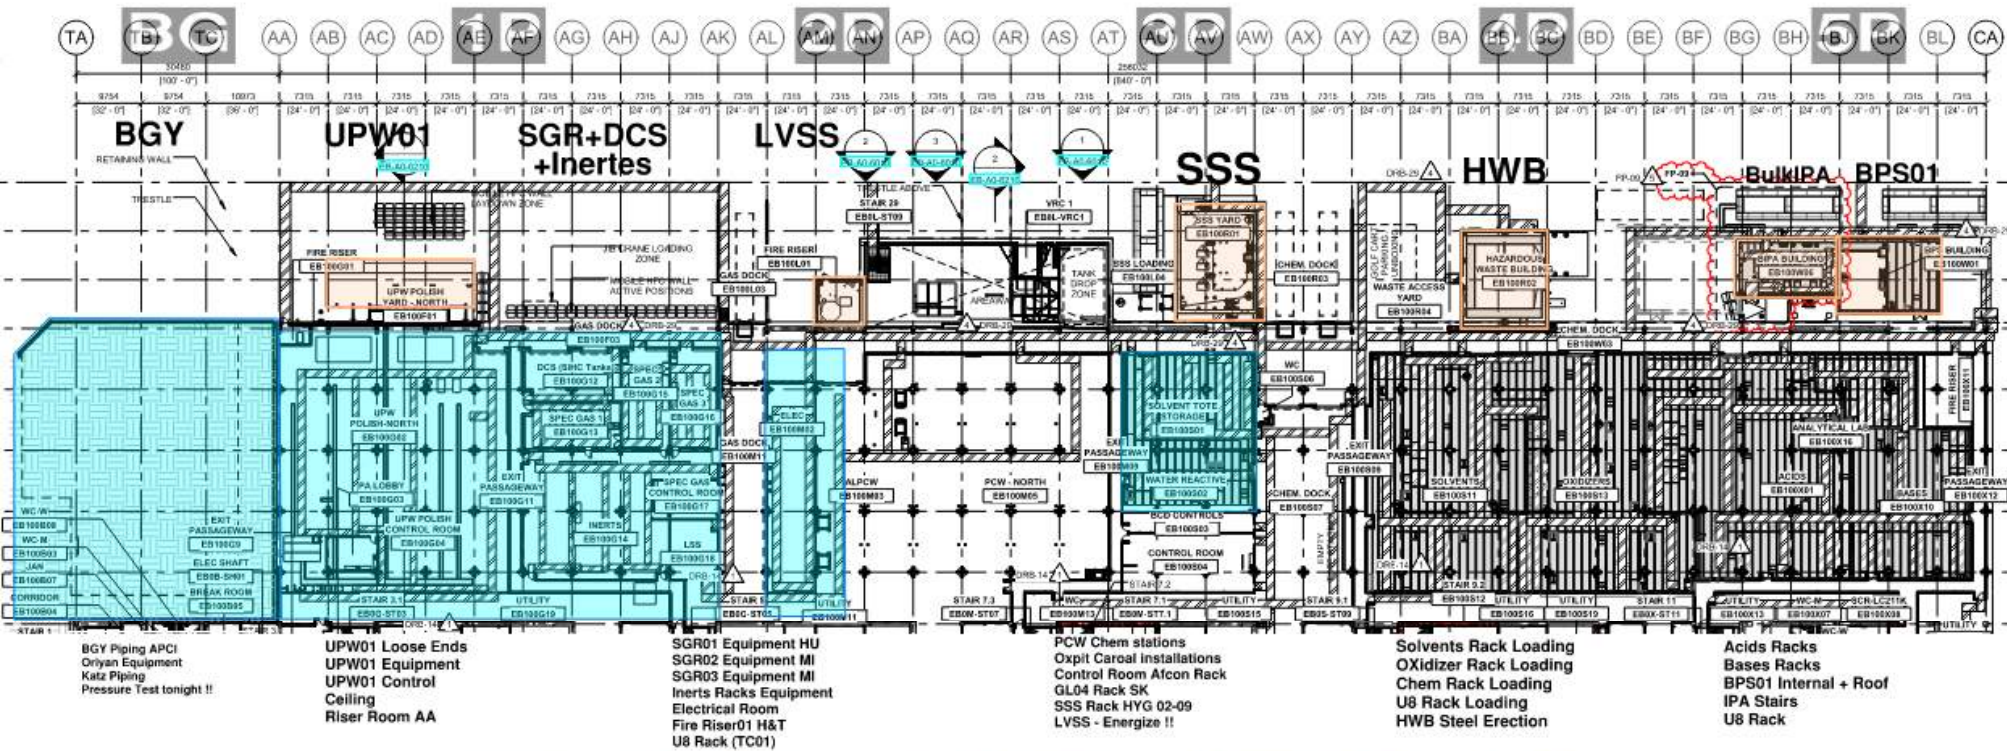


PSSS-Roof

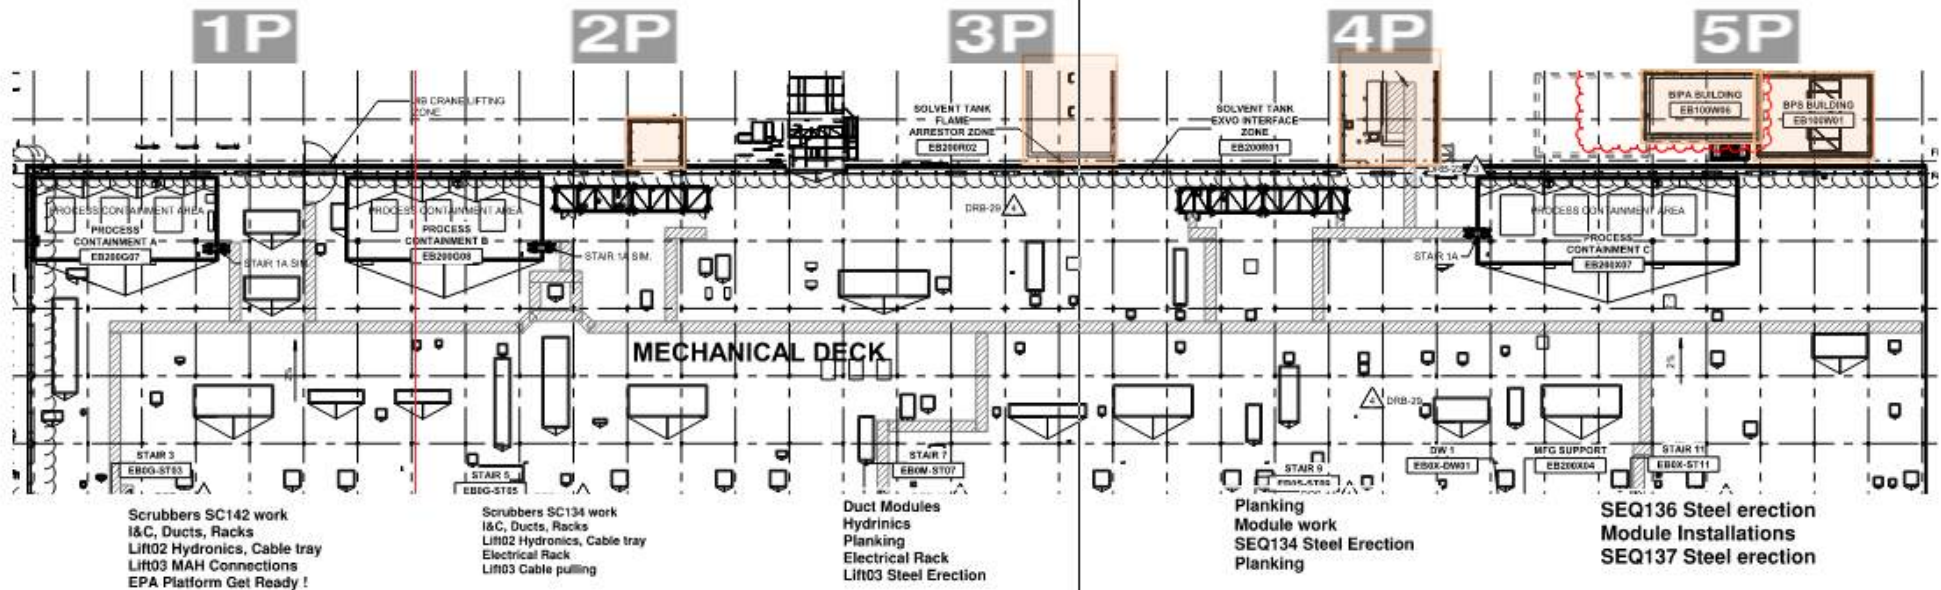




WJG 01J, 02J LIFT 2 & 3

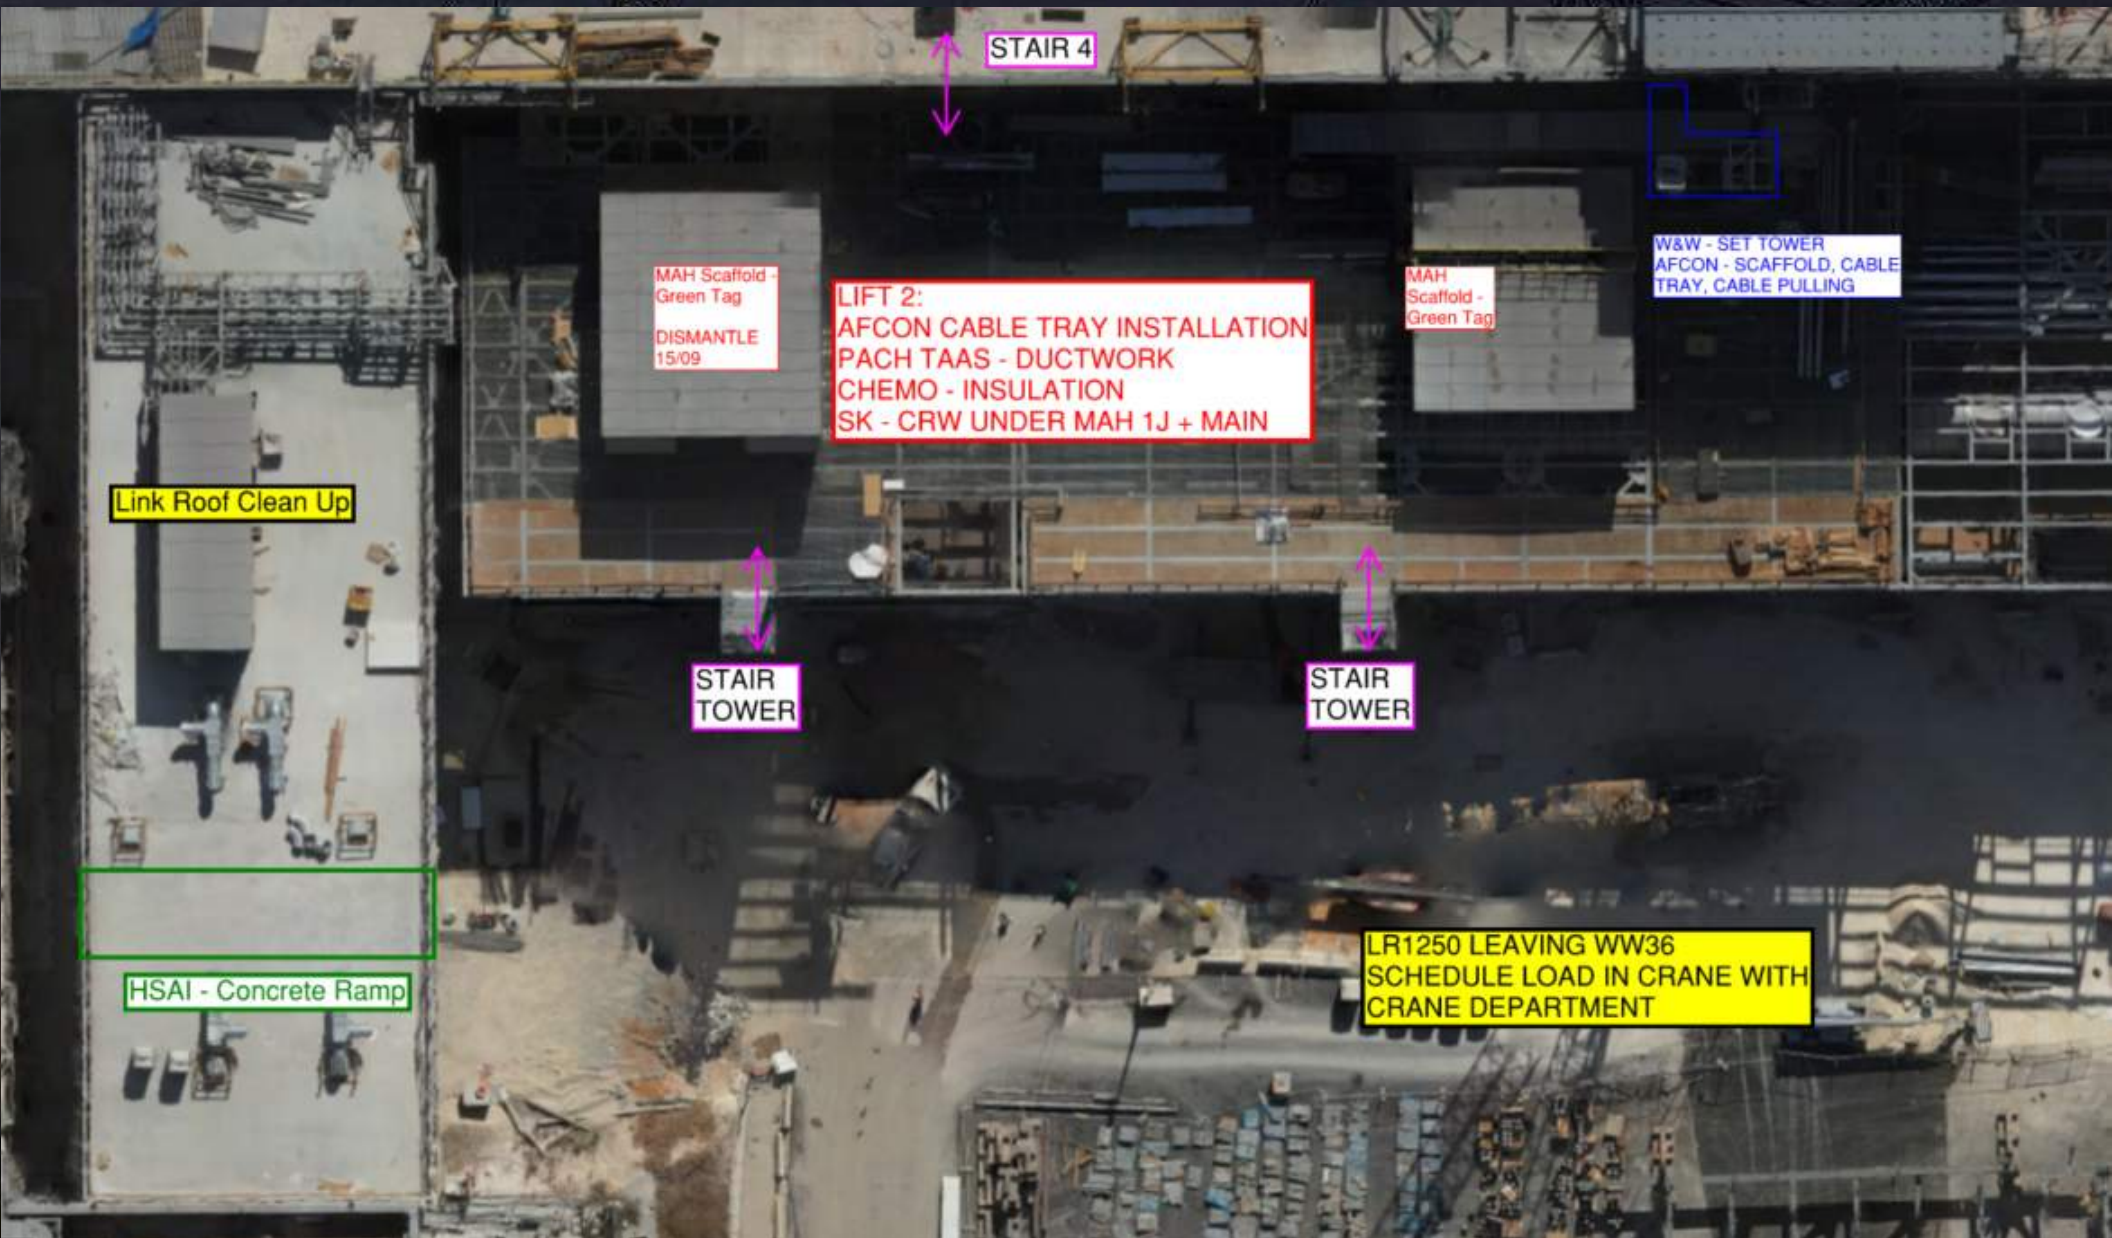



WJG 03J, 04J, 05J LIFT 2 & 3





WJG UTILITY LEVEL BUILD OUT

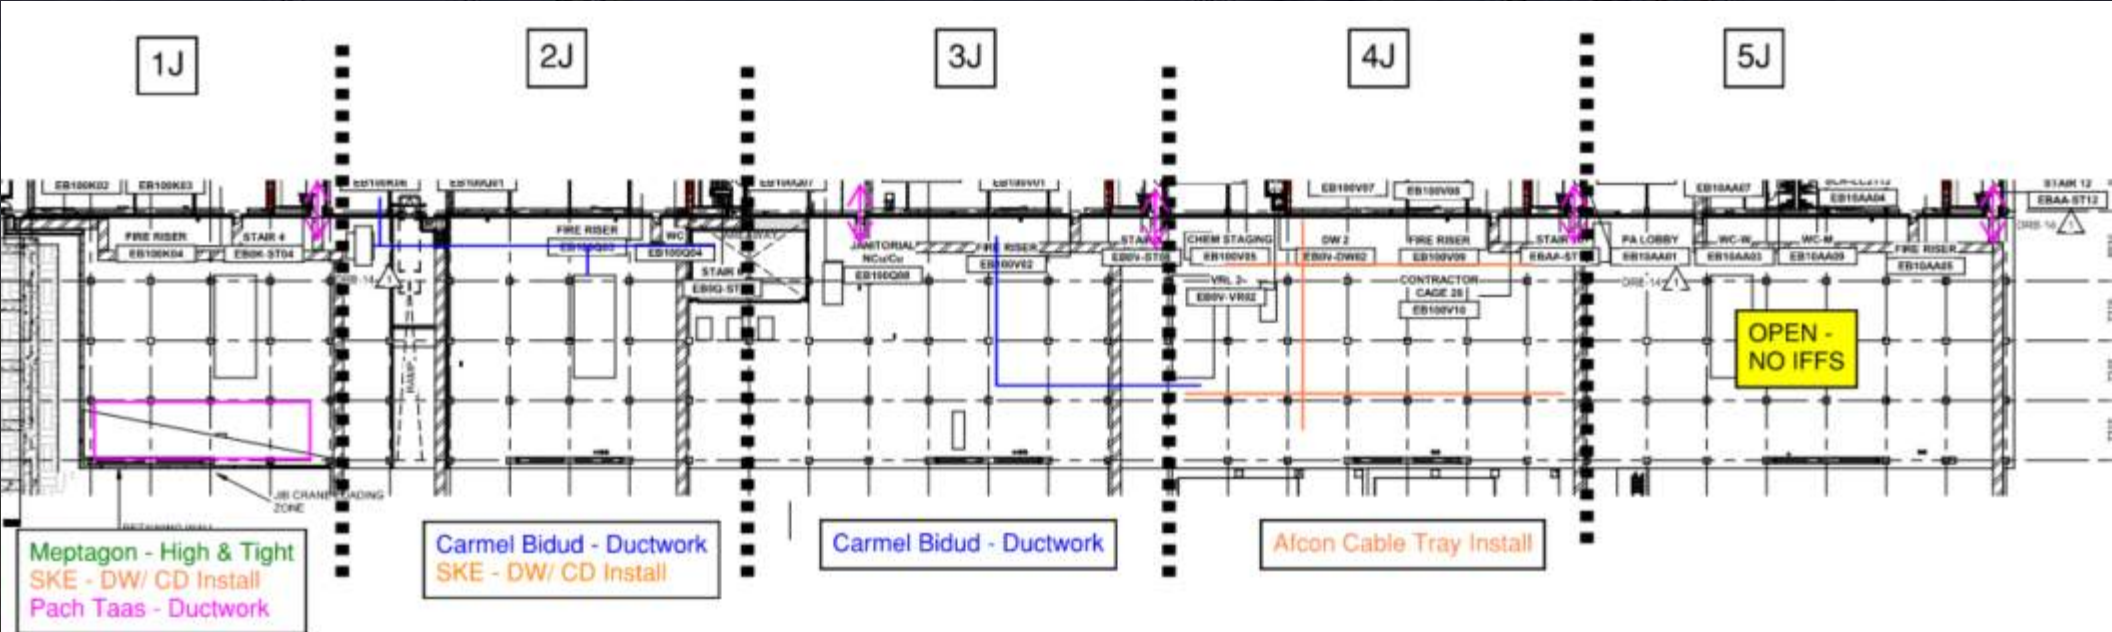


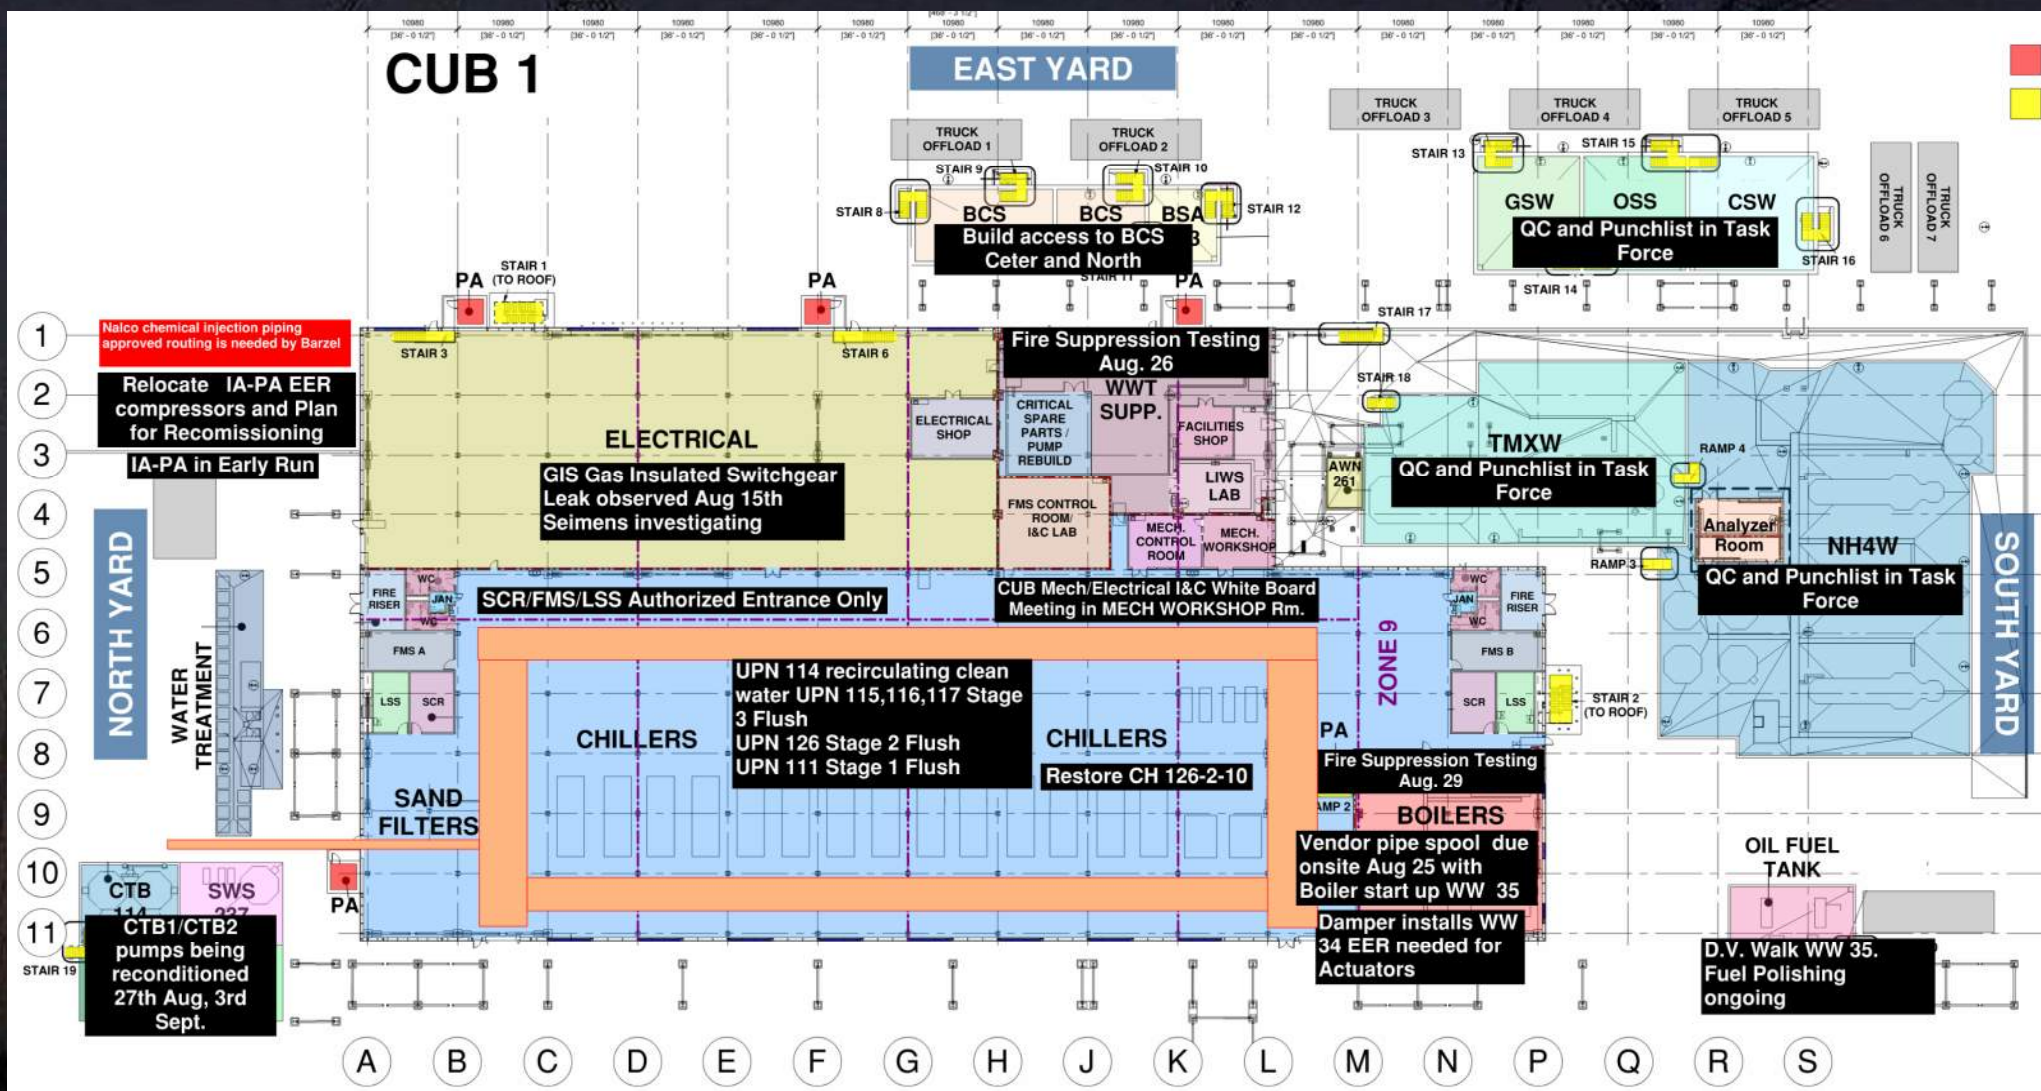

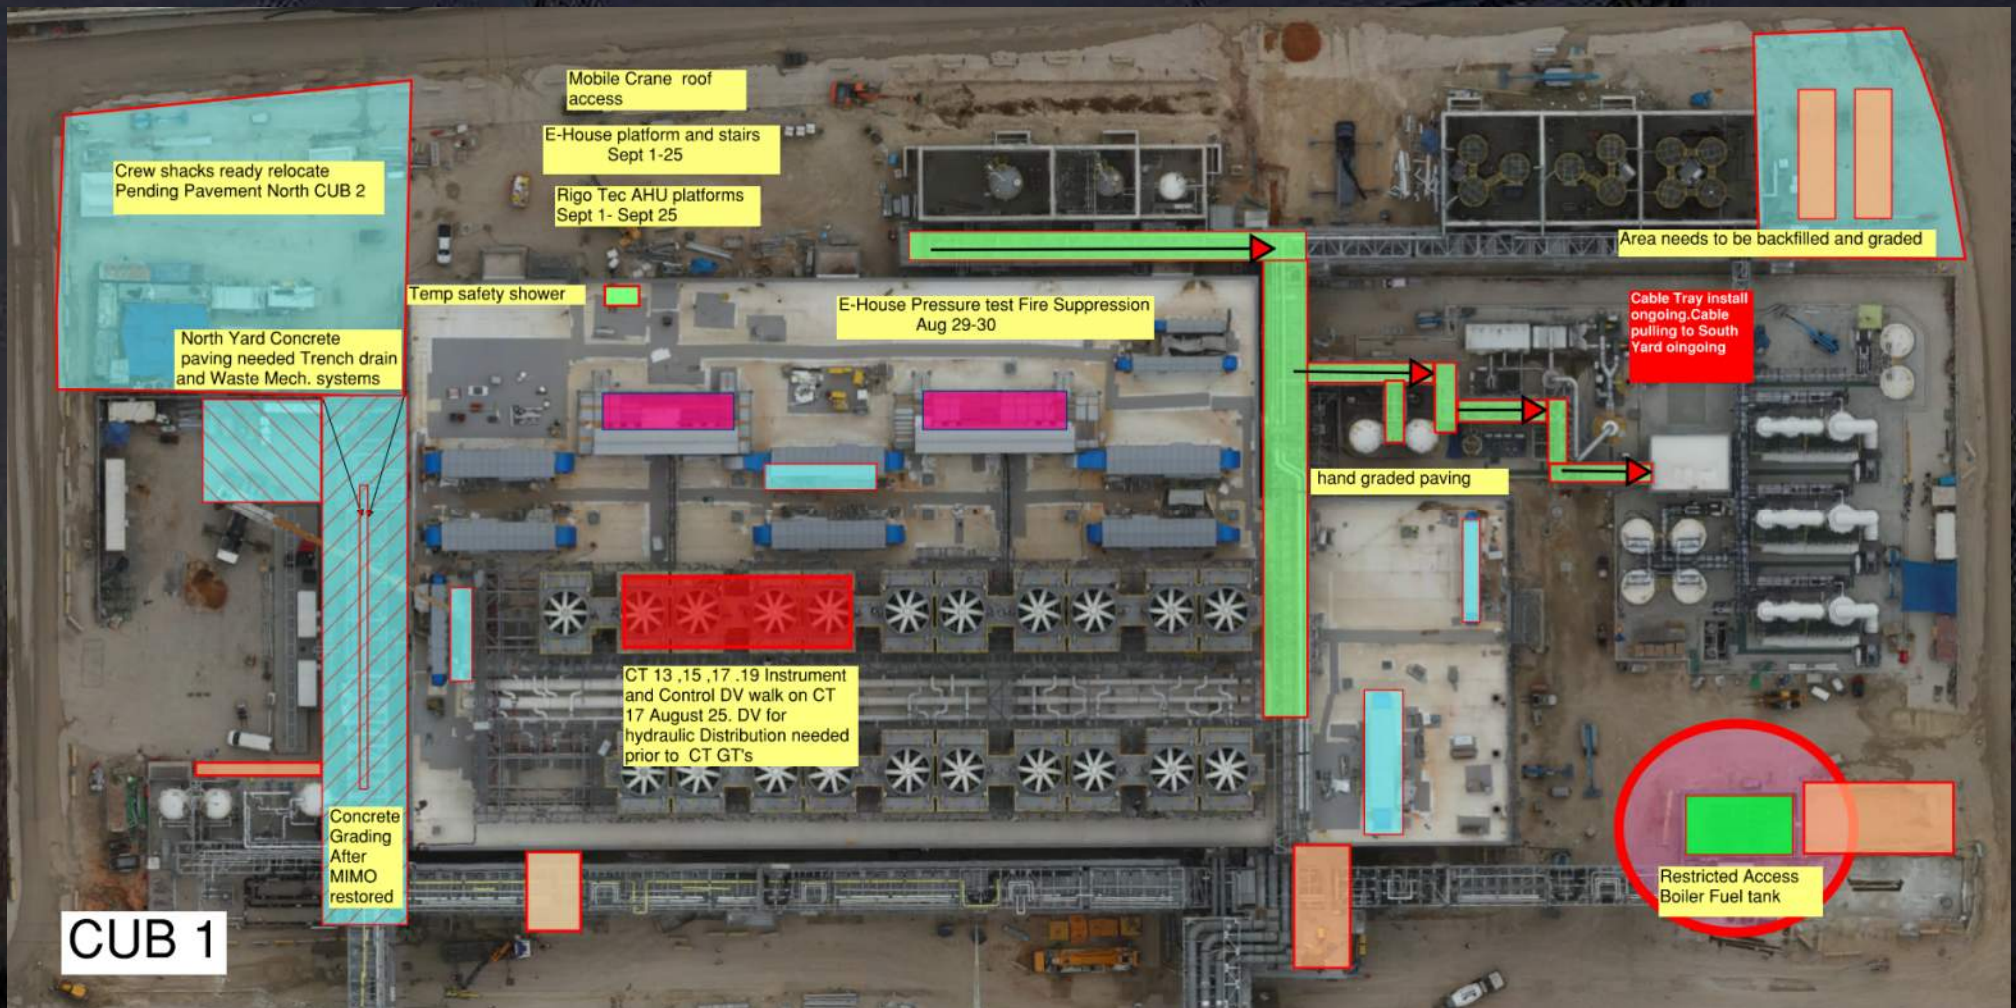

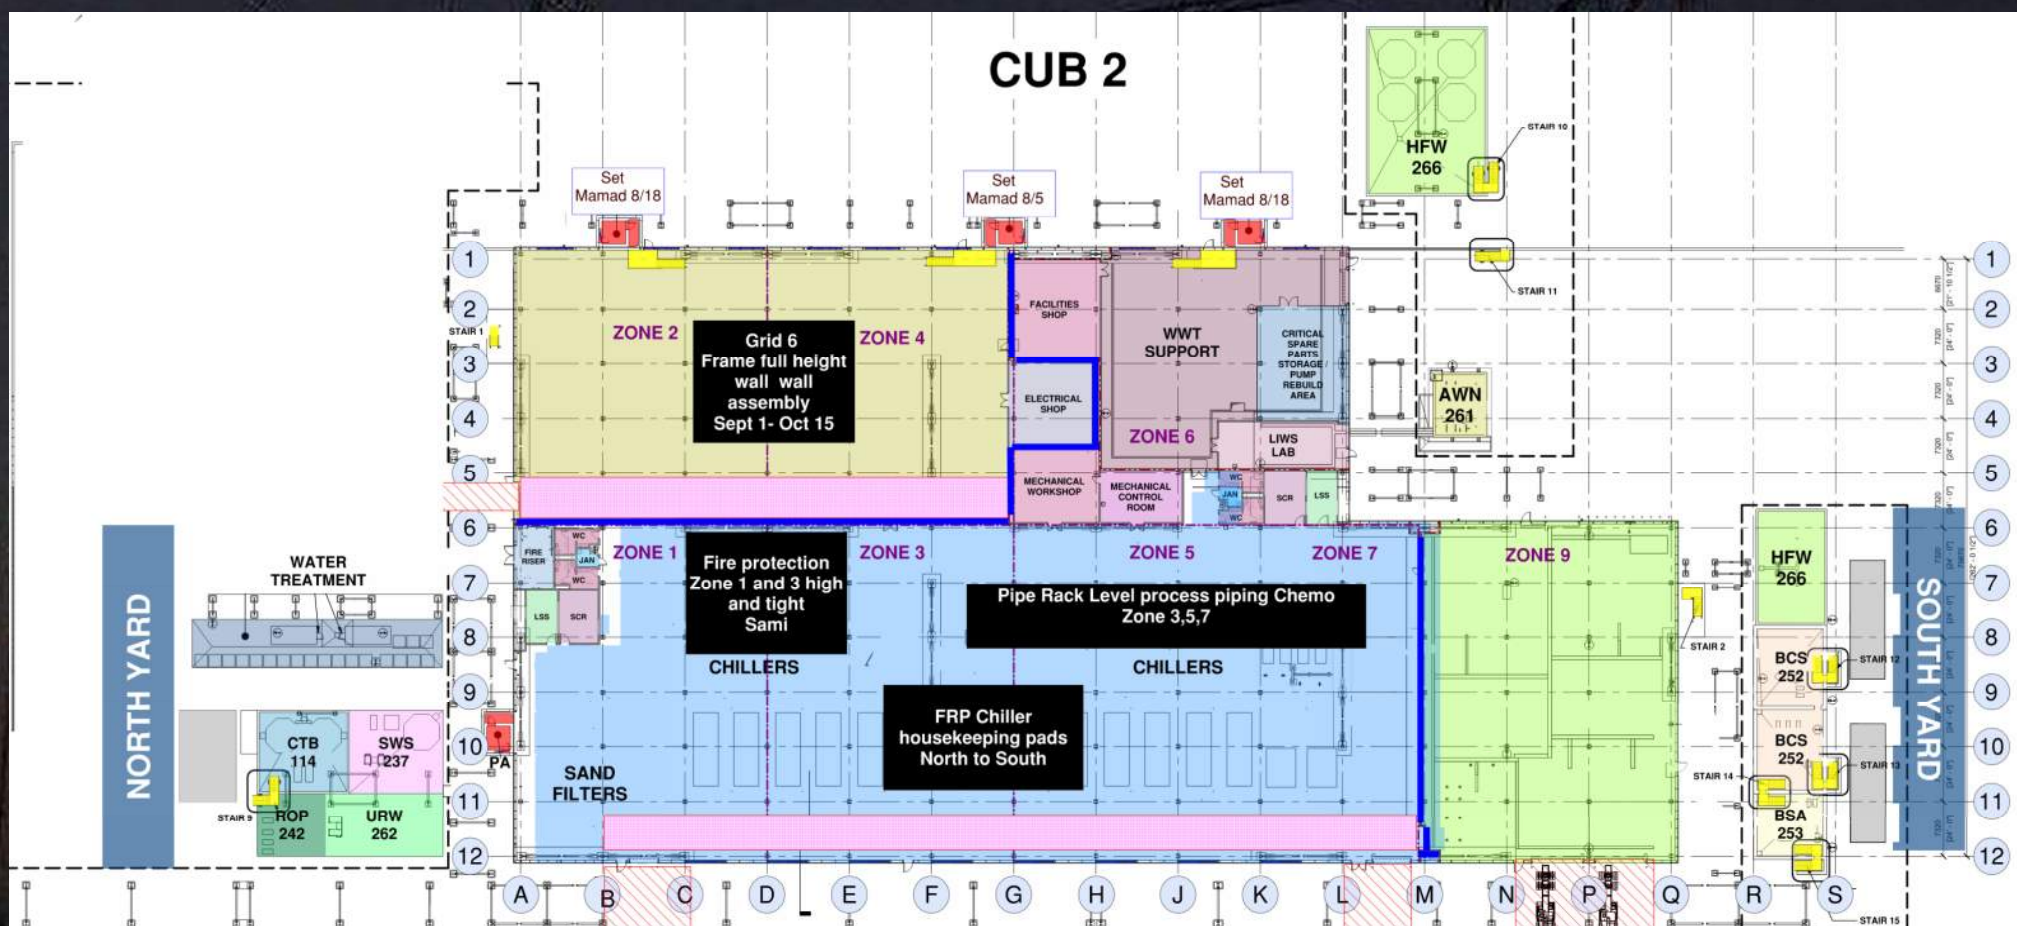

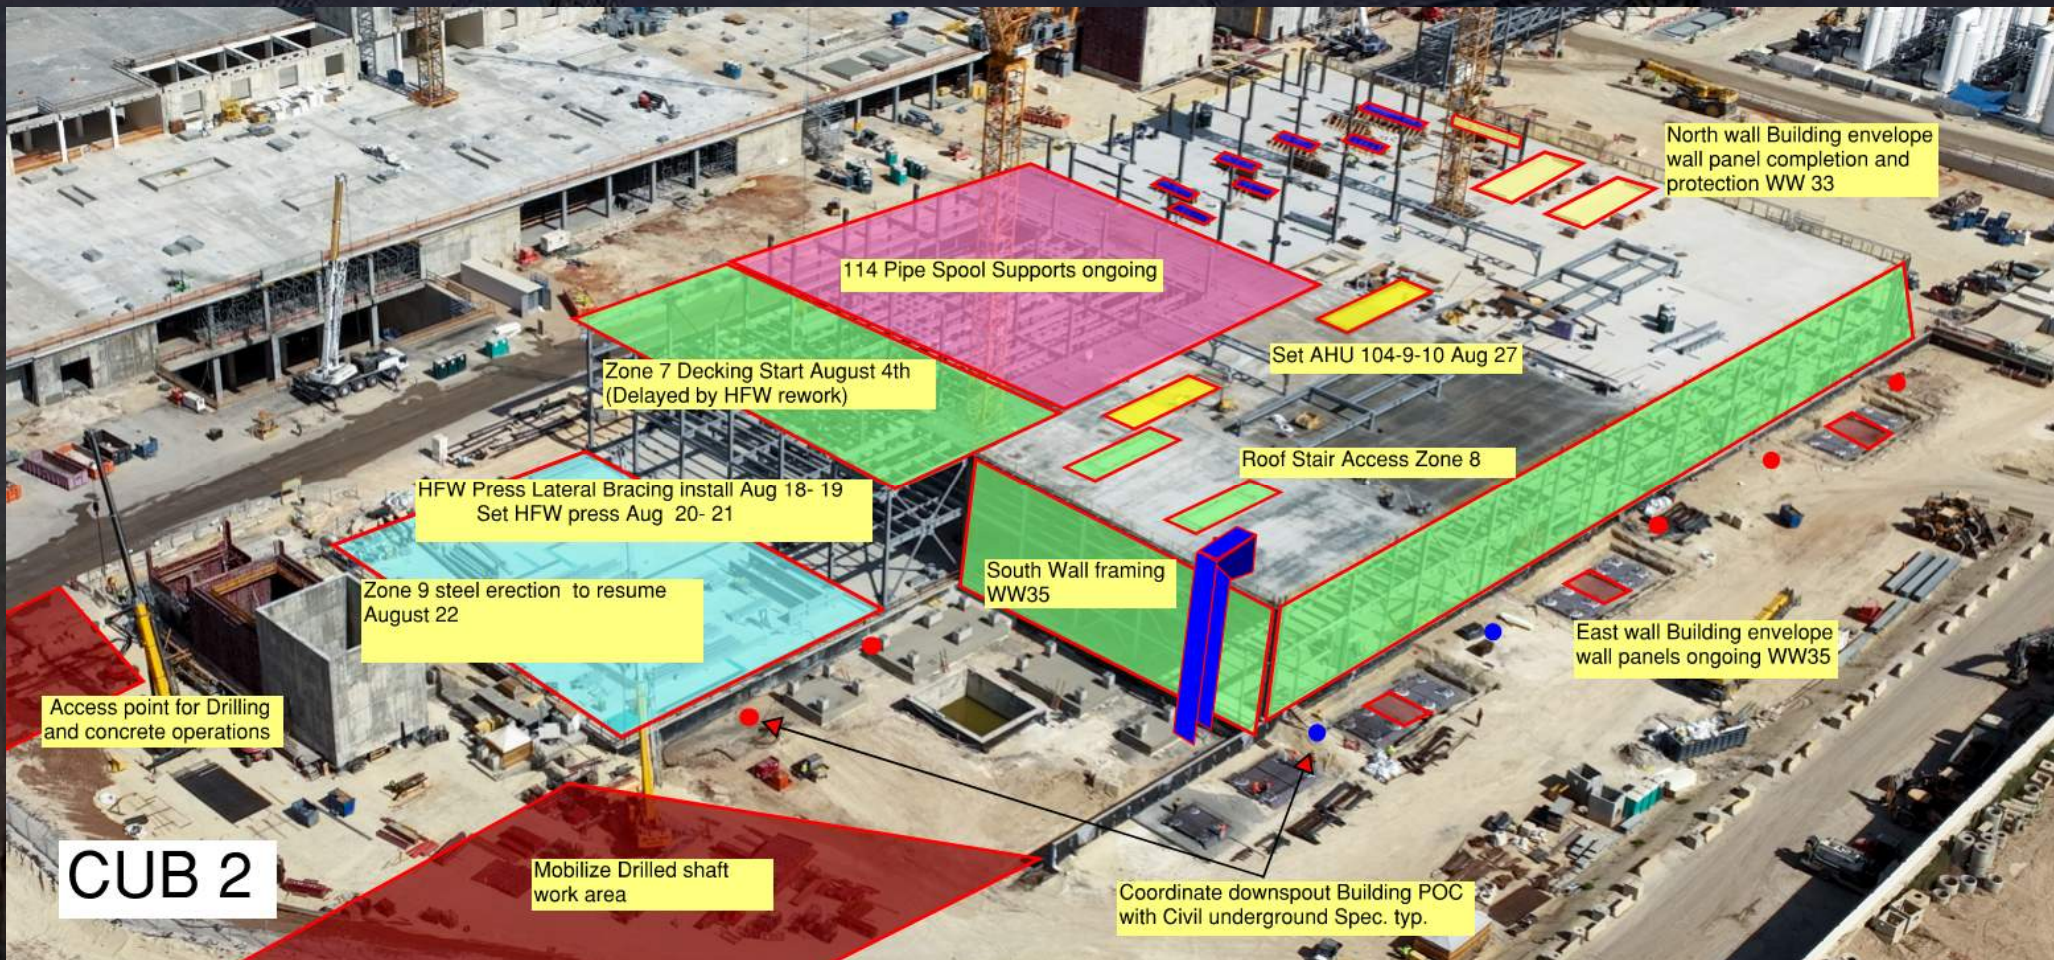

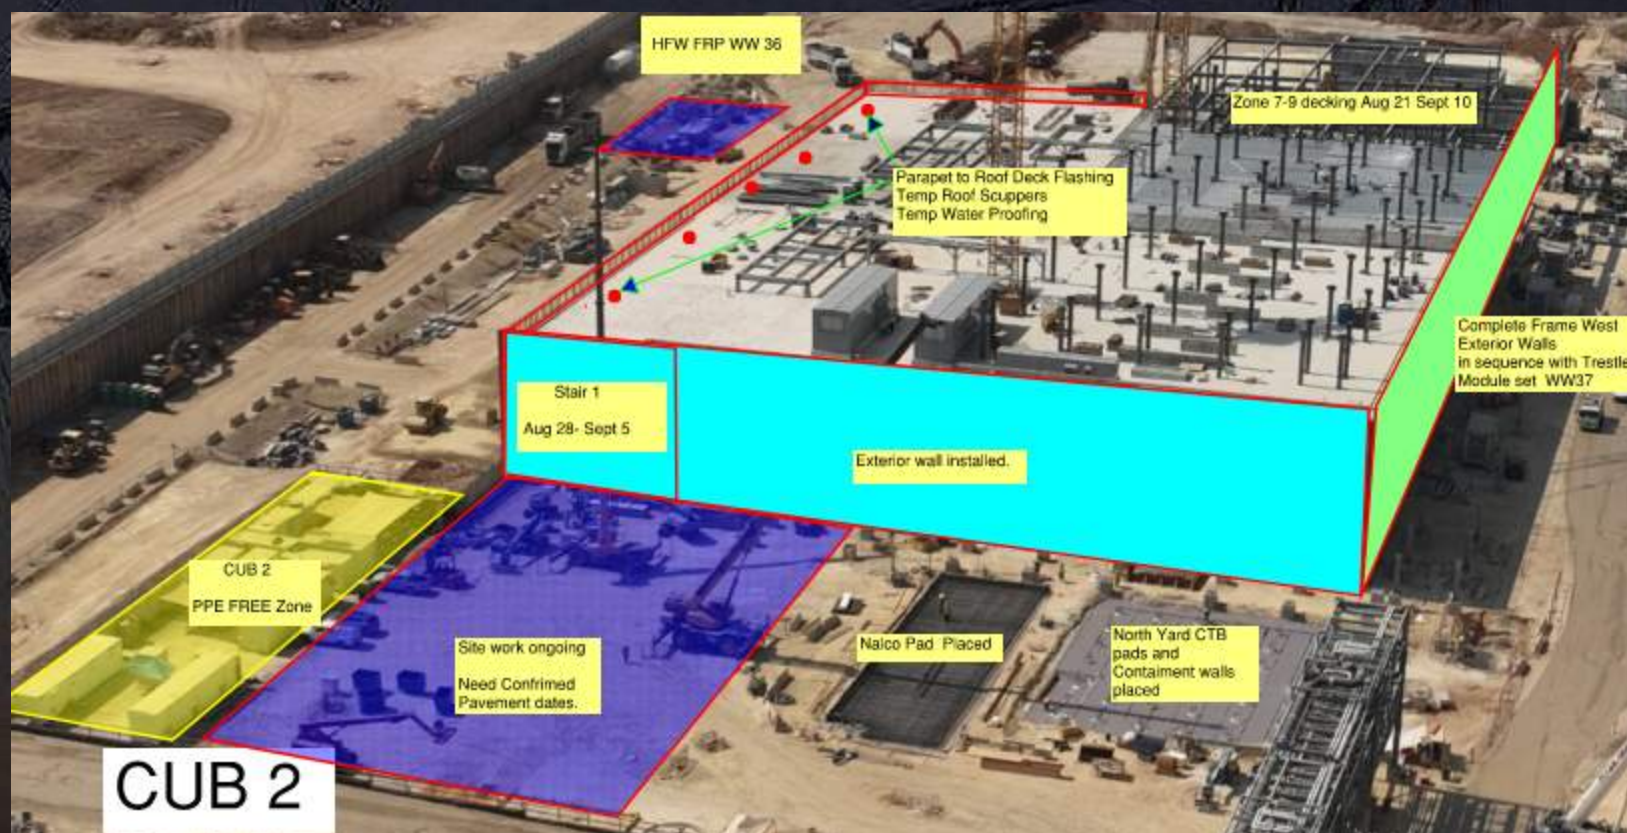

Elmor-
Z2- red valve - grounding
SES & AIS pulling&term control cables


Elctrosafe
pull control cables AIS,
SES, LVSS


NO ENTRY
HV ENERGIZED AREA

TMT Z 8 Soil replacement
-Excav by Vac truck &
Backhoe, chipping rocks by
hand . curb stone works

JS- south SES
remove temp fence

TMT all site
clean & seal
sewage manholes

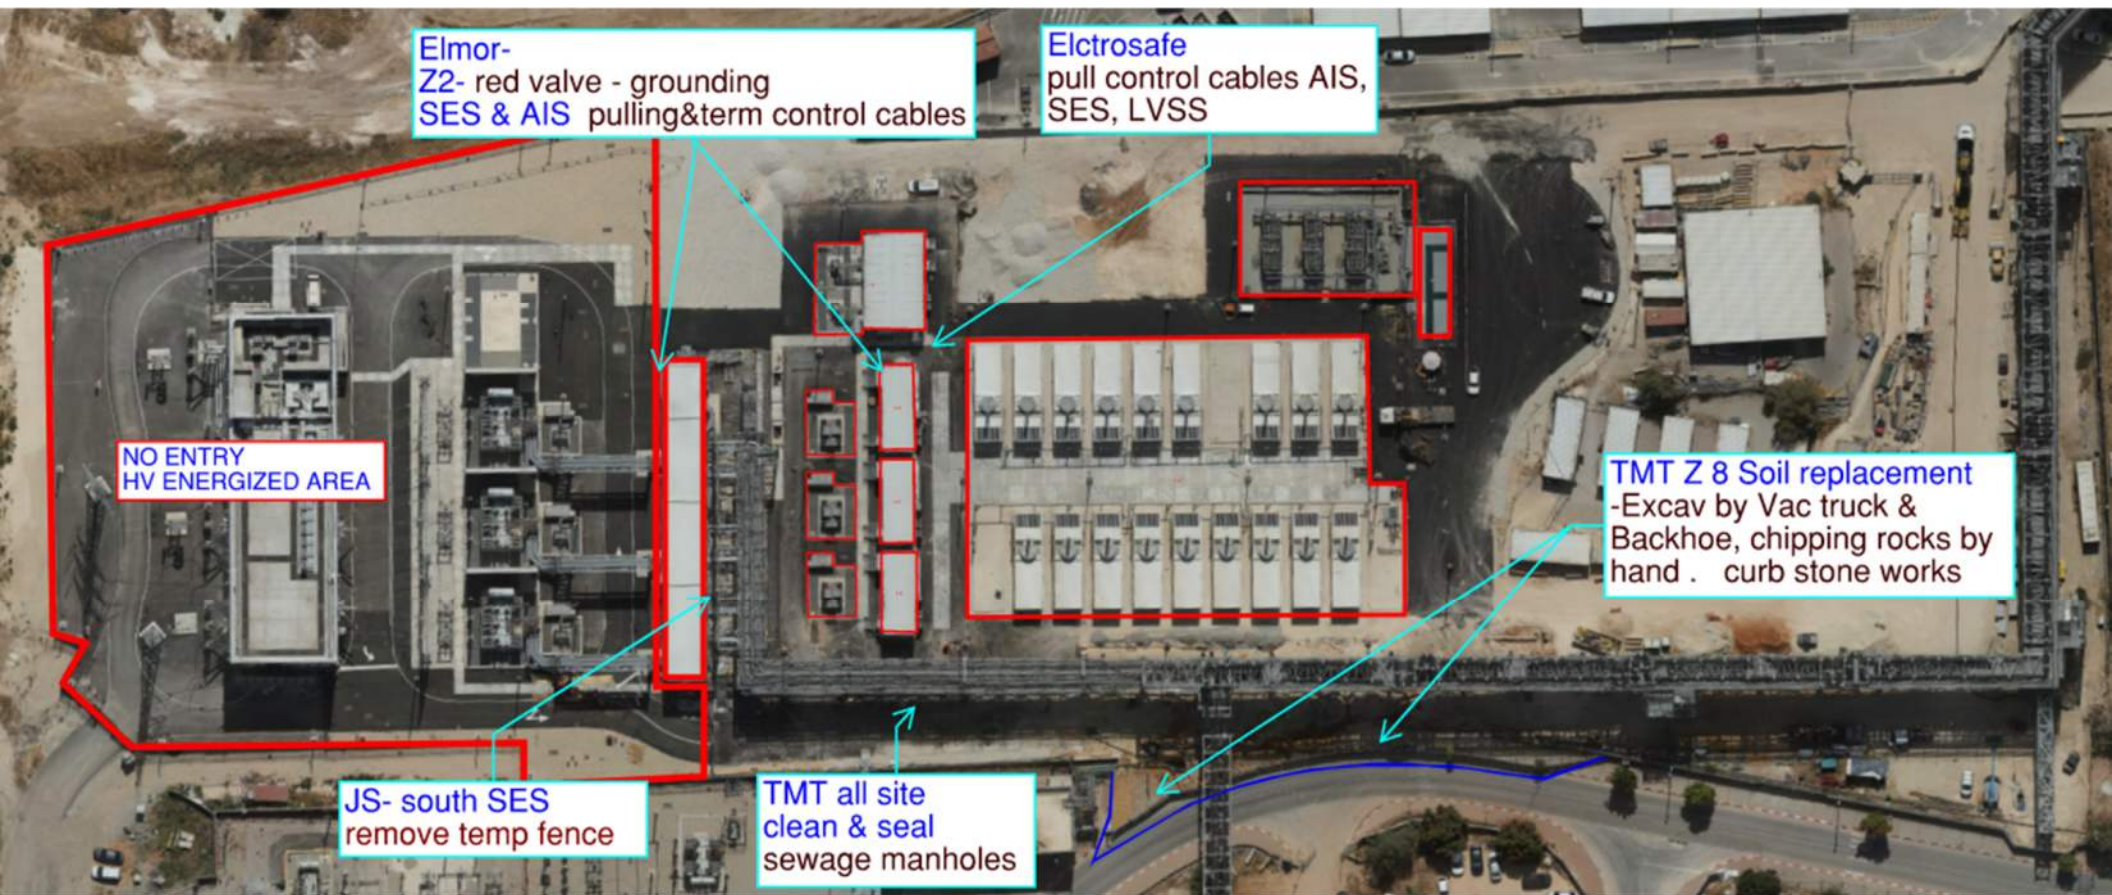

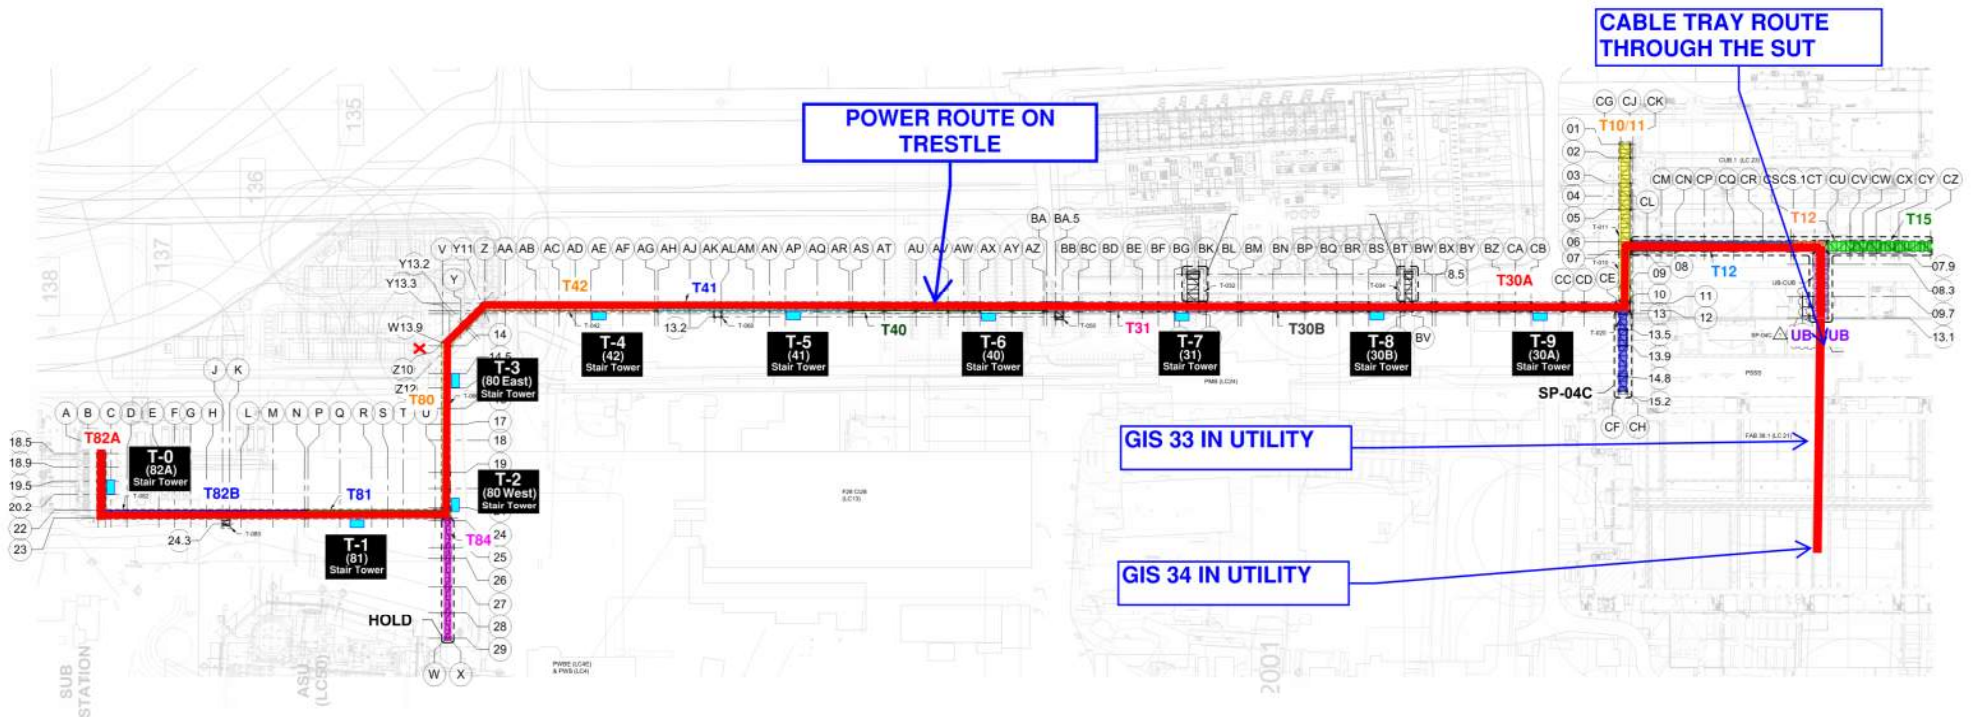





HOFFMAN CONSTRUCTION COMPANY



Trestle Lesico NDT-10", 7 welds 28/08/24

22:00-05:00

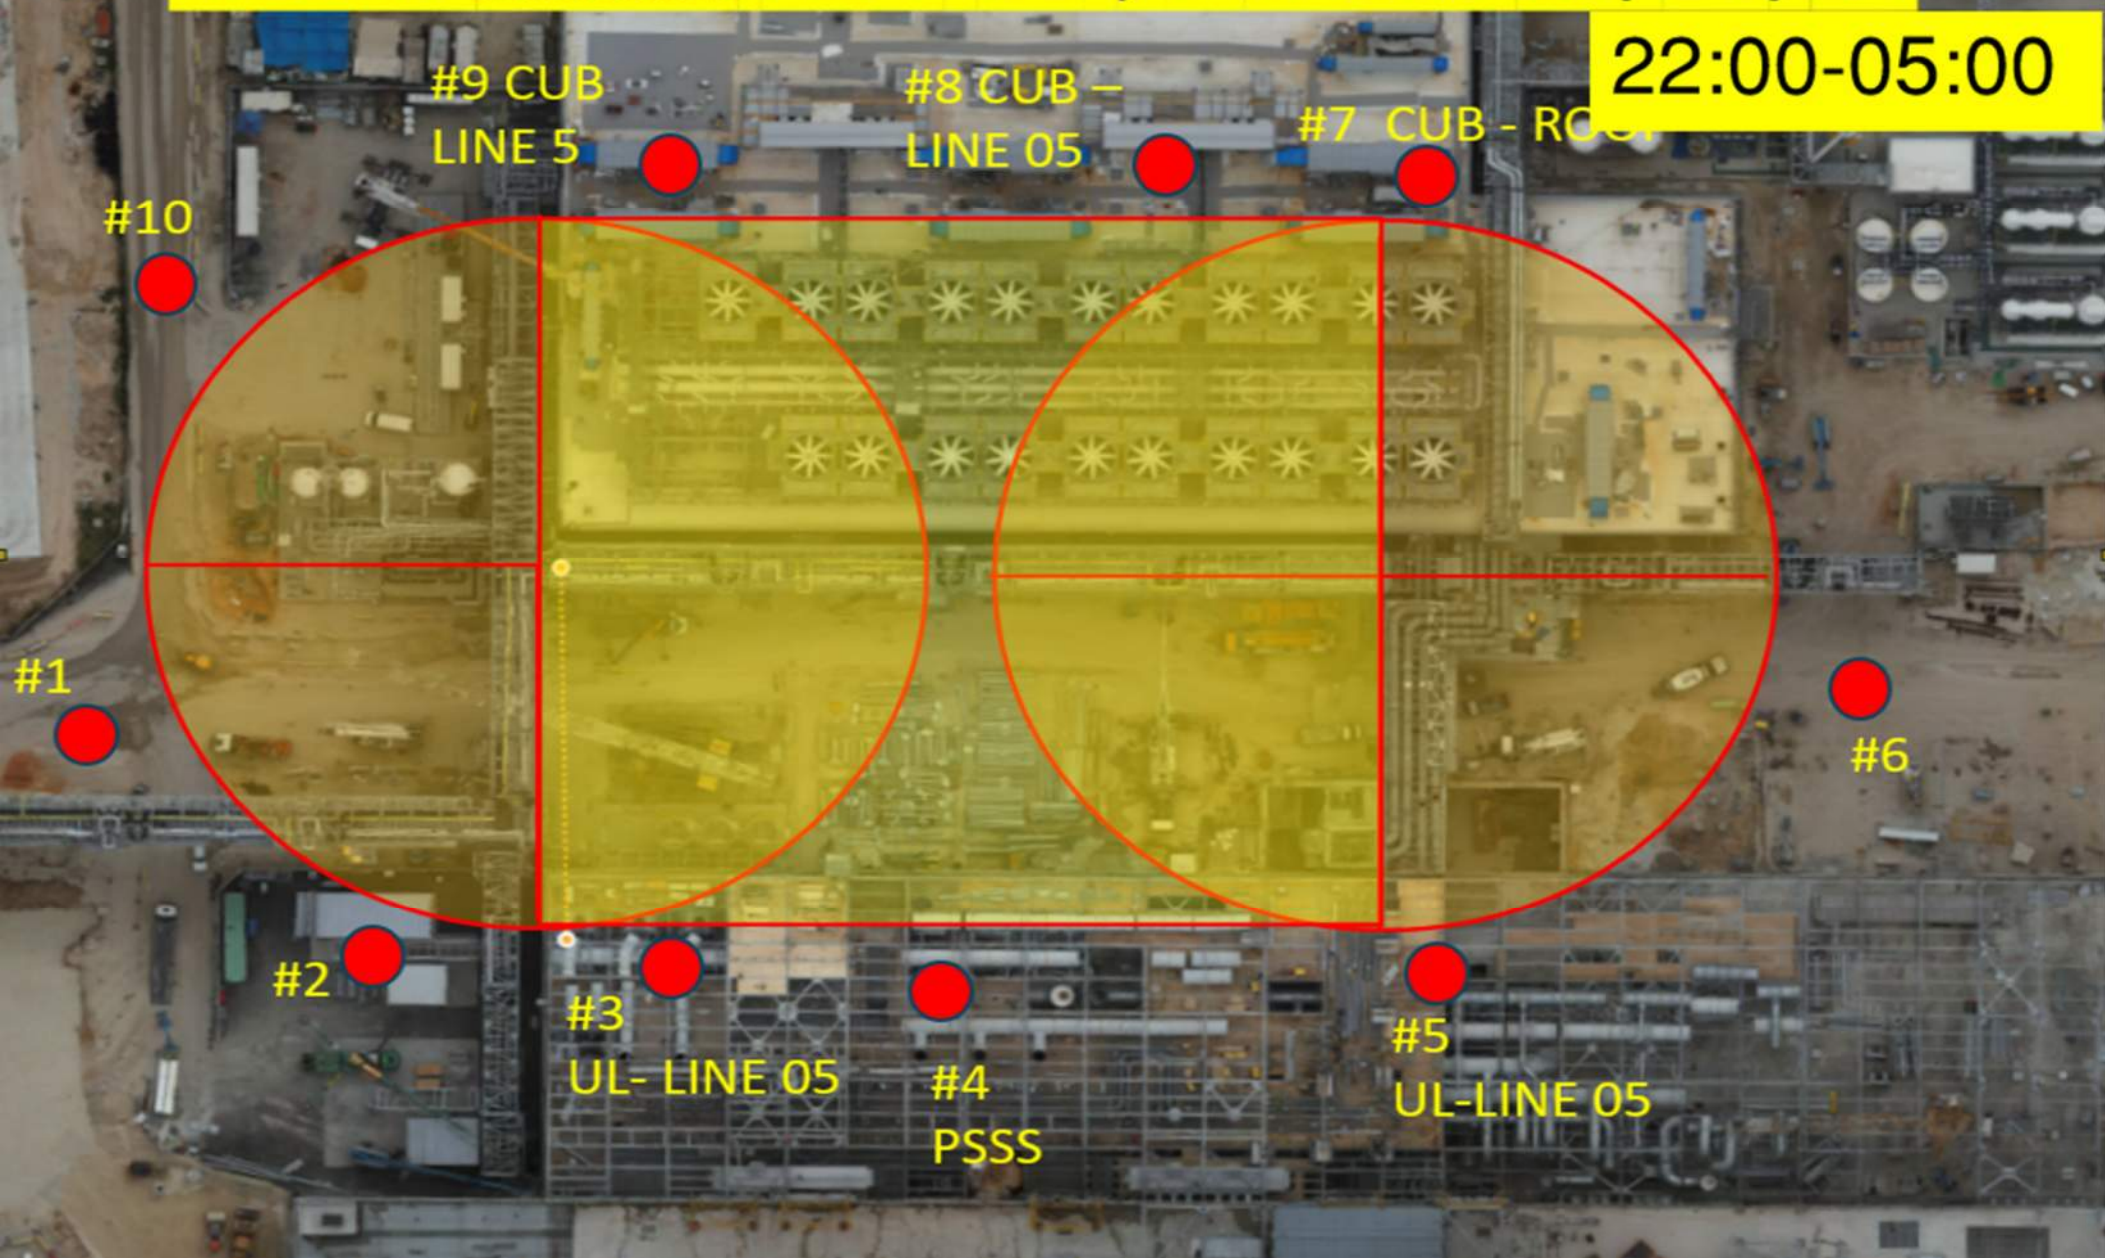




HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

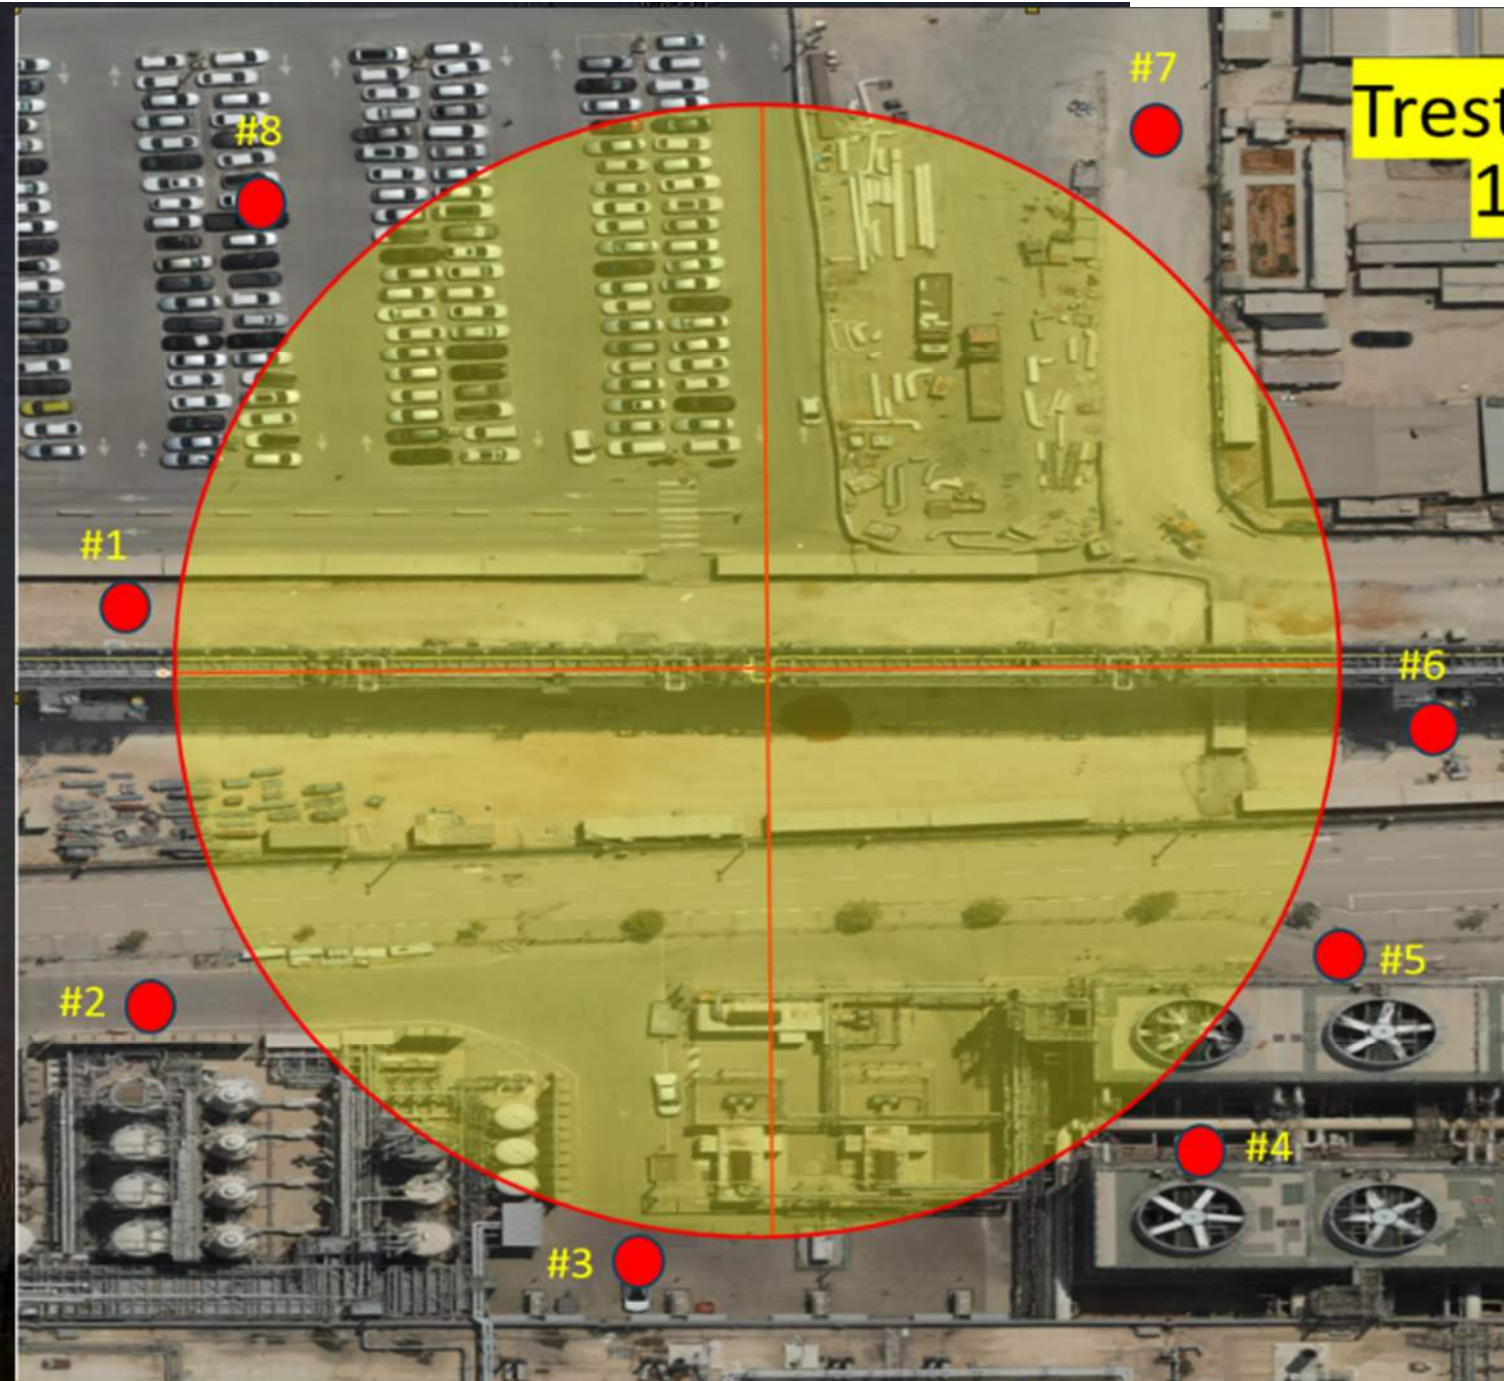

**Trestle Lesico NDT-
12", 2 welds**

29/08/24

22:00-05:00




HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

Trestle Lesico NDT-10"-8" 7 welds 29/08/24


22:00-05:00

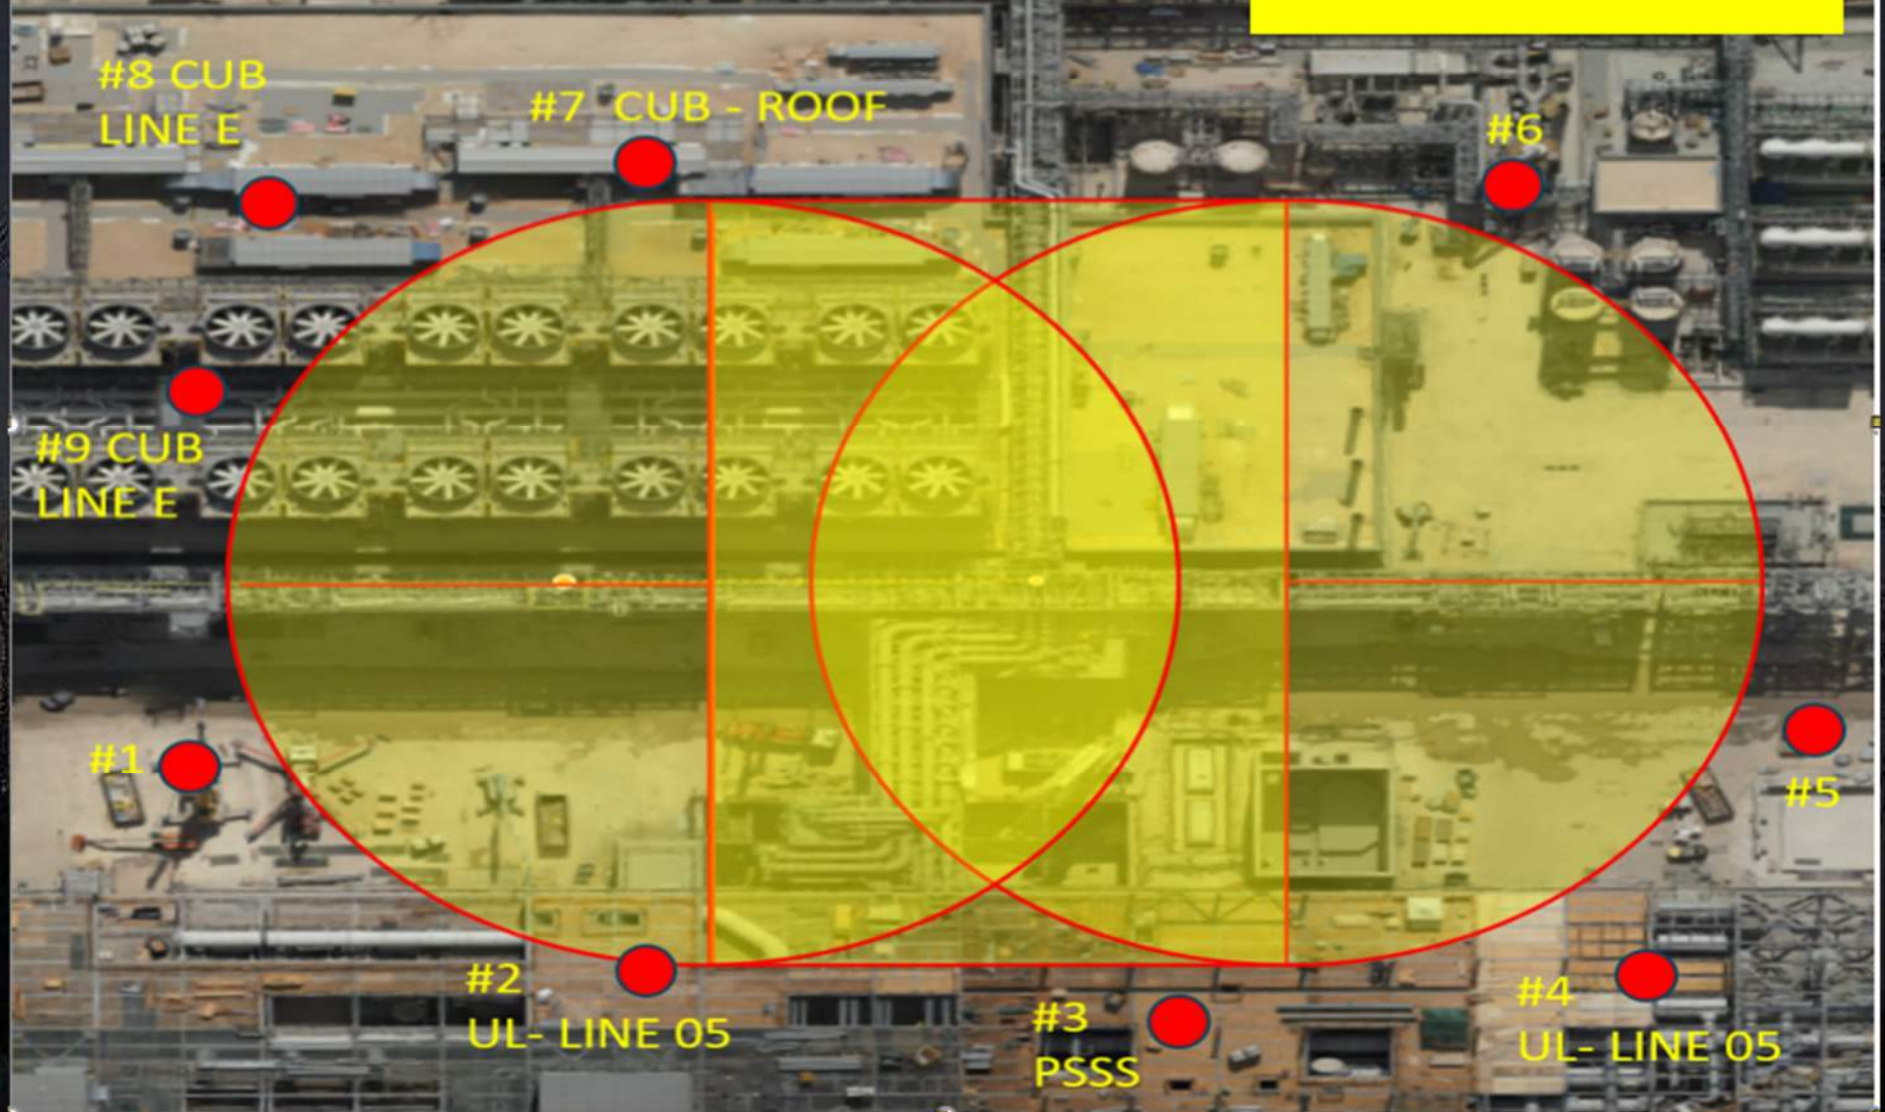


Lesico 12" natural gas pipe pressure test exclusion zone

Wednesday, September 4th 18:00 -Thursday, September 5th 01:00

All access to vehicles within exclusion zone will cut off at 17:50

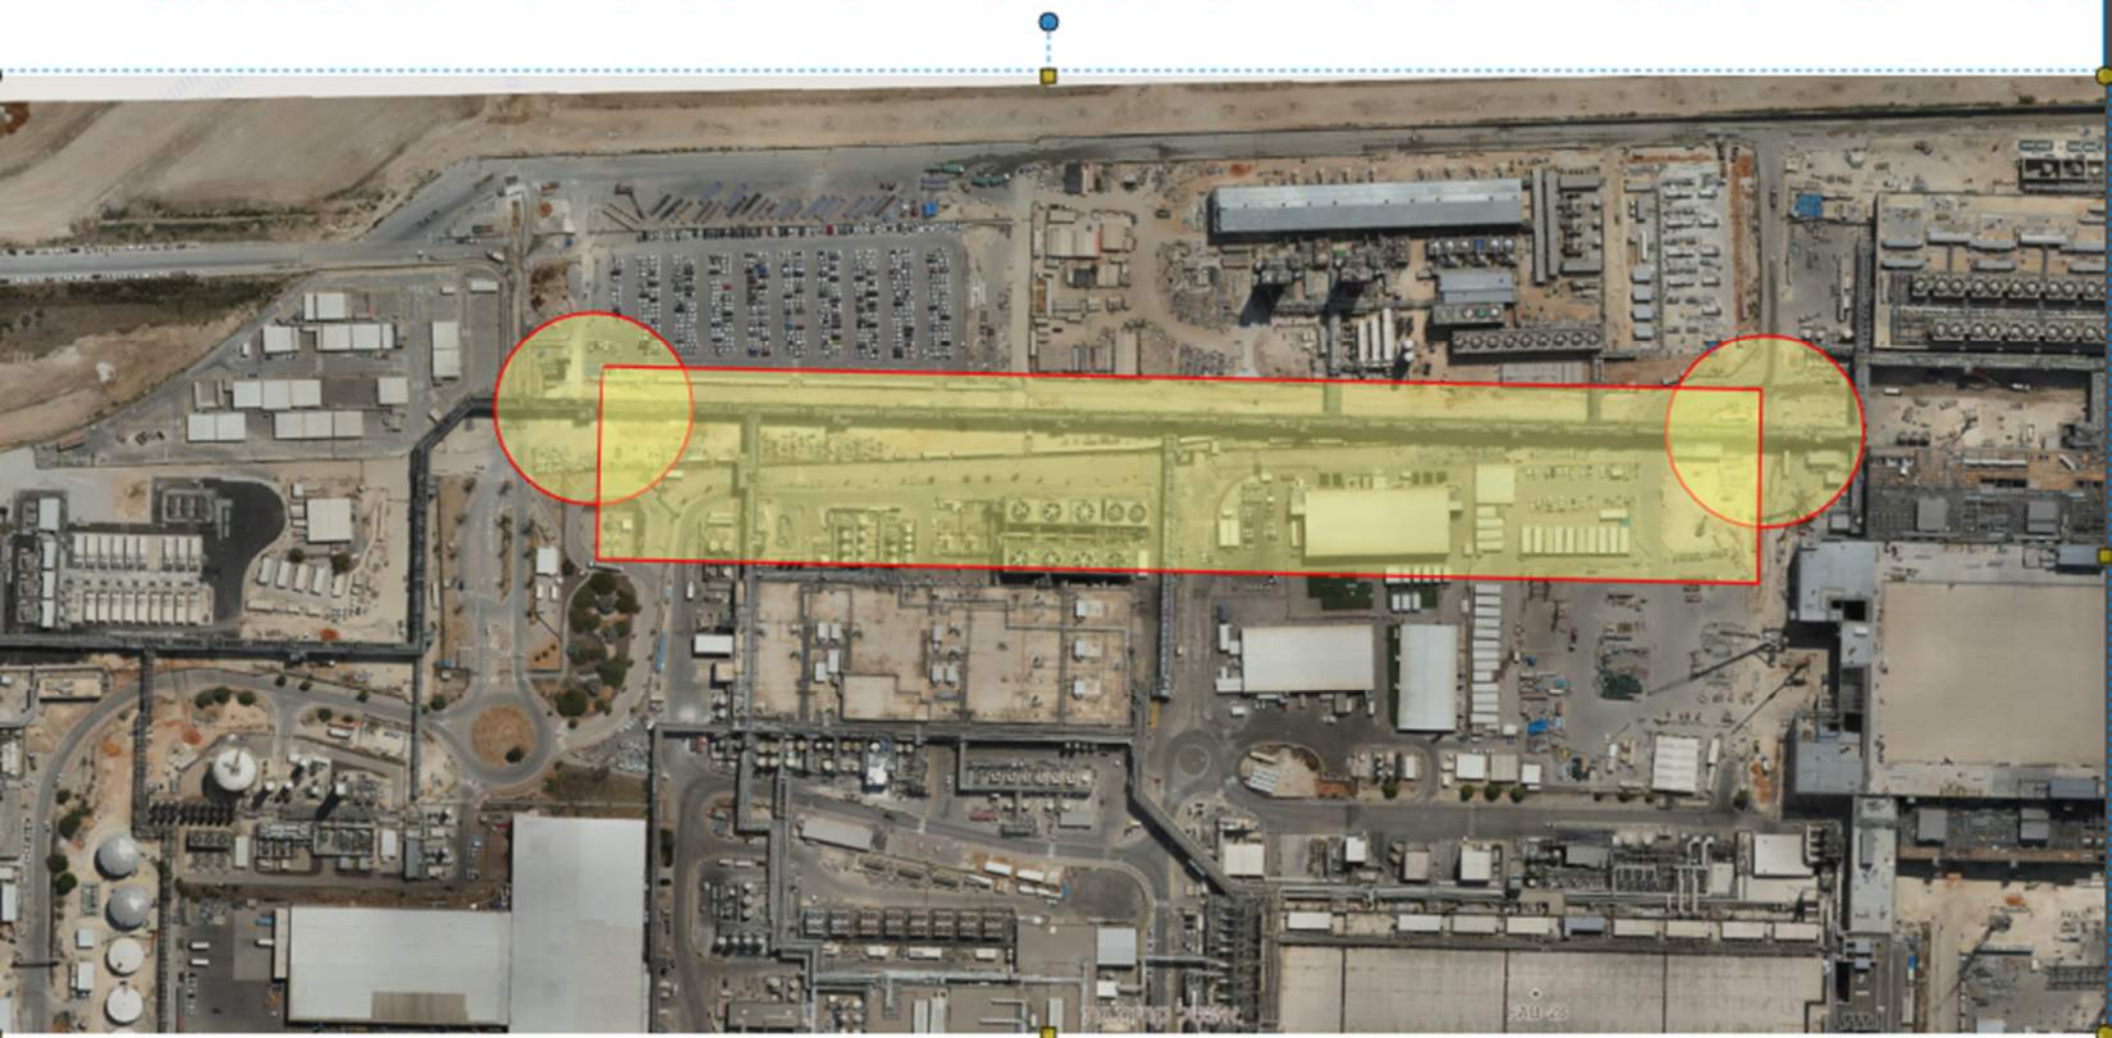



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

BGC VACUM TANKS AREA

Area out of BGC site will be marked with
YELLOW stripe.

And 2 spotters will be posted!!(yellow)


Starting –Sunday night September 1st at 22:00


Finish on Monday Sep 2nd at 05:00am.

Safety spotter



Safety spotter

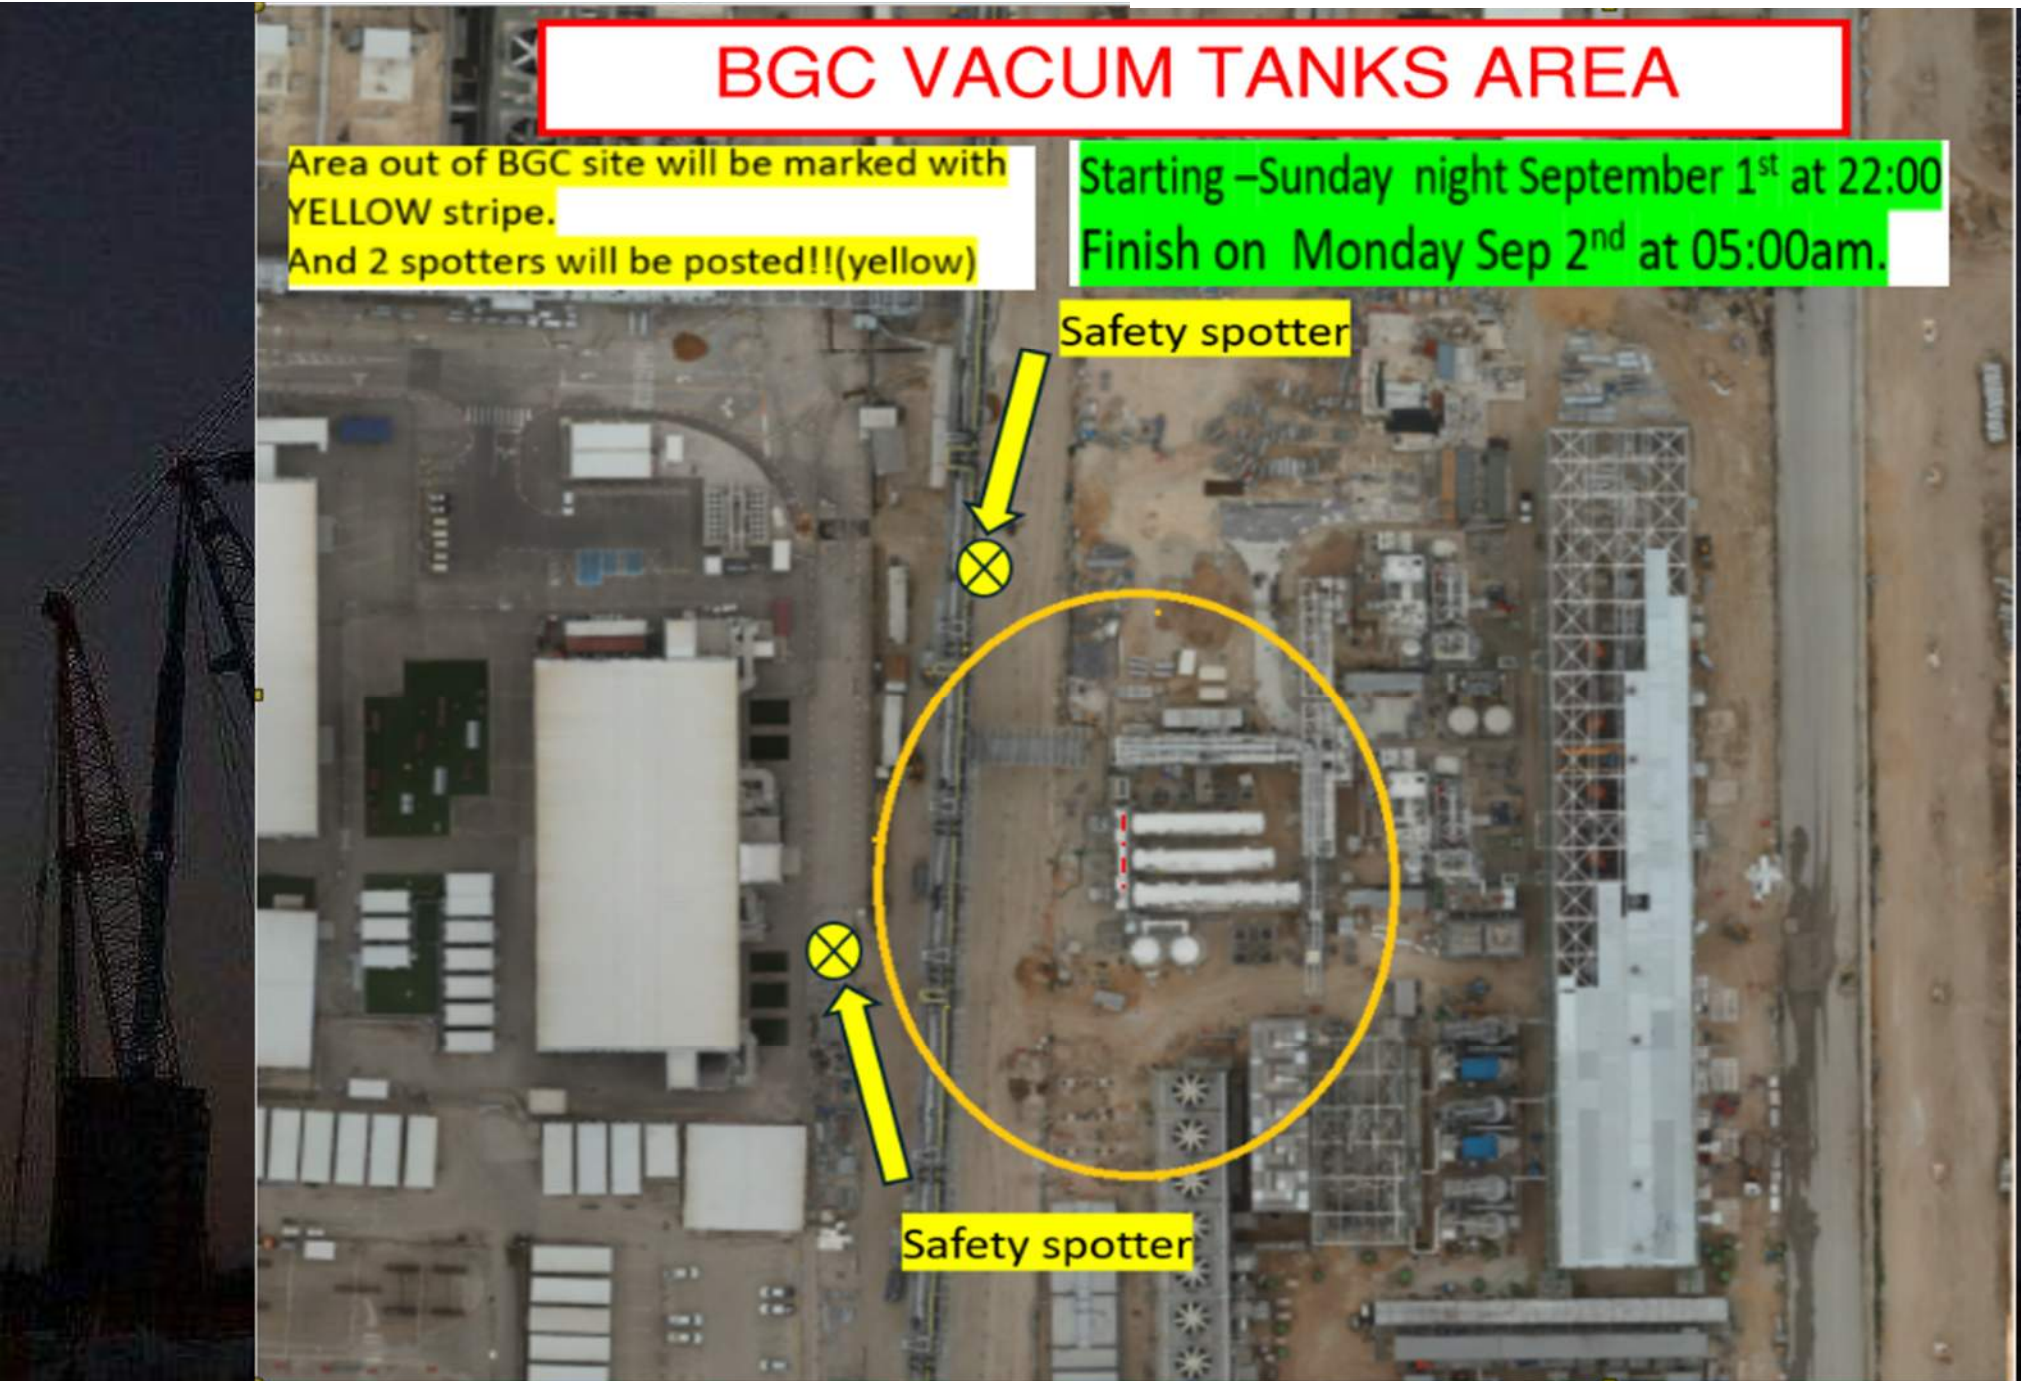

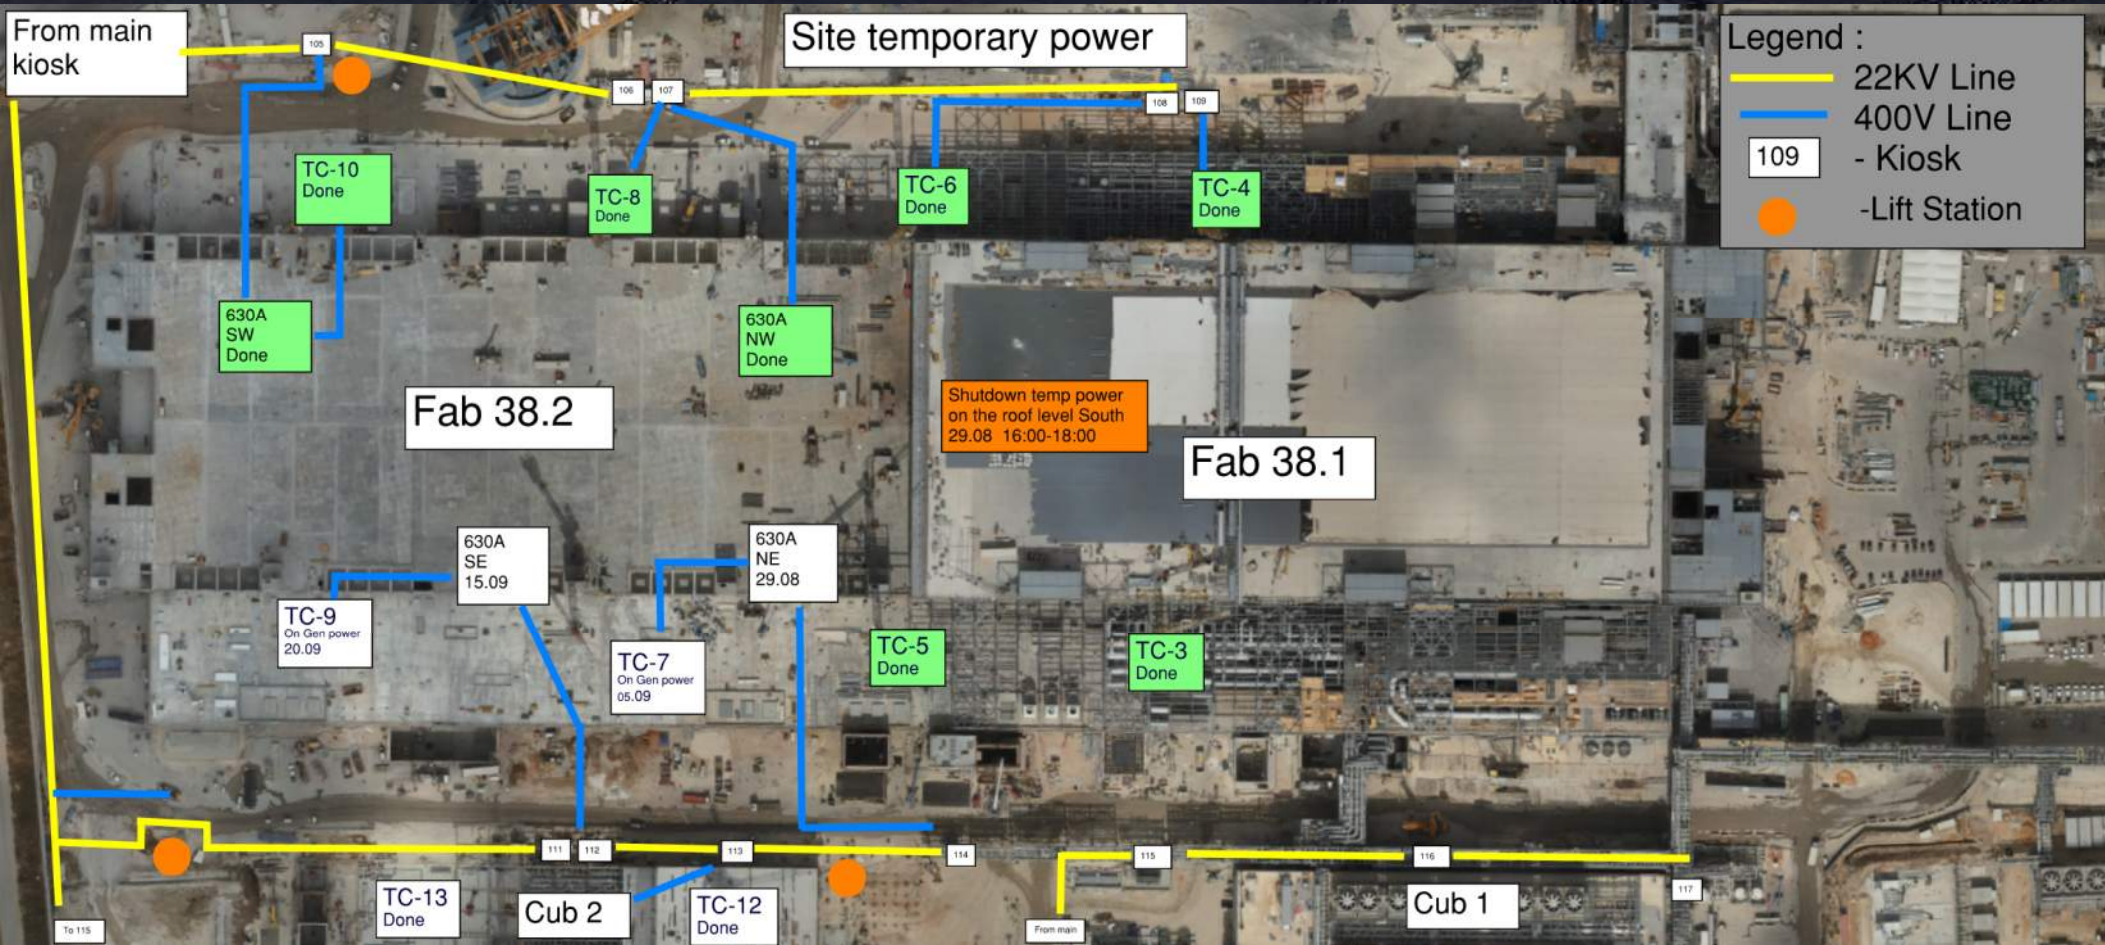



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Gate B





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

Road 33 CLOSED – 1700 on 29-Aug to 0700 on 1-Sept

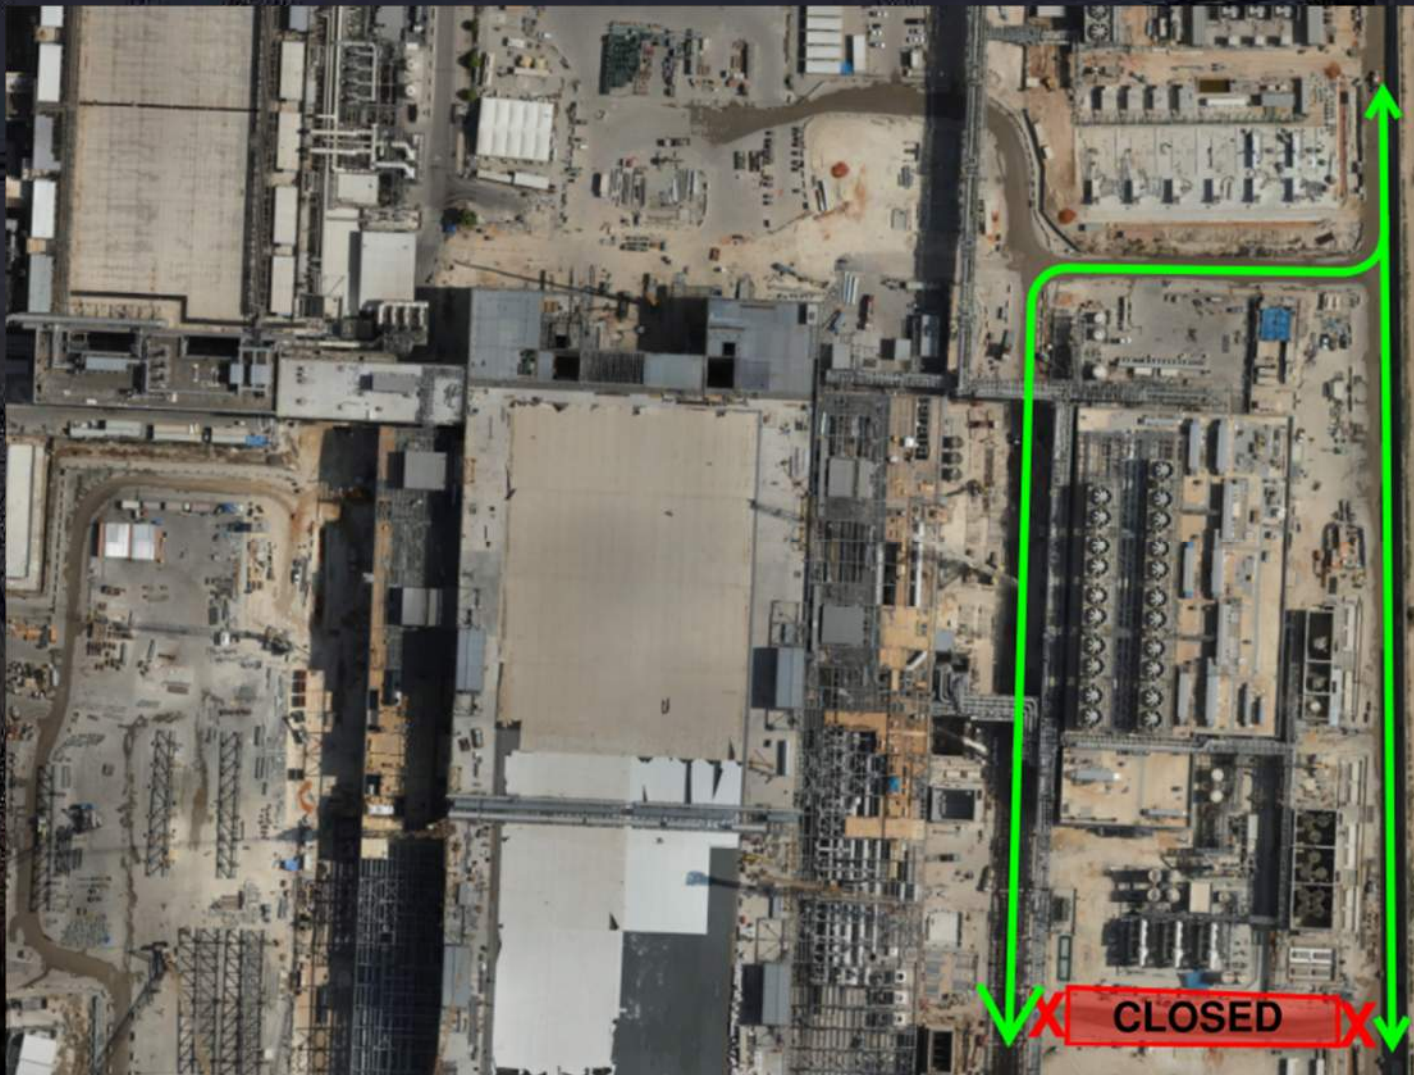



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South





Daily Coordination Meeting

Site Logistics

Cleanup: Subcontractor shall always keep the project free from the accumulation of waste materials caused by its employees, Subcontractor's employees, or Work on the project. Subcontractor shall continually and thoroughly cleanup and remove from jobsite, at its sole expense, all waste, debris, surplus equipment and surplus materials resulting from Subcontractor's operations. If Subcontractor fails to clean up such waste, debris, surplus materials and surplus equipment, such clean up and removal will be done by others and costs for this work will be deducted from the Subcontract by Contractor.





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

Site Cleanup







Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

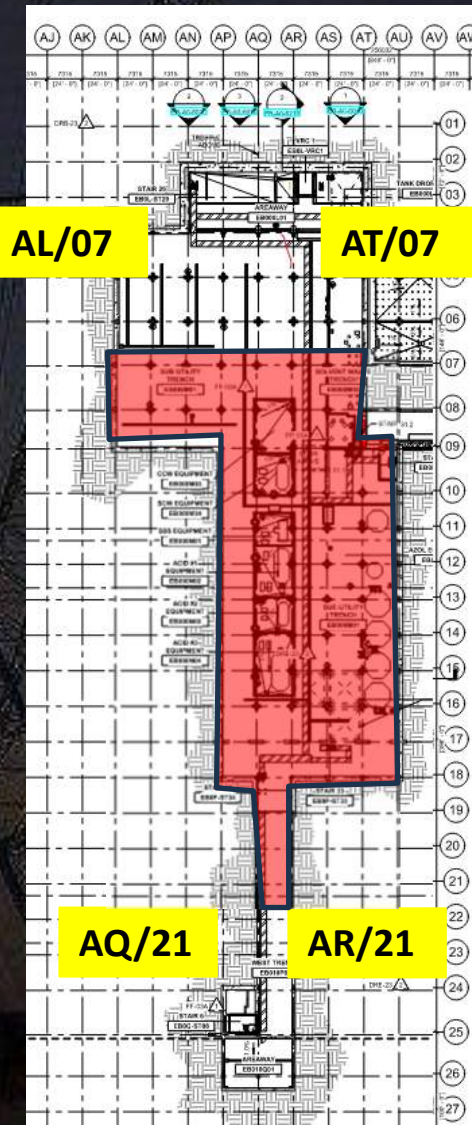

SUT2

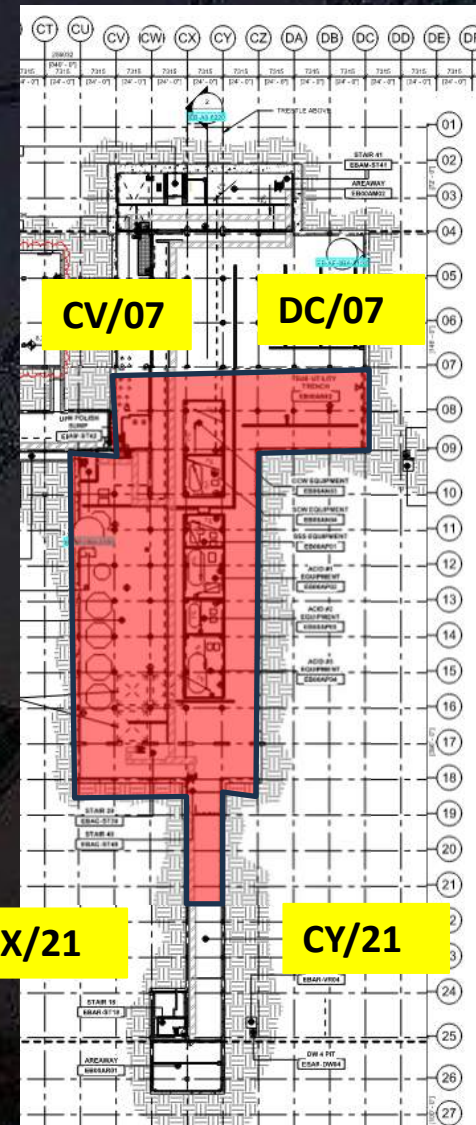





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics - Protected Areas (Utility Level)

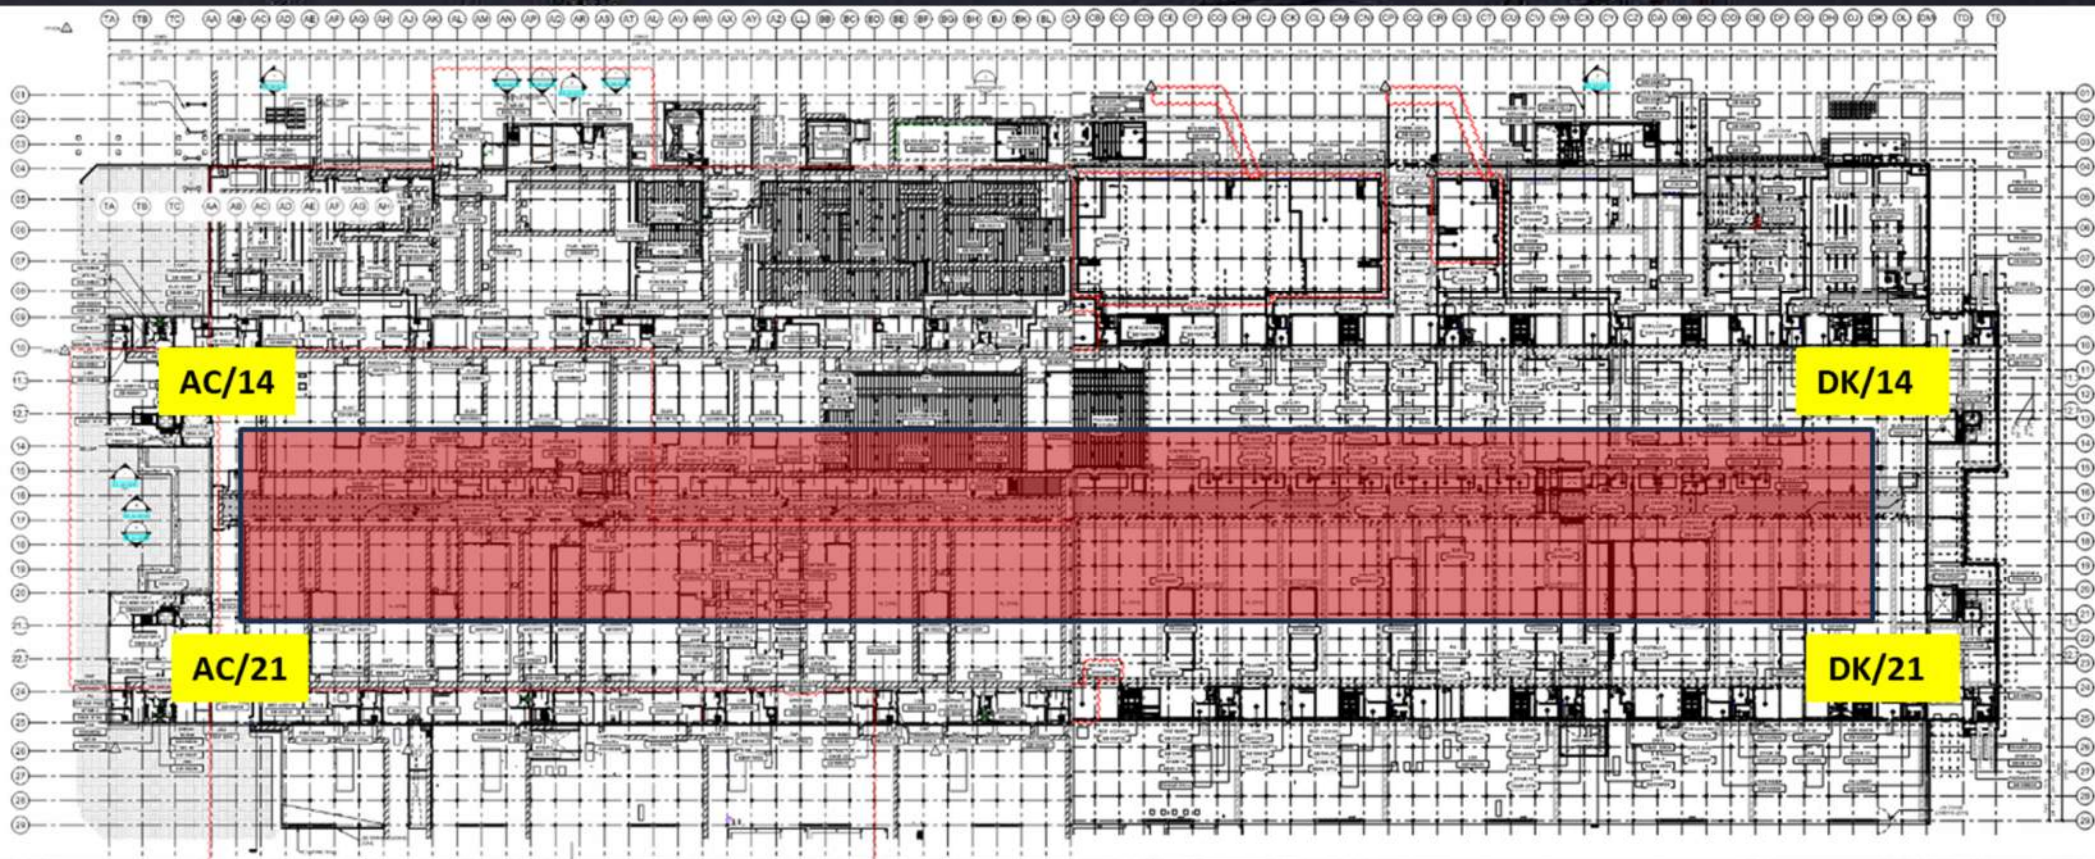

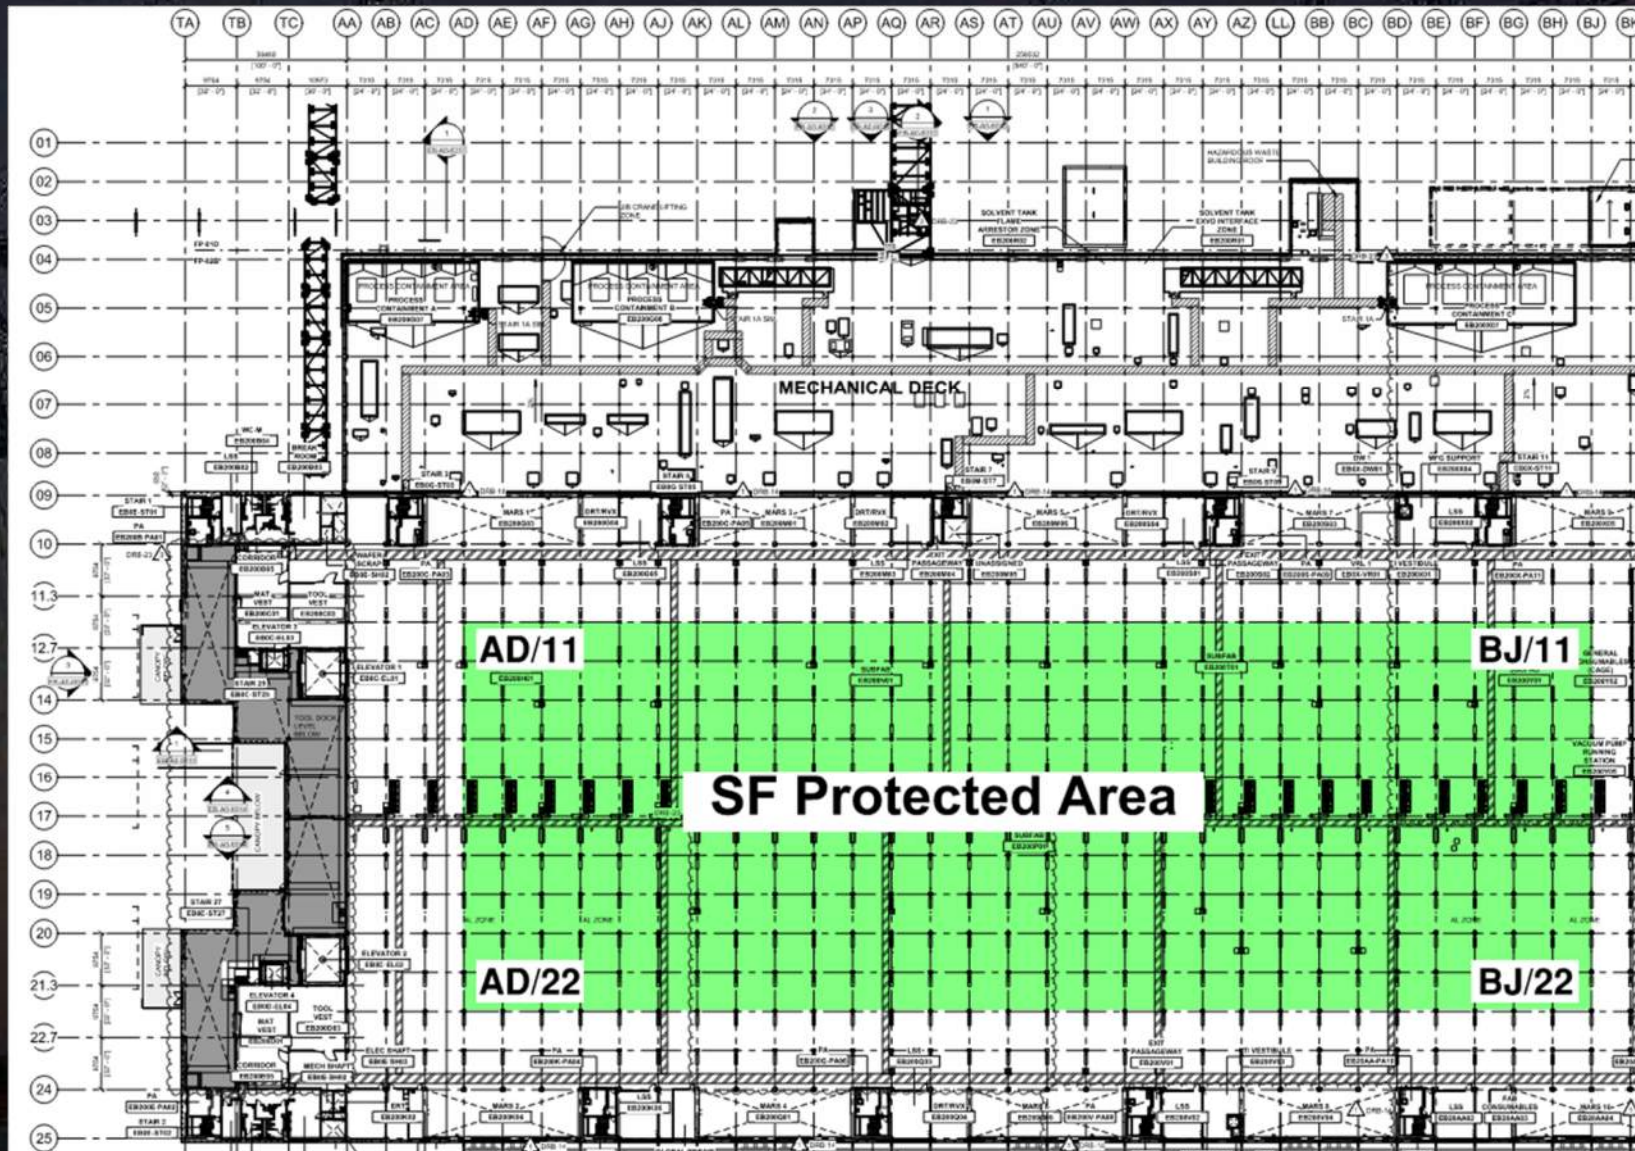




Daily Coordination Meeting

Site Logistics


Protected Areas

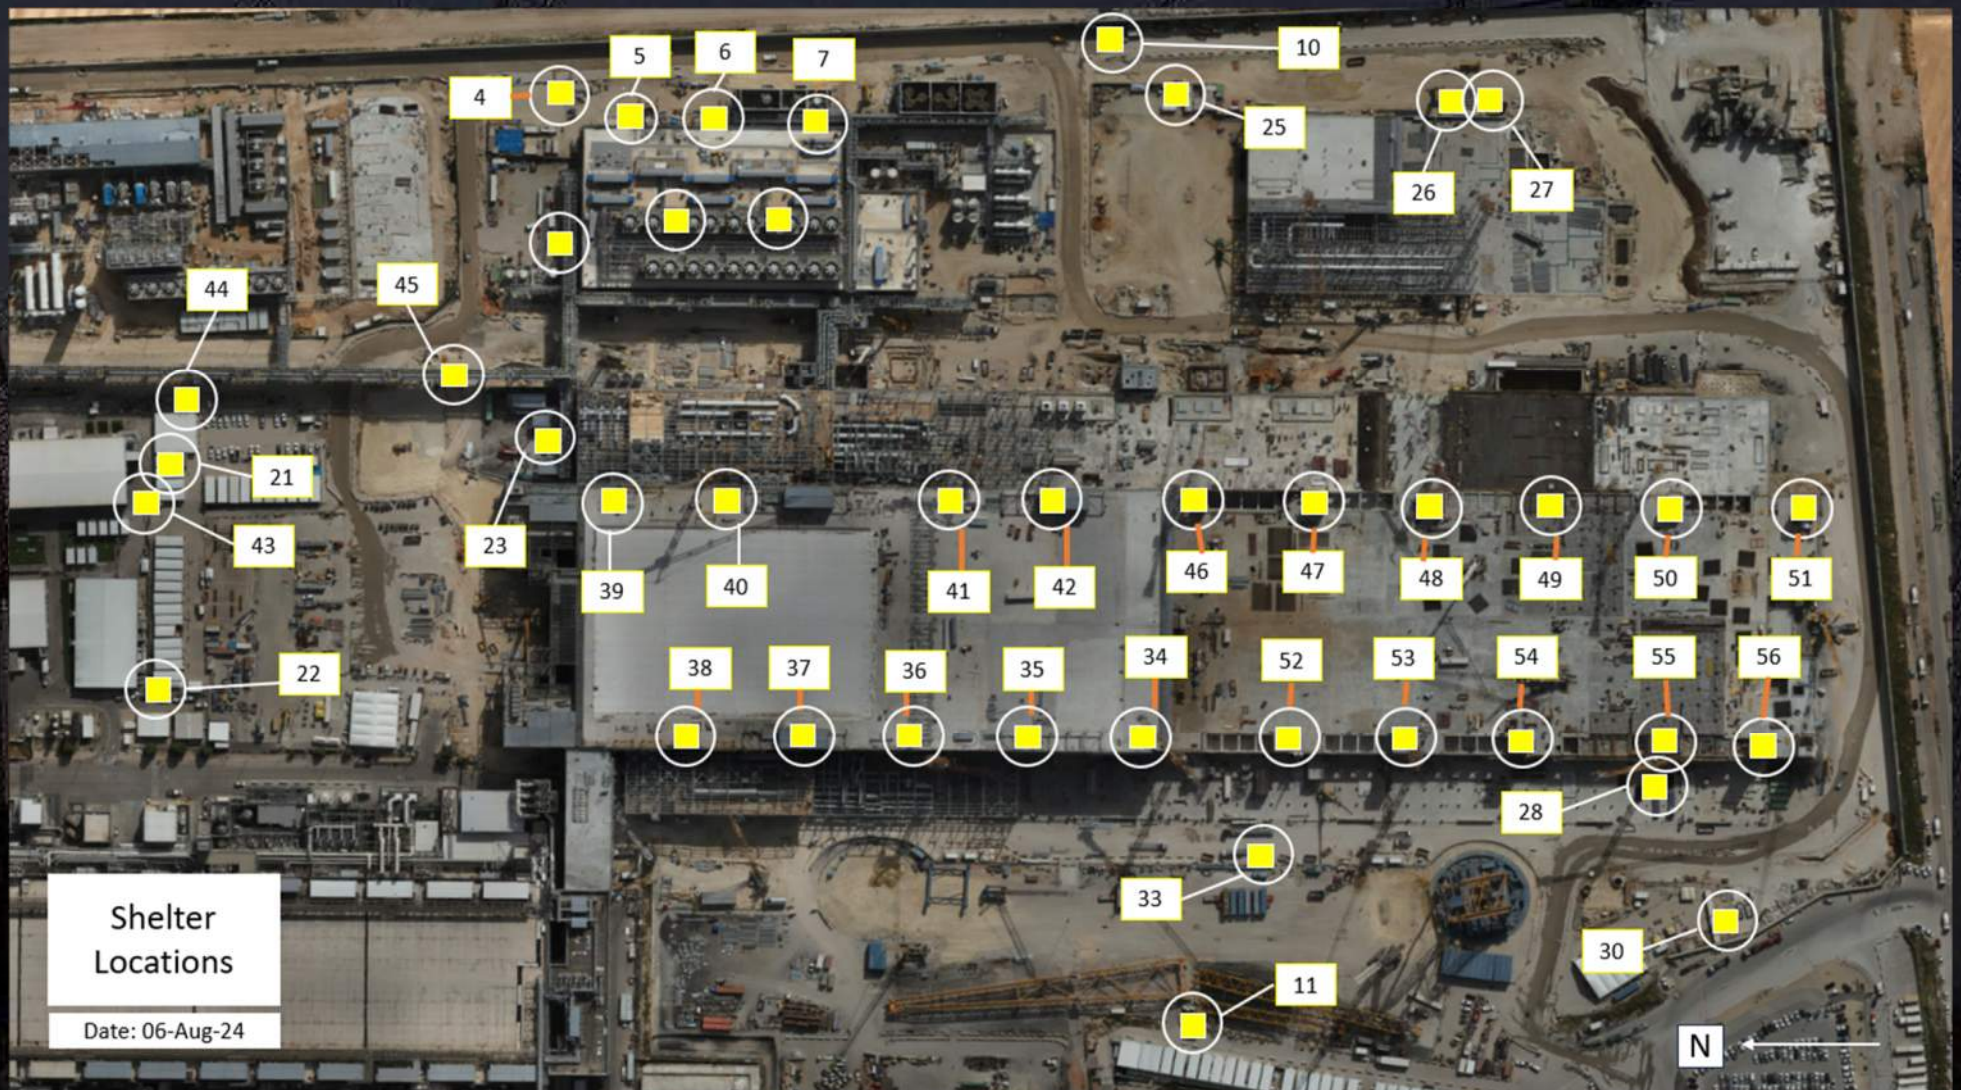


Daily Coordination Meeting


WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

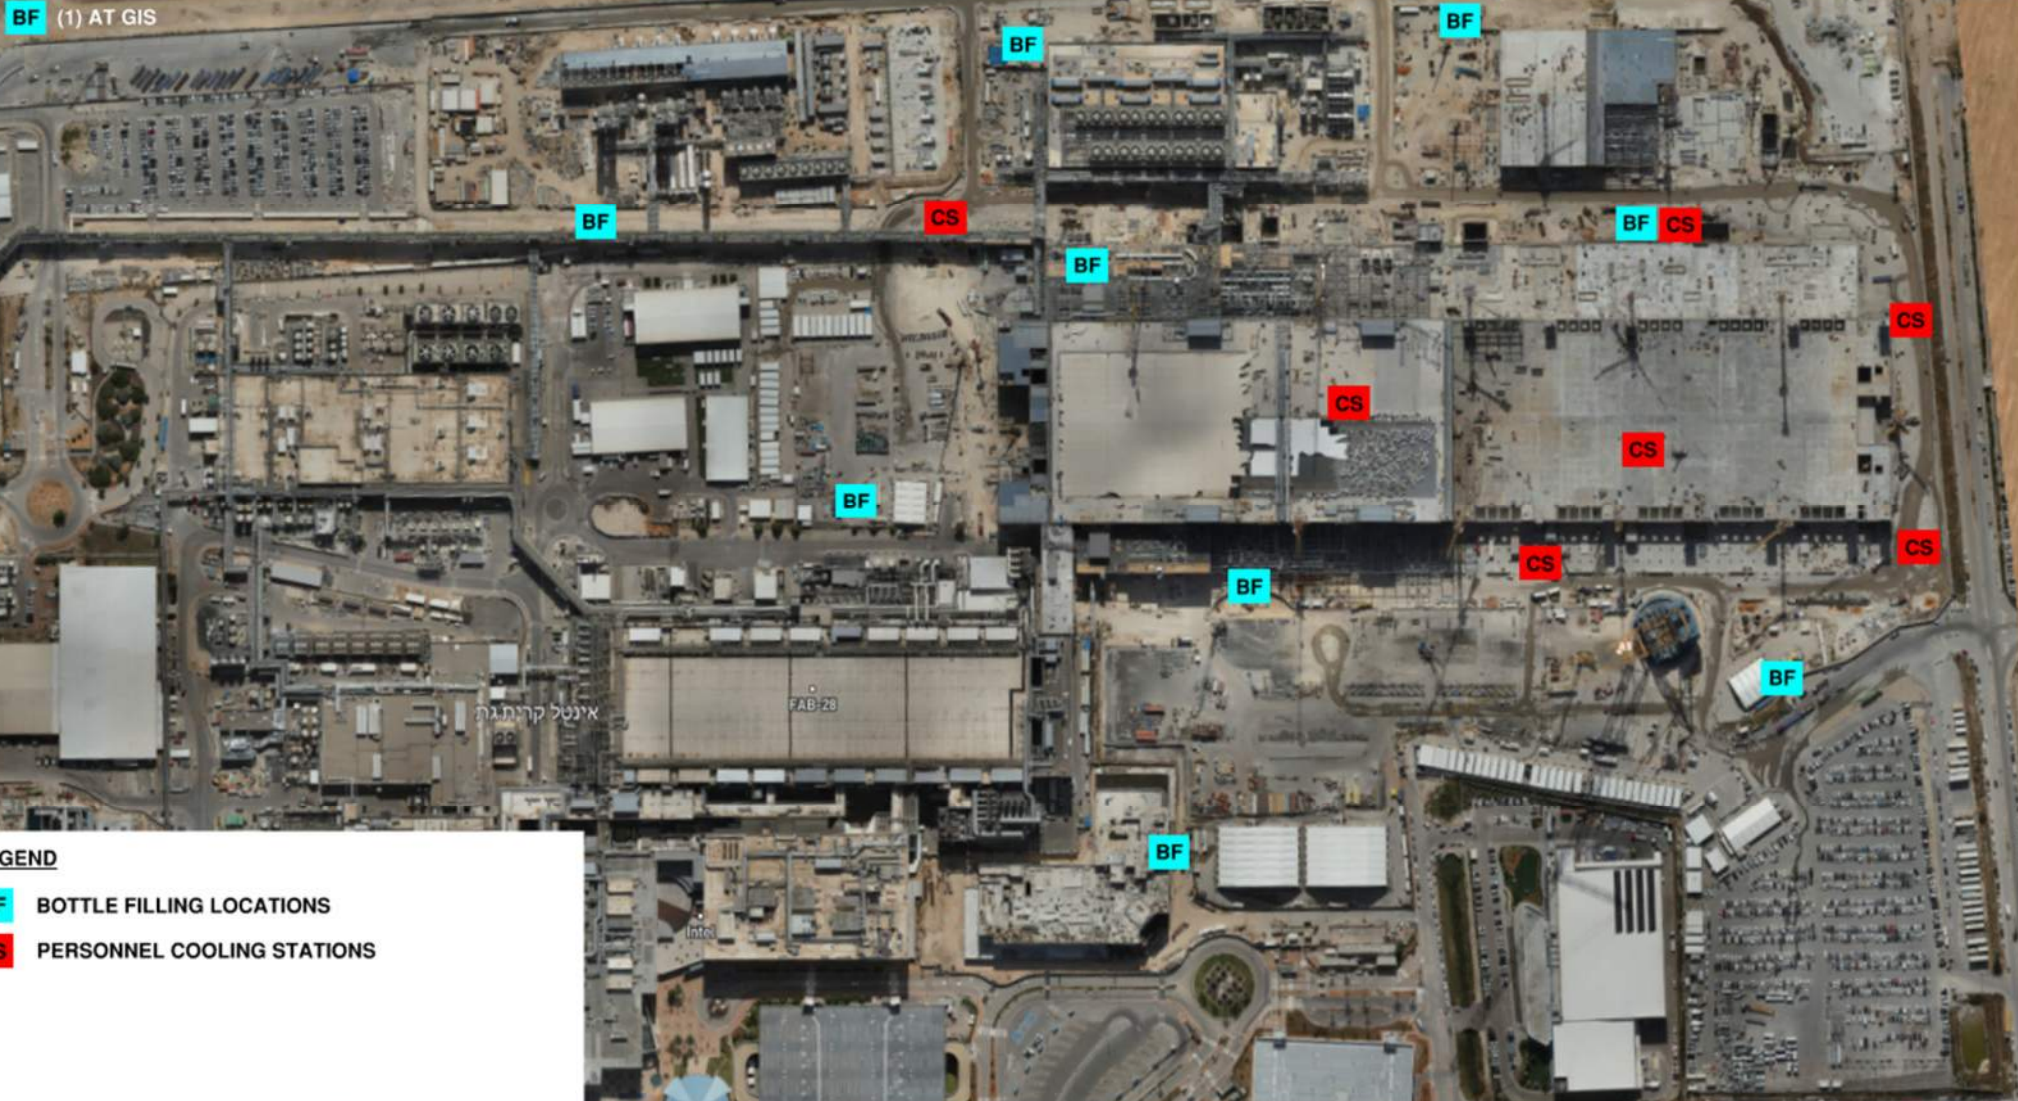

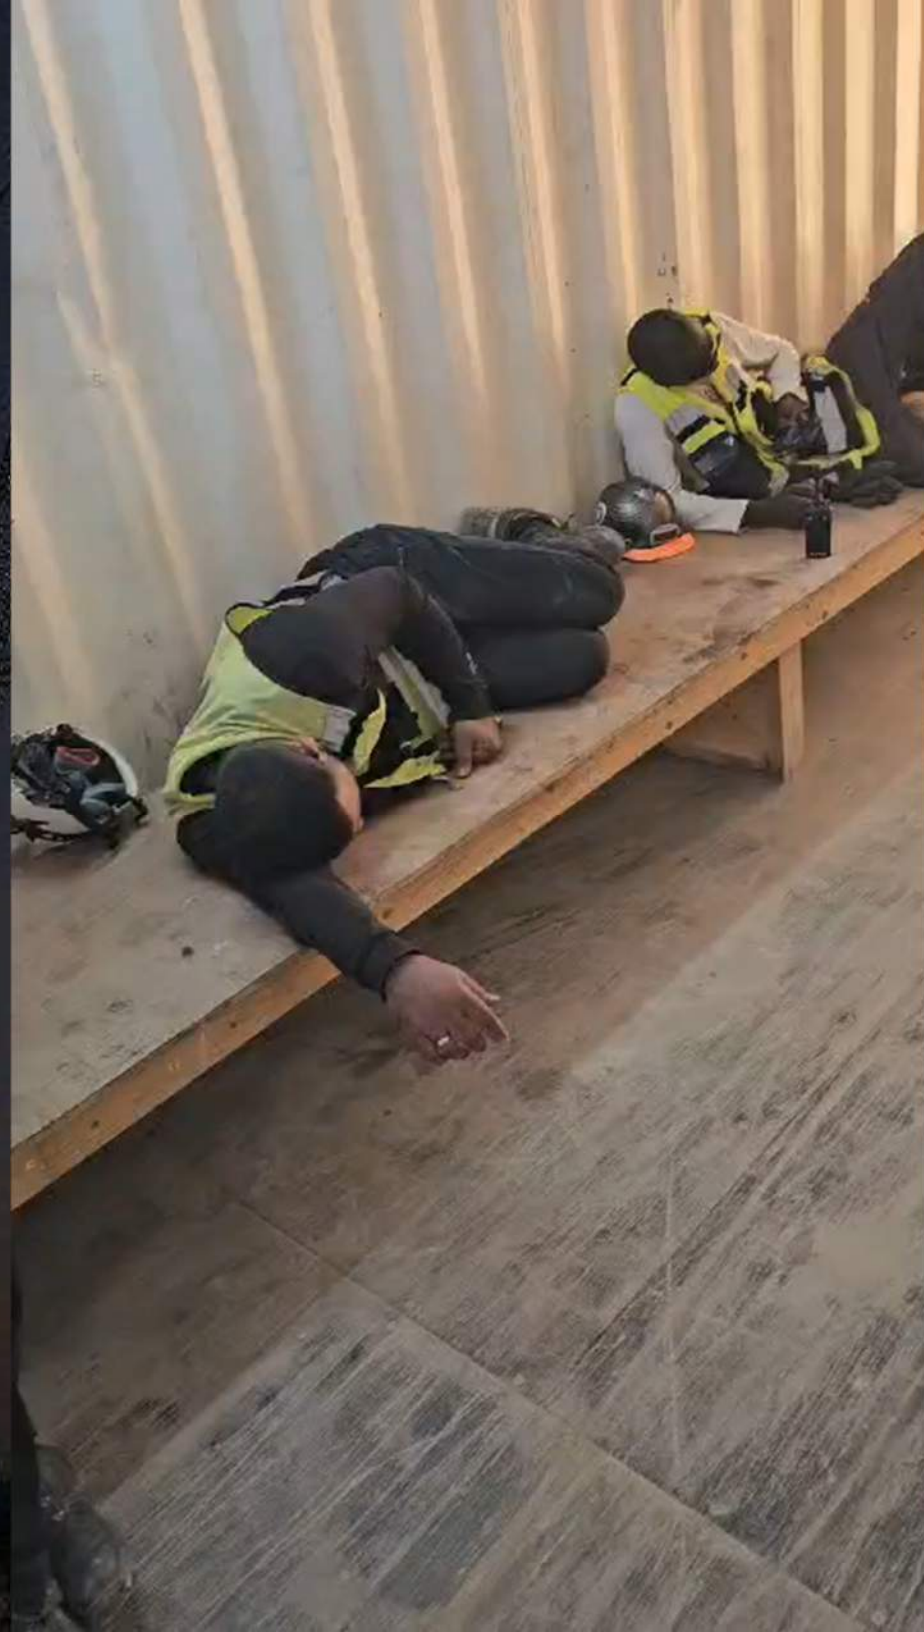

Speeding on site

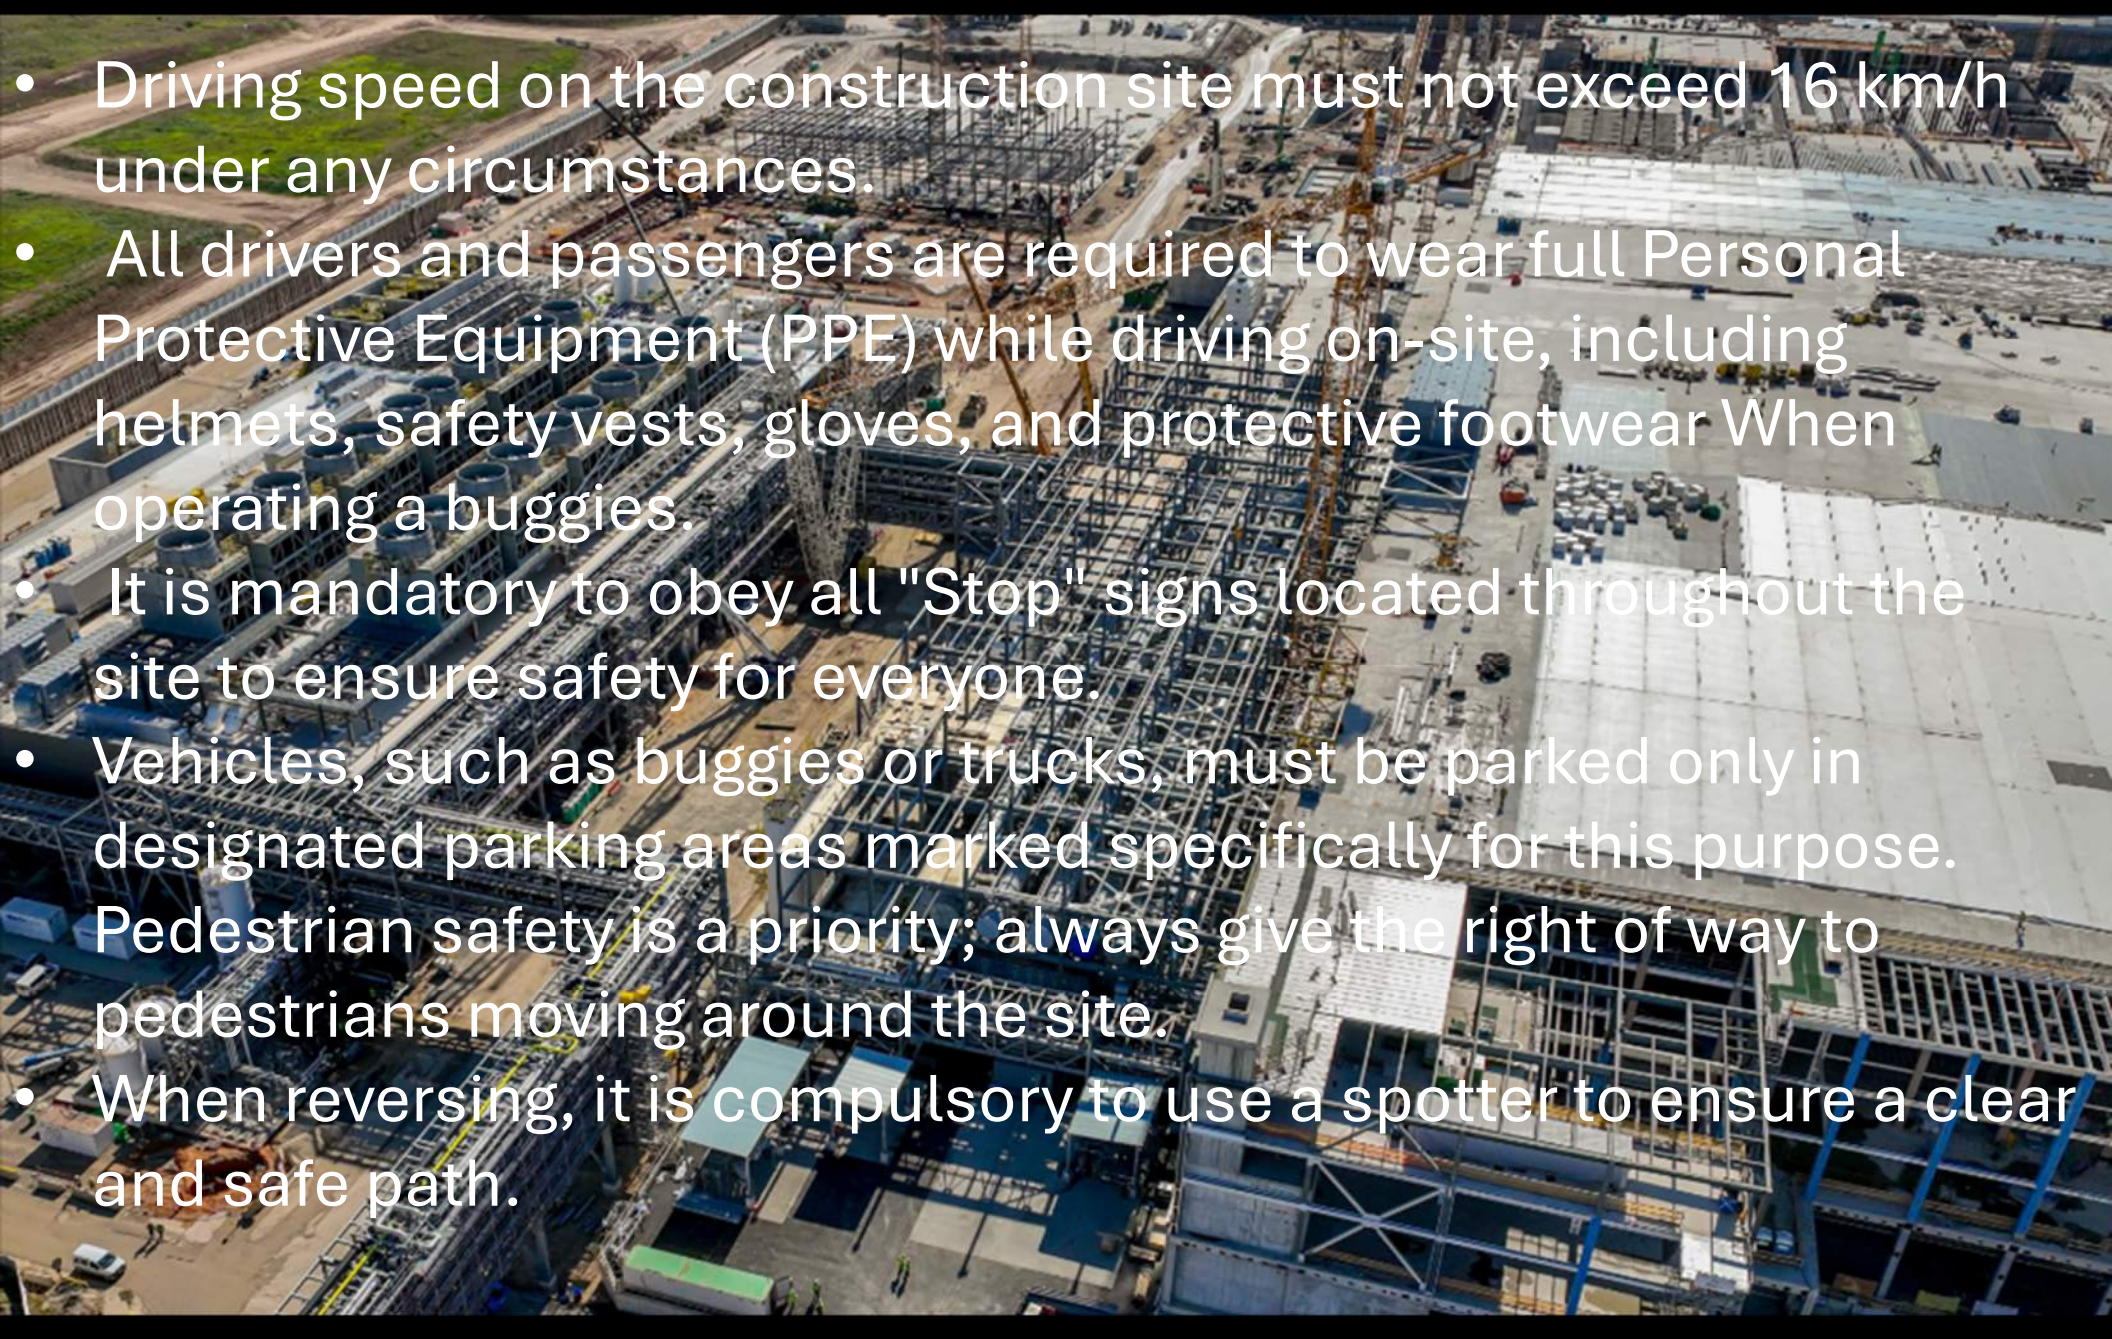- 
- Driving speed on the construction site must not exceed 16 km/h under any circumstances.
 - All drivers and passengers are required to wear full Personal Protective Equipment (PPE) while driving on-site, including helmets, safety vests, gloves, and protective footwear When operating a buggies.
 - It is mandatory to obey all "Stop" signs located throughout the site to ensure safety for everyone.
 - Vehicles, such as buggies or trucks, must be parked only in designated parking areas marked specifically for this purpose. Pedestrian safety is a priority; always give the right of way to pedestrians moving around the site.
 - When reversing, it is compulsory to use a spotter to ensure a clear and safe path.

Heat Index- August 29th

	temperature (°F)															
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
50	81	83	85	88	91	97	99	103	108	113	118	124	131	137		
55	81	84	86	89	93	97	101	106	112	117	124	130	137			
60	82	84	88	91	95	100	105	110	116	123	129	137				
65	82	85	89	93	98	103	108	114	121	128	136					
70	83	86	90	95	100	105	112	119	126	134						
75	84	88	92	97	103	109	116	124	132							
80	84	89	94	100	106	113	121	129								
85	85	90	96	102	110	117	126	135								
90	86	91	98	105	113	122	131									
95	86	93	100	108	117	127										
100	87	95	103	112	121	132										

 Caution
  Extreme Caution
  Danger
  Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

HCC/EHS Weekend Work- 30.08.2024

White Board Meeting in Beavers at 06:30

Superintendents

- Jesse Fritch - 052-3697329
- Yehuda Yehuda - 052-3614292
- Ibrahim A –
- Zach Niebergall - 052-3471103
- Josh Naylor - 052-5192718
- Mark McCabe - 052-2294912
- Ken Power - 052-2531428
- Bernard Hilbrunn - 054-6781350
- Leon Koen - 052-2239637
- Yossi Atias - 052-3060790

CSA CM

MEP

CX/QA

Cranes

- Craig Mowry - 052-300-2769

Safety

- Safety Foreman- Hay Halfon- 052-8049342 Hay-Halfon@Hoffmancorp.com
- Safety Assistant- Wael Abu Arar-052-3573834
- Safety Professional- Rizik Dhabre- 052-3768988 Rizik-Dhabre@Hoffmancorp.com

Subcontractor Weekend Work- 30.08.2024

FAB

- **Elram** – INT 9,10,17,24 lines columns wrap, CR 9,25line -shaft walls (EHS Shlomo Amar – 0545551702, Supervisor Ivan - 0545868048)
Afcon – CR – 1W,2E, 2W, INT-1E, 2E,1W, LINK Rack install (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- **Chemo** – INT -2E+2W 10" pipe install +racks (EHS Lila - 0547886704, Supervisor Winai 0528090588)
- **W&W** - 17-18 Line added the beams 24 line - catwalks (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
Rolling Plains – INT 4DA -5RA AK South, AV couth, Mars Shaft 3E, (Supervisor Codrin 0546594273, EHS Oleg - 0542689370)
- **Talad** – CR 1W – Drilling holes, 6-7W metal lids install (EHS Guy 0544915407, Super Igor 0544509386)
- **Sela** – 1st coat at 1E Cleanroom (EHS Shmuel 0506306031, super Rudi 0507422319)
- **SNJ** – Victor – 054-9220163
Liron – 052-8939558

Utility Level

Chemo

- Ehs lilach 0547886704
- Foreman sergey 0544659688

HYG

- Ehs Salah 0507773119
- Foreman Avishai 0503303939

Combe UPW

- Ehs: Michael 0525506596
- Foreman; Edward 0526419894

Elram

- Foreman: Shlomo 0545551702
- Ehs: shy 0523632132

Afcon electrical

- Ehs Steven 0559129333
- Foreman Perdit 0552742935

Subfab

Belfor

- TTNW – Wall Remediation.
- Team Lead : Salame Abu El Asal 0546651886

Afcon E

- Mars 1E/W Ducts
- Team Lead : Anklesh Yadav 0559648722

WW Steel

- Elevator Shaft 1
- Team Lead : Michael 0523605006

Pach Taas

- Mars 1E/W & 2E
- Team Lead : Nuriel 0549012343

Lesico

- SF Zone 5
- Team lead: Gabriel 0549892929

Chemo

- TTNW
- Team lead: Sergey 0544659688
- Safety: Lilah 057886704

- Clean Room

PSSS

PachTaas:

- Meir 050-2161429
- Andrey 050-2998167

W&W :

- Tonny 050-7870320
- Michel L. 052-4093401

Chemo A. :

- Lilach 054-7886704
- Sergey 054-4659688

Combe UPW :

- Eduard 052-6419894
- Shimon 054-5348843

Elram :

- Eliaz 052-6380964

Afcon EL :

- Charls 055-2798559
- Pradeep 055-2742935
- Sarat 055-2740190

Siding

Subcontractor Weekend Work- 30.08.2024

WJG

W&W – Steel Erection 3J

- Foreman: Chris Isaac – 052-588 3215
- Safety: Moshe 054-801 2959

Afcon – 1J/2J Lift 2 Cable Tray

- Foreman: Sarat 055-274 0190
- Safety: Pradeep 055-2742935

Pach Taas: 1J UL, 2J Lift 2 Module Bolting

- Foreman: Nuriel 054-9012343
- Safety:

Chemo: 4J & 5J Lift 2 Piping

- Foreman: Stav 054-7175157
- Safety: Rotem 054-4477112

Site

Derech Afar – Fire protection water

Supervision = Raed: 054-2442030

EHS = Alex: 054-5403849

Olizki – Sweepers and water trucks

Supervision = Shimon: 052-4702921

EHS = Ben: 052-4033565

Trestle

SNJ:

SUT steel 4 workers

T10-11/ T30A PIPING 8 WORKERS

- FORMAN HAMADA SALEM tel. 0543516972
- Safety trestle Alon Matan tel. +972 50-989-5008

GIS/NEY

TMT:

- Seal & clean drainage & sewage manholes 4 workers
- Forman- Yehuda Adler - +972 52-5567780
- Safety- Mital Dvir - +972 53-3001124

CUB

Chemo Aharon:

- Dudu - 0509808846
- Leonid - 0548883878

Sami Najami:

- Shlomi - 0504757537

Meptagon:

- Raziel - 0584360845
- Itsik – 0587441140

SIG

- Nodar - 0546393261

CUB Mechanical team for 24 hours Friday and Saturday coverage.

- Friday Day Aekphisit 05275617574
- Friday Night Wattana 0544259081
- Saturday Day Aekphisist 05275617574
- Saturday Night Praphum 052893774

ON call EK Supervisor 0523623552

Daily Coordination Meeting



14:00 Sign In
