

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- **Loose Ends**
- **Prepare for Long Weekend, What System Need Support**
- **Rain in Forecast**




Cub @ Zone 7
@ 12:00 am

Cub @ Zone 7
@ 12:00 am

FAB-28



UTILITY LEVEL MOD1

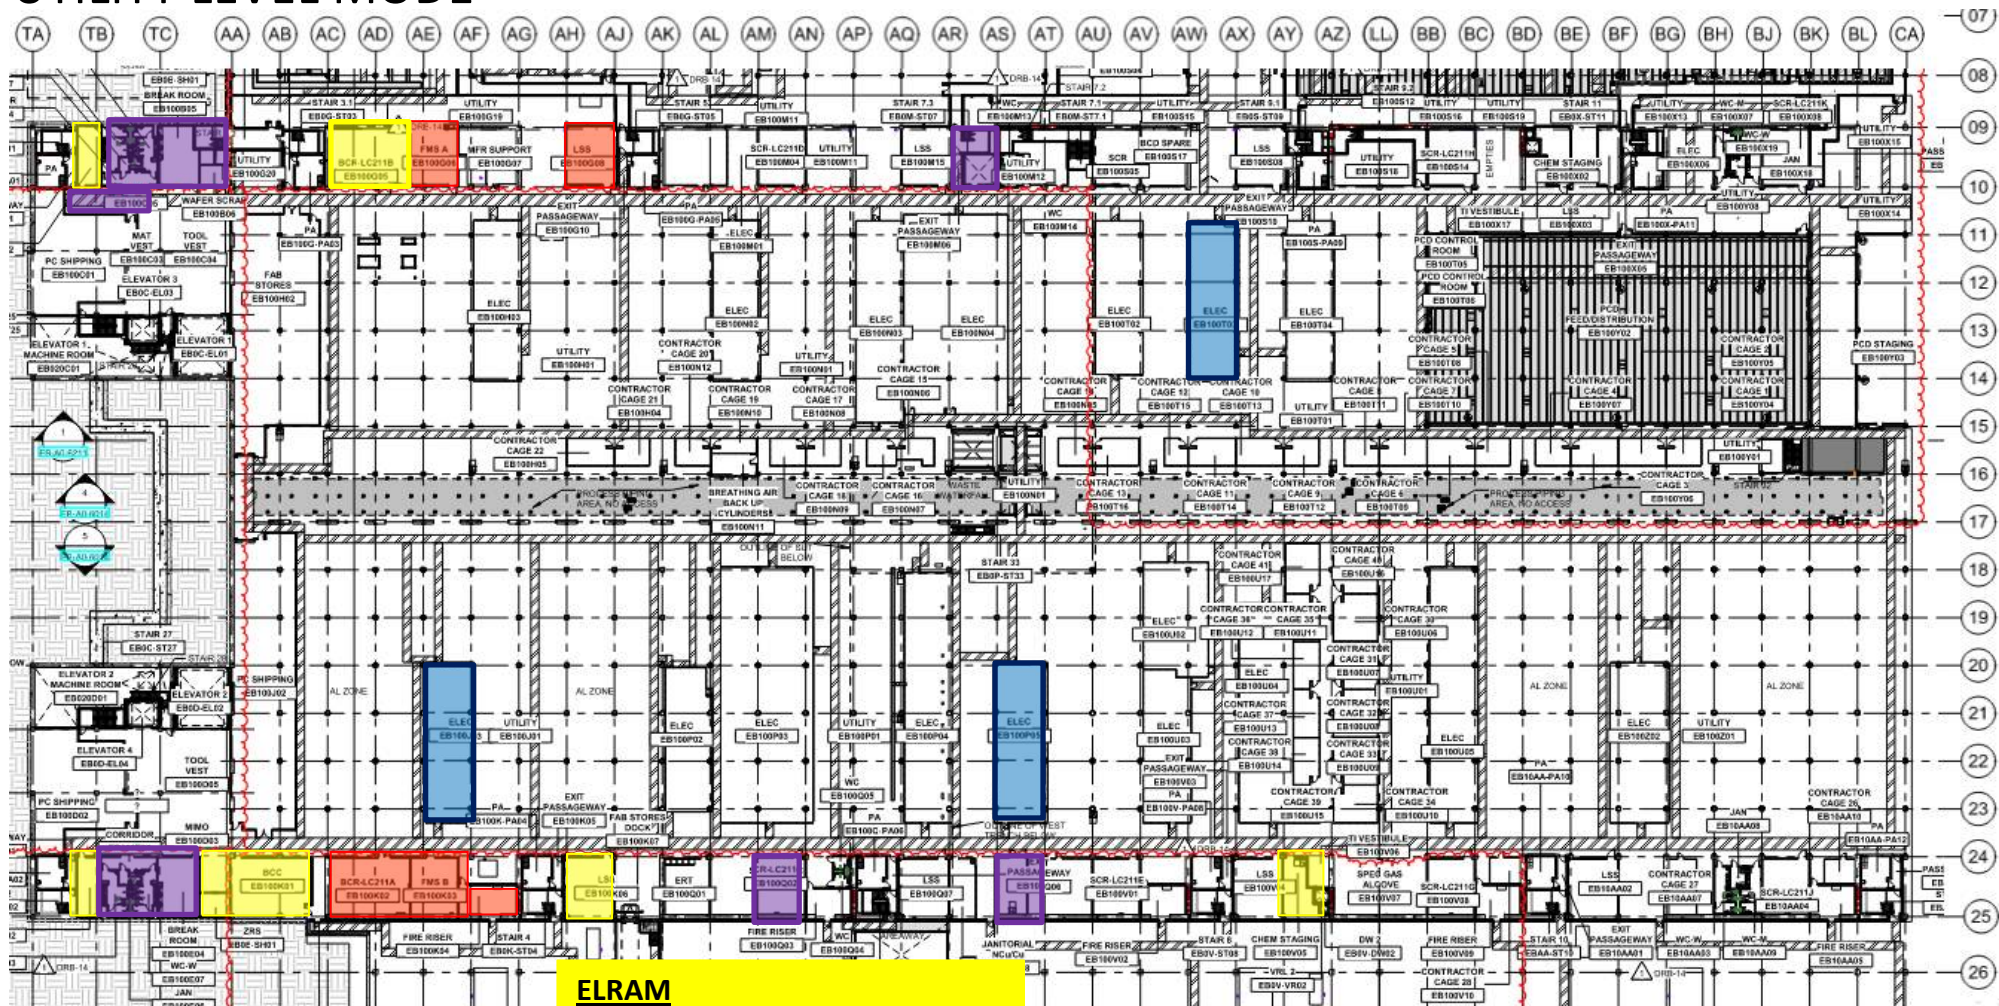

BELFOR

TTNE - Corridor + Toilets + Break R
Stairs 7.3
Wafer scrap
TTNW - Toilets + Break R
SCR 2W
Exit pass 3W


ELRAM

Ongoing
LSS TTNW + TTNE
BCR 1E
CHEN STAGING
LSS 2W
Chem staging
BACKING
BCR 1E+1W – Pending funding
LSS's

MEP+Electrical


Ready for re-install
FMS A 1E
FMS B 1W
Fire Risers 1W
BCC

UTILITY LEVEL MOD2

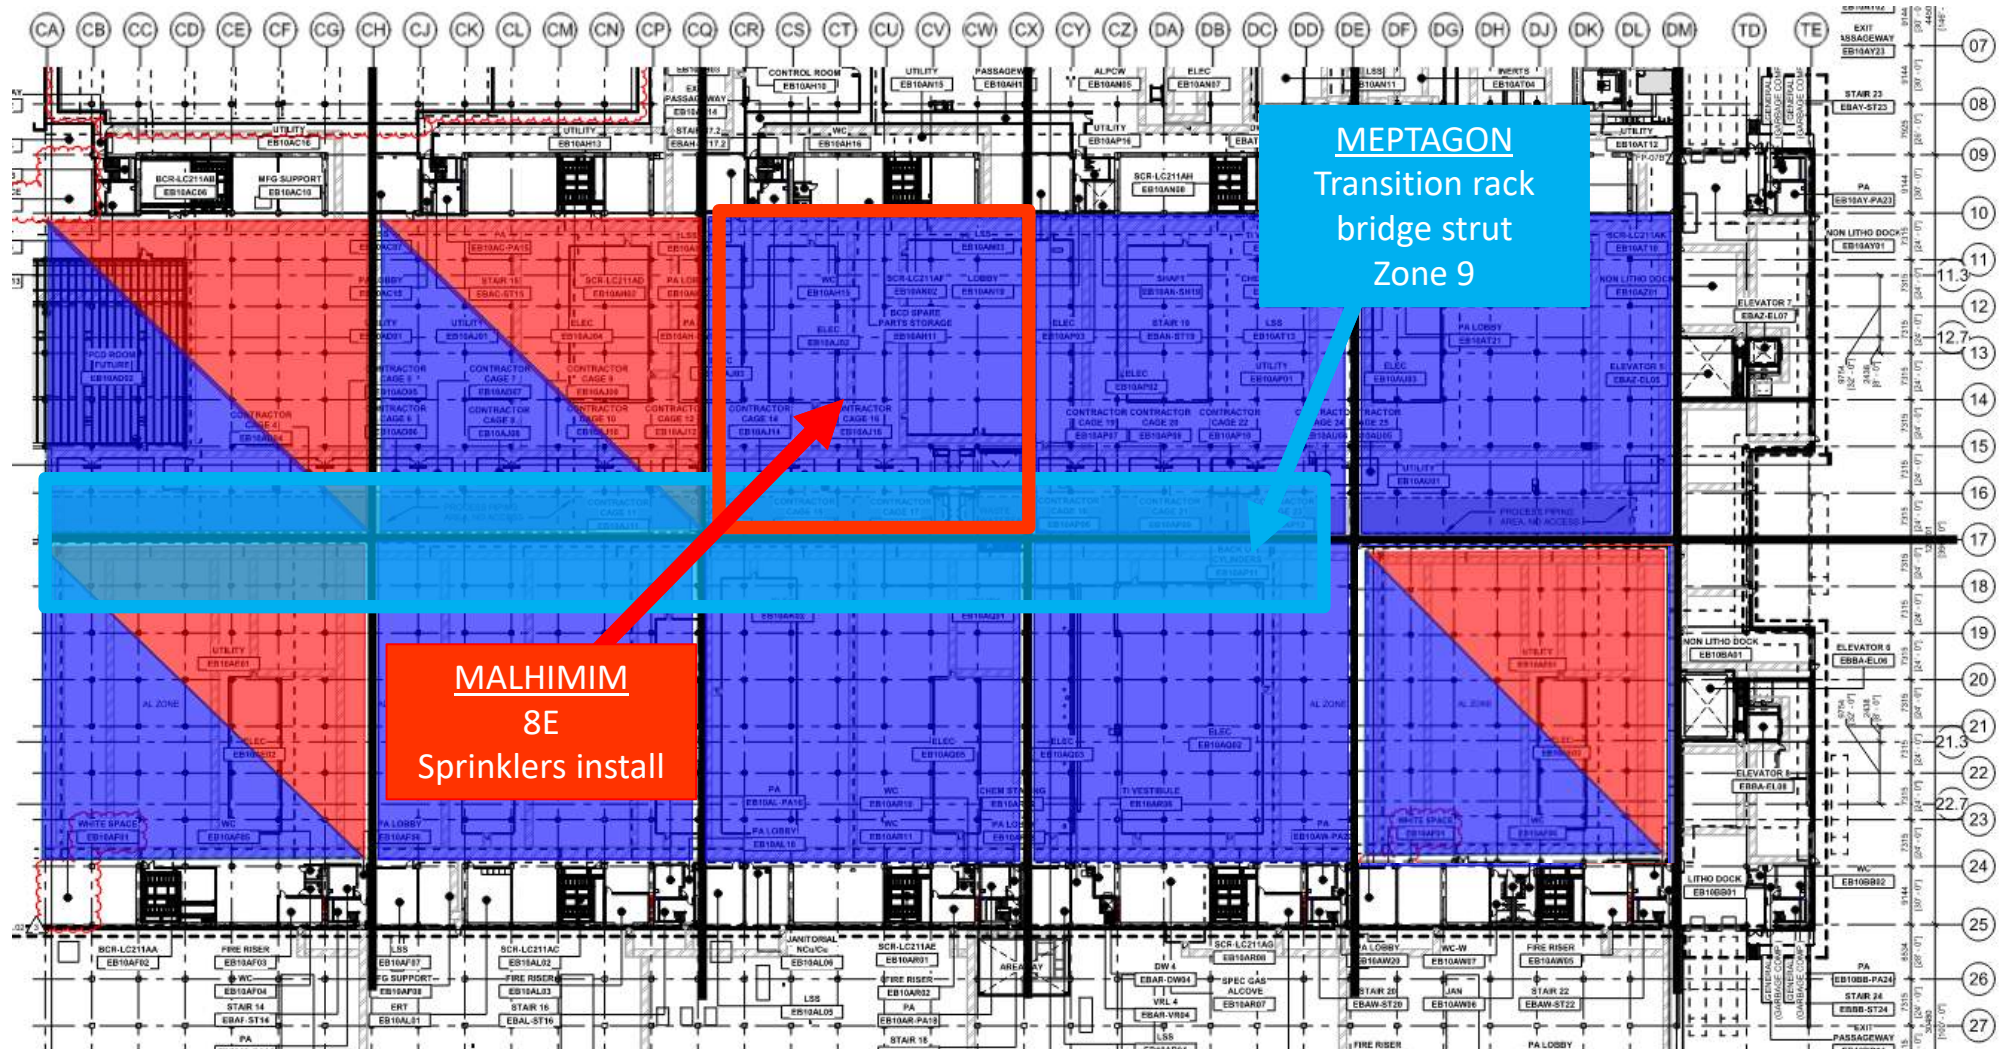




SUT 38.1 LEVEL

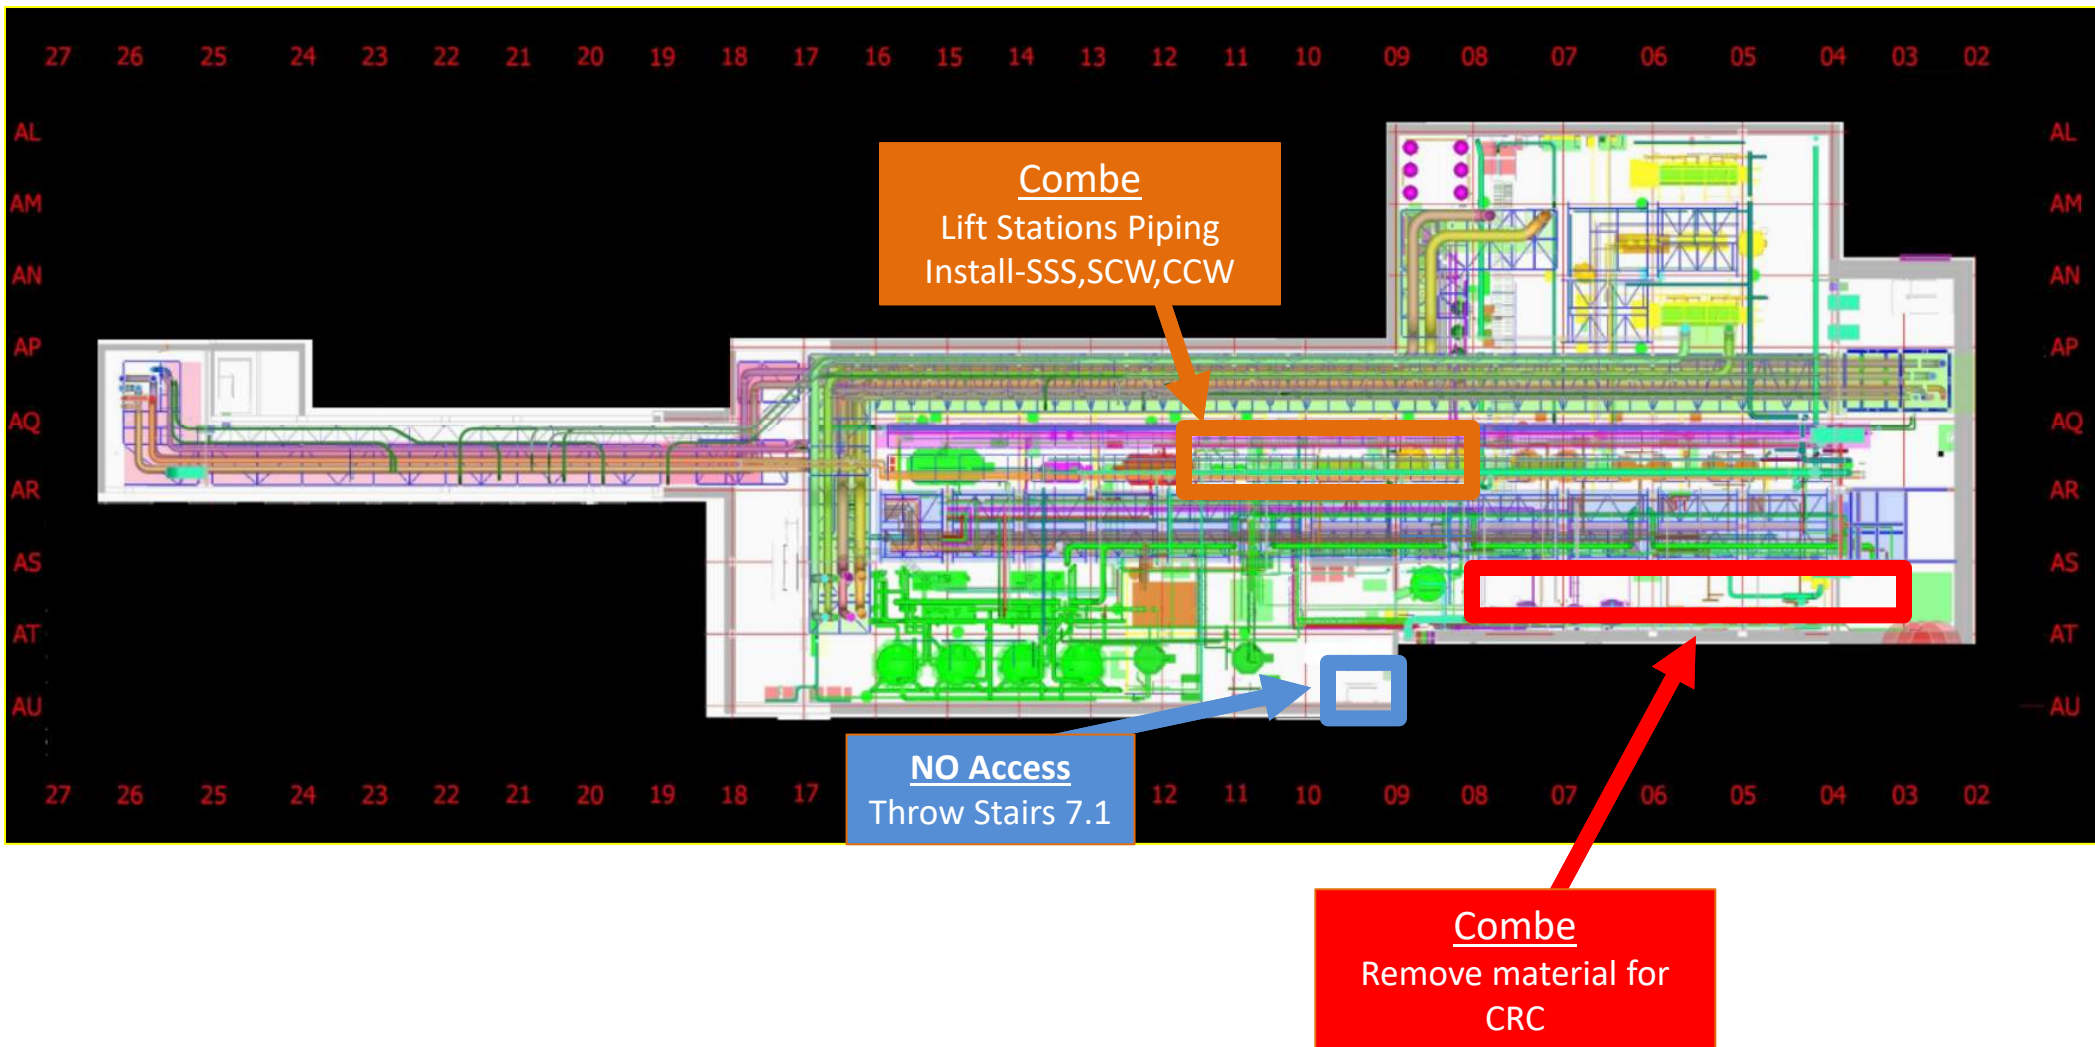


SUBFAB BUILDOUT MOD 1

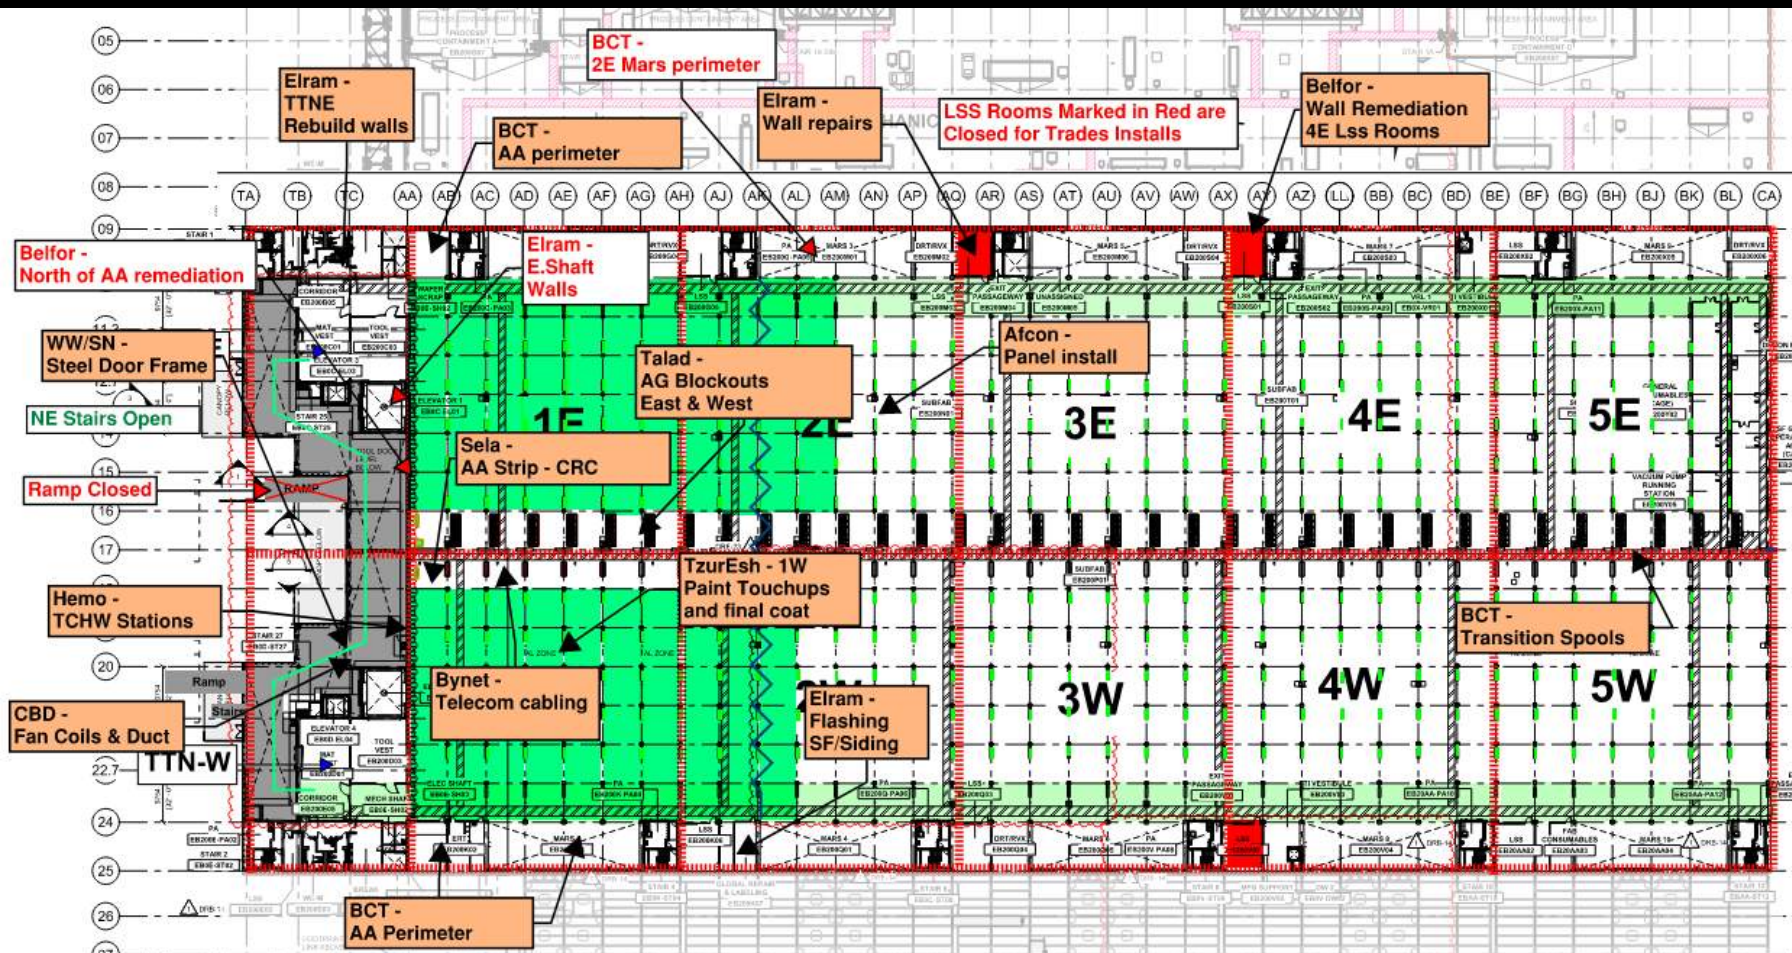


SUBFAB CRC TOPCOAT




SUBFAB CRC TOPCOAT

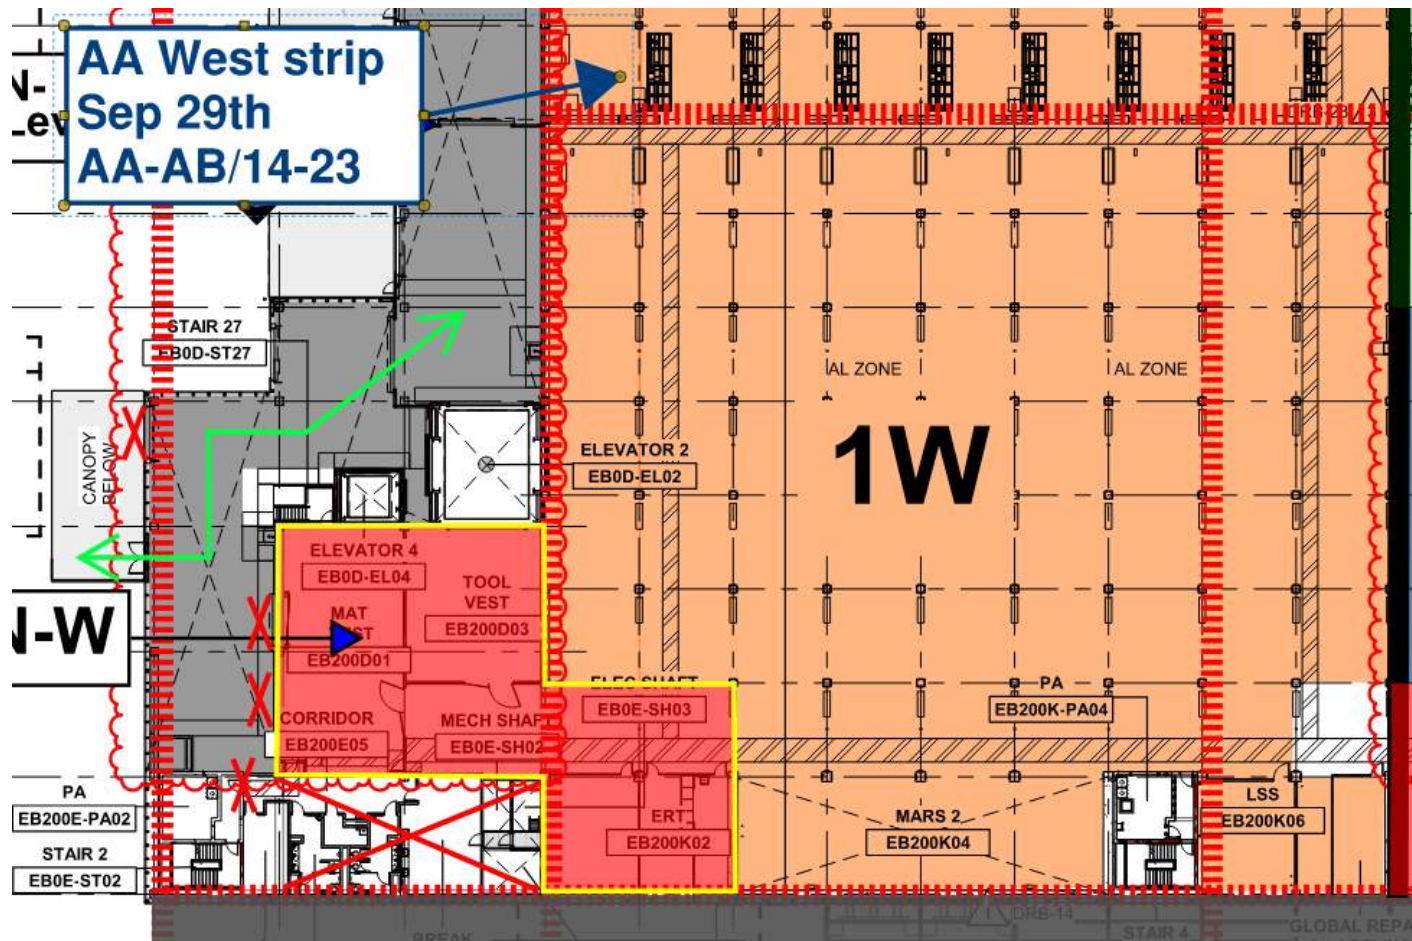


BCT Pressure Test Exclusion Zone

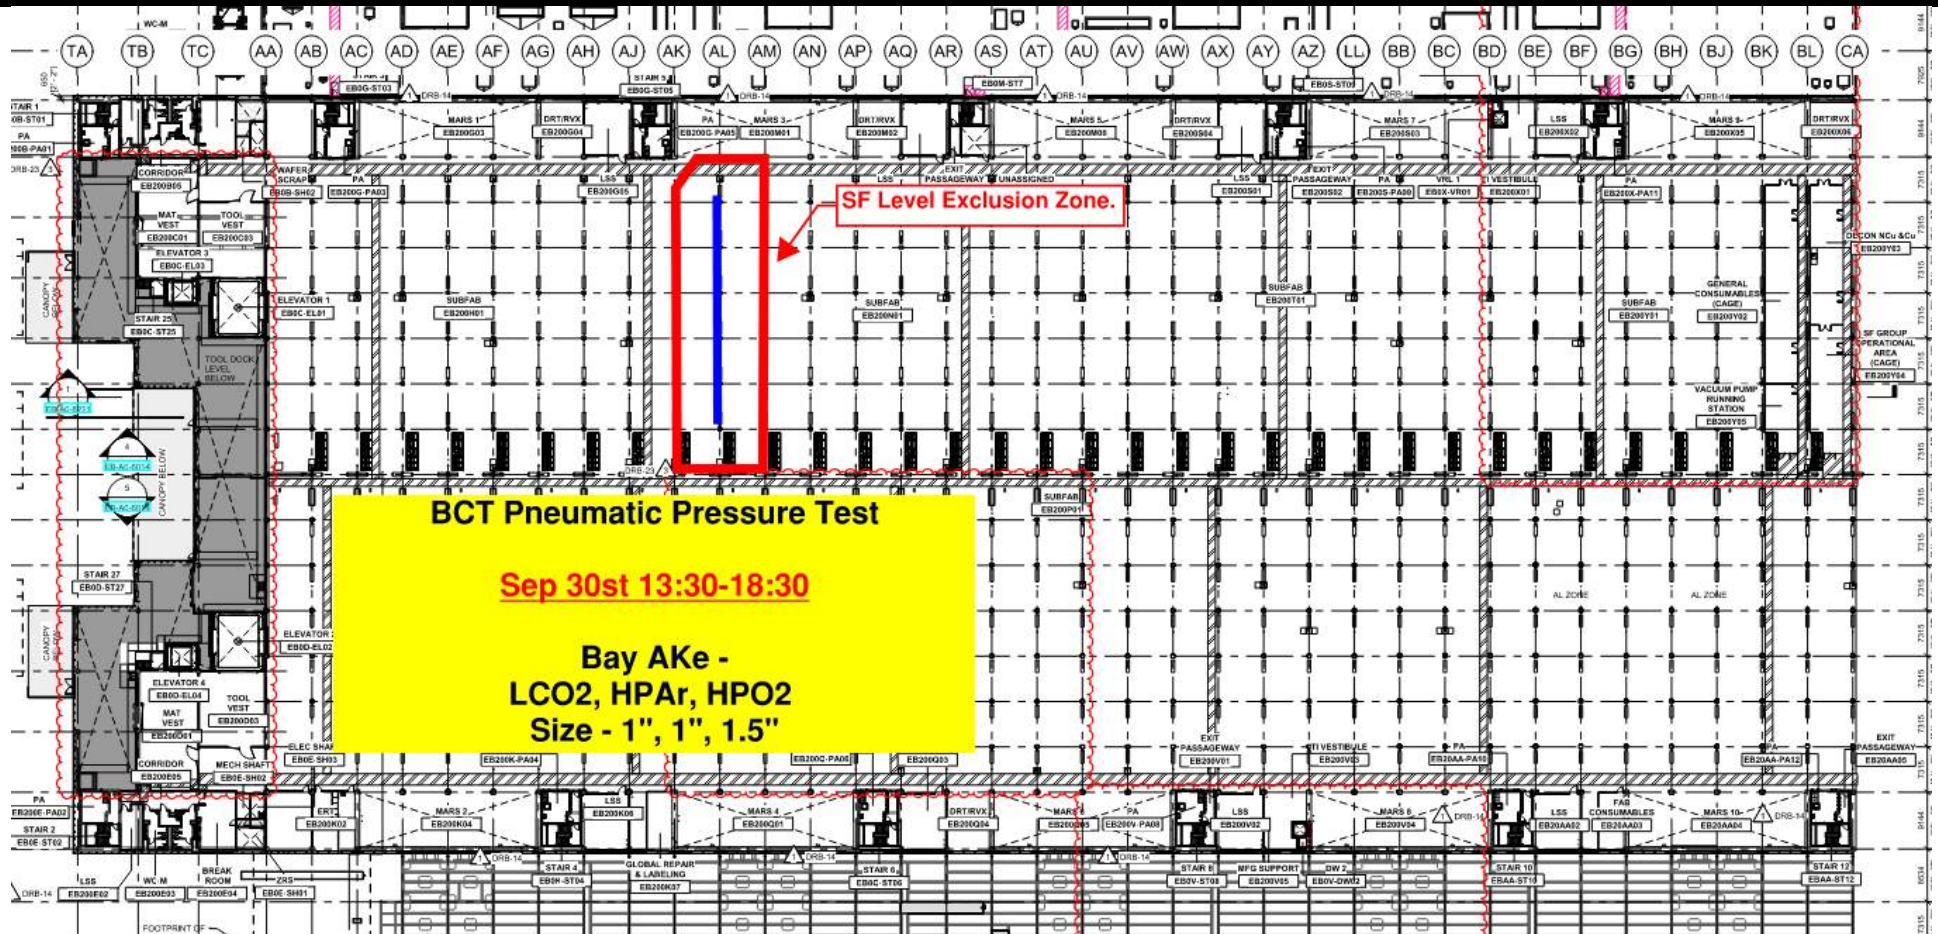

BCT Pressure Test Exclusion Zone

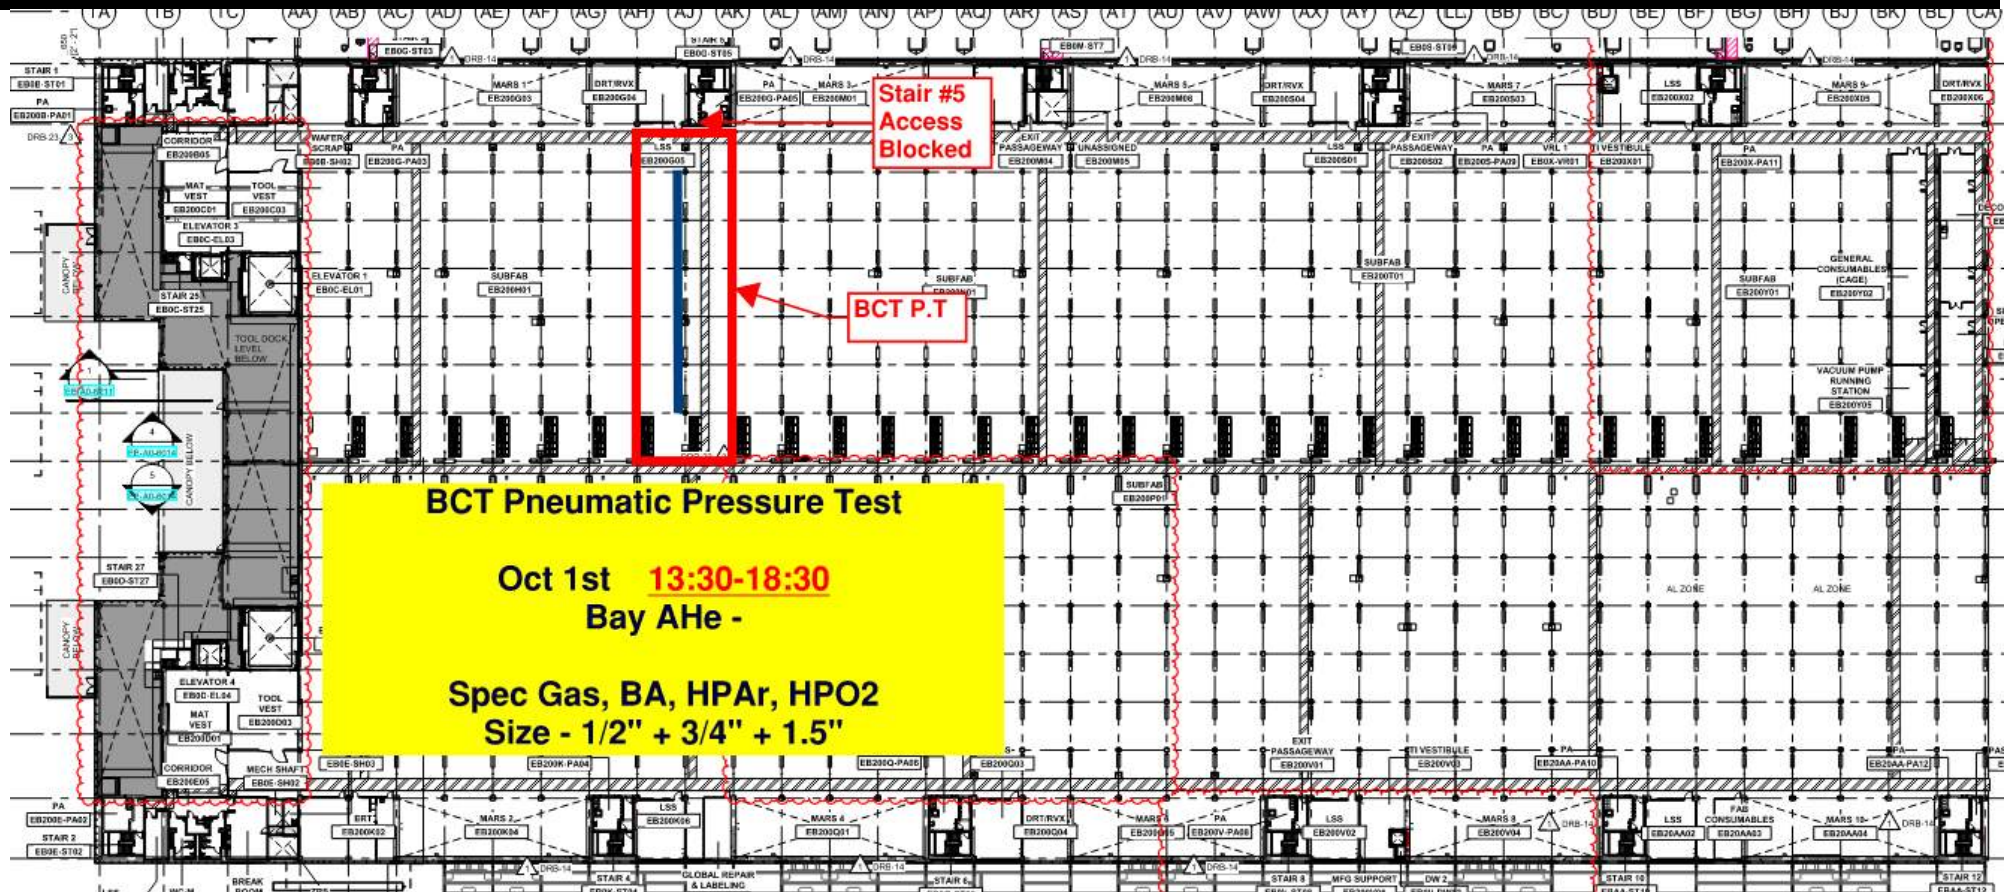

SUBFAB BUILDOUT MOD 2

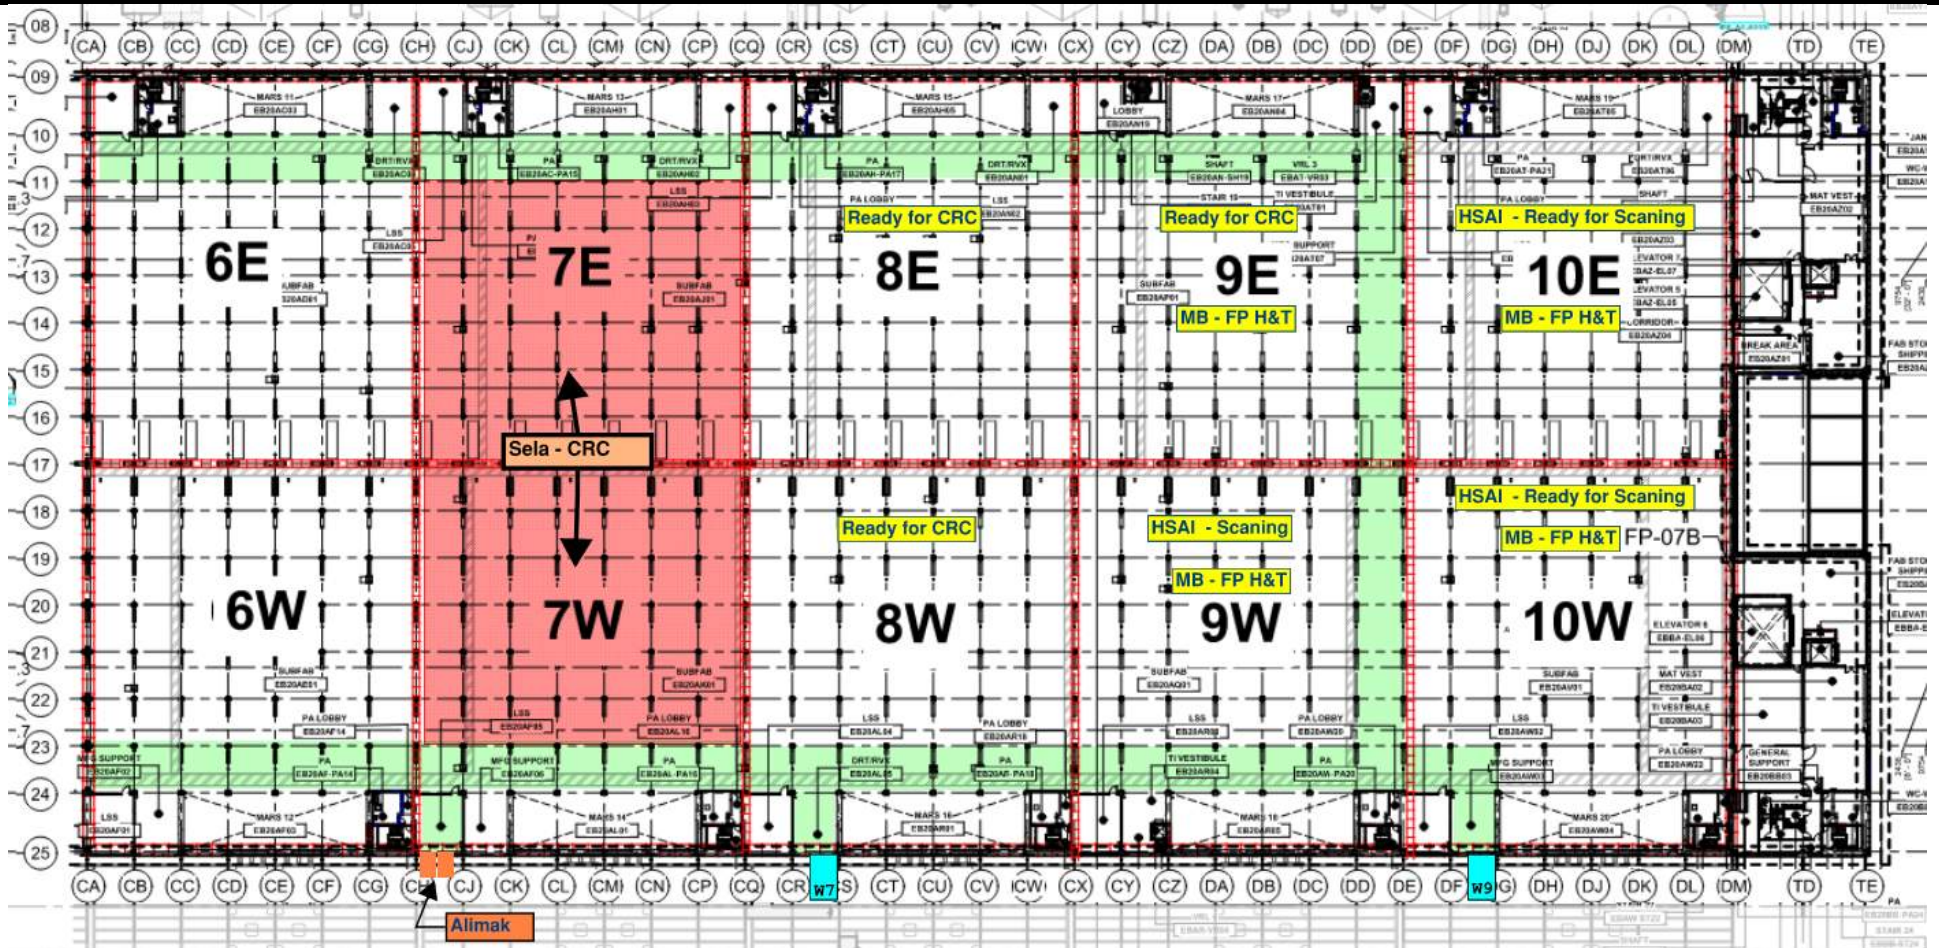


Clean room


protocols apply!!


1. only electrical booms & scissors.
2. Booties for all wheels is a must.


sella crc 1E zone.


All subs working over head must protect 4da working areas with protective sheets to prevent plaster waste or any other waste from falling down on fresh crc coat

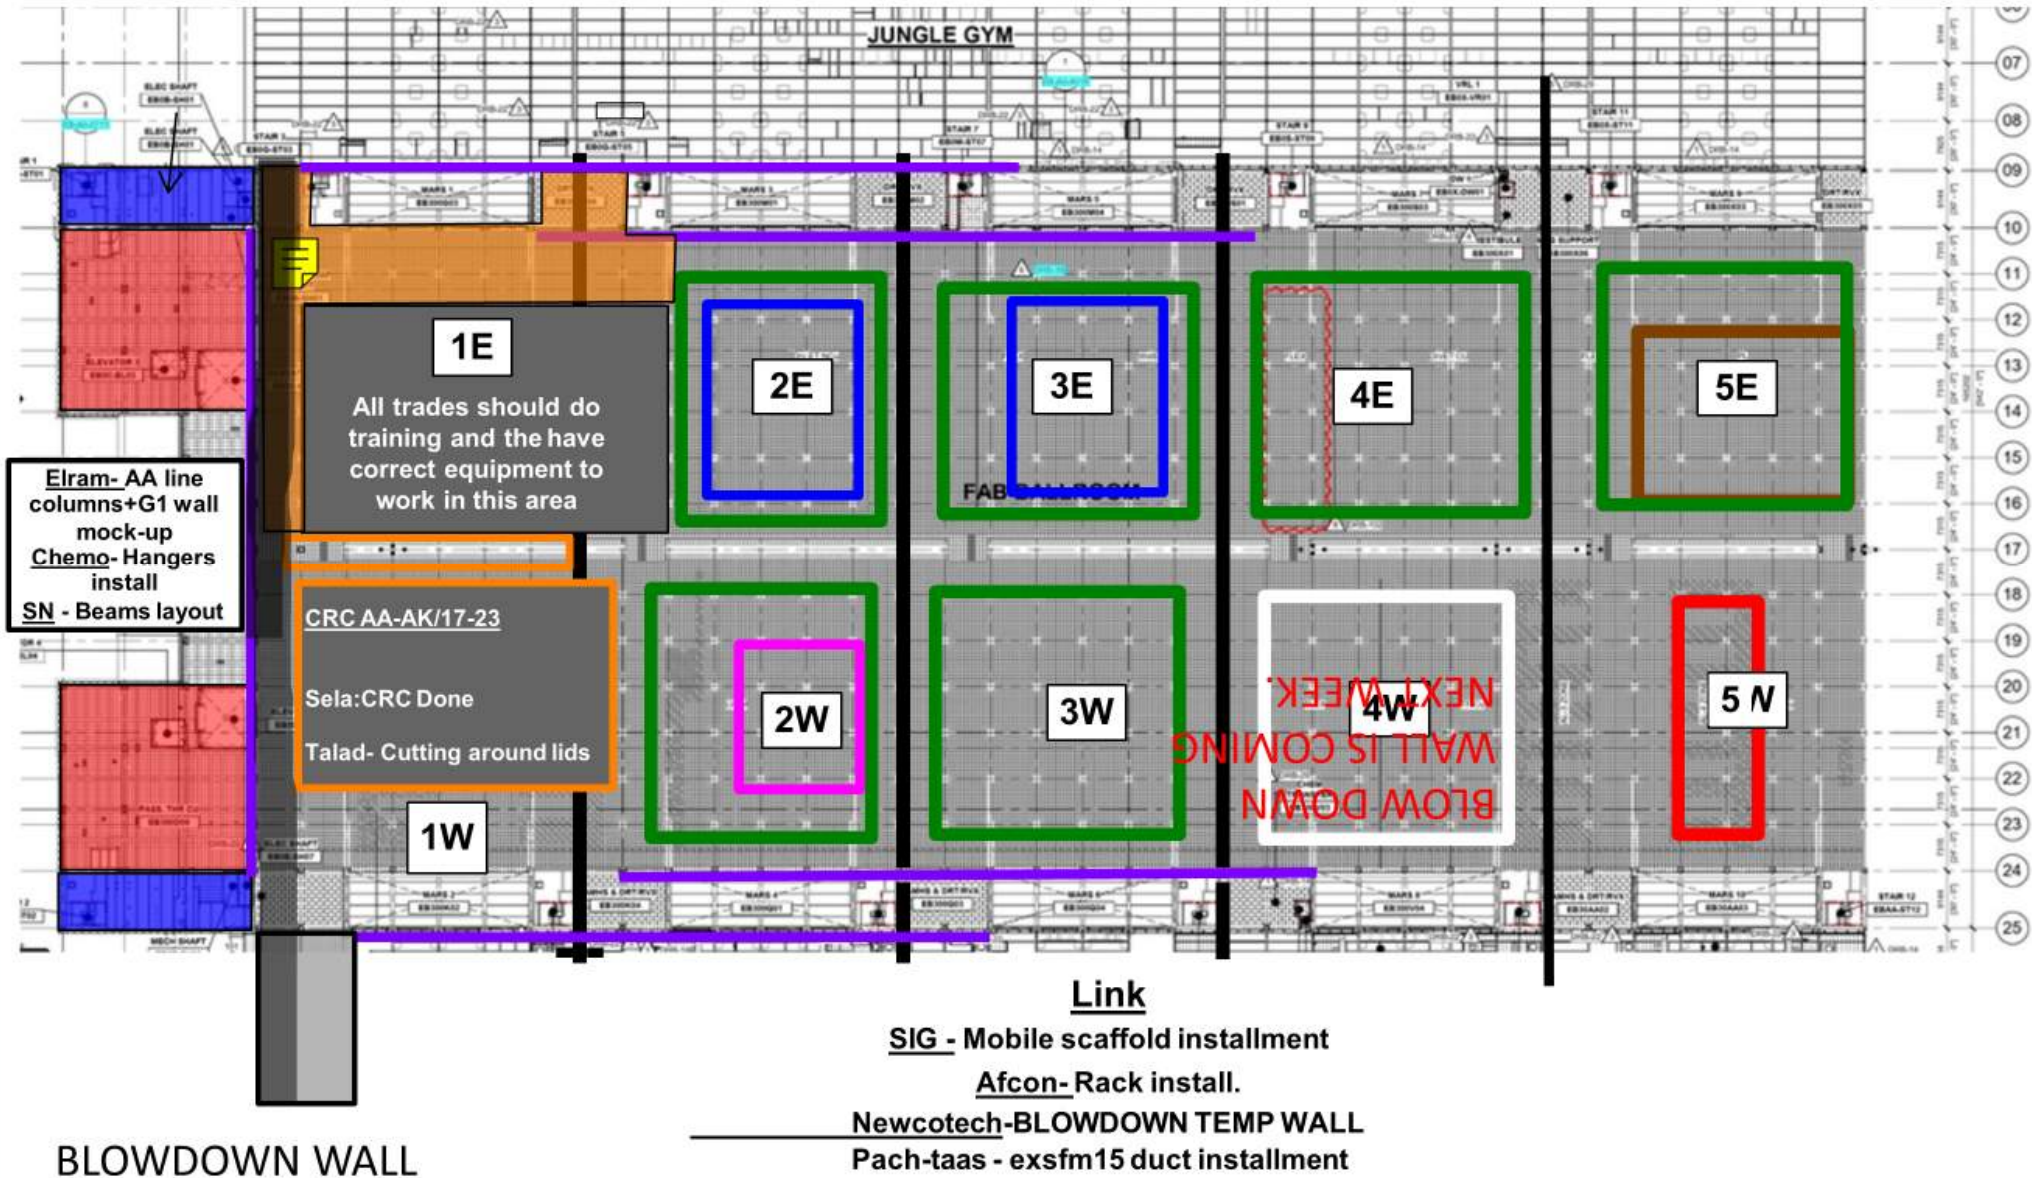

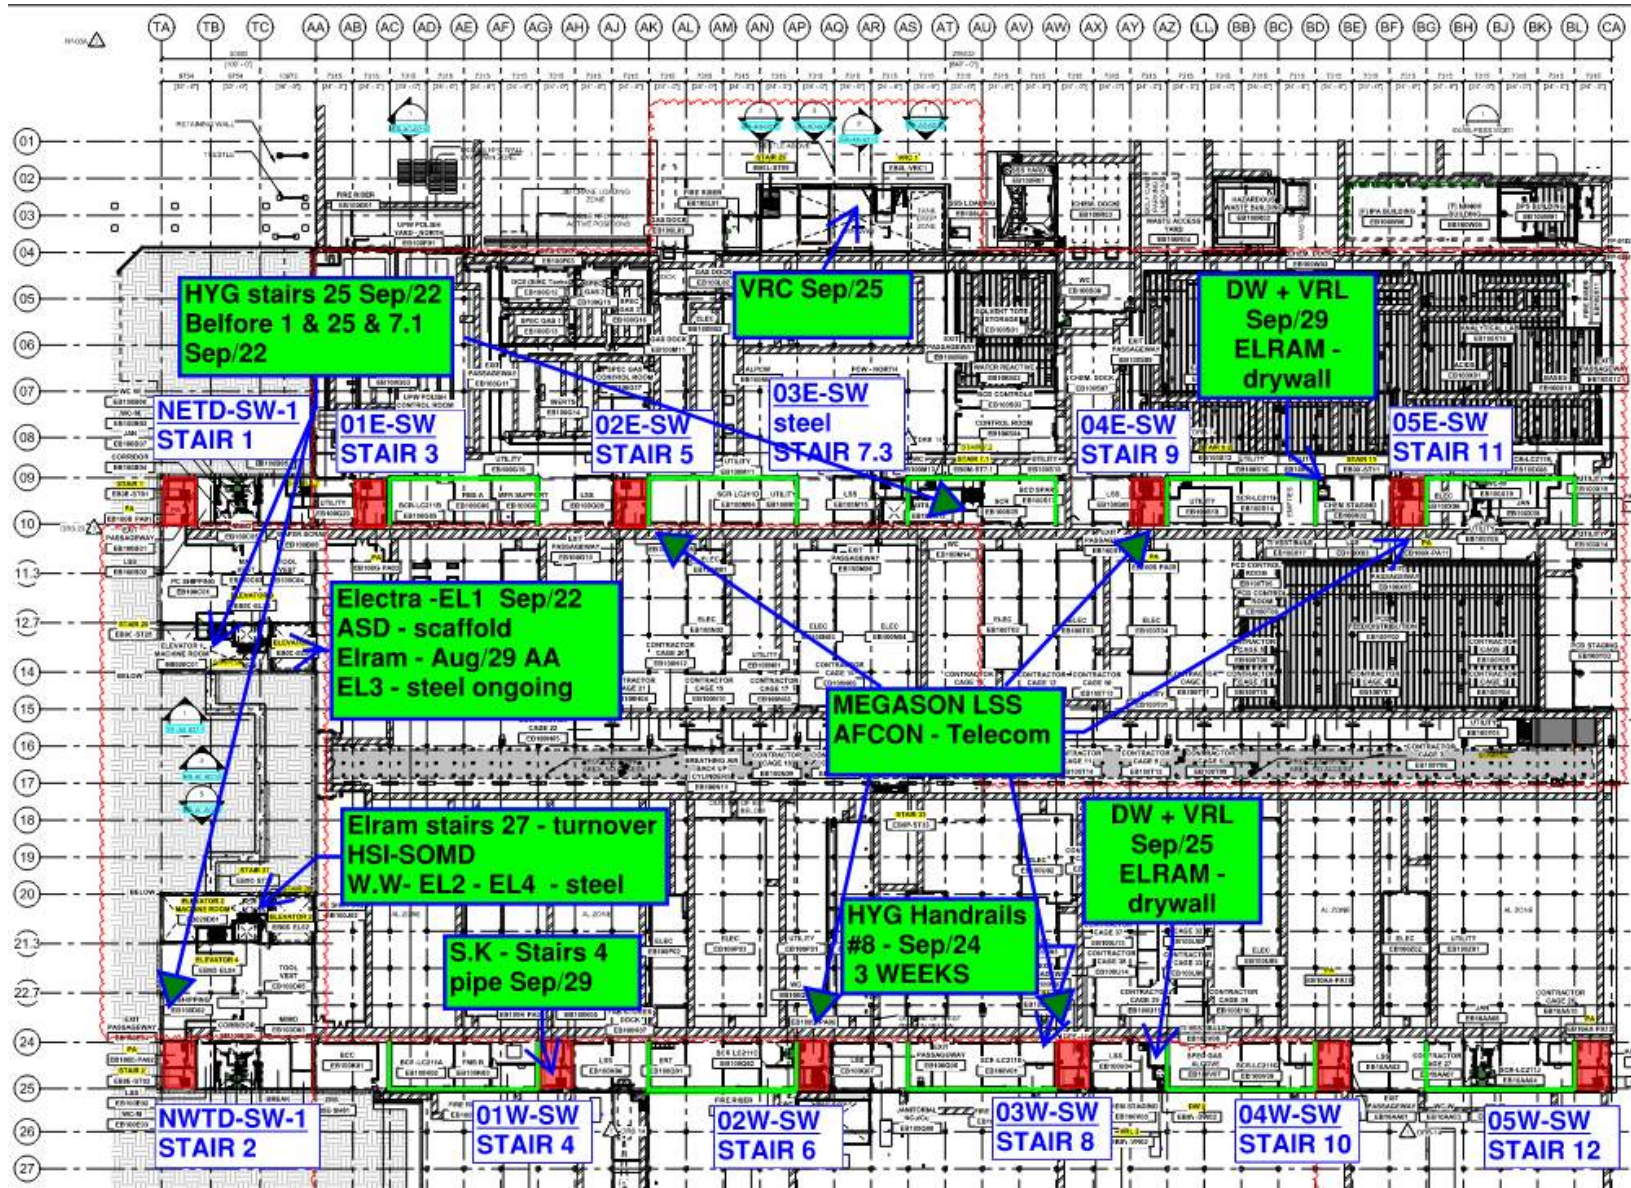

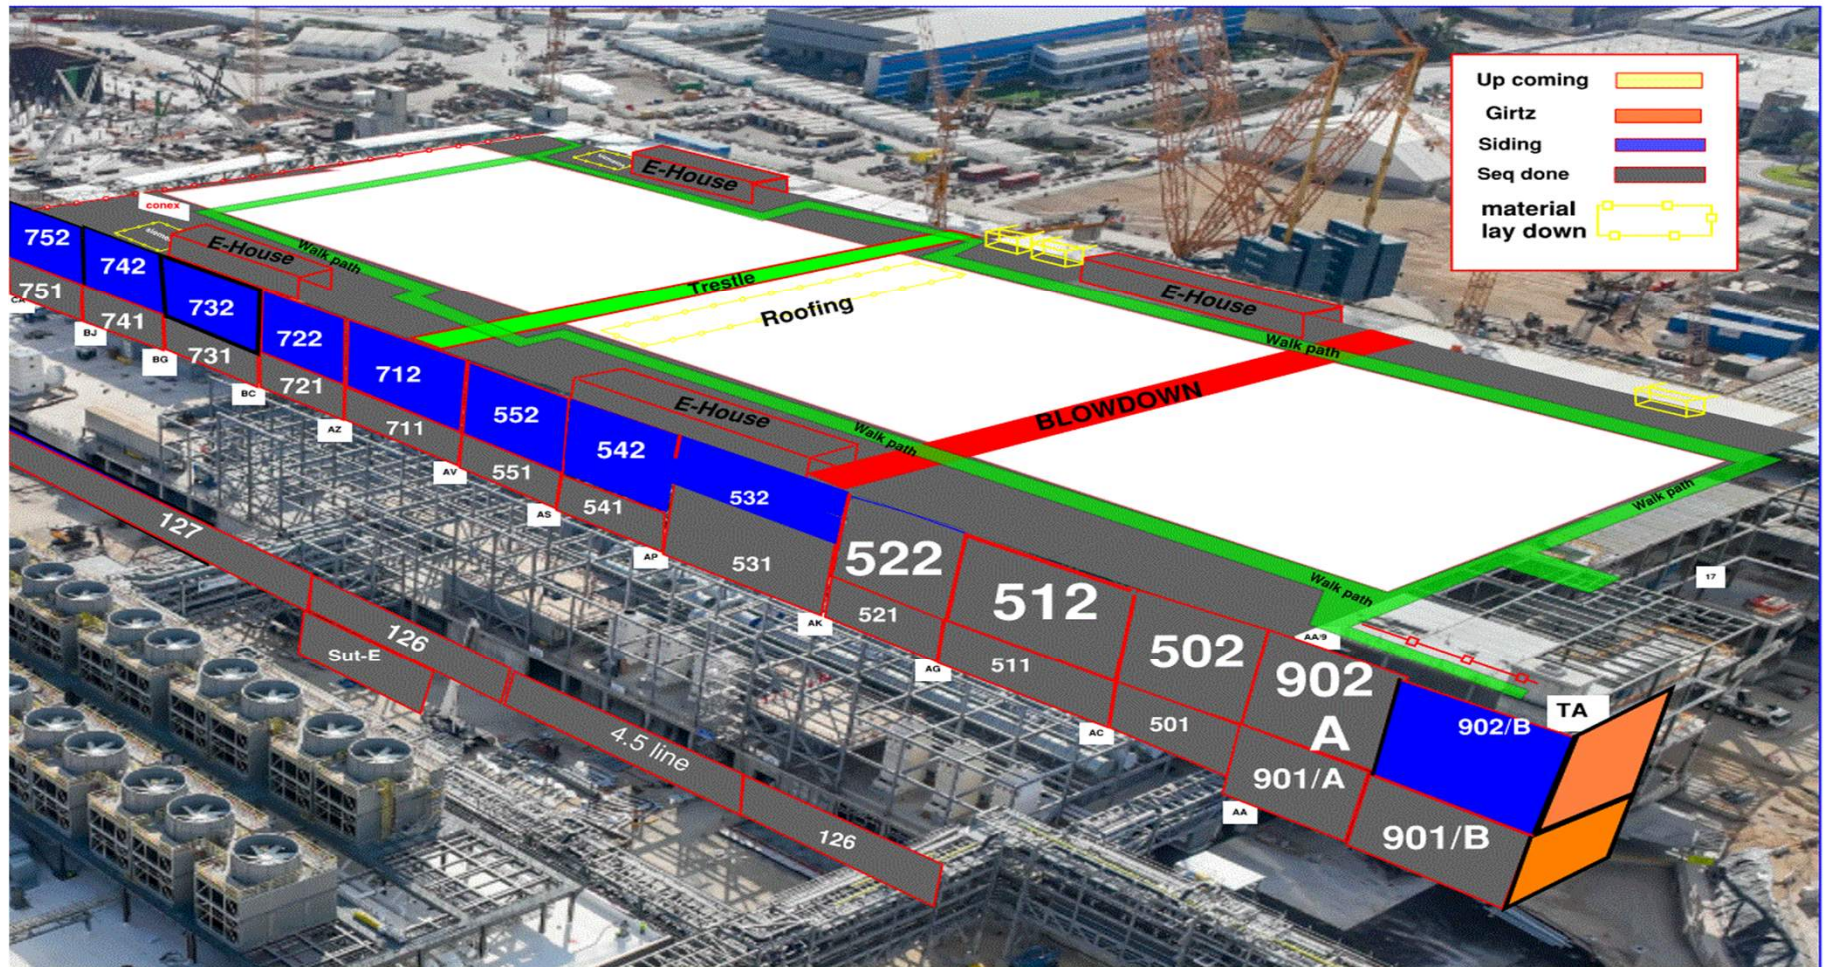

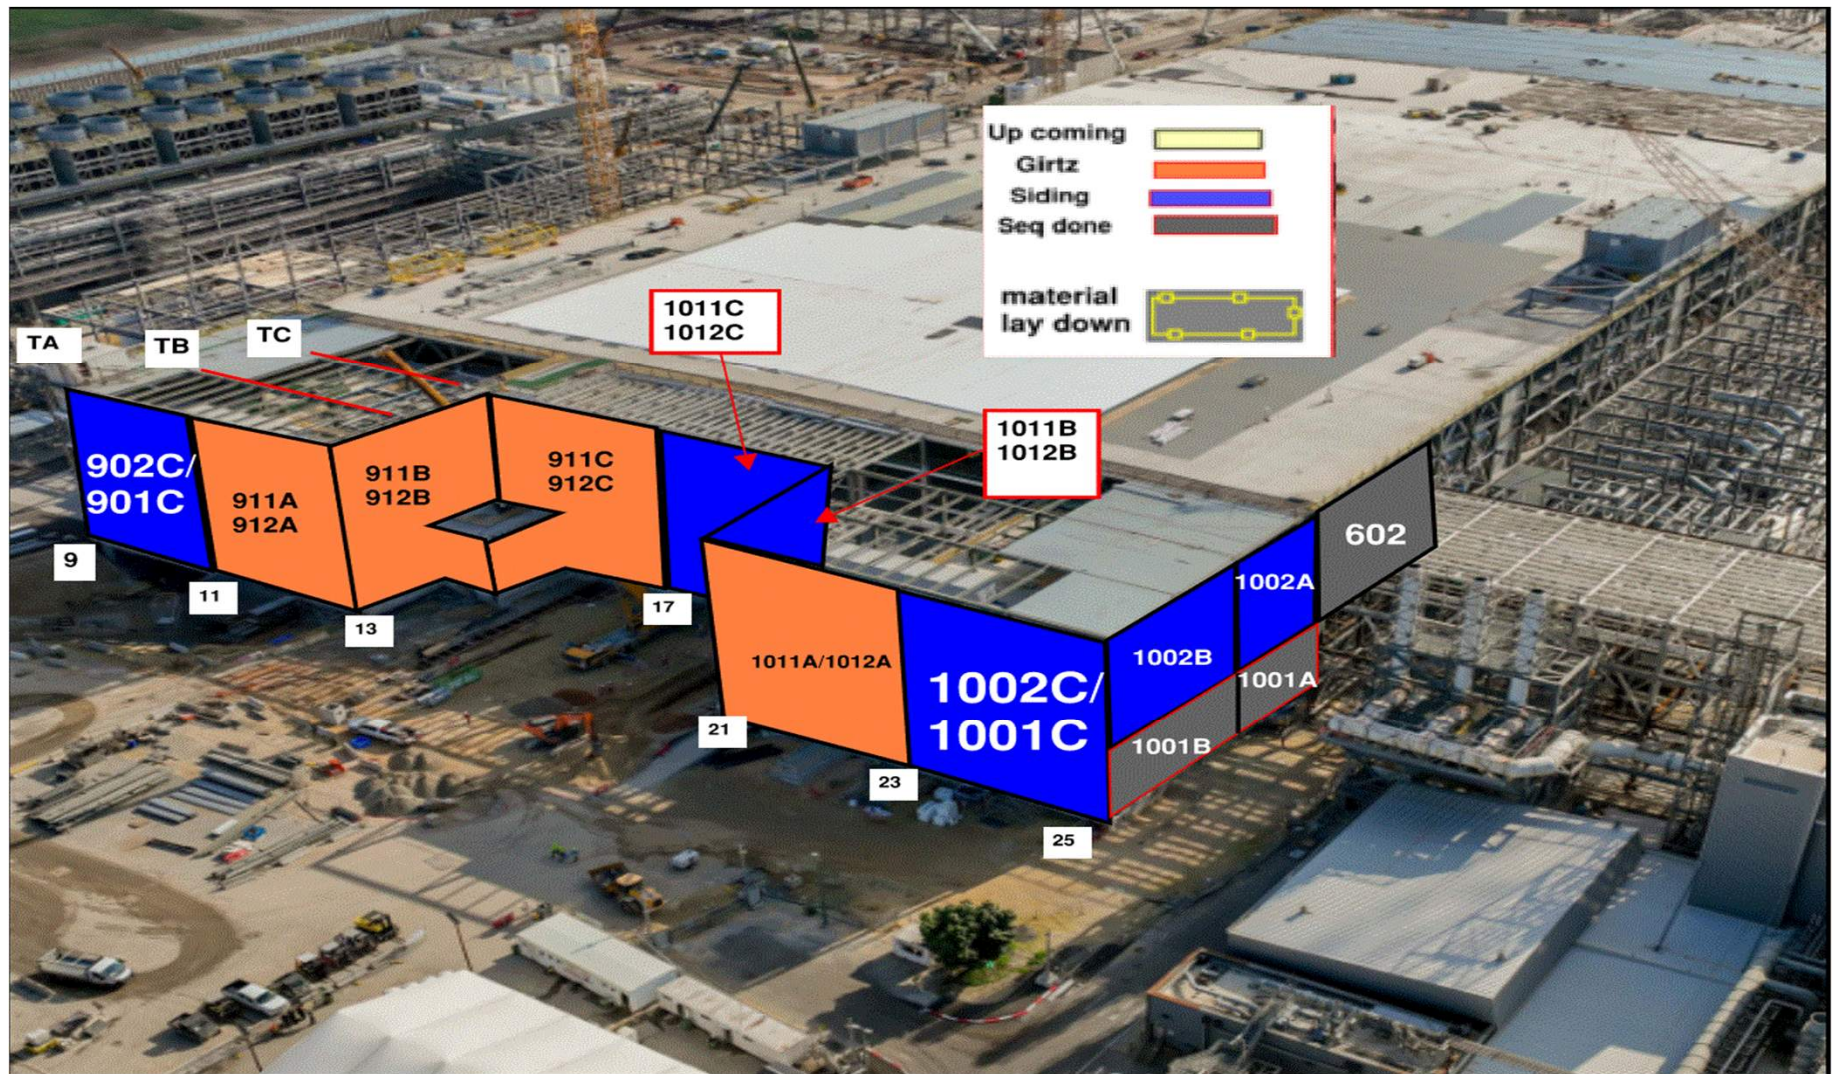

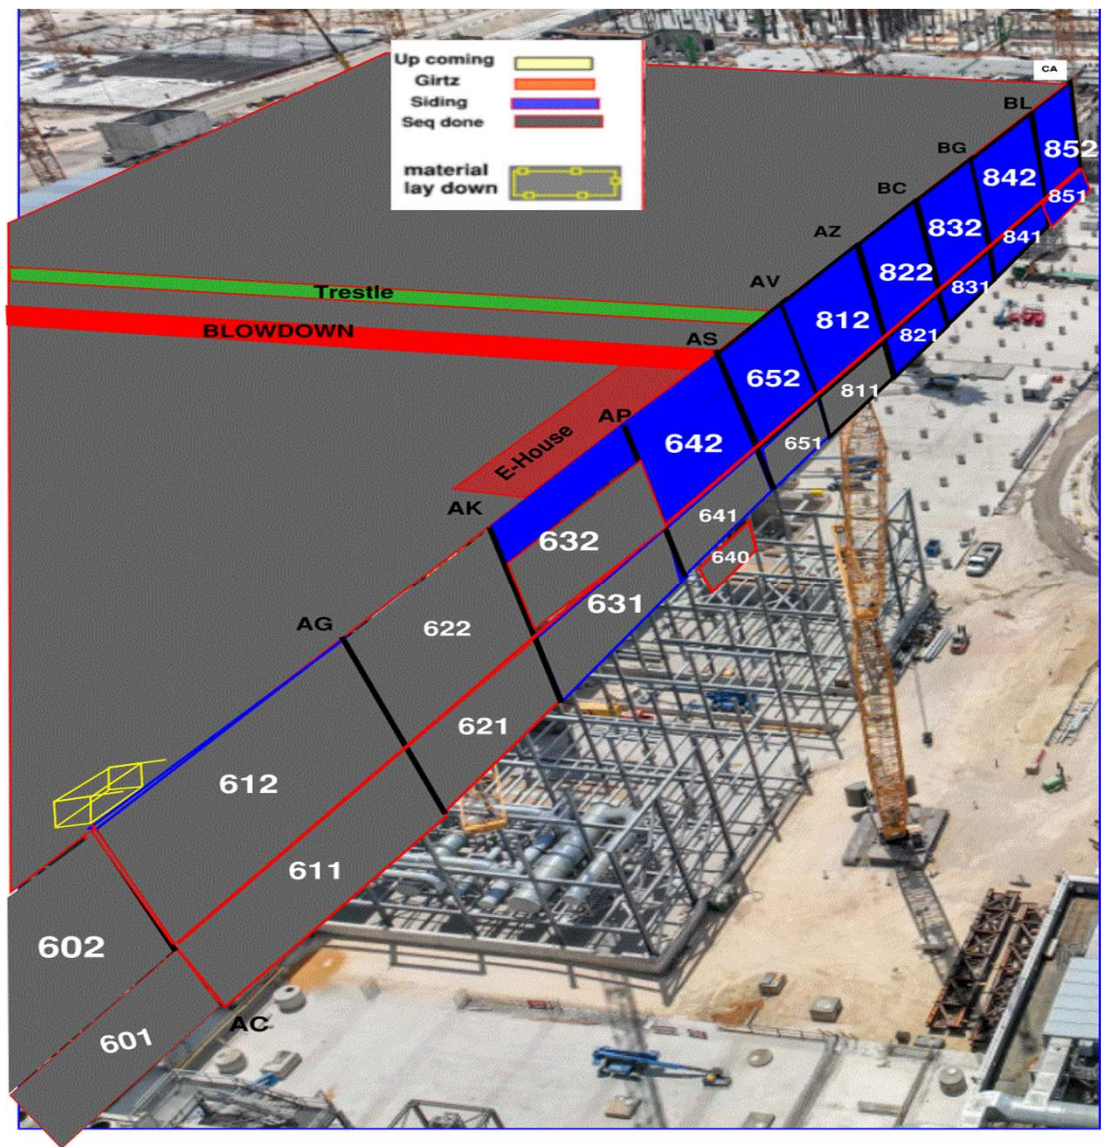

Siding - East FAB - PSSS

[illegible]

Siding - West FAB - JYG

BLOWDOWN 30%

[illegible]


SUT - West				
AP	5	AP2	5	AP
5	5	5	5	5
100%	100%	100%	100%	100%
1	1	1	1	1
2	2	2	2	2
3	3	3	3	3
4	4	4	4	4
5	5	5	5	5

EB-08A-SUB-4/UTILITY - 132.797

PSSS.1


Utility Level 1YA

PSSS Roof 2SA

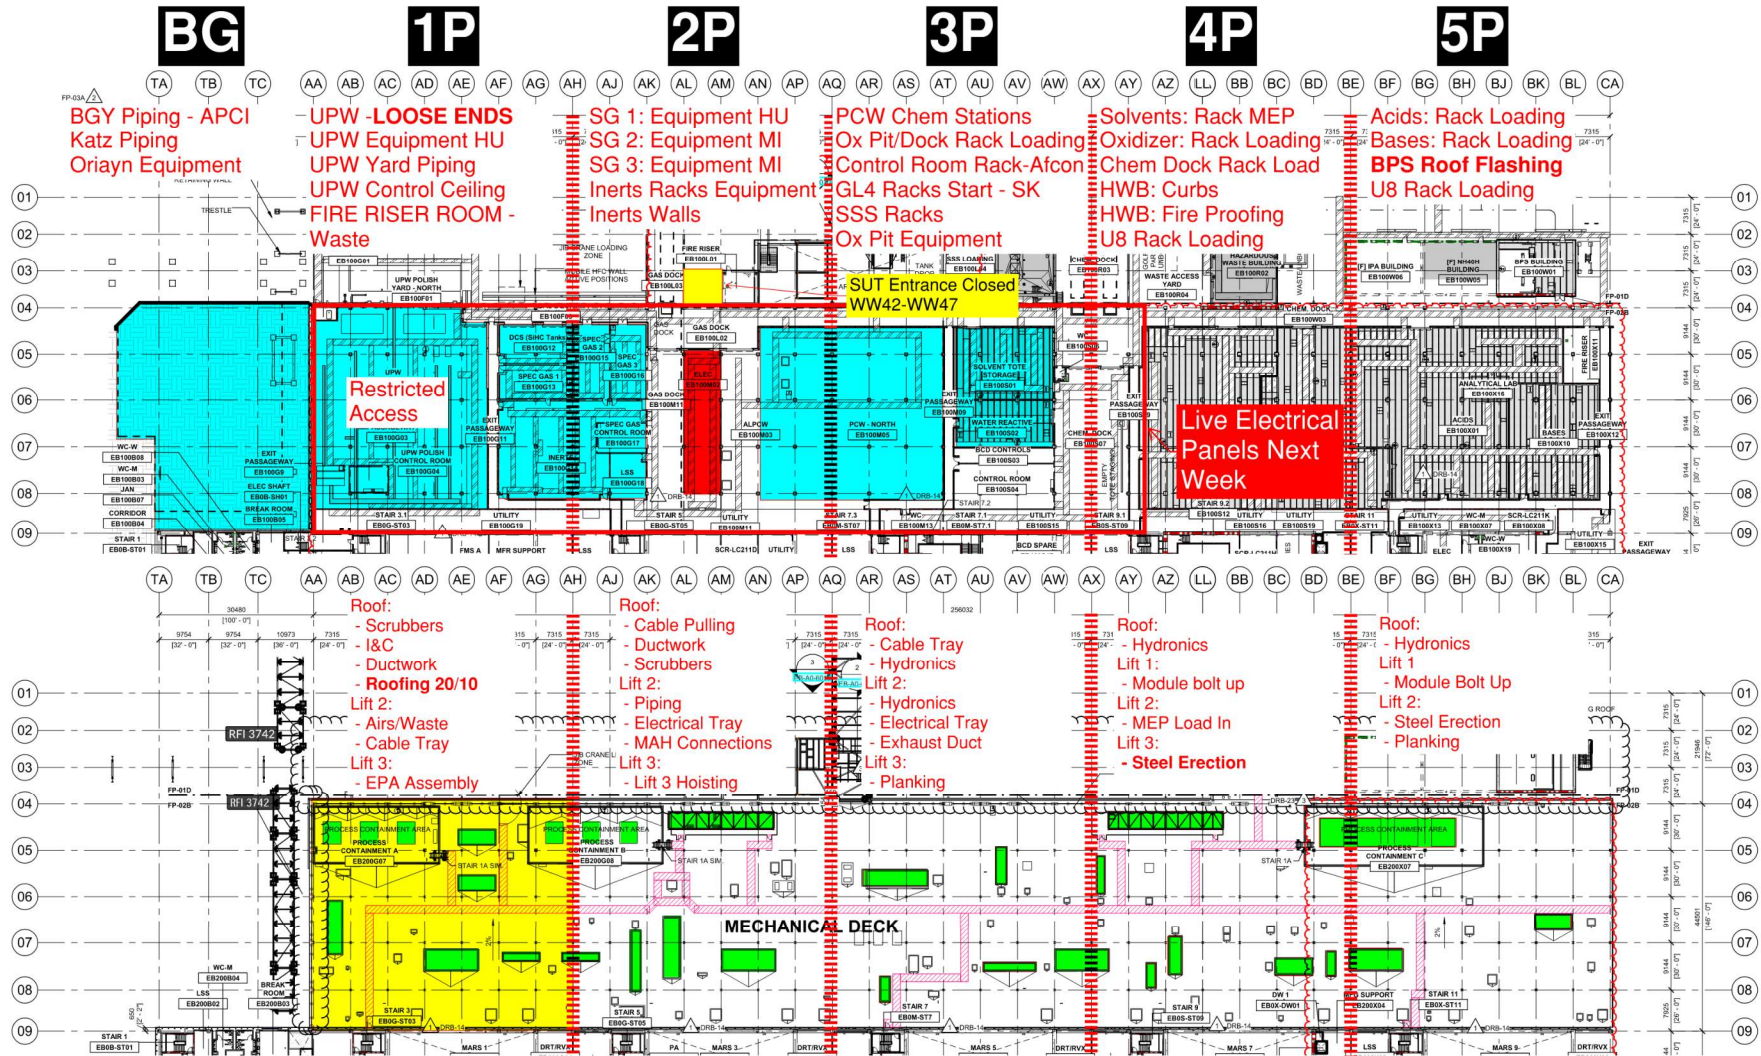


PSSS.2

Utility Level
1YA

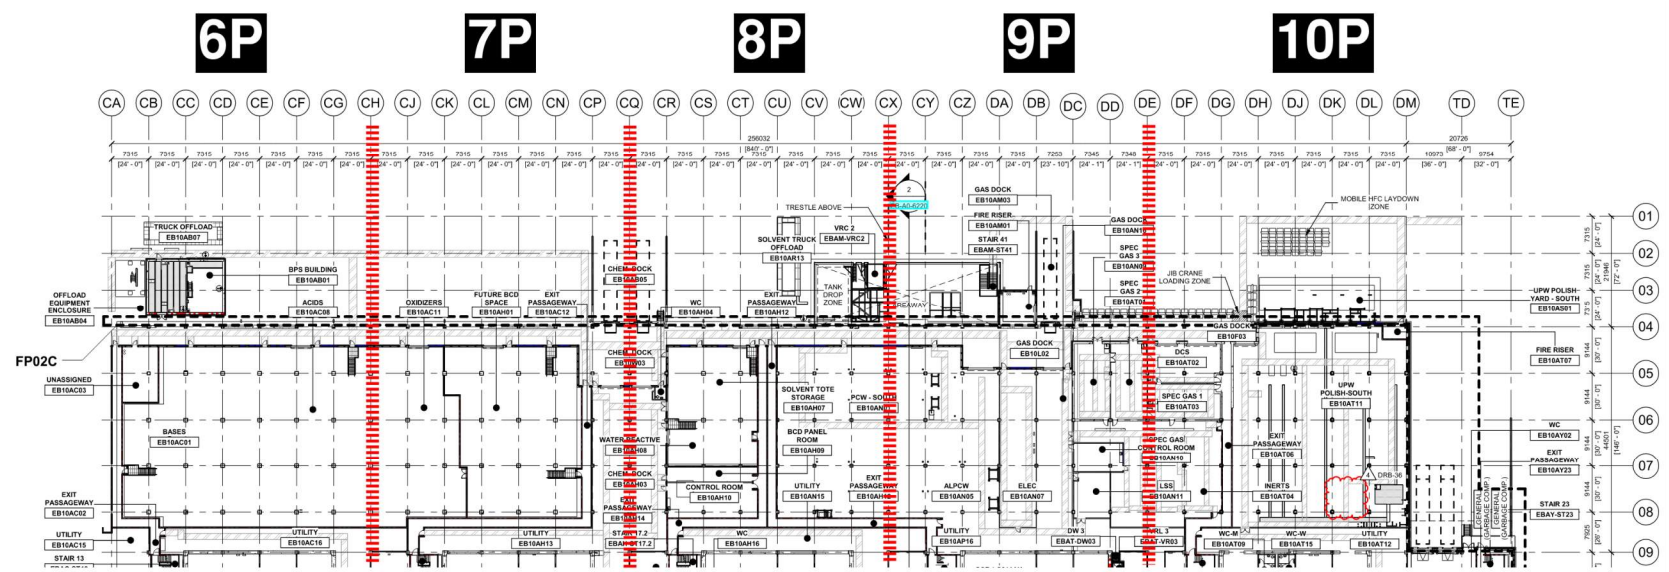

PSSS Roof
2SA

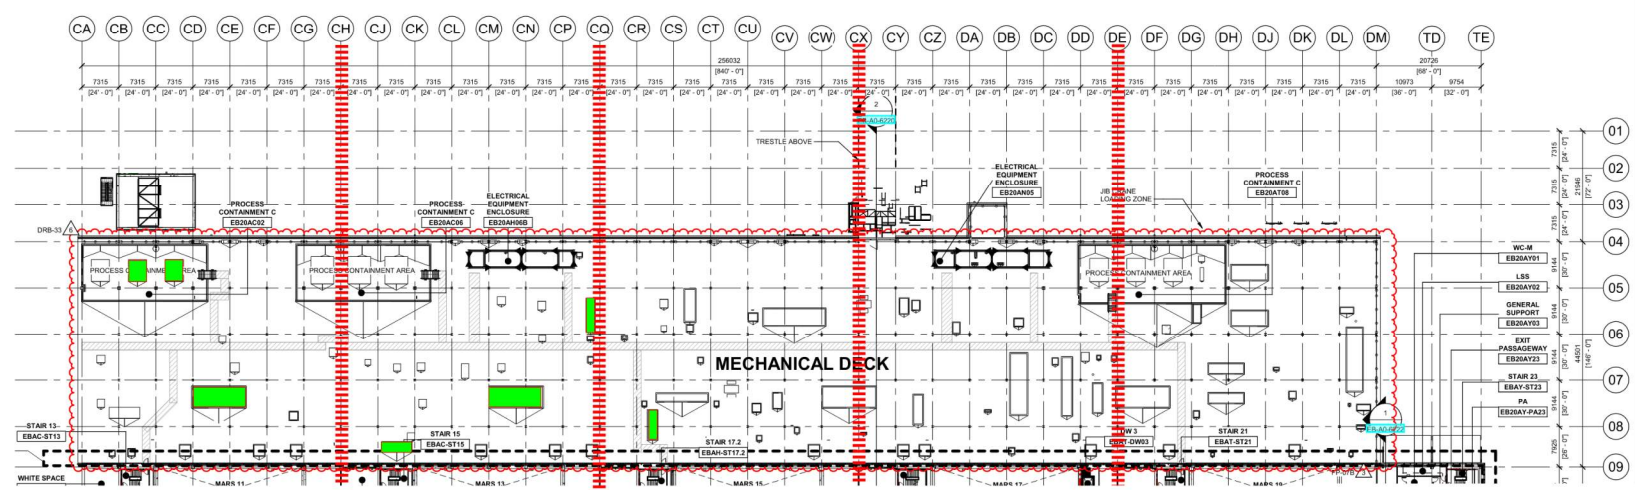










HOFFMAN CONSTRUCTION COMPANY

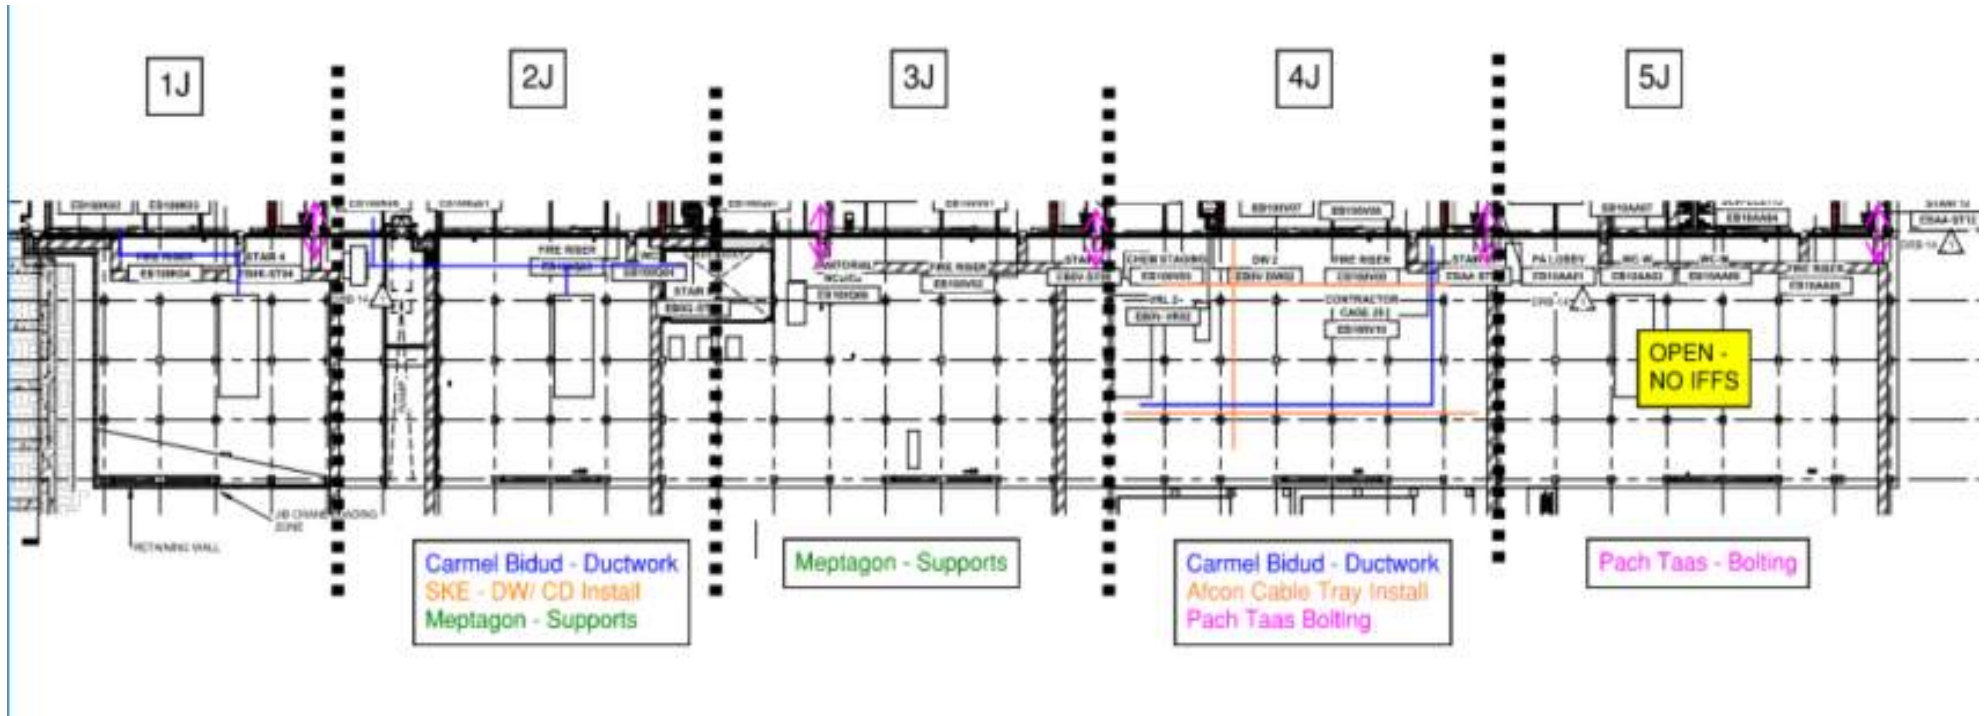


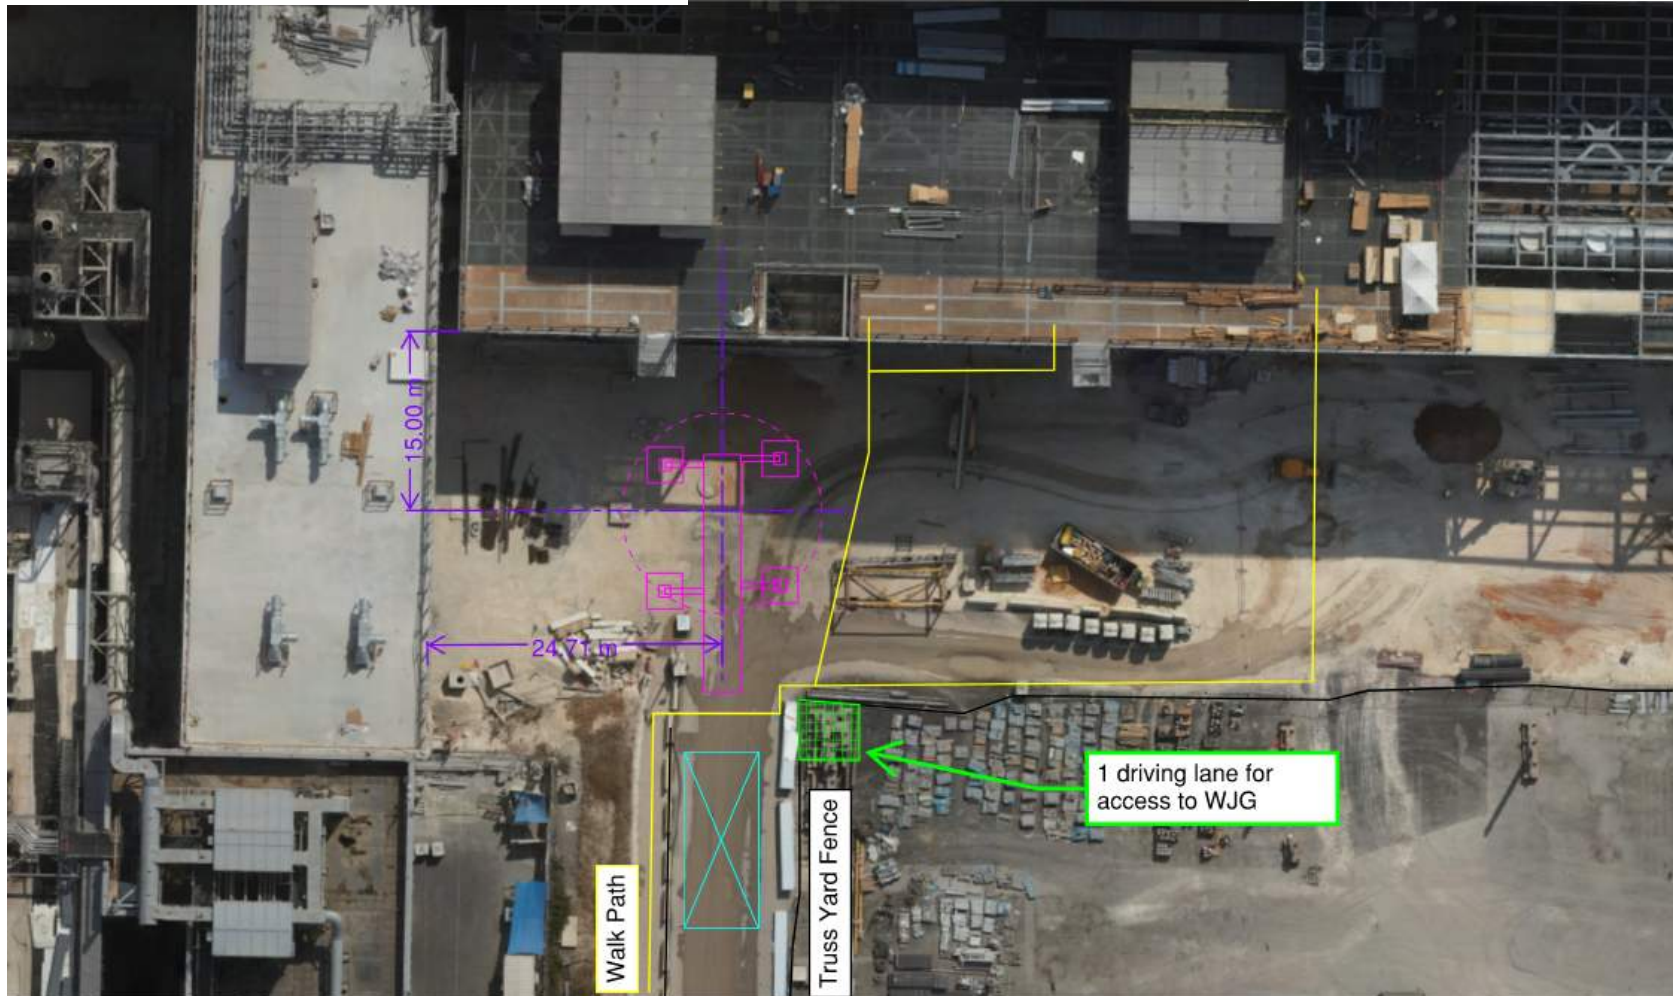




CUB 1

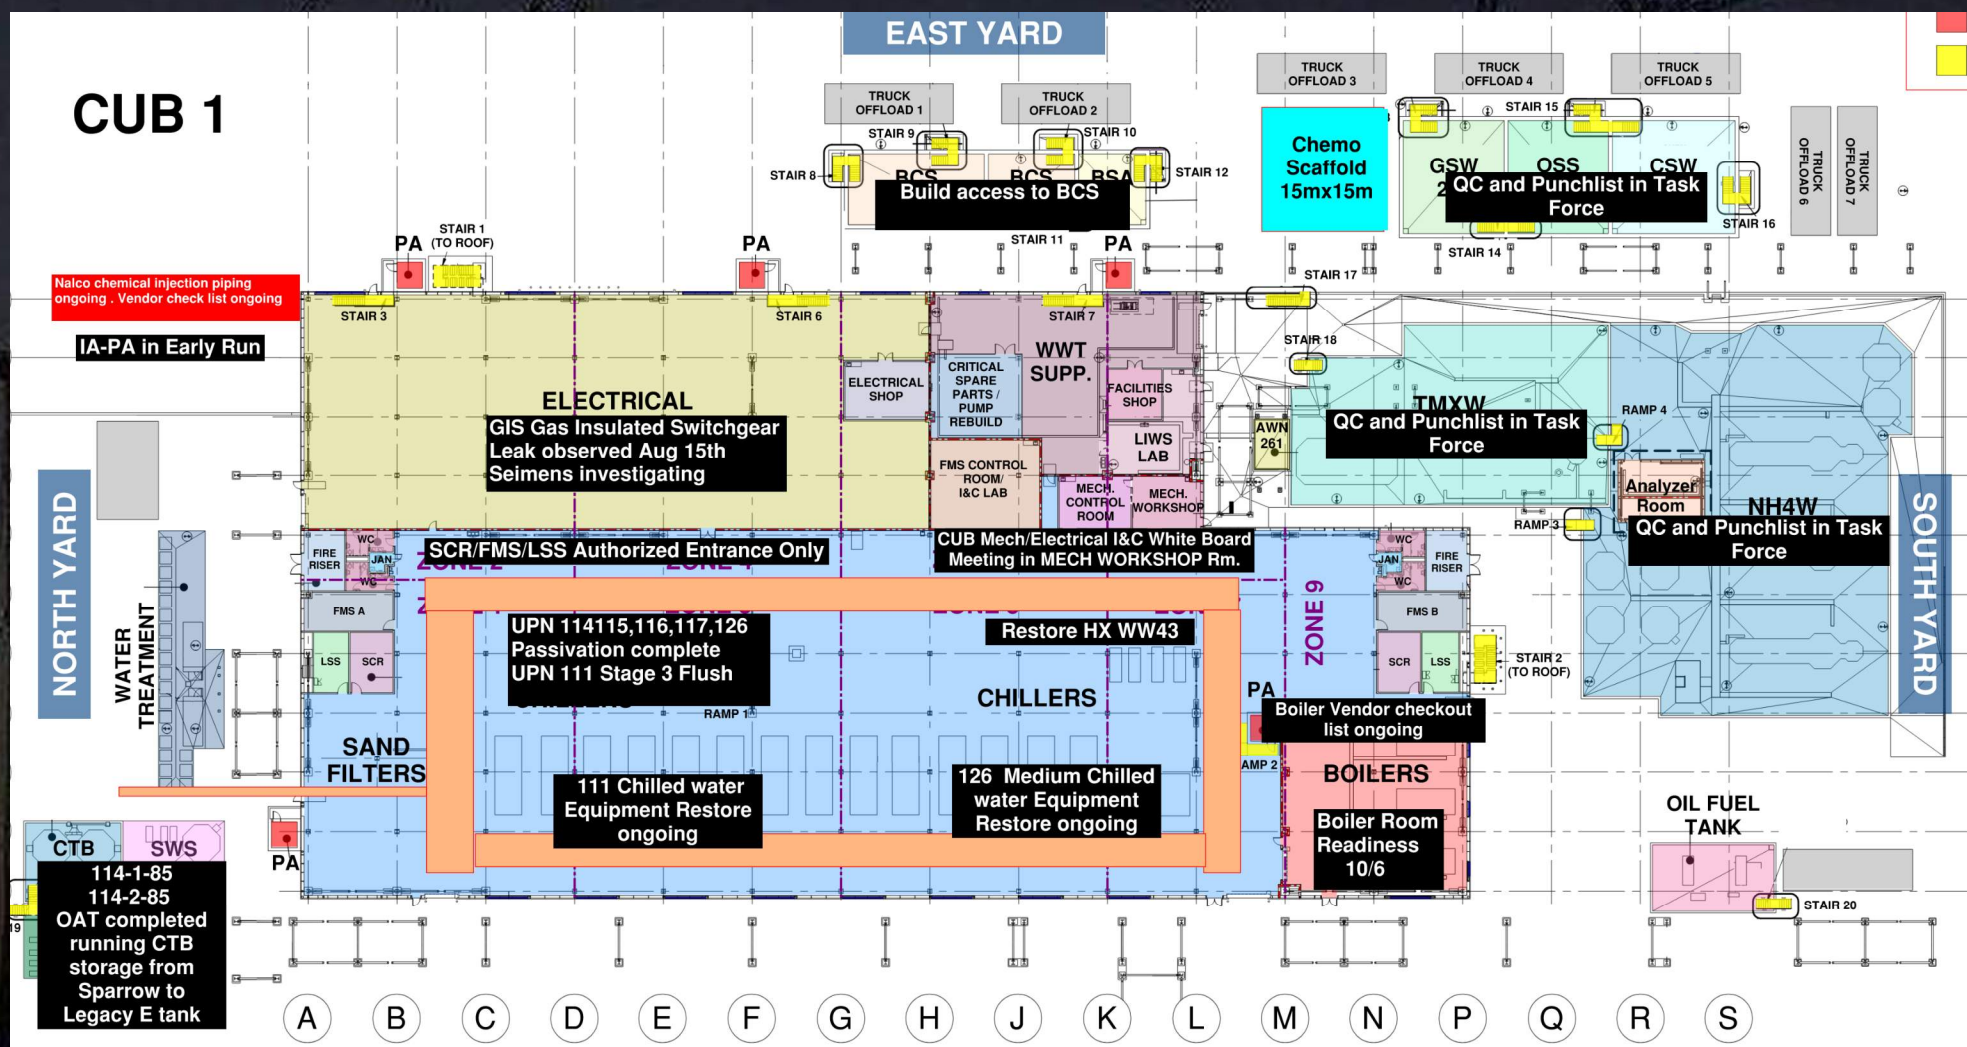

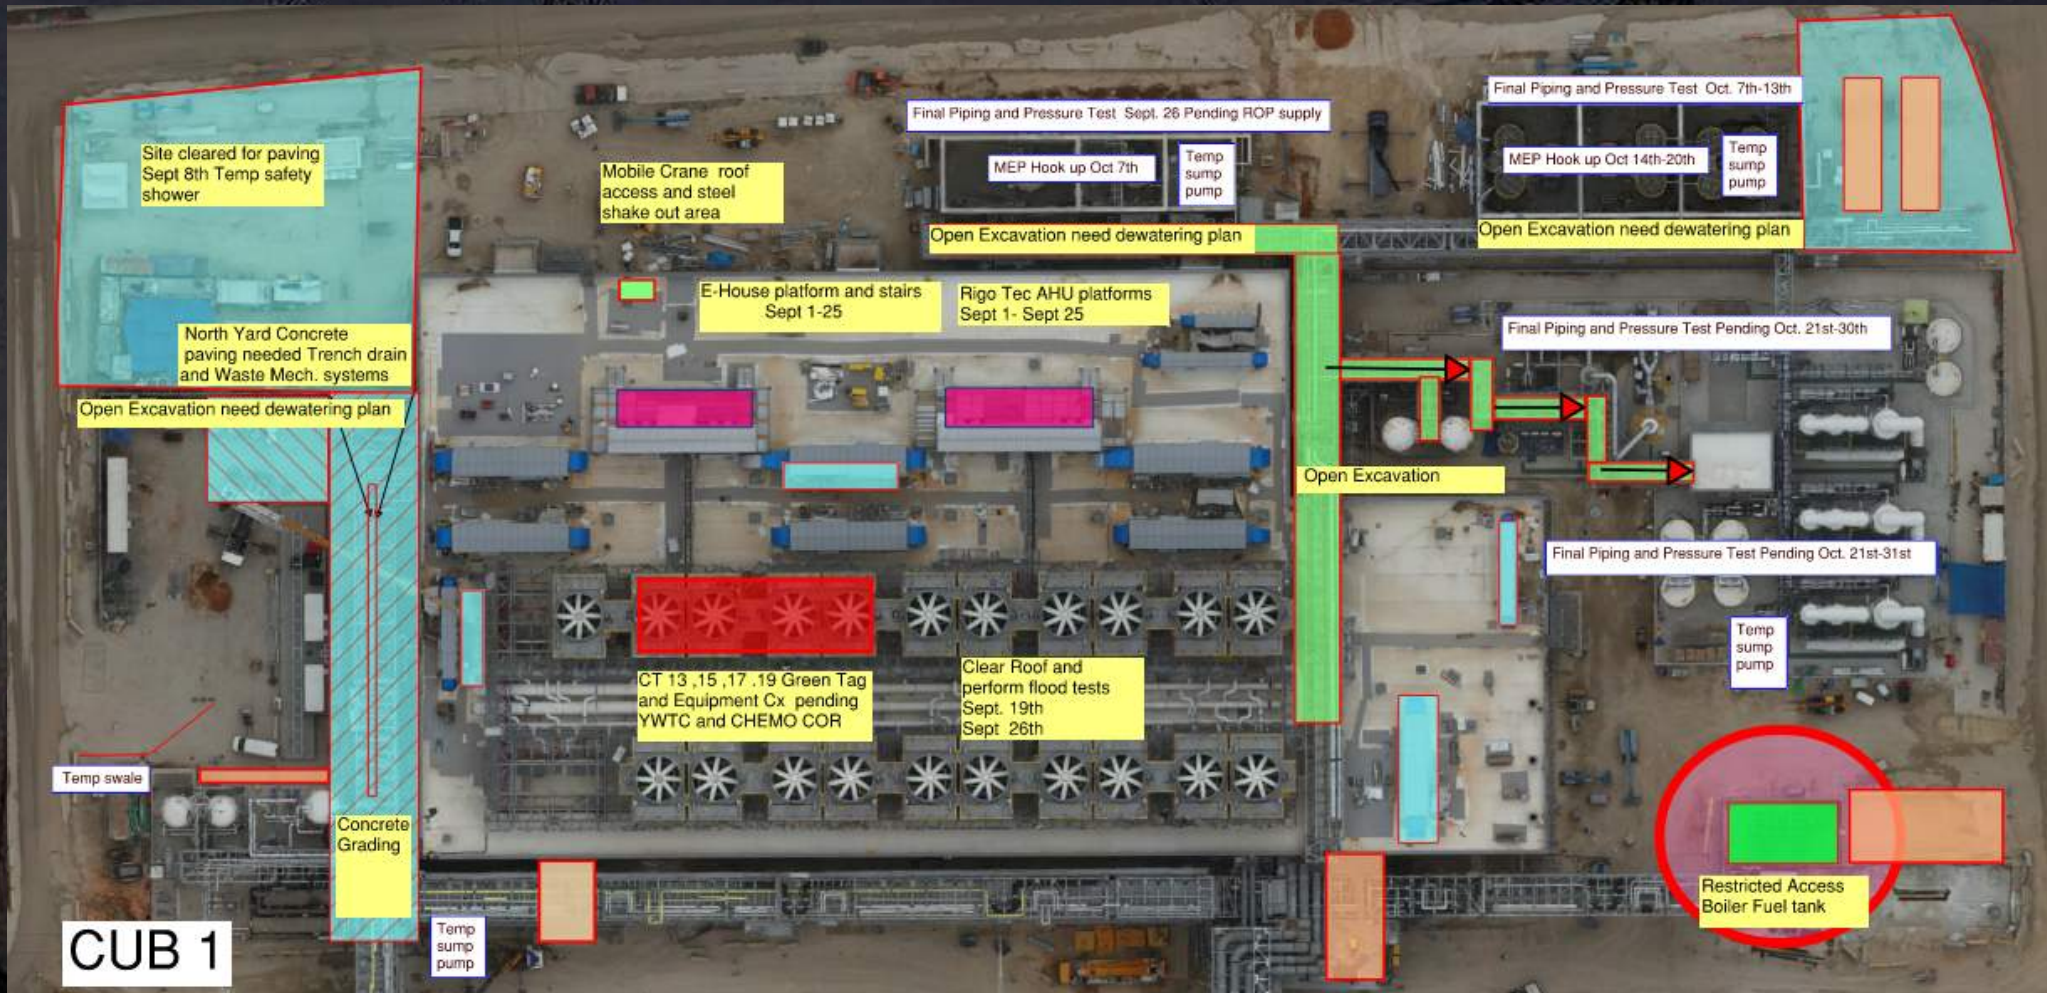

NORTH YARD



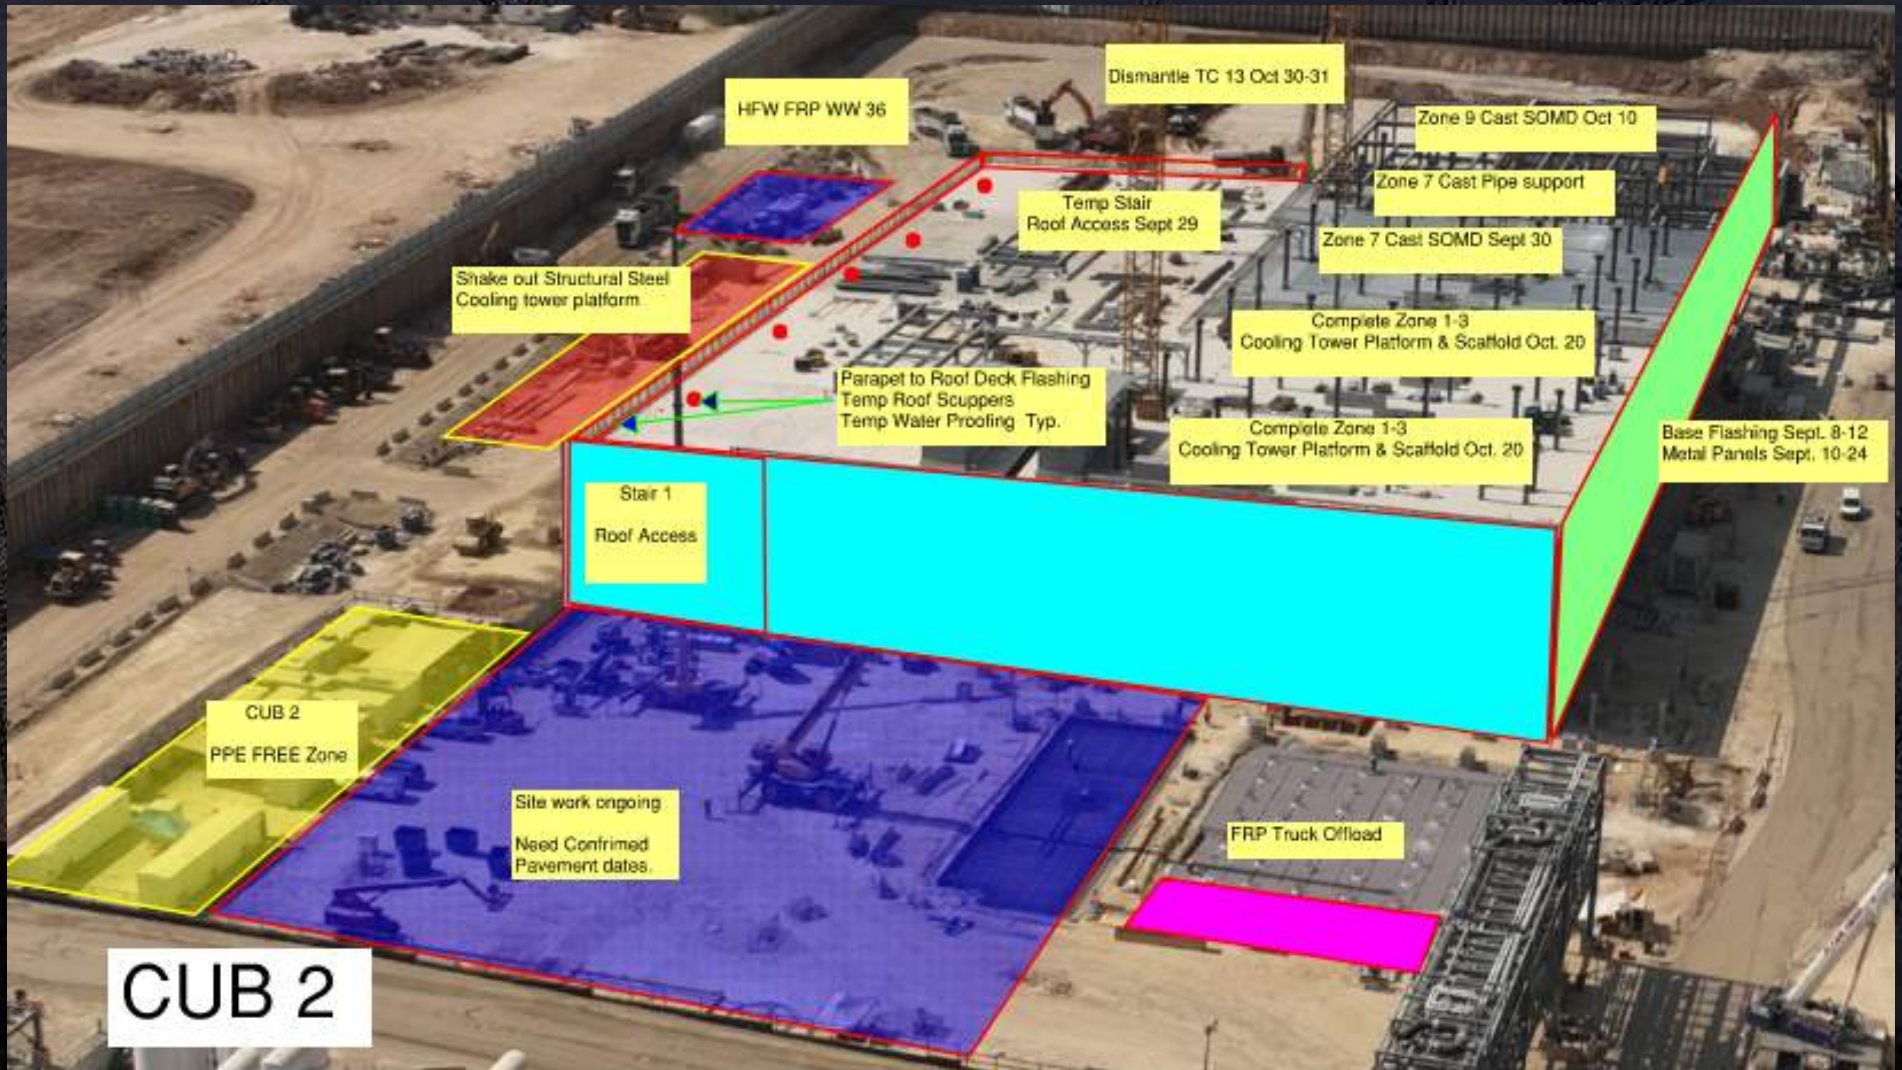





El mor:
LVSS: trays installing +
cable terminations.

Meptagon:
AIS E-gens: panel terminations
Generators: fire detection tests

TMTeam:
Paving Area
dates: 29-30.10.24
Impact: west road will be closed.




HOFFMAN CONSTRUCTION COMPANY

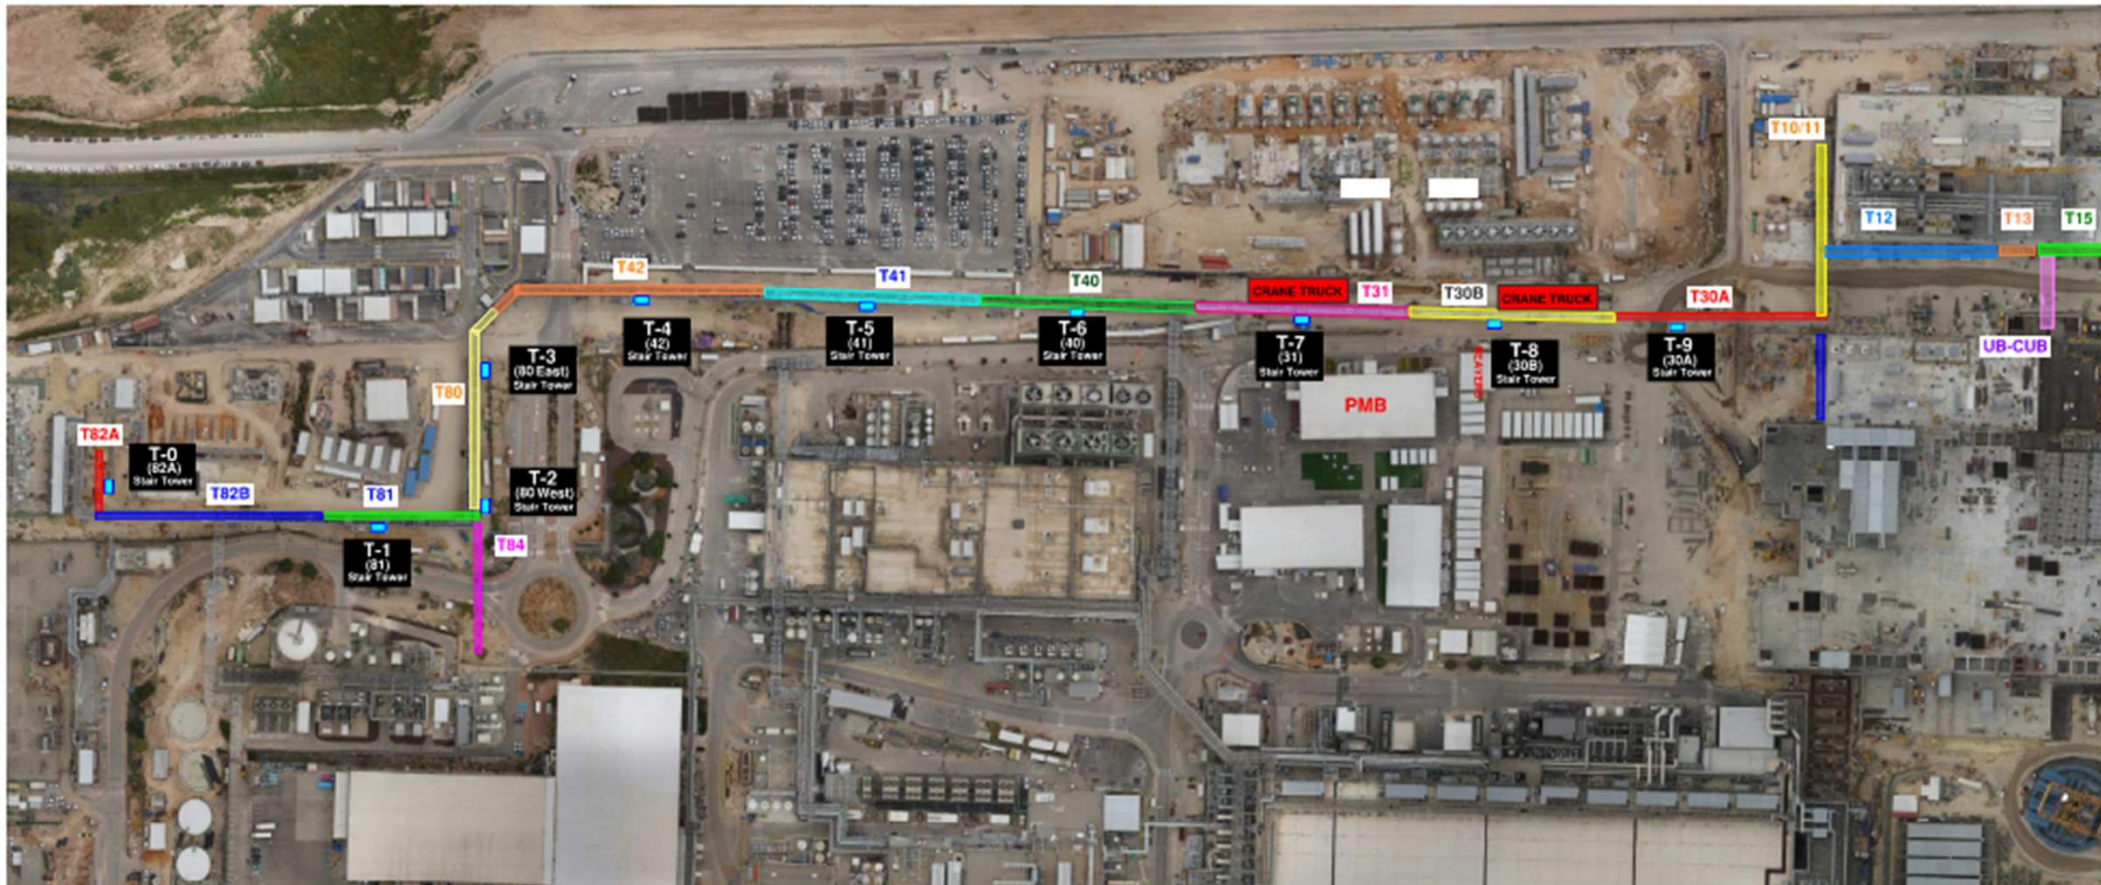

NO PARKING OR MATERIAL STORAGE

BSGS



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

T19 -ERECTION SEQUENCE

06/OCT

01/OCT


30/sep

29/sept

25-26/sept

23-24/sept

22/sep

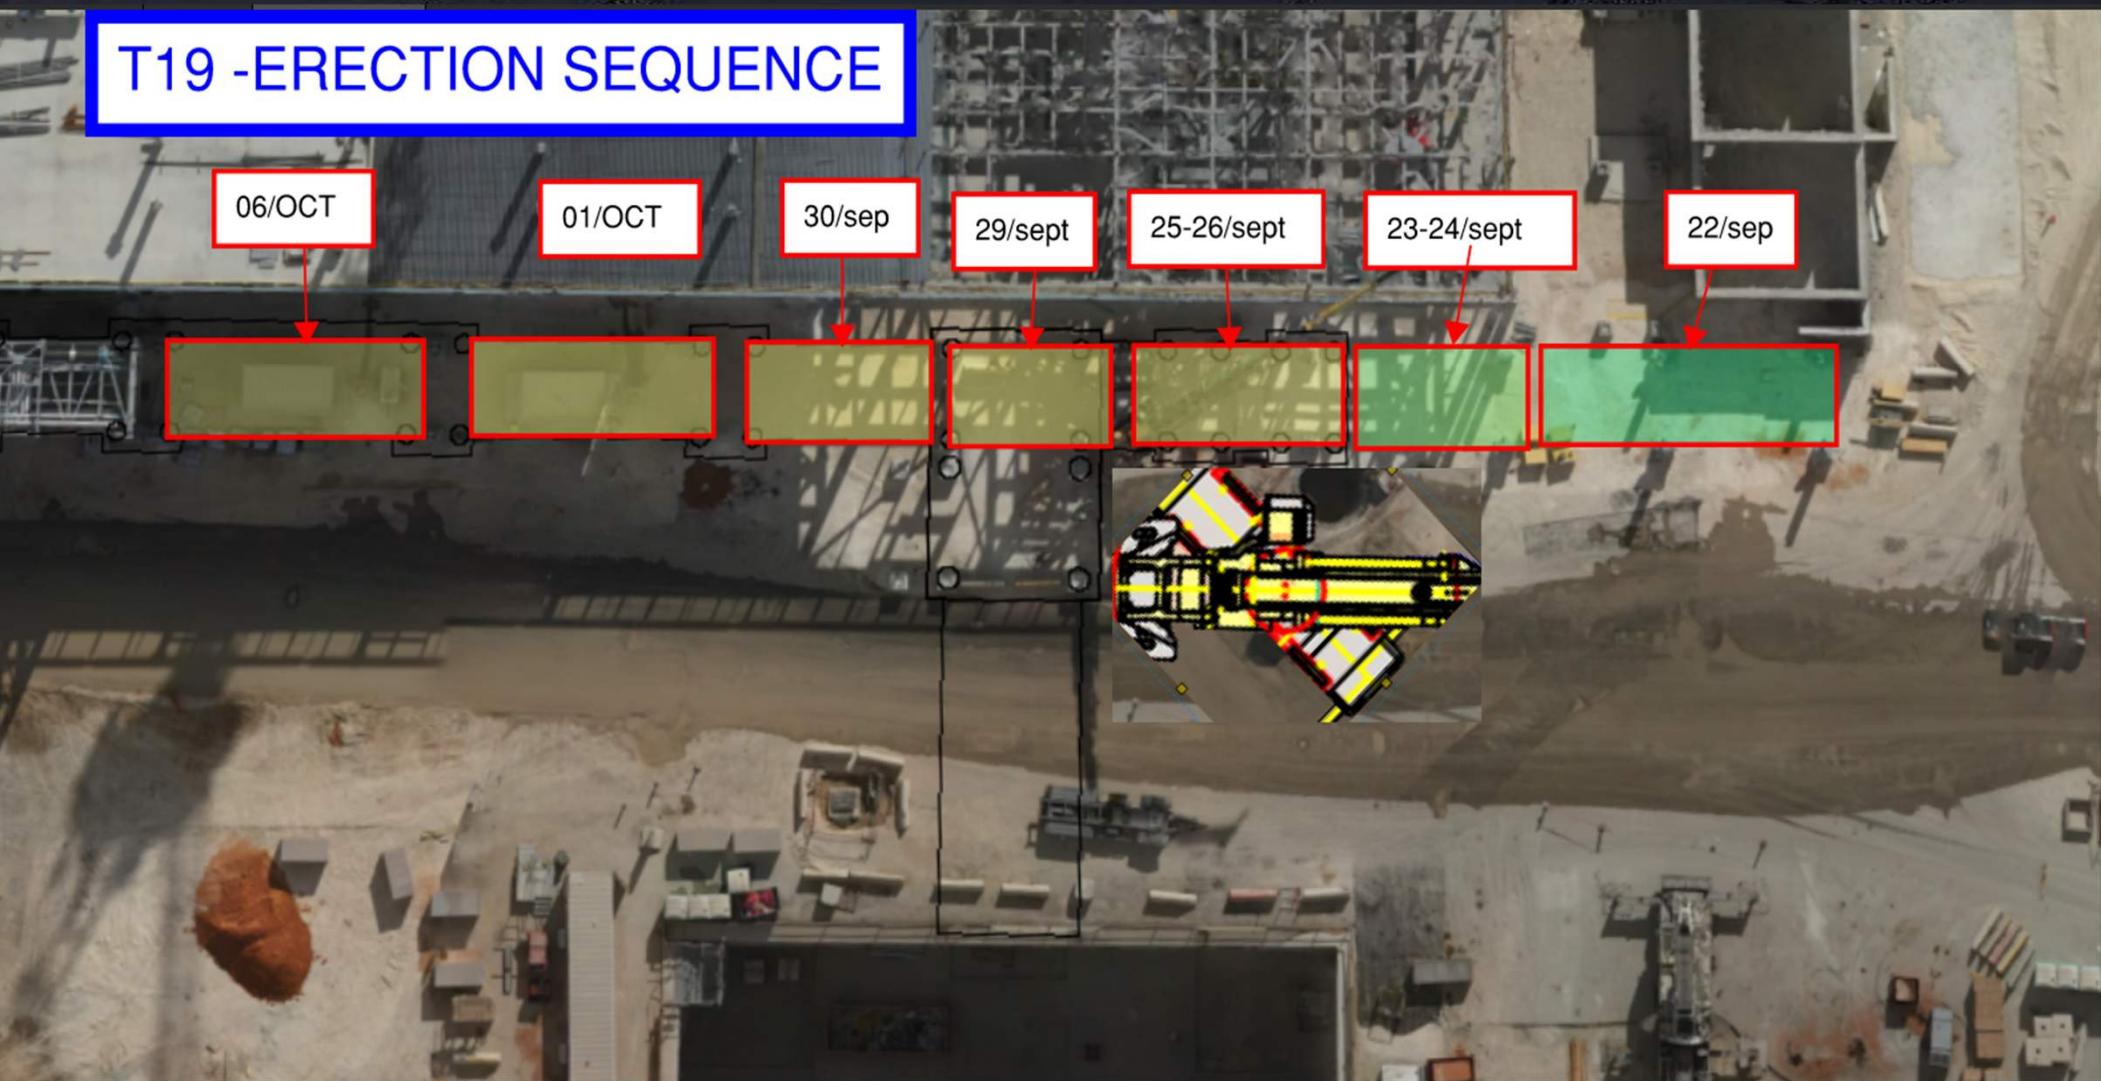

From main kiosk

Site temporary power

Legend :

— 22KV Line

— 400V Line

109 - Kiosk

● - Lift Station

Fab 38.2

Upcoming shutdown
Fab(all floors); JG; PSSS
05-Oct 00:00 to 05:00
W1;W2;W3
E1;E2;E3
Sunday morning

Cub 2

Cub 1

TC-9
On Gen
power
10.09

630A
SE
Done

TC-7
On Gen power
Done

630A
NE
Done

TC-5
Done

TC-3
Done

TC-10
Done

630A
SW
Done

TC-8
Done

630A
NW
Done

TC-6
Done

TC-4
Done

TC-13
Done

TC-12
Done

From main

To 115



Daily Coordination Meeting

Site Logistics

North






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North IQ Staging Access

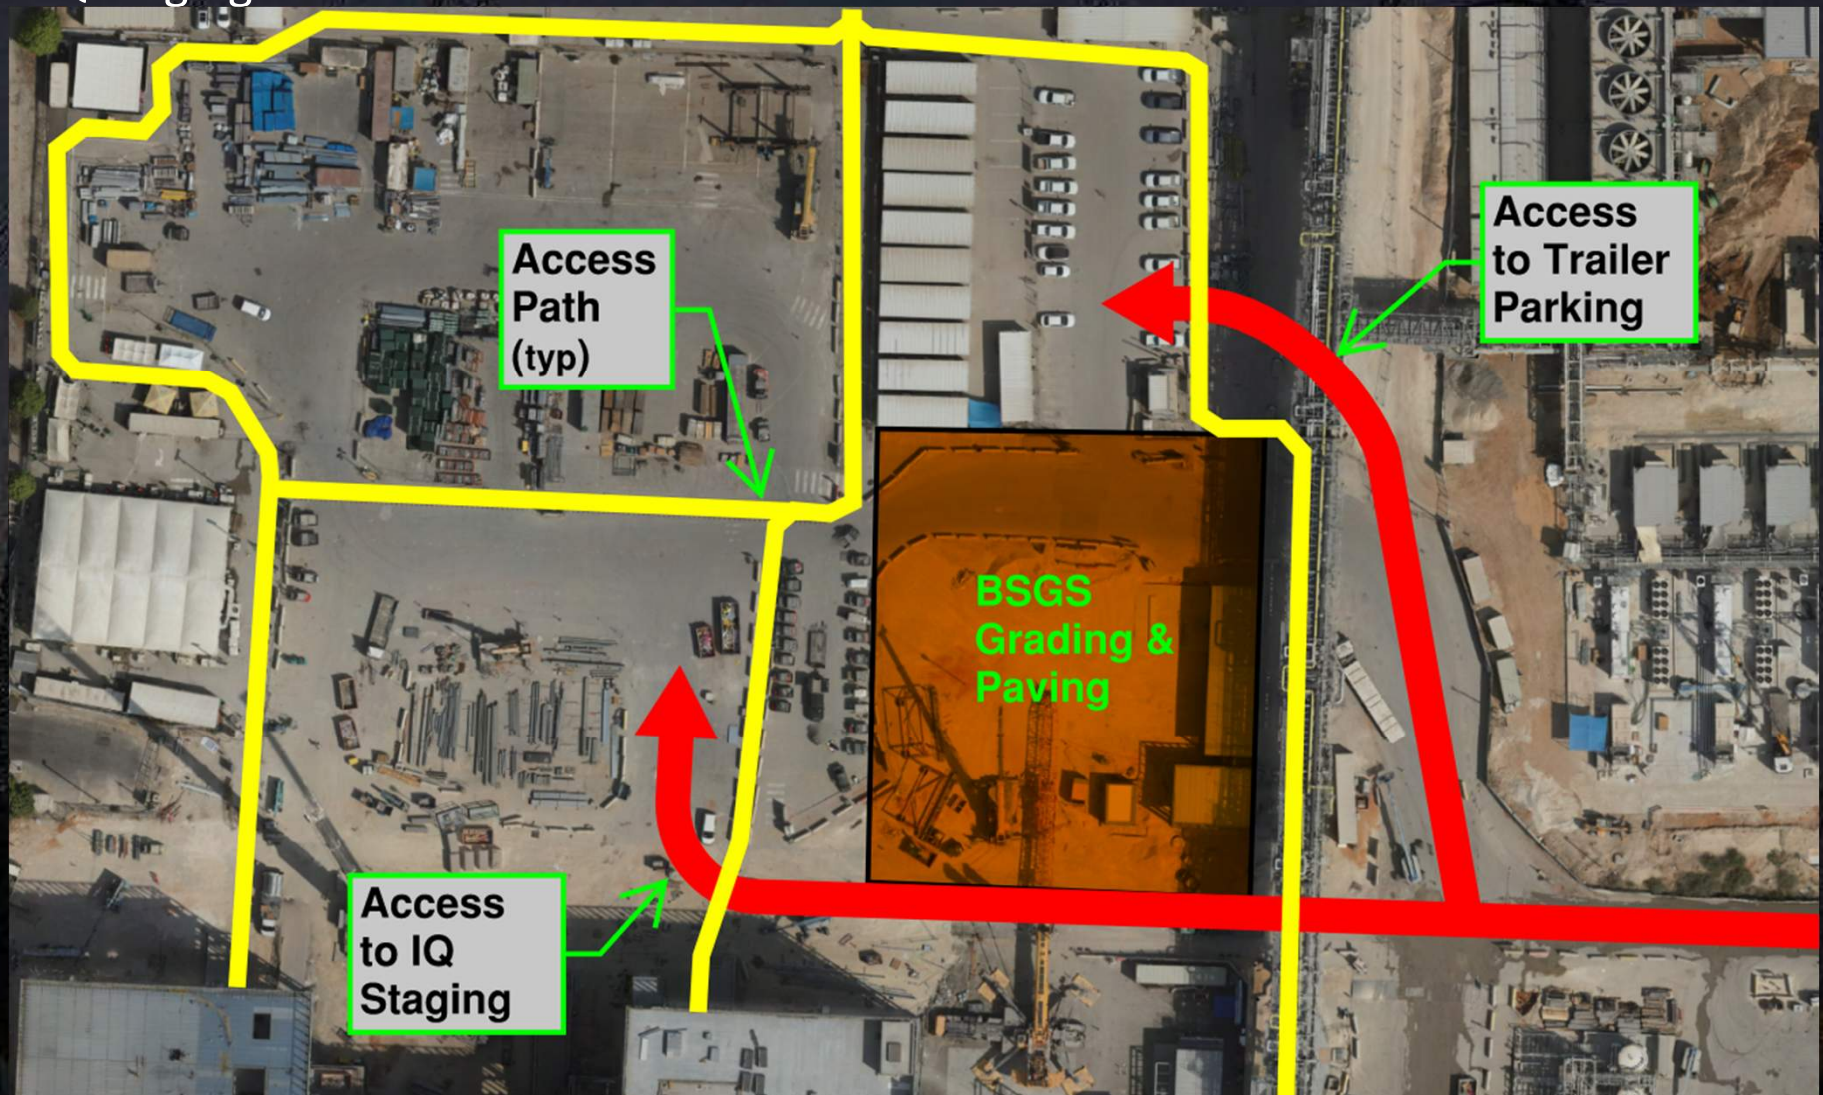




Daily Coordination Meeting

Site Logistics

South

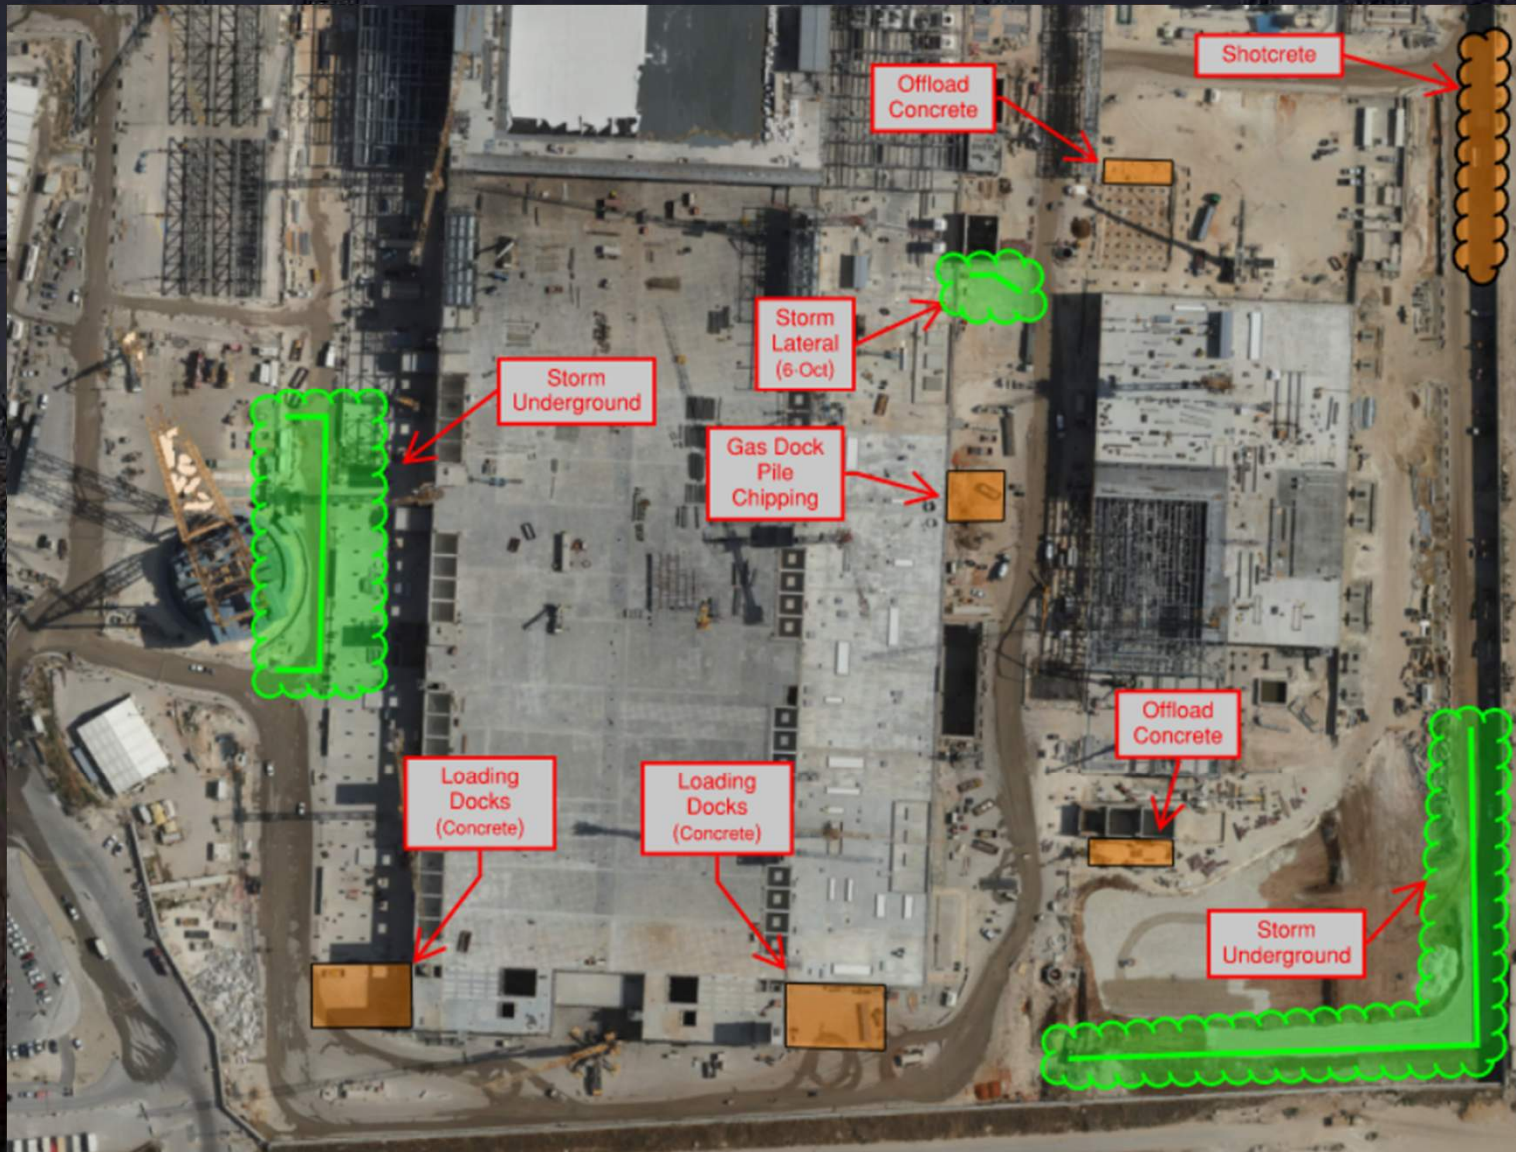





Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

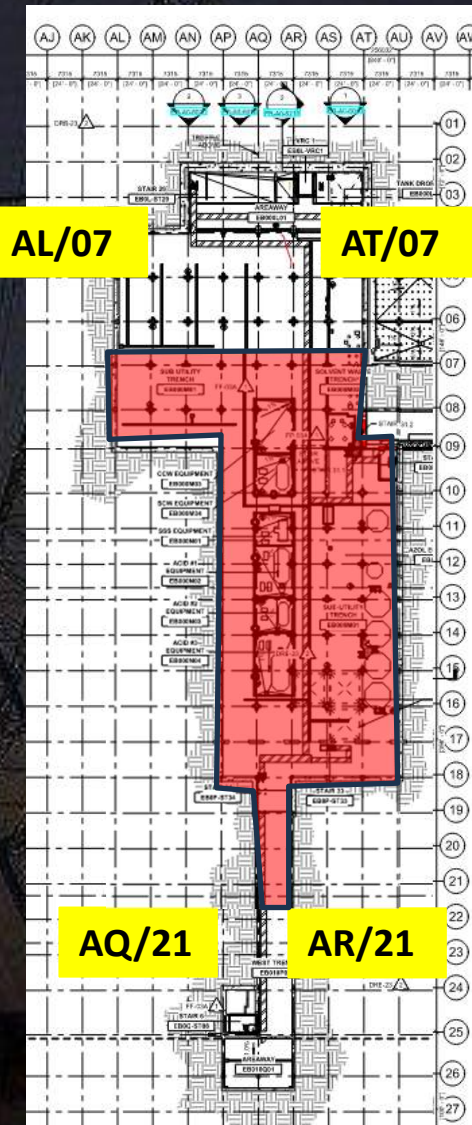

SUT2

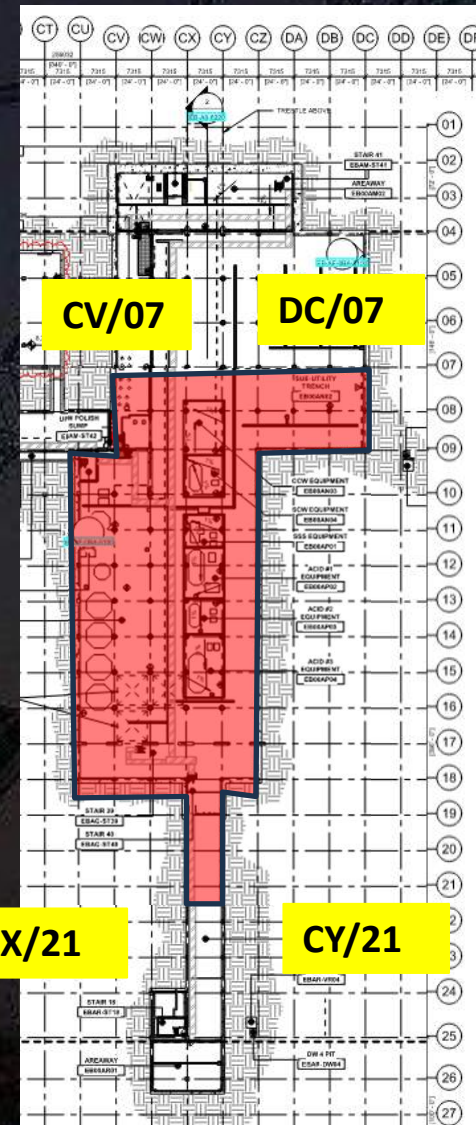




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting


Site Logistics - Protected Areas (Utility Level)

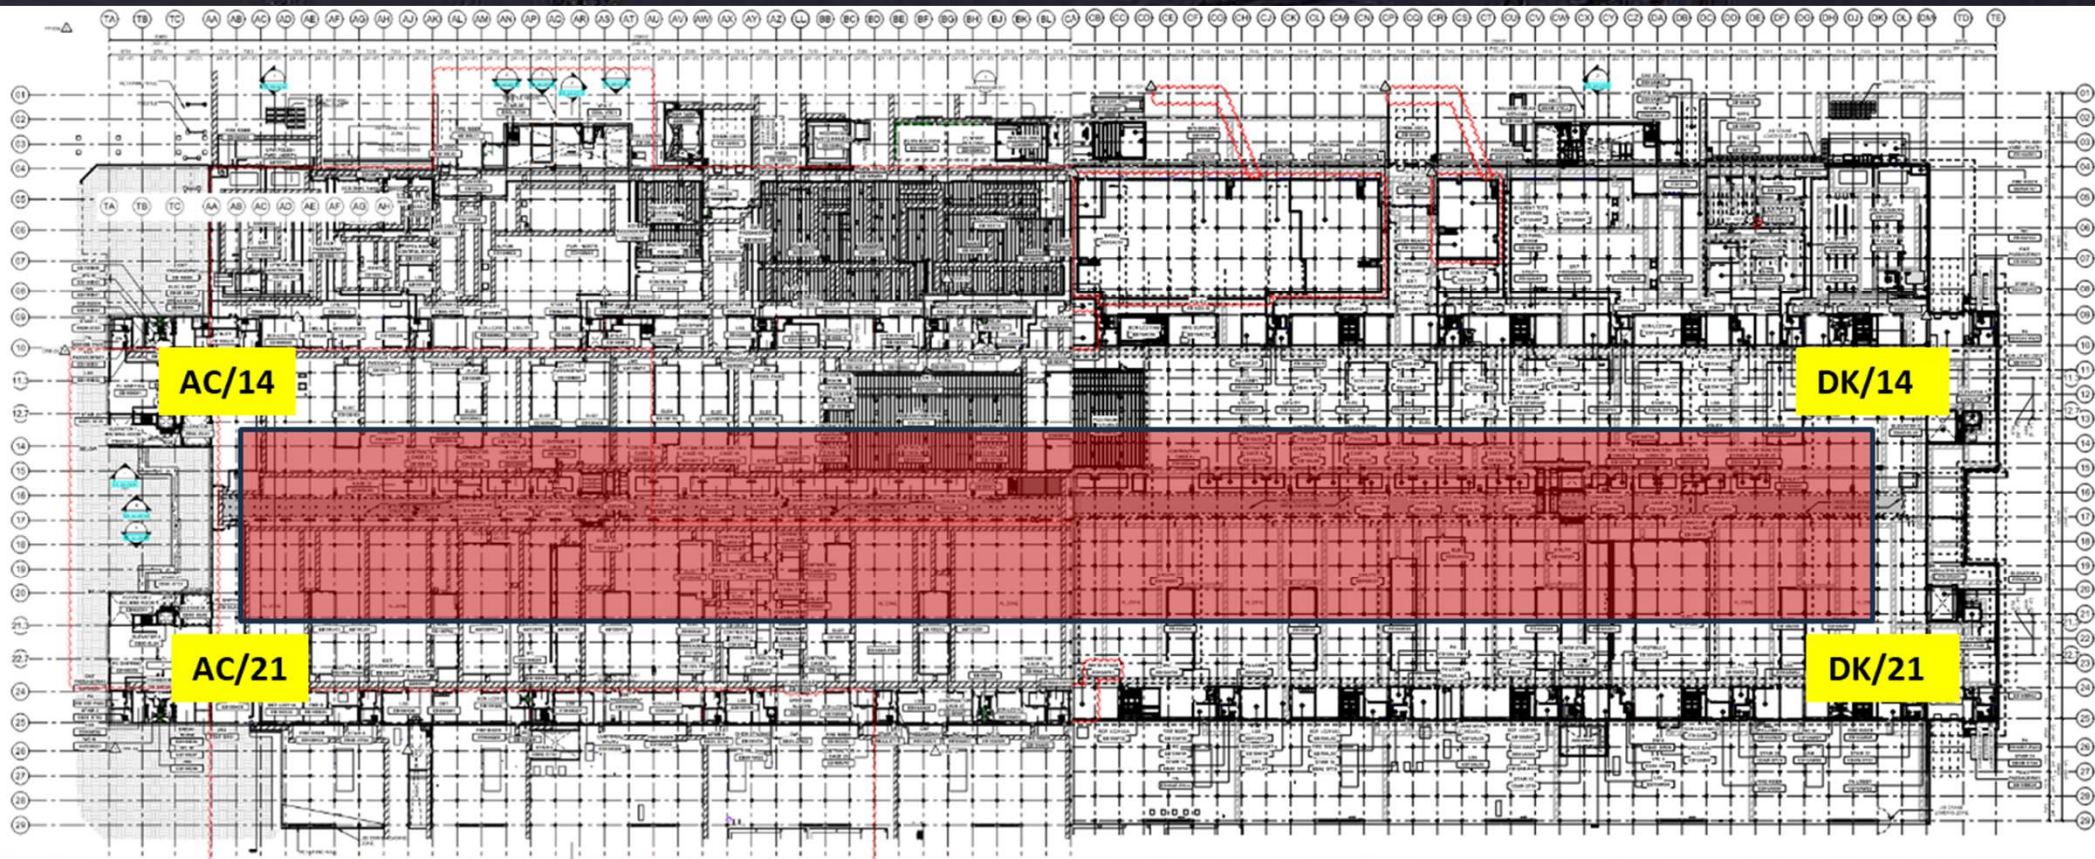



Daily Coordination Meeting

Site Logistics - Protected Areas (Subfab Level)

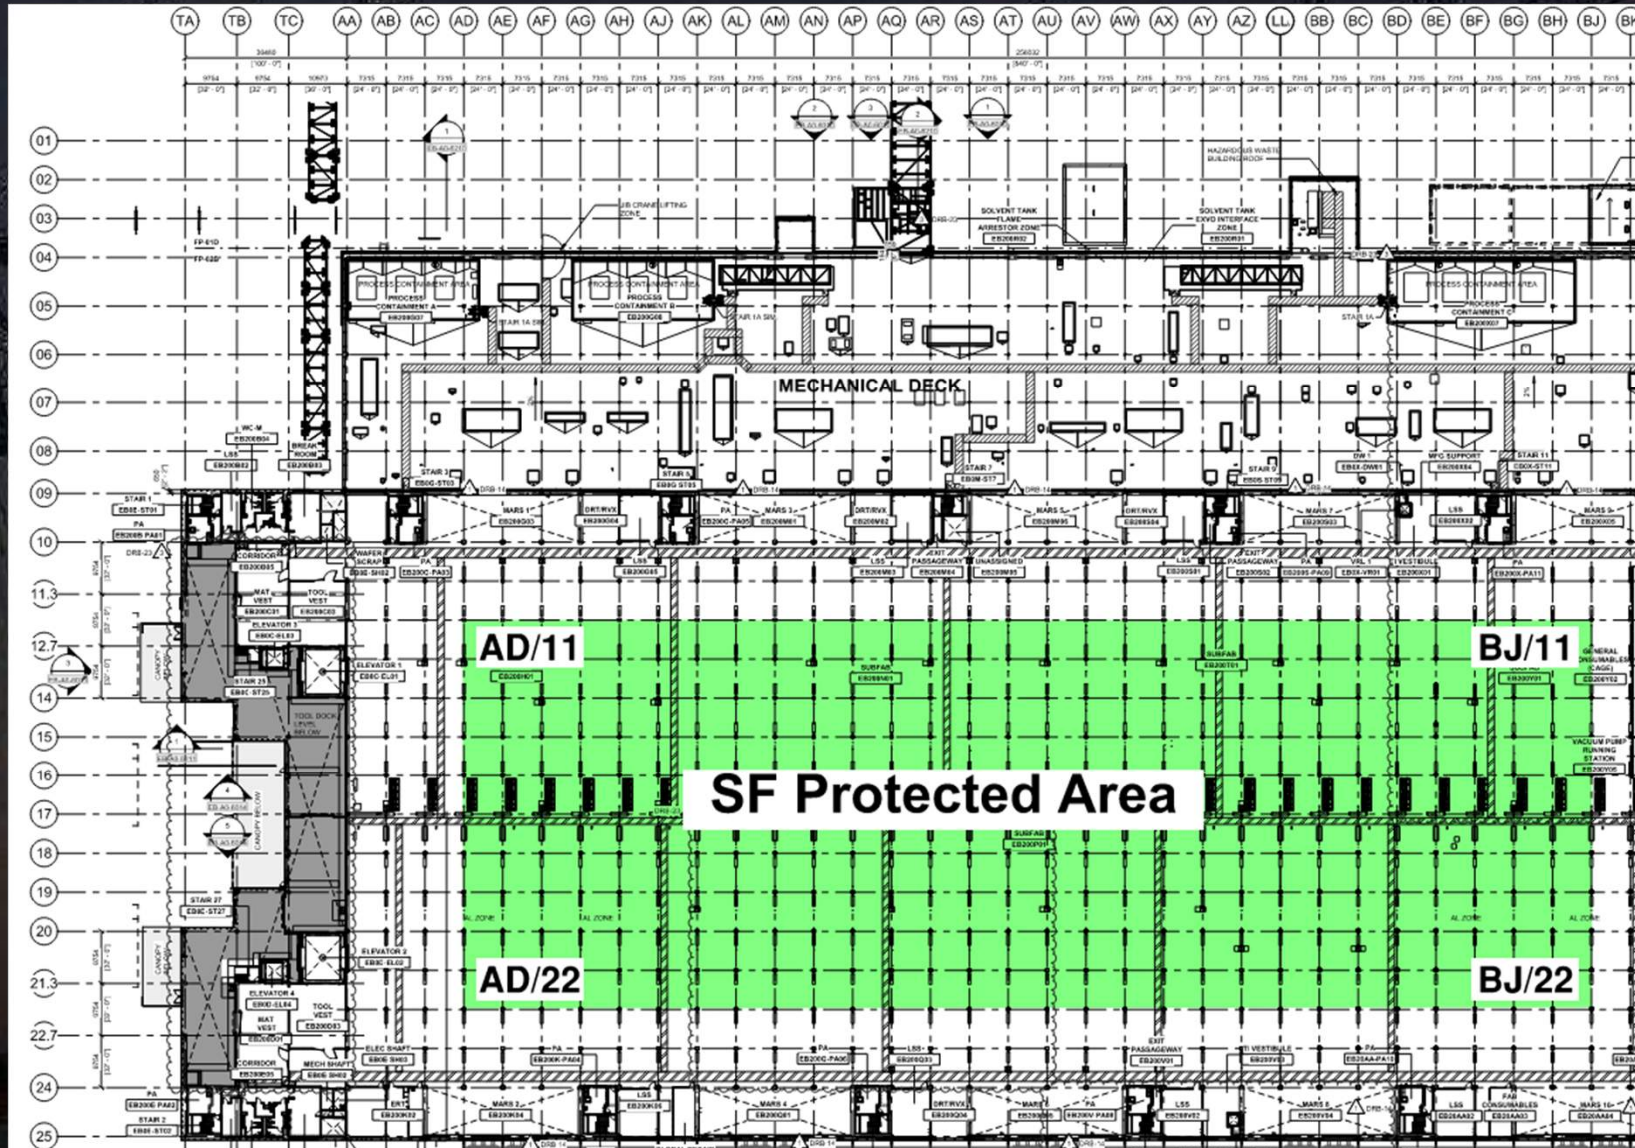




Daily Coordination Meeting

Site Logistics

Protected Areas

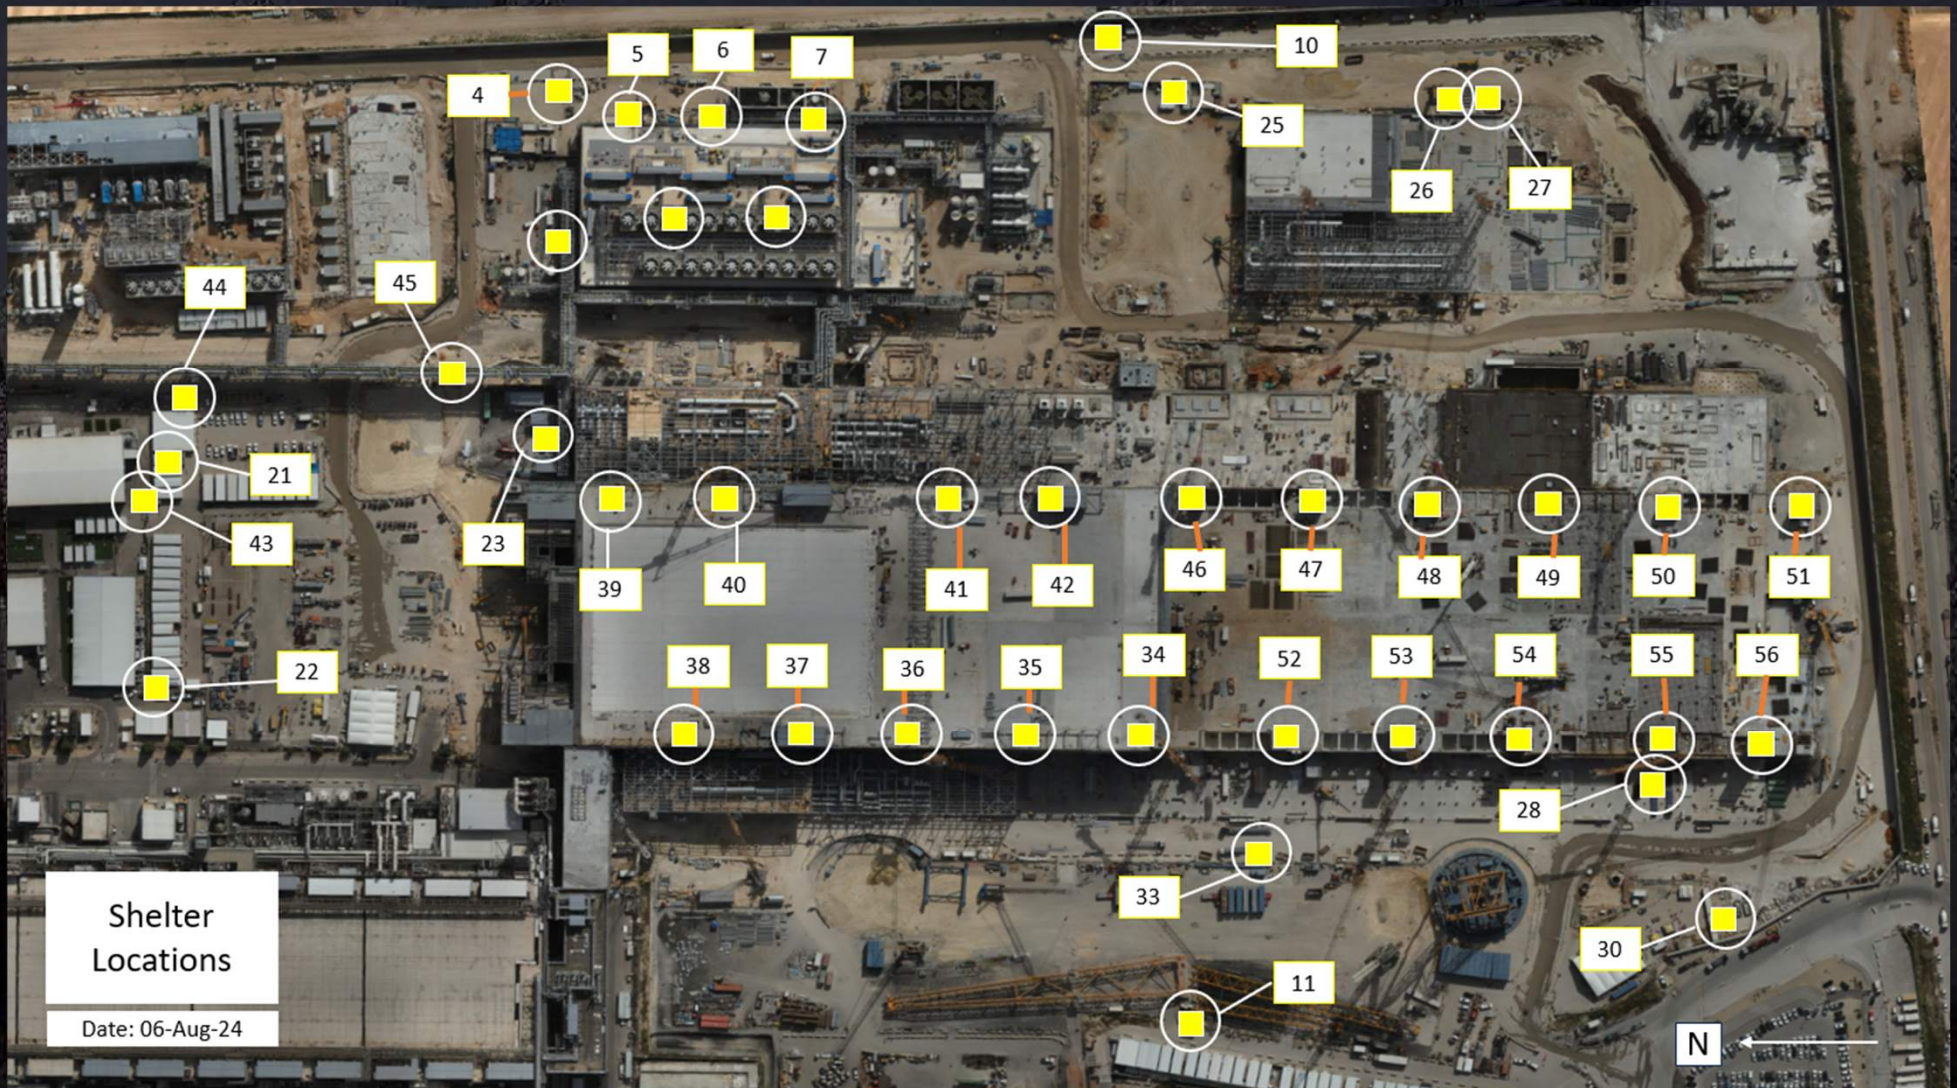

Change in Personnel

- Remember, we need to have plans for all personnel that are absent from the project.
- Make sure that all key roles are properly filled and communicated.
- This is often overlooked with our crews, so don't forget to make sure that key roles within crews are filled by personnel with training and knowledge to do the role they're being asked to perform.
- If there is no management for your company on the project, you cannot have workers on the project.

HCC/EHS Weekend Work- 27.09.2024

White Board Meeting in Beavers at 06:30

Superintendents

Brian Grevious 052-5394339

Igor Shuster 054-4743767

Josh Noll 052-5590653

Husein Abu Hammad 052-4106872

CSA CM

Tarek Nairoukh 052-6636782

Idan Turjeman 052-4093025

MEP

David Jollands 052-3961675

Andy Jollands 052-9659290

Paruic O'Reilly 052-3571665

OSM

CX/QA

Darryl Hicks 052-3215975

Cranes

Brady Prouty 052-6047531

Safety

Safety Foreman- Adir Elmakayes- 054-7254767 Adir-Elmakayes@Hoffmancorp.com

Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com

Safety Officer - Arkady Gerber-050-6851432 Arkady-Garber@Hoffmancorp.com

Subcontractor Weekend Work- 27.09.2024

FAB

UTILITY LEVEL

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

EIram

Foreman: Shlomo

0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

Pach Taas

Perim Rack Aae

Team Lead : Nuriel 0549012324

Afcon E

PA/Stairs

Team Lead : Avi Eli 0526008487

Chemo

TTNW

Team lead: Tommy 0523759408

Safety: Lilah 0547886704

Belfor

TTNE / TTNC

Team Lead: Salame 0546651886

HYG

SF Zones 3- White steel touchups/Mamad plates weld/

Stair # 8

Salah 0507773119

WW Steel

Elevator 3

Teddy 0522392473

Clean Room

W&W 17-18 Line added the beams 10-24 line – catwalks, MOD2: steel fan deck east west, infill ongoing (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

Talad – CR 1W – Drilling holes, 1 metal lids removal (EHS Guy 0544915407, Super Igor 0544509386)

Sig – 5W INT Platforms MIMO CB-CC/25 (EHS Beni 0506232032, Super Nodar 0546313261)

EIram – CR Level 9,25 line, AA line 2W shafts walls INT level 9,10,17,24 column wrap (EHS Royi 0538312234, Super Bonio 0544236899)

Afcon – CR – 2E-5E, 2W-5W, INT- 2E-3E, 3E-3W ,LINK Rack install (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Sela – 1E-AB-AK/10-12 CRC (EHS Shmuel – 0506306031, Supervisor Yuval 0502649246)

Subcontractor Weekend Work- 27.09.2024

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2, and EPA Platform
1&2P

Foreman – Vadim – 052-6229005

Safety – Offek – 050-7838486

Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-
2P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-4P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

W&W – SEQ 135, 137

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Elram – 5P Corridor, UPW Ceiling

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Lesico – 5P UN2 Welding

Foreman – Selvin – 052-4787370

Safety – Itay – 054-2336103

Combe UPW – UPW Room Piping and Yard

Foreman – Boris – 054-8346412

Safety – Abed – 052-5148747

SNJ Flashing – BPS Roof

HSAI – BPS Blast Walls

Foreman – Dave – 052-4121028

Safety – Sam – 052-5259268

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

WJG

Pach Taas

Adiv Pereg- EHS

Netanel Ivgi – Forman

Siding

SAMI NAJAMI -ROOF METAL

SAMI NAJAMI -PANTRETION

SAMI NAJAMI -GERTZ

Victor 0549220163

Subcontractor Weekend Work- 27.09.2024

CUB

Sami Najami CUB 2:

Husein - 0526917461

Alon - 0509895008

Meptagon I+C:

Raziel - 0584360845

Netanel - 0538398999

Pach Taas:

Adiv - 0506909390

Nati - 0543301880

ETC south yard:

Yosef - 0506708990

Leonid - 0545991846

S.K.E:

Reynato - 0548991623

HSAI

Chemo Aharon:

Dudu - 0509808846

Leonid – 0548883878

Date: 27 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.SARAWUT KHRUEASING, AC5094850, TEL 052-3628607 (Leader)

Date: 28 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.YOTSAWAT

Trestle

SNJ:

PIPES –UB CUB

ISOLATION –UB CUB

STEEL

FORMAN- BASHIR YONES - tel. 05273649963

SAFETY TRESTLE-Alon Matan tel. +972 50-989-5008

Site

Derech Afar – Shotcrete, Storm water bypass at Sarens & Fire protection water

Supervision = Raed: 054-2442030

EHS = Alex: 054-5403849

Olizki – Sweepers and water trucks

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

TM Team – LSS underground

Supervision = Nadav: 052-5893171

EHS = Alon: 054-7711469

GIS/NEY

Daily Coordination Meeting



14:00 Sign In
