

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- Death onsite today – moment of silence



SUT 38.1 LEVEL

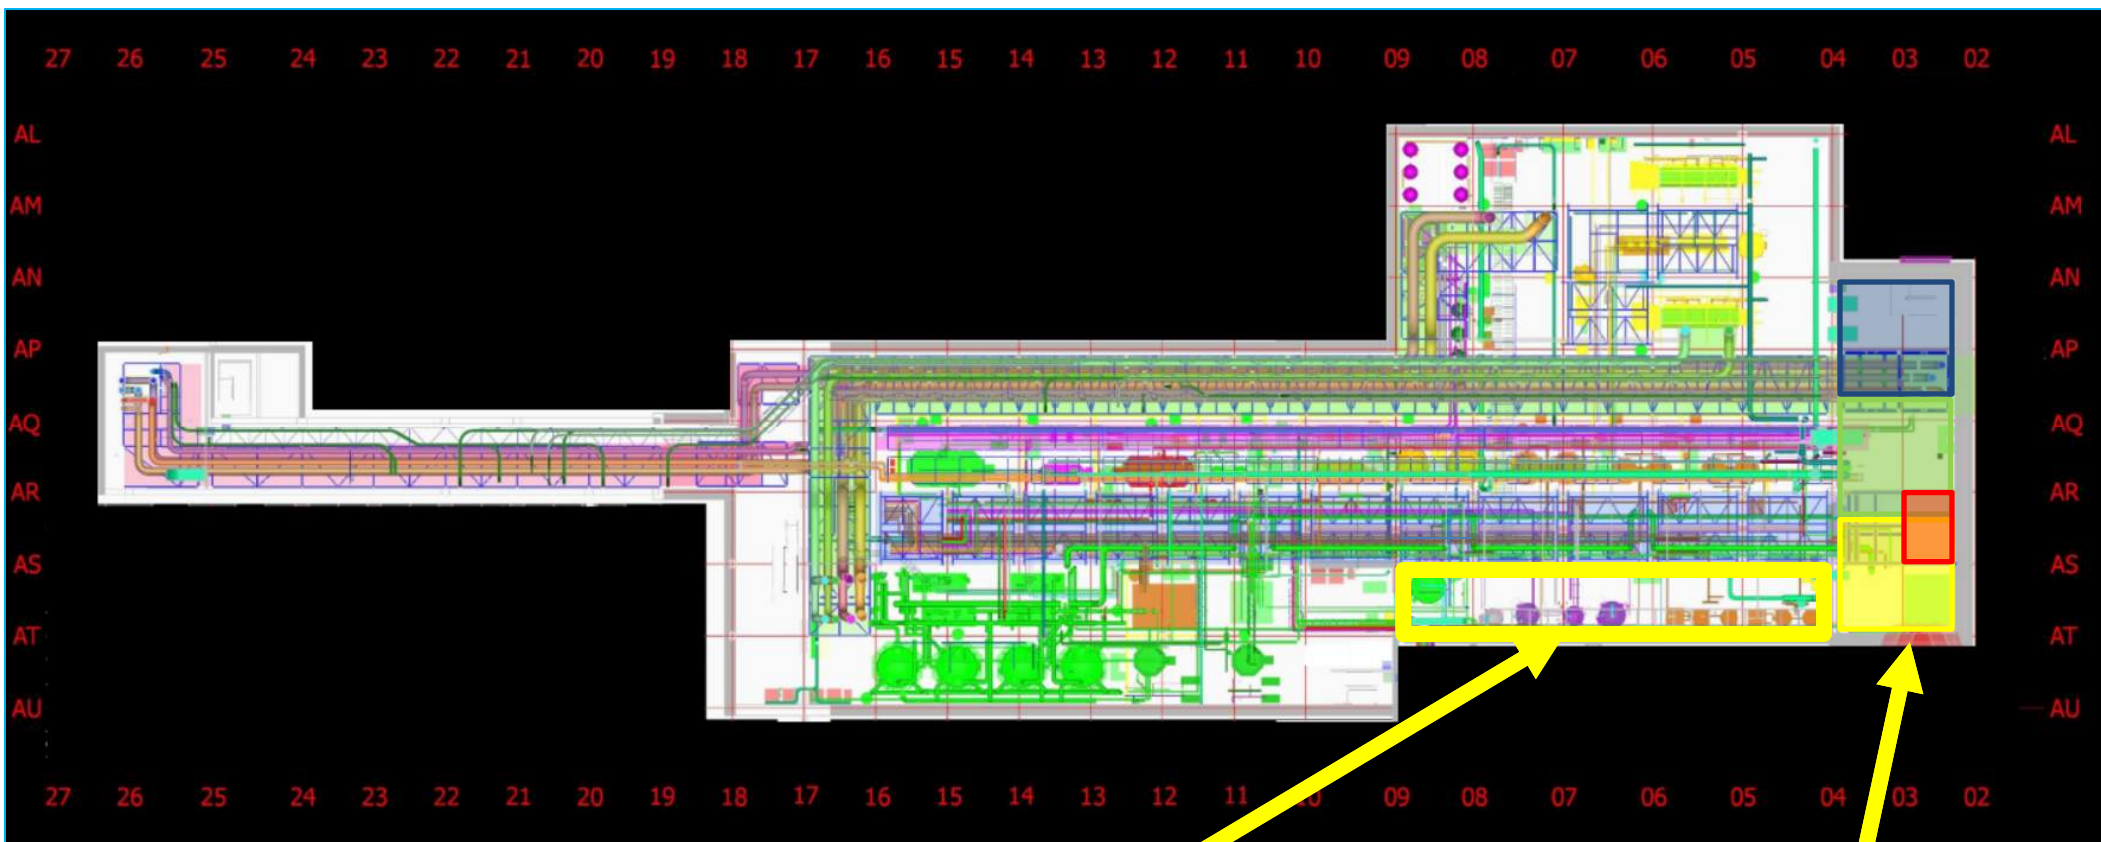


Solvent room.
CRC

Topping slab Schedule

- Pour 1 – 1/9 – 1/13
- Pour 2 – 1/15 – 1/20
- Pour 3 – 1/22 – 1/27
- Pour 4 – 1/29 – 2/4

SUT 38.2 LEVEL


Rack 4b
Lifting
schedule
#6 –

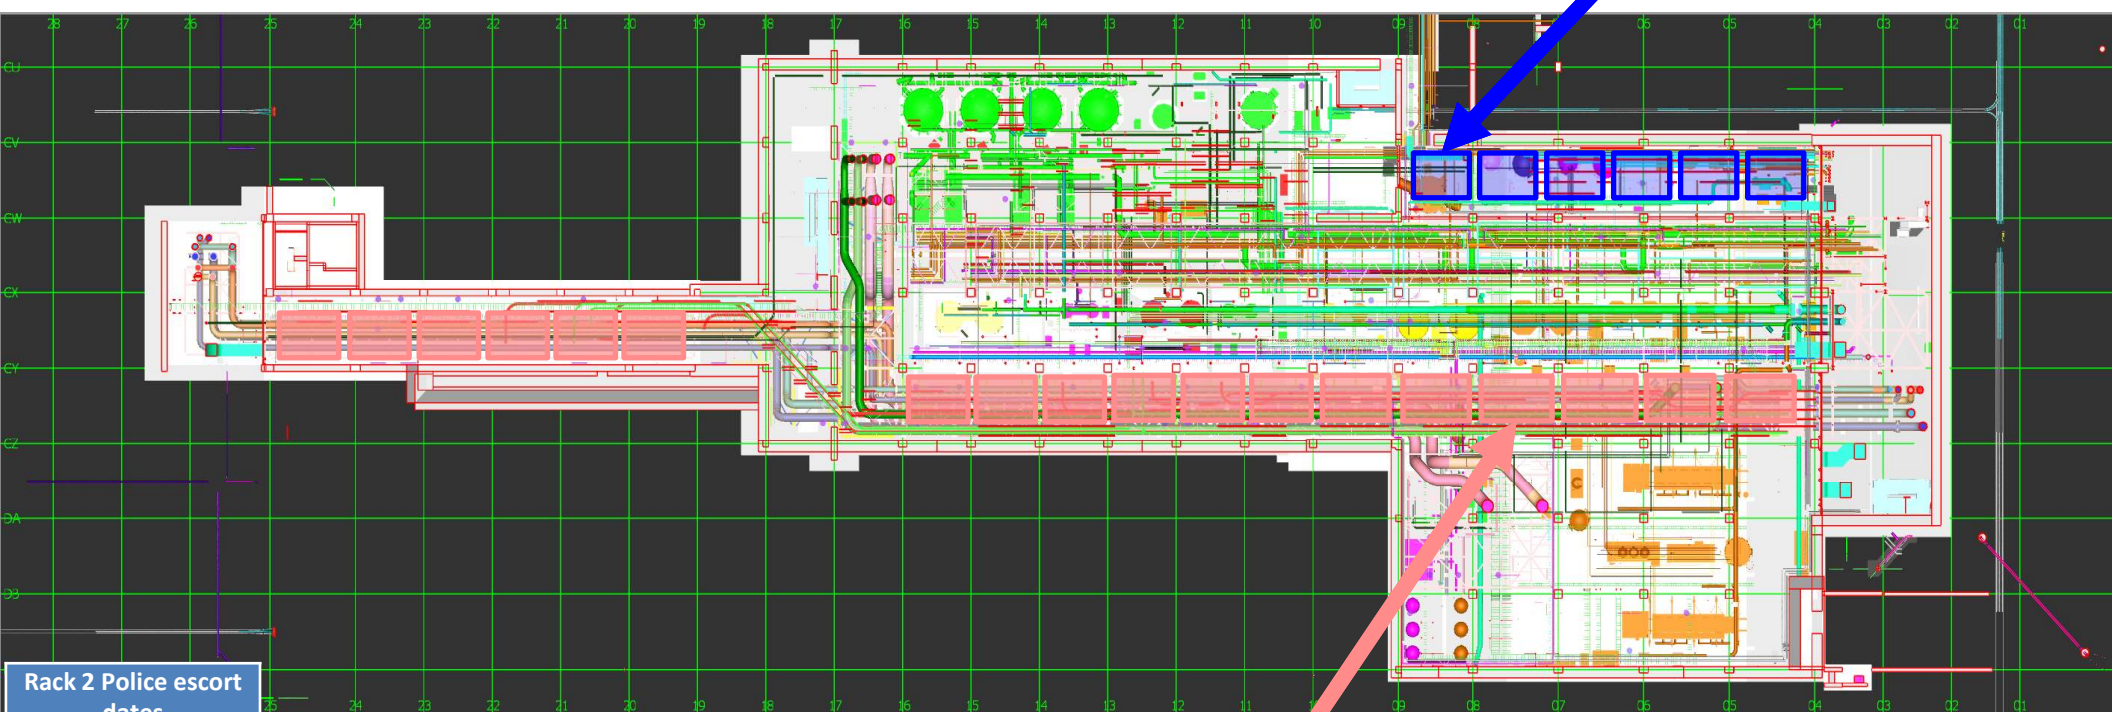


Rack 2 Police escort dates
v24.11.24
v25.11.24
v3.12.24
v9.12.24
v12.12.24
v15.12.24
v17.12.24
v22.12.24
5.1.25
14.1.25 > 2.2.25
3.2.25
9.2.25

Rack 2
MIMO -
Module #9
5th of Jan


SUBFAB BUILDOUT MOD 1

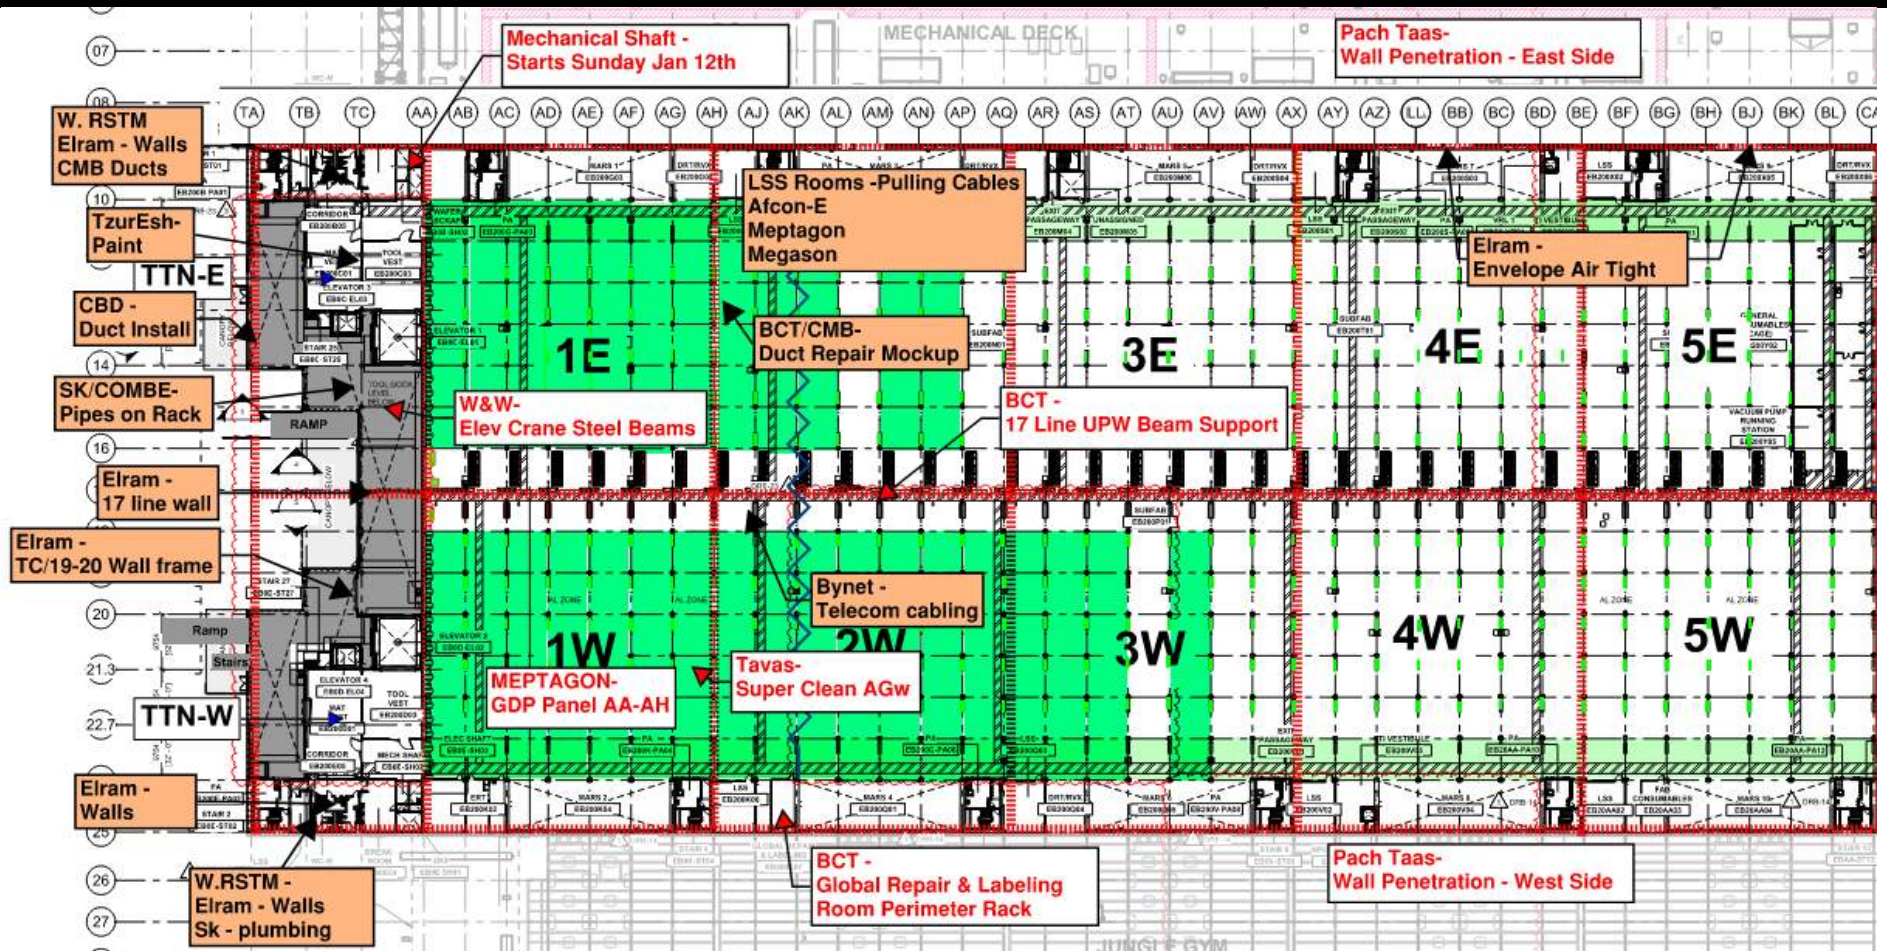


SUBFAB CRC TOPCOAT

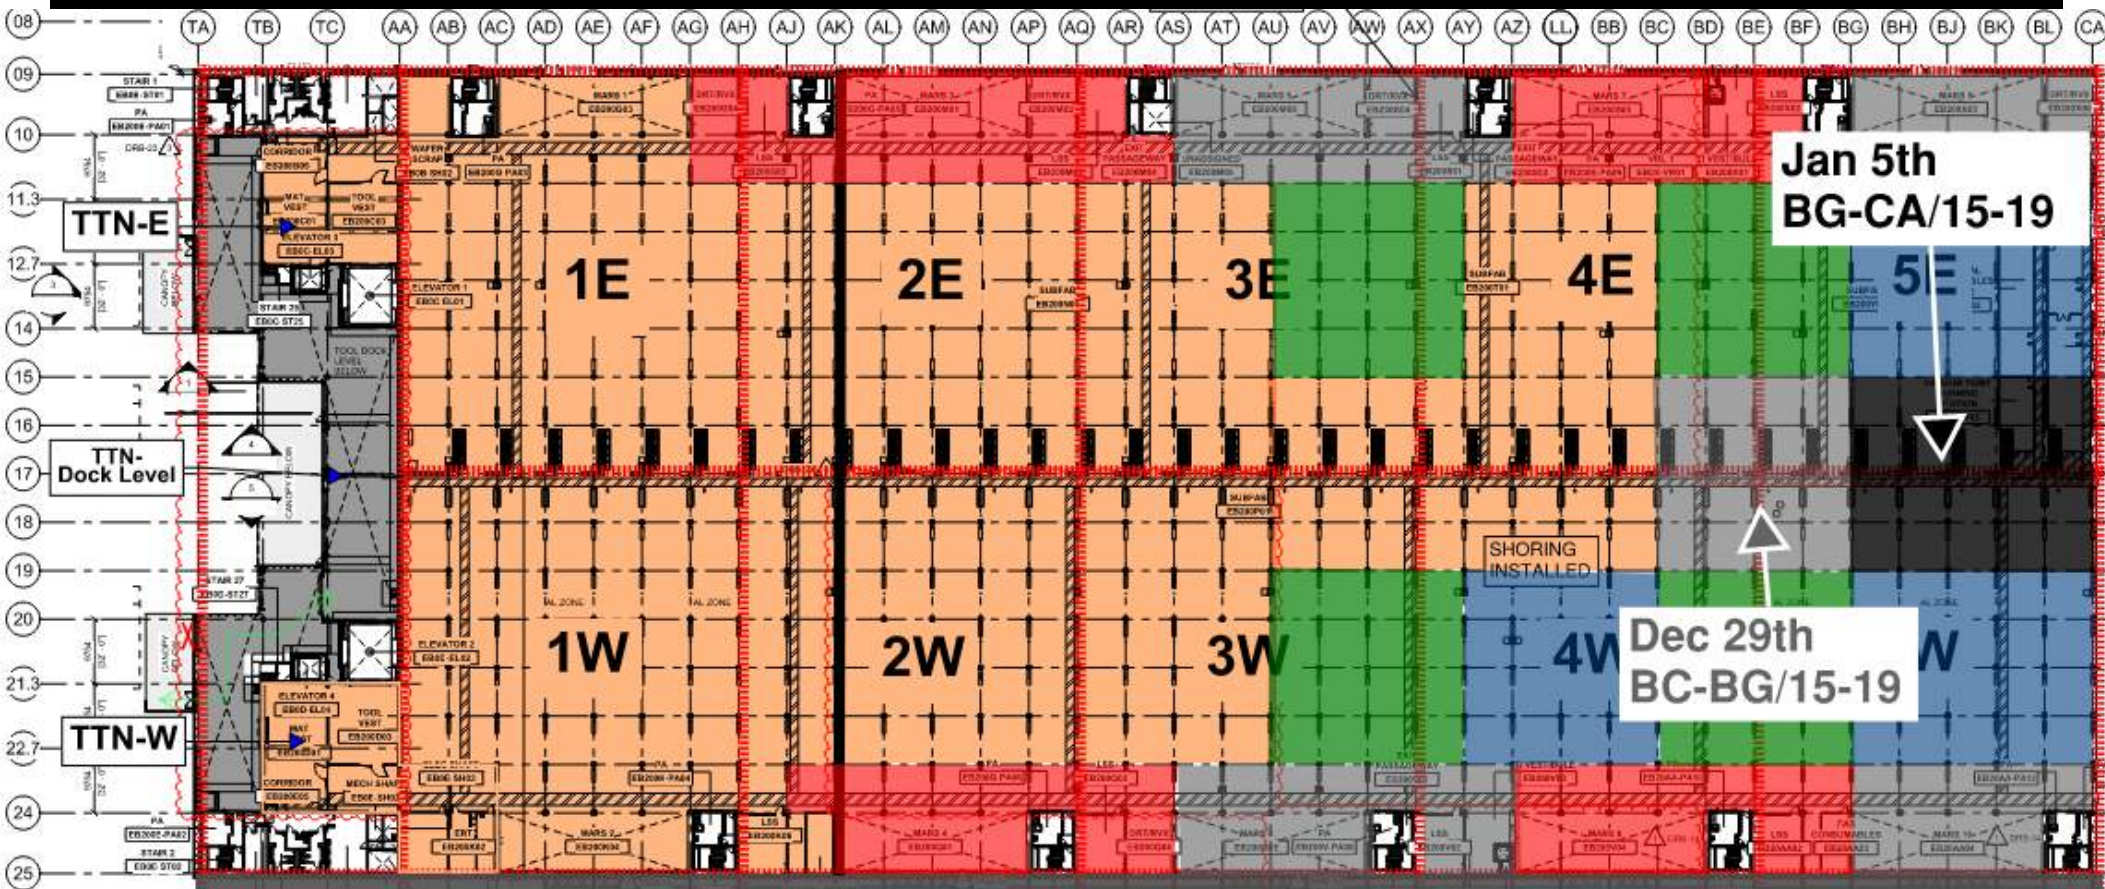


BCT Pressure Test Today

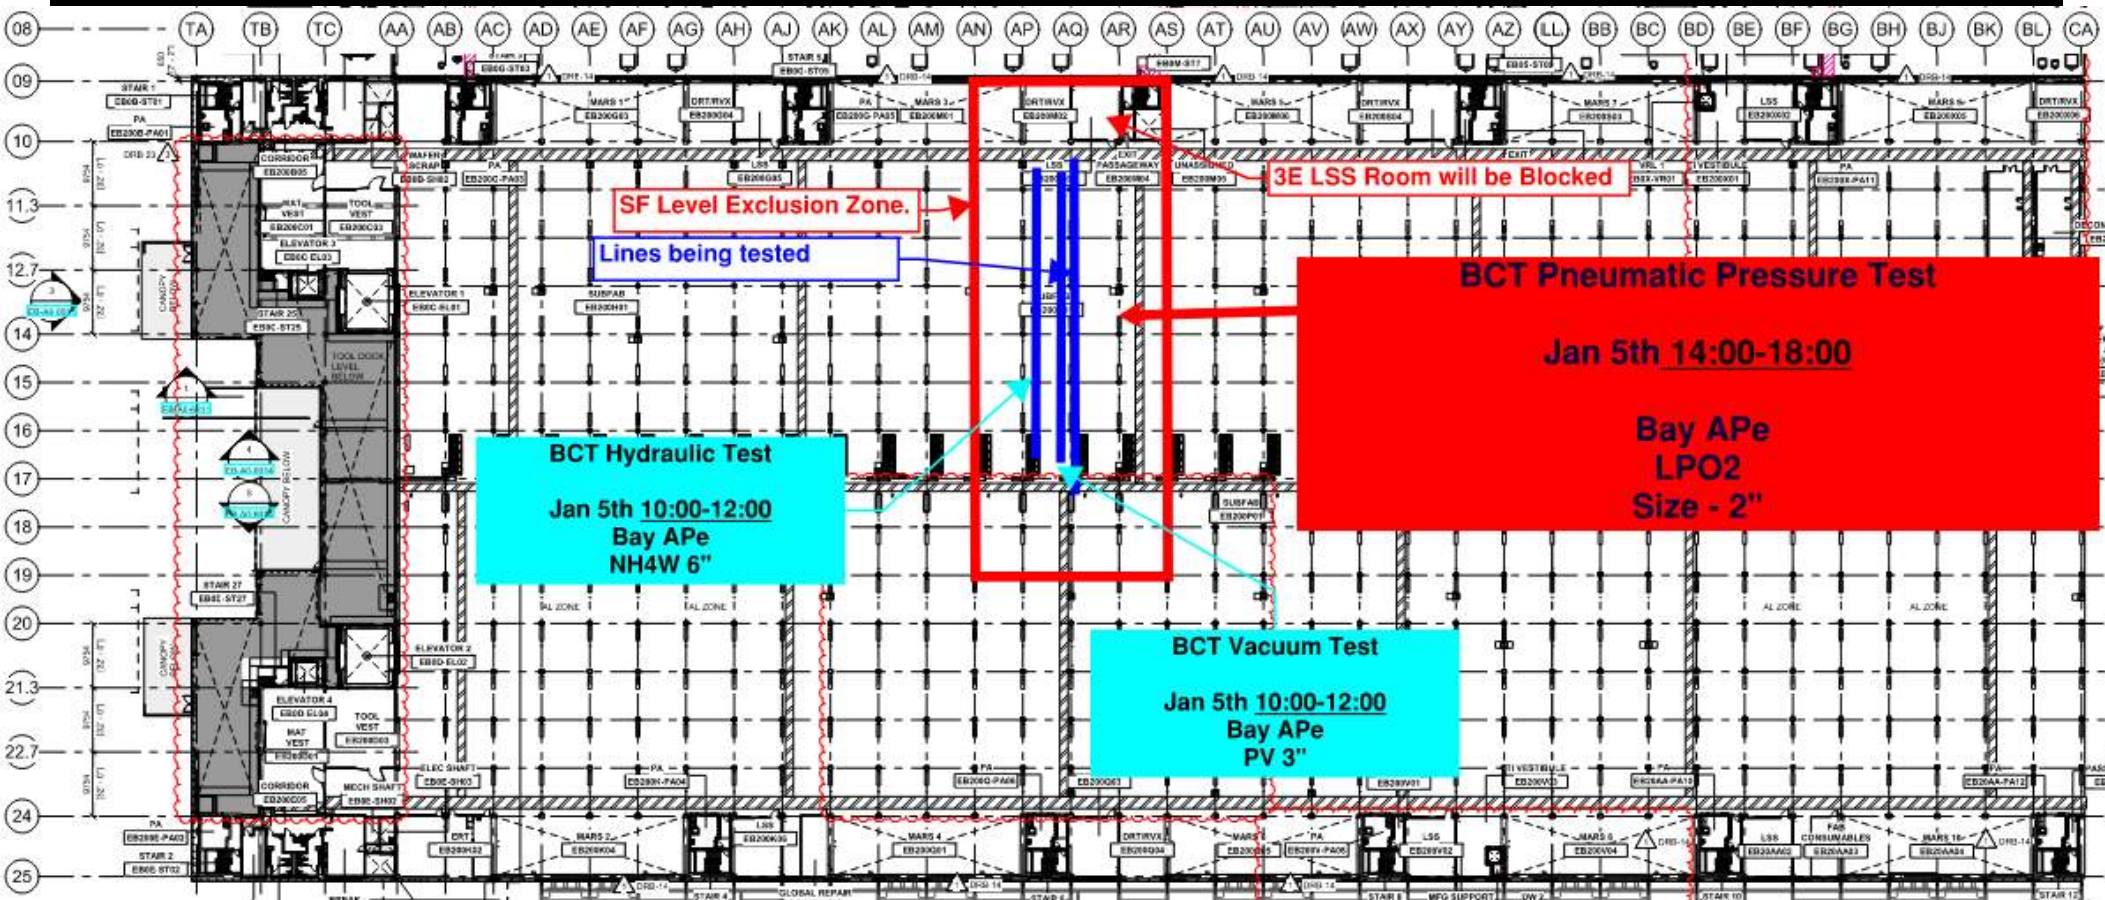



BCT Pressure Test Tomorrow

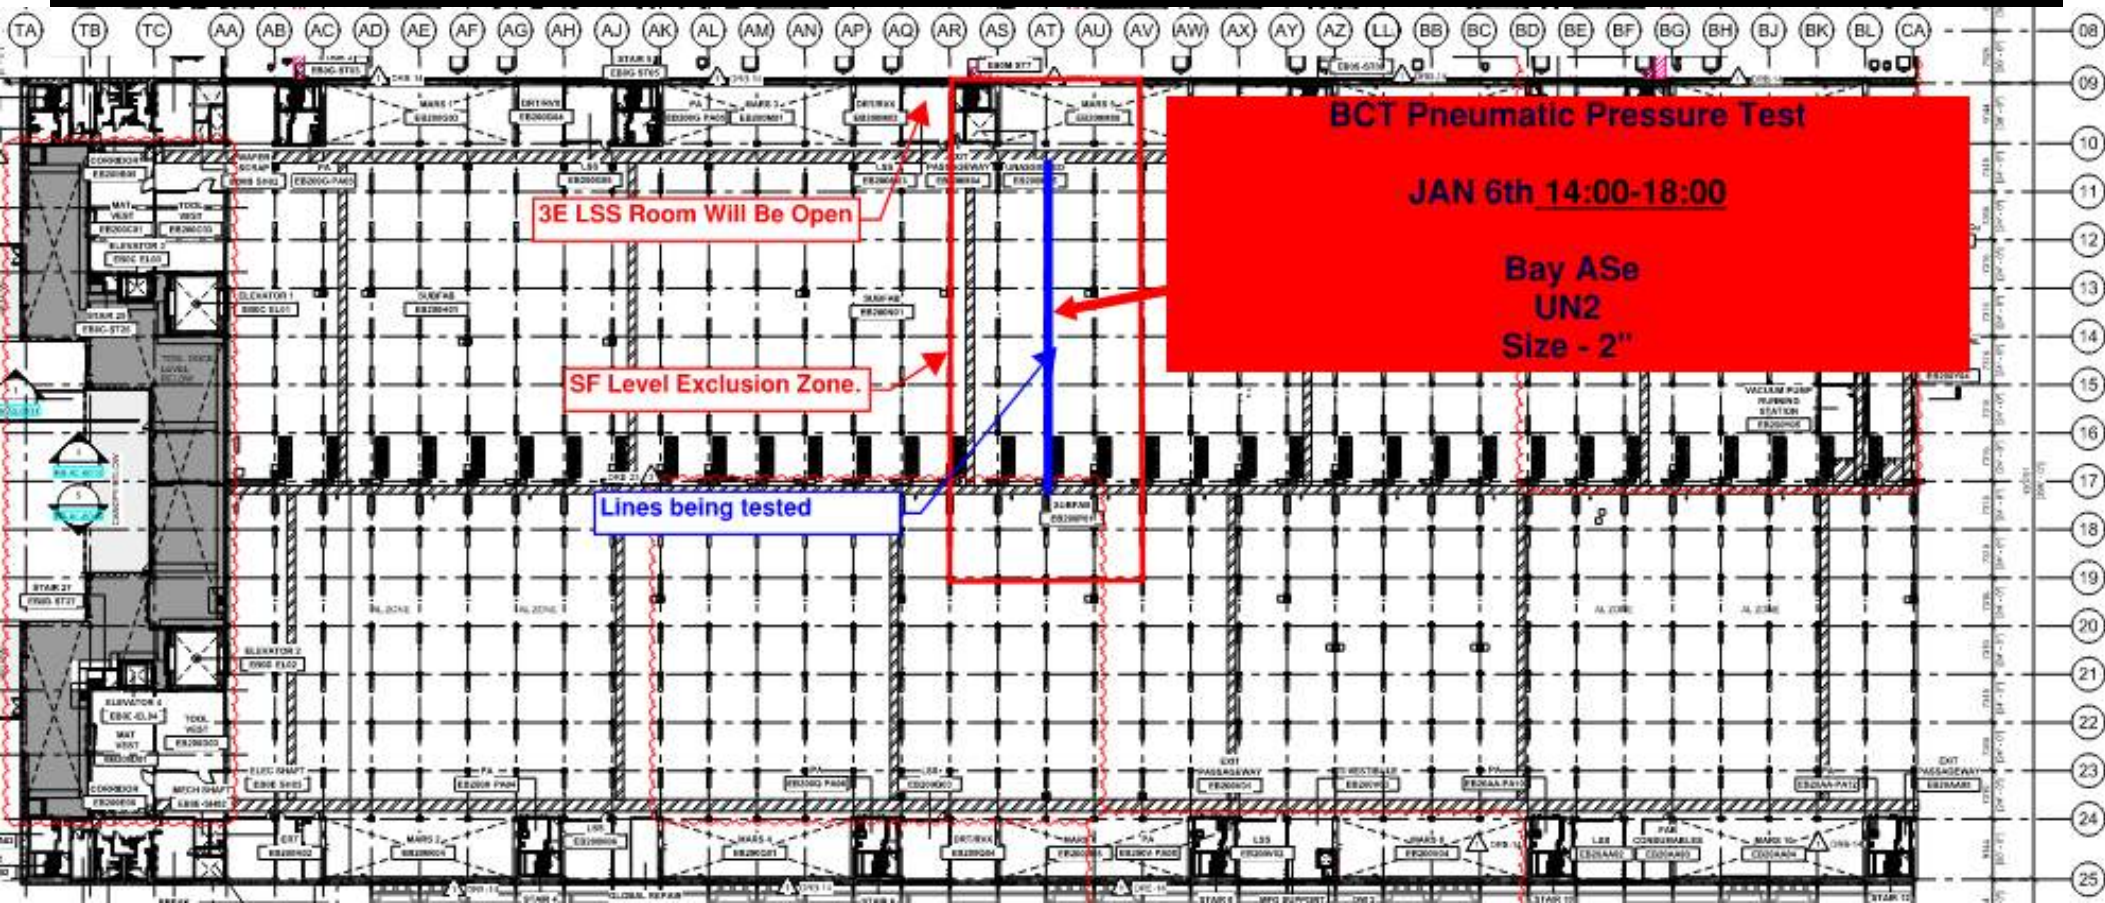


SUBFAB BUILDOUT MOD 2

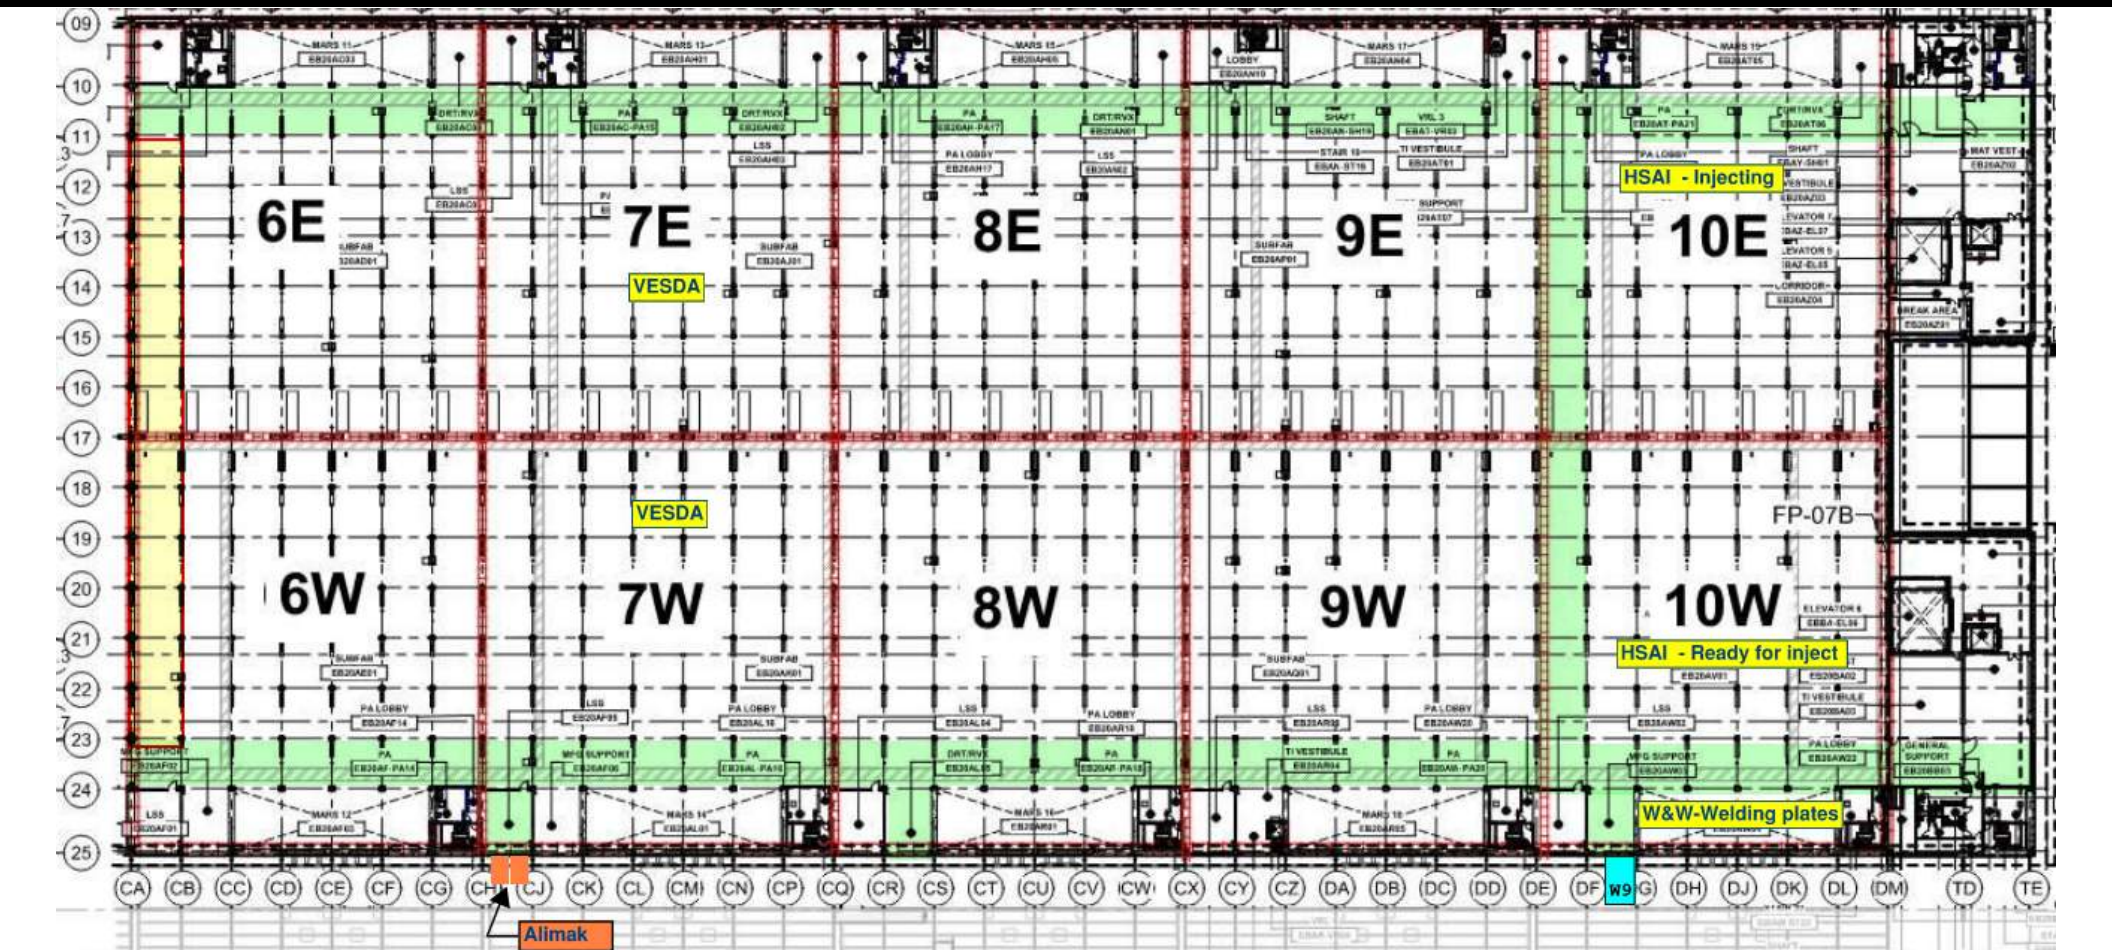


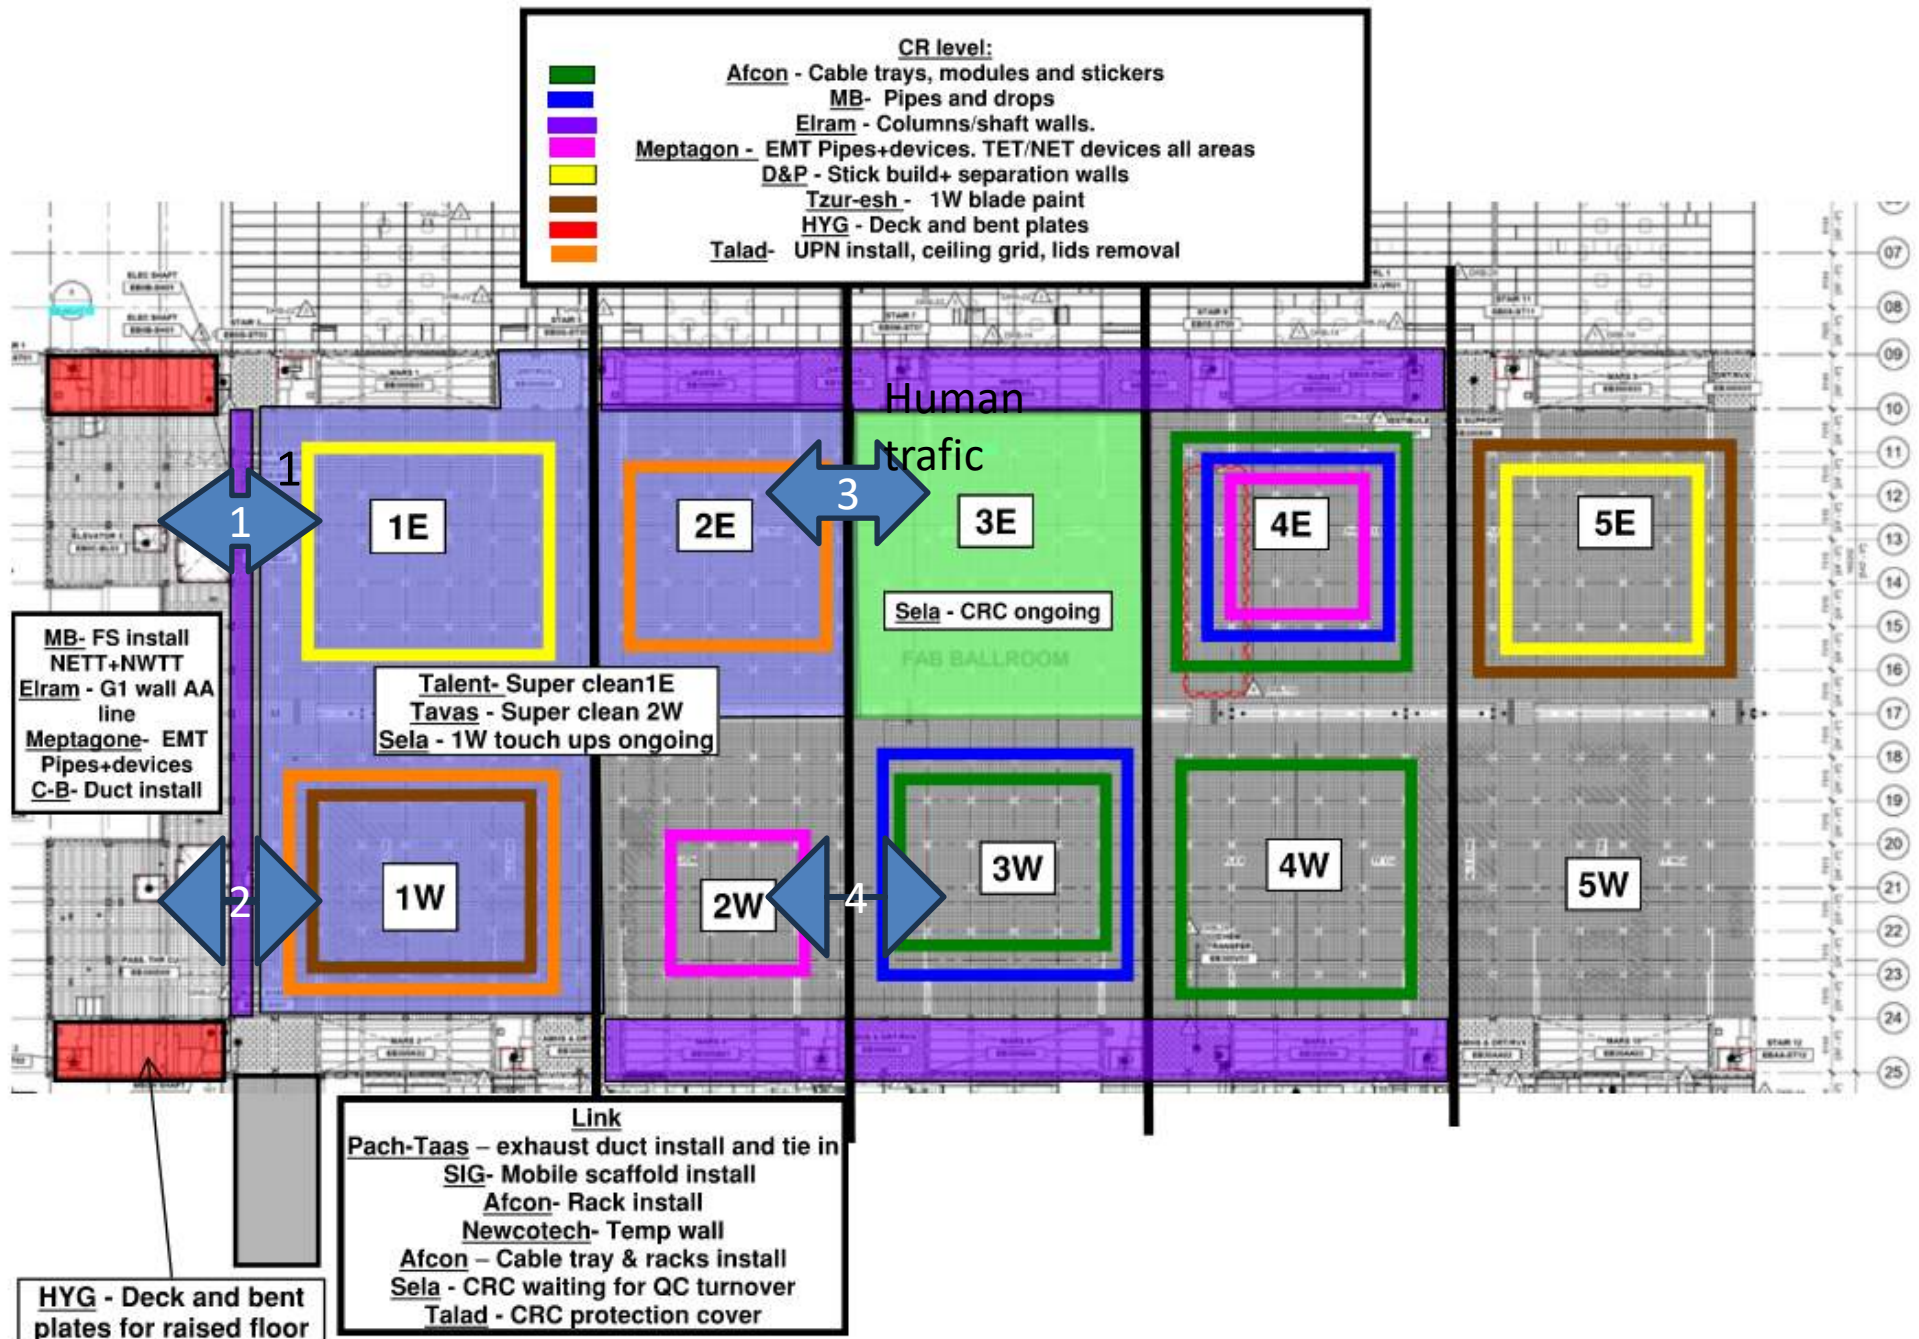


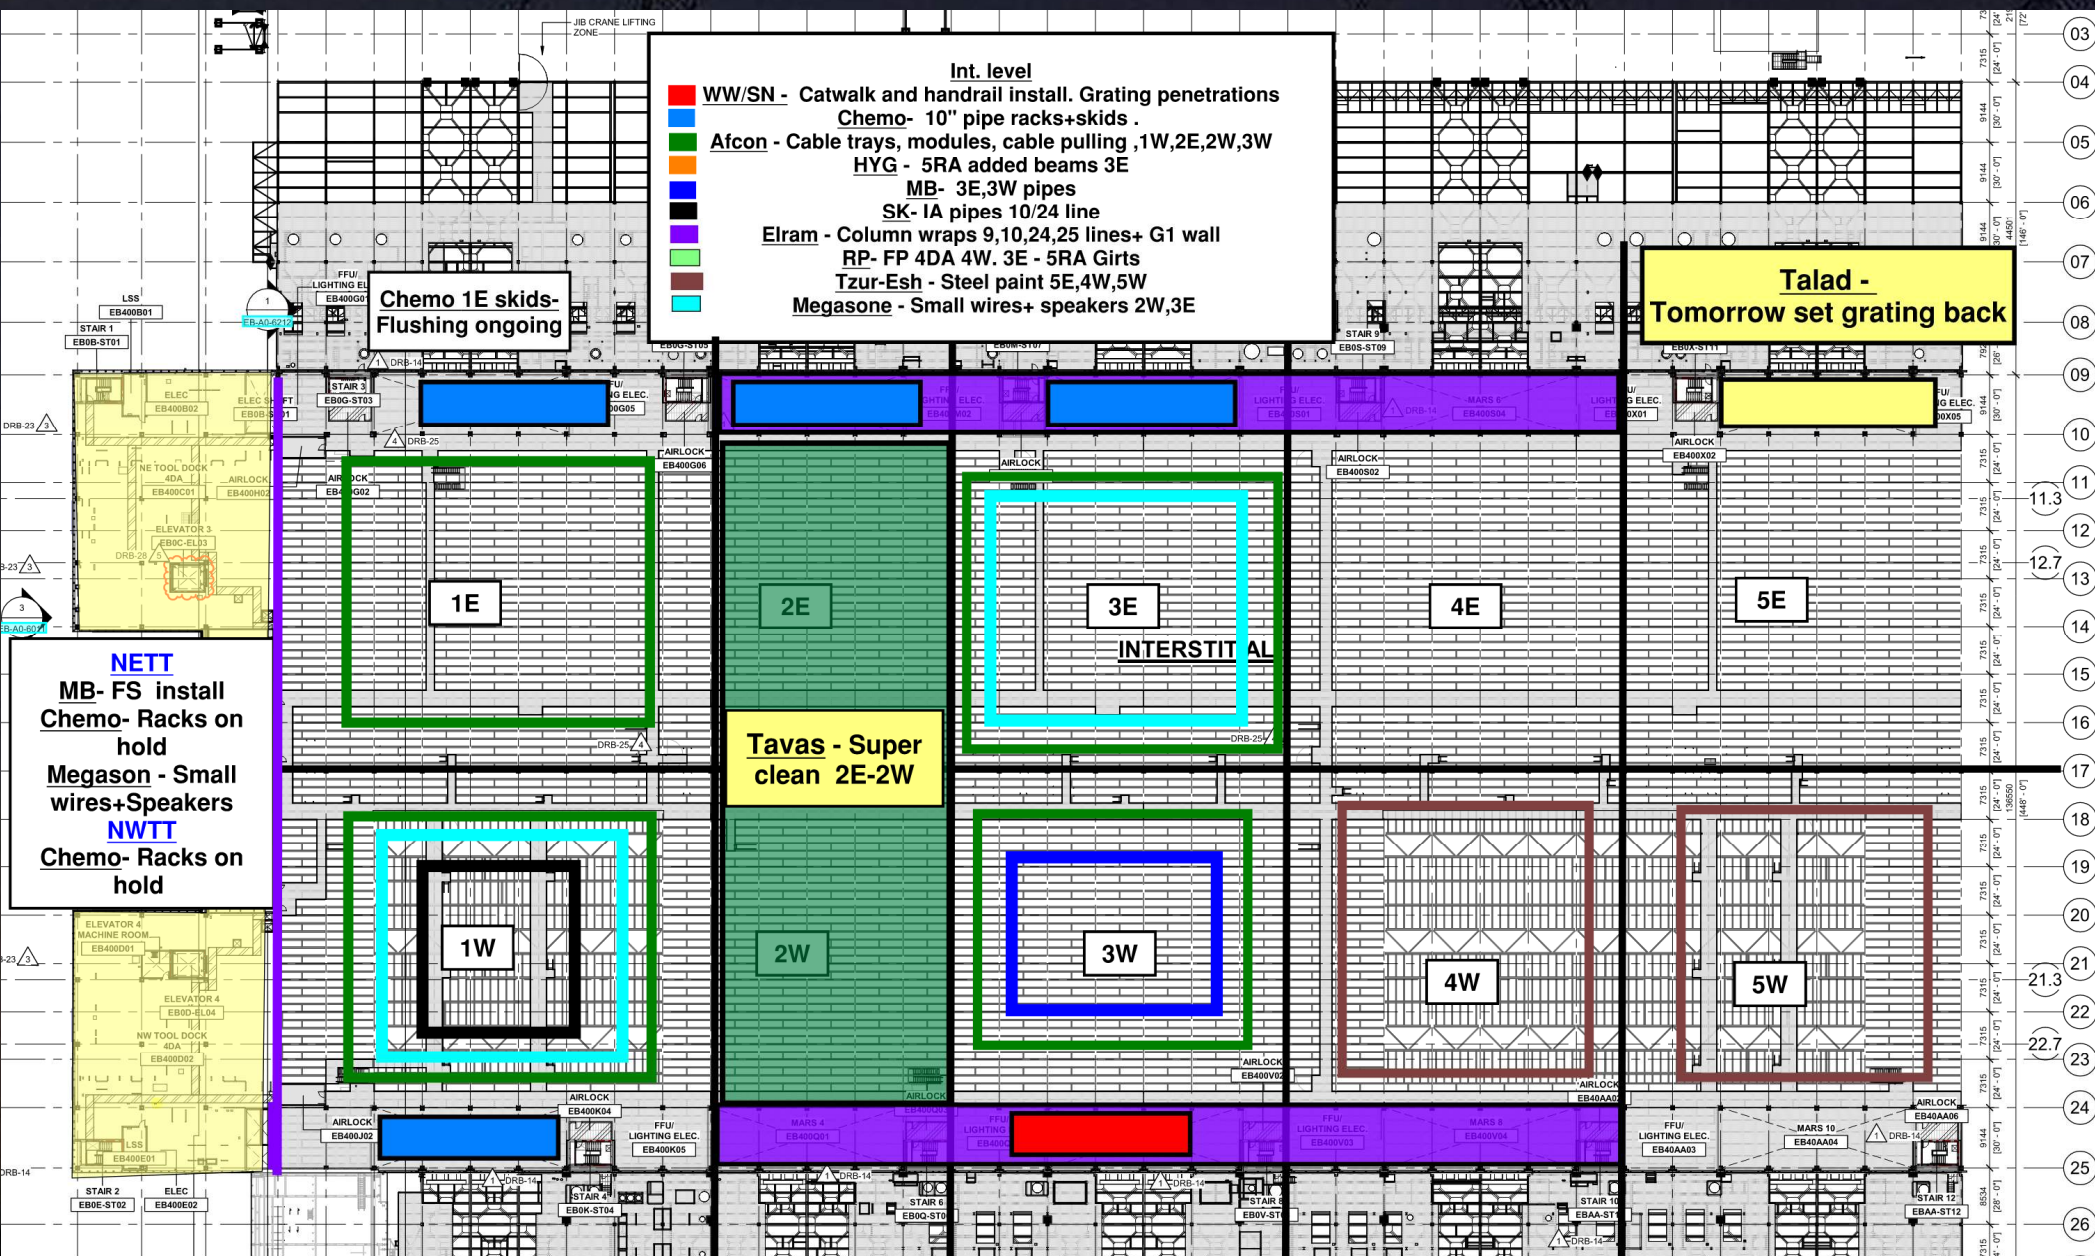



Last call for clearing heavy
equipment. Roof is closing this
week

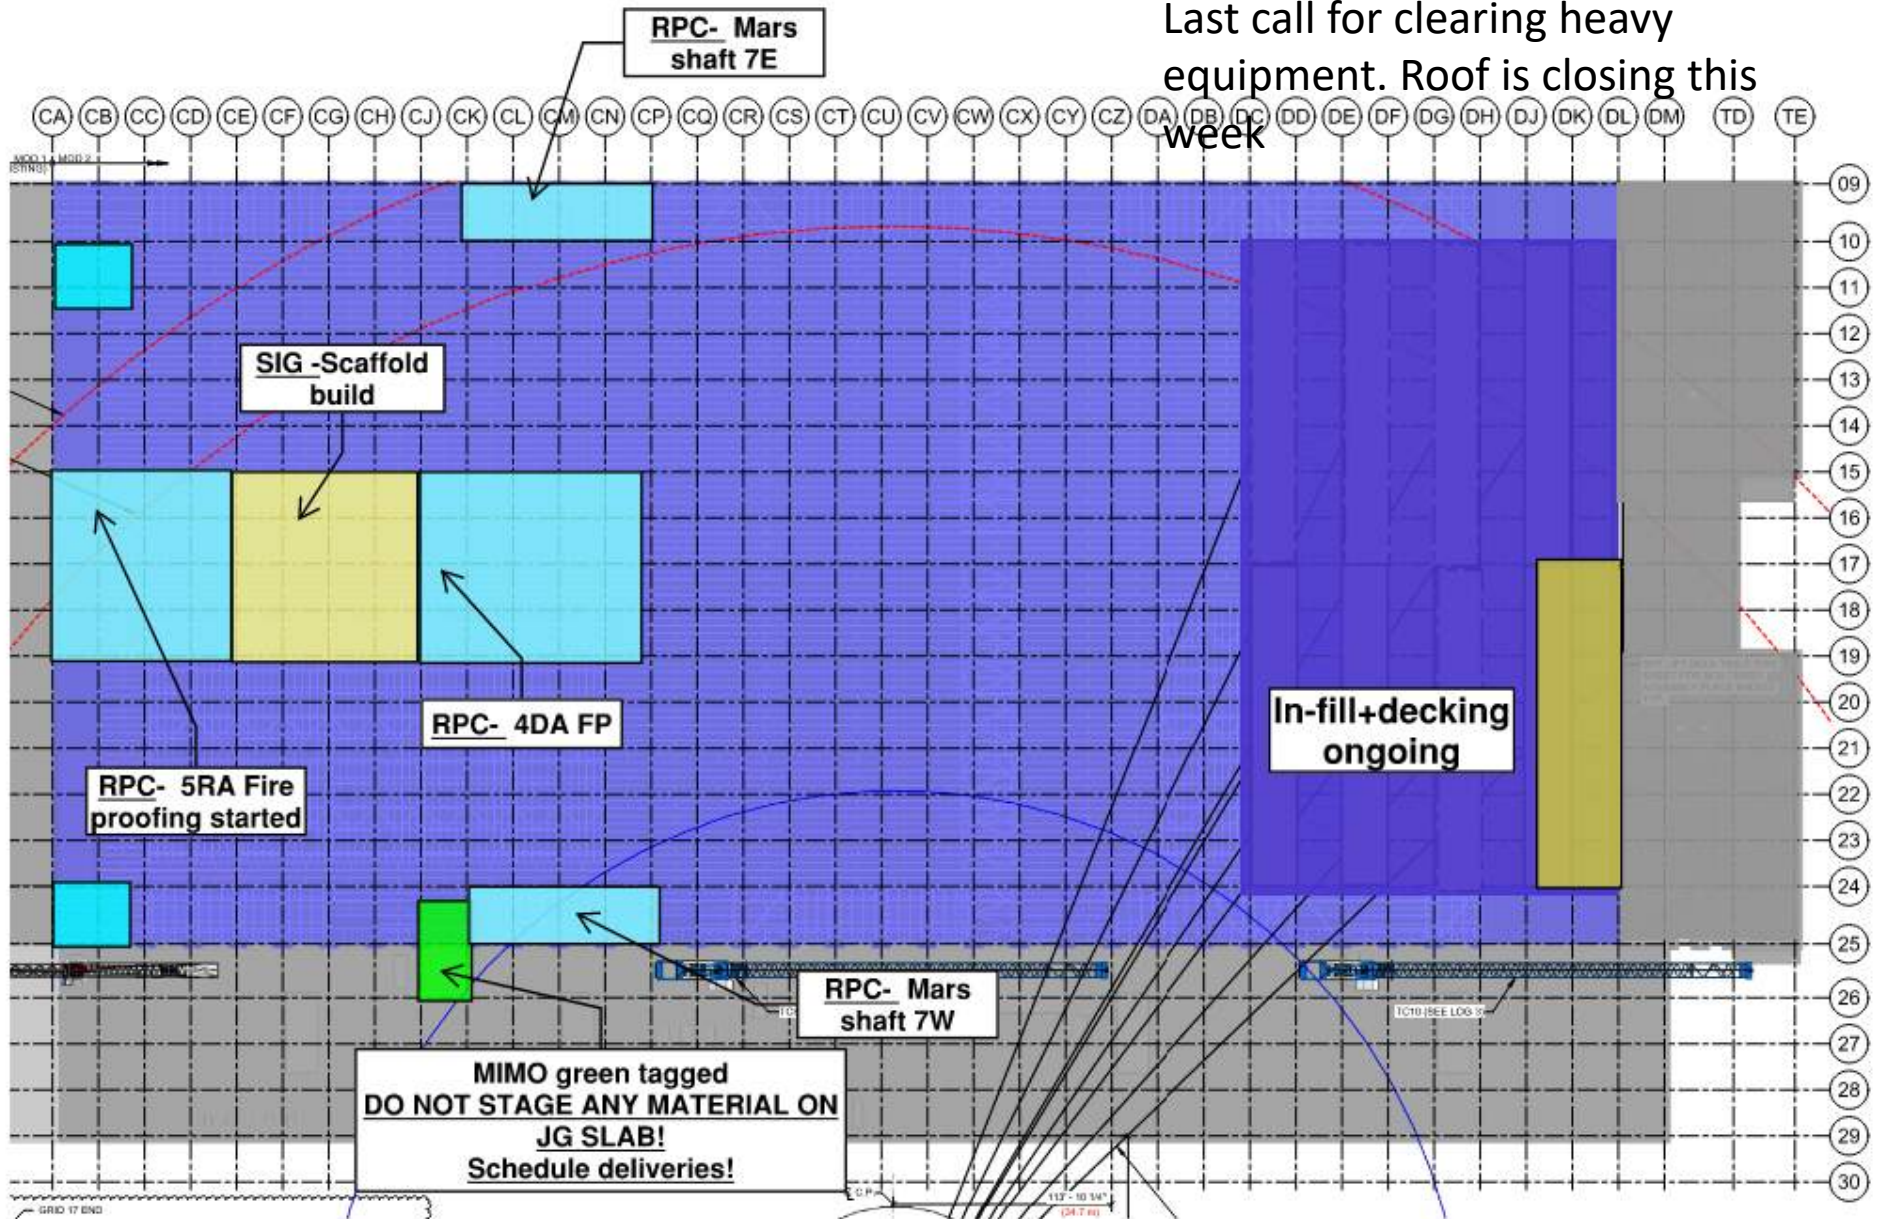

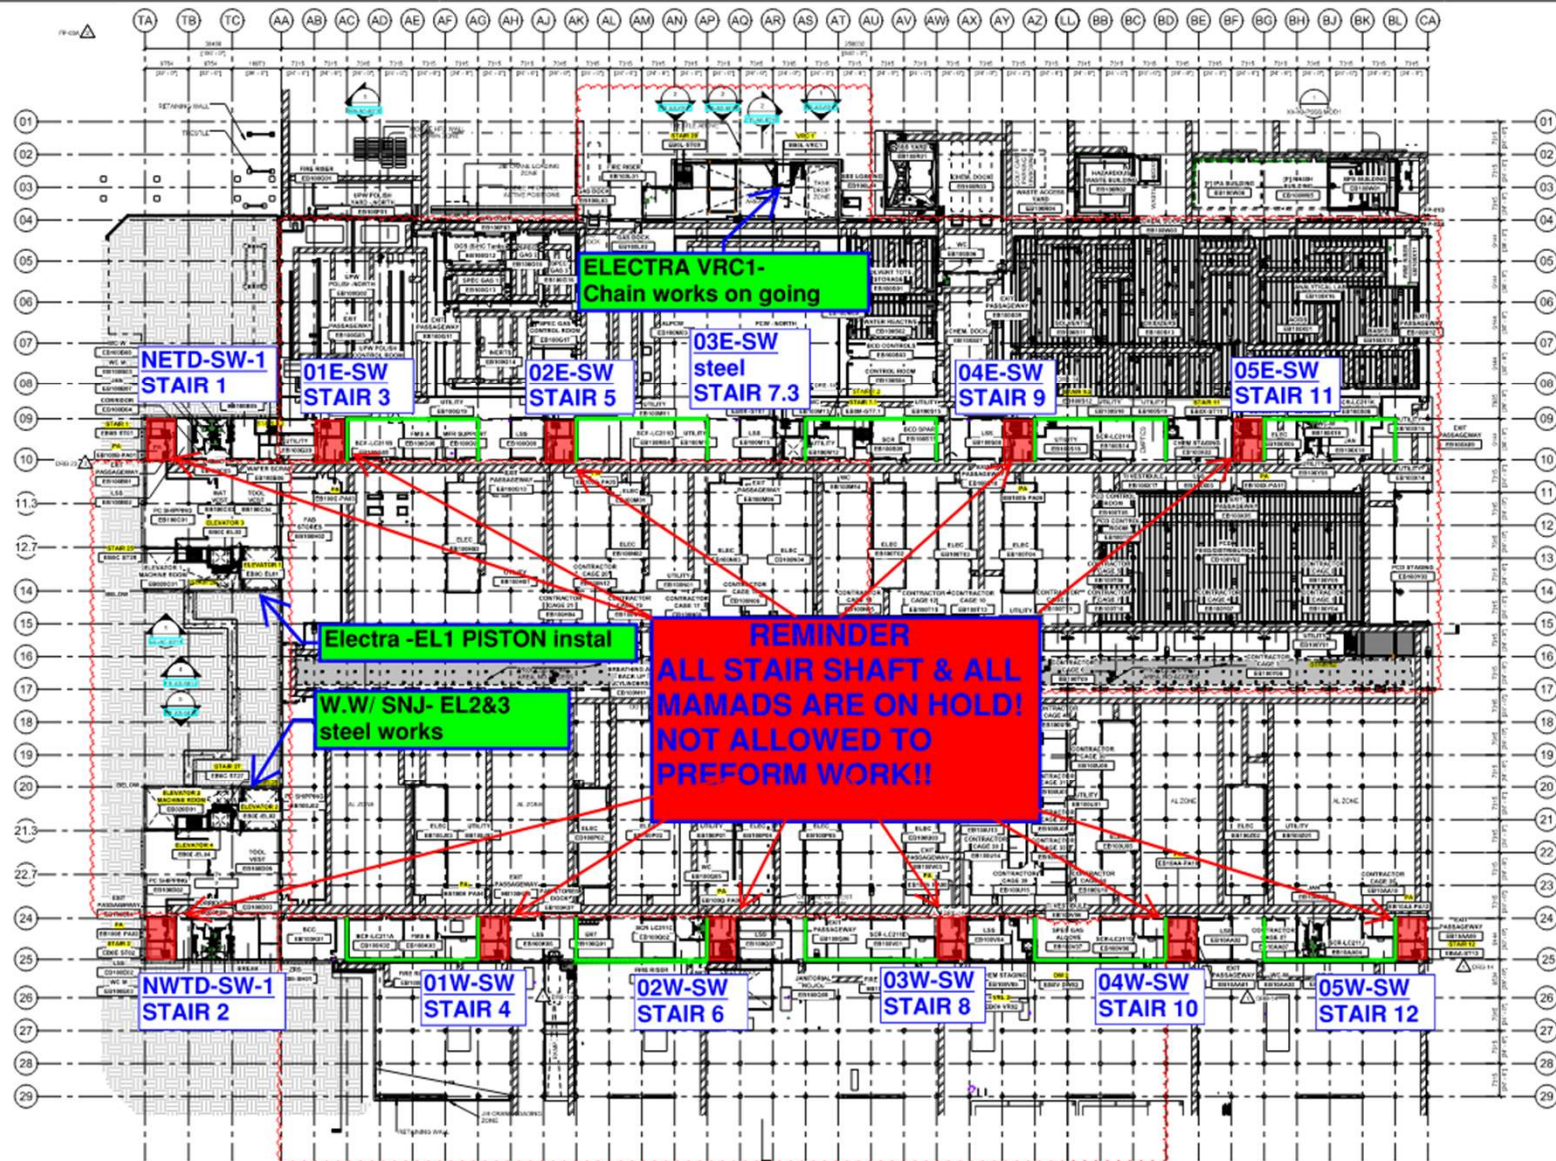

Siding - West FAB - JYG

BLOWDOWN 30%

	TA	TB	TC	AA	AB	AC	AD	AE	AF	AG	AH	AI	AK	AL	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BJ	BK	BL	CA				
	1001/1002			601/602			511/612				621/622				631/632				641/642				651/652				811/812				821/822				831/832				841/842				851/852	
	29	28	28	15	15		31	31	31	31	31	31	31	31	30	21	31	31	31	31	31	31	21	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31				
	100%	100%	96%	100%	100%		100%	100%	100%	100%	100%	100%	100%	100%	100%	90%	90%	90%	90%	100%	100%	87%	77%	77%	85%	100%	100%	100%	85%	85%	85%	61%	61%	61%	100%	90%	74%	74%	74%	61%				


Link

EB


Siding - East FAB - PSSS


BLOWDOWN 30%

[illegible]

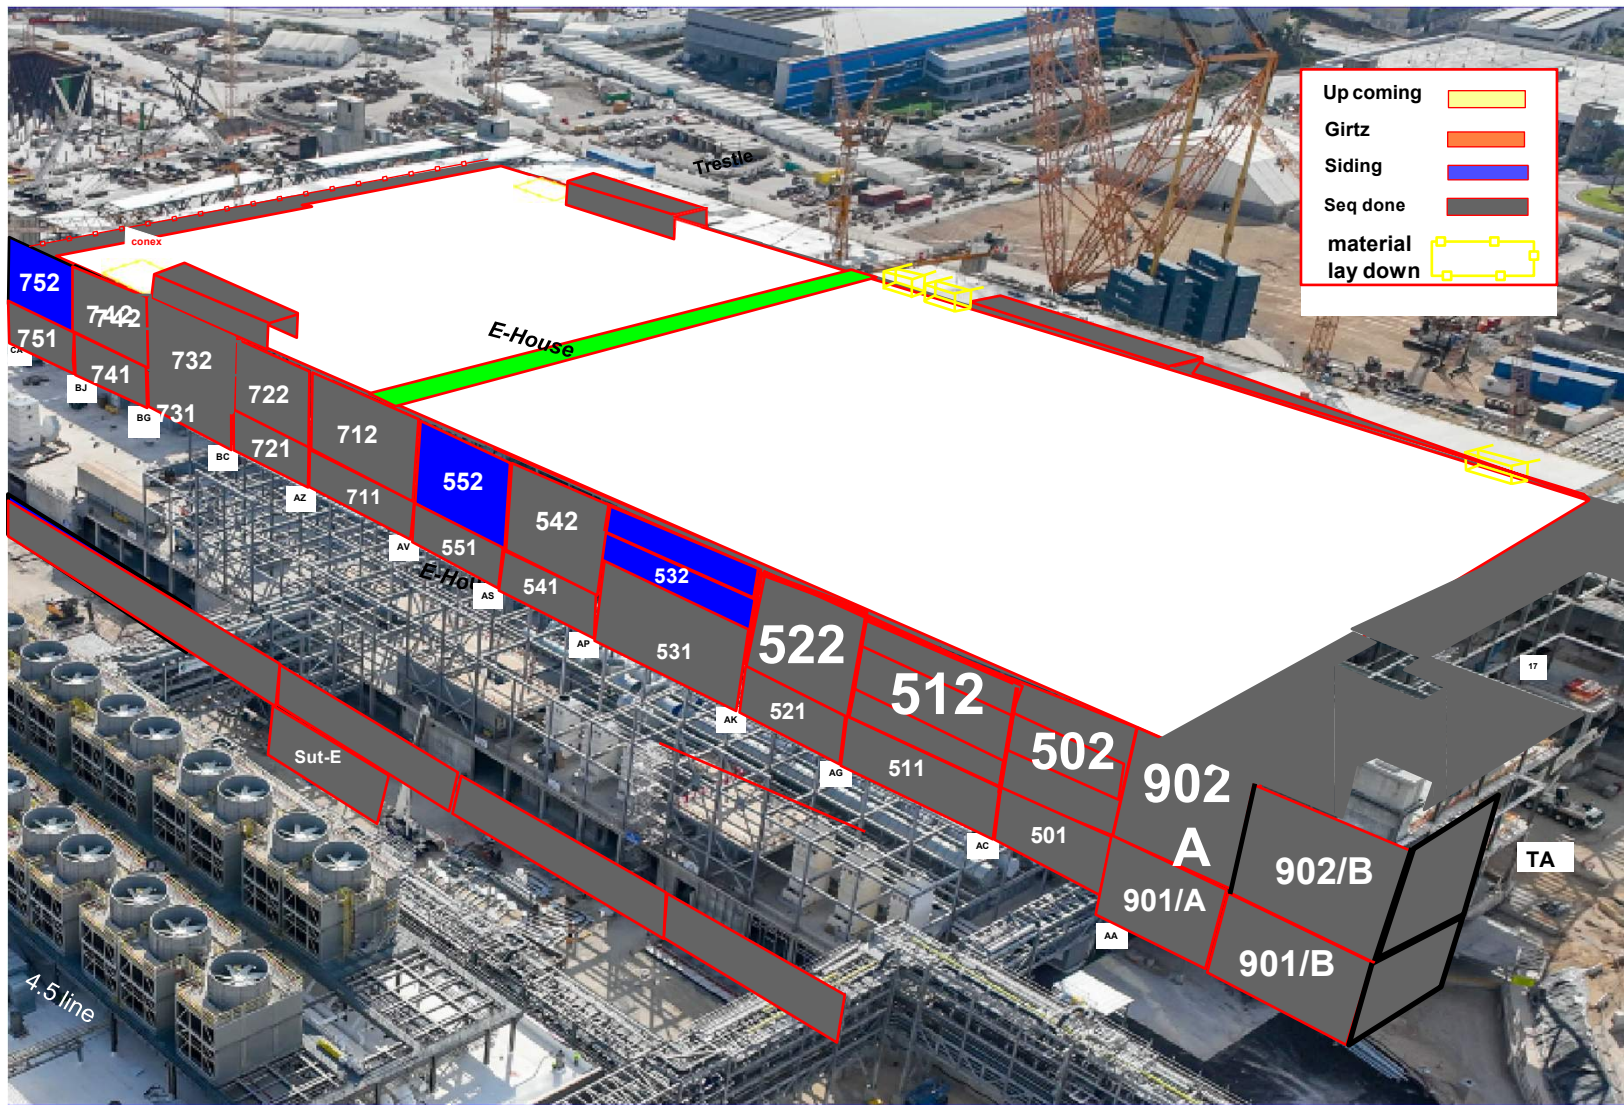

Walkpath

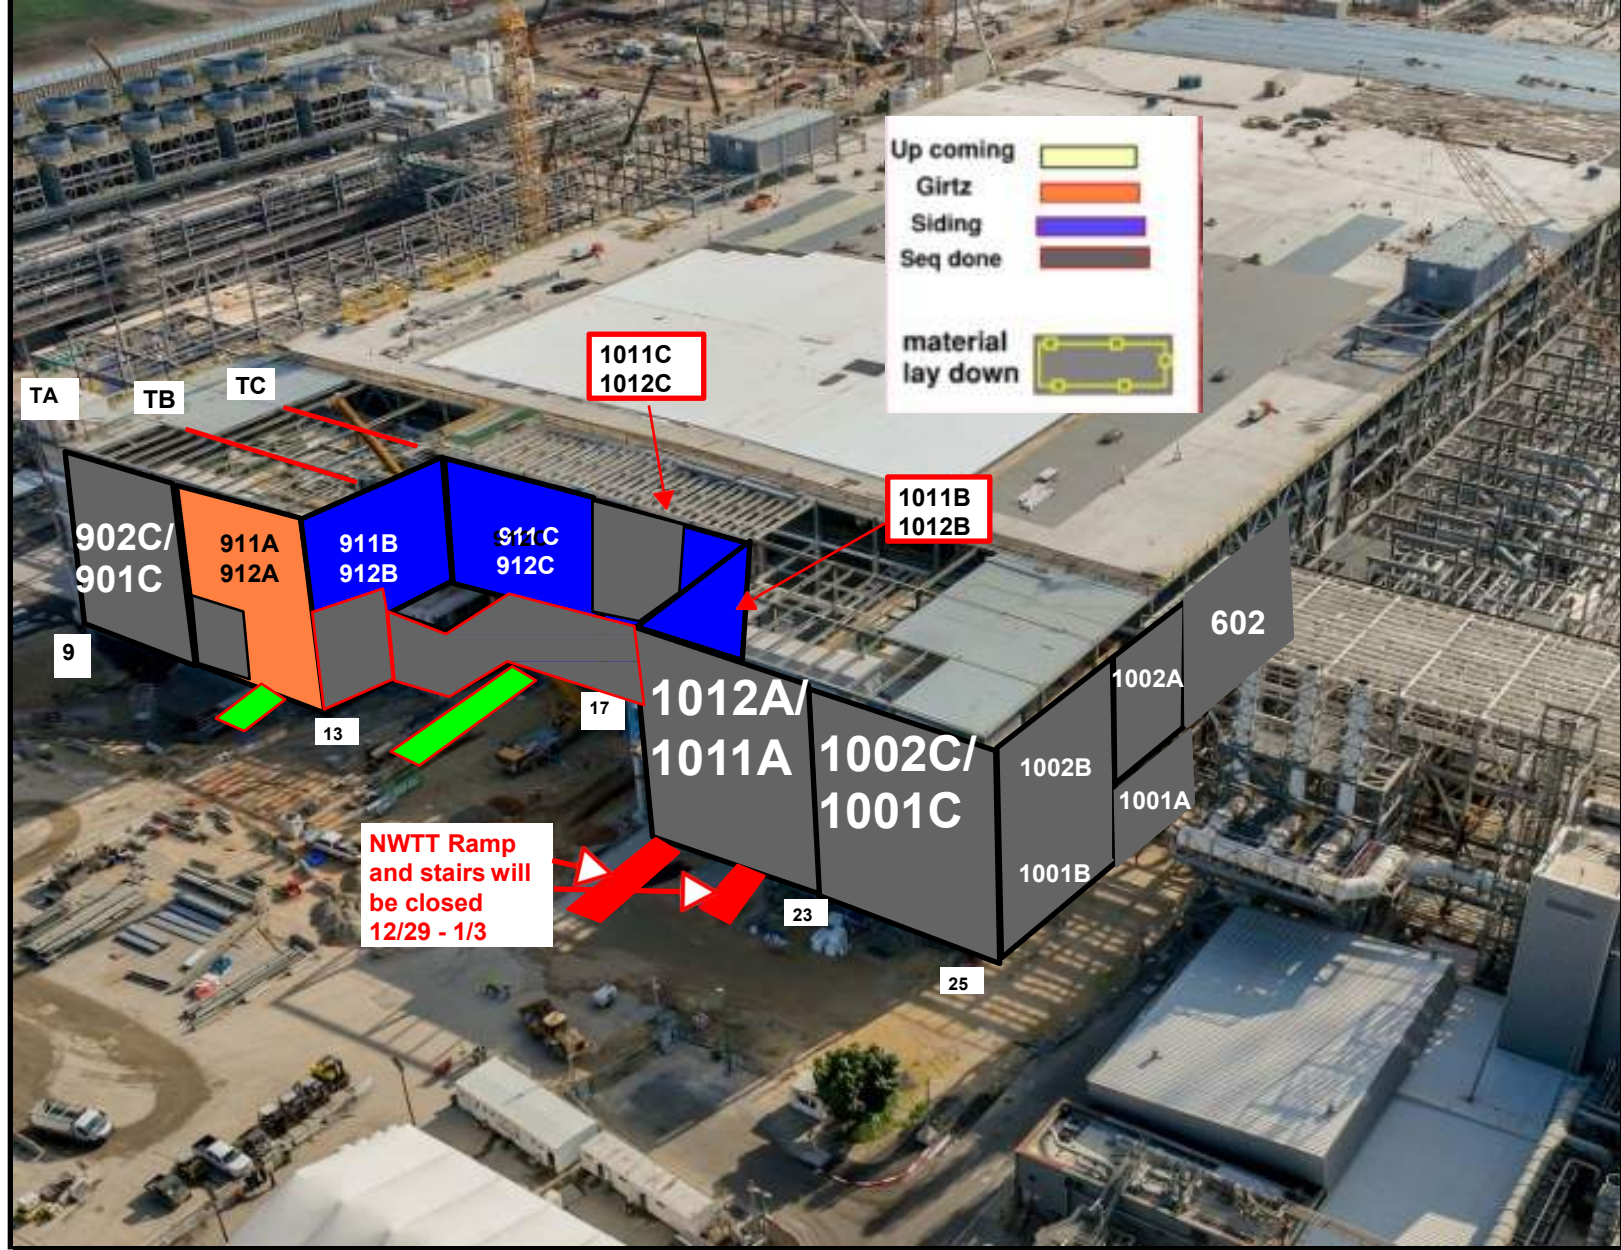

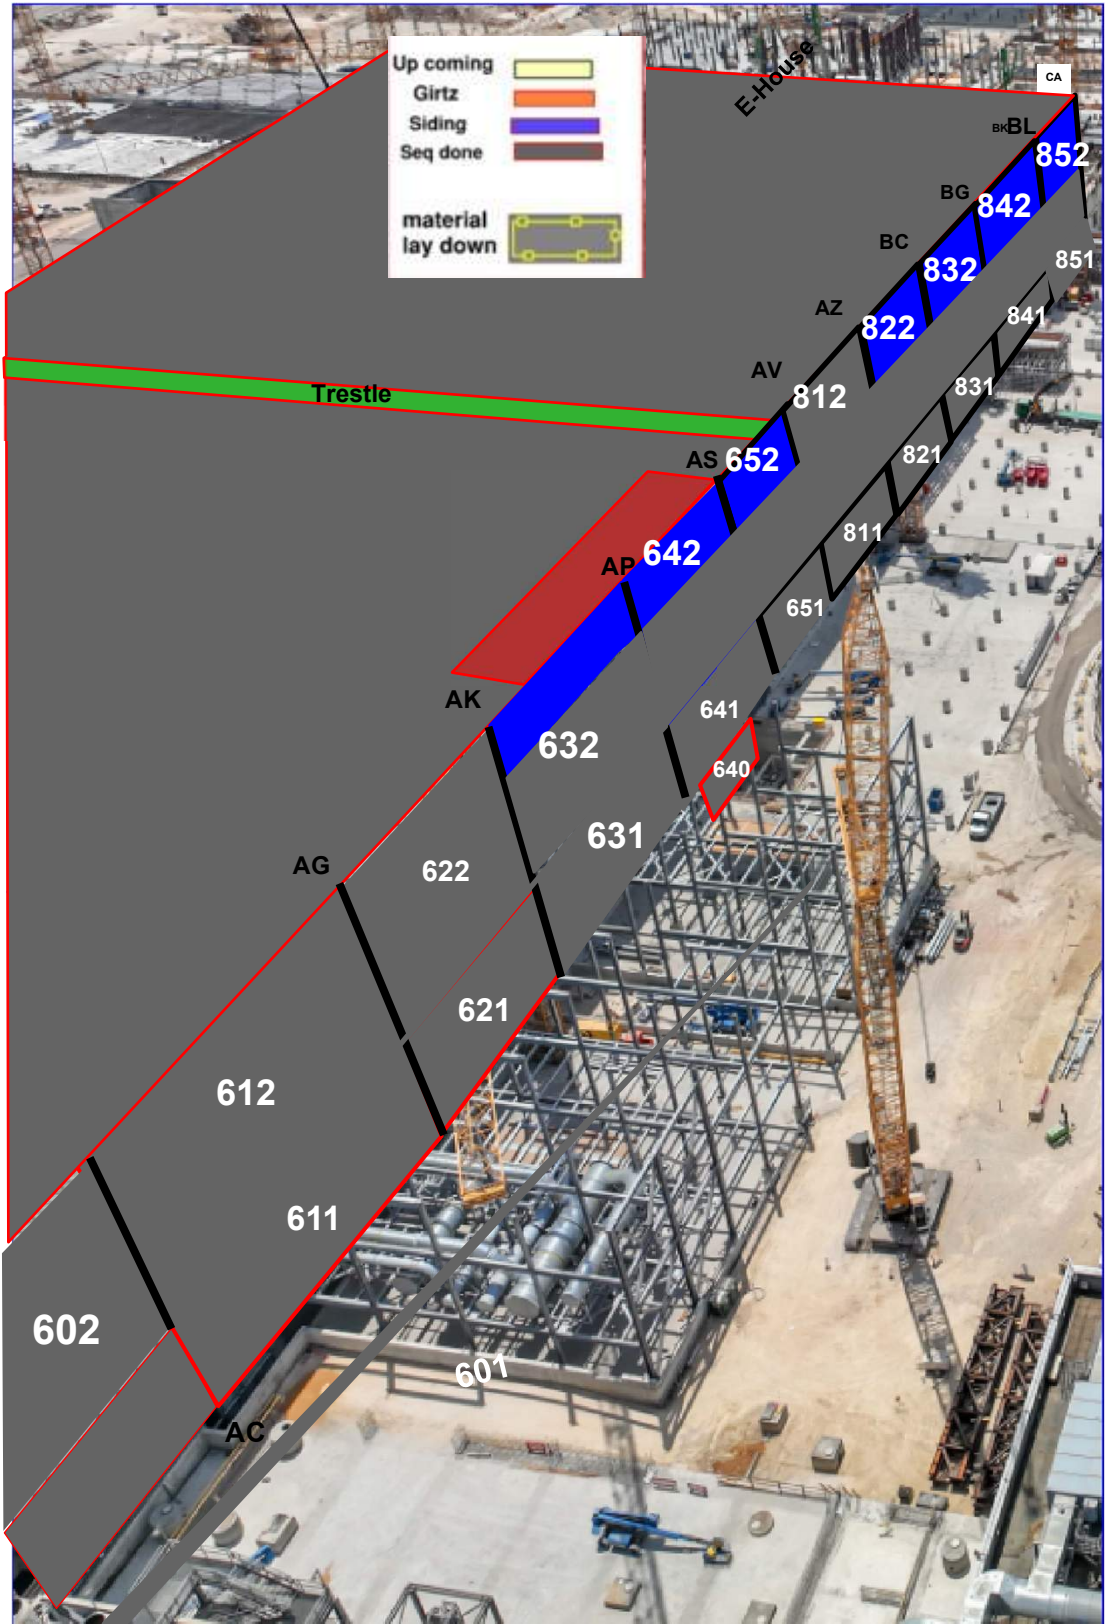



Up coming

Girtz

Siding

Seq done

material lay down

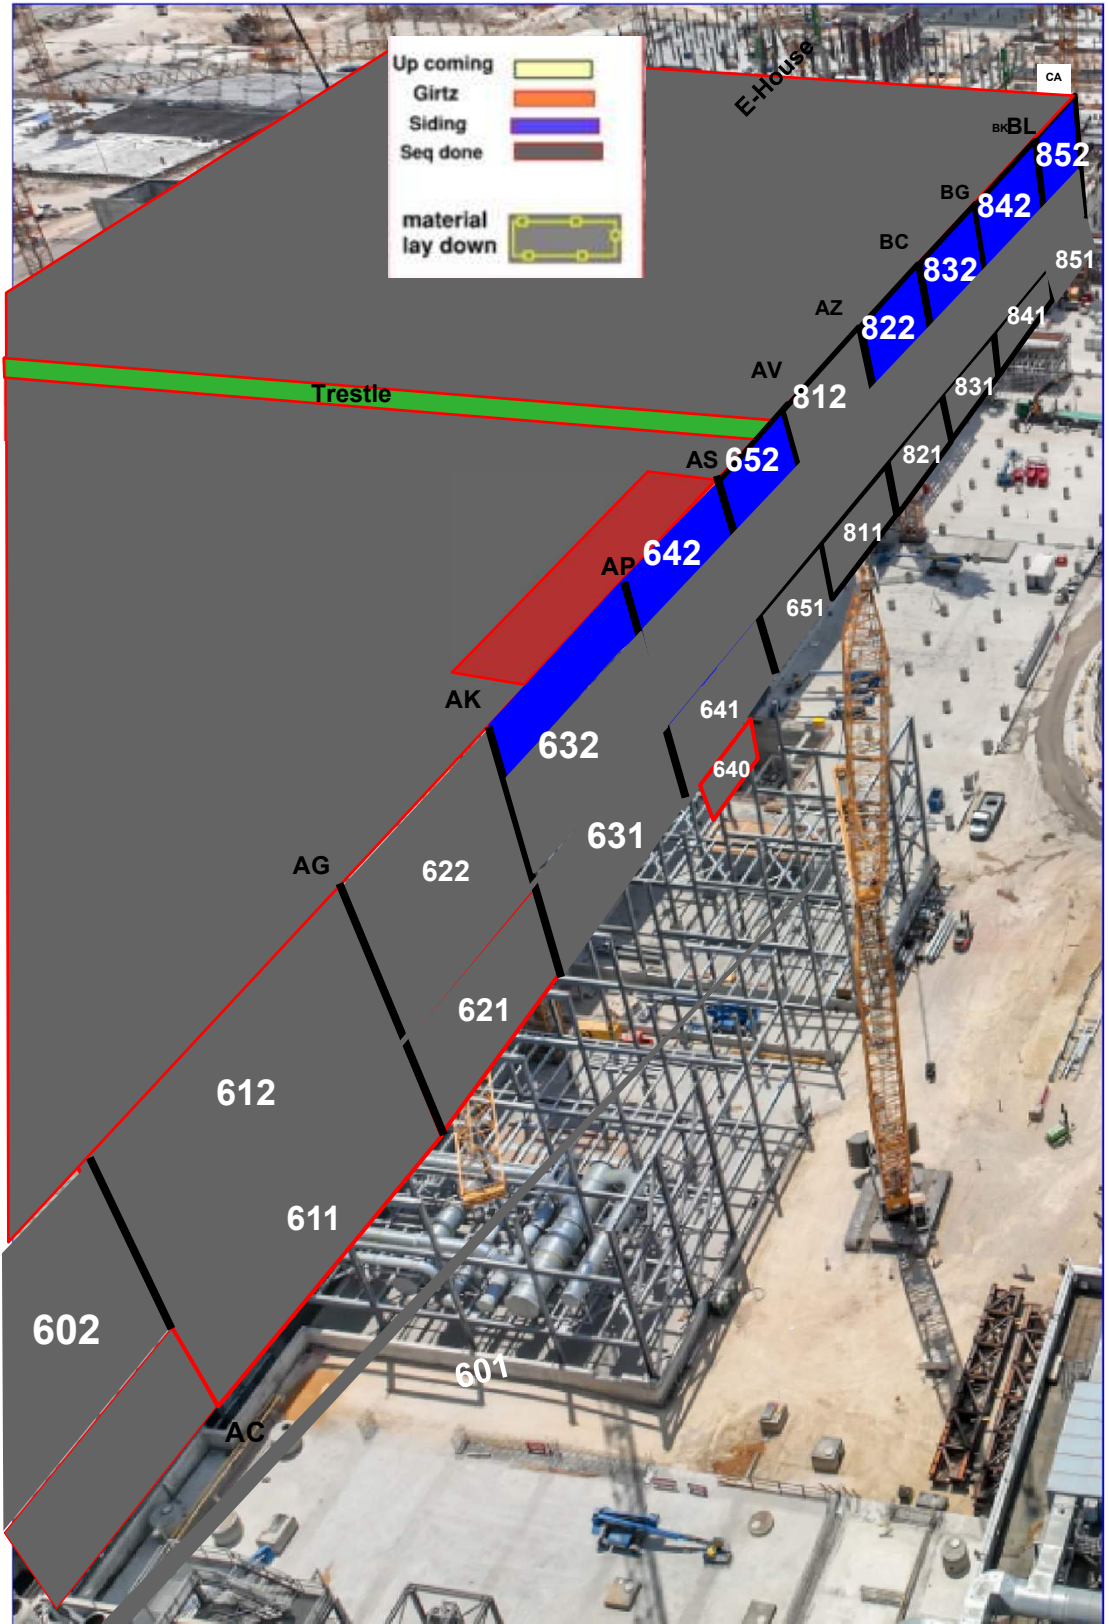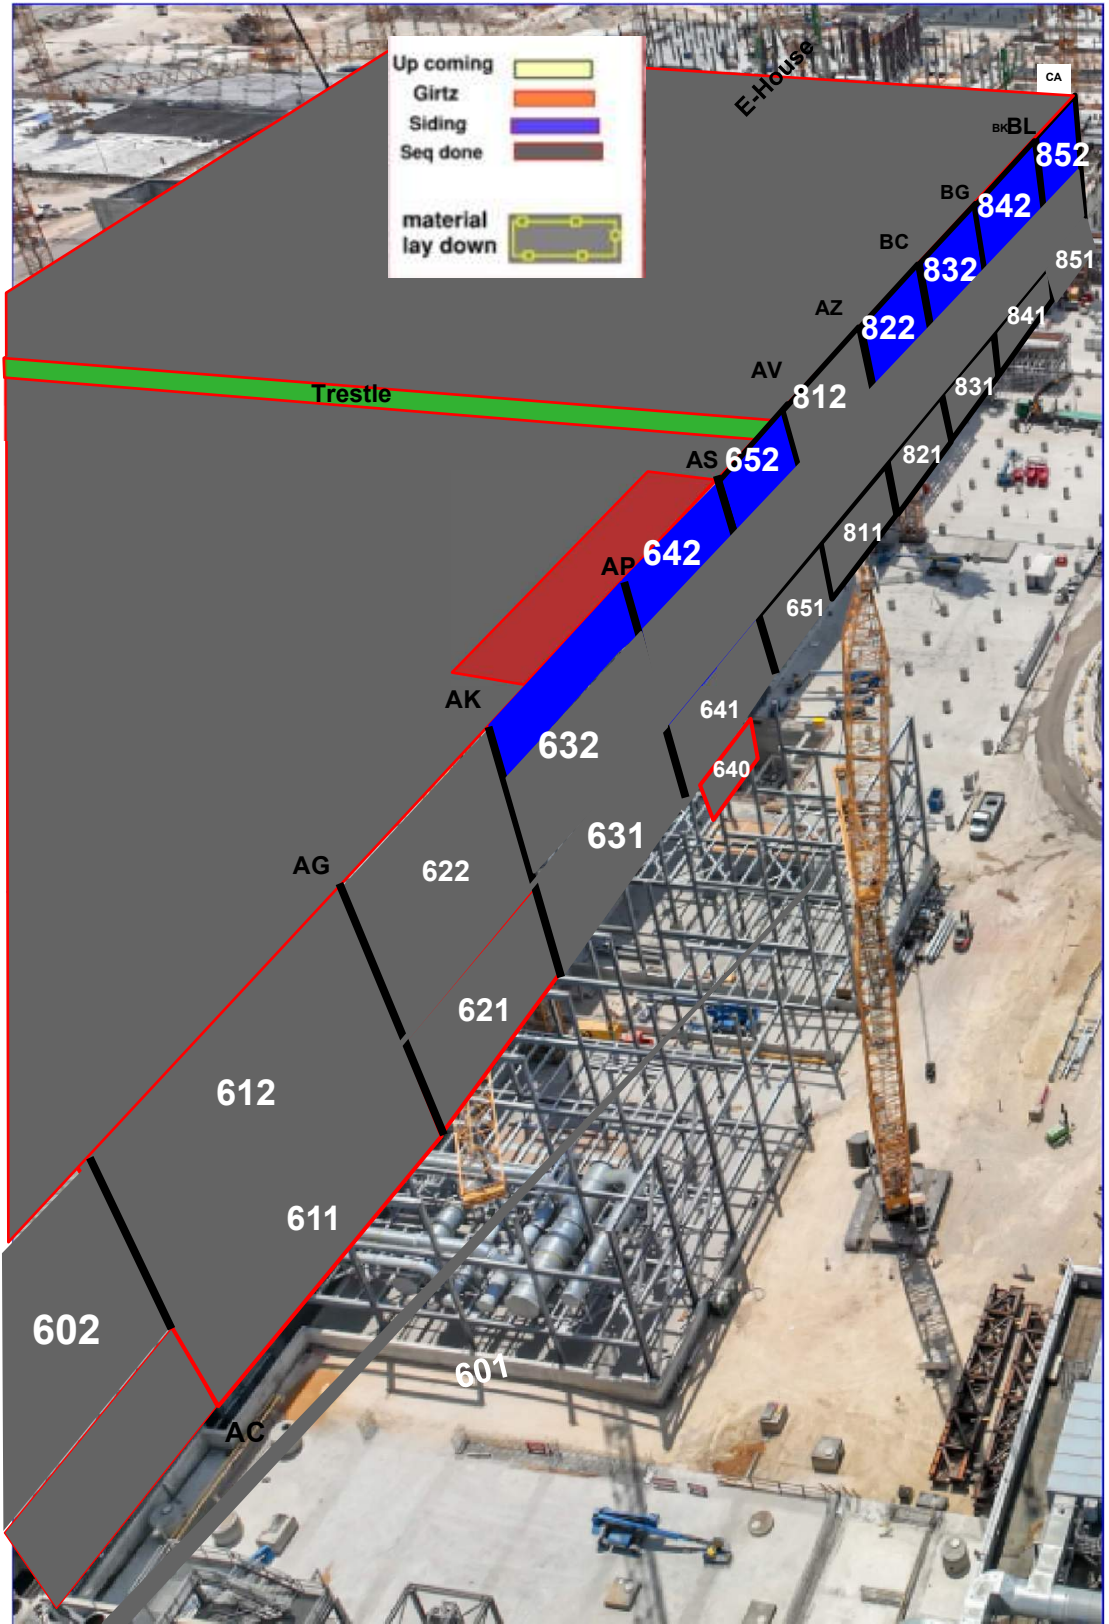


Mod 2 E House Roof
Picks.

Jan 6th @ 4:00 AM
Jan 8th @ 4:00 AM

Area to be
Closed for
Swing


Condensed
Barricade
for Bolting.

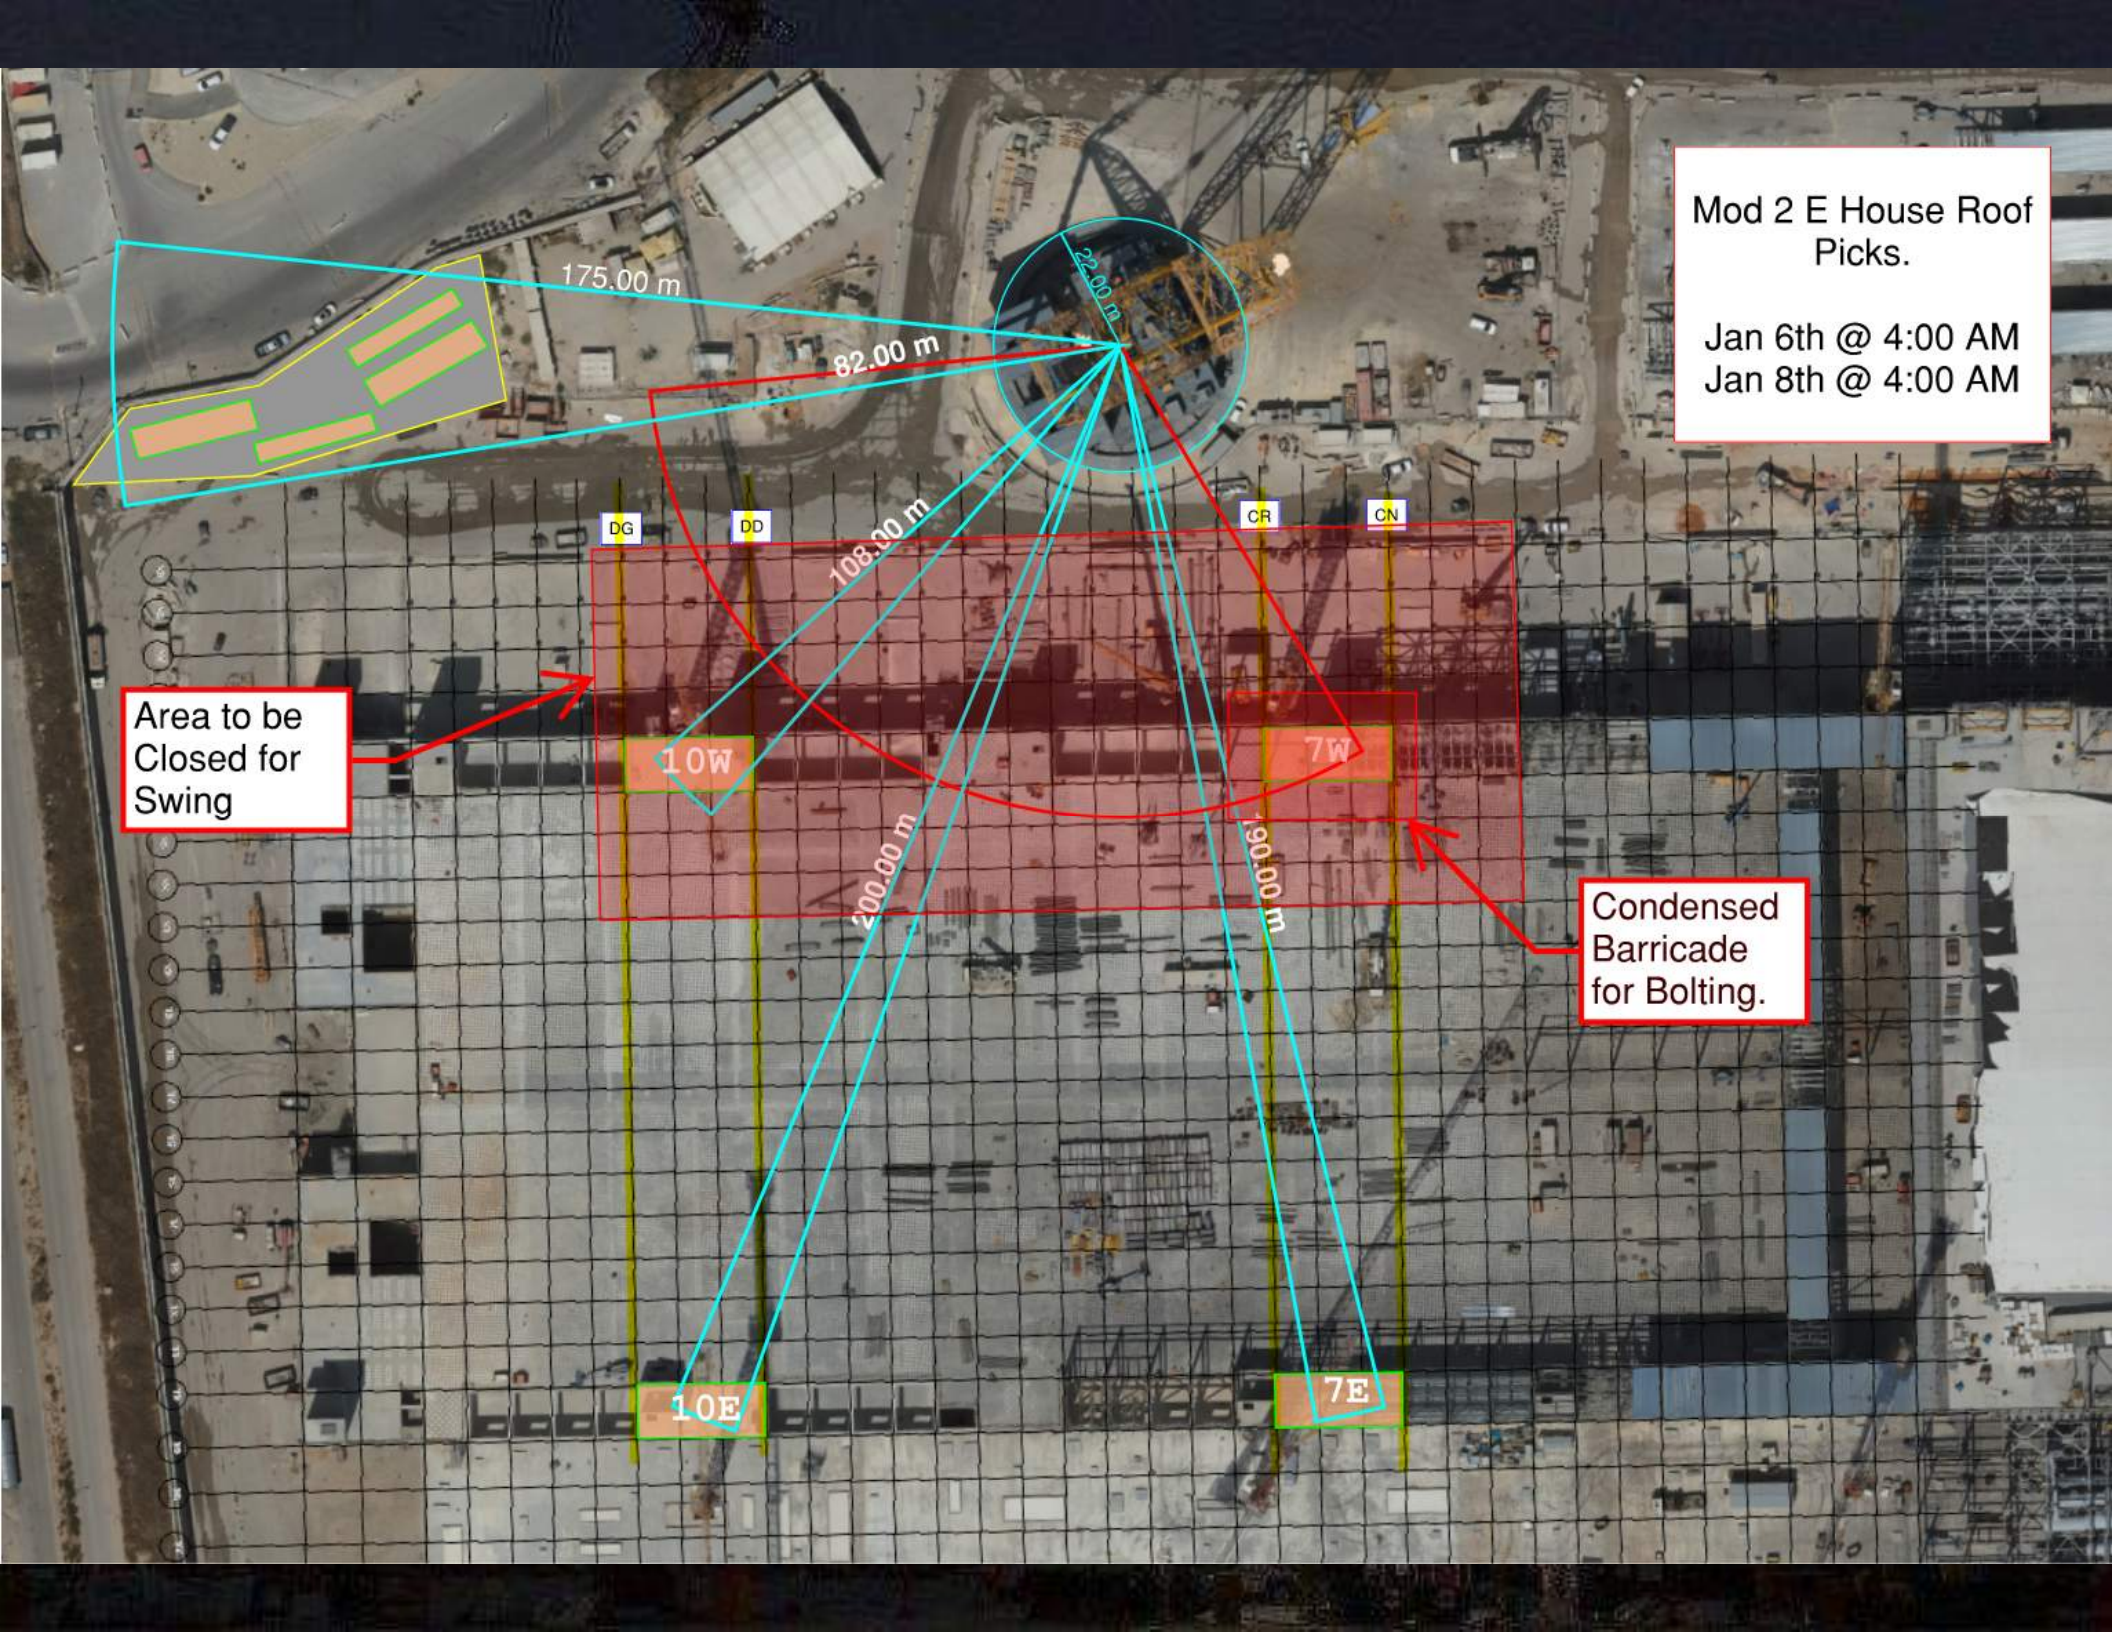

PSSS.1

Utility Level
1YA

PSSS Roof
2SA

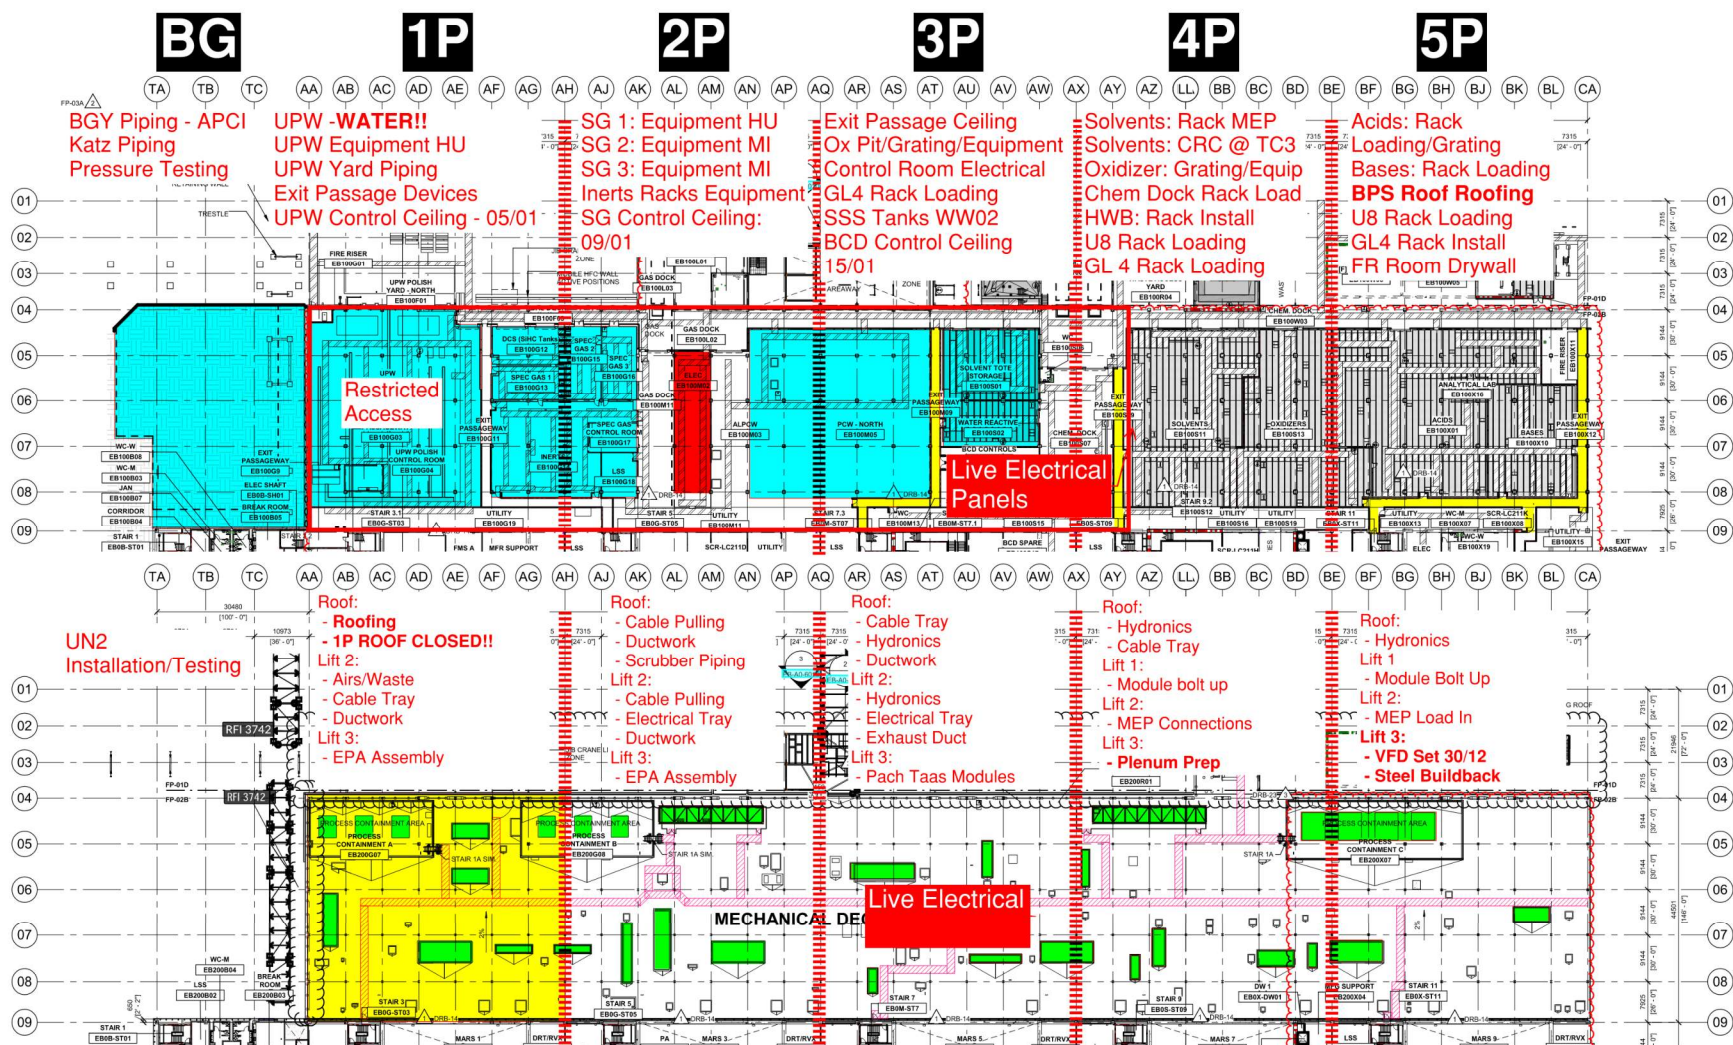

PSSS.2



PSSS Pressure Tests

BG

1P


2P

3P


4P

5P


Utility Level
1YA

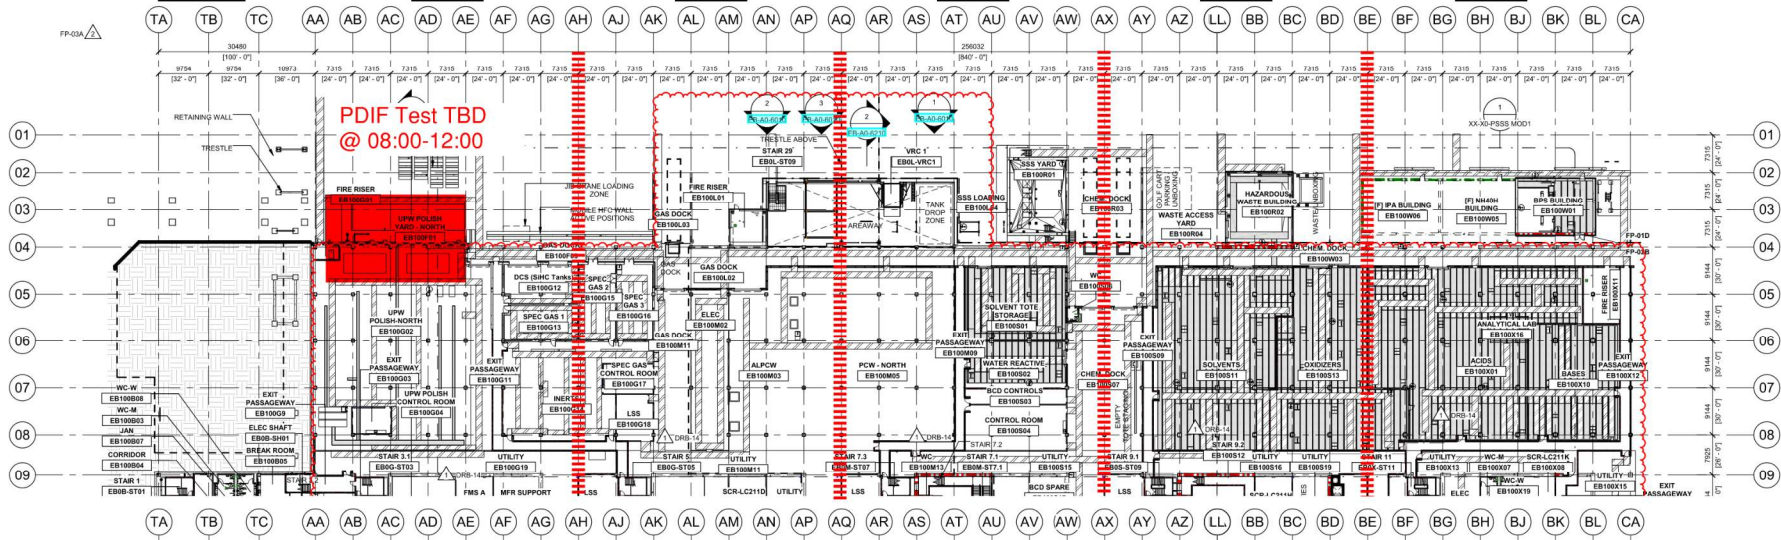

PSSS Roof
2SA

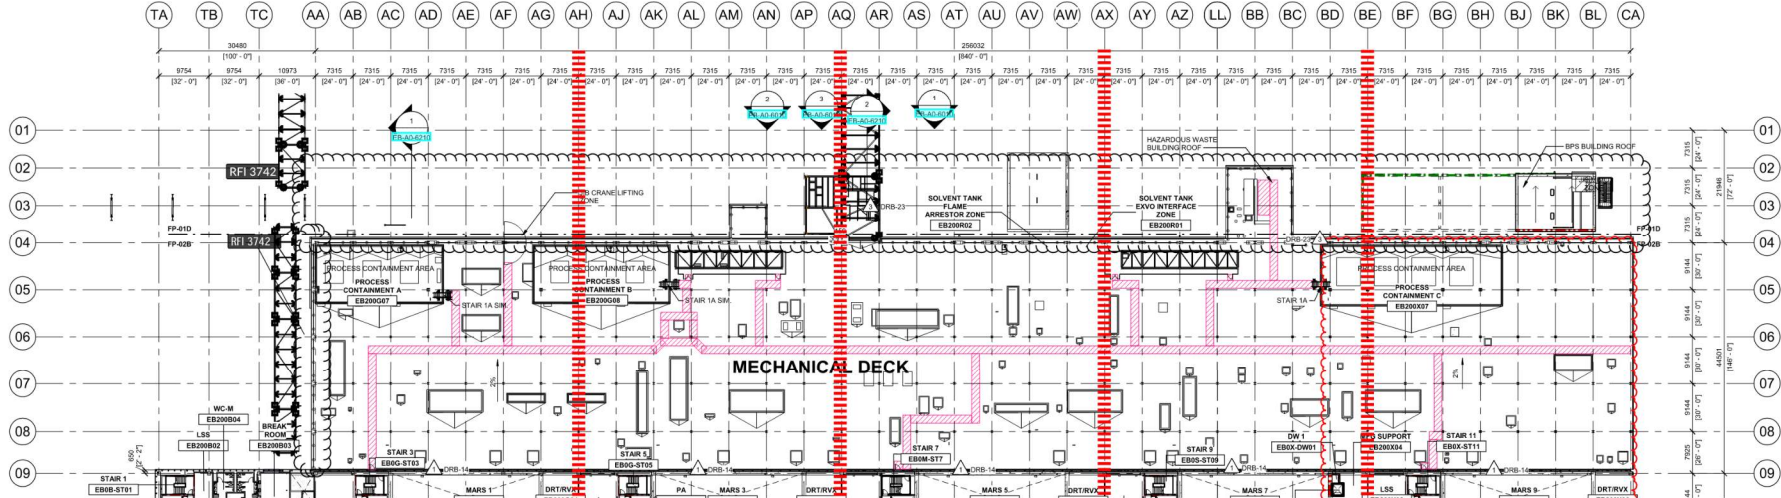

PSSS

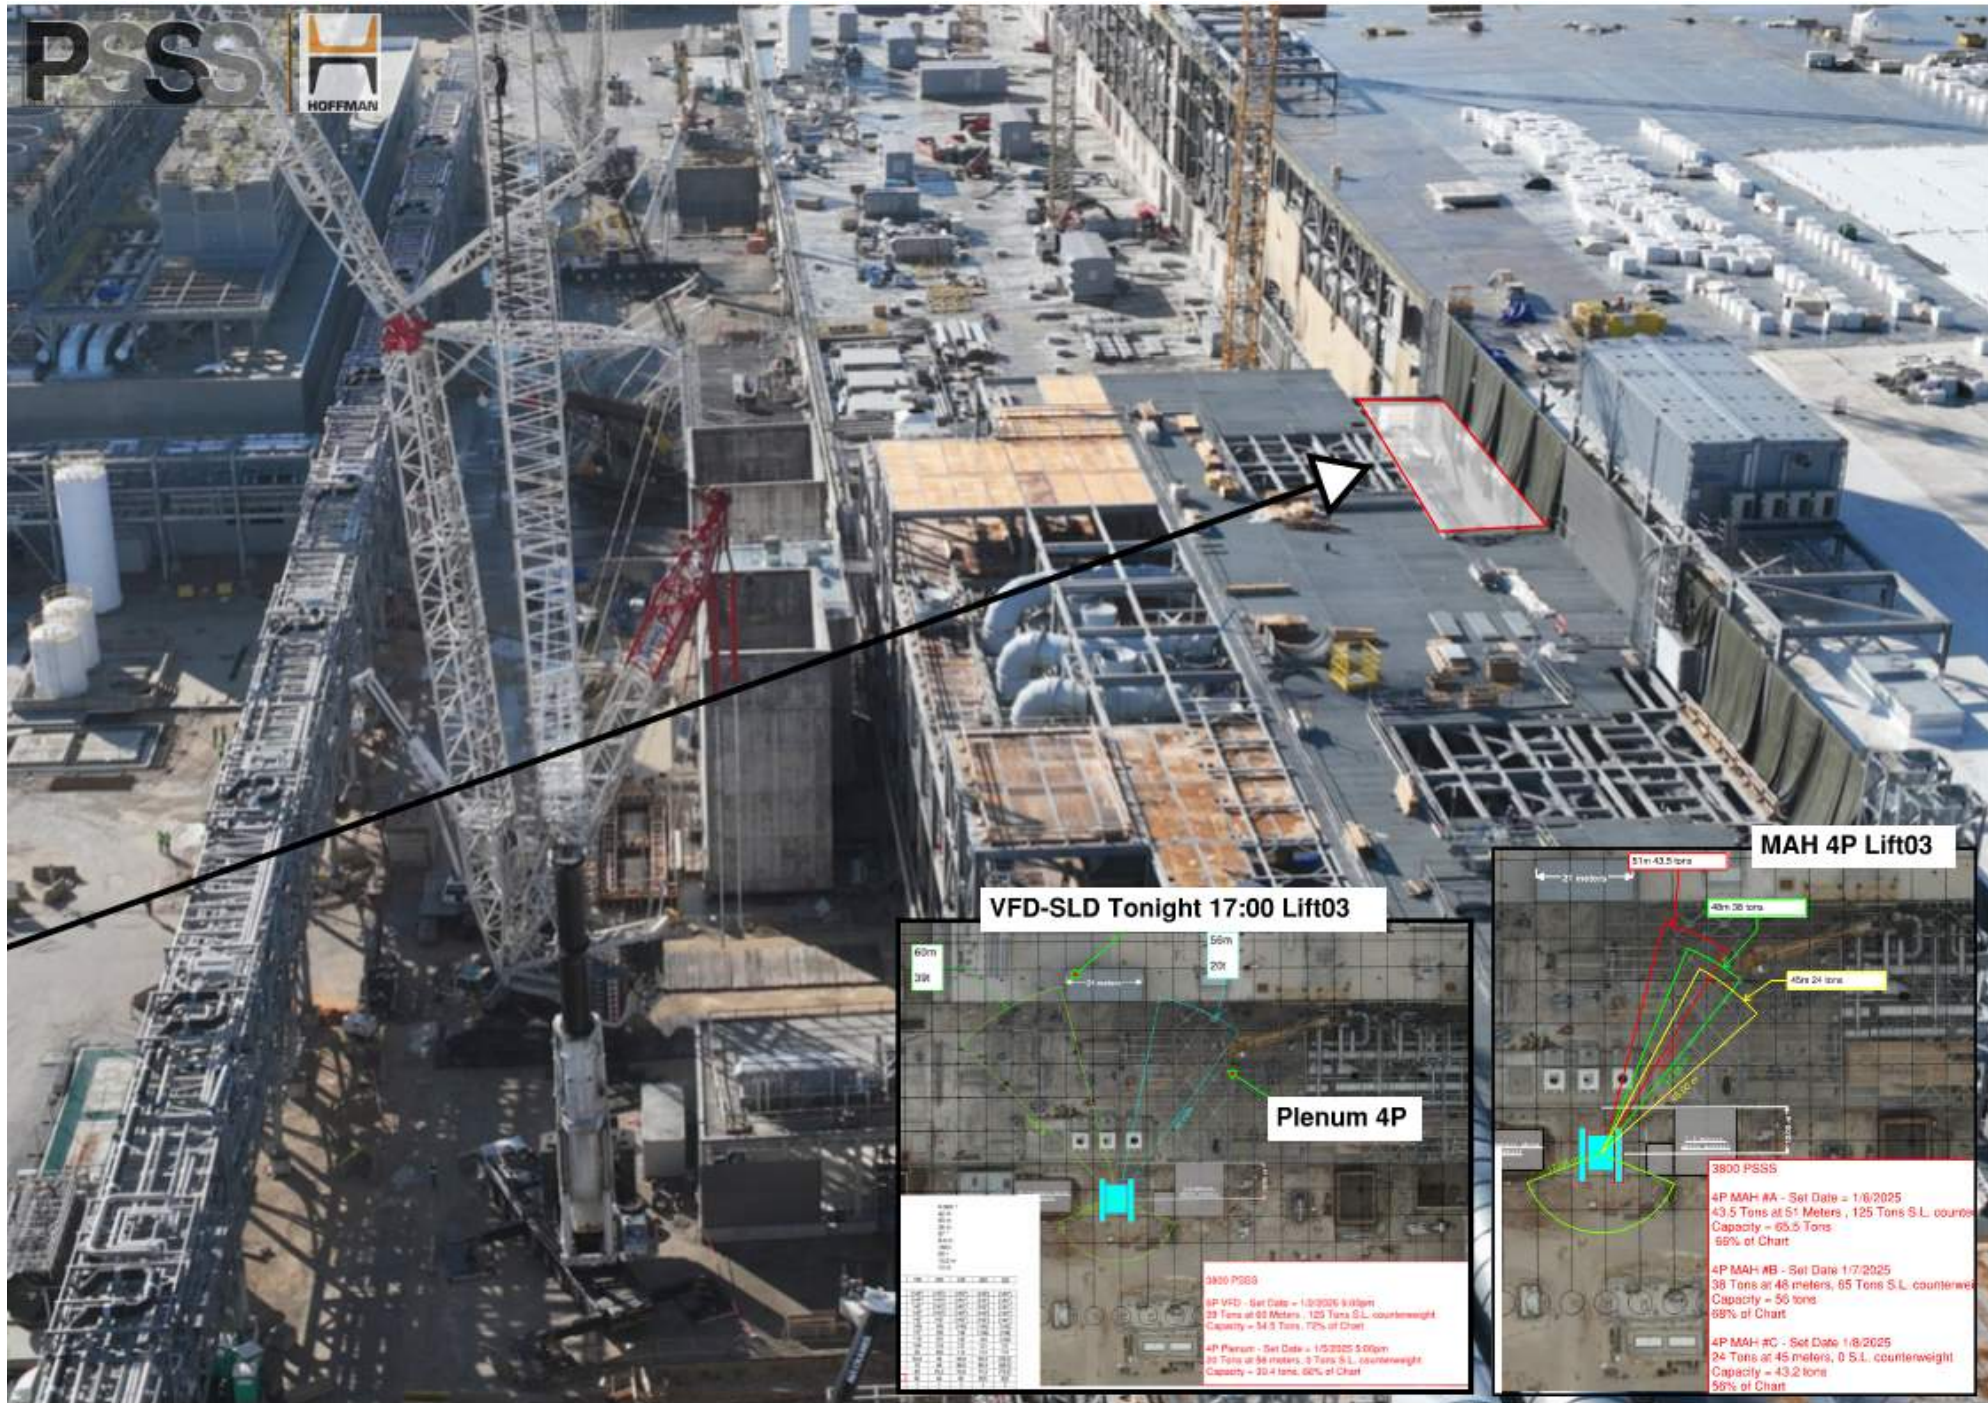


VFD-SLD Tonight 17:00 Lift03



MAH 4P Lift03







WJG 01J, 02J LIFT 2 & 3




WJG 03J, 04J, 05J LIFT 2 & 3

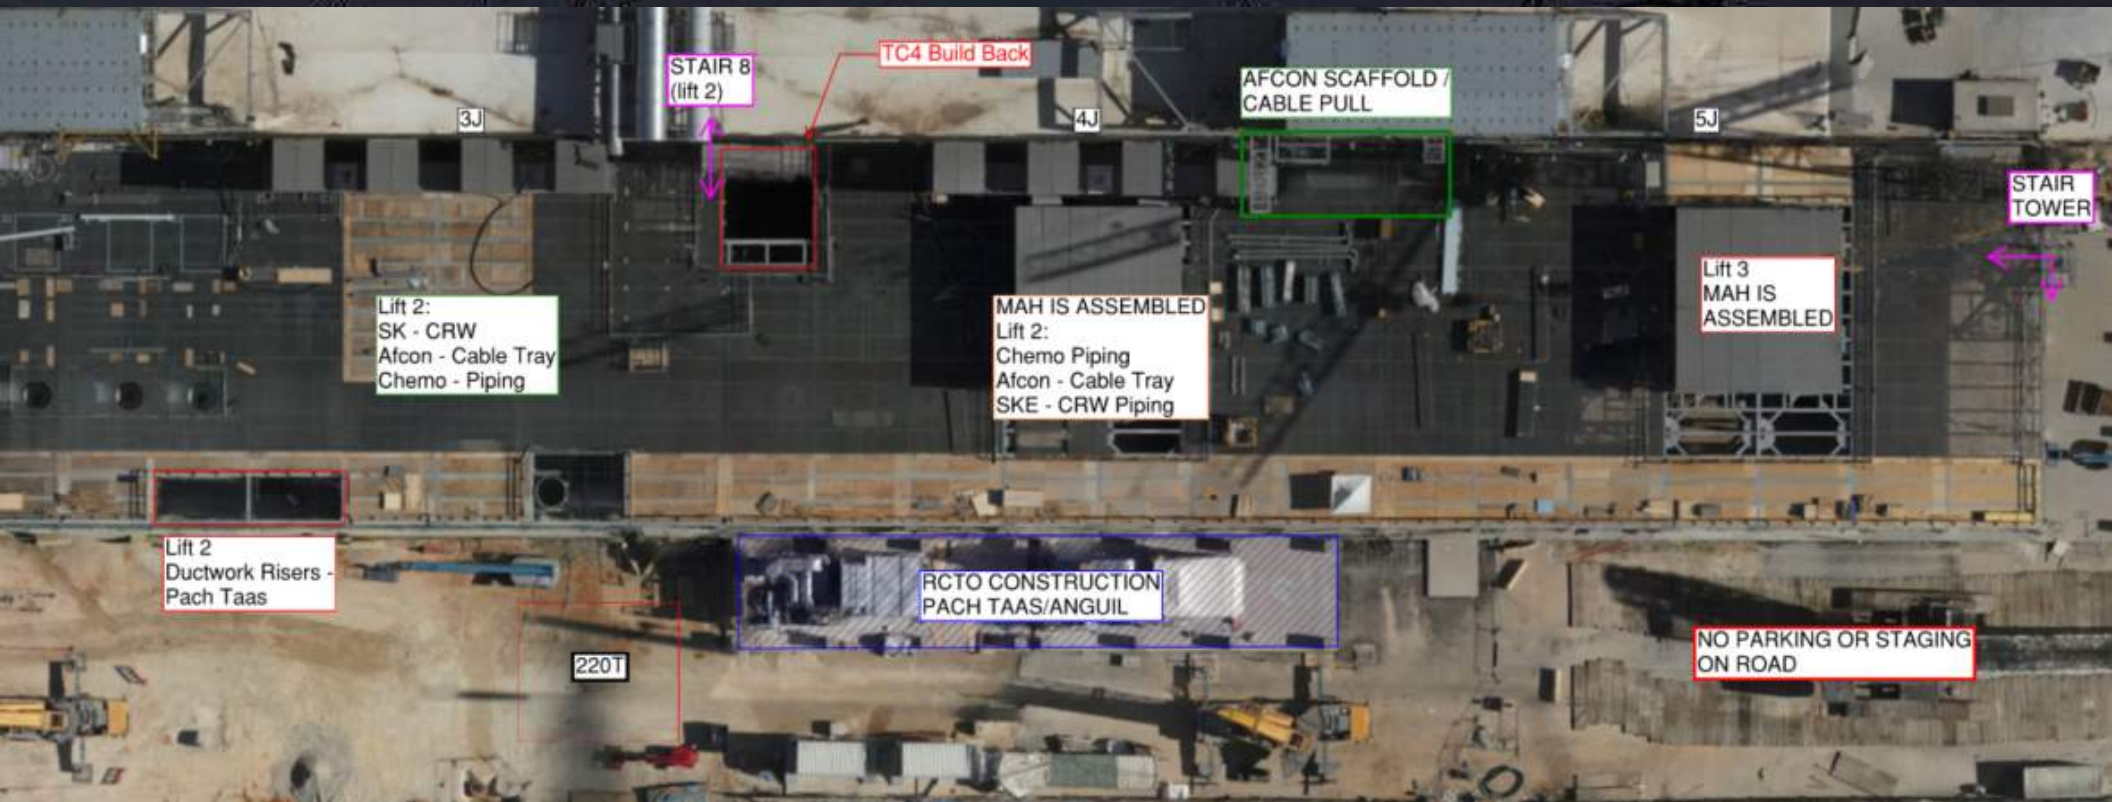



WJG UTILITY LEVEL BUILD OUT

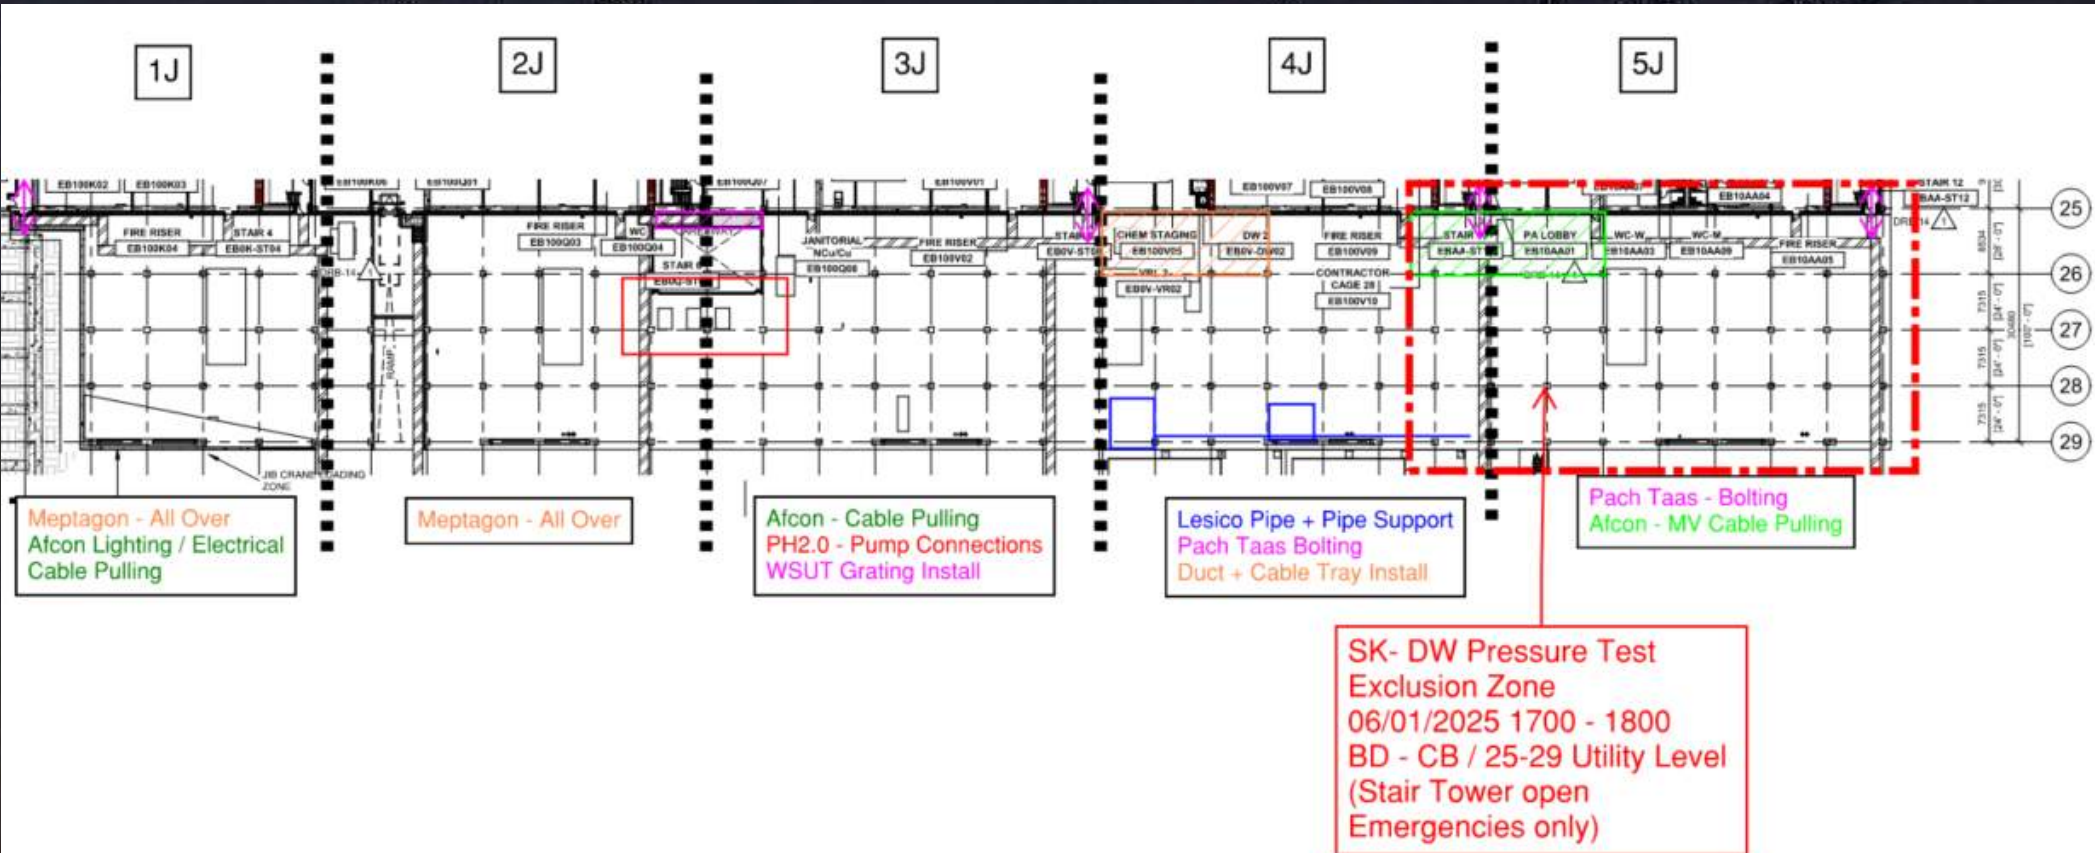

CUB 1 Intel Fuel Off-Load




CUB 1 Intel Fuel Off-Load







CUB 1

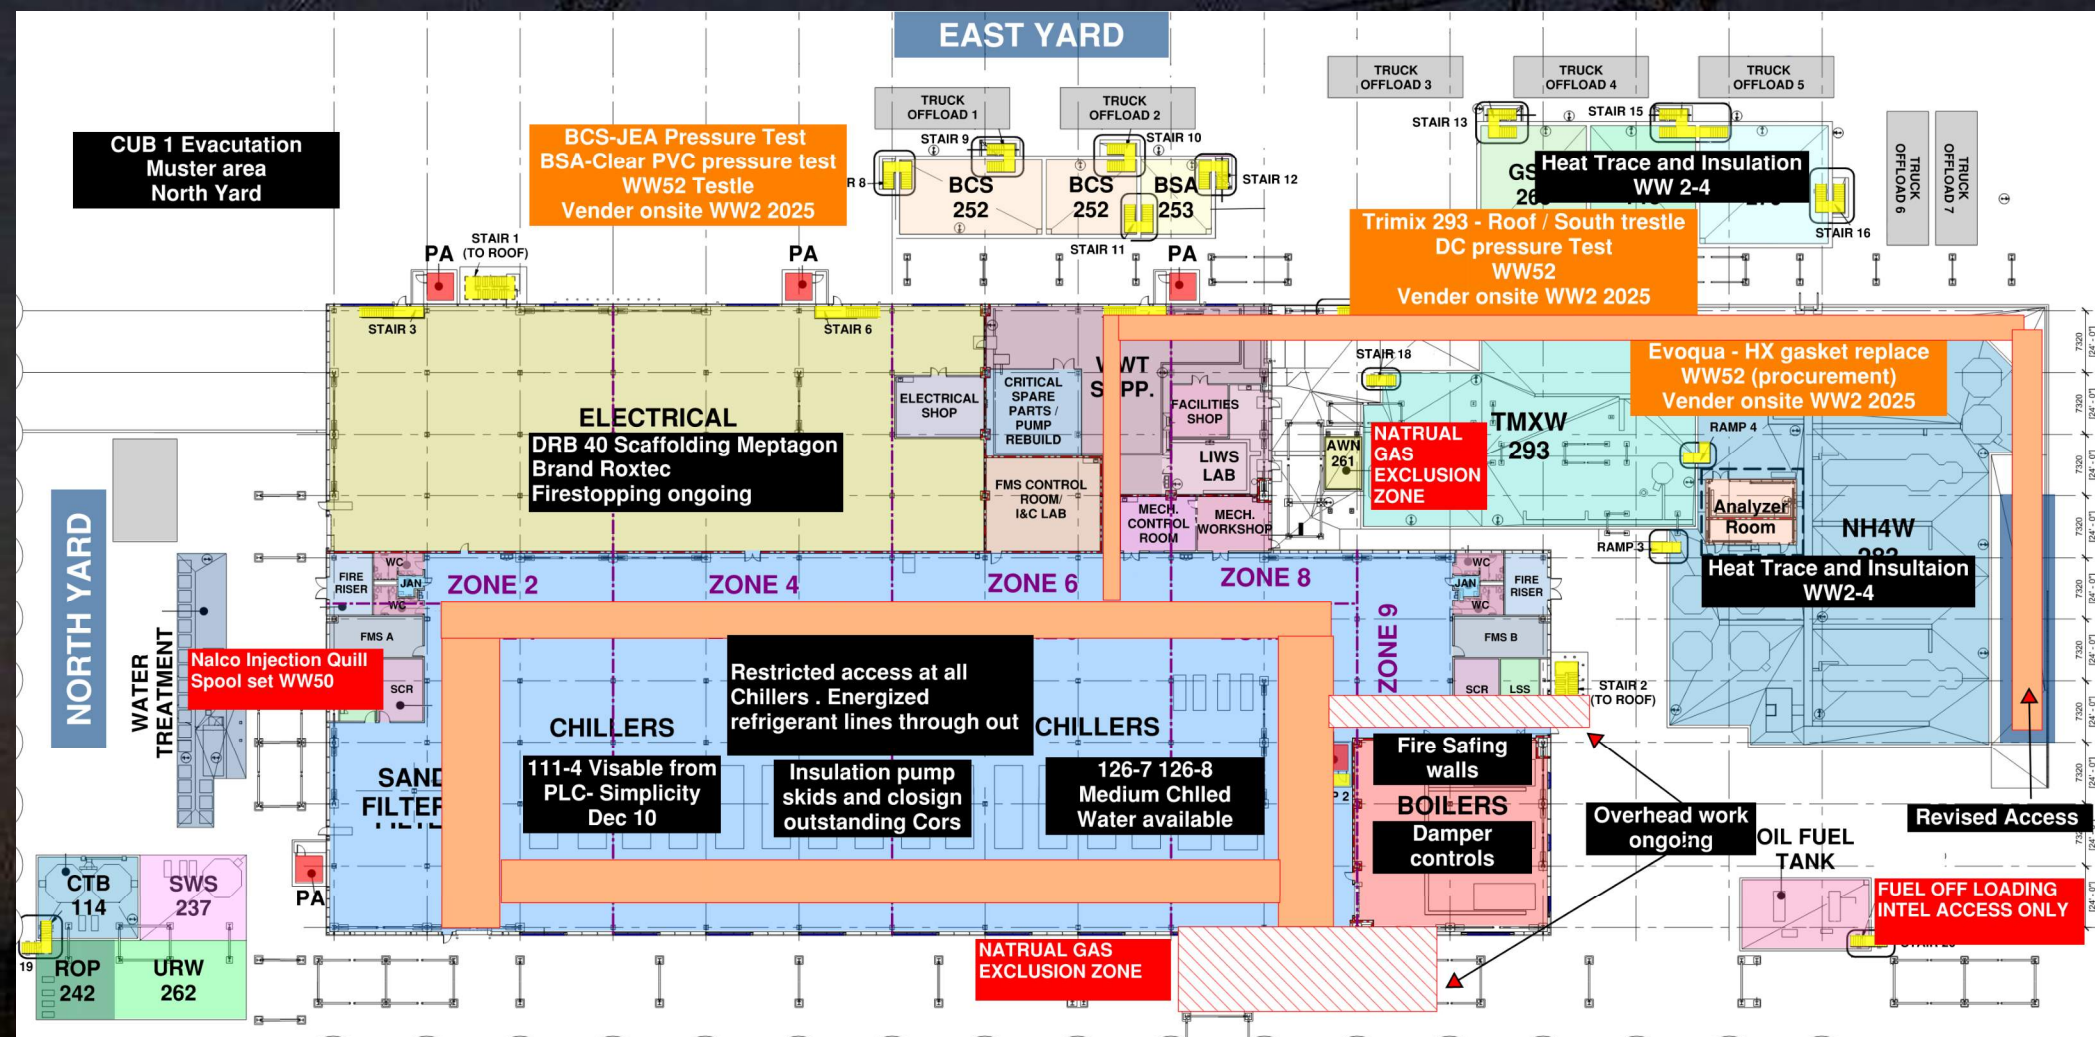

CUB 1 – EXTERIOR/ROOF

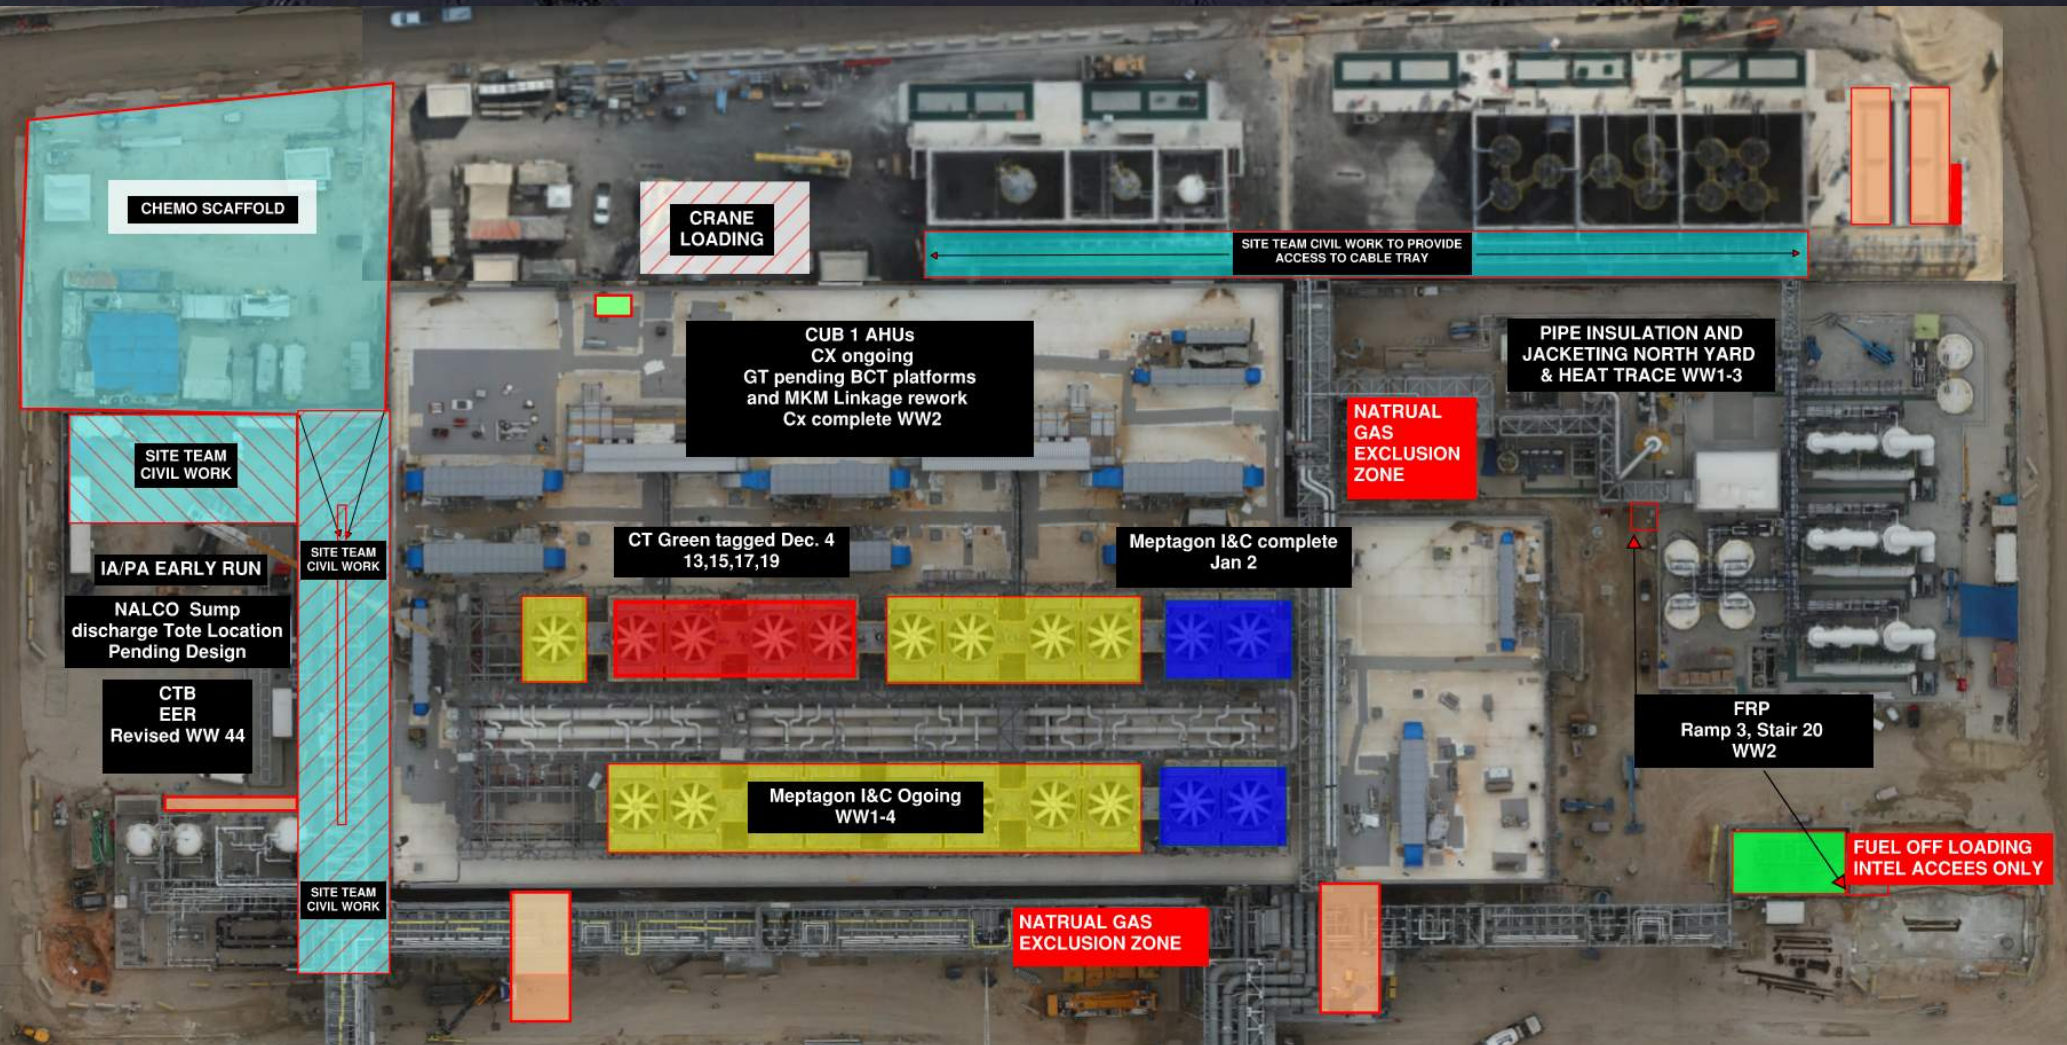


CUB 2- Load in ,H&T, Framing and Sheetrock

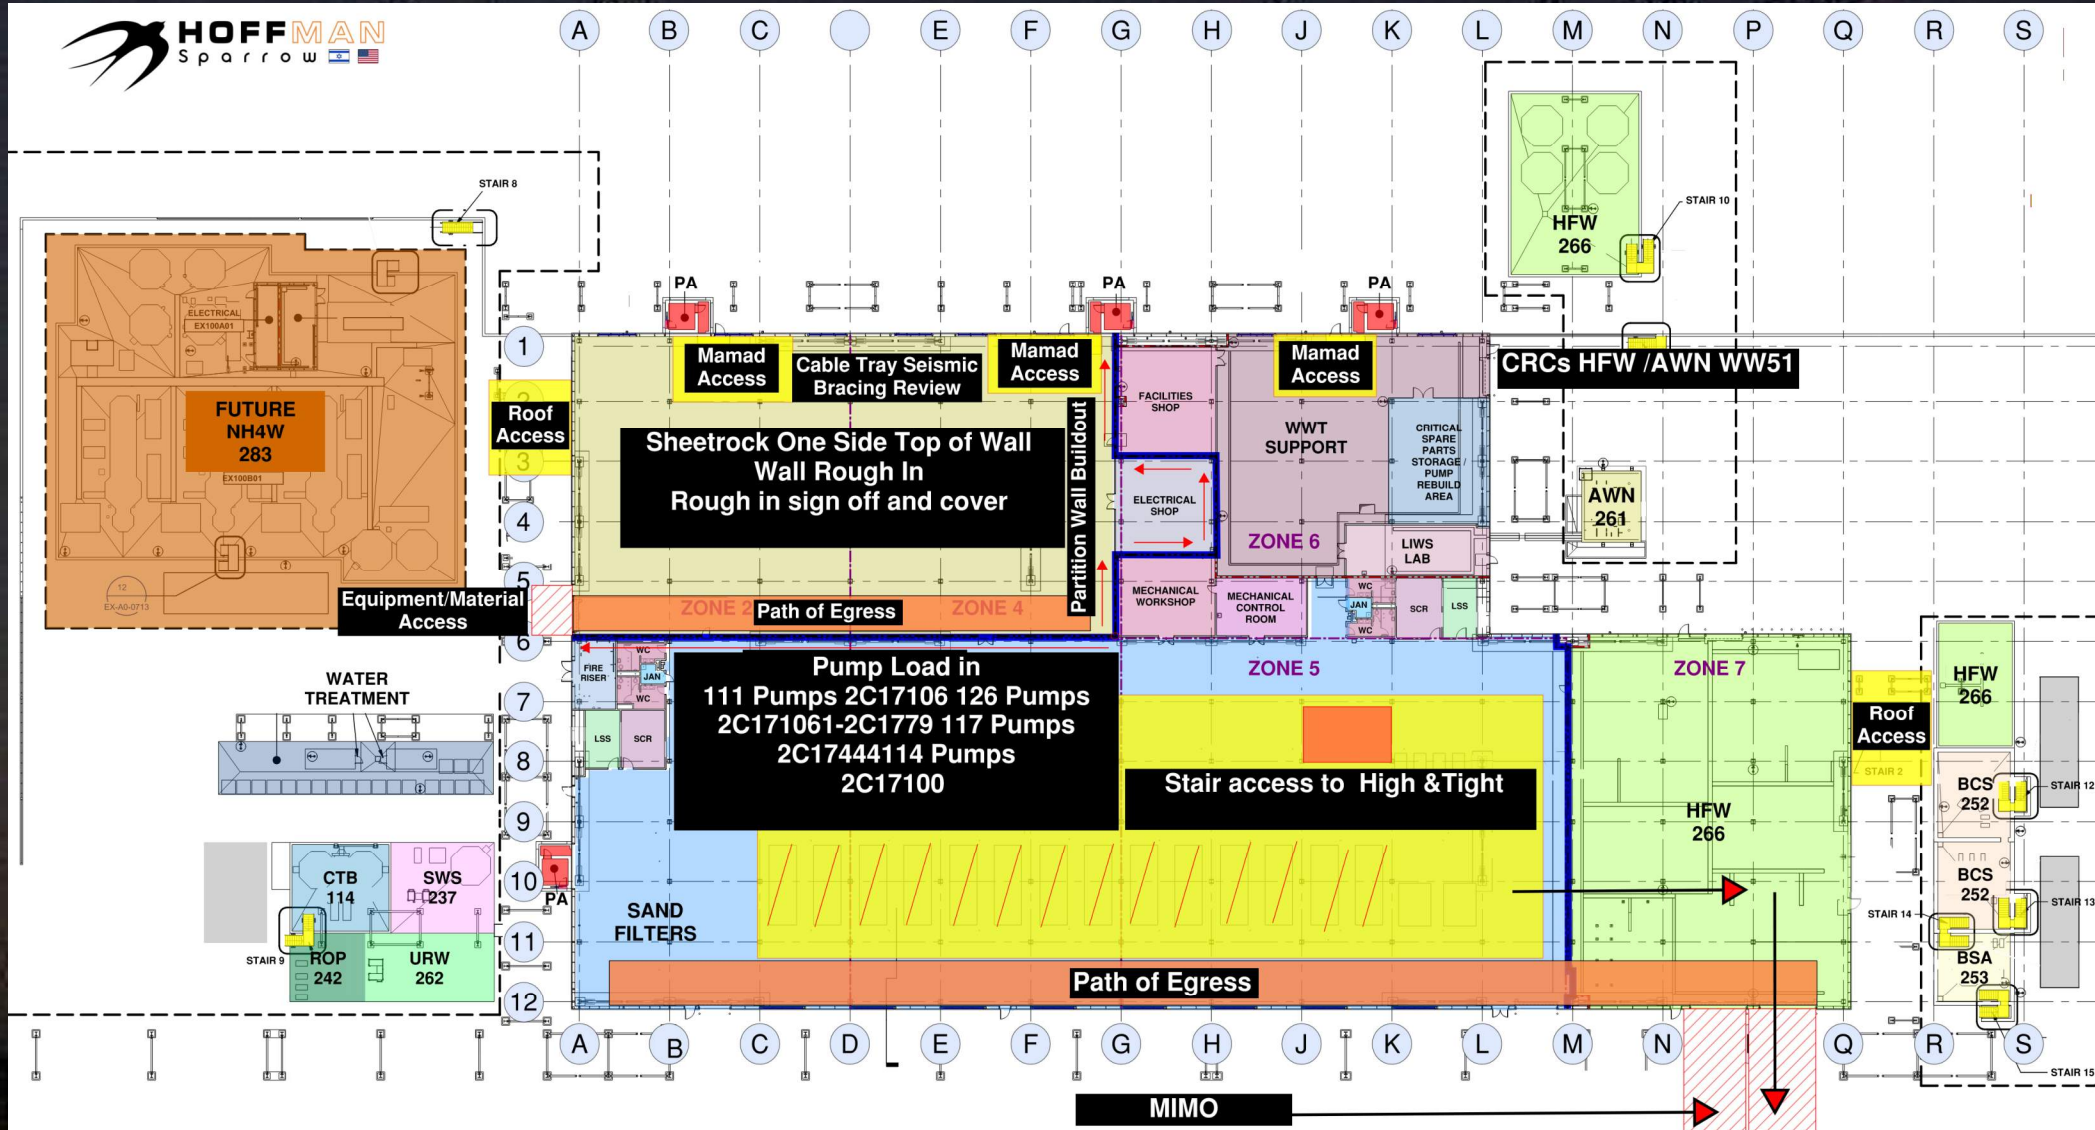



CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY

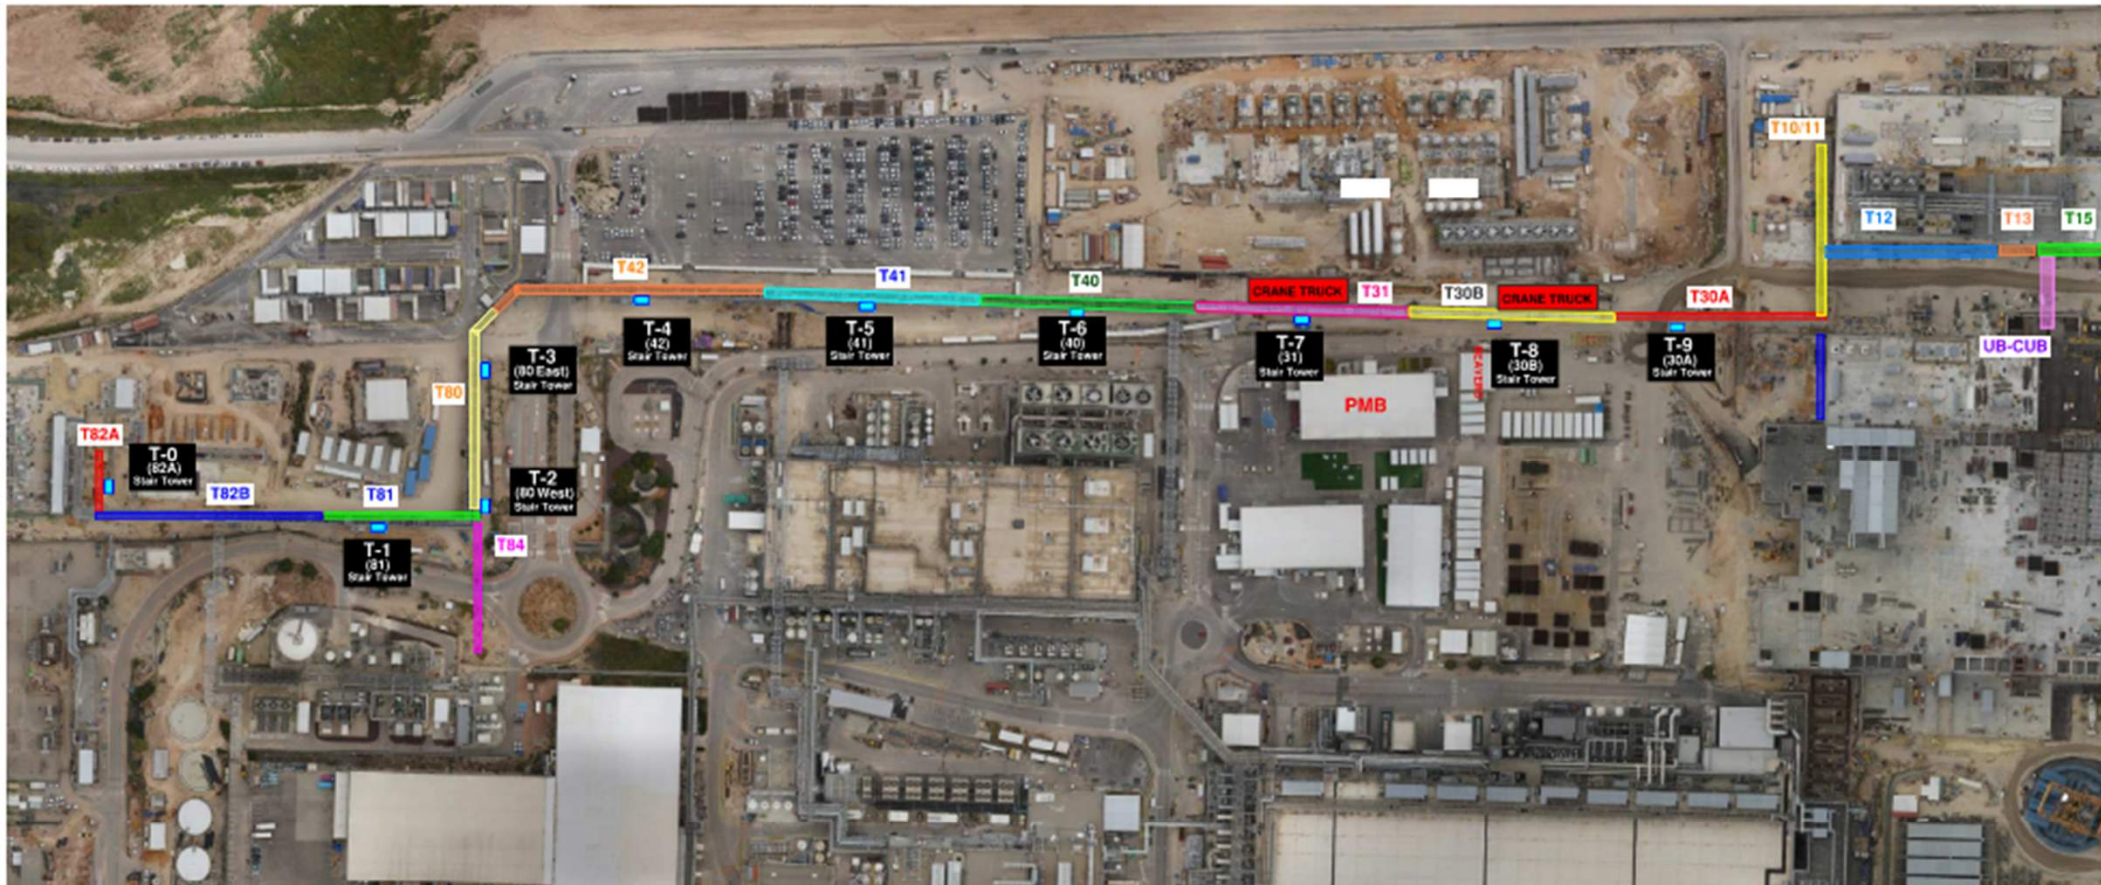



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

Starting –Monday Jan 6th night at 19:00
Finish Tuesday Jan 7th at 05:00am.

Starting –Tuesday Jan 7th at 19:00
Finish Wednesday Jan 8th at 05:00am

Starting –Wednesday Jan 8th at 19:00
Finish Thursday Jan 9th at 05:00am


BGC - NDT

Safety spotter

No impact on PMB
entrance\Exit

Safety spotter

Safety spotter

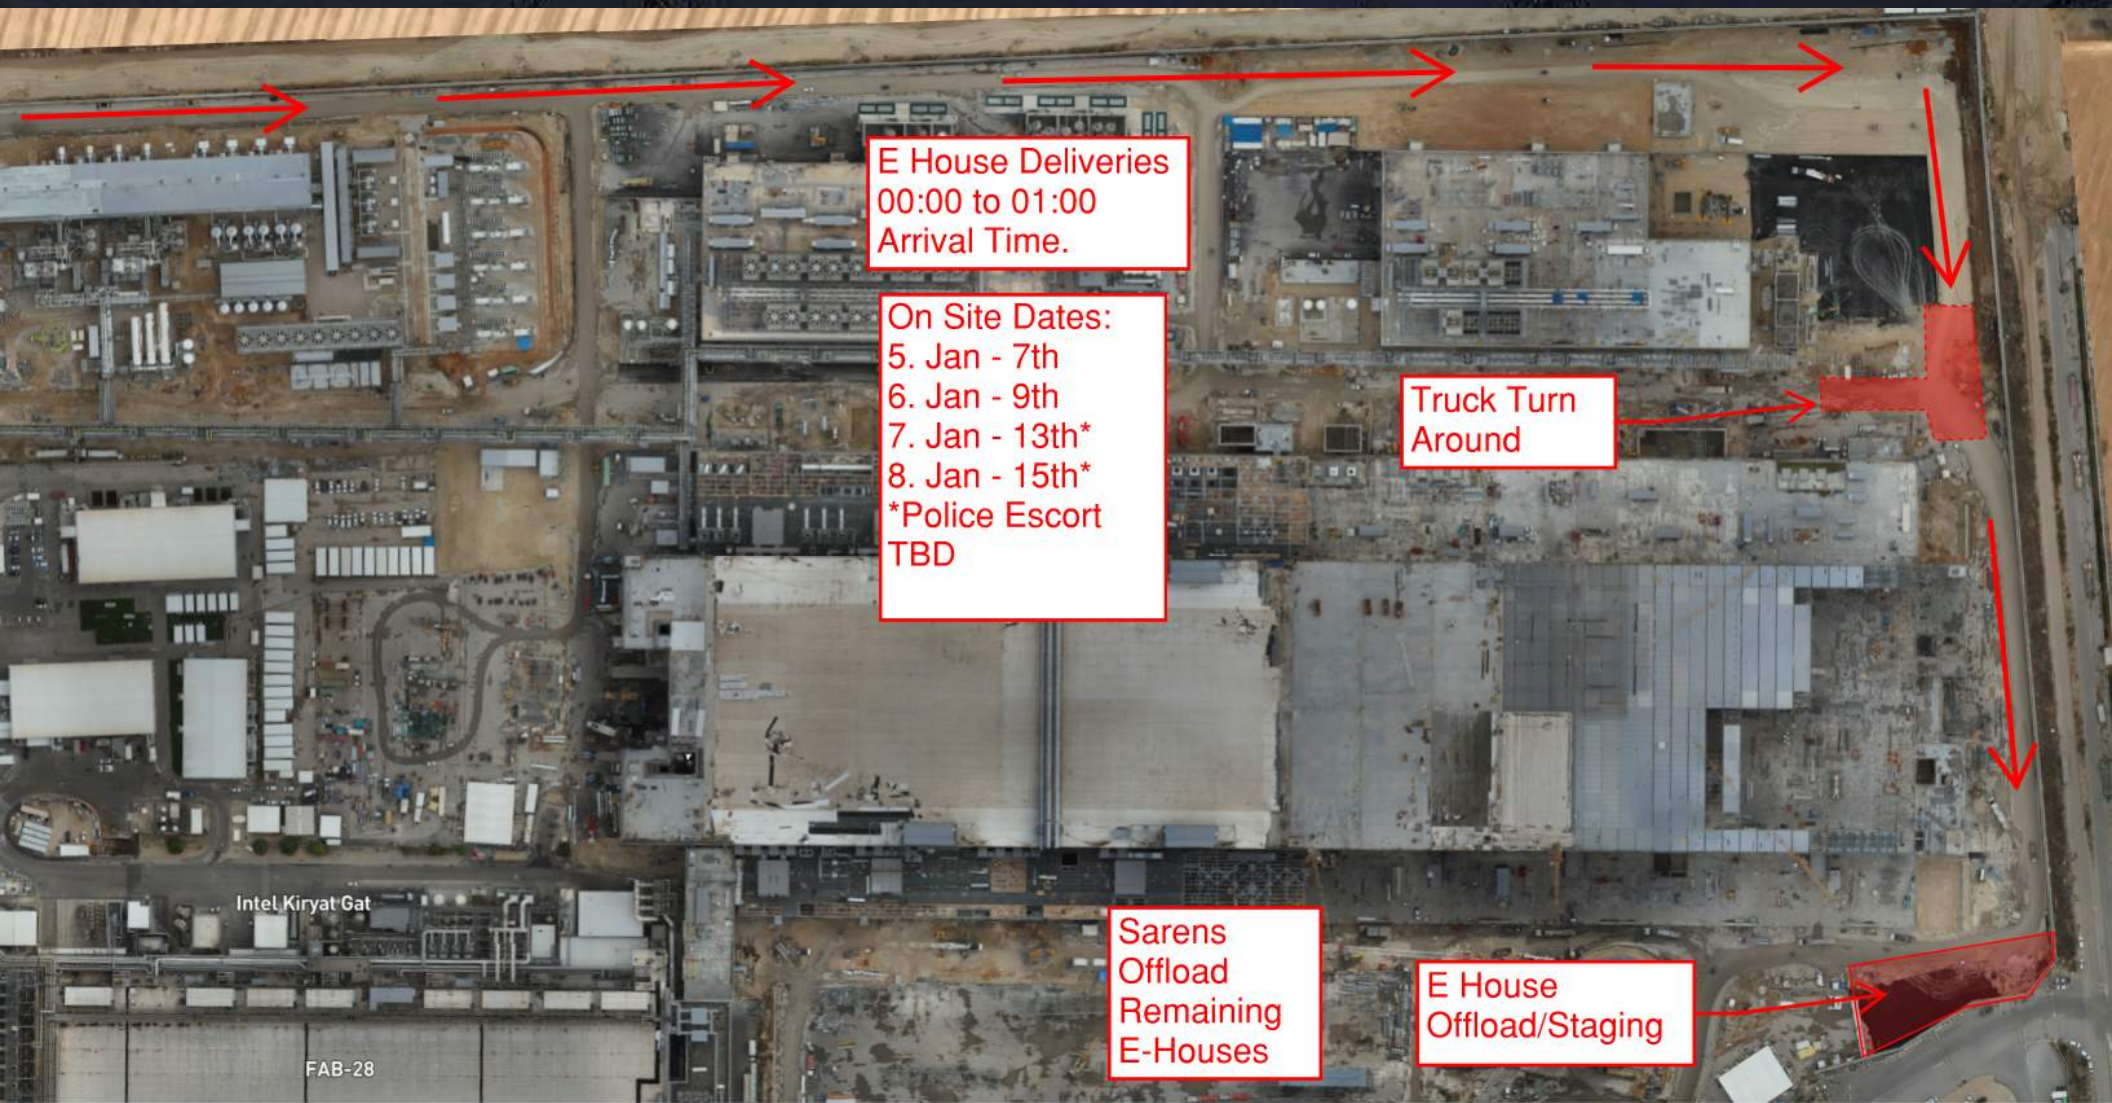

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:
5. Jan - 7th
6. Jan - 9th
7. Jan - 13th*
8. Jan - 15th*
*Police Escort
TBD


Truck Turn
Around

Sarens
Offload
Remaining
E-Houses

E House
Offload/Staging

Intel Kiryat Gat

FAB-28

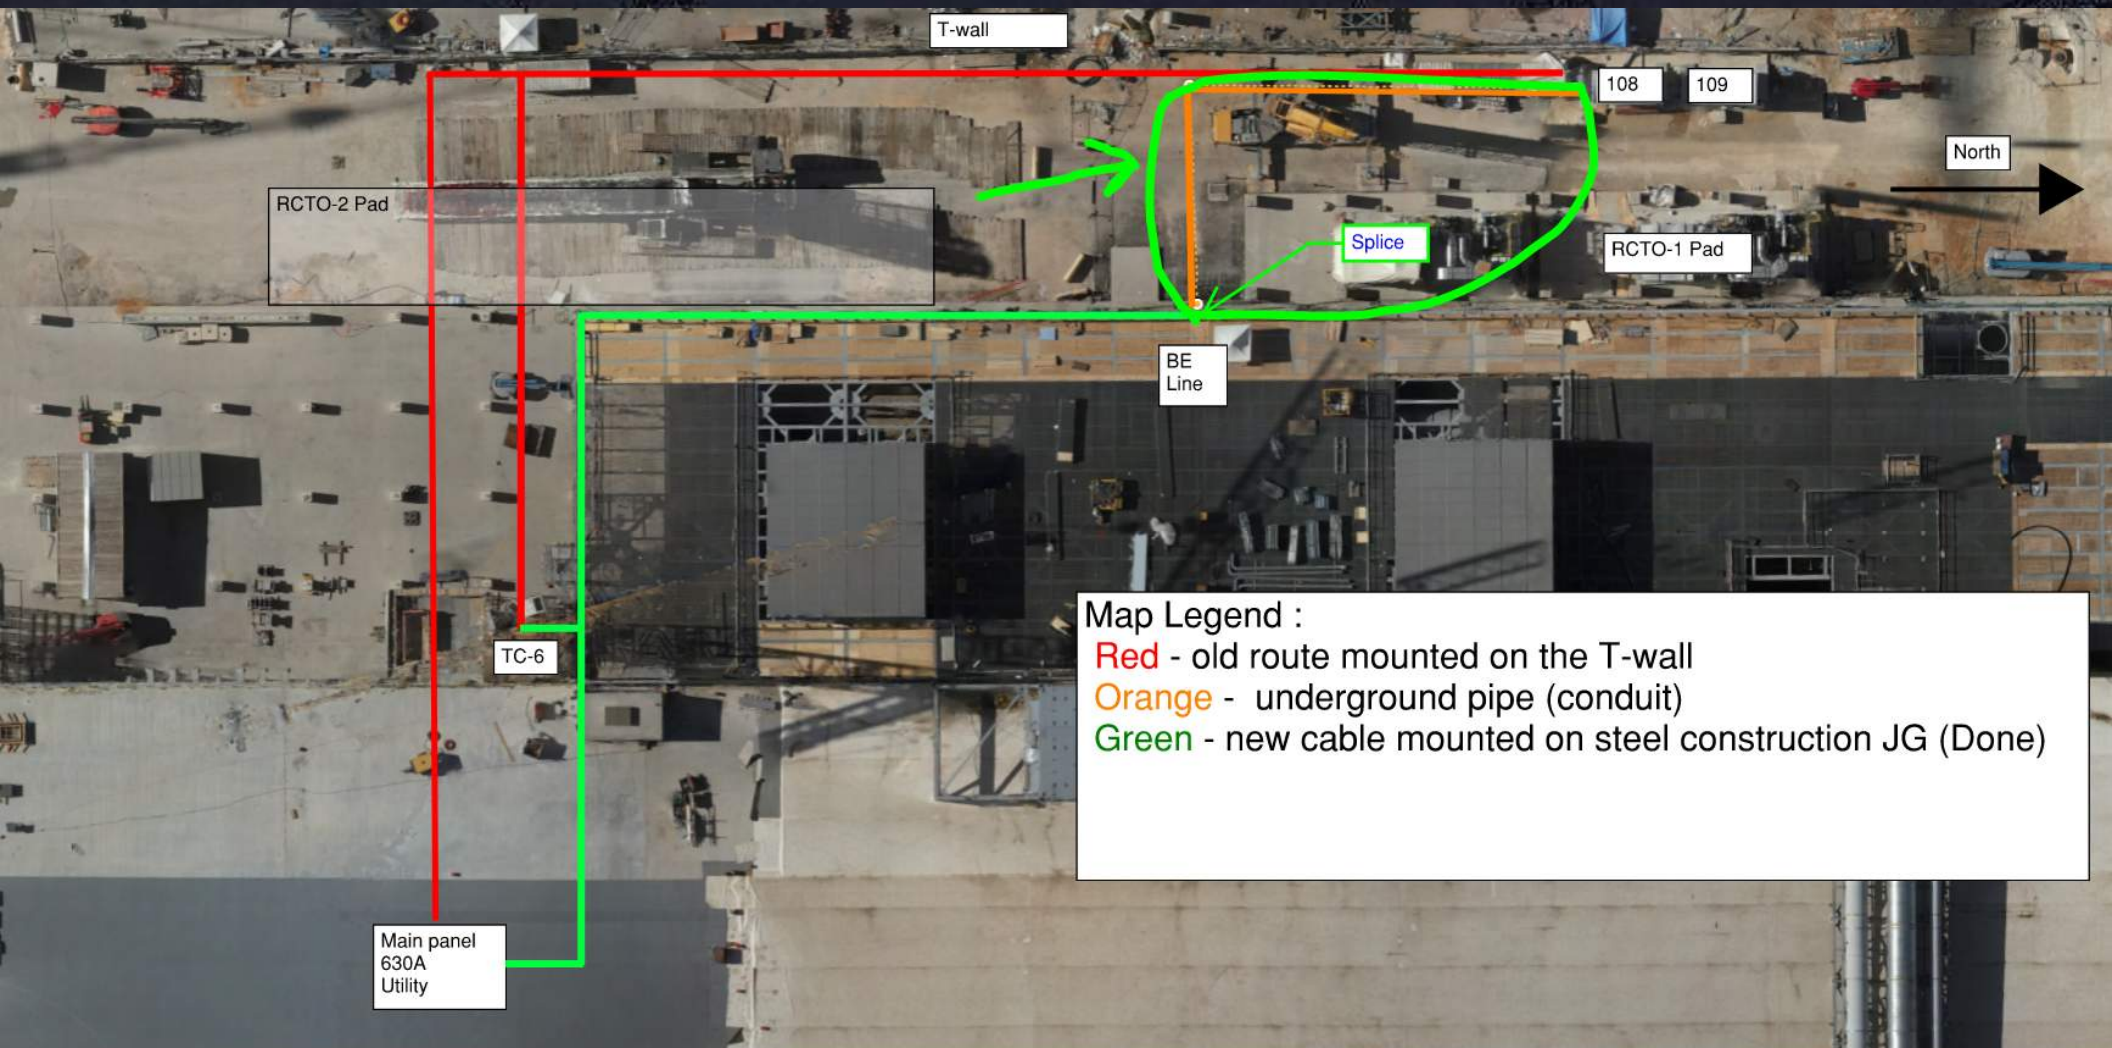

Map Legend :

- Red - old route mounted on the T-wall
- Orange - underground pipe (conduit)
- Green - new cable mounted on steel construction JG (Done)



HOFFMAN CONSTRUCTION COMPANY




Daily Coordination Meeting

Site Logistics

600 Car Park

Boring

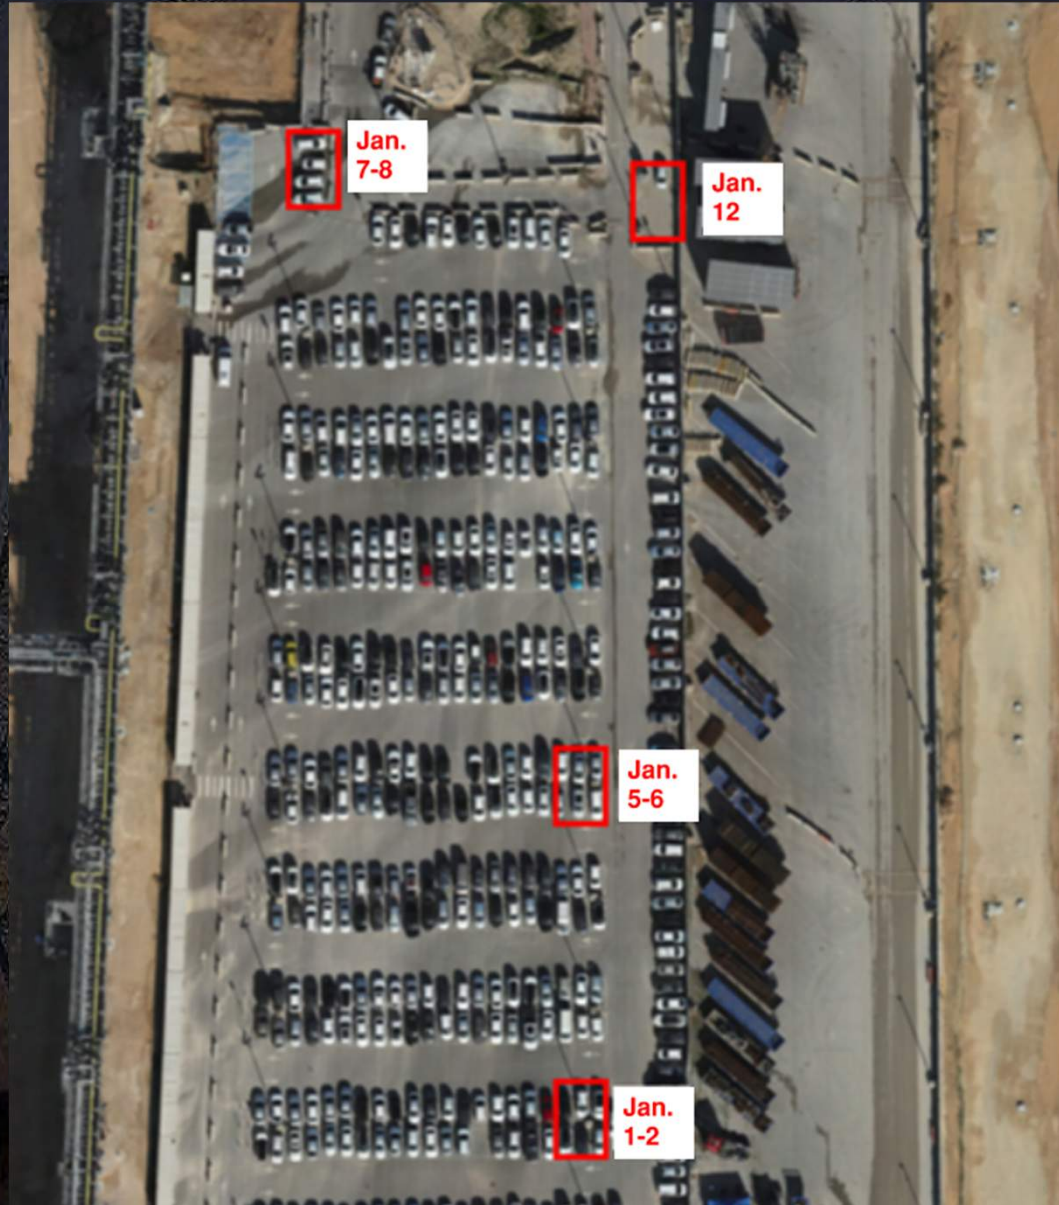



Daily Coordination Meeting

Site Logistics North





Daily Coordination Meeting

Site Logistics
South





LEARN FROM EVERYTHING

PROJECTEAGLE
2024



ALL INJURIES ARE PREVENTABLE | PEOPLE ARE THE SOLUTION | SUCCESS IS THE PRESENCE OF SAFETY

DATE/TIME OF INCIDENT: 12/28/24, 02:50 PM

LOCATION EQ Deck 52.1 AJ-25
:

WHAT HAPPENED?

Crew was performing rework on two pieces of grating. They tried to remove the smaller of the two pieces but were unable to get it to come loose. As the crew took out the screws of the larger piece, the small piece of grating fell and punctured a cooling coil, causing it to leak water.

CURRENT SITUATION/CONTAINEMENT?

Leak from cooling coil lasted approximately 8 minutes and the water was shut off to that unit. Immediate cleanup was performed by Hoffman job services. The area is secured and isolated and no further hazard is in the area.

ROOT CAUSE

Work Planning / Incomplete – Inadequate Plan

WHAT CAN THE PROJECT LEARN FROM THIS INCIDENT?

Identifying any systems that may need to be bulletproofed during area pre-walks with superintendents and system owners and relaying the procedures on how to do so to crew.

WHAT CORRECTIVE ACTIONS ARE BEING TAKEN?

- Create a step-by-step procedure with identified hold points when securing loose grating.
- Submit a SWPR for any rework that will be performed in EQ Deck 52.1 area.
- Ops contacts to be shared with superintendents and safety so they can be notified of any issues with systems before modifying them.



HCC/EHS Weekend Work- 03.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Shelby Standefer 052-3440752

Yakov Malka 052-3459250

Yakov Alon 052-4671271

CSA CM

Charlie Aitken 052-6041443

Ilyssa Ingenthron 052-5732553

MEP

David Chavez 052-2756390

Denis Ryan 052-2962447

Pauric O'Reilly 052-3571665

Lara Salaymeh 052-2410953

Abhilash Parameswaran 052-6938827

Cranes

Craig Mowry 052-300-2769

Safety

Safety Foreman- Mohammad Zakakti- 054-8121212 Mohammad-Zakakti@Hoffmancorp.com

Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com

Safety Professional- Nassim Yones- [052-2208434](tel:052-2208434) Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 03.01.2025

FAB

Utility Level / Roof / Stair Shaft

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Megason

Subfab

Pach Taas

BAe Wall Penetration

Itamar 0509301917

Afcon E

MARSes, E LSS Rooms

Avi Eli: 0526008487

Chemo

TTNW

Tomi: 0523759408

SELA

AY-BC 15-19

Avihen 0548155302

MEGASON

LSS Rooms

Israel 0526869393

Clean Room

Talad – CR 2 E – UPN Install, 4E Grating (EHS Marcelo 0523540242, Super Igor 0544509386)

Sig – 10 GUYS 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)

Afcon – CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)

Chemo –30 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)

Megason - 16 GUYS INT LEVEL + 7 GUYS ON UTILITY LEVEL FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT

Sela – 2E CRC (Supervisor yoav 0548076339 , EHS SERGEY 0526650046)

Protocol - aa+ak lines.

Talent solution 1w_+ 1e + interstitial.

Subcontractor Weekend Work- 03.01.2025

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2 1-3P

Foreman – Itamar – 050-9301917

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2

Foreman – Pradeep - 055-2742935

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-5P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcelo – 054-5210133

Safety – Majdi – 054-6192581

WJG

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 4J/5J Lift 2 Piping & Link Roof

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

Pach Taas: All over

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

Subcontractor Weekend Work- 03.01.2025

CUB

S.K.E - CUB 1:

Renato - 0548991623

Marzuk - 0548830263

Chemo Aharon - CUB 1:

Dudu - 0509808846

Leonid - 0548883878

D&P - CUB 2:

Constantino - 0545501602

David - 0548894447

Sami Najami - CUB 1 test + CUB 2:

Husein - 0526917461

Faiz - 0502227962

Alon - 0509895008

HSAI:

Sergey - 0552728807

Trestle

Siding

Sami Najami

Forman- Abed Kilani 054-5501880

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Elmor – Site Lighting Underground

Supervision = Shlomi: 050-9182260

EHS = Daniel: 052-2584171

Olizki – Offload 18 & CUB1 trench drains, South GUT road excavation

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
