

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:

- Weekend work

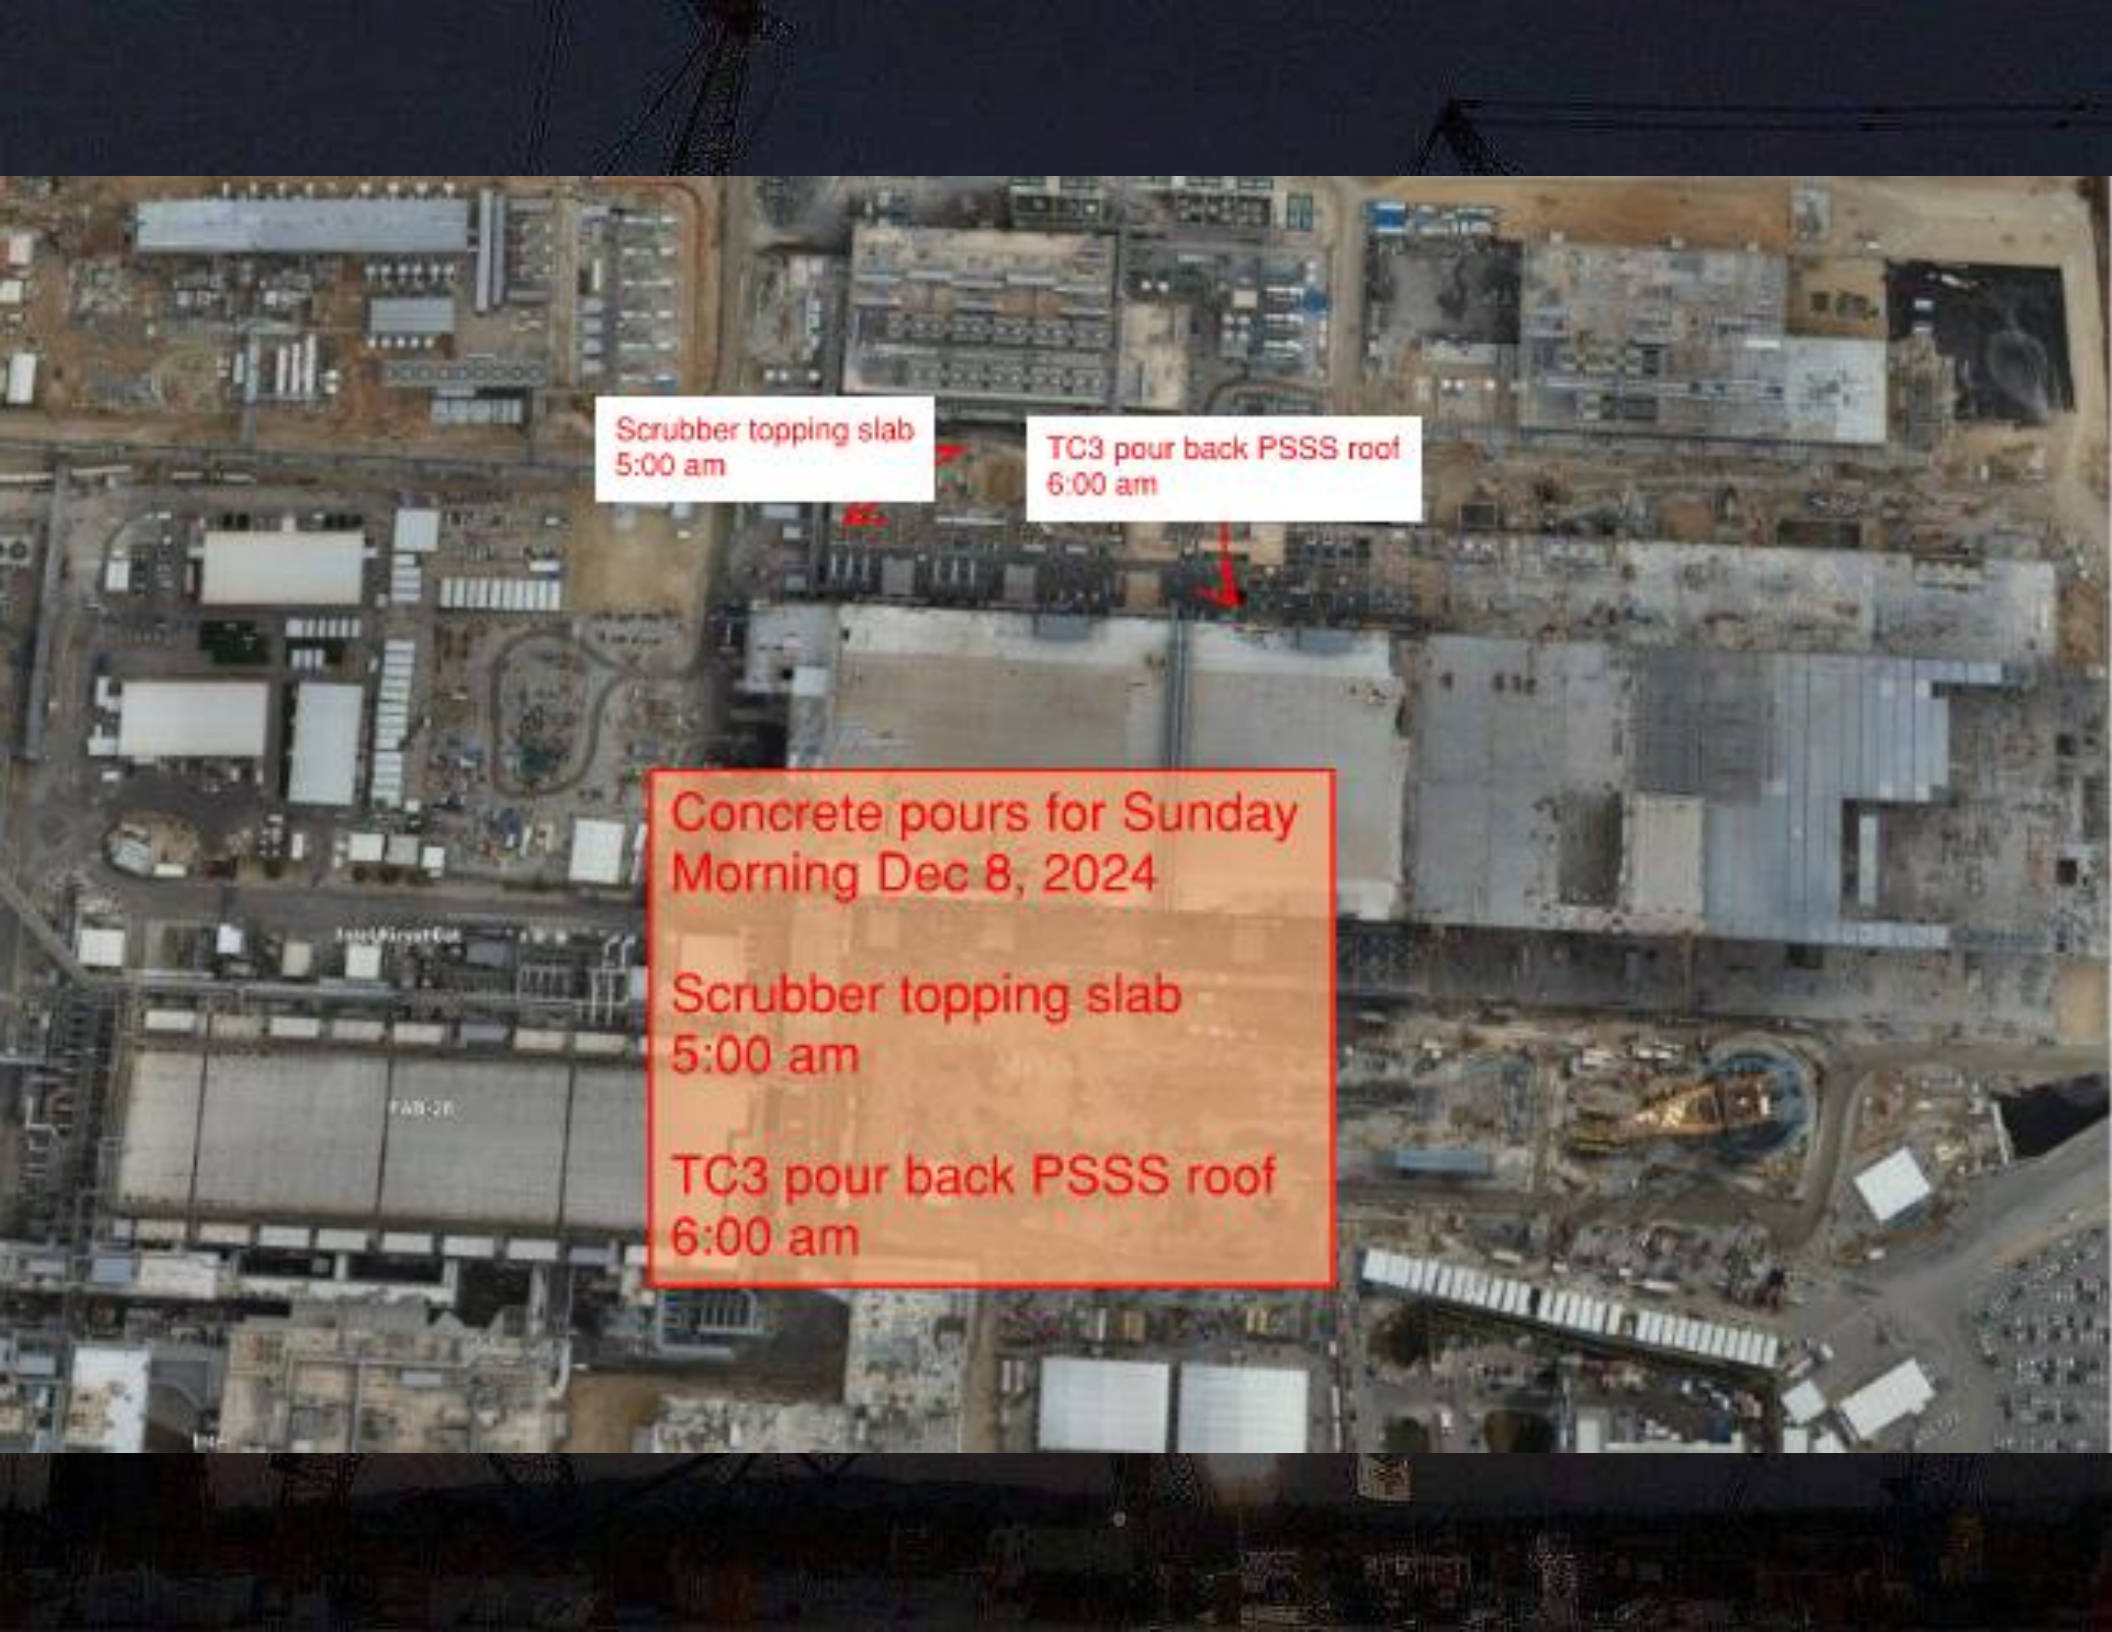

Scrubber topping slab
5:00 am

TC3 pour back PSSS roof
6:00 am


Concrete pours for Sunday
Morning Dec 8, 2024

Scrubber topping slab
5:00 am

TC3 pour back PSSS roof
6:00 am



UTILITY LEVEL MOD1

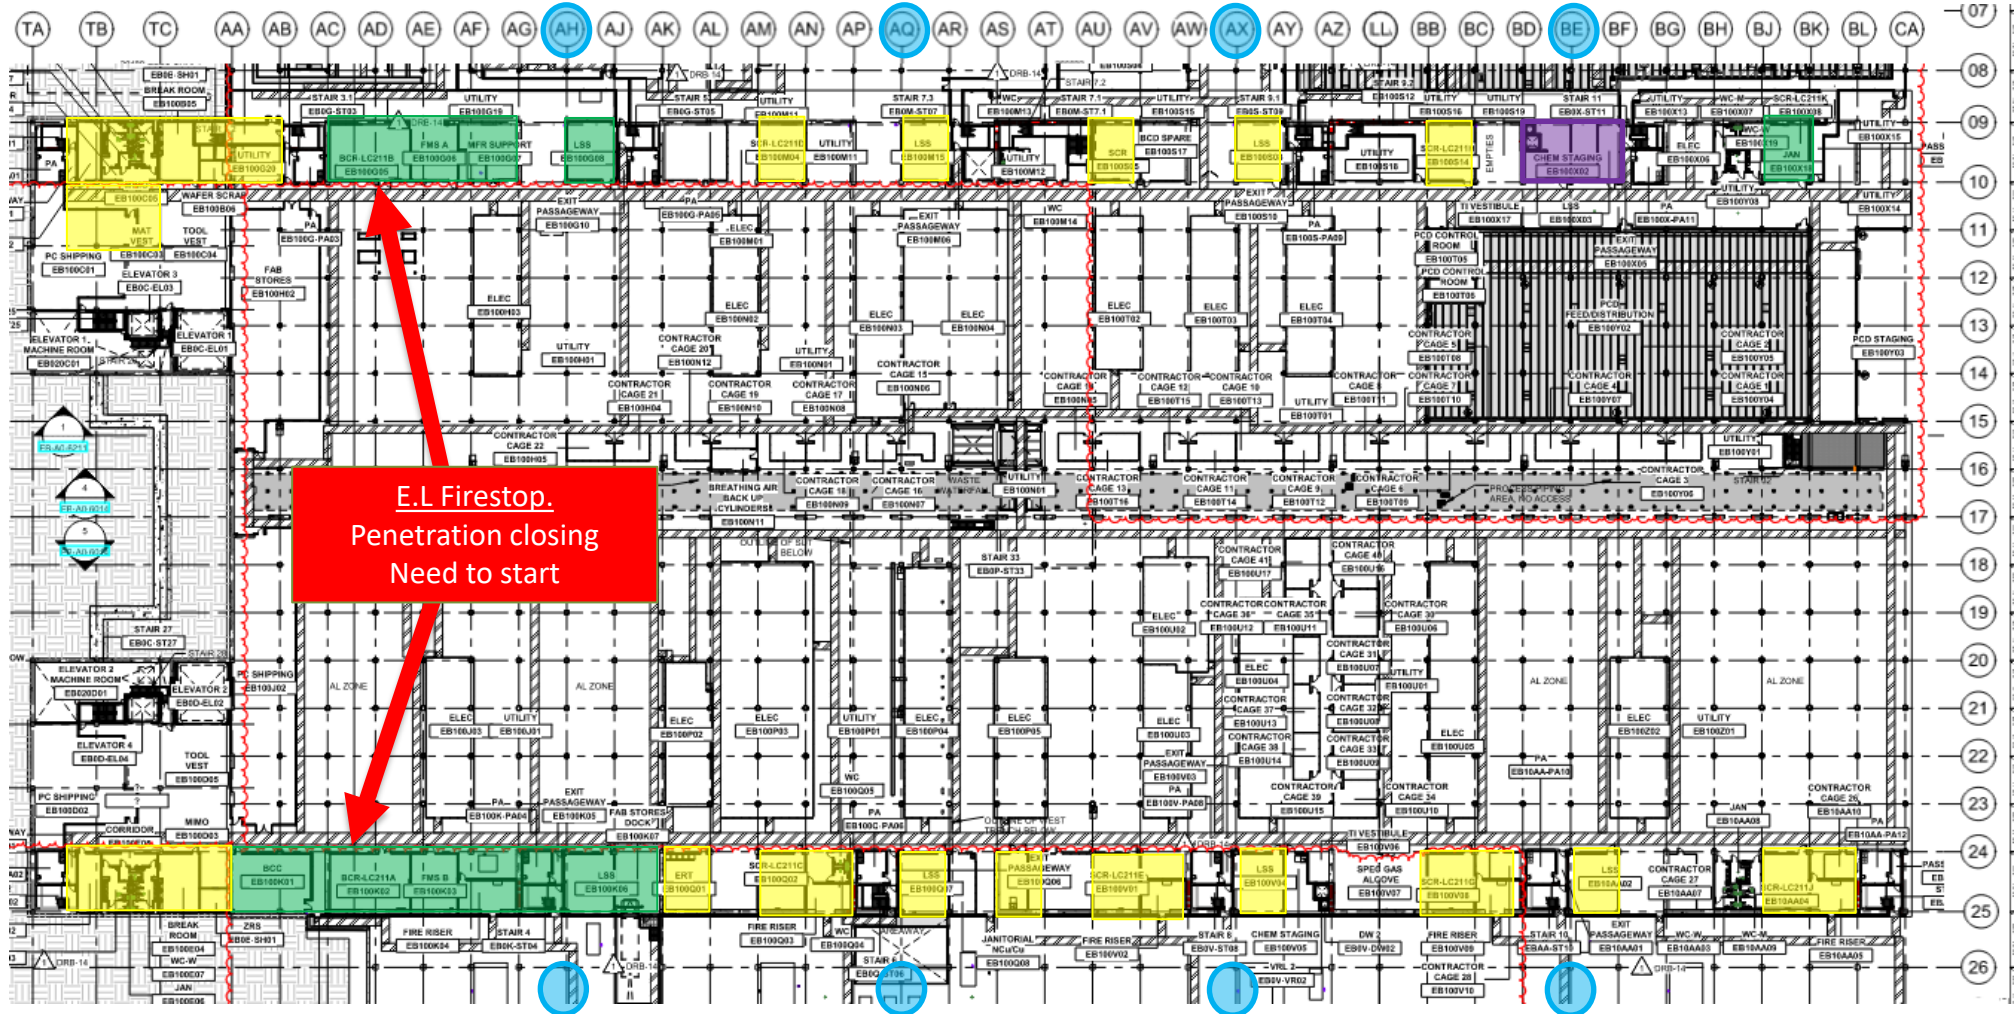

E.L Firestop.
Penetration closing
Need to start


BELFOR
Mold remediation

ELRAM
Drywall install

MEP+Electrical
Ready for re-install



UTILITY LEVEL MOD2

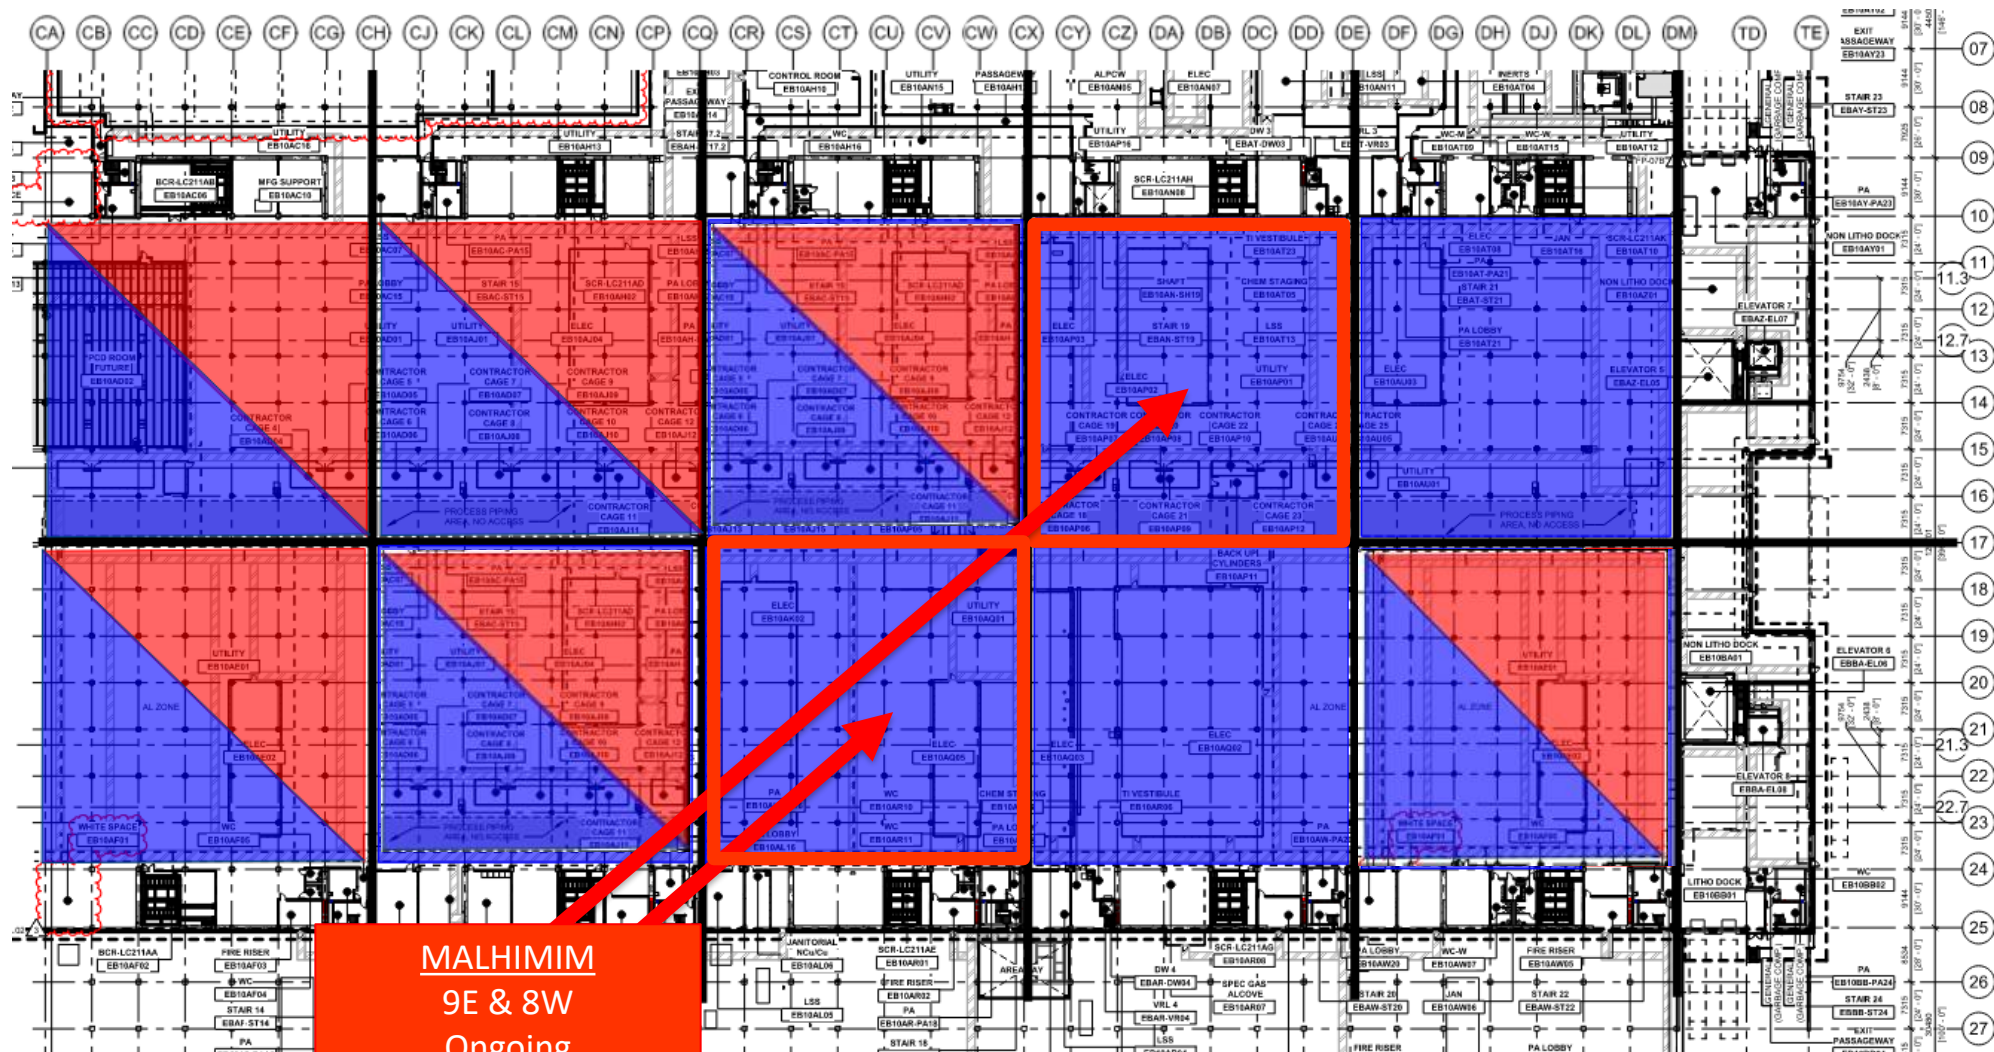

MALHIMIM
9E & 8W
Ongoing
Need completion date

Telecommunications Room

BCR-LC211A

Restricted Work Area

**DO NOT PROP OPEN
THIS DOOR!**

For access, please coordinate your activity with:


Dominic Schwartz, Bynet - 050 719 0936

Sean Neill, Hoffman Supt.- 052 250 6892






SUT 38.1 LEVEL

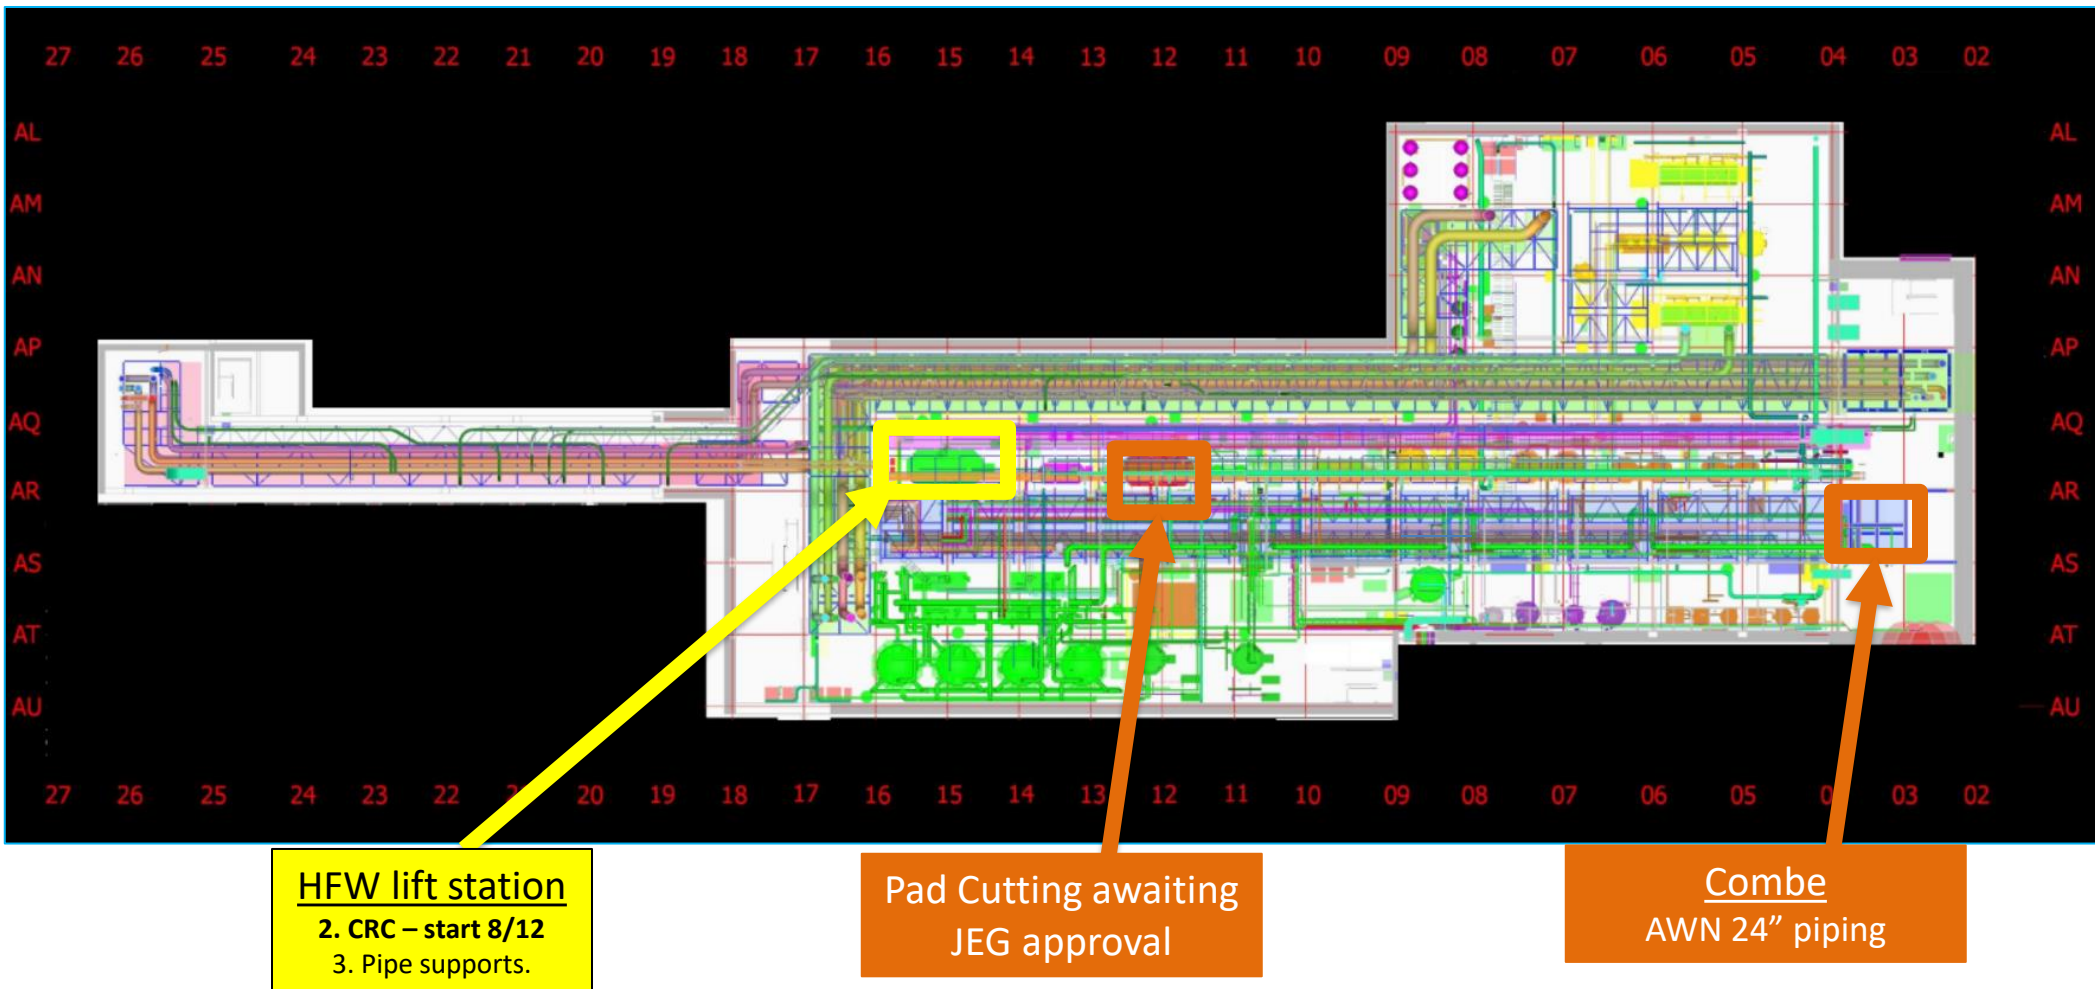


SUT 38.2 LEVEL

Rack 4b
Lifting
#1-08/12
#2-11/12
#3-16/12

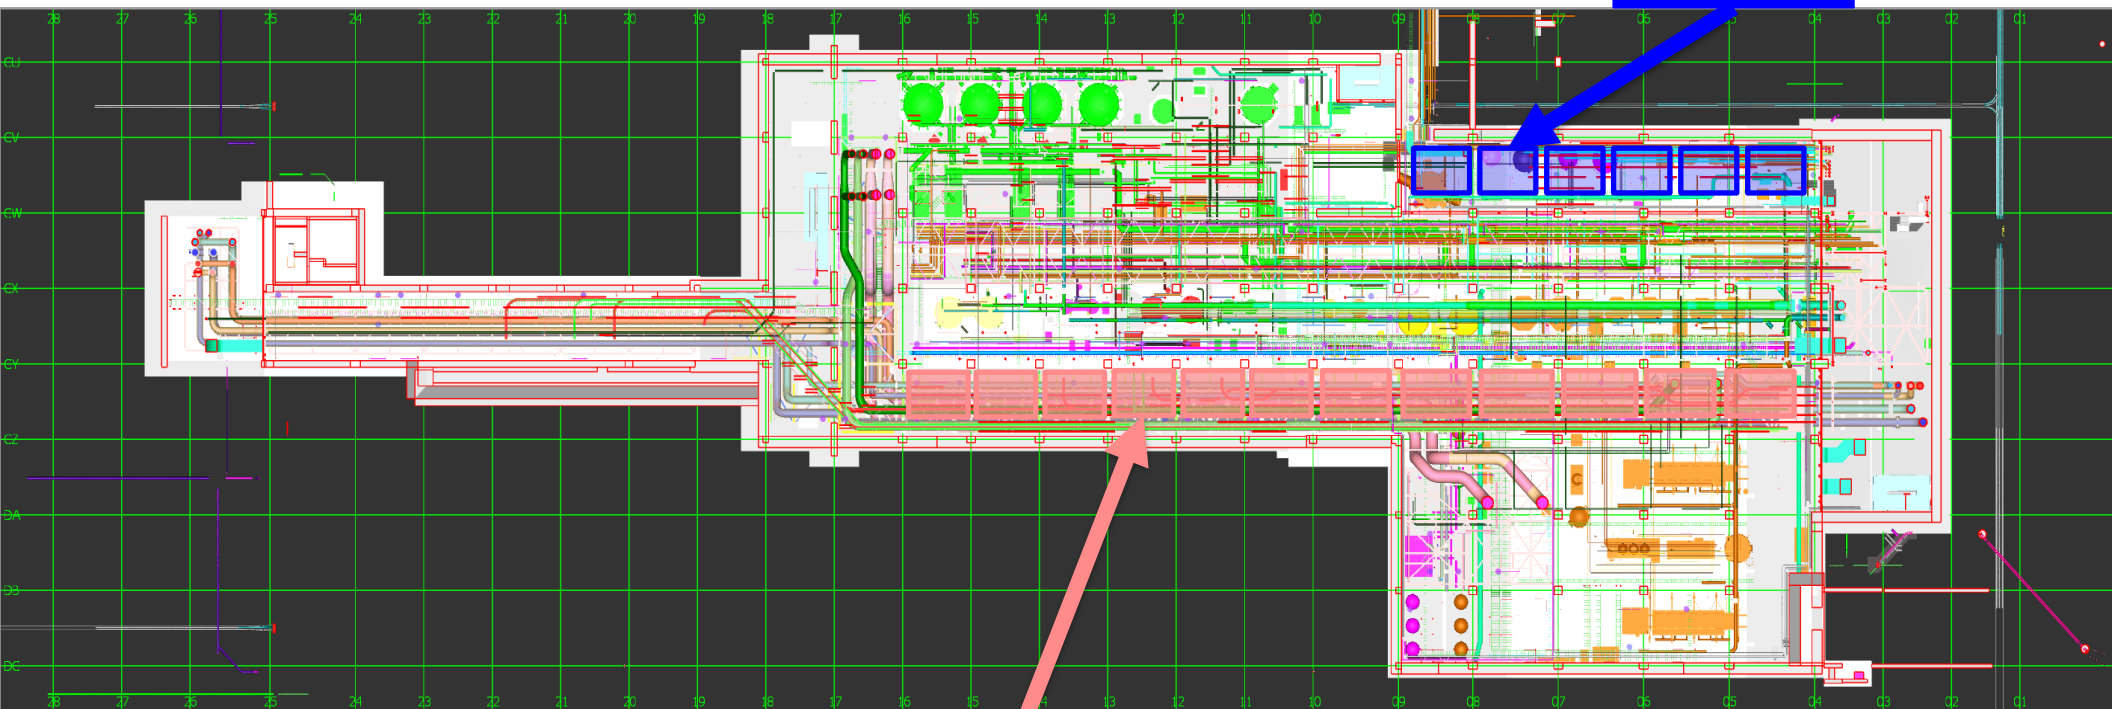


Rack 2
MIMO -
Module #4
12th of Dec


SUBFAB BUILDOUT MOD 1

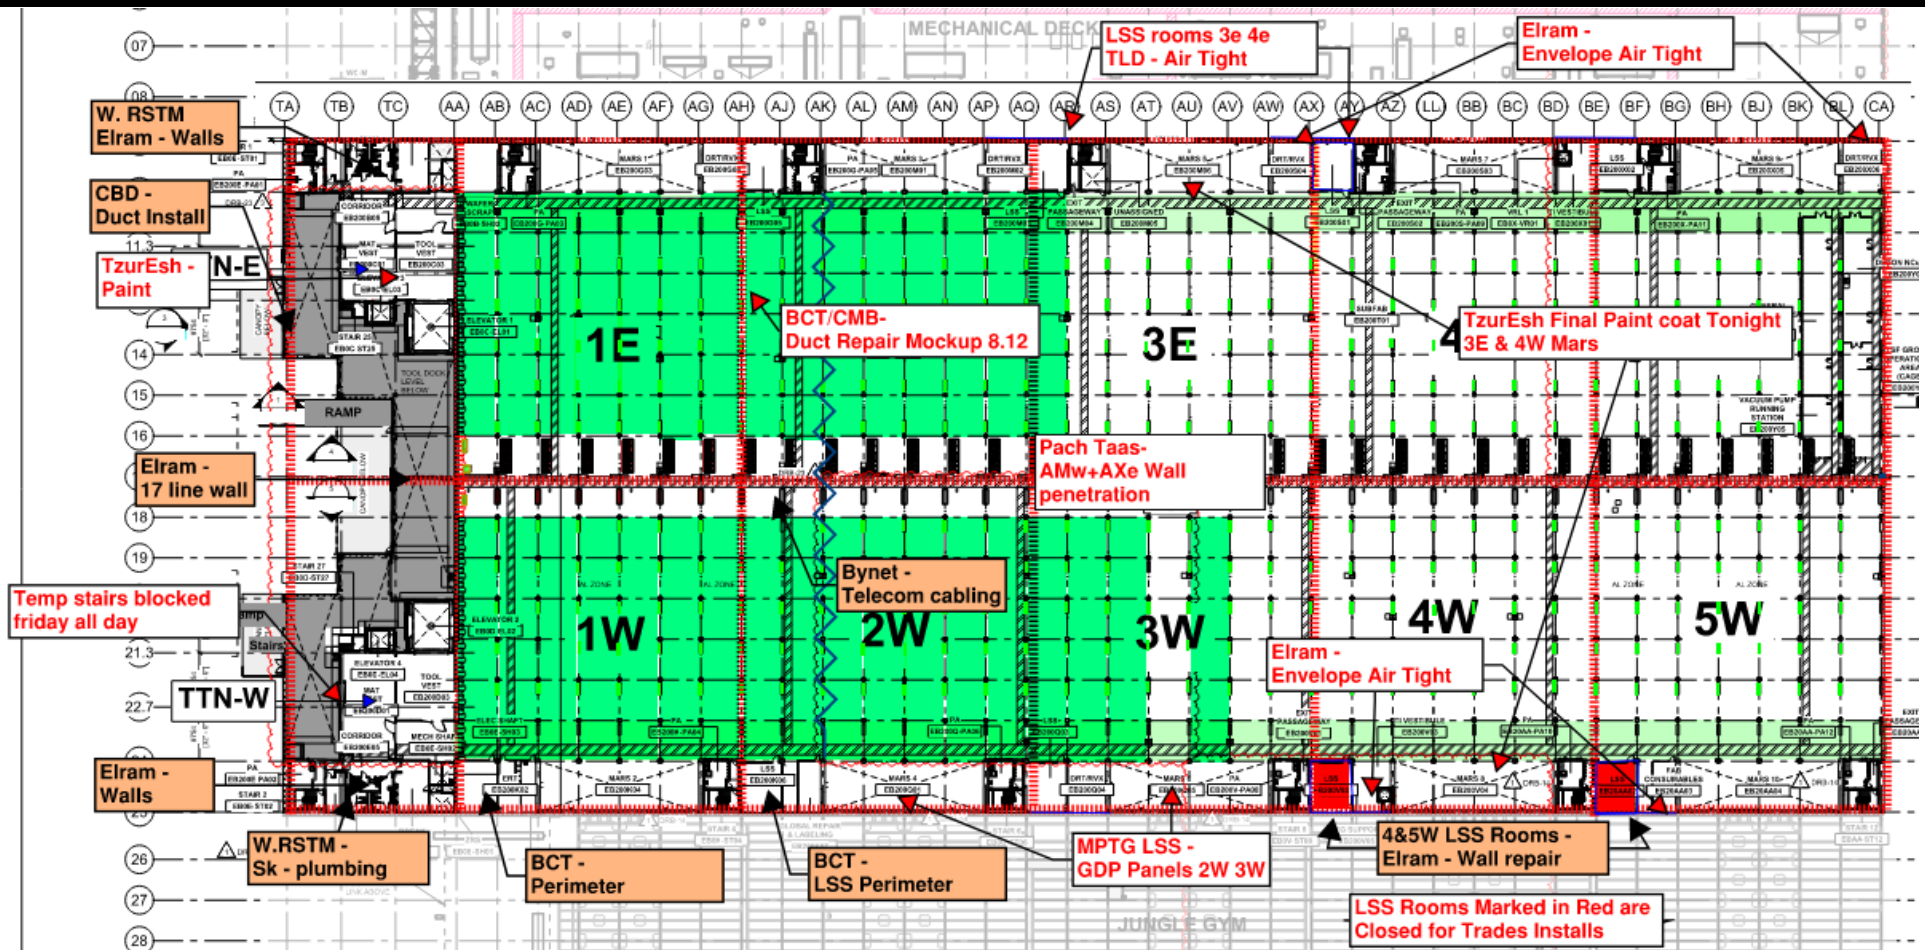



SUBFAB CRC TOPCOAT

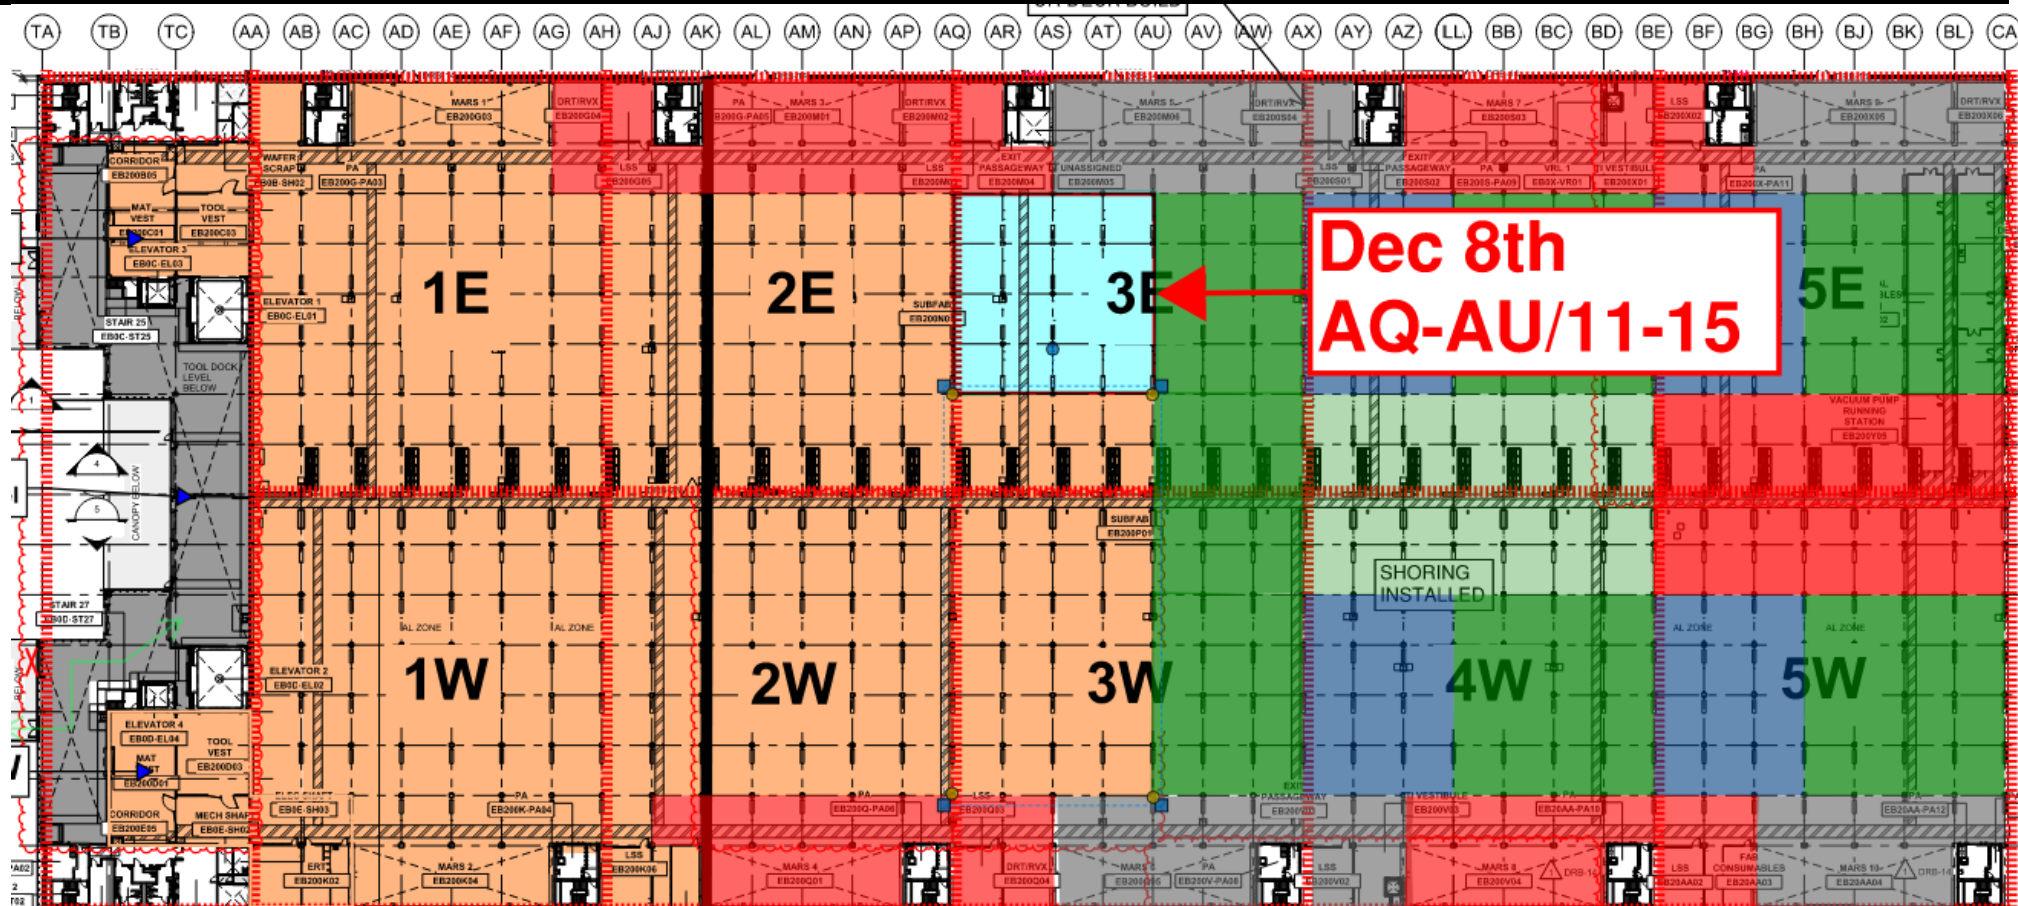


SUBFAB BUILDOUT MOD 2


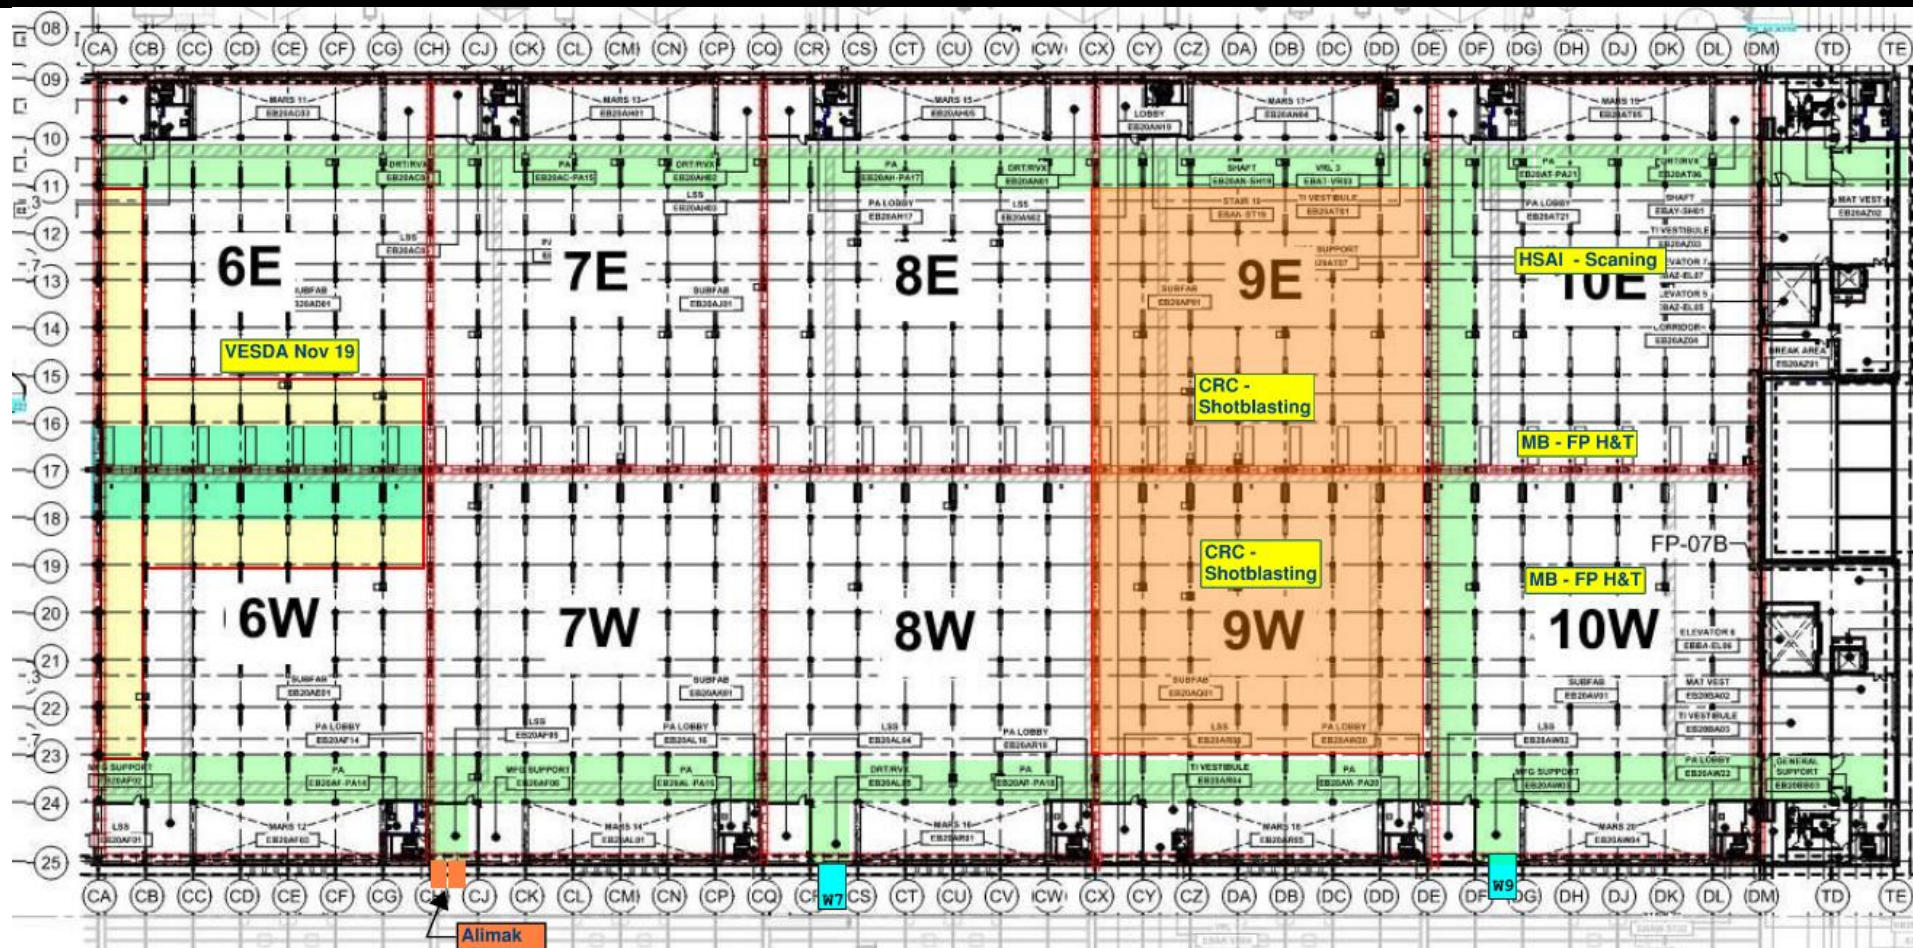


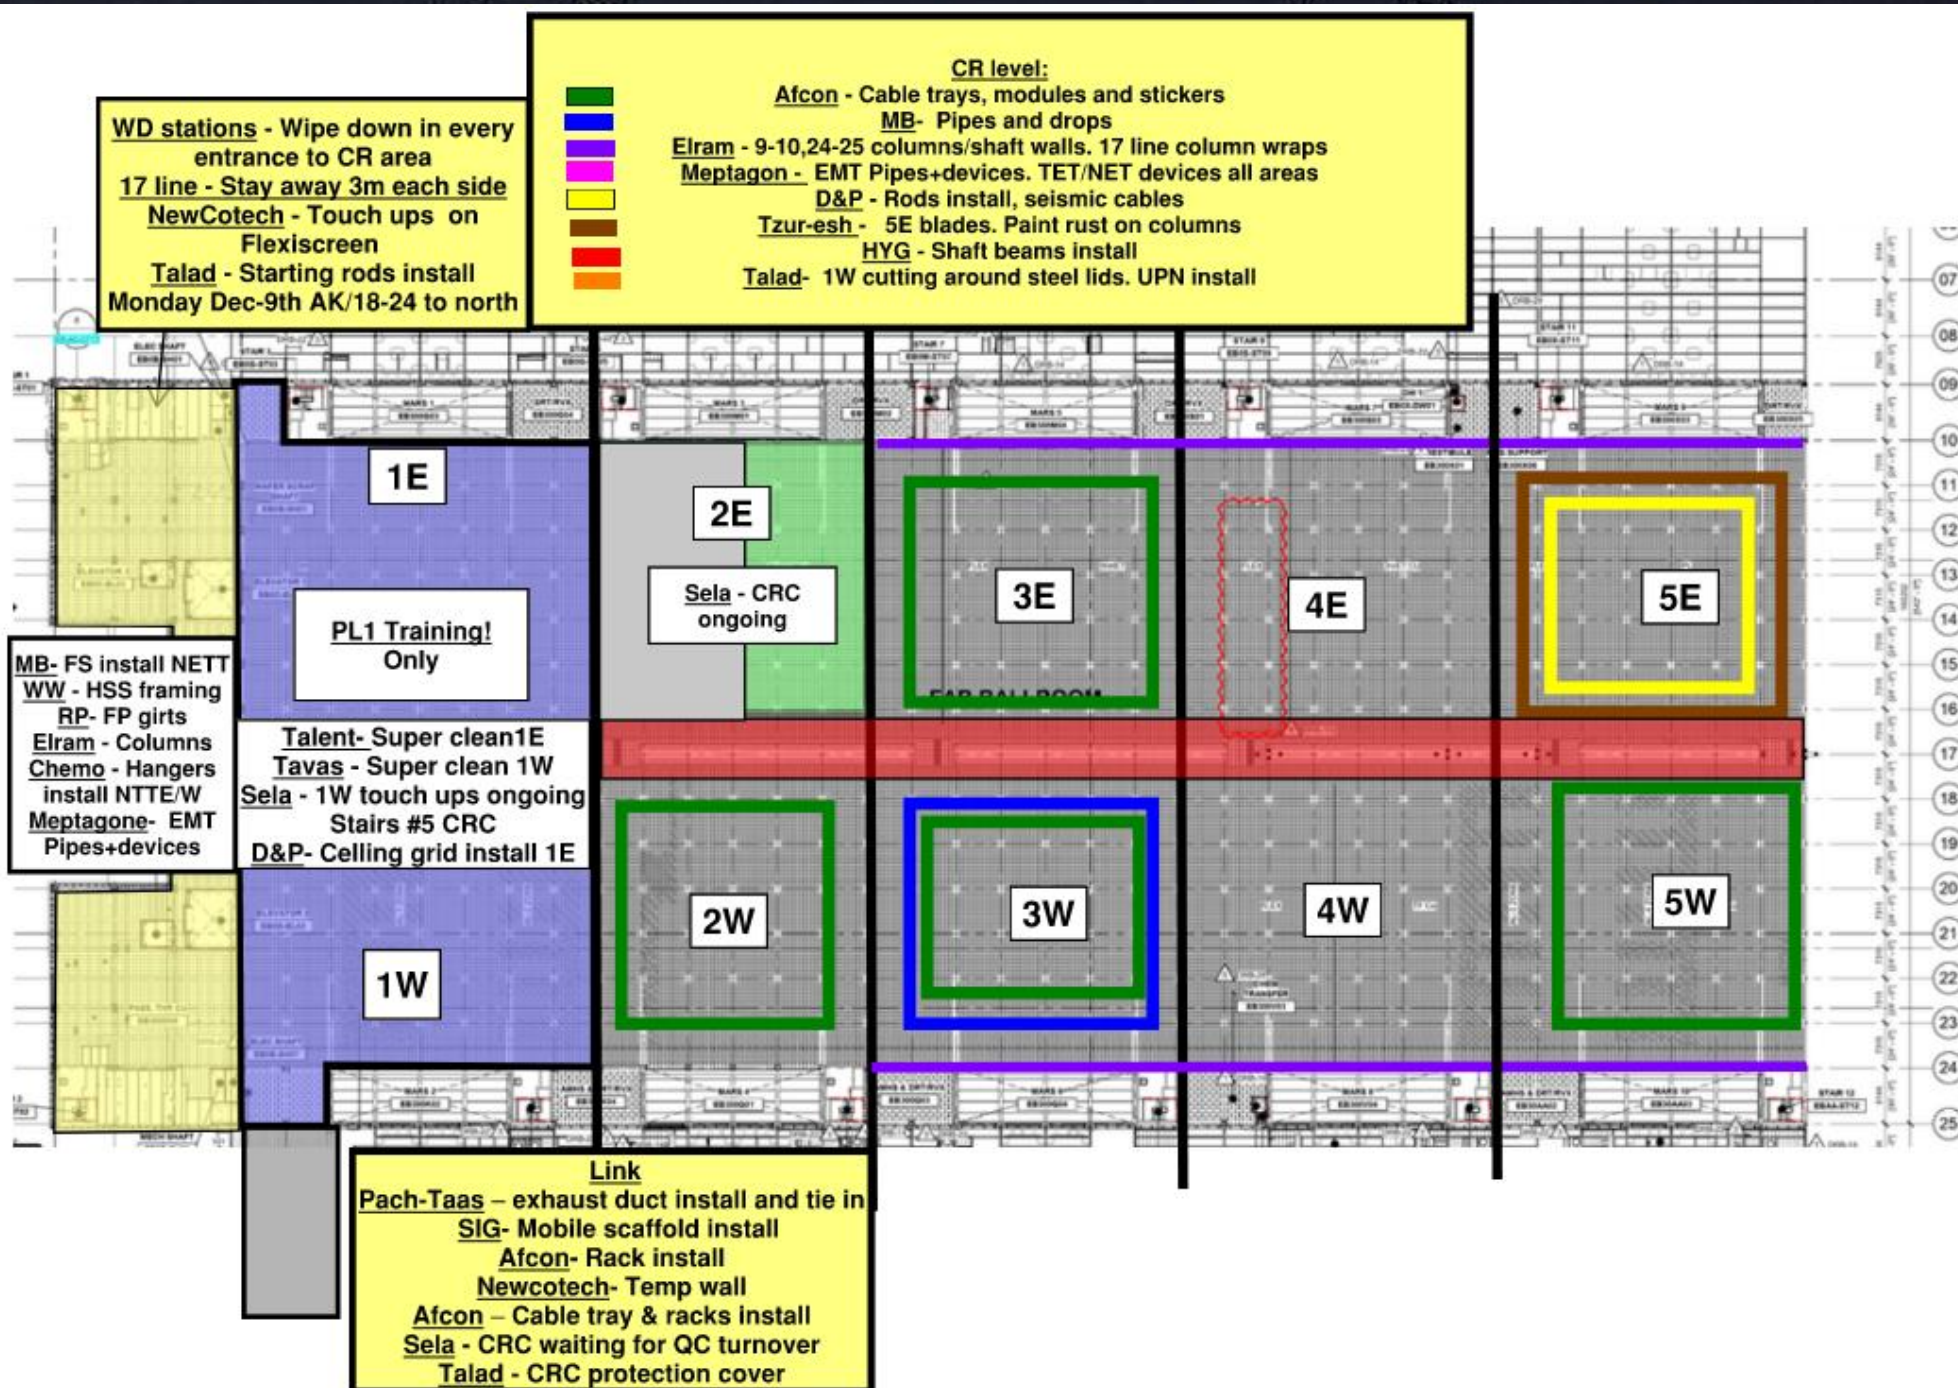


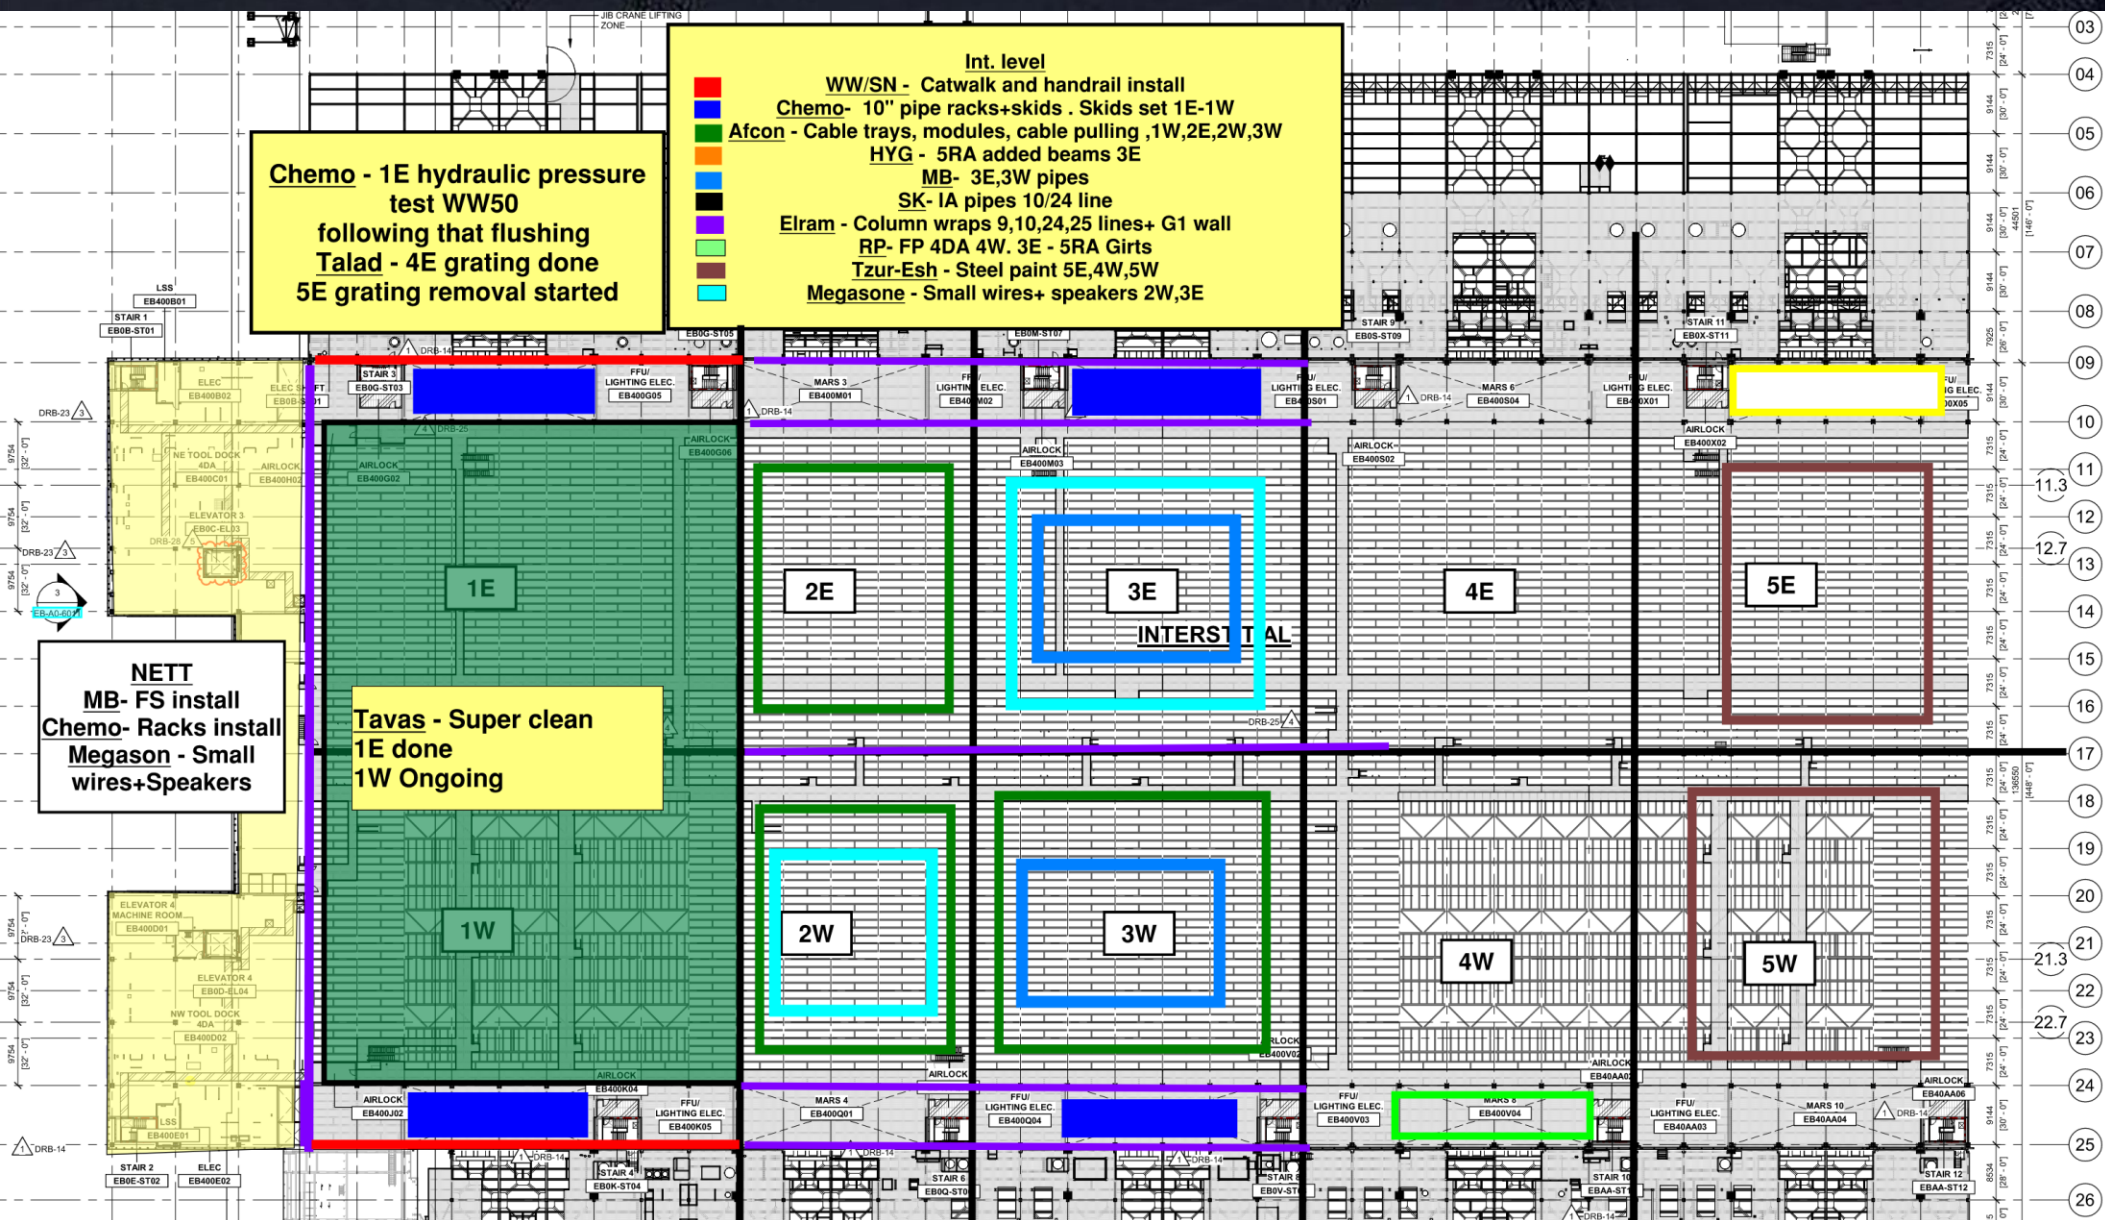

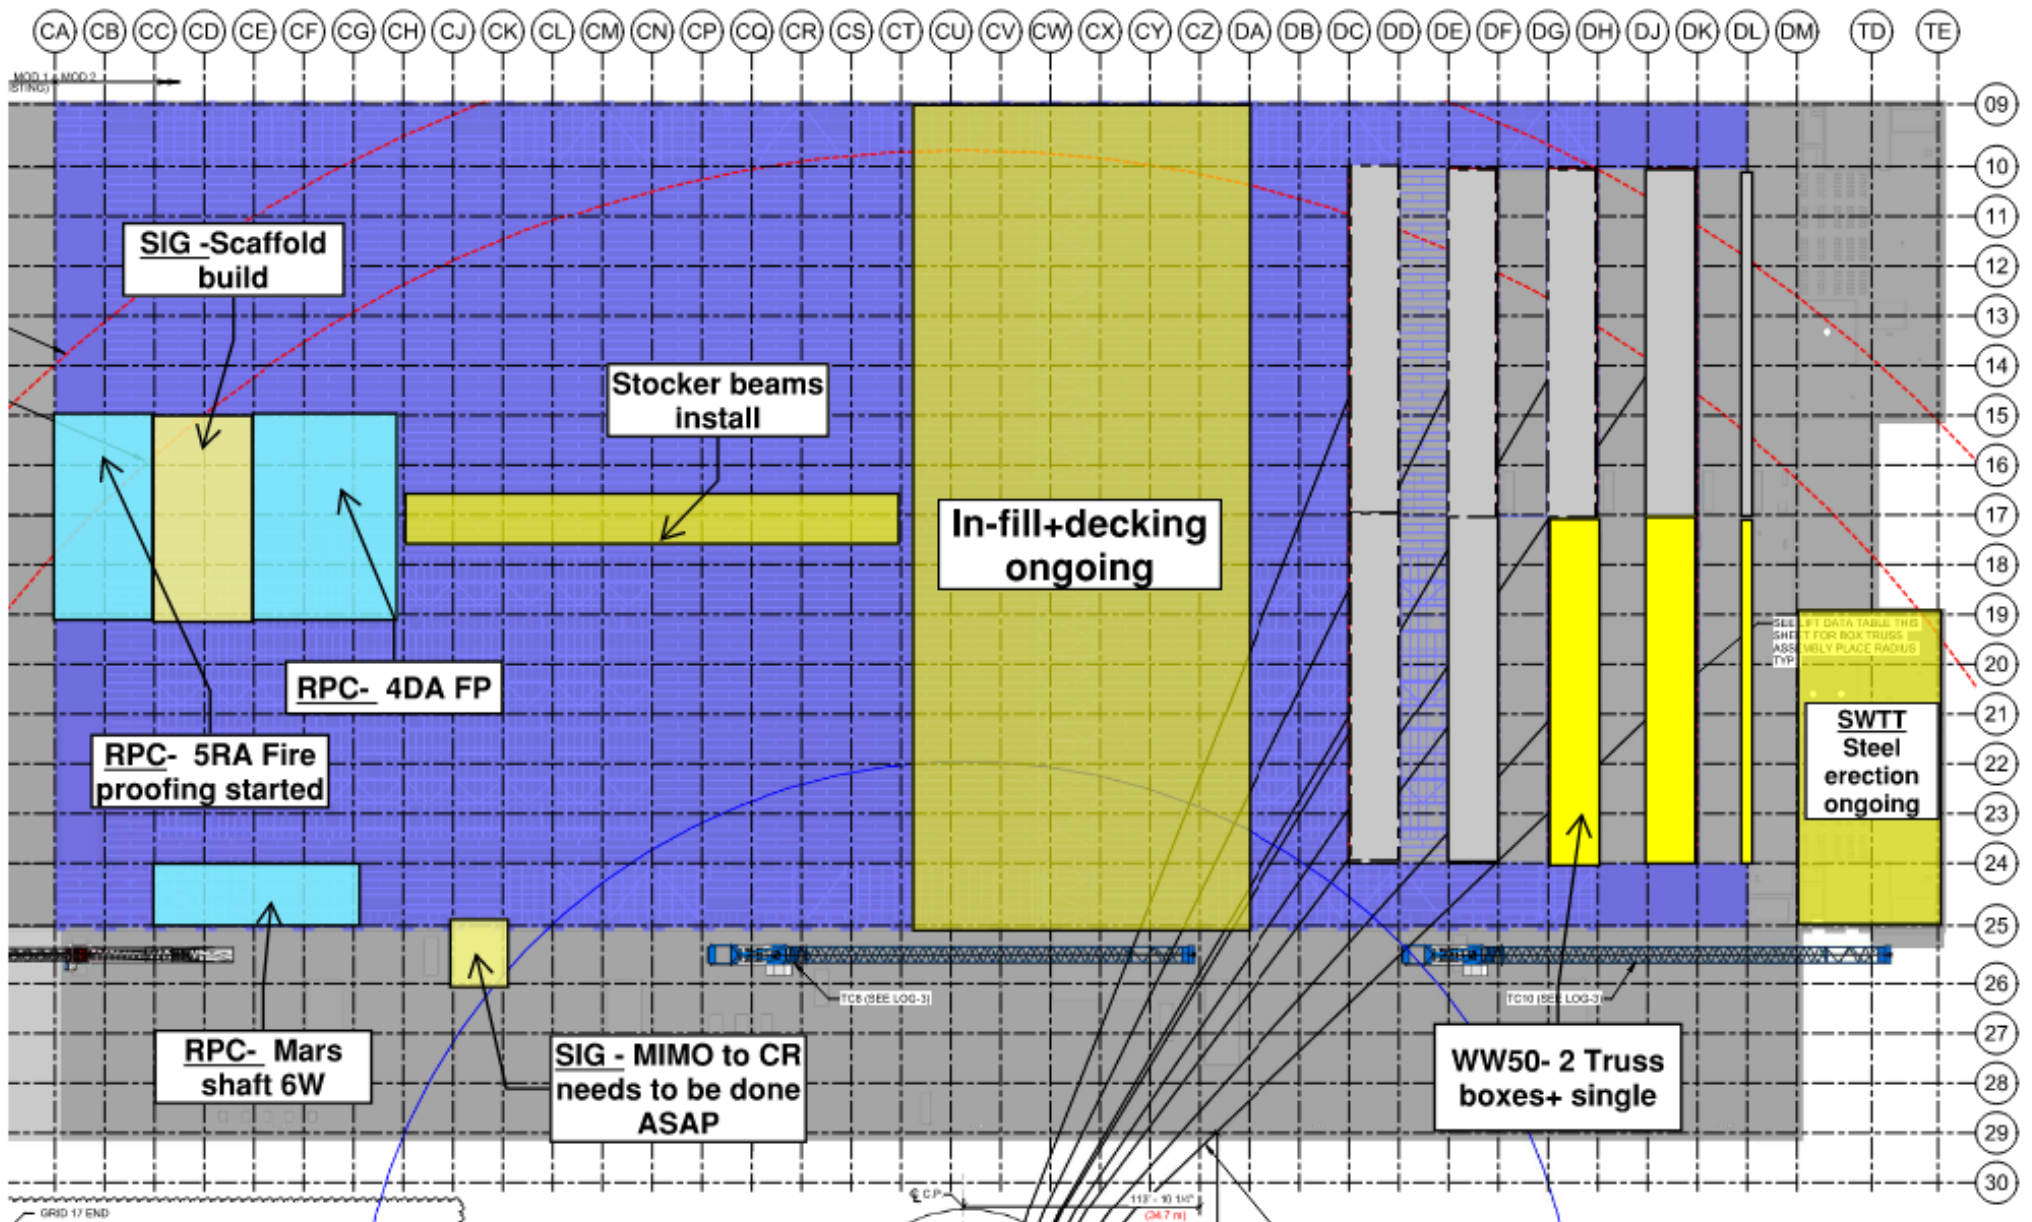


Violations Control WW49 – Stop work

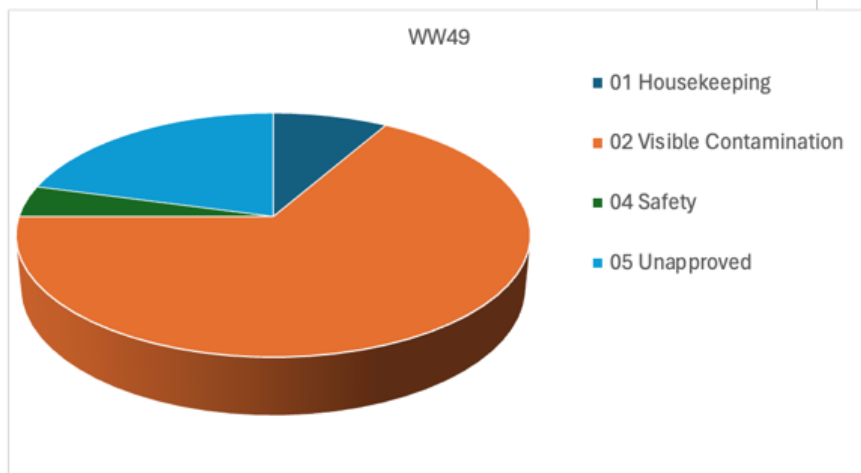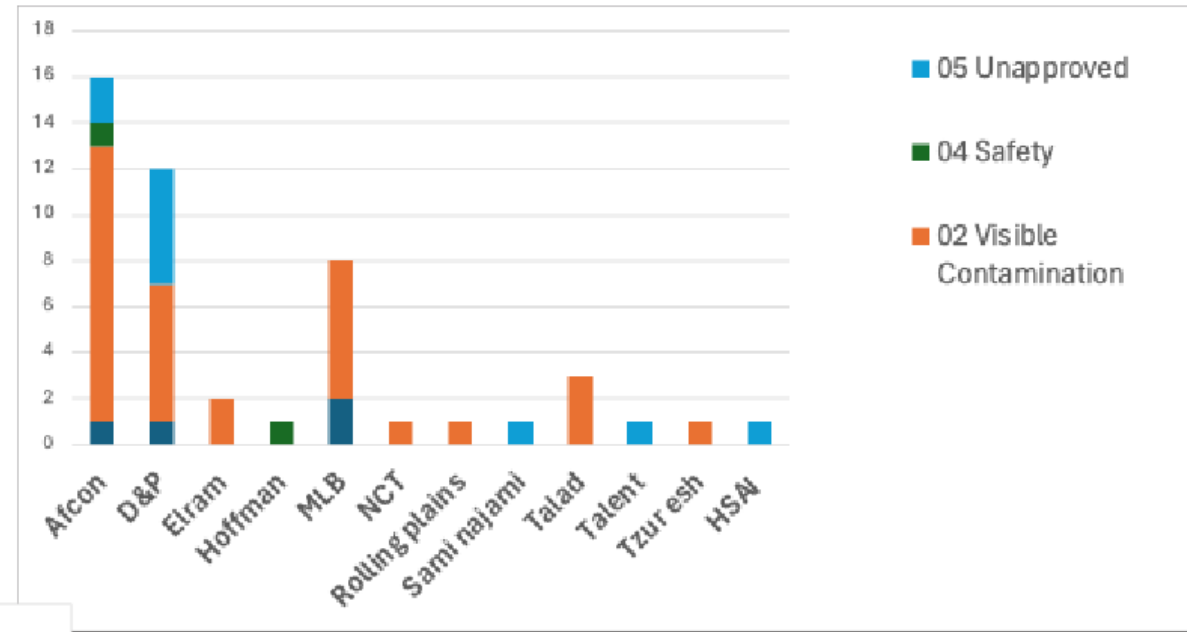

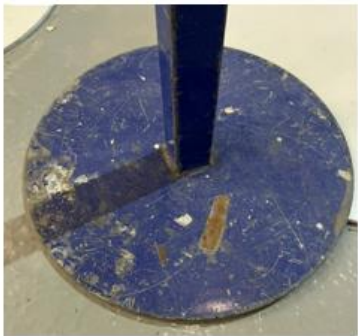

Year	WW	Date	AC/11	AC/13	AC/15	AC/18	AC/20.5	AC/22	AG/11	AE/13	AG/15	AE/18	AG/20.5	AE/22	PL 5	PL4 > 1000	PL 3 > 10K	PL 2 => 100K	PL 1 > 1 mil	OOS
			1	2	3	4	5	6	7	8	9	10	11	12	1	1000	10000	100000	1000000	10000000
		7													1	1000	10000	100000	1000000	10000000
2024	49	1	456940	444320	455680	424860	439520	416740	418180	418480	435320	441800	431320	407000	1	1000	10000	100000	1000000	10000000
	49	2	537400	547420	690940	779540	715720	650840	1127860	1007140	1098880	1066100	835400	793540	1	1000	10000	100000	1000000	10000000
	49	3	569940	562880	562840	568920	569280	565560	612080	571720	587680	577860	581820	584180	1	1000	10000	100000	1000000	10000000

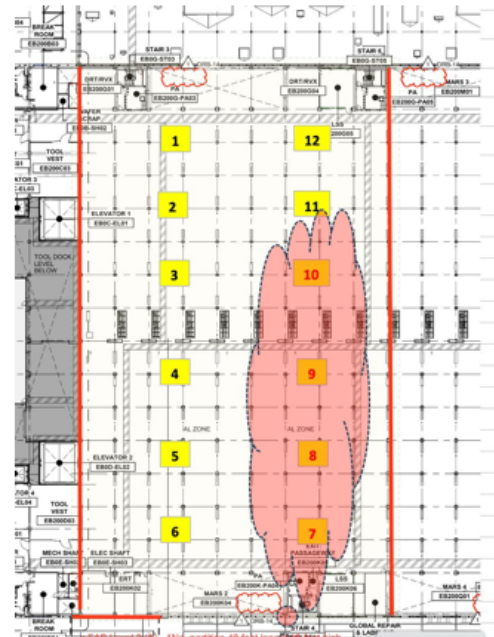

Problem statement: Increased of particles count level over Phase 1 CR floor


- OOS at AG-AE line (sample points 7-10)
- Other sample point just about twice the particles level of Sunday morning (After weekend).
- Observations at the interstitial show high levels at same locations (no reference)


Current actions:

- Protocol team and Floor Supervisors were instructed to make sure interstitial area is left clean and tidy by end of day
- Communication was presented at the Afternoon supt meeting (Nir Soli)
- Night shift Supervisor (Fred) was informed to focus night shift working teams.



CR Level

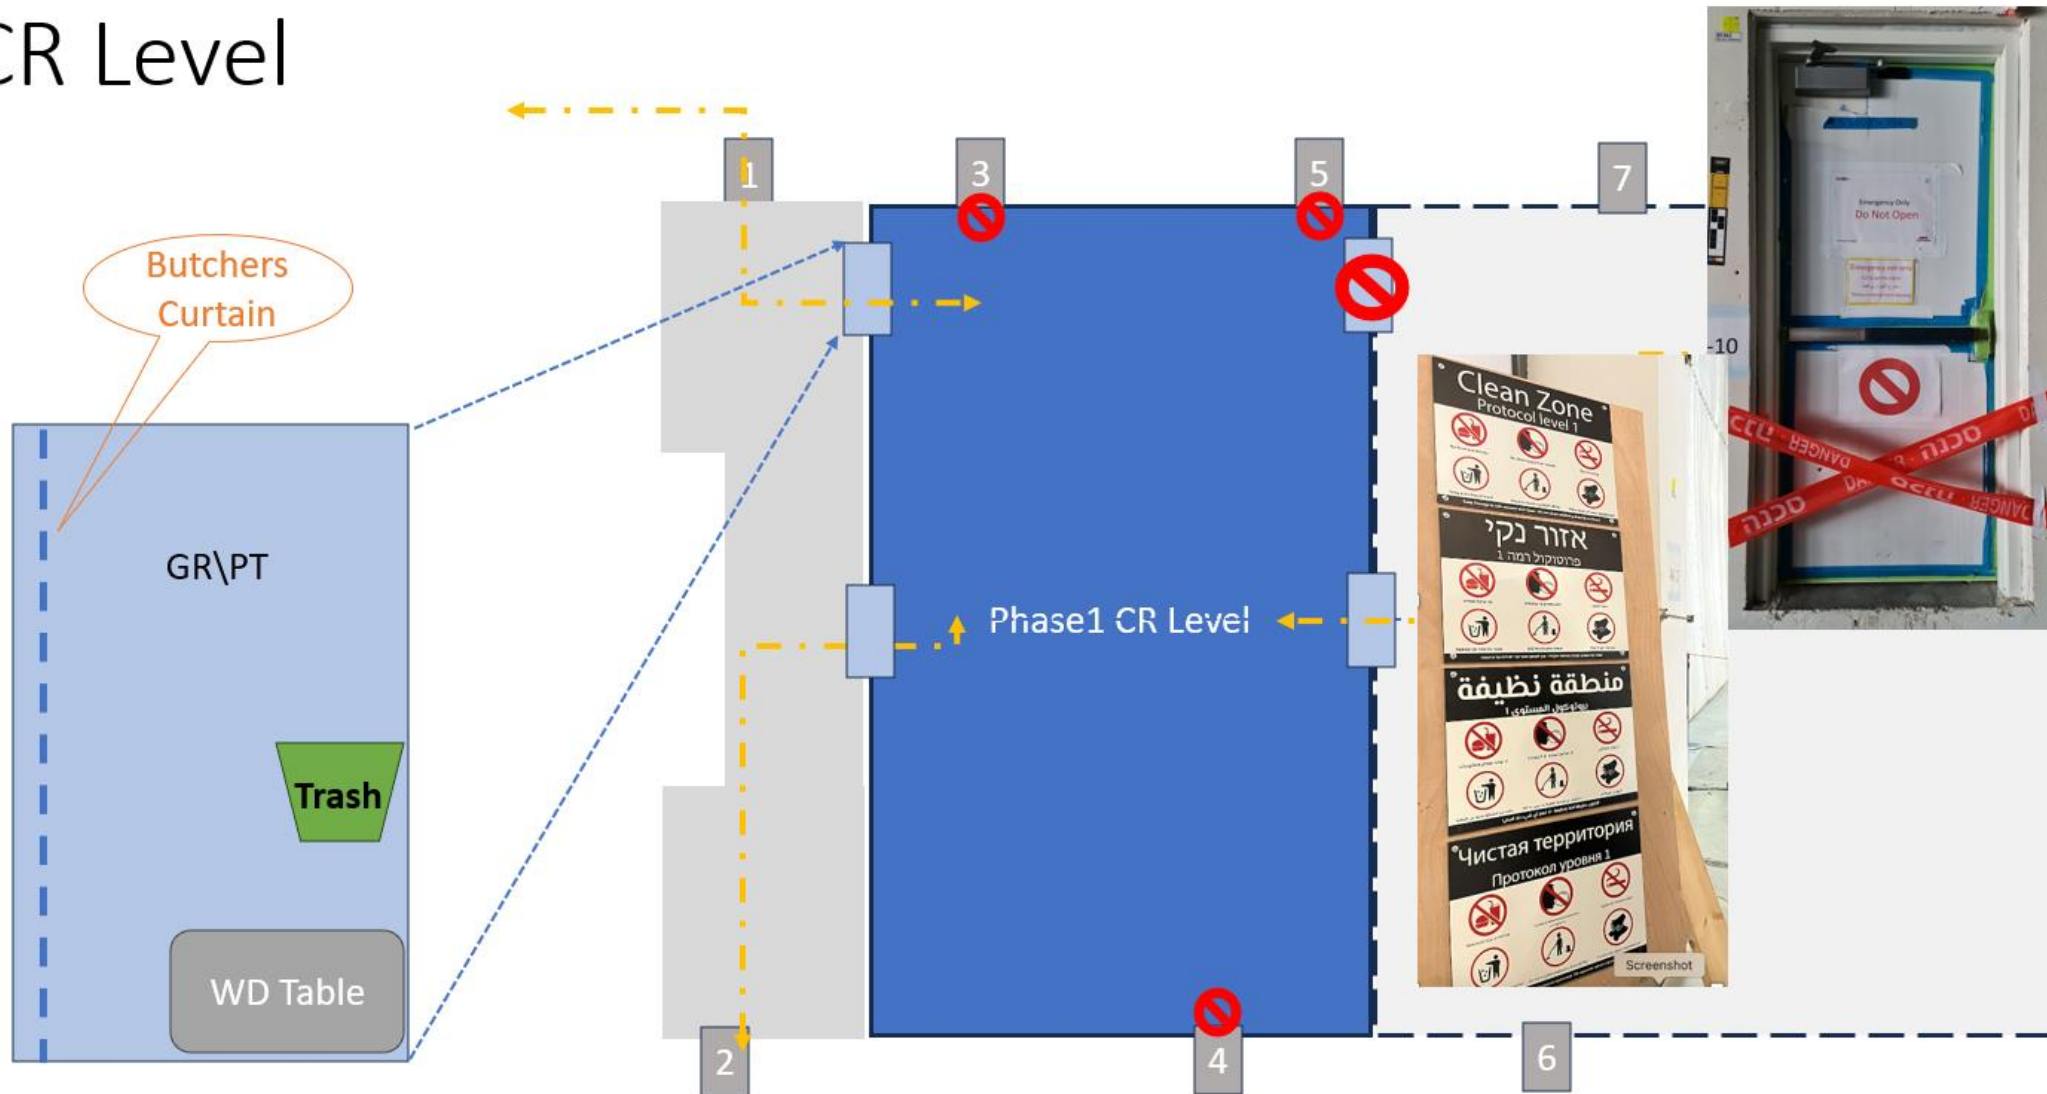

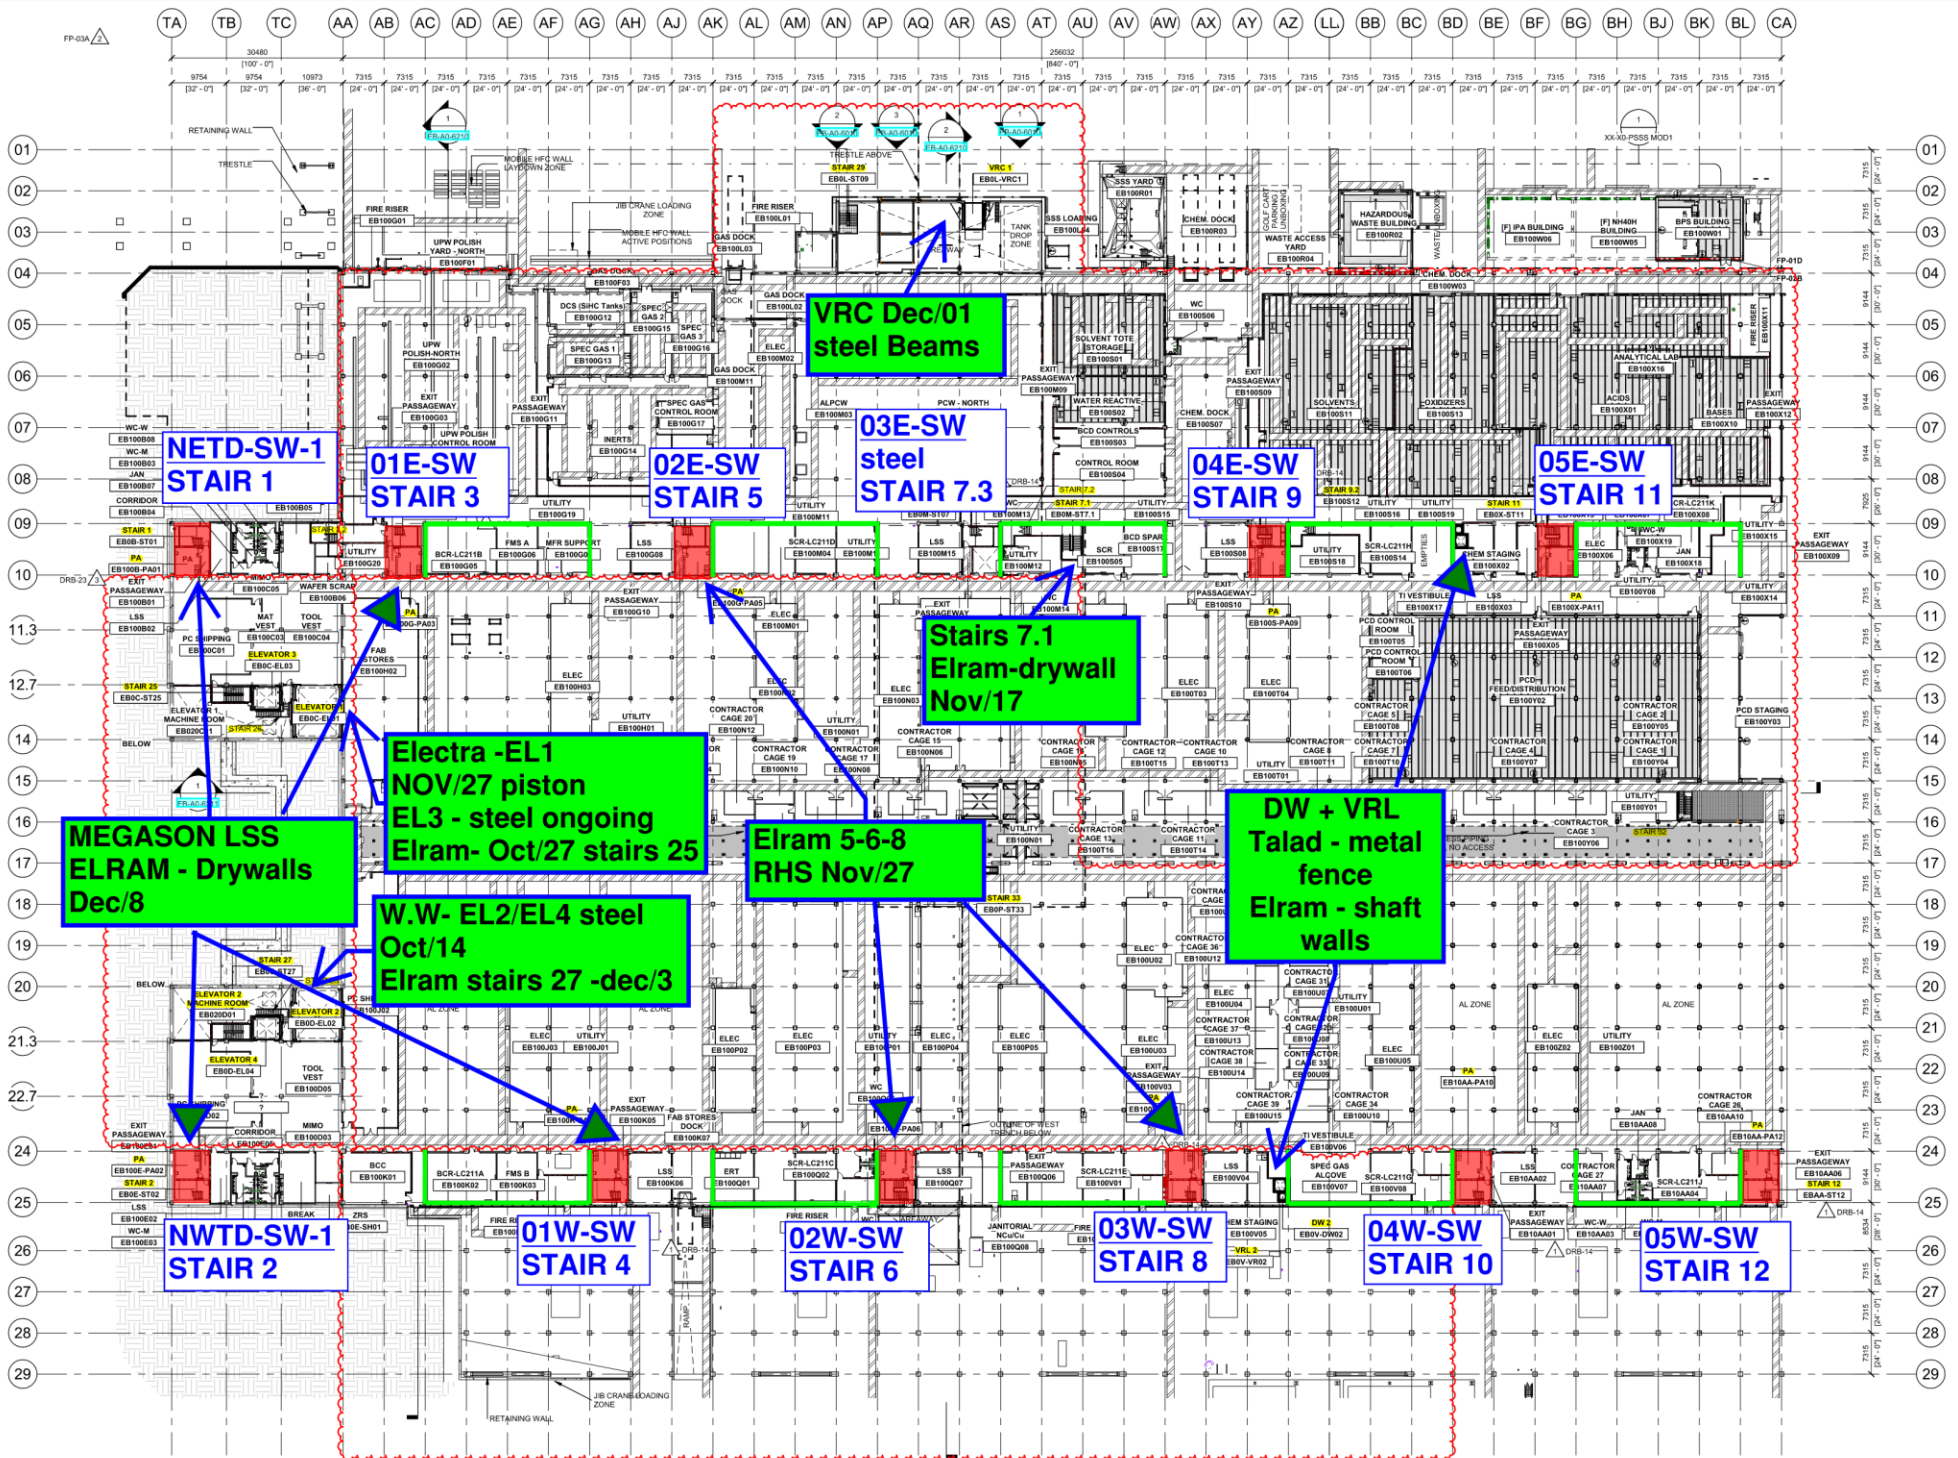


Siding - East FAB - PSSS


[illegible]


Siding - West FAB - JYG

[illegible]

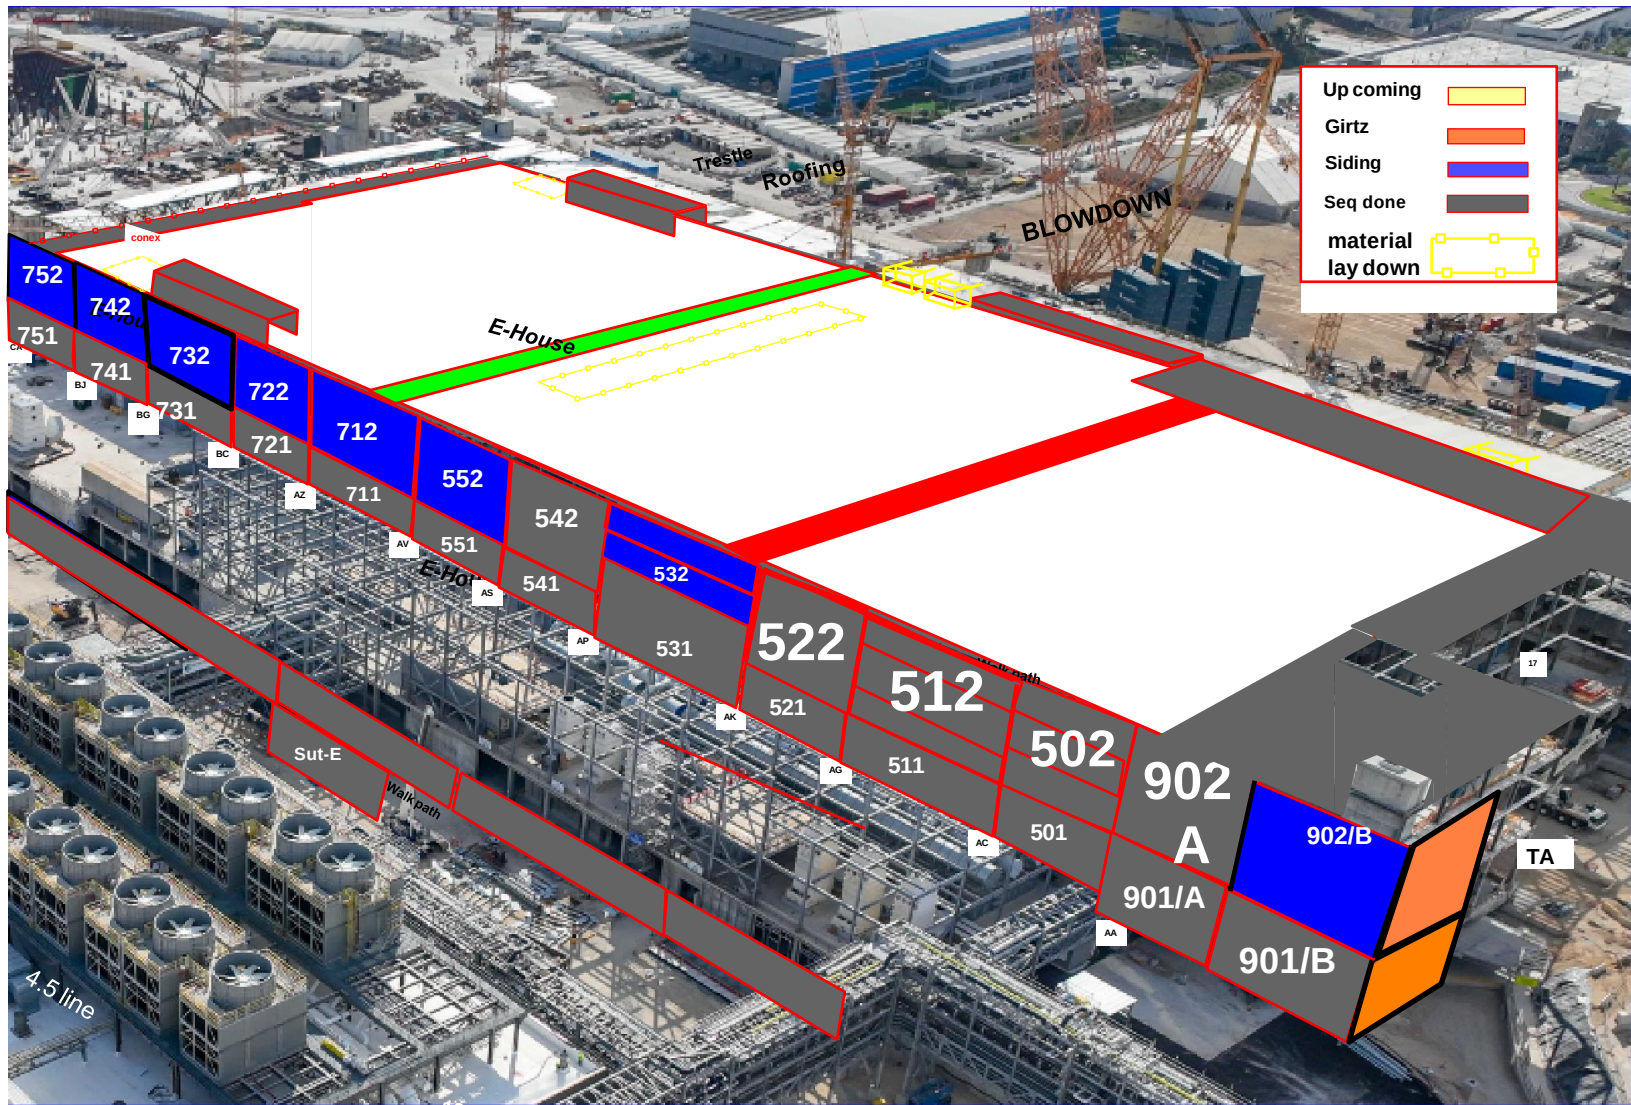

Walk path

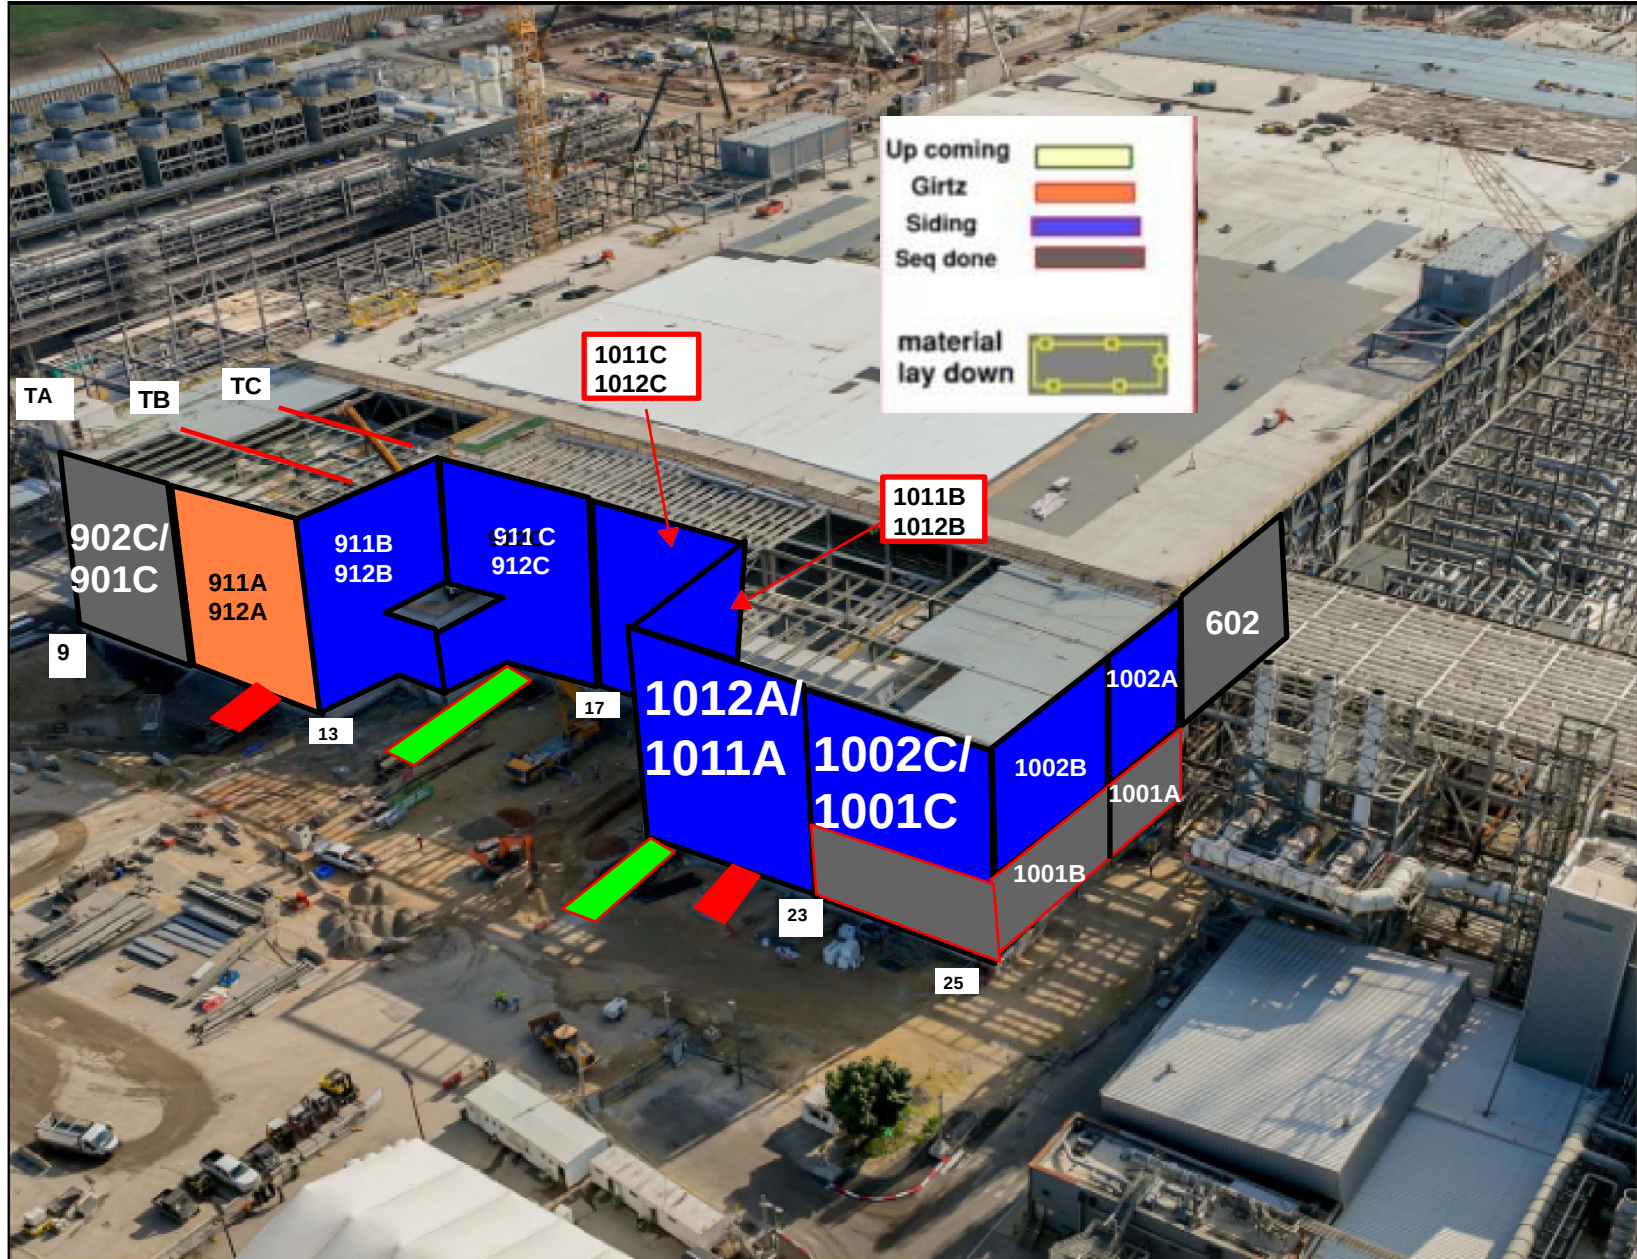


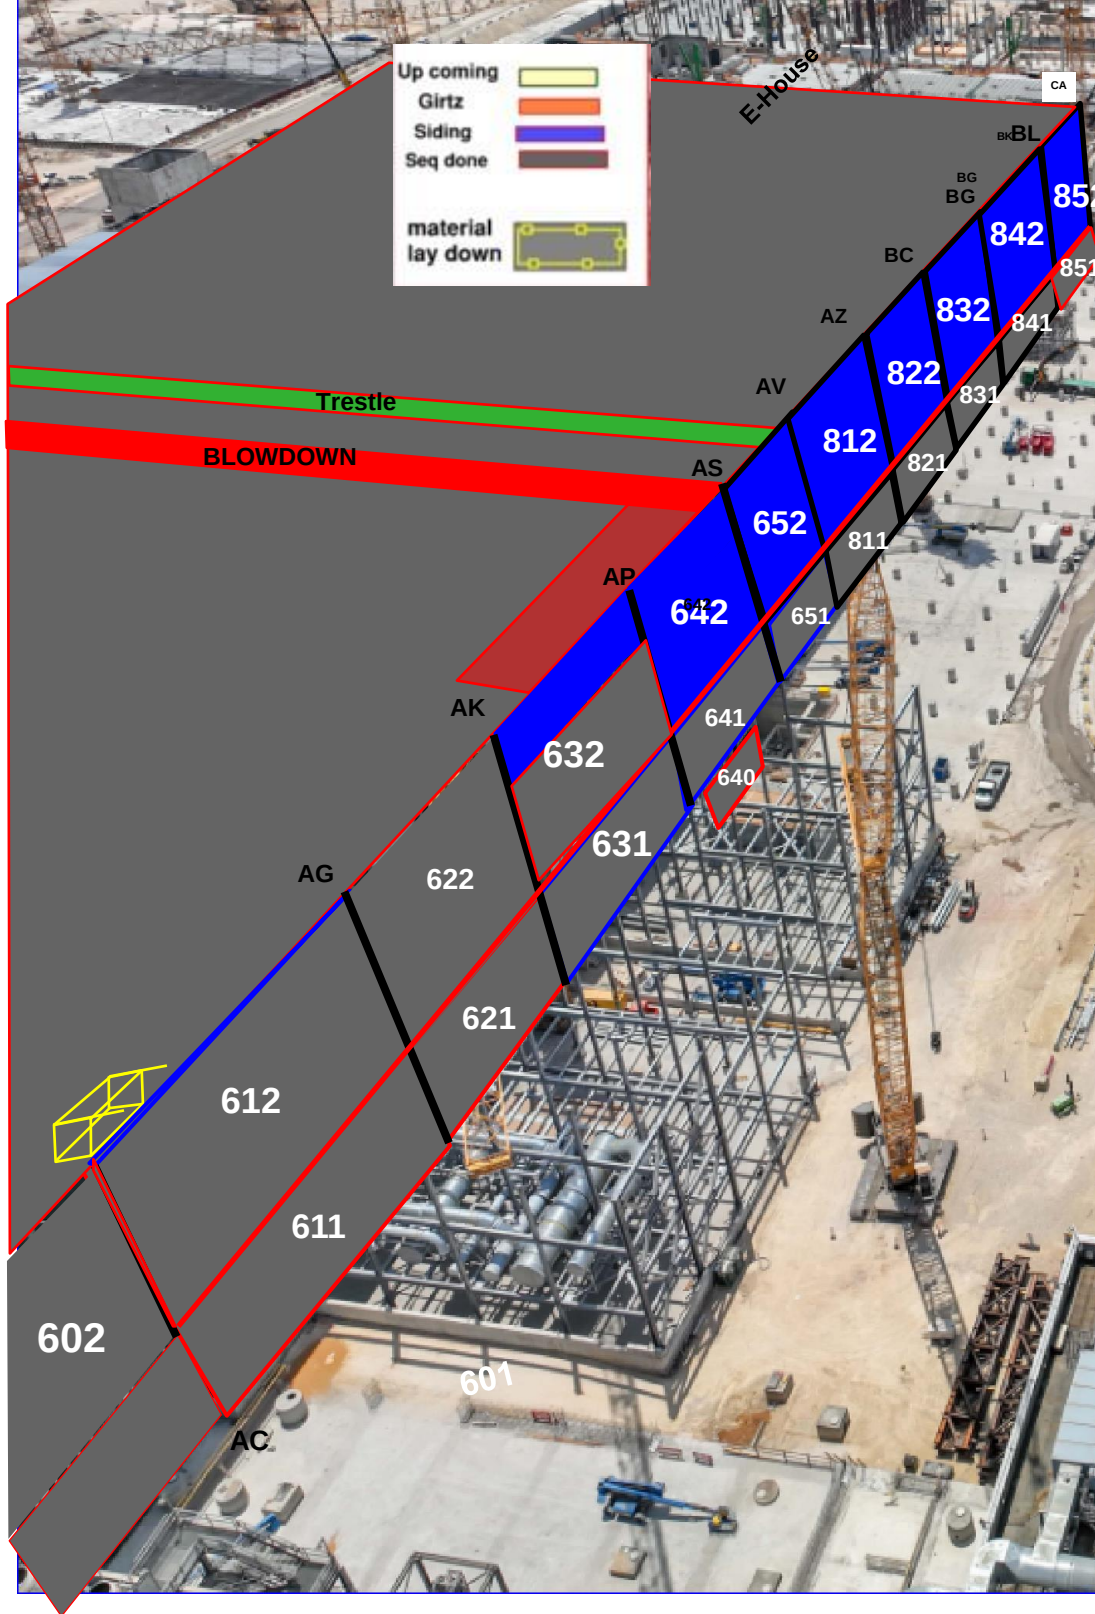

PSSS.1

Utility Level 1YA


PSSS Roof 2SA

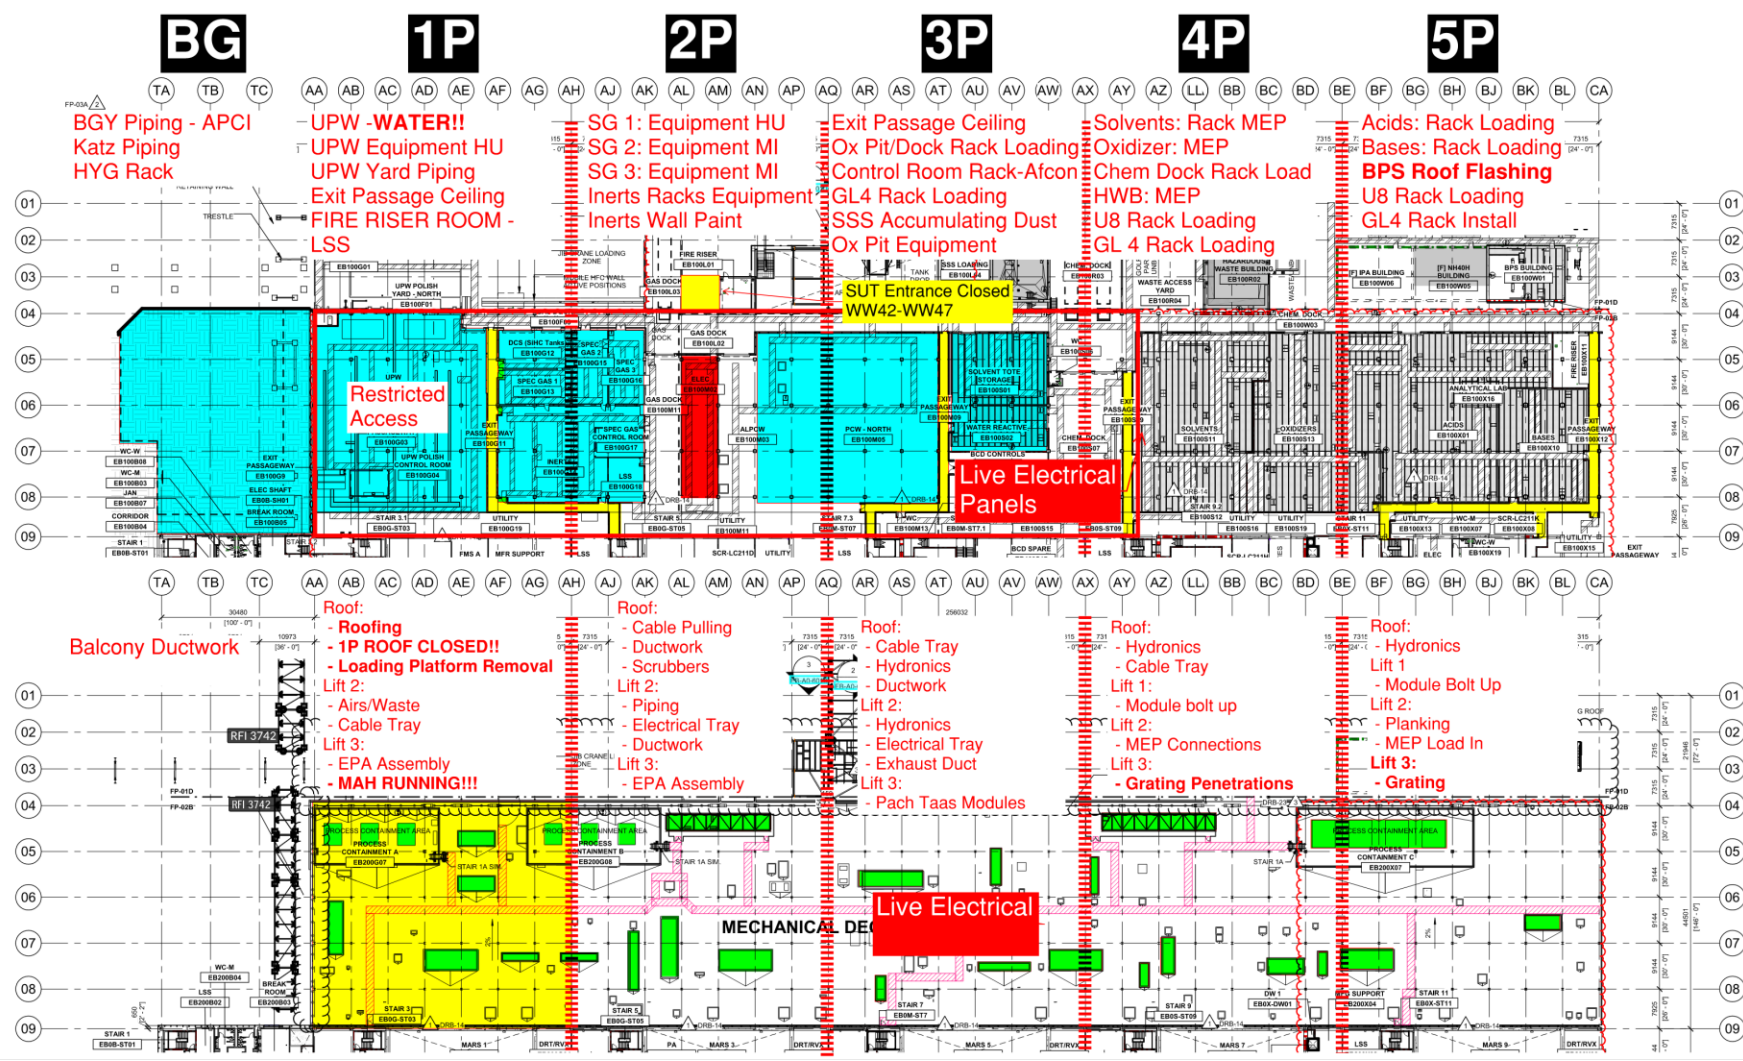


PSSS.2

Utility Level
1YA

PSSS Roof
2SA

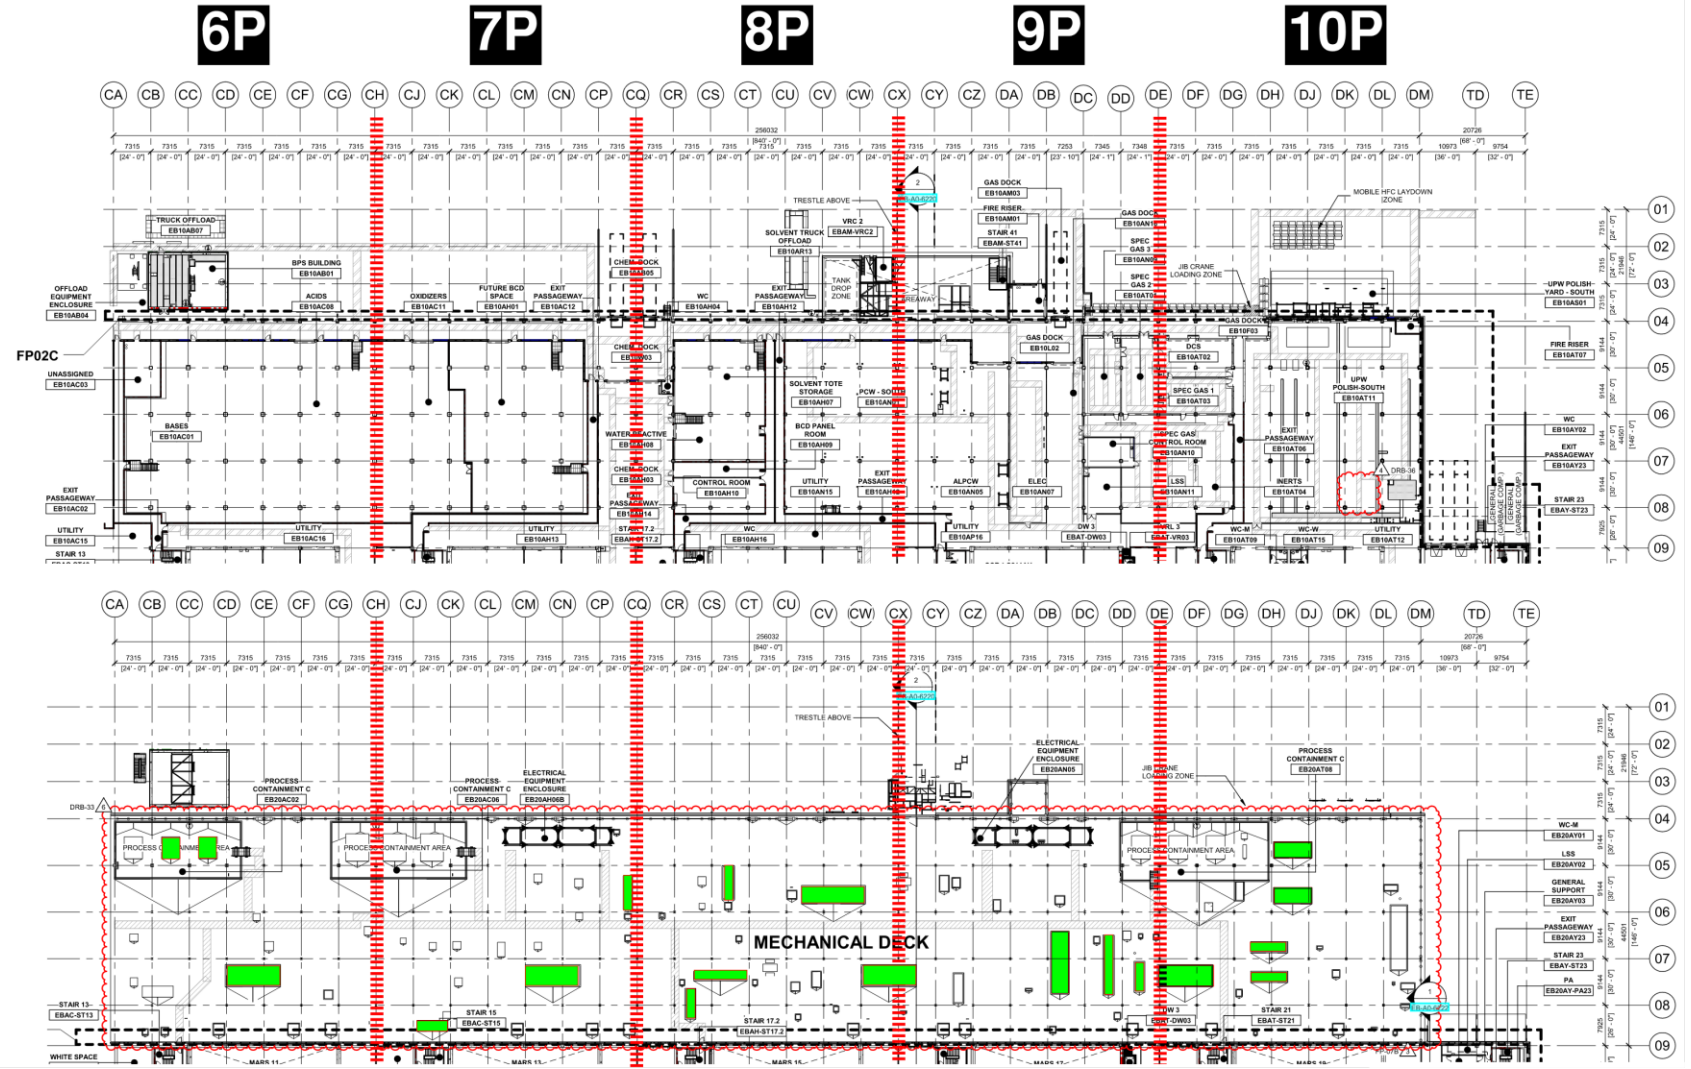

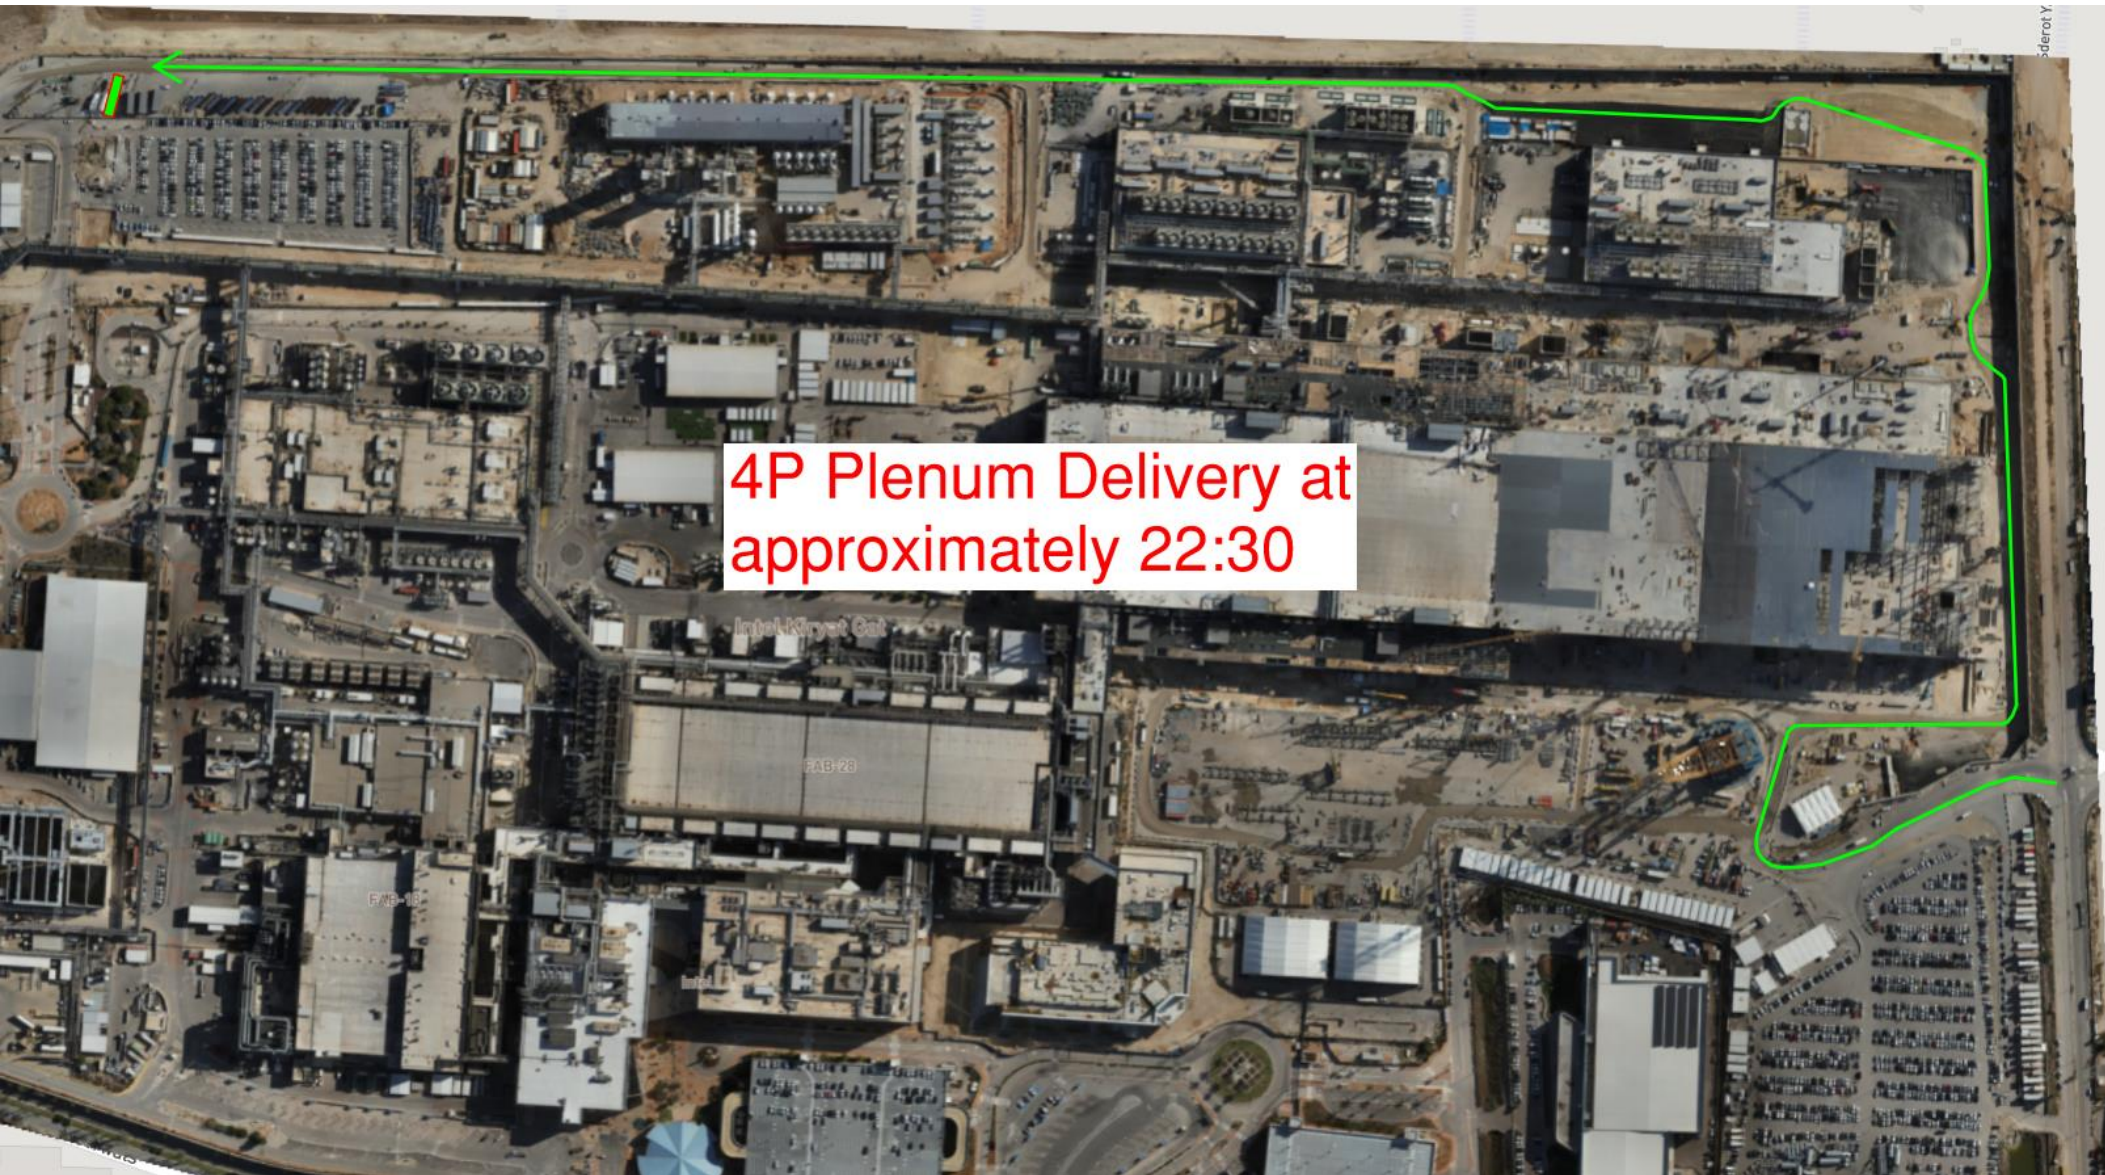

4P Plenum Delivery at
approximately 22:30

Intel Kreyet Gate

FAB-28

FAB-18



WJG 01J, 02J LIFT 2 & 3






WJG 03J, 04J, 05J LIFT 2 & 3






MAH101-9/10-00 Set WW50

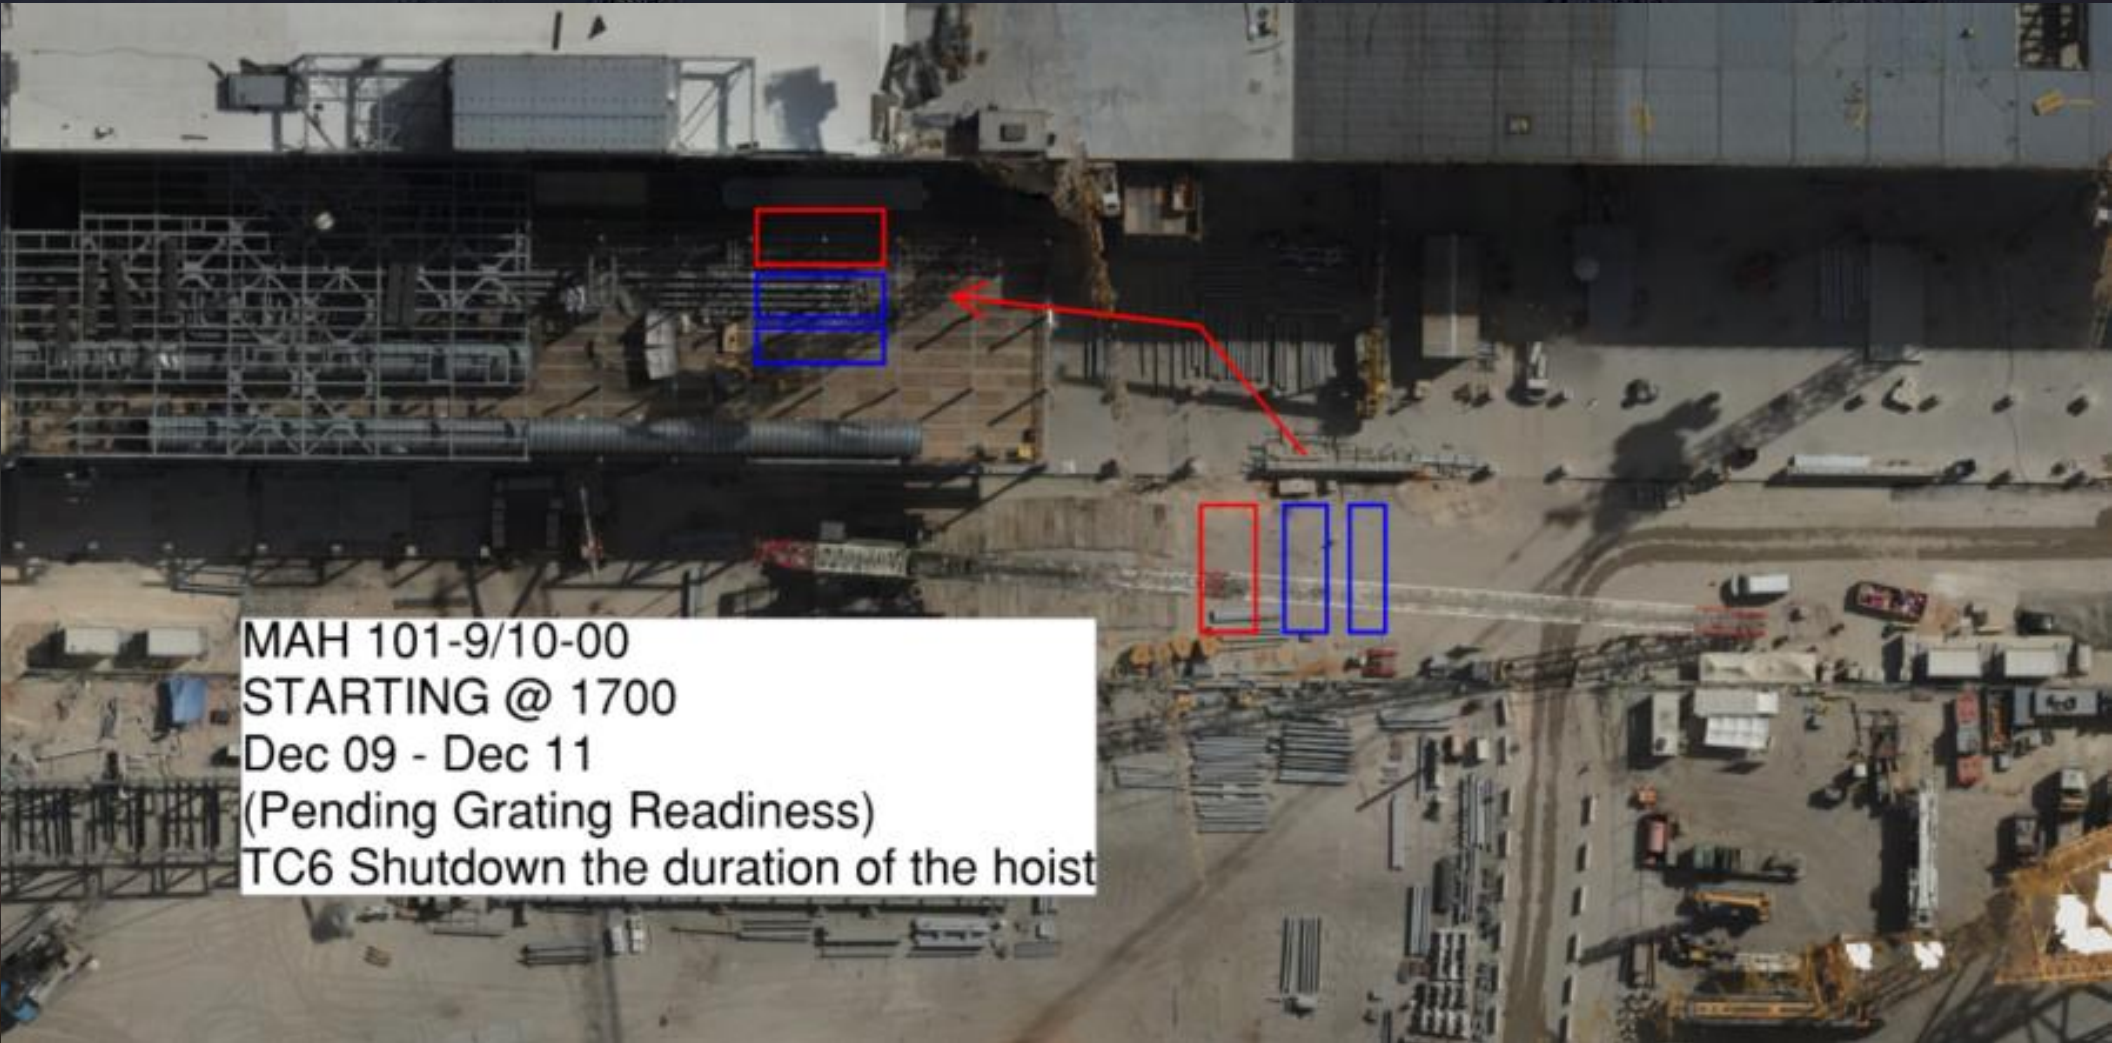



WJG UTILITY LEVEL BUILD OUT






CC3800 DEMOB WW51






CUB 1


CUB 1 COORDINATION MAP

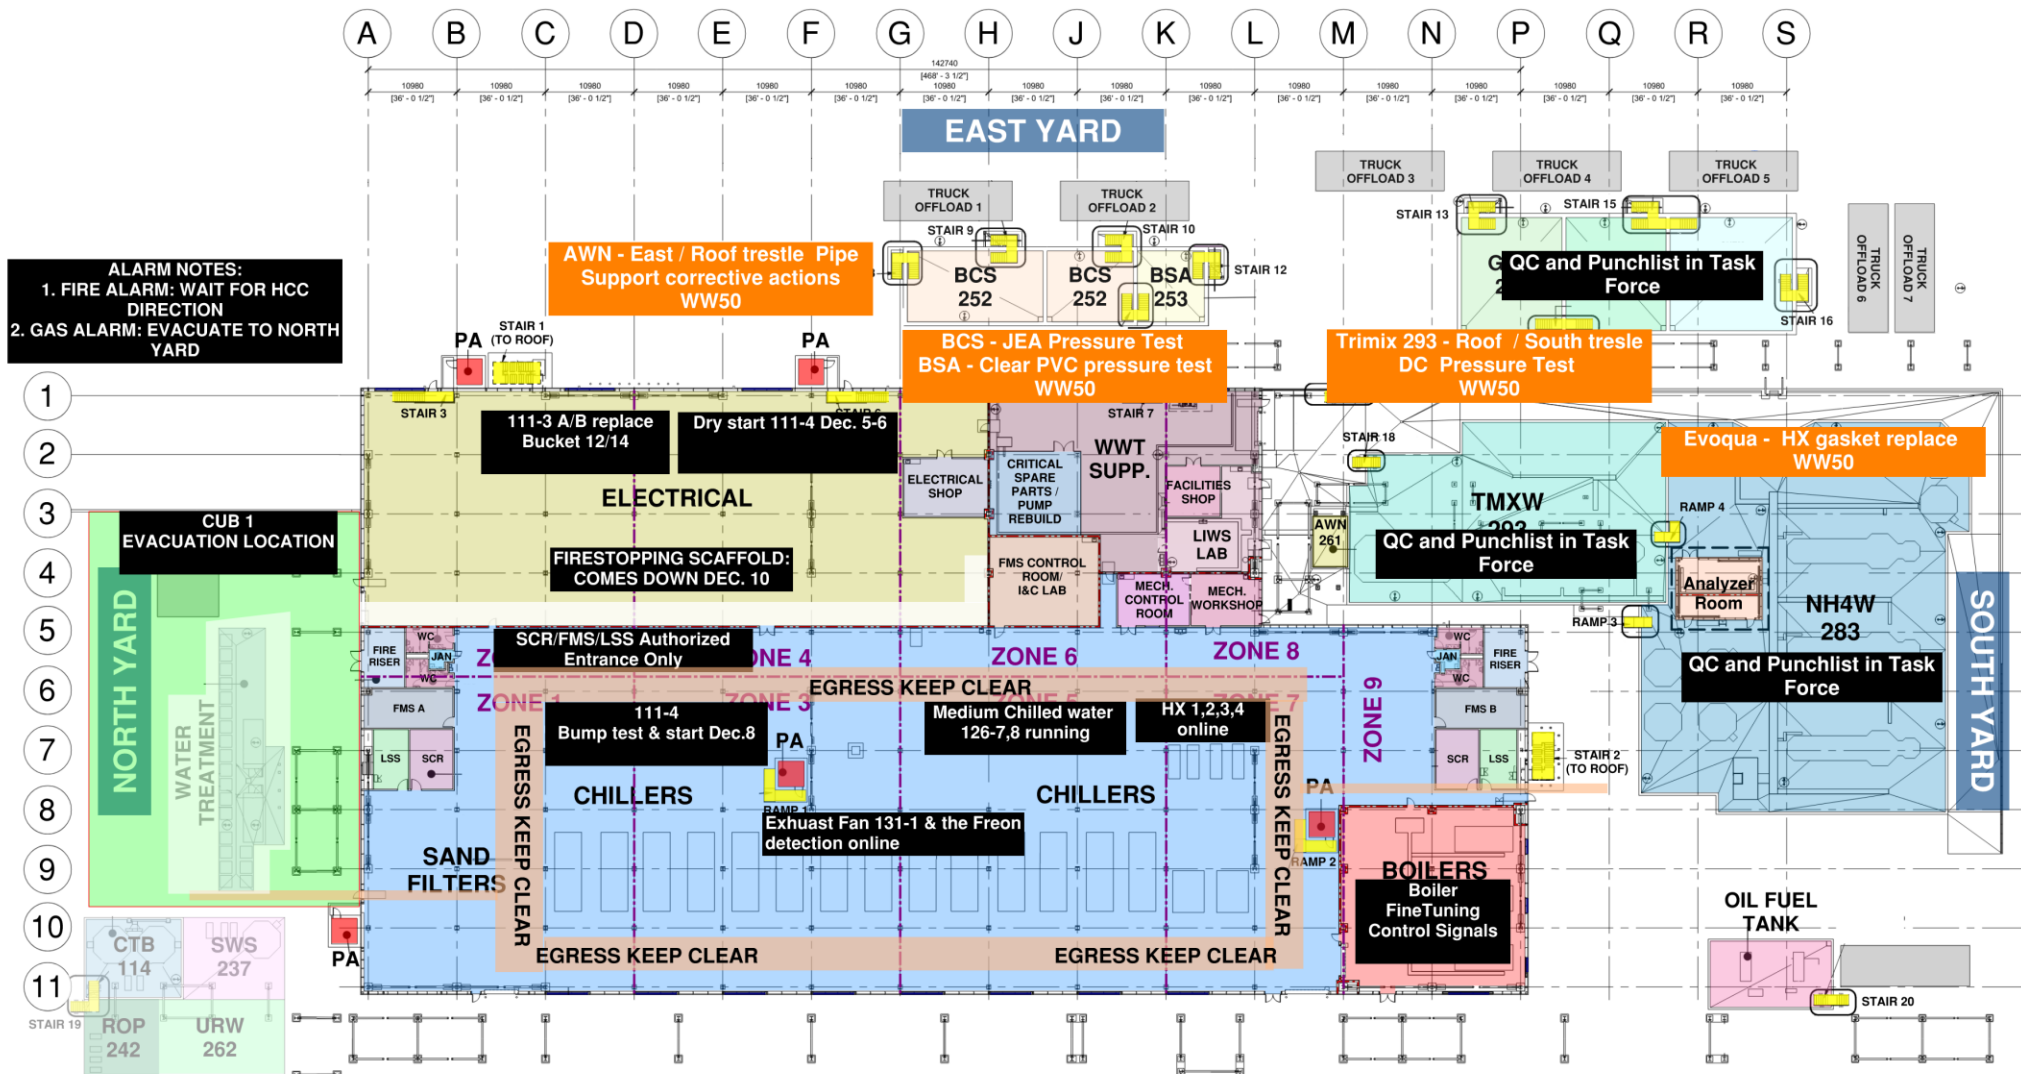


CUB 1 – EXTERIOR/ROOF

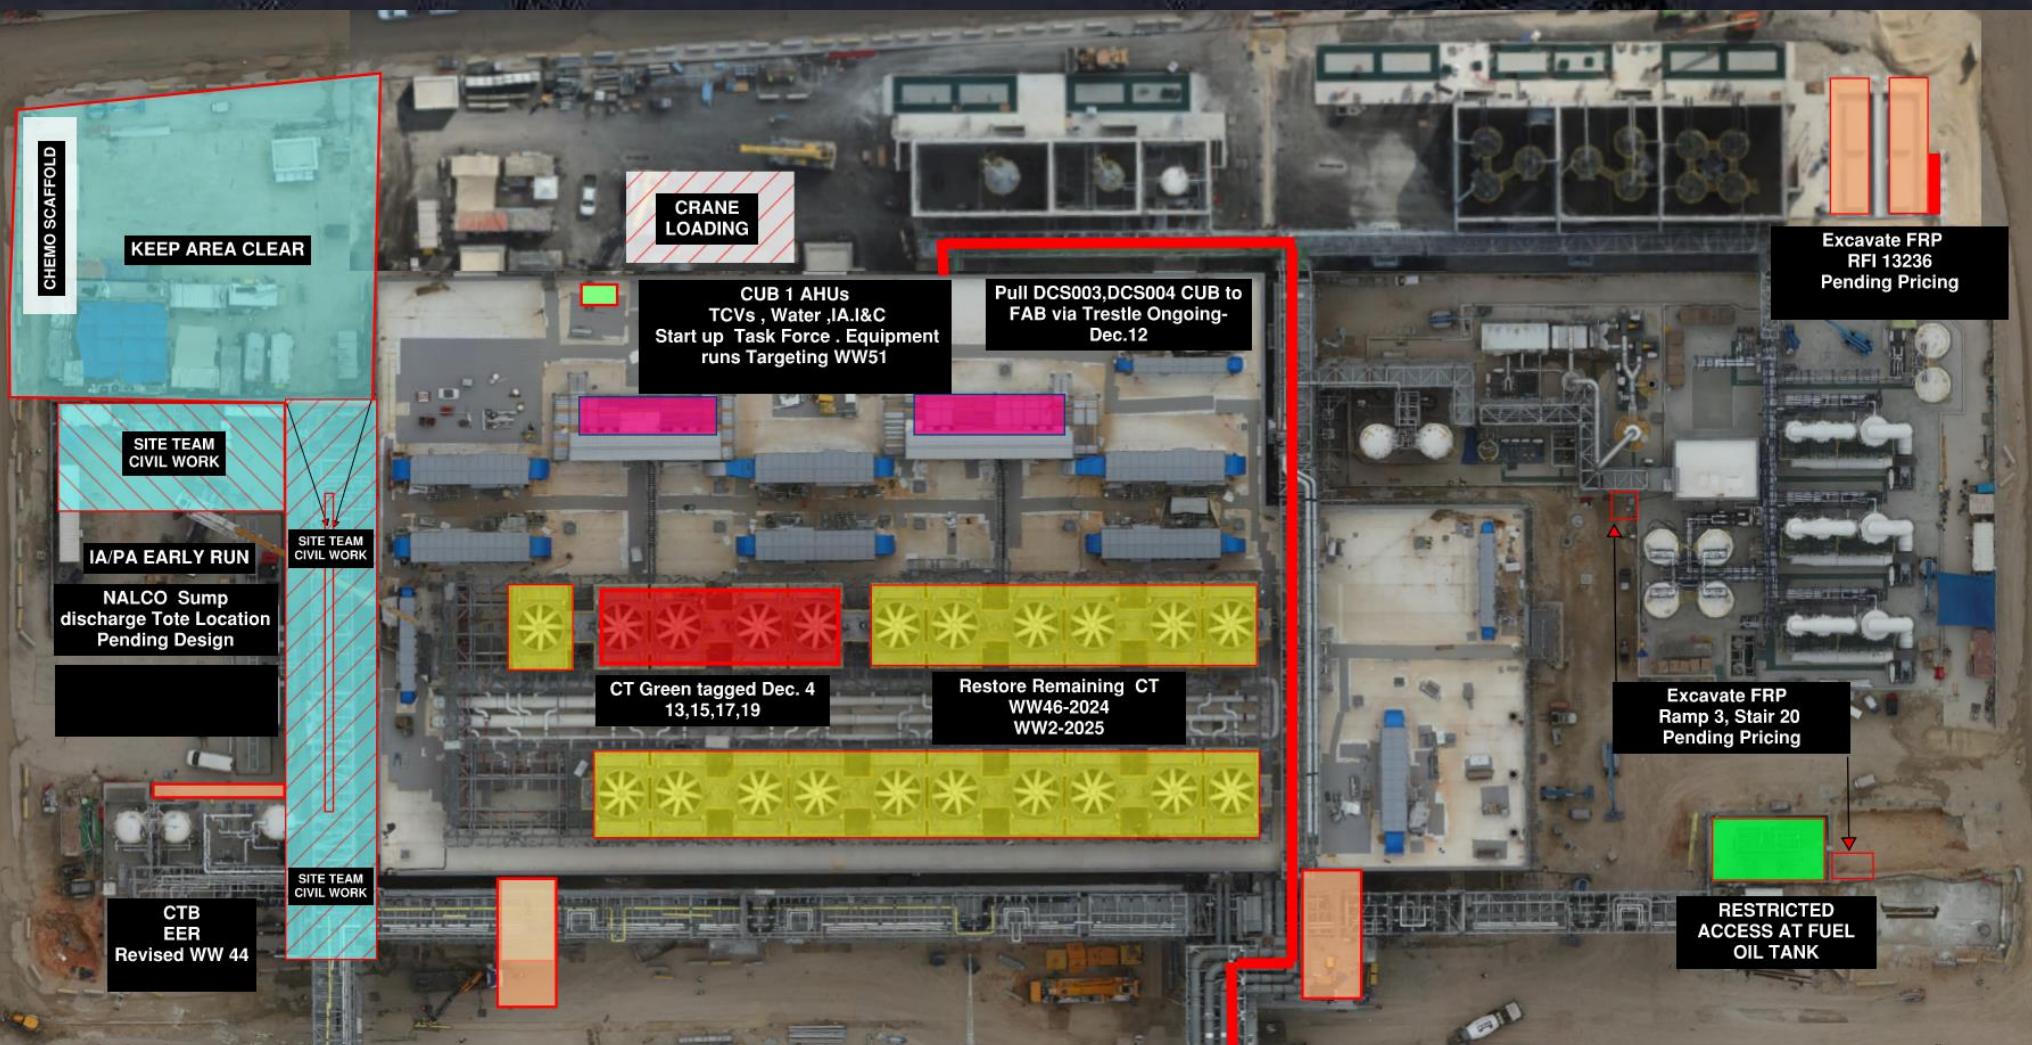

CUB 2 COORDINATION MAP

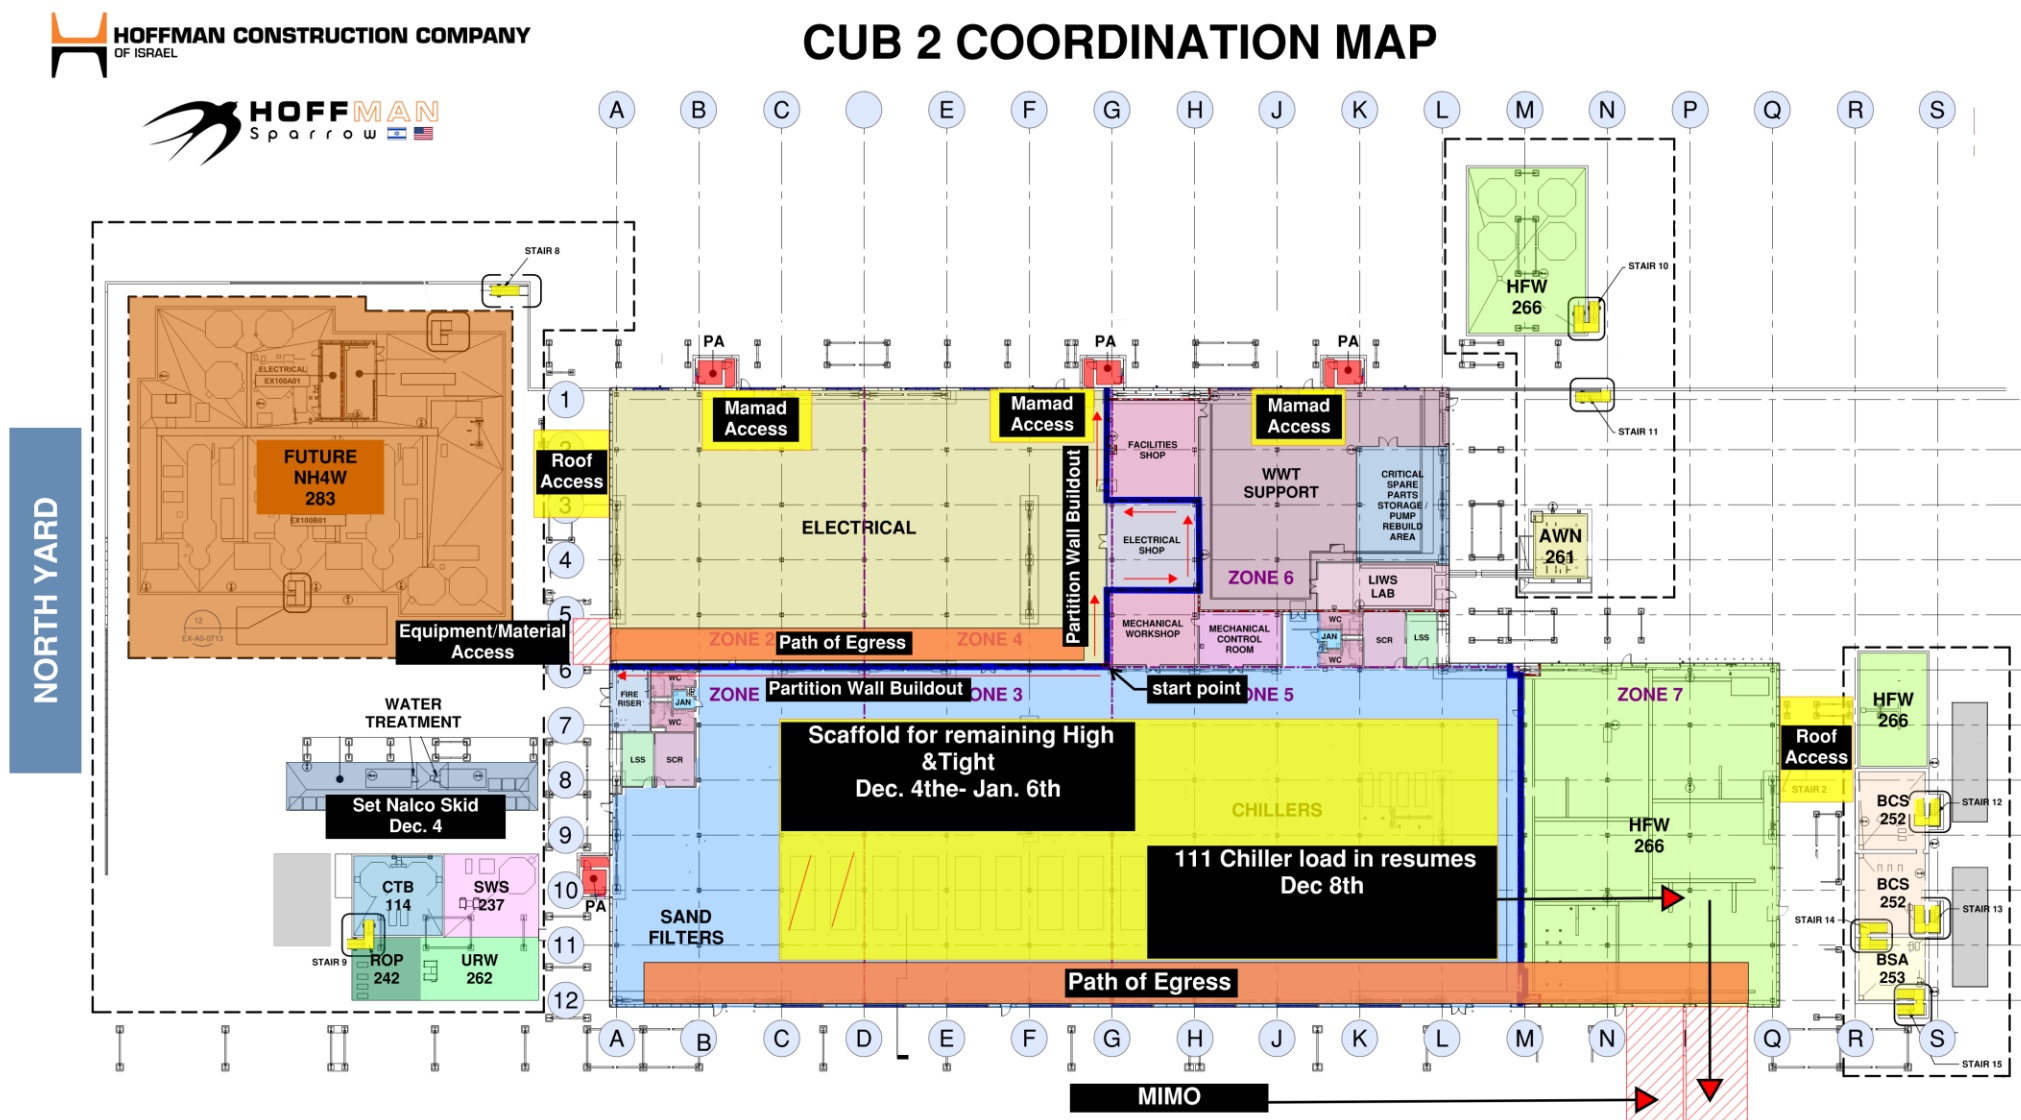



CUB 2 – EXTERIOR/ROOF

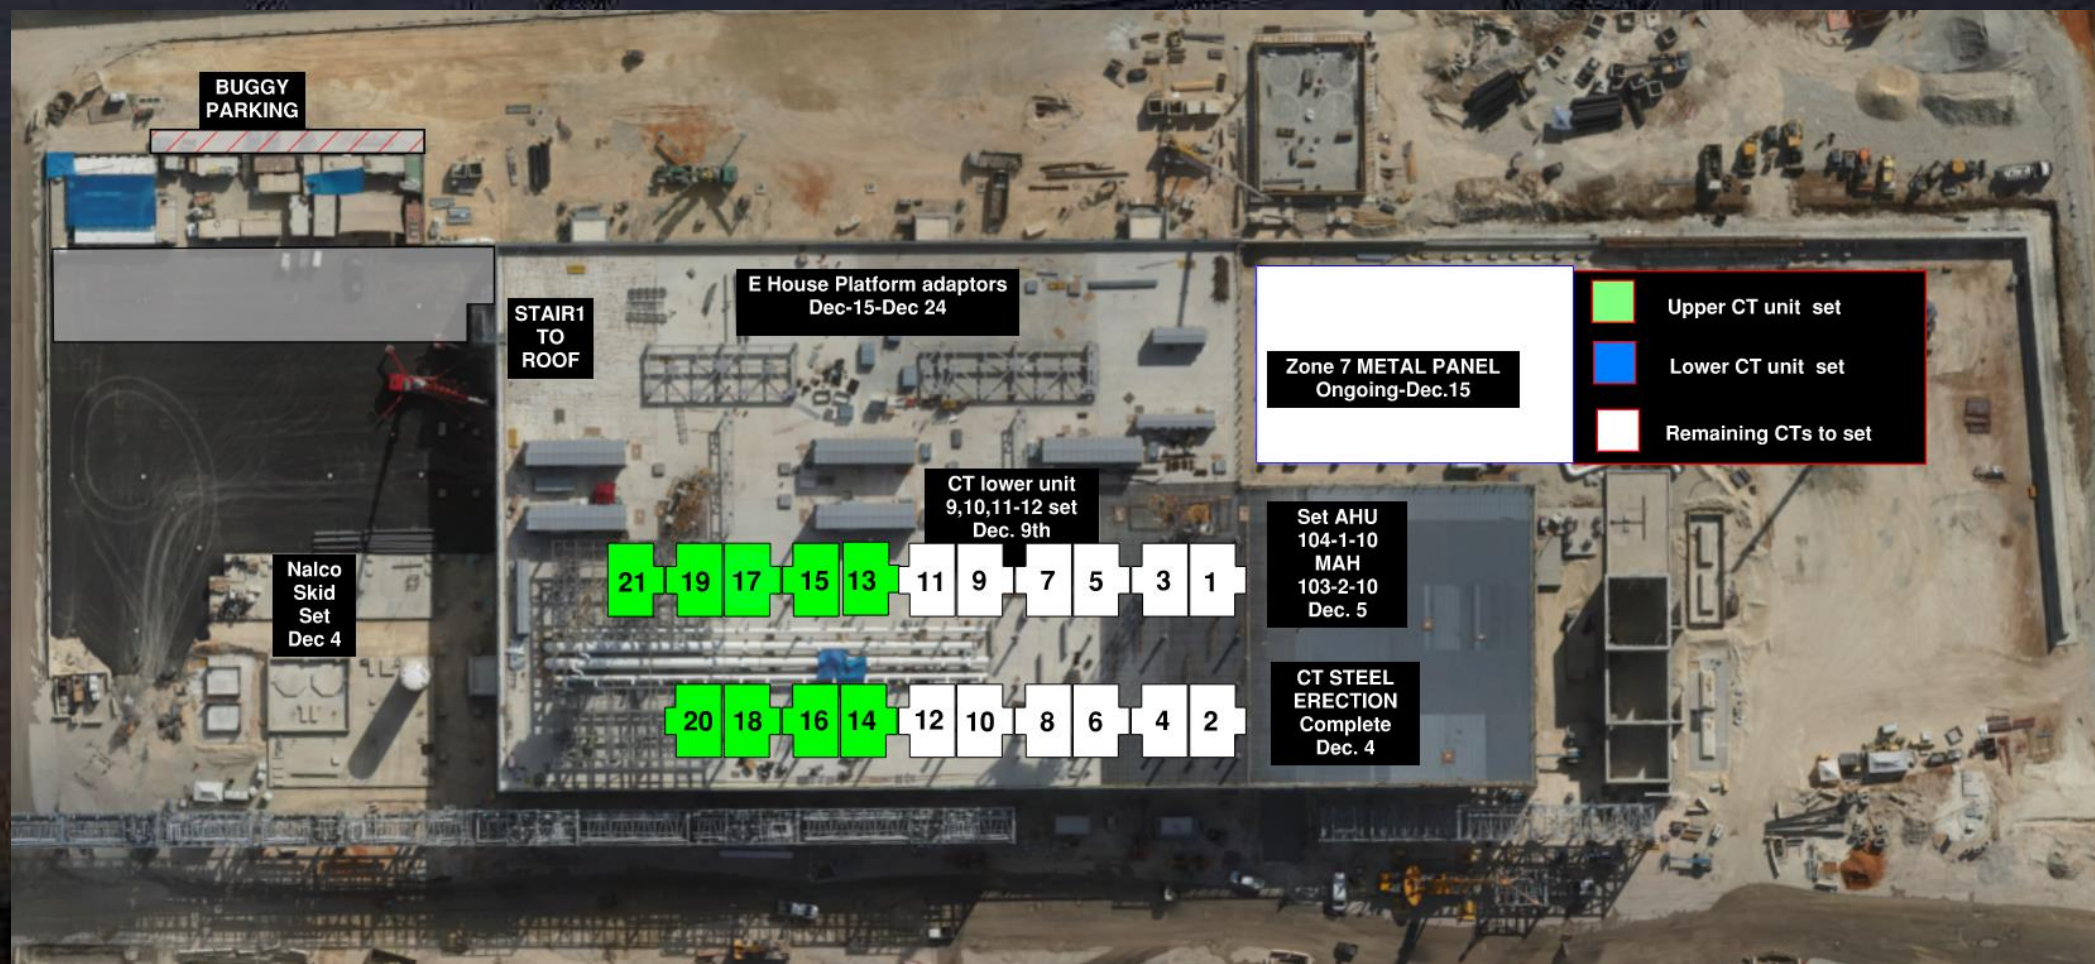



GIS GATE
closed 29/Dec /2024

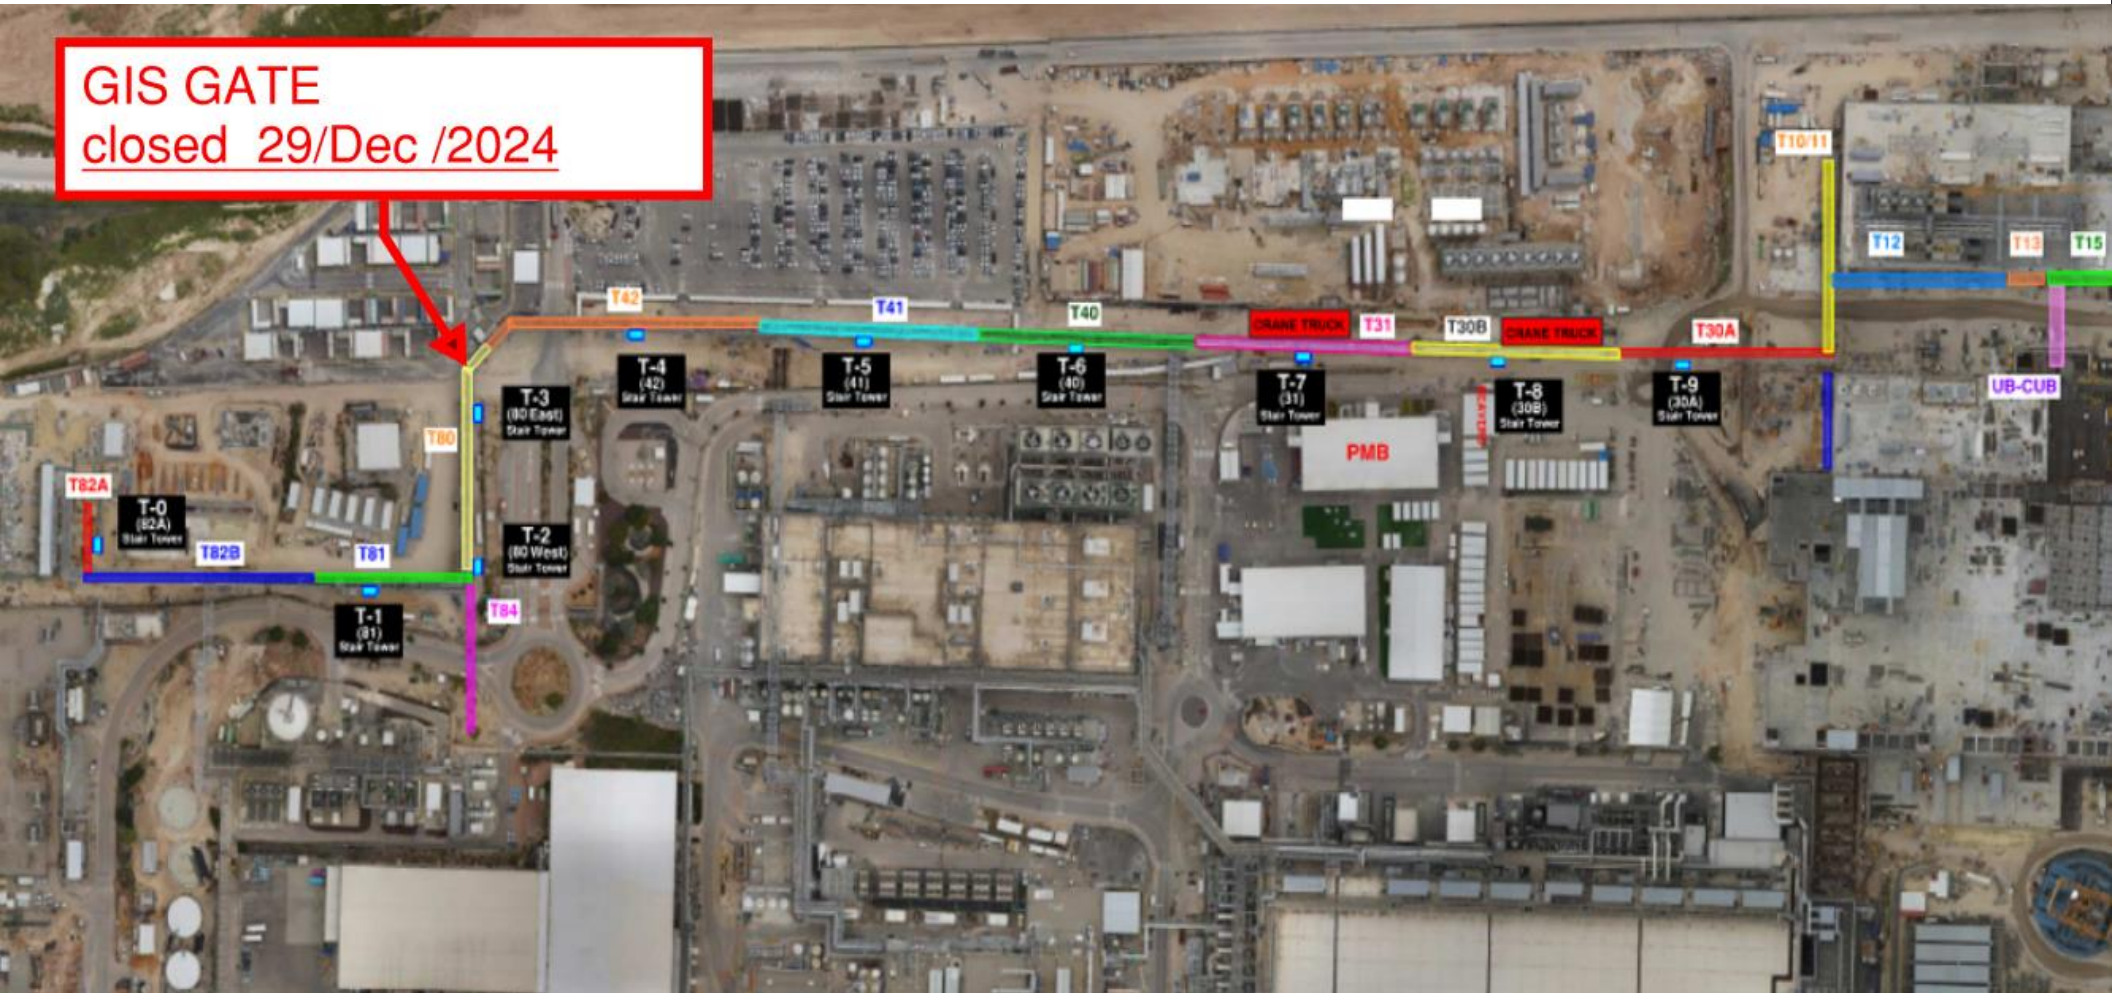



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow



T18

DEC 3th - DEC 11th

DEC 8th



DEC 9th


DEC 10th

done

done

done





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

BGC - NDT

Starting –Sunday night December 8^h at 19:00
Finish Monday December 9th at 05:00am.

Safety spotter

Safety spotter



Truck will hold outside of Gate B for ~30 min. while Siemens attaches lifting Lugs

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:
1. Dec -11th
2. Dec -17th
3. Dec - 19th
4. Dec - 24th
5. Dec - 30th
6. Jan - 2nd
7. Jan - 7th
8. Jan - 10th

Truck Turn
Around

Tandem Mobile
Offload 4,5,6

Sarens
Offload
1,2,3,7,8

E House
Offload/Staging

Intel Kiryat Gat


FAB-28



Daily Coordination Meeting

Site Logistics


North

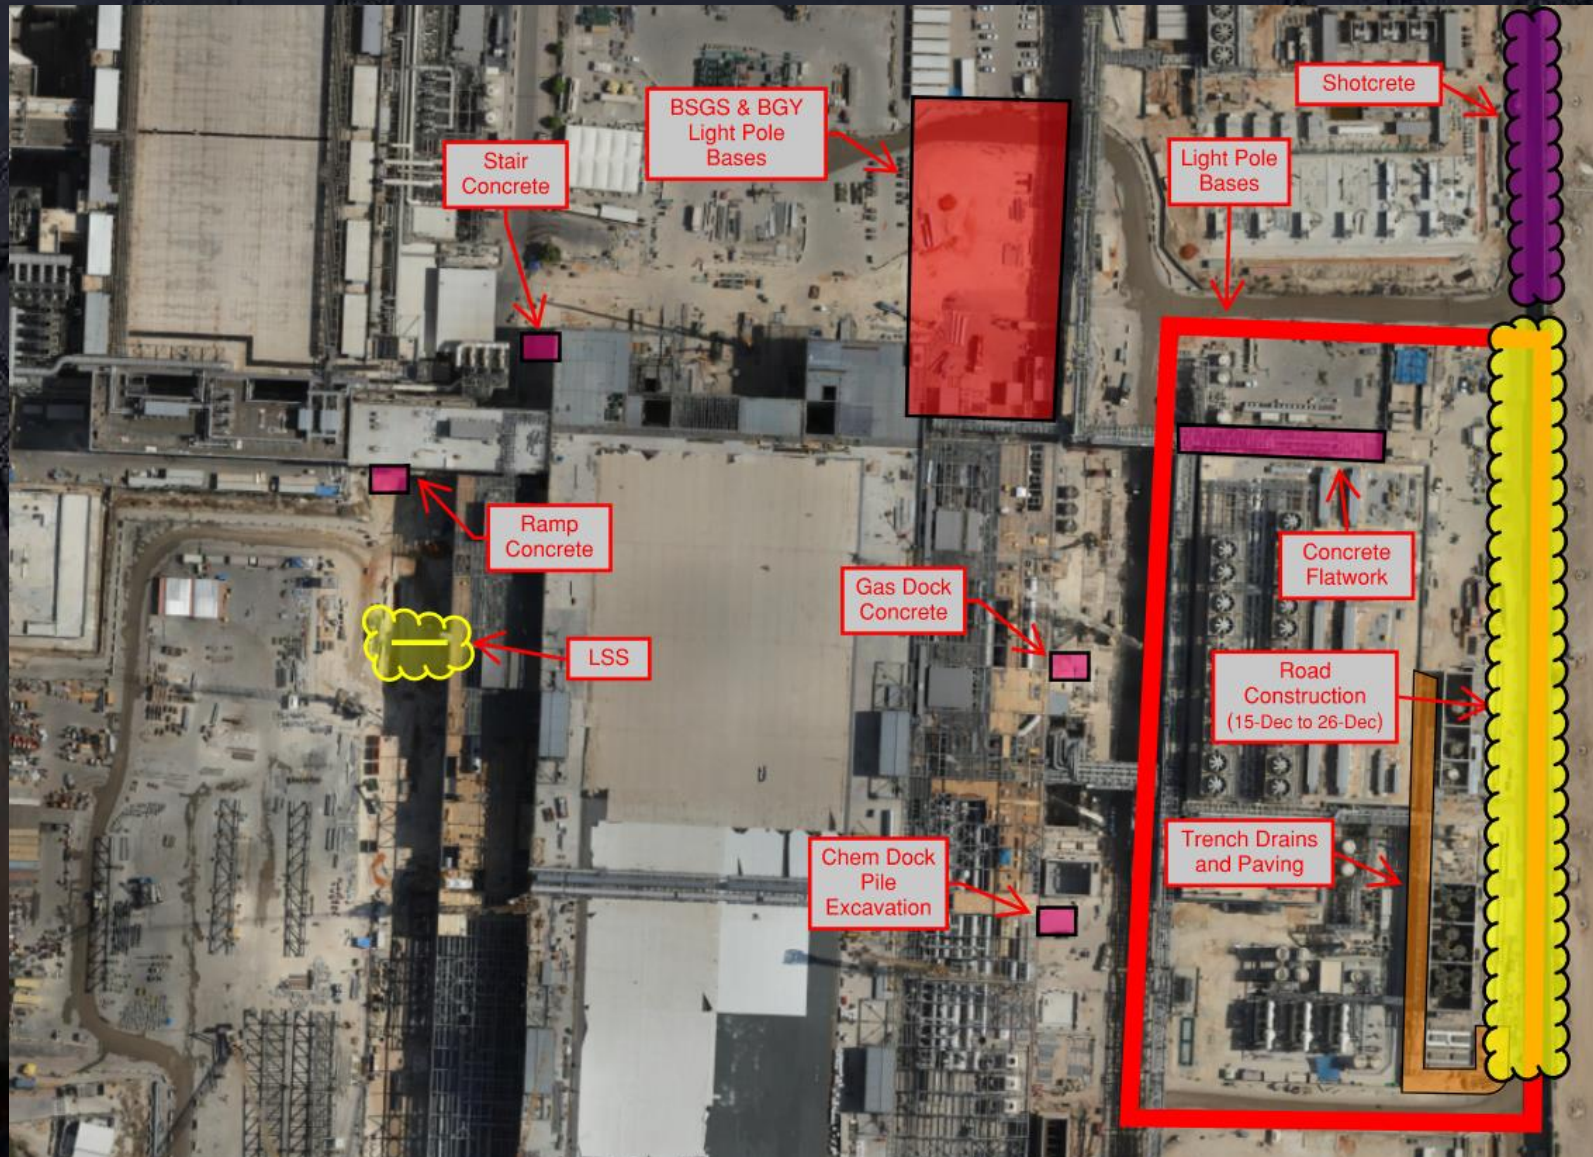

Daily Coordination Meeting

Site Logistics

East CUB1 Road Closure

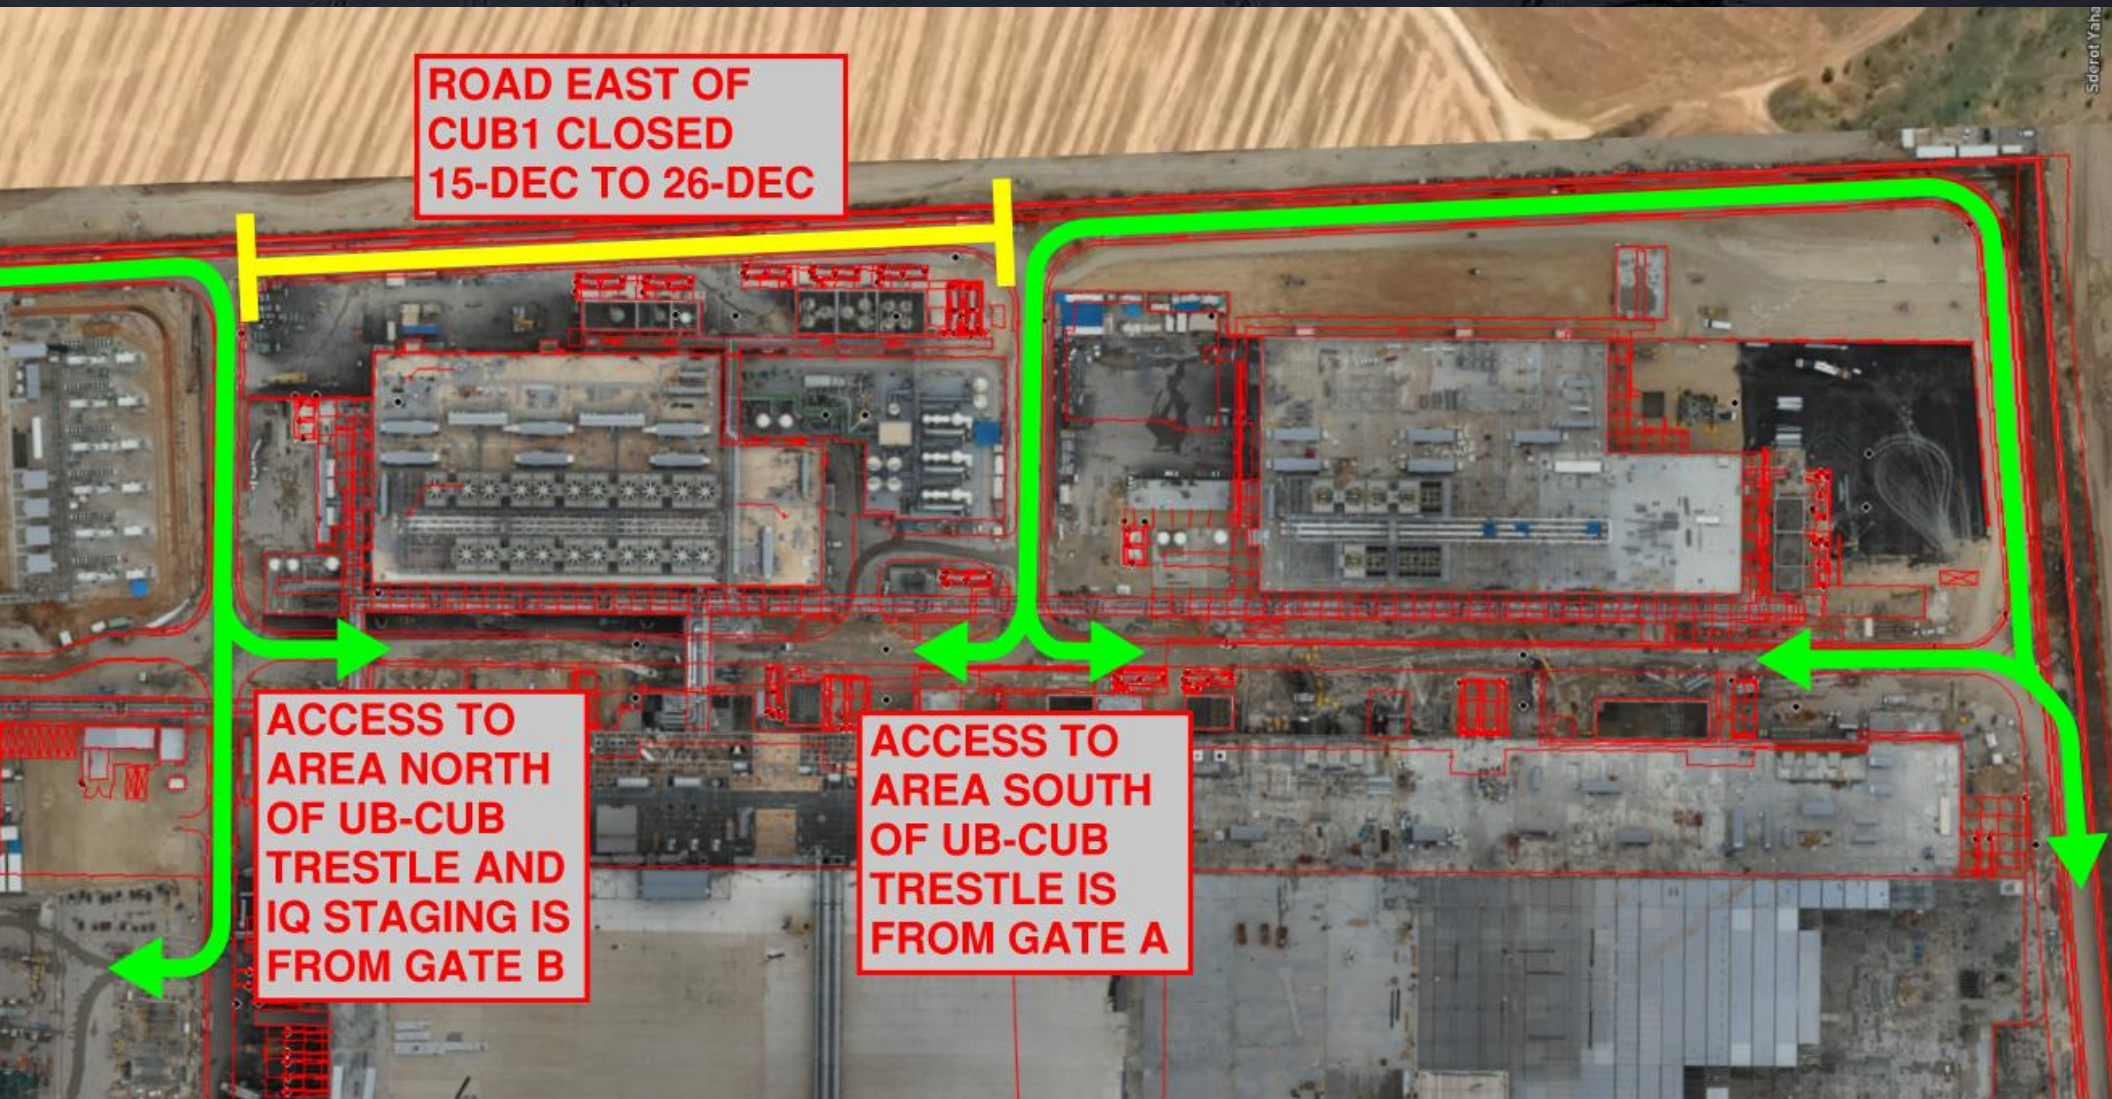




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting


Site Logistics

South

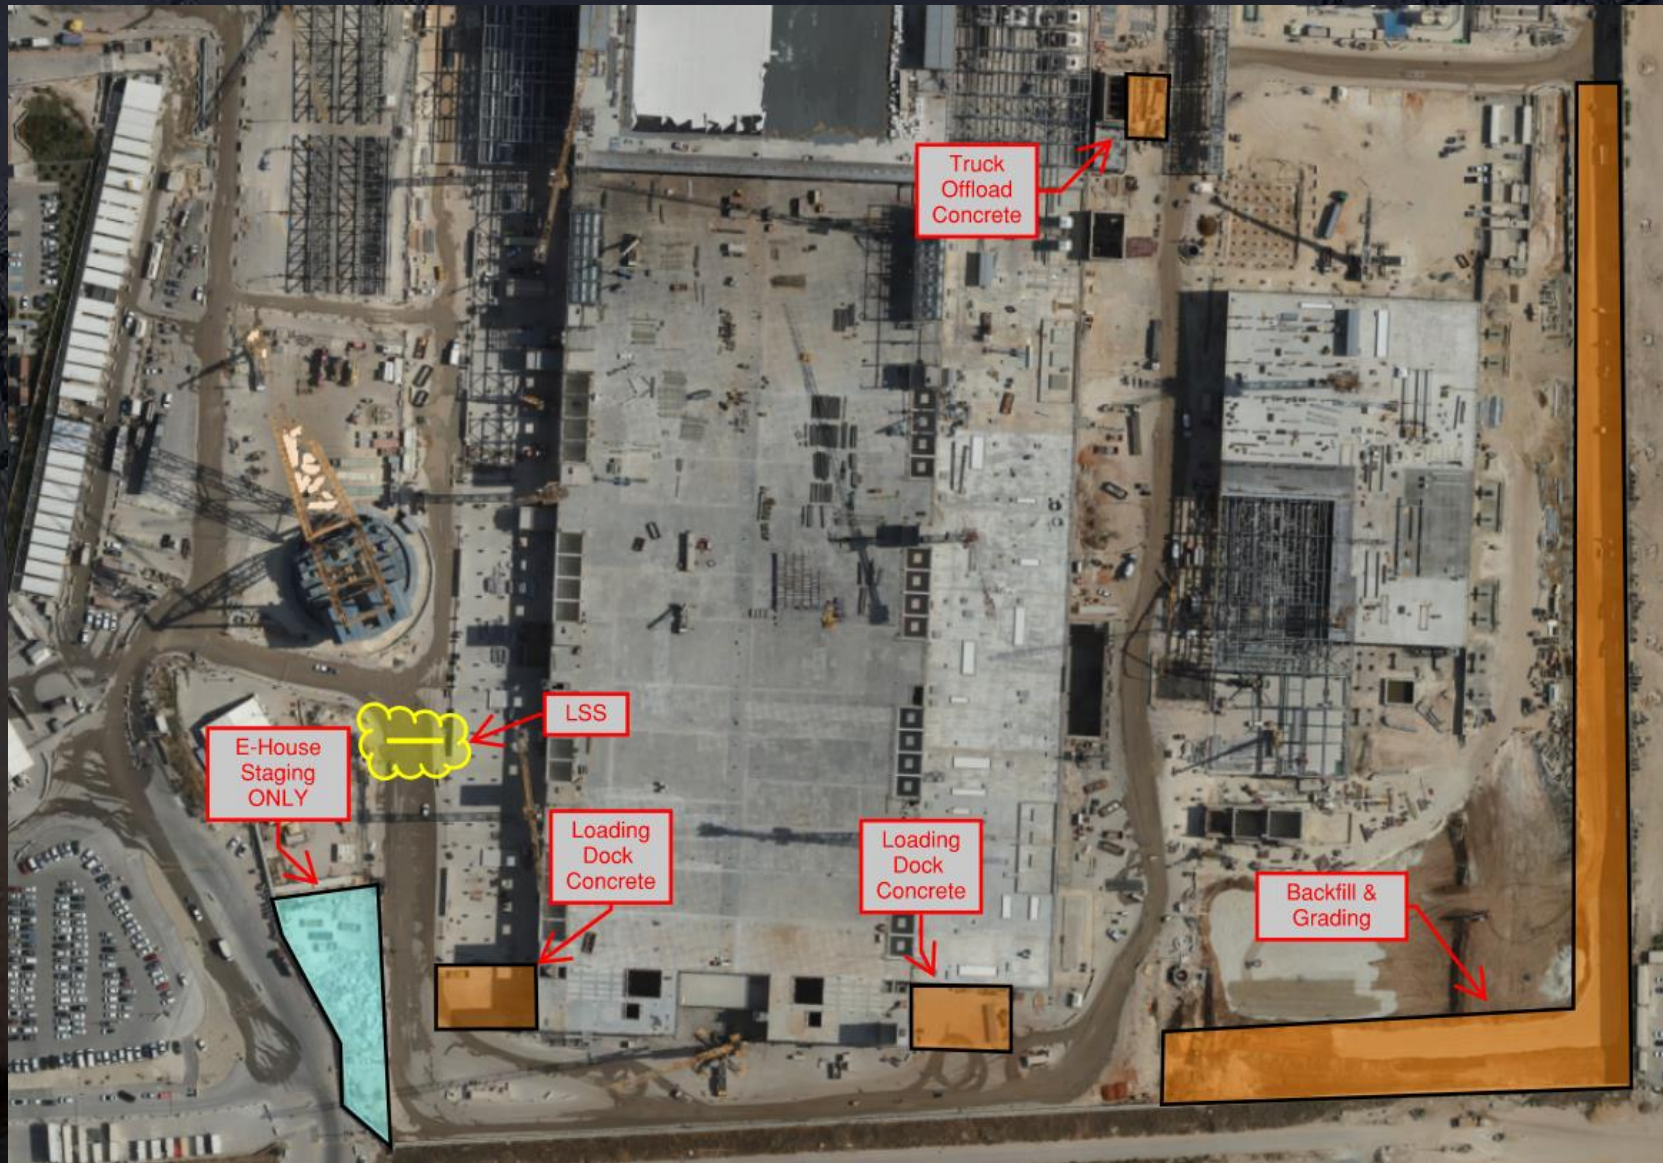



Not being caught Infront the line of defense

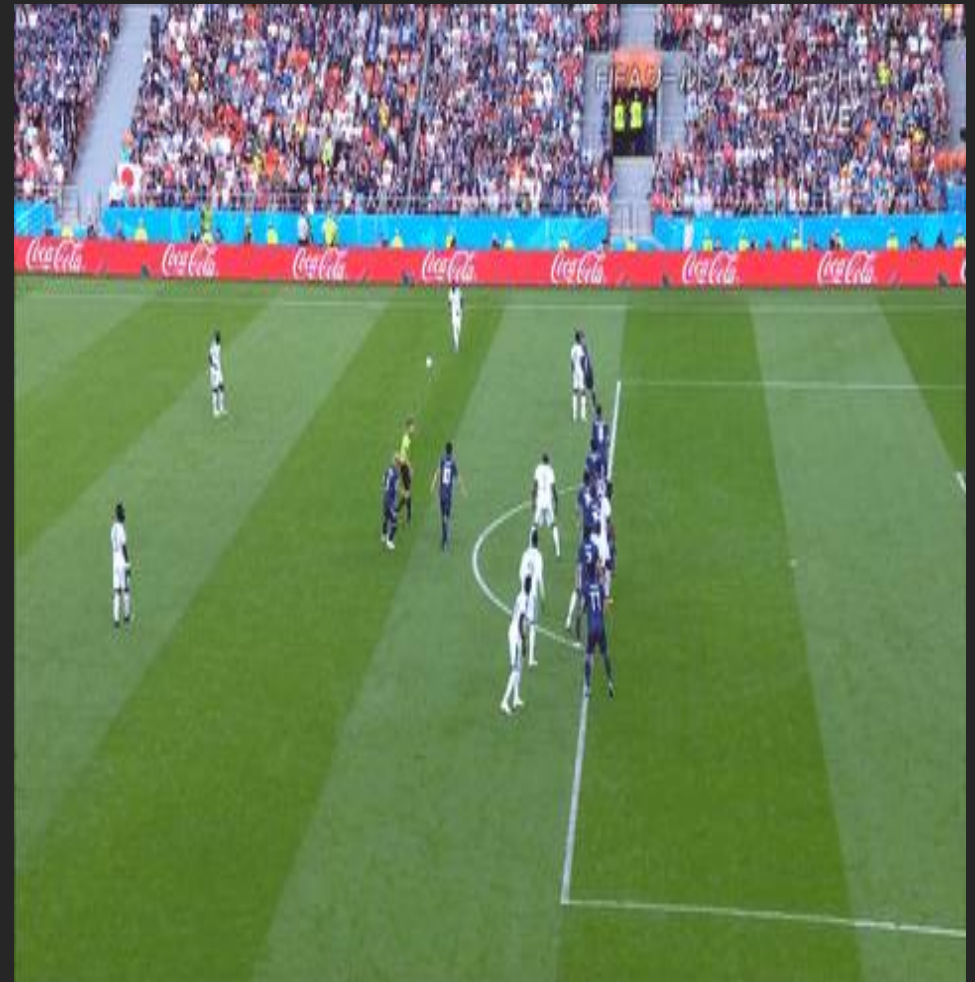



Not being caught Infront the defense line

First, when we talk about the "defense line for the worker," most people think it refers to full PPE. However, it's important to remember that PPE is the last line of defense before an injury or accident. Before the PPE defense line, there are other crucial lines and processes.

We must ensure that the task is approved and ready for action, that all relevant approvals are in place, and that the plans are accurate and detailed. It's essential to verify that the workers have received the appropriate training before the task, ensuring they are aware and prepared for any scenario, including emergencies.

Additionally, the work area and work route should be thoroughly checked before starting the job.

Don't allow yourself or the workers under your supervision to be caught Infront the line of defense. The consequences could be catastrophic, as a lack of knowledge, tools, or proper task management could be dangerous.

HCC/EHS Weekend Work- 06.12.2024

White Board Meeting in Beavers at 06:30

Superintendents

Michael Carpenter 052-7583027

Sahar Samin 052-2759653

Netanel (Nati) Grably 054-4887622

Eyad Abd Al Wely 052-3287236

CSA CM

Nikol Loboda 052-3124965

Ben Tayar 052-3173040

Dana Chelly 052-4729048

MEP

John McCrudden 052-3756957

Hillel Mashiah 052-6175084

Michael Ohehir 052-4168879

OSM

CX/QA

Raymond Griffin 052-6941063

Cranes

Maksym Panov 055-9181086

Safety

Safety Foreman - Rami Al Jaar 052-6169466 Rami-AlJaar@Hoffmancorp.com

Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com

Safety Professional- Loay Alamour-053-2557899

Subcontractor Weekend Work- 06.12.2024

FAB

Utility Level / Roof / Stair Shaft

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

SK

Ehs Om 0542072285

Foreman Shy 0545654760

Subfab

Pach Taas

AHw Ducts.

AMw+AXe Wall Penetration

Nethanel 0543301880

Afcon E

TTN ,MARSES

Avi Eli 0526008487

Chemo

TTNE RSTM

Tommy: 0523759408

SELA

MOD2

Yuvel: 0502649246

Clean Room

Talad – fun deck – greetings Install, 4E

Grating (EHS Mati s. 050-4887477, Super Igor 0544509386)

Sig – 10 GUYS 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)

Elram – CR Level 9,25 line columns , upper shaft wall, FOREMAN SHAY LEVI - 0523632132 (Bonio 0544236899)

Afcon – CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pulling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Rolling Plains – 22 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super Cordin 0546594273, EHS Ovidiu 0546993648)

Chemo –30 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)

Talent –12 GUYS CR Level 1E– Superclean (Supervisor YOSSIEHS –052-6557130 EHS RAVID SHRAGA 050-7111588

Sela – 2E CRC (Supervisor Yuval VANUNU 0502649246, EHS SHMUEL KUSHNIR - 0506306031)

PACH TAAS- LINK - FOREMAN NATANEL 0543301880 SAFETY OFEK - 0507838486

Subcontractor Weekend Work- 06.12.2024

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2 1-3P

Foreman – Vadim – 053-5552472

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-5P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

W&W – 138 Grating (lift 3 5P)

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Elram – 3P and 4P Exit Passage Ceiling

Foreman – ???

Safety – ???

HSAl – 1P Scrubber Containment/TC3 @ Roof

Foreman – Dave – 052-4121028

Safety – Hiam

Lesico – H2 Vent/BGY

Foreman – Saju Paily – 052-7755967

Safety – Shilat – 050-05891373

HYG – AA/5 Rack and BCD Grating

Foreman –

Safety –

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

WJG

W&W – grating / Detail Work

Foreman: Chris

Safety: Tony

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 5J Lift 2 Piping

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

SK: Lift 2 Piping

Foreman: Taufik: 054 94333592

Pach Taas: All over

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

Subcontractor Weekend Work- 06.12.2024

CUB

D&P CUB 2:

Constantine – 0545501602

David – 0548894447

Chemo Aharon CUB 1:

Eli – 0549966318

Leonid – 0548883878

S.K.E CUB 1:

Reynato – 0548991623

Marzuk – 0548830263

Sami Najami CUB 2:

Husein – 0526917461

Alon – 0509895008

HSAI Yards:

Sergey – 0552728807

Trestle

PIPES – 20 workers UB CUB+ T30

STEEL – 8 workers UB CUB

INSULATION- 11 workers UB CUB

FORMAN

MUCHLES - tel. 0527364996

SAFETY TRESTLE

Alon Matan tel. 050-989-5008

GIS/NEY

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Elmor – Site Lighting

Supervision = Afik: 054-8842825

Olizki – Sweepers and water trucks, offload 18 & CUB1 north concrete PCC

Supervision = Or: 052-4917313

Daily Coordination Meeting



14:00 Sign In
