

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- Trade damage

UTILITY LEVEL PRESS TEST

Lesico
HPOFA test
3/9
From 17:00
till 5:00

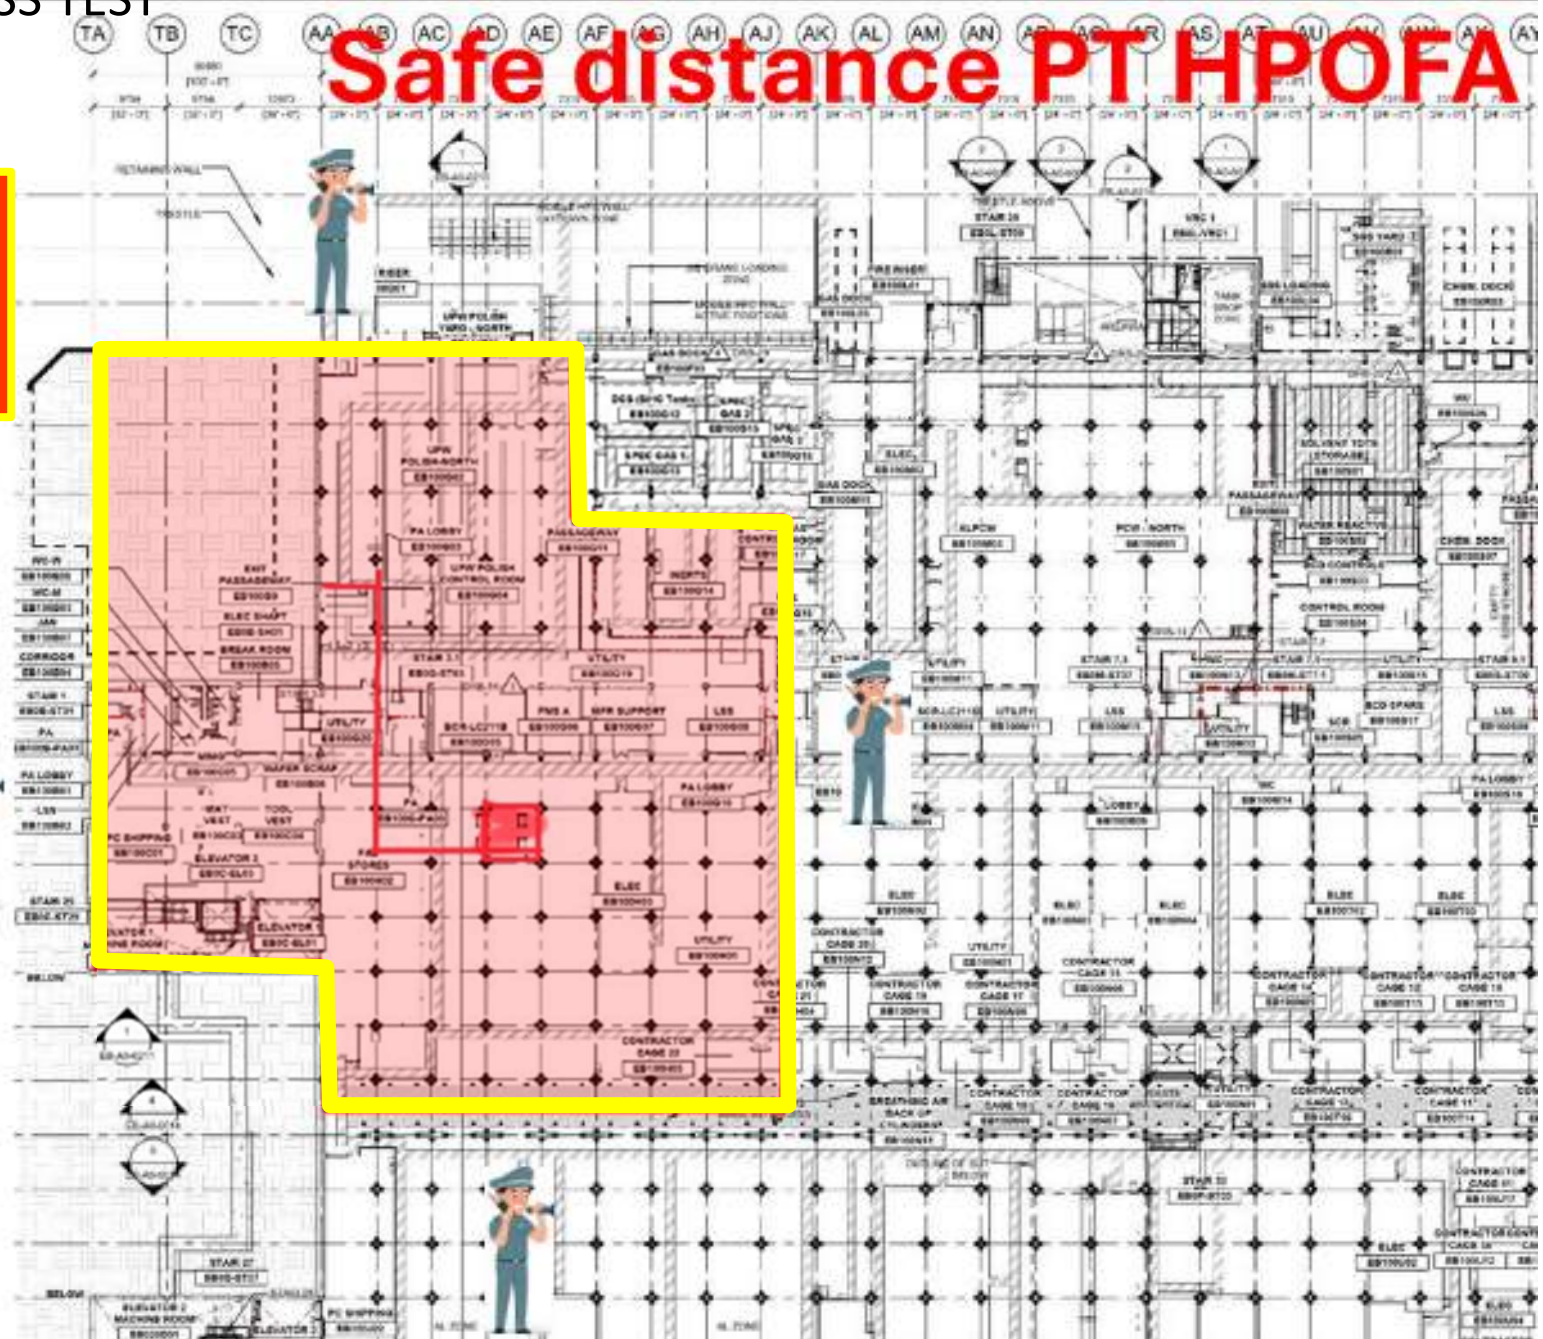



TA TB TC AA AB AC AD AE AF AG AH AJ AK AL AM AN AP AQ AR AS AT AU AV AW AX AY AZ LL BB BC BD BE BF BG BH BJ BK BL CA

08 09 10 11 12 13 14 15 16 17 18 22 23 24 25 26

EB100G01 EB100G02

SK TTNE WC'S design walk statuts

ELRAM ERT roof Stairs 7.1 Chem stag TTNW OH door Break room E

TZUR ESH PCD Bathtub Done

COMBE PCD Bathtub/pi Waste pipe support

SK
TTNE WC'S
design walk
statuts

ELRAM
ERT roof
Stairs 7.1
Chem stag
TTNW OH door
Break room E

TZUR ESH
PCD Bathtub
Done

COMBE
PCD Bathtub/pit
Waste pipe supports


CARMEL DUCT
Remove duct for RHS install
Till 3/11

HYG
Install RHS
3/10


SamiN
TTNW WC'S
pressure test
ongoing



SUT 38.1 LEVEL

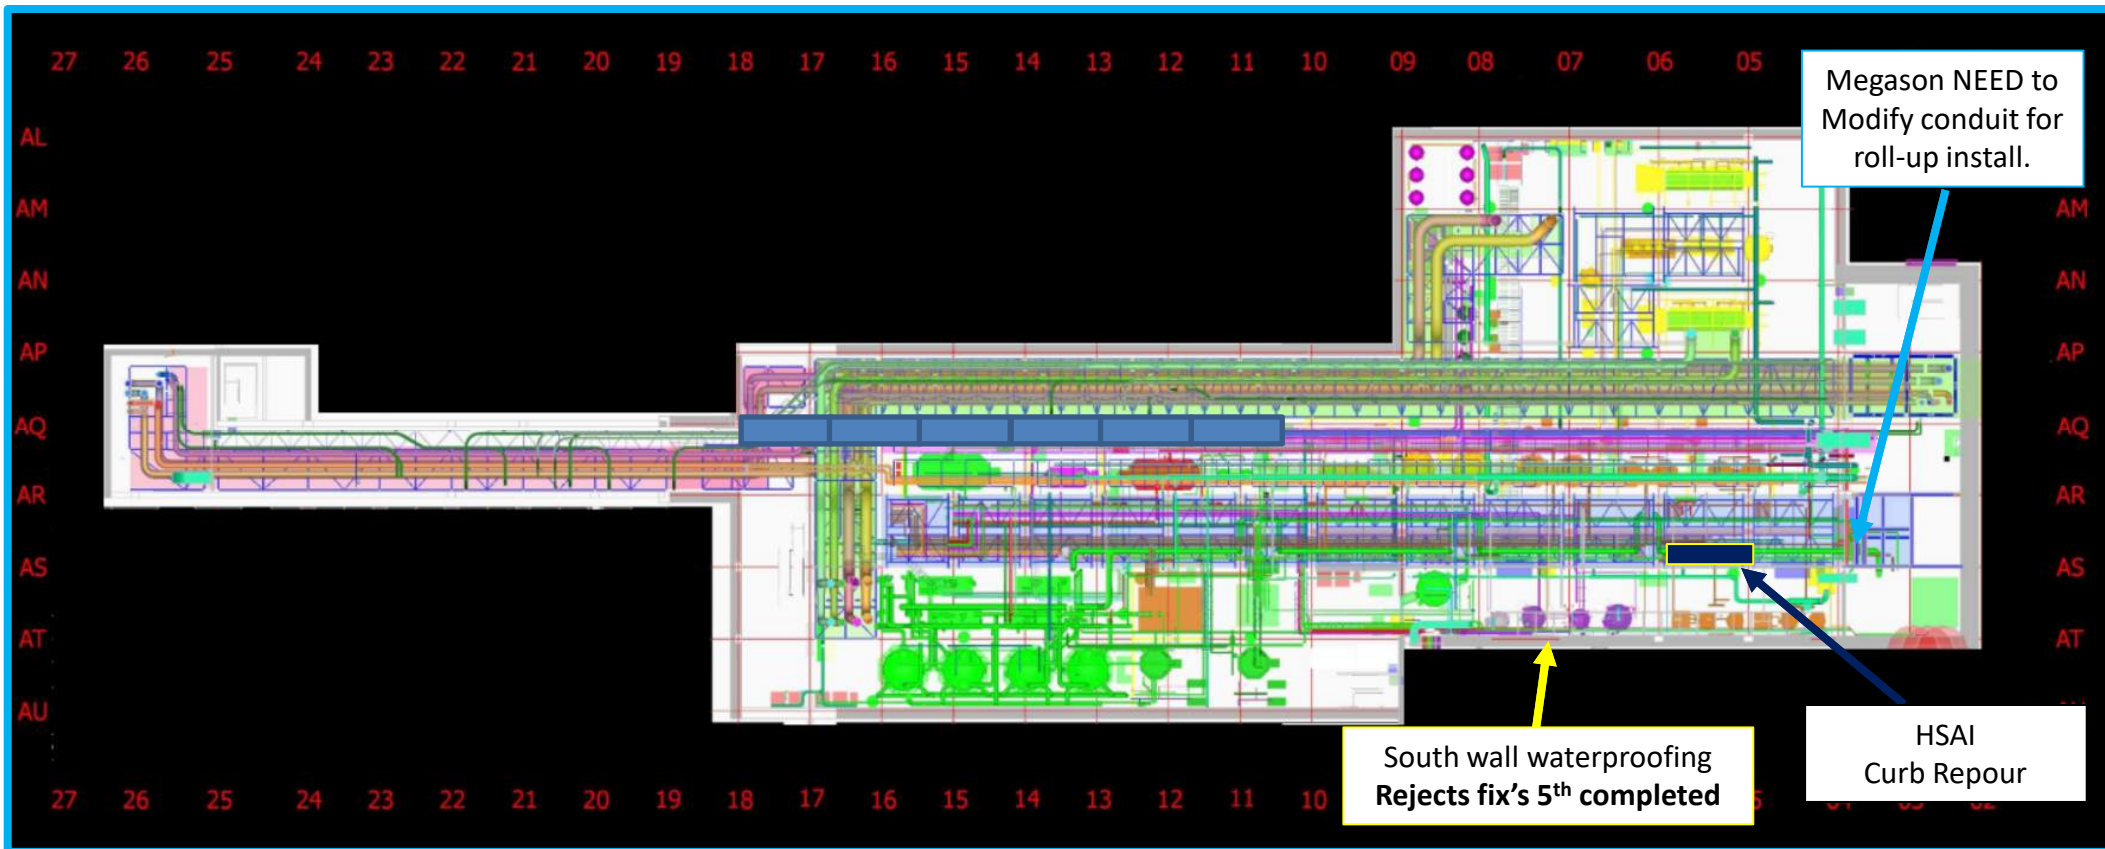

SUT 38.2 LEVEL

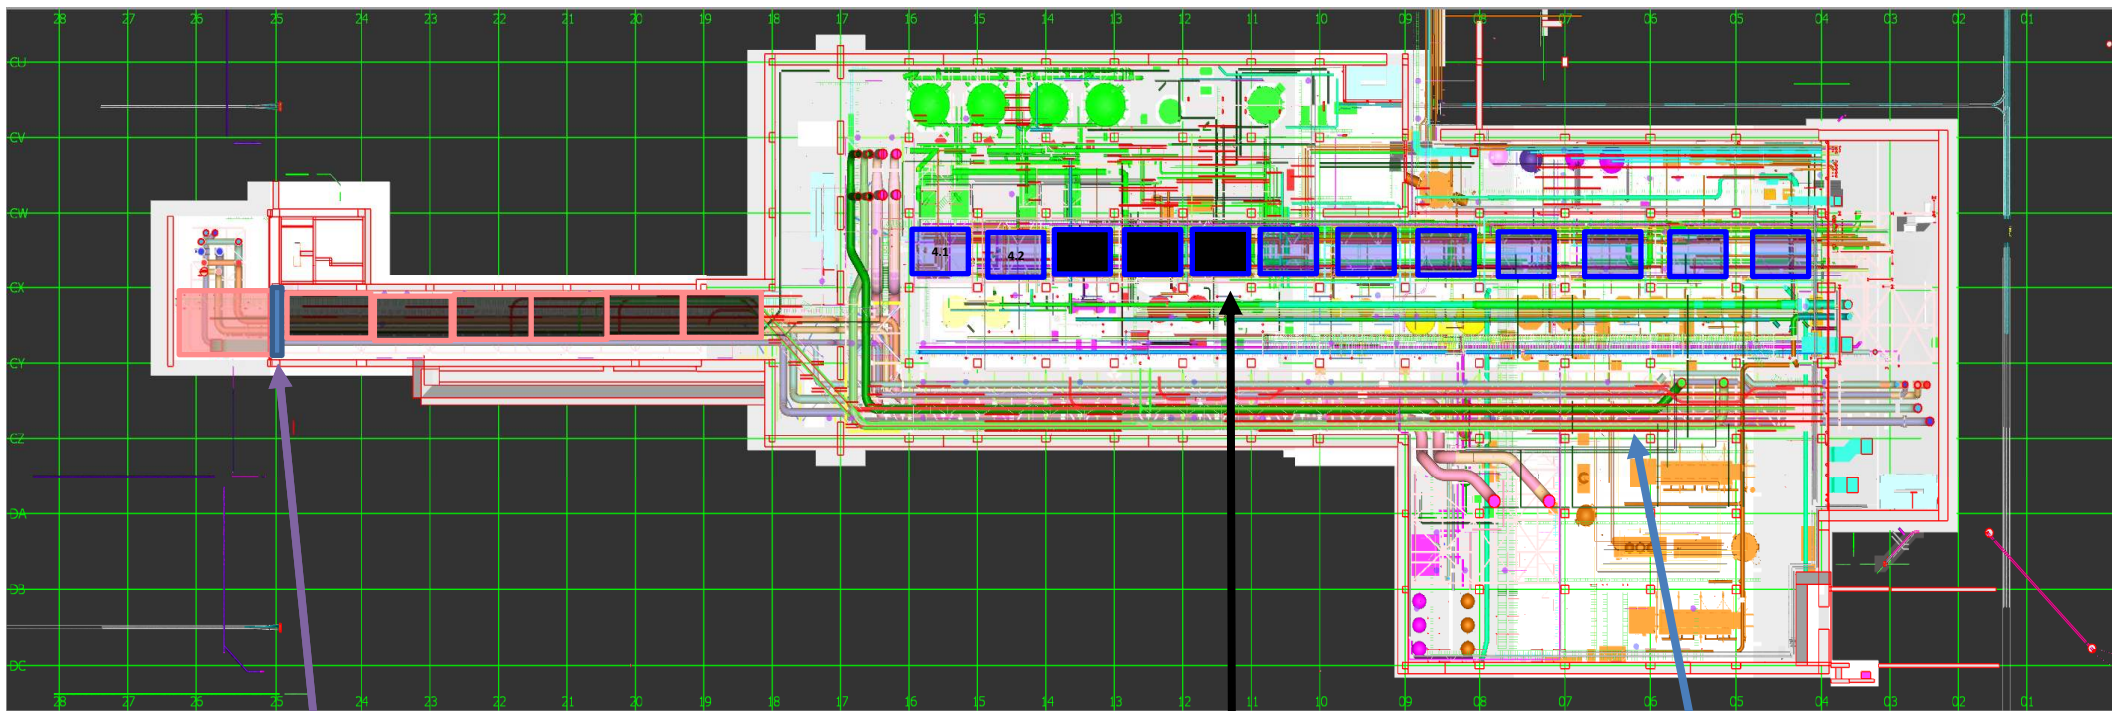


Rack 6
Mep insert conduits
HSAl curb pour start 11th


Rack 4 Upper
Lifting schedule:
M#4.5 – 4/3/25
M#4.6 – 6/3/25
M#4.7 – 10/3/25

Rack 2
Piping
connection

SUBFAB BUILDOUT MOD 1

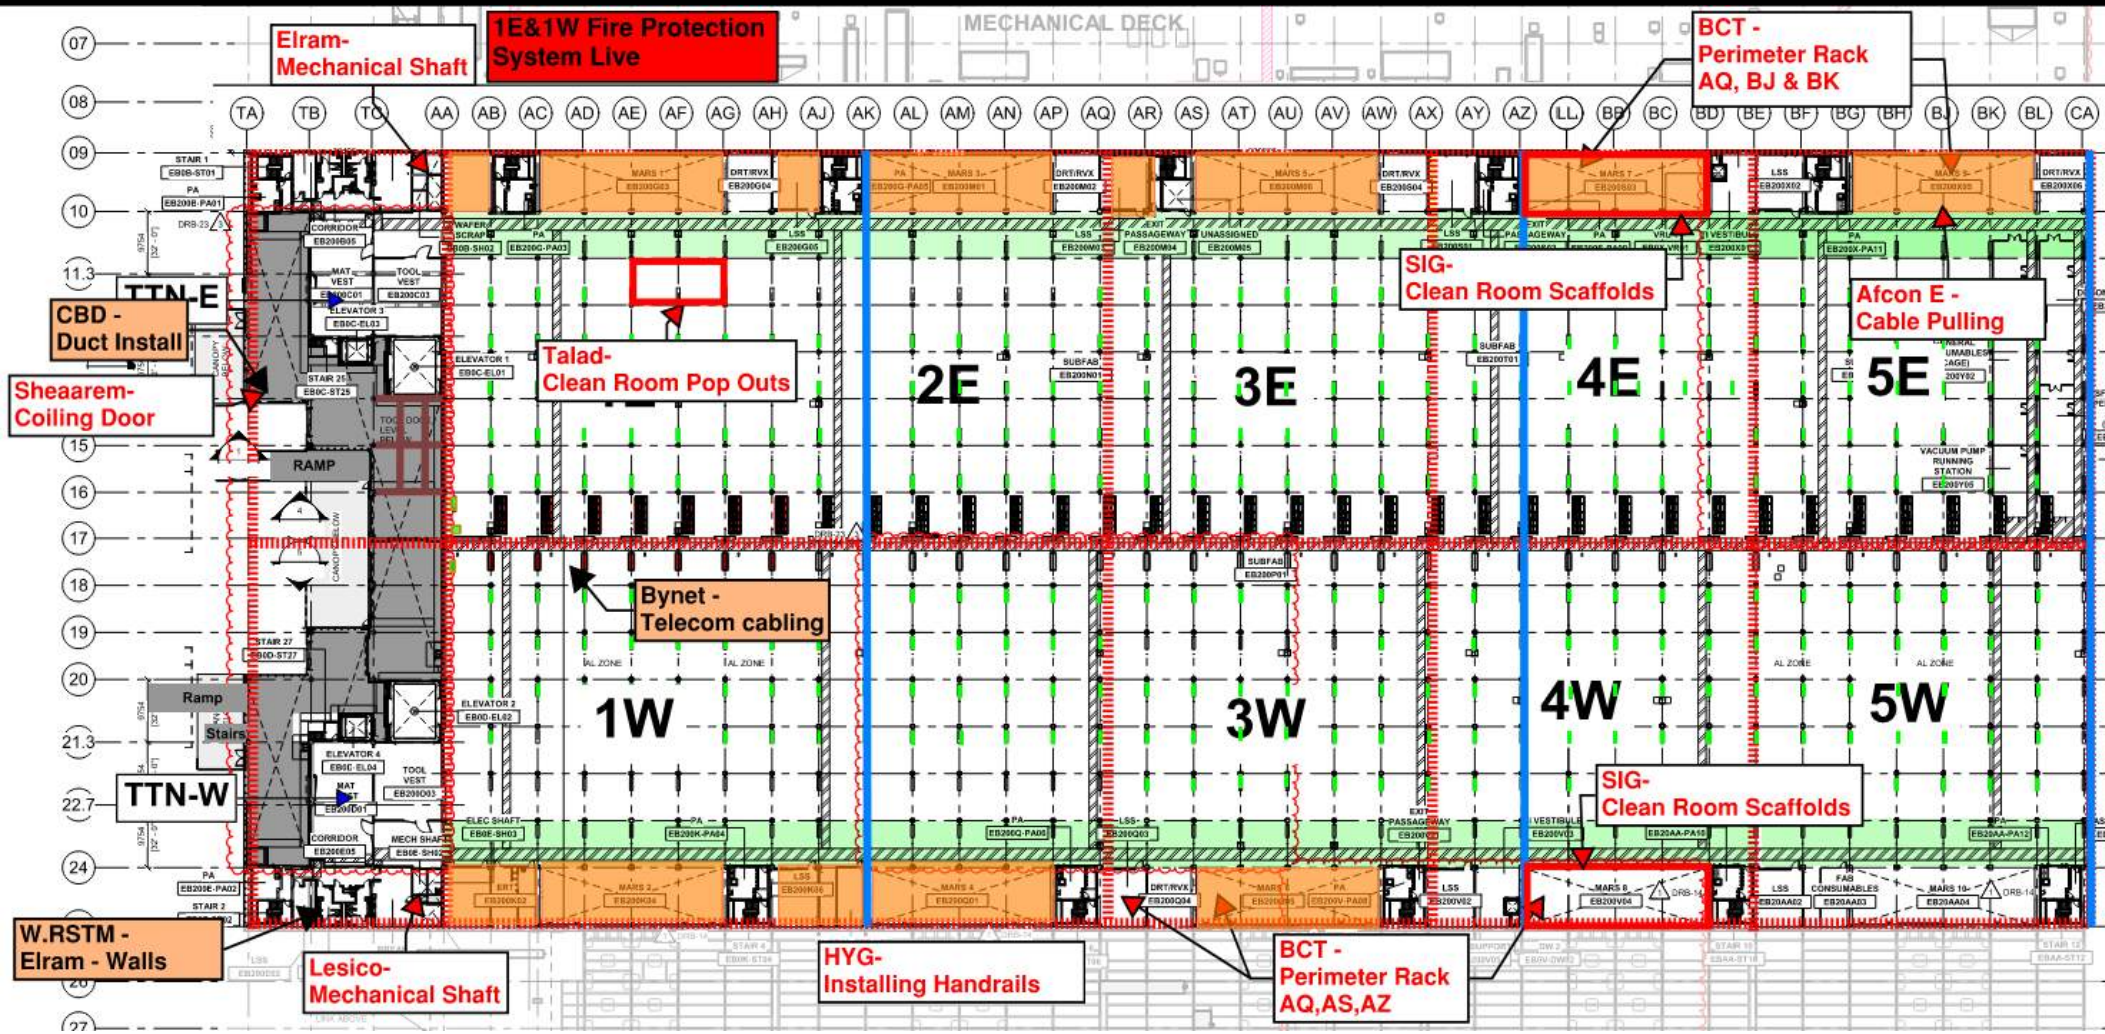



SUBFAB CRC TOPCOAT

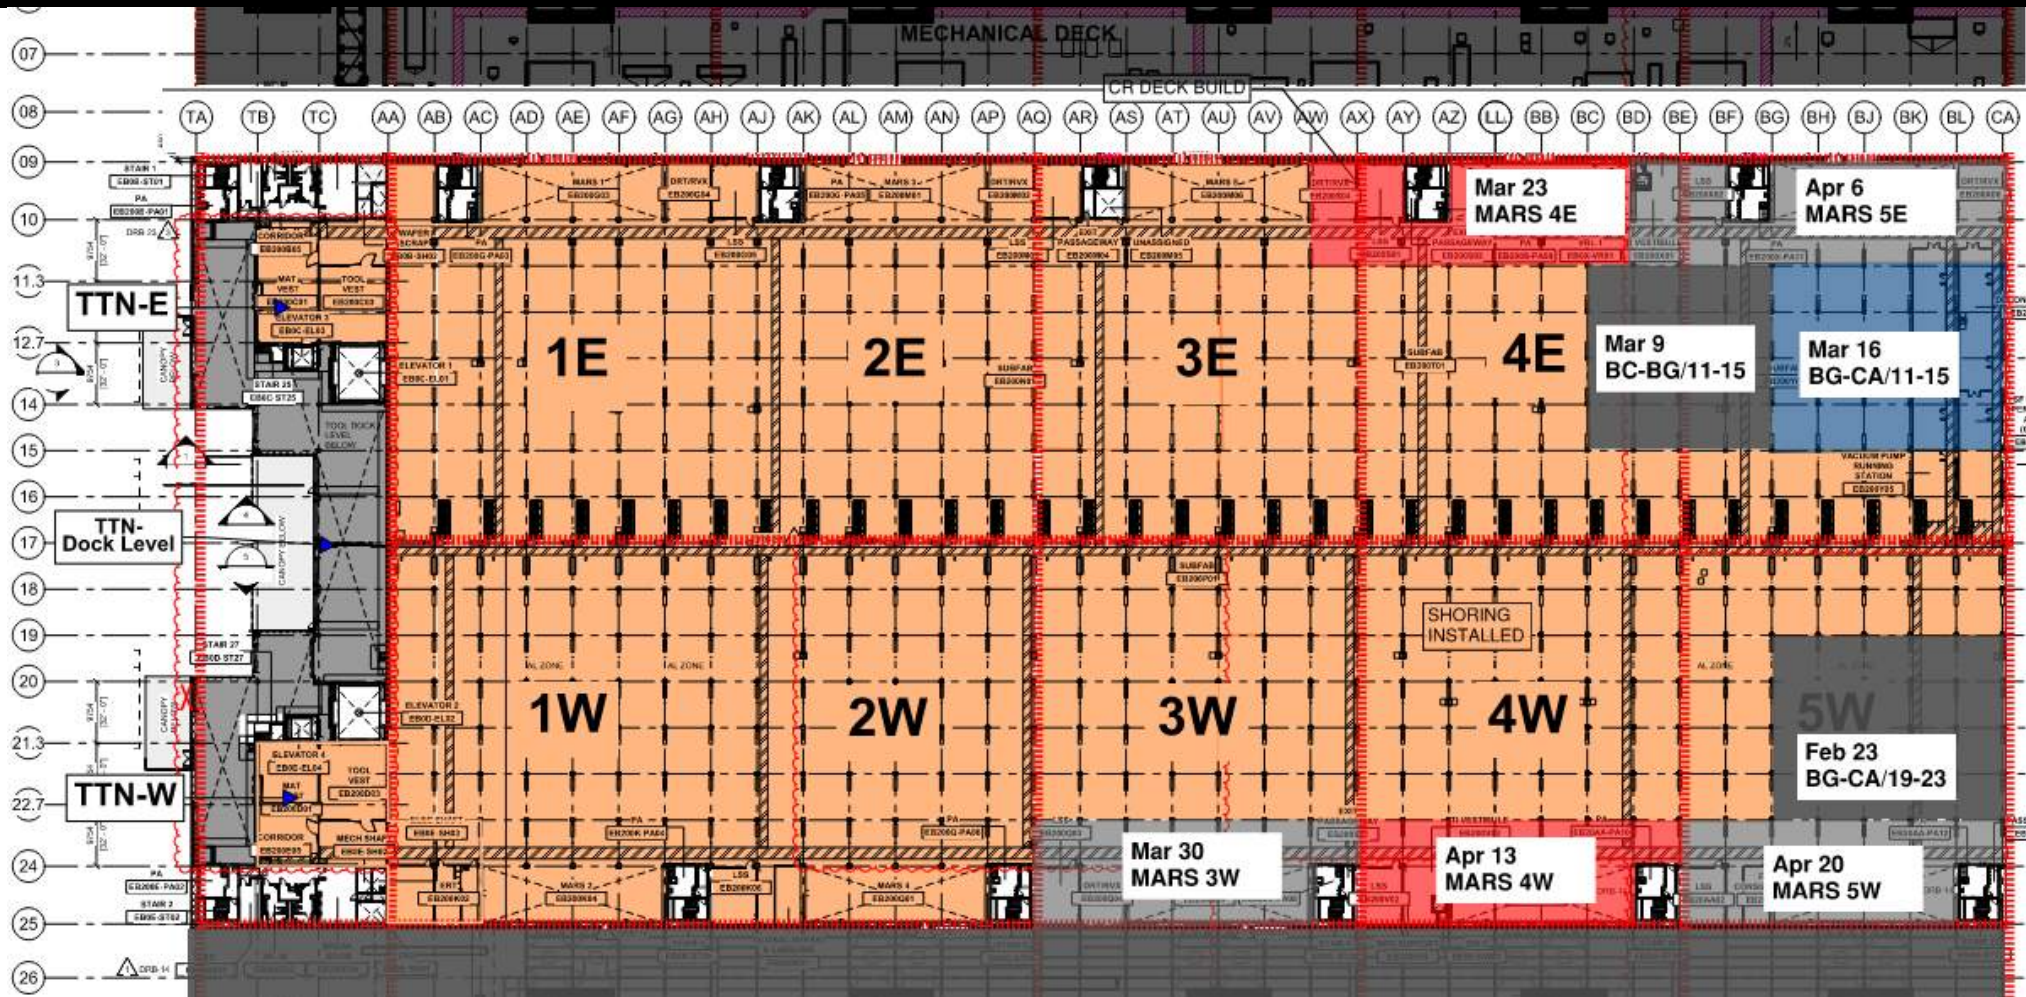


The floor plan displays a grid of rooms from 6E to 10W. Key features include:


- Room Layouts:** Rooms are arranged in a grid, with labels such as 6E, 7E, 8E, 9E, 10E, 6W, 7W, 8W, 9W, and 10W.
- Elevators and Stairs:** Multiple elevator shafts and stairwells are indicated throughout the plan.
- Service Areas:** Includes restrooms (e.g., W.C., M.F.), storage areas (e.g., STORAGE), and other utility spaces.
- Color Coding:** Rooms 10E and 10W are highlighted in orange. Other rooms have different background colors or patterns.
- Annotations:** Various technical notes and abbreviations are present, such as "MGSN - Vesda" and "Allmak".

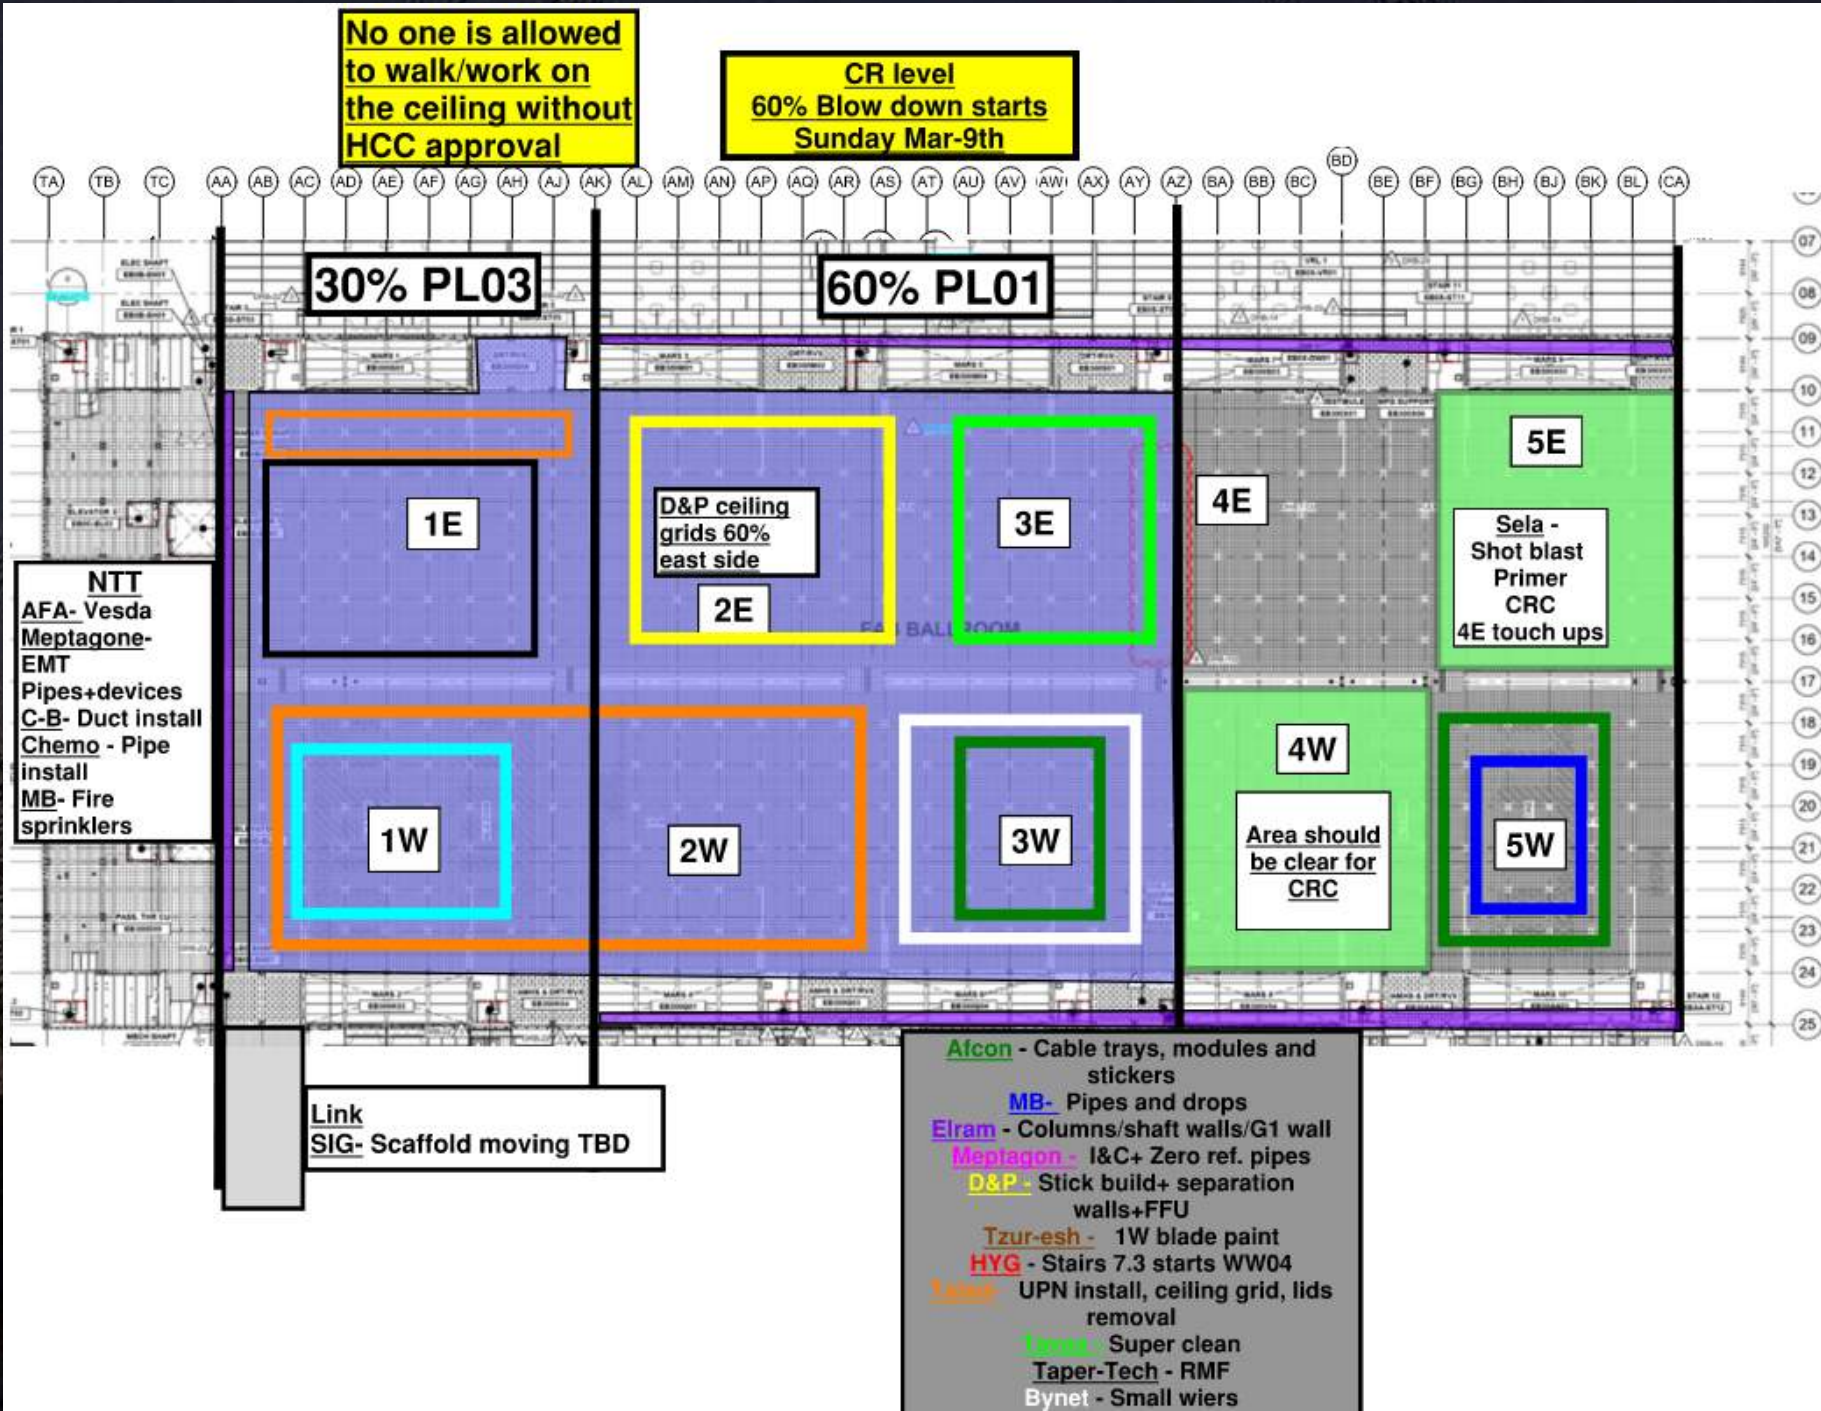

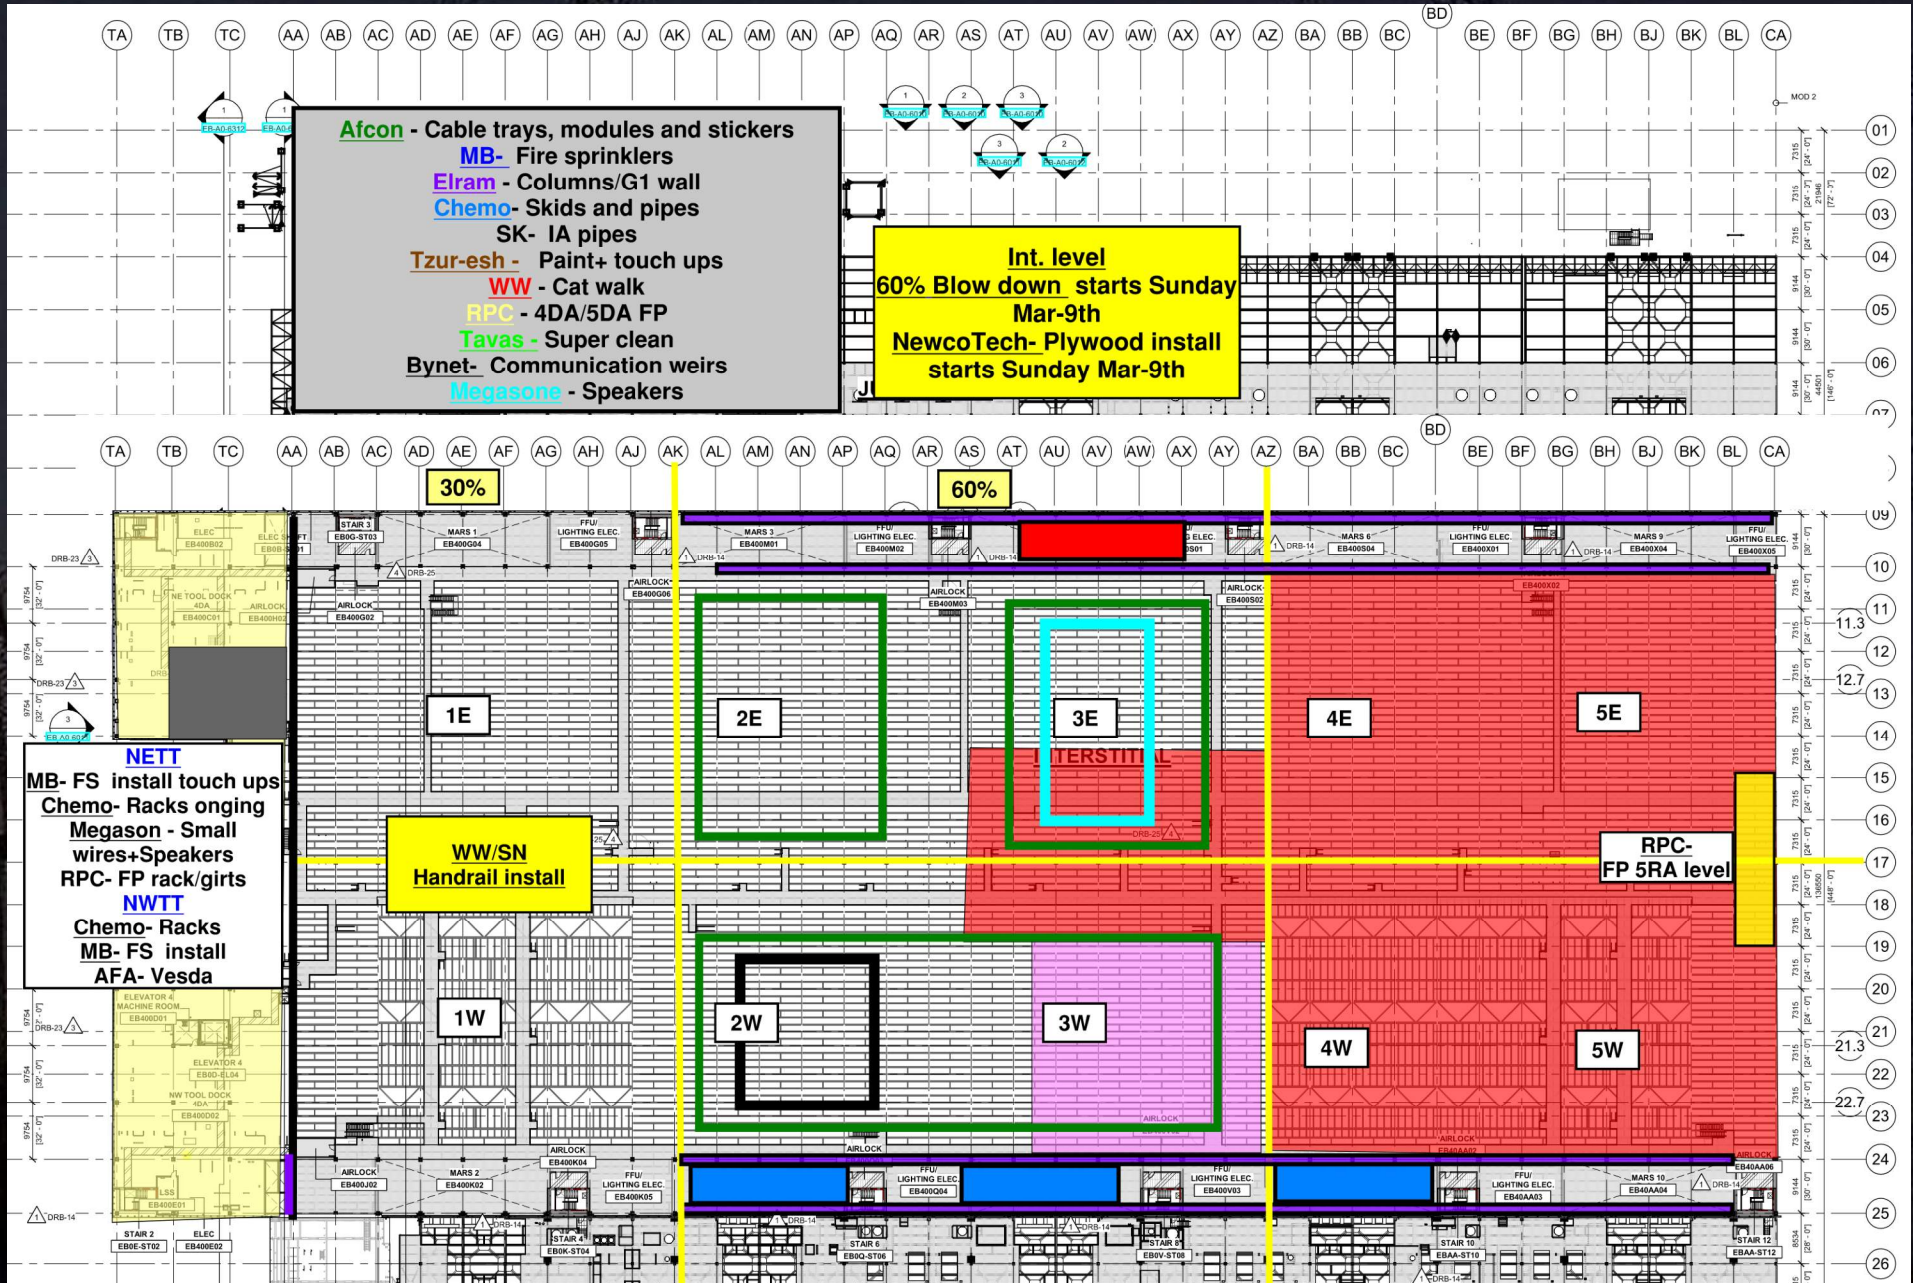


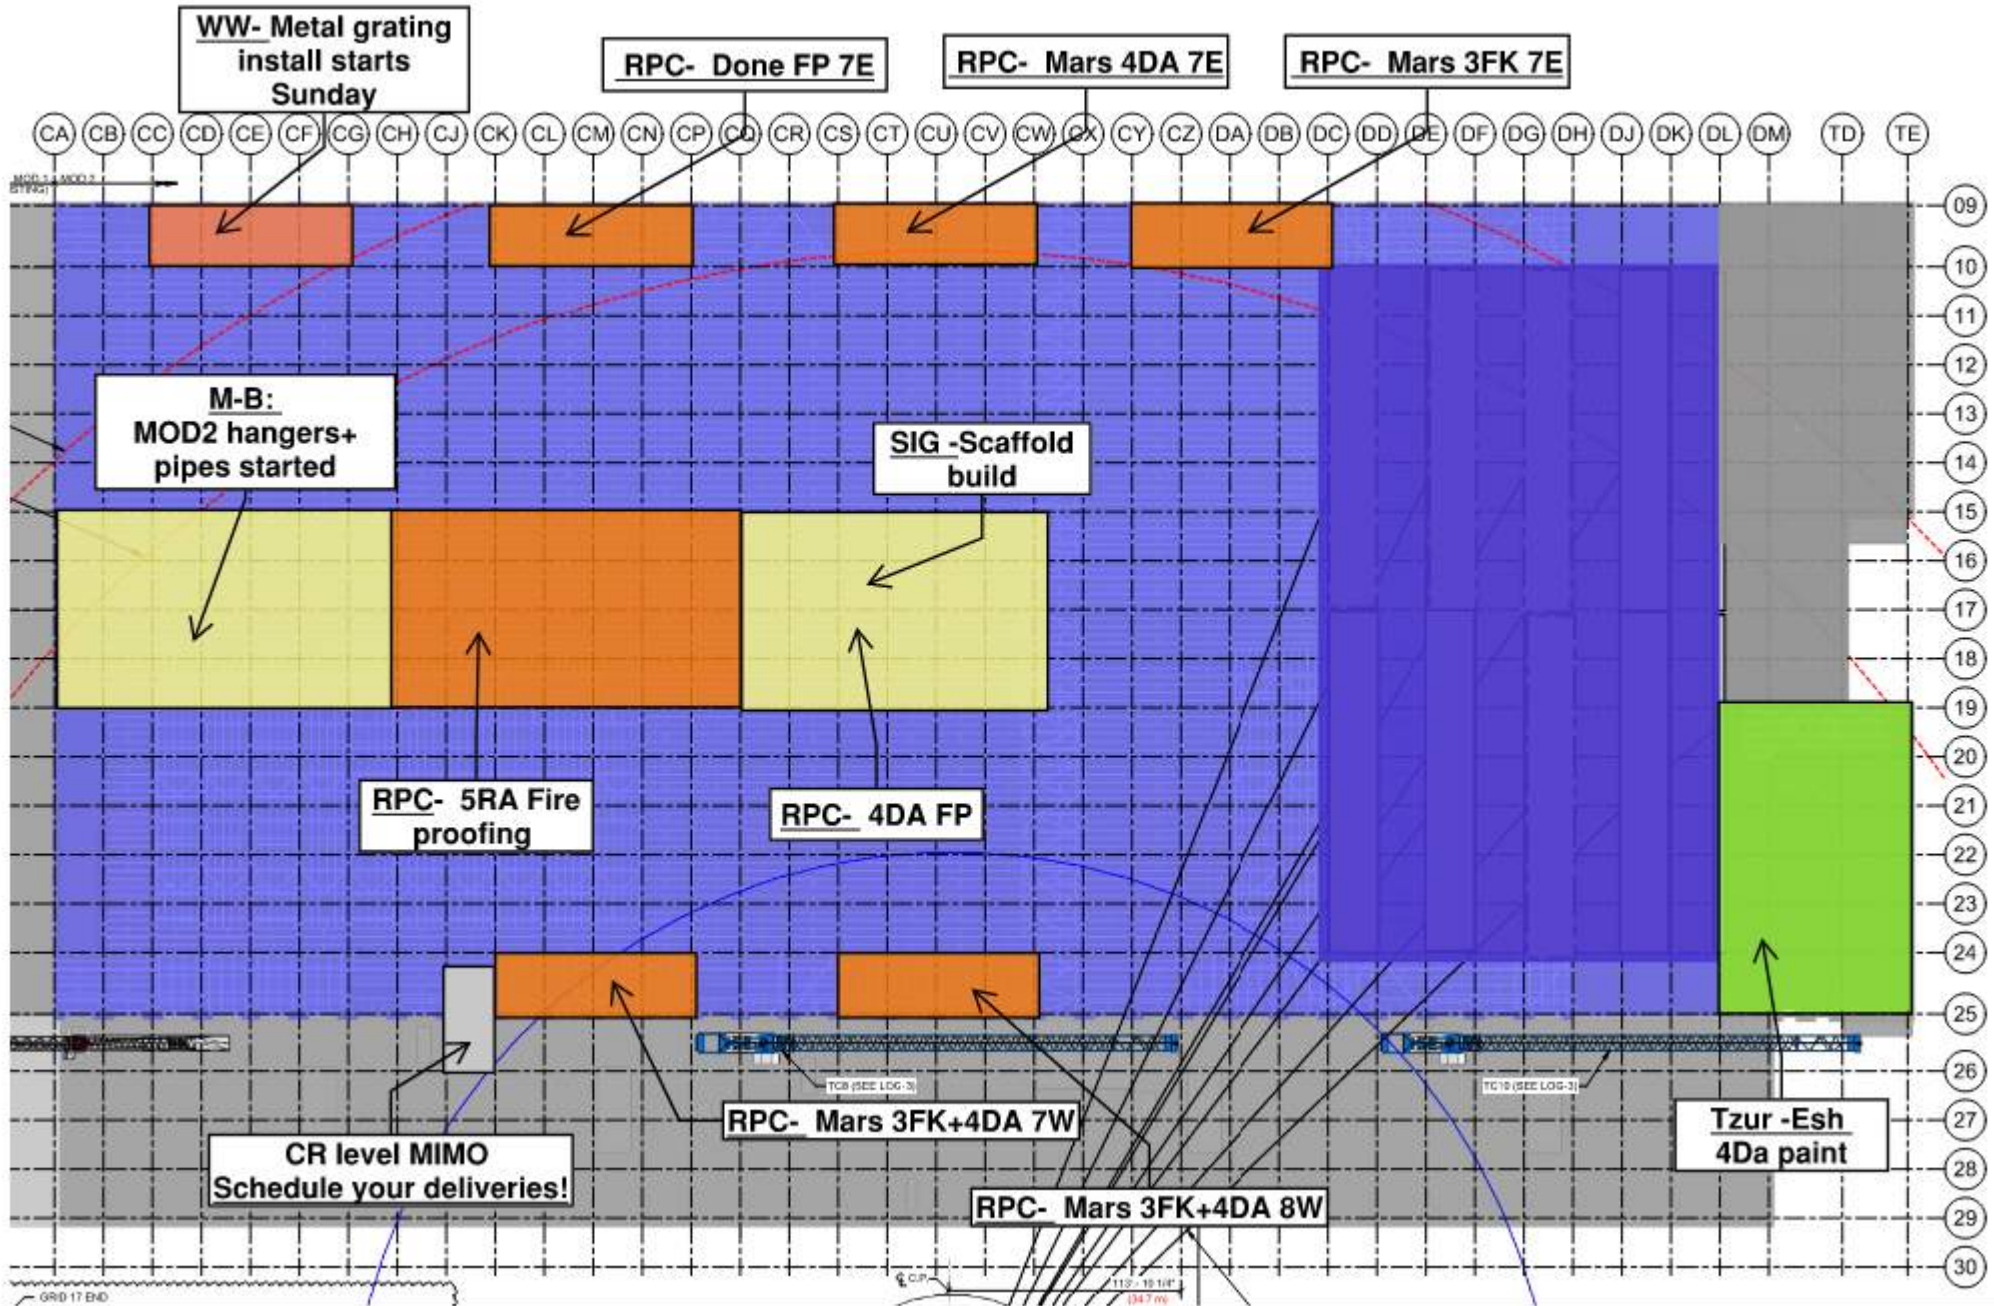

Siding Penetration Request Form



Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

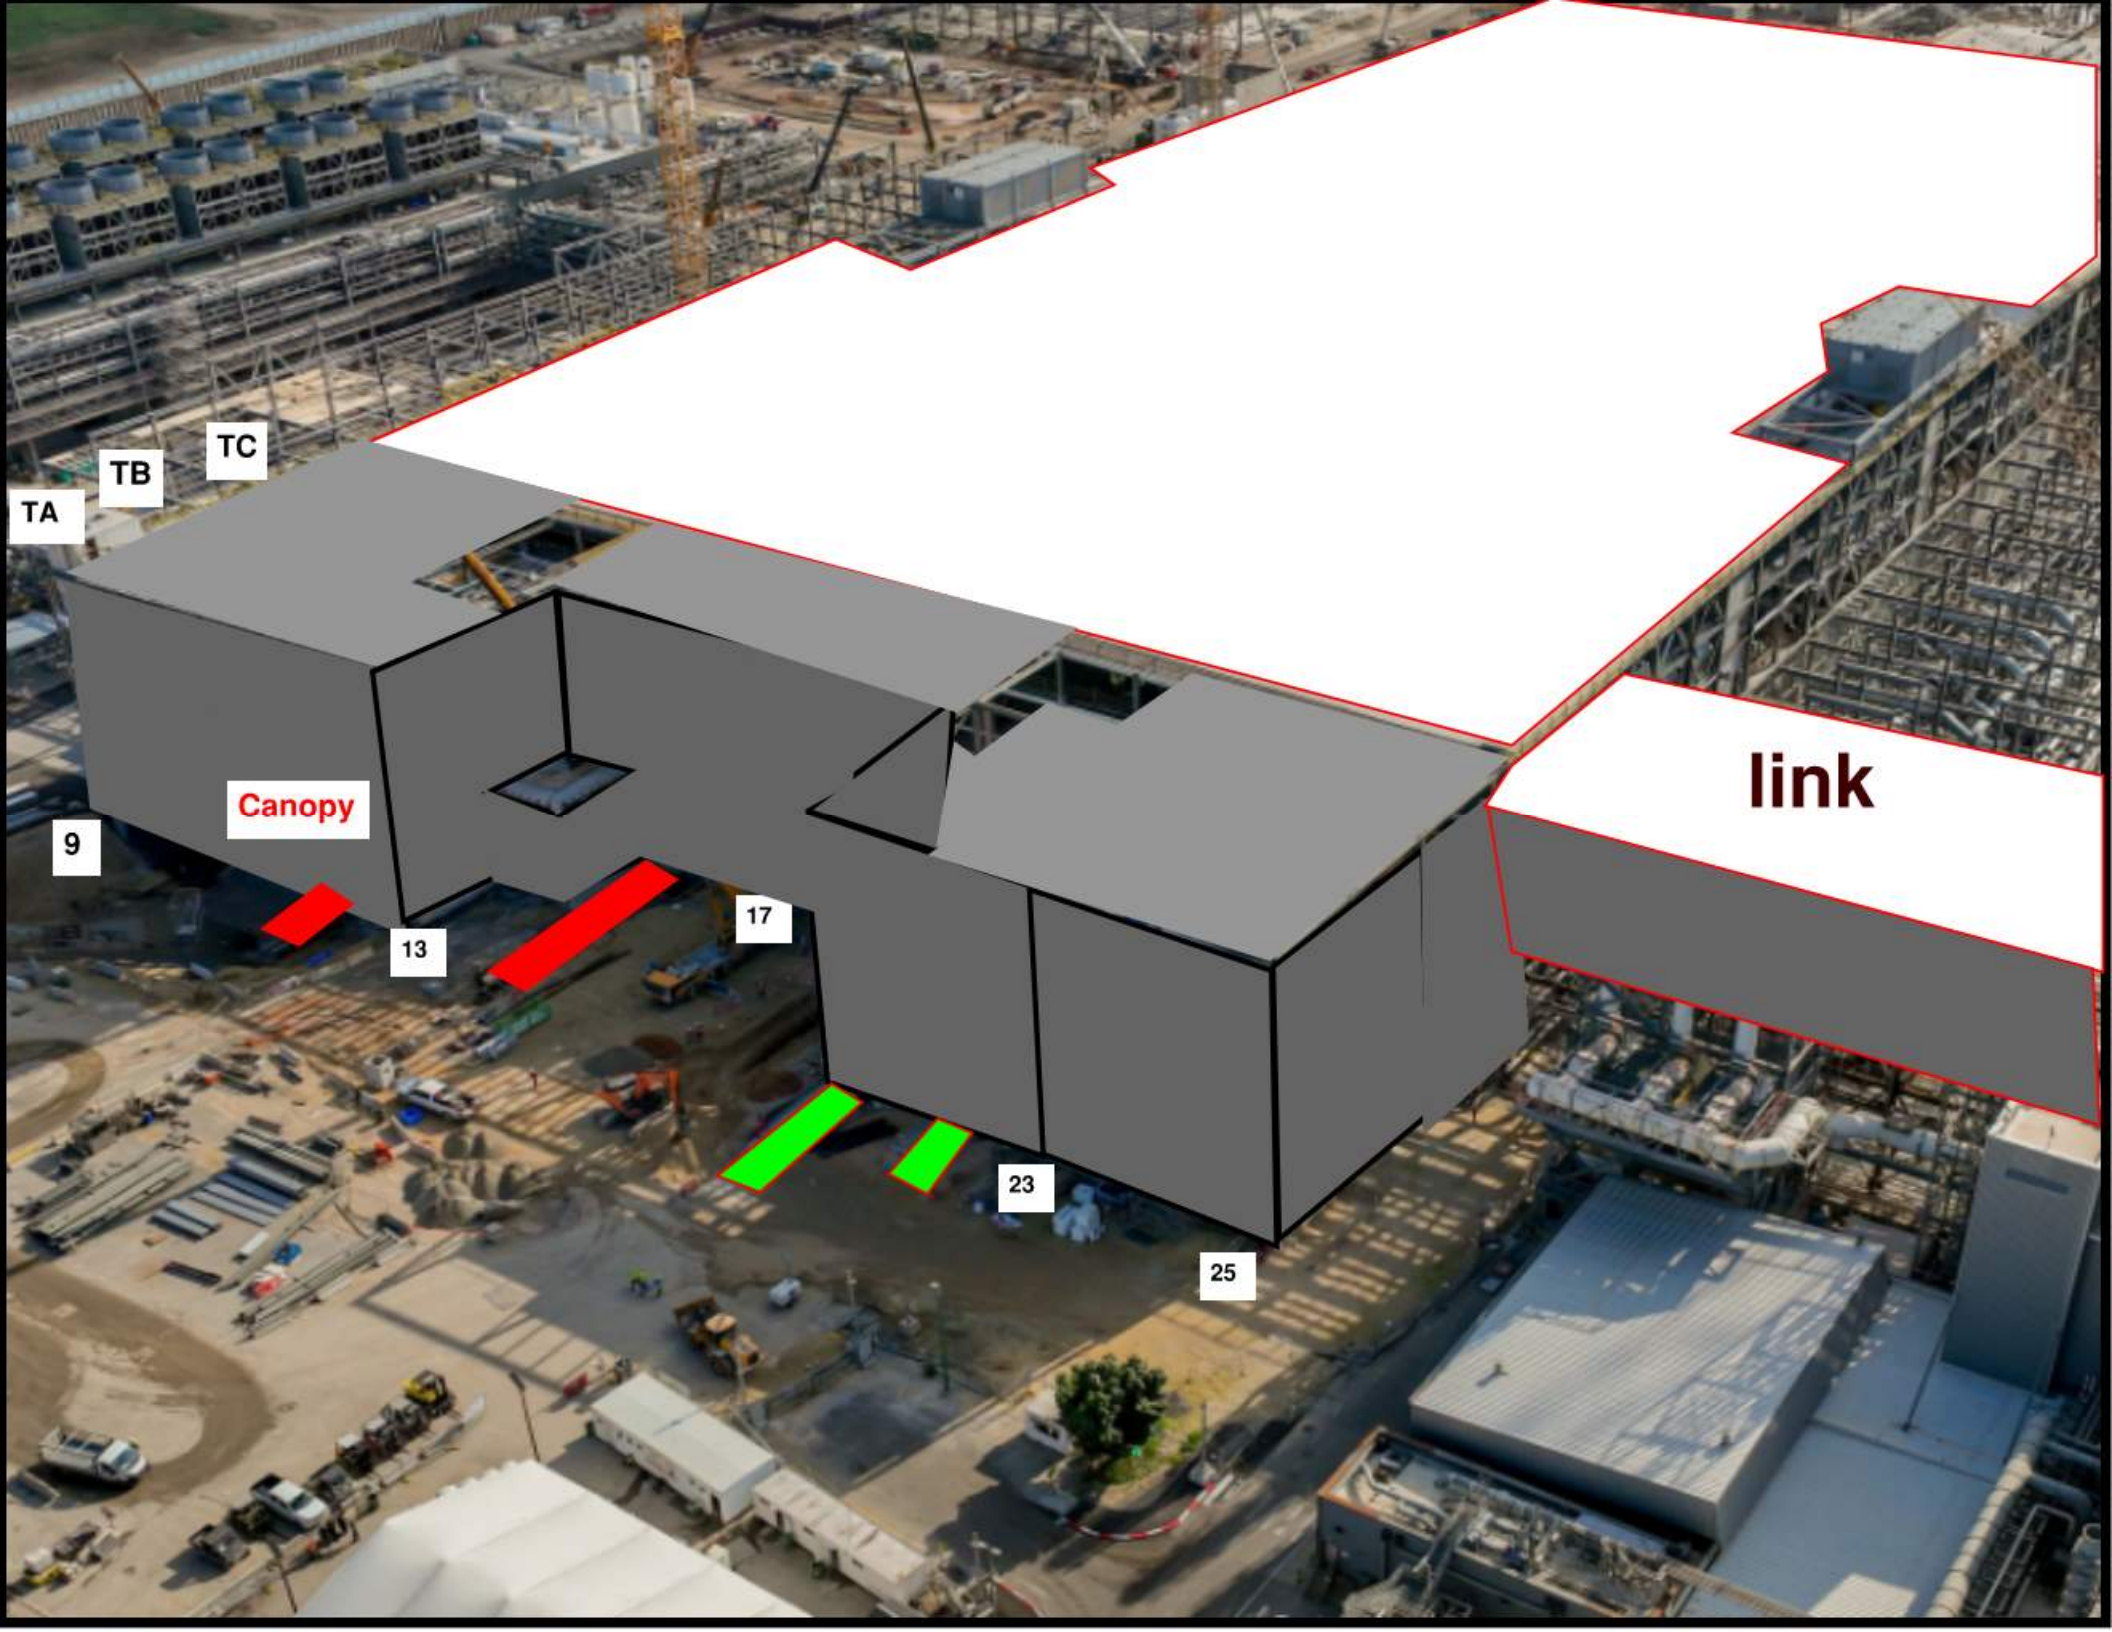

TA

TB

TC

Canopy

9

13

17

23

25

link



MOD 2 EASTSIDE GIRTS/SIDING

2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

MOD 2 WESTSIDE GIRTS/SIDING

READY FOR GIRTS 

INSTALLING GIRTS 

READY FOR PANELS 

PANELS INSTALLED 

2602/
2601

M
I
M
O

2612/
2611

MIMO
2622/
2621

2632/
2631

2642/
2641

2652/
2651

2812/
2811

2822/
2821

2832/
2831


2842/
2841

2852/
2851

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

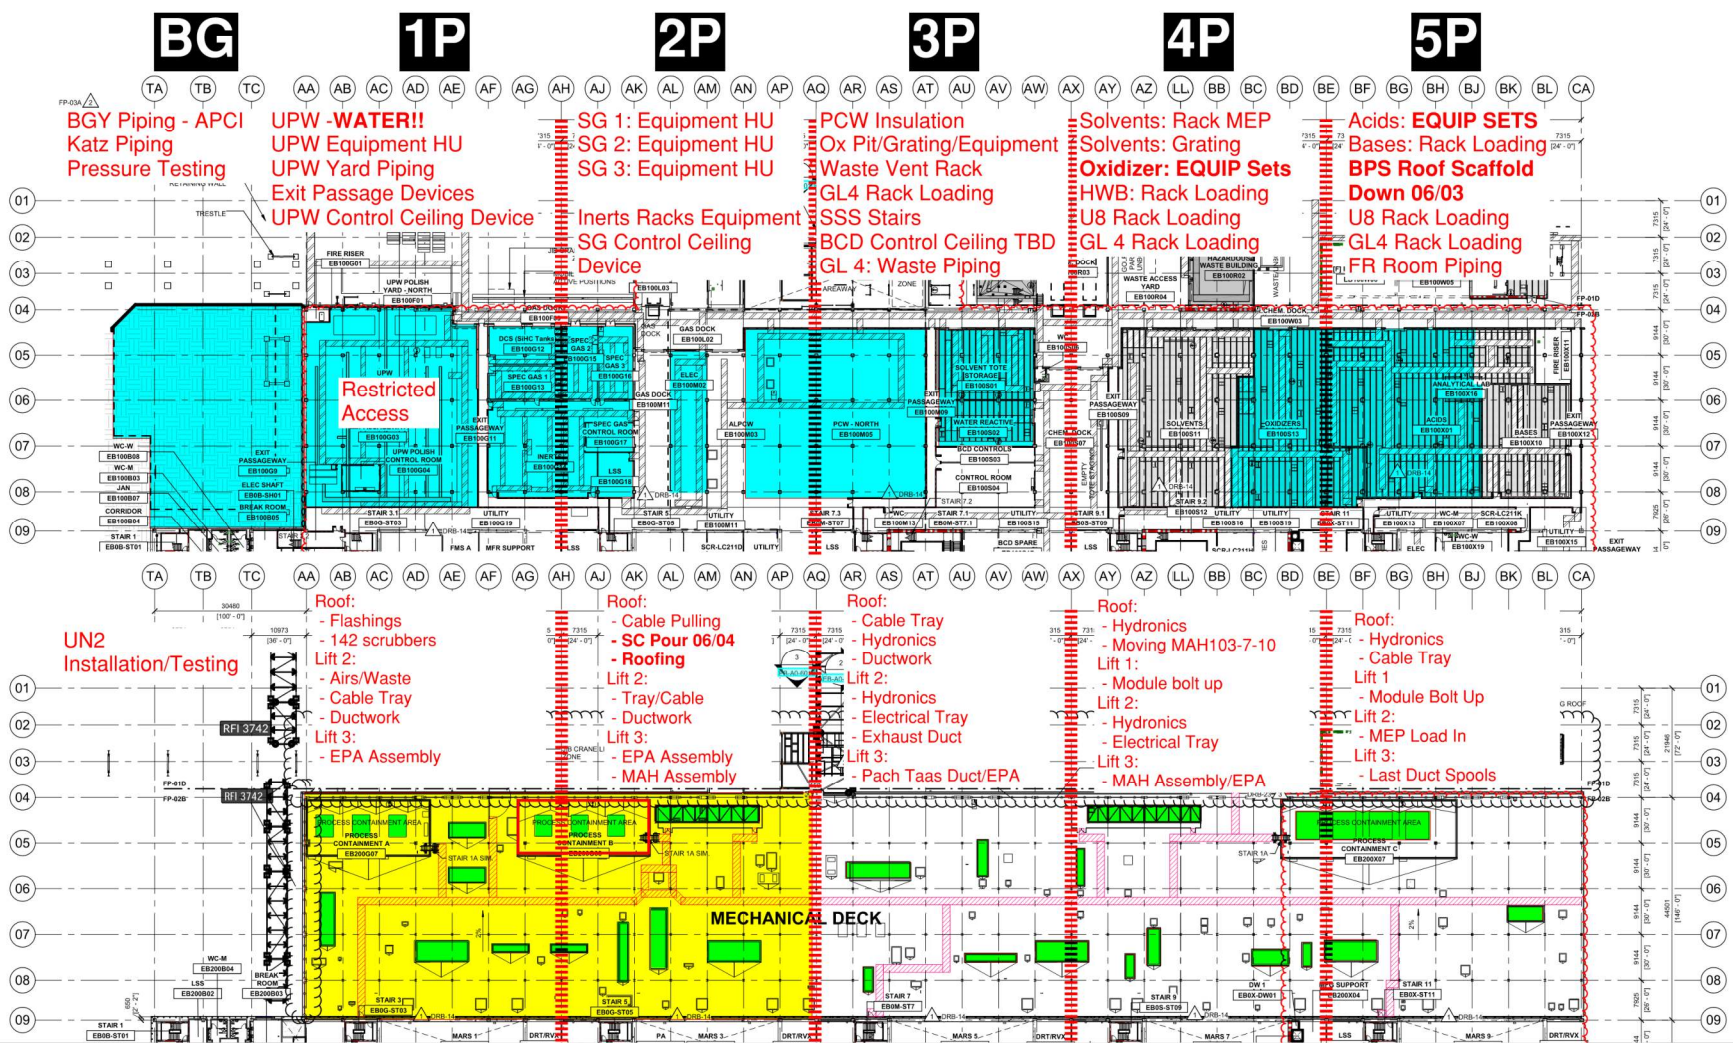

PSSS.2


Utility Level
1YA

PSSS Roof
2SA

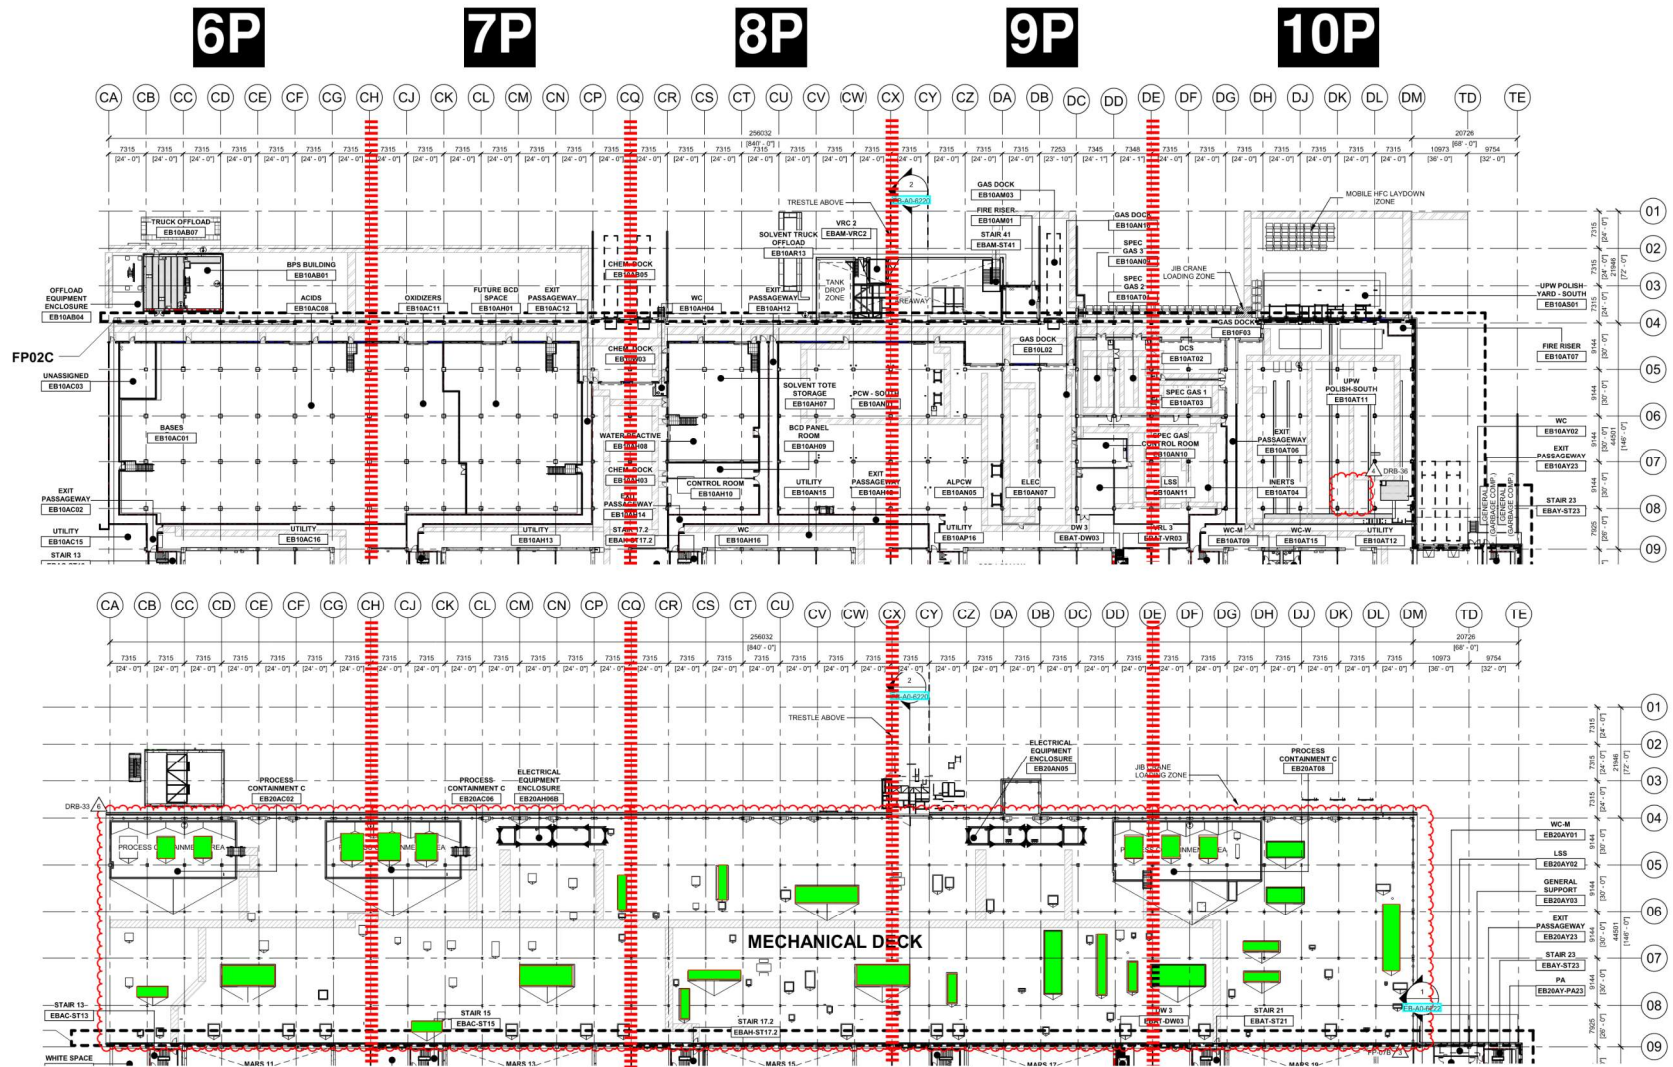

PSSS Pressure Testing

Utility Level
1YA

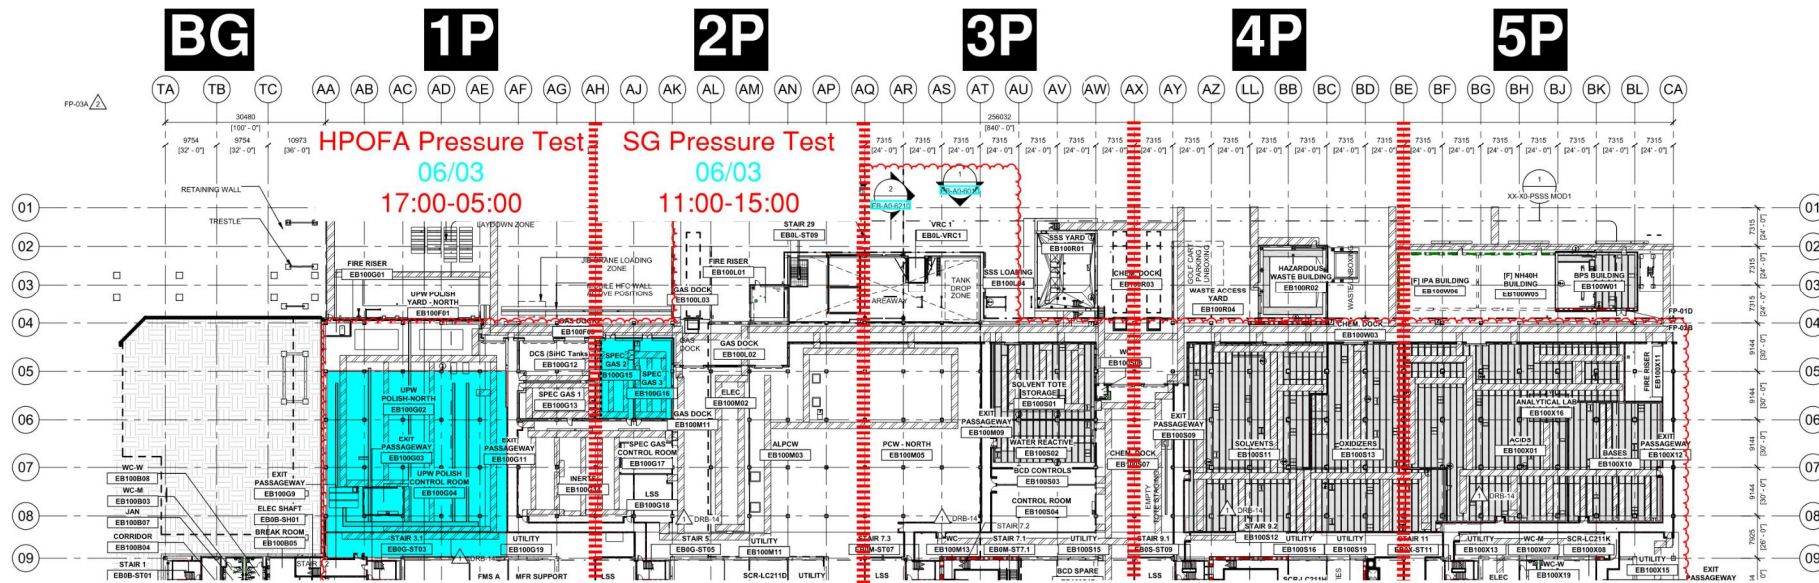

BGY Closed WW11 For UN2 Blowdown



WJG – UL


* Carmel Bidud - installation of ducts from small AH to FAB

* Pach Taas - installation of modules in west SUT.
* Pach Taas - installation of spools to wall panels

* Megason - working on LSS in AS line


* SK - installation of 3" cooper pipe
* W&W - welding of shims for outriggers
* MB - installation of FP pipes to lift 3

* Chemo - performing passivation on UPN 117

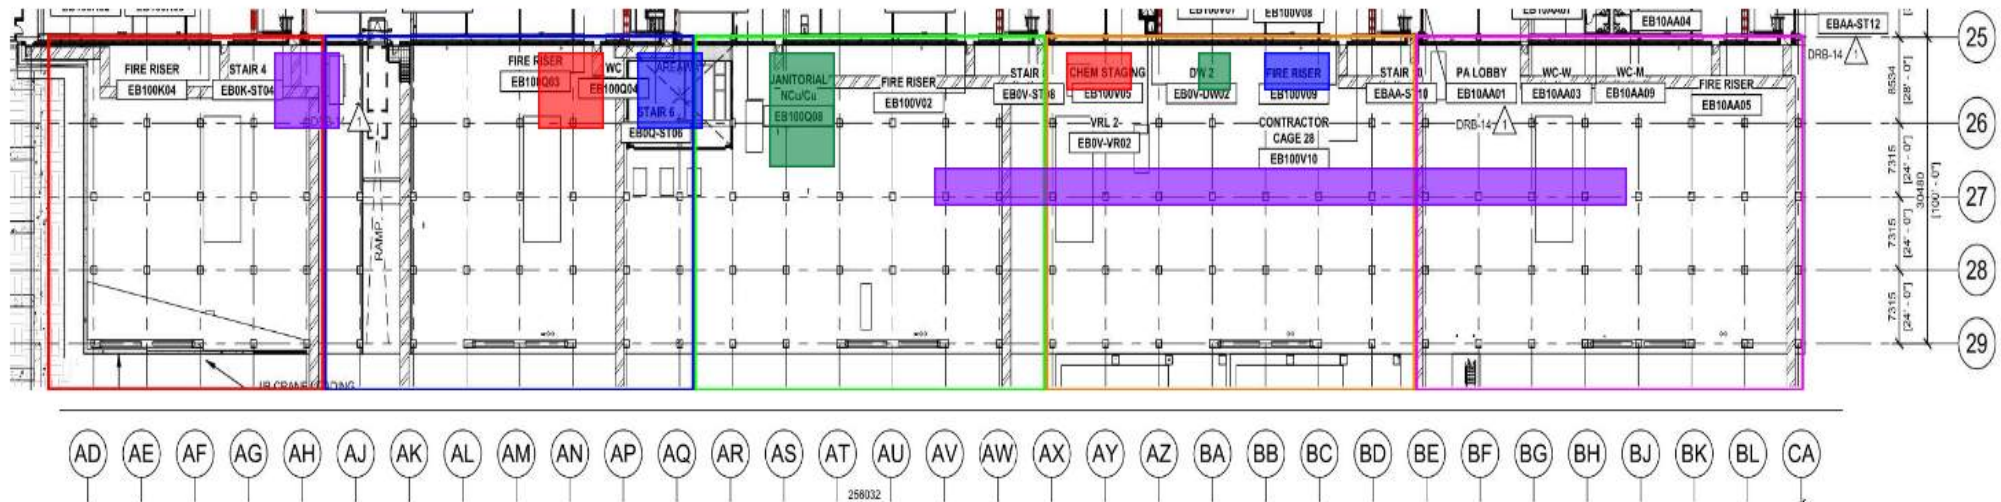

WJG – Lift 2

		* Pach Taas -connection to single stack to exhaust fans	* Carmel Bidud - dismantling MAH scaffold	* Chemo - performing passivation on UPN 117
--	--	---------------------------------------------------------	-------------------------------------------	---------------------------------------------

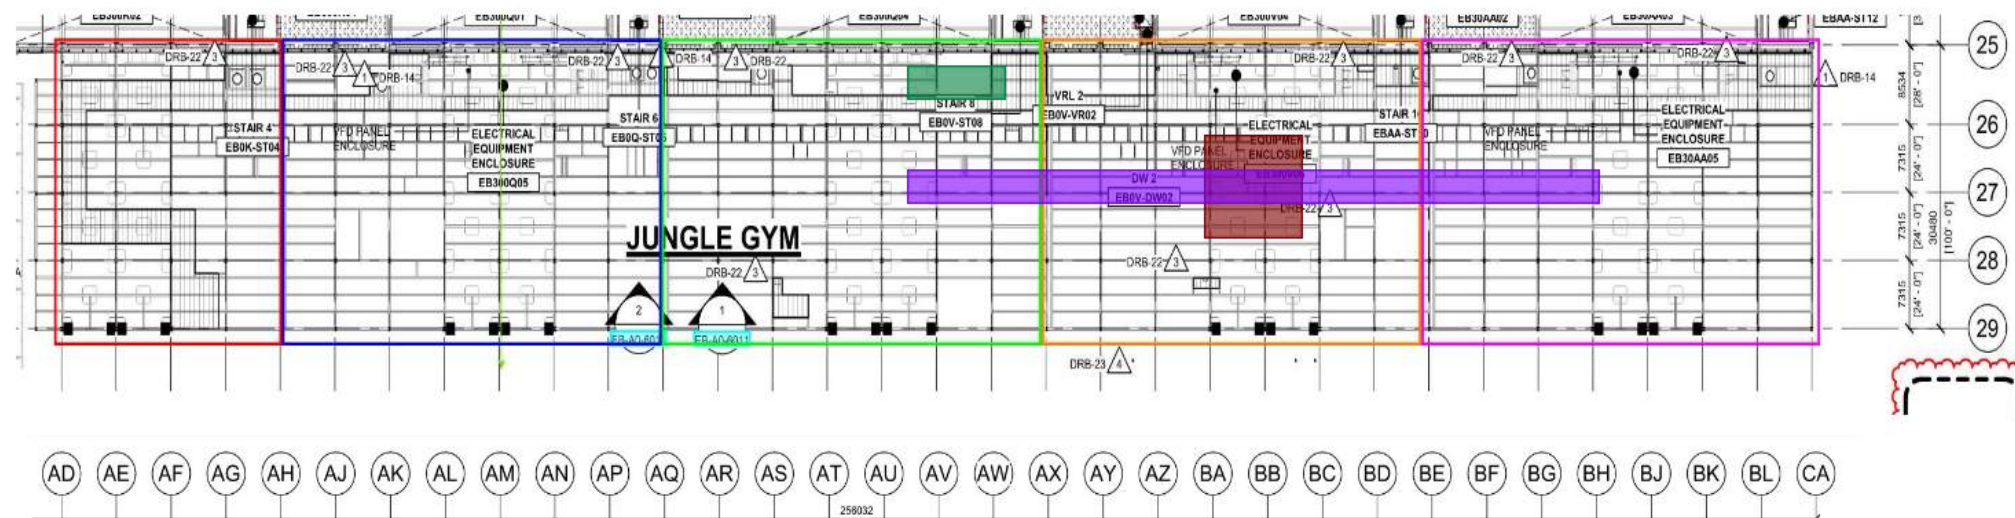

WJG – Lift 3

W&W - welding supports for gratings			* SN removing grating for Pach Taas equipment set	* Chemo - installation of MARS pipes
-------------------------------------	--	--	---------------------------------------------------	--------------------------------------





Crane logistics


truck crane
located at AG-AH.

Crane: 750 ton crane
located at AV-AW.






CUB 1

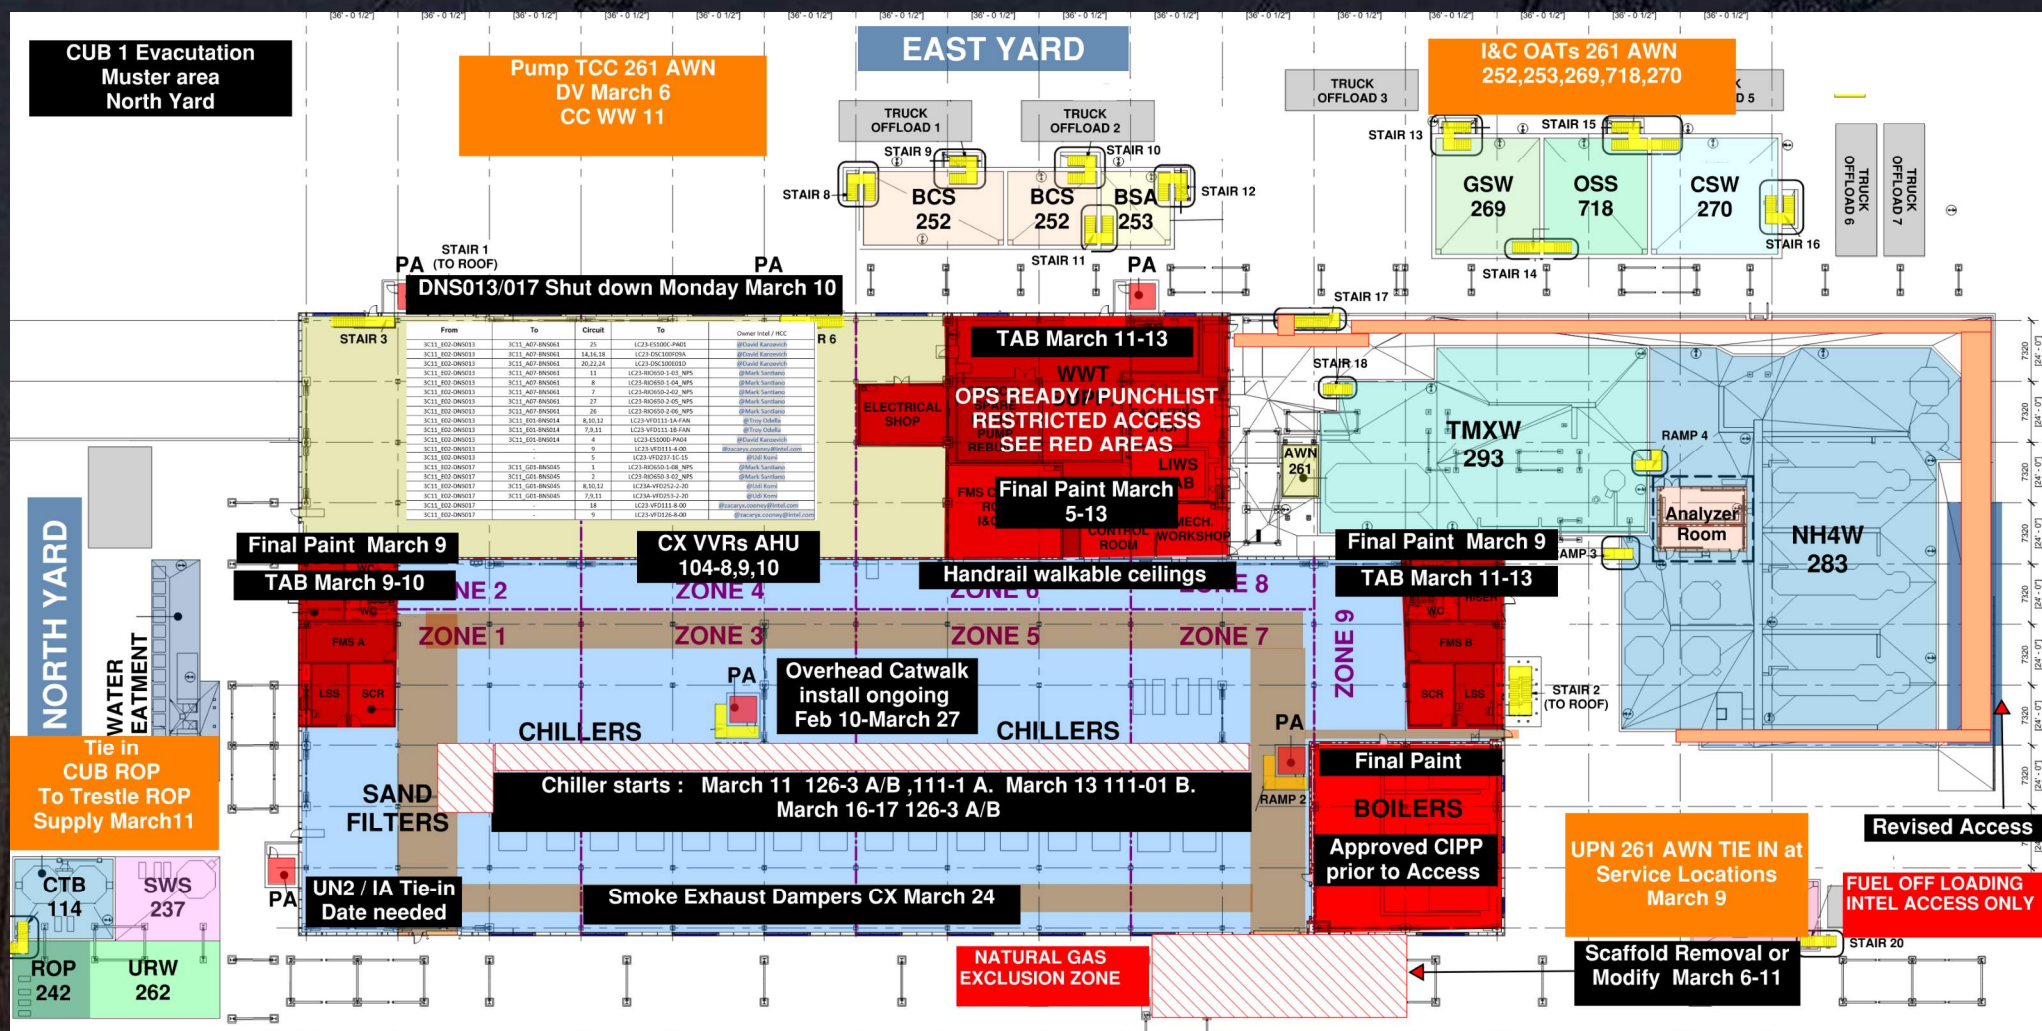


CUB 1 West Wall coordination /Trestle/Site

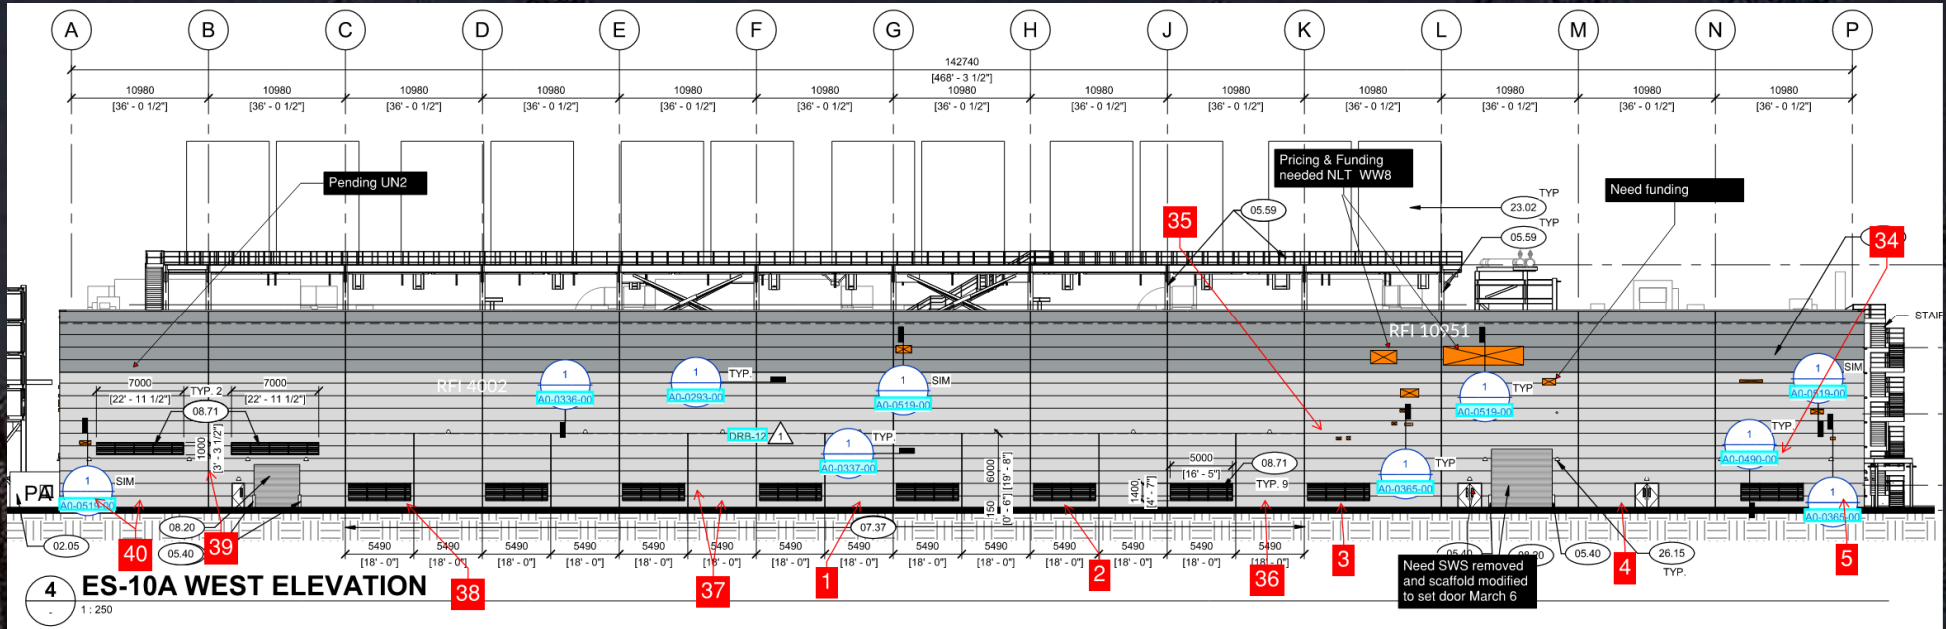


- Waste Systems Pressure Testing Wrap up 3d March 4-5
- Trestle Scaffold removal 5d March 6-11
- Metal flashings and Panel work Man Door 5-7d March 12-20
- Claim Envelope ready for DVs March 20
- DV acceptance list and corrections 7d April 2
- Ops Ready April 3
- Concrete removal Site Grading Form rebar pour concrete 5-7 d March 23-March 31
- Bullards 2d April 1-2


CUB 1 – EXTERIOR/ROOF

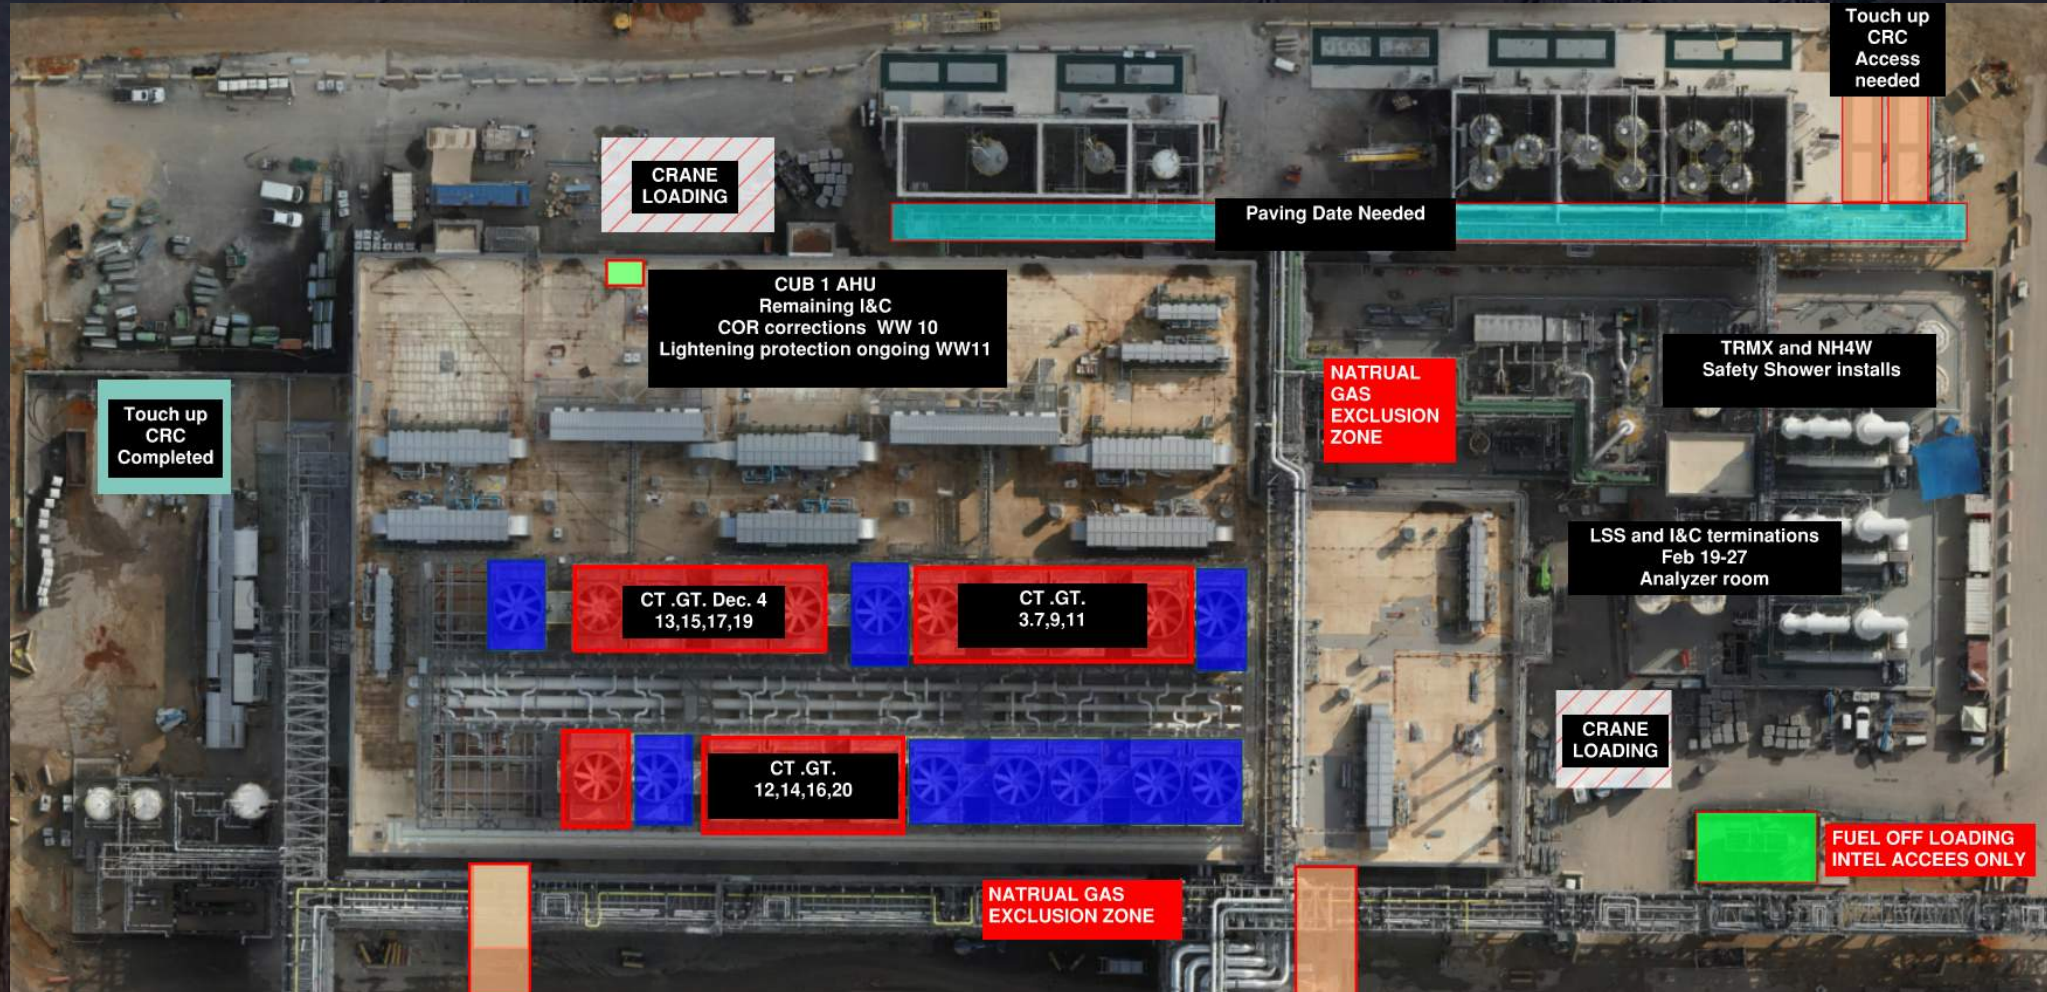


CUB 2- Load in ,H&T, Framing and Sheetrock

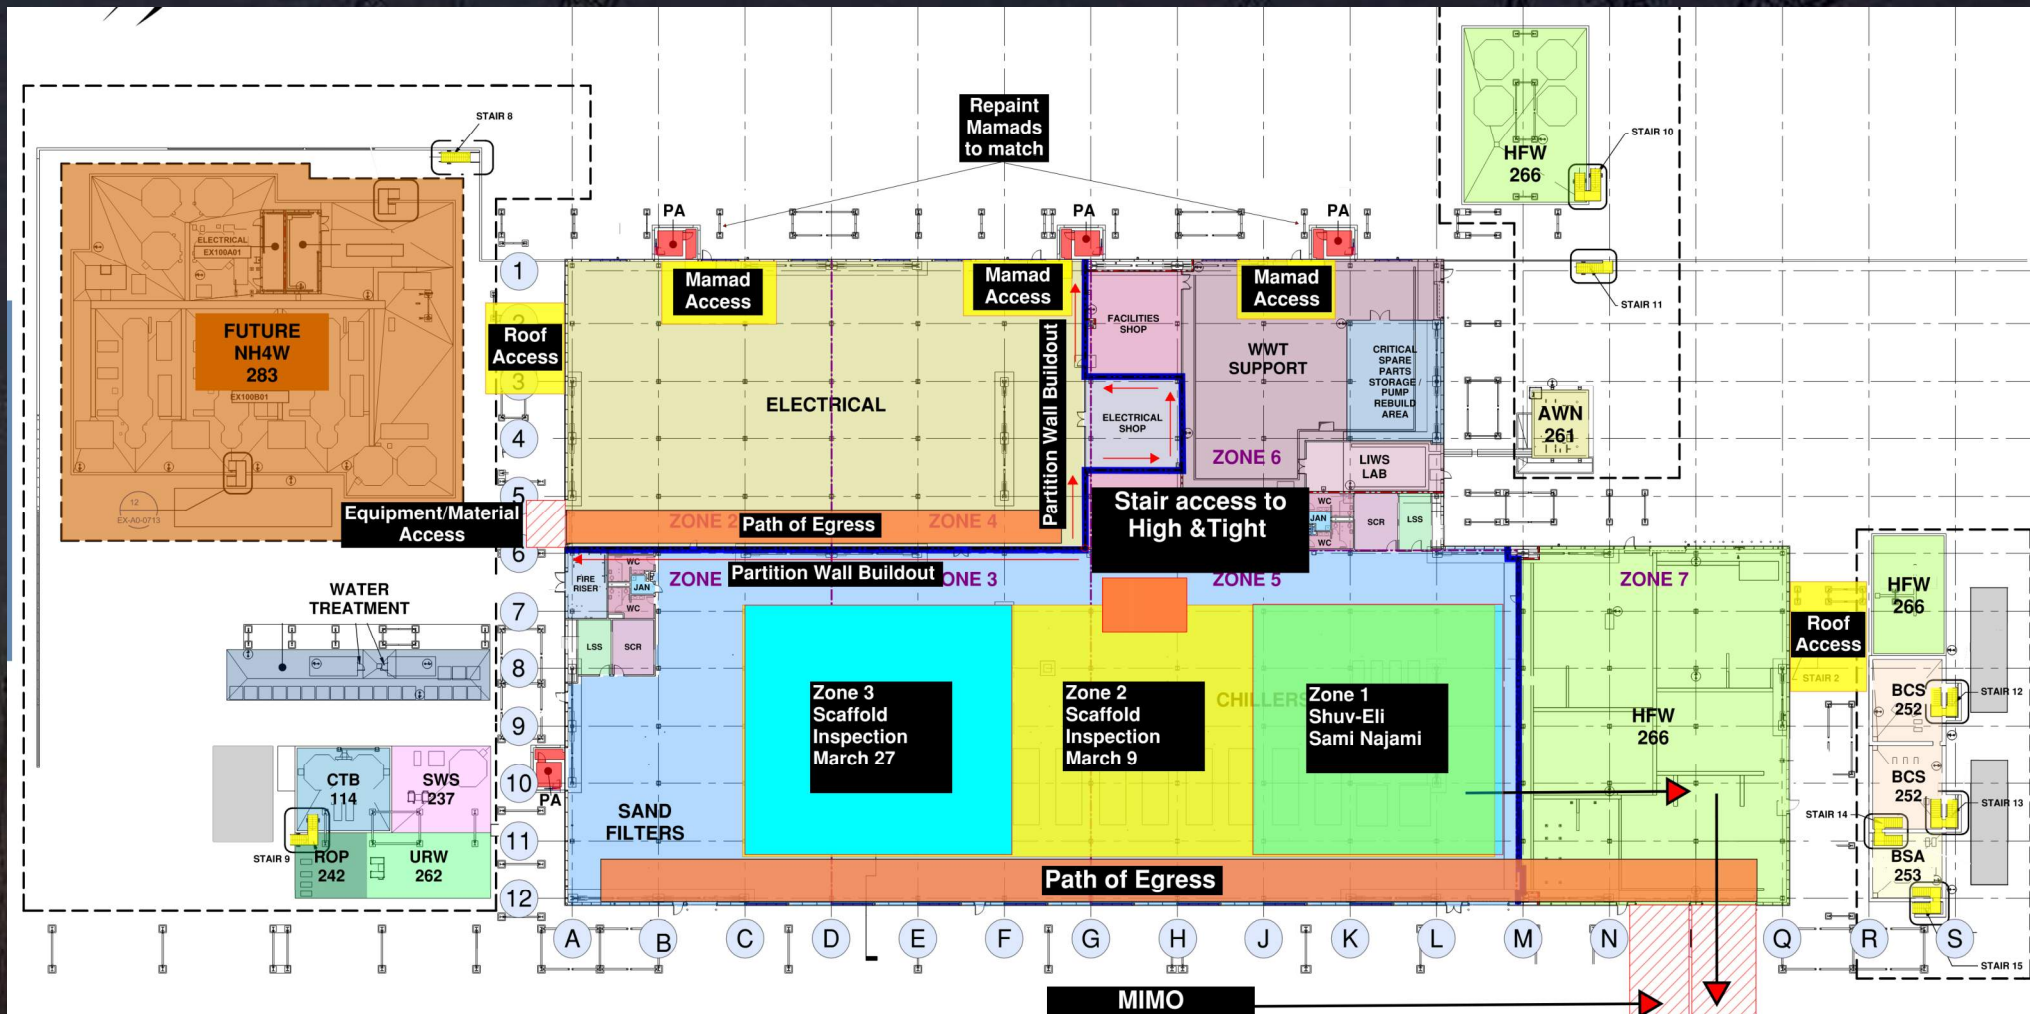


CUB 2 – EXTERIOR/ROOF

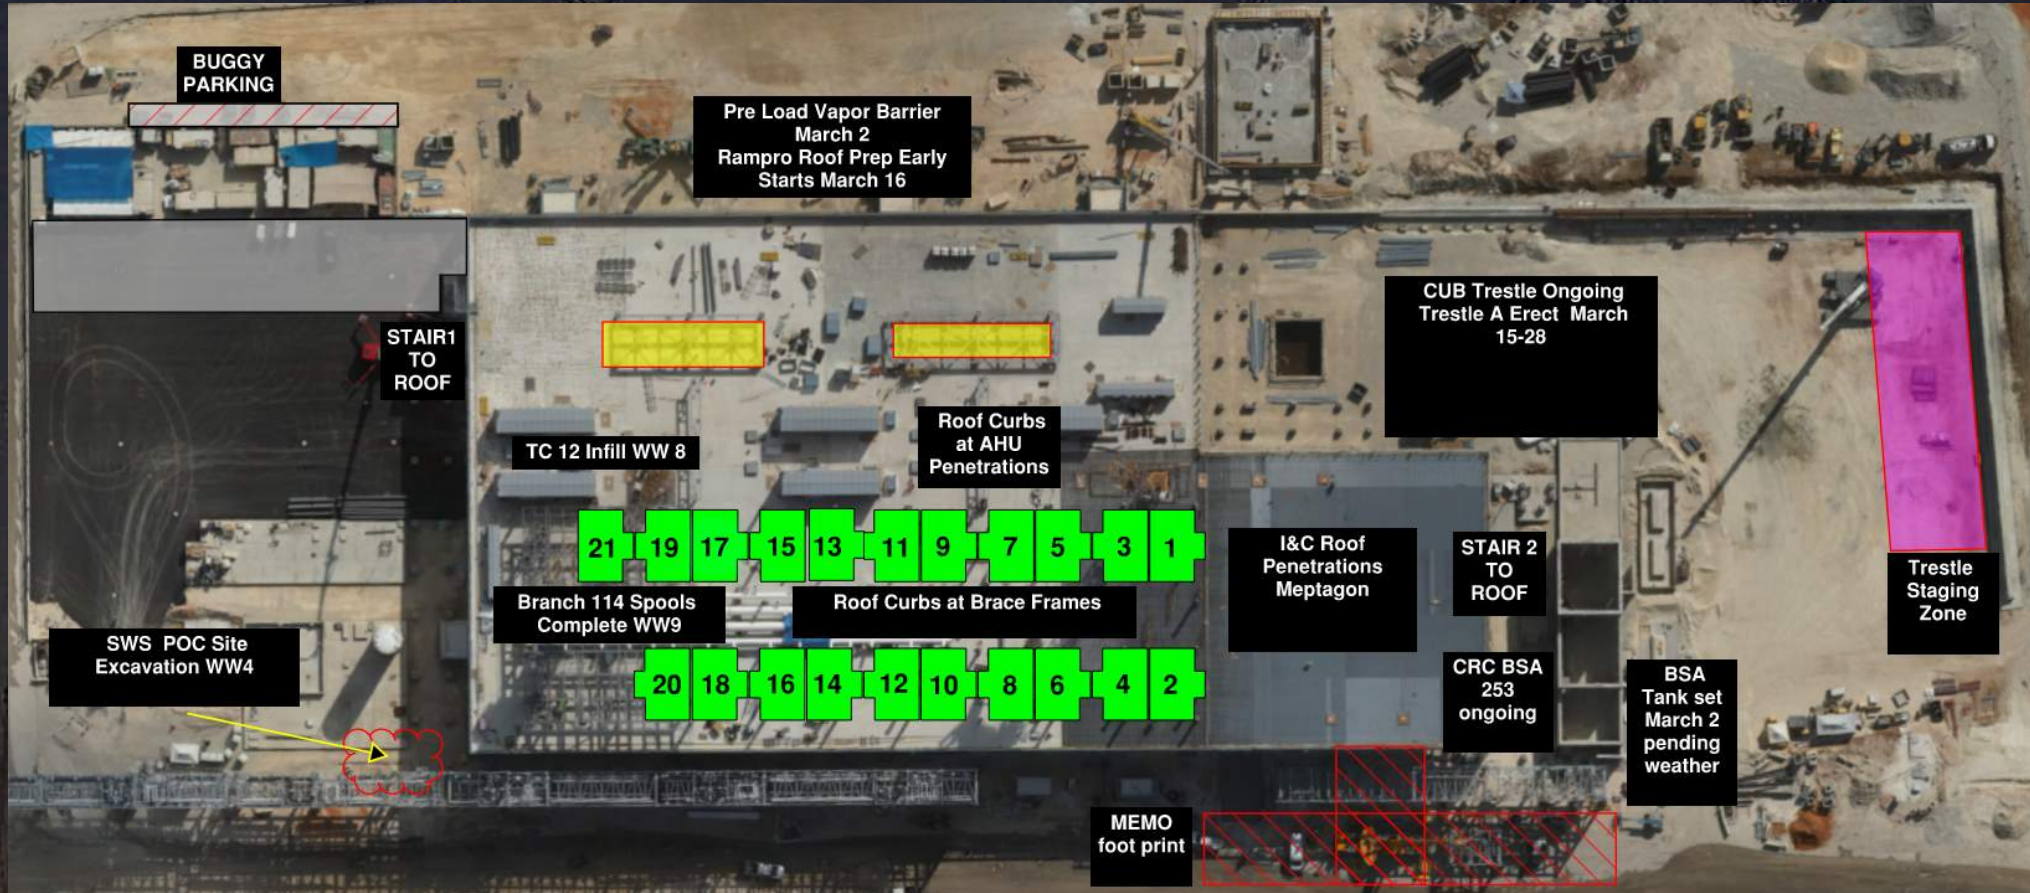



HOFFMAN CONSTRUCTION COMPANY

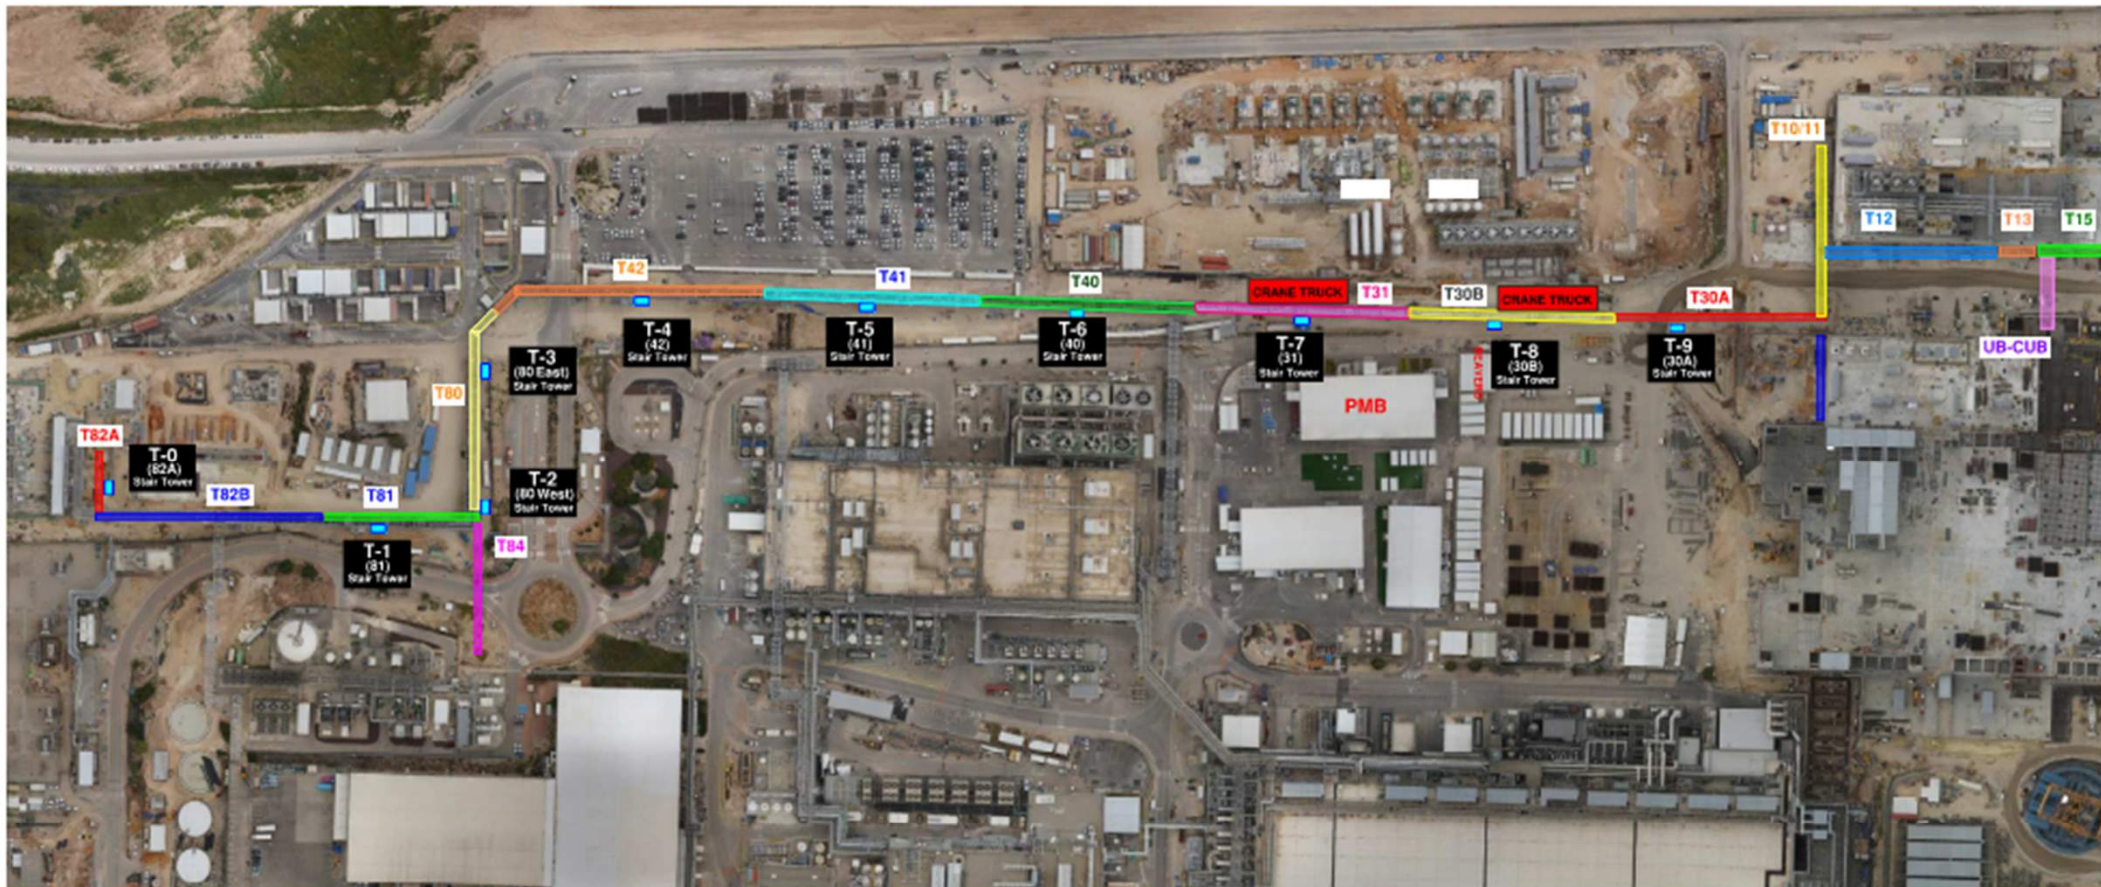

From main kiosk

Site temporary power

Legend :

— 22KV Line

— 400V Line

109 - Kiosk

● - Lift Station

TC-10

TC-8

TC-6

630A SW

630A NW

630A SW

630A NW

Fab 38.1

Fab 38.2

North

Temp power shutdown
Start: 09-Mar-5:00 PM
End: 09-Mar- 6:00 PM
Clean-room+Roof E4+E5
SB, lights.

TC-9

630A SE

630A NE

TC-7

630A NE

Cub 2

TC-12
Done

Cub 1

To 115

From main


117



Daily Coordination Meeting

Site Logistics

North

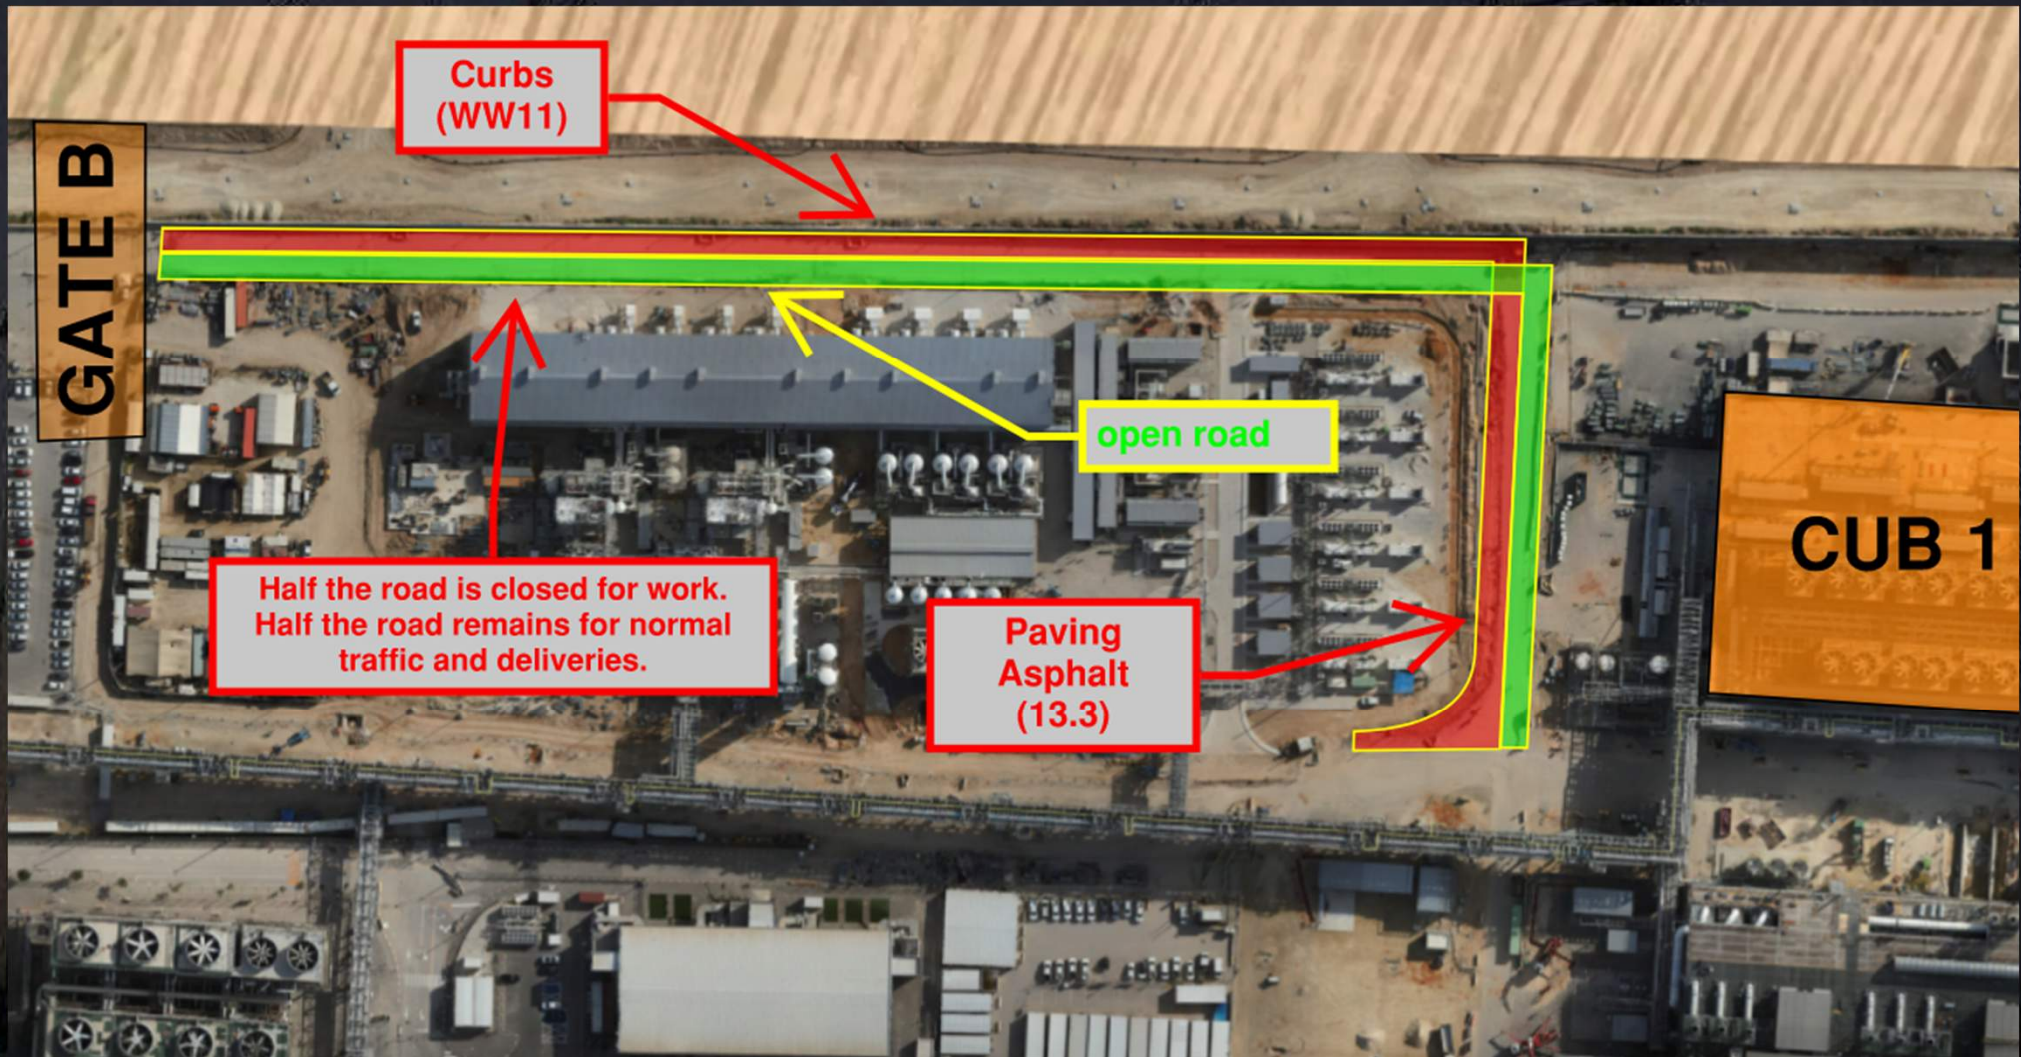



Daily Coordination Meeting

Site Logistics

North






Daily Coordination Meeting

Site Logistics

South

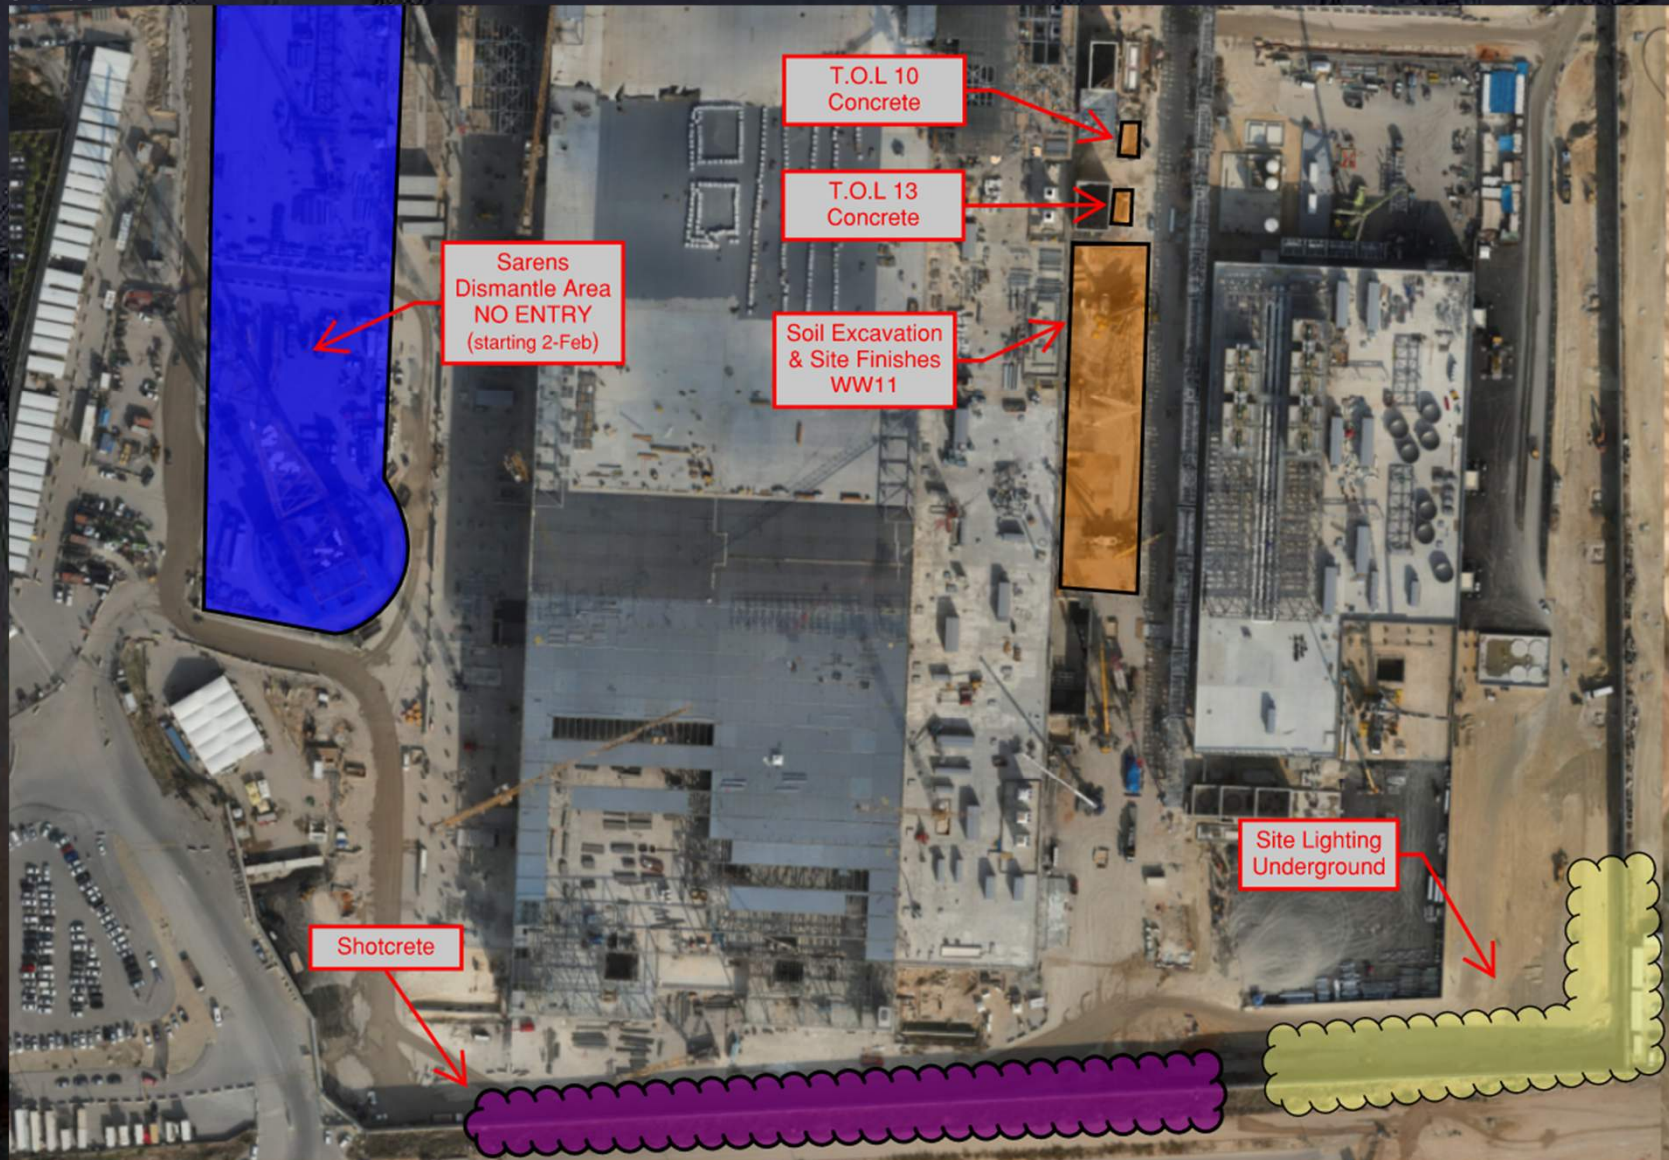



Inspections

- This is a reminder regarding inspections on our site.
- There are items like MEWP, scaffolds, forklifts, etc., which are examples of equipment or surfaces that require a visual inspection every day before starting work.
- Work in the area can only begin after a successful inspection and approval (checklist).
- Of course, there are other items, such as electrical tools, which require an inspection by a certified electrician every three months. However, a visual inspection must still be conducted every day before using the equipment.
- It is essential to adhere to these procedures and remember that there is personal responsibility for the operators of the various tools.

Daily Coordination Meeting



14:00 Sign In
