


Daily Coordination Meeting


General Topics:

- Vehicle passes- changing next week
- Weekend work




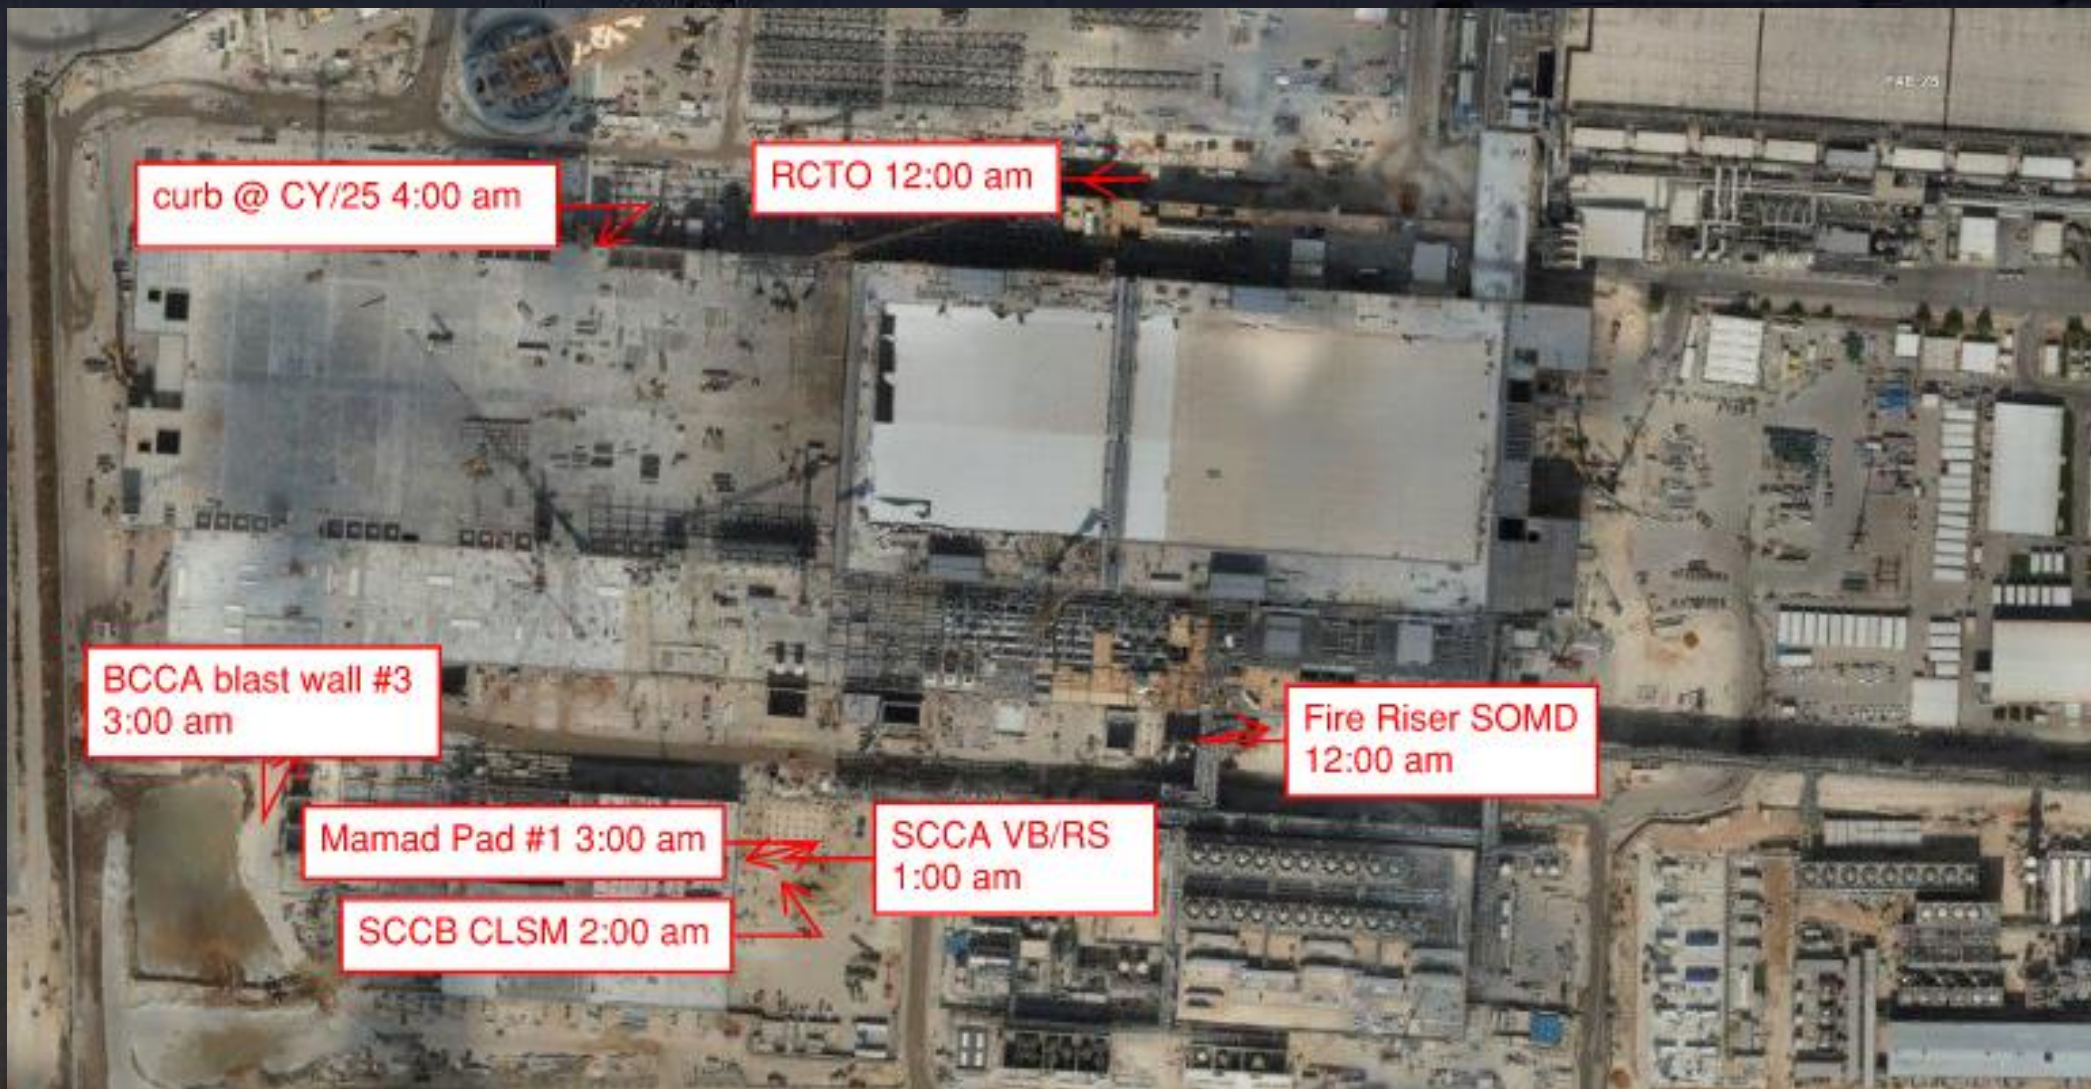


UTILITY LEVEL MOD1

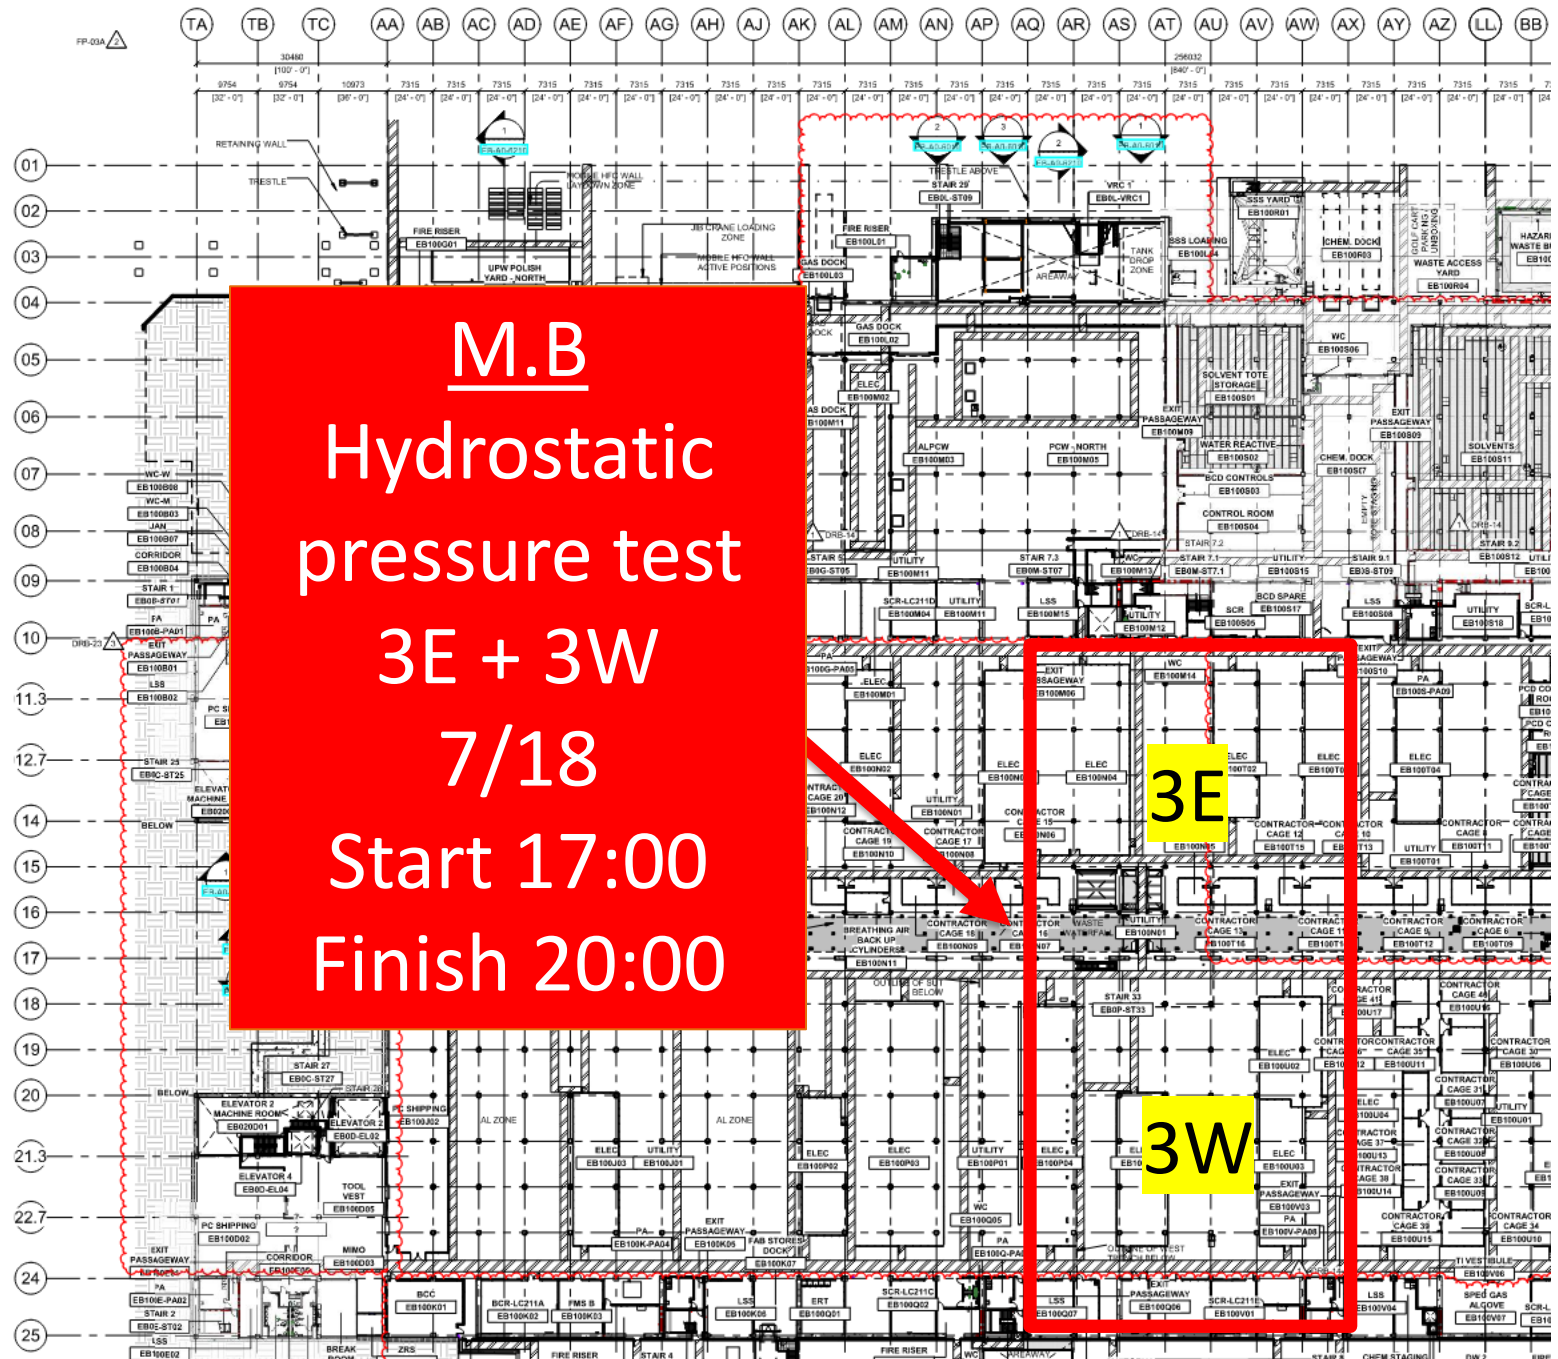

UTILITY LEVEL MOD1

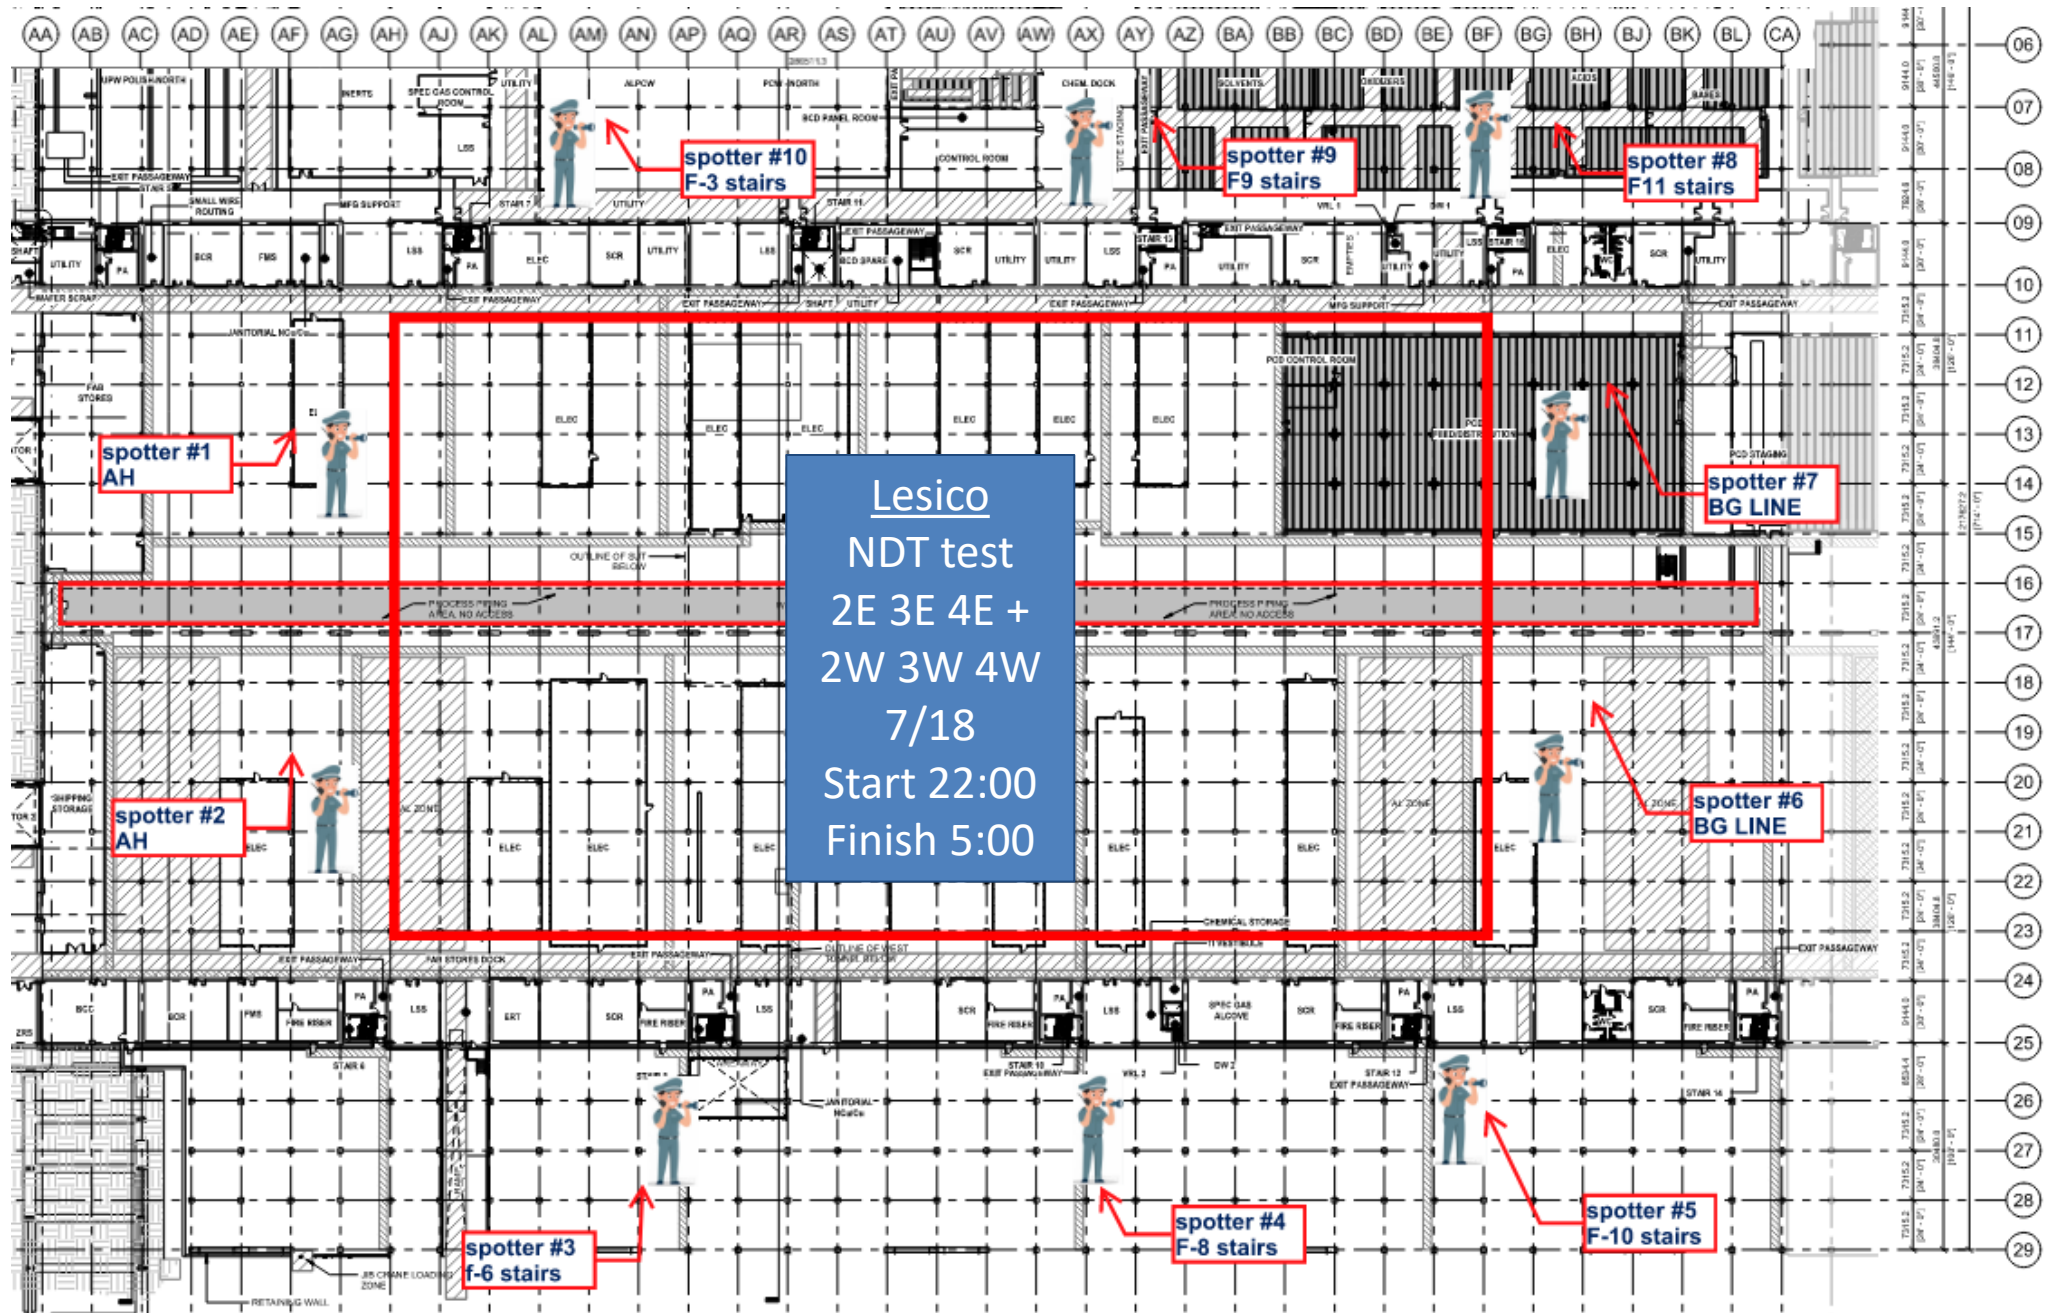

Lesico
NDT test
effected
zone at SUB
FAB
7/18
Start 22:00
Finish 5:00

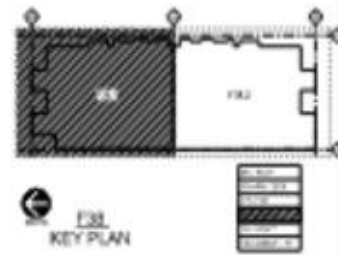

GENERAL NOTES


1. THE WORK SHALL BE IN ACCORDANCE WITH THE LATEST EDITIONS OF THE FOLLOWING STANDARDS AND SPECIFICATIONS:
2. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.
3. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.
4. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.
5. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.
6. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.
7. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.
8. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.
9. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.
10. THE WORK SHALL BE COMPLETED WITHIN THE SPECIFIED TIME FRAME.

KEYED NOTES:

SCOPE OF WORK

PROLIMINARY NOT FOR CONSTRUCTION OR BID		Jacobs 2001 10th Avenue, NE Atlanta, Georgia 30329	
		PROGRAMMING 80%	
		1E - DMS	
		Intel	
UG21 - ARCHITECTURAL SURFING LEVEL - 33A OVERALL FLOOR PLAN			
DATE: 07/18/2018		JOB NO: 20A-00000	


UTILITY LEVEL MOD2

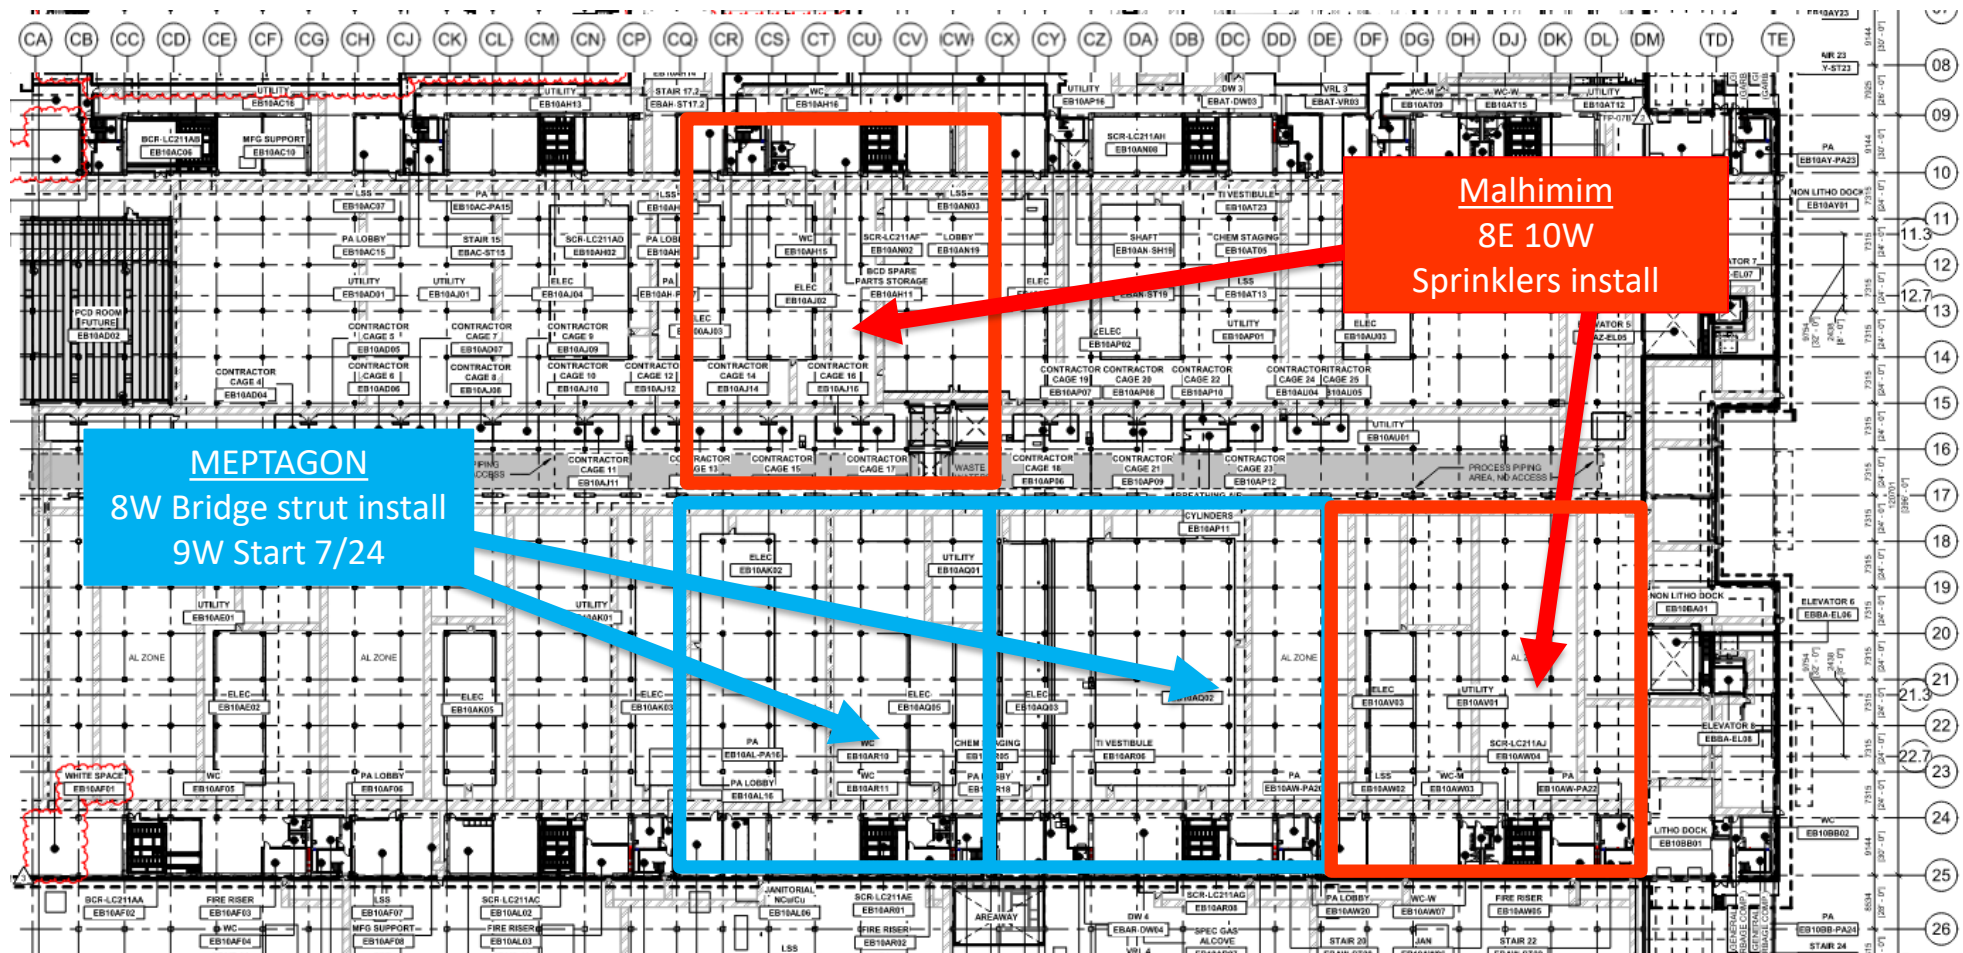



SUT 38.1 LEVEL


SKE
Safety shower's
Need Bulletproofing

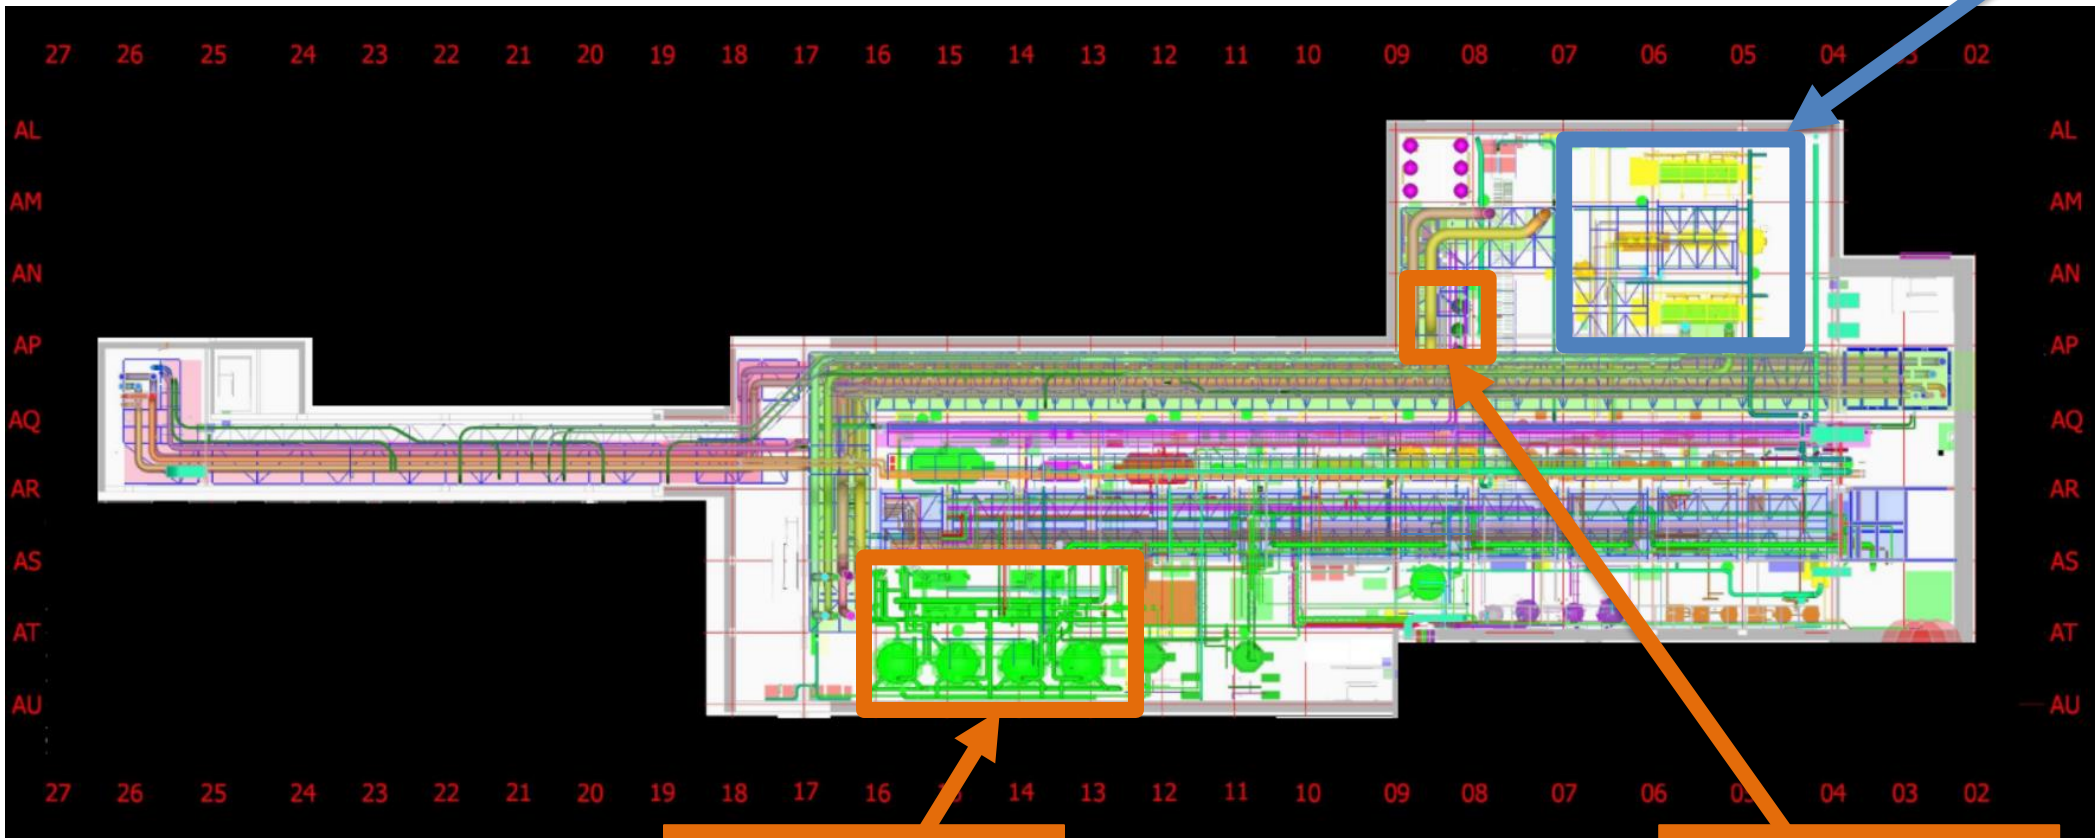


AWN-
Piping Connections.

SWS
Hx hock up


SUT 38.2 LEVEL


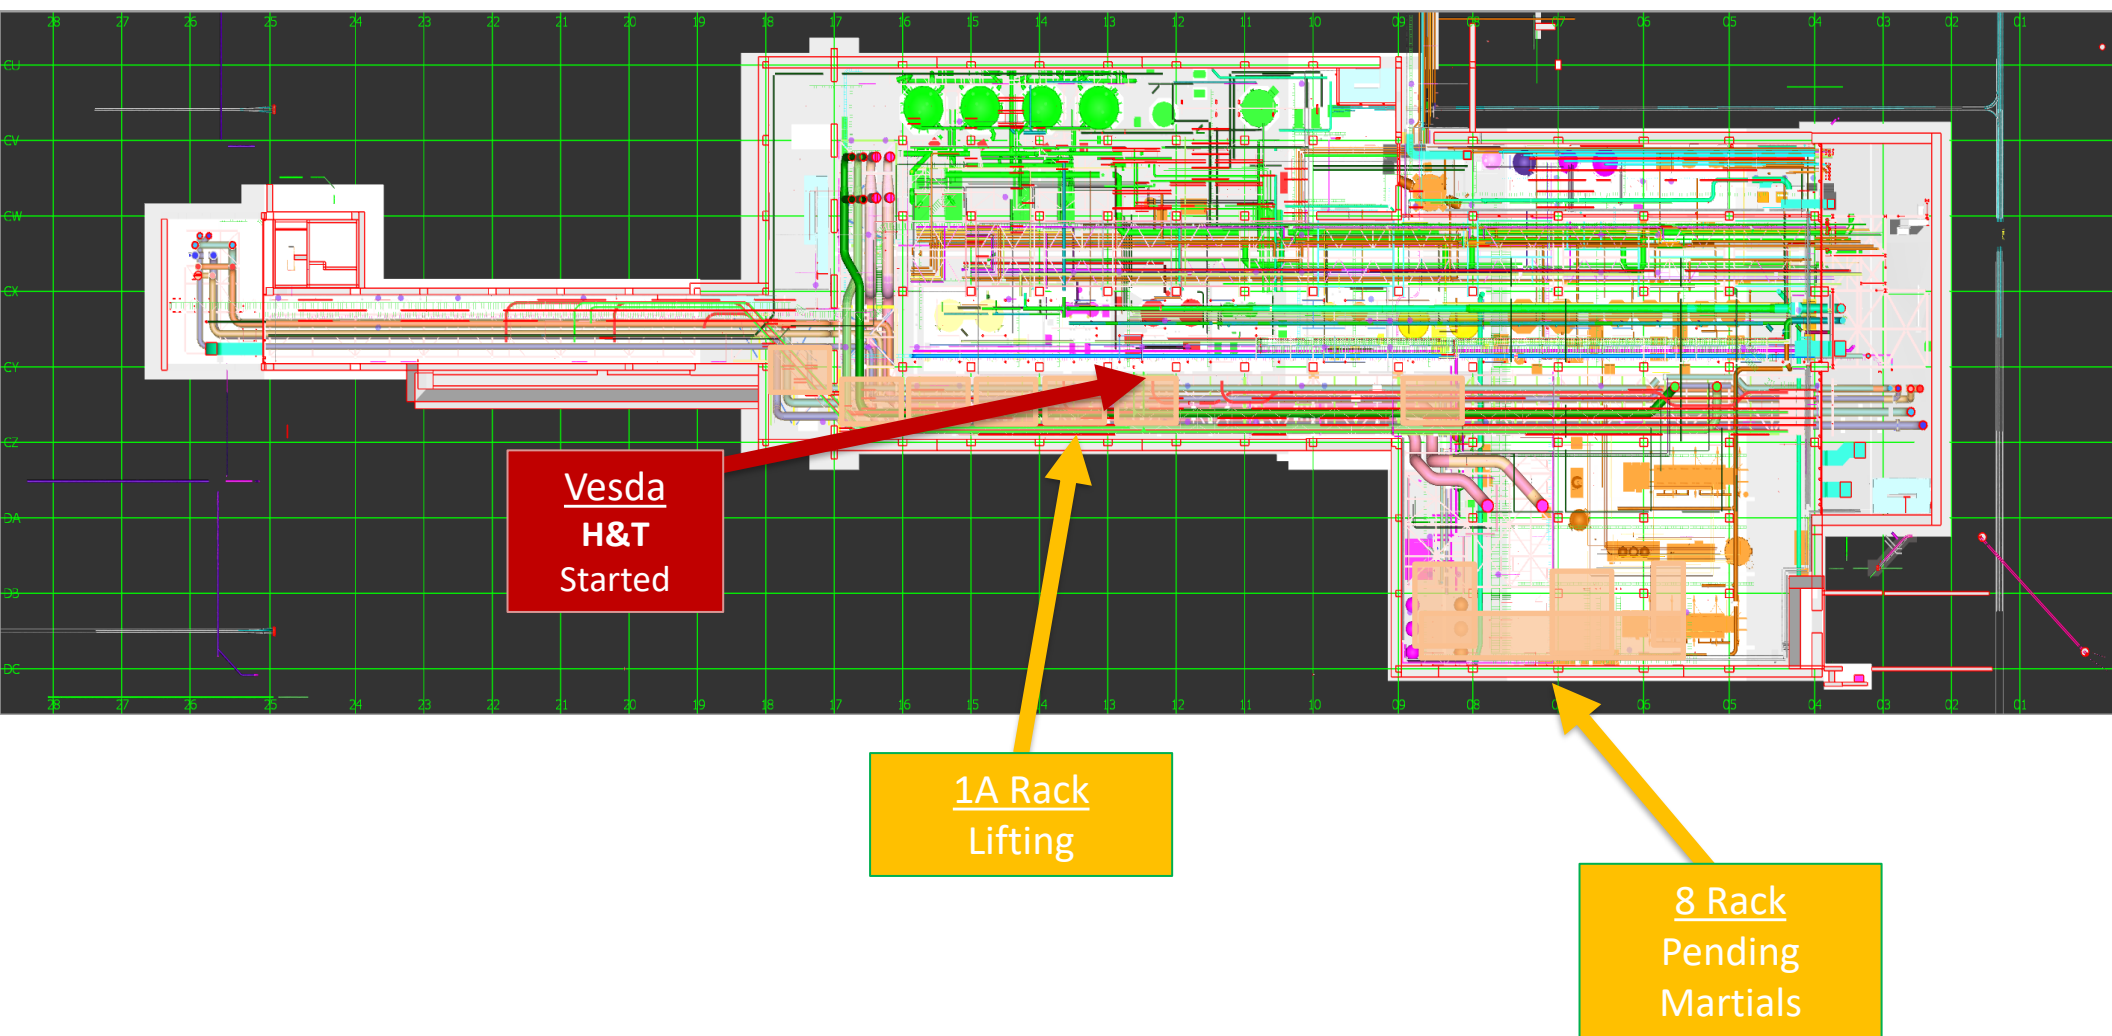



SUBFAB BUILDOUT MOD 1

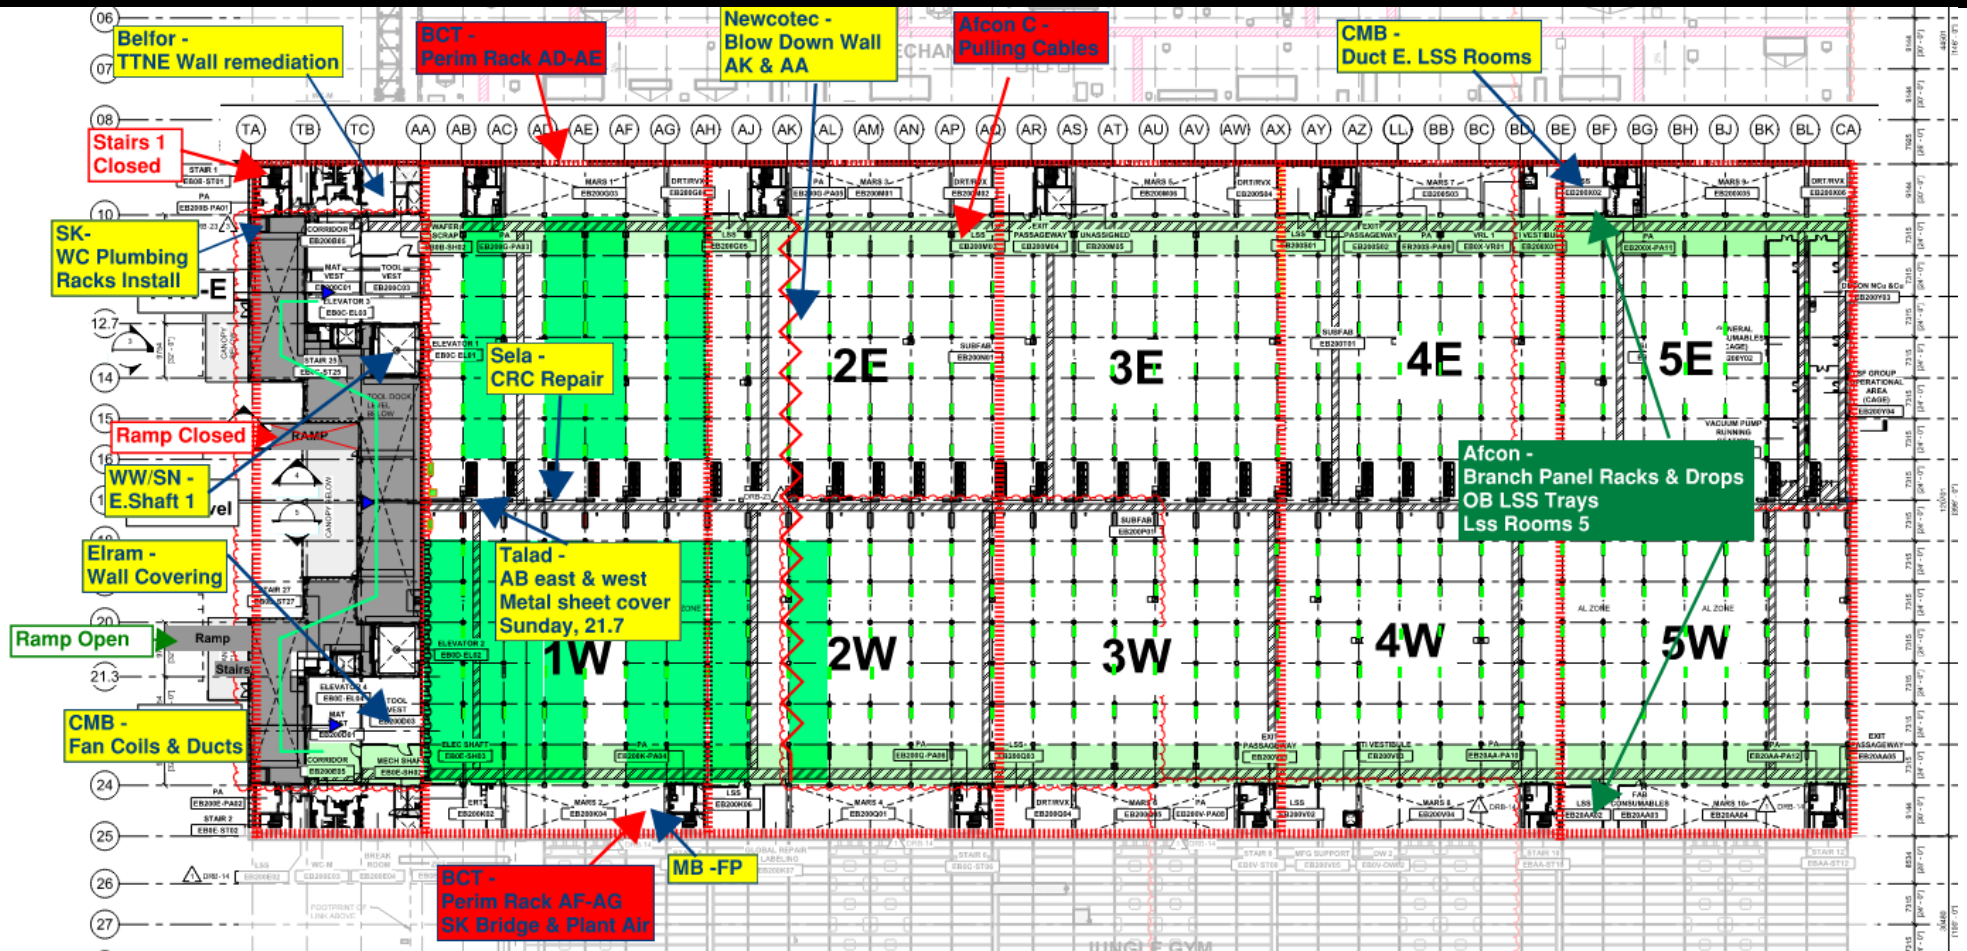



CB - 3FK Platform Jul 23 (Swing)
Tzur Esh - Steel paint Jul 24 (Day)
Pach Ta'as - Coils set Jul 25 (Swing/Day Crane pending)

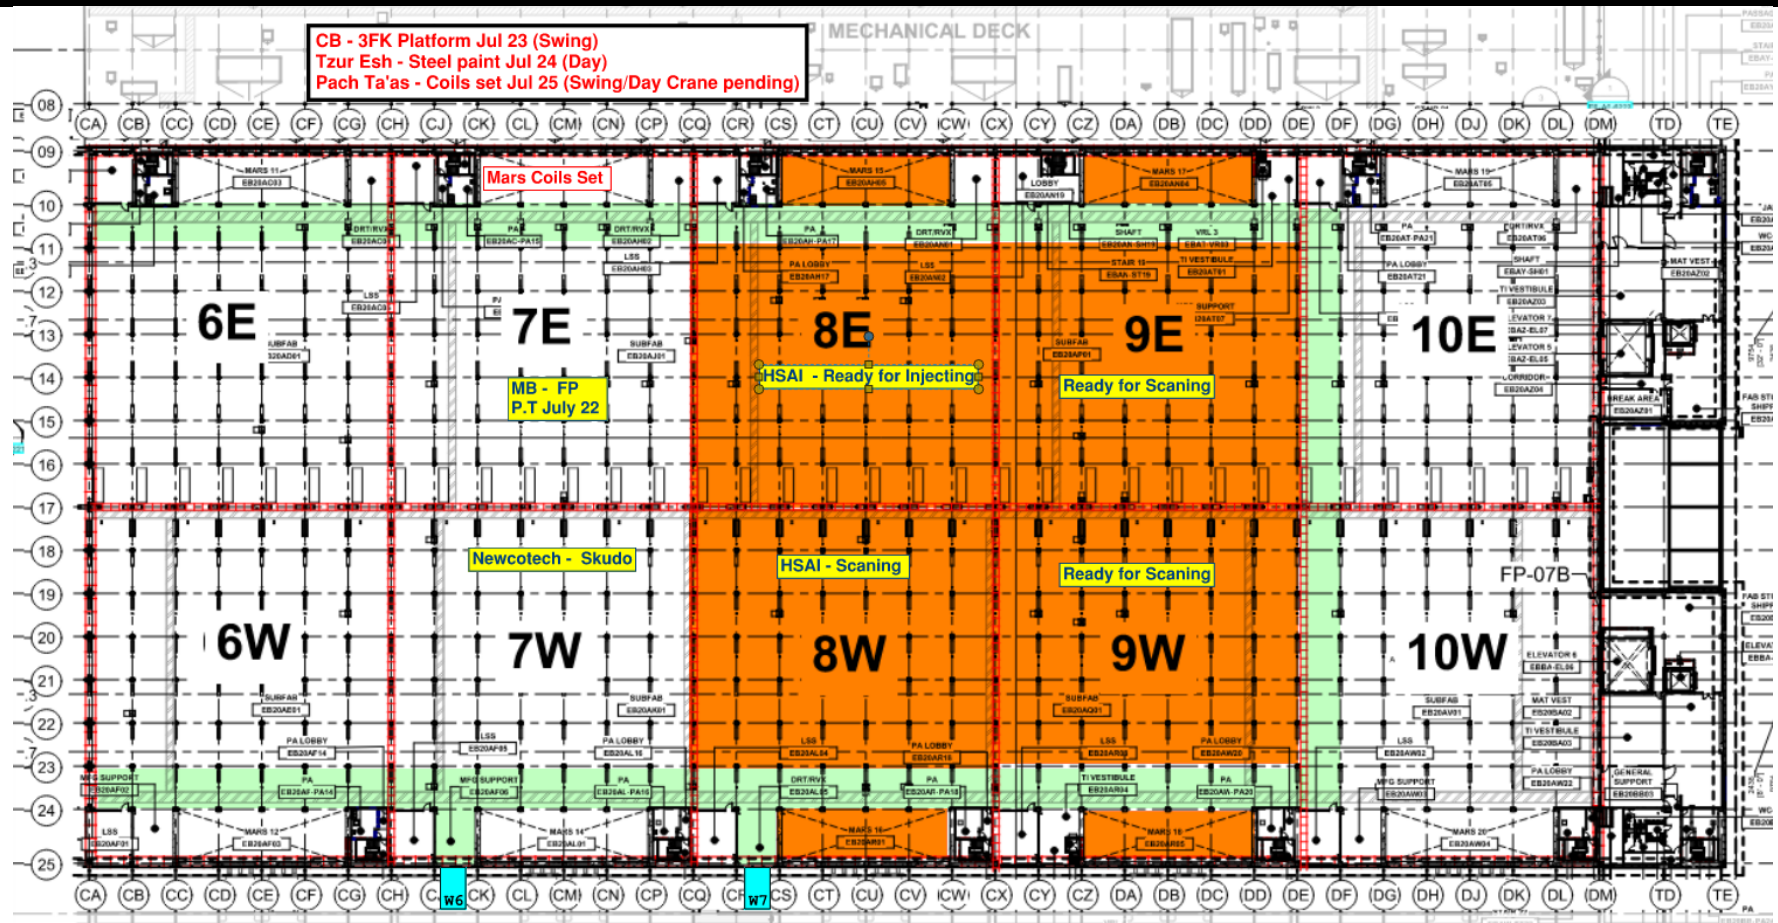


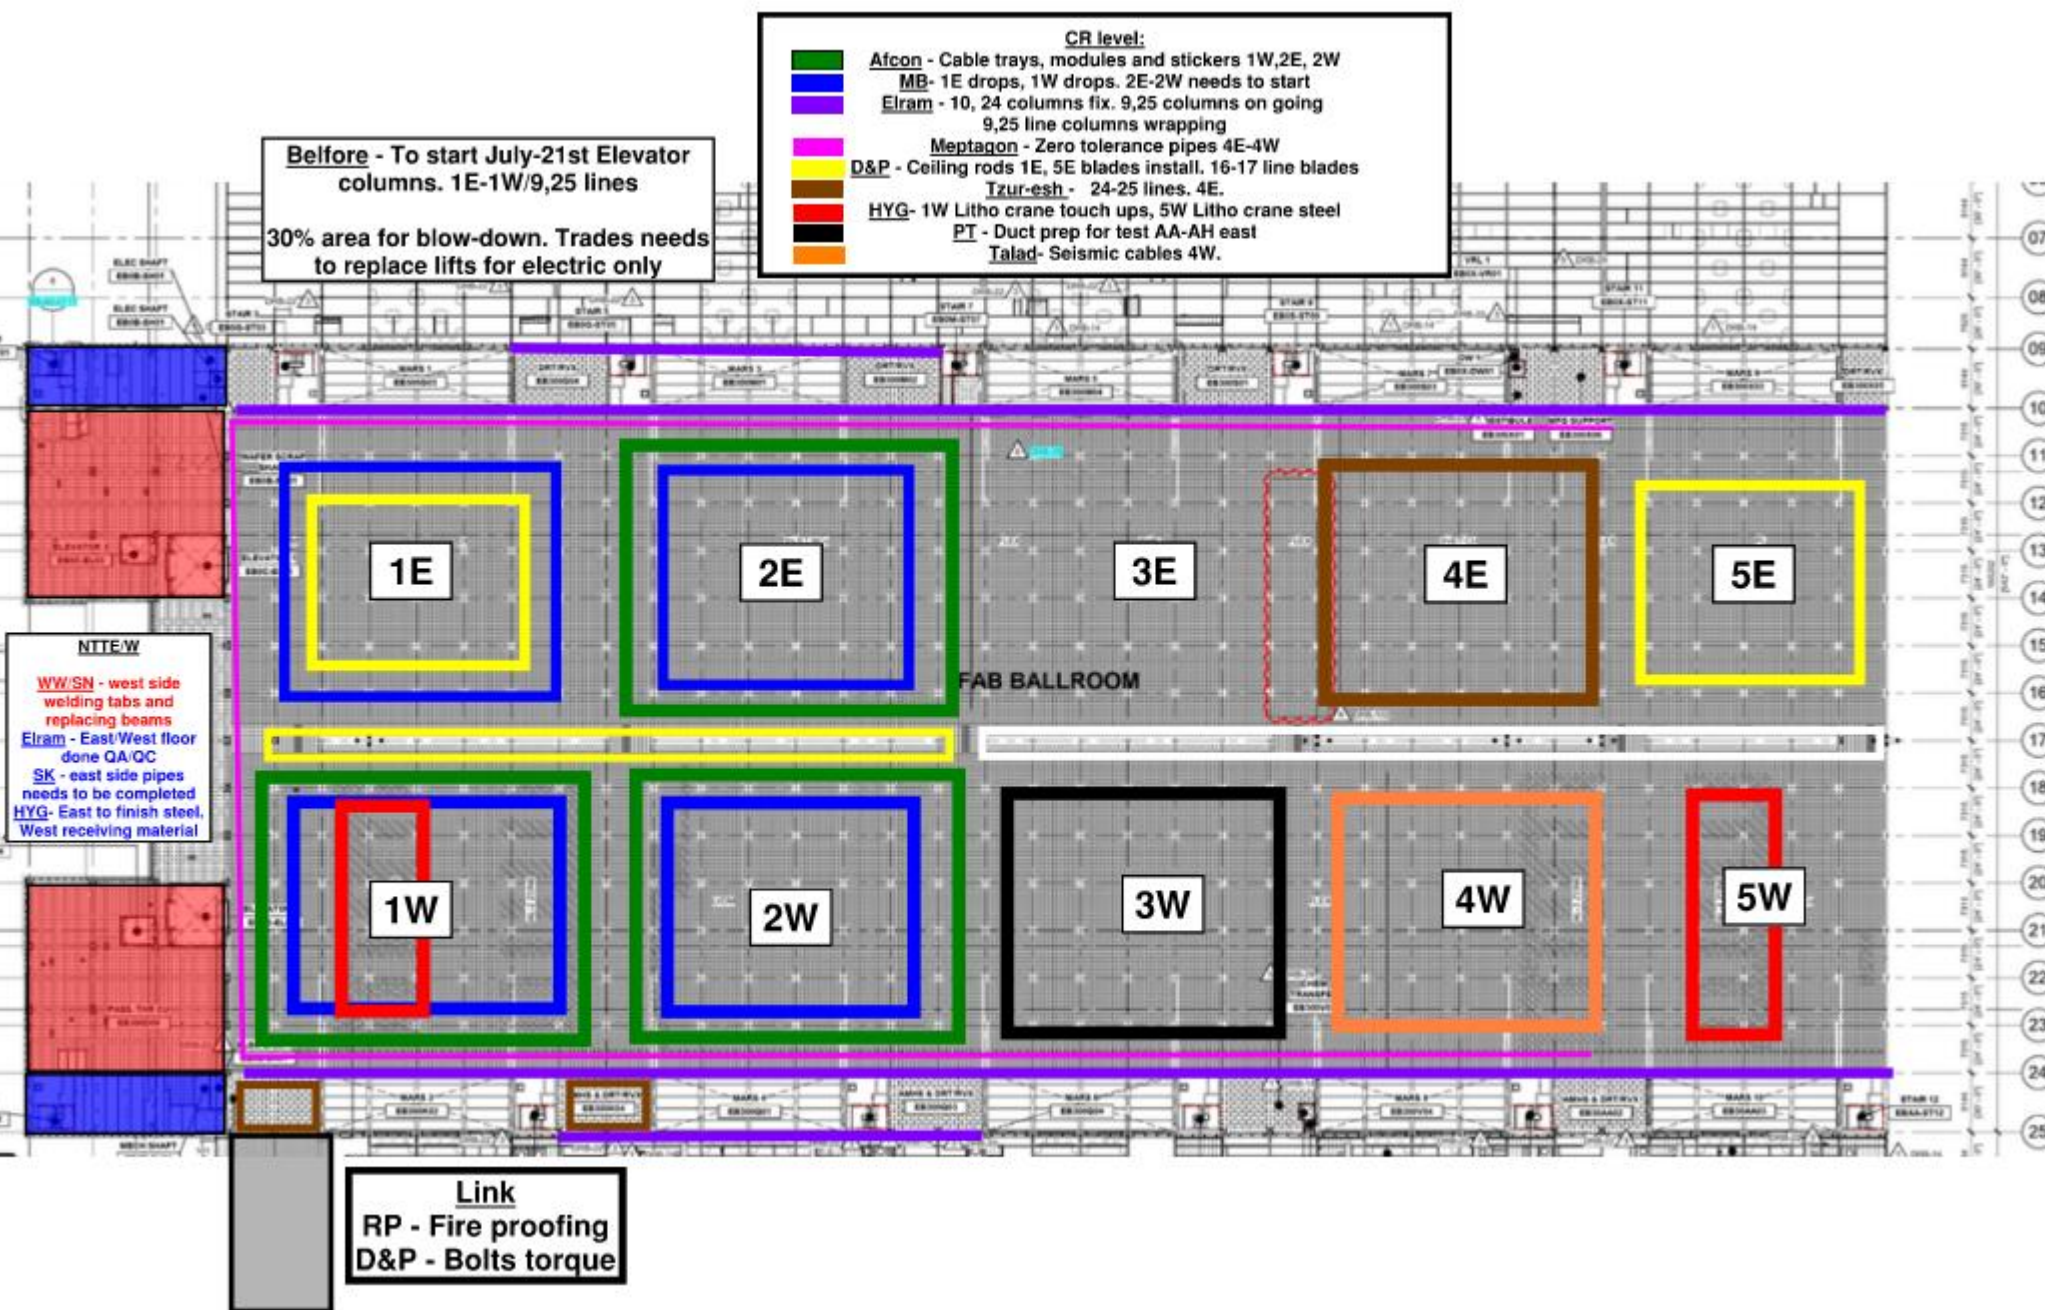


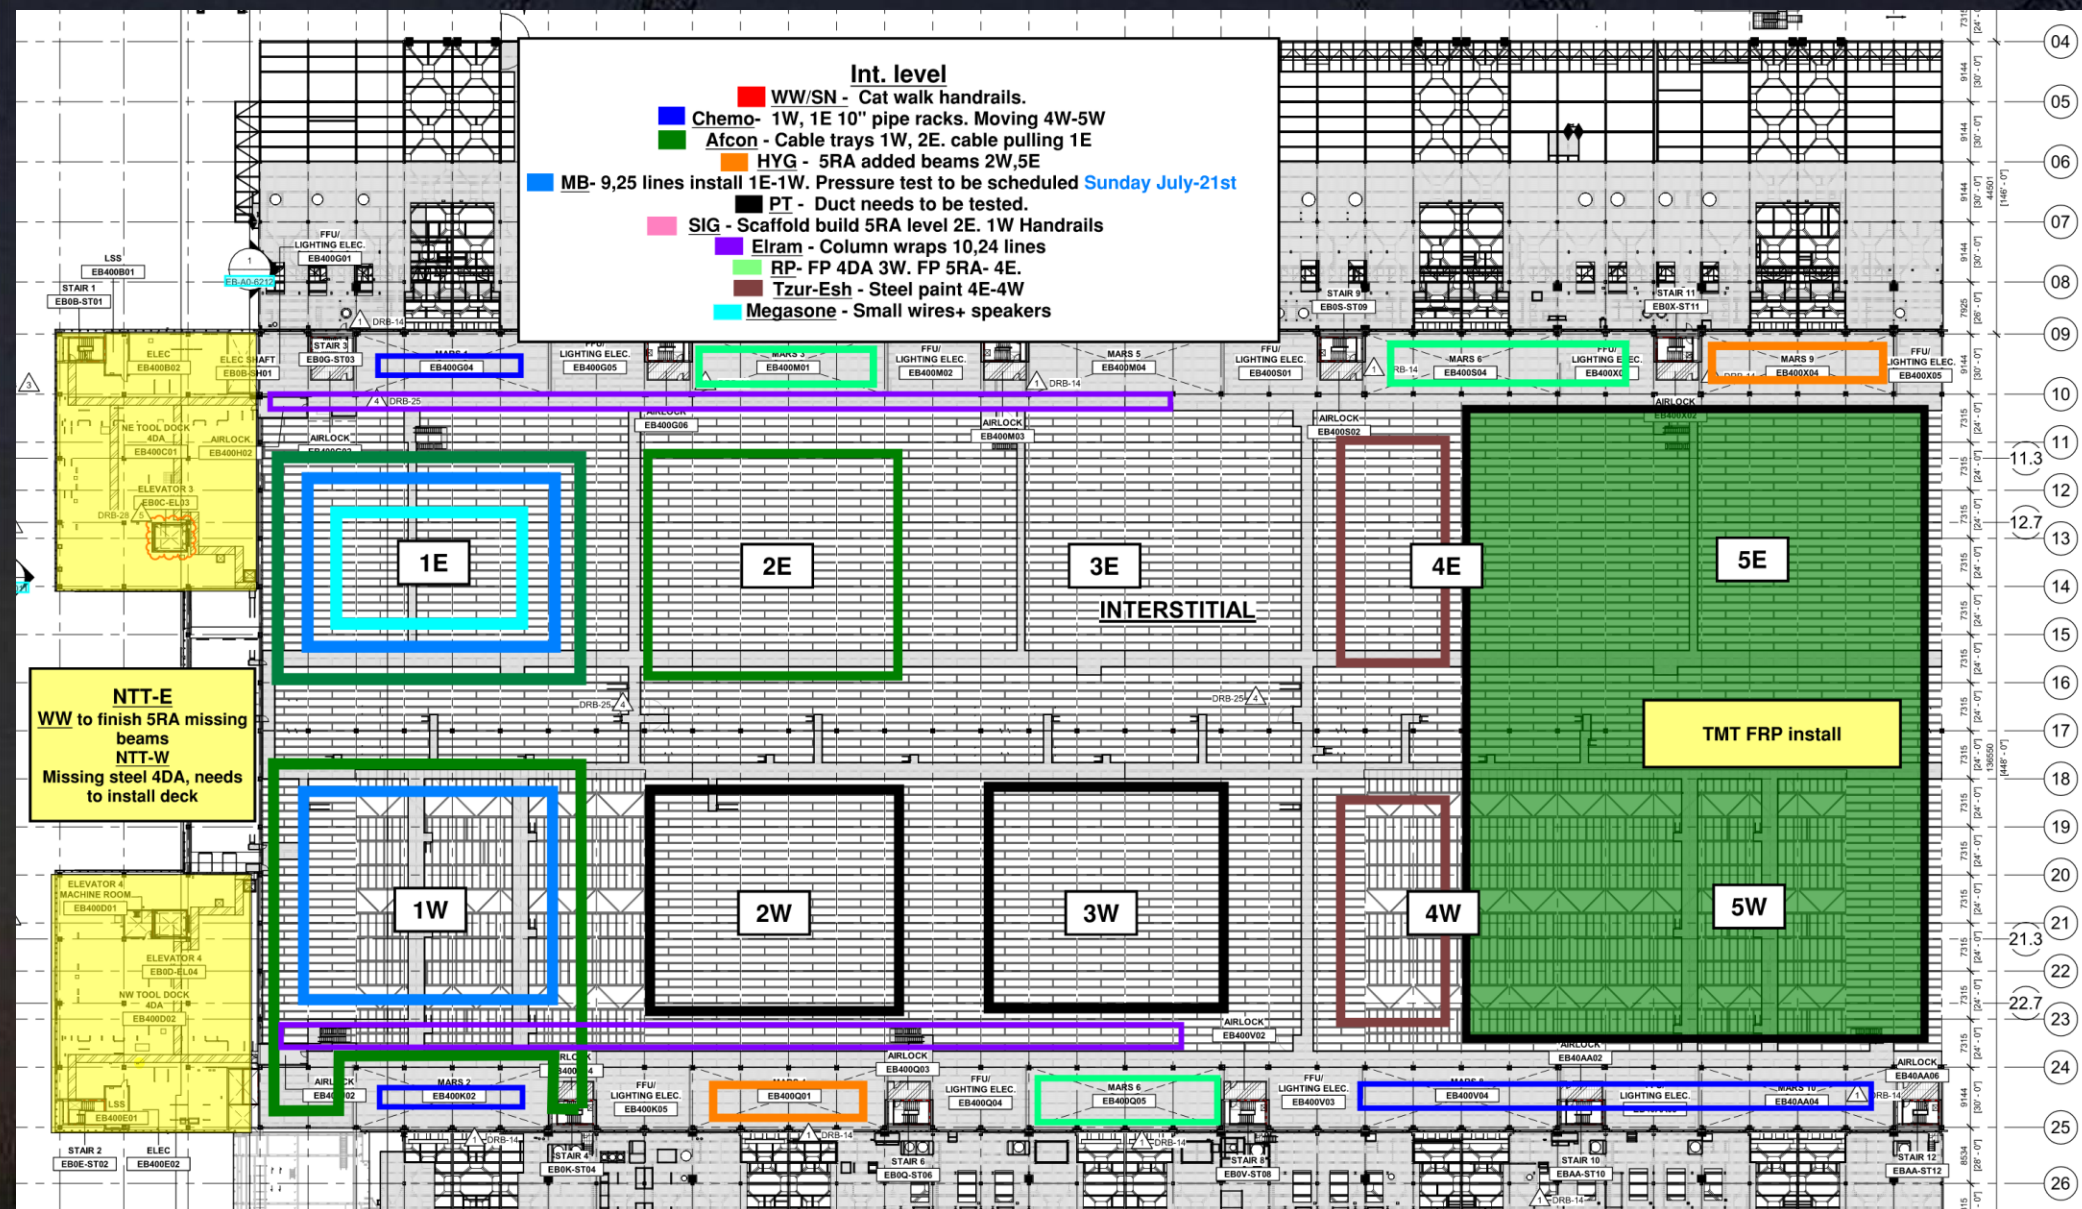

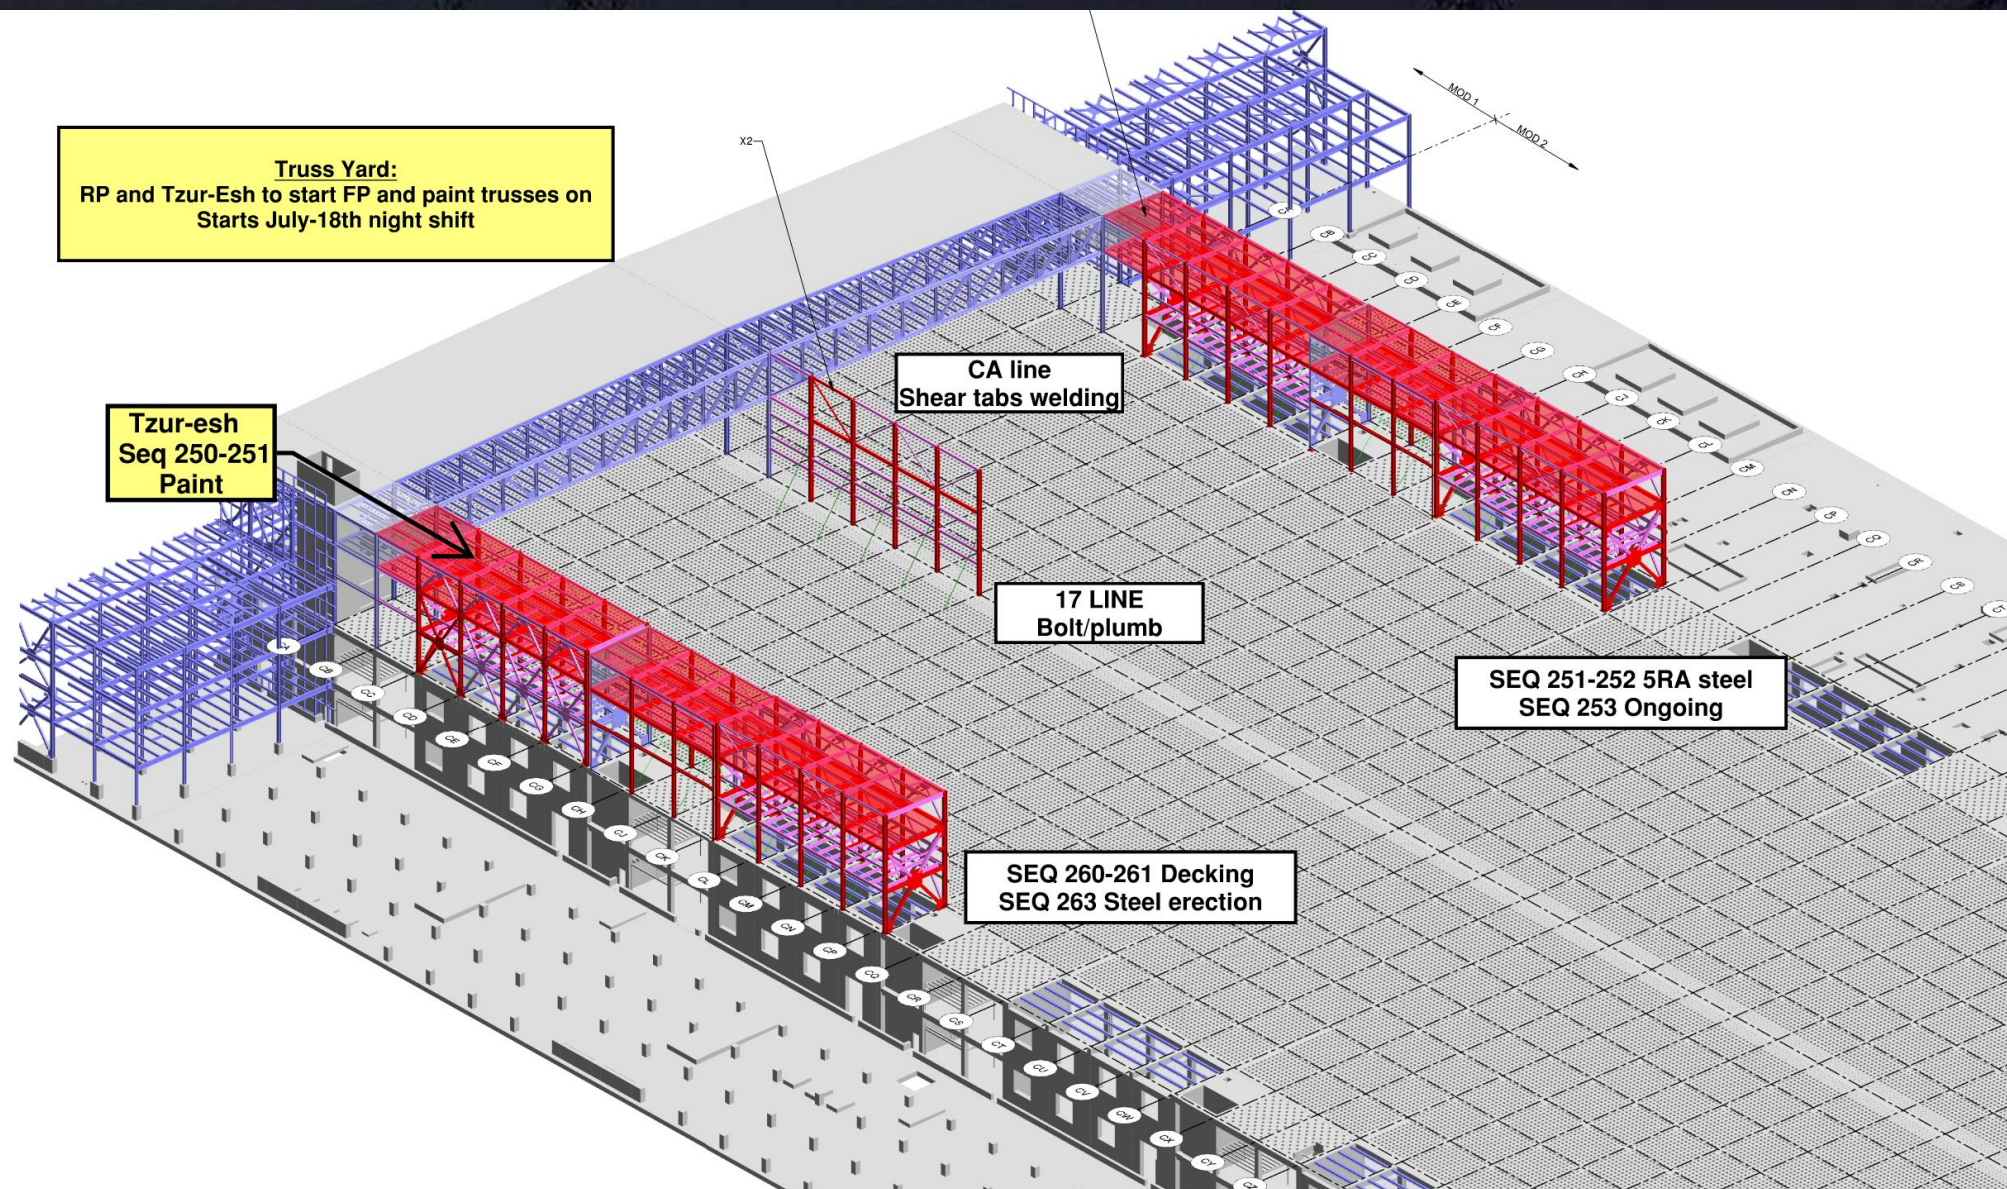

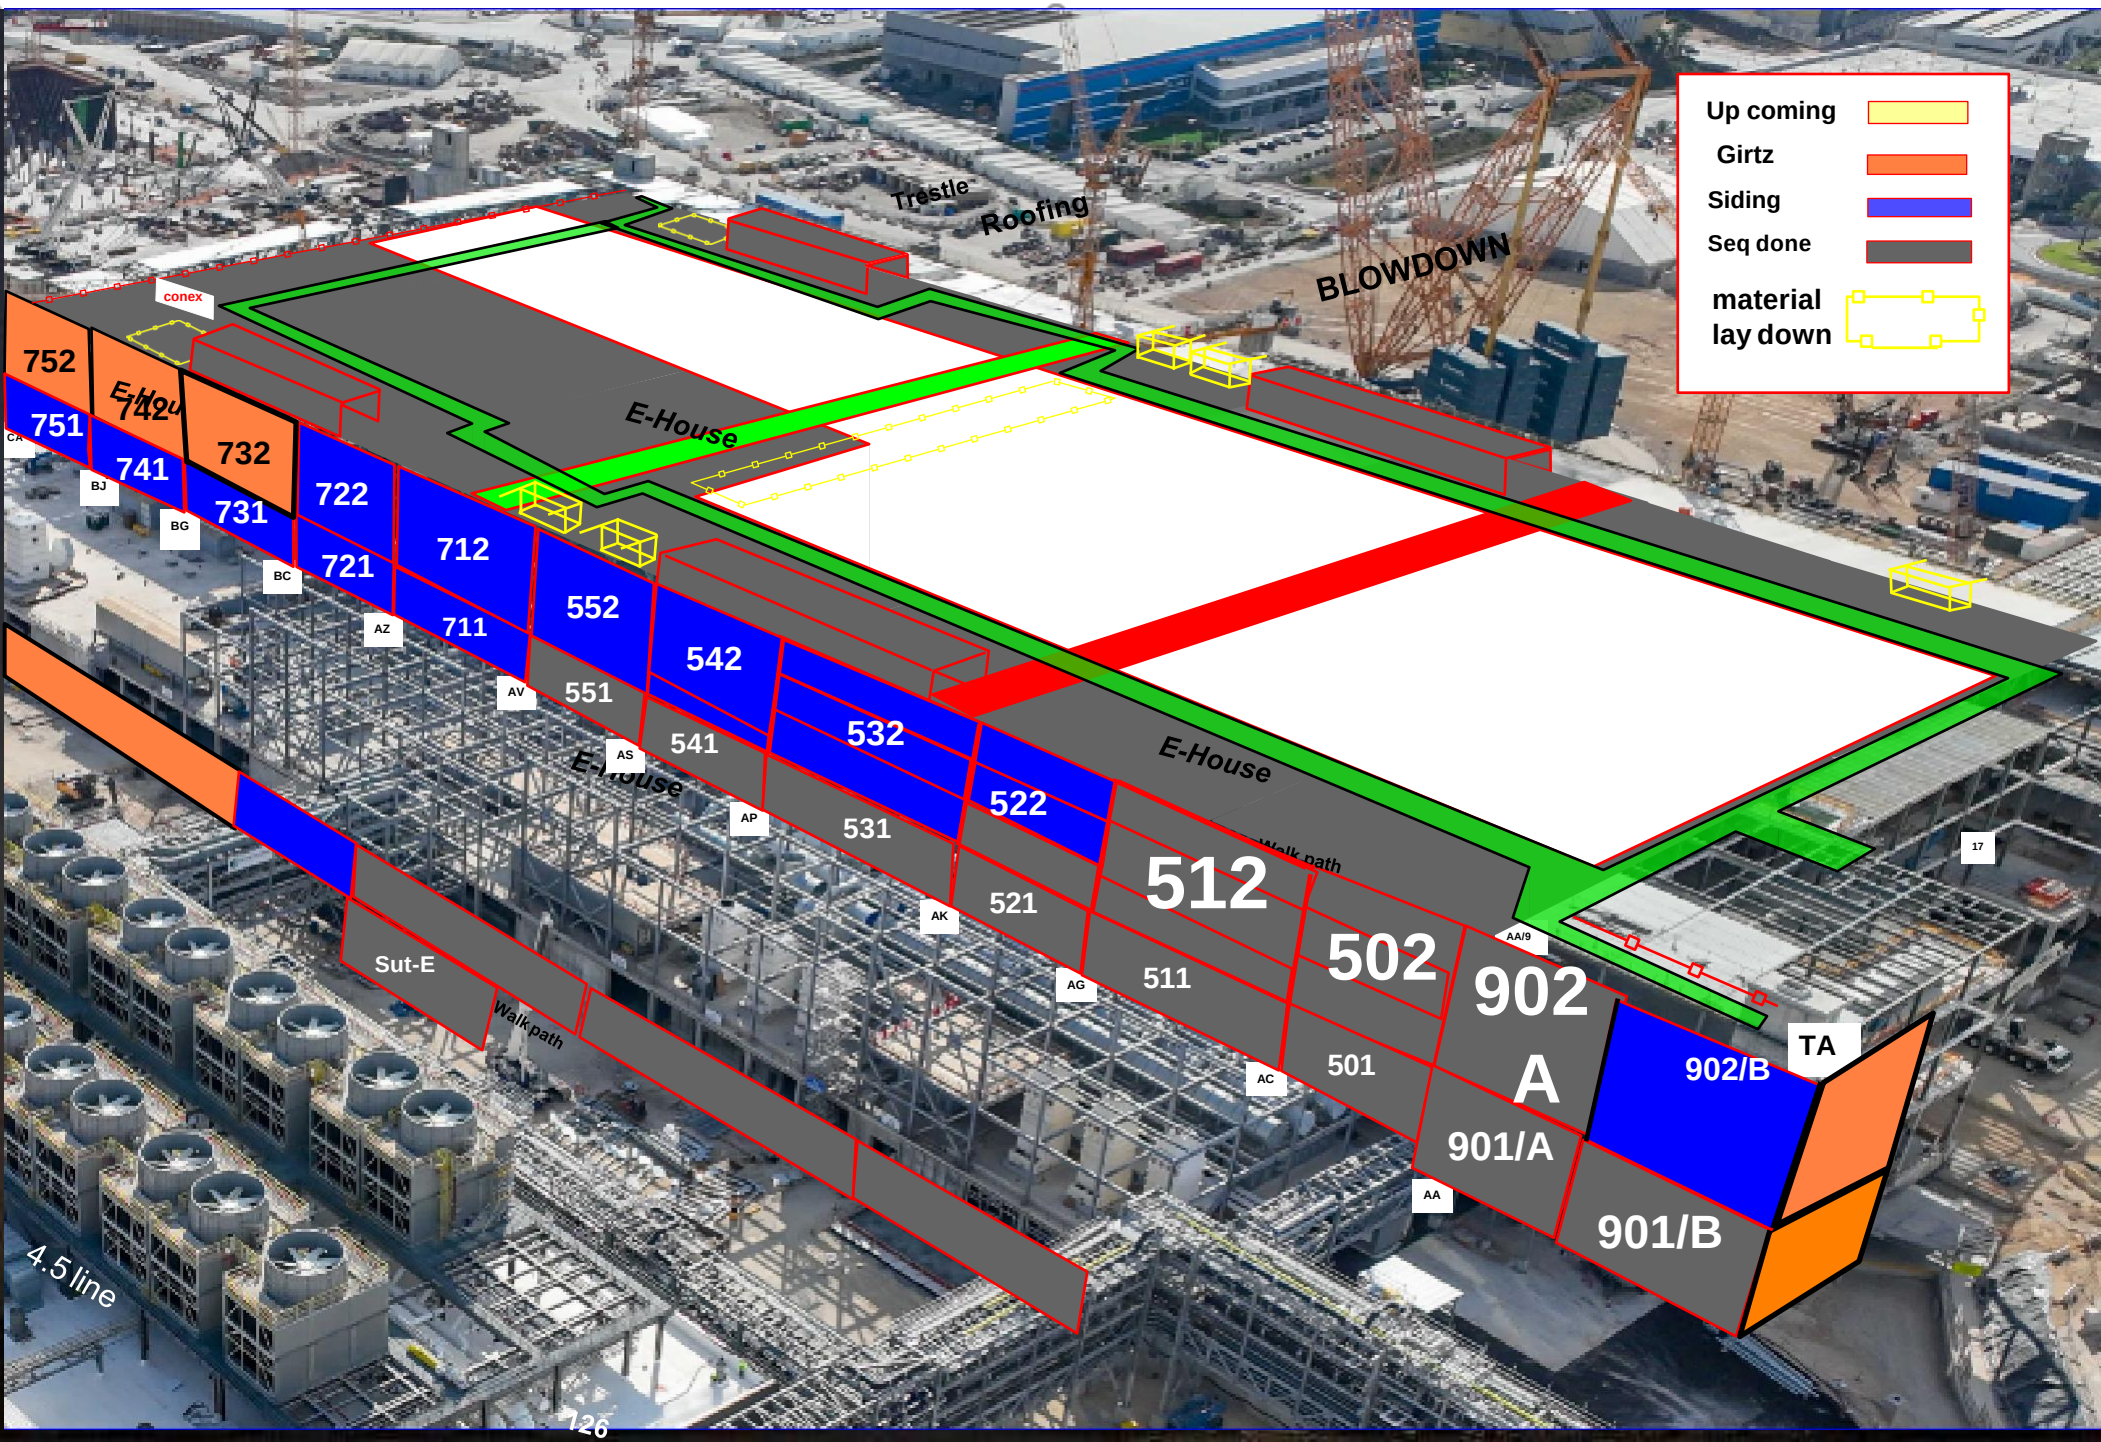

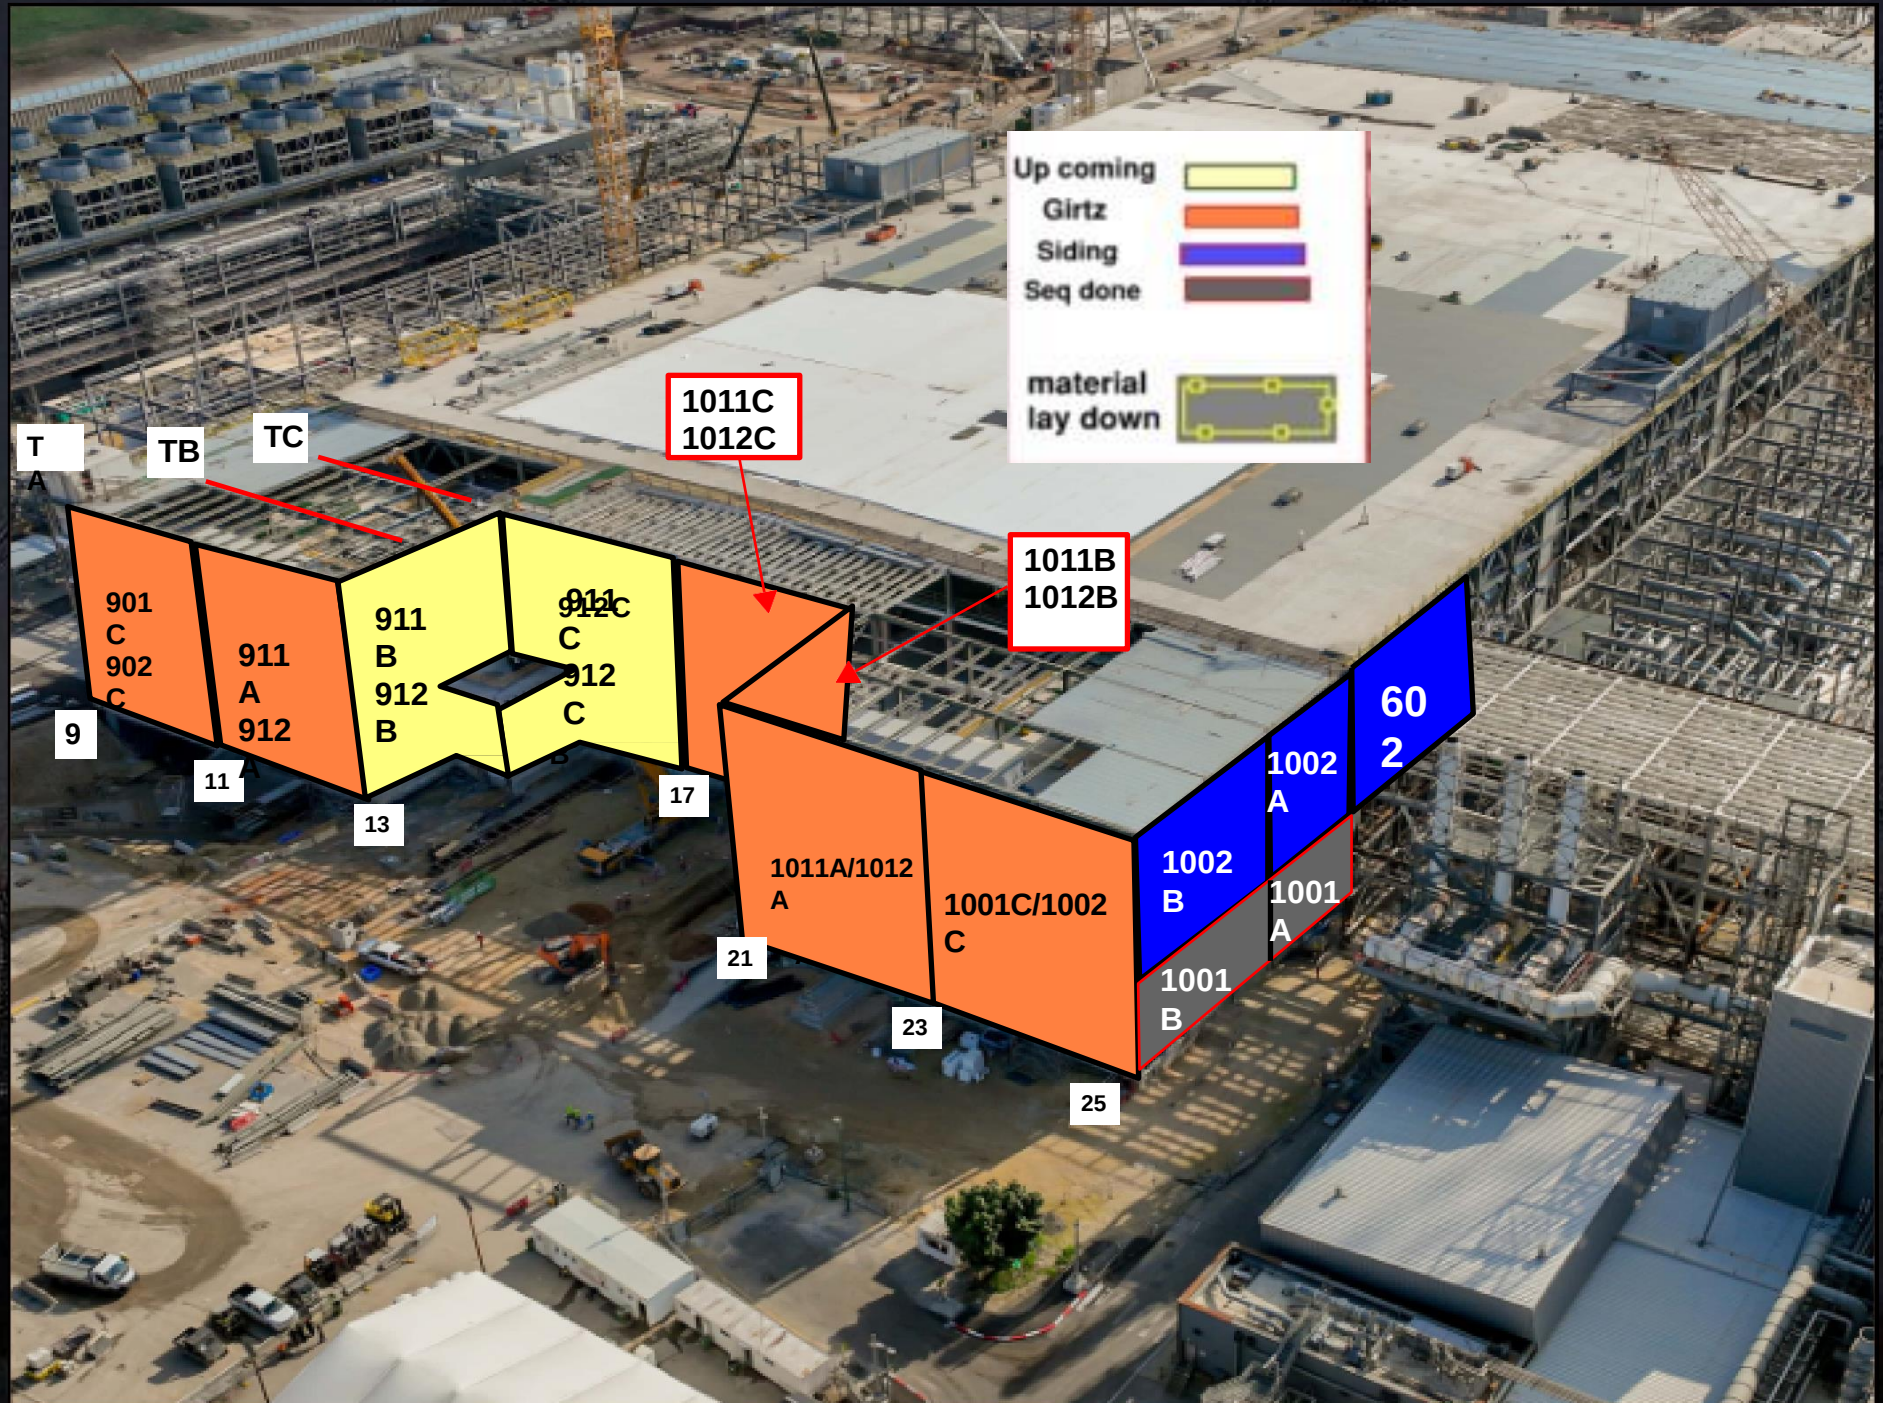


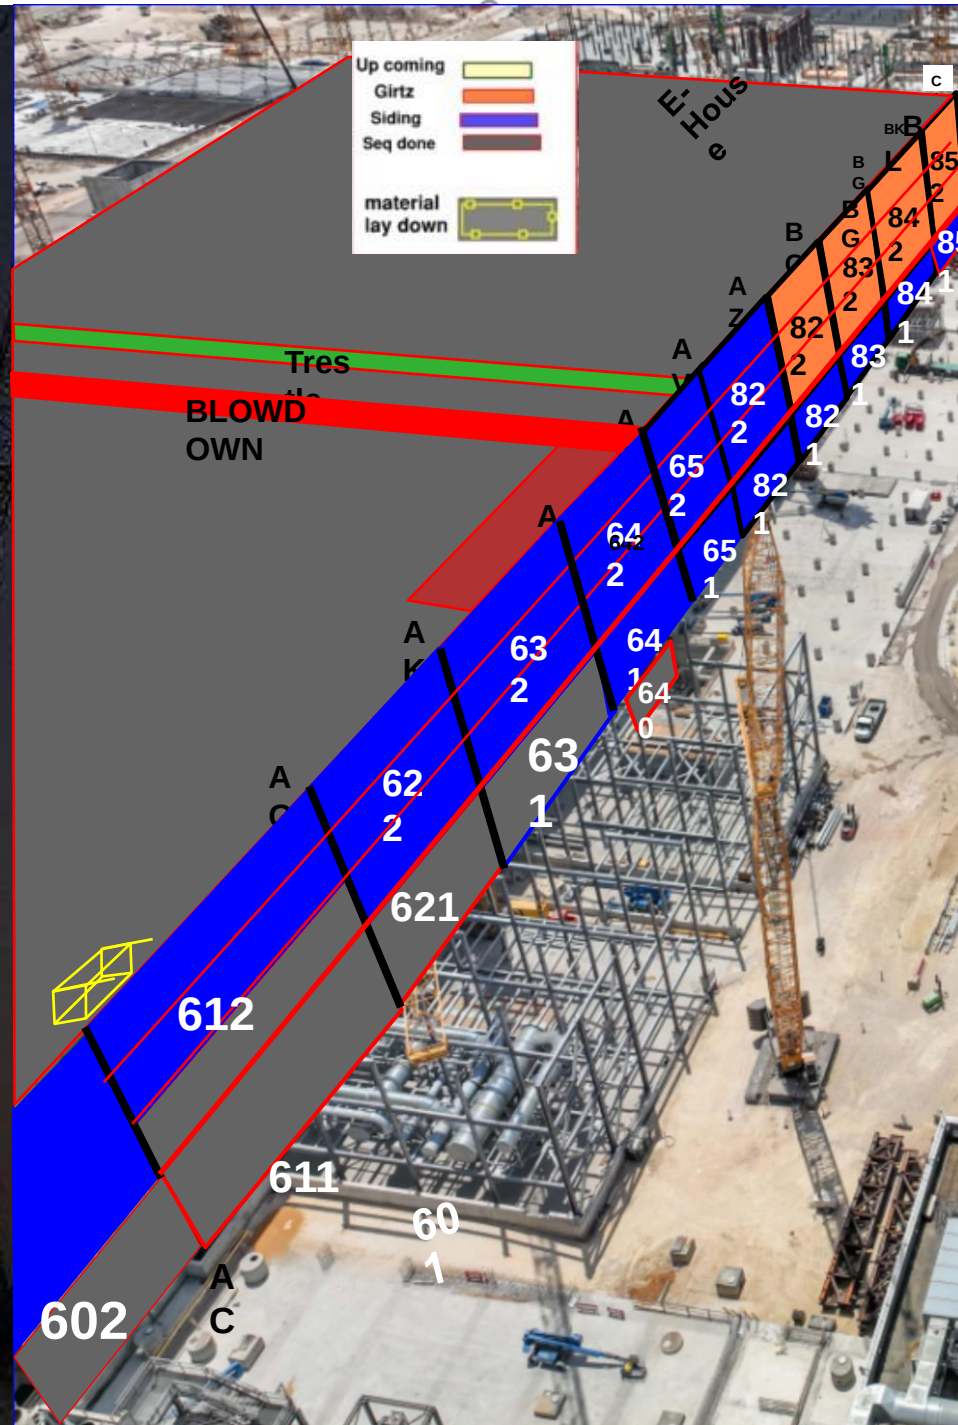

PSSS.1

Utility Level
1YA

PSSS Roof
2SA

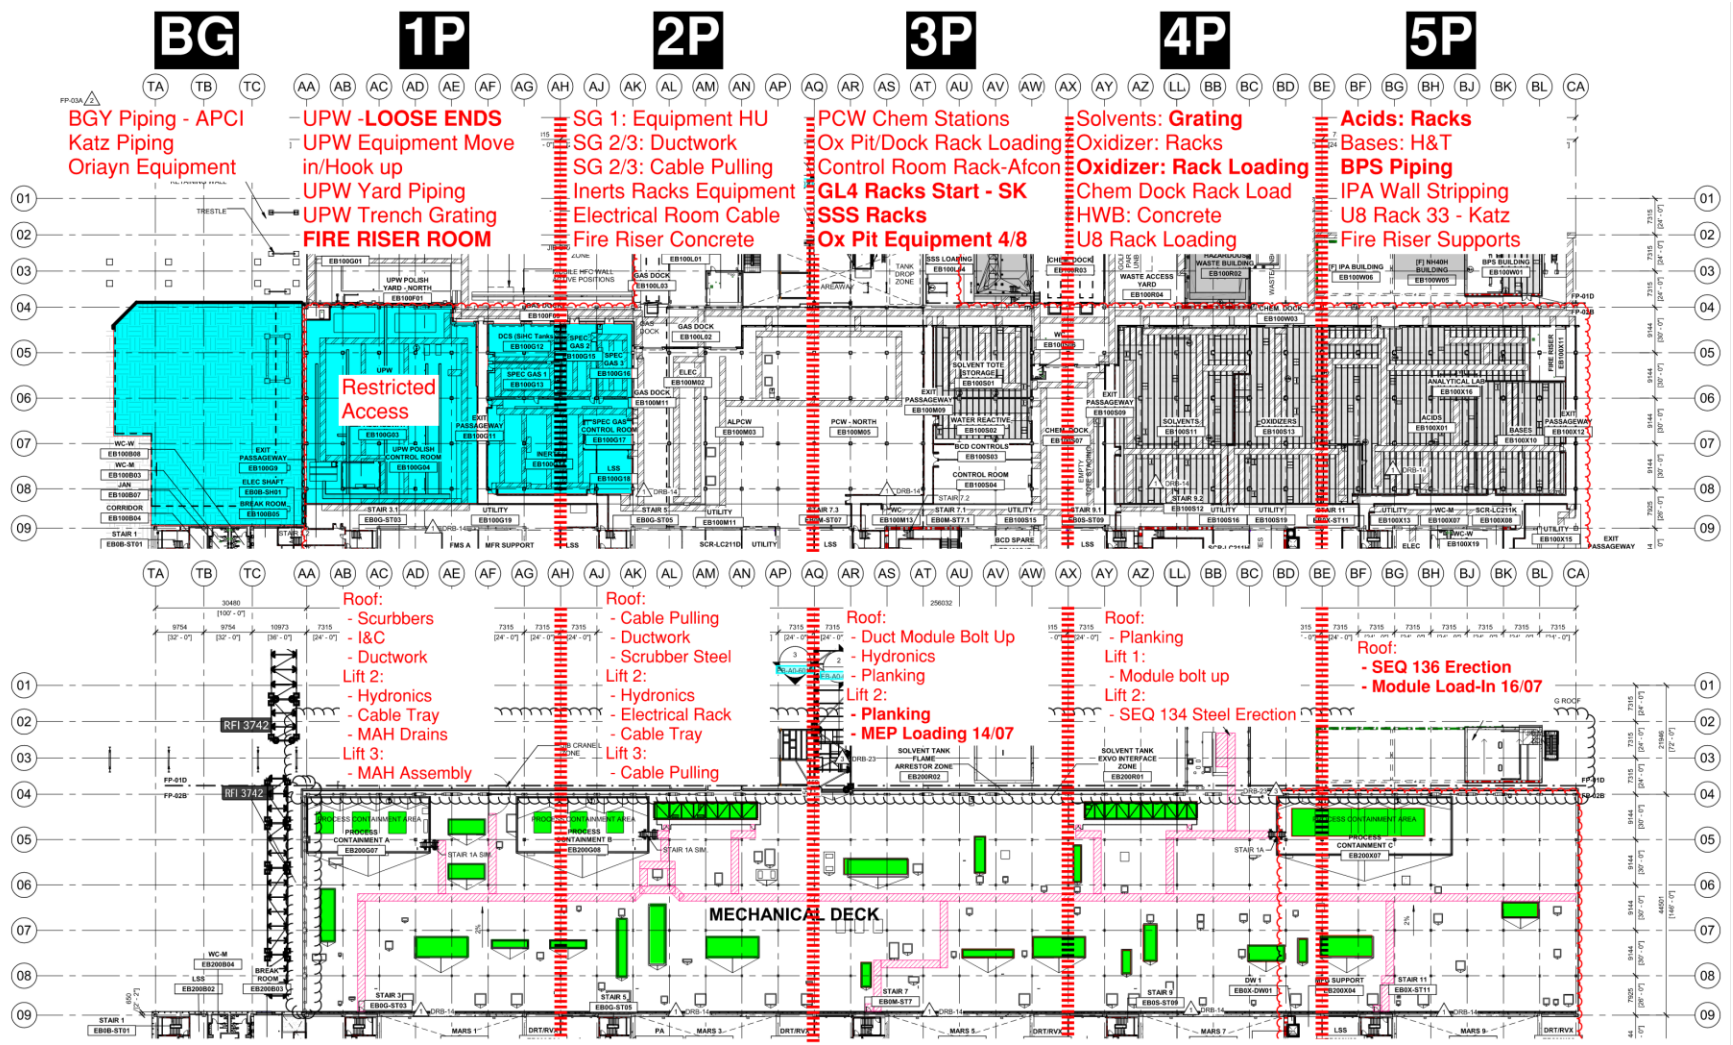


PSSS.2

Utility Level


1YA

PSSS Roof 2SA

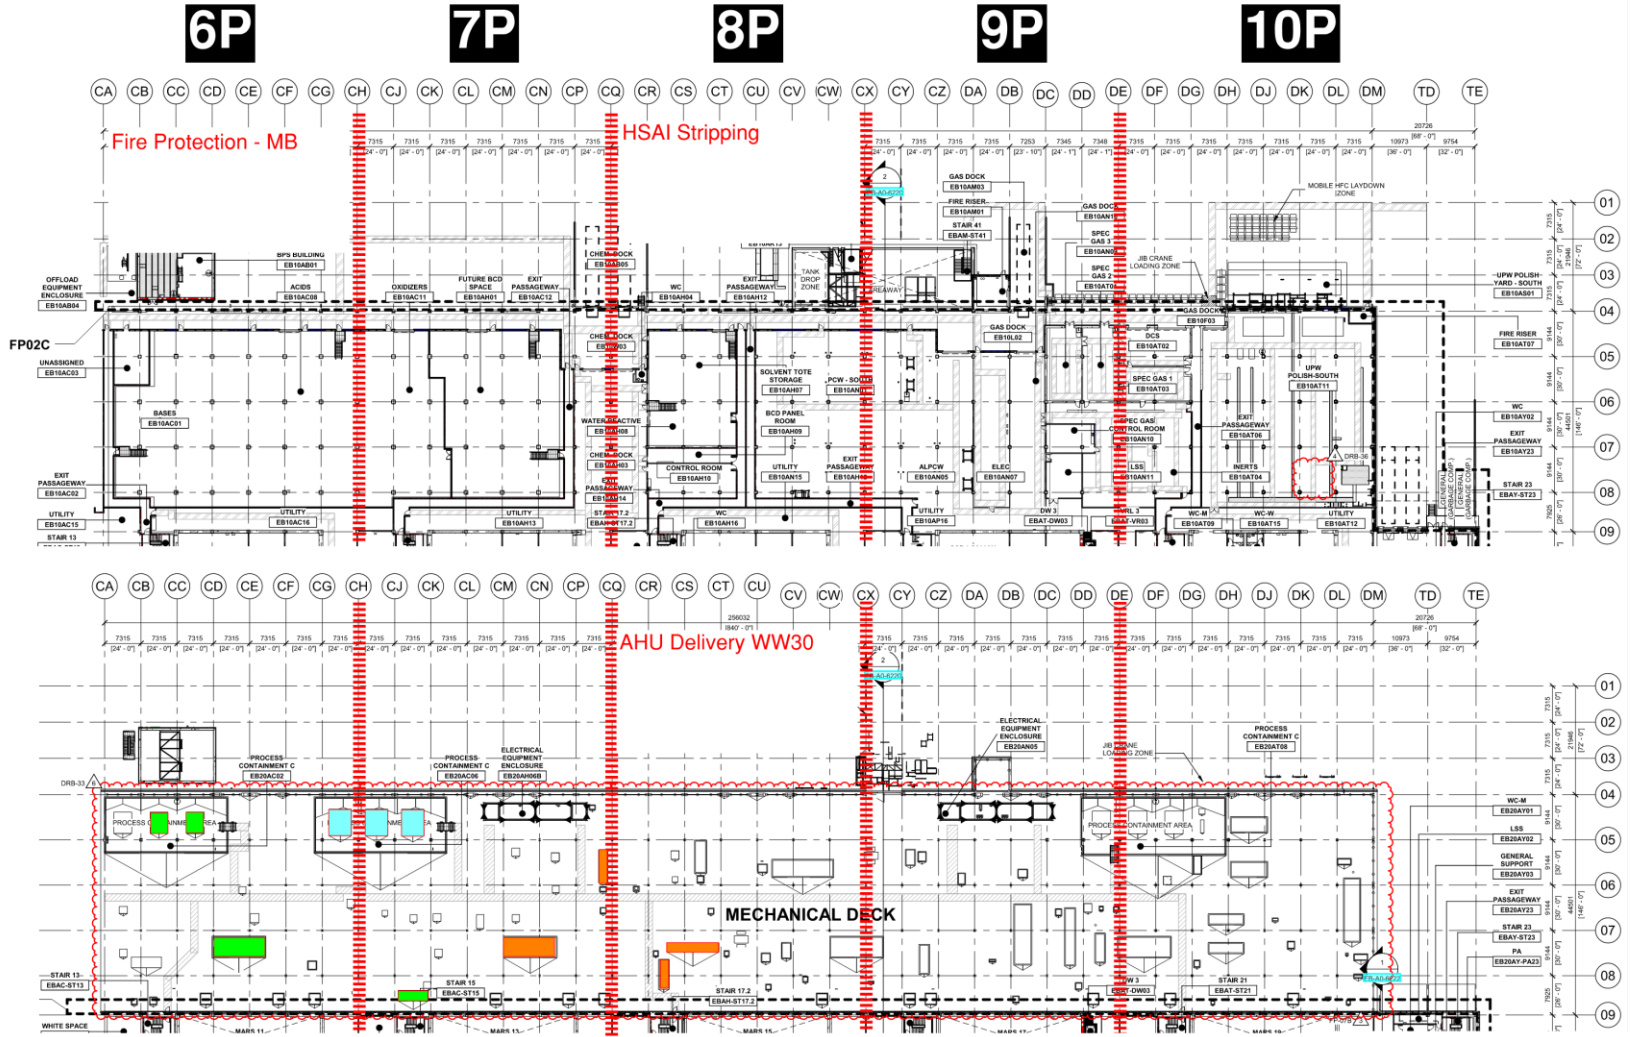


PSSS DMAG DISMANTLE

- July 21st-25th
 - UPW MIMO CLOSED
 - GAS MIMO CLOSED
 - GUT ROAD BLOCKED FROM TRESTLE BRIDGE TO TRESTLE BRIDGE

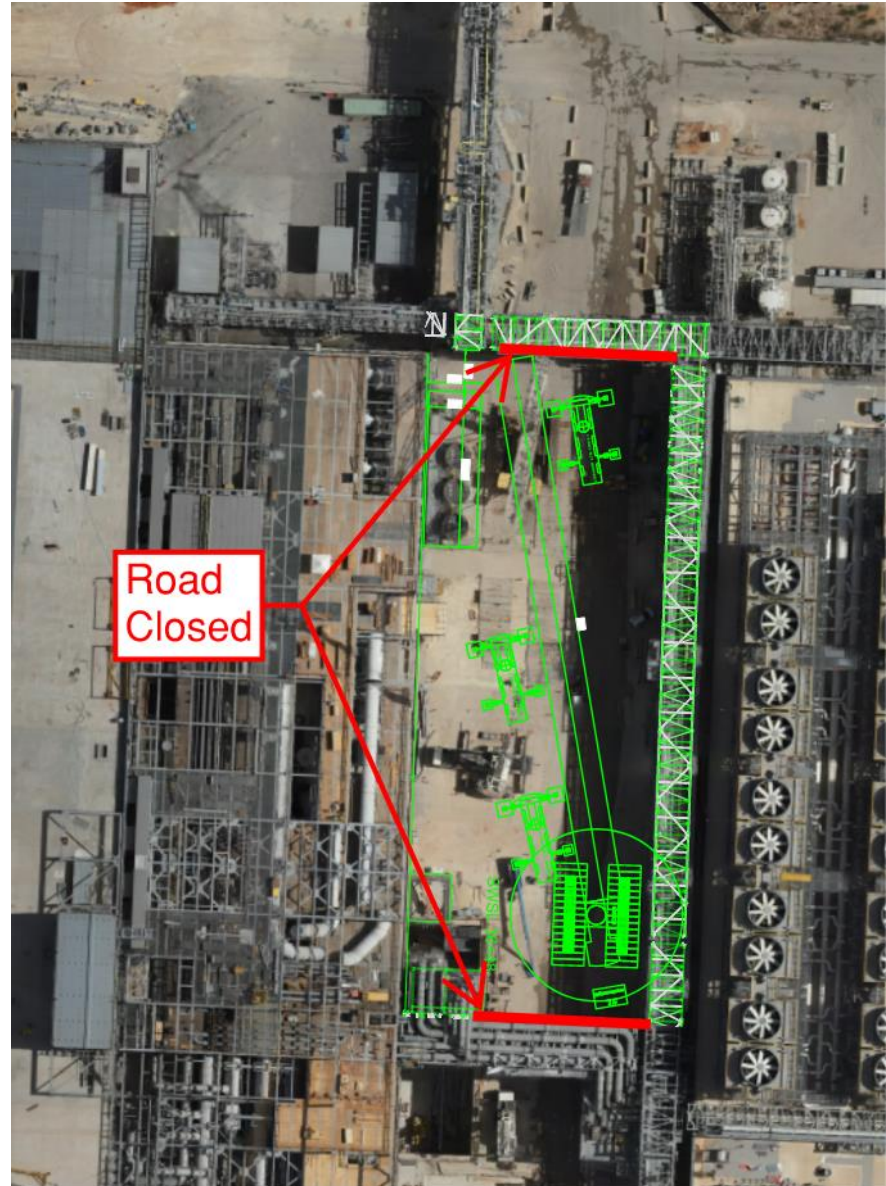

EJG/WJG Grating/Planking Penetrations



JG Grating/Planking Penetrations

Type of Penetration *
What side of the building is the penetration located?

Location of Penetration *
Provide gridlines of where the penetration is needed

Zone of Penetration *
What zone is the penetration

Lift of Penetration *
What lift of Steel is the penetration

Gridlines of Penetration *
Input the gridlines of where the penetration is located

Size of Penetration *
Put size of penetration required in mm

Contact Company *

Contact Number *
Contact number in the case of questions

Contact Email *
Email of person to get notifications on penetration

Layout Confirmation *
Confirmation that layout has been confirmed by requesting contractor. If layout is incorrect, the requesting contractor will be responsible for all fixes, build backs, replacement, etc. cost associated with the incorrect layout.
☐

Photo of Layout in the field *
Upload a photo of the layout once complete

Drag and drop files here or [browse files](#)

☐ Send me a copy of my responses



WJG 01J, 02J LIFT 2 & 3





WJG 03J, 04J, 05J LIFT 2 & 3








WJG UTILITY LEVEL BUILD OUT

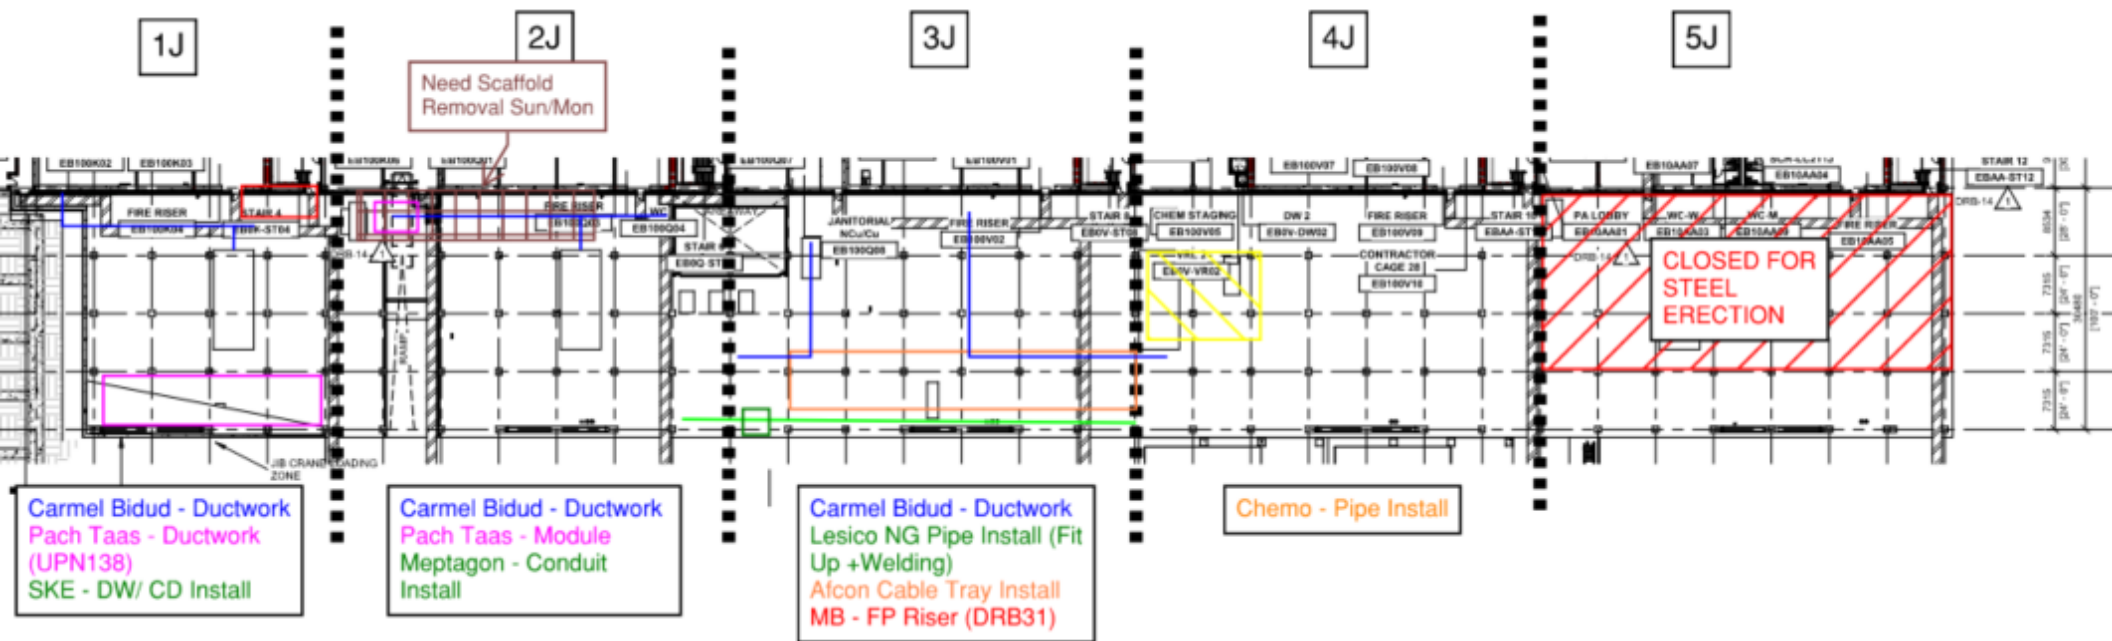

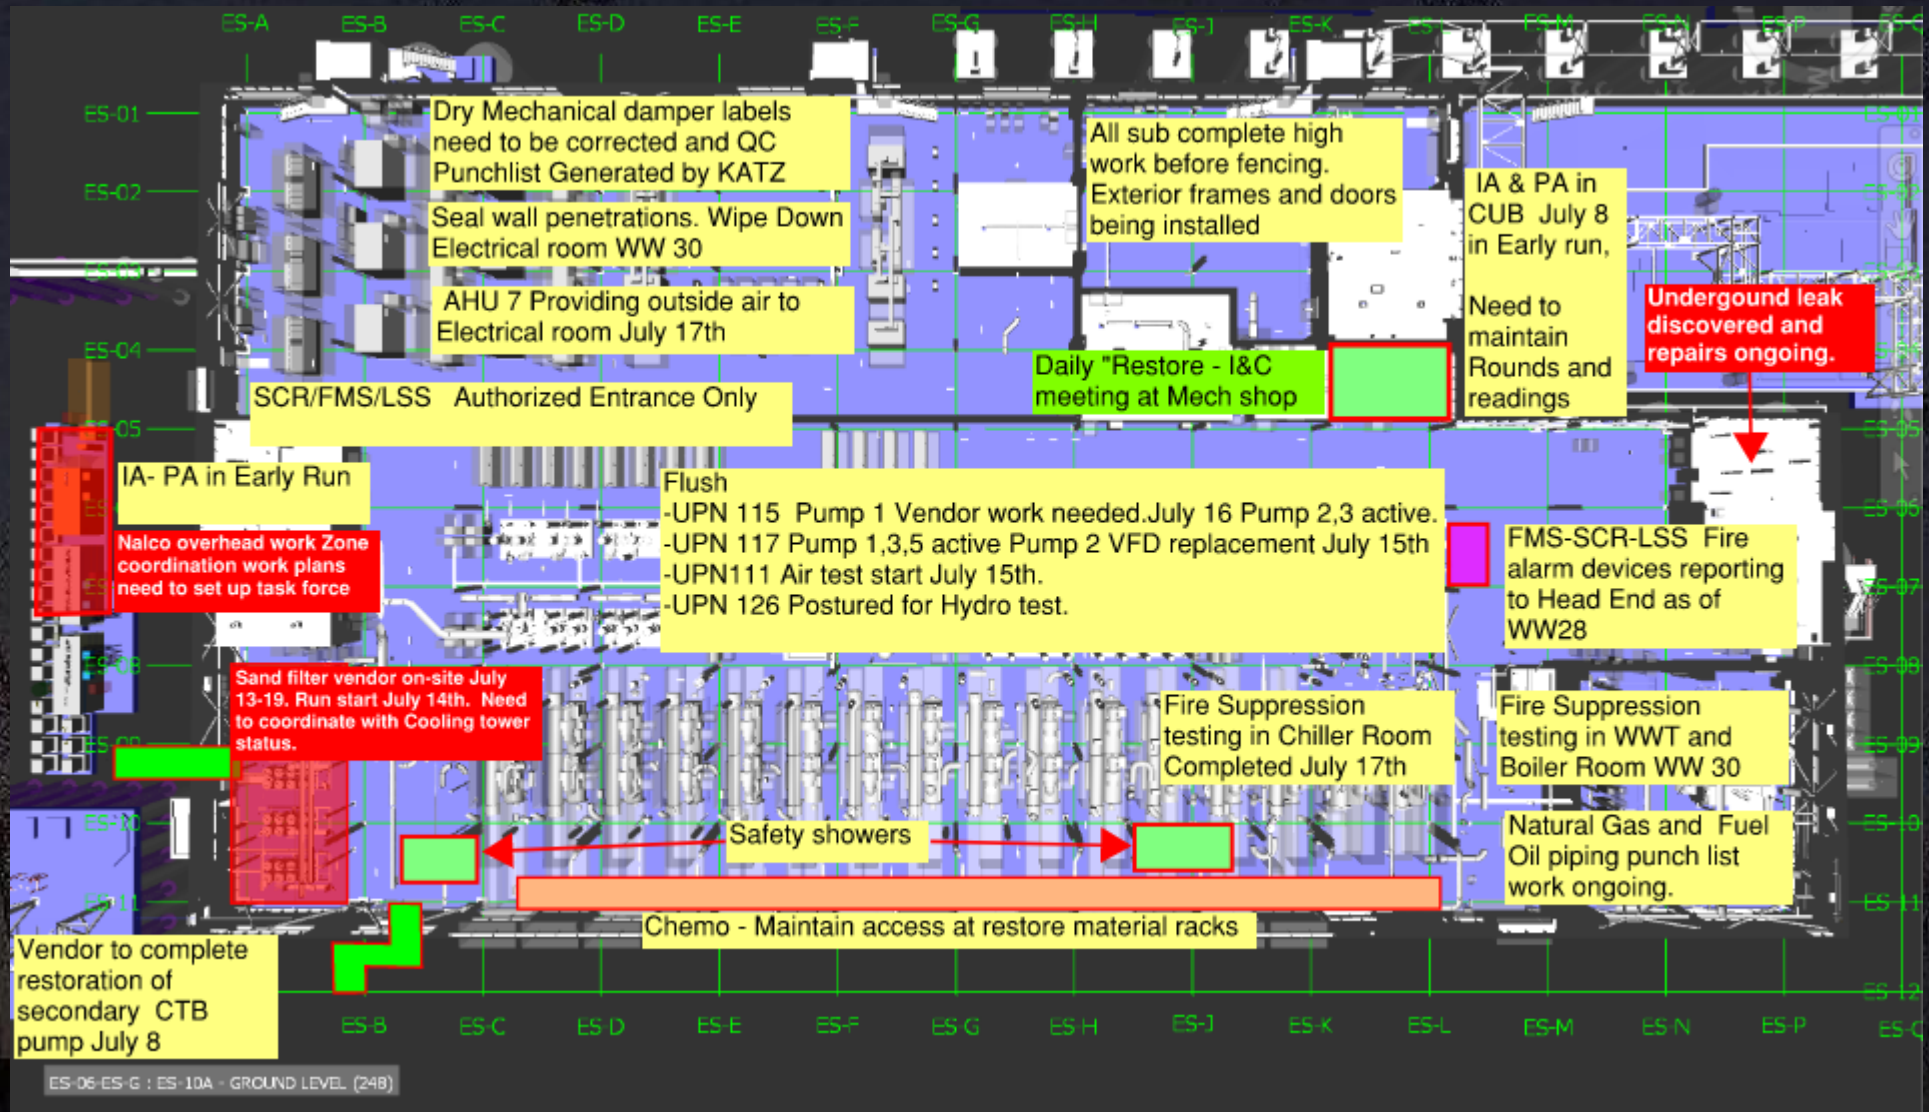

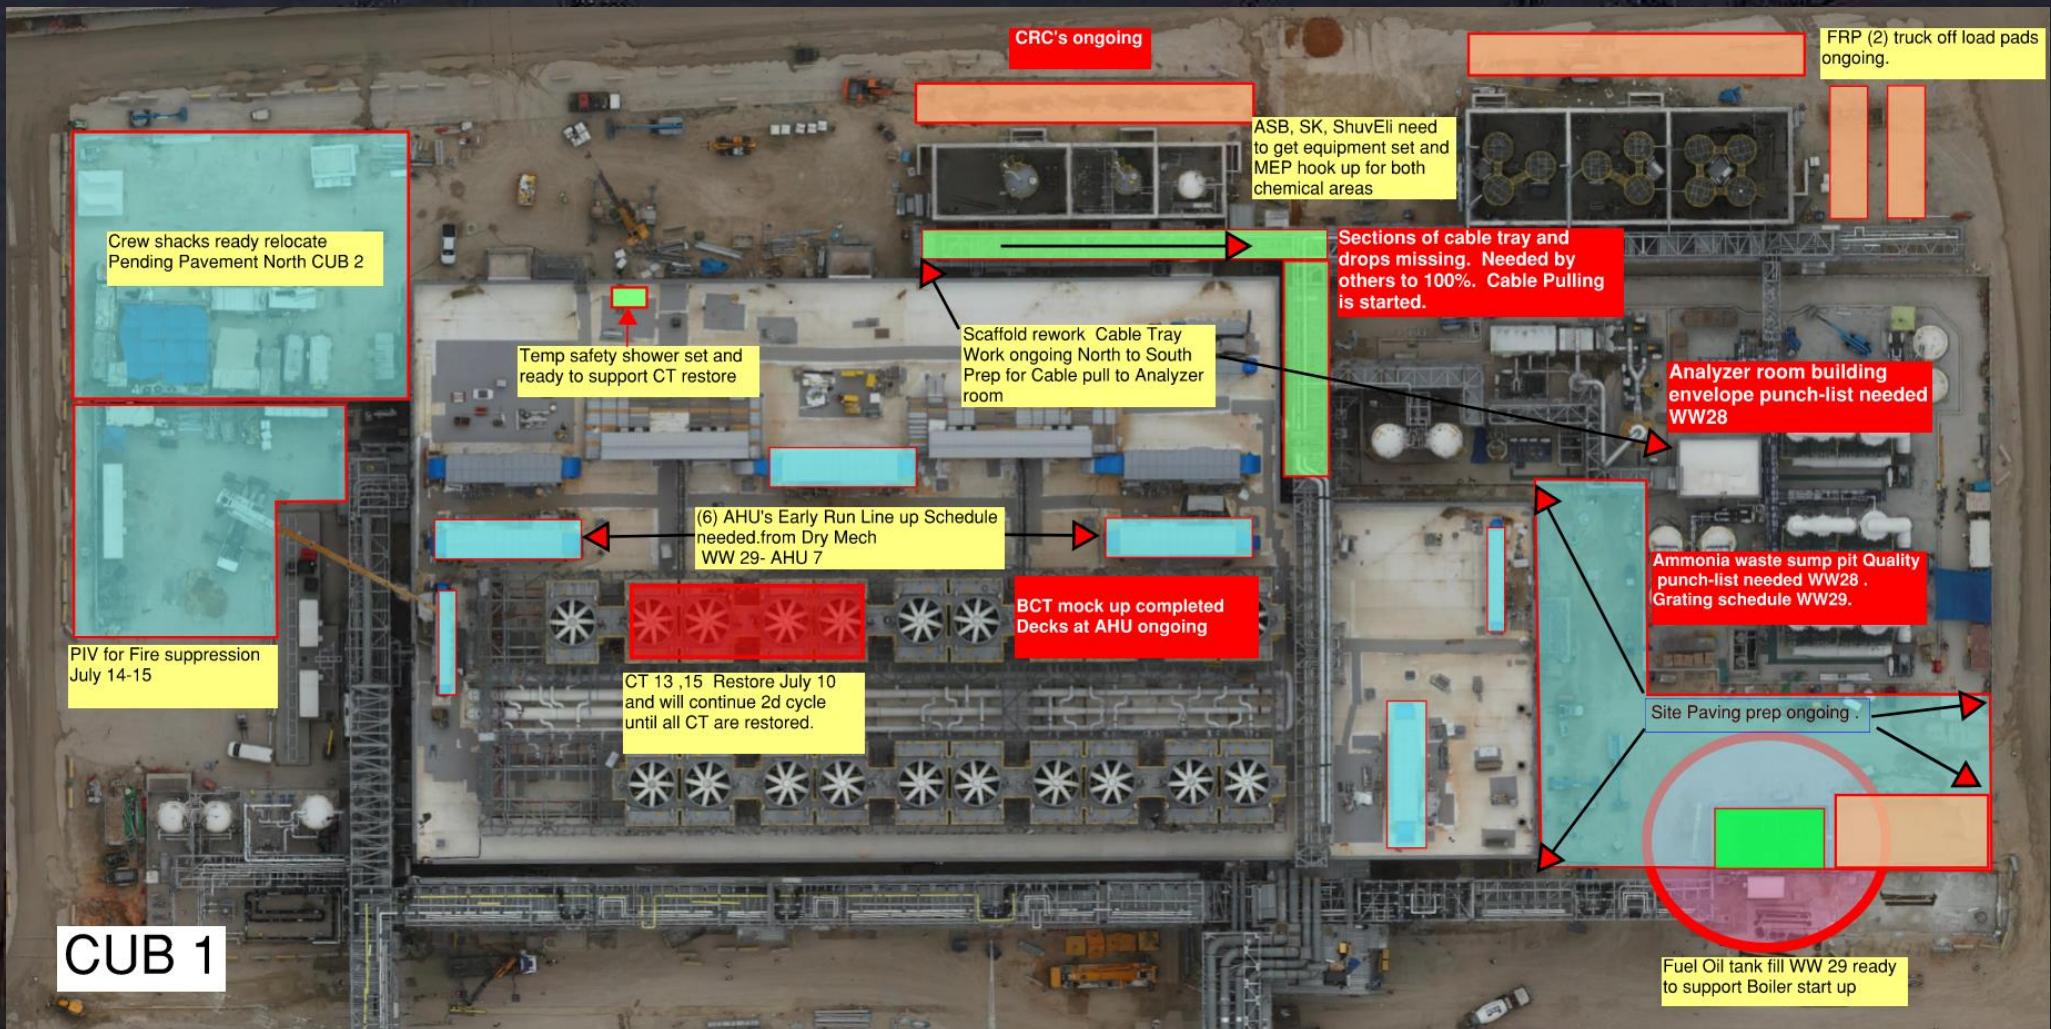

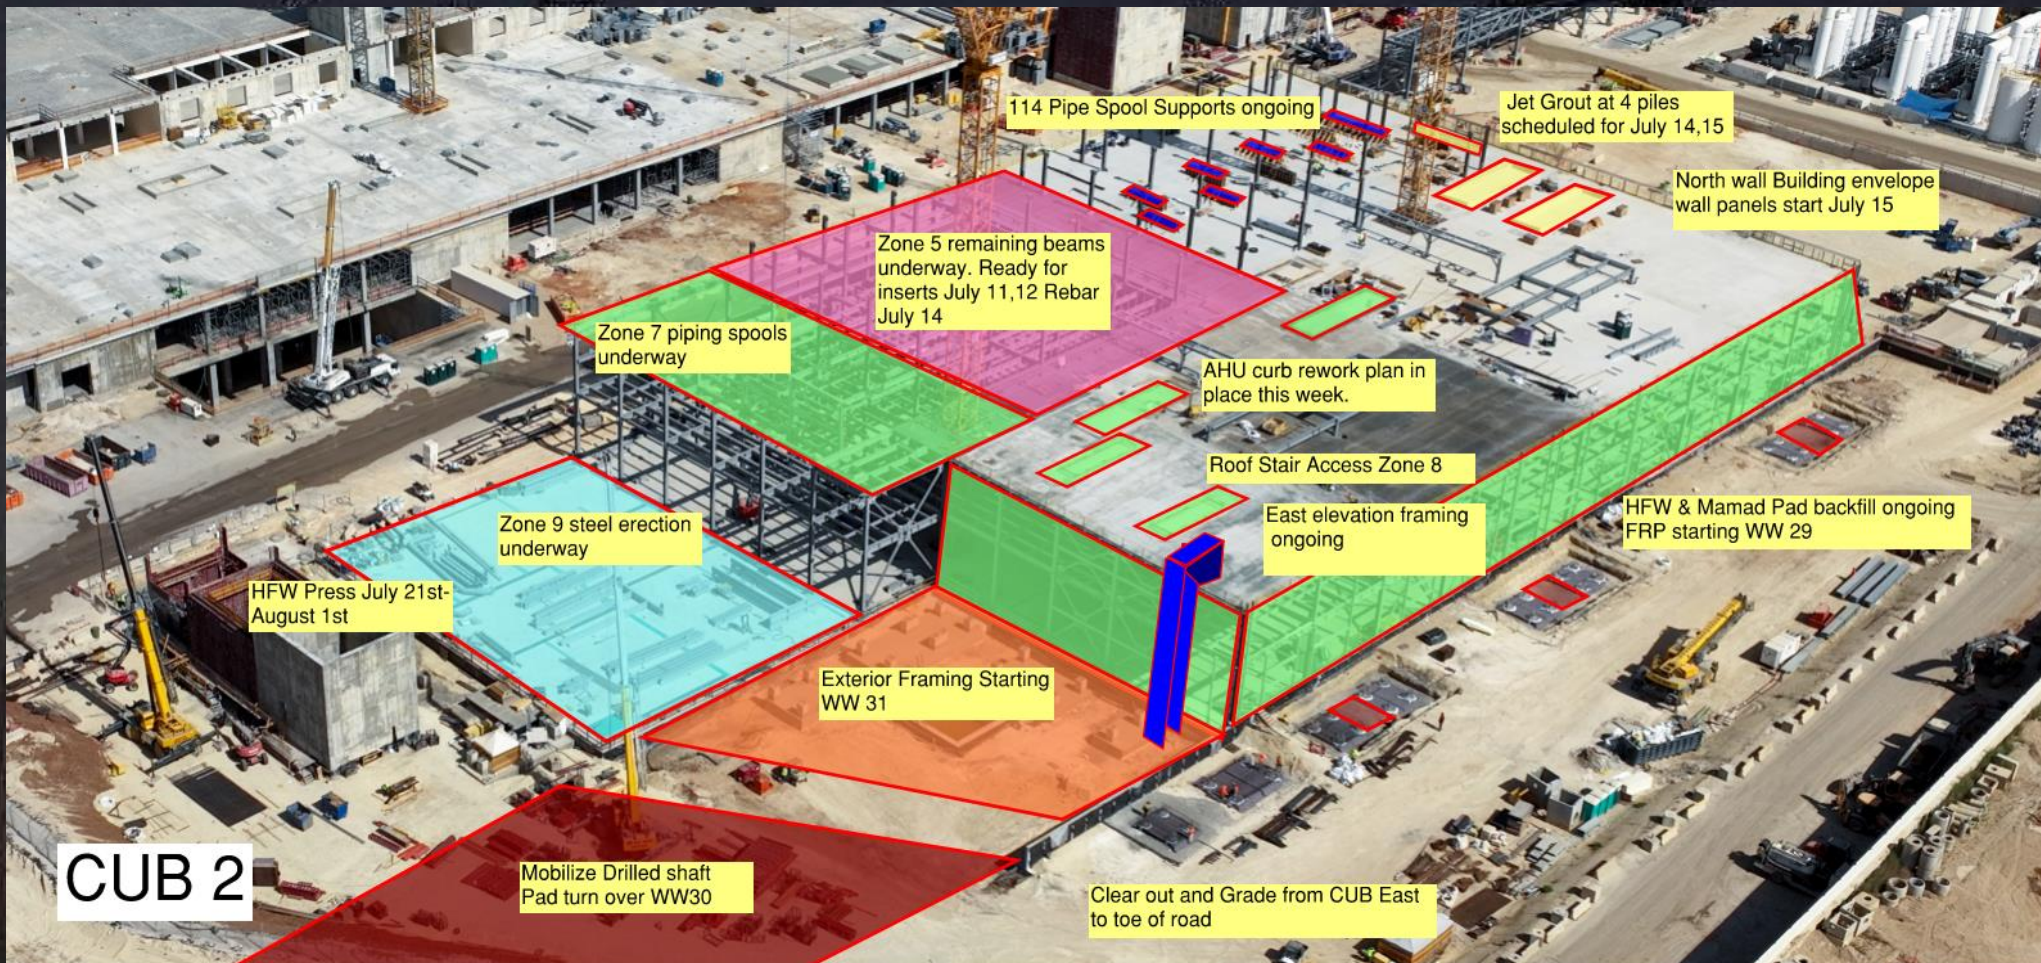

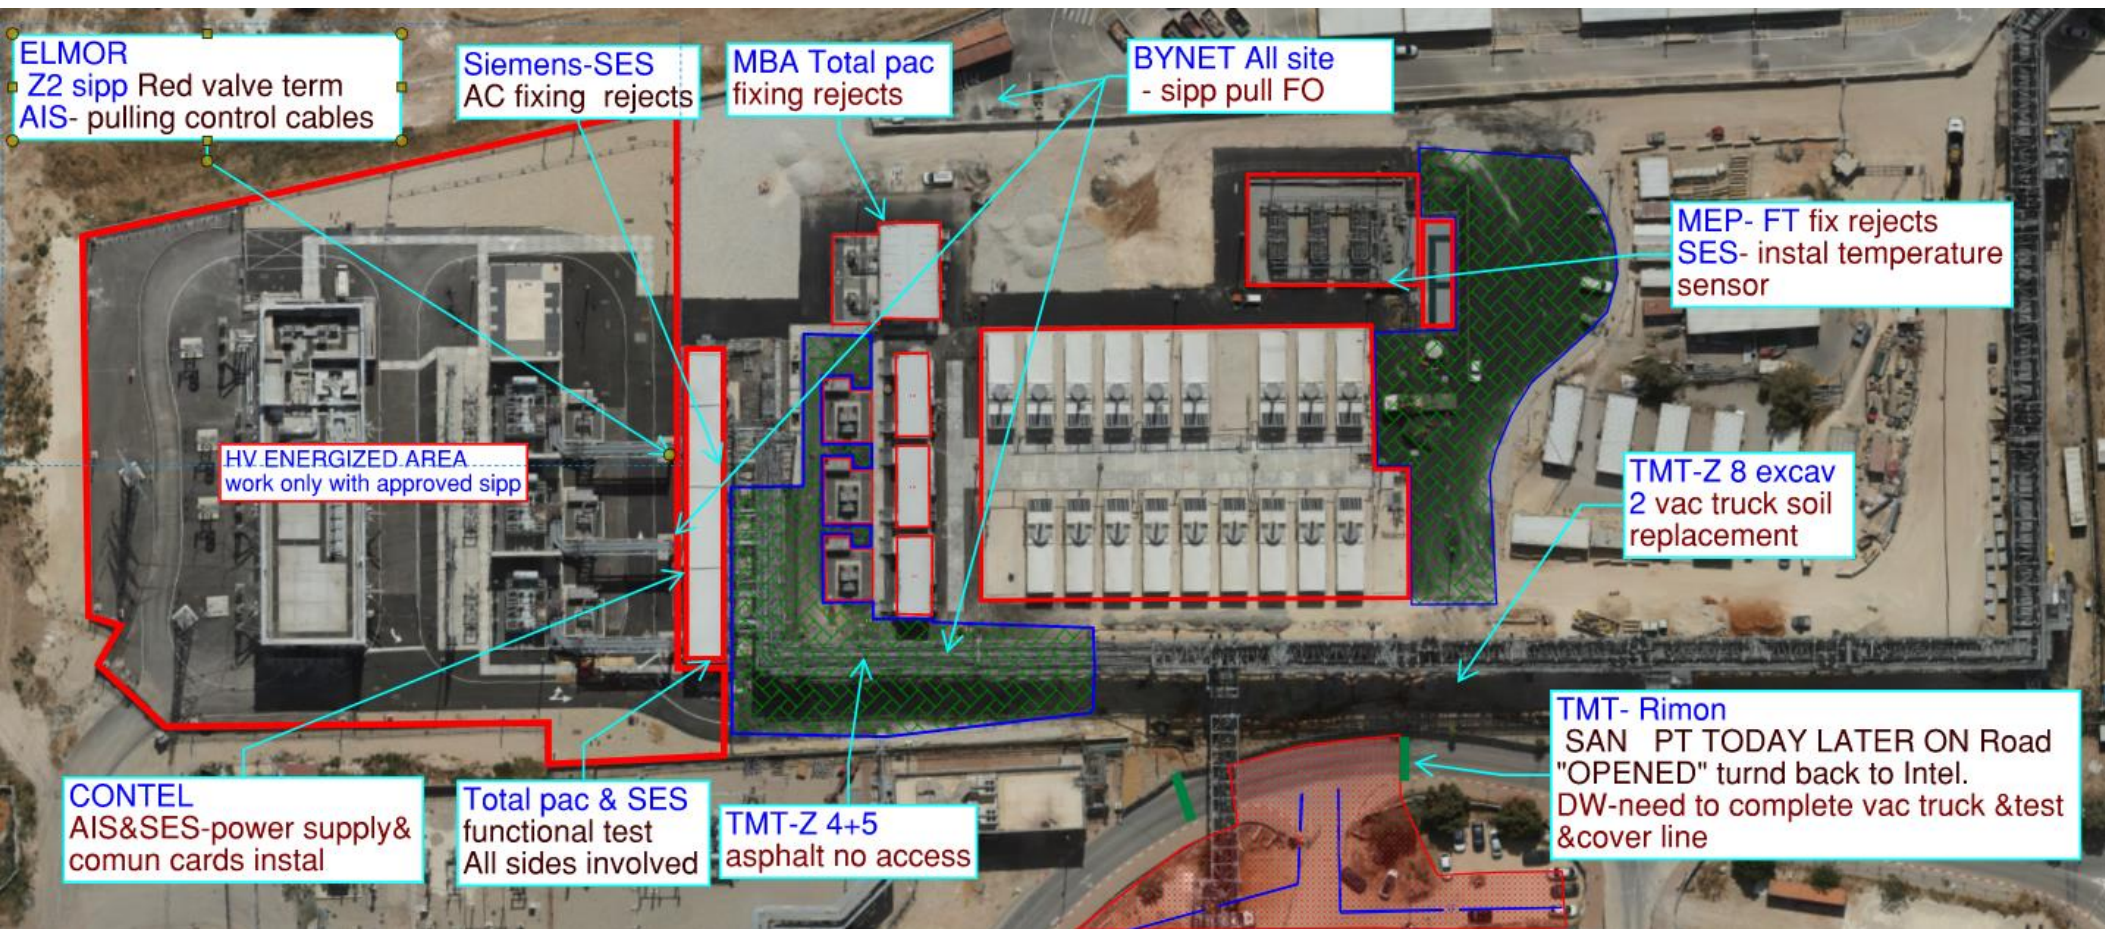

Trench lids will be instal 5/9/24
complete your sow before.


crane
locati
on

HRA AREA

Planning machinery-
truck, boom lift, fork
... etc work- requires
coordination in
advance Hcc Sup &
meet the requirement
before starting work
to insure not damage
facilities

For all subs
for compeleting SOW to submit microshedule till
25.07.24 for each sow , including disconnect &
evacuate trailers & material & must comply with
P6 SCHEDULE 100%
after NEY area turned to intel need sipp all NEY



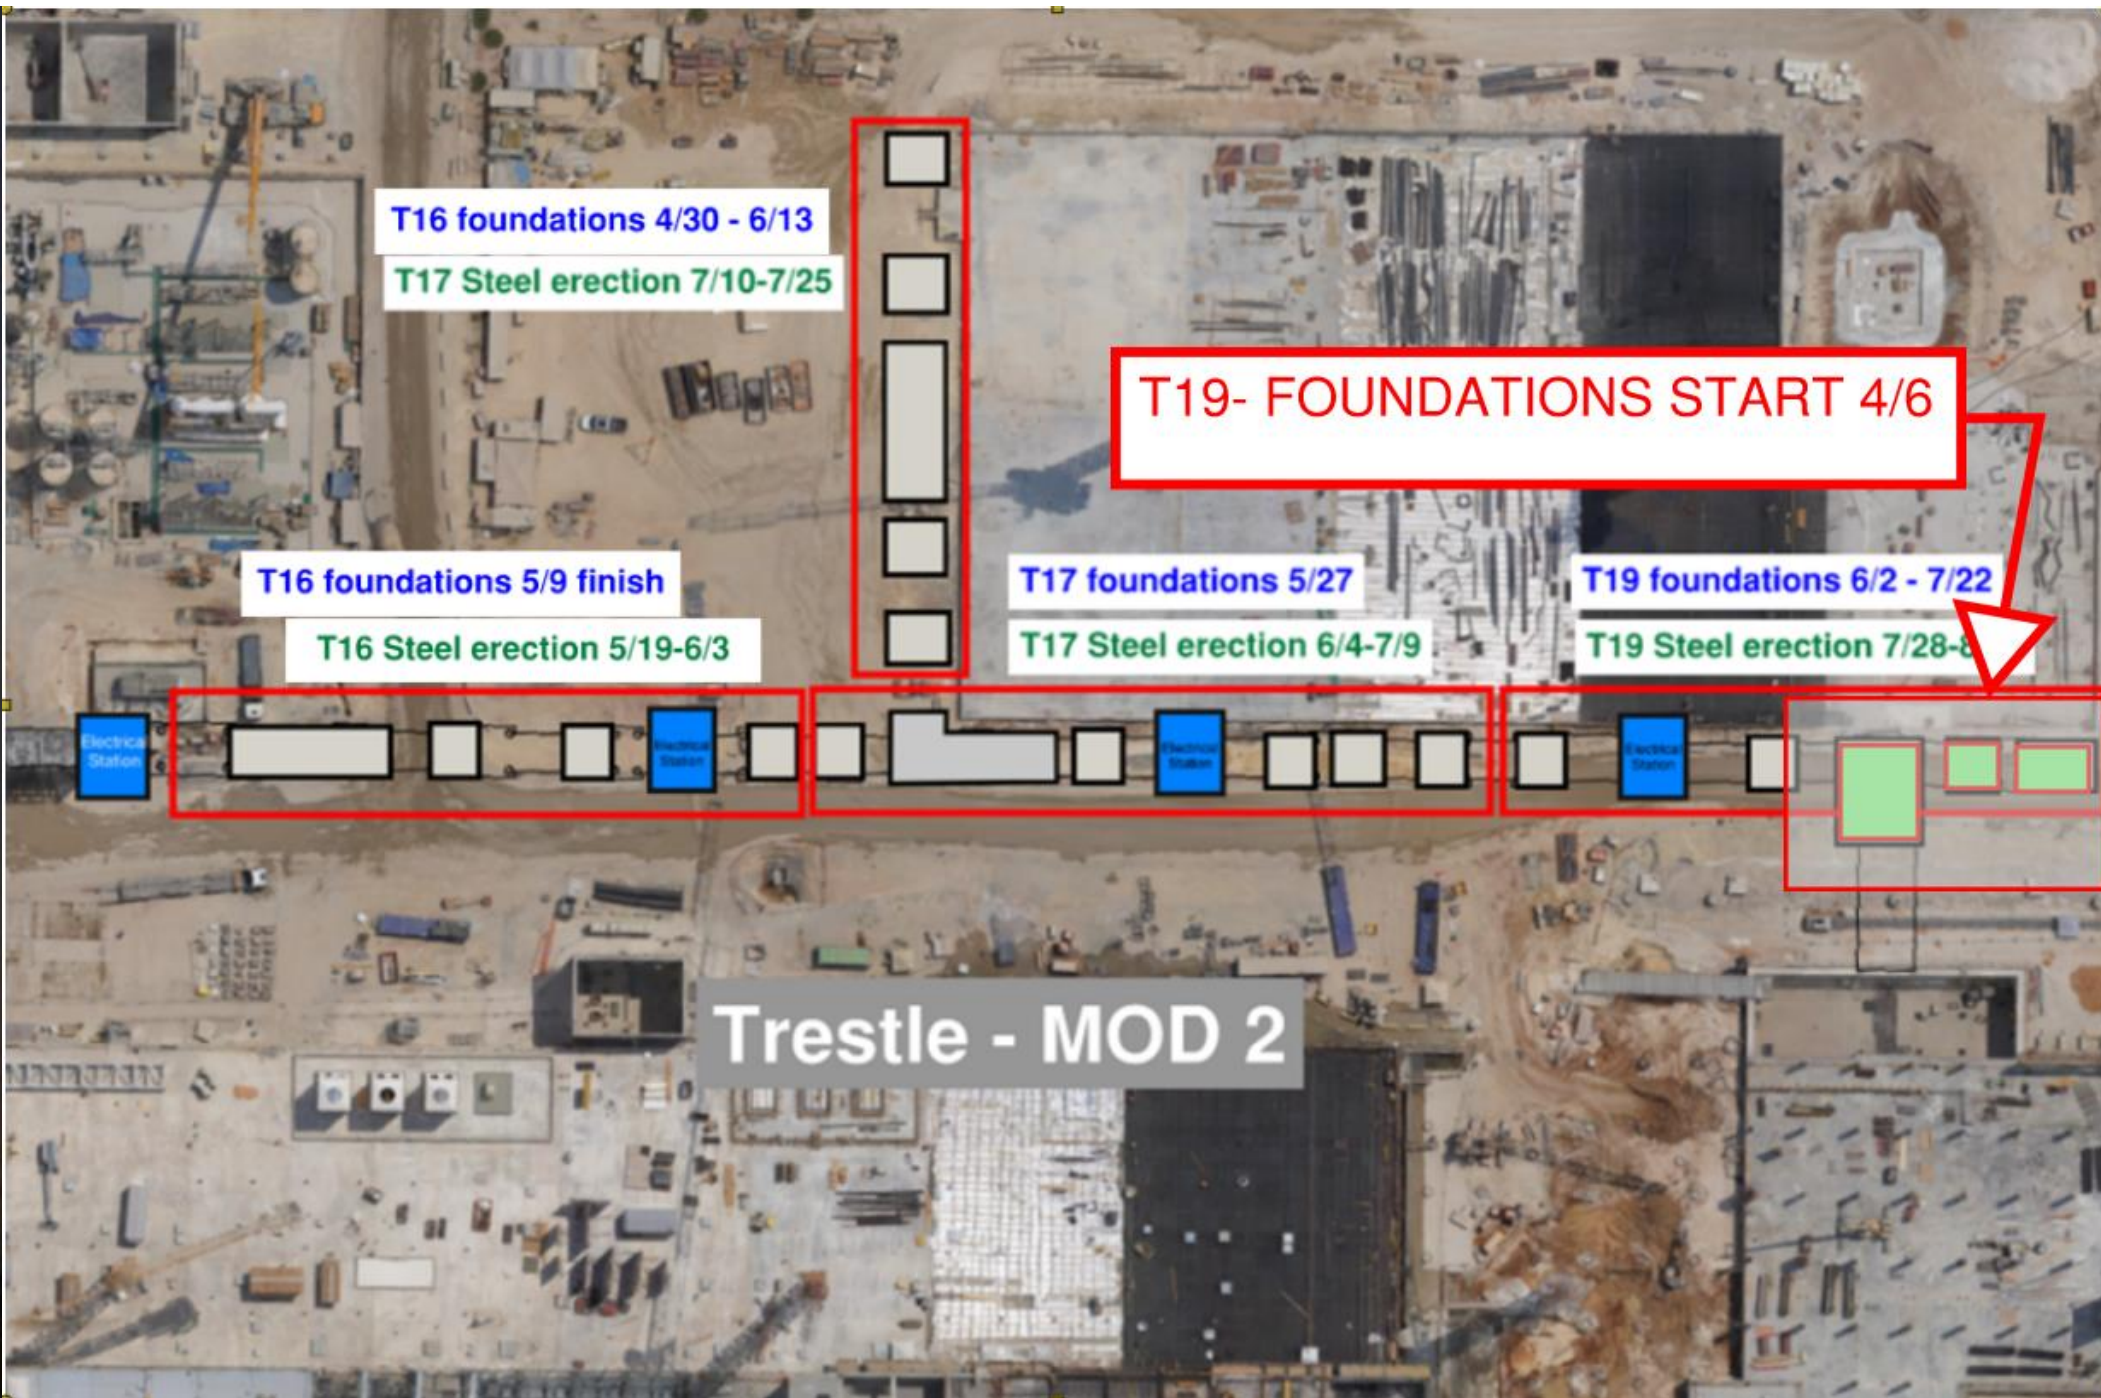




2 Modules delivered to the site today 22:00


Modules

Spreader

10m

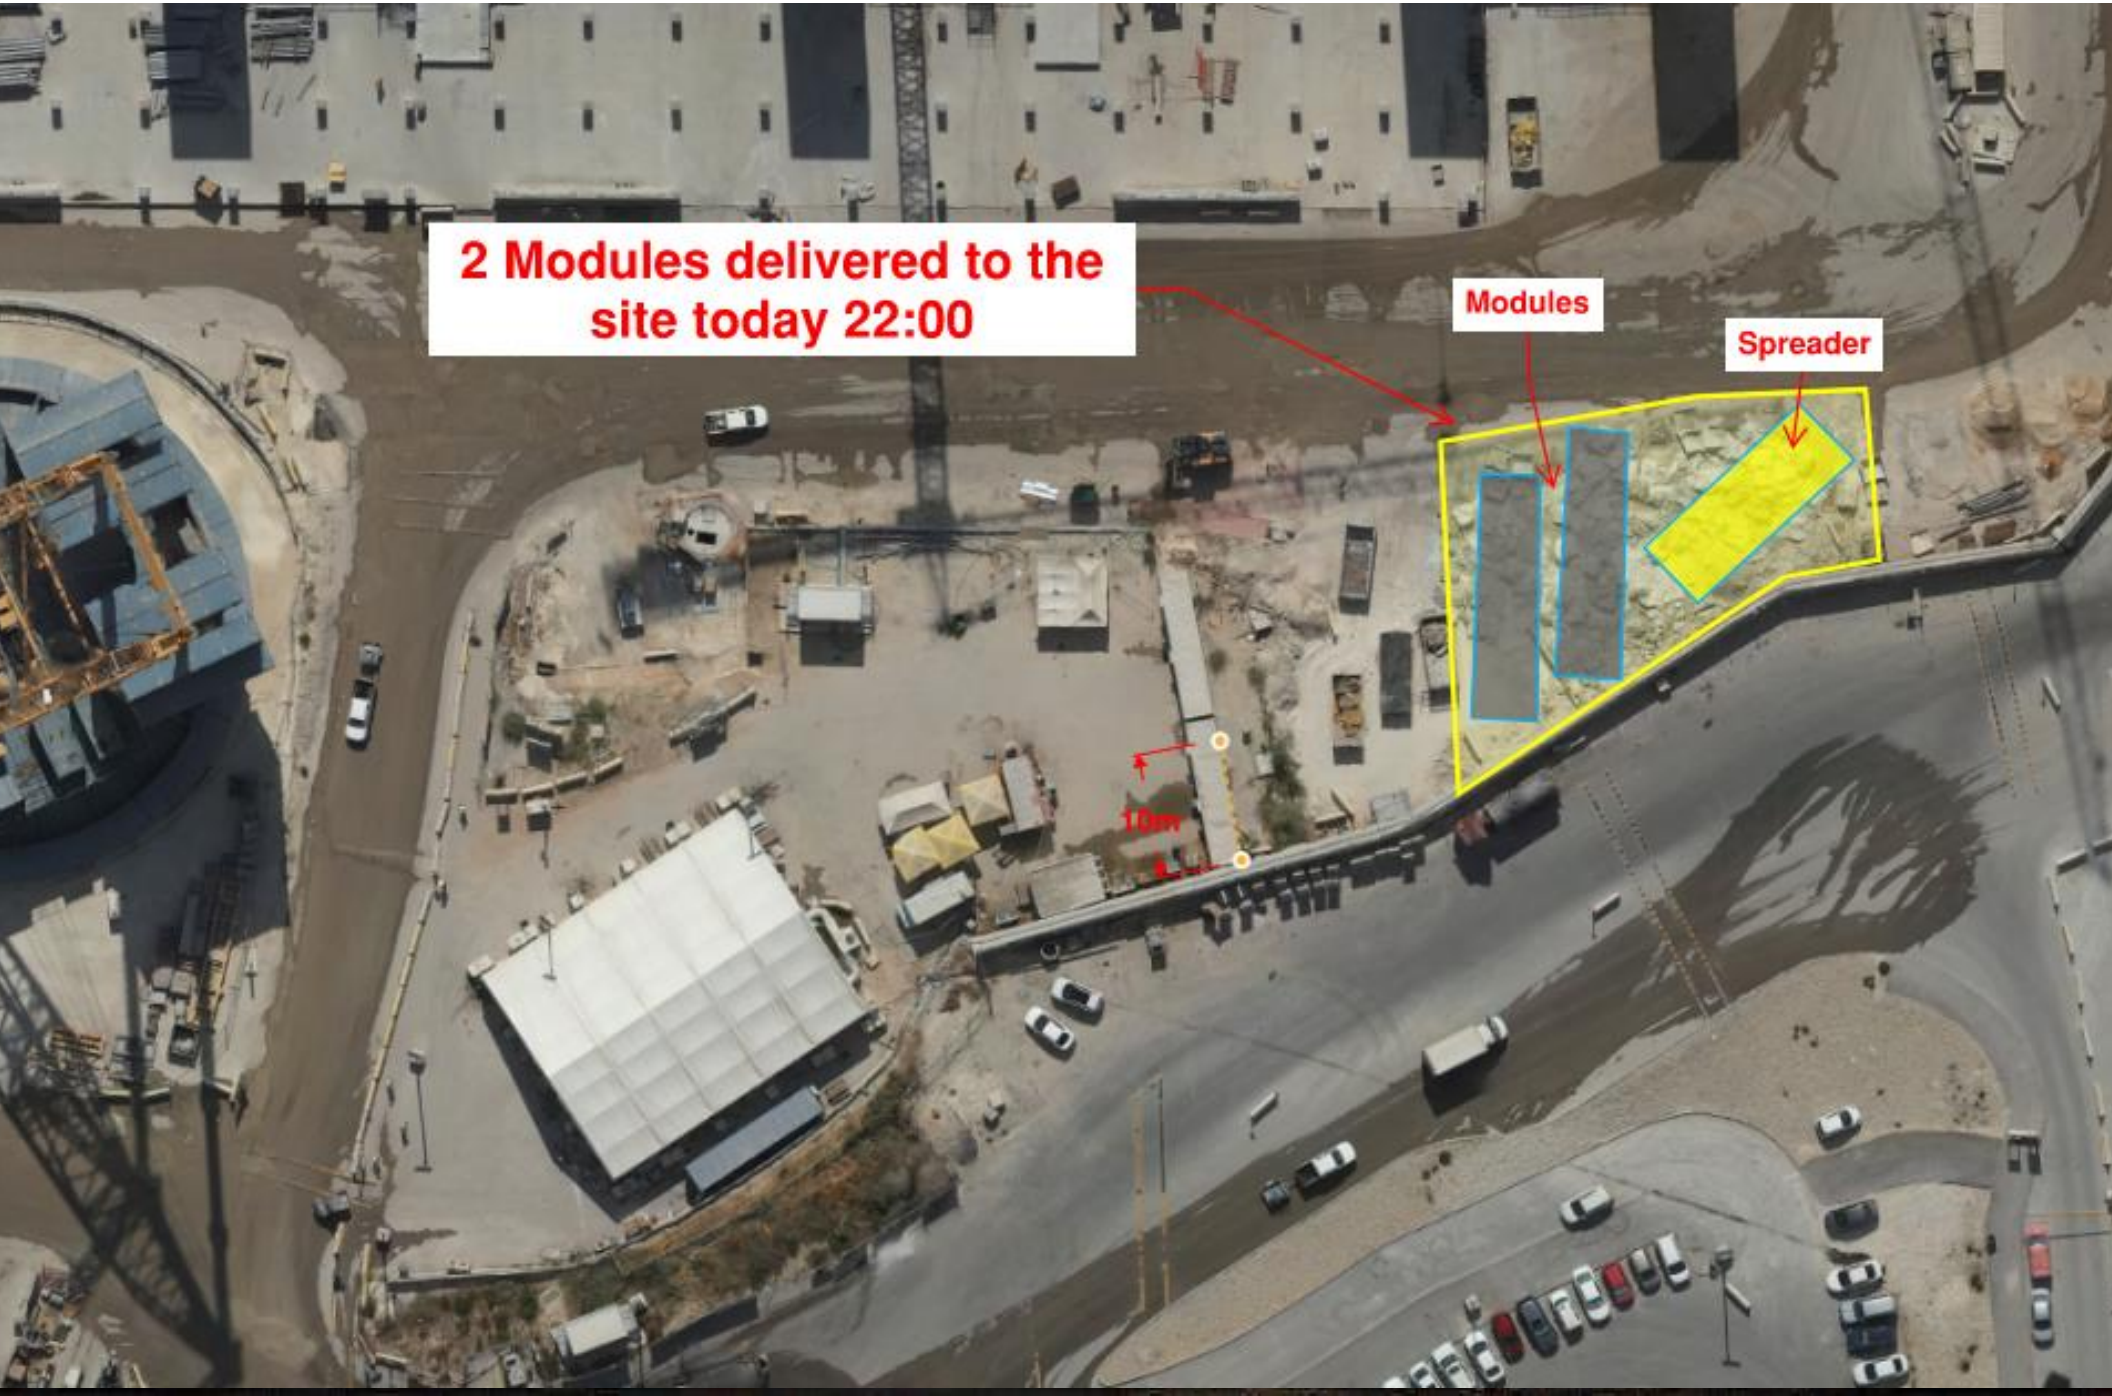

Daily Coordination Meeting

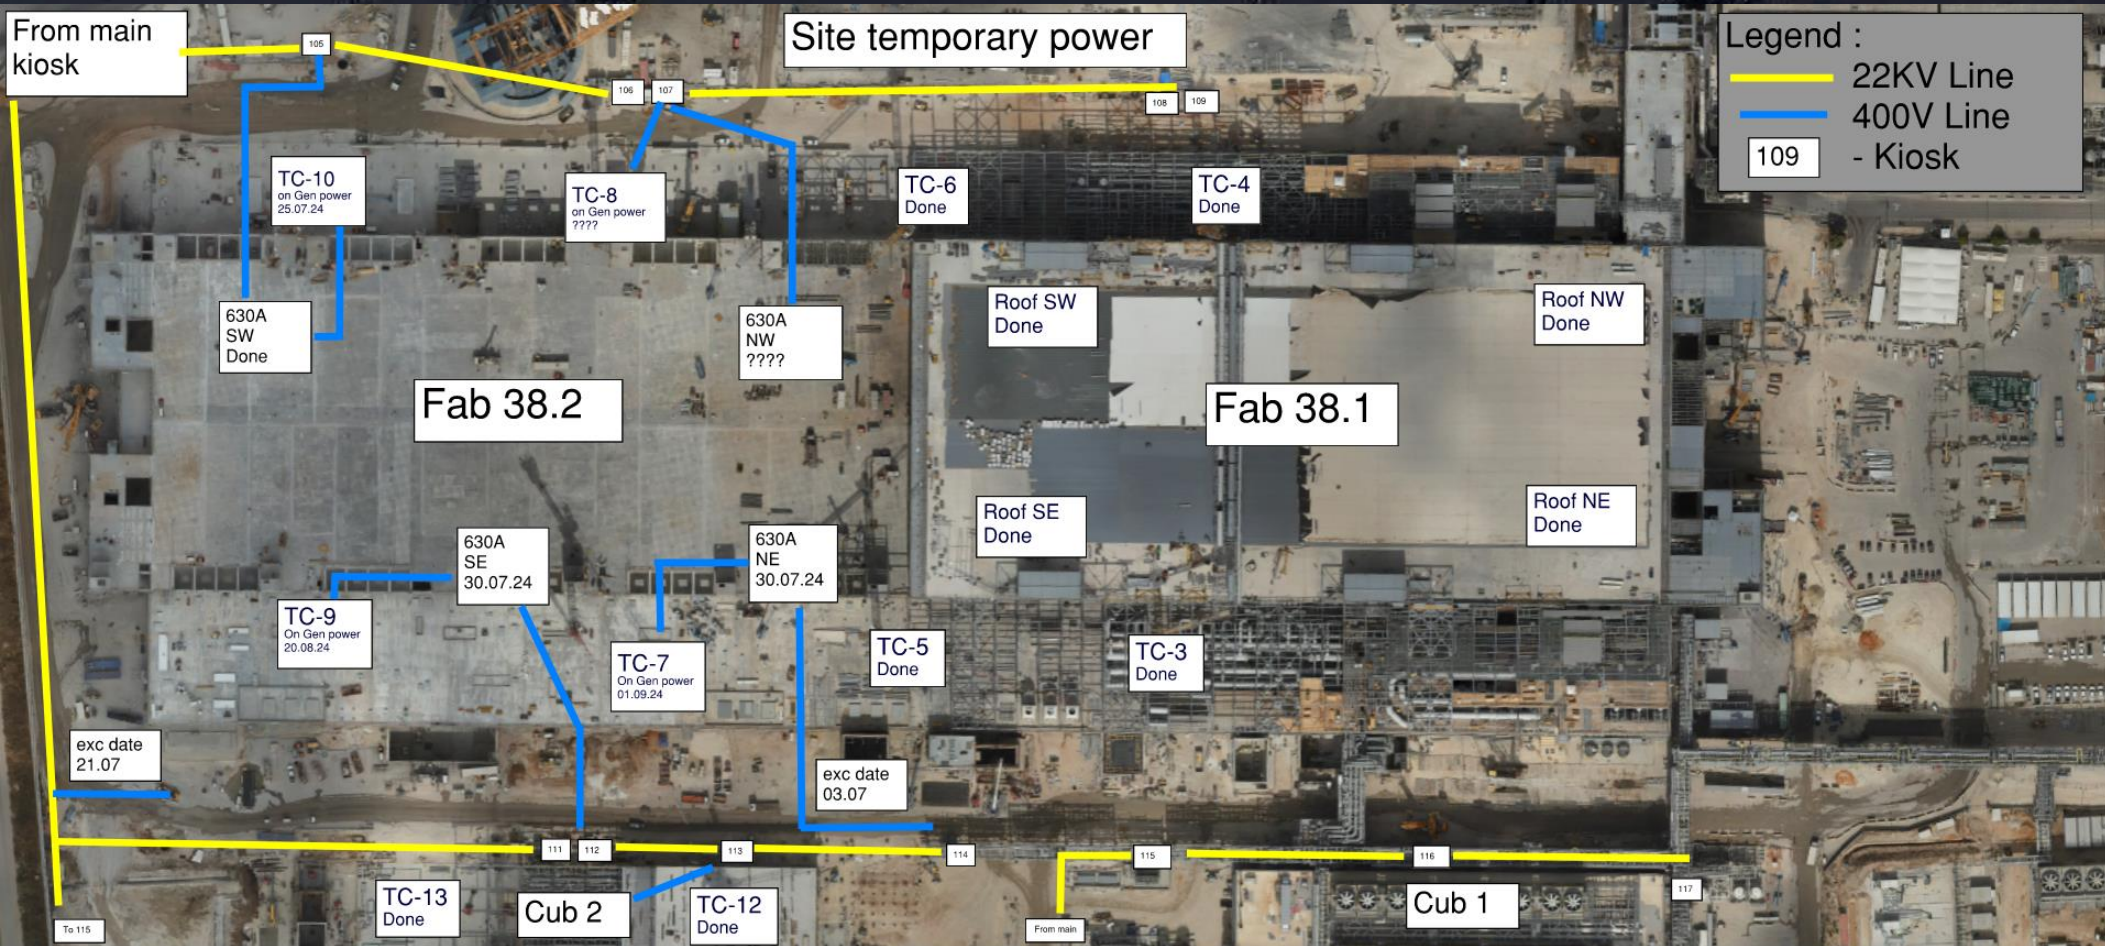

Daily Coordination Meeting

Site Logistics
North Gate B






Daily Coordination Meeting

Site Logistics

Traffic Plan

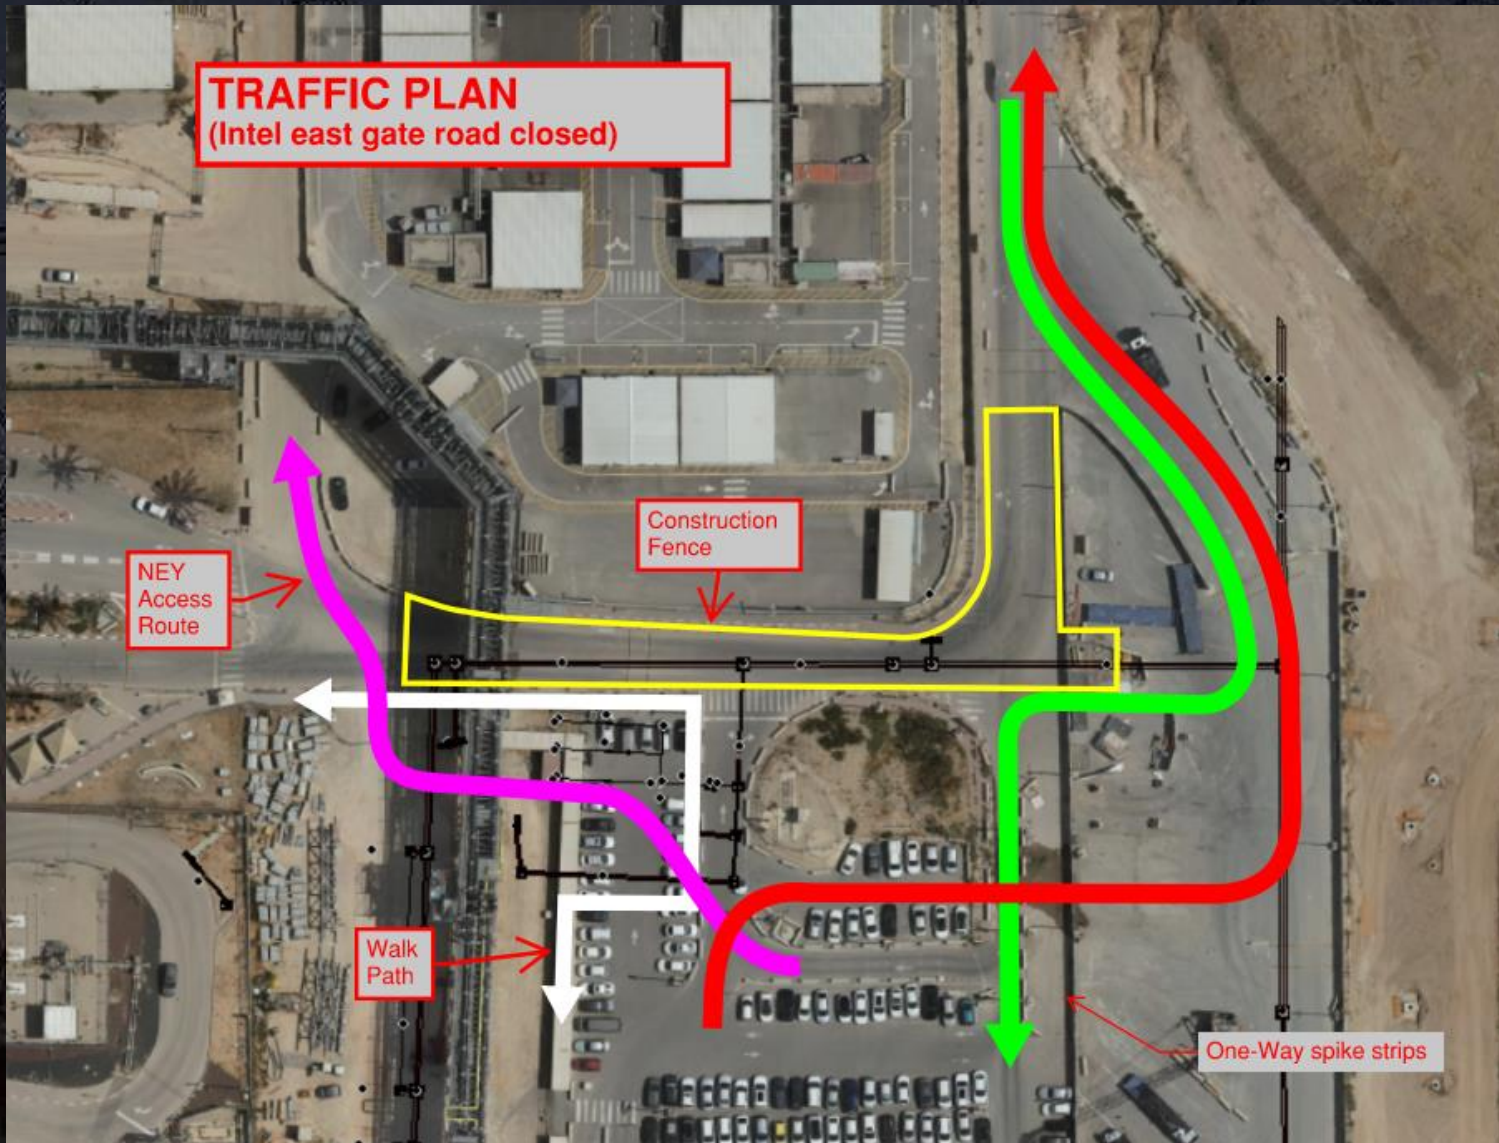

Daily Coordination Meeting

Site Logistics

North



Daily Coordination Meeting

Site Logistics

IQ Access






Daily Coordination Meeting

Site Logistics

South

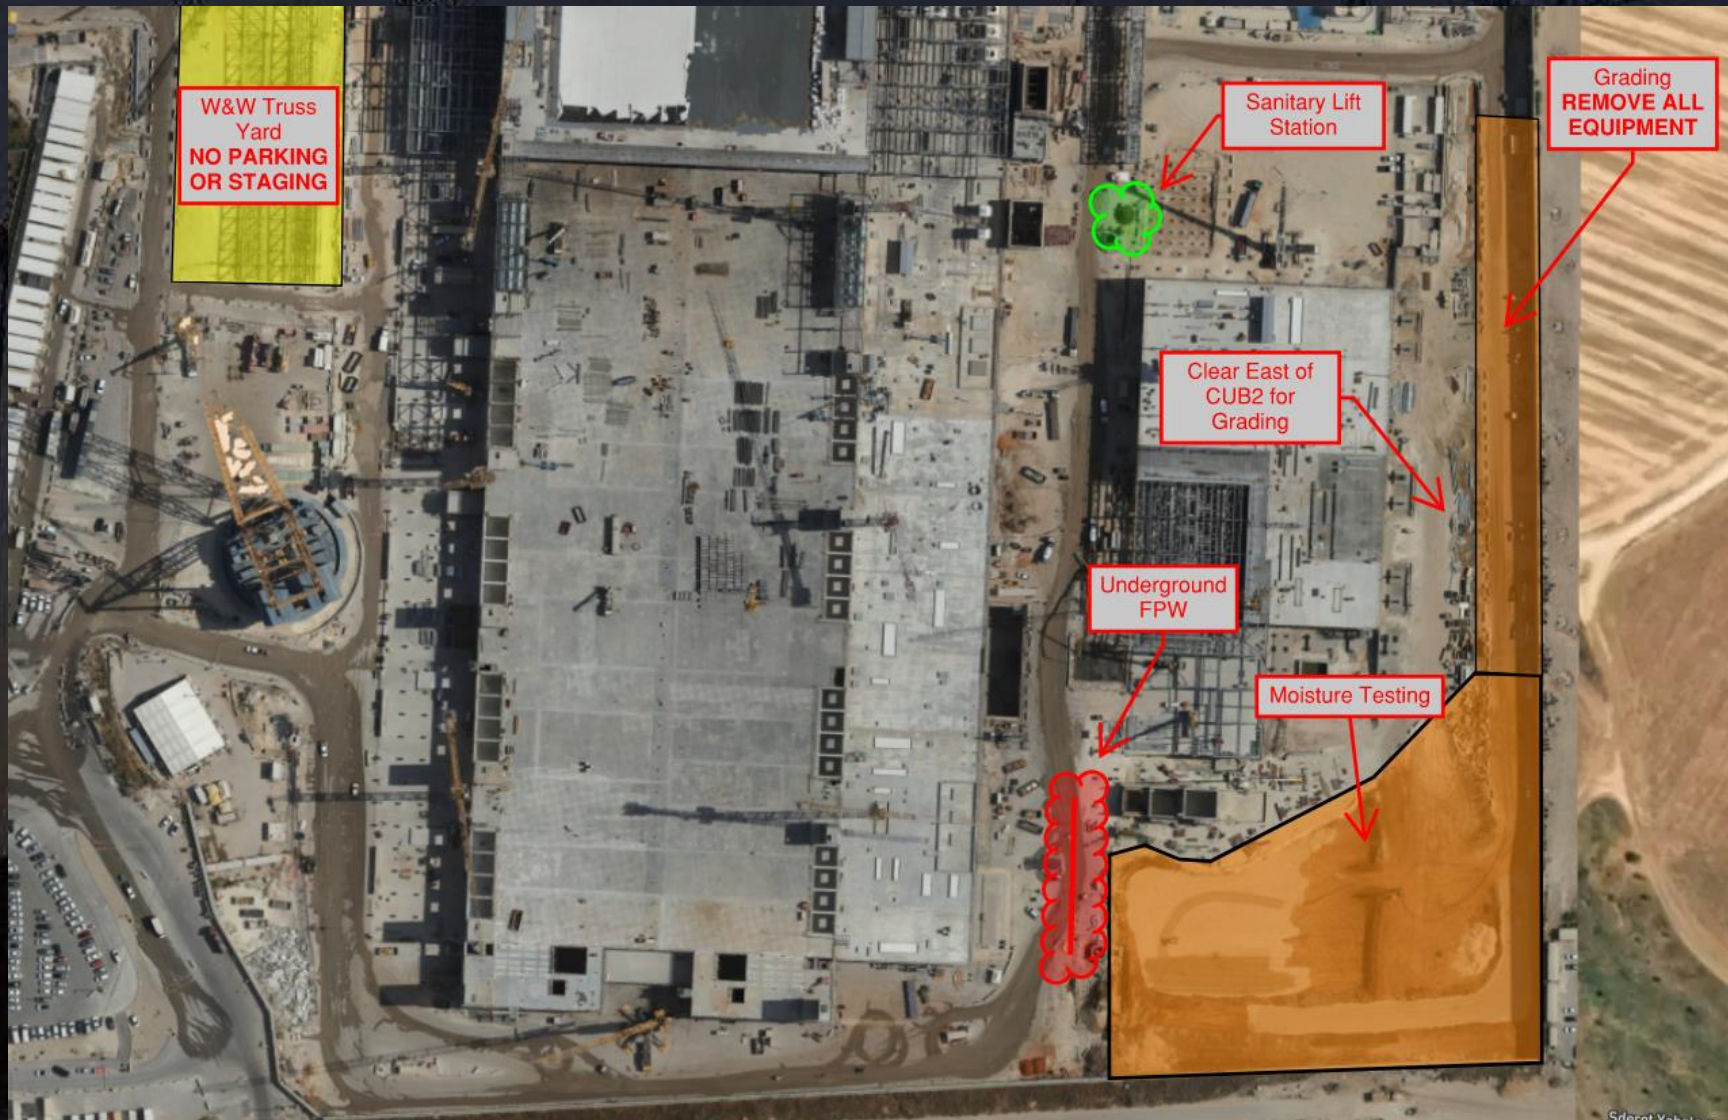



Daily Coordination Meeting

Site Logistics


SW Parking Lot



Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

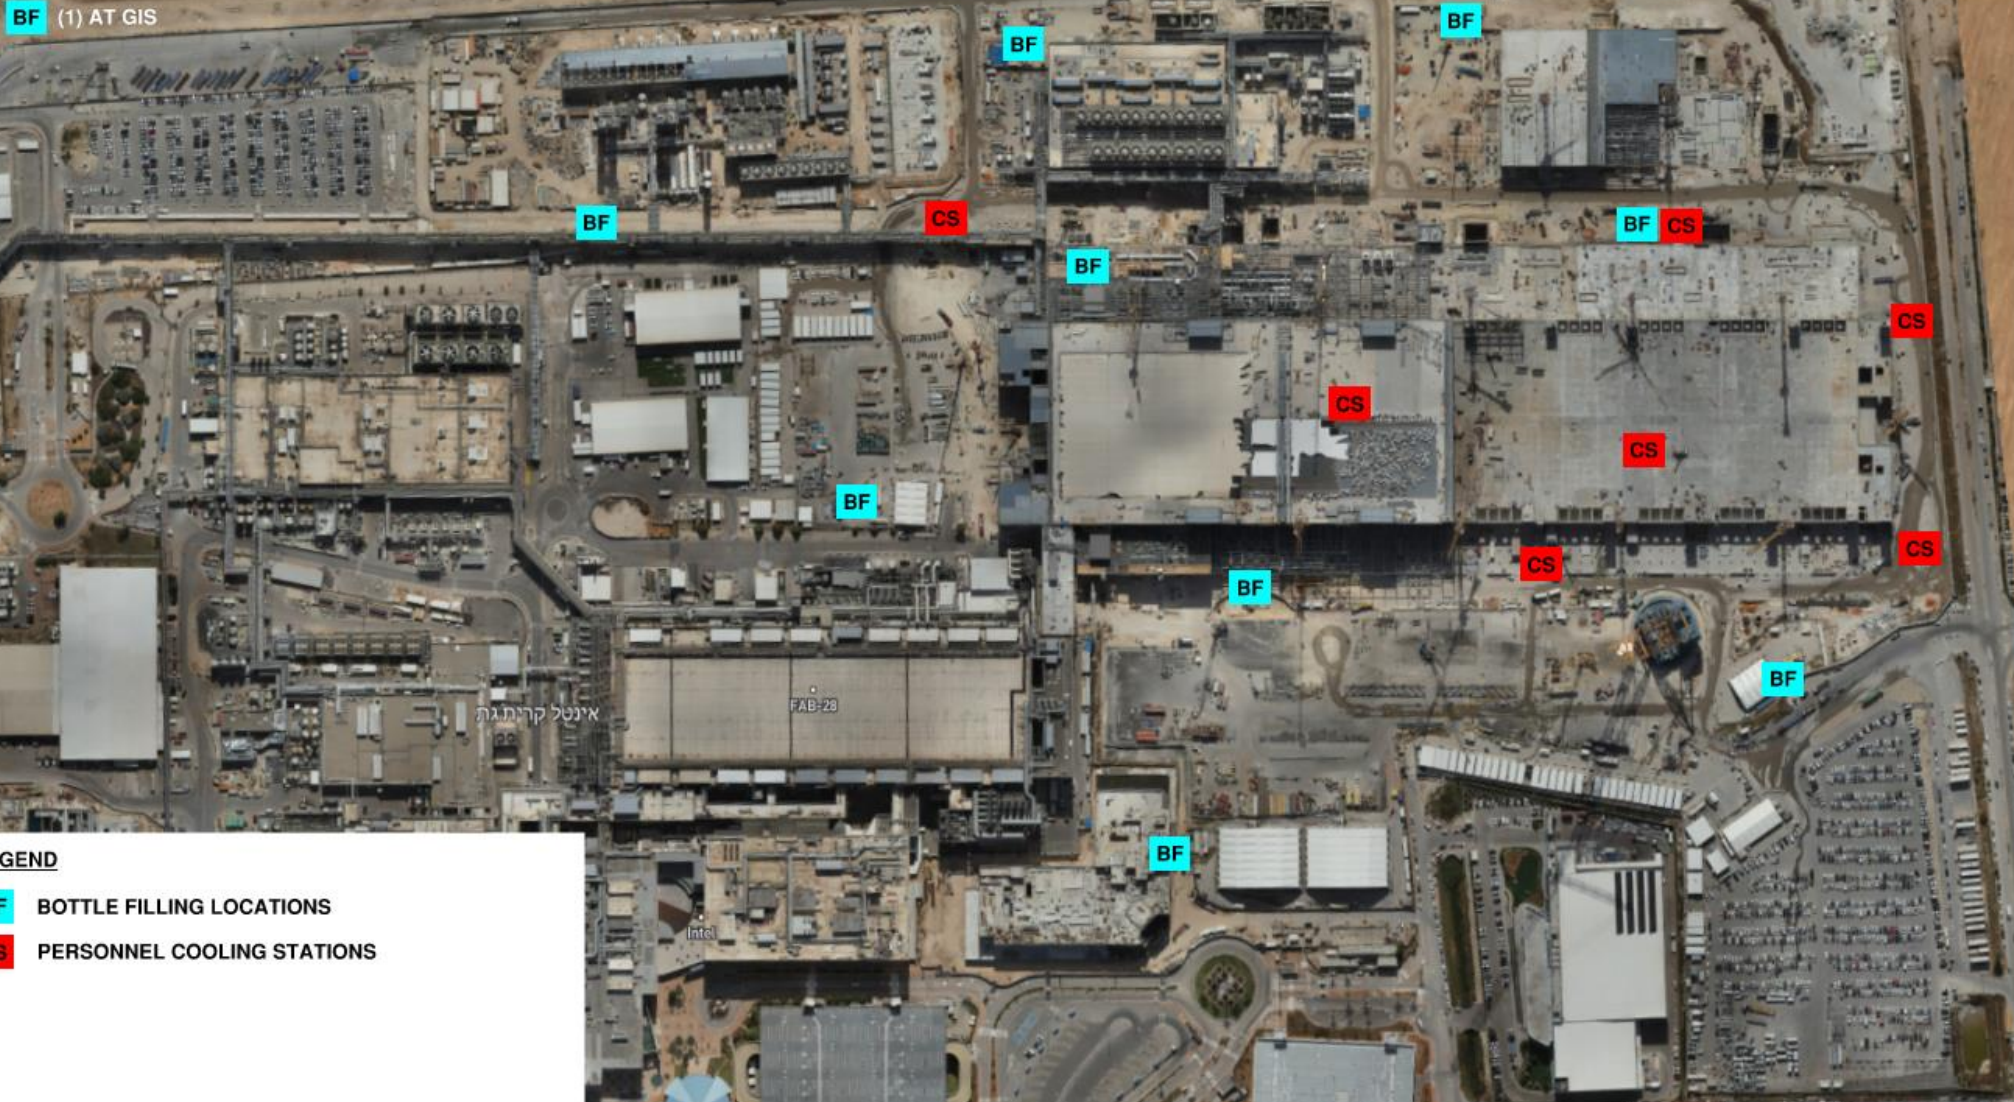

Commissioning



82 PGA Tour Wins

15 Major Wins



Commissioning

Get it Done!

- **ETC – SW650 1 & 2** (CUB)
 - Please send us a photo or upload to EXTO for the updating tagging so we can close COR and GT
- **HCC/Rockwell – PLCs and RIOs** (CUB)
 - Please complete the final 12 questions in the OAT checklist, so we can get all of these GTs
- **Shuv-Eli – 131 and 135 Exhaust Fans** (CUB)
 - Complete Electrical CC step in EXTO
- **AS Barzel – PMP114-3-10**
 - Please complete Process CC step in EXTO
- **Chemo - Cooling Towers and 115/116/117 Pumps**
 - Complete the Mech Wet CC Step in EXTO (11 more TCCs)

MEWP Safety

- Seeing an increase in personnel not operating MEWPs to our best practices on site. Some reminders:
- Spotters are required for all movement of MEWPs- this includes up and down.
- The emergency stop button must be pressed whenever the MEWP is not being actively moved.
- Lower the MEWP before traveling.
- Secure all tools and materials at heights.
- Do not elevate yourself inside the MEWP basket.
- Turtle mode only inside the building.
- Maintain safe distances from workers and live systems.

Heat Index- July 21st

	temperature (°F)																	
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110		
Relative Humidity (%)	40	80	81	83	85	88	91	94	97	100	103	106	109	114	119	124	130	136
	45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137		
	50	81	83	85	88	91	95	99	103	108	113	118	124	131	137			
	55	81	84	86	89	93	97	101	106	112	117	124	130	137				
	60	82	84	88	91	95	100	105	110	116	123	129	137					
	65	82	85	89	93	98	103	108	114	121	128	136						
	70	83	86	90	95	100	105	112	119	126	134							
	75	84	88	92	97	103	109	116	124	132								
	80	84	89	94	100	106	113	121	129									
	85	85	90	96	102	110	117	126	135									
	90	86	91	98	105	113	122	131										
	95	86	93	100	108	117	127											
100	87	95	103	112	121	132												

Caution

Extreme Caution

Danger

Extreme Danger

Extreme Caution Bordering on Danger

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress
- Additional water breaks mandated. (Can be in work area)
- Increased rotation and monitoring of workers and area conditions.

HCC/EHS Weekend Work- 19.07.2024

White Board Meeting in Beavers at 06:30

Superintendents

- Elaina Farley 052-6043861
- Netanel (Nati) Grably 054-4887622
- Sahar Samin 052-2759653

CSA CM

- Nitzan Mulay 052-3257365
- Idan Turjeman 052-4093025

MEP

- George Sweeten 052-2155396
- Omri Tesler 052-5065846
- Andy Jollands 052-9659290
- David Gilmore 052-5430289

QA/Cx

- Peter

Cranes

- Yossi Atias 052-3060790

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Gaber Aloka-050-2238719 Gaber-Aloka@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 19.07.2024

FAB

- Dvir.ie
Manager on site is Daniel Bitton 052-312-8268
EHS Manager is Guy Ishbit 054-491-5407

Utility Level

- His ul
- Dvir ul
- Pach ul
- Chemo ul
- Roll.p ul
- Ww ul
- Hyg ul
- Elram ul
- Afcon elc ul

Clean Room

- Elram – INT 17,24 lines, CR 10,24 line -shaft removal
(EHS Shlomo Amar – 0545551702, Supervisor Ivan - 0545868048)
- Afcon – CR – 2E, 2W, INT-1E, 2E,1W
(EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Chemo – INT -1E+1W 10” pipe install +racks
(EHS Rotem - 0544477112, Supervisor Maor – 0509889071)
- W&W 1E-Handrail, 17 Line added the beams
(EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- Rolling Plains – INT 4DA fireproofing Balkony 2E, LINK AW- B6,9,10, 5RA Level, AK-AQ 25 5 RA, GL9-10 5RA AK-AP
(Supervisor Godrin 0546594273, EHS Oleg - 0542689370)

Subfab

- Afcon E – SF LSS Rooms.
Avieli - 0526008487.

PSSS

- Pach Taas – Module bolting PSSS Roof and Lift 2
Foreman – Serg – 053-3397567
Safety – Mier – 050-2161209
- W&W – SEQ 131,134,136, and 2P Scrubber Grating
Foreman – Mike Lagana – 052-4093401
Safety – Gary Lambert – 1-405-833-8910
- Katz – U8 Rack 7 Plate Install
Foreman - Polishchuk - 054-750-1845.
Safety – Ofer Ilsar - 054-675-6690
- Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2
Foreman – Charles – 055-2740190
Safety – Stevan – 055-9129333
- MB – 1P Fire Riser Room
Foreman – Ahmad – 054-7298597
Safety – 052-6054955
- Combe UPW – UPW Room, UPW Yard, and Water Reactive Piping
Foreman – Boris – 054-8346412
Safety – Shimon Ben Amo – 052-5148747
- Chemo A. – PSSS Roof and Lift 2
Foreman – Maor – 050-955-9071
Safety – Rotem – 054-447-7112
- HSAI – BIPA & MOD2 Stripping
Foreman – Dave – 052-4121028
Safety – Sam – 052-5259268

Girts

Subcontractor Weekend Work- 19.07.2024

WJG

- W&W – Steel Erection 5J
Foreman: Chris Isaac – 052 588 3215
Safety: Moshe 054 801 2959
- Afcon – 3J UL Cable Tray, 2J Lift 2 Cable Tray
Foreman: Sarat 055 274 0190
Safety: Pradeep 055 274 2935
- Pach Taas: 1J UL, 2J Lift 2 Module Bolting
Foreman: Nuriel 054 901 2343
Safety:
- Chemo: 2J & 3J Lift 2 Piping
Foreman: Stav 054 717 5157
Safety: Rotem 054 447 7112

Site

- Derech Afar – Sanitary lift station & underground fire protection
Supervision = Raed: 054-2442030
EHS = Alex: 054-5403849
- Olizki – Sweepers and water trucks, truck offloads, concrete flatwork (PCC) & excavation
Supervision = Yossi: 052-2180485
EHS = Ben: 052-4033565
- TM Team – Telecom & asphalt cutting outside gate B
Supervision = Nadav Zaitman: 054-5893171
EHS = Meital Dvir: 053-3001124

Trestle

- Sami Najami piping – T-41 area
- Sami Najami Steel – SUT area
- Sami Najami Foundations - West of CUB2 area

CUB

- Chemo- Forman Dudu 0509808846
- Chemo-Safety-Daniel 0525217434
- Sami Najami-Forman 0526917461
- Sami Najami- Safety 0509895008

GIS/NEY
