

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:


- Follow Road Signs – Stop, 16kph



Link Beam
6:00 am


SW Loading dock
ramp 5:00 am

UTILITY LEVEL MOD1

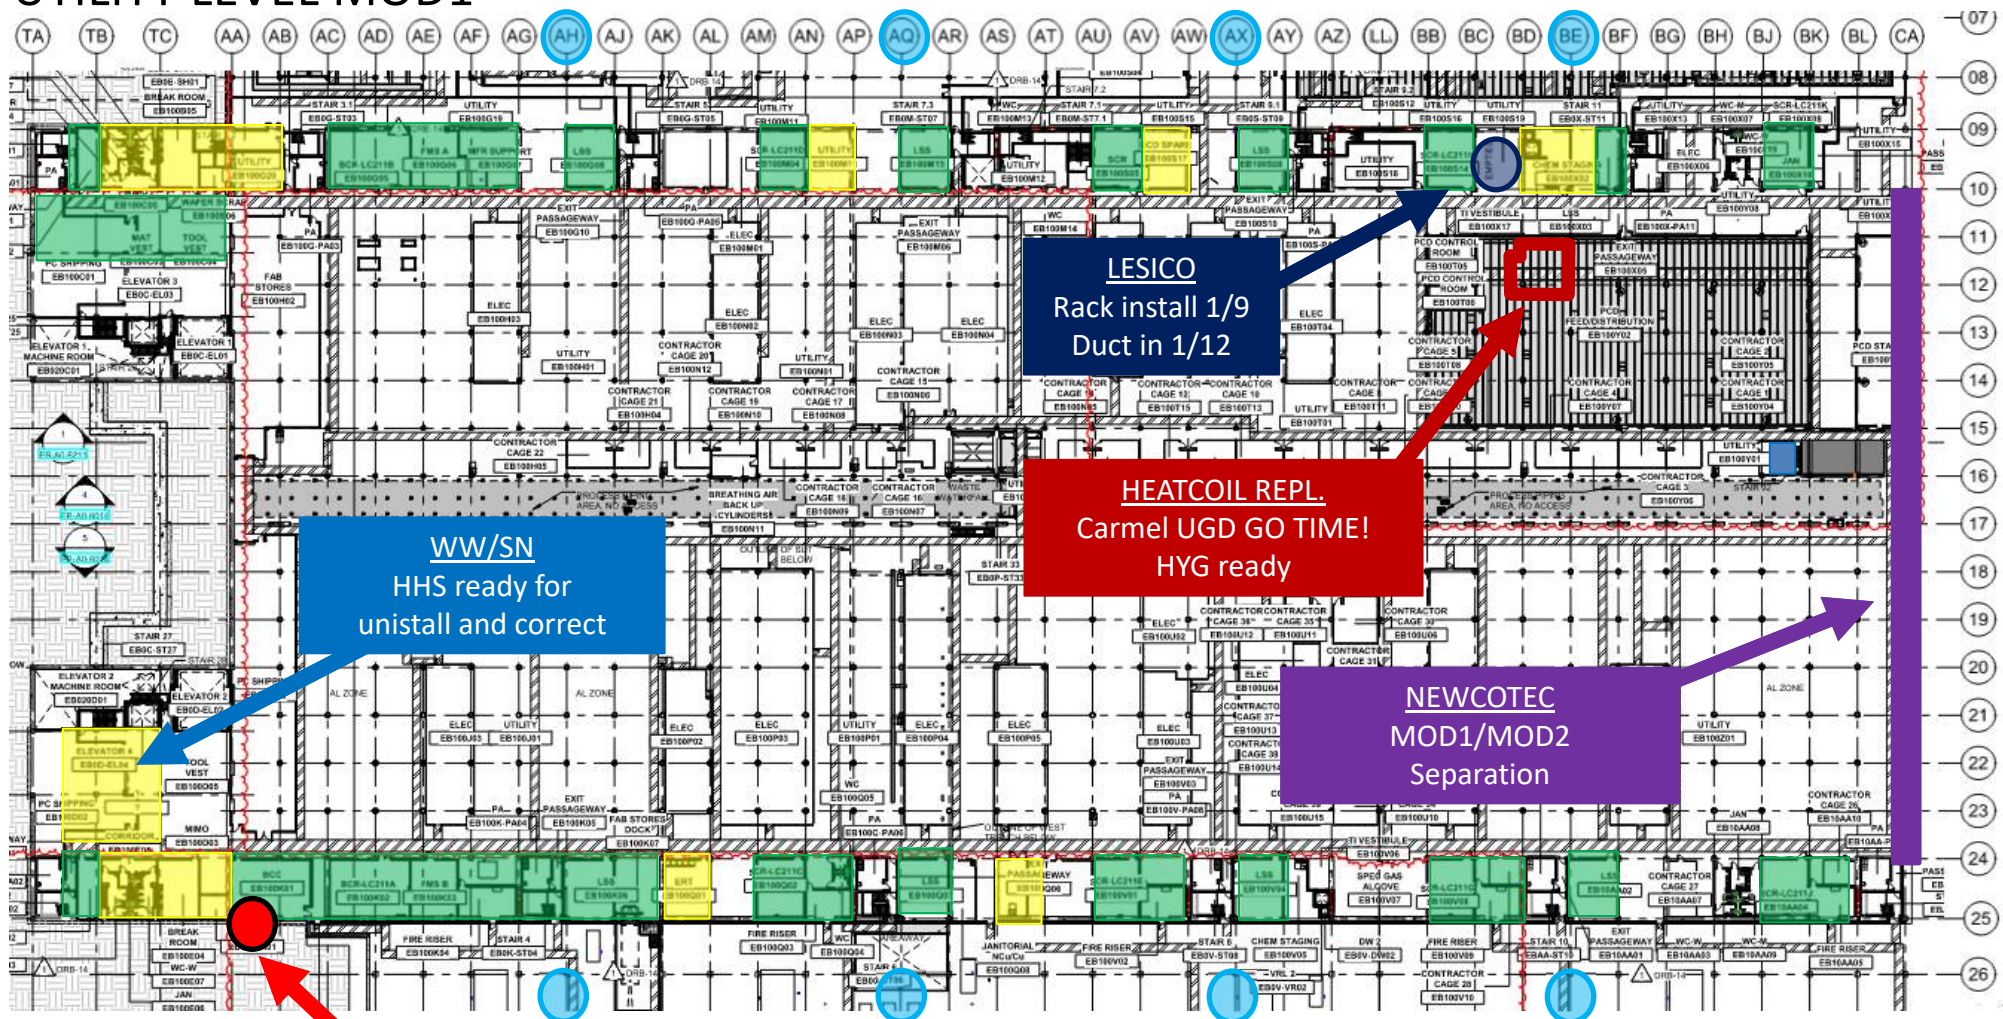




UTILITY LEVEL MOD2

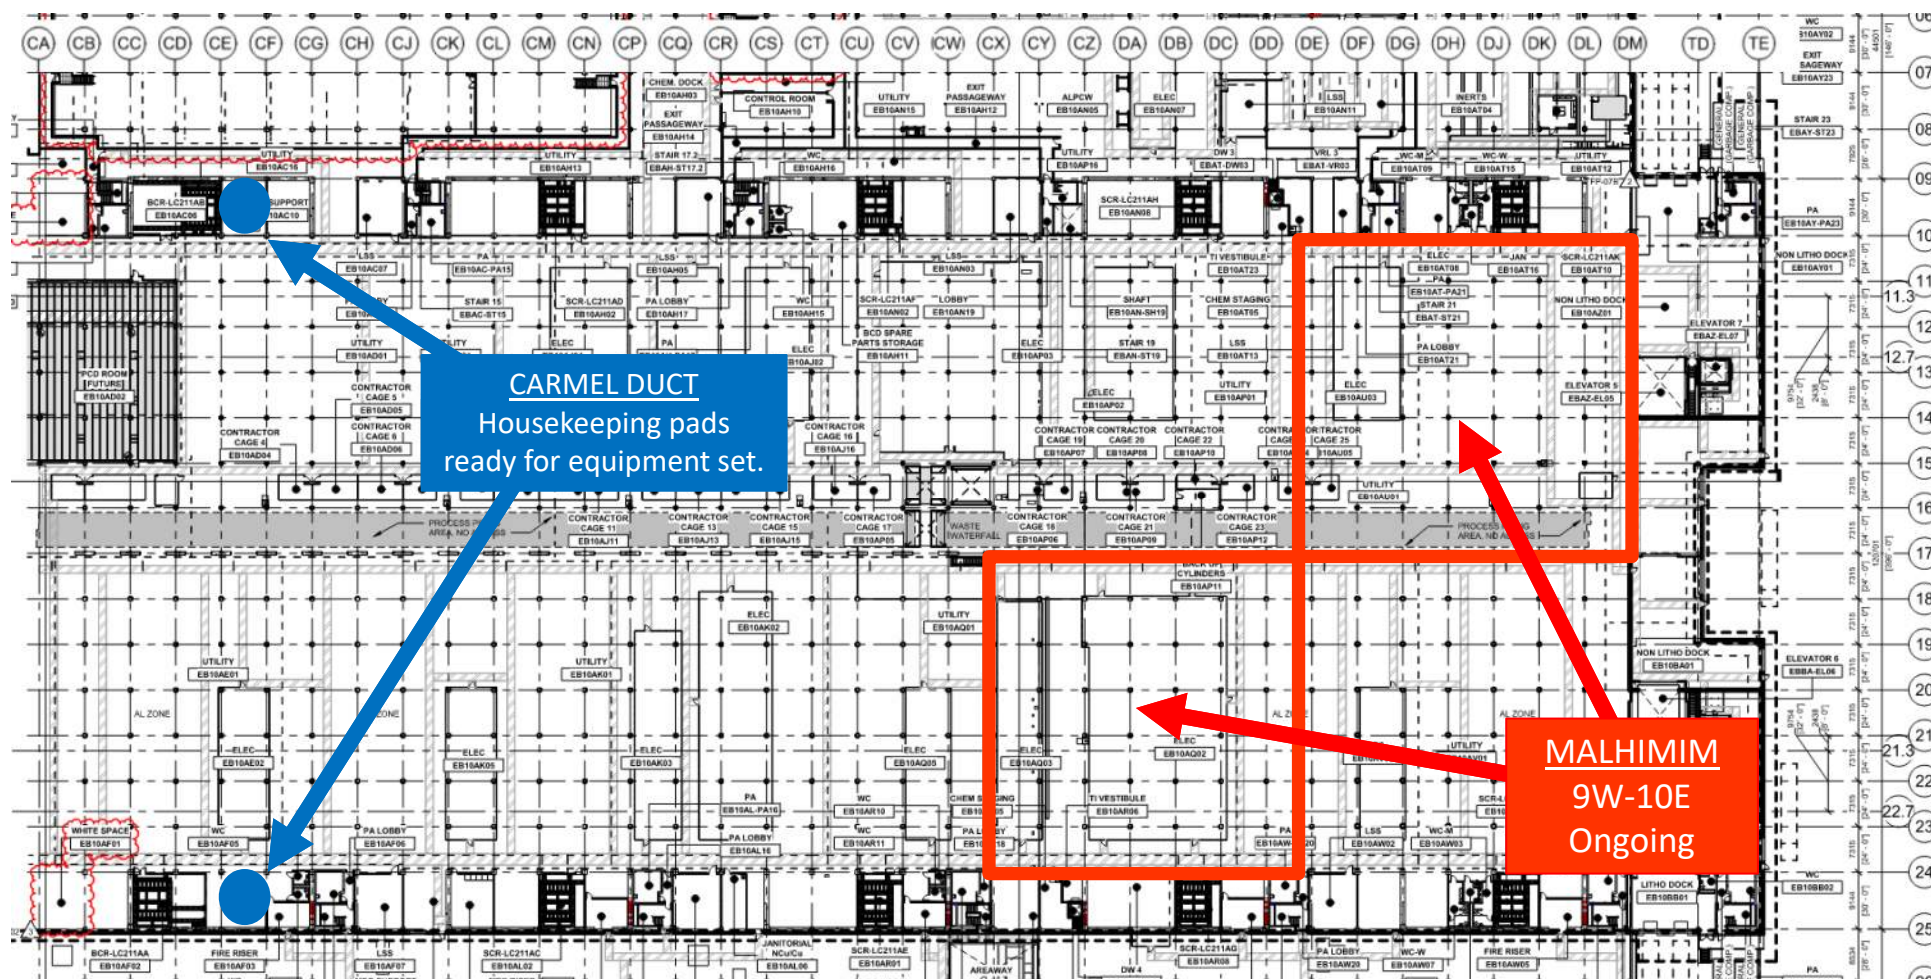


SUT 38.1 Accesses & Egress

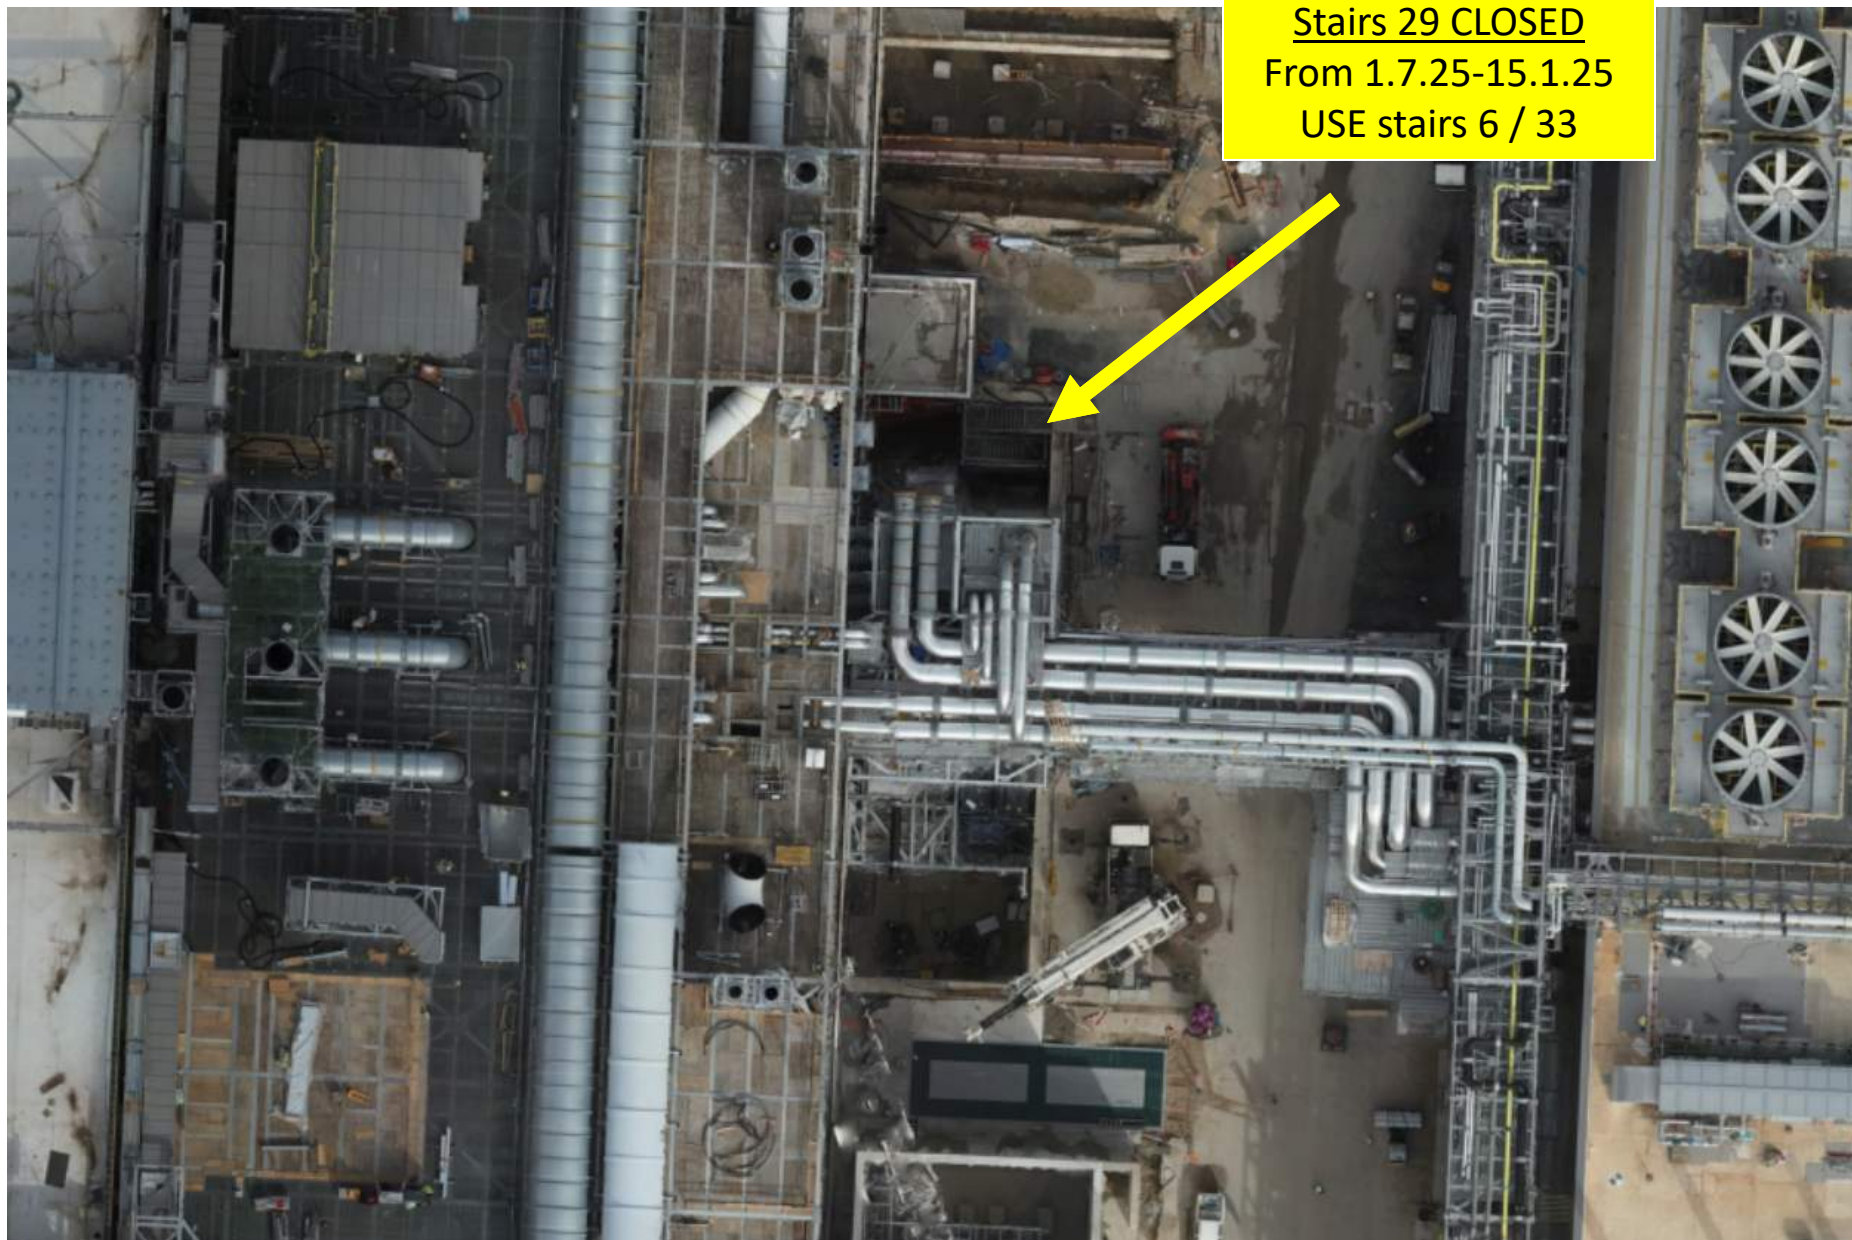

Stairs 29 CLOSED
From 1.7.25-15.1.25
USE stairs 6 / 33

SUT 38.1 LEVEL

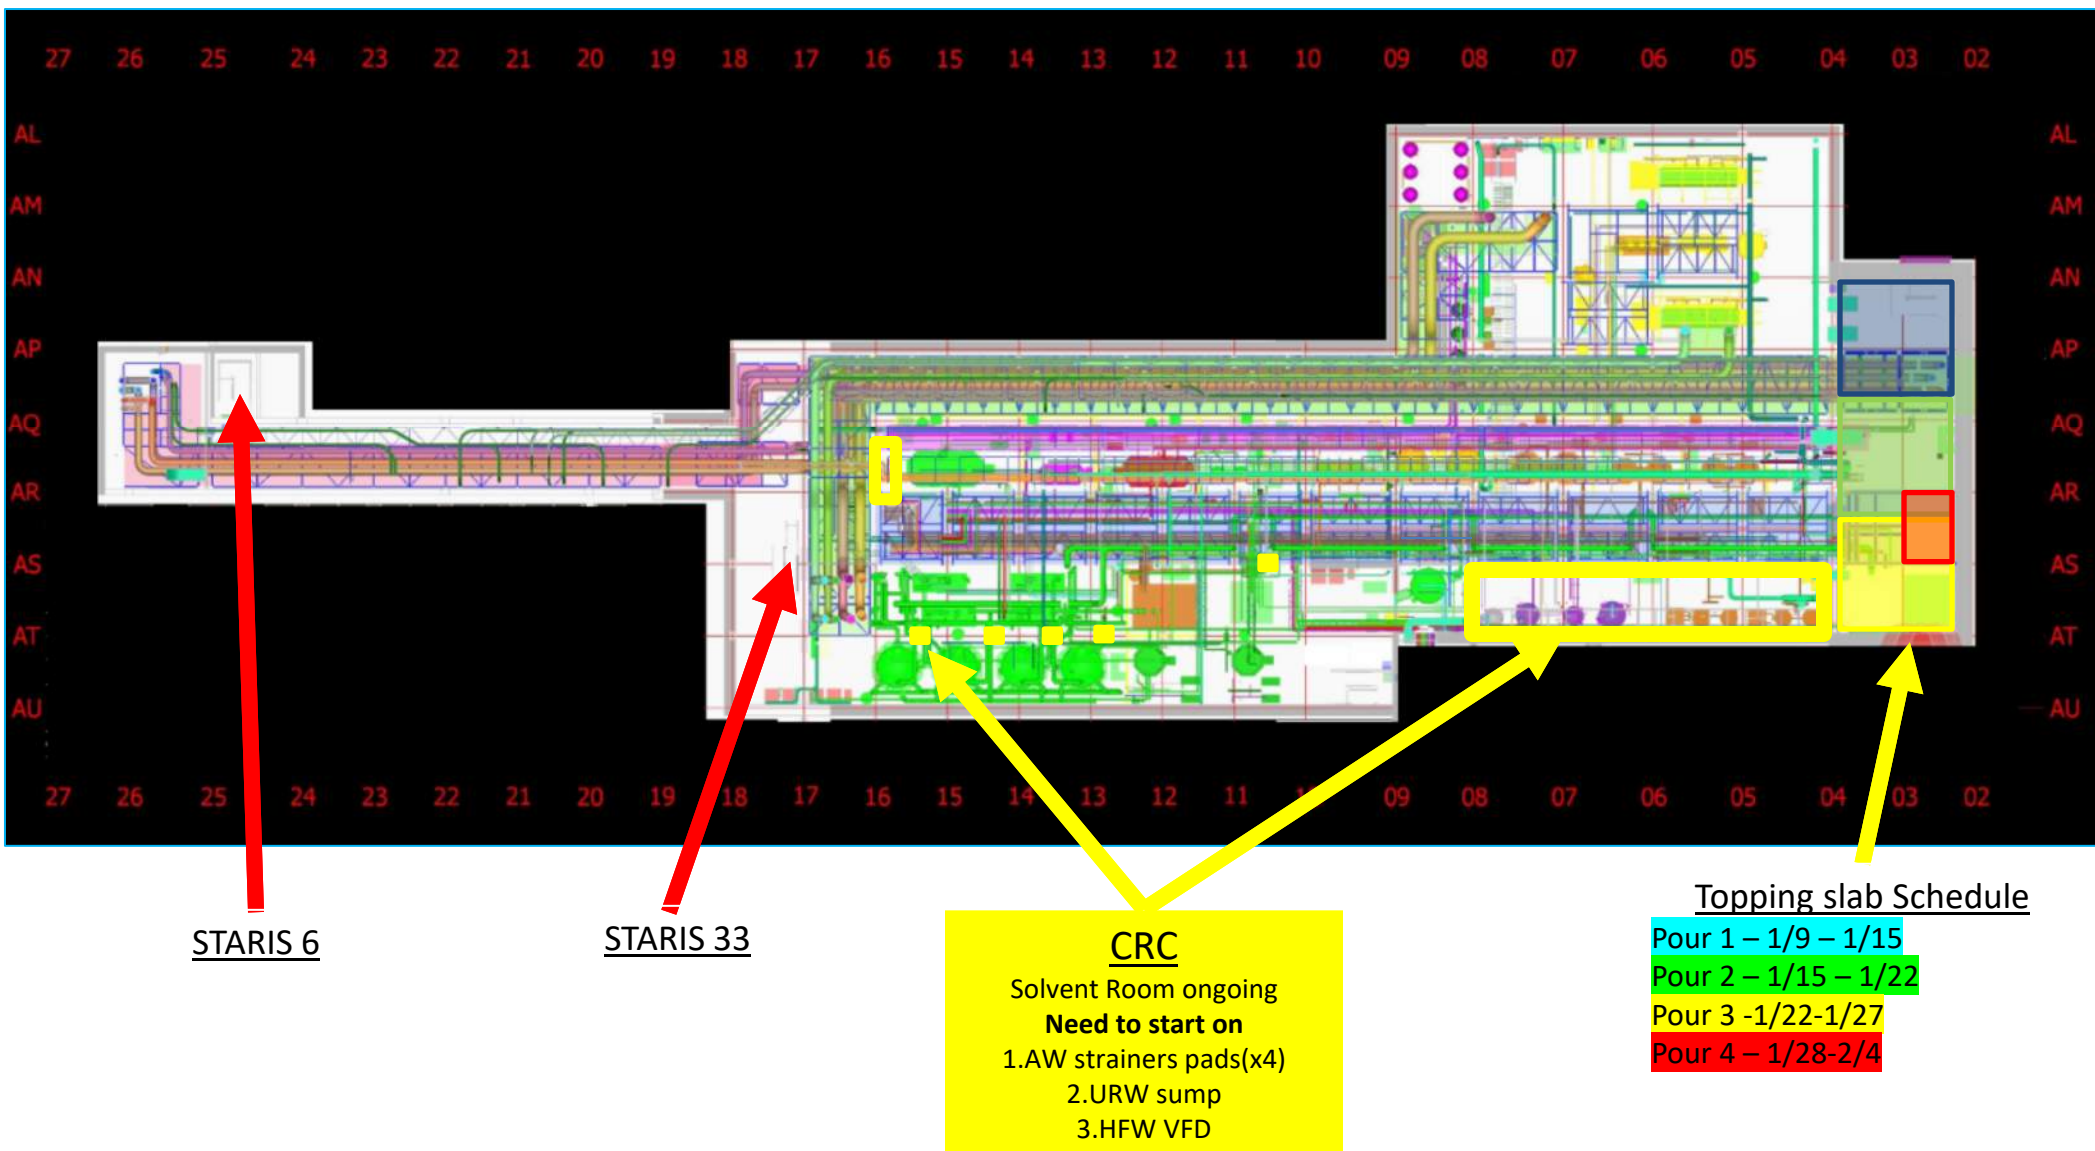




HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL

Rack 4b
Lifting
schedule
#6 –

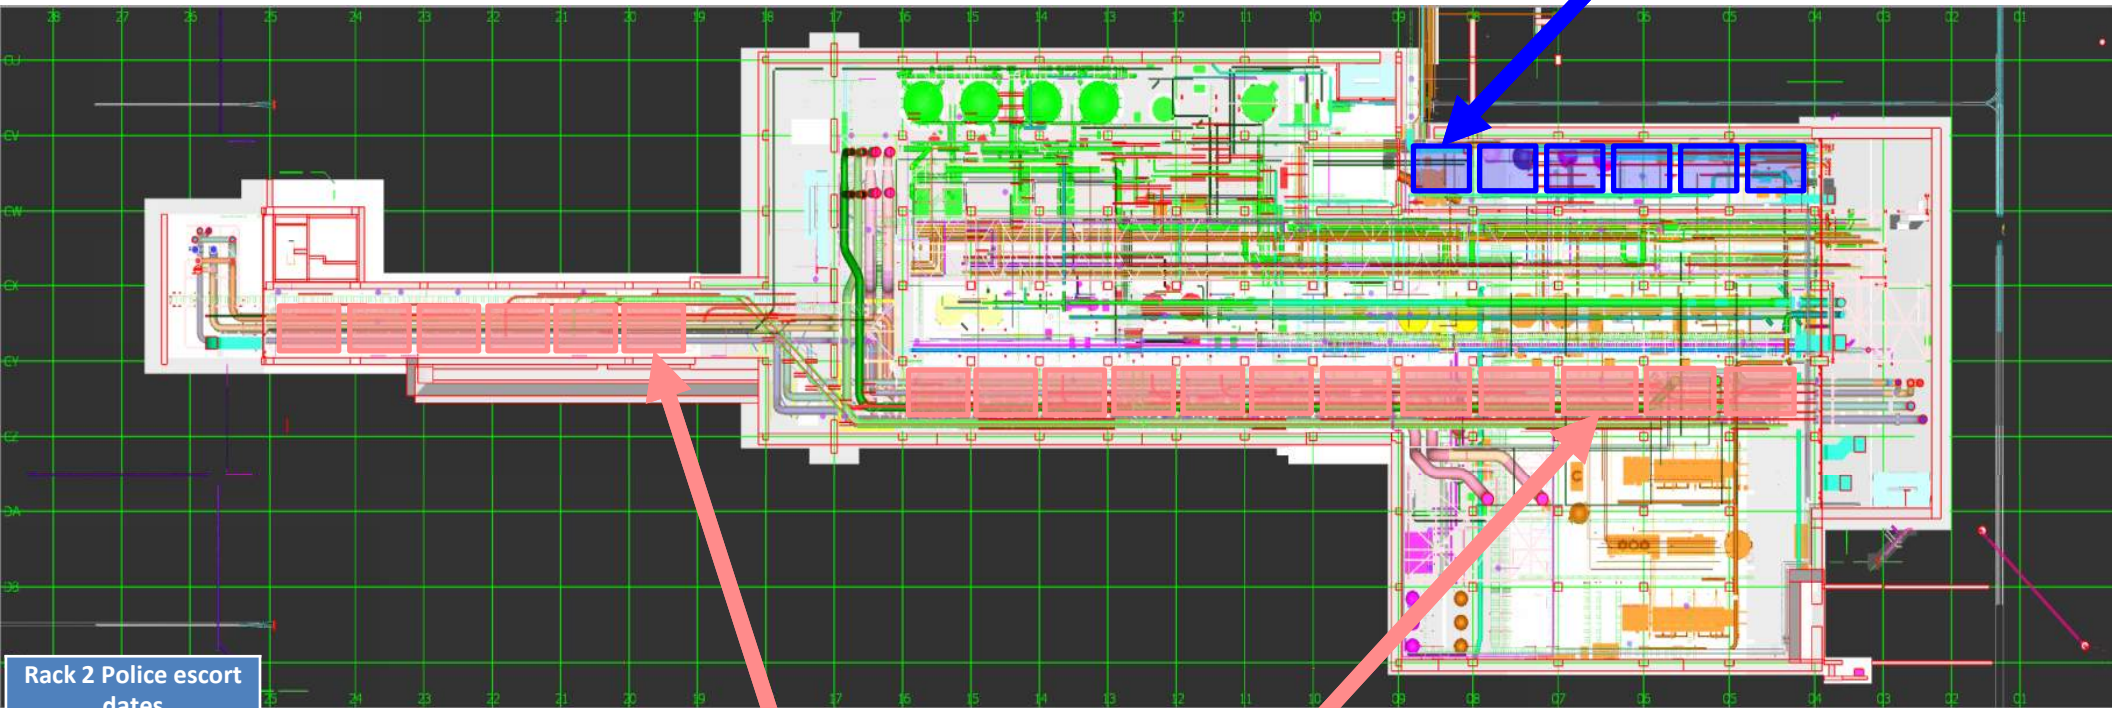


Rack 2 Police escort dates	
v24.11.24	
v25.11.24	
v3.12.24	
v9.12.24	
v12.12.24	
v15.12.24	
v17.12.24	
v22.12.24	
5.1.25	
14.1.25 > 2.2.25	
3.2.25	
9.2.25	


Rack6
MIMO -
Module #1
12.2.25

Rack 2
MIMO -
Module #10
2.2.25


SUBFAB BUILDOUT MOD 1

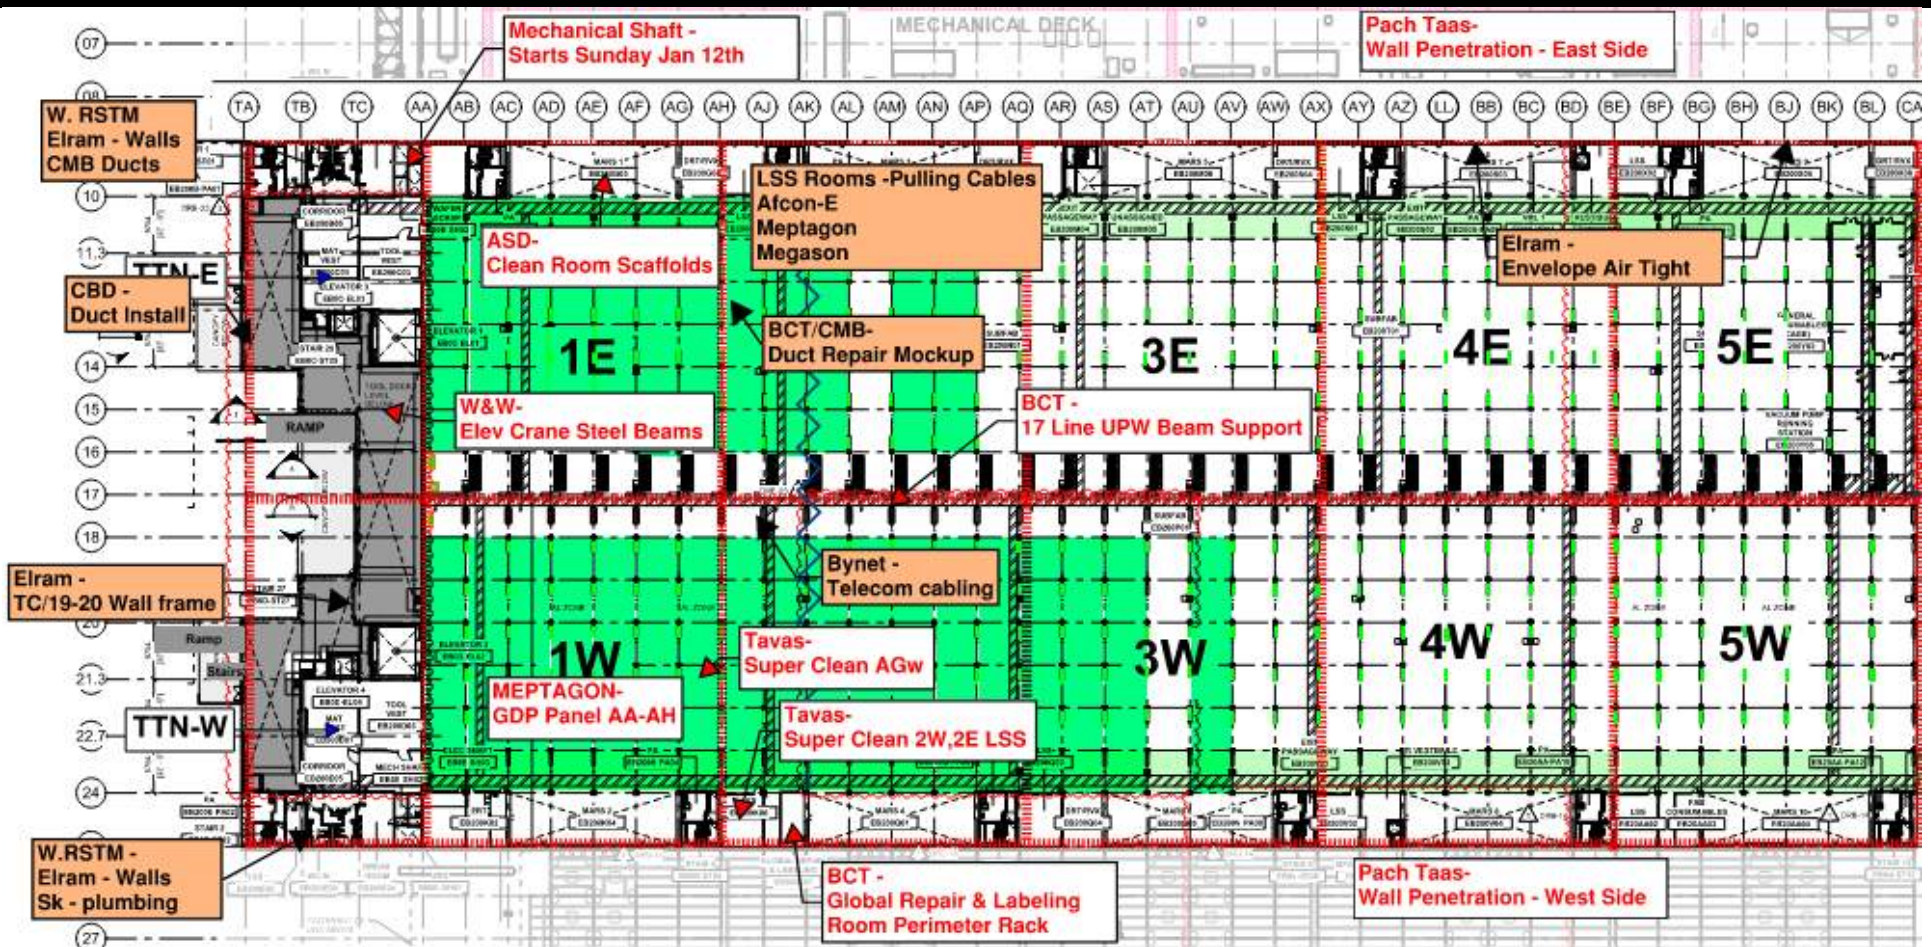


SUBFAB CRC TOPCOAT

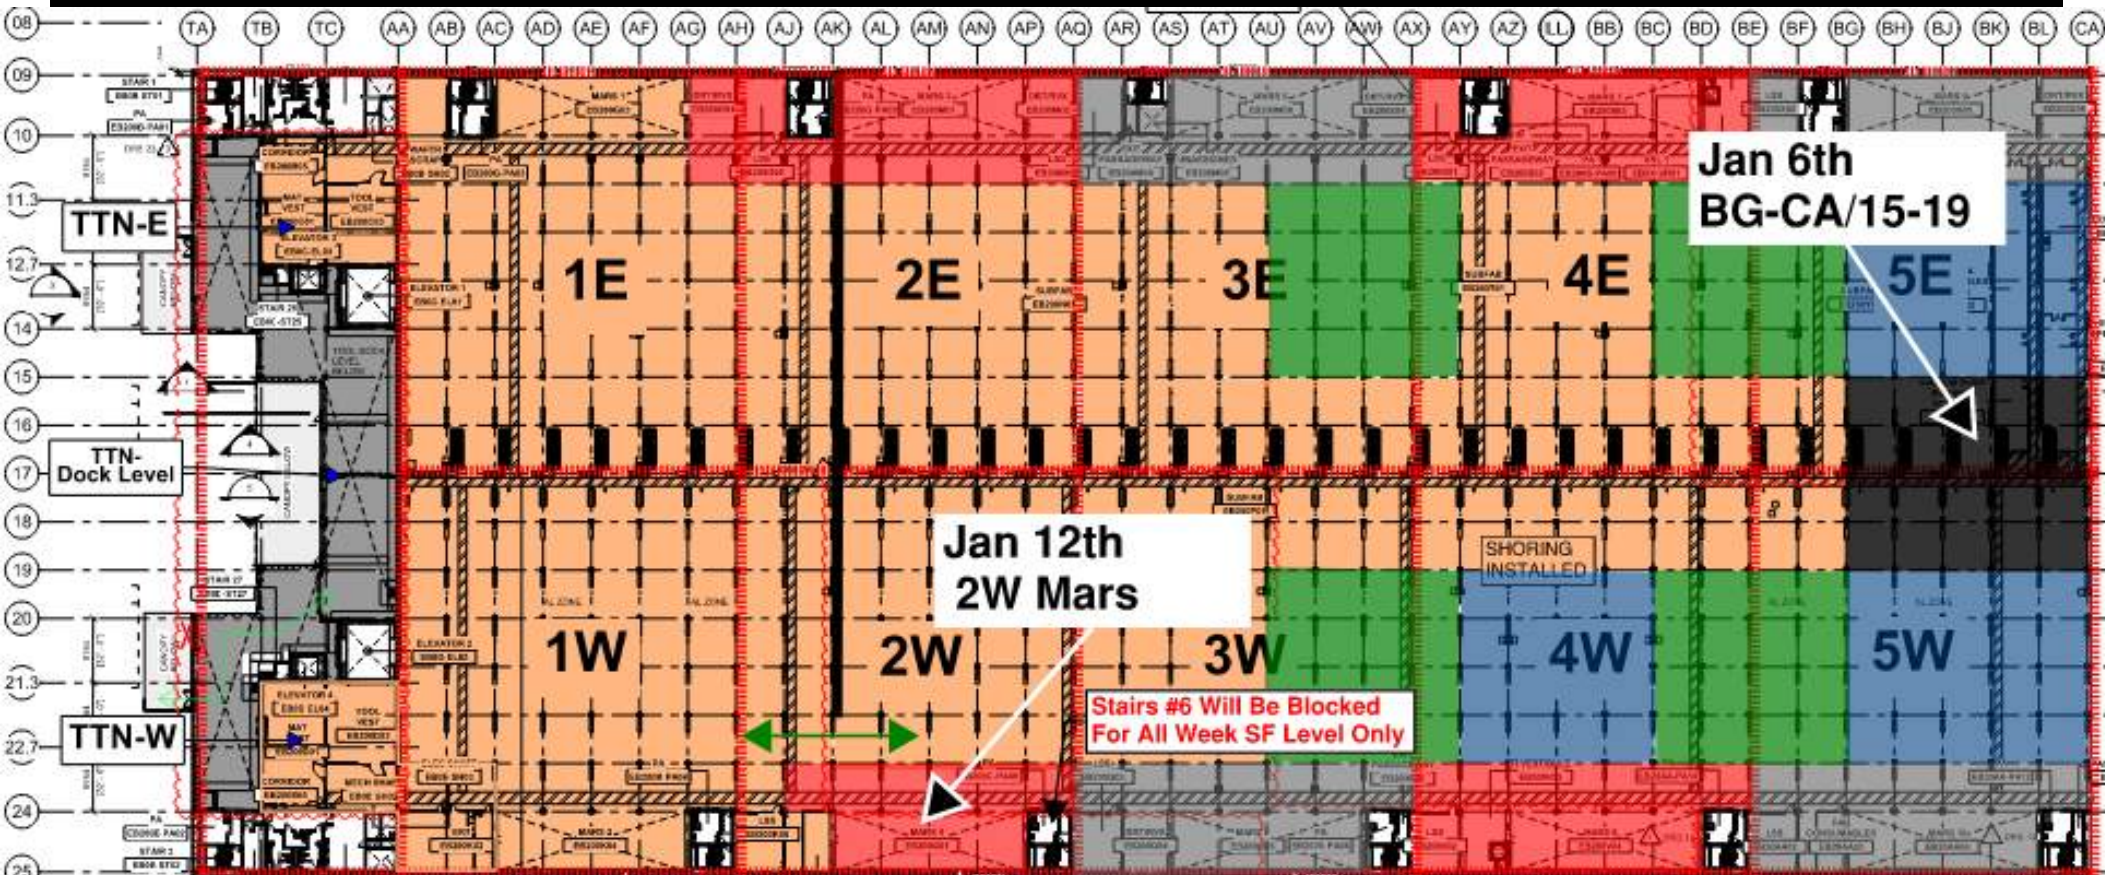


BCT Pressure Test Today

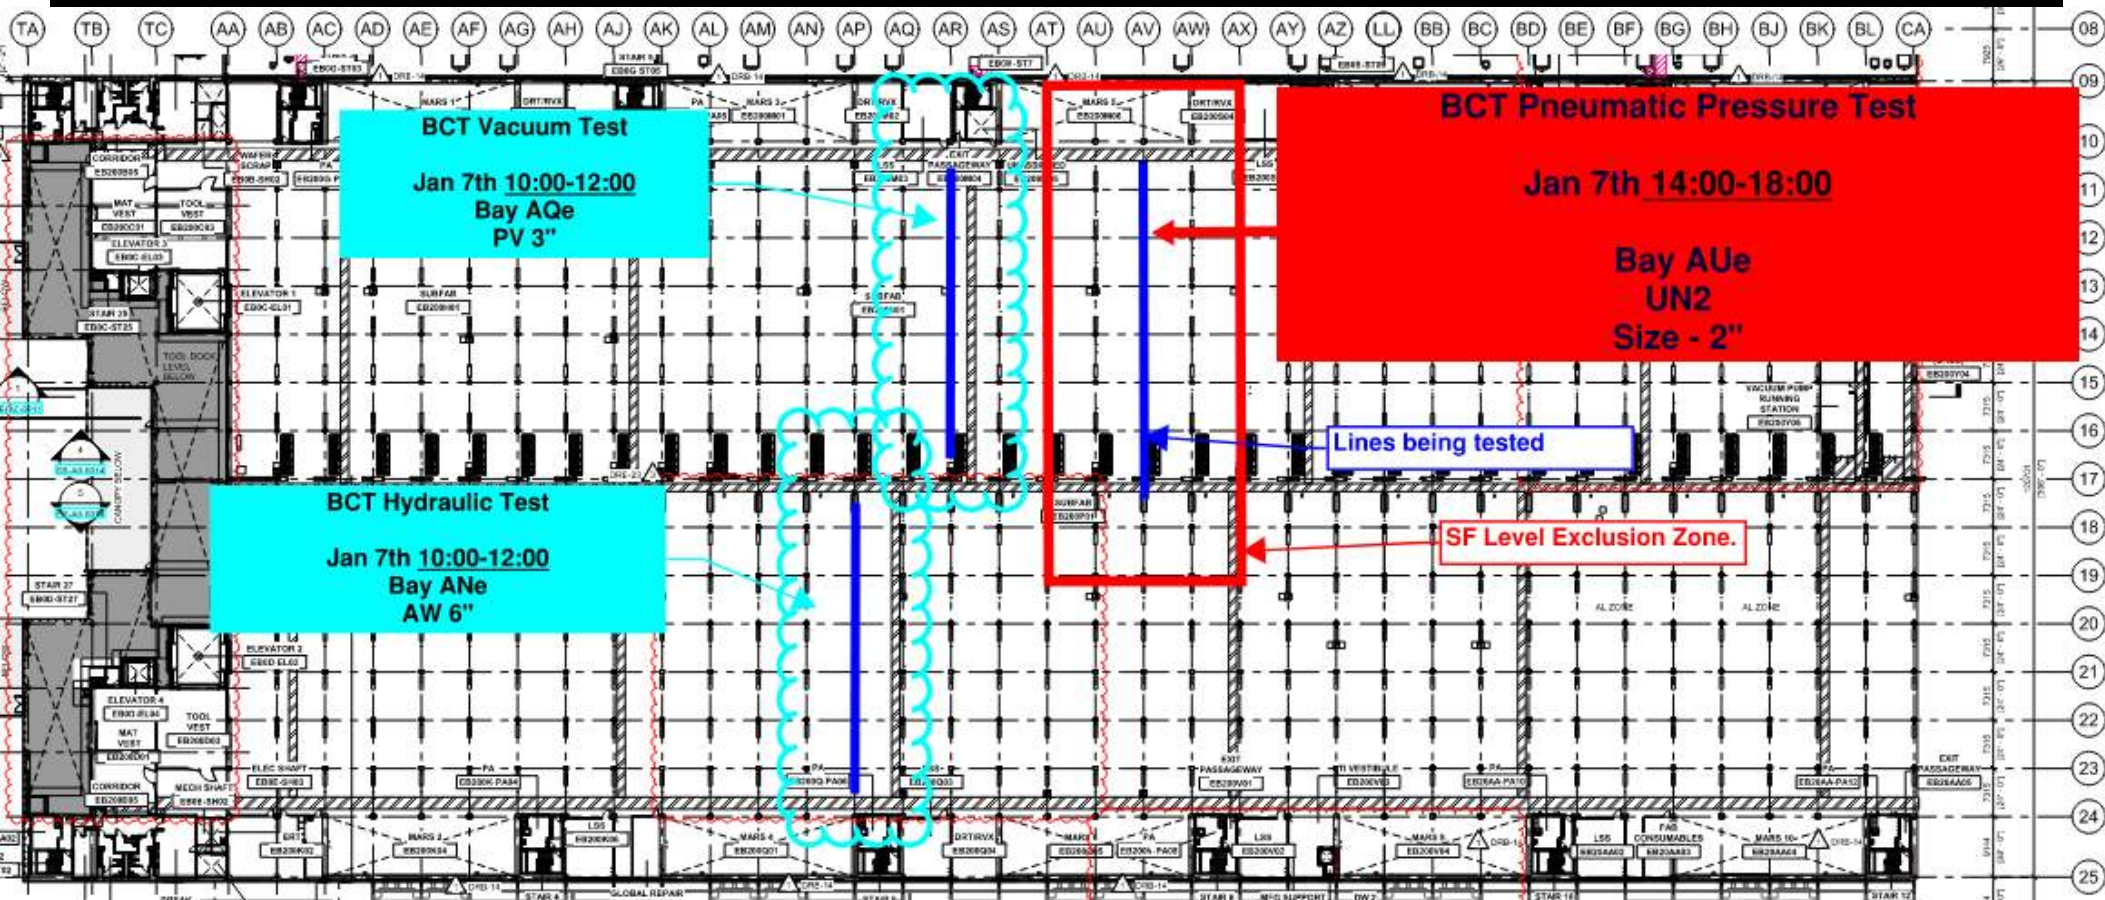



BCT Pressure Test Tomorrow

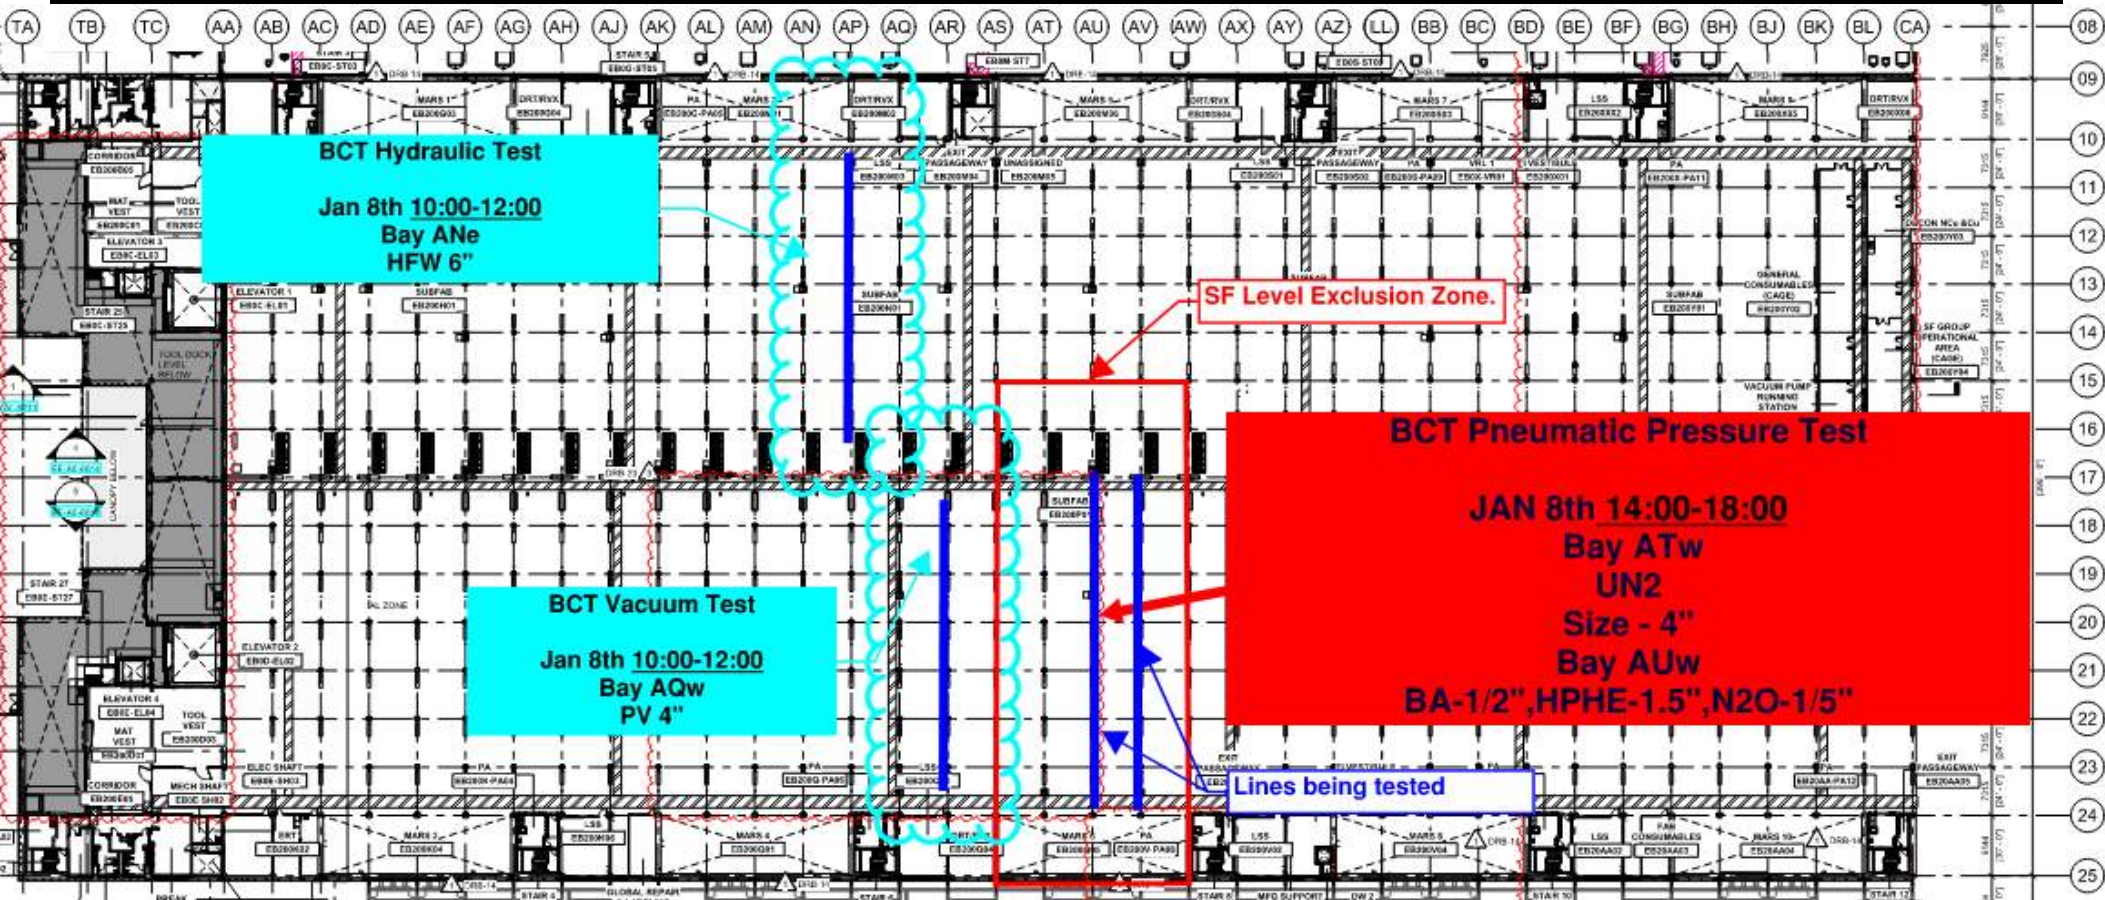

SUBFAB BUILDOUT MOD 2

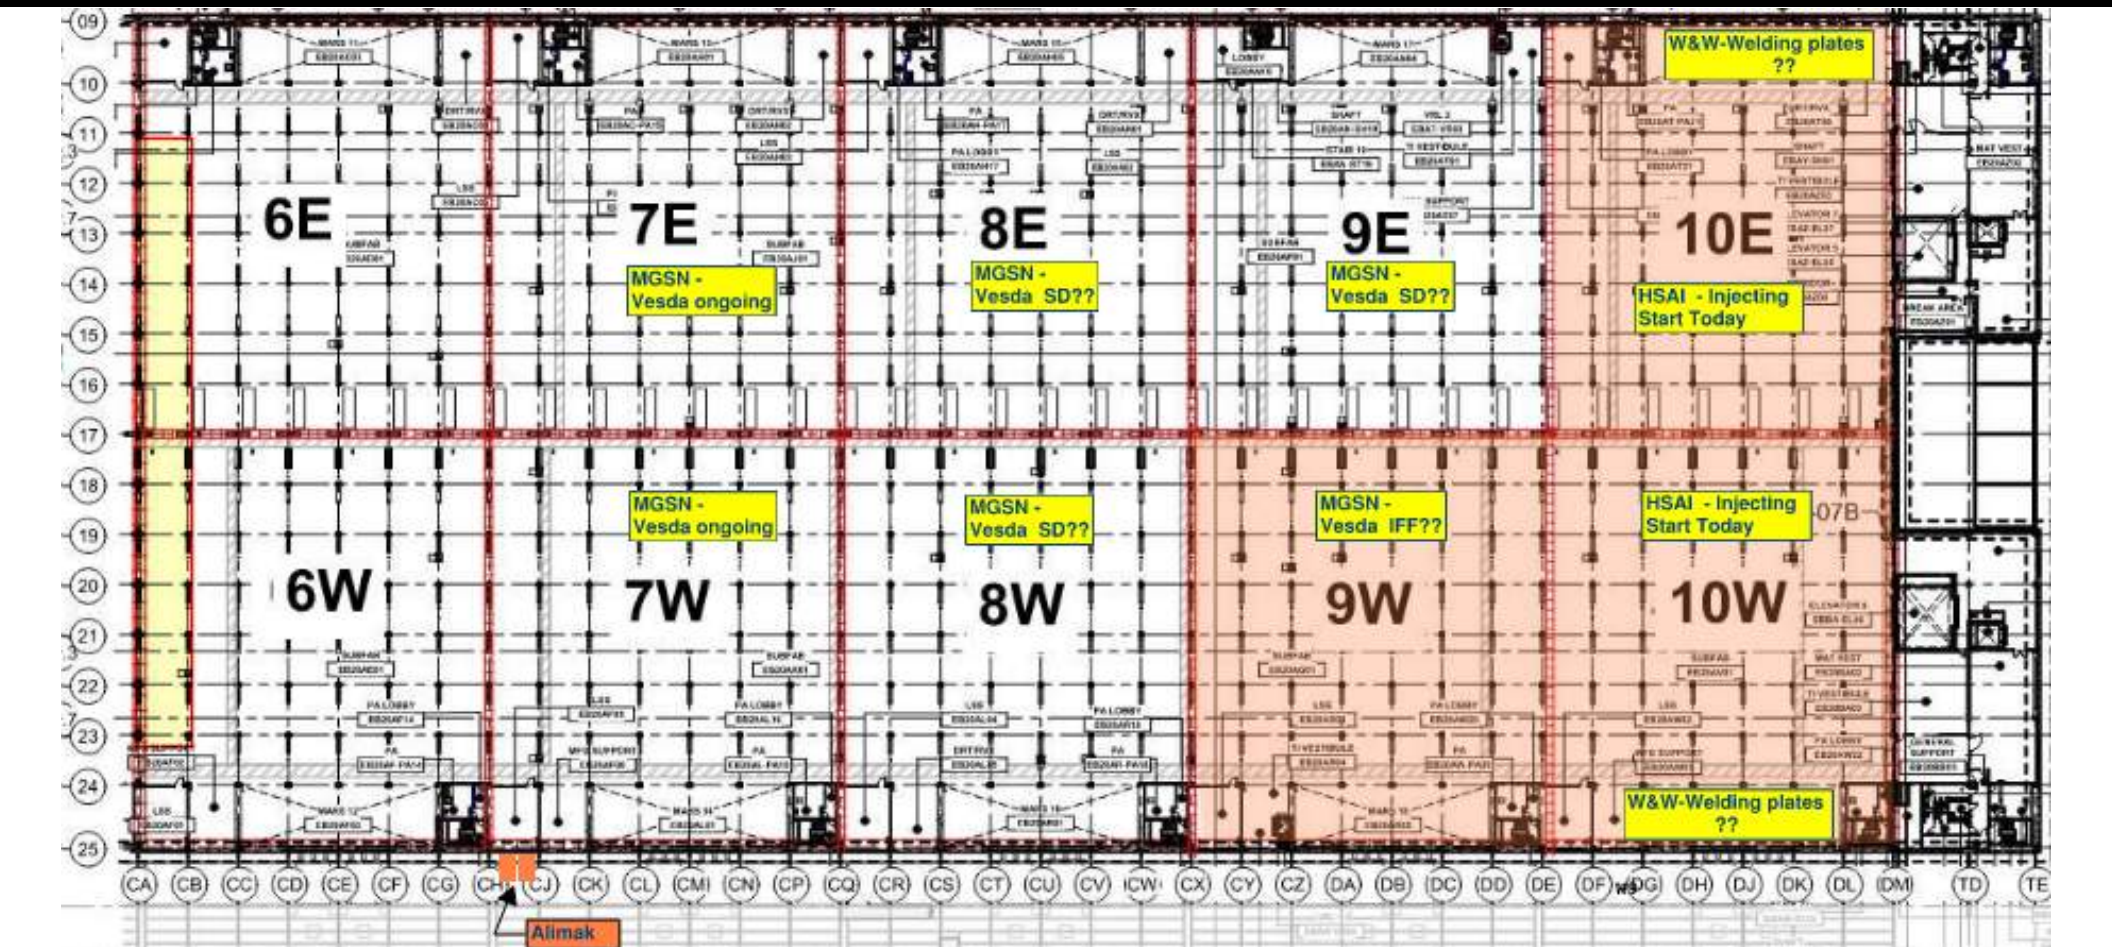


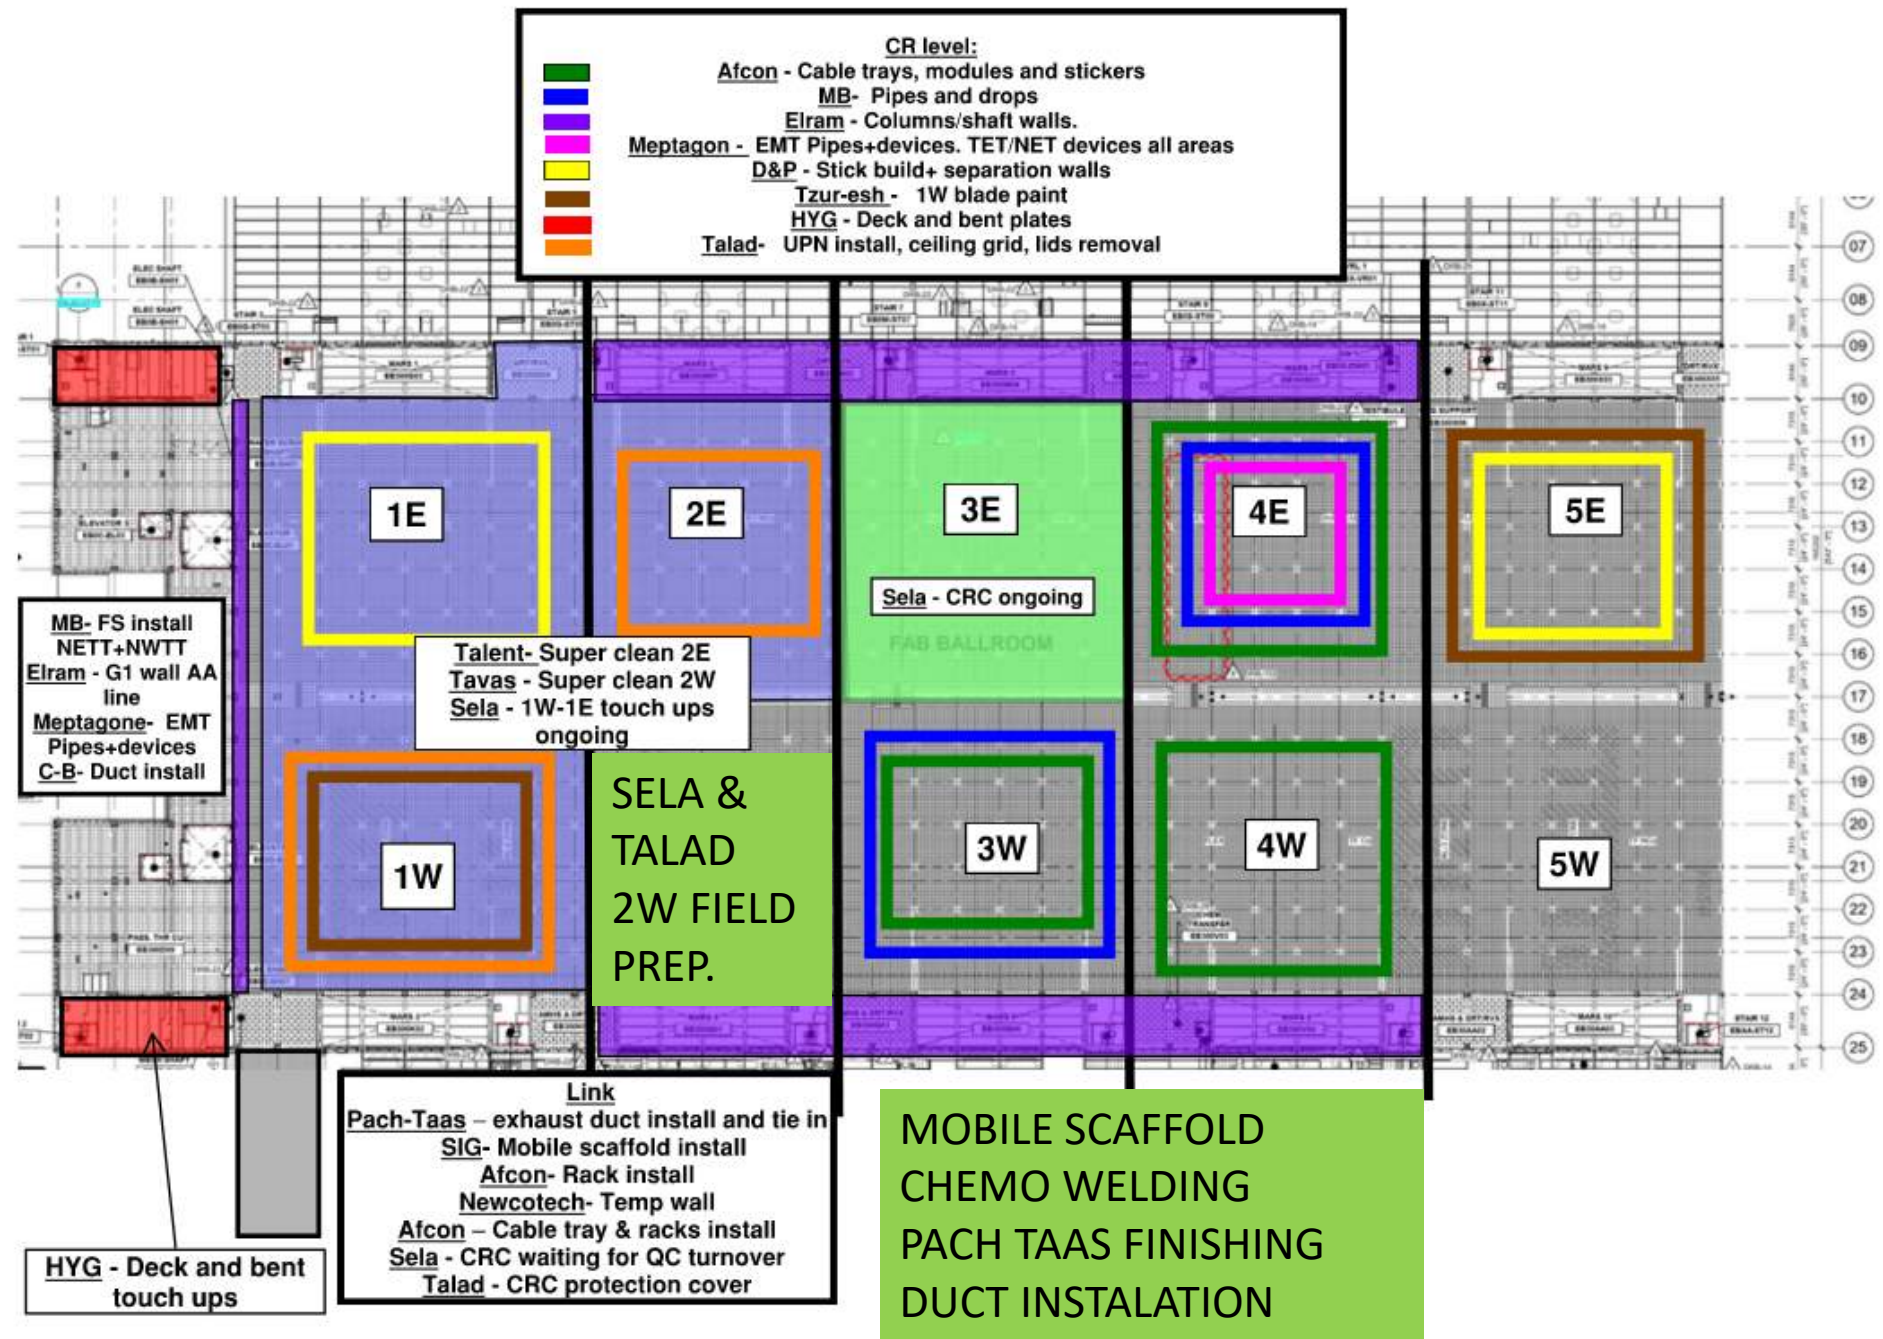


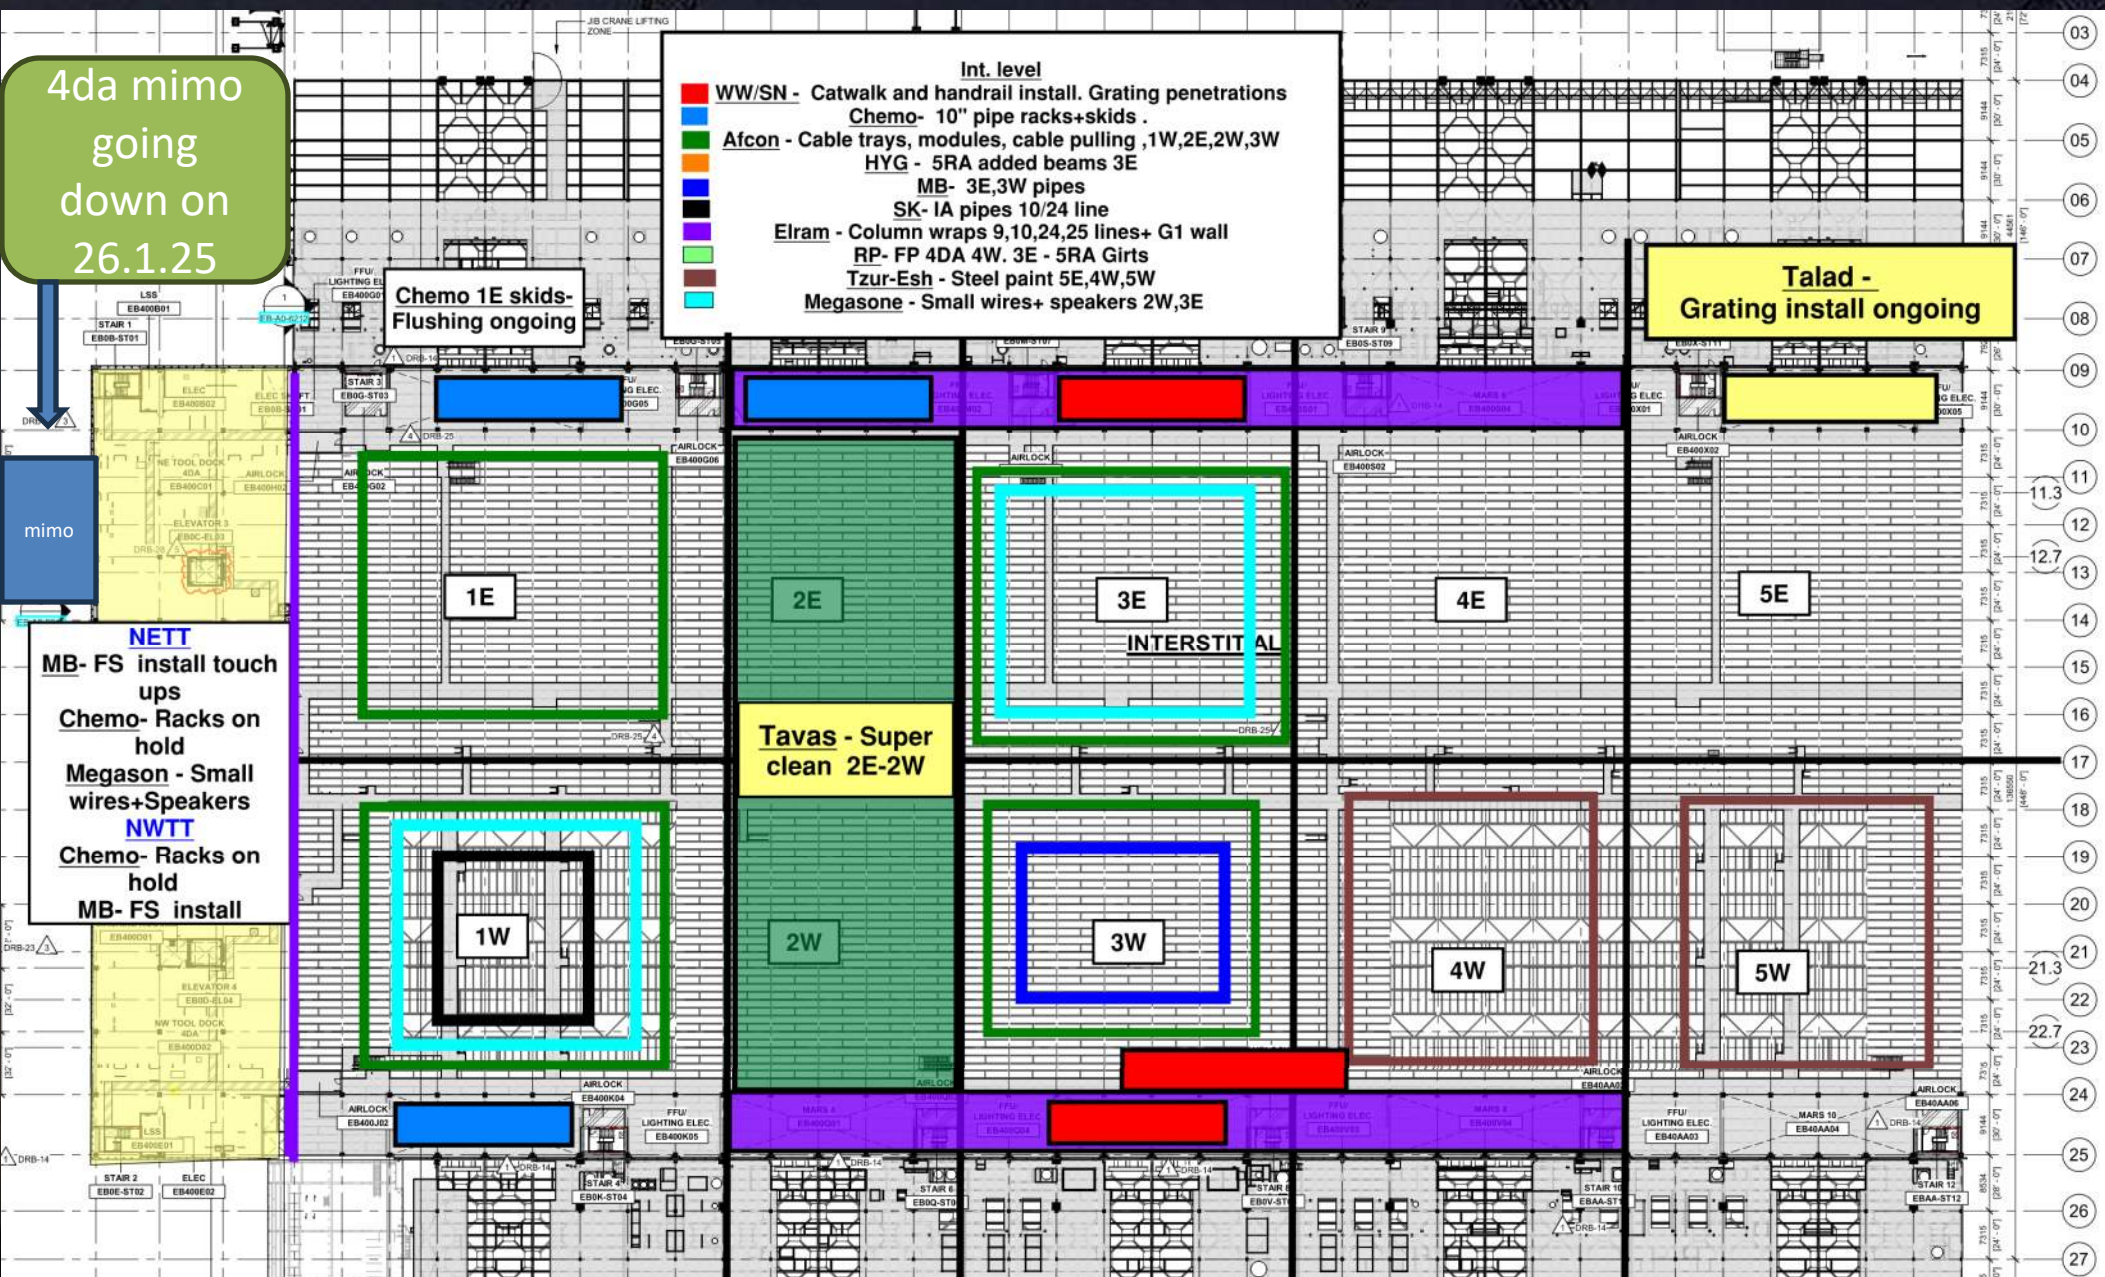



ROOF IS CLOSING THIS WEEK.

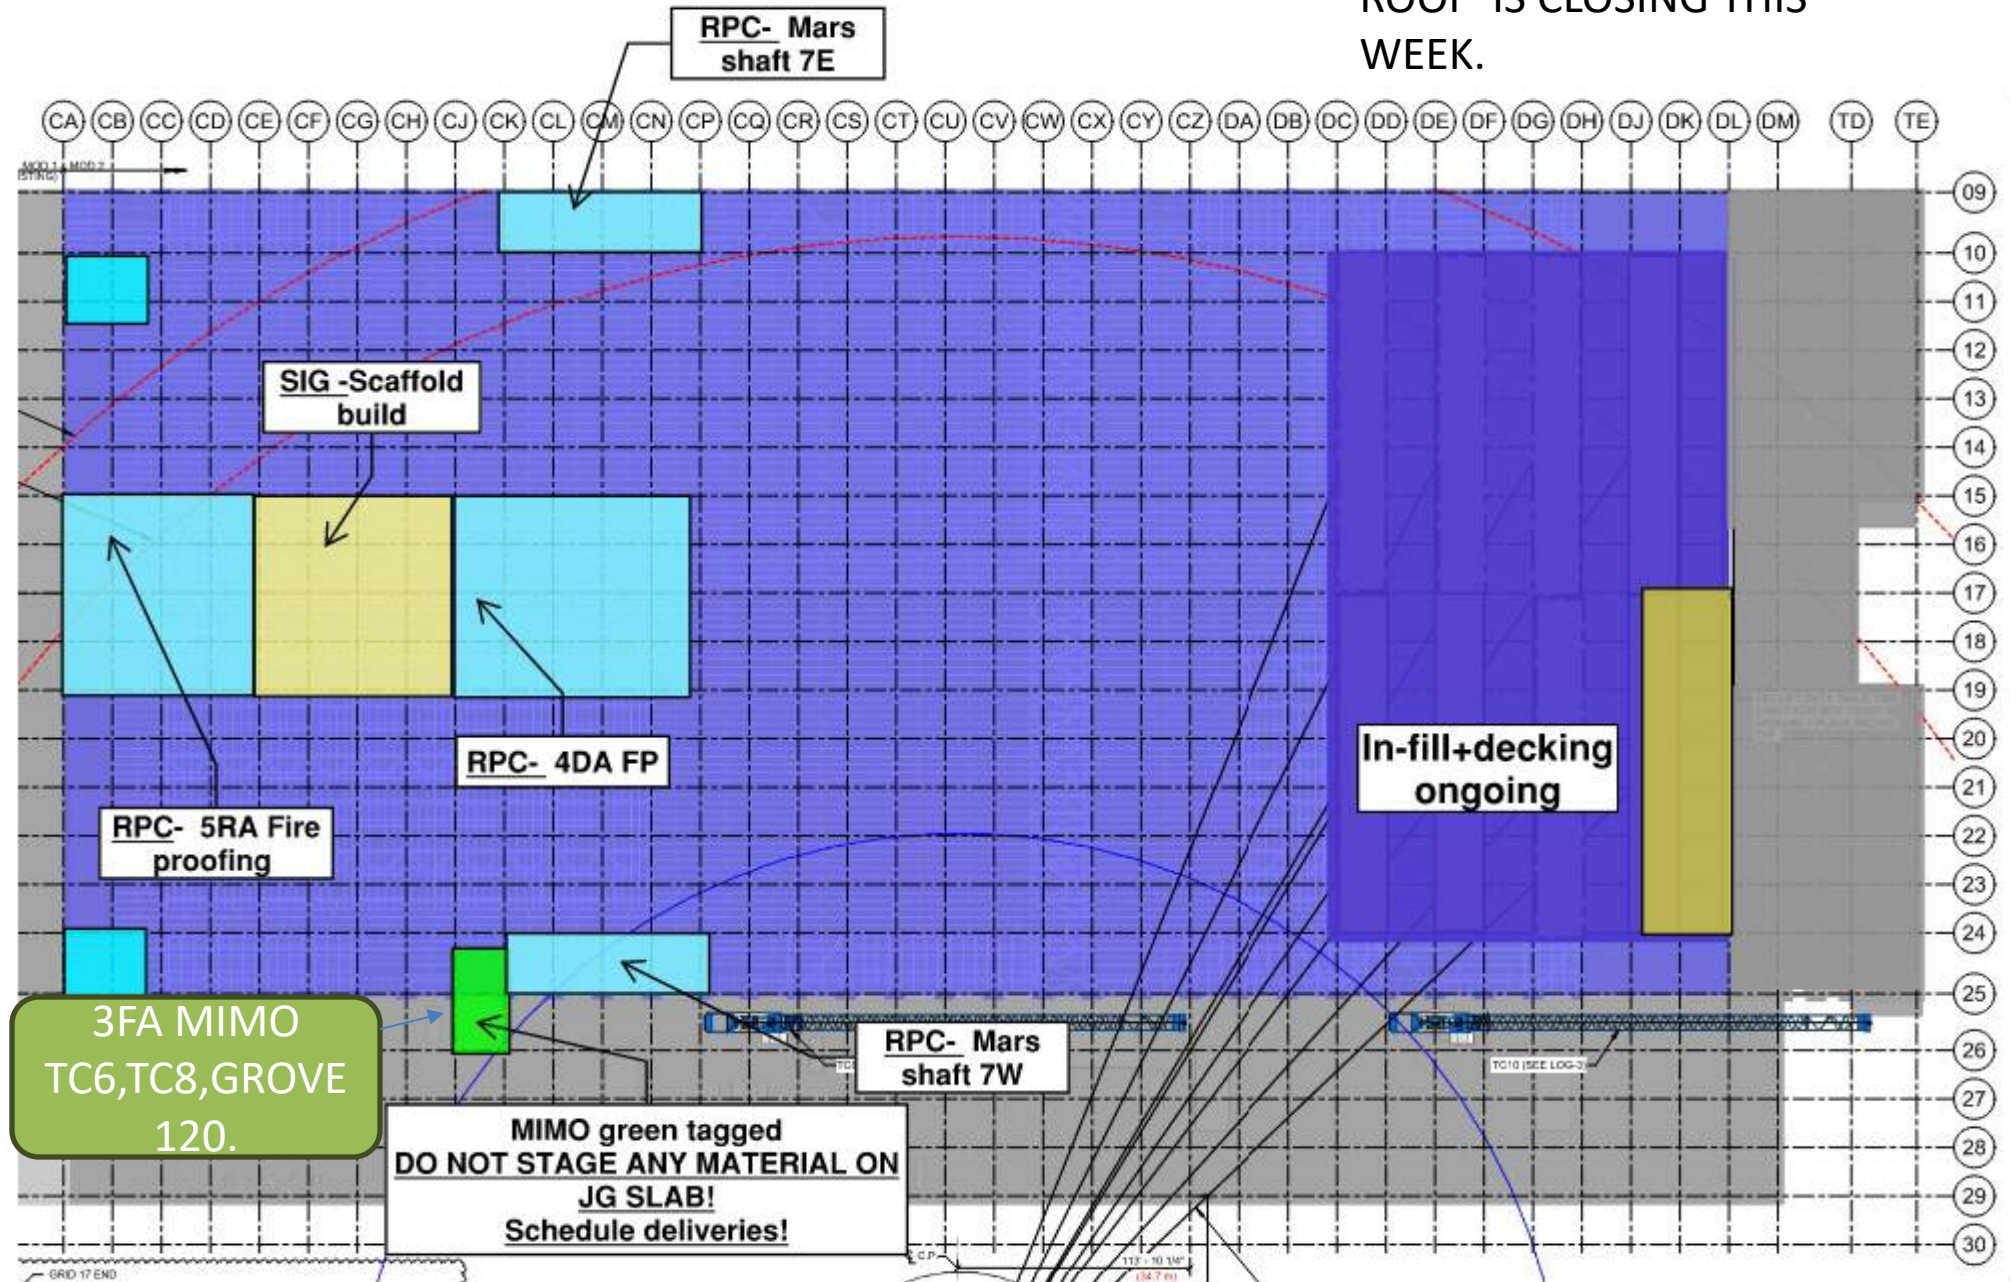

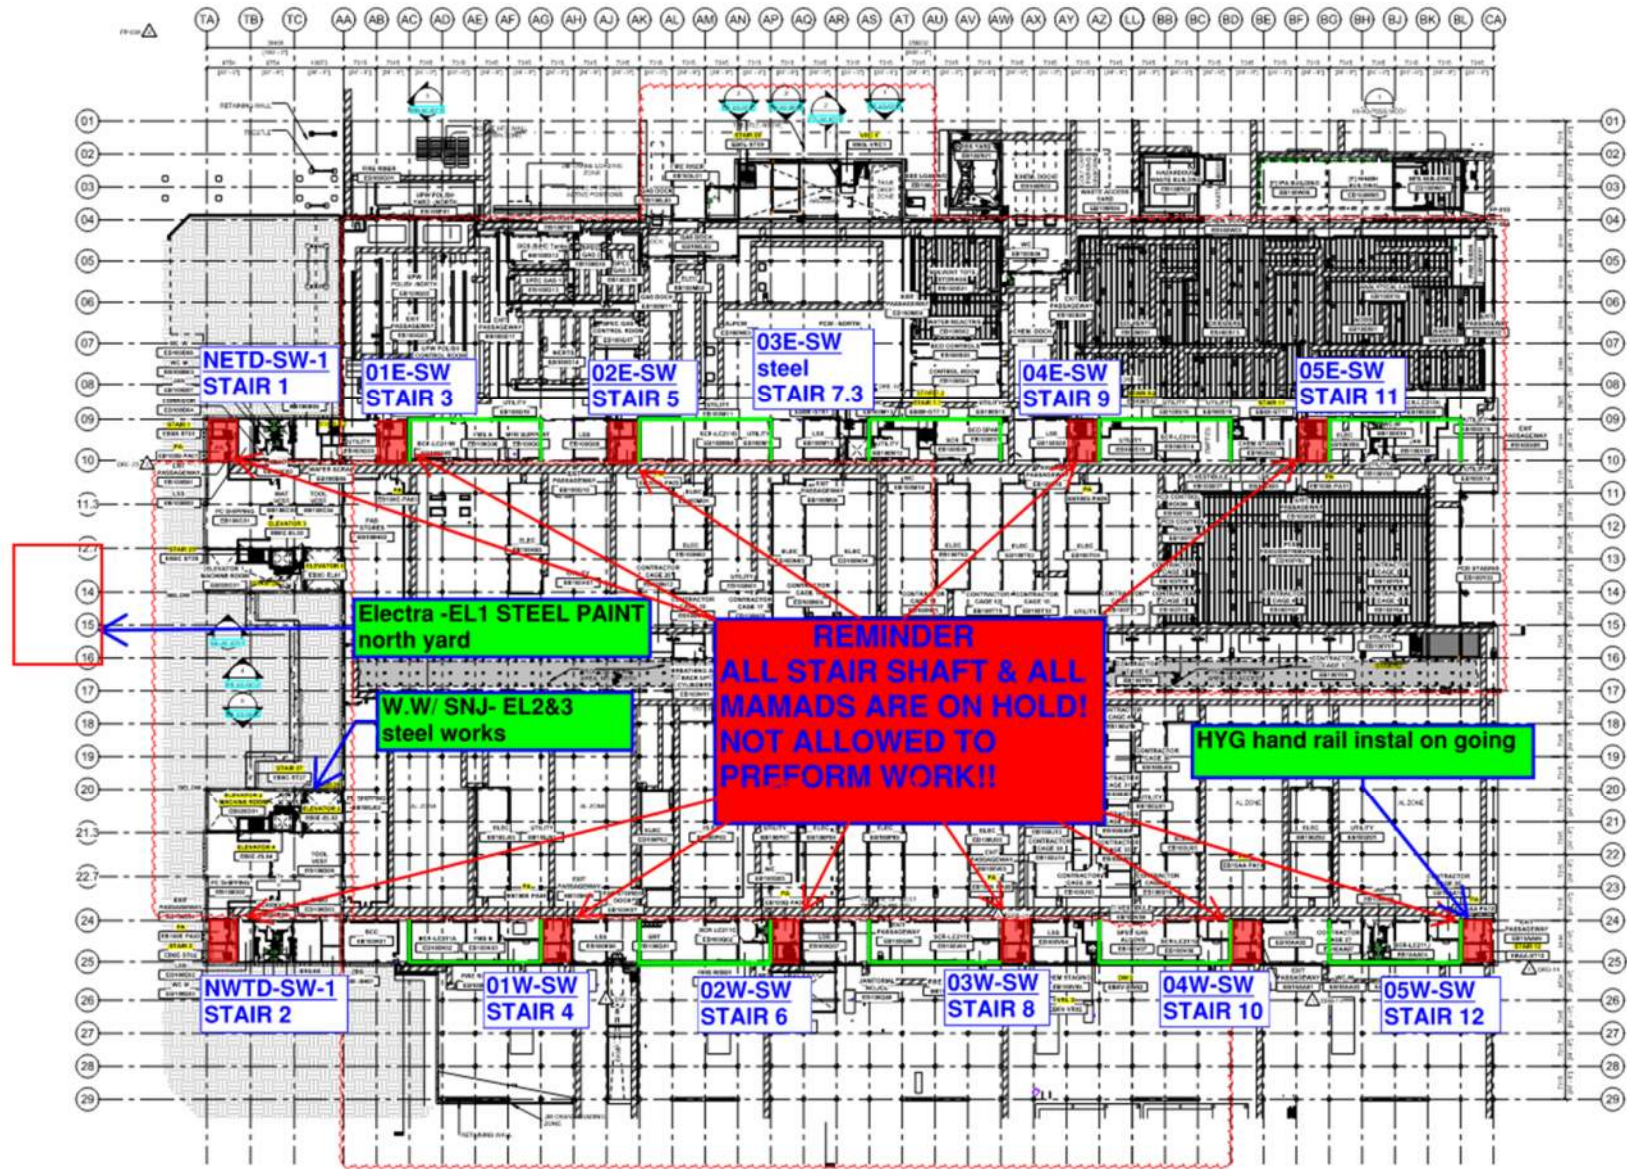


Mod 2 E House Roof
Picks.

Jan 8th @ 4:00 AM

Area to be
Closed for
Swing

Condensed
Barricade
for Bolting.

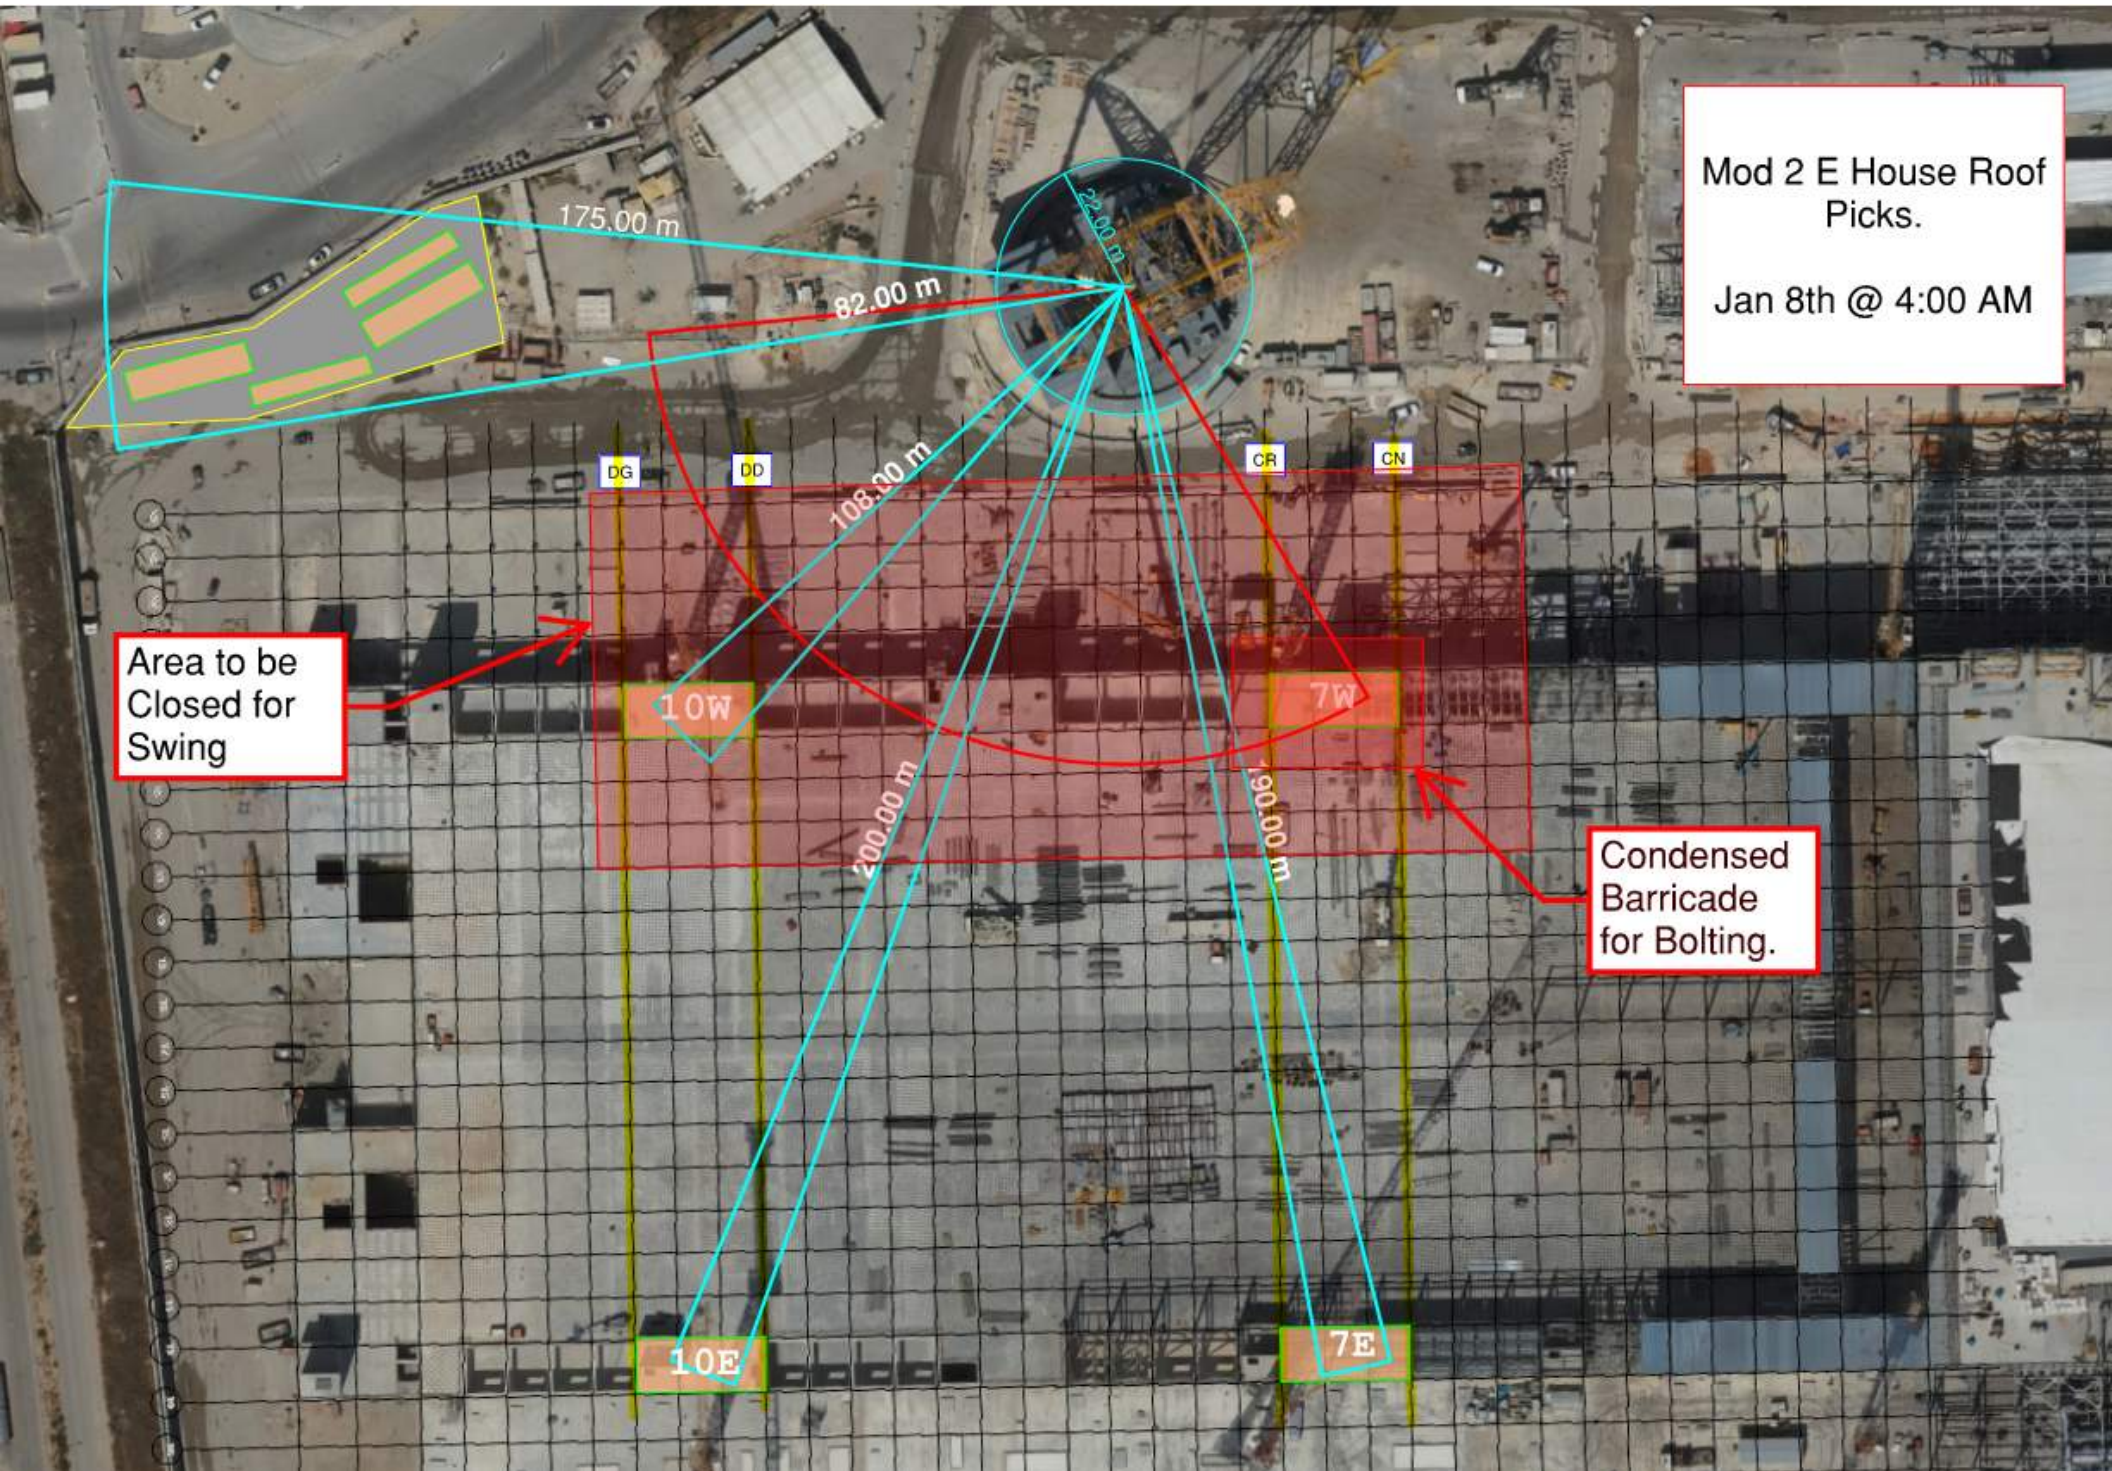

Siding - West FAB - JYG


BLOWDOWN 30%


Link


Siding - East FAB - PSSS

BLOWDOWN 30%

[illegible]

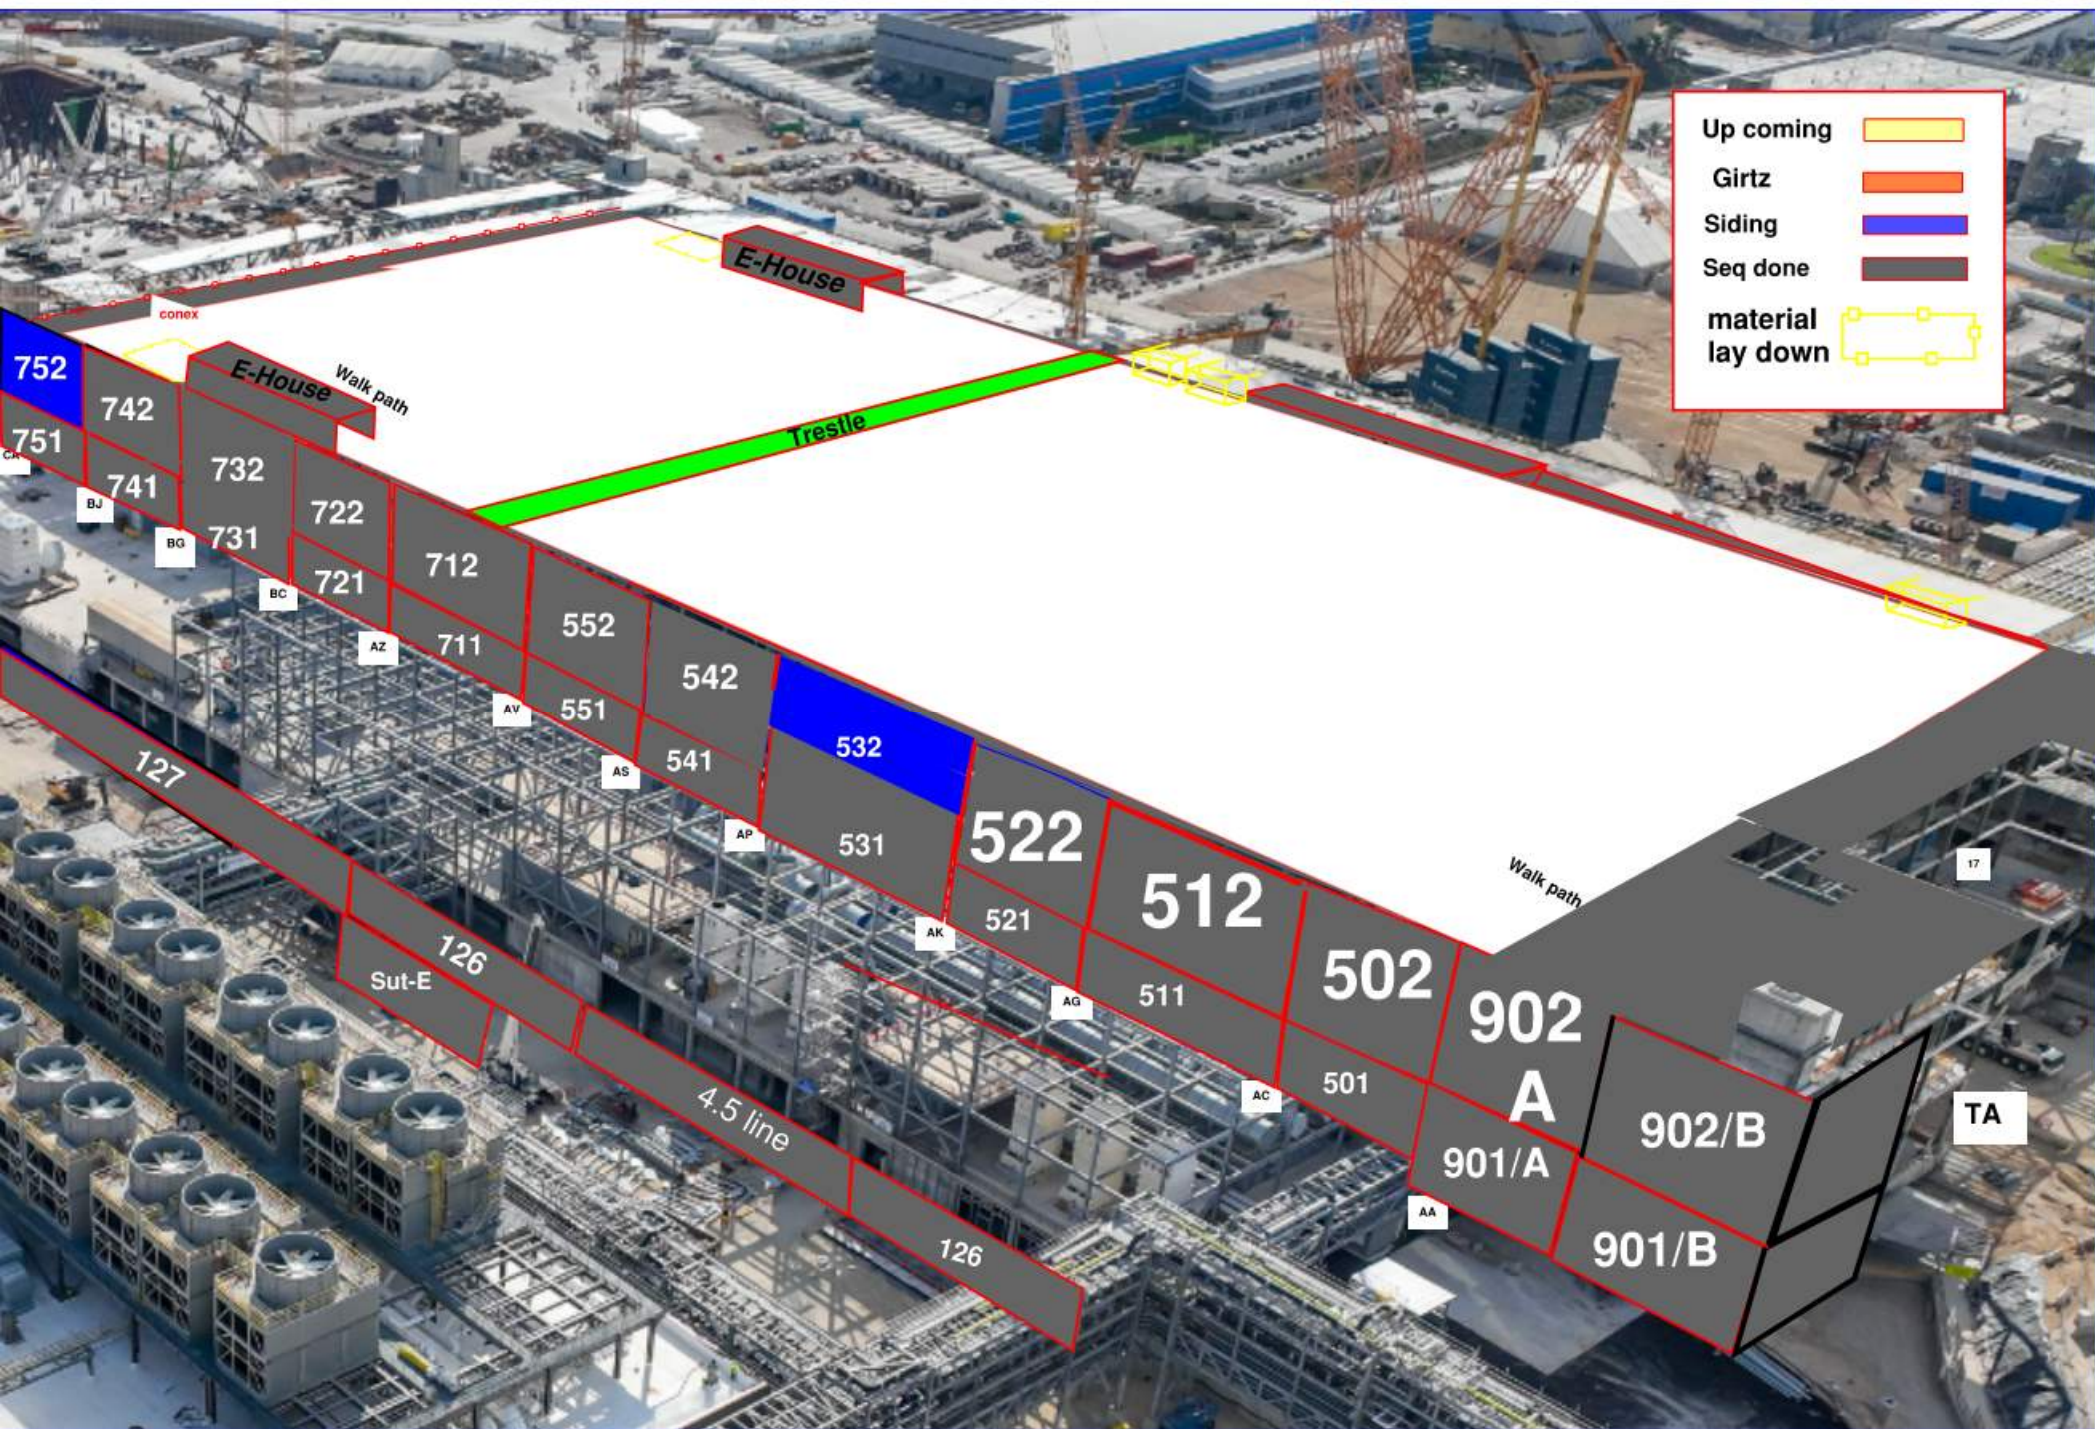

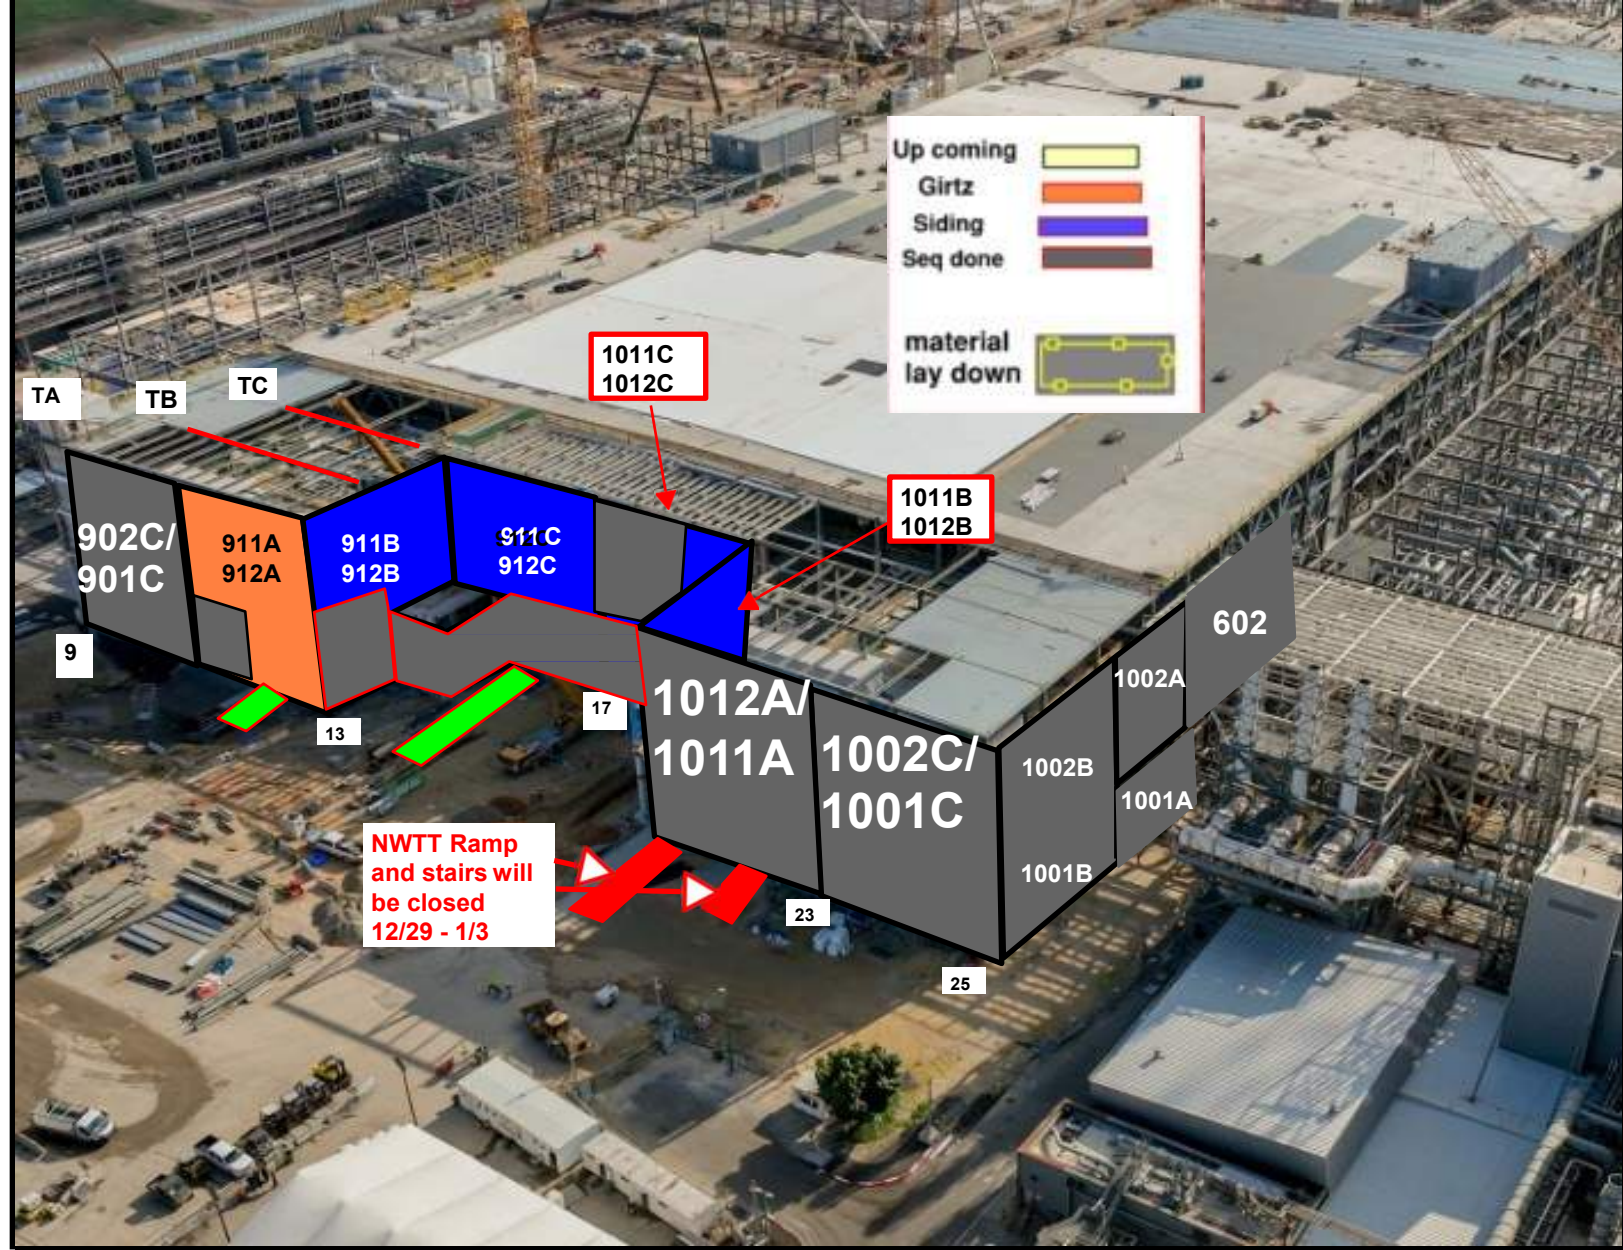


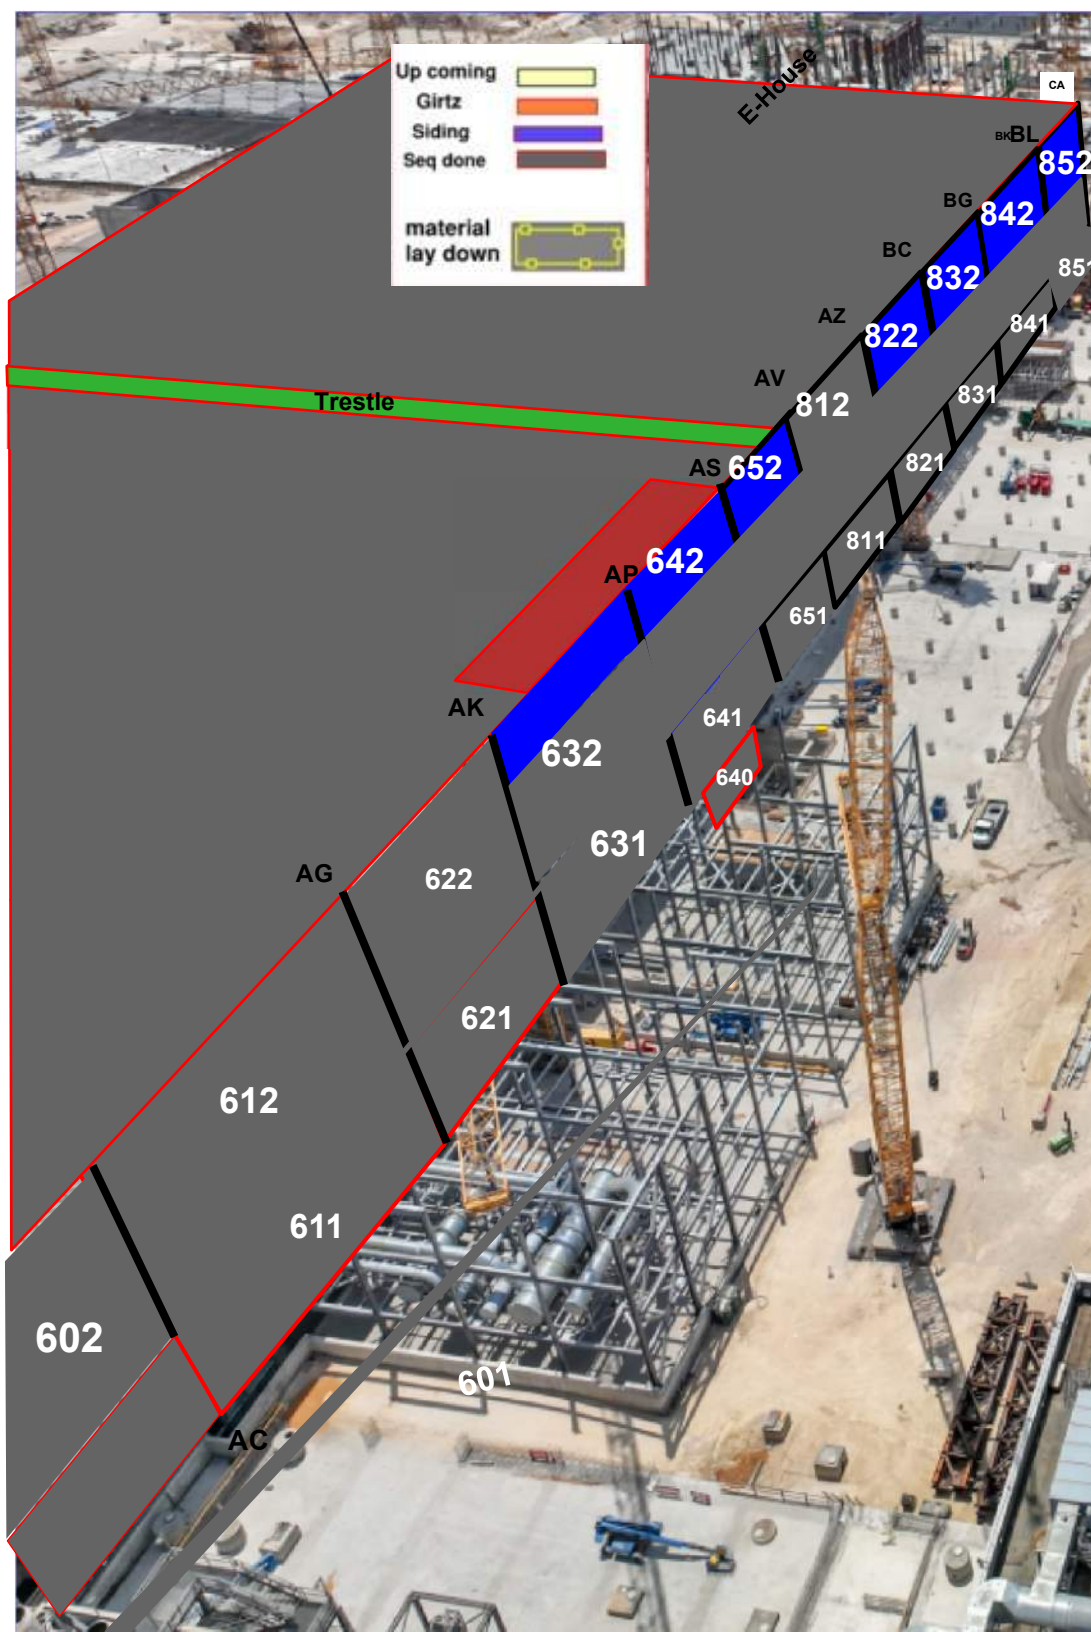


PSSS.1

Utility Level
1YA

PSSS Roof
2SA

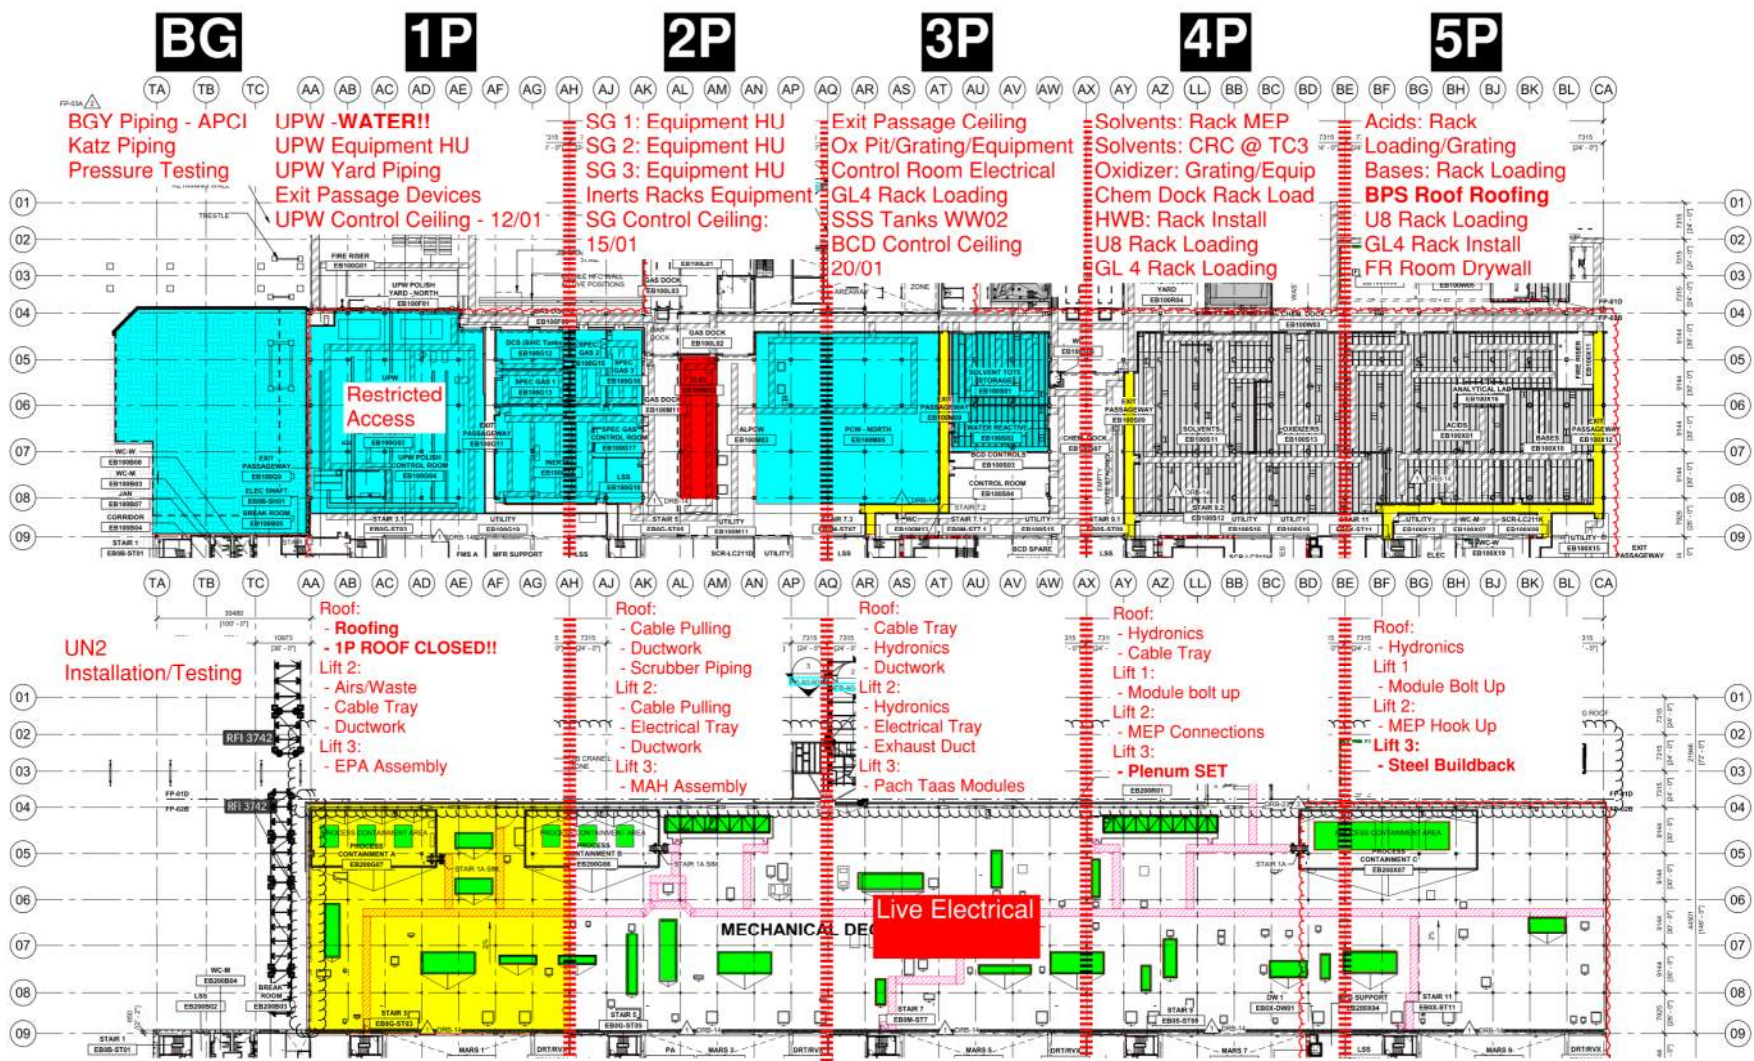


PSSS.2

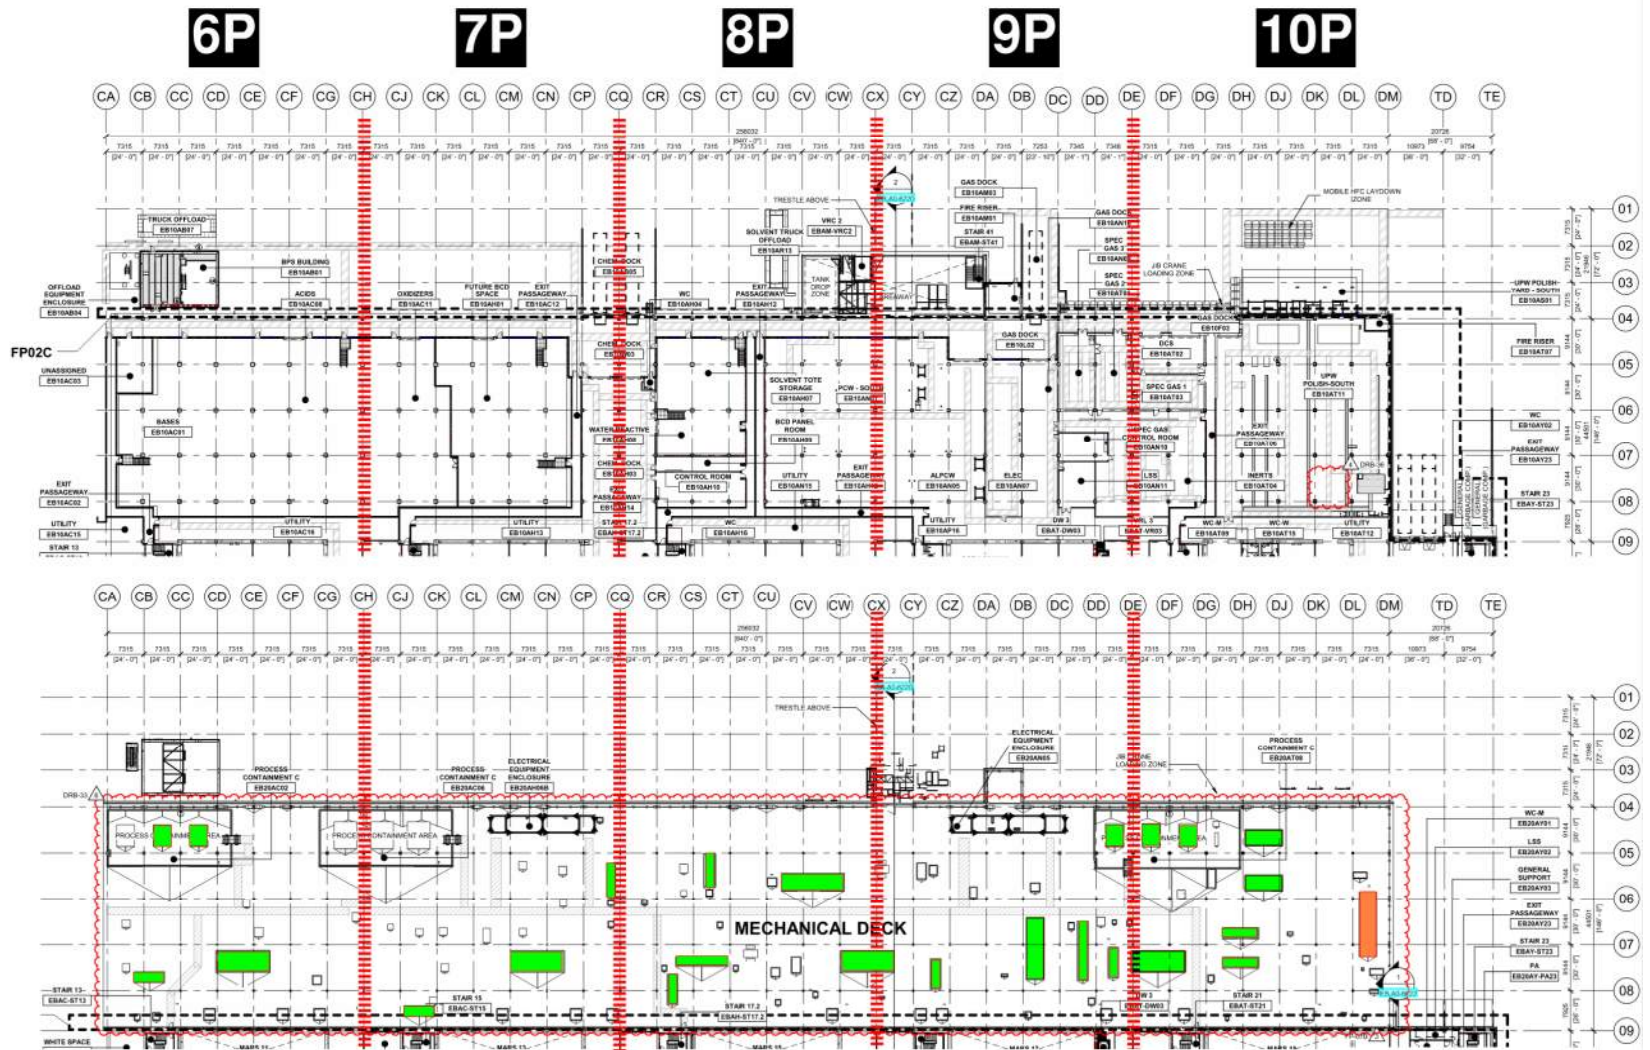


PSSS Pressure Tests

Utility Level
1YA

PSSS Roof
2SA

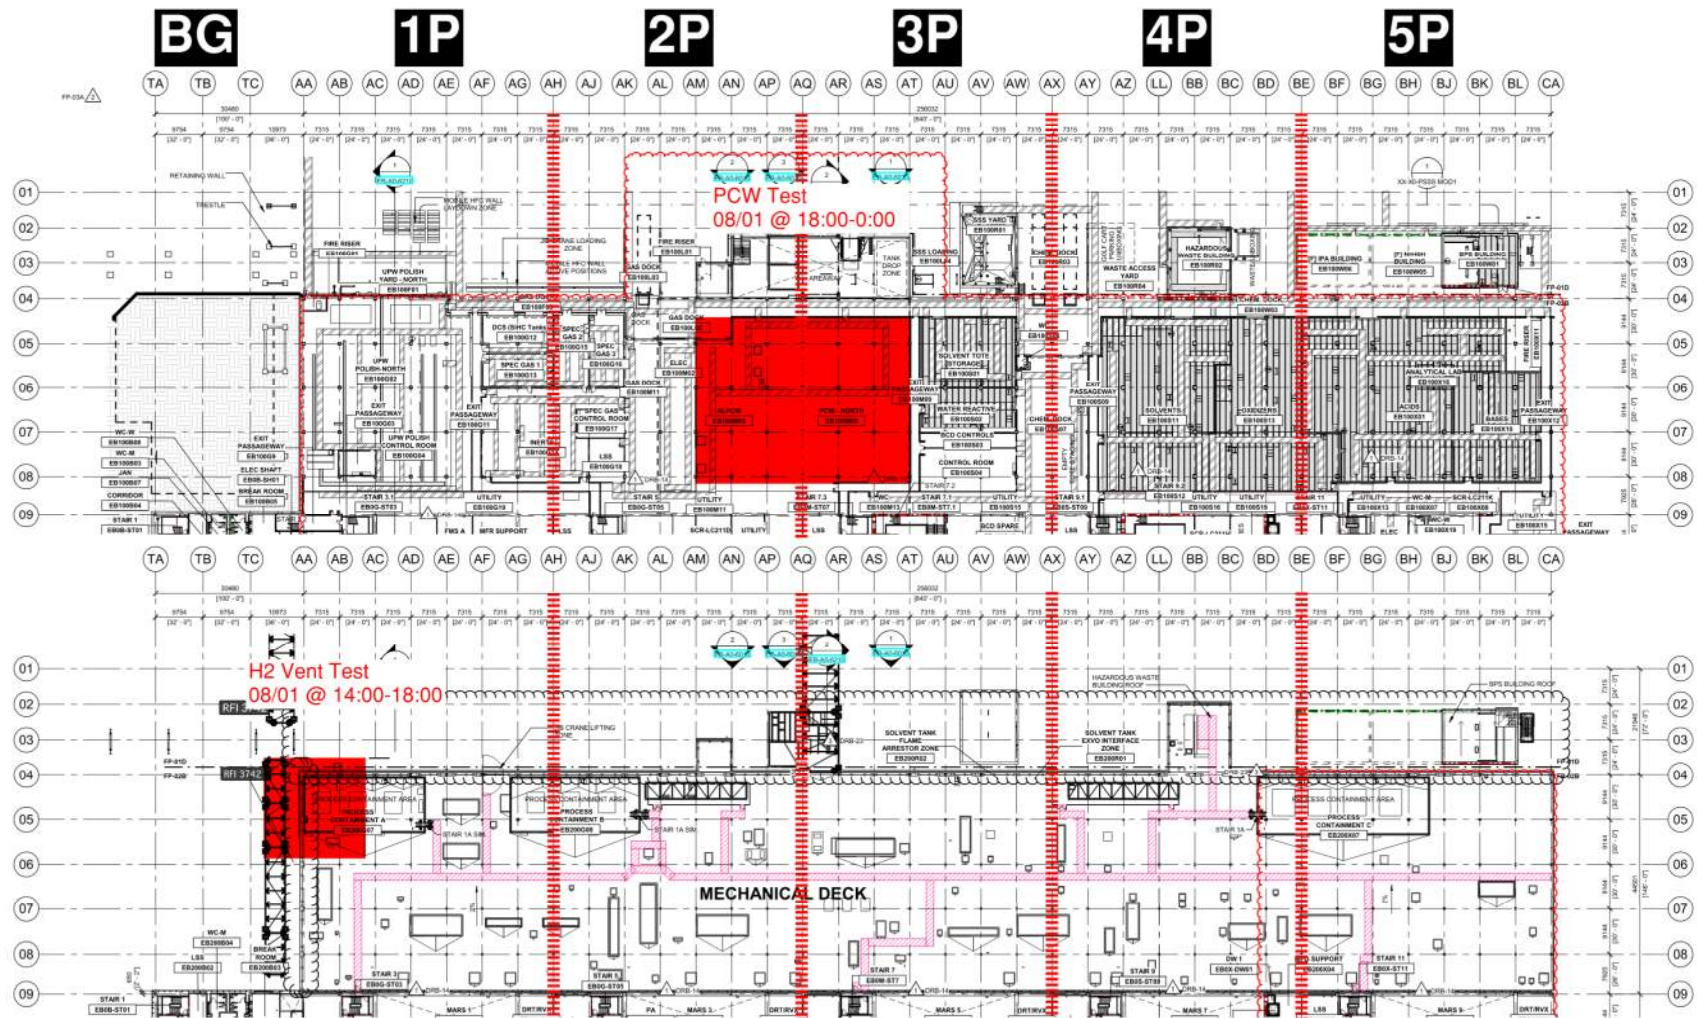


3800 Hoisting WW02

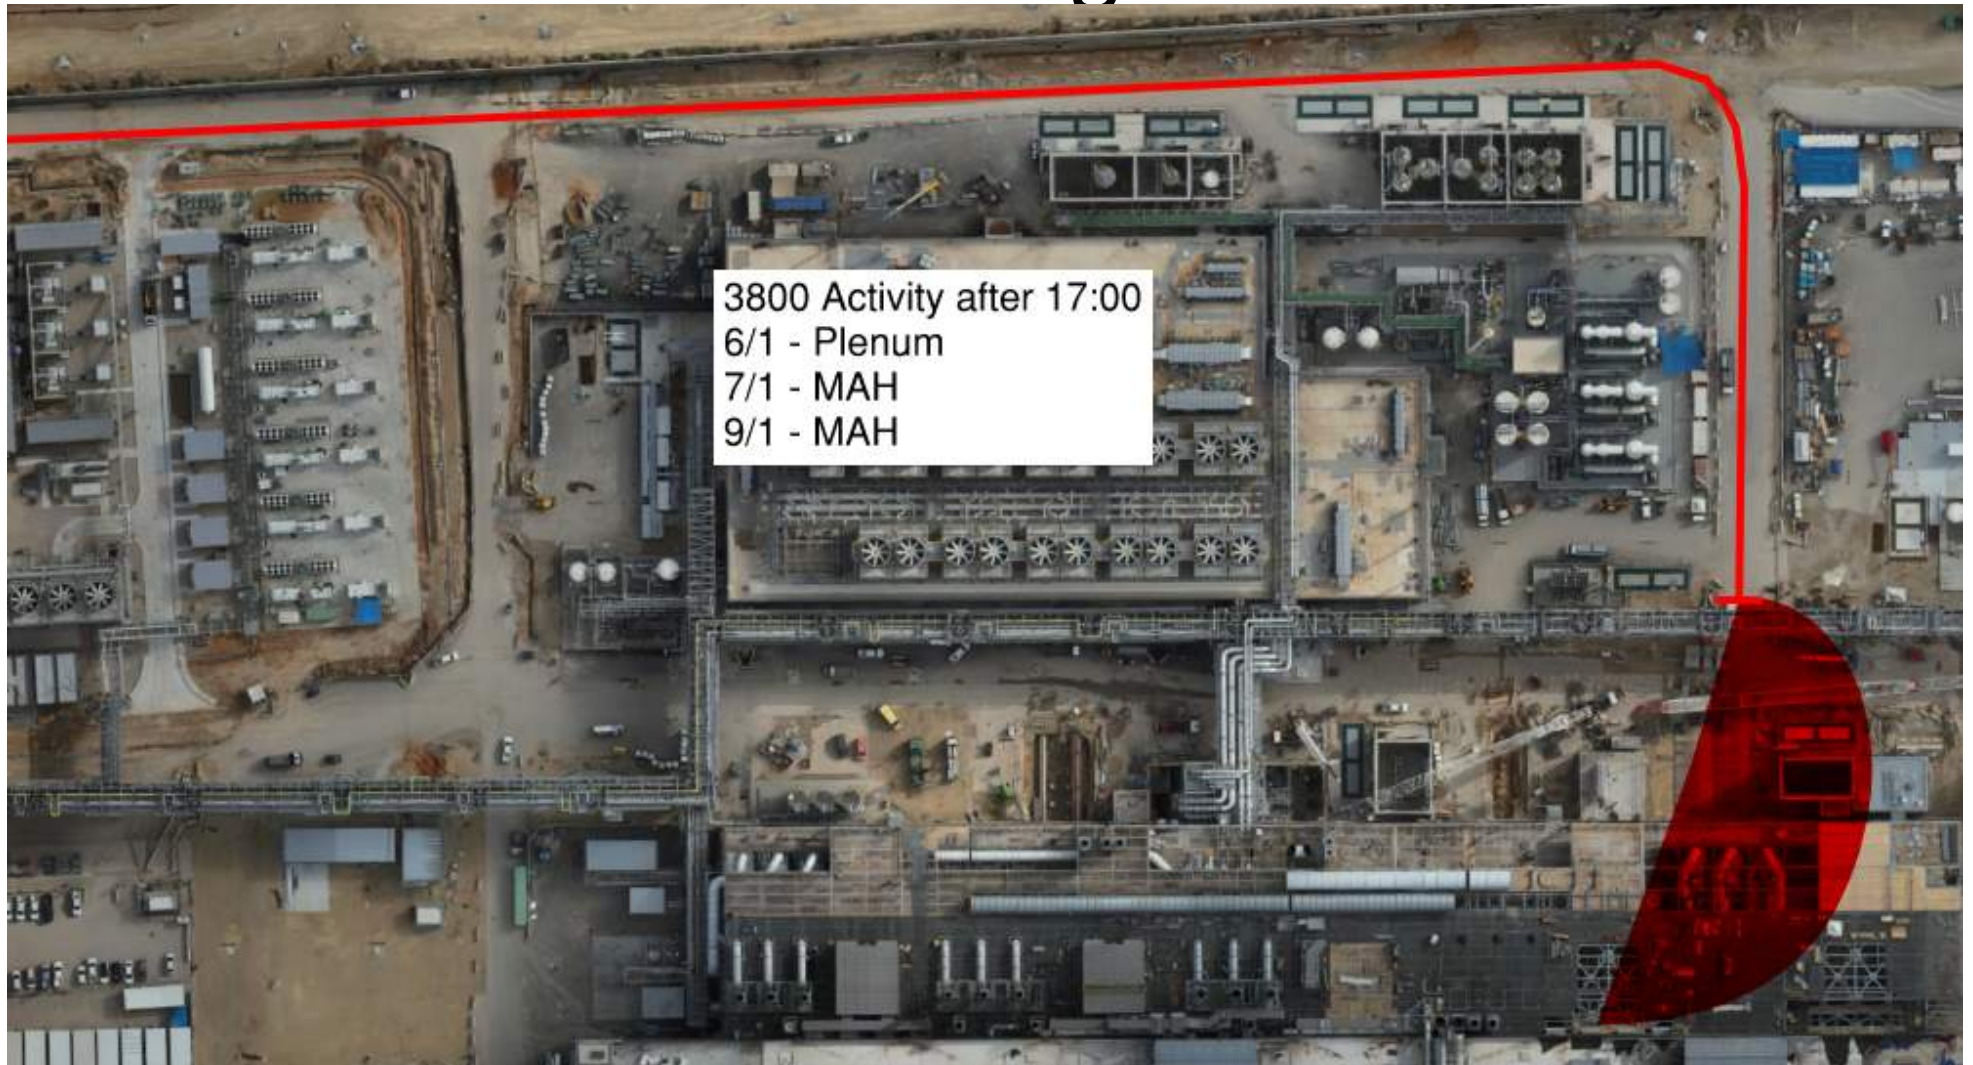

WJG 01J, 02J LIFT 2 & 3




WJG 03J, 04J, 05J LIFT 2 & 3

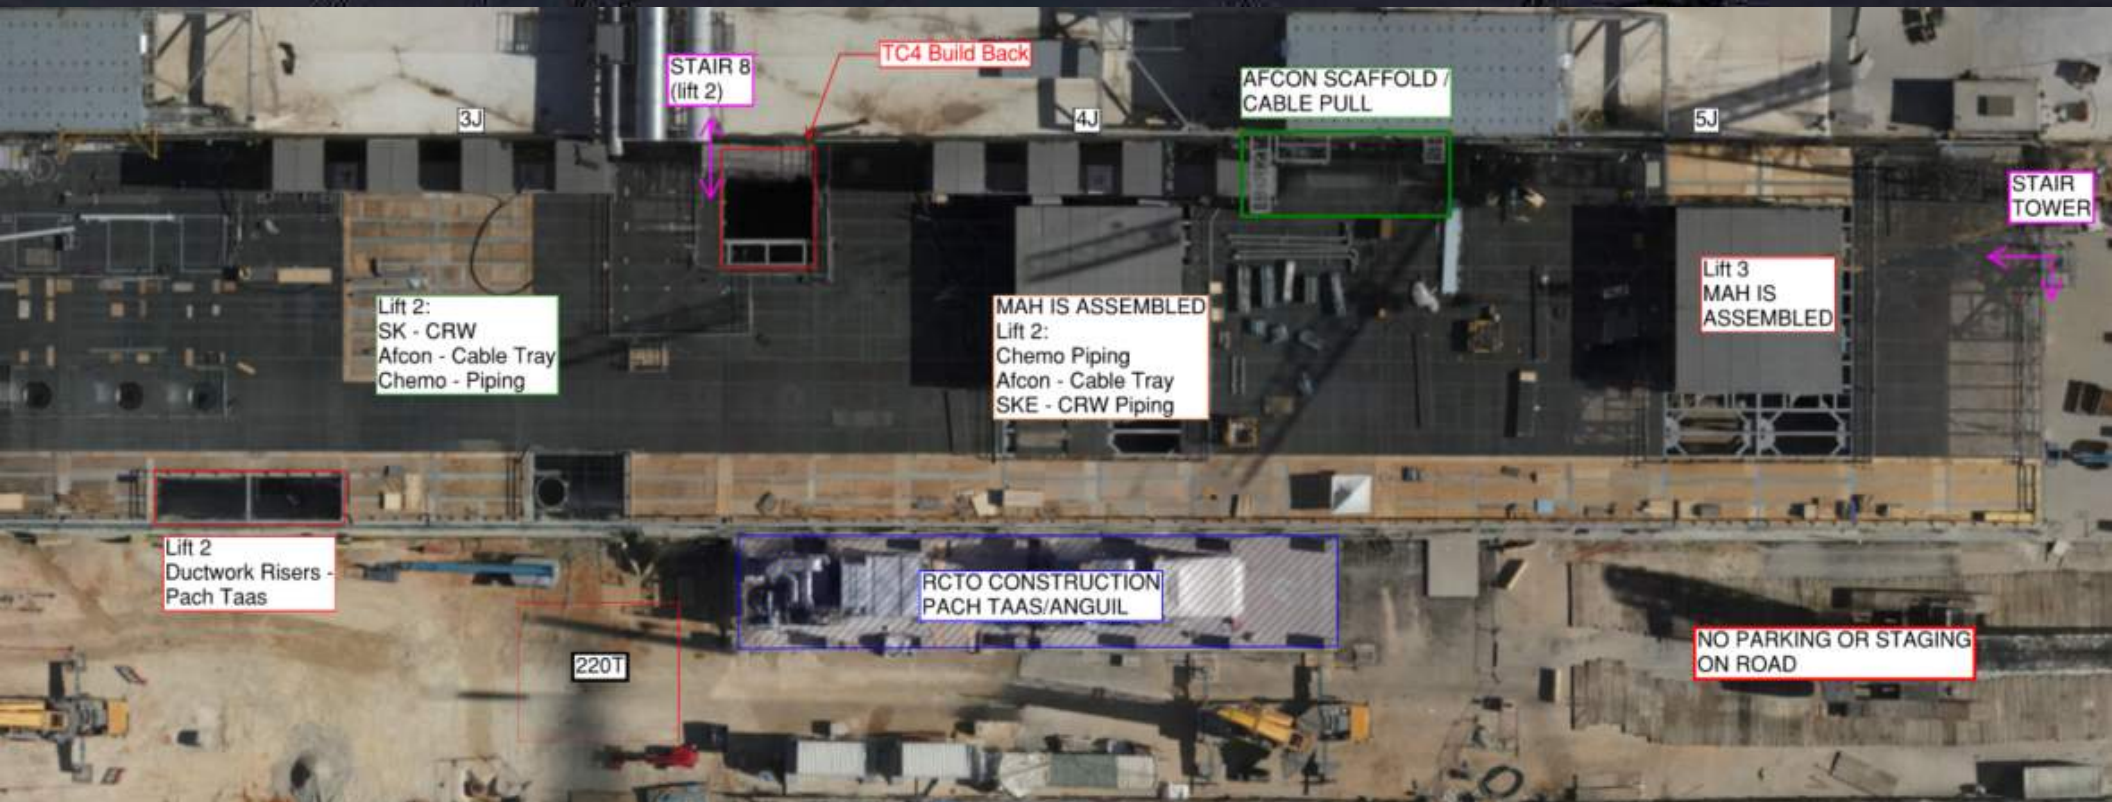



WJG UTILITY LEVEL BUILD OUT

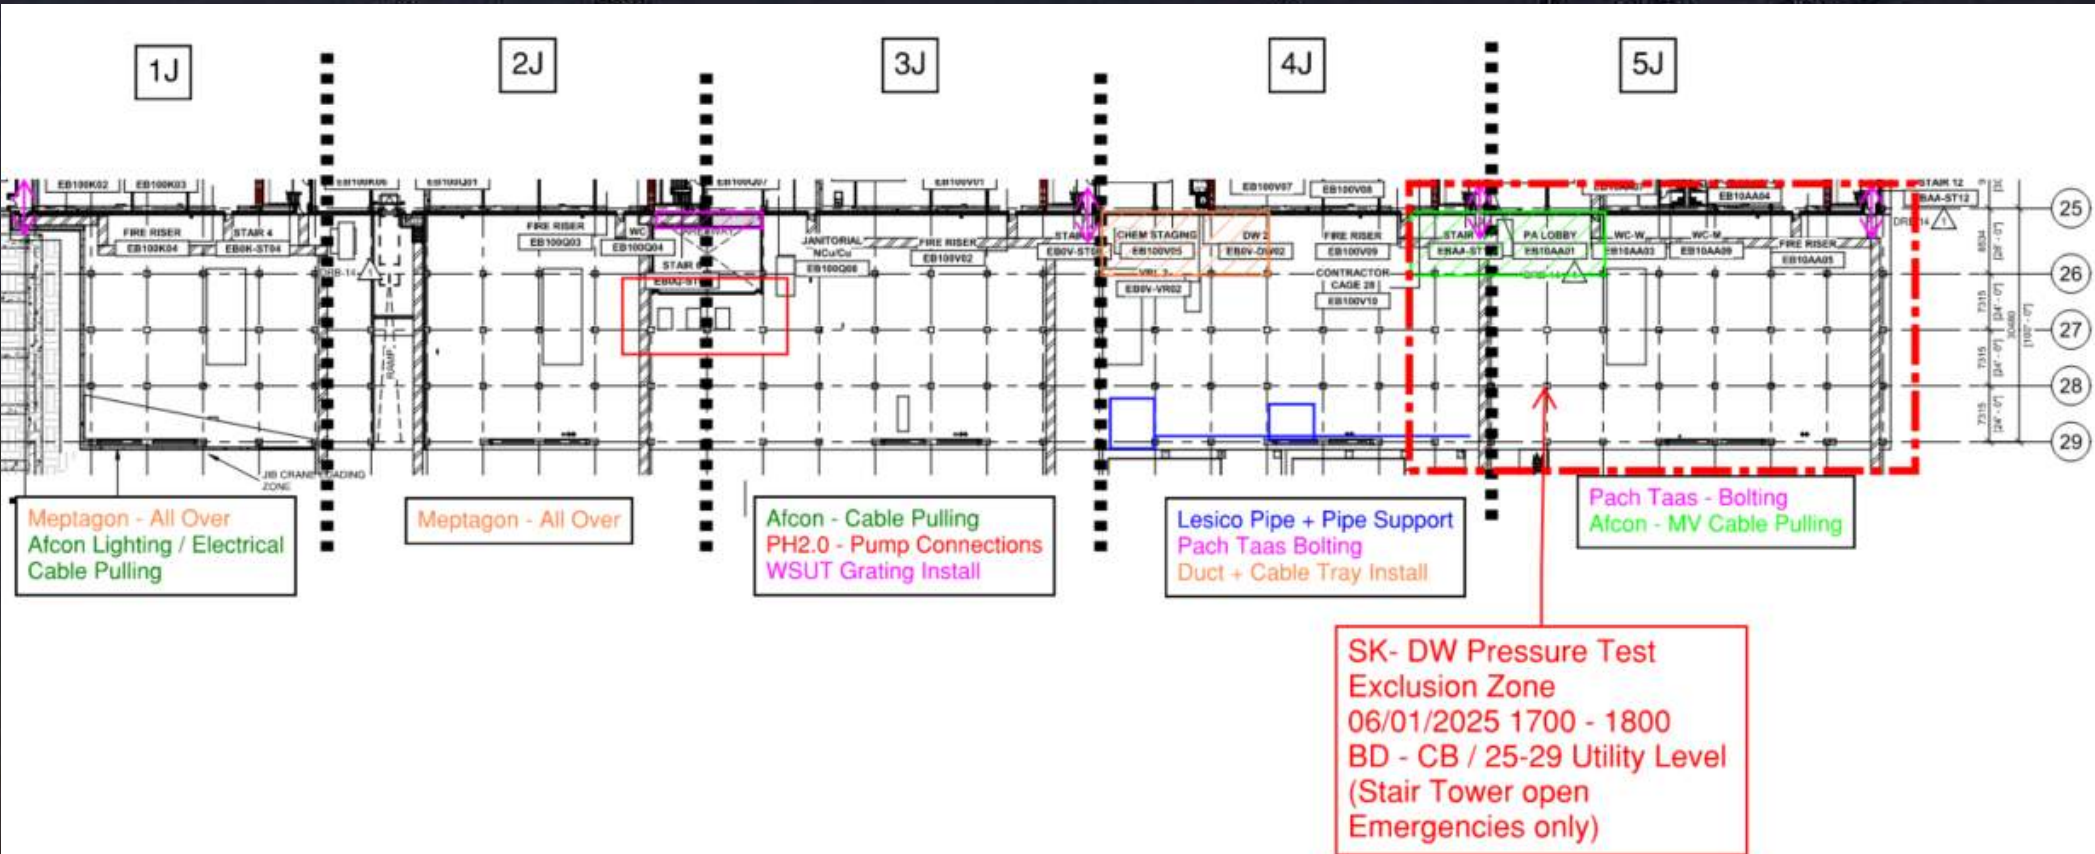


CUB 1 Intel Fuel Off-Load







CUB 1

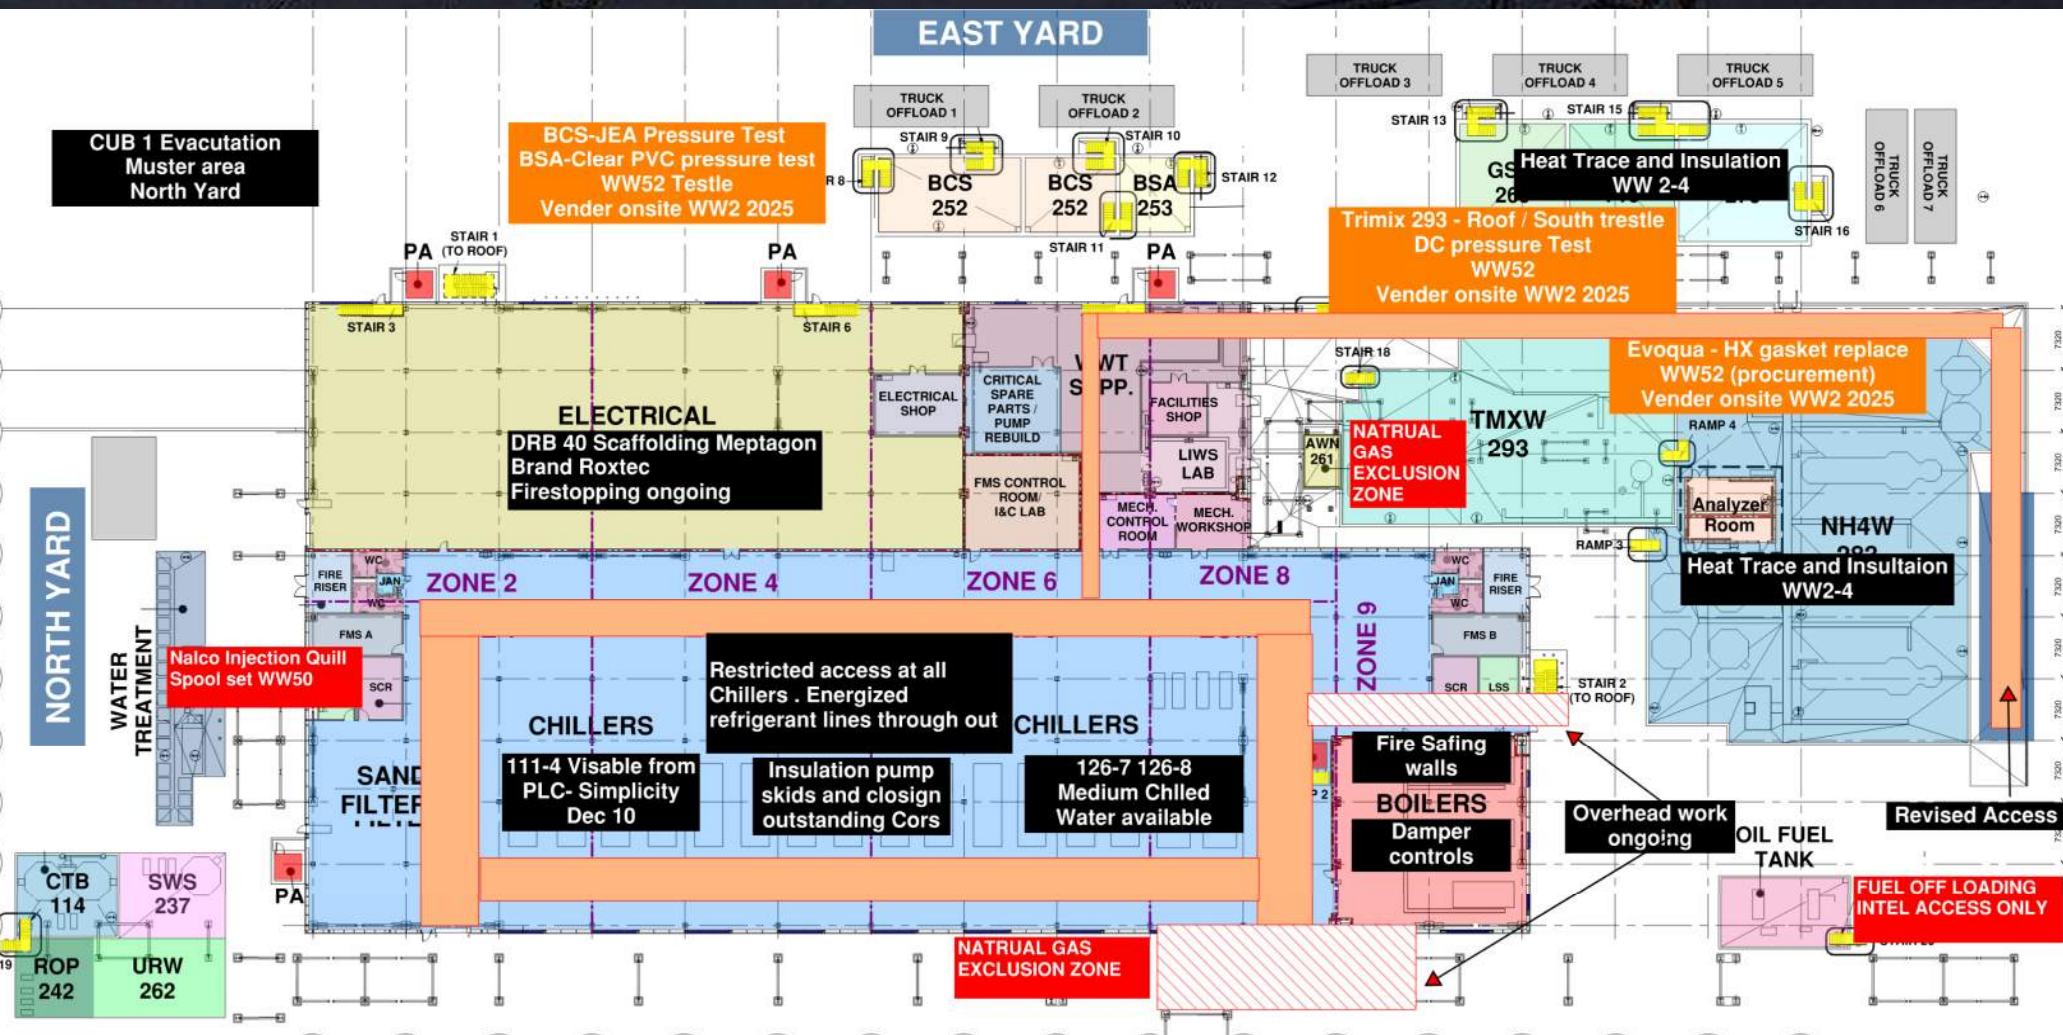

CUB 1 – EXTERIOR/ROOF

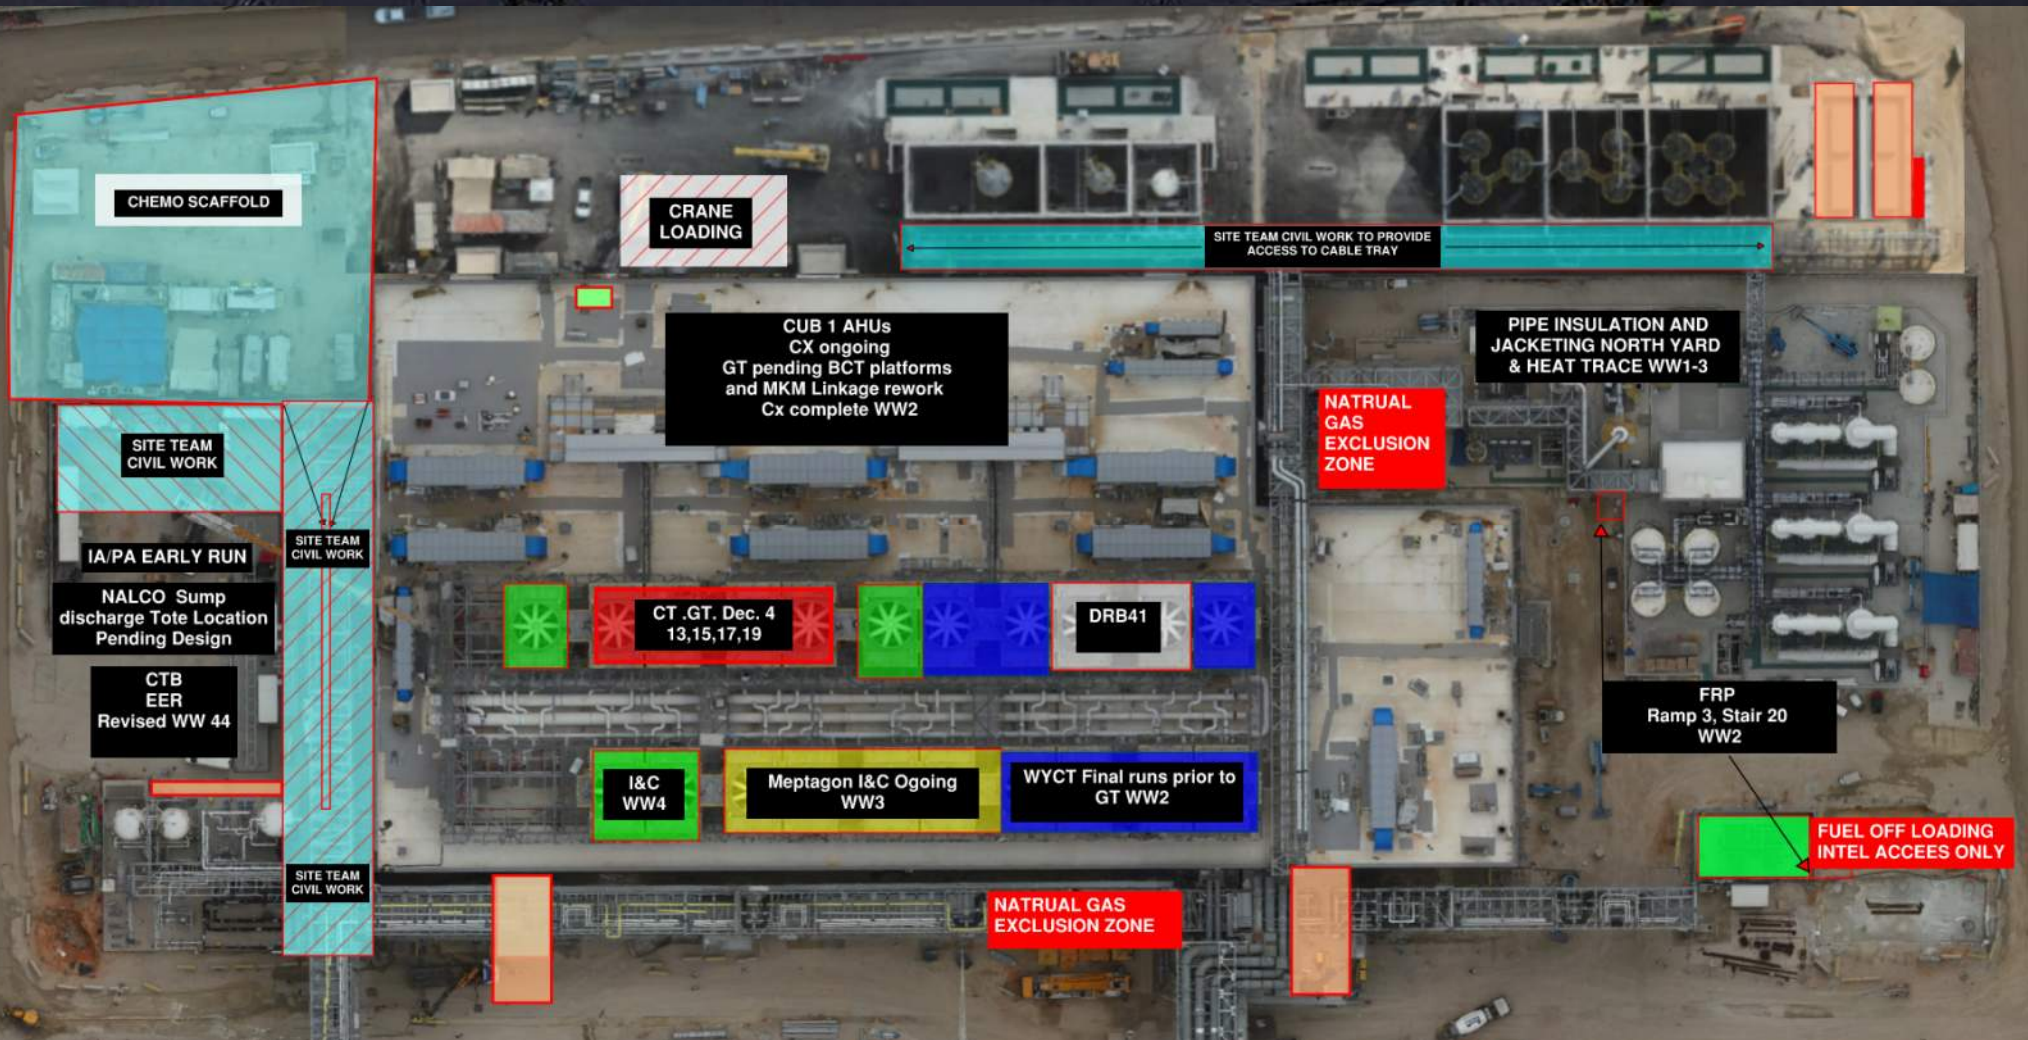

CUB 2- Load in ,H&T, Framing and Sheetrock

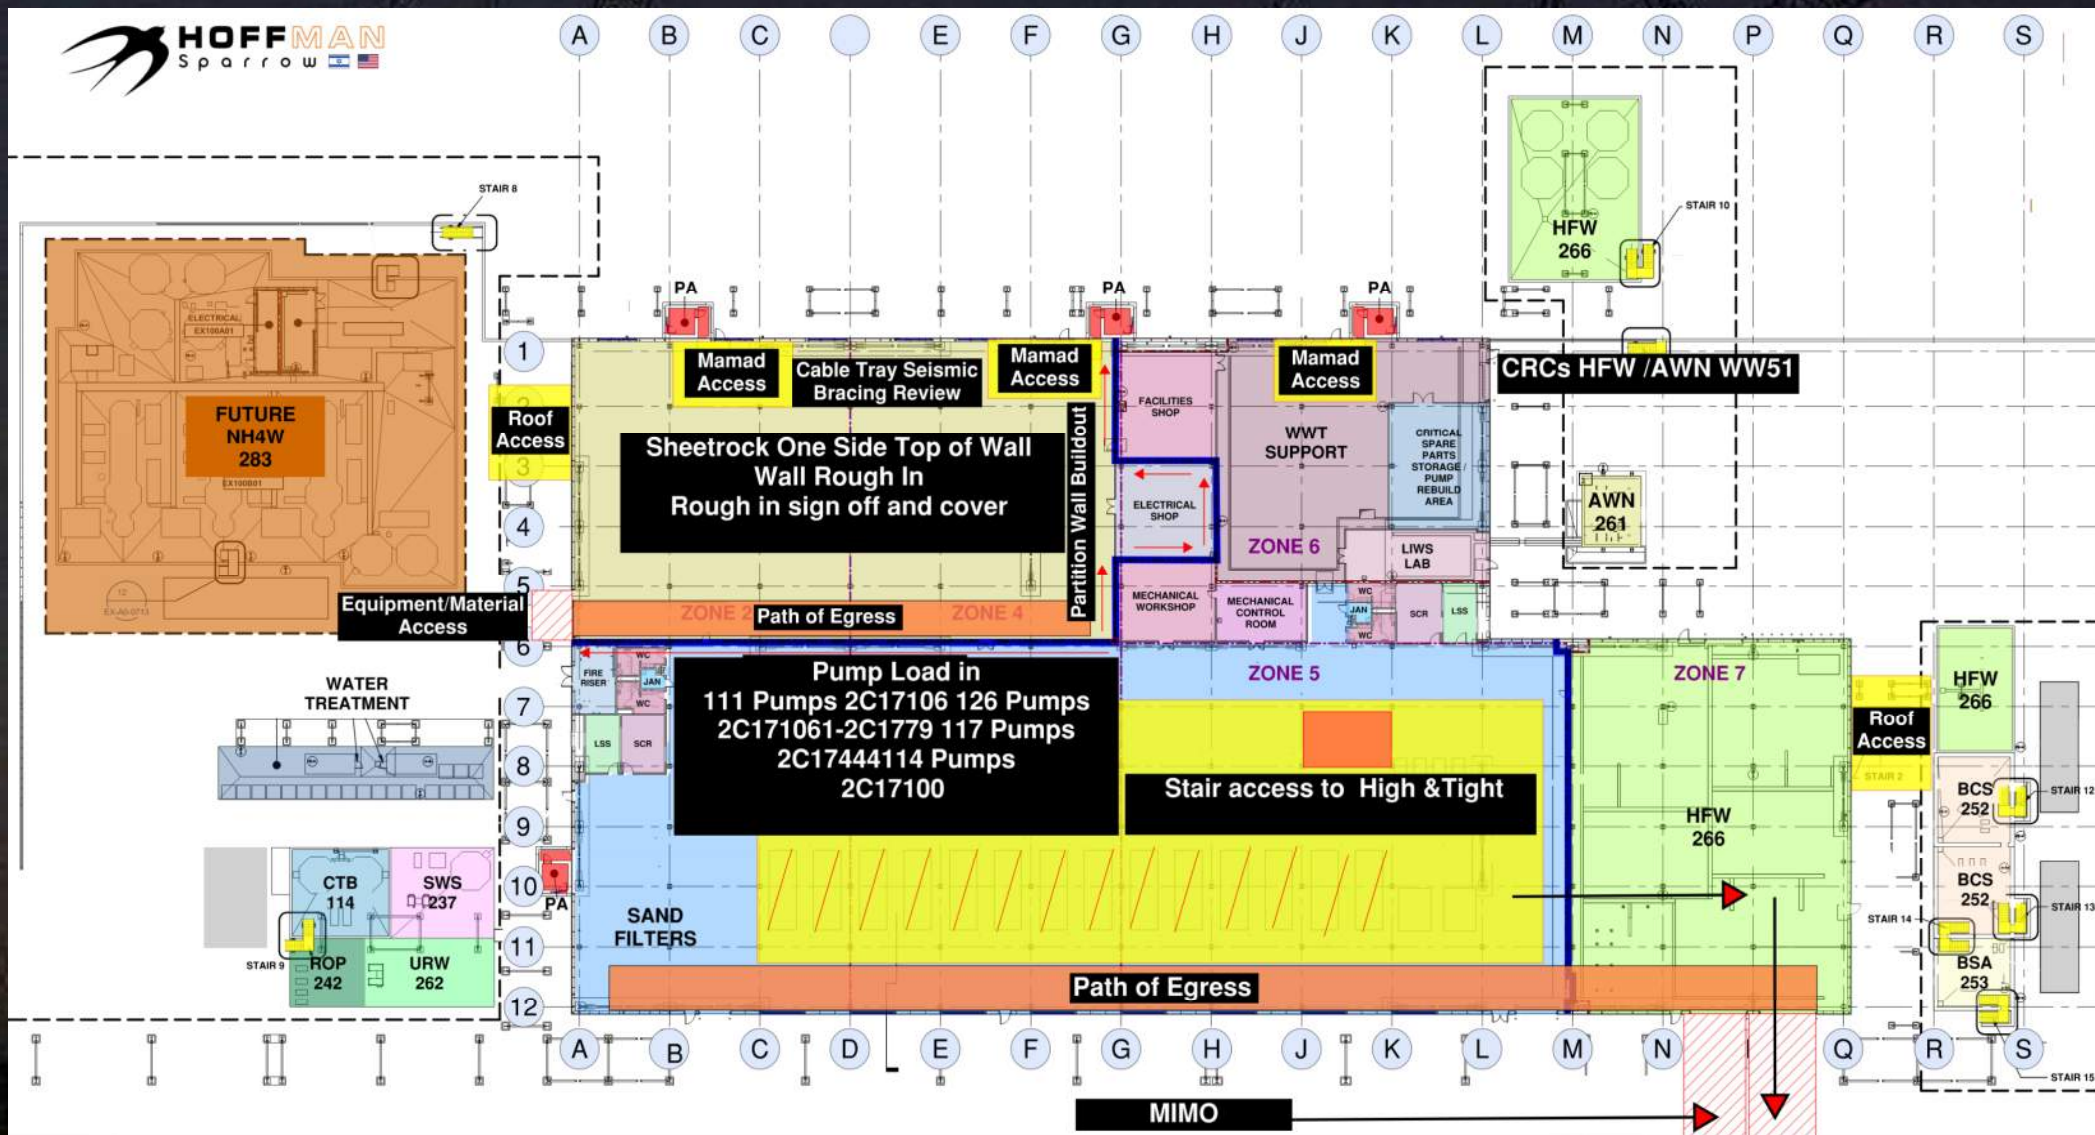


CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

Starting –Monday Jan 6th night at 19:00
Finish Tuesday Jan 7th at 05:00am.

Starting –Tuesday Jan 7th at 19:00
Finish Wednesday Jan 8th at 05:00am

Starting –Wednesday Jan 8th at 19:00
Finish Thursday Jan 9th at 05:00am


BGC - NDT


Safety spotter

No impact on PMB
entrance\Exit

Safety spotter

Safety spotter

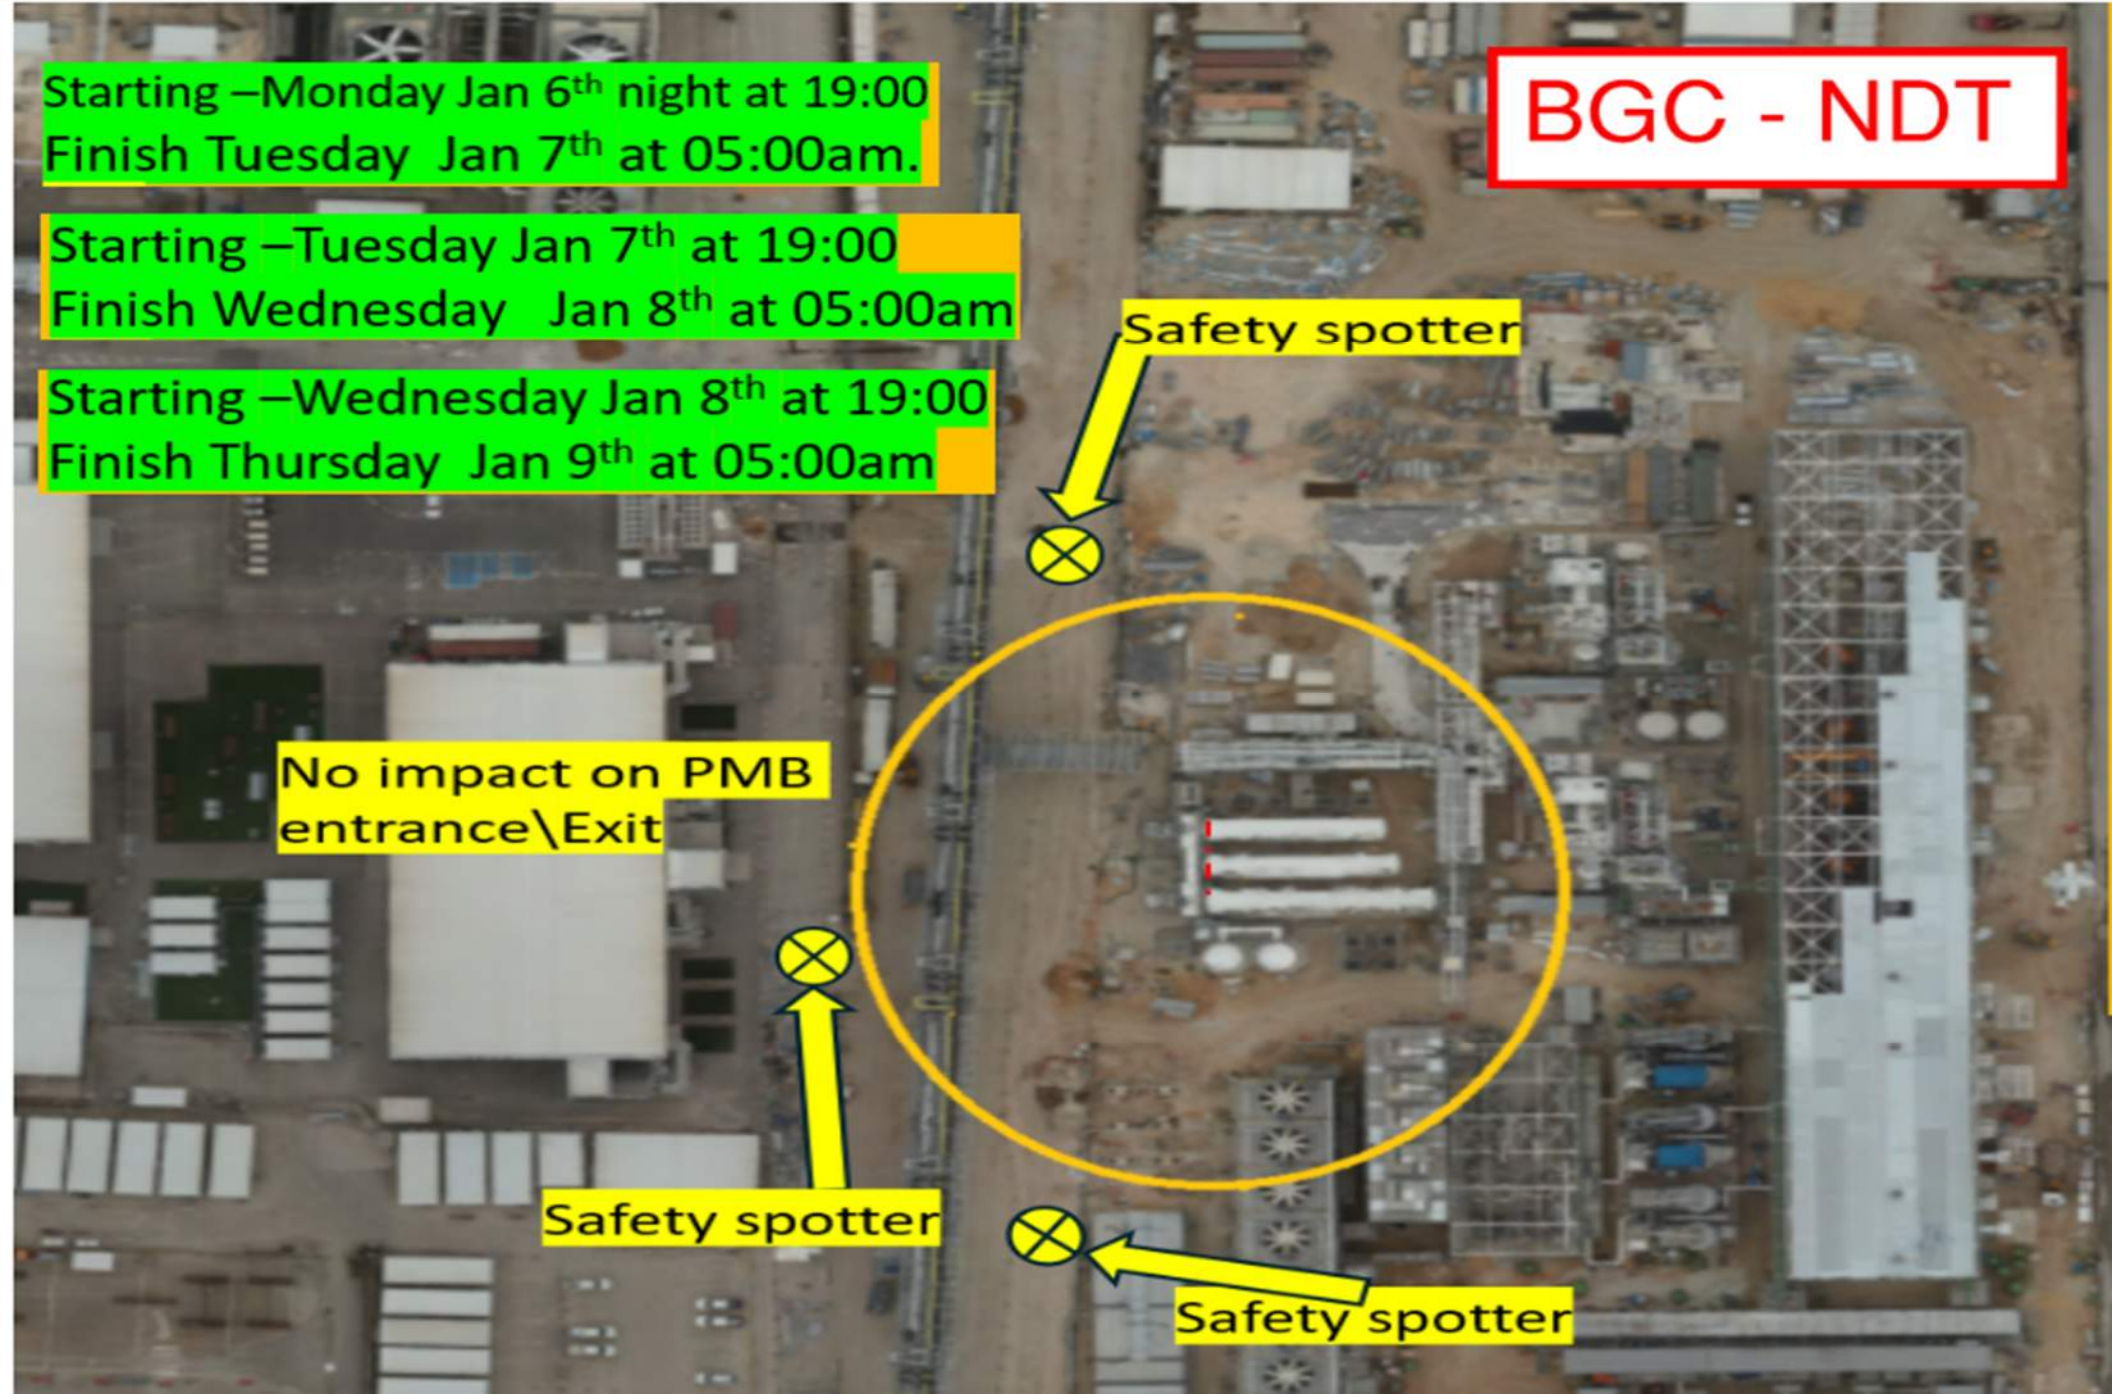

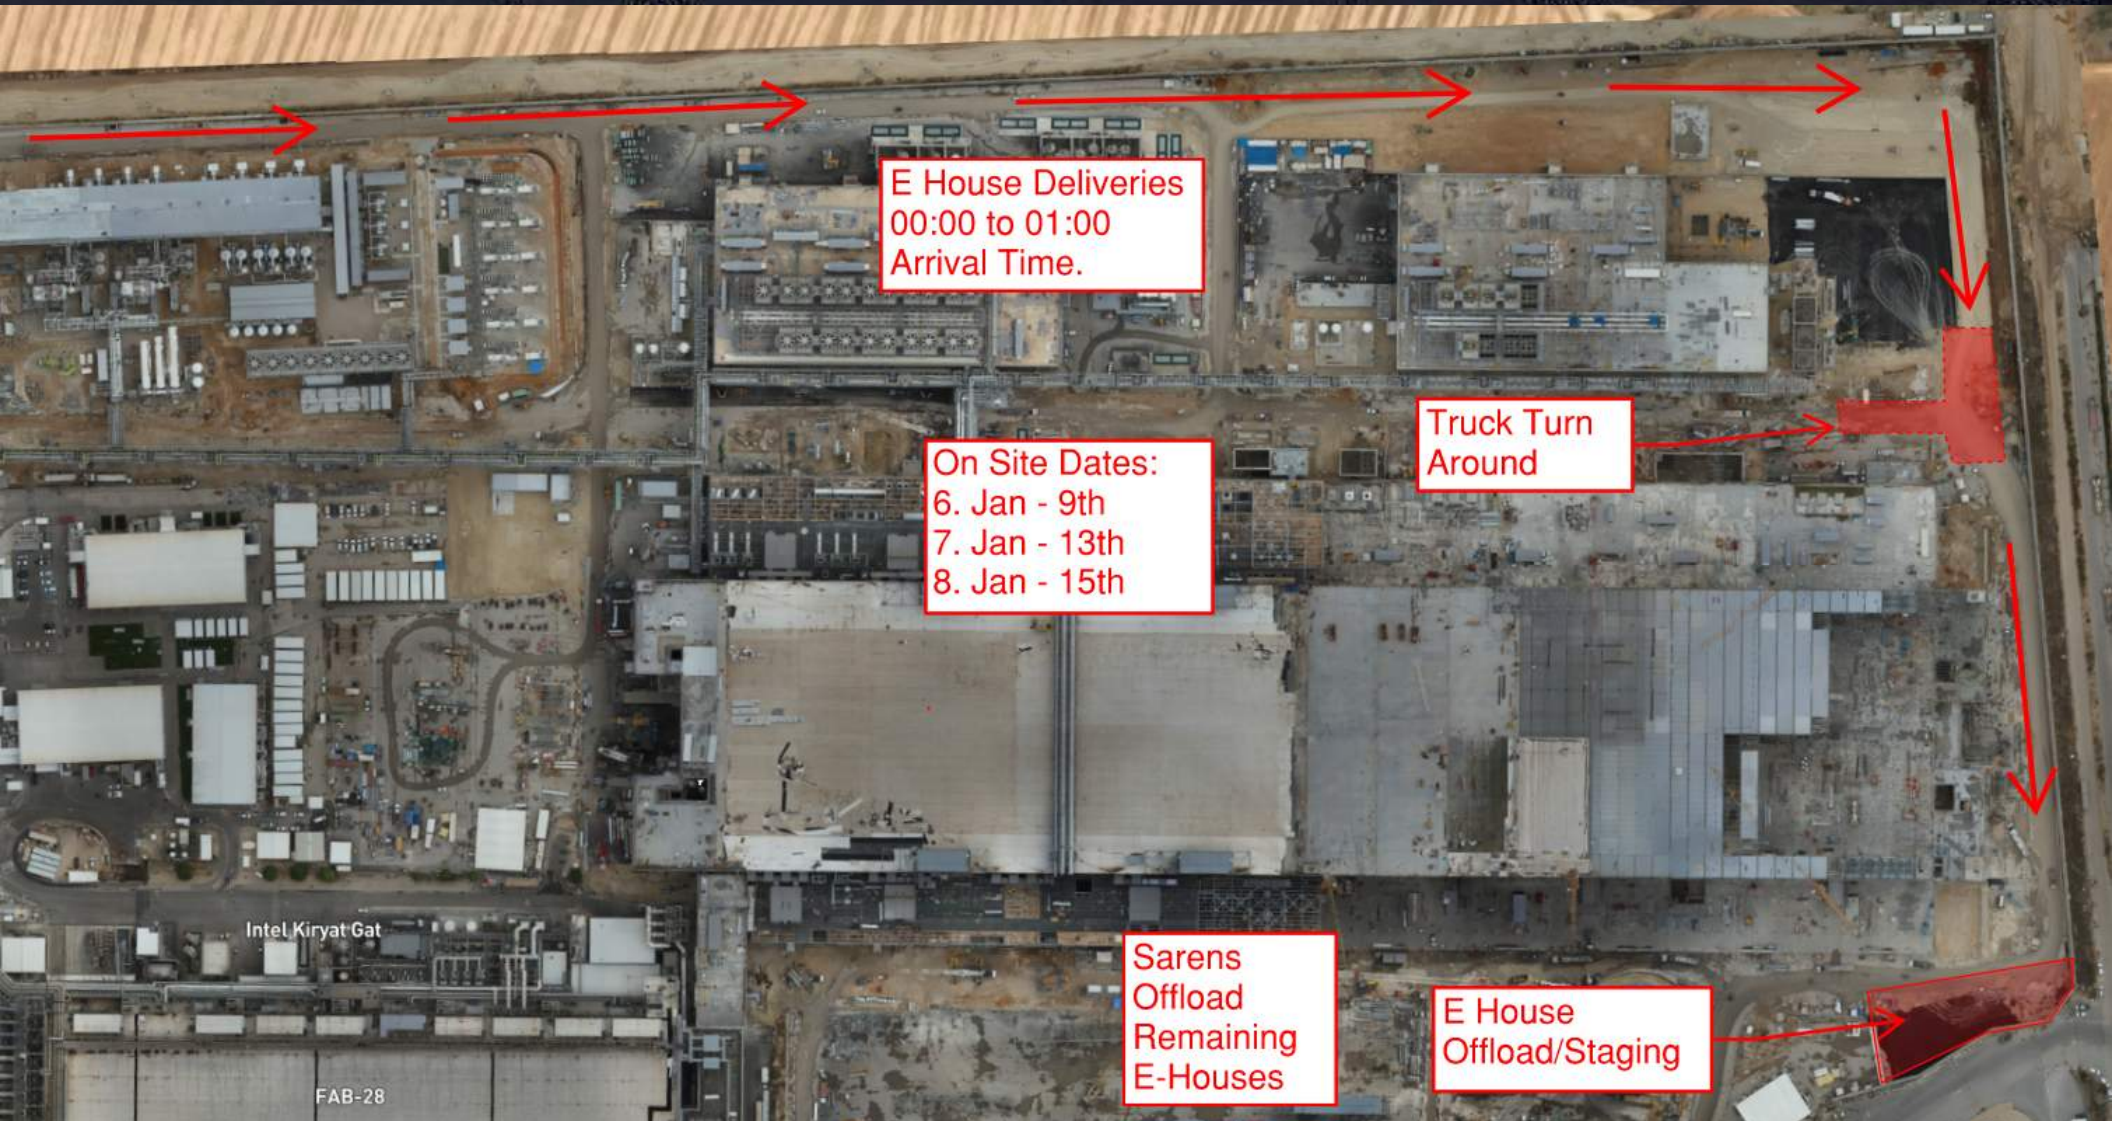

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:
6. Jan - 9th
7. Jan - 13th
8. Jan - 15th


Truck Turn
Around

Sarens
Offload
Remaining
E-Houses

E House
Offload/Staging

Intel Kiryat Gat

FAB-28

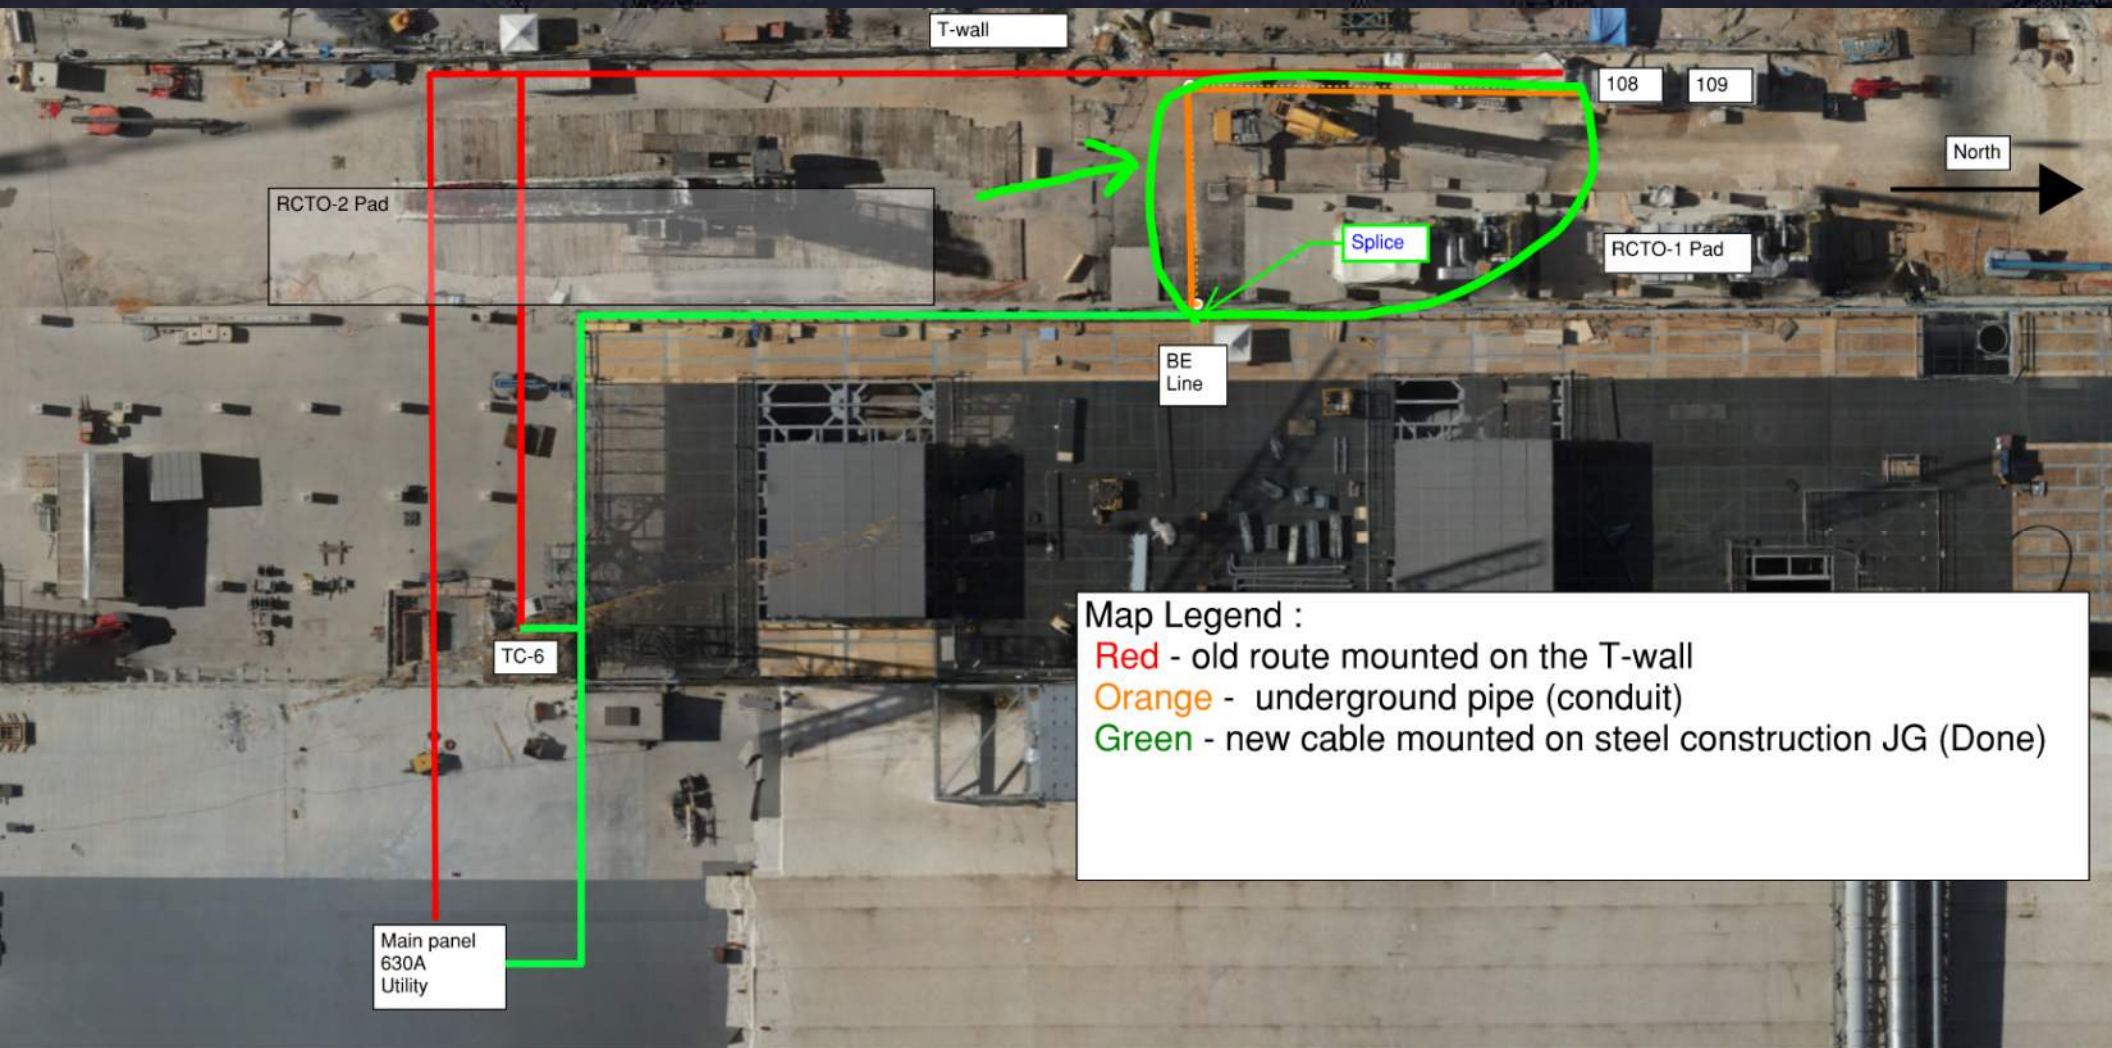

Map Legend :

- Red - old route mounted on the T-wall
- Orange - underground pipe (conduit)
- Green - new cable mounted on steel construction JG (Done)



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

600 Car Park

Boring





Daily Coordination Meeting

Site Logistics North





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
South



Basic Scaffold Safety

- 
- Scaffold built on the project need to be submitted to the HCC Foremen via the Scaffold request form before they are erected.
 - Scaffolds must be inspected before they are opened by HCC foremen, and weekly.
 - Daily inspections required by the contractor using them.
 - All personnel using scaffold must have WAH training AND Safe Scaffold Use training.
 - Do not modify scaffolds for any reason. If scaffolds must be modified the proposed changes need to be submitted and approved by HCC foremen.

JANUARY 13TH
10:30 - 12:00



KADIMA
BUM

PLEASE SIGN UP HERE TO
RECEIVE THE CALENDAR INVITE

HCC/EHS Weekend Work- 03.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Shelby Standefer 052-3440752

Yakov Malka 052-3459250

Yakov Alon 052-4671271

CSA CM

Charlie Aitken 052-6041443

Ilyssa Ingenthron 052-5732553

MEP

David Chavez 052-2756390

Denis Ryan 052-2962447

Pauric O'Reilly 052-3571665

Lara Salaymeh 052-2410953

Abhilash Parameswaran 052-6938827

Cranes

Craig Mowry 052-300-2769

Safety

Safety Foreman- Mohammad Zakakti- 054-8121212 Mohammad-Zakakti@Hoffmancorp.com

Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com

Safety Professional- Nassim Yones- [052-2208434](tel:052-2208434) Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 03.01.2025

FAB

Utility Level / Roof / Stair Shaft

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Megason

Subfab

Pach Taas

BAe Wall Penetration

Itamar 0509301917

Afcon E

MARSes, E LSS Rooms

Avi Eli: 0526008487

Chemo

TTNW

Tomi: 0523759408

SELA

AY-BC 15-19

Avihen 0548155302

MEGASON

LSS Rooms

Israel 0526869393

Clean Room

Talad – CR 2 E – UPN Install, 4E Grating (EHS Marcelo 0523540242, Super Igor 0544509386)

Sig – 10 GUYS 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)

Afcon – CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)

Chemo –30 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)

Megason - 16 GUYS INT LEVEL + 7 GUYS ON UTILITY LEVEL FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT

Sela – 2E CRC (Supervisor yoav 0548076339 , EHS SERGEY 0526650046)

Protocol - aa+ak lines.

Talent solution 1w_+ 1e + interstitial.

Subcontractor Weekend Work- 03.01.2025

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2 1-3P

Foreman – Itamar – 050-9301917

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2

Foreman – Pradeep - 055-2742935

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-5P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcelo – 054-5210133

Safety – Majdi – 054-6192581

WJG

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 4J/5J Lift 2 Piping & Link Roof

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

Pach Taas: All over

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

Subcontractor Weekend Work- 03.01.2025

CUB

S.K.E - CUB 1:

Renato - 0548991623

Marzuk - 0548830263

Chemo Aharon - CUB 1:

Dudu - 0509808846

Leonid - 0548883878

D&P - CUB 2:

Constantino - 0545501602

David - 0548894447

Sami Najami - CUB 1 test + CUB 2:

Husein - 0526917461

Faiz - 0502227962

Alon - 0509895008

HSAI:

Sergey - 0552728807

Trestle

Siding

Sami Najami

Forman- Abed Kilani 054-5501880

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Elmor – Site Lighting Underground

Supervision = Shlomi: 050-9182260

EHS = Daniel: 052-2584171

Olizki – Offload 18 & CUB1 trench drains, South GUT road excavation

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
