

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:

- Winds this afternoon & tomorrow - secure material
- Weekend work

UTILITY LEVEL MOD1

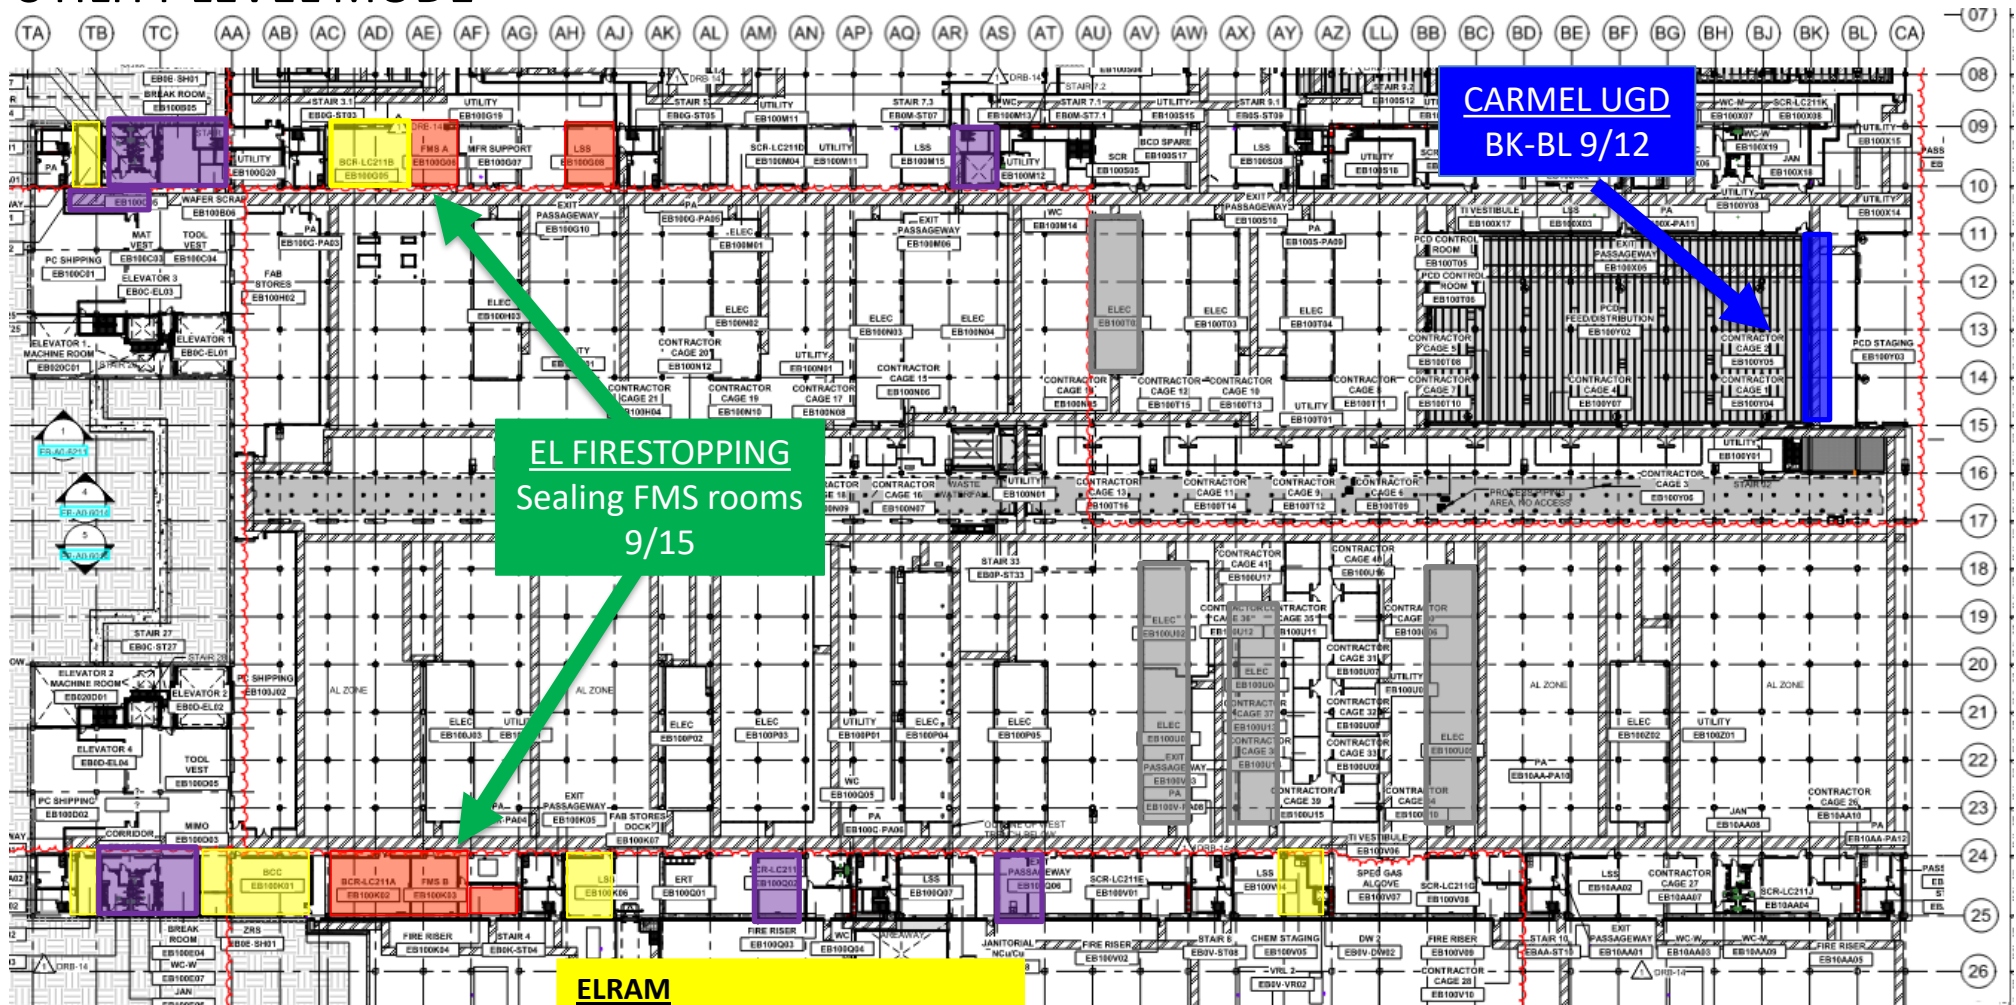

BELFOR
 TTNE - Corridor + Toilets + Break R
 Stairs 7.3
 Wafer scrap
 TTNW - Toilets + Break R
 SCR 2W
 Exit pass 3W

ELRAM
 Ongoing
 LSS TTNW + TTNE
 BCR 1E
 CHEN STAGING
 LSS 2W
 Chem staging
 BACKING
 BCR 1E+1W – Pending funding
 LSS's

MEP+Elctrical
 Ready for re-install
 FMS A 1E
 FMS B 1W
 Fire Risers 1W
 BCC



MEPTAGON

10W
9/17


MALHIMIM

9/17

Sprinklers install
9/17




SUT 38.1 LEVEL

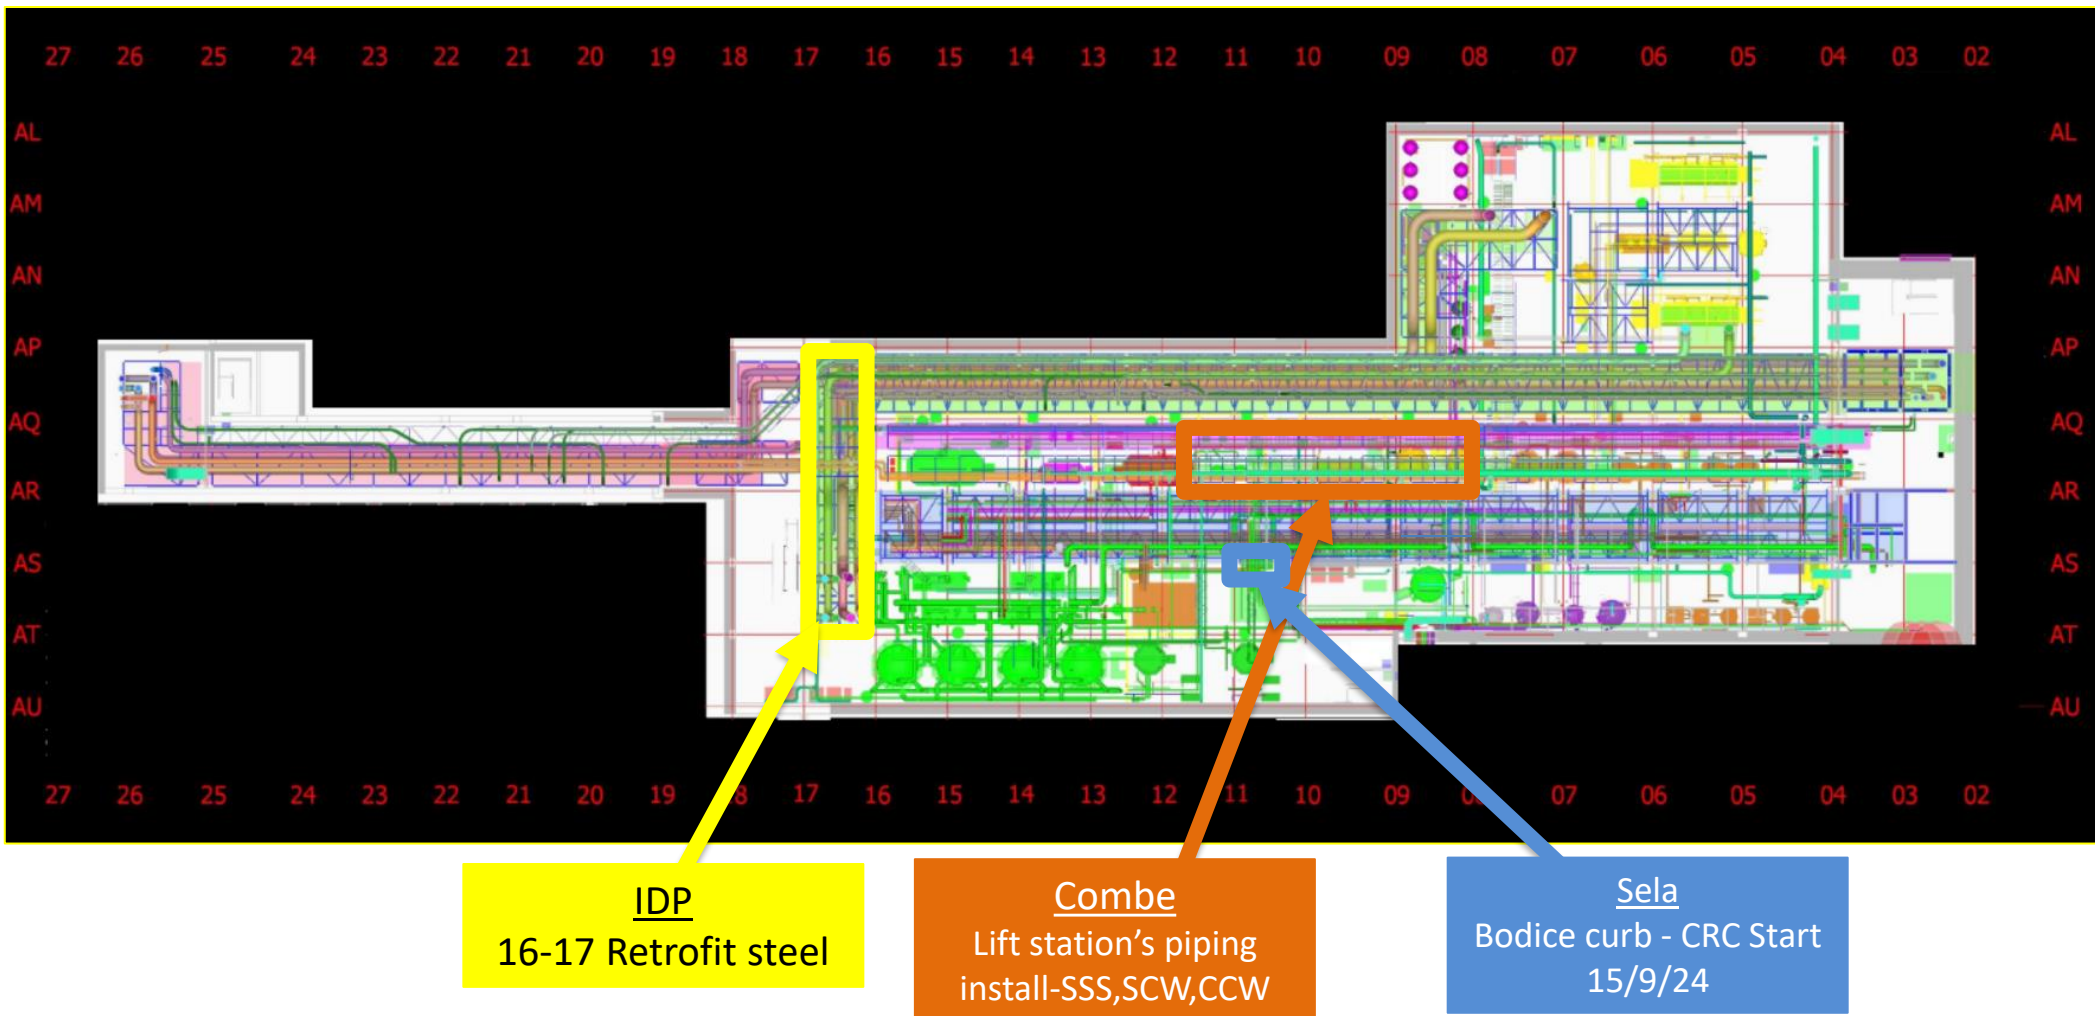





SUT 38.2 LEVEL

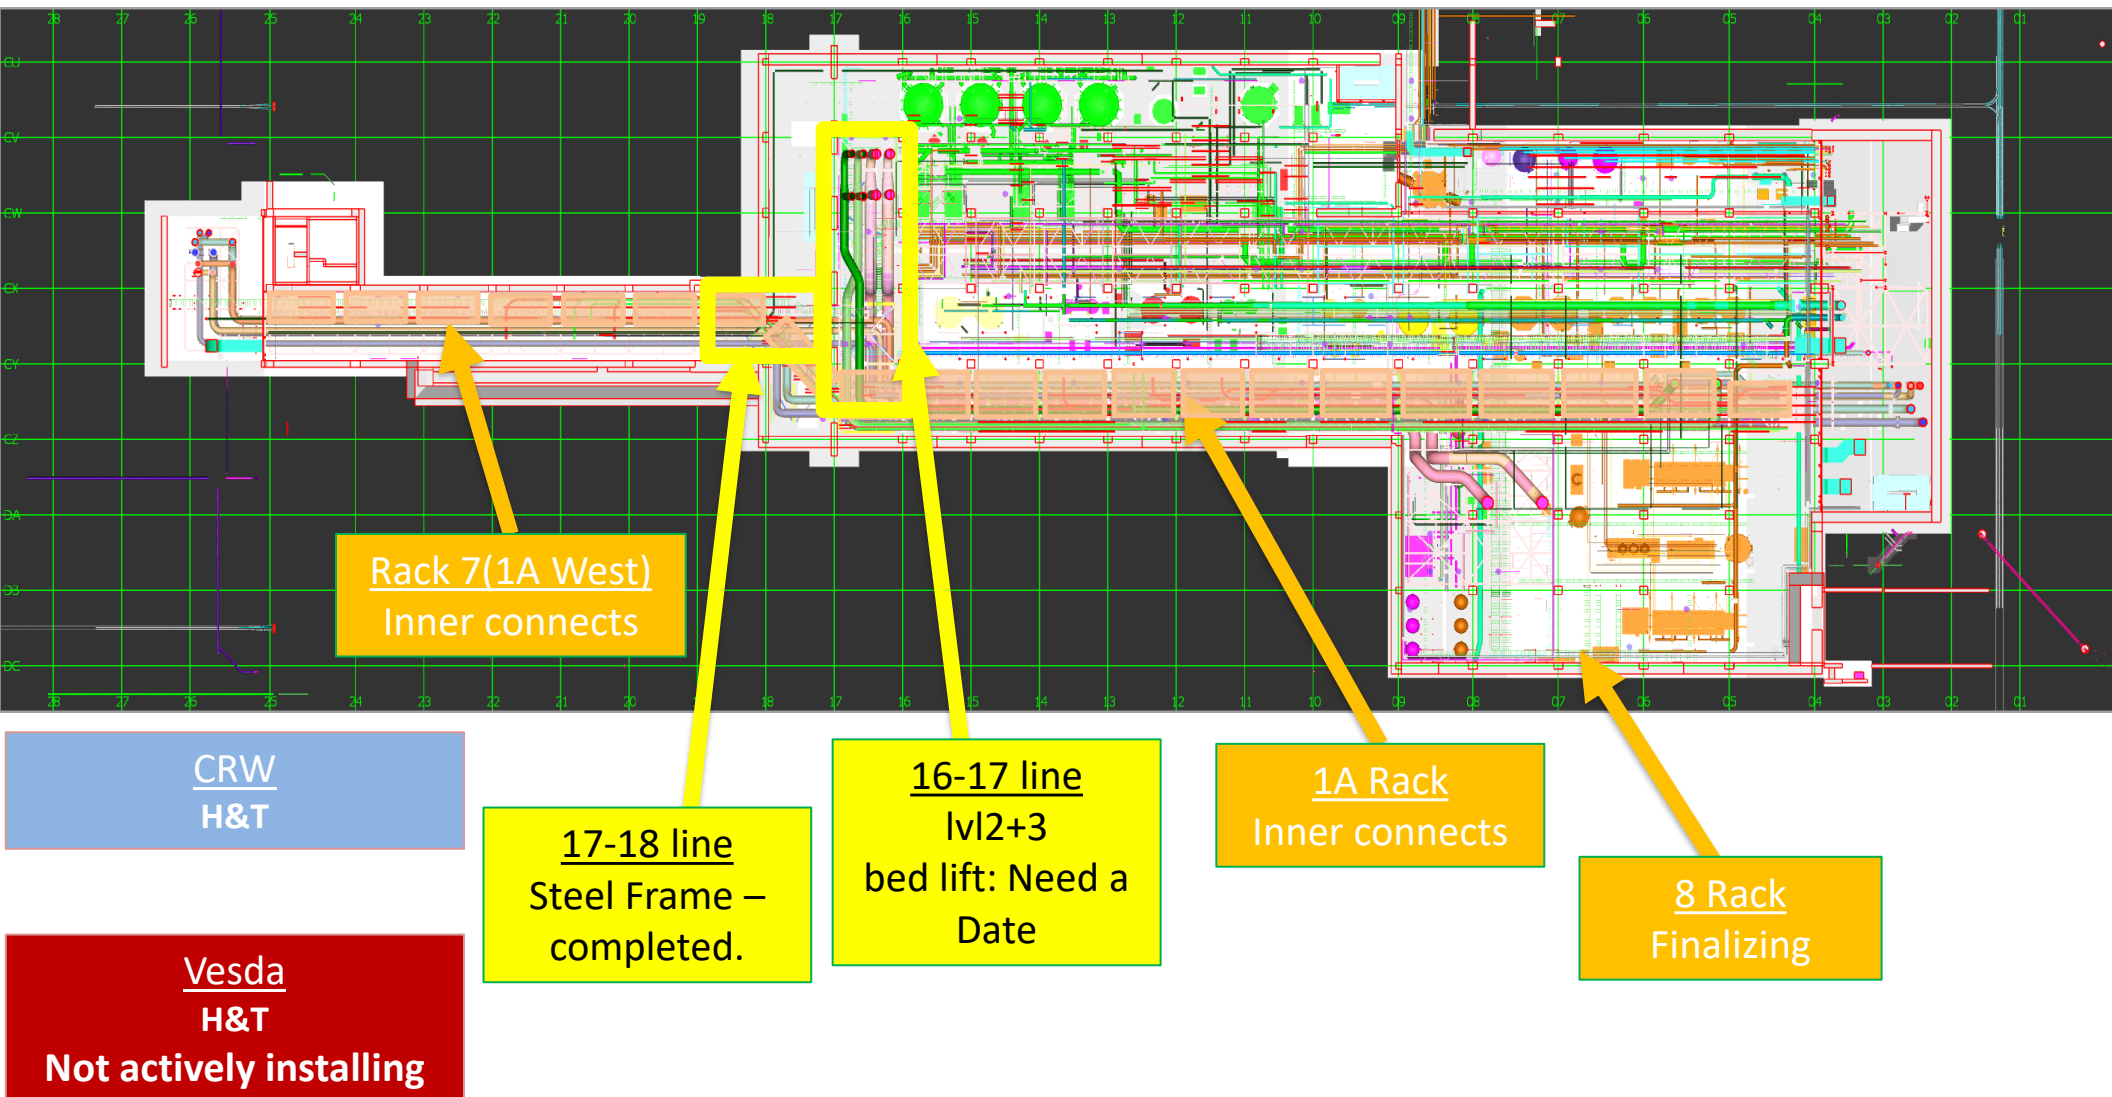


SUBFAB BUILDOUT MOD 1

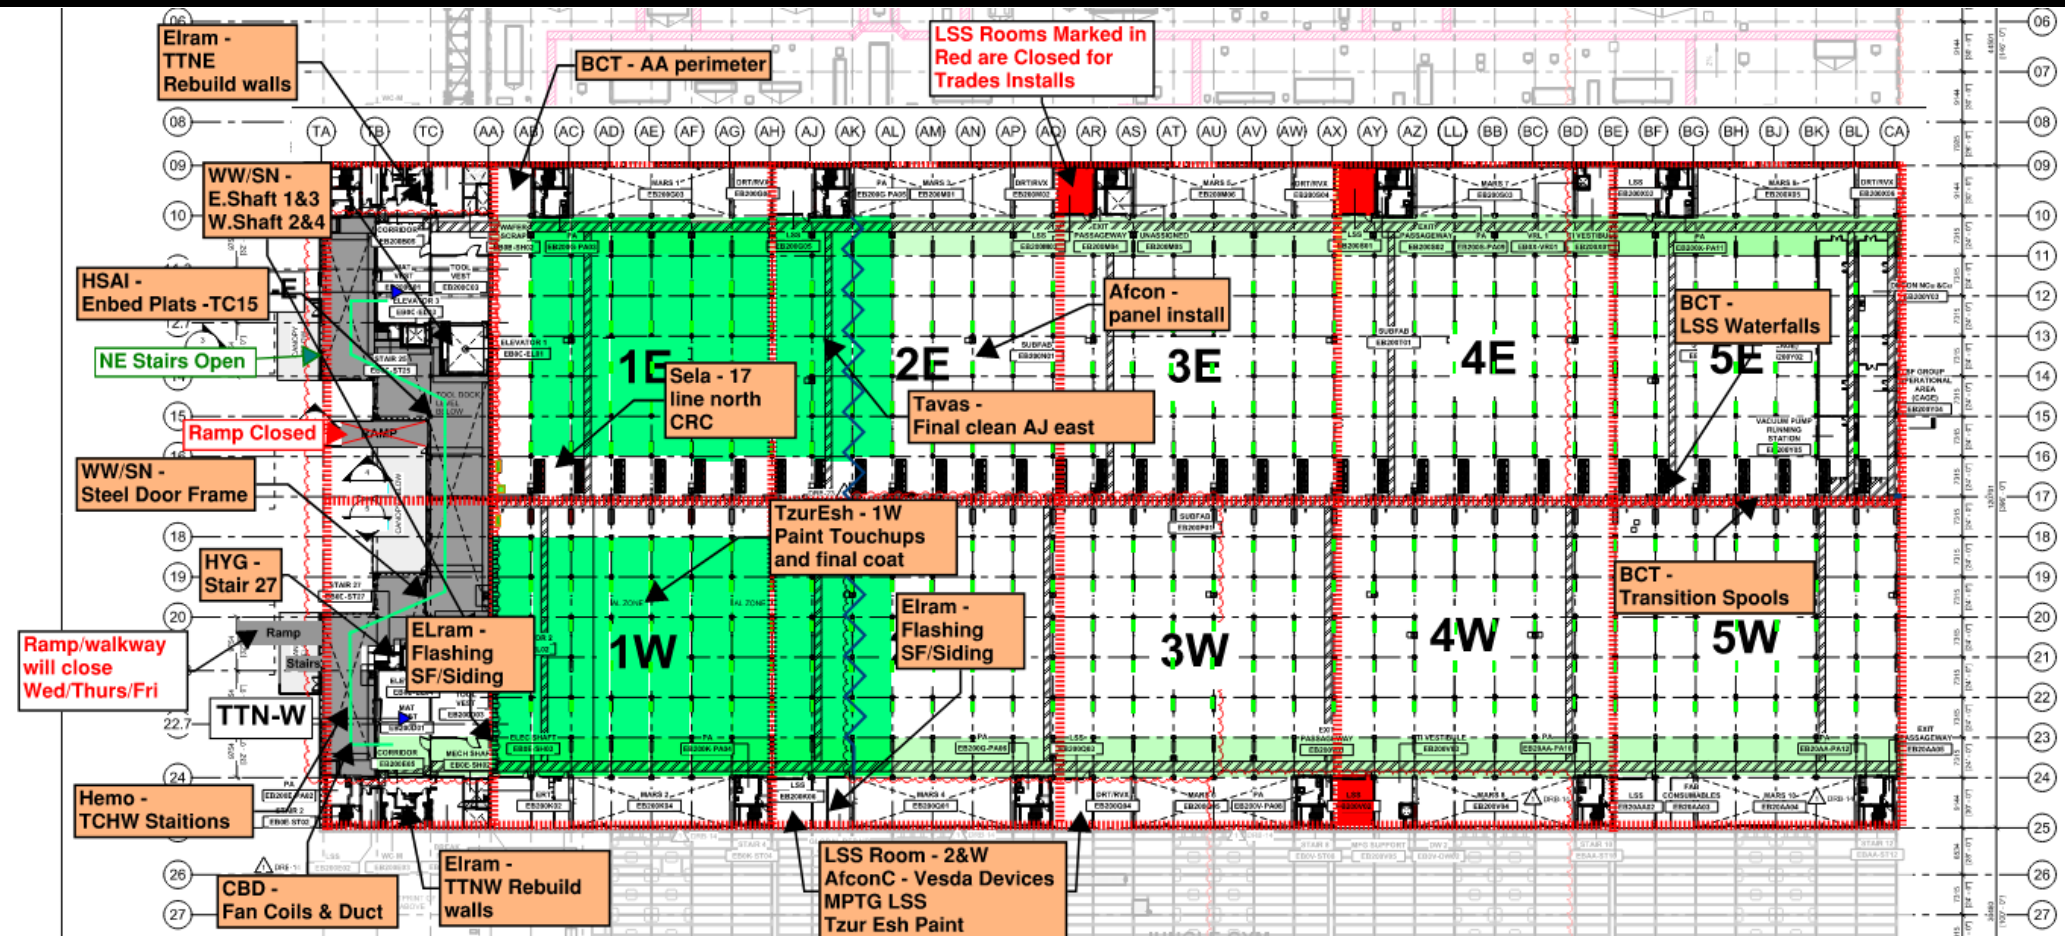


SUBFAB CRC TOPCOAT


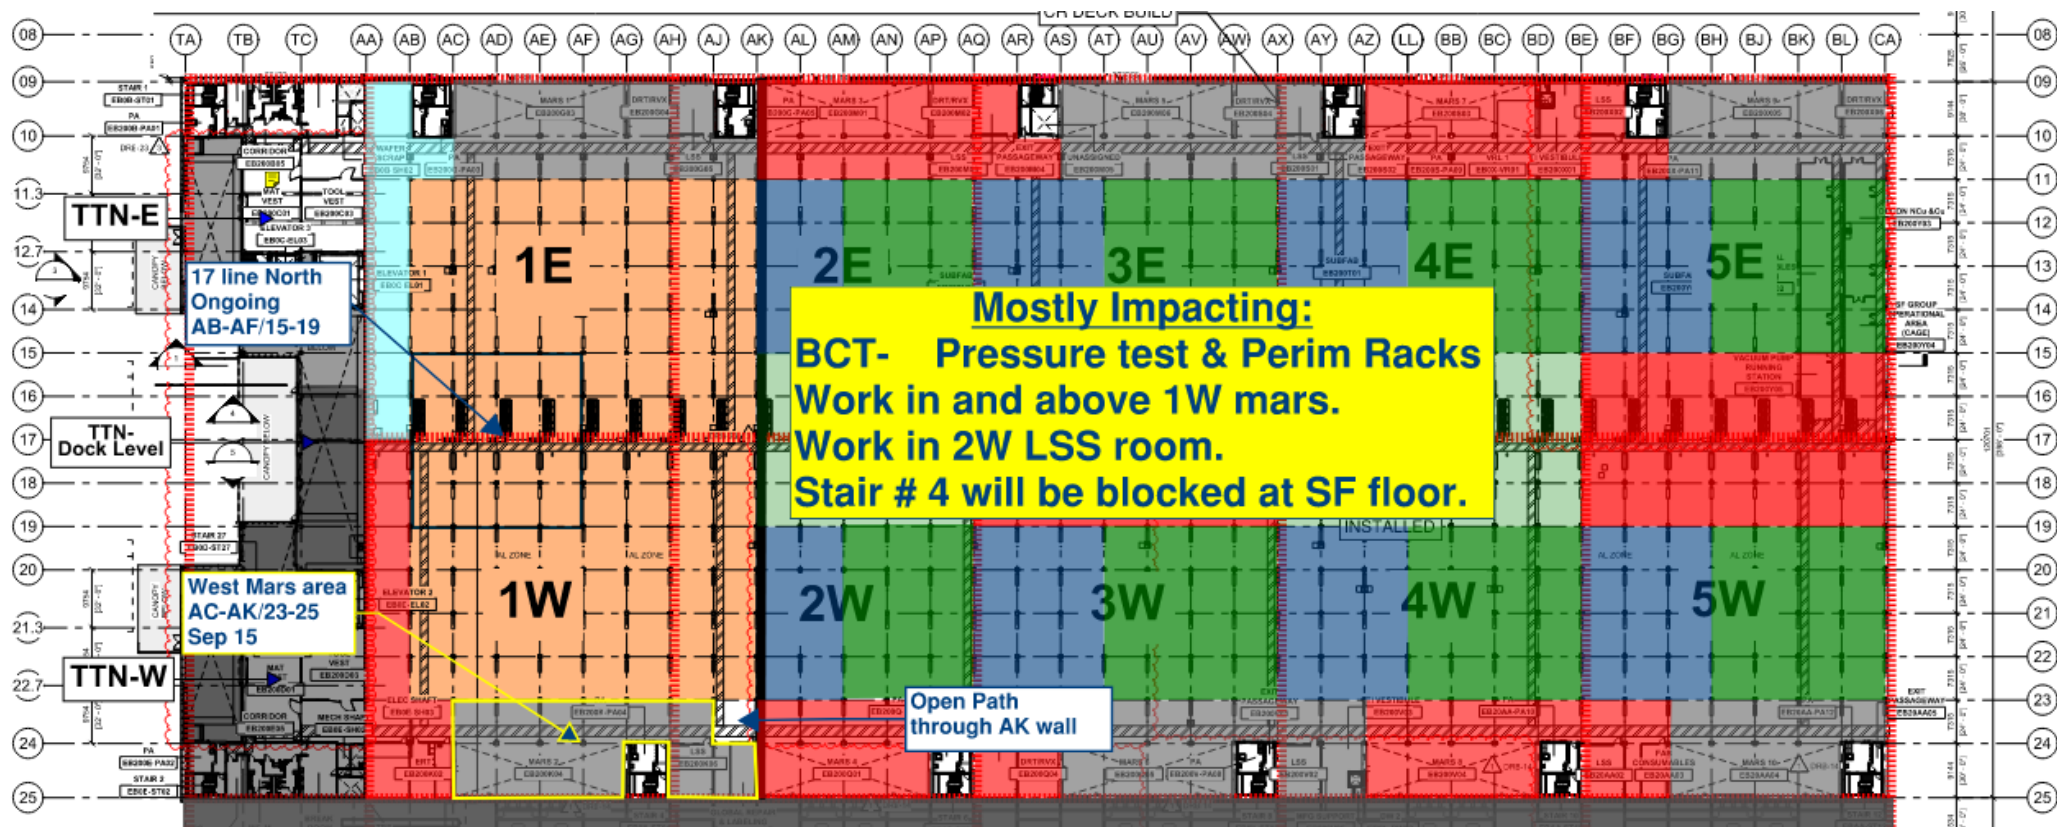


SUBFUB PRESSURE TEST EXCLUSION ZONES

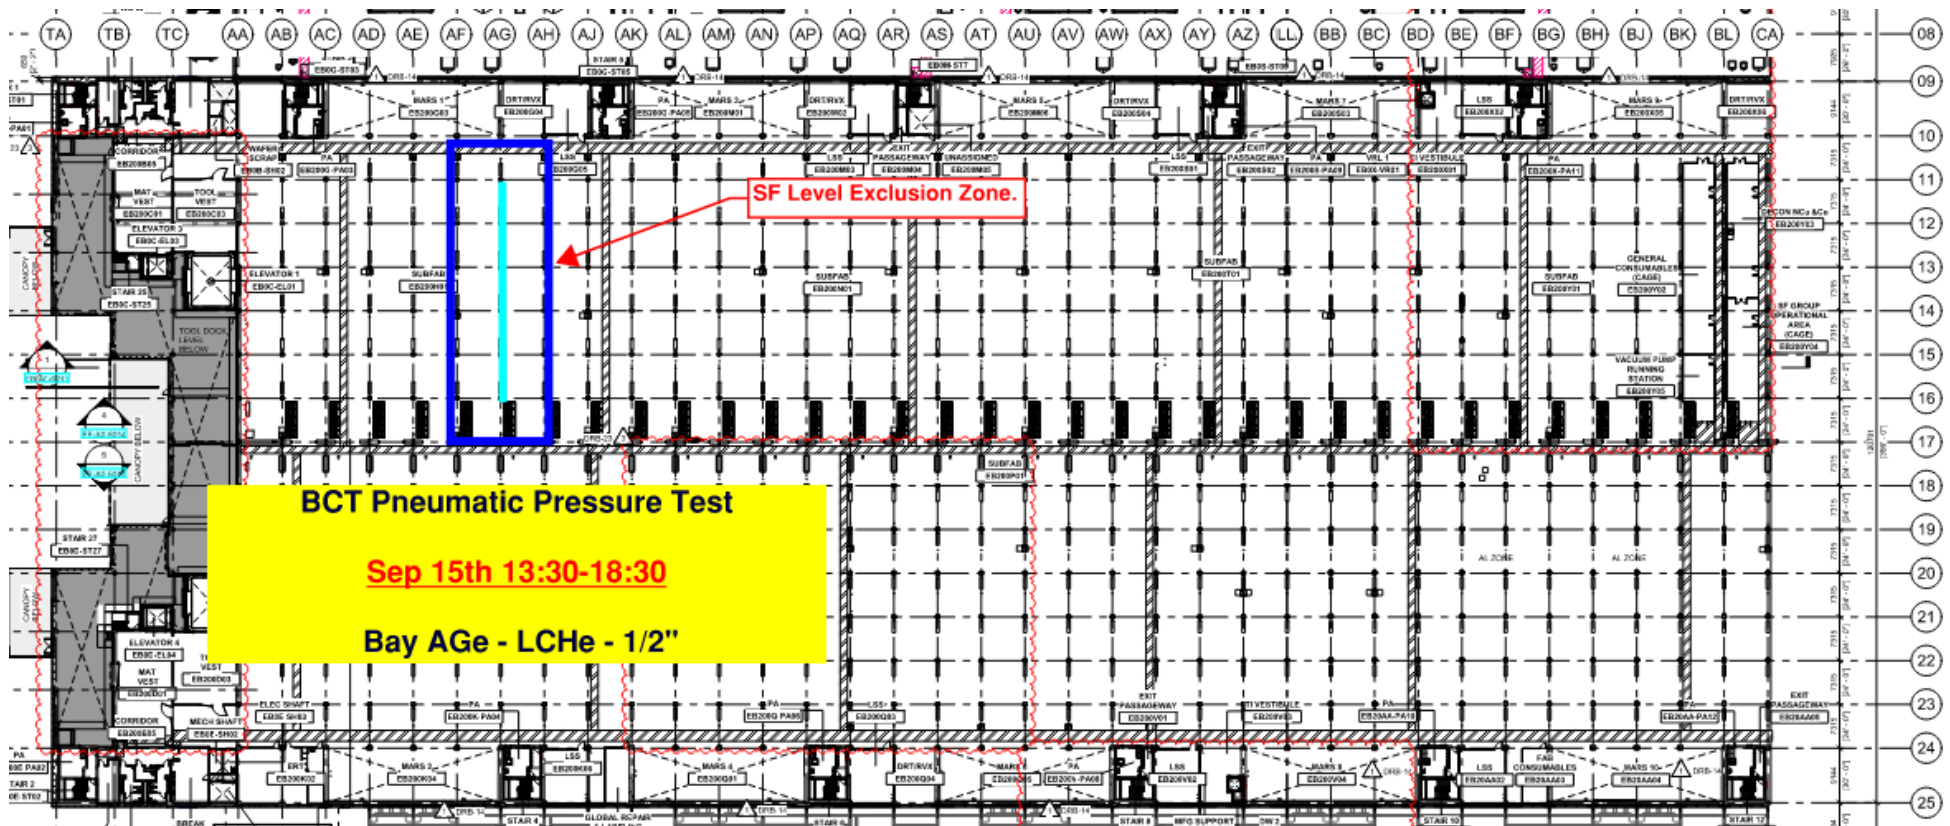

[illegible]

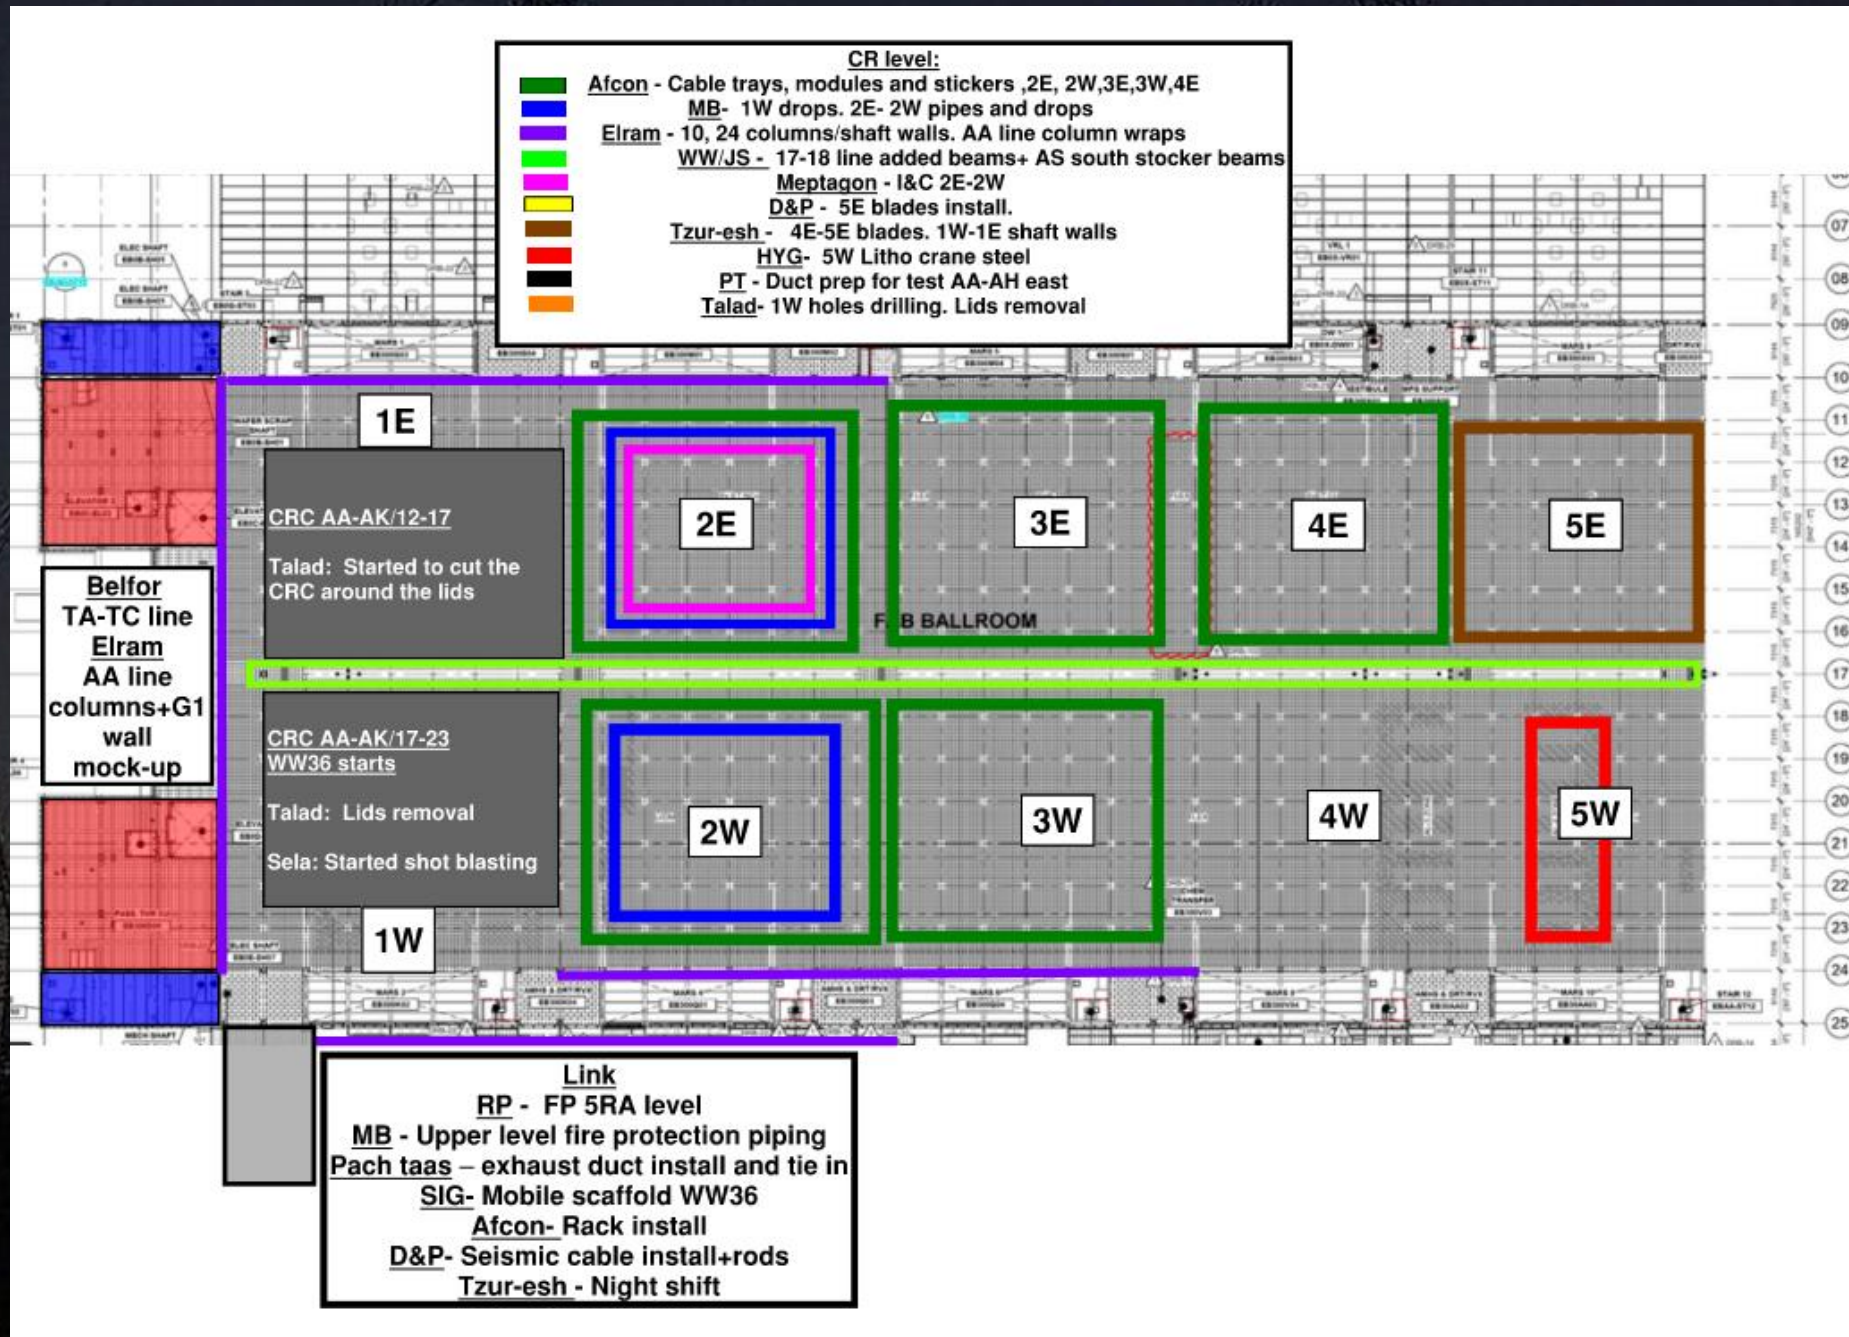

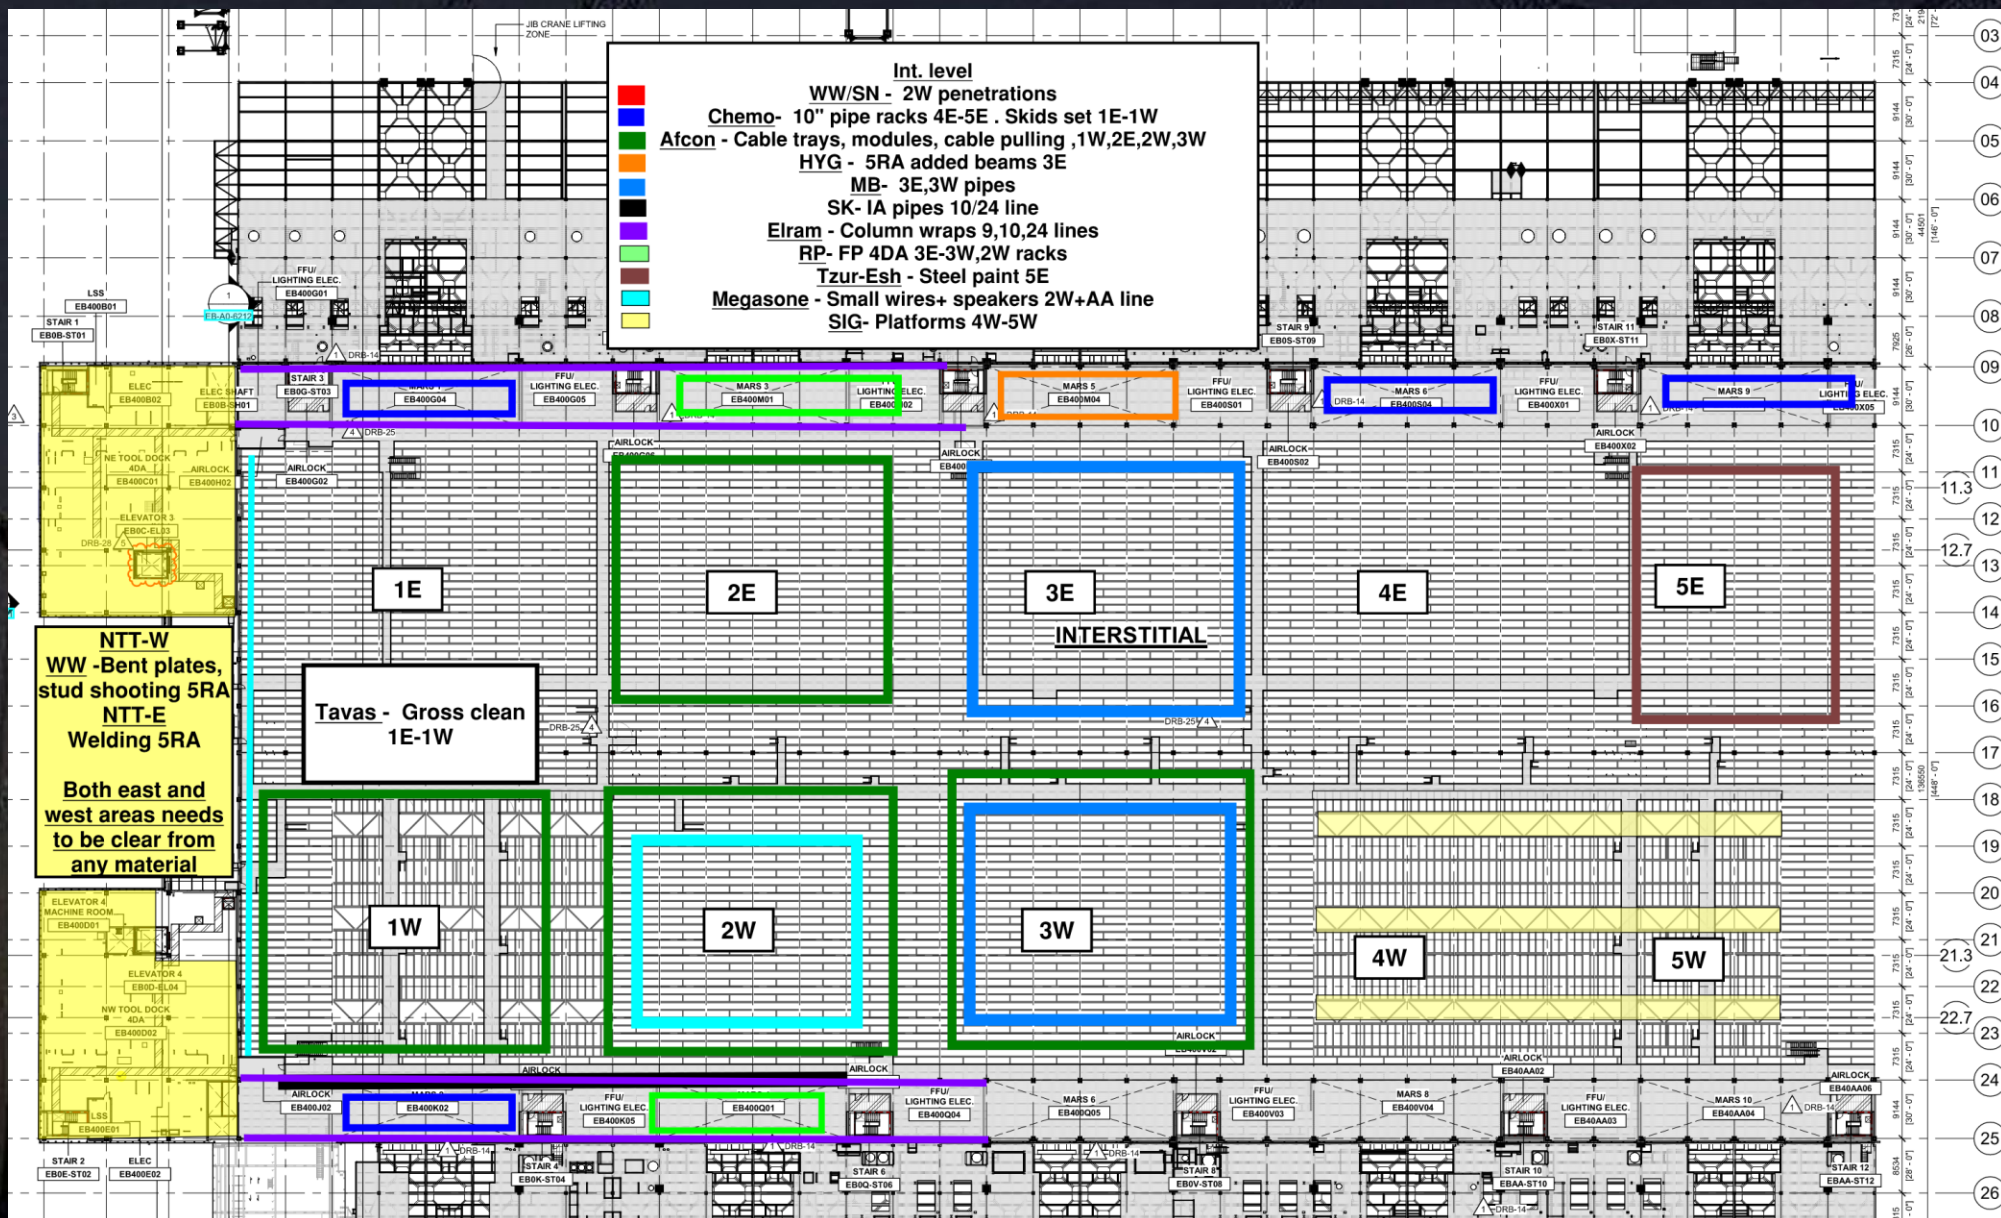



HOFFMAN CONSTRUCTION COMPANY



Truss Yard:
RP and Tzur-Esh to start FP and paint trusses on night shift


Infill ongoing


Tzur-esh
MOD2 paint


MIMO 4DA level CB-CC
SIG ongoing


SEQ 270-271 Ongoing

SEQ 281 ongoing

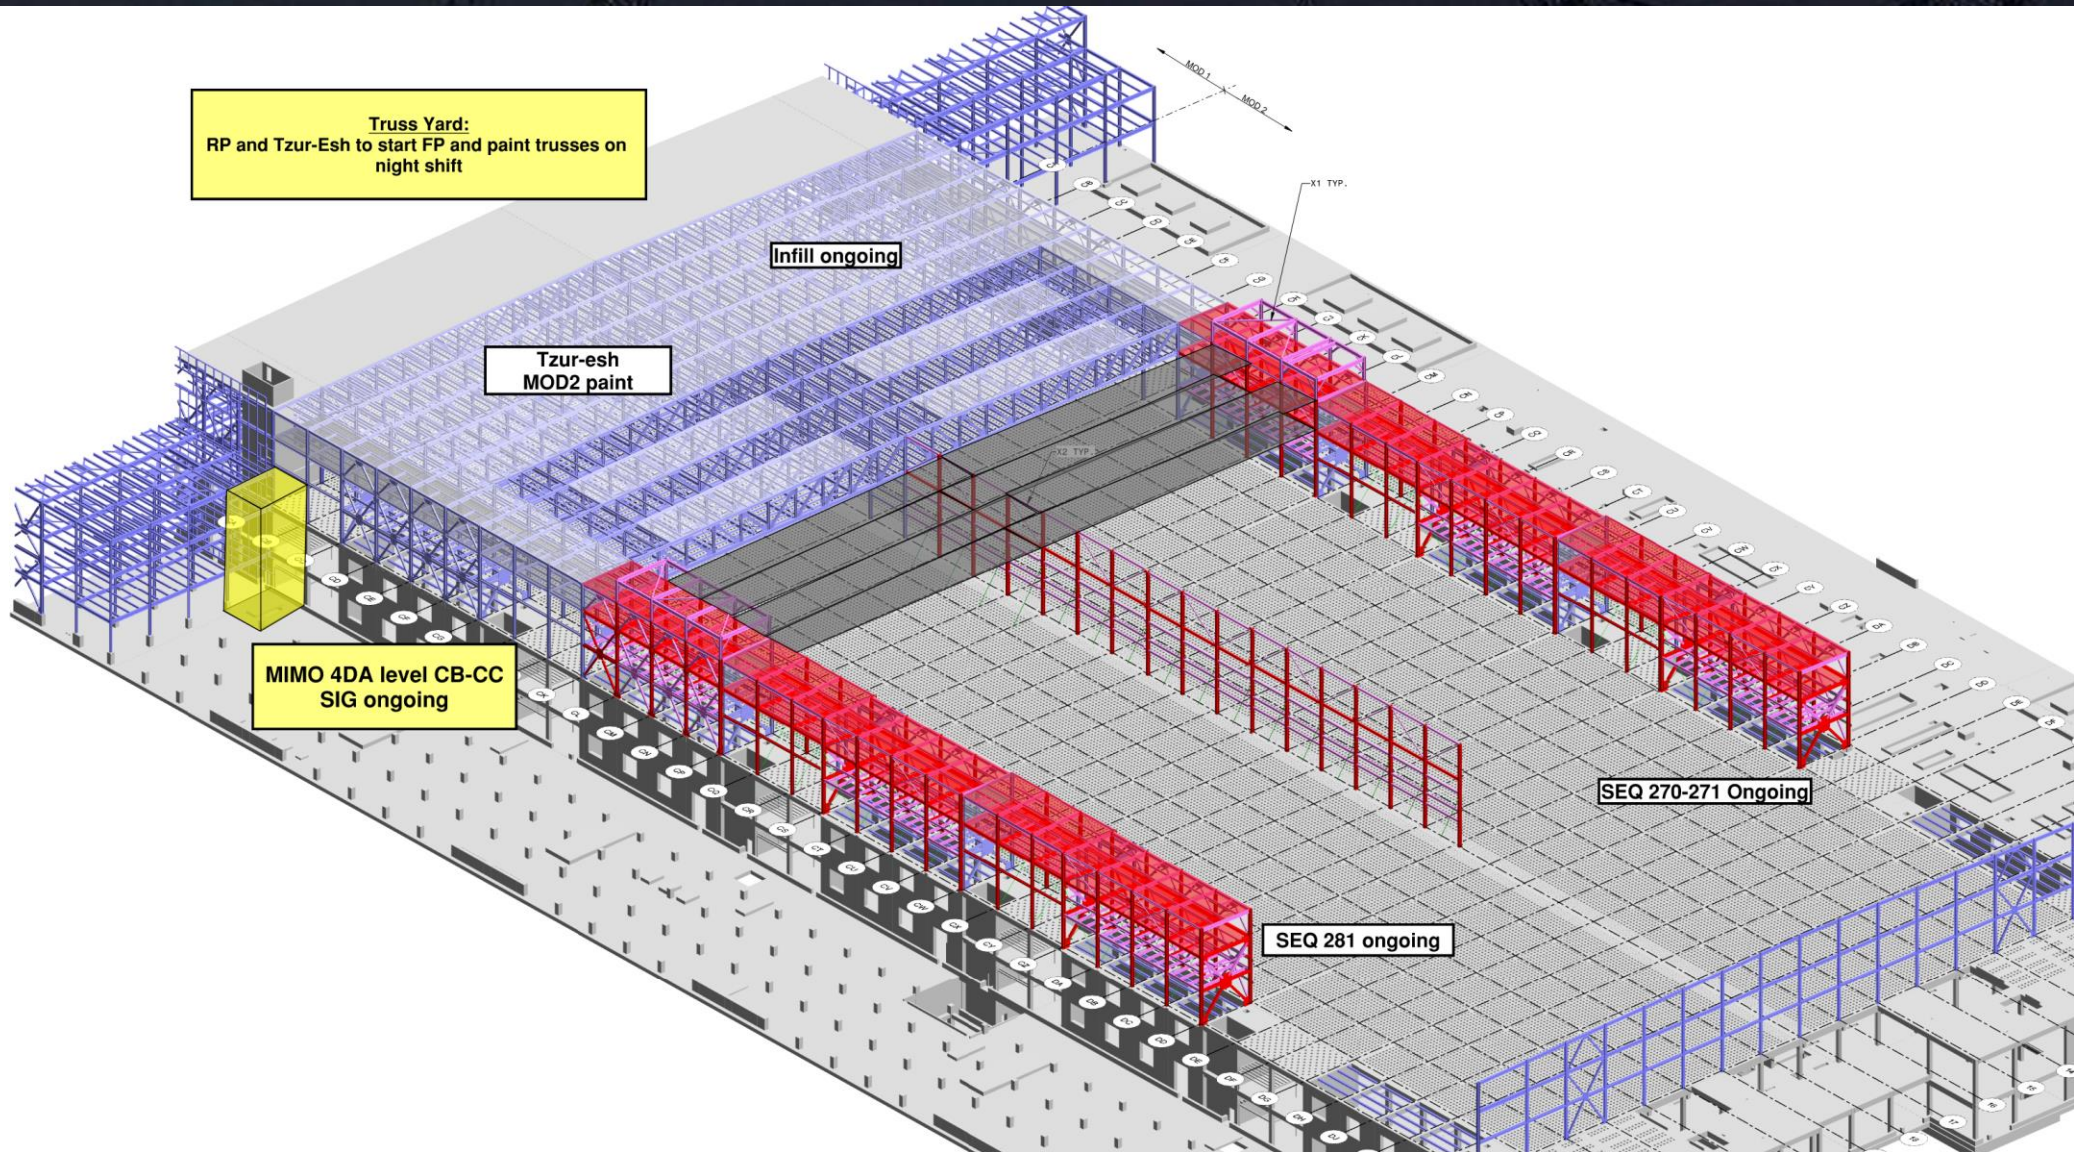

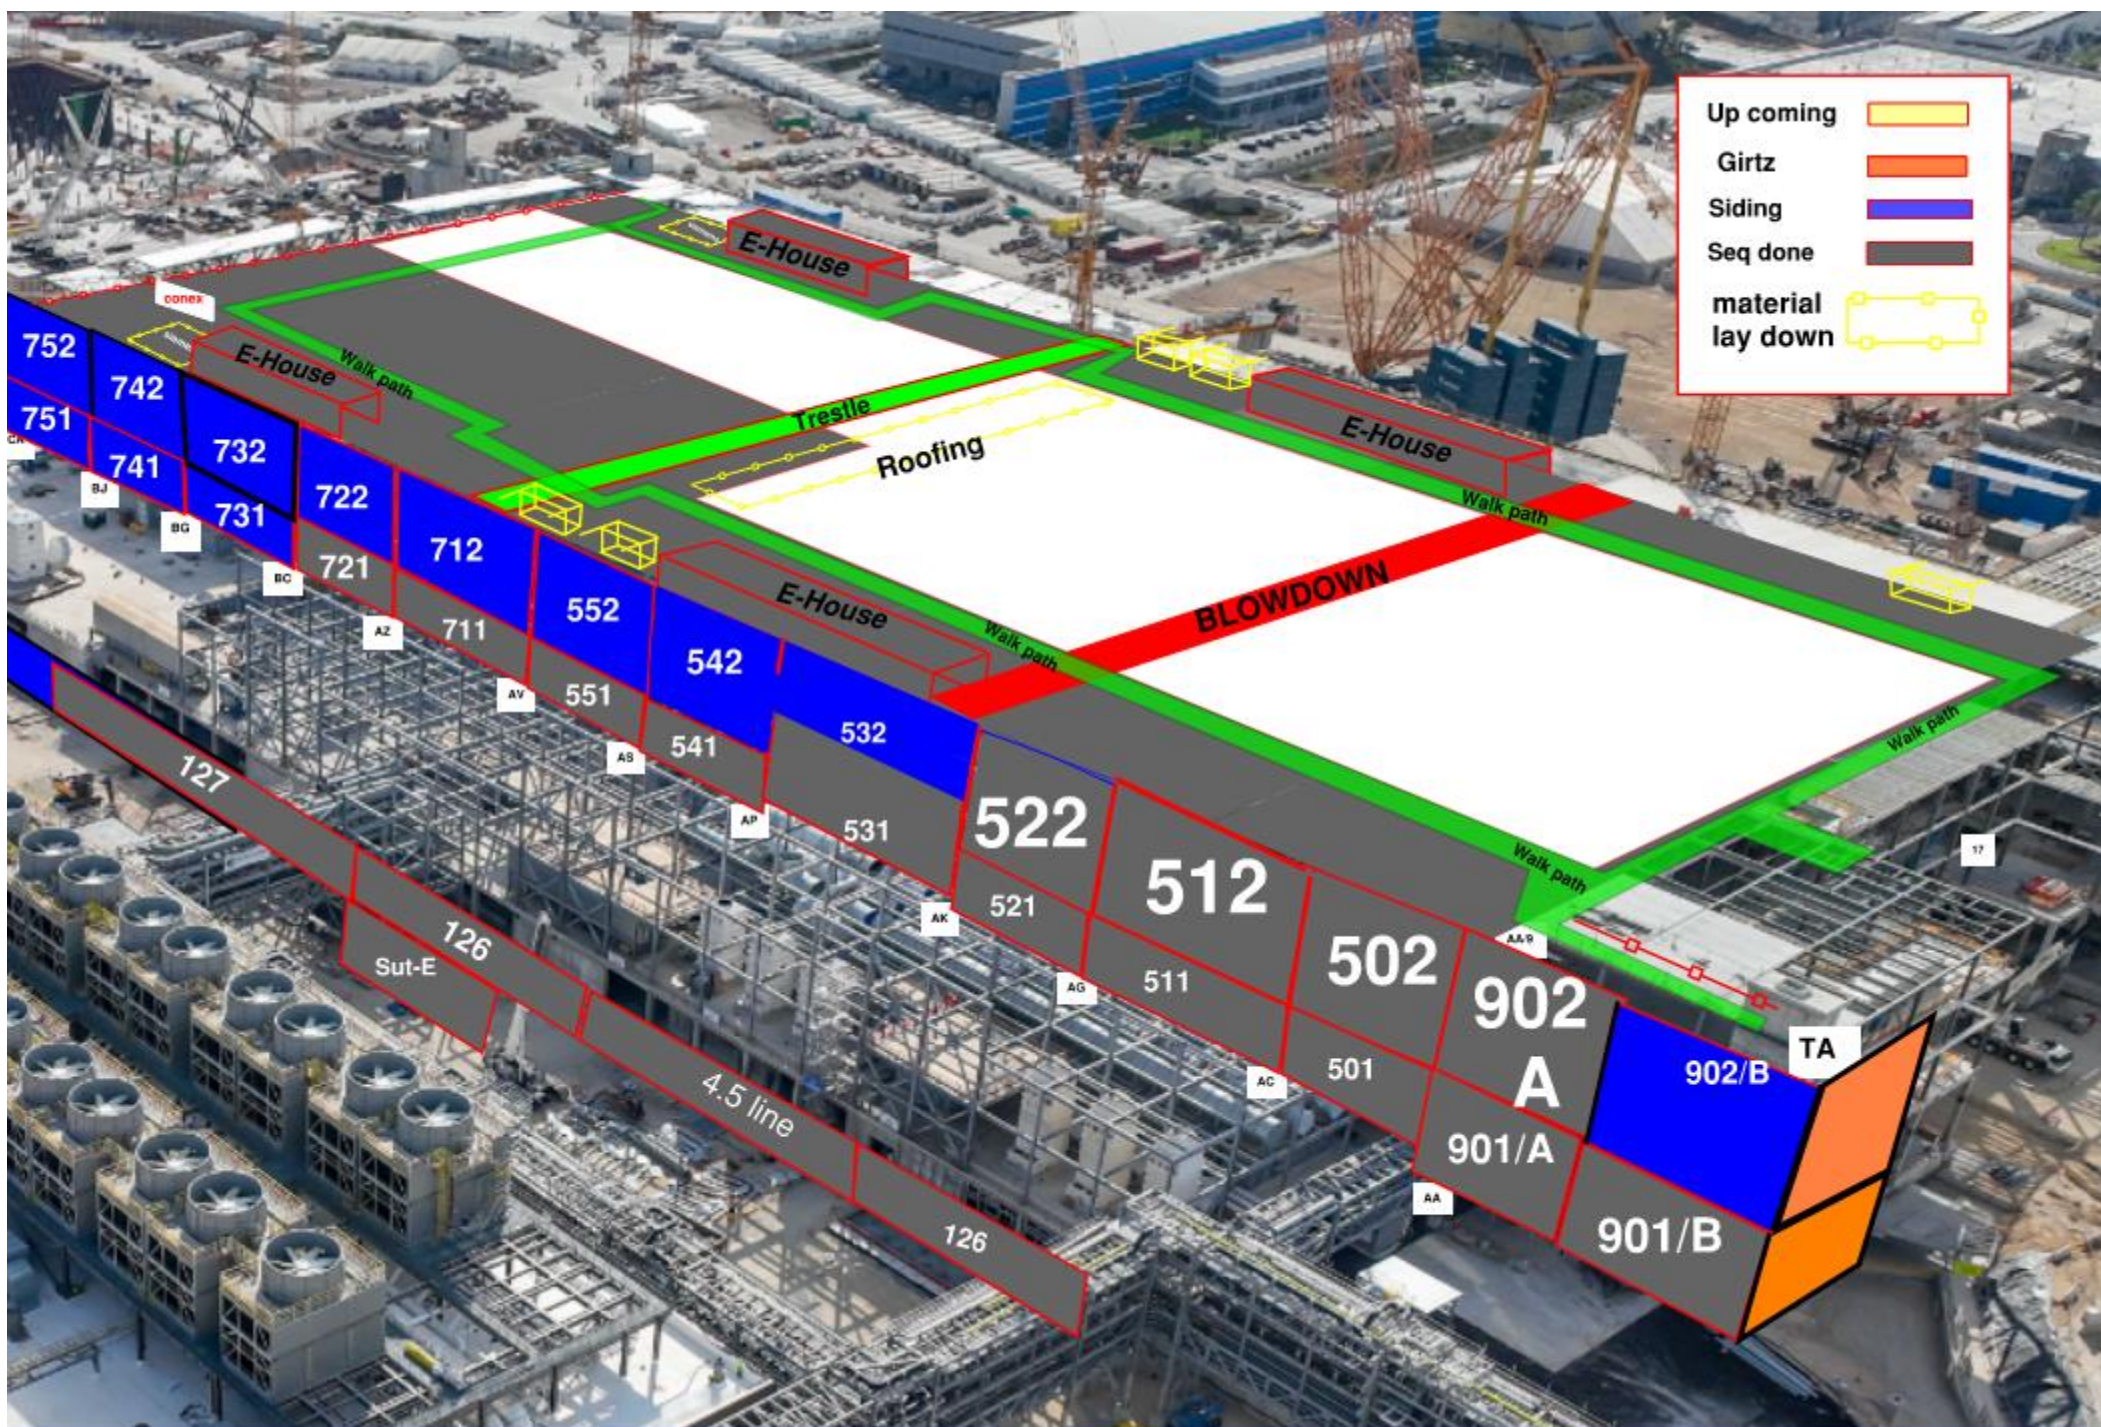

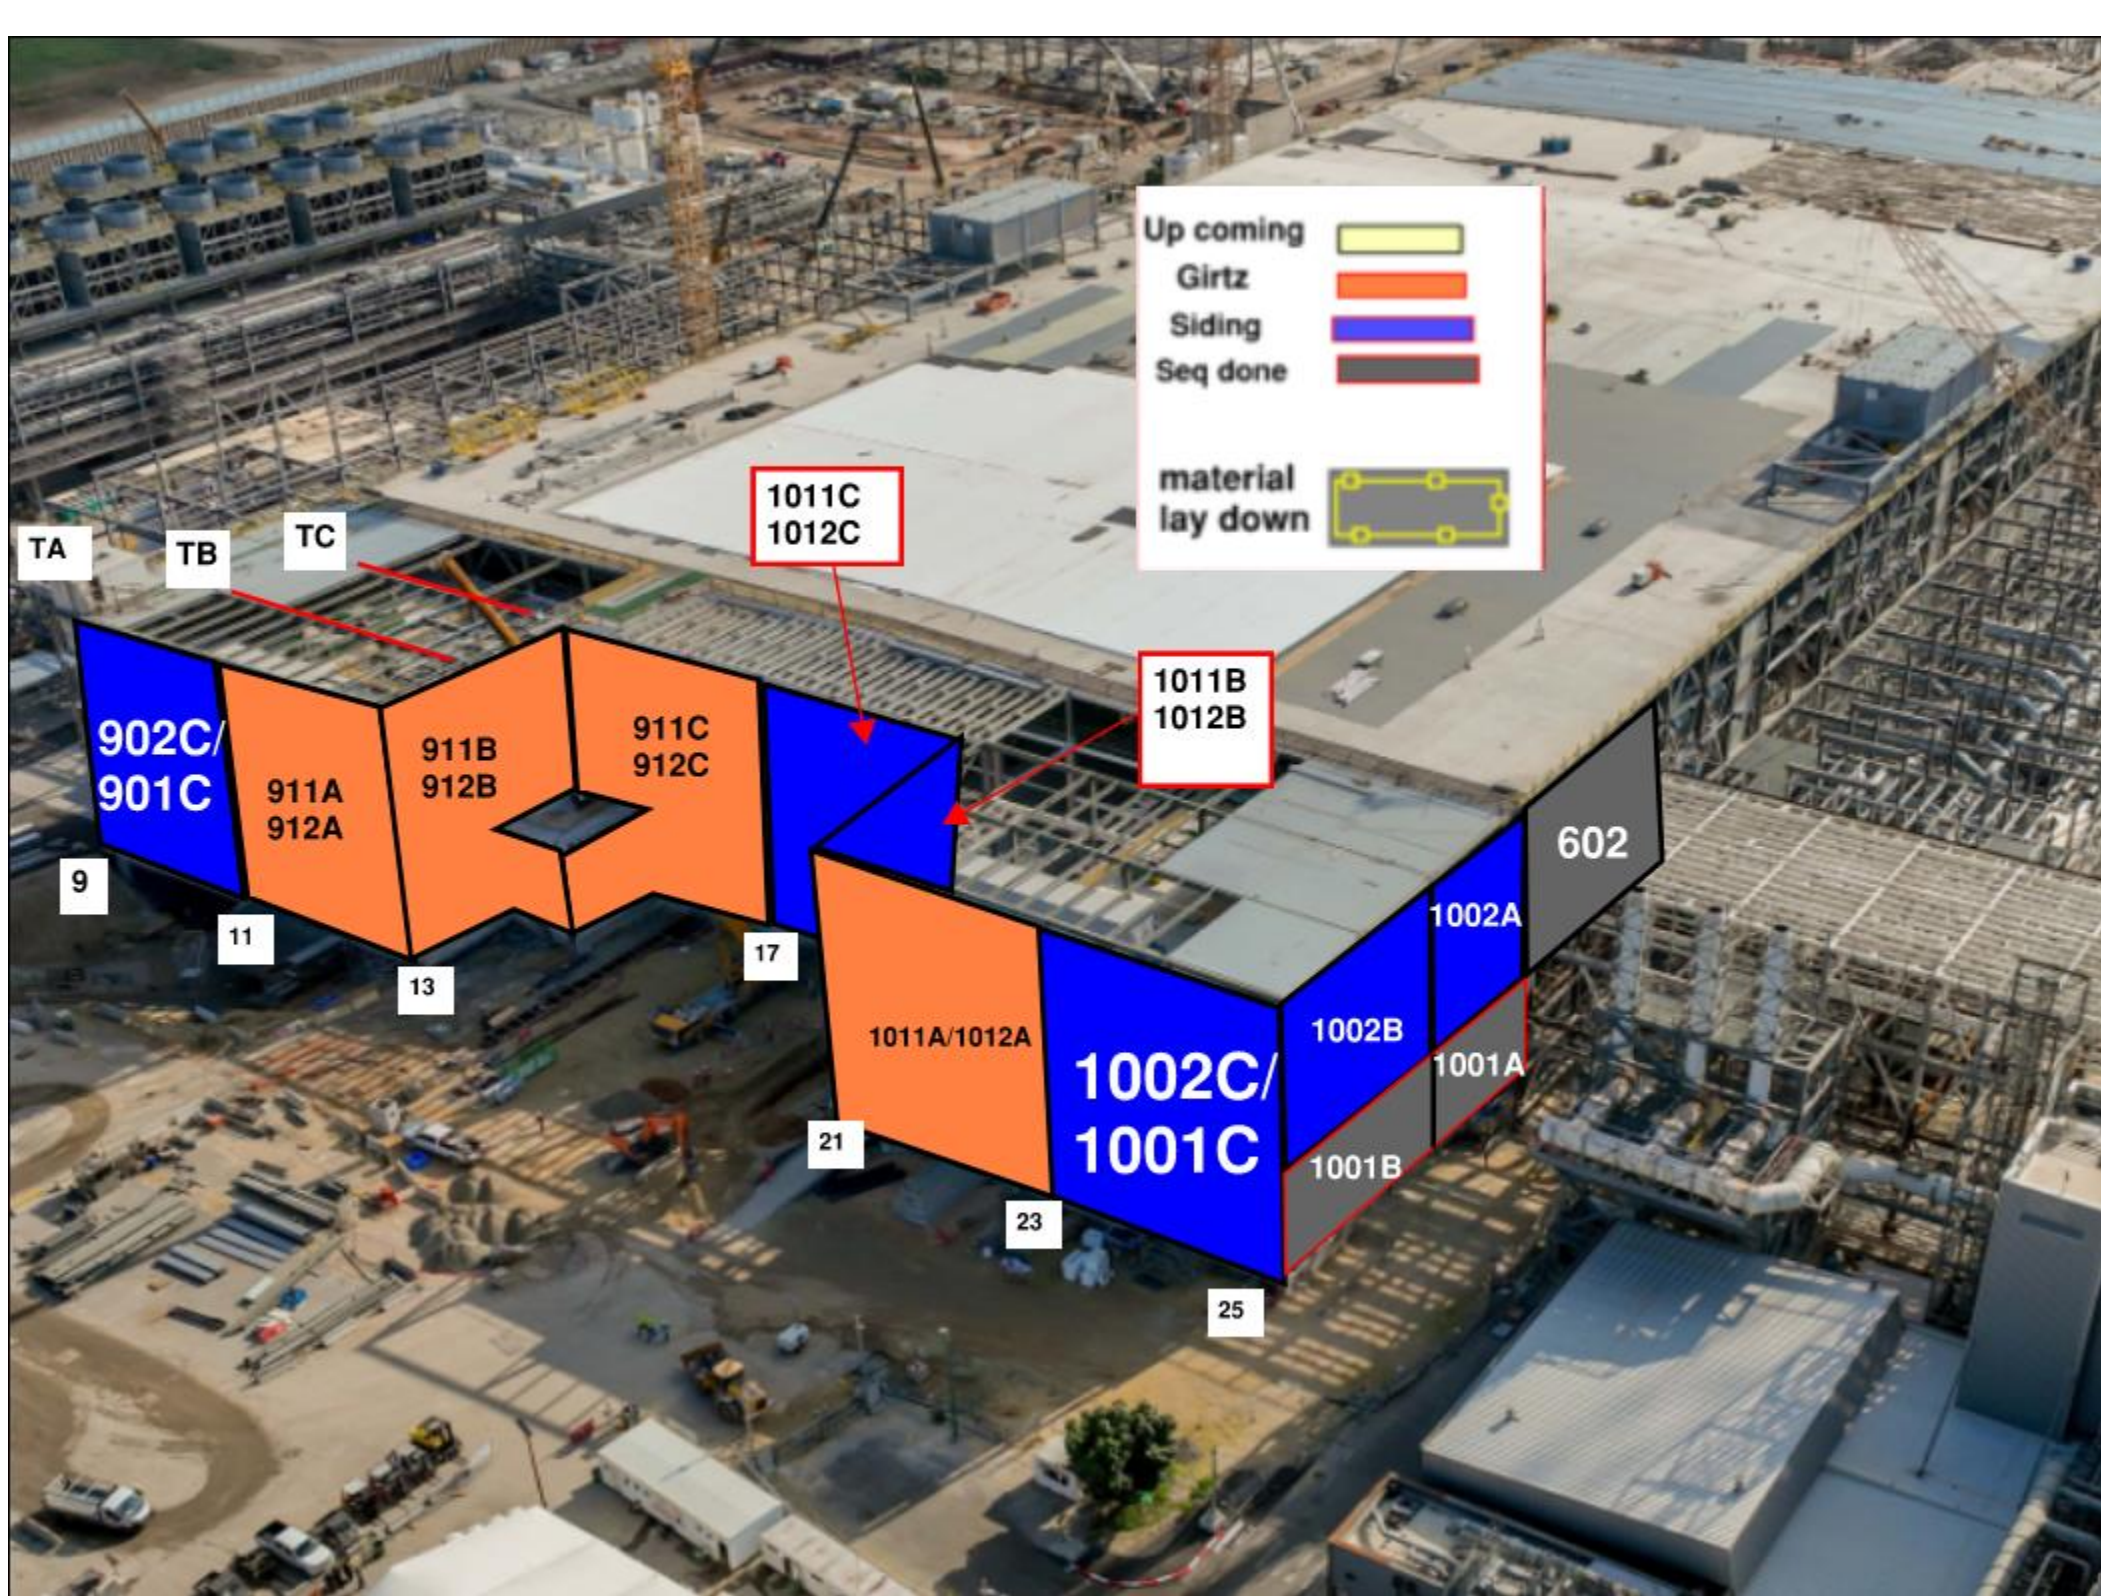

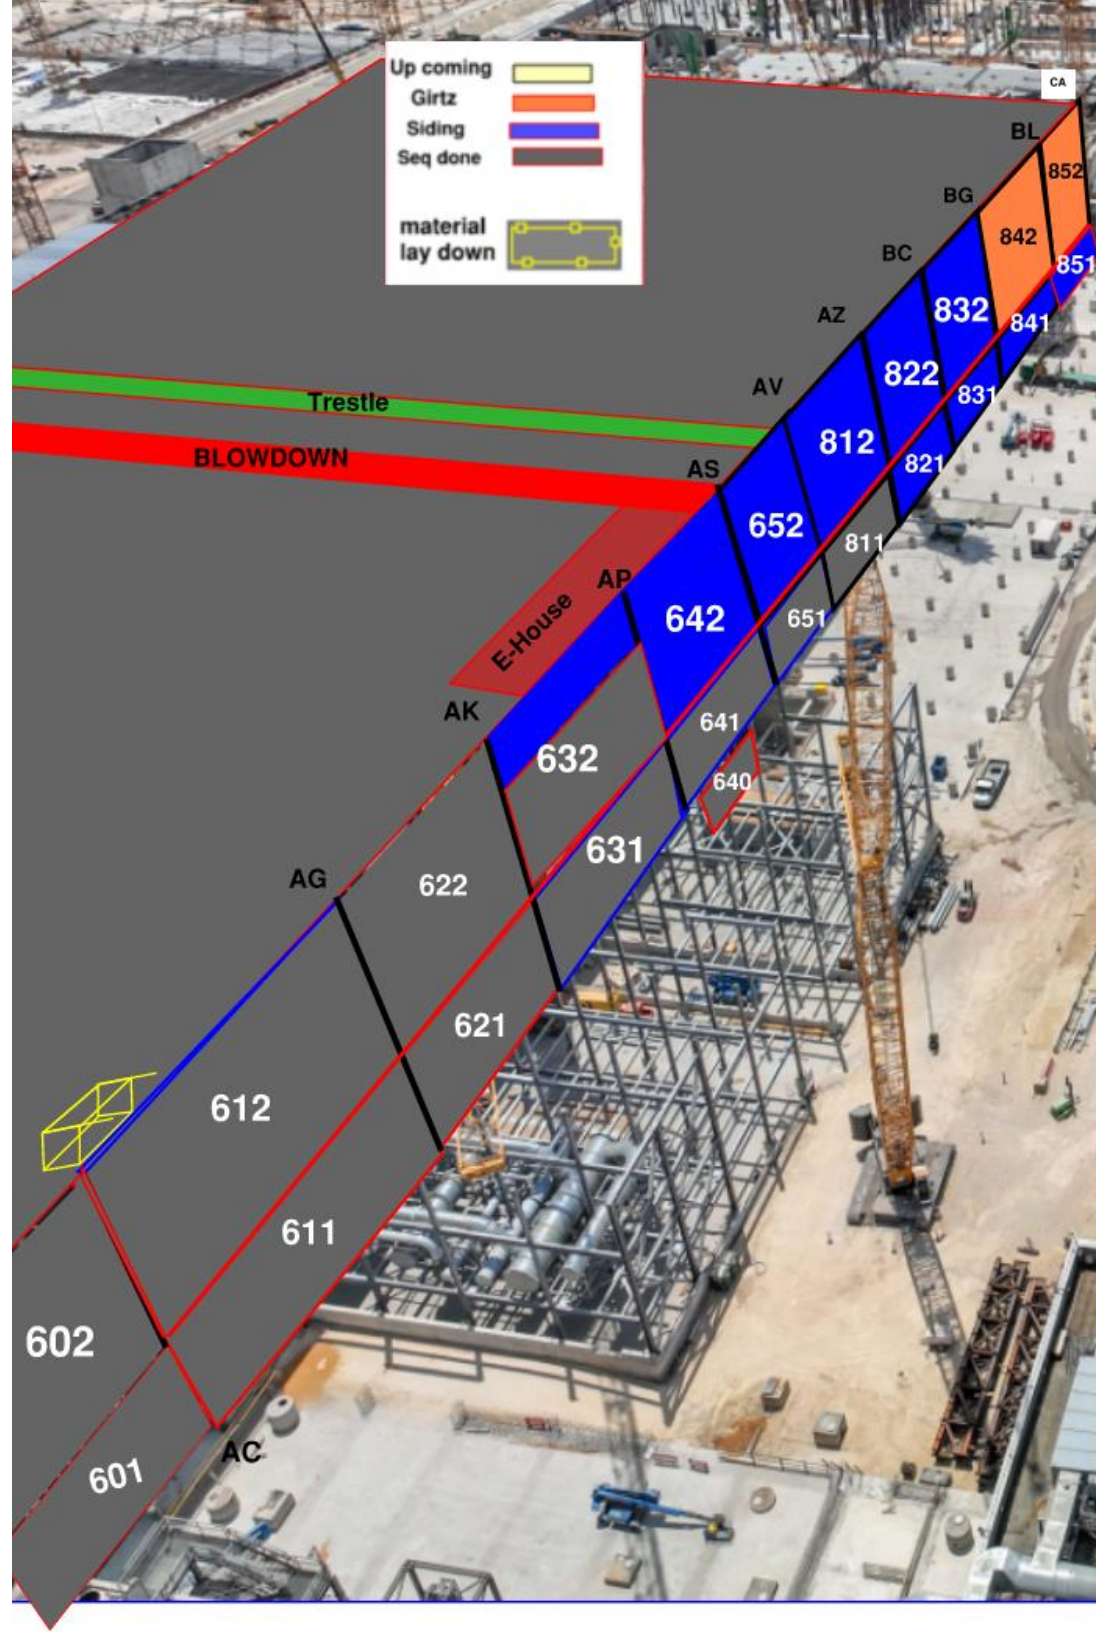

Siding - East FAB - PSSS

BLOWDOWN 30%

[illegible]

Siding - West FAB - JYG


BLOWDOWN 30%

	TA	TB	TC		AA	AB	AC	AD	AE	AF	AG	AH	AJ	AK	AL	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA					
	1001/1002				601/602		611/612				621/622				631/632				641/642				651/652				811/812				821			
Total	28	28	28		15	18		31	31	31	31	28		31	31	31	31		31	31	31		31	31	31		31	31	31		31			
Installed	8	14	10		15	18		31	31	31	31		31	31	31		31	23	23	13		9	9	14		6	6	14	14	6				
%	29%	50%	36%		100%	100%		100%	100%	100%	100%		100%	100%	100%		100%	74%	74%	42%		29%	29%	45%		19%	19%	19%		19%	19%	45%	45%	19%
5RA	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
4DA	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
3FK	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
3FA	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
2SA SF	0	1	0		1	1		1	1	1	1		1	1	1	1	1	0		0	0	1		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
UL	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0		1	1		1	1	1	1		1	1	1	0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0		0	0	0		0	0	0	0	0	0	0	0	0		

PSSS.1


Utility Level
1YA

PSSS Roof
2SA

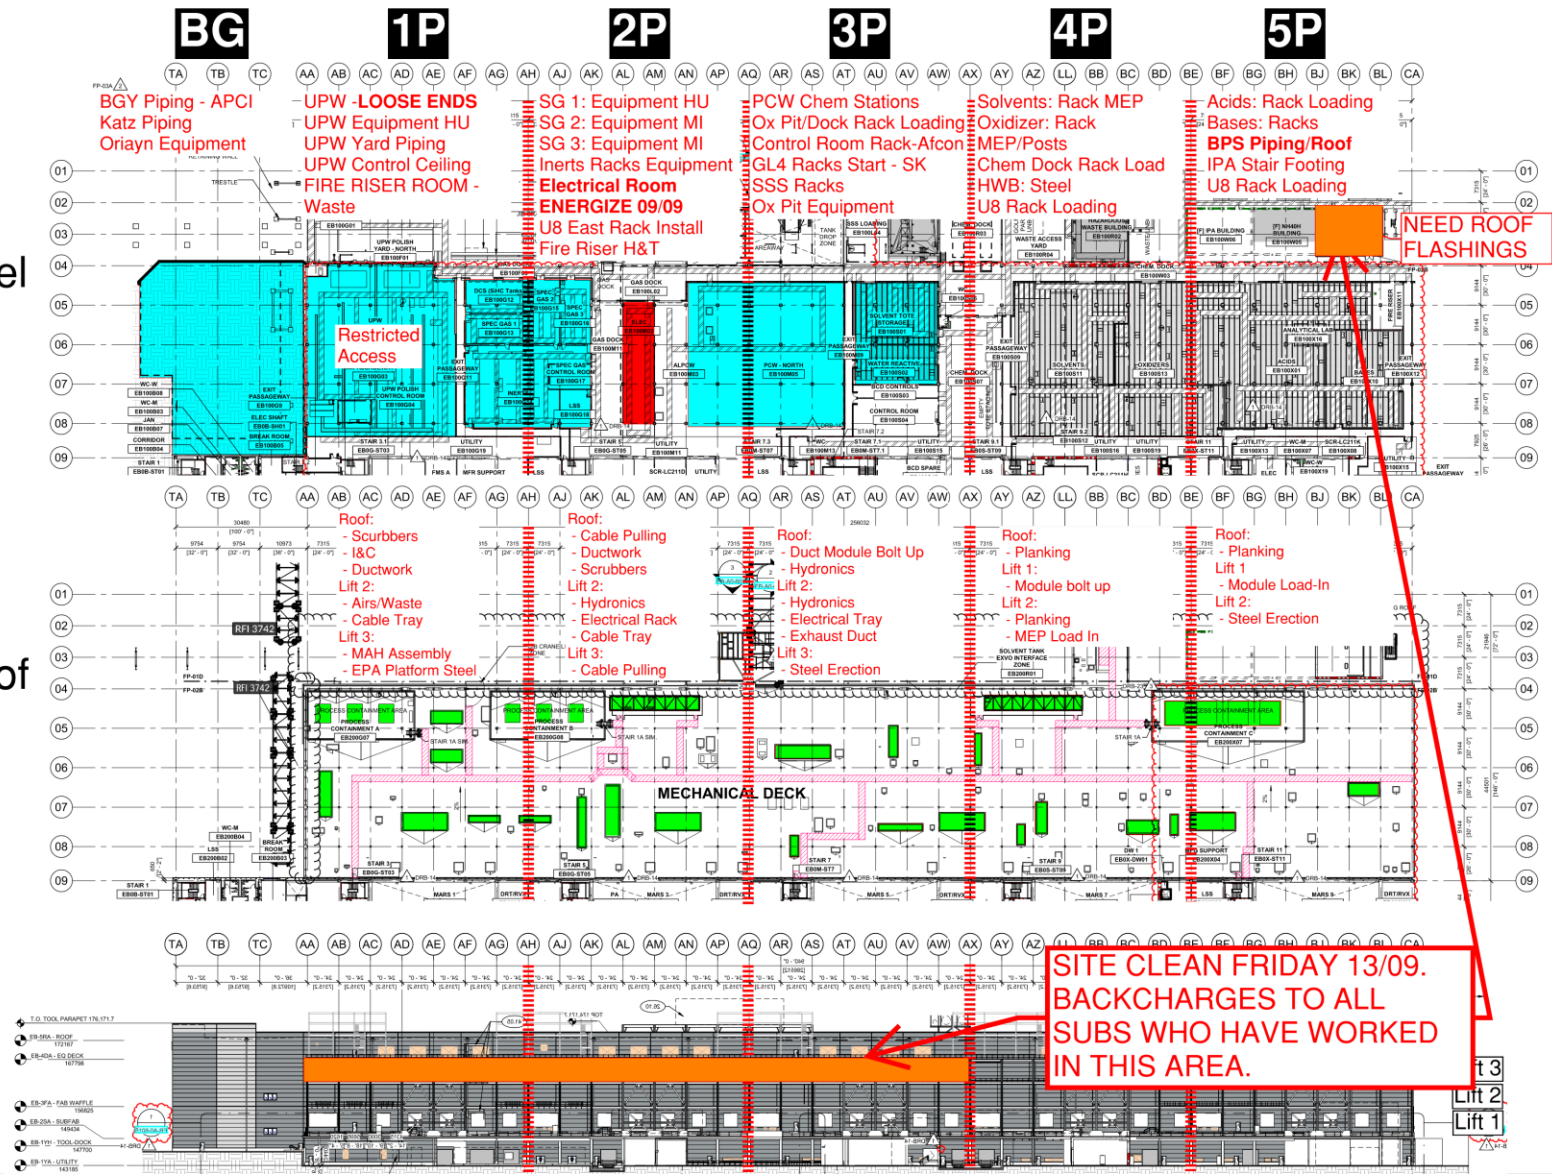


PSSS.2


Utility Level
1YA

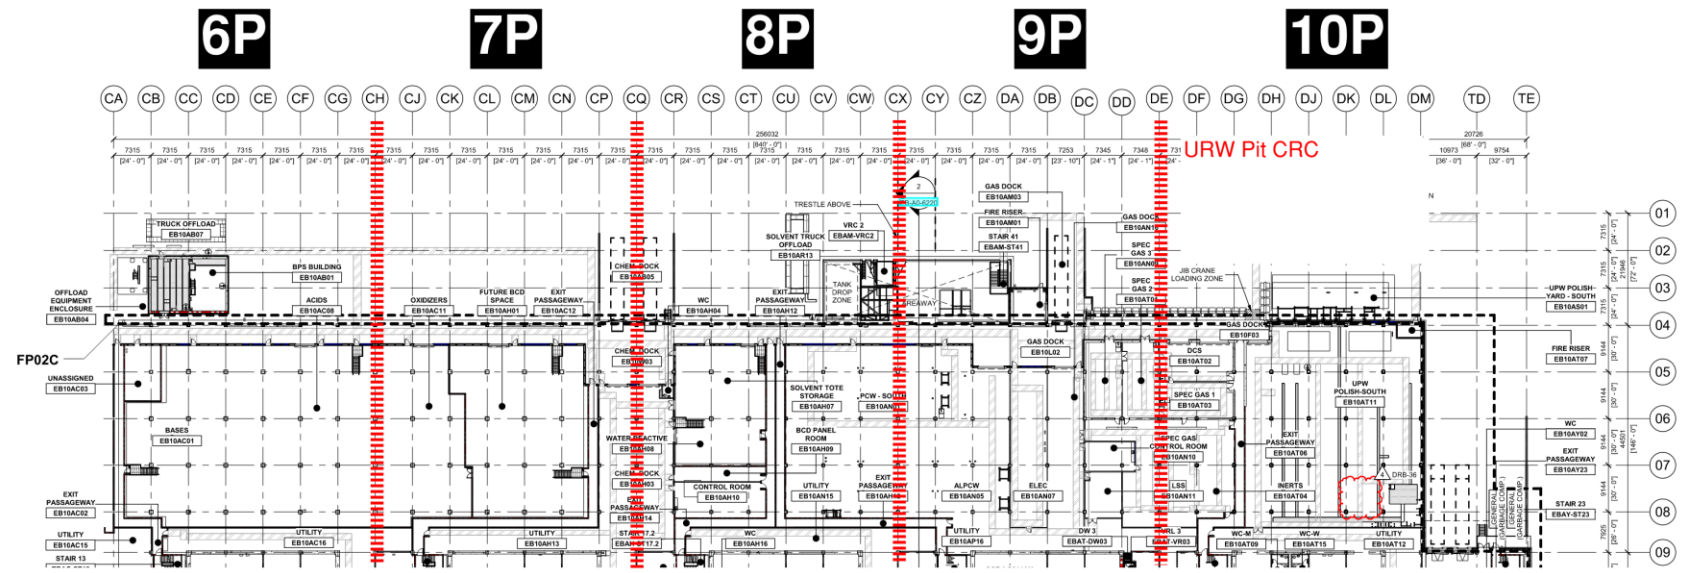

PSSS Roof
2SA

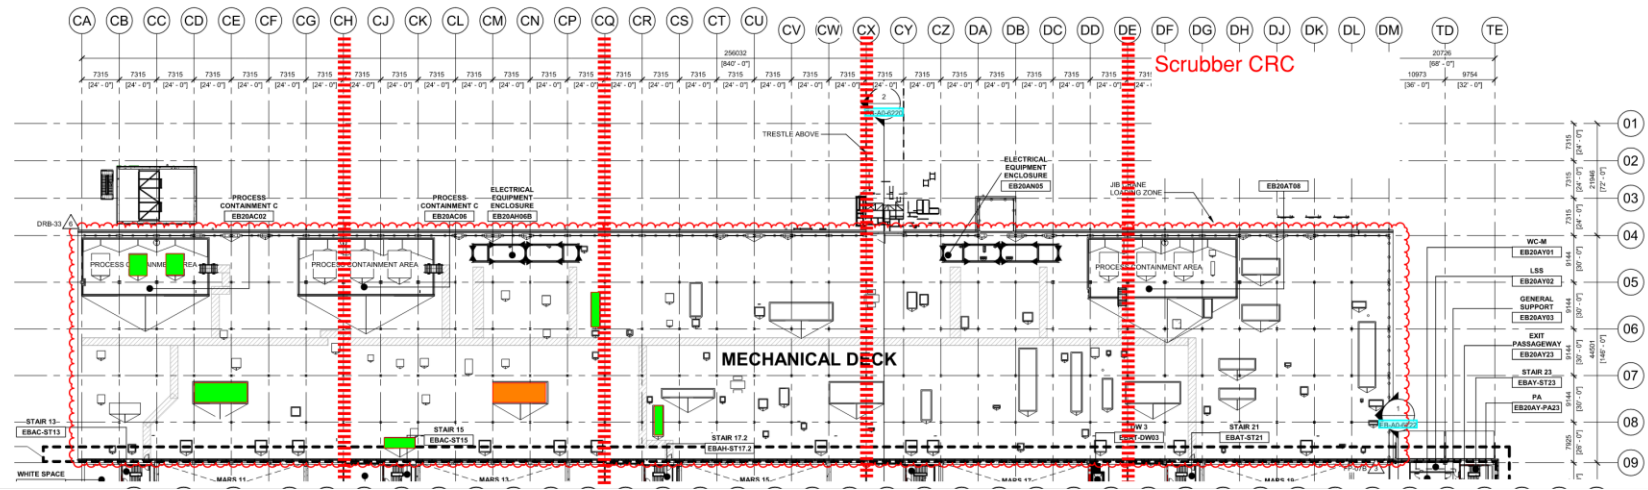


PSSS
CLEAN
13/09

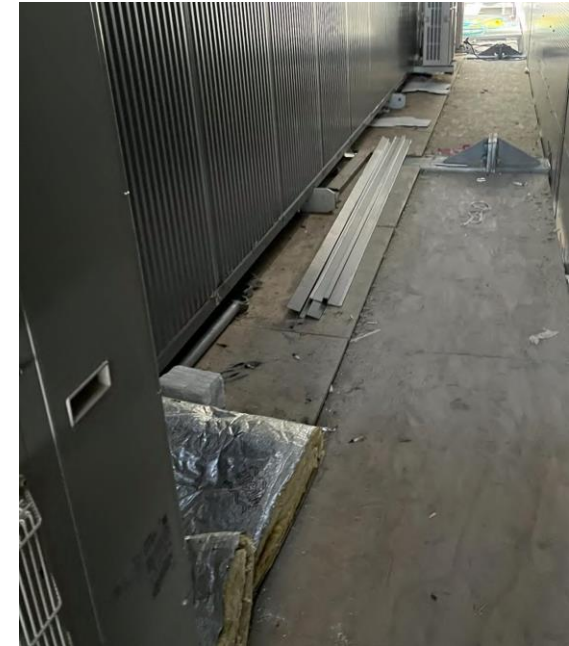




WJG 01J, 02J LIFT 2 & 3

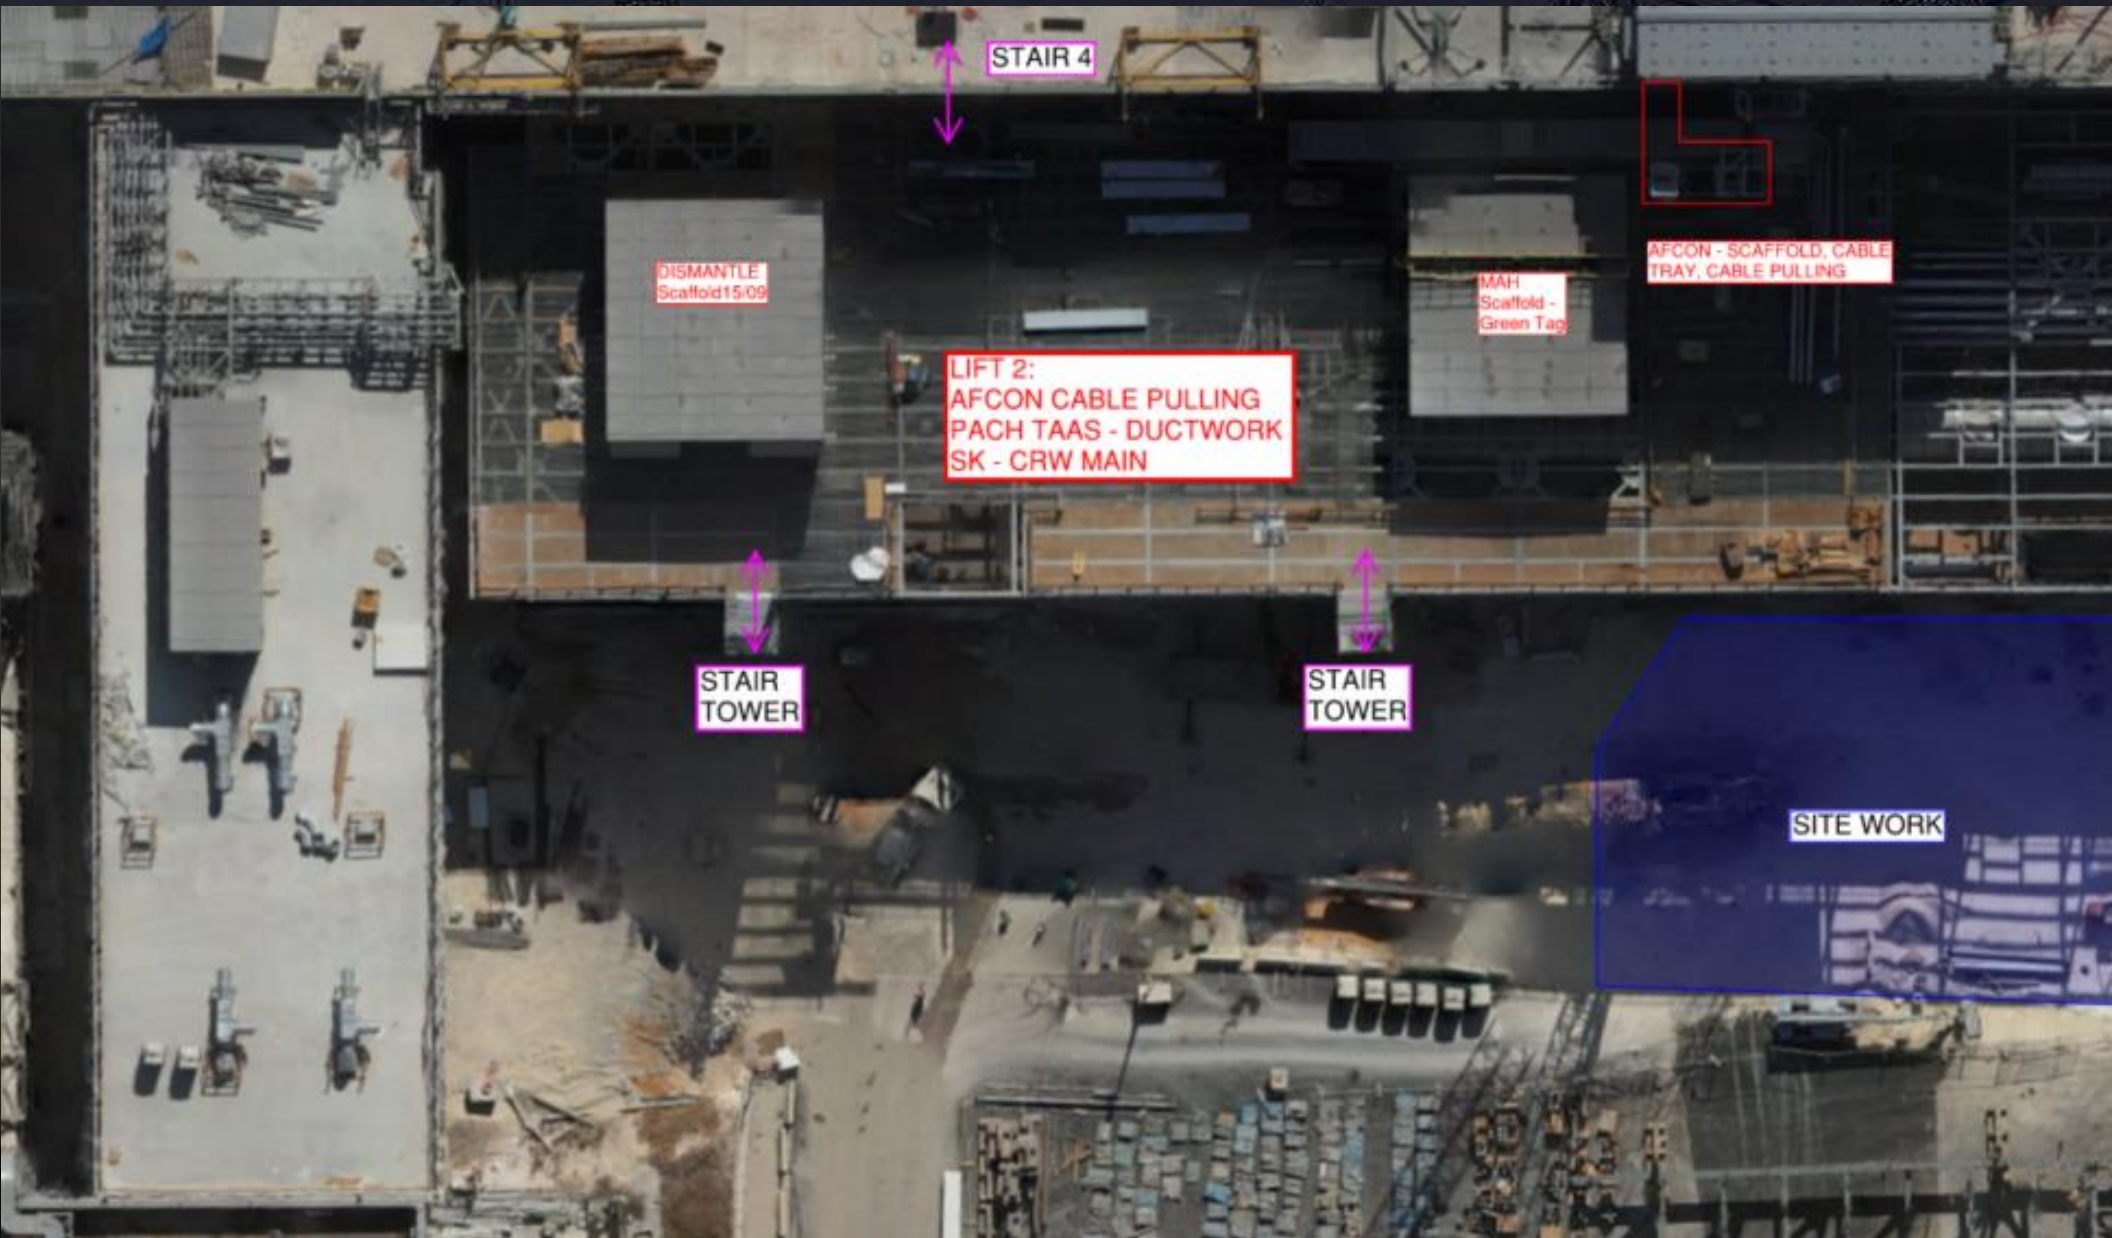




WJG 03J, 04J, 05J LIFT 2 & 3



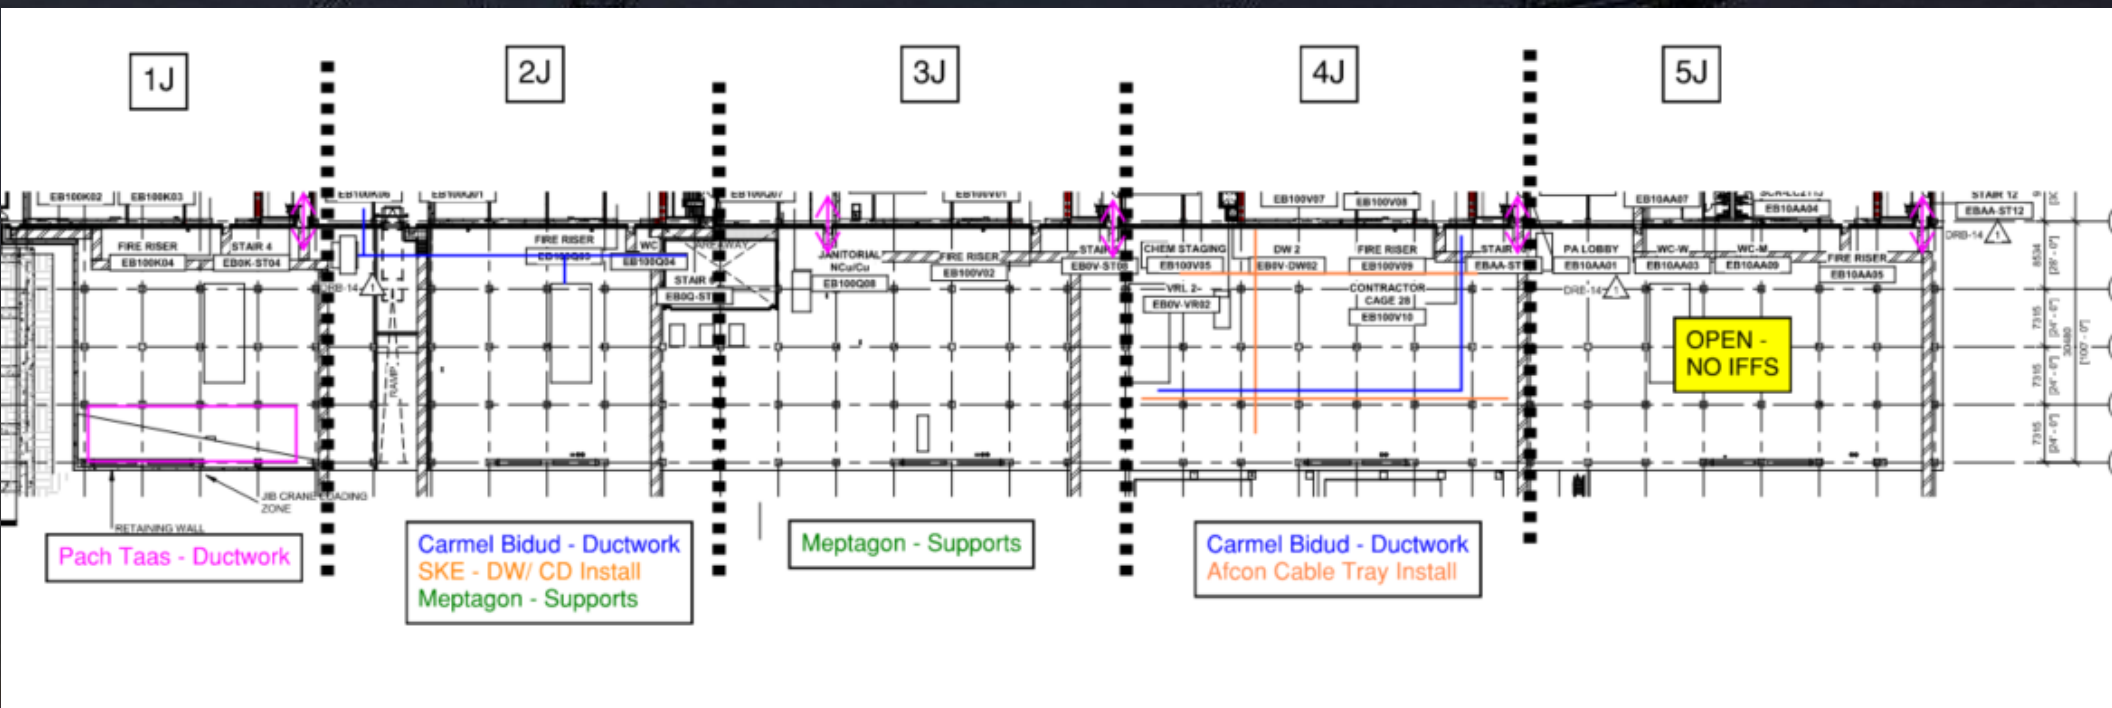


WJG Closed Night Shift 17/09/2024

SKE IA/PA PNEUMATIC TEST
138 PSI - 8 Hour
30m EXCLUSION ZONE
MAIN GL 28 @ UTILITY LEVEL
Date: 17/09/2024
2100 - 0600

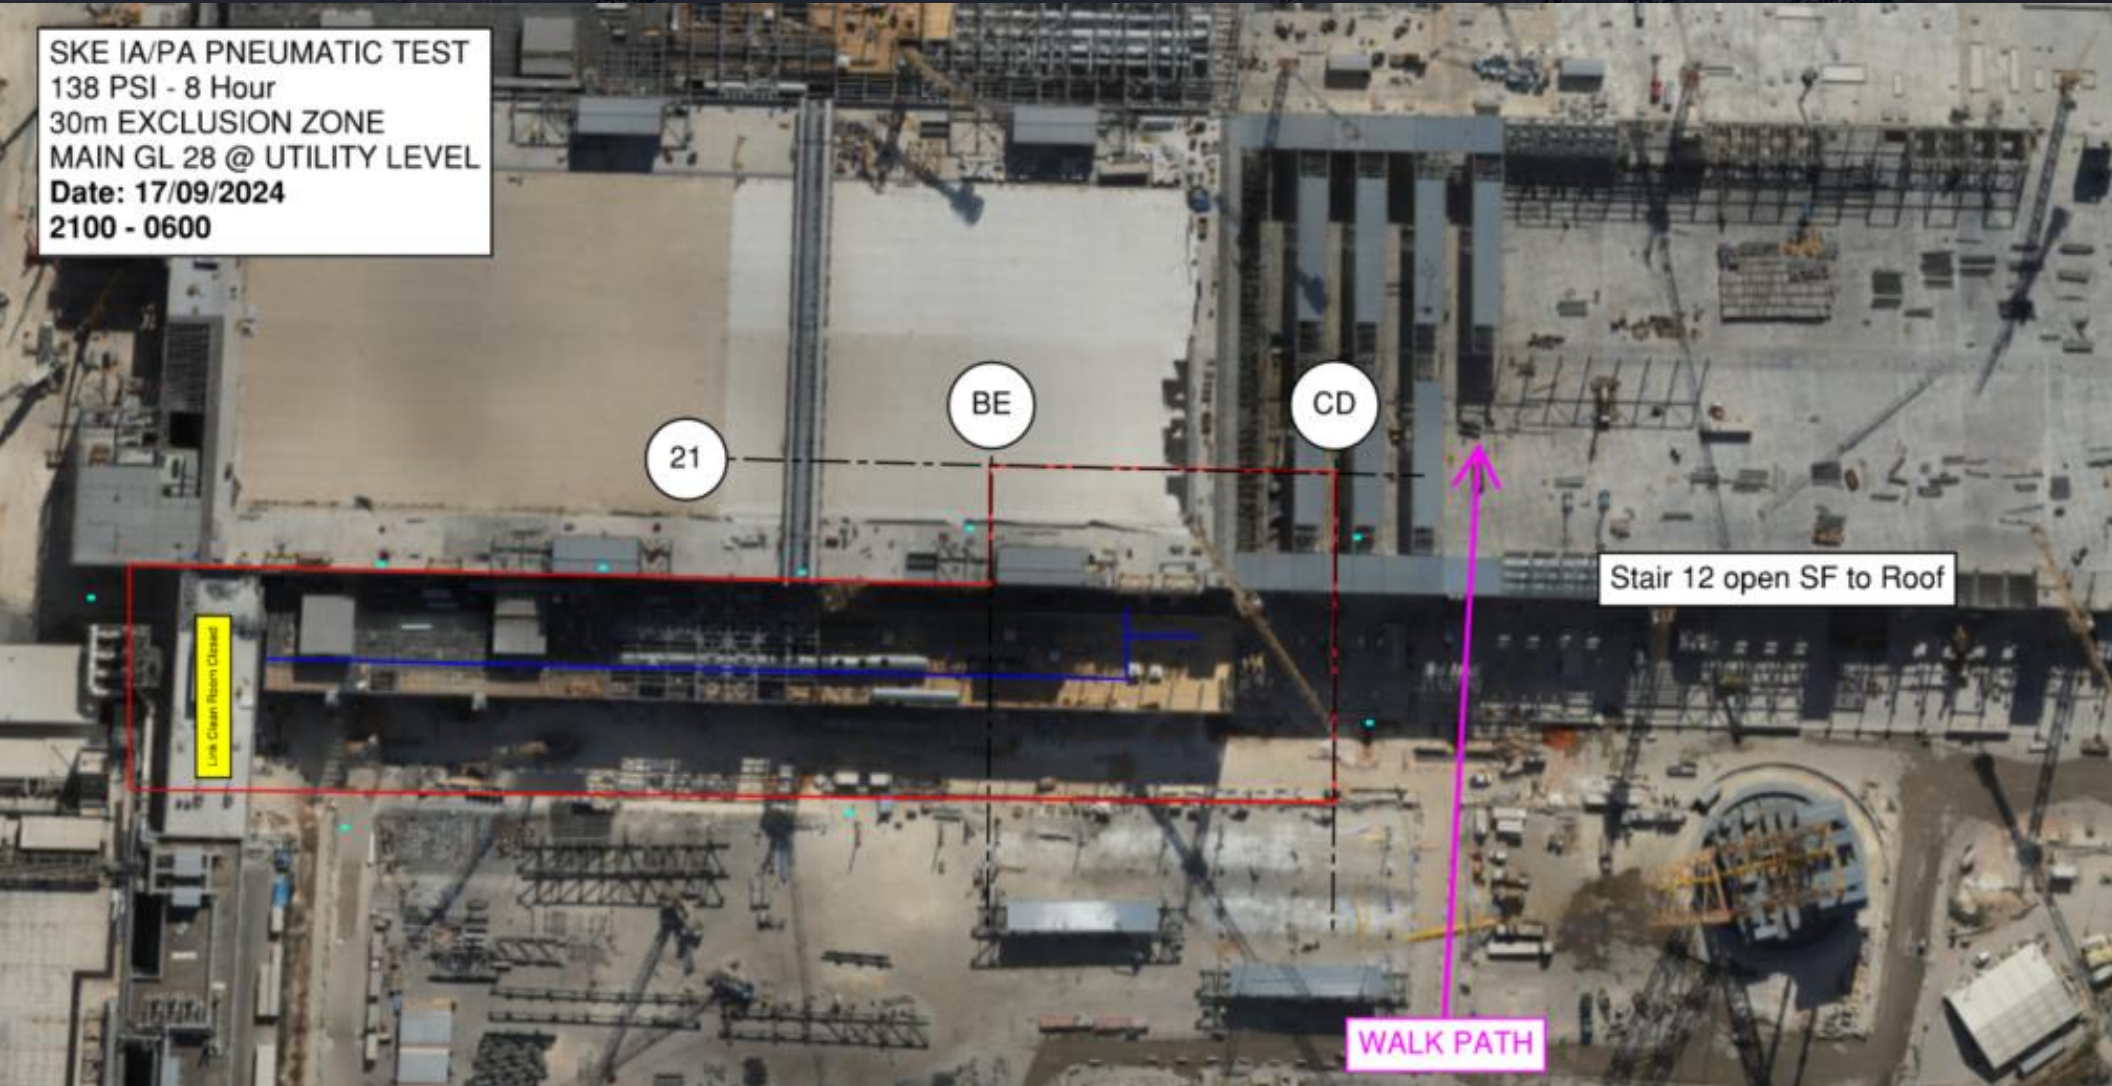

VFD SET 16/09/2024 & 18/09/2024

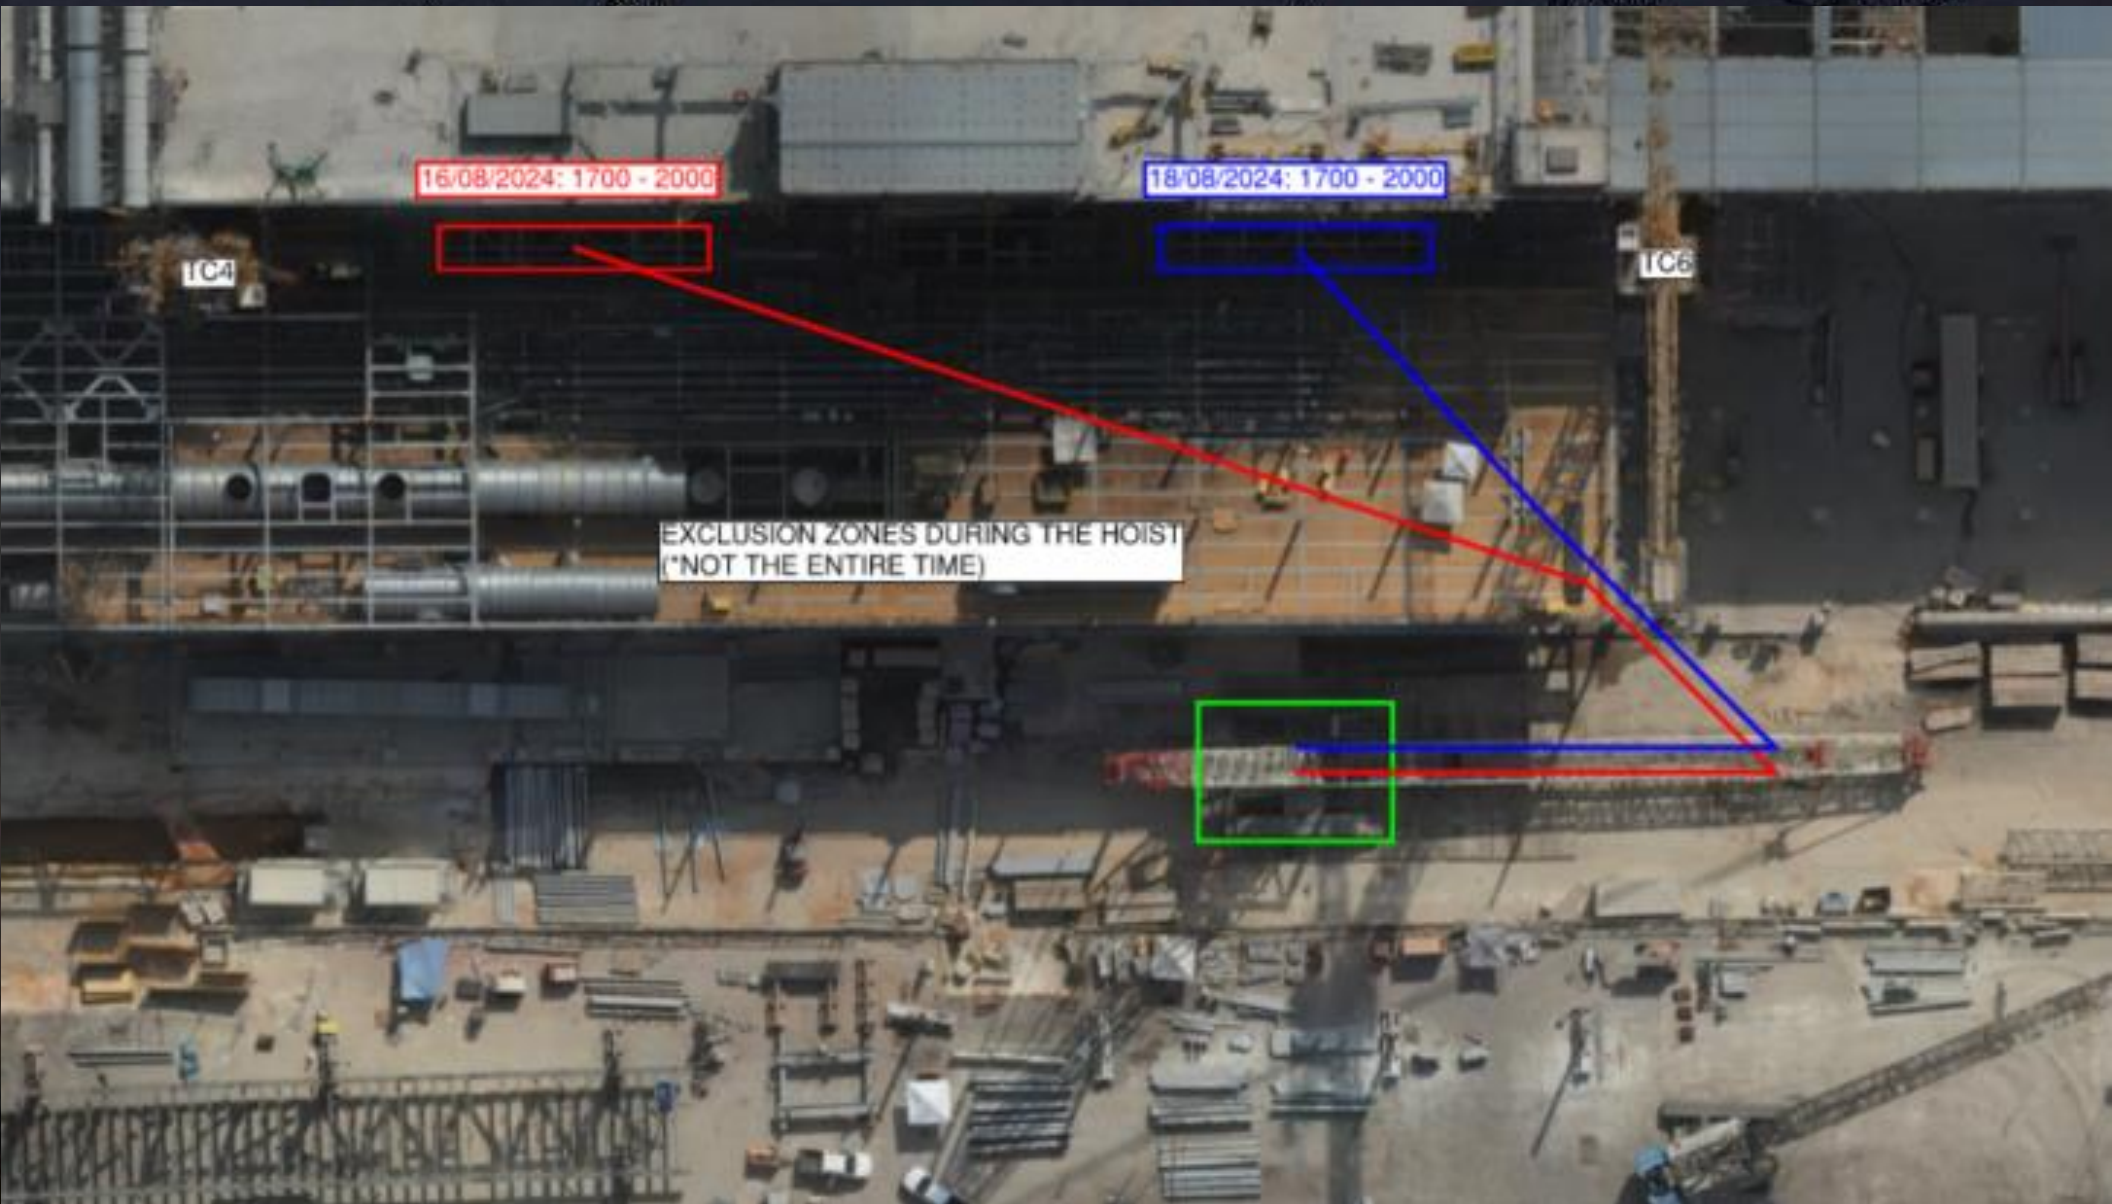


UPN 126/113
Fab




Passivation Ongoing
UPN126/113
North side EJG/WJG

Boiler Flush and Restore ongoing



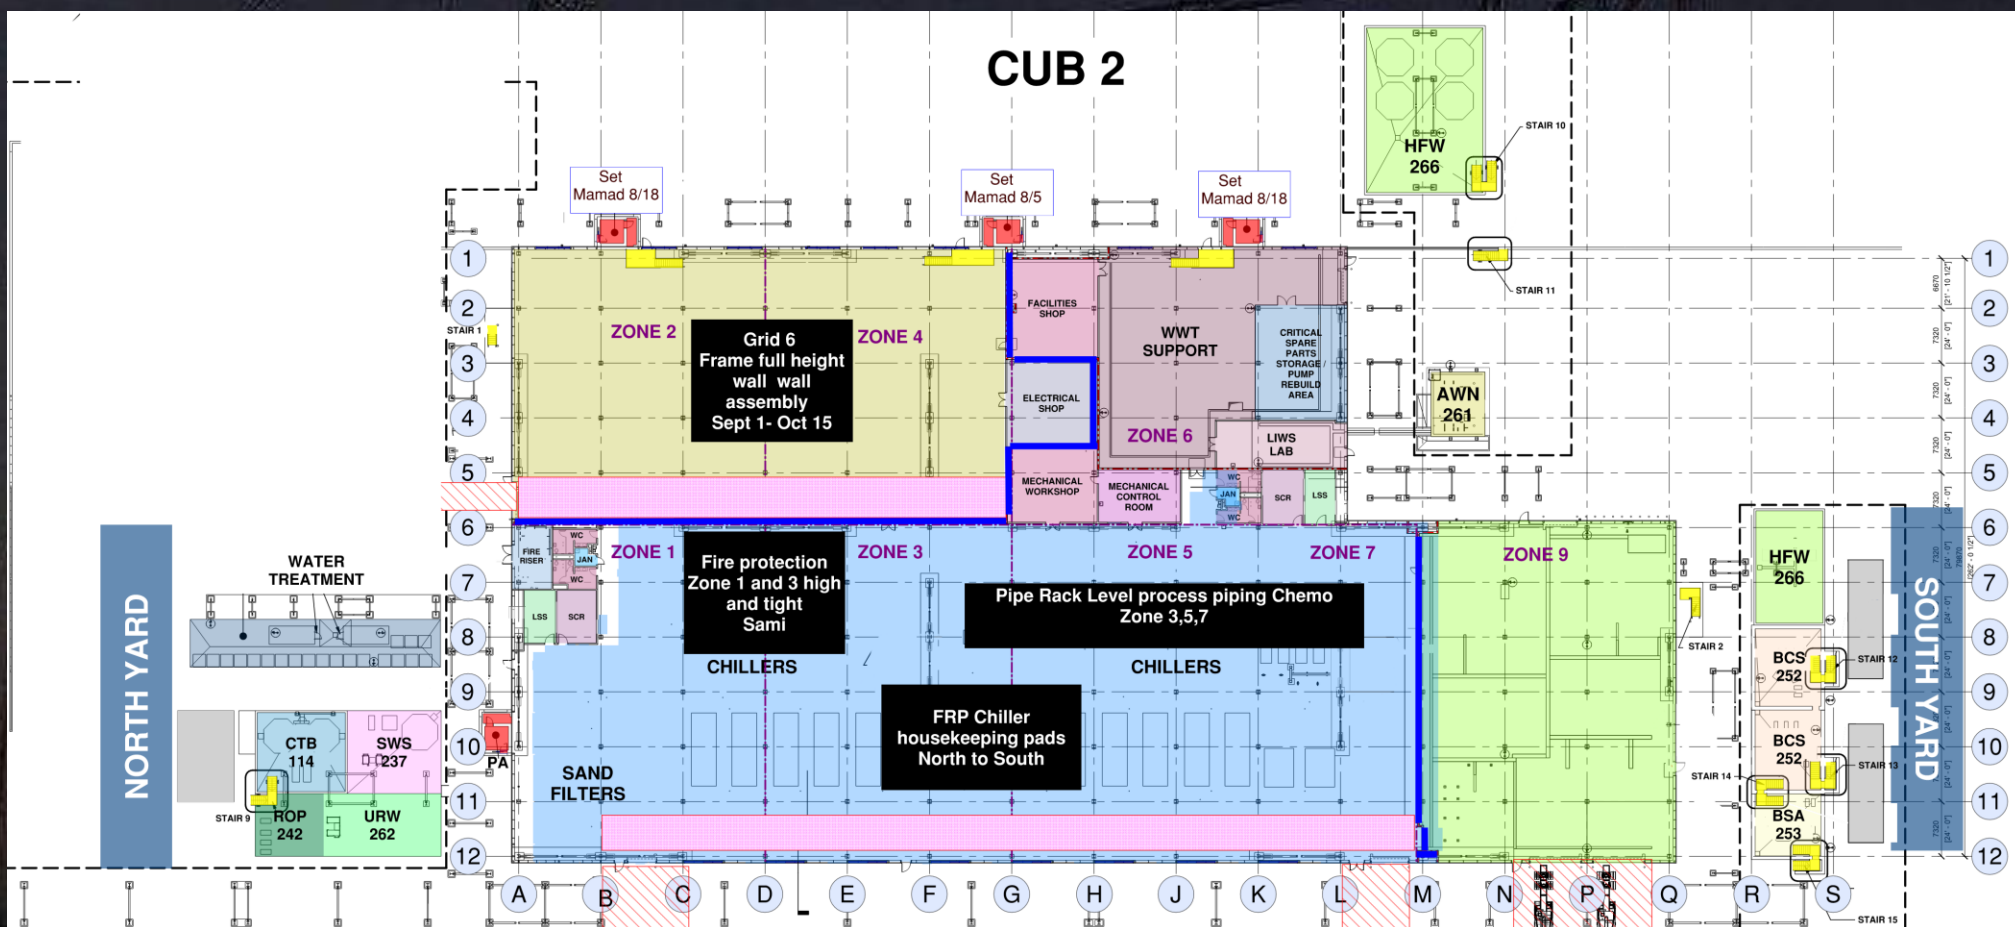

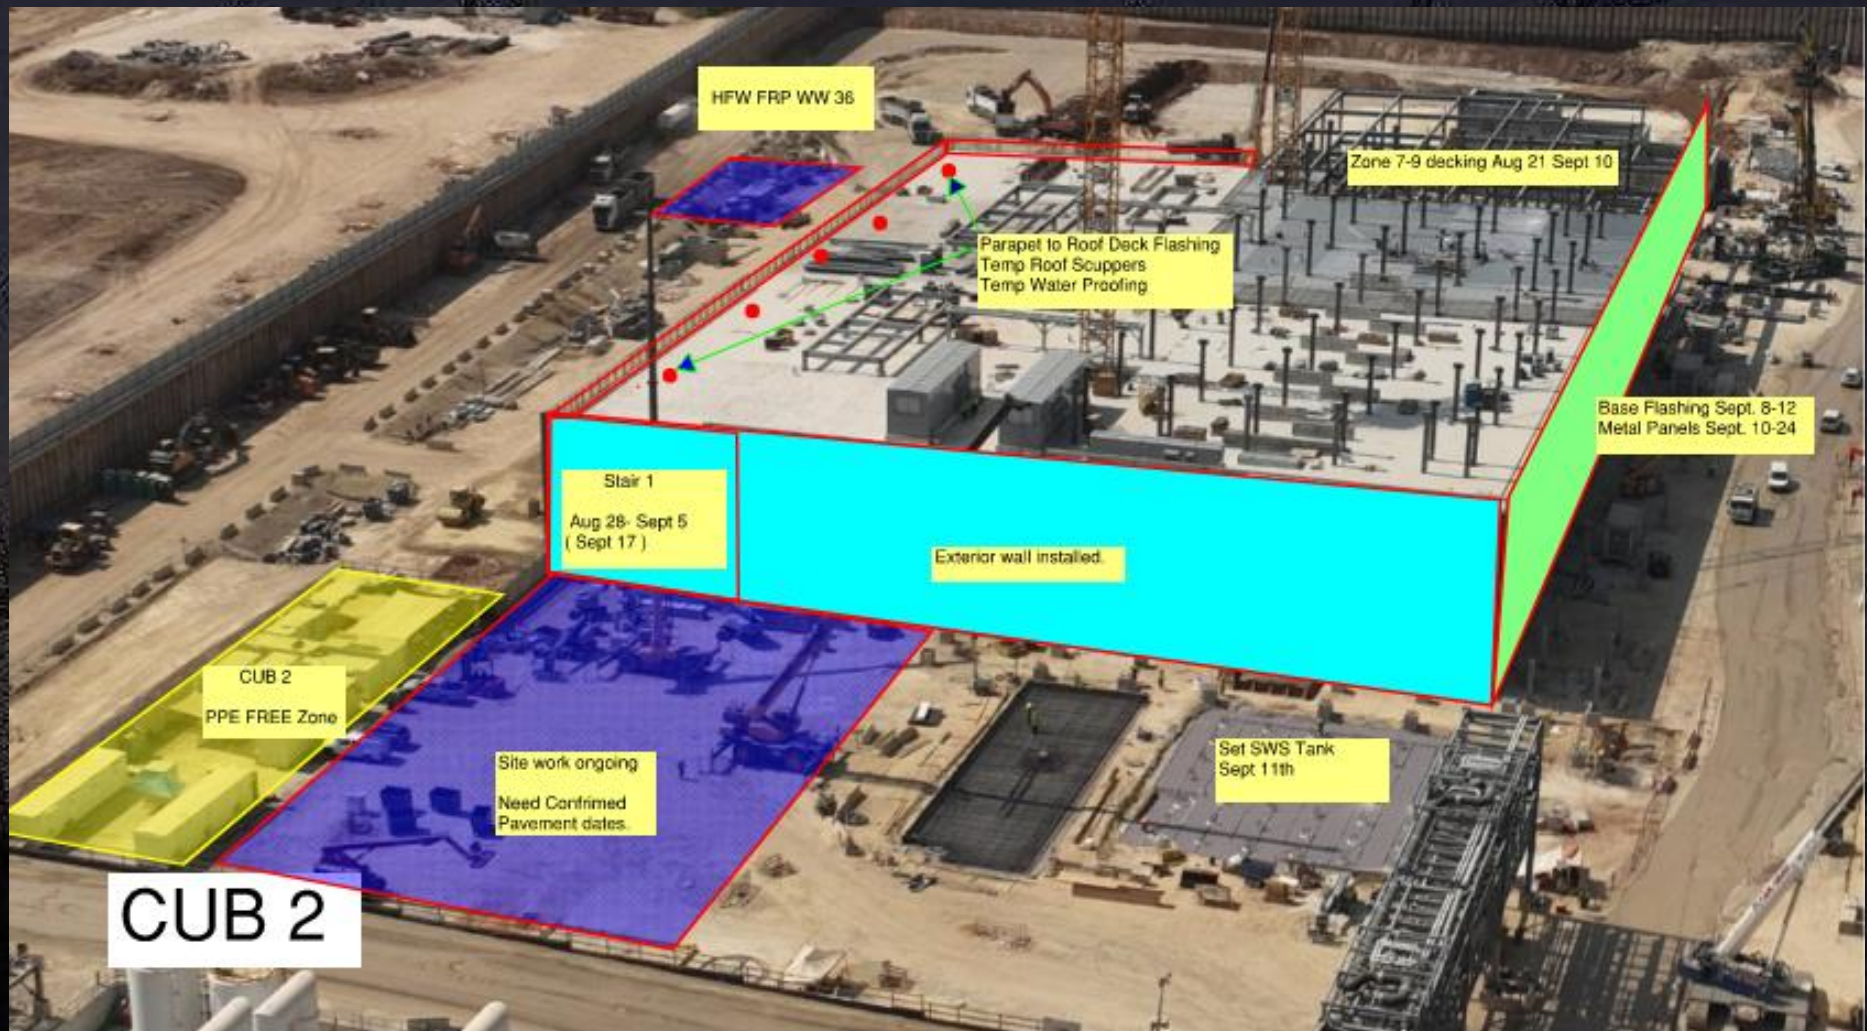

SES- SIPP

Elmoe- 1145- term control cables
MEP-- CAT 5 cable pull&term
Electrosafe-All facilities- tie-in OAT &FAT

FK electra

- rejects&changing wiring
generators pannels


Elmor- zone 1
1118 sipp- LOTTO
DE-energized XFMRs
531&532 change portal
screws -

NO ENTRY
HV ENERGIZED AREA

TMT Z 8 Soil replacement
backfilling Type A & compacting

TMT-
clean & seal sewage &
Drainage manholes

TMT DID NOT COMPLETE
CLEANUP
NEED JOB SERVICES
WORKERS&FORKLIFT FOR
FRIDAY

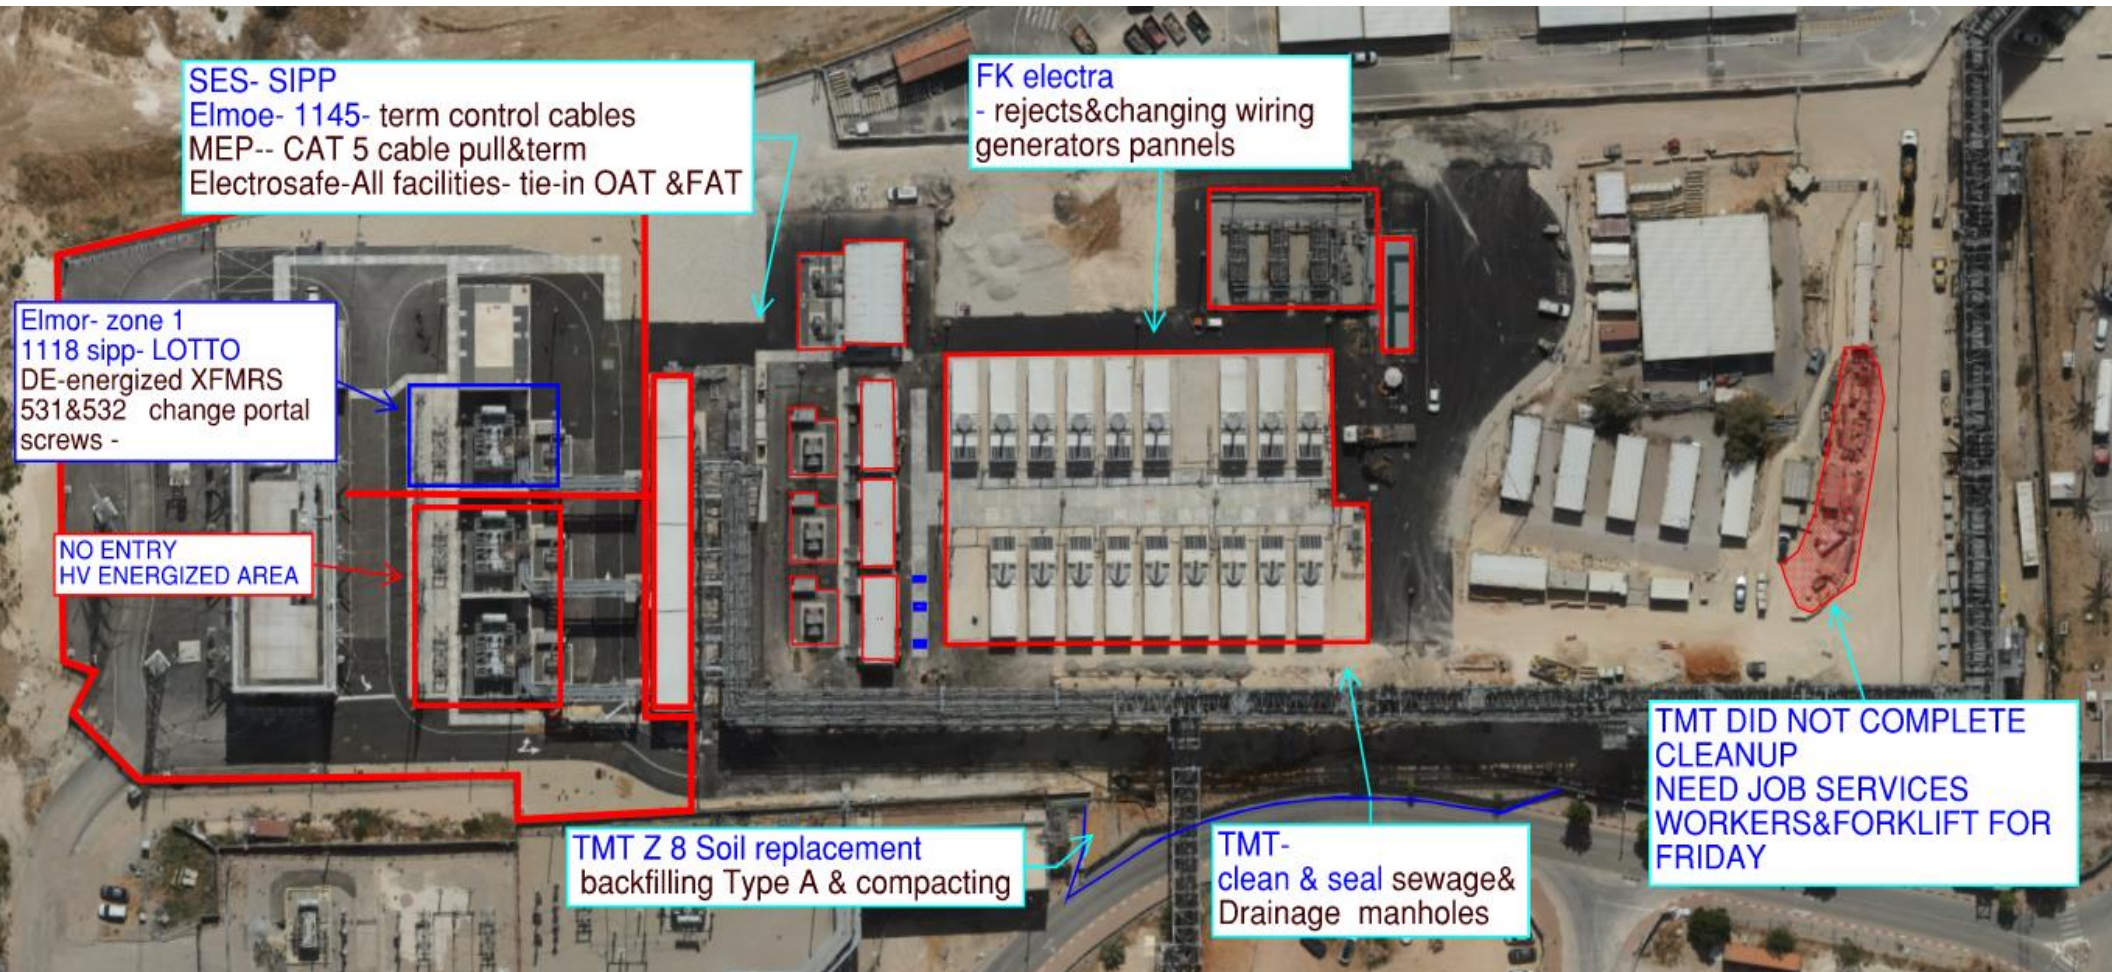


- TMT

EVACUATE MATERIALS
12.9 before noon

-



September 8th 7:00am to 8:00am.

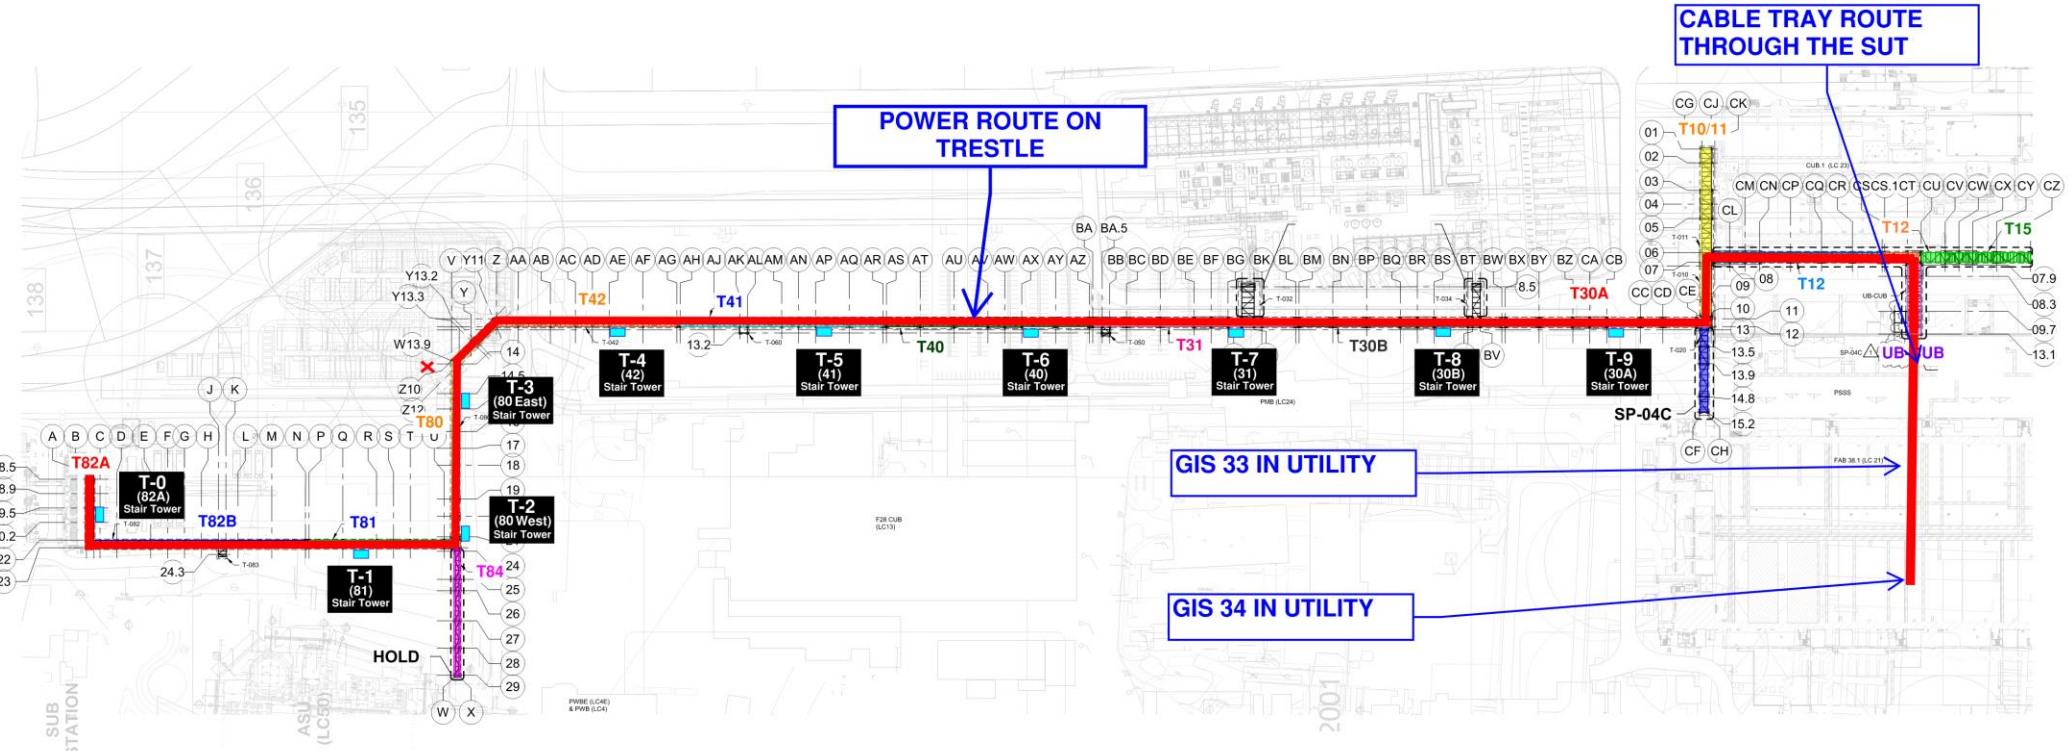






HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

LESICO NG - AIR FLUSHING WED. SEPT. 11th 20:00 - 24:00
EXPECT LOUD BURSTS OF AIR DURING FLUSHING PROCESS
SPOTTERS WILL BE ON SITE PROTECTING EXCLUSION ZONE AND CONTROLLING VEHICLE TRAFFIC

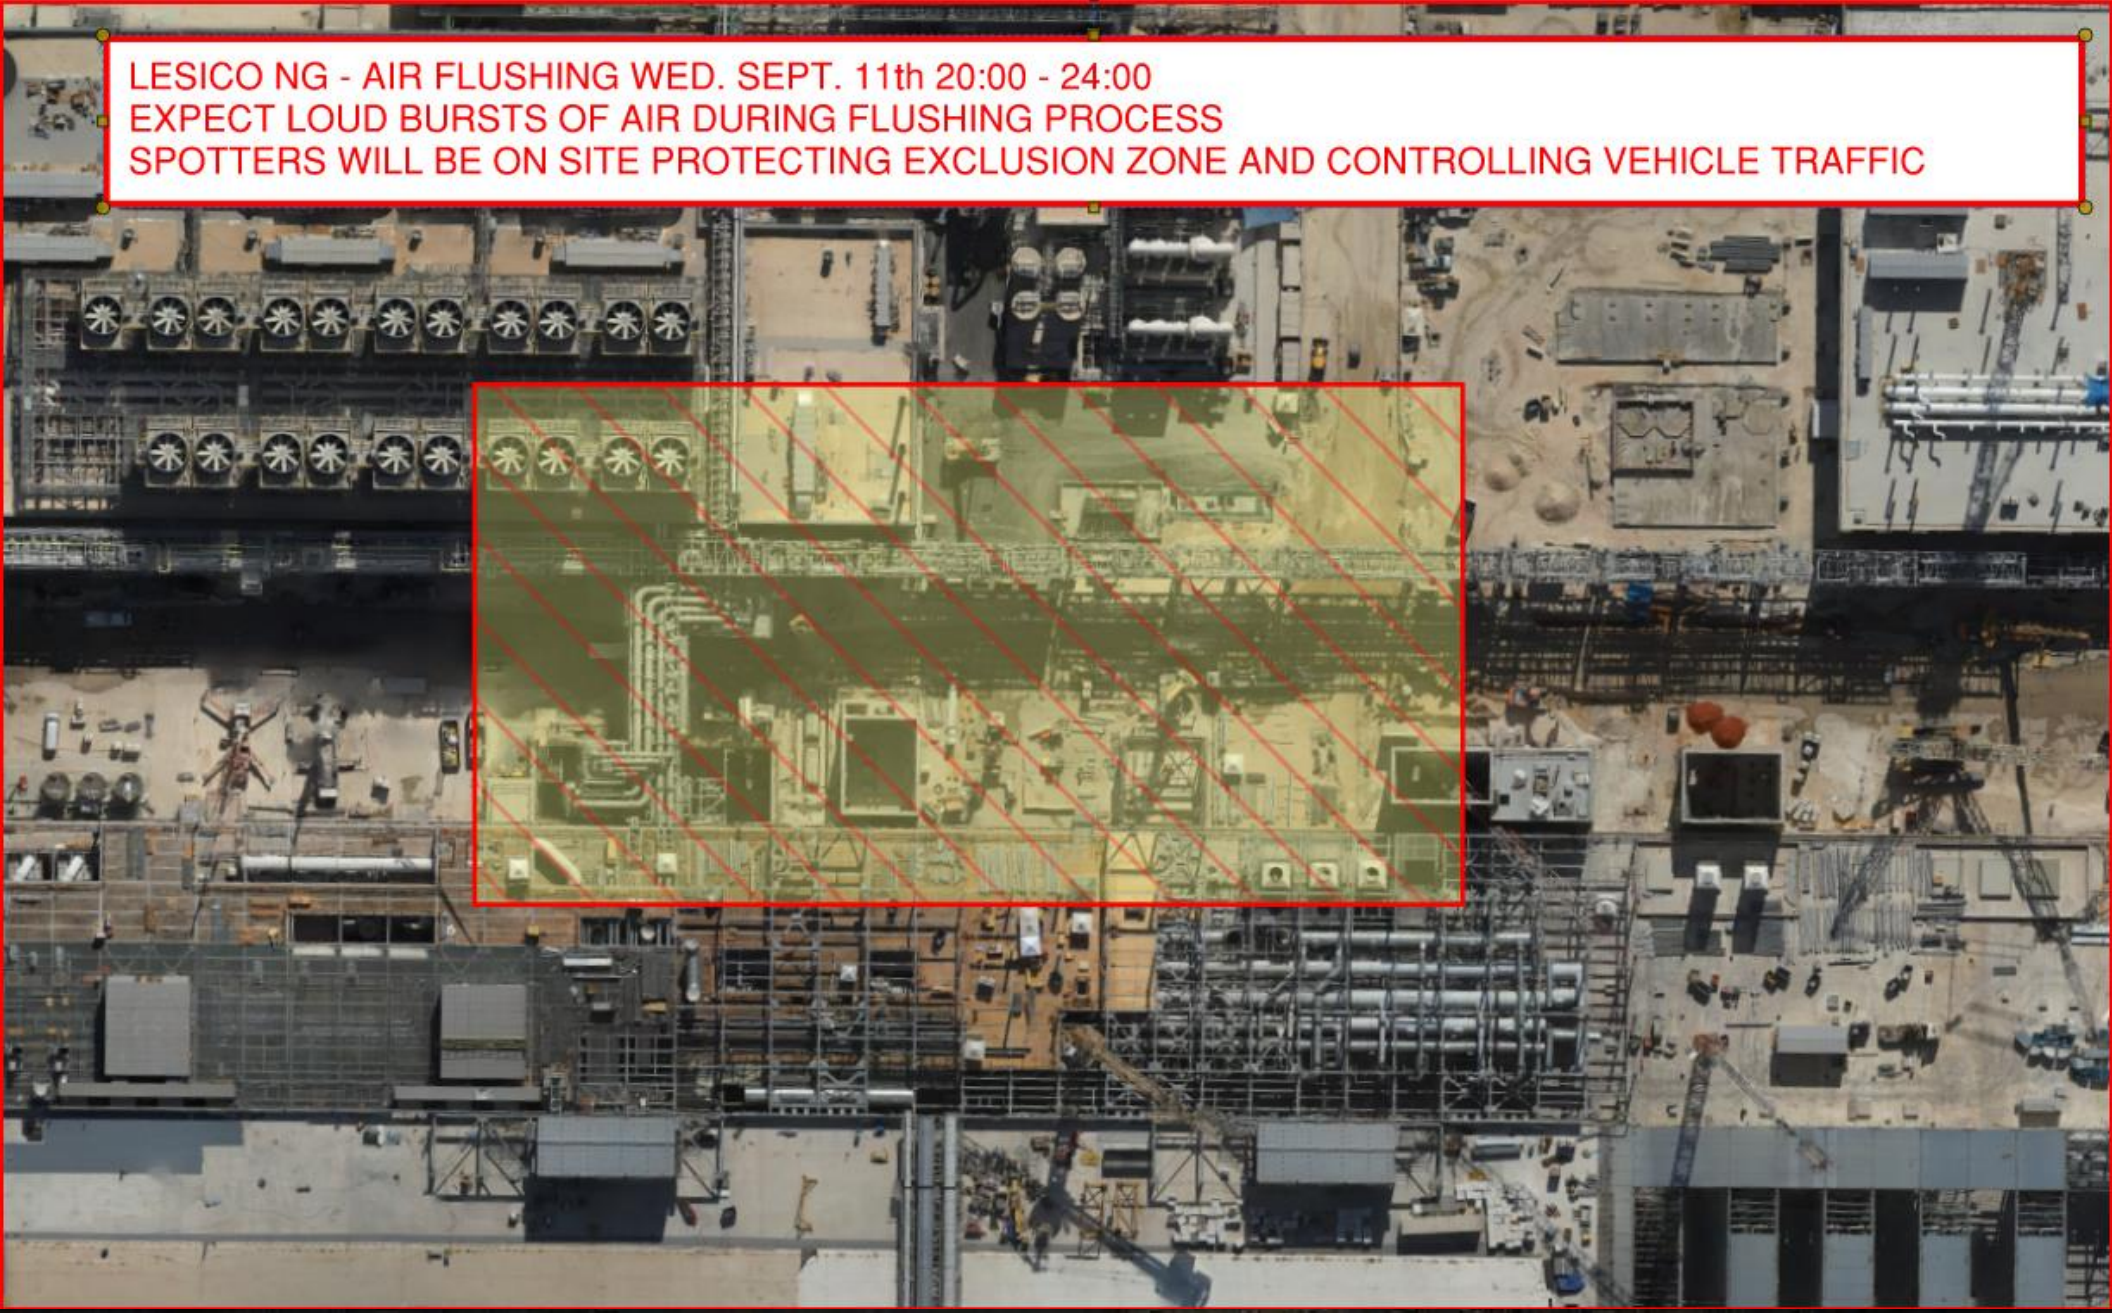




HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

LESICO NG PRESSURE TEST THUR.
SEPT 12th 01:00 - 05:00

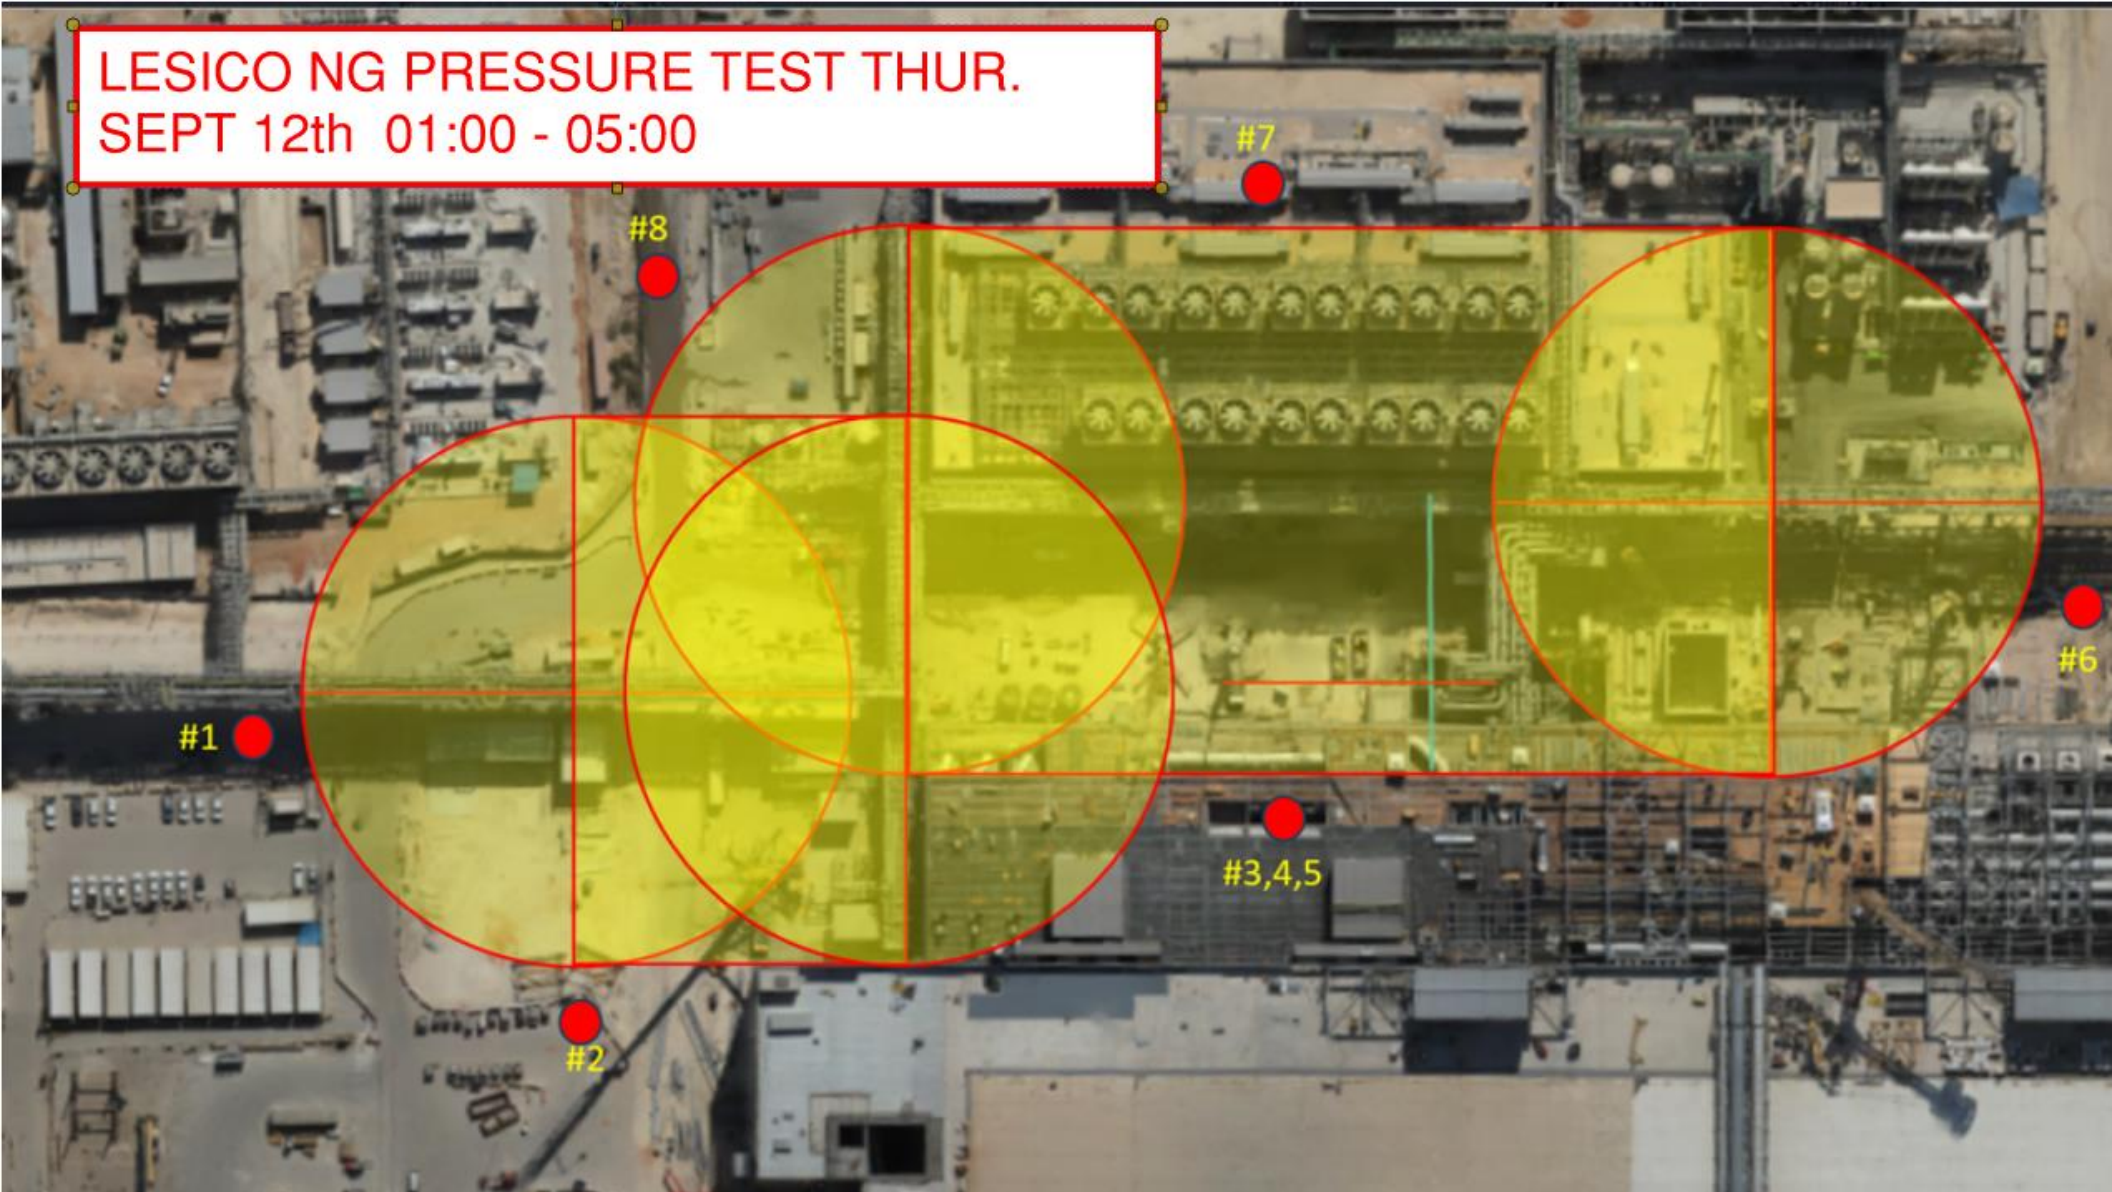

Daily Coordination Meeting


Site Logistics
North Gate B



Daily Coordination Meeting

Site Logistics


North

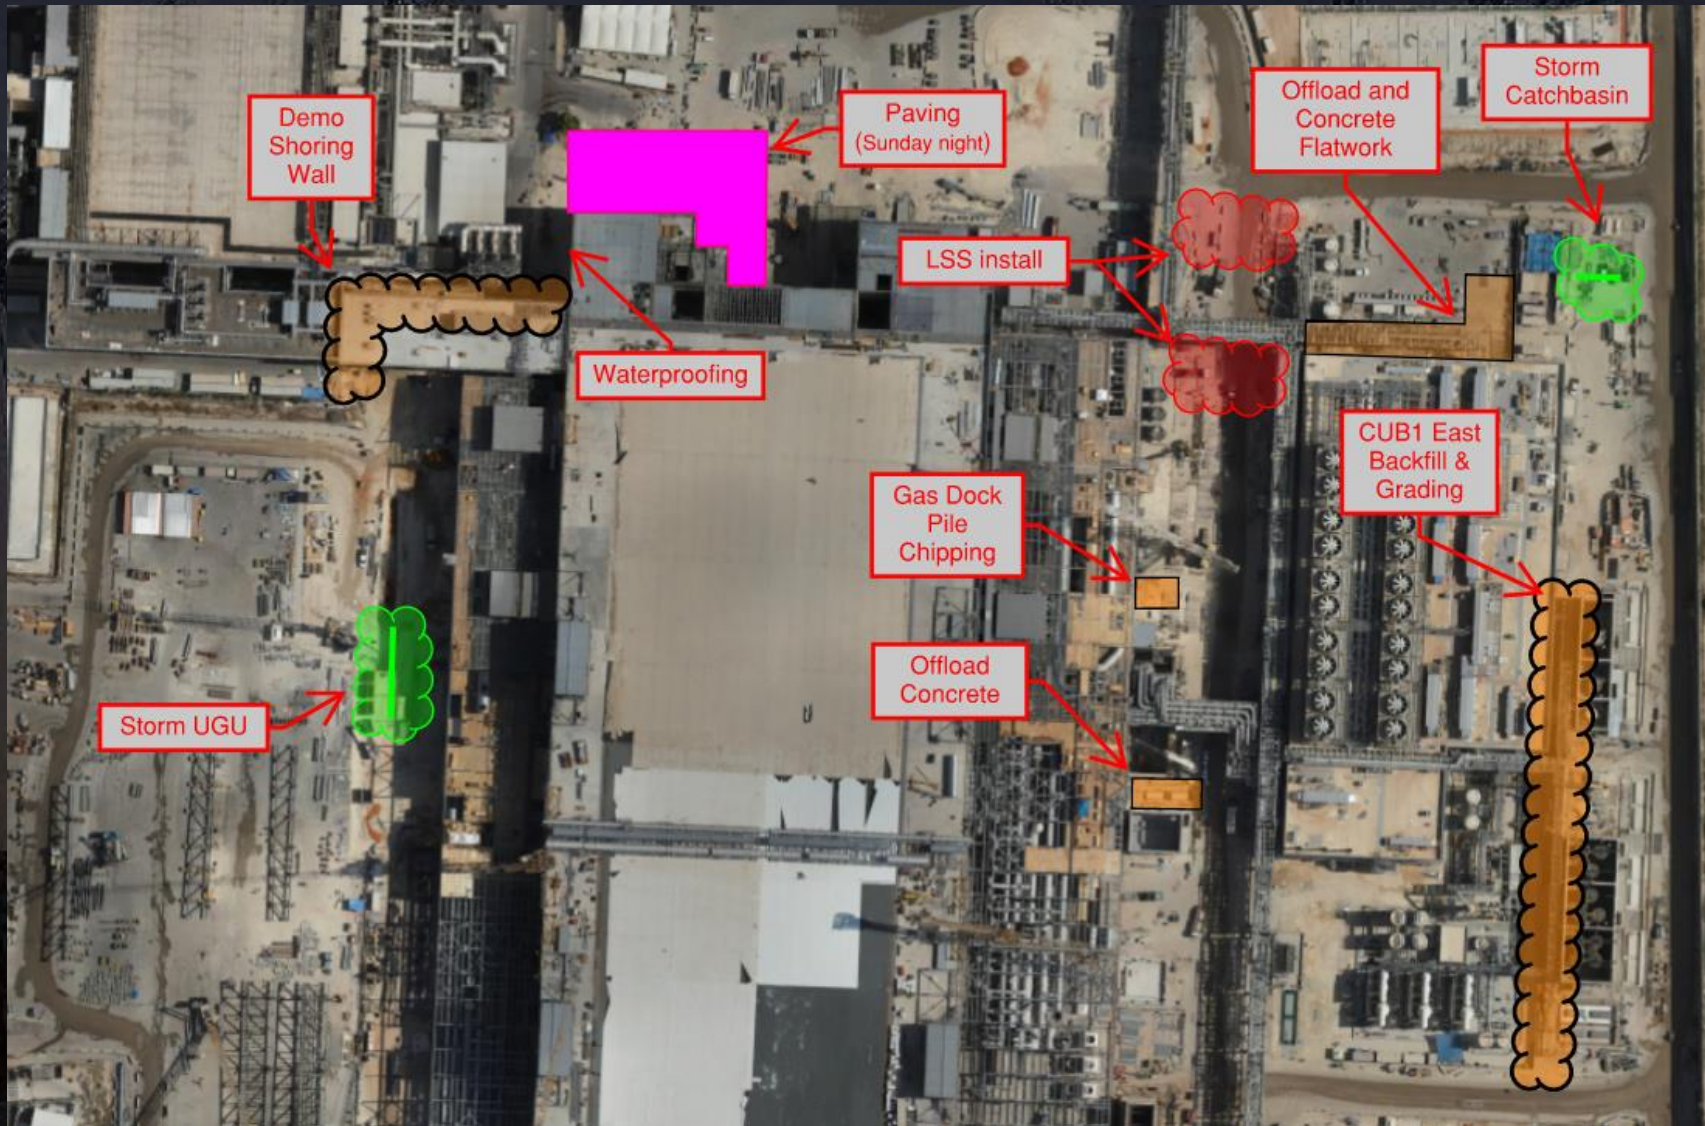

Daily Coordination Meeting

Site Logistics

South

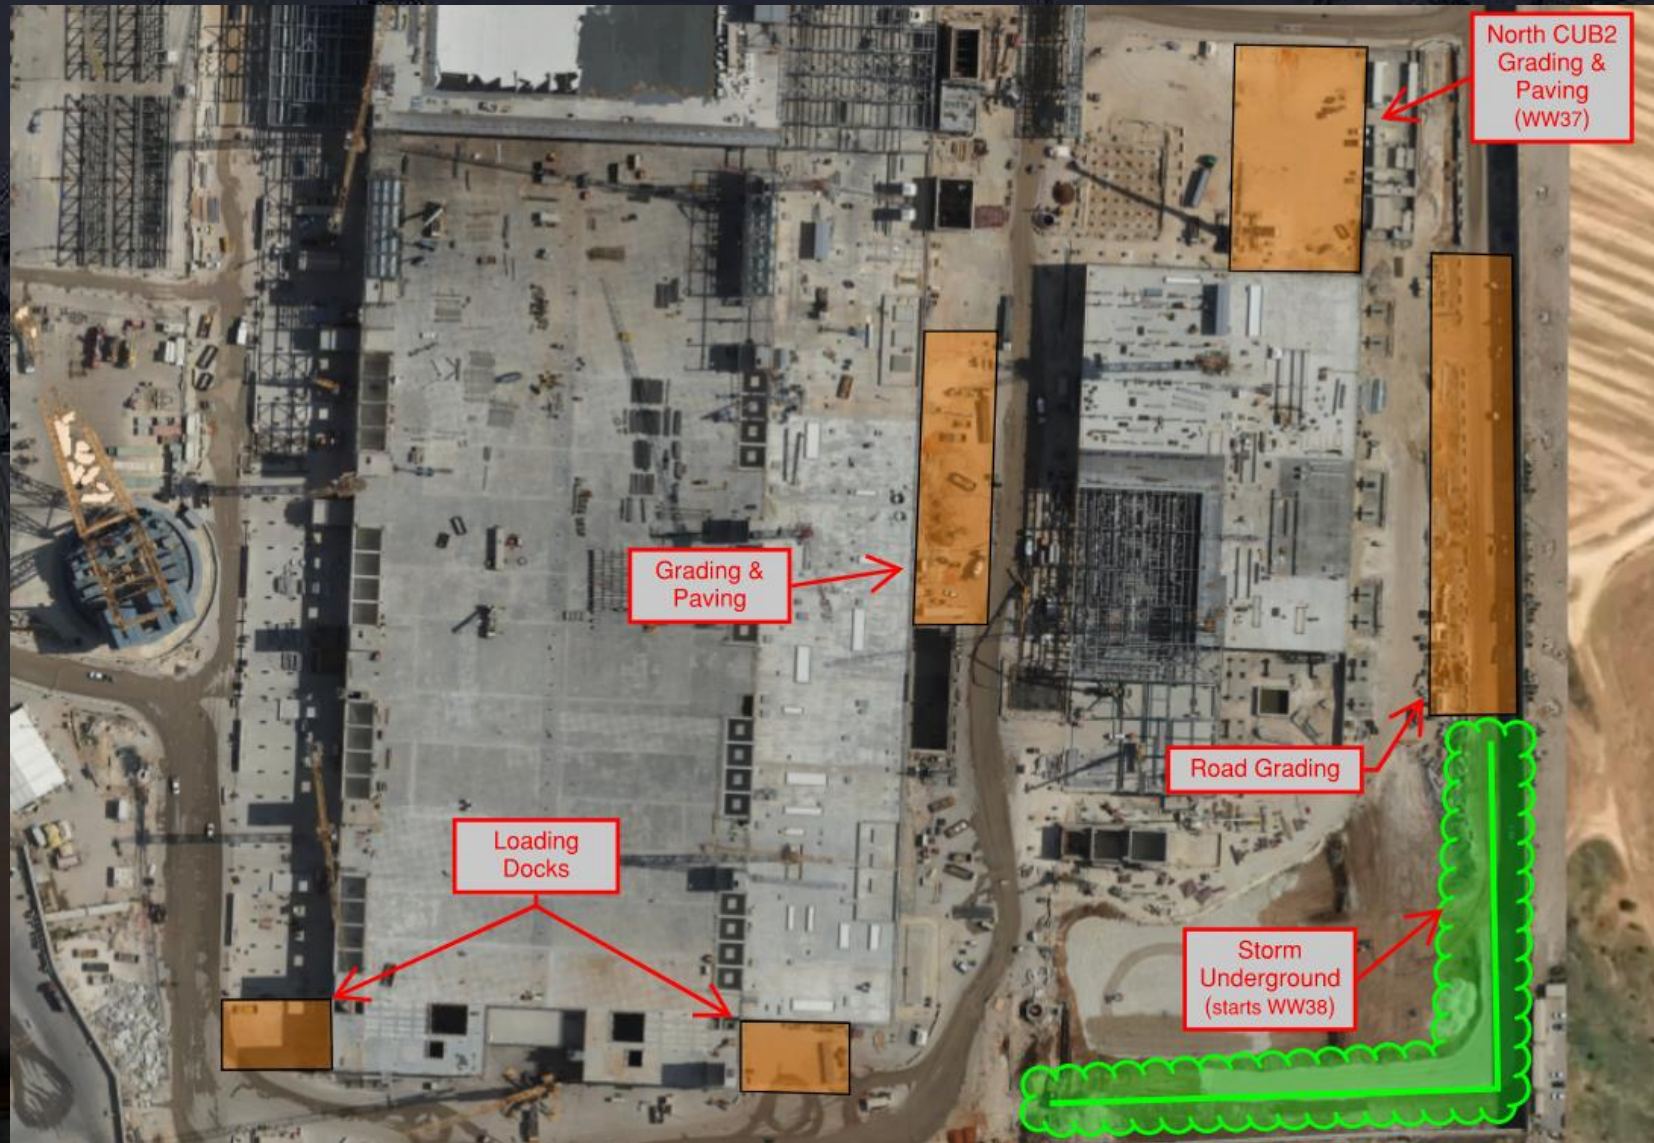

Daily Coordination Meeting

Site Logistics

Cleanup: Subcontractor shall always keep the project free from the accumulation of waste materials caused by its employees, Subcontractor's employees, or Work on the project. Subcontractor shall continually and thoroughly cleanup and remove from jobsite, at its sole expense, all waste, debris, surplus equipment and surplus materials resulting from Subcontractor's operations. If Subcontractor fails to clean up such waste, debris, surplus materials and surplus equipment, such clean up and removal will be done by others and costs for this work will be deducted from the Subcontract by Contractor.

AREA IN ORANGE = NEY CLEANUP WHICH ALSO INCLUDES THE TRESTLE FRIDAY, 13-September-2024

***BACKCHARGES WILL BE SENT TO AFFECTED SUBCONTRACTORS, COST FOR EMPTY PALLETS AND WOOD WILL BE DIVIDED AMONG ALL SUBCONTRACTORS IN THE AREA.**

***ROPE AROUND MATERIAL DOES NOT MAKE IT ACCEPTABLE TO STORE ITEMS FOR MORE THAN 3 DAYS**



TRESTLE

NEY

Communication- Overdo It

- Still encountering people in the field- managers, team leaders, EHS personnel, and workers that are claiming that nobody has told them of basic expectations on site.
- If you are in this meeting, you have a duty to share what you are told here with the rest of your team and helping to ensure that the information gets to your workers.
- Some basics encountered today:
 - Workers performing work need to have access to the plans they're supposed to follow.
 - Fall protection plans are required when working outside of MEWPs and wearing a harness.
 - No driving on the GUT road- for deliveries only.
 - Chin straps are required when wearing a helmet- even when not working at heights.
 - Gloves and glasses are required to be worn when not in a PPE free area.
 - Red rope cannot be left up when the hazard is no longer present.
 - All buggies require a sticker.

Heat Index- September 15th

	temperature (°F)															
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
50	81	83	85	88	91		99	103	108	113	118	124	131	137		
55	81	84	86	89	93	97	101	106	112	117	124	130	137			
60	82	84	88	91	95	100	105	110	116	123	129	137				
65	82	85	89	93	98	103	108	114	121	128	136					
70	83	86	90	95	100	105	112	119	126	134						
75	84	88	92	97	103	109	116	124	132							
80	84	89	94	100	106	113	121	129								
85	85	90	96	102	110	117	126	135								
90	86	91	98	105	113	122	131									
95	86	93	100	108	117	127										
100	87	95	103	112	121	132										

 Caution

 Extreme Caution

 Danger

 Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

HCC/EHS Weekend Work- 13.09.2024

White Board Meeting in Beavers at 06:30

Superintendents

Nir Gueta 054-3324775

CSA CM

Anas Dakkak 052-2328086

Tarek Nairoukh 052-6636782

Vladimir Gotlib 052-4629124

MEP

David McBride 052-5379828

Lara Salaymeh 052-2410953

James Sweeten 052- 2787165

CX/QA

Patrick Blunt 052-3155787

Cranes

Hadar Shem Tov 054-669-3626

Safety

- Safety Foreman -Waseem Alhozil- 052-358-4978 Waseem-Alhozil@Hoffmancorp.com
- Safety Assistant- Gaber Aloka-050-2238719 Gaber-Aloka@Hoffmancorp.com
- Safety Professional - Hamad Hammoudeh- 051-2405061 Hamad-Hammoudeh@Hoffmancorp.com

Subcontractor Weekend Work- 13.09.2024

FAB

Dvir- FAB at CUB.

manager on site-Daniel Bitton 052-312-8268

EHS Manager-Guy Ishbit 054-491-5407

Utility Level

Lesico : ilya0543369795

Chemo: stav 0547175157

ETC :shady 0523794510

HYG:niv 0524418527

Elram noam 0505213845

Subfab

Afcon – panel install – Avi Eli 052-600-8487

Chemo – Tool Tower – Tomi – 052-375-9408

HYG – Stair 6 – Saleh – 050-777-3119

WW – Elev. 1 – Teddy – 052-239-2473

Sela – 17 line – Yoav – 054-807-6339

Clean Room

- Afcon – CR – 1W,2E, 2W, INT- 2E,1W, 3E, 3W ,LINK Rack install (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Chemo – INT -4E+5E 10” pipe install +racks 1W-1E (EHS Lila - 0547886704, Supervisor Winai – 0528090588)
- W&W 17-18 Line added the beams 24 line – catwalks, NTTE, NTTW 5RA decking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- Talad – CR 1W – Drilling holes, 1 metal lids removal (EHS Guy 0544915407, Super Igor 0544509386)
- Sig – 5W INT Platforms MIMO CB-CC/25 (EHS Beni 0506232032, Super Nodar 0546313261)
- Sela – 1W CRC (EHS Sergey 0526650046, Super Yoav 0548076339)
- Elram – CR Level 9,25 line, AA line 2W shafts walls INT level 9,10,17,24 column wrap (EHS Royi 0538312234, Super Roni 0507196939)

Subcontractor Weekend Work- 13.09.2024

PSSS

- Pach Taas – Module bolting PSSS Roof and Lift 2
- Foreman – Vadim – 052-6229005
- Safety – Offek – 050-7838486
- Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- W&W – SEQ 132, 137
- Foreman – Willie – 052-6145521
- Safety – Gary Lambert – 1-405-833-8910

WJG

W&W – Steel Erection 4J, Hot work – Road, 4J/5J lift 2
Foreman: Chris Isaac 052 588 3215
Safety: Moshe 054 801 2959

Afcon – 2J Lift 2, 4J UL Cable Tray
Foreman: Sarat 055 274 0190
Safety: Pradeep 055 274 2935

Pach Taas: 1J UL, 2J Lift 2 Module Bolting
Foreman: Nuriel 054 901 2343
Safety:

Chemo: 5J Lift 2 Piping
Foreman: Sergey 054 465 9688
Safety: Lilach 054 788 6704

Siding

SN

Victor- 0549220163
Liran- 052-8939558
Ranpro- Roofing- FAB
Alen- 054-9265809
Tal- 054-8313469

Subcontractor Weekend Work- 13.09.2024

CUB

Sami Najami CUB 2:
Husein - 0526917461
Alon - 0509895008

Chemo Aharon:
Dudu - 0509808846
Leonid - 0548883878

Flushing 111,115,116,117,126
13/09
Day: Yothanasak - 0523911674
Night: Praphun - 0528093774
14/09
Day: Yothanasak - 0523911674
Night: Sathit - 0528103789

Overall: EK - 0523623552

ETC south yard:
Yosef - 0506708990
Shlomi - 0528235757

Trestle

SNJSUTSTEEL
UB CUB Pipe Insulation
FORMANBASHIR YONES – tel. 05273649963
SAFETY TRESTLE Alon Matan – tel. +972 50-989-5008

Site

- **Derech Afar** – West storm UGU
Supervision = Raed: 054-2442030
EHS = Alex: 054-5403849
- **Elmor** – Electrical (south CUB1 yard)
Supervision = Fhami: 054-5707735
EHS = Matanya: 052-5108711
- **Olizki** – Sweepers and water trucks, Truck offload 12 (north CUB1 yard)
Supervision = Fhami: 054-5707735
EHS = Matinya: 052-4033565
- **TM Team** – LSS underground (GUT road)
Supervision = Rafi: 050-8723363

GIS/NEY

TMT- Tomorrow
Foereman/PM- Ido Daus.050 8662620
Safety- Sharon Elimelech/ Nitzan shimoni.054 8159504

1. Manholes water stand test.
2. Chipping of rock in the DW line edge. For installation of 2 valves.

Daily Coordination Meeting



14:00 Sign In
