

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:





TC3 pour back
UL
3:00am

Truck off load #14
5:00 am

BIPA Plinths
6:00 am

SUT1 Strainer
pads
6:30 am

SETD Curb
7:00 am

Link ramp
7:30 am

SUT1 Strainer pads
6:30 am

TC3 pour back UL
3:00 am

Truck off load #14
5:00 am

BIPA Plinths
6:00 am

SETD Curb
7:00 am

Link ramp
7:30 am

אינטל קרית גת




TRUSS SET
9W
Tomorrow
Start 4:00am

TRUSS SET
9W
Tomorrow
Start 4:00am



UTILITY LEVEL MOD1

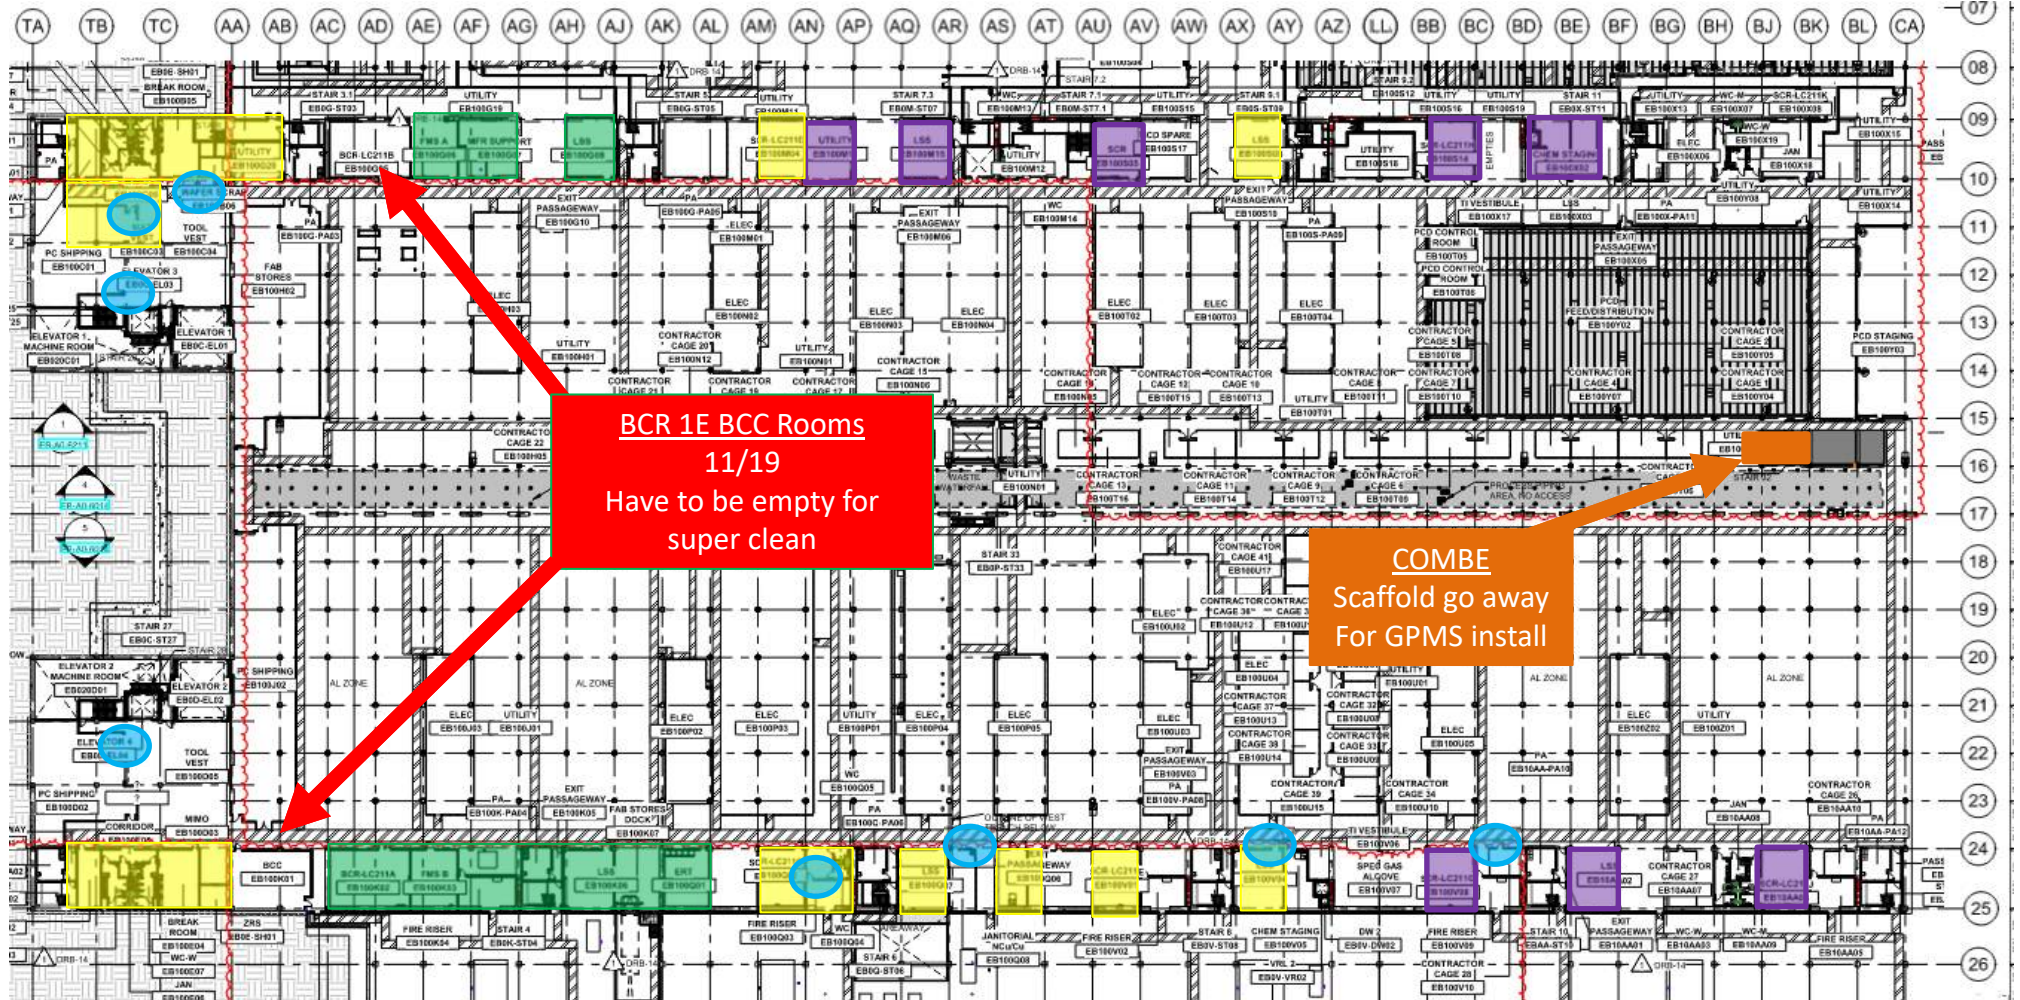


BELFOR
Mold remediation


ELRAM
Drywall install

MEP+Electrical
Ready for re-install


UTILITY LEVEL MOD2

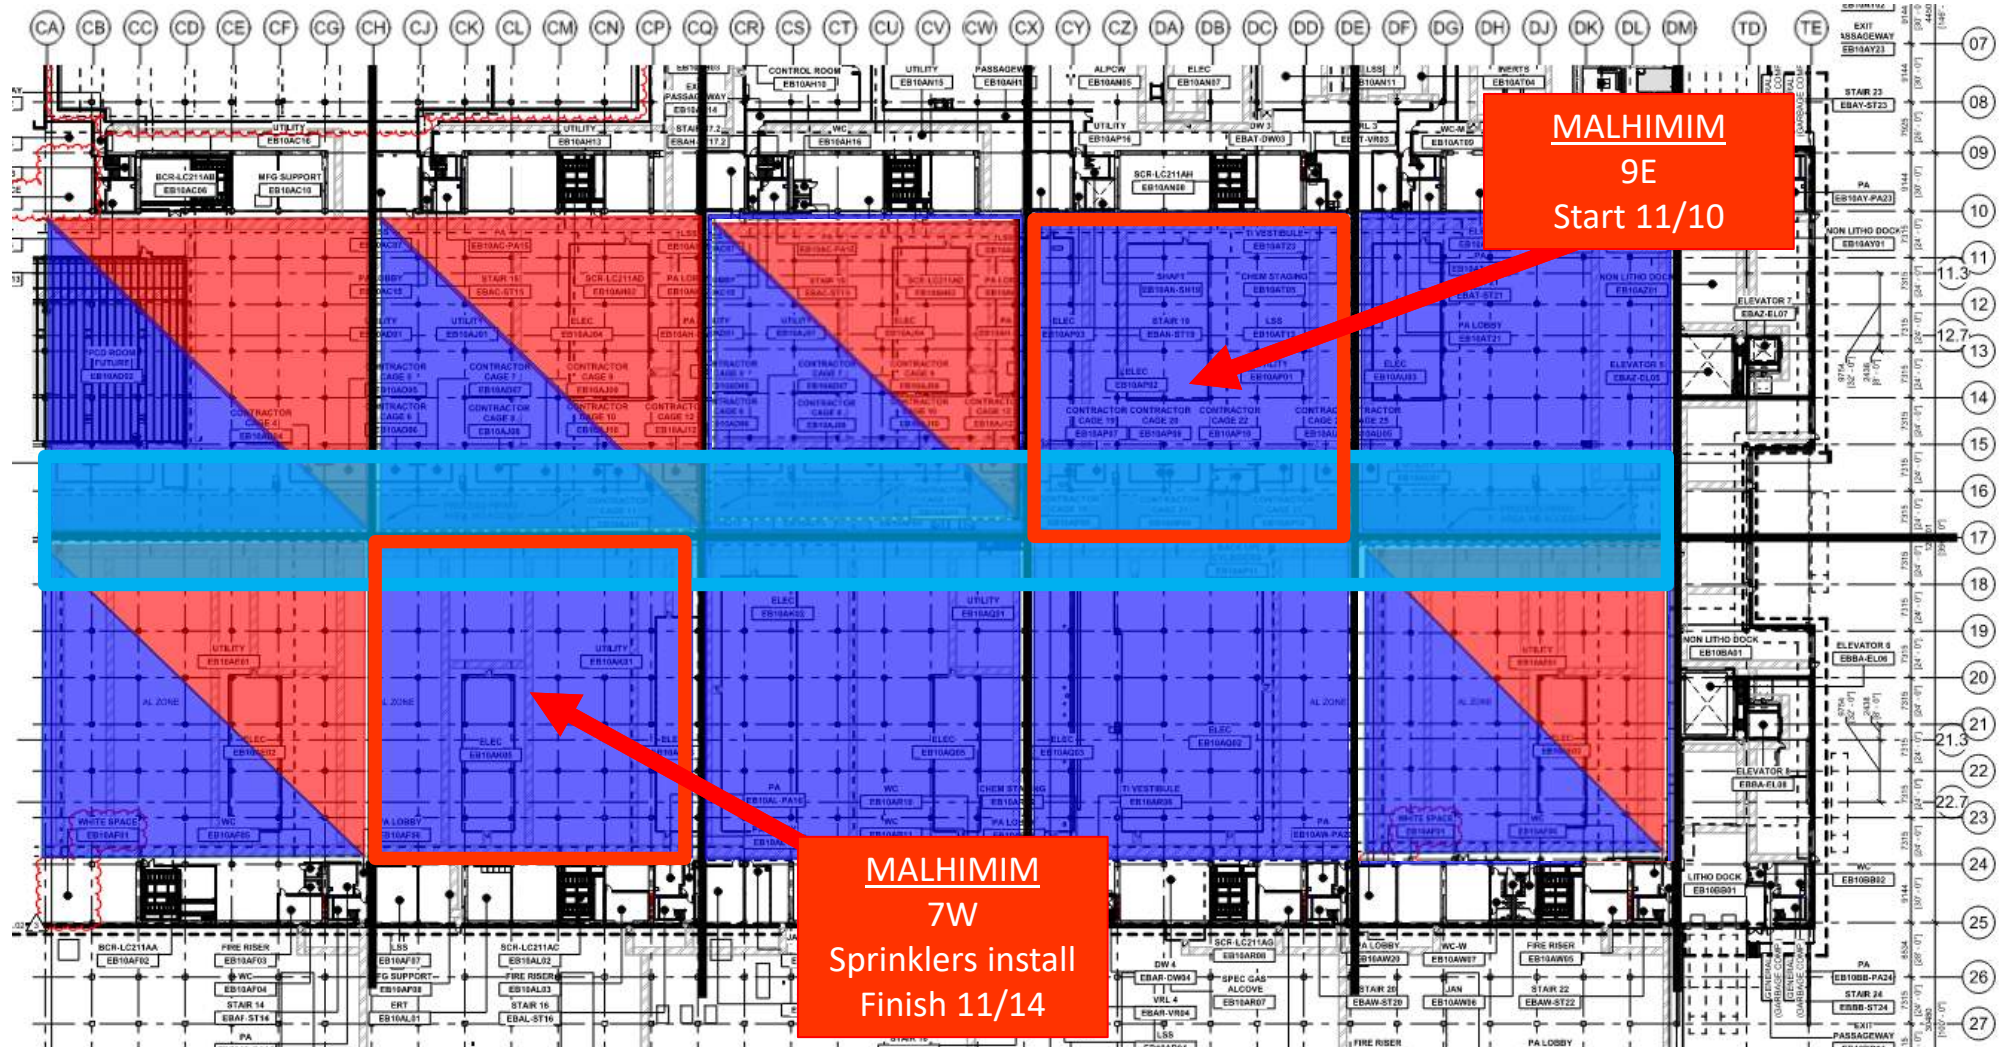


SUT 38.1 LEVEL

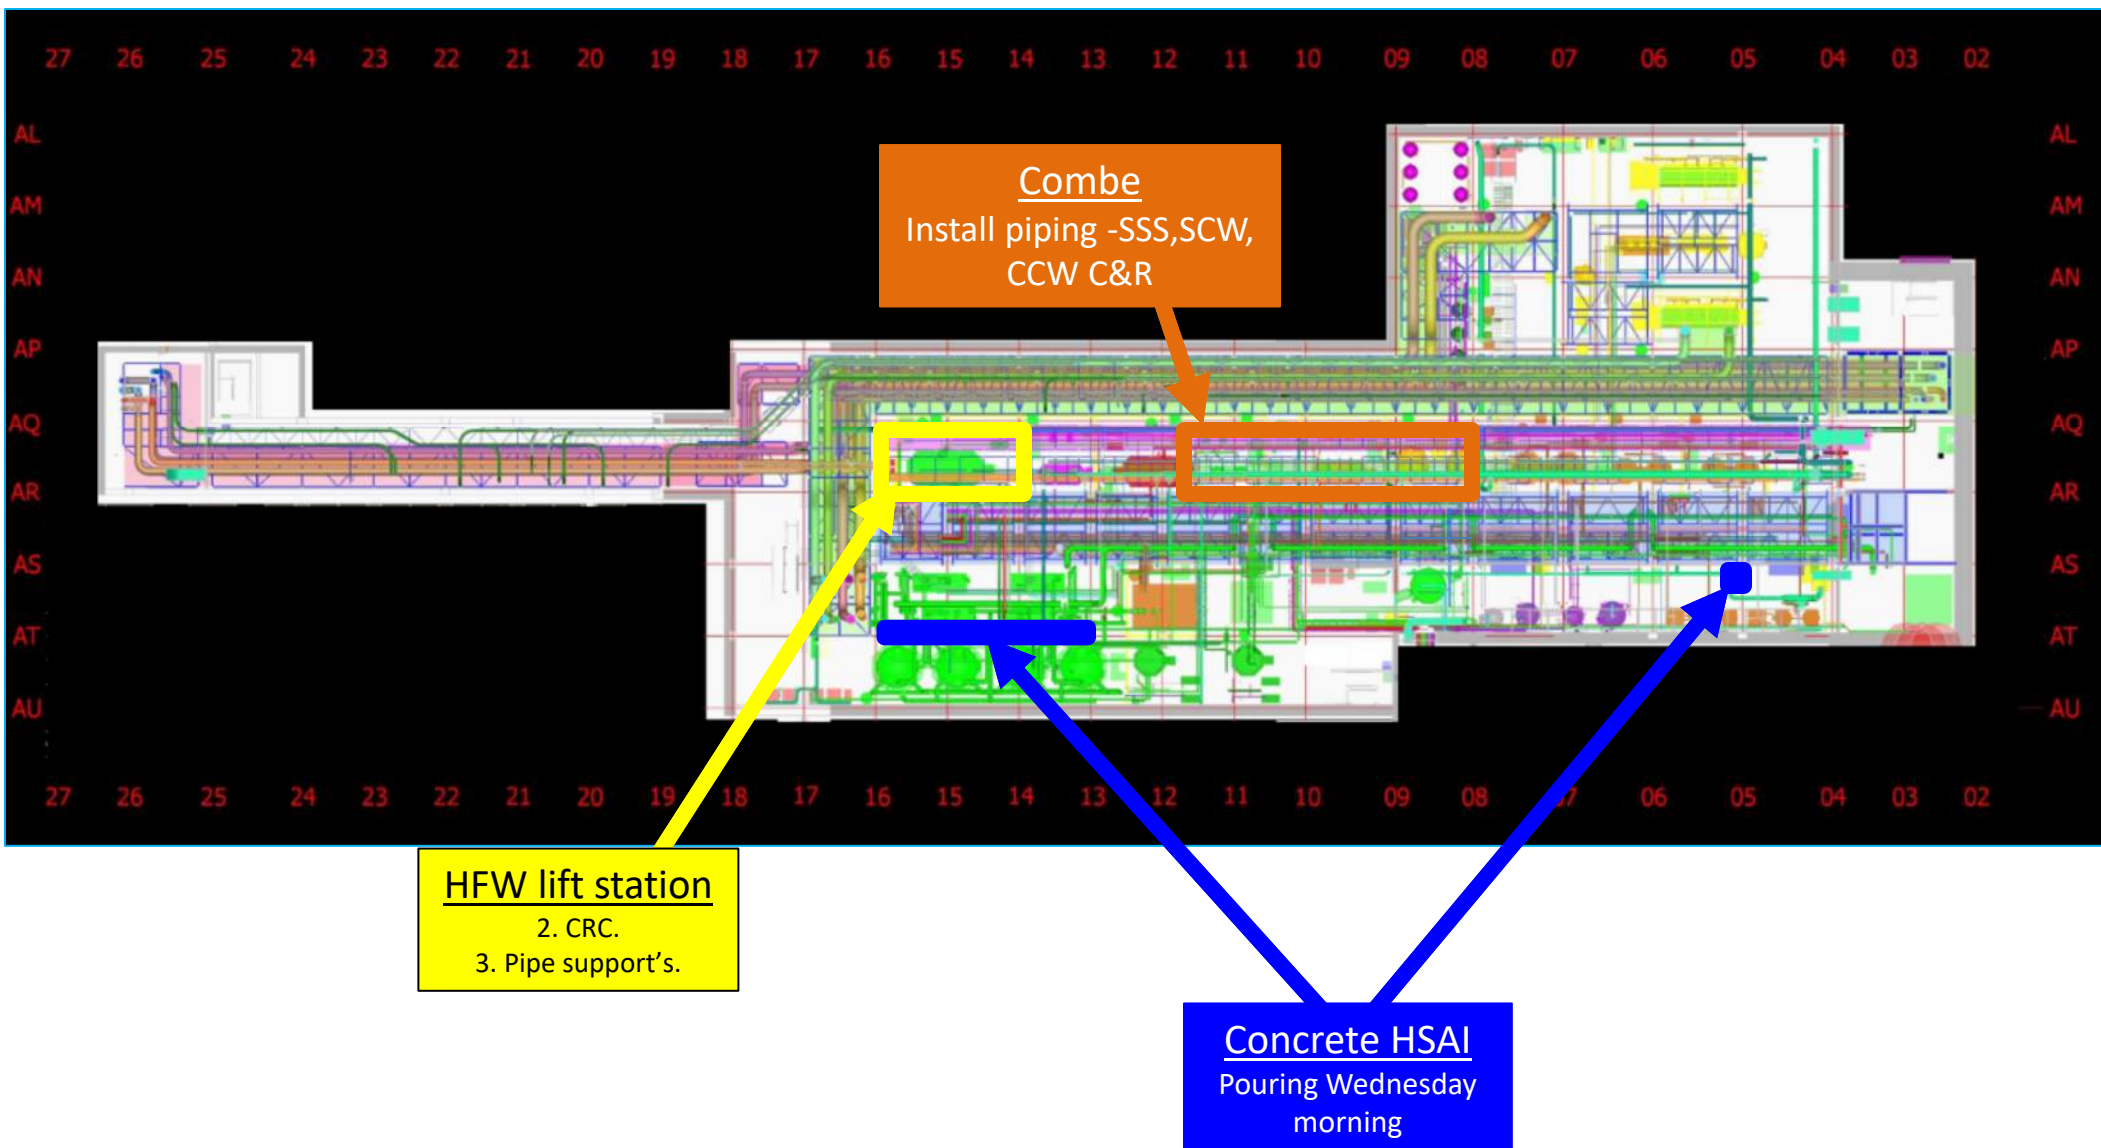


SUT 38.2 LEVEL

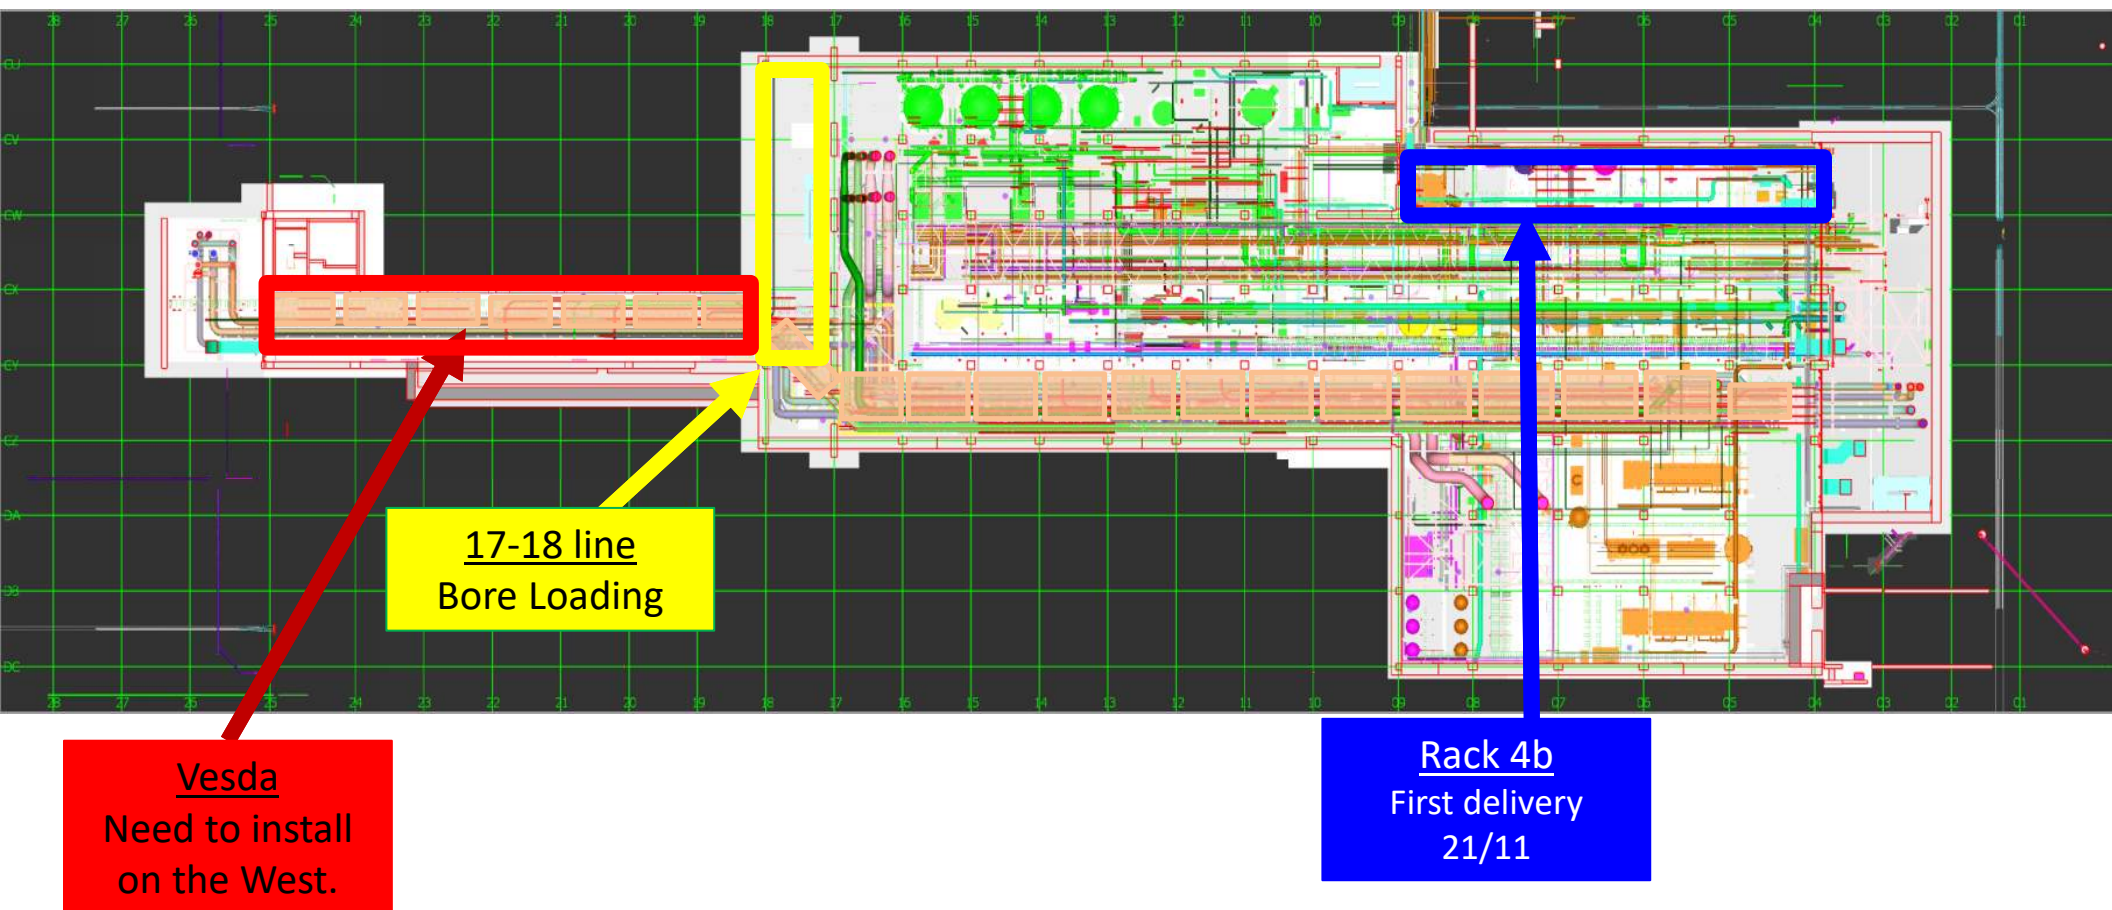


SUBFAB BUILDOUT MOD 1

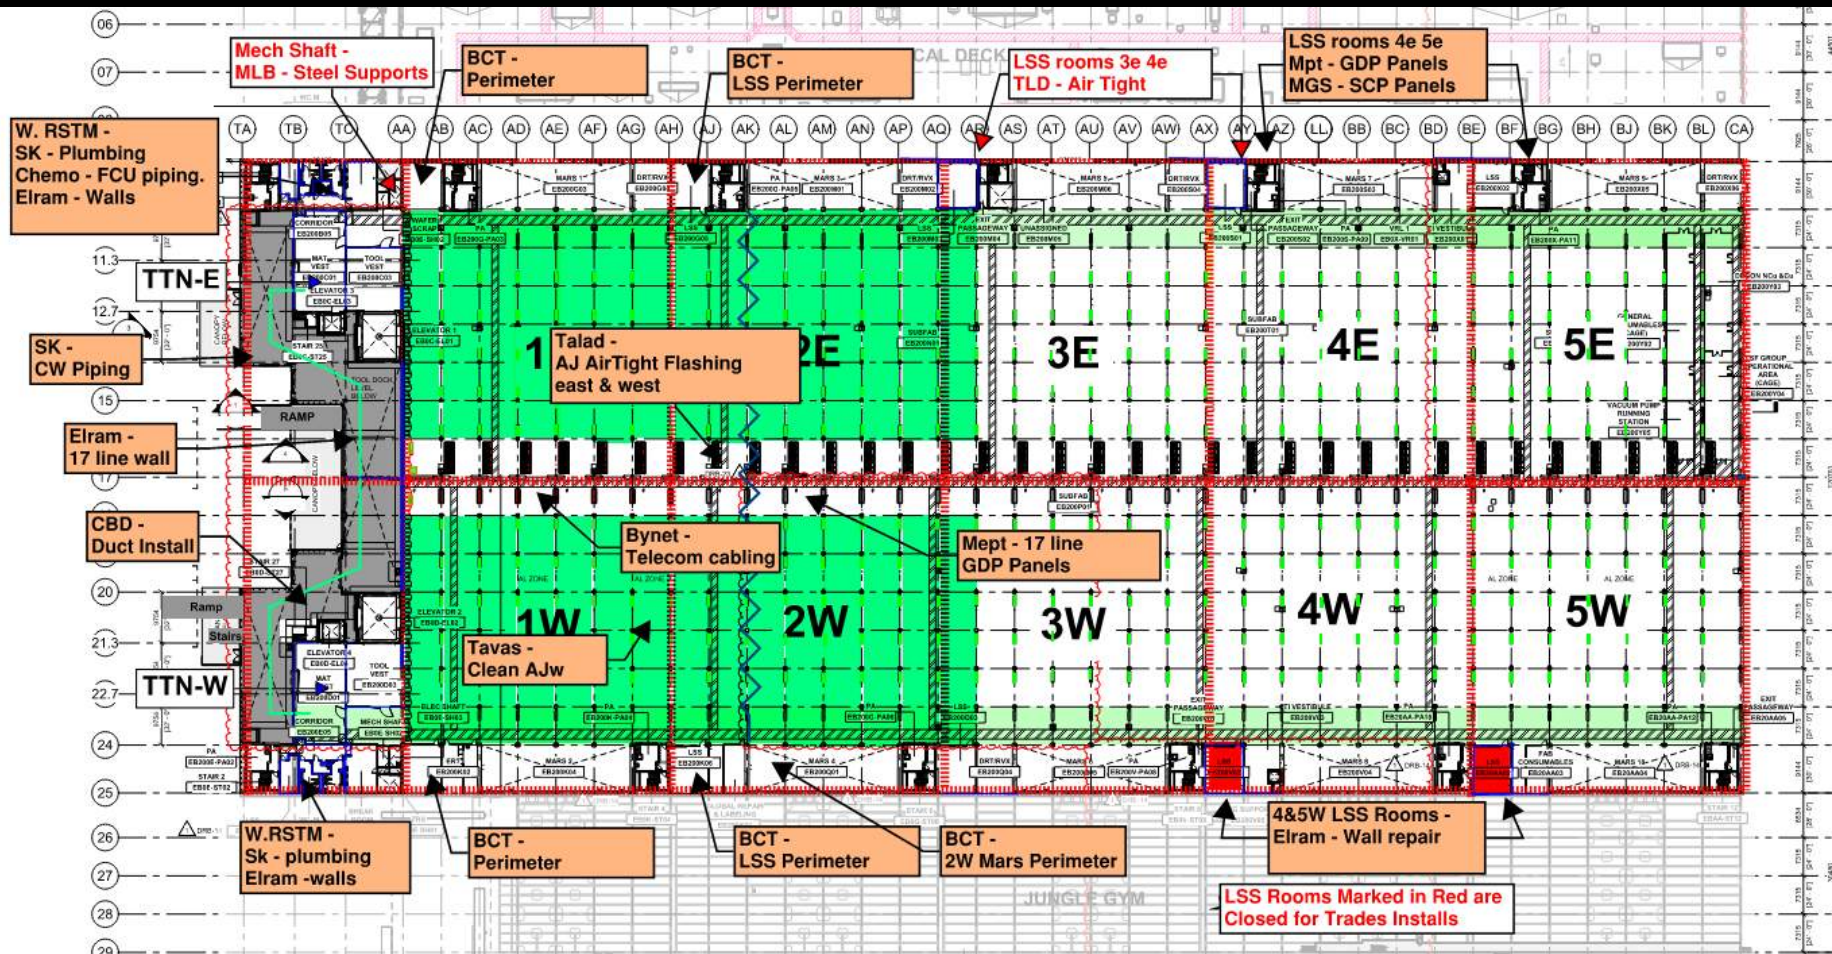


SUBFAB CRC TOPCOAT

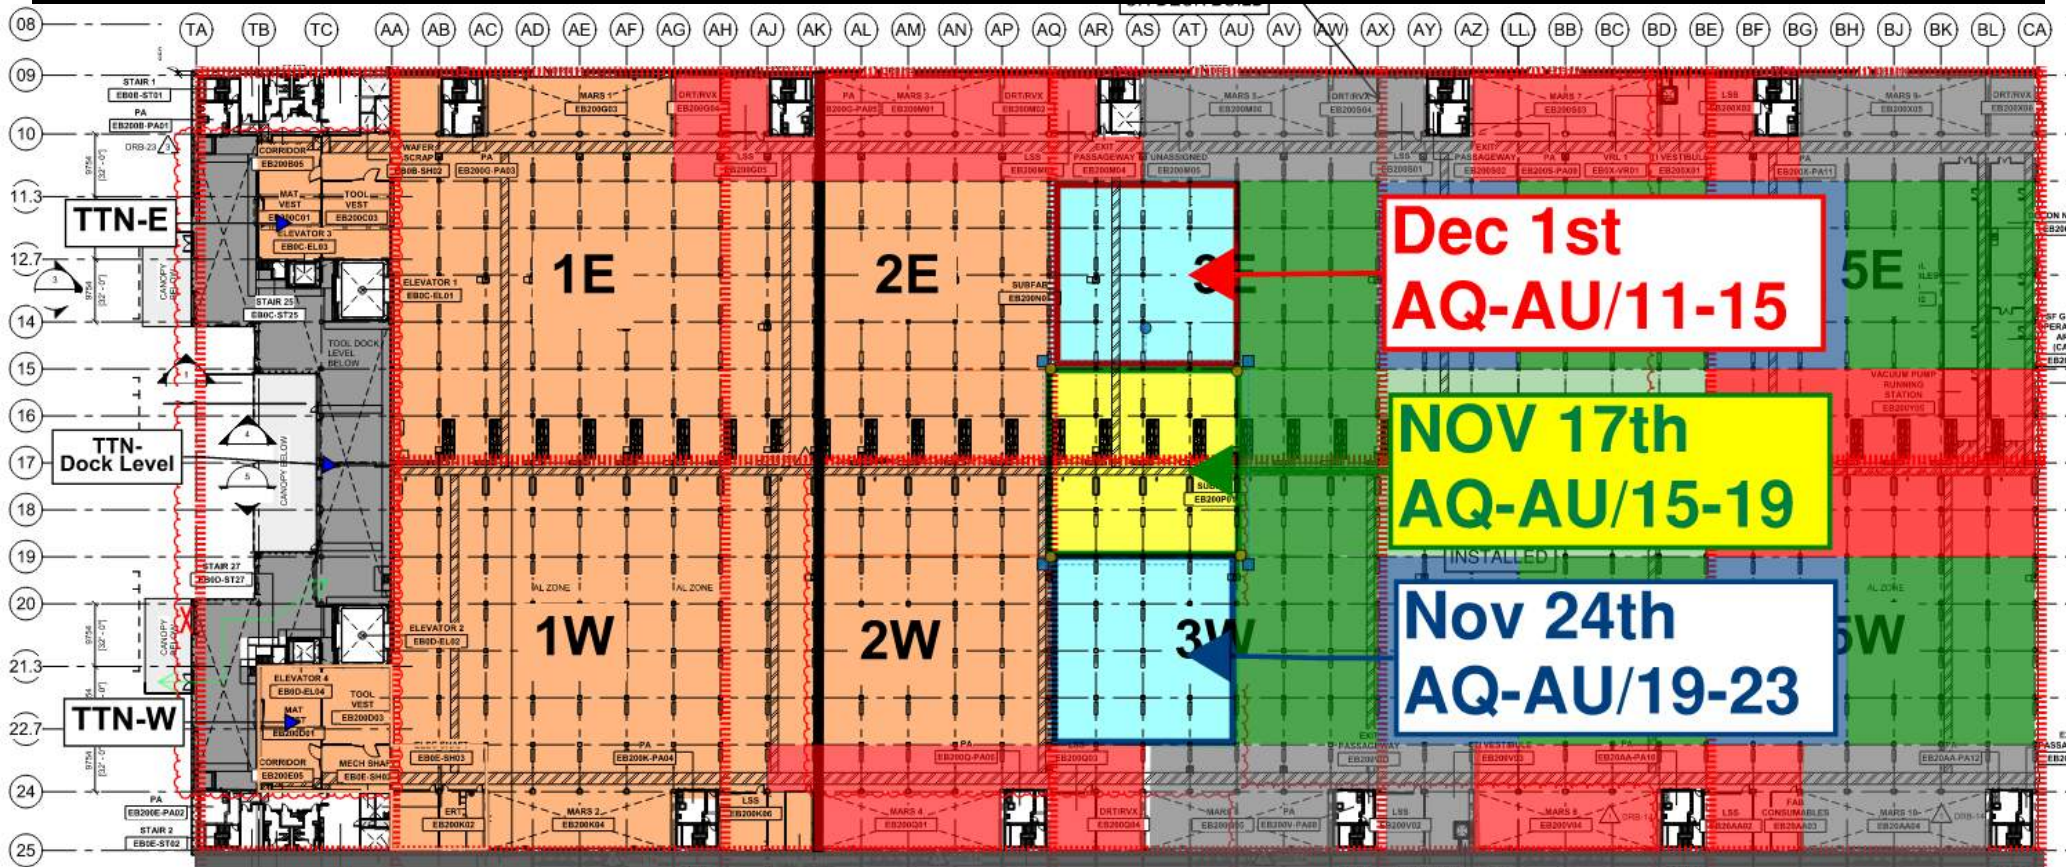


BCT Pressure Test Today

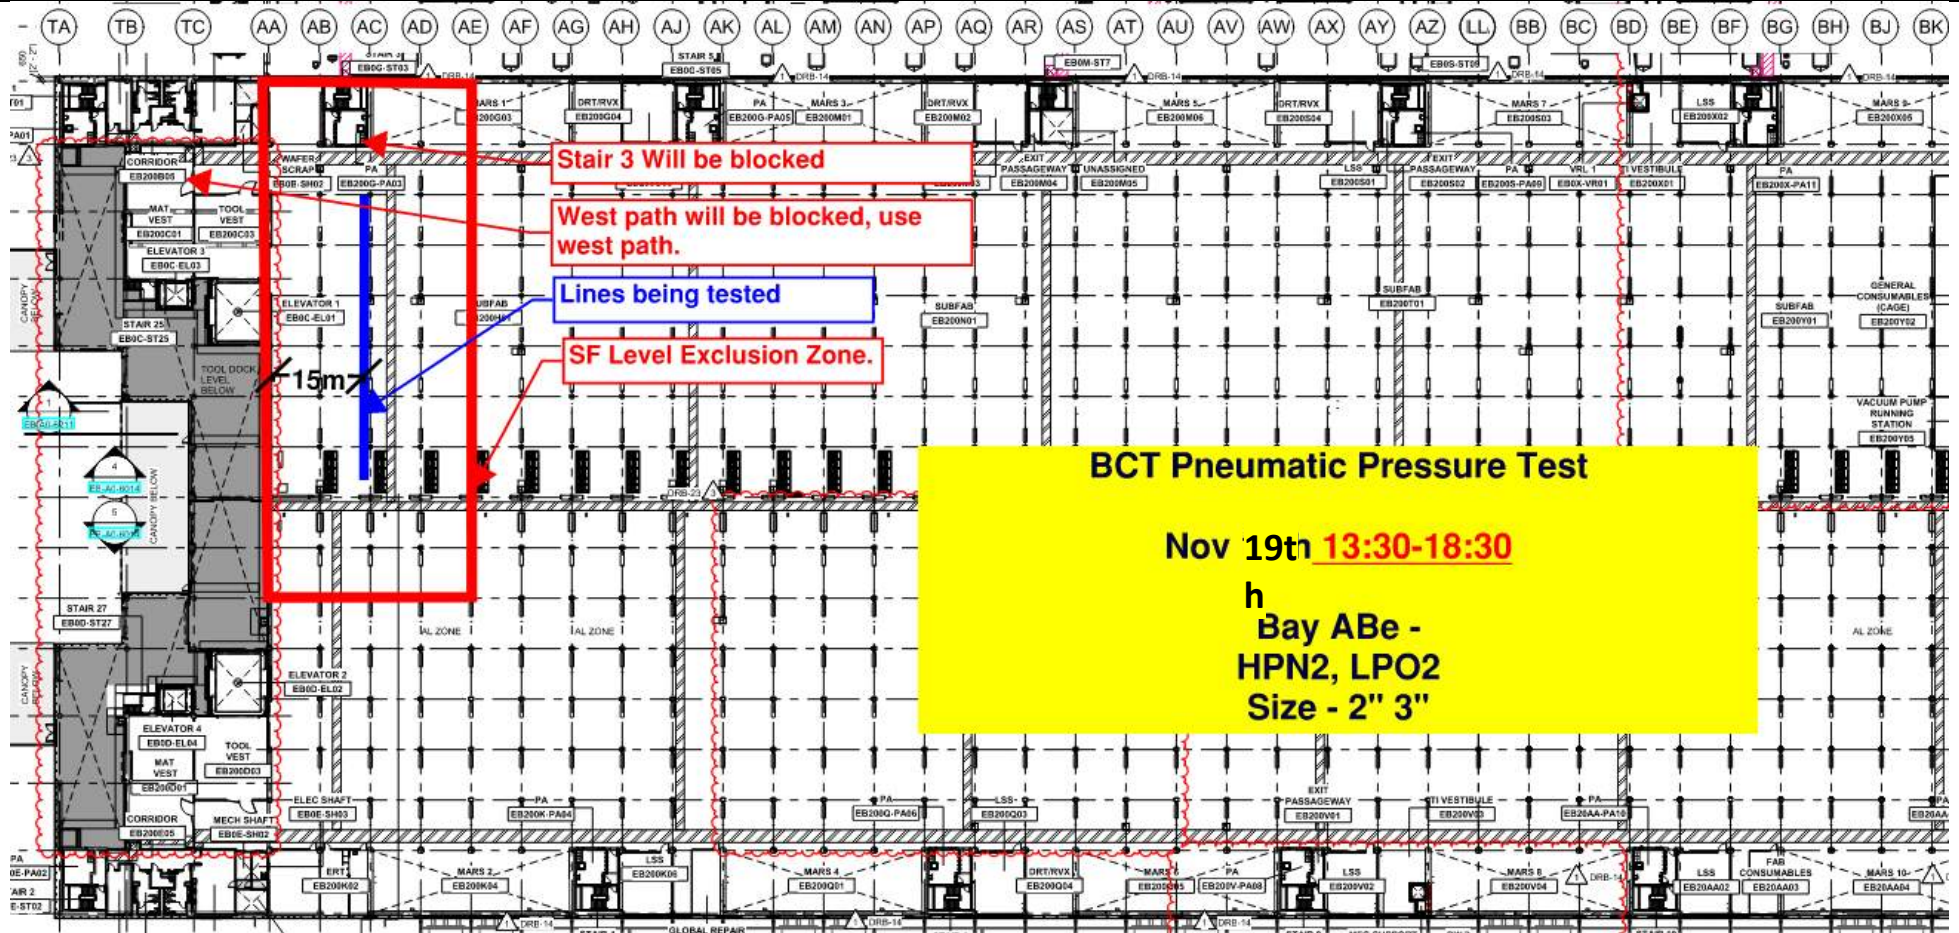



BCT Pressure Test Tomorrow

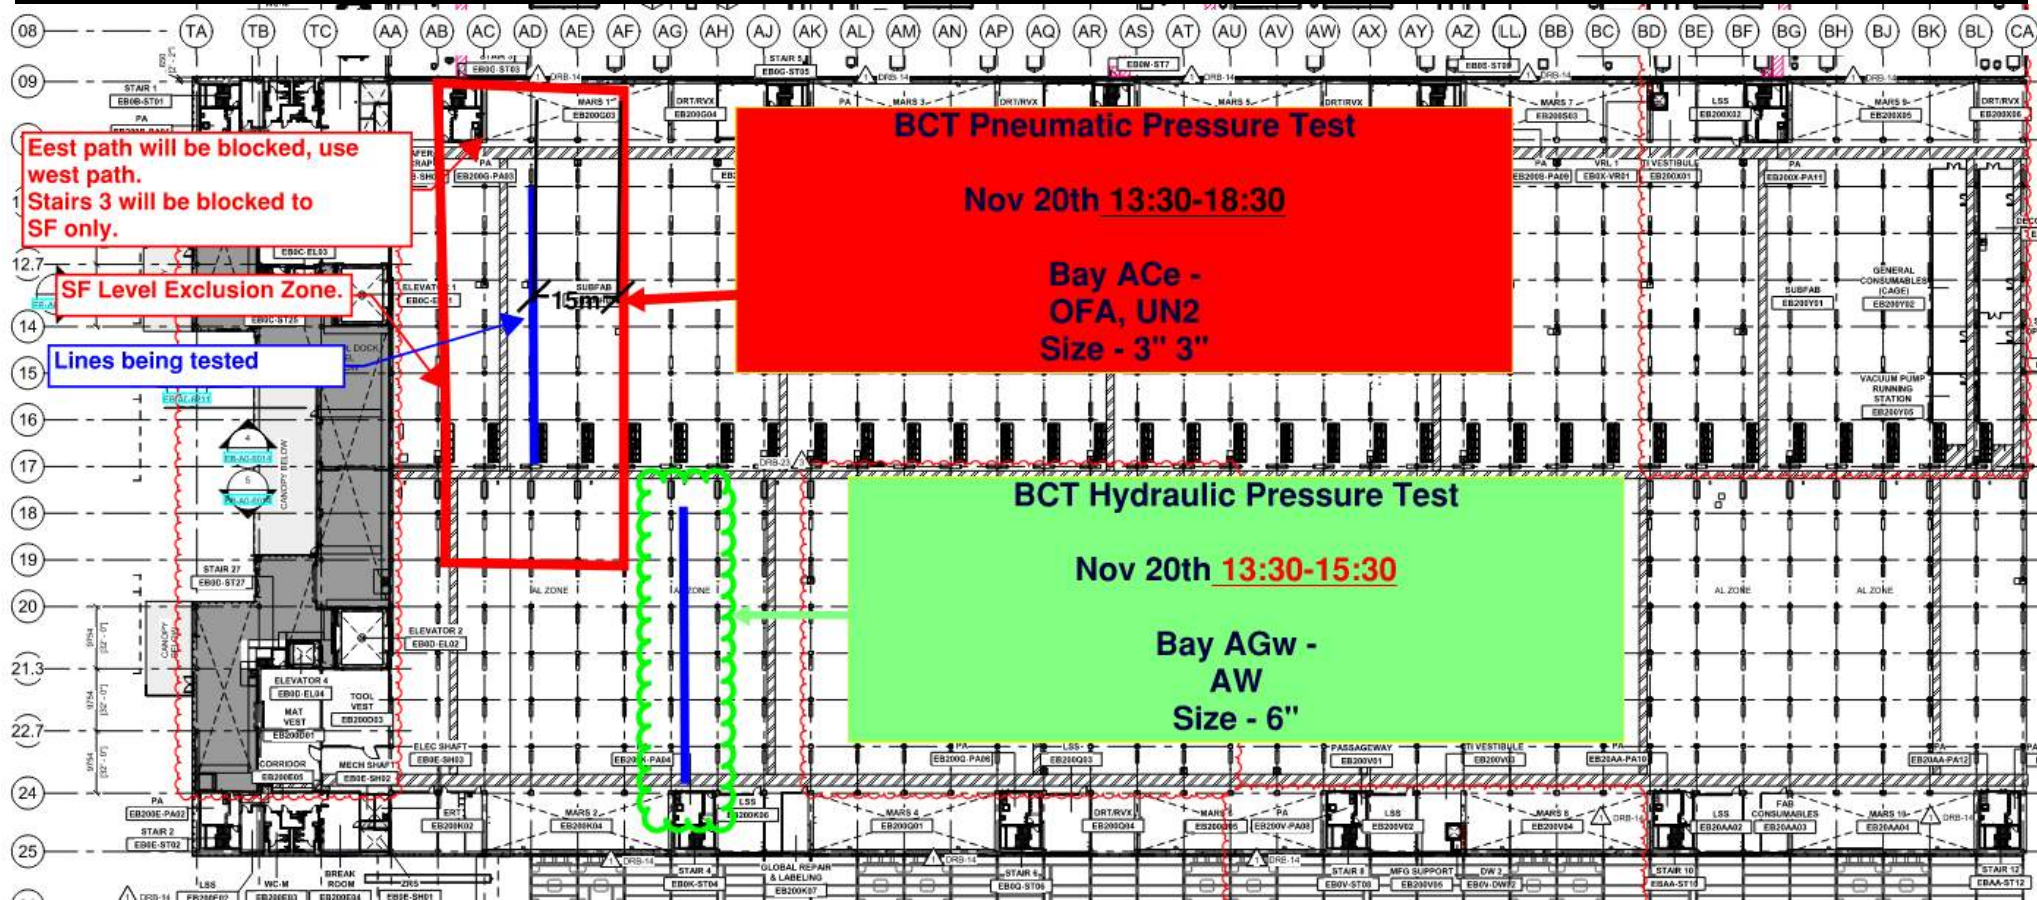

SUBFAB BUILDOUT MOD 2

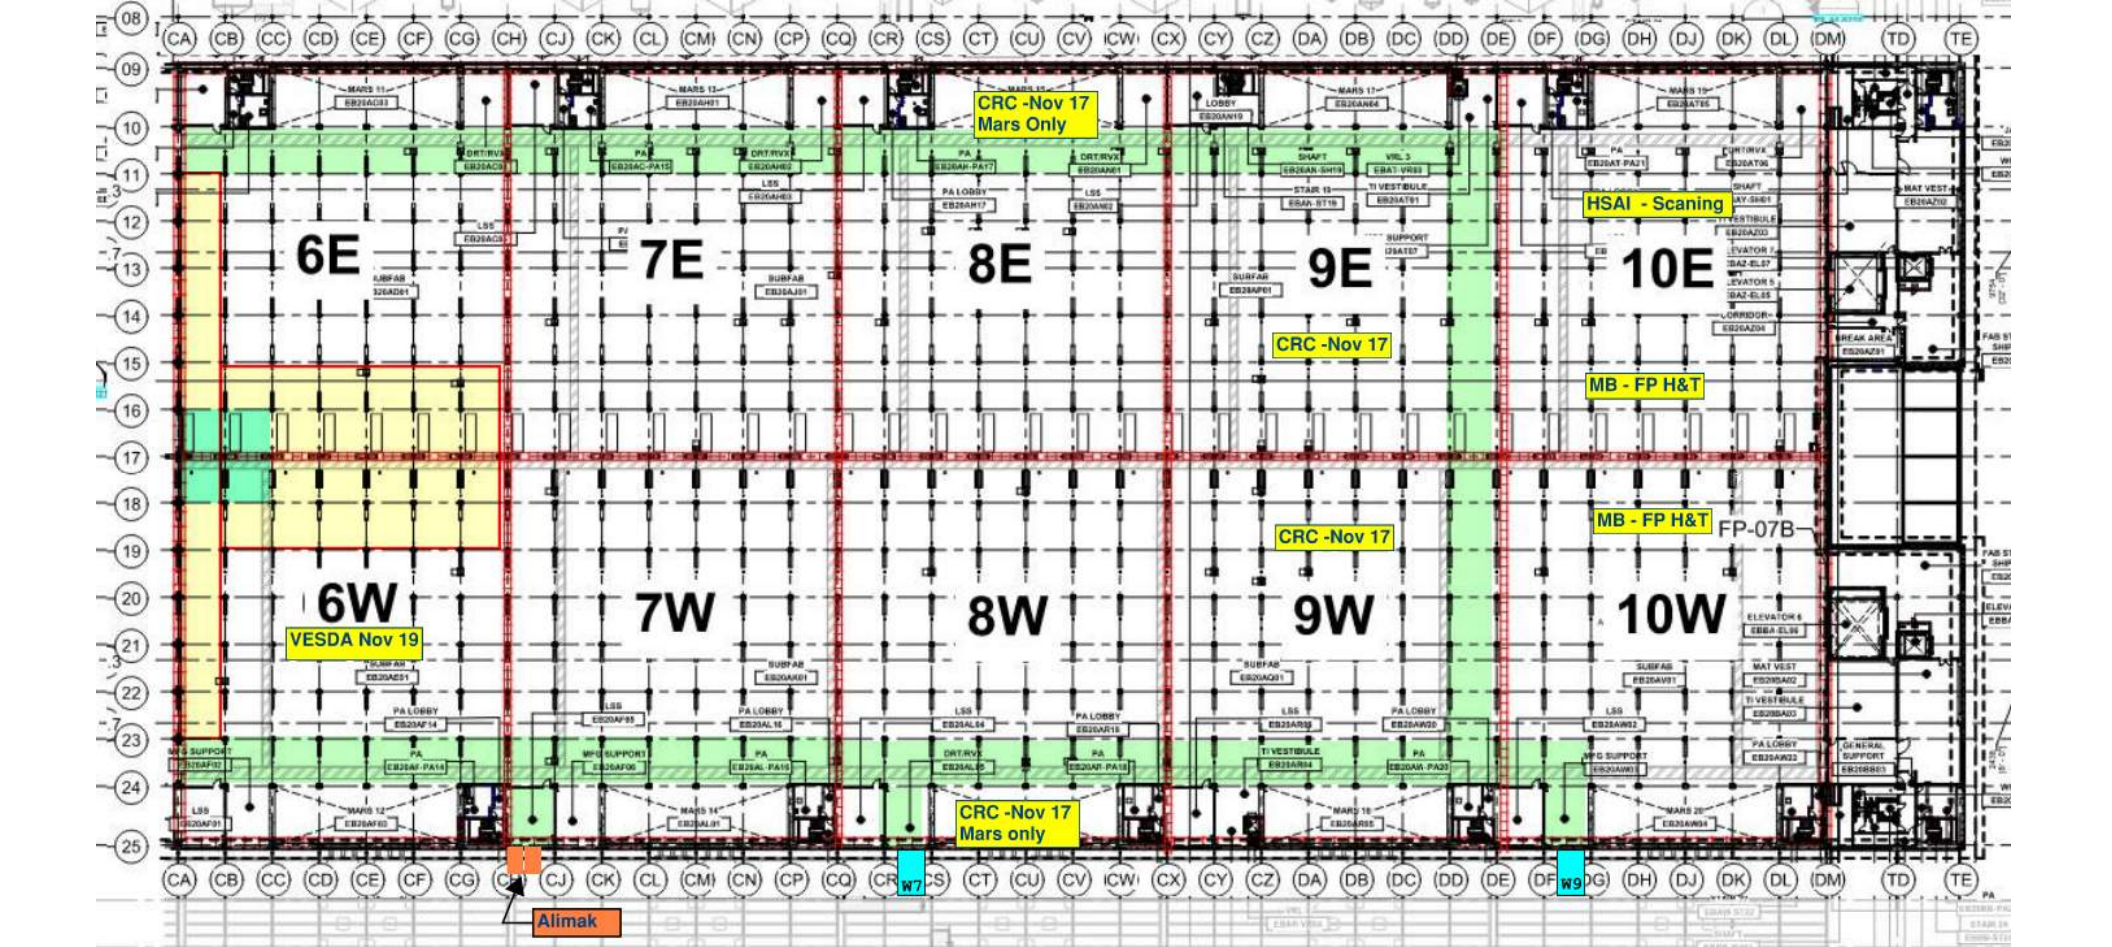

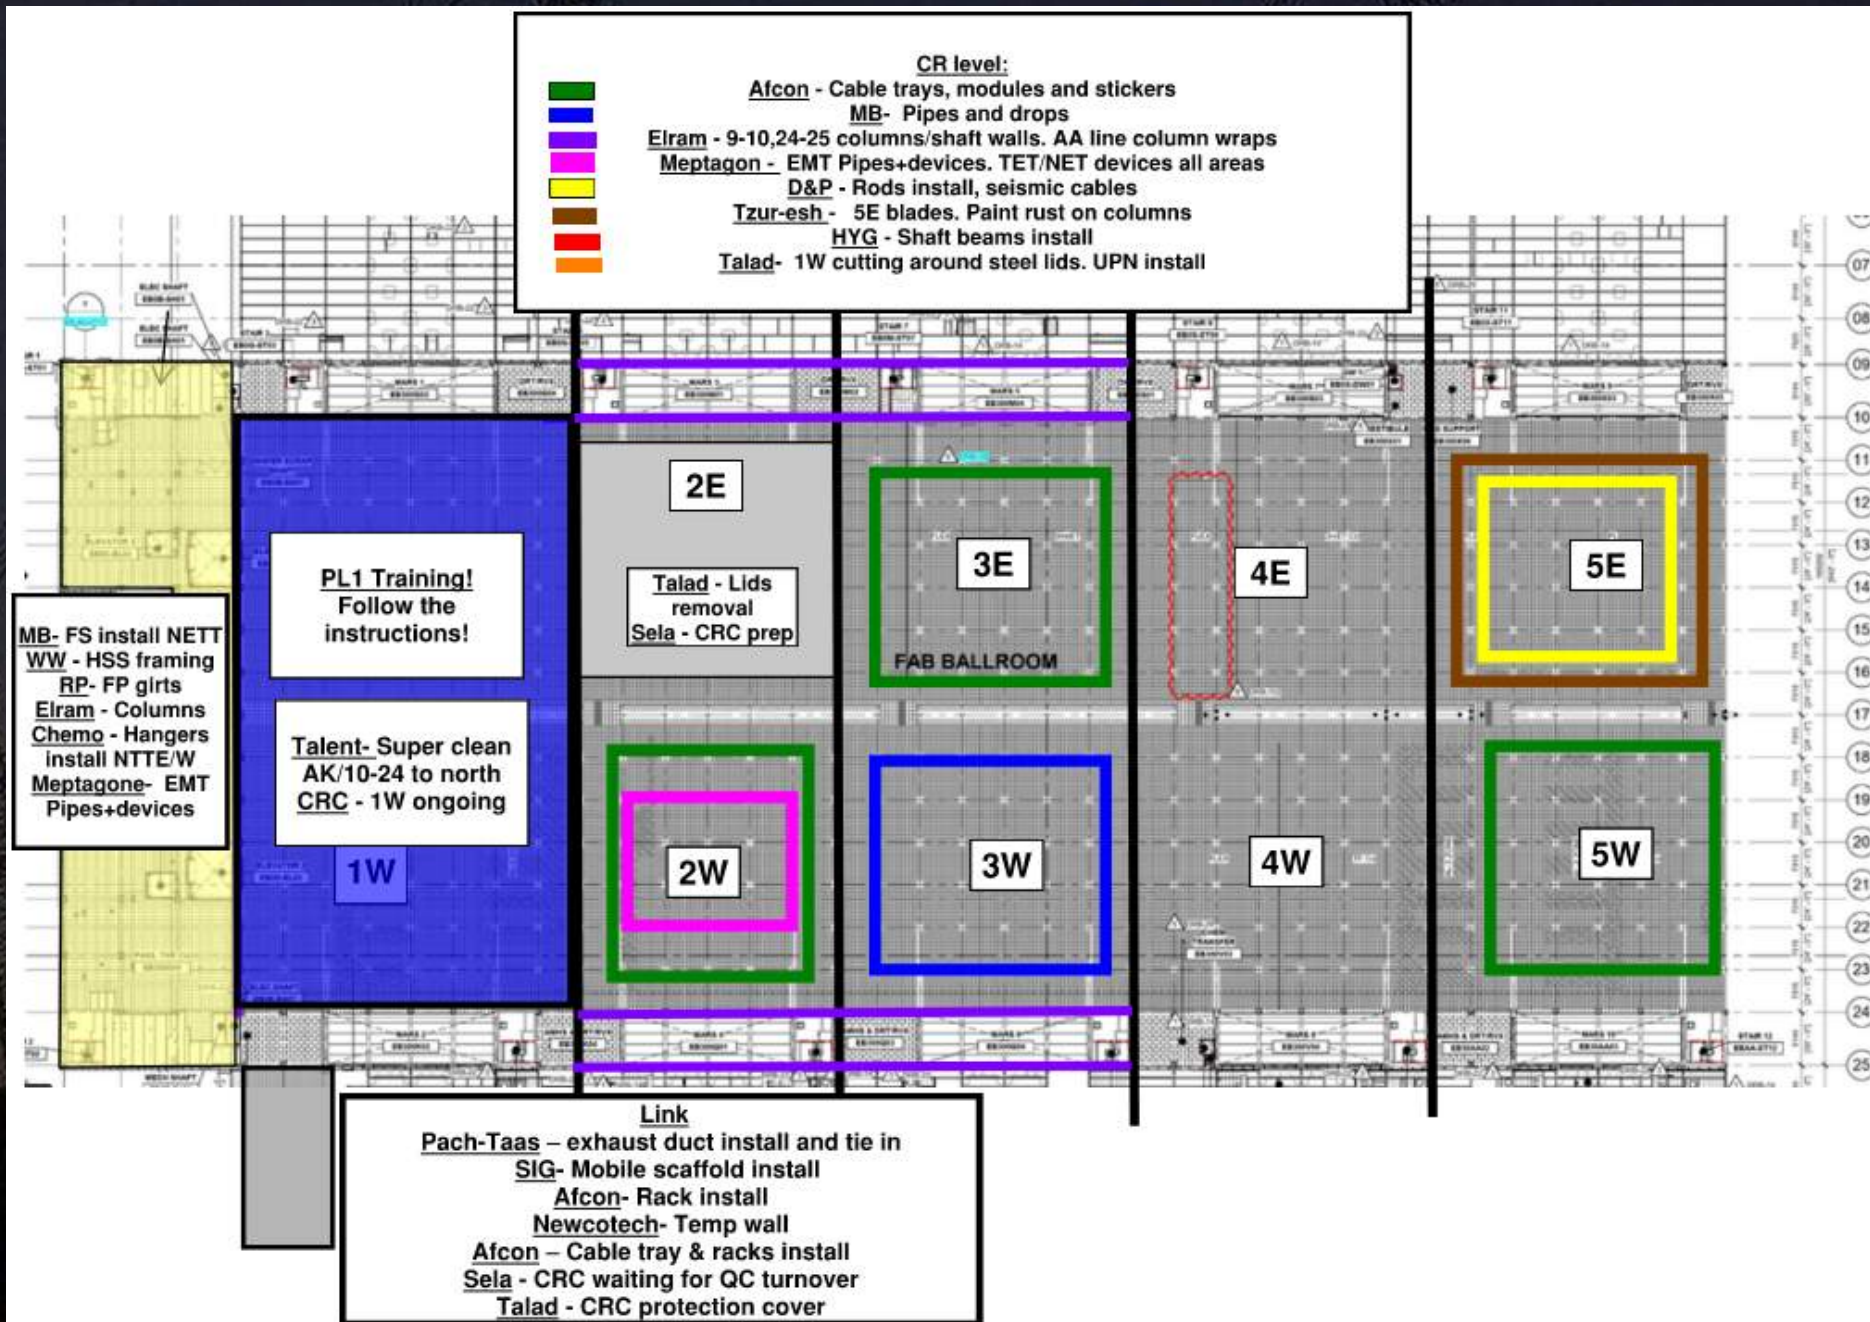

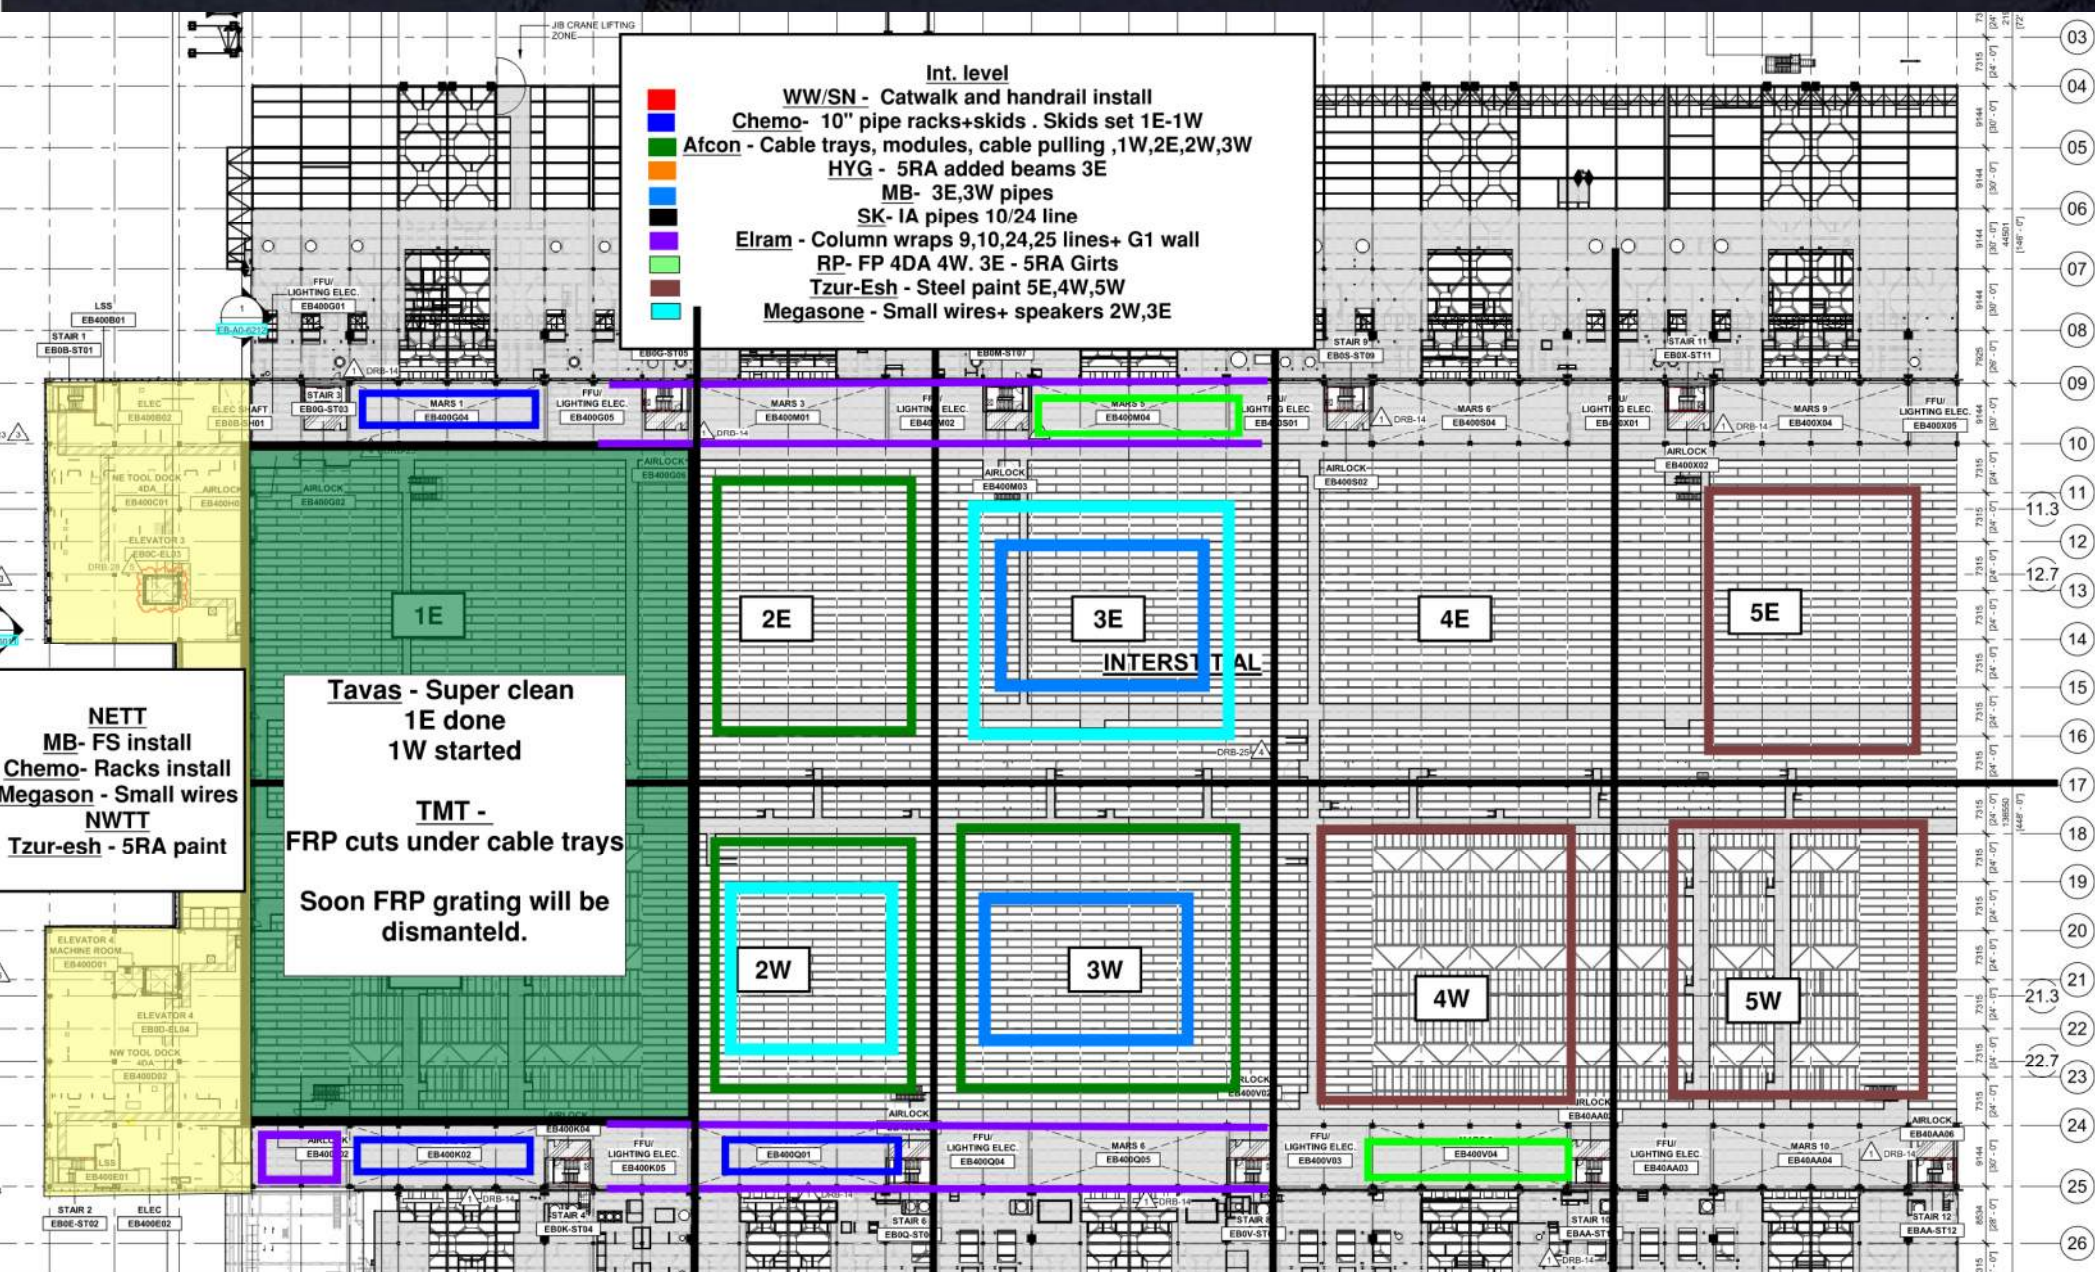



RPC - FP CA-CD
Tzur-esh - 4DA paint

In-fill ongoing


SETT
Steel
erection
onglong


Truss #24 set
Wednesday Nov-20th

SEE LIFT DATA TABLE THIS
SHEET FOR BOX TRUSS
ASSEMBLY PLACE RADIUS
TYP.

TCR (SEE LOG-3)

TC10 (SEE LOG-3)

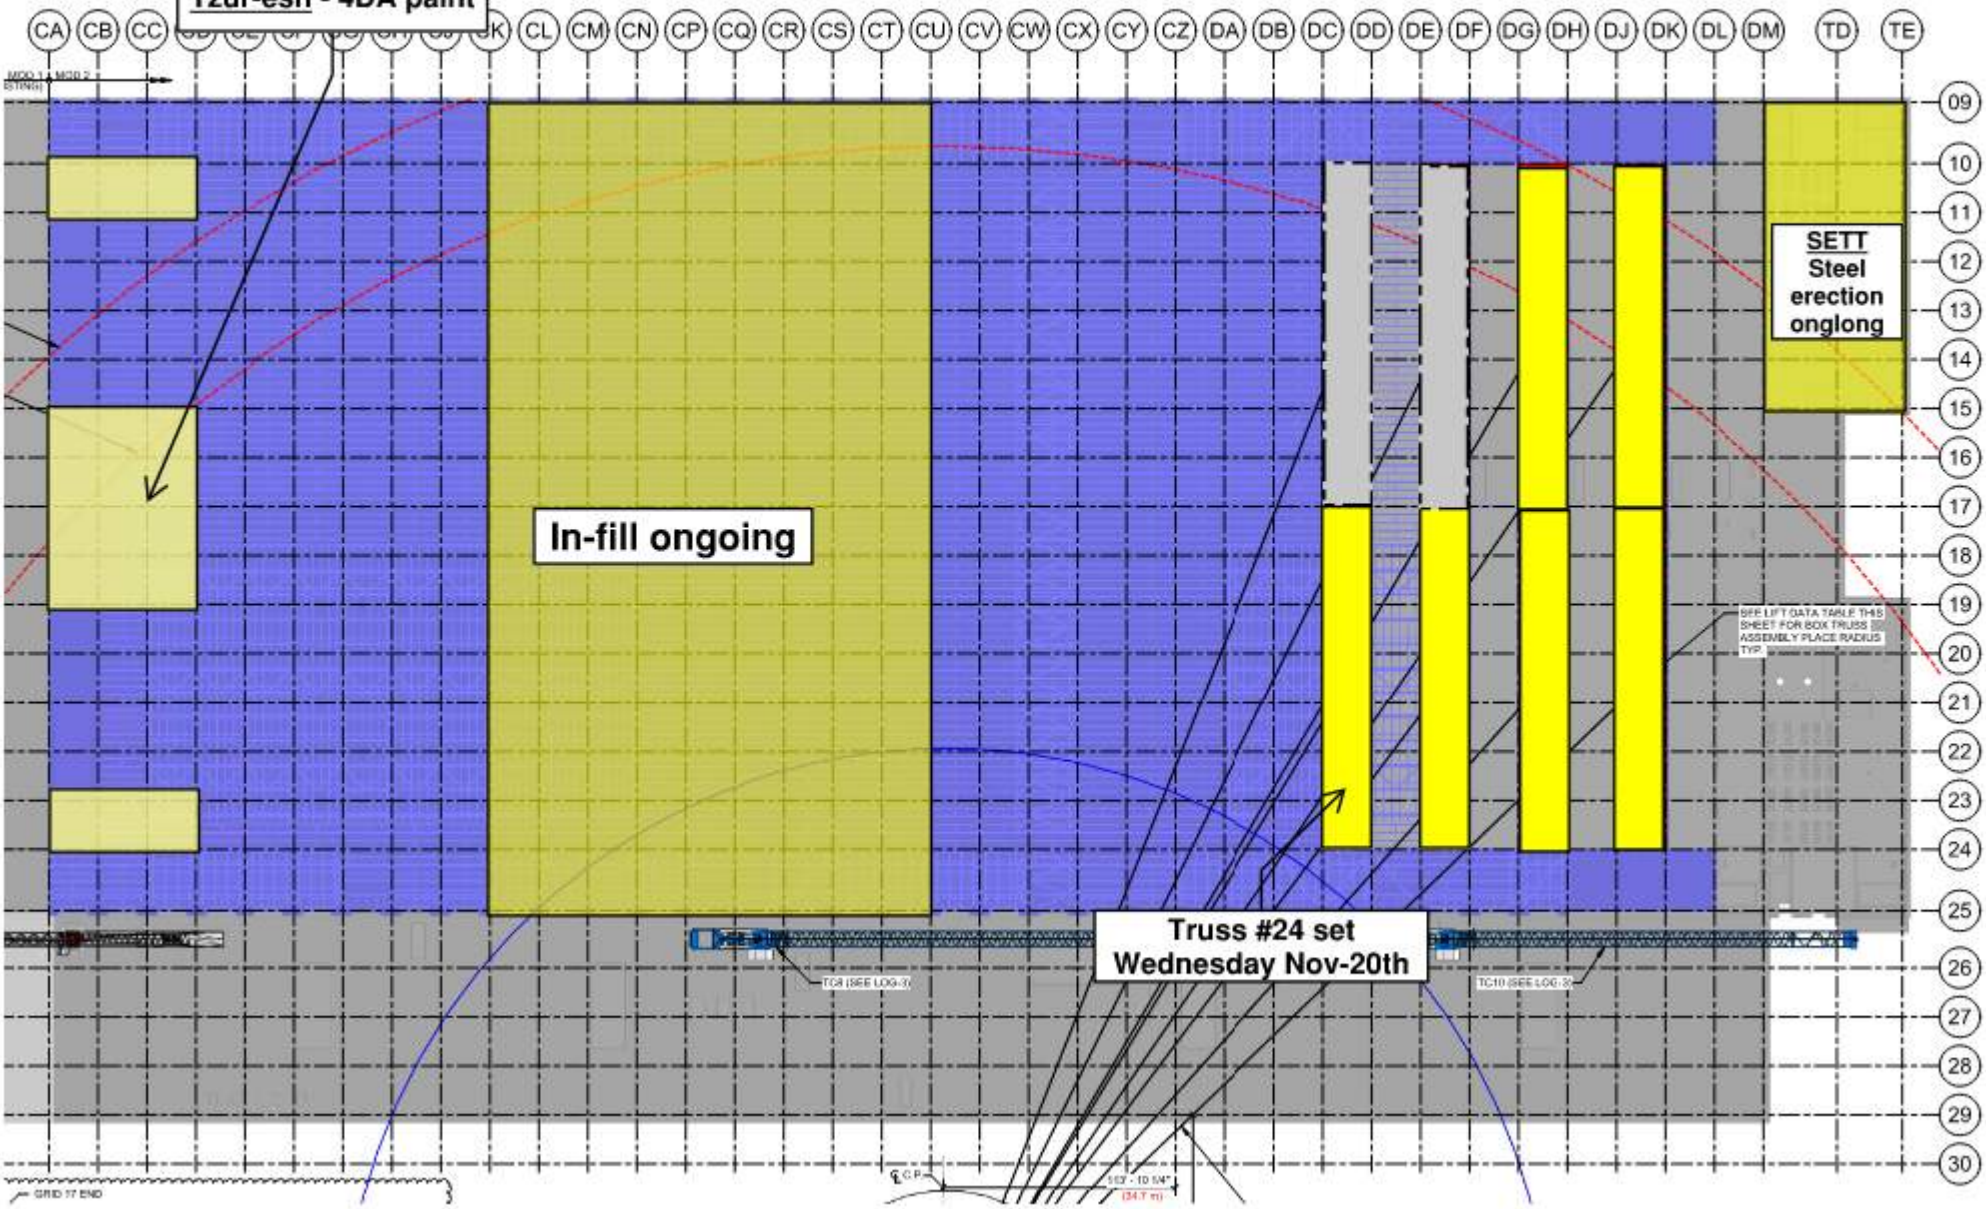

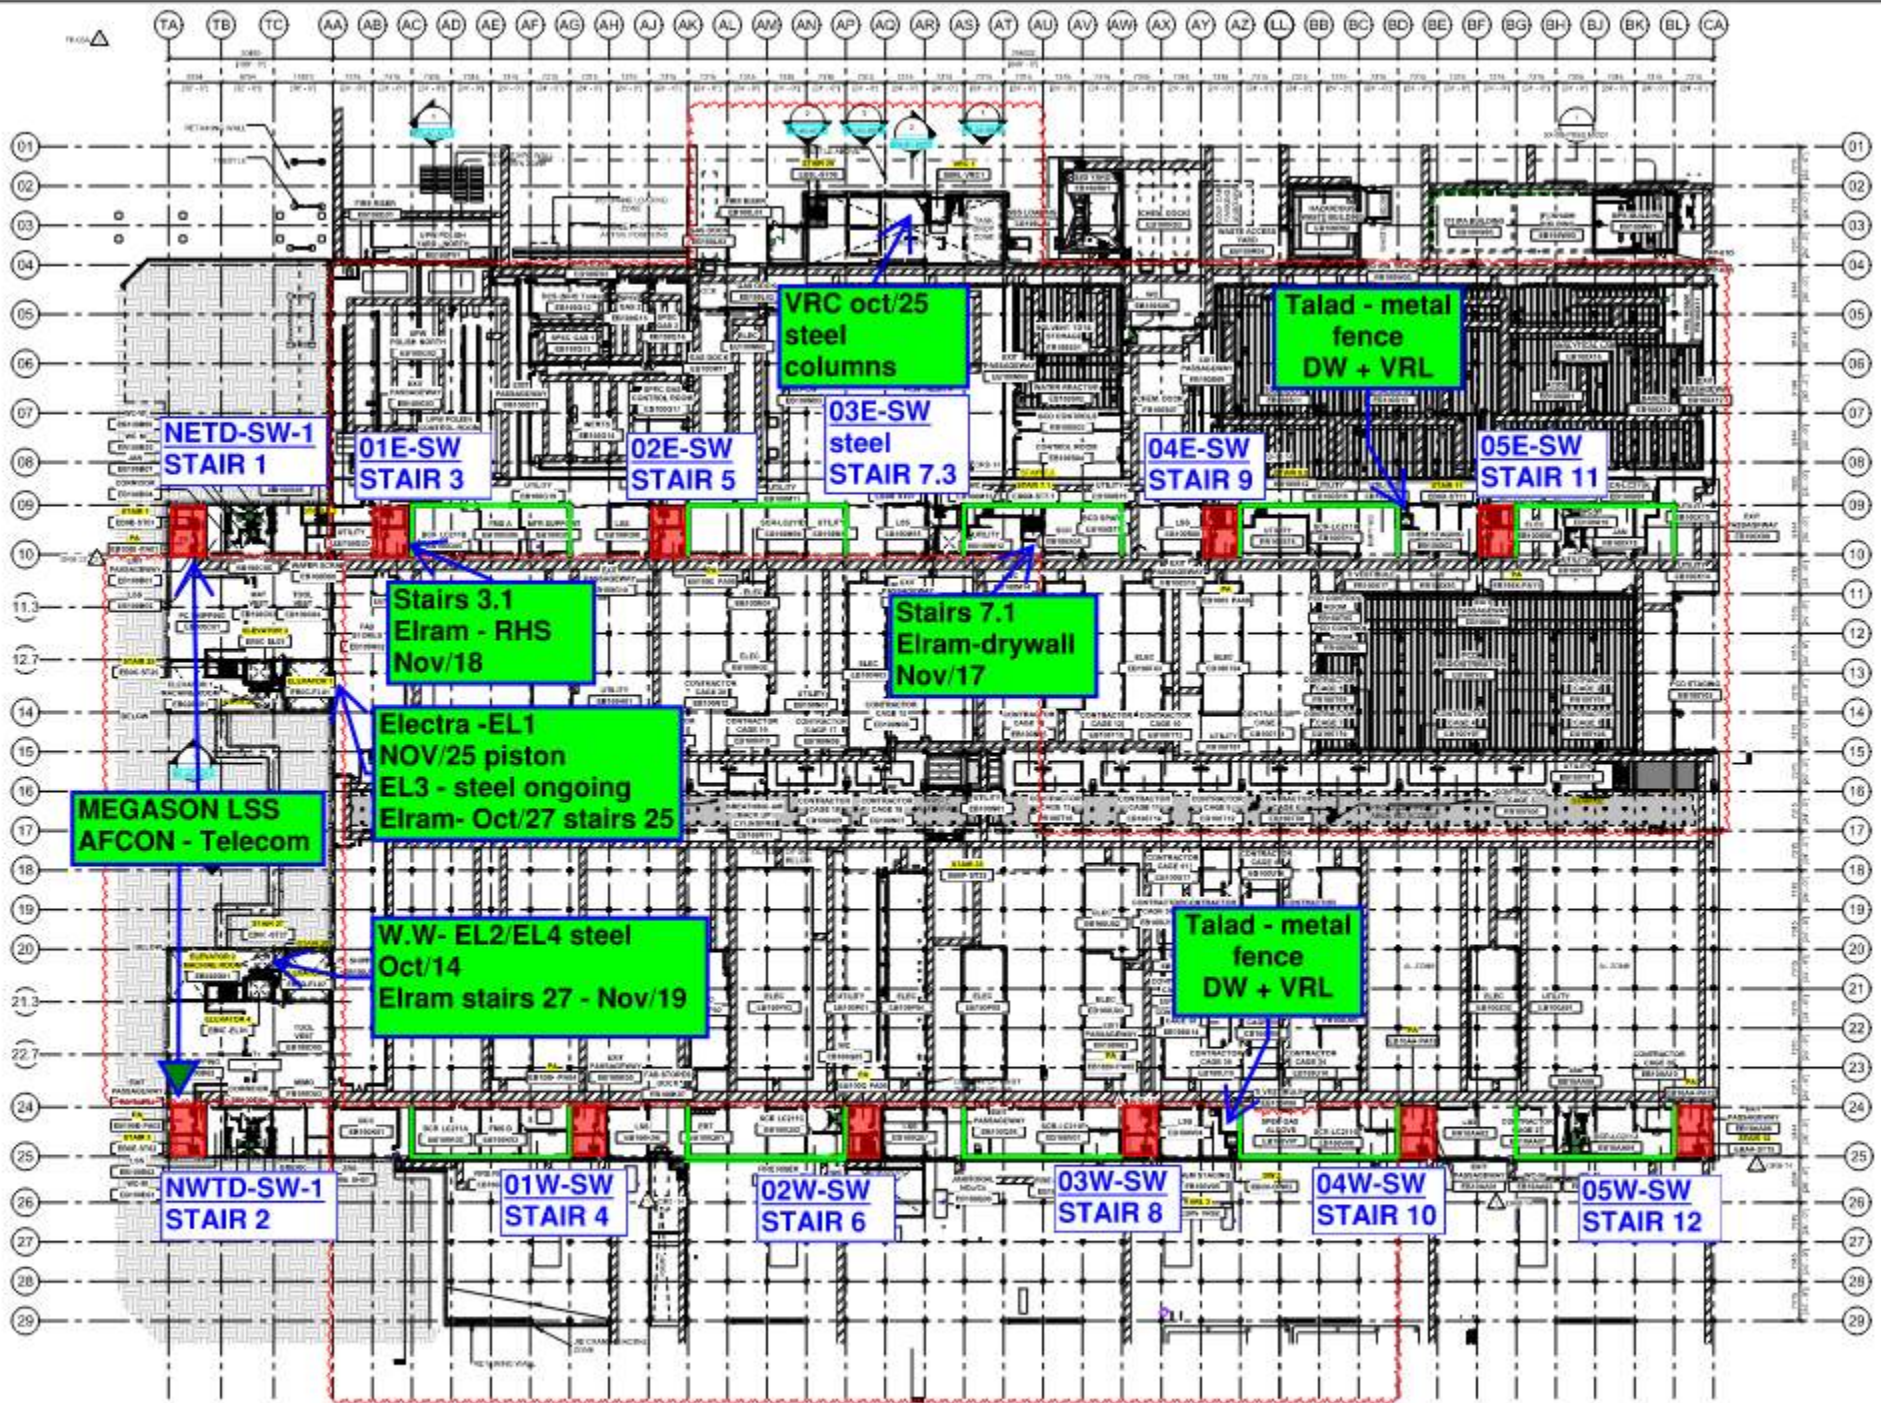

Siding - West FAB - JYG


BLOWDOWN 30%

[illegible]


Siding - East FAB - PSSS


BLOWDOWN 30%

[illegible]

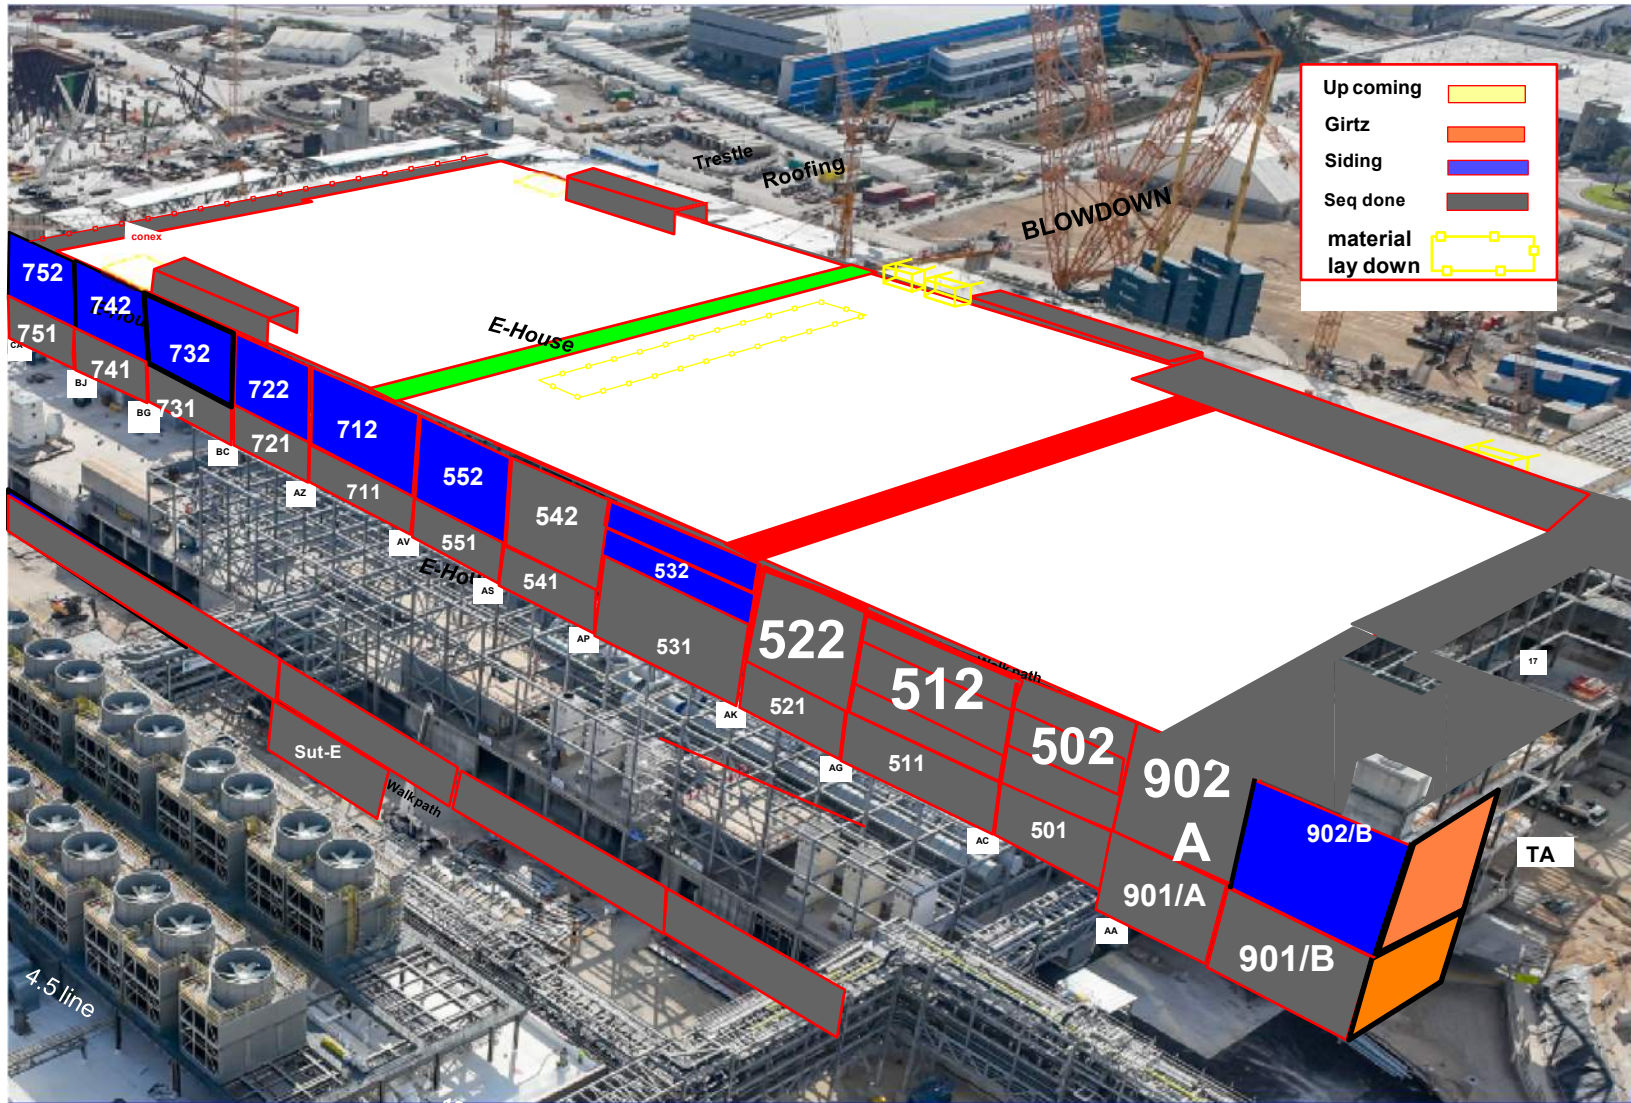

Walkpath

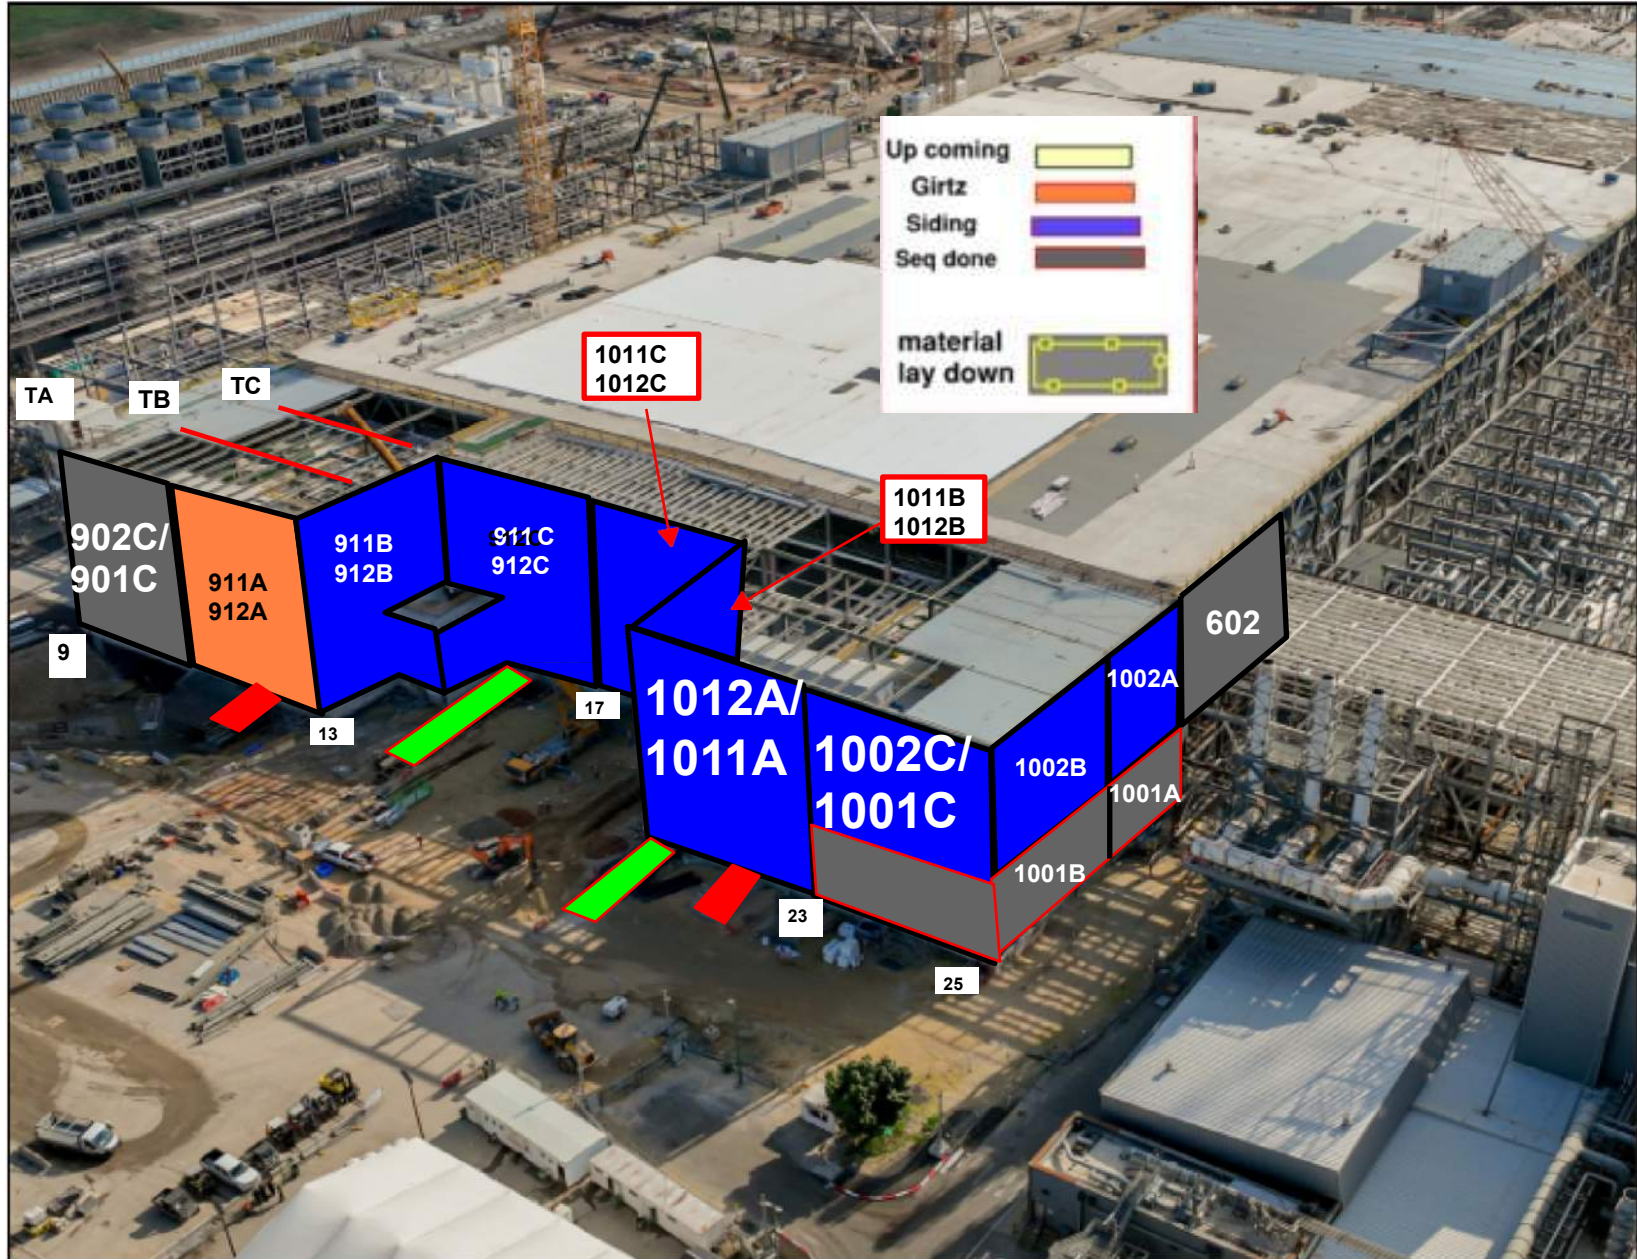


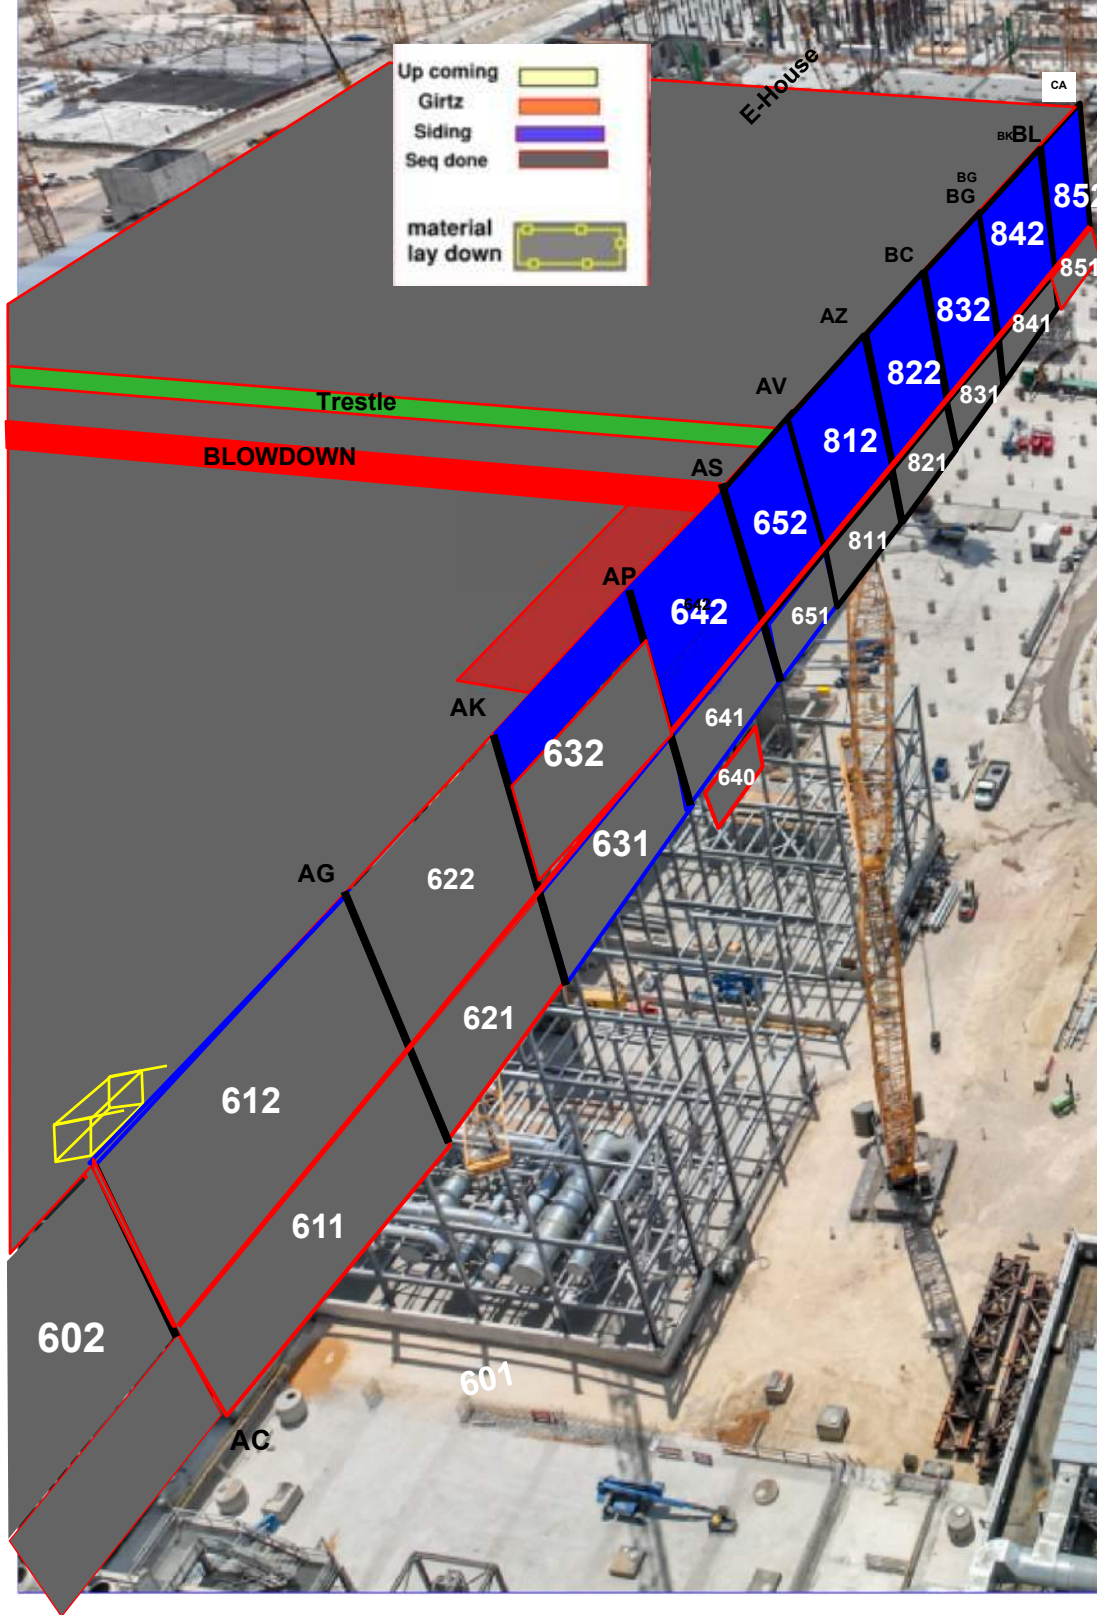

PSSS.1


Utility Level
1YA

PSSS Roof
2SA

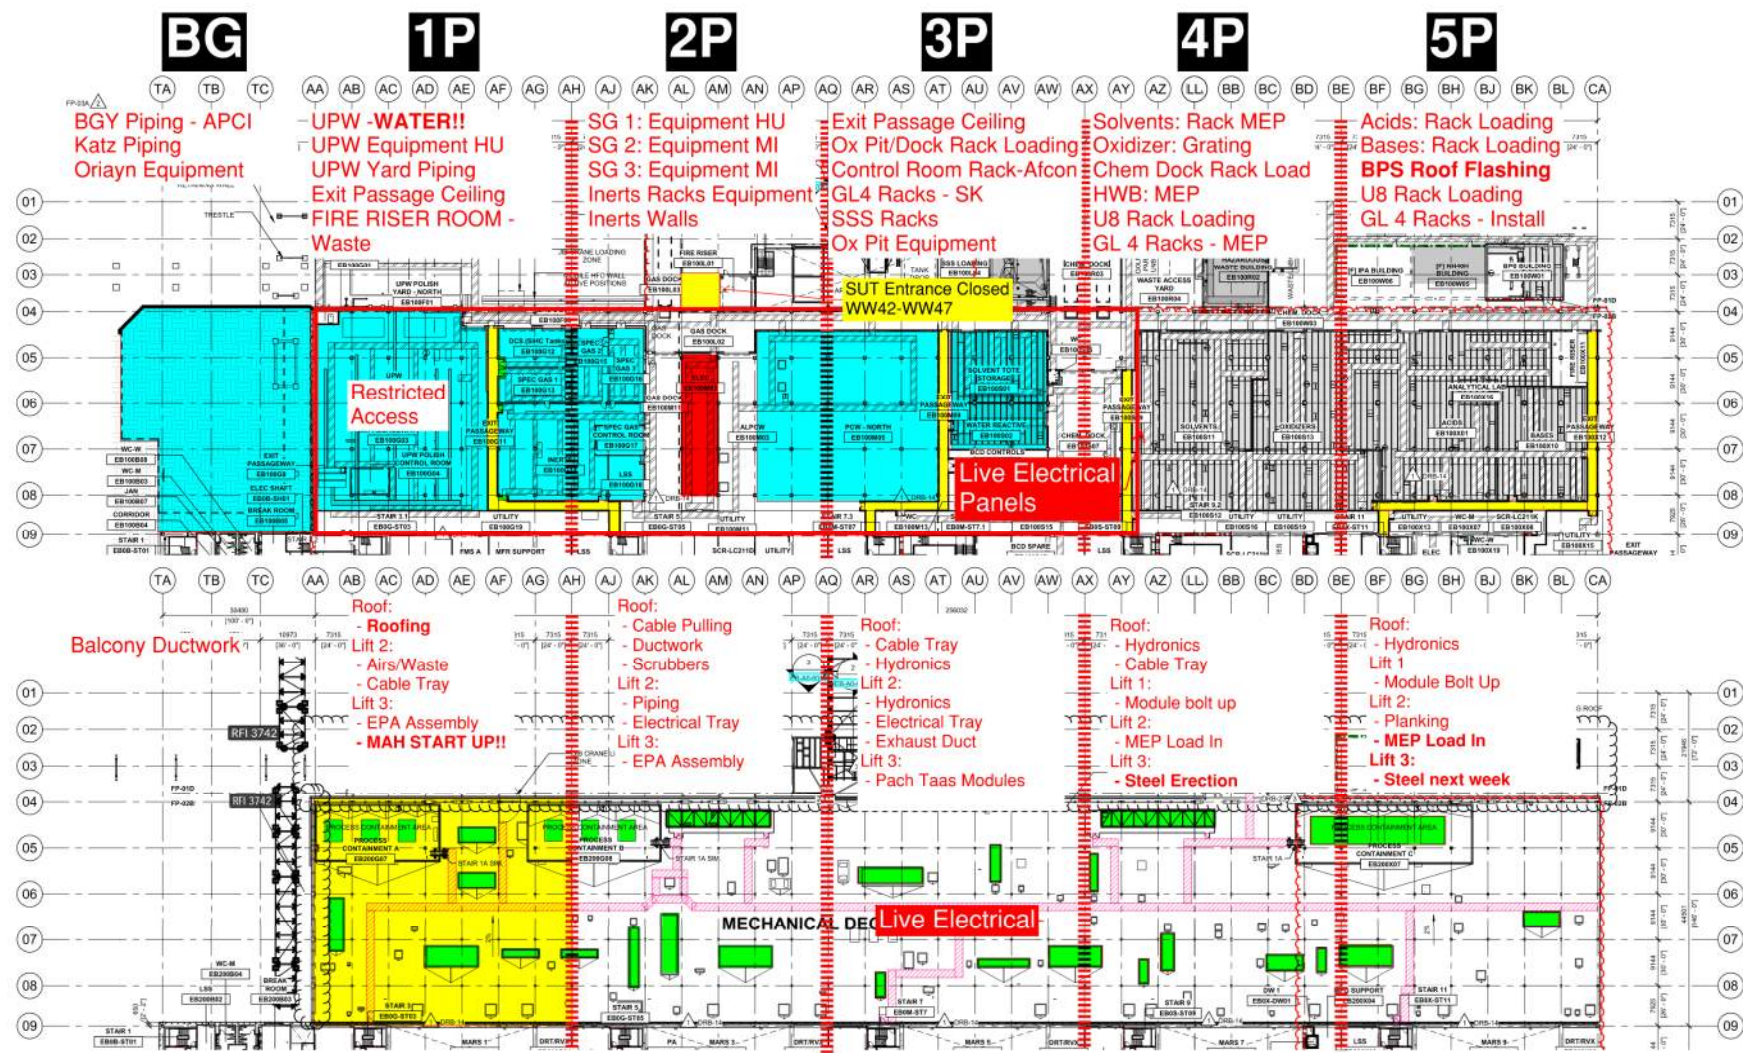


PSSS.2


Utility Level
1YA

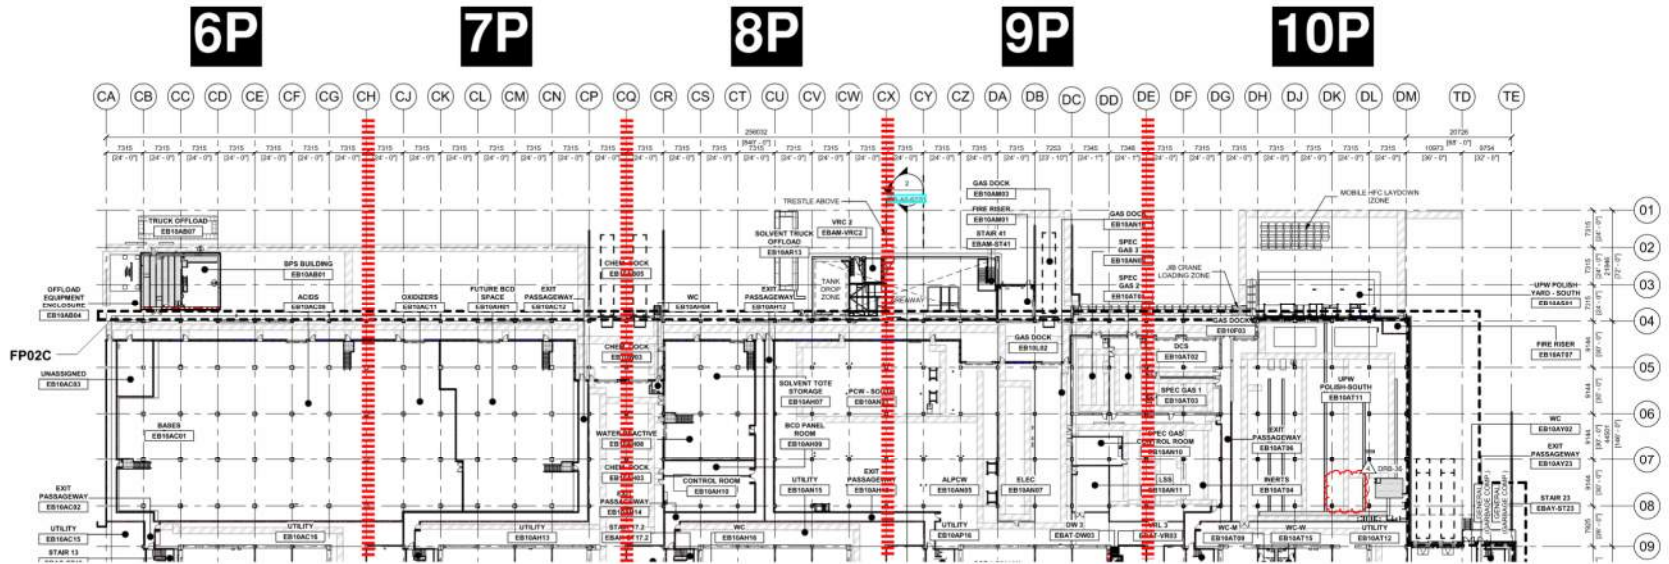


PSSS Roof 2SA

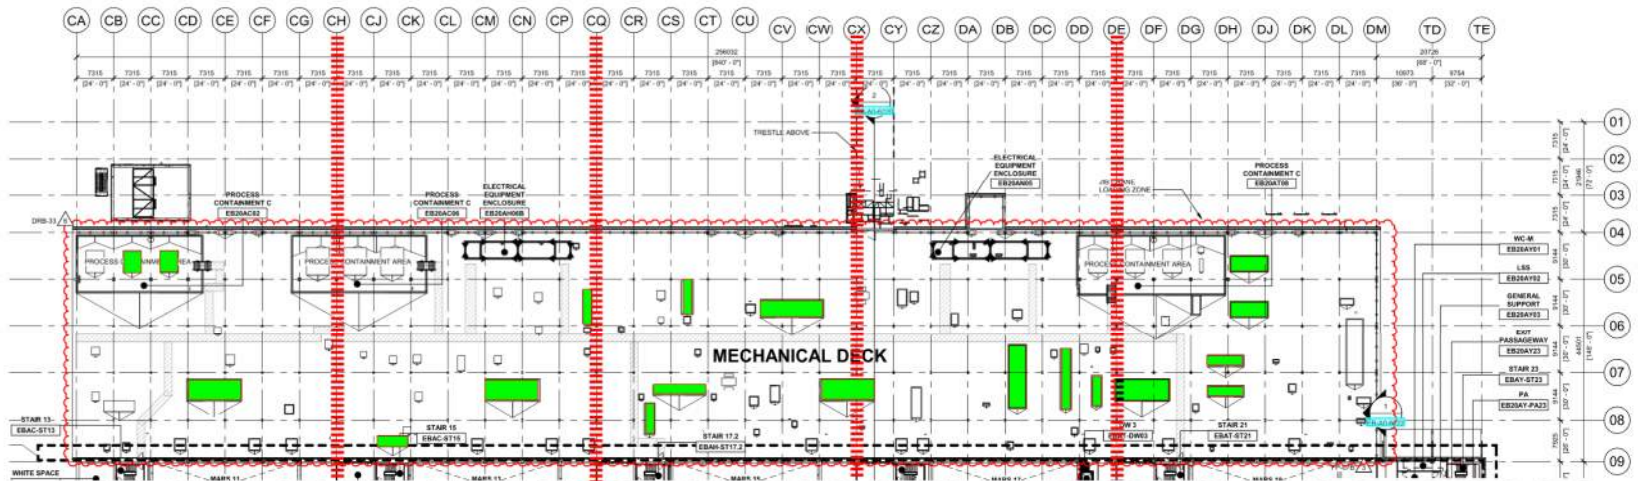


PSSS Clean Up
If PSSS is not clean
by 17:00 today all
crews in the PSSS
will be cleaning
tomorrow until all
areas are deemed
acceptable.

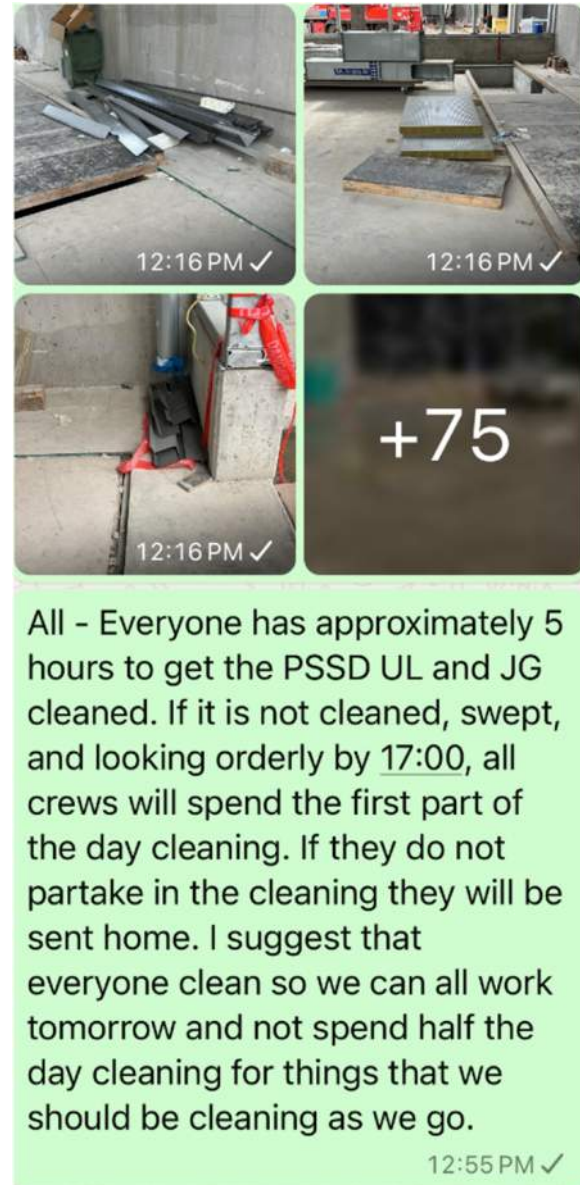


Trade Damage Needs to Stop

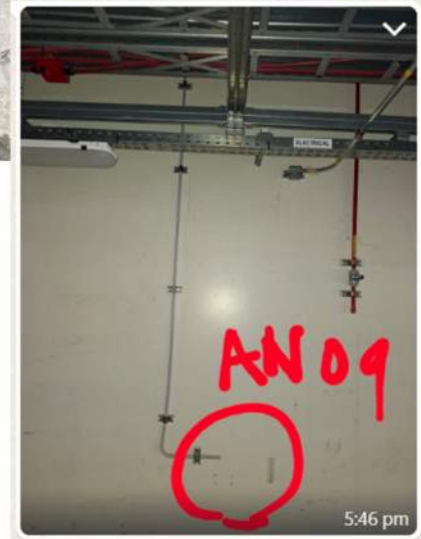


WJG 01J, 02J LIFT 2 & 3

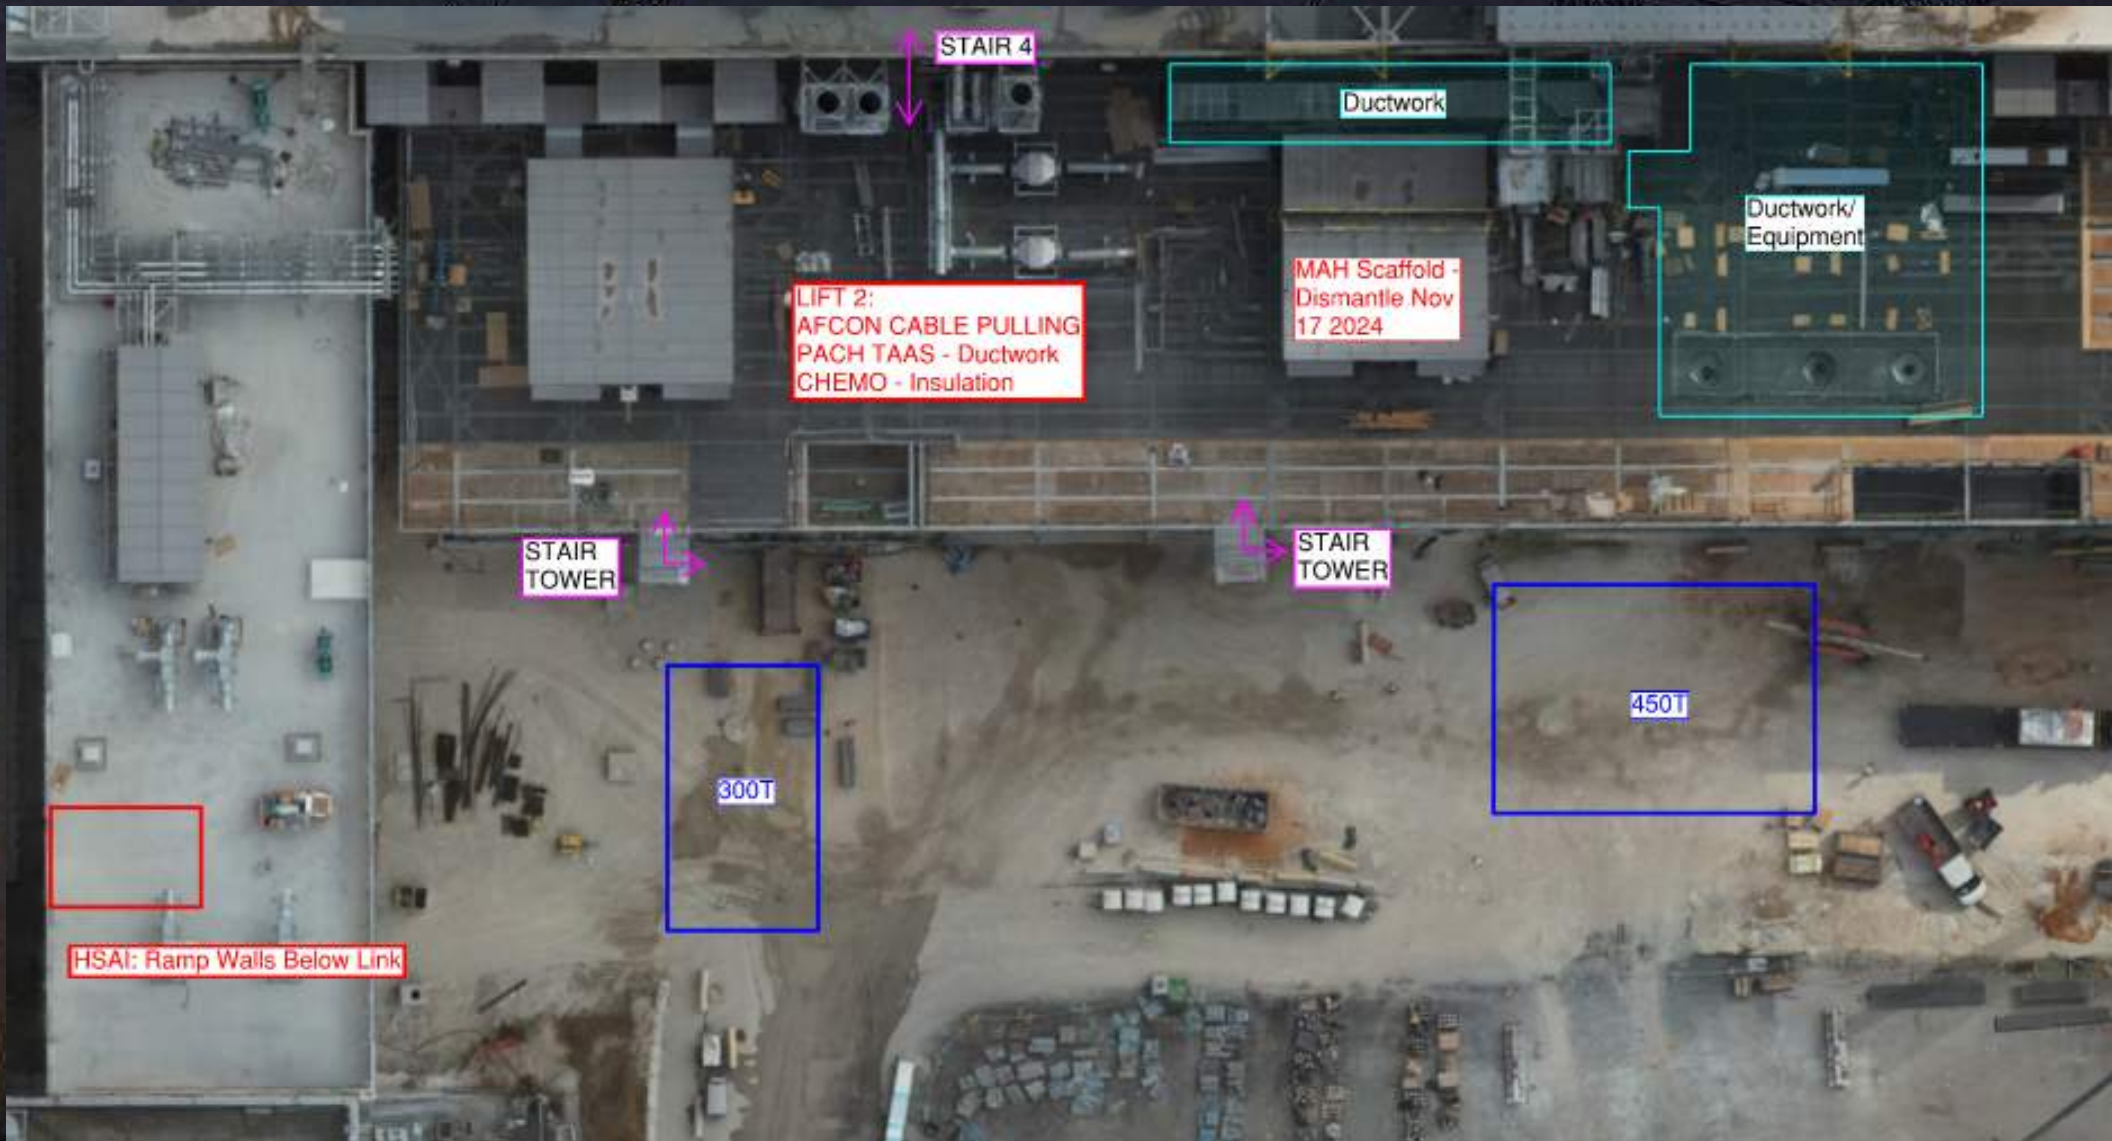

WJG 03J, 04J, 05J LIFT 2 & 3

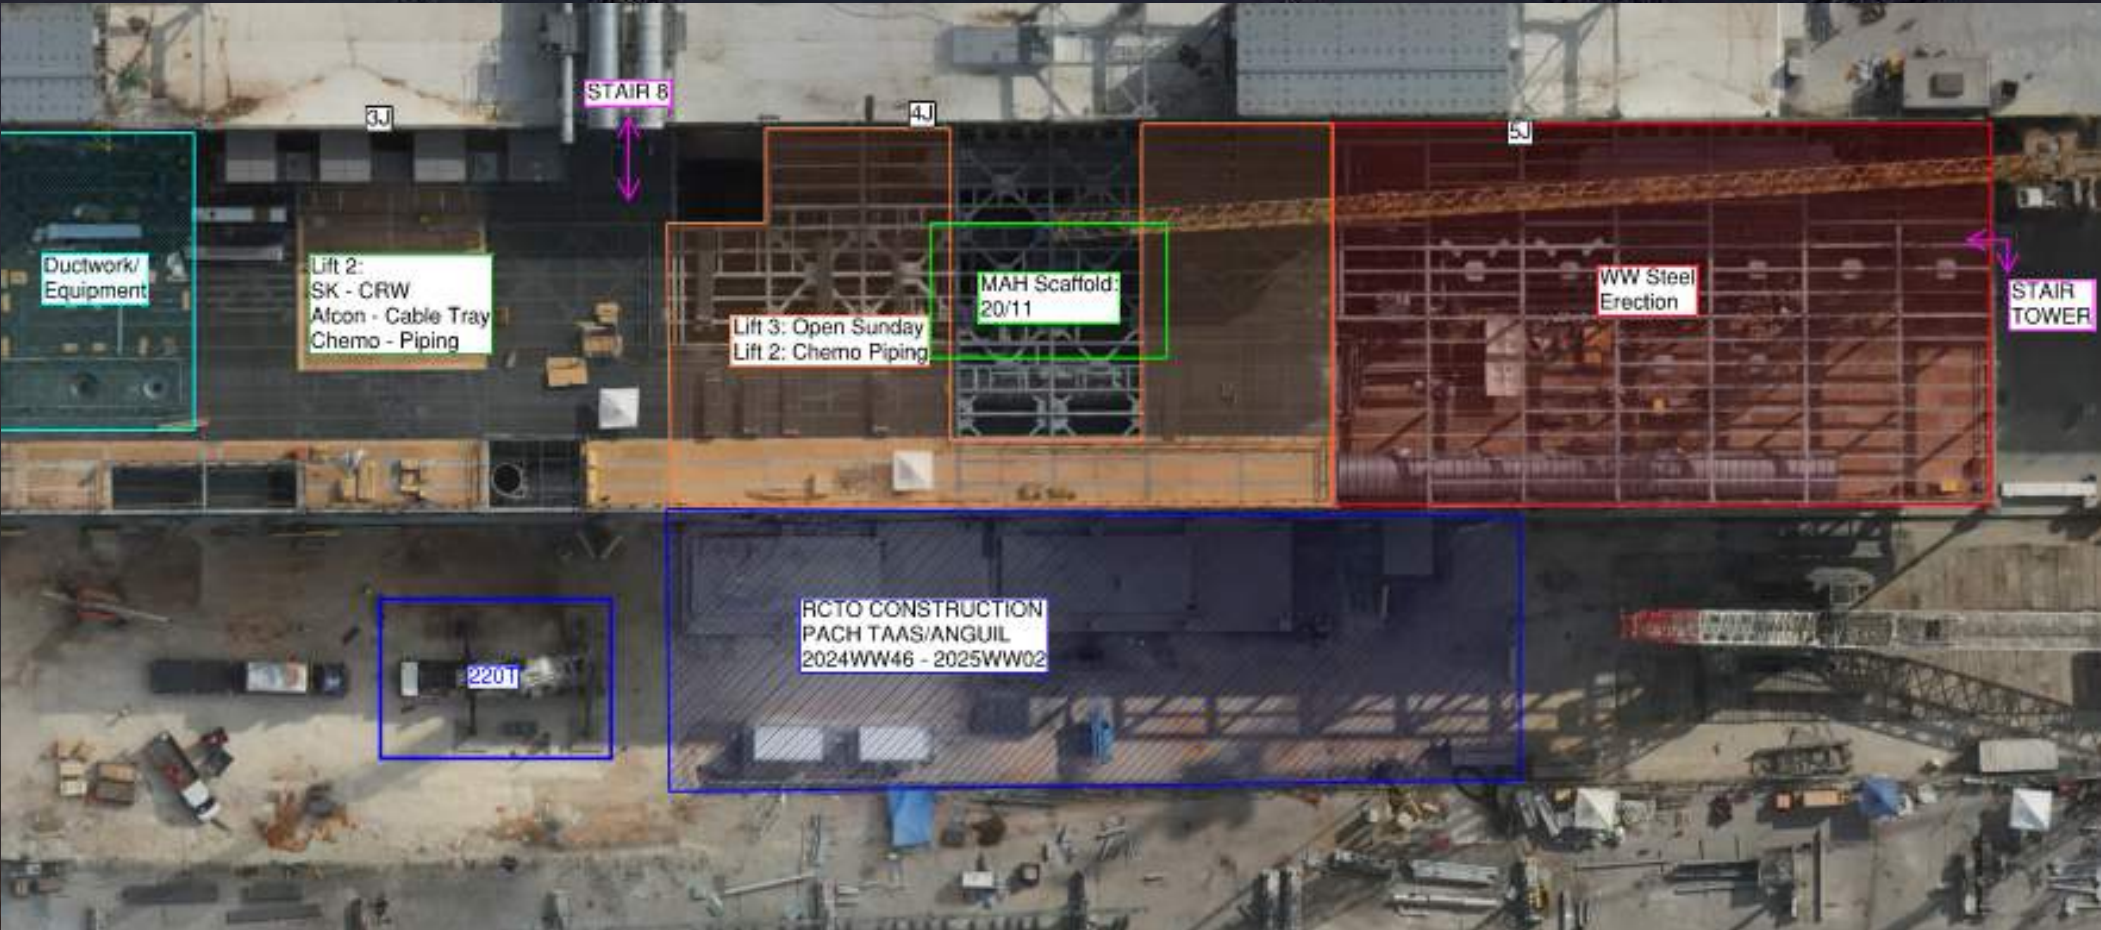


MAH101-7/8-00 Set WW47

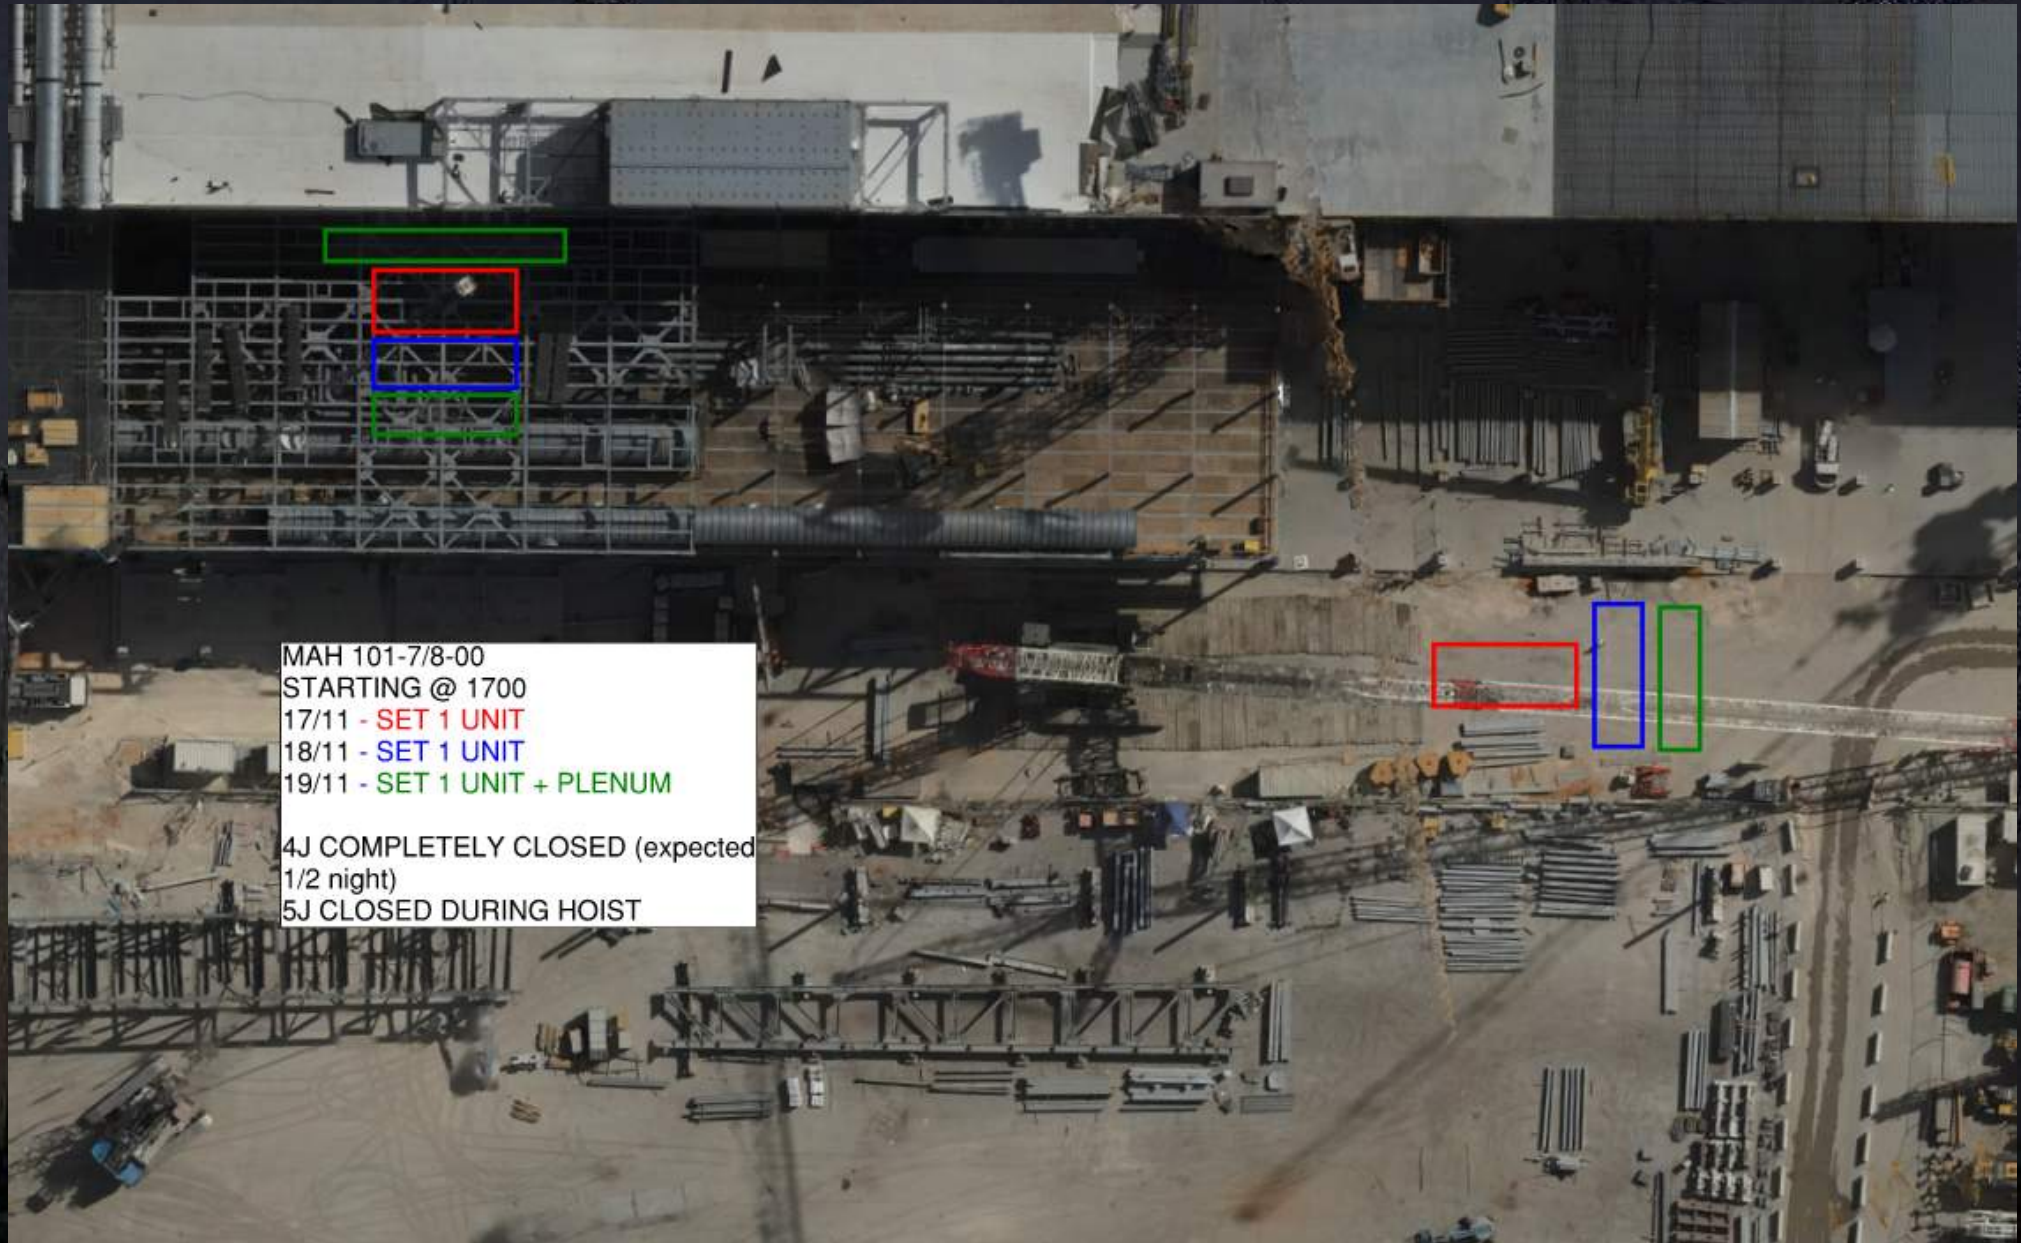



WJG UTILITY LEVEL BUILD OUT

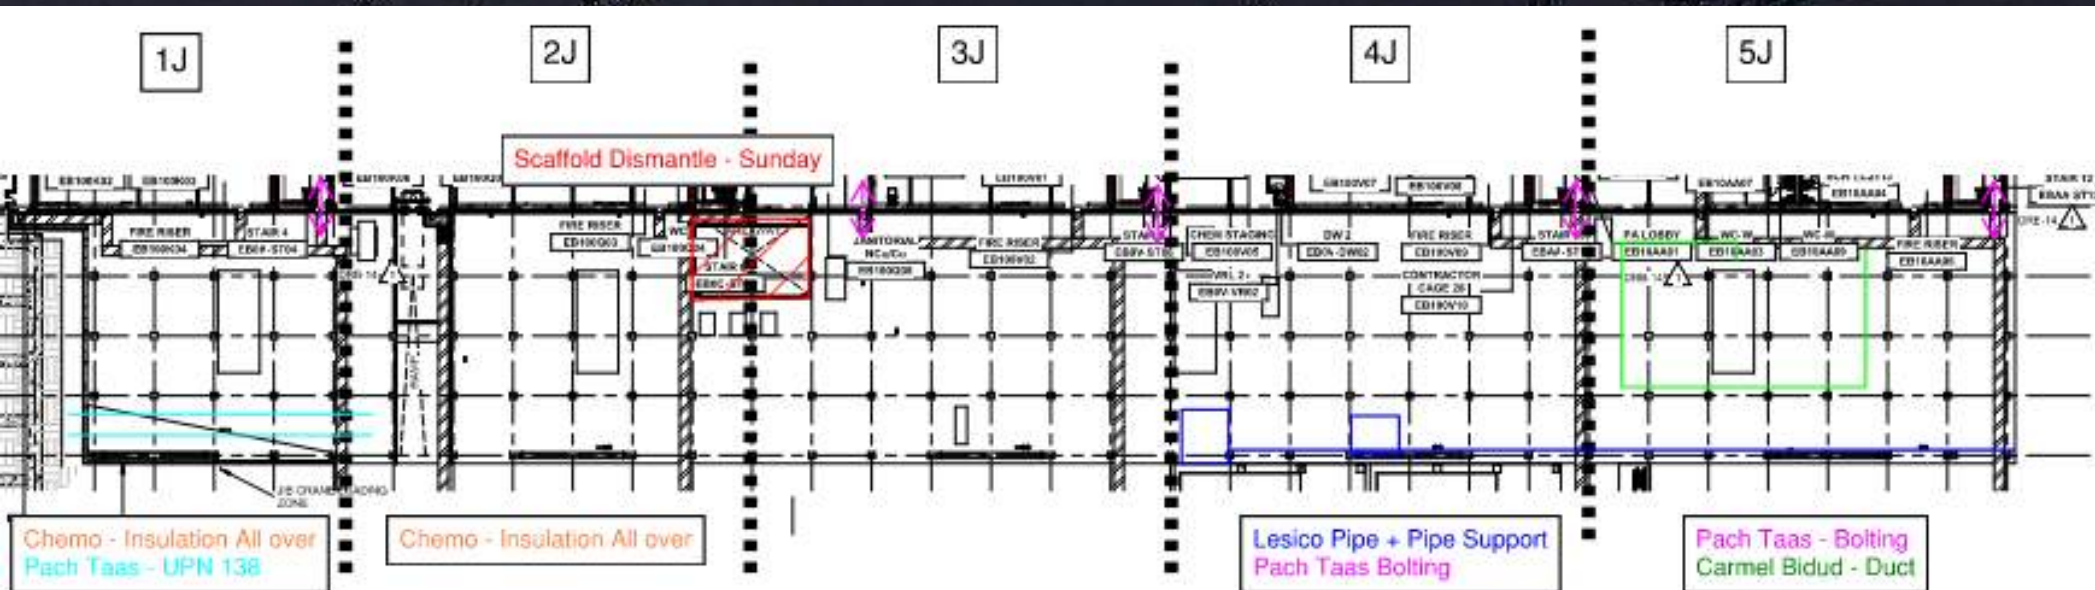

CUB 1 EVACUATION MUSTER LOCATION

NORTH YARD

WATER TREATMENT

SAND FILTERS

CHILLERS


BOILERS

EGRESS KEEP CLEAR

NOTE:


1. REFRIGERANT DETECTION SYSTEM IS LIVE.
2. IF ANY ALARM IS SOUNDED-ALL WORKERS MUST EVACUATE THE BUILDING
3. EVACUATION LOCATION TO E IN NORTH YARD OF CUB 1

CUB 1 – EXTERIOR/ROOF

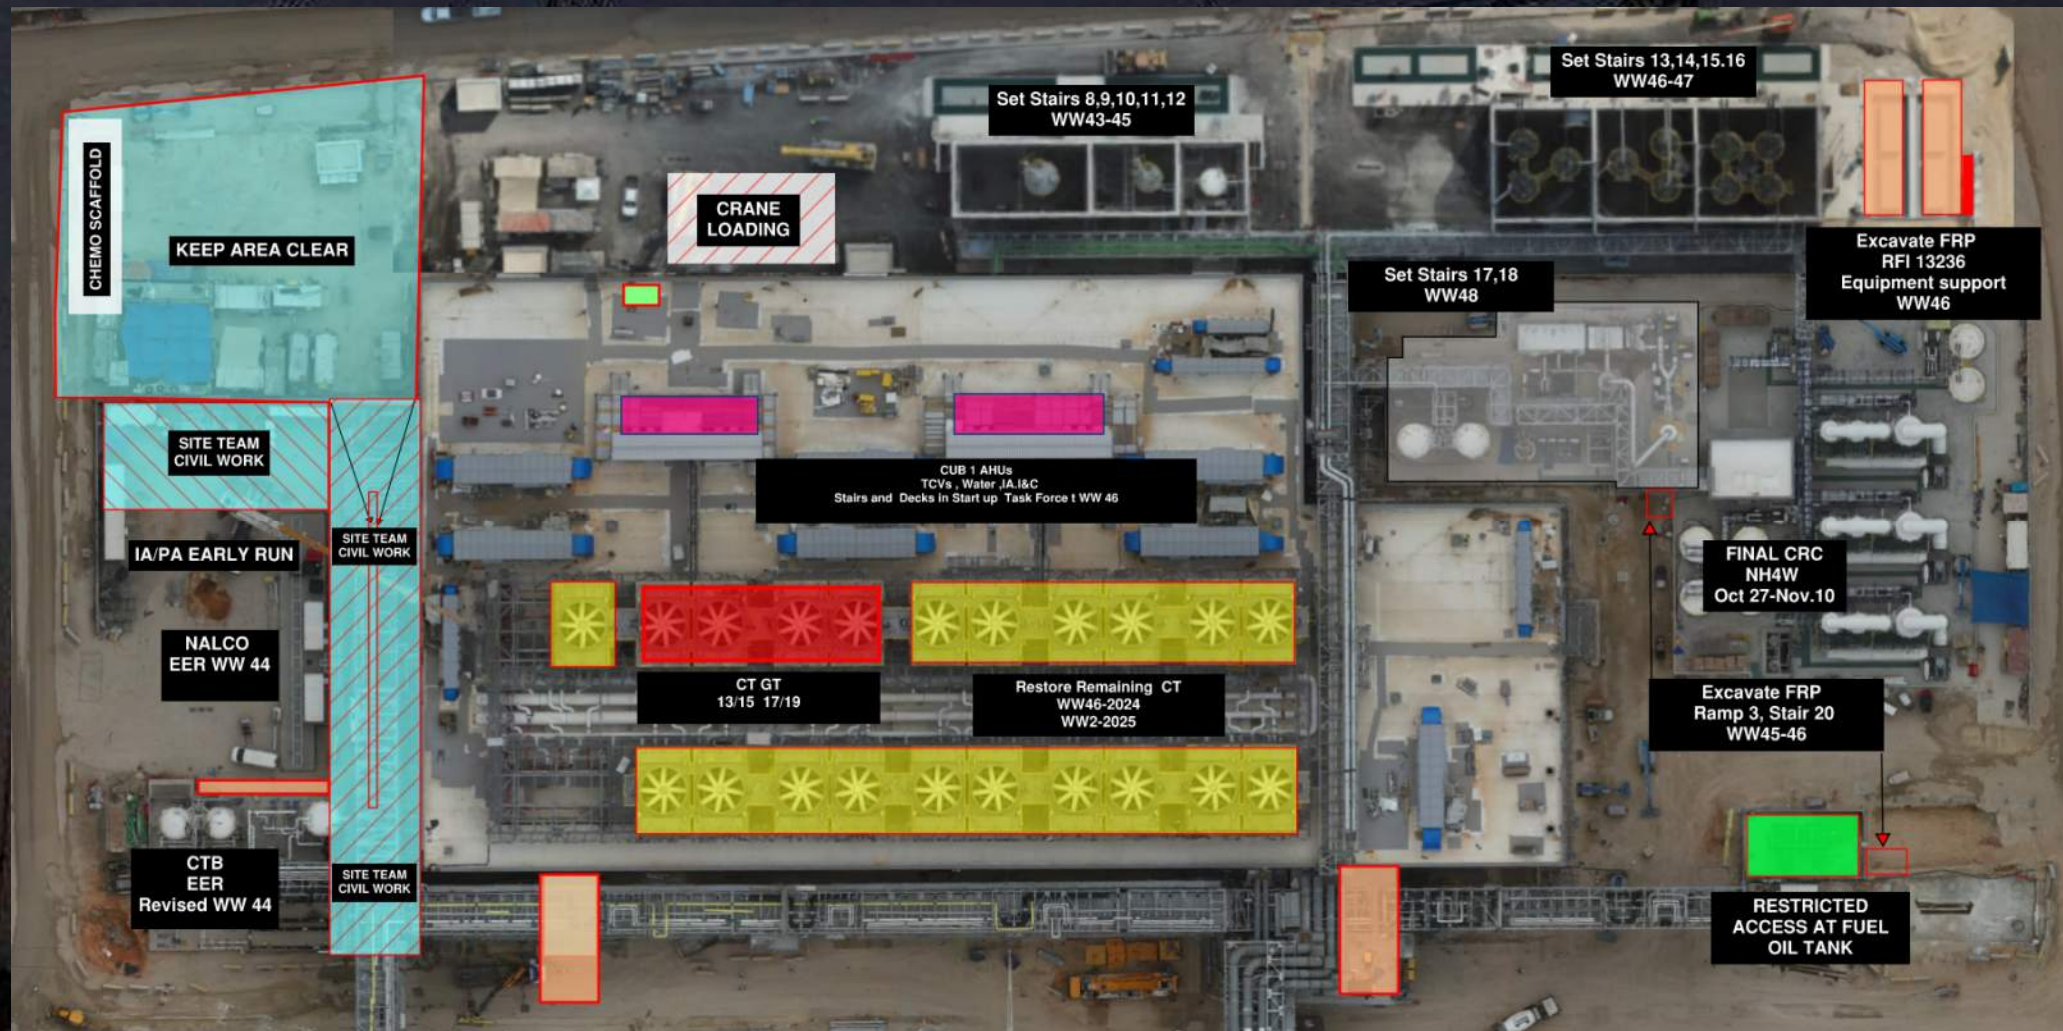


CUB 2- Load in and H&T

CUB 2 COORDINATION MAP

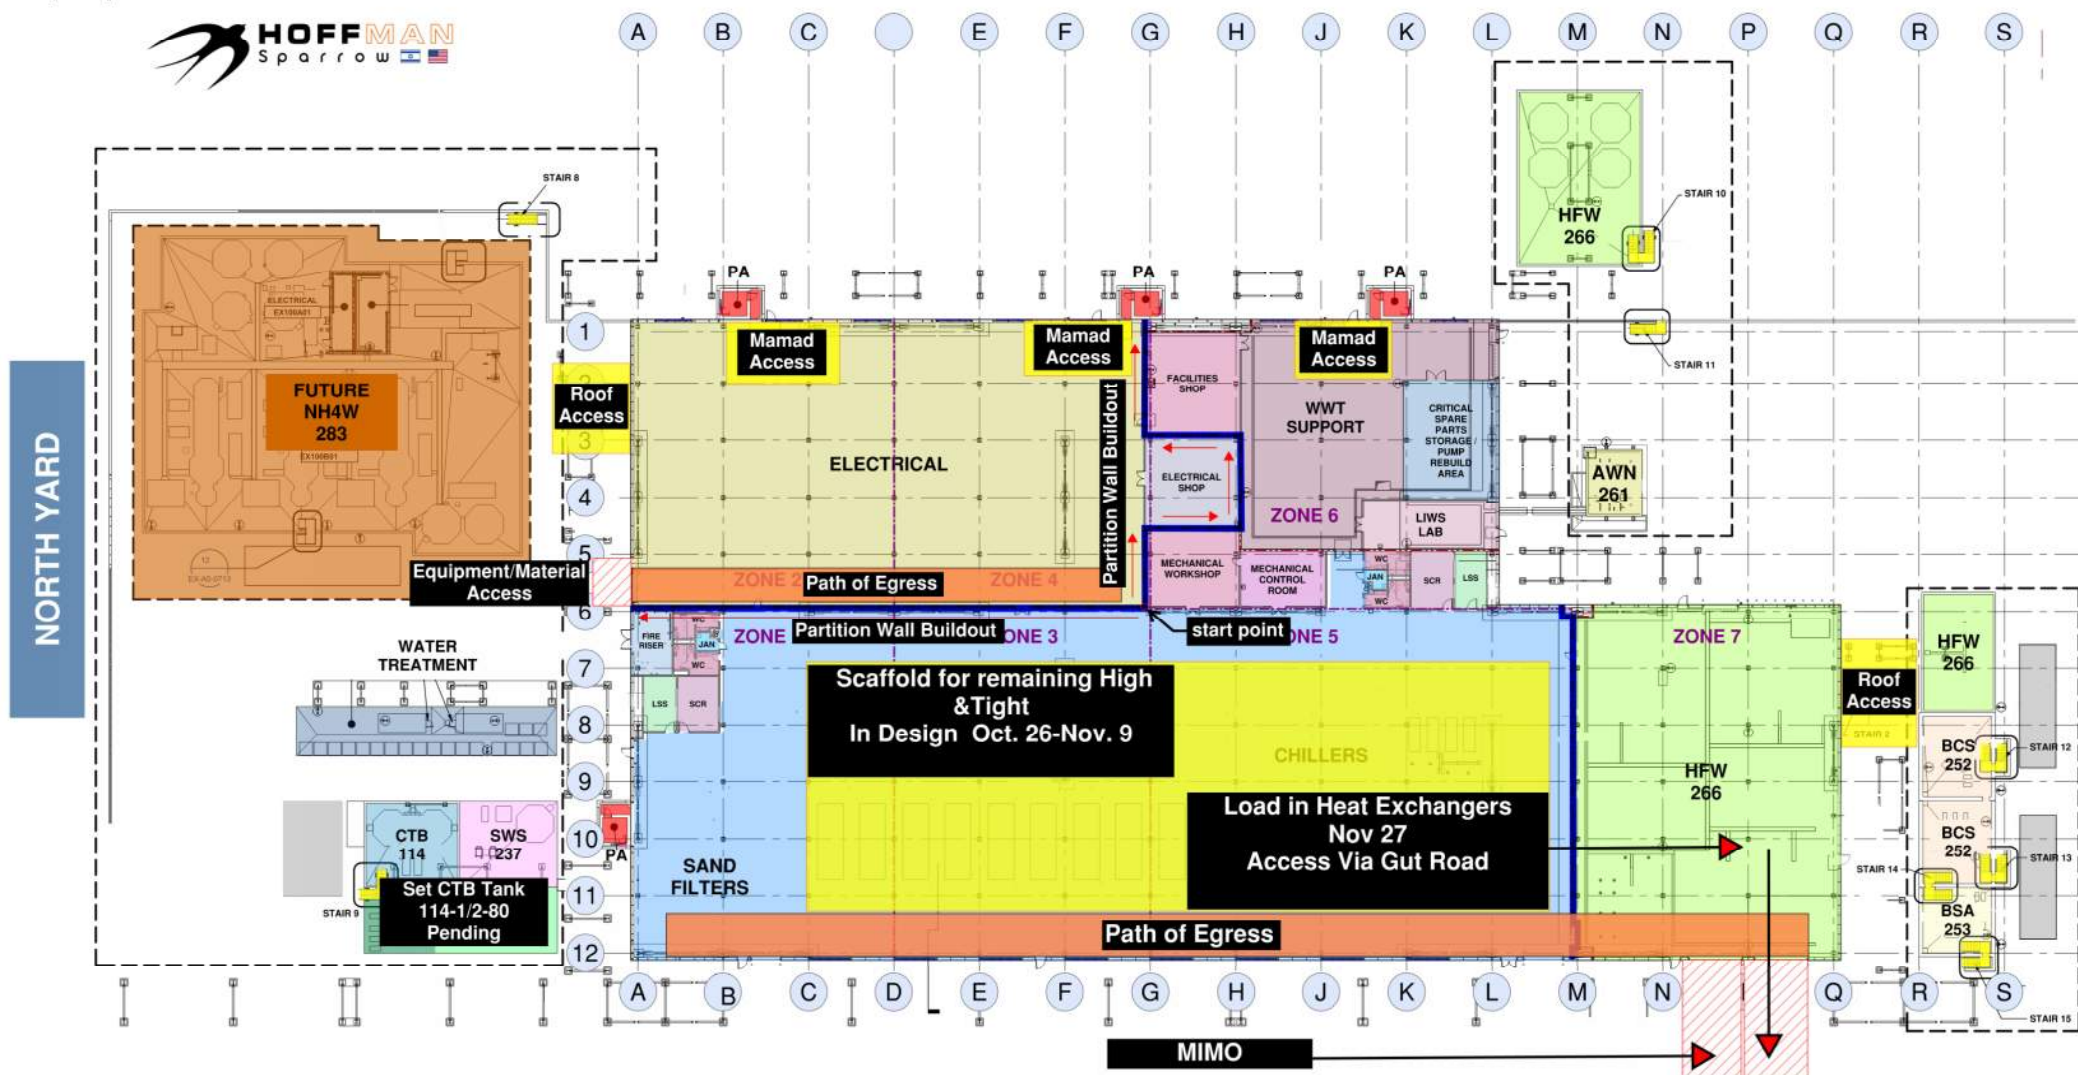

CUB 2 – EXTERIOR/ROOF

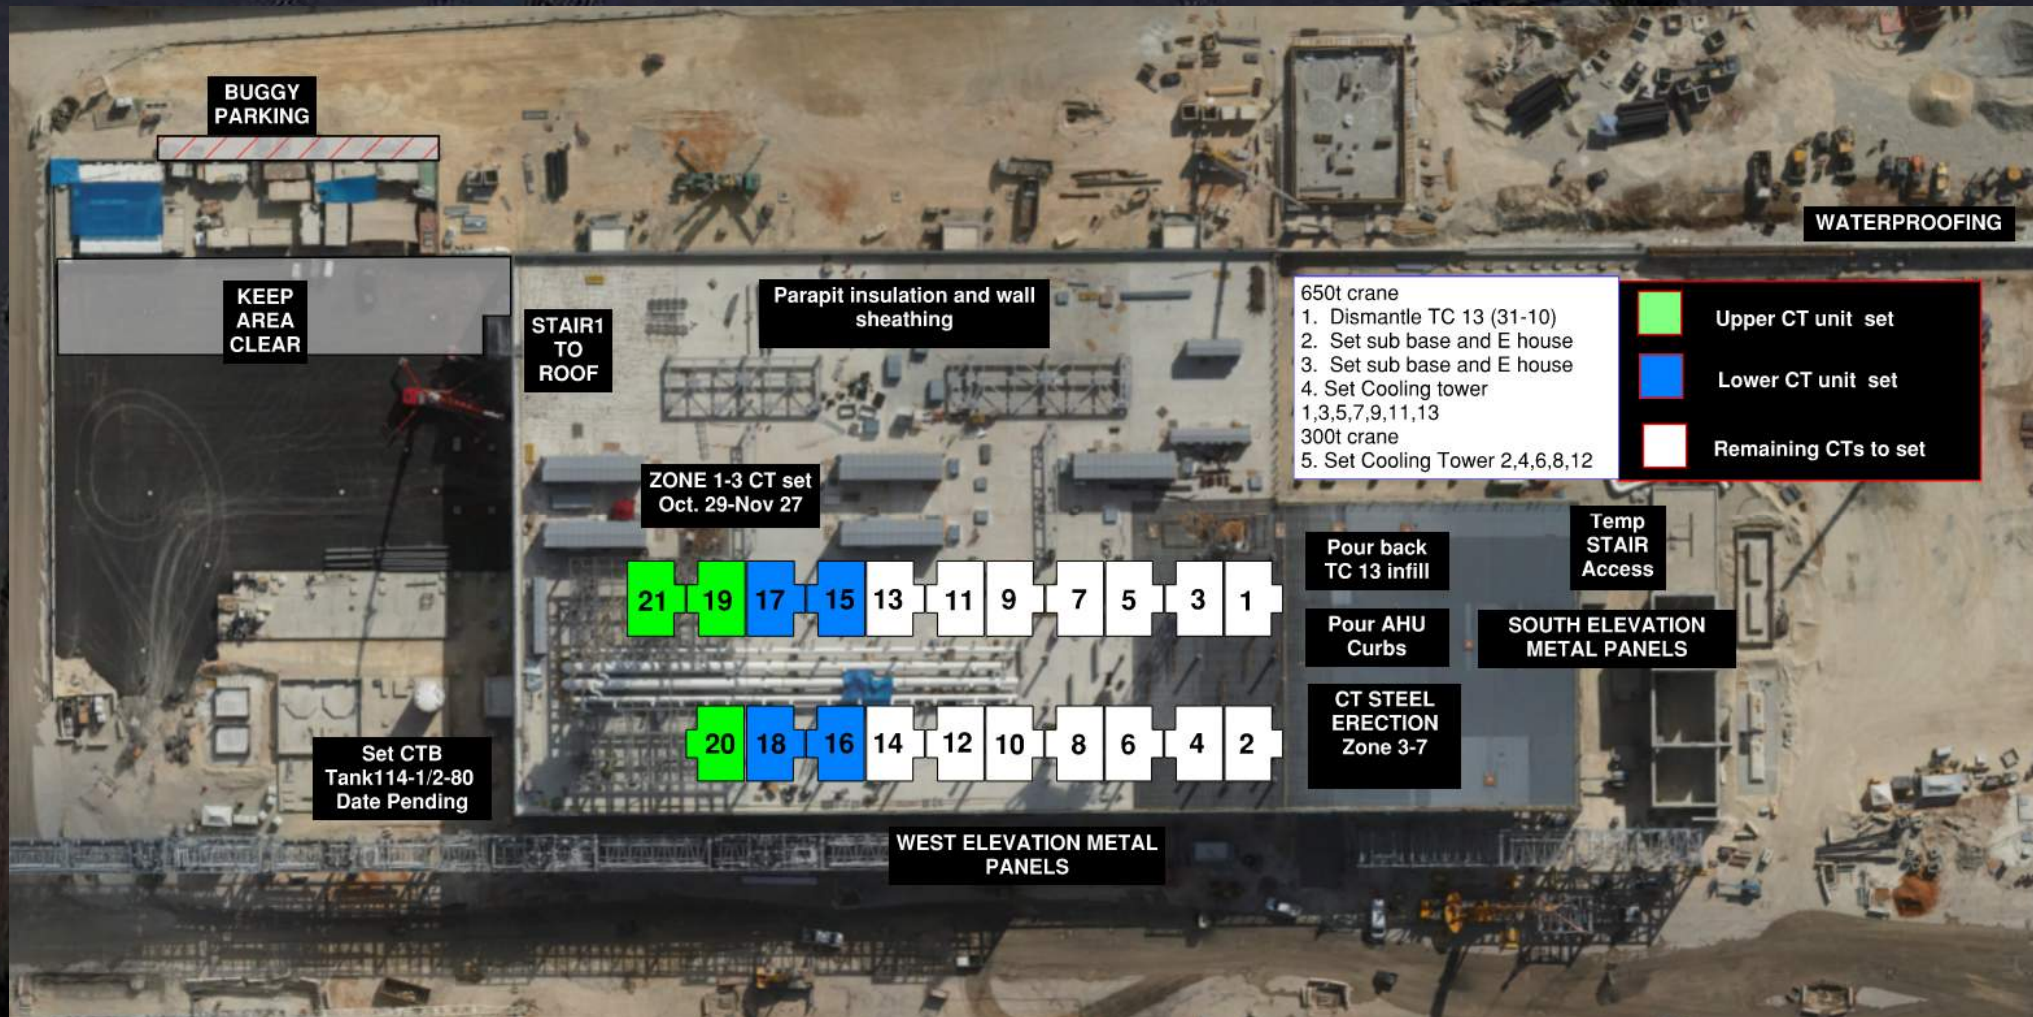

CUB 2 – Crane Logistics

PROPOSE TO ADD
12M JIB
EXTENSION TO
SUPPORT
COOLING TOWER
STEEL ERECTION

NEW RADIUS
SHOWN IN RED

FOR REVIEW





HOFFMAN CONSTRUCTION COMPANY






Daily Coordination Meeting

Site Logistics

North

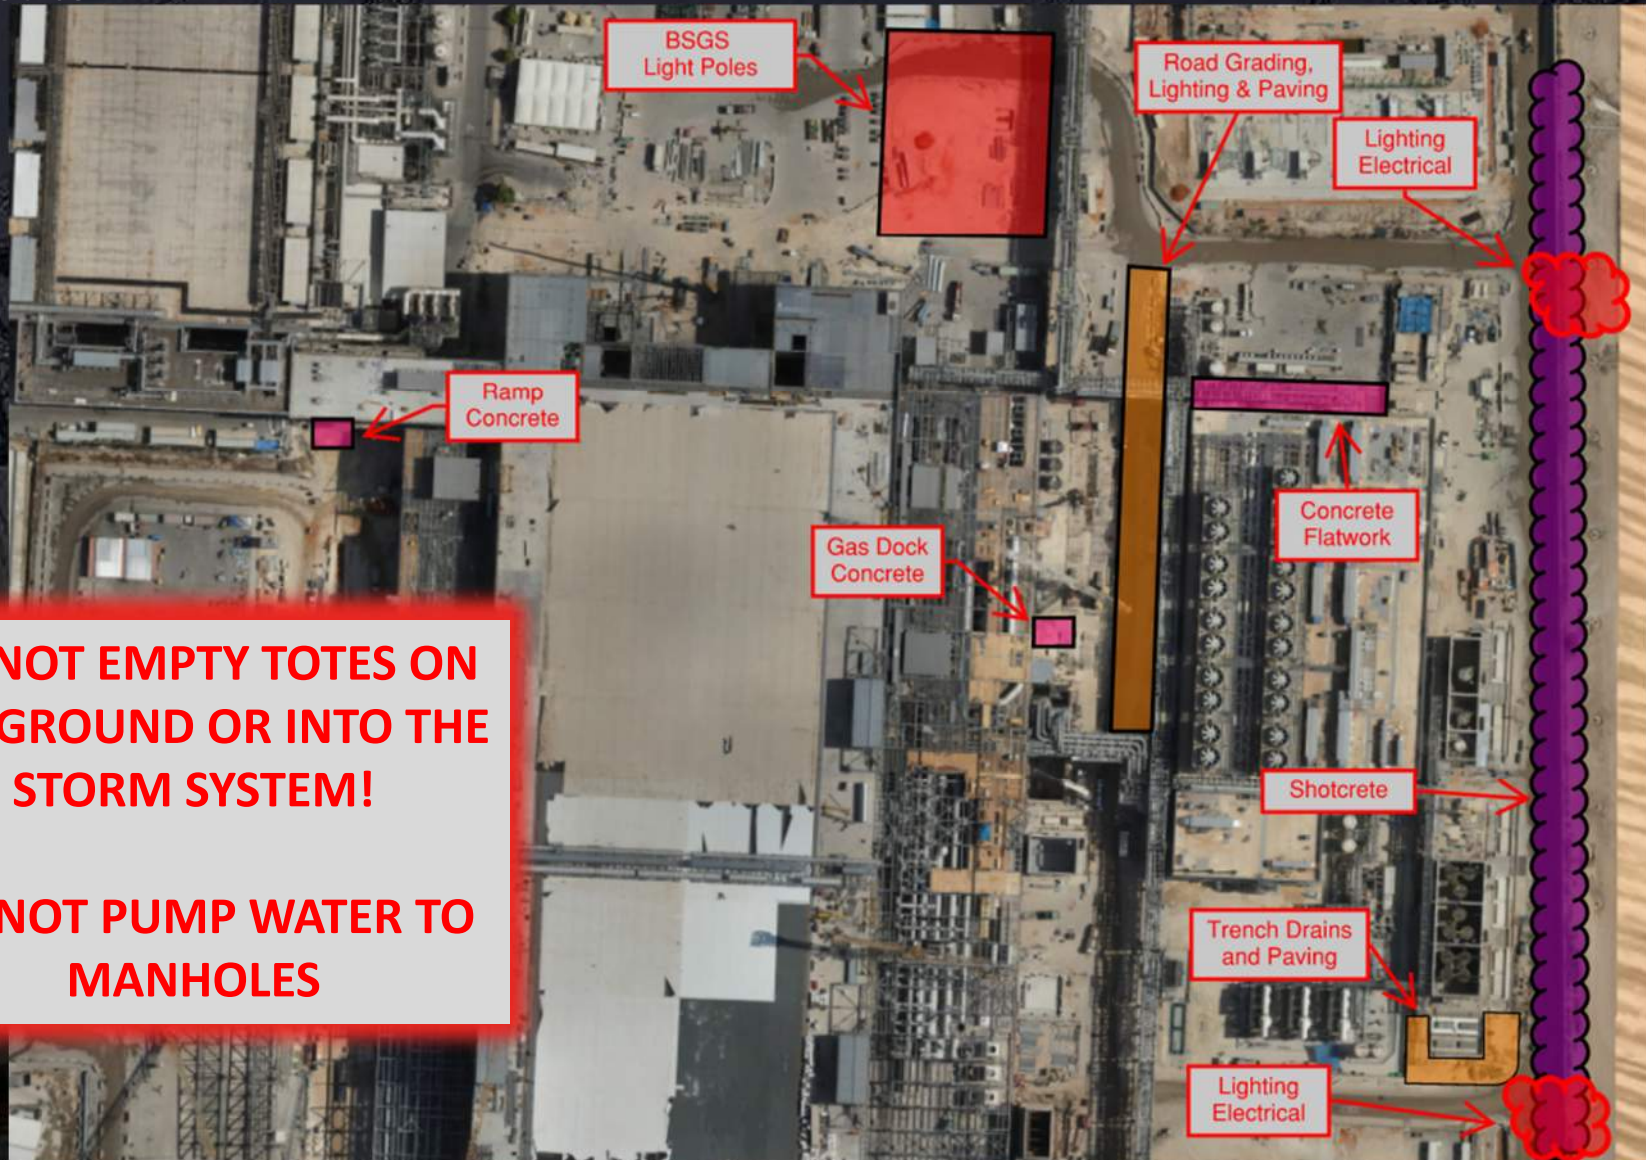

**DO NOT EMPTY TOTES ON
THE GROUND OR INTO THE
STORM SYSTEM!**


**DO NOT PUMP WATER TO
MANHOLES**



Daily Coordination Meeting

Site Logistics

South

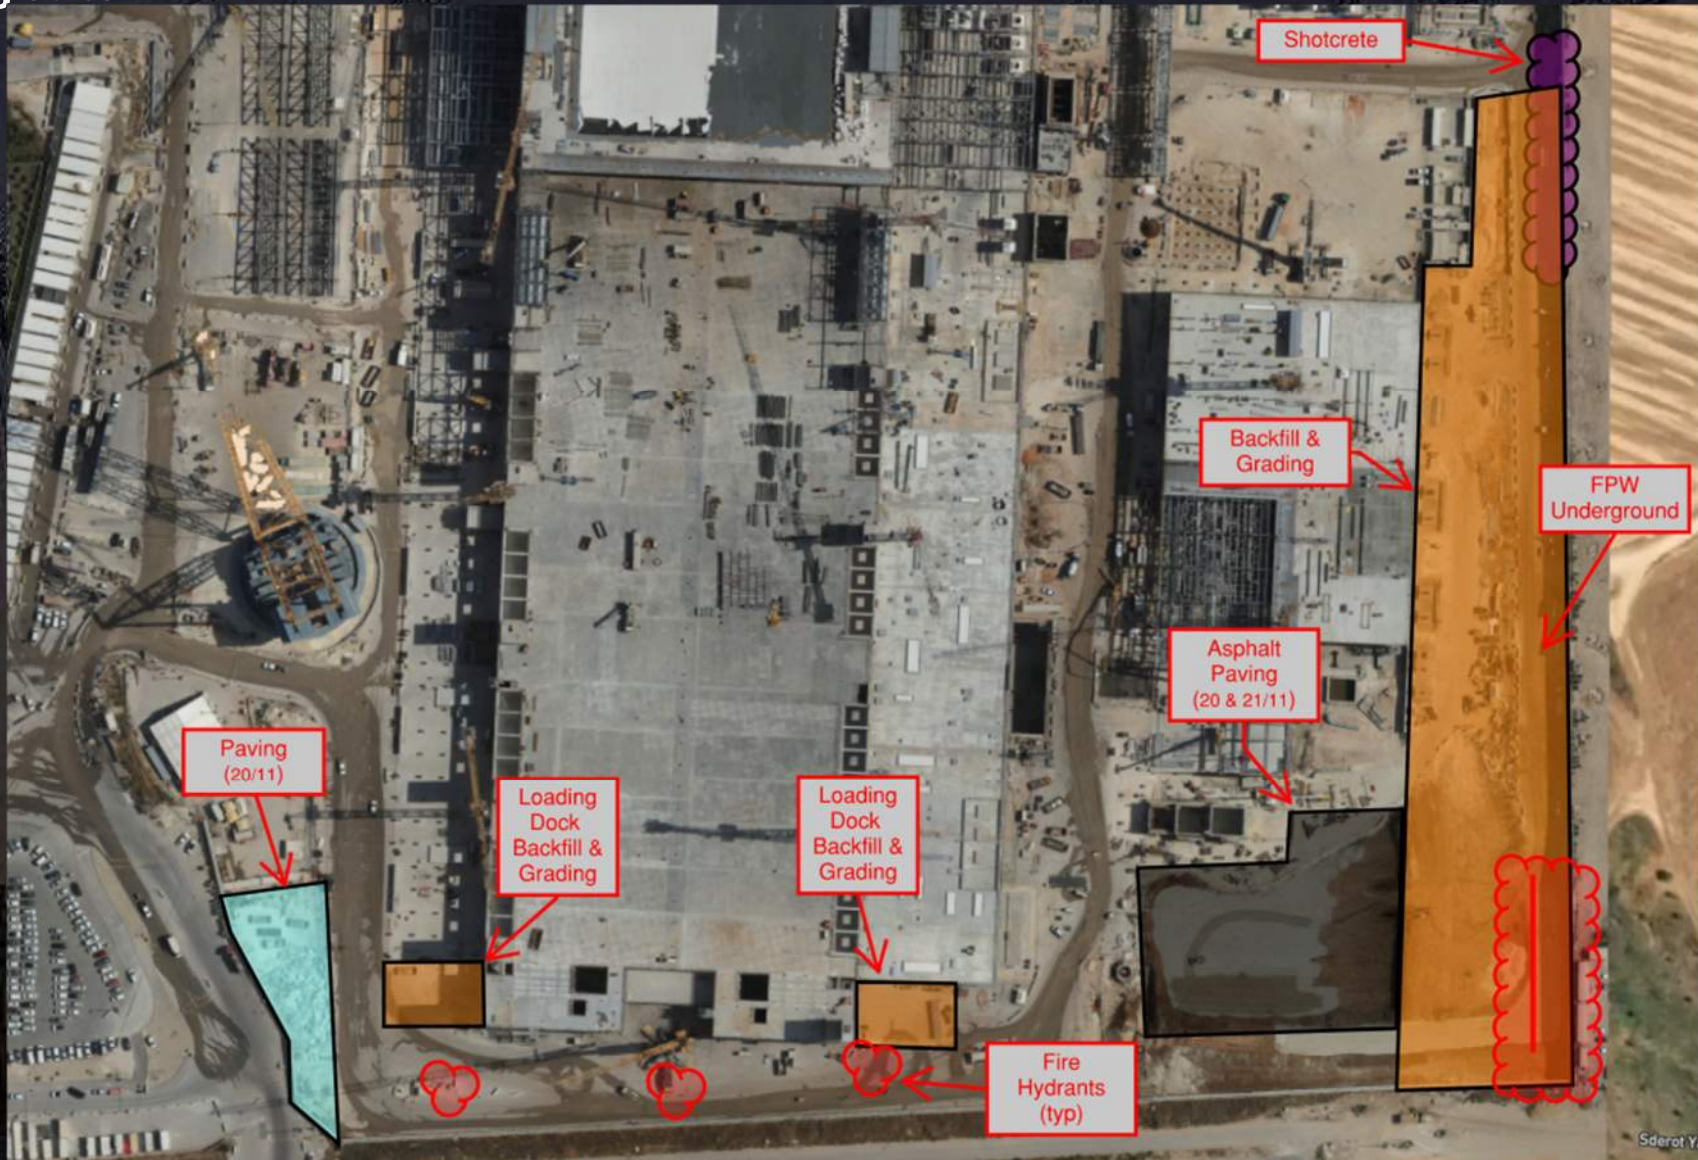




Open CORs by Subcontractor

WW 46 – 575 CORs

WW 47 – 606 CORs

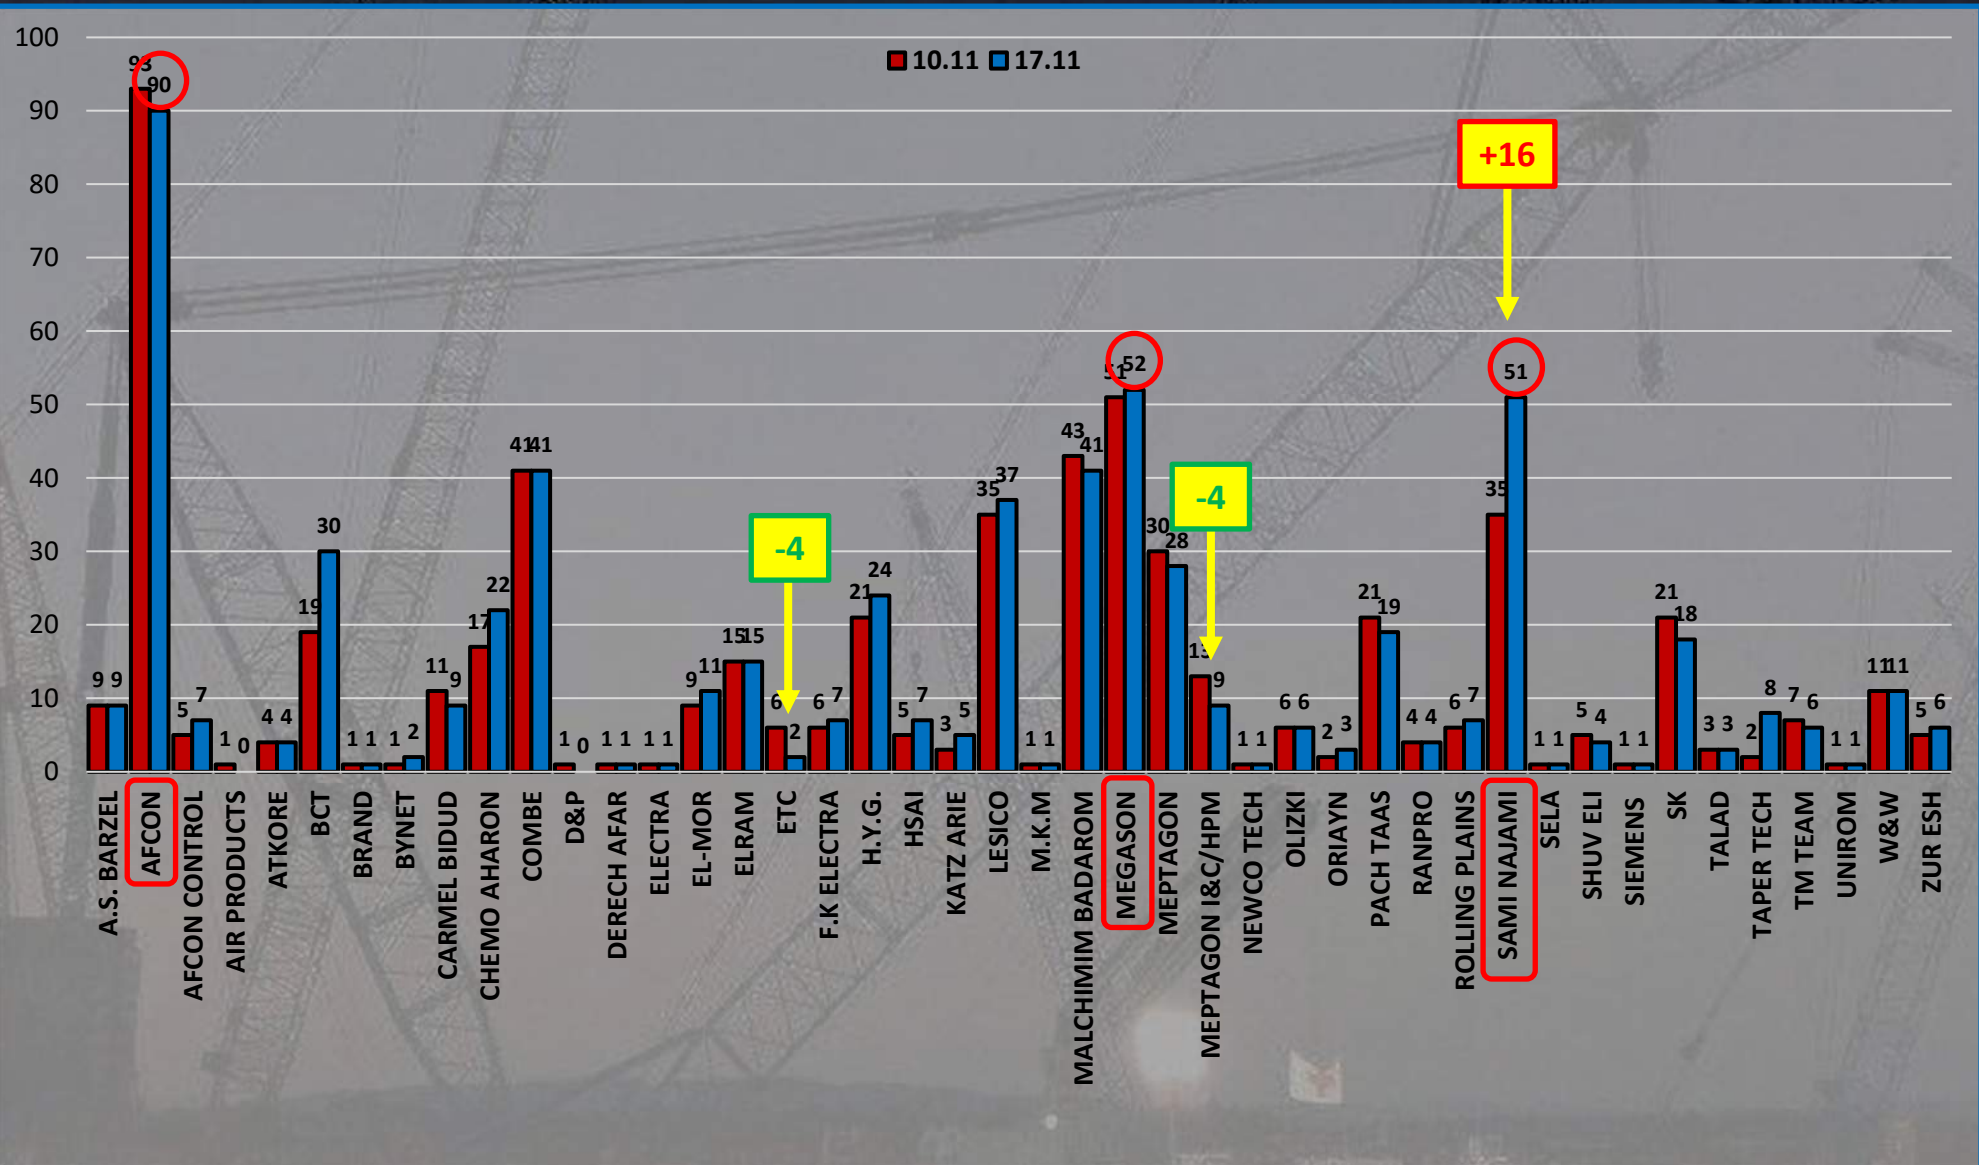




Overdue CORs by Subcontractor

WW 46 – 154 CORs

WW 47 – 182 CORs

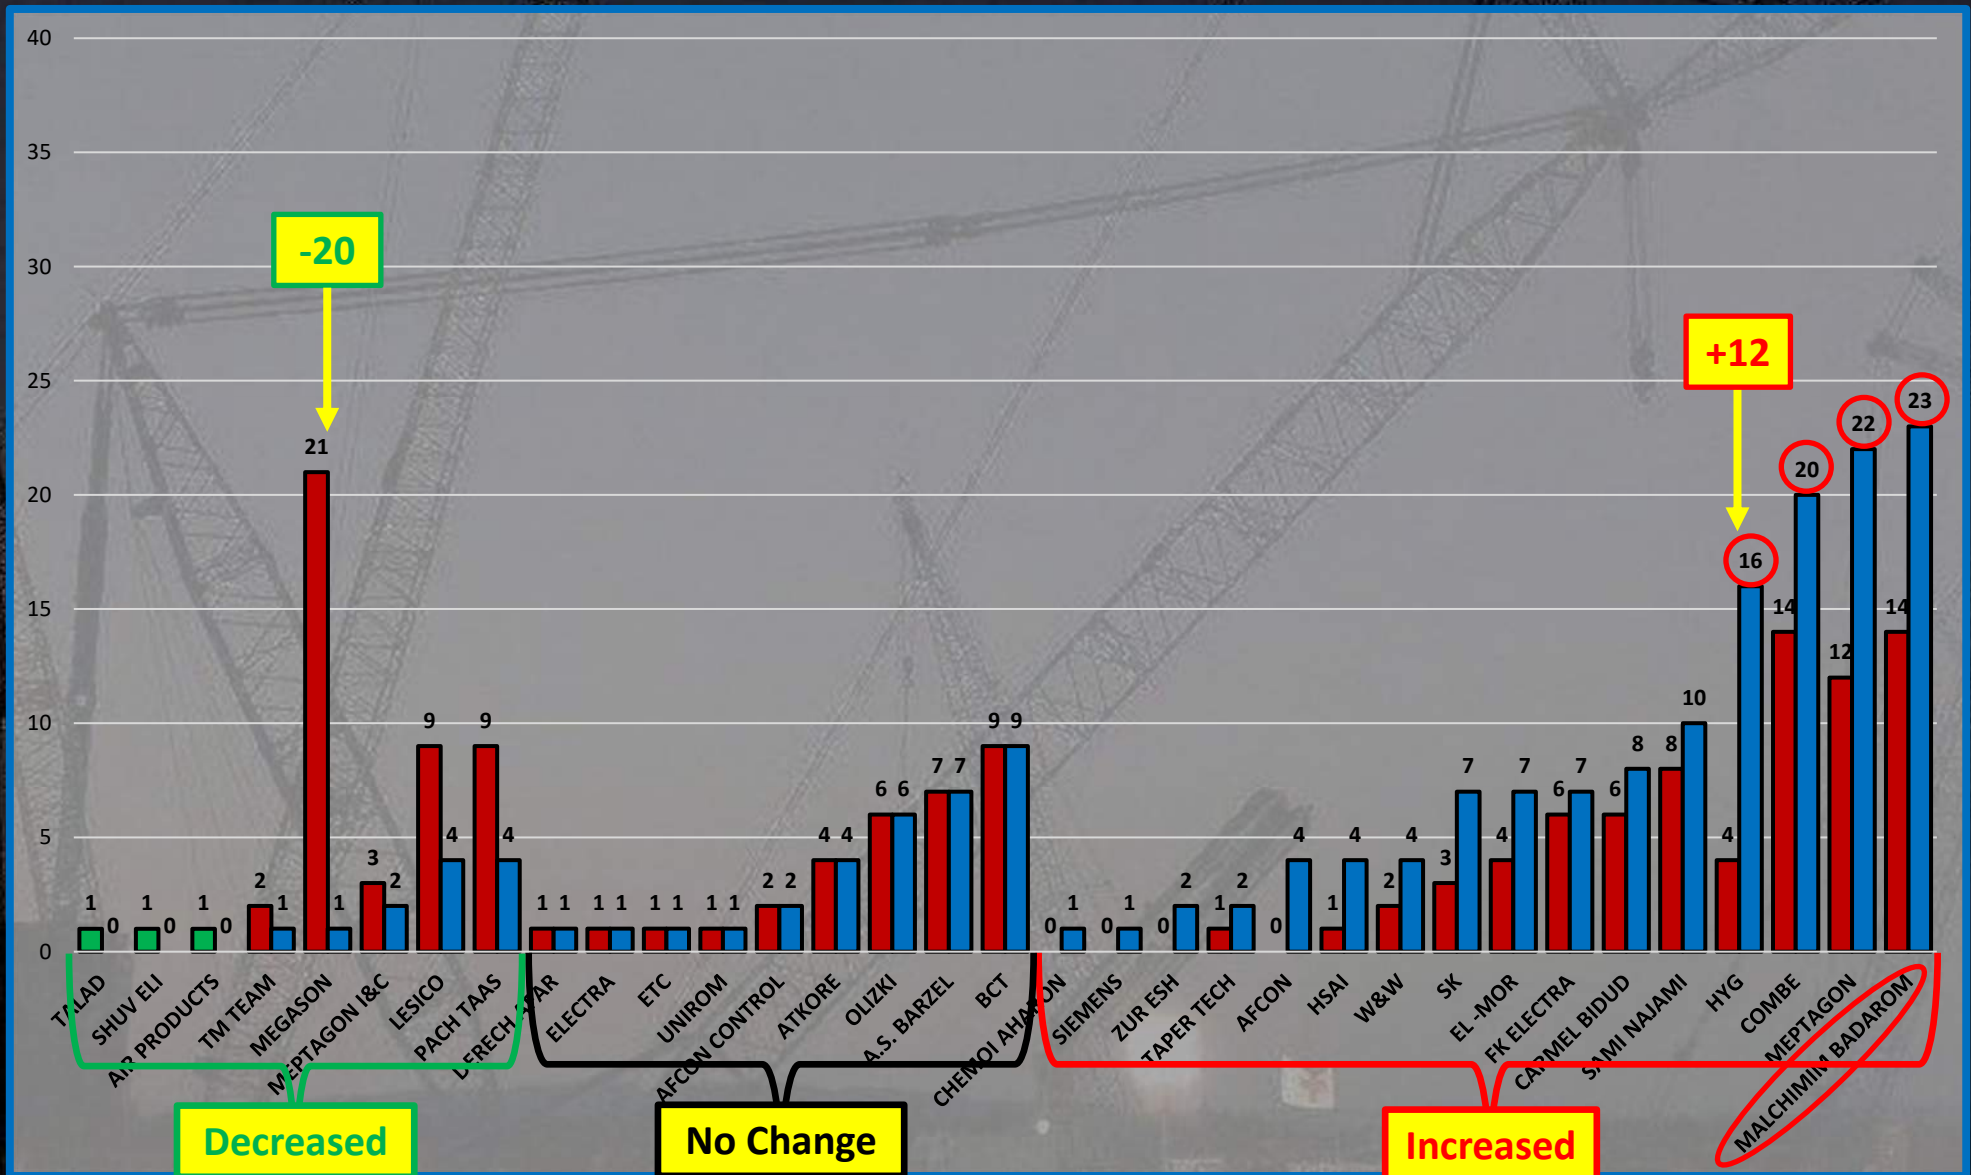


Controlling Hazards

- First step to controlling hazards is to identify them.
- Ensure that we are keeping risk assessments up to date as methods and areas change to identify potential hazards.
- Once hazards are identified we need to be selecting the BEST (not the minimum) controls to protect people from that hazard. For instance, if someone could be cut by something, instead of defaulting to gloves identify if it is feasible to remove the sharp edge or cover it. If someone could trip on something, don't just tell them to watch out for it, remove the tripping hazard.
- If there is a tool that would protect your workers better, it's expected that the tool is used, rather than just relying on people doing their work perfectly and without mistakes.
- We cannot have a defeatist attitude toward controlling hazards. If a hazard is present, we need to be ensuring that our teams have the proper training and tools to either eliminate the hazard, or safeguard against it.

Hierarchy of Controls

- Our project is becoming over reliant on PPE and administrative controls.
- We should instead be focusing our efforts on eliminating or reducing hazards or having engineering controls.
- For example: guardrails are an engineering control.

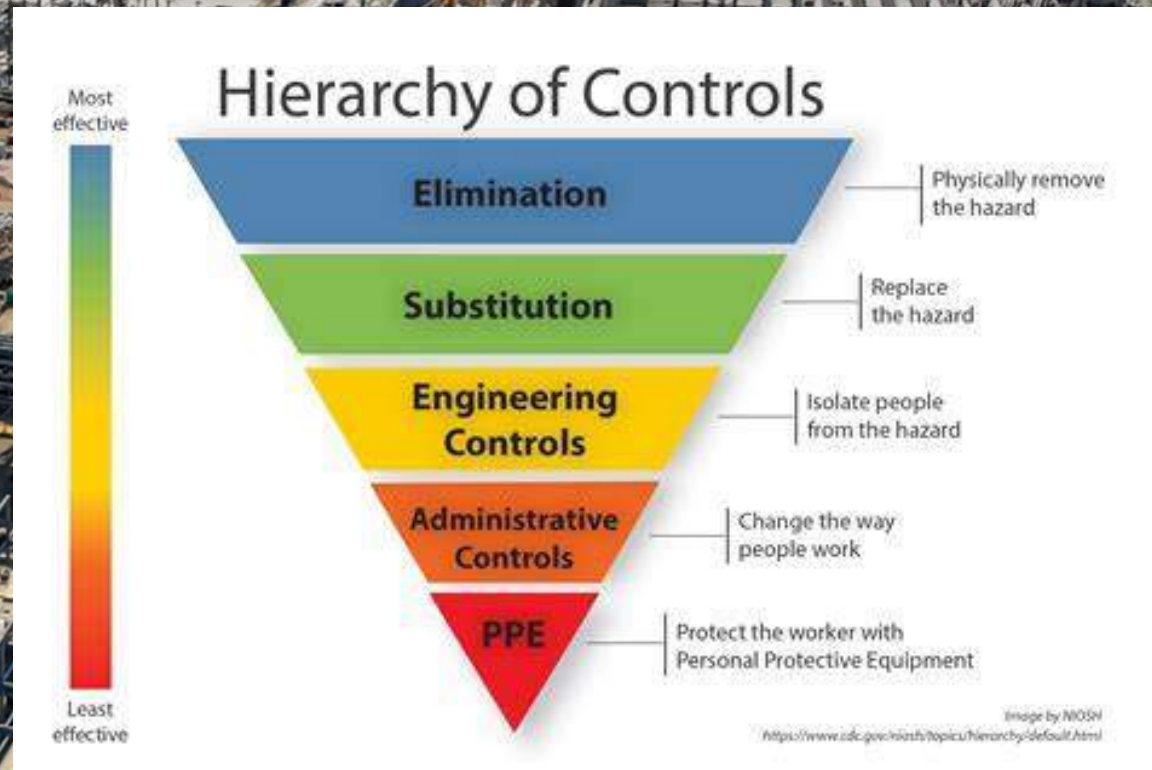

HCC/EHS Weekend Work- 15.11.2024

White Board Meeting in Beavers at 06:30

Superintendents

Fred Dumorne - 052-2506949

Mark McCabe - 052-2294912

Ken Power - 052-2531428

Ori Klain - 052-3764728

Soli N

CSA CM

Leonid Khomich - 053-2722138

Idan Turjeman - 052-4093025

Maor Tzuri - 050-6558817

MEP

Sharon Aronovich - 050-6680986

OSM

Gavin (Patrick) Leamy - 052-3562725

CX/QA

Hadar Swissa - 052-3467273

Cranes

Yossi Attias - 052-3060790

Safety

- Safety Foreman- Hay Halfon- 052-8049342 Hay-Halfon@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional – Anan Ragbe- 058-7708886 Anan-Rajbi@Hoffmancorp.com

Subcontractor Weekend Work- 15.11.2024

FAB

Utility Level / Roof / Stair Shaft

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

SK

Ehs Om 0542072285

Foreman Shy 0545654760

Subfab

- **Pach Taas**

- 1w & 1e mars
- Vadim: 0526229005

- **Afcon E**

- SF LSS rooms
- Raz 0546838626

- **W&W**

- Elevator
- Nick: 0524074972

- **Chemo**

- TTNW RSTM
- Tommy: 0523759408

Clean Room

- Talad – CR 1W – UPN Install, 4E Grating (EHS Marcelo 0523540242, Super Igor 0544509386)
- Sig – 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)
- Elram – CR Level 9,25 line columns , upper shaft wall, TB-TC/25 Columns (EHS Royi 0538312234, Super Bonio 0544236899)
- Afcon – CR – 2E boxes 2W module, 5W supports, 3E lighting, 1W -1E cable pilling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Rolling Plains – INT NTT 5RA, Marshaft 3E, 5RA, MOD2 CA CD17,24,10 (Super Cordin 0546594273, EHS Ovidiu 0546993648)
- Chemo – INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS Lila - 0547886704, Supervisor Winai – 0528090588)
- Talent – CR Level 1E/2E – Superclean (Supervisor Netanel 0536210487 EHS – Hasan 0542662054)
- Sela – 1E-1W CRC (Supervisor David 0524382997, EHS Shmuel – 0506306031)
- IDP - Safety Officer: Shmuel Kushnir,
Phone: 050-630-6031
Supervisor: Avichai Timsit, Phone: 050-944-4945
Activity: Roofing the structure on the western side of the cleanroom using a boom lift

Subcontractor Weekend Work- 15.11.2024

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 1-3P
- Foreman – Vadim – 053-5552472
- Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling 1-5P UL and 1-3P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 1-5P
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- W&W – SEQ 135, 138 (lift 3 3P)
- Foreman – Willie – 052-6145521
- Safety – Gary Lambert – 1-405-833-8910
- Elram – 1P and 2P Exit Passage Ceiling
- Foreman – ???
- Safety – ???
- Combe UPW – UPW Room Piping and Yard
- Foreman – Boris – 054-8346412
- Safety – Shimon – 054-5348843
- Carmel Duct – 5P UL, 4P Roof, UPW room
- Foreman – Hitam –
- Safety – ???
- SK Engineering – GL4 Rack UL, Lift 2 2P Piping
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112

WJG

W&W – Steel Erection 5J lift 2 Erection / Detail Work

Foreman: Chris Isaac 052 588 3215

Safety: Moshe 054 801 2959

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 4J Lift 2 Piping

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

SK:

Foreman: Taufik: 054 94333592

Pach Taas: UL Ductwork

SIG

Foreman: Roman: 054 797 2205

Safety: Alex 054 797 9219

Siding

Sami Najami

Abed 054-5501880

Subcontractor Weekend Work- 15.11.2024

CUB

H.S.A.I:

CUB 1: at southeast corner .

CUB 2: at roof & north yard.

contact person : Serghei: 055-272-8807

Brand:

In the southwest corner of Cub 2, work is underway to cover panels.

contact person: Dima: 050-9958780

Sela:

south yard of cub 1 – NH4W & TOL 6+7

contact person: David: 052-4382997, Shmuel: 050-6306031

Sami Najami:

CUB 1: electrical room and roof.

contact person: Ibraheem : 054-9571402, Matan: 050-9895008.

Trestle

Sami Najami

19 employees

Matan Alon is a safety

Mochals Atallah - foreman

GIS/NEY

Site

Derech Afa – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Olizki –

Sweepers and water trucks, backfill CUB2 south & offload 18

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
