

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:





Scrubber topping slab
5:00 am

Parapet wall stair 1 roof
6:00 am

Scrubber topping
slab
5:00 am


Parapet wall stair 1
6:00 am

Intel Kinyat Gat

FAB-26

Intel

UTILITY LEVEL TRUSS

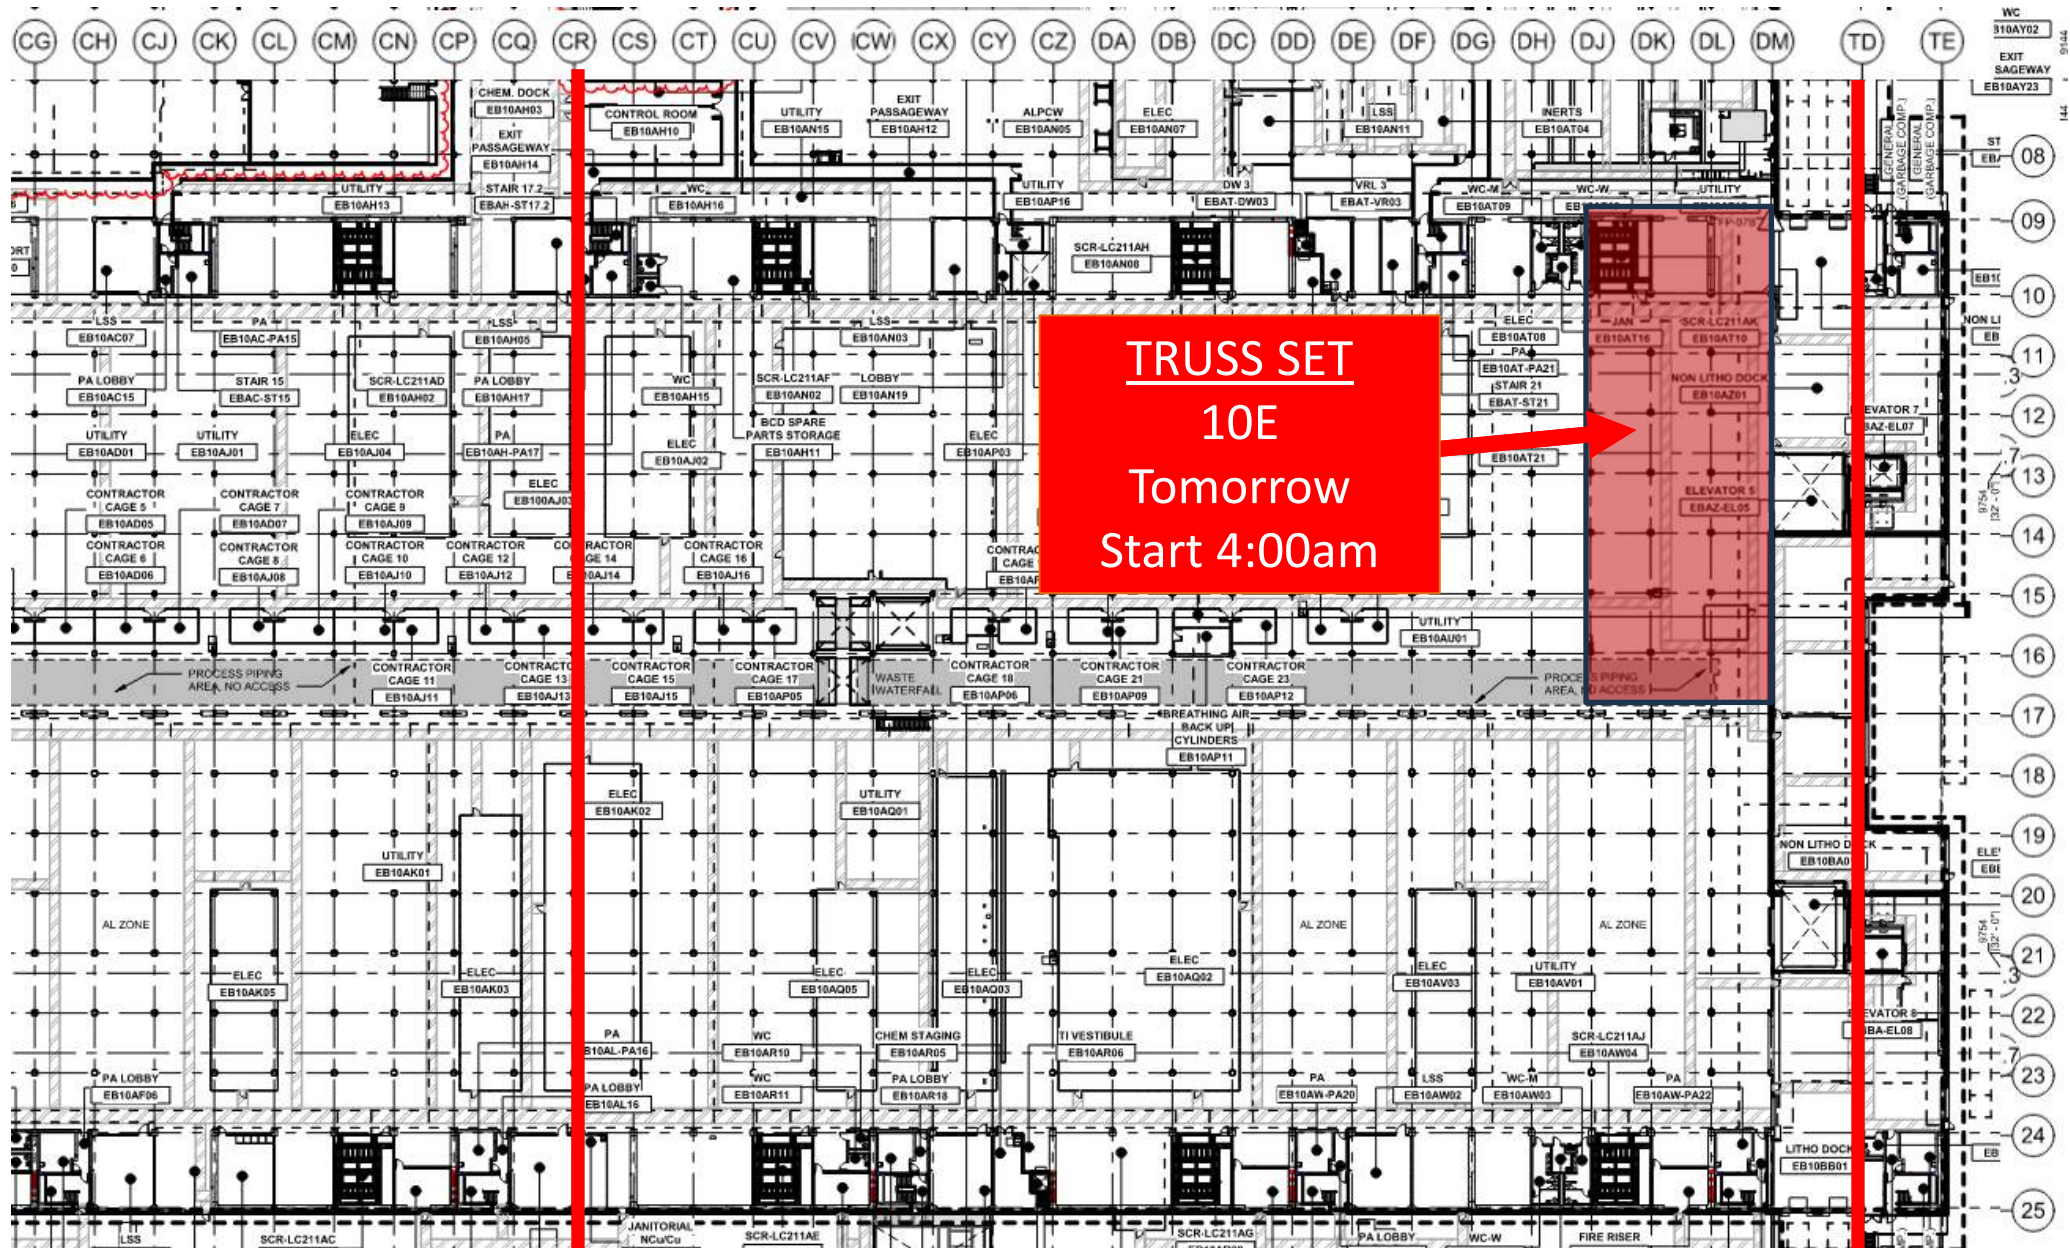



A detailed floor plan of a building, likely a data center or industrial facility, showing various rooms, corridors, and equipment. The plan is color-coded with yellow, green, and purple areas. A green callout box with a white arrow points to a specific location in the upper right quadrant of the plan. The text inside the box reads:

Heat coil rep.
Afcorn remove cable tray
Start 12/2

The plan includes numerous labels for rooms and equipment, such as "ELEVATOR 1", "ELEVATOR 2", "ELEVATOR 3", "ELEVATOR 4", "ELEVATOR 5", "ELEVATOR 6", "ELEVATOR 7", "ELEVATOR 8", "ELEVATOR 9", "ELEVATOR 10", "ELEVATOR 11", "ELEVATOR 12", "ELEVATOR 13", "ELEVATOR 14", "ELEVATOR 15", "ELEVATOR 16", "ELEVATOR 17", "ELEVATOR 18", "ELEVATOR 19", "ELEVATOR 20", "ELEVATOR 21", "ELEVATOR 22", "ELEVATOR 23", "ELEVATOR 24", "ELEVATOR 25", "ELEVATOR 26", "ELEVATOR 27", "ELEVATOR 28", "ELEVATOR 29", "ELEVATOR 30", "ELEVATOR 31", "ELEVATOR 32", "ELEVATOR 33", "ELEVATOR 34", "ELEVATOR 35", "ELEVATOR 36", "ELEVATOR 37", "ELEVATOR 38", "ELEVATOR 39", "ELEVATOR 40", "ELEVATOR 41", "ELEVATOR 42", "ELEVATOR 43", "ELEVATOR 44", "ELEVATOR 45", "ELEVATOR 46", "ELEVATOR 47", "ELEVATOR 48", "ELEVATOR 49", "ELEVATOR 50", "ELEVATOR 51", "ELEVATOR 52", "ELEVATOR 53", "ELEVATOR 54", "ELEVATOR 55", "ELEVATOR 56", "ELEVATOR 57", "ELEVATOR 58", "ELEVATOR 59", "ELEVATOR 60", "ELEVATOR 61", "ELEVATOR 62", "ELEVATOR 63", "ELEVATOR 64", "ELEVATOR 65", "ELEVATOR 66", "ELEVATOR 67", "ELEVATOR 68", "ELEVATOR 69", "ELEVATOR 70", "ELEVATOR 71", "ELEVATOR 72", "ELEVATOR 73", "ELEVATOR 74", "ELEVATOR 75", "ELEVATOR 76", "ELEVATOR 77", "ELEVATOR 78", "ELEVATOR 79", "ELEVATOR 80", "ELEVATOR 81", "ELEVATOR 82", "ELEVATOR 83", "ELEVATOR 84", "ELEVATOR 85", "ELEVATOR 86", "ELEVATOR 87", "ELEVATOR 88", "ELEVATOR 89", "ELEVATOR 90", "ELEVATOR 91", "ELEVATOR 92", "ELEVATOR 93", "ELEVATOR 94", "ELEVATOR 95", "ELEVATOR 96", "ELEVATOR 97", "ELEVATOR 98", "ELEVATOR 99", "ELEVATOR 100".

Heat coil rep.
Afcon remove cable tray
Start 12/2

BELFOR Mold remediation


ELRAM

MEP+Elctrical
Ready for re-install




MALHIMIM
9E & 8W
Ongoing


SUT 38.1 LEVEL

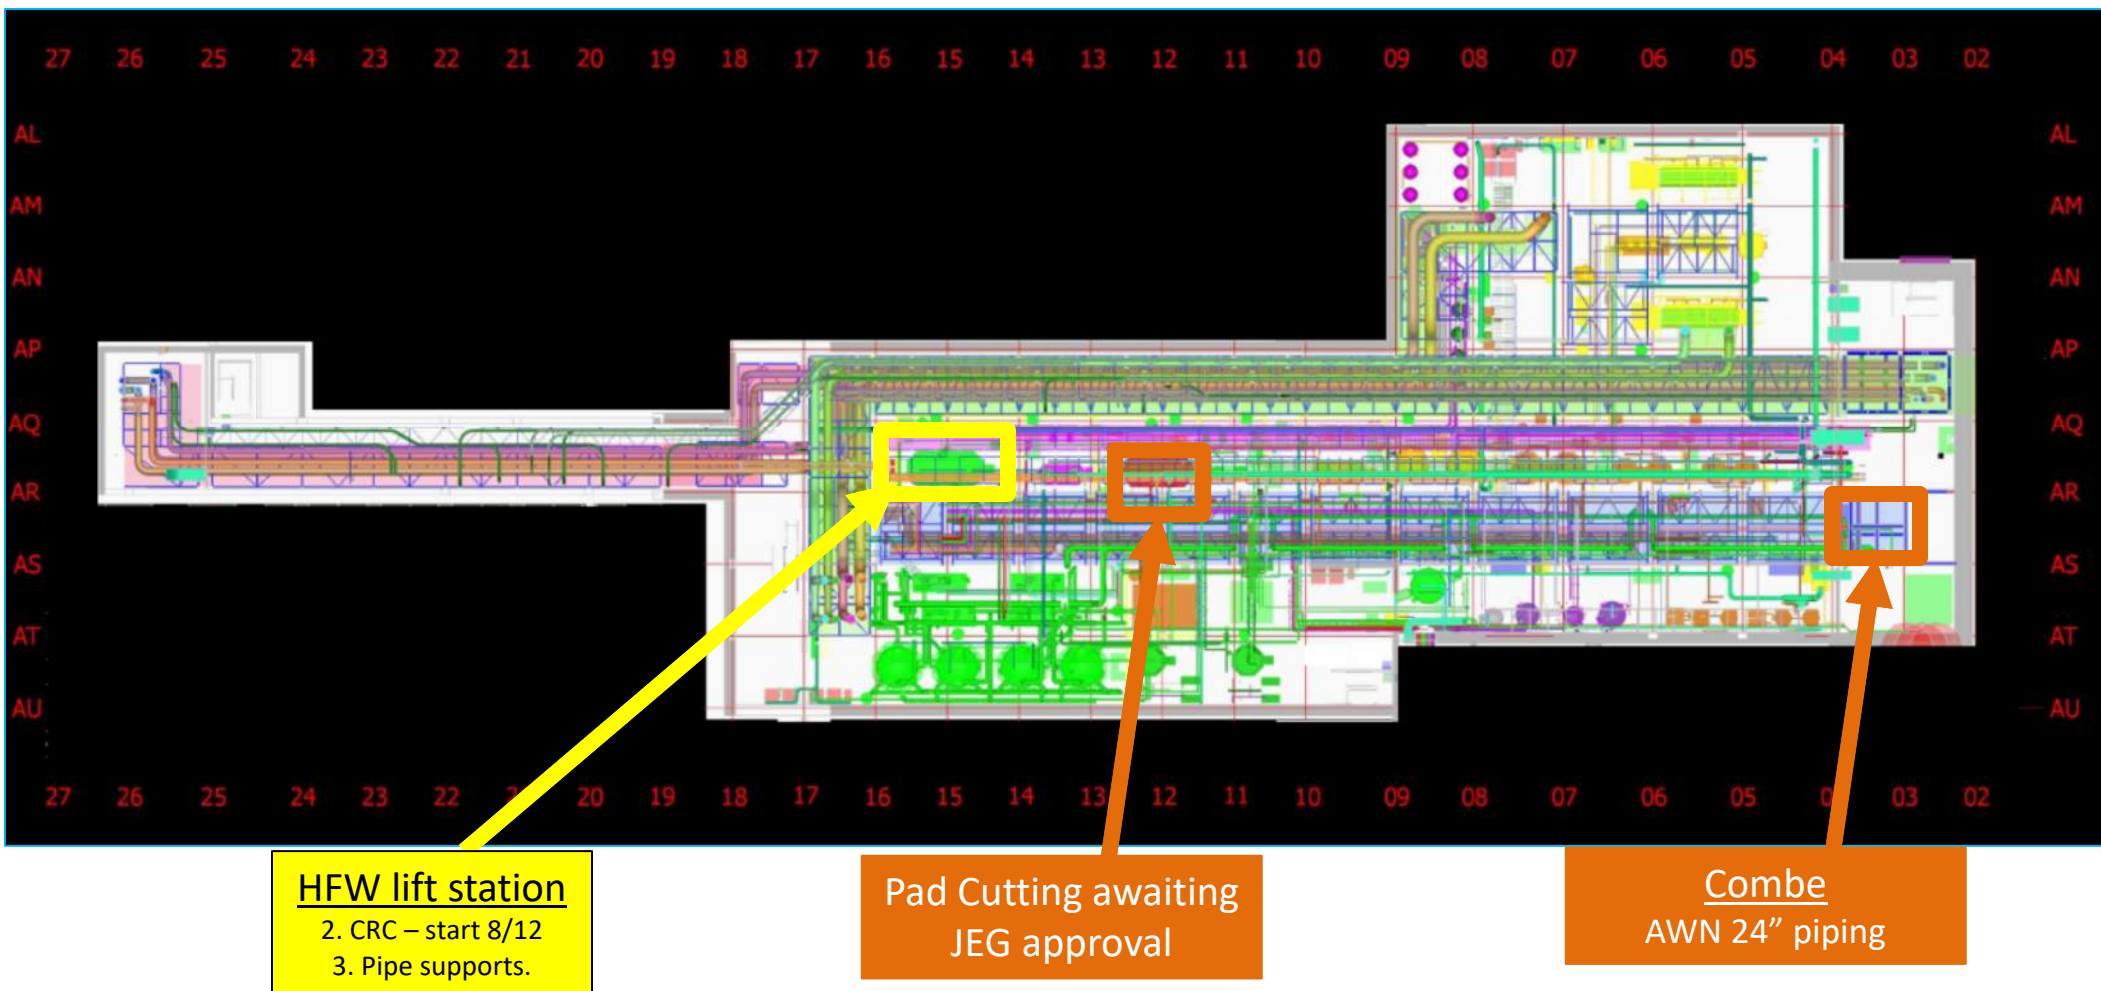


SUT 38.2 LEVEL

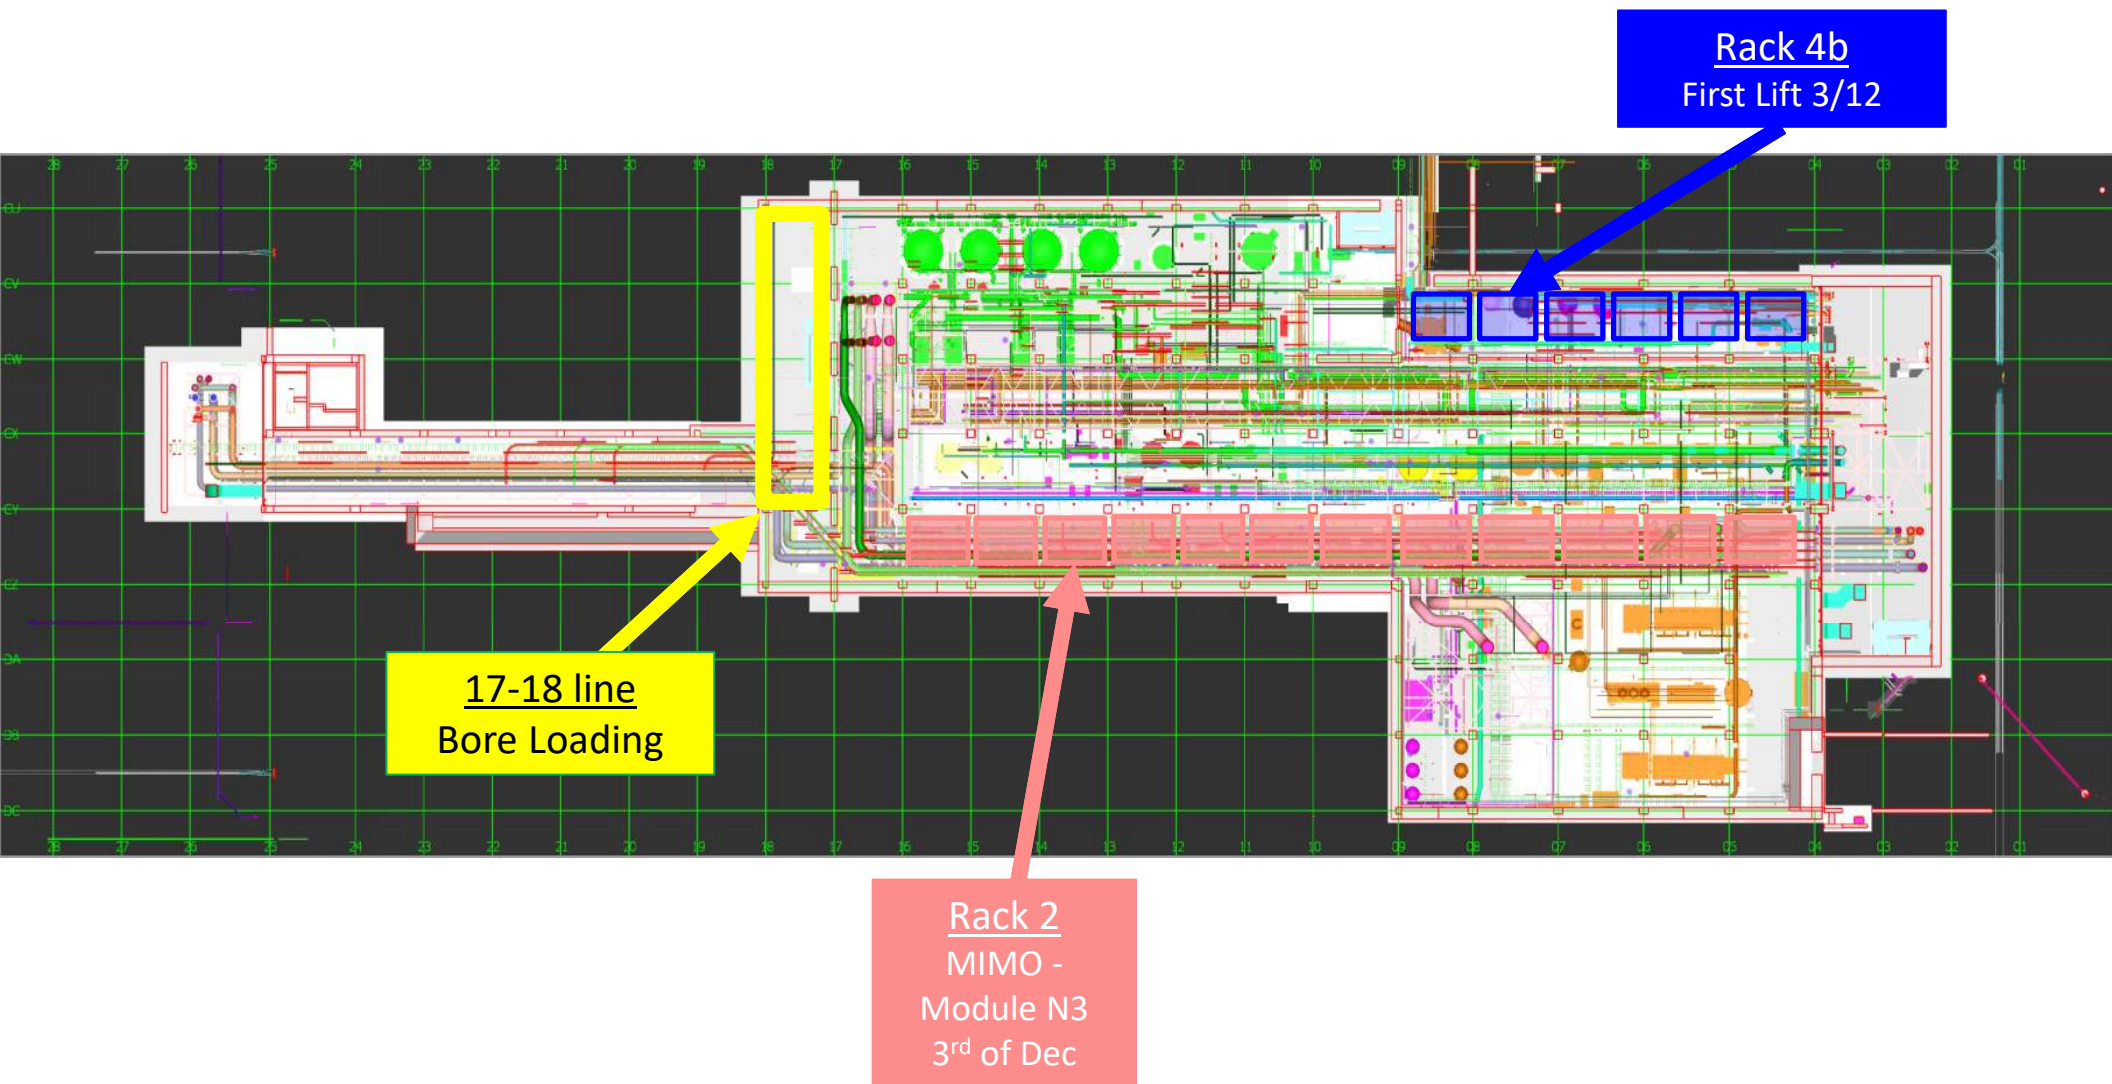


SUBFAB BUILDOUT MOD 1

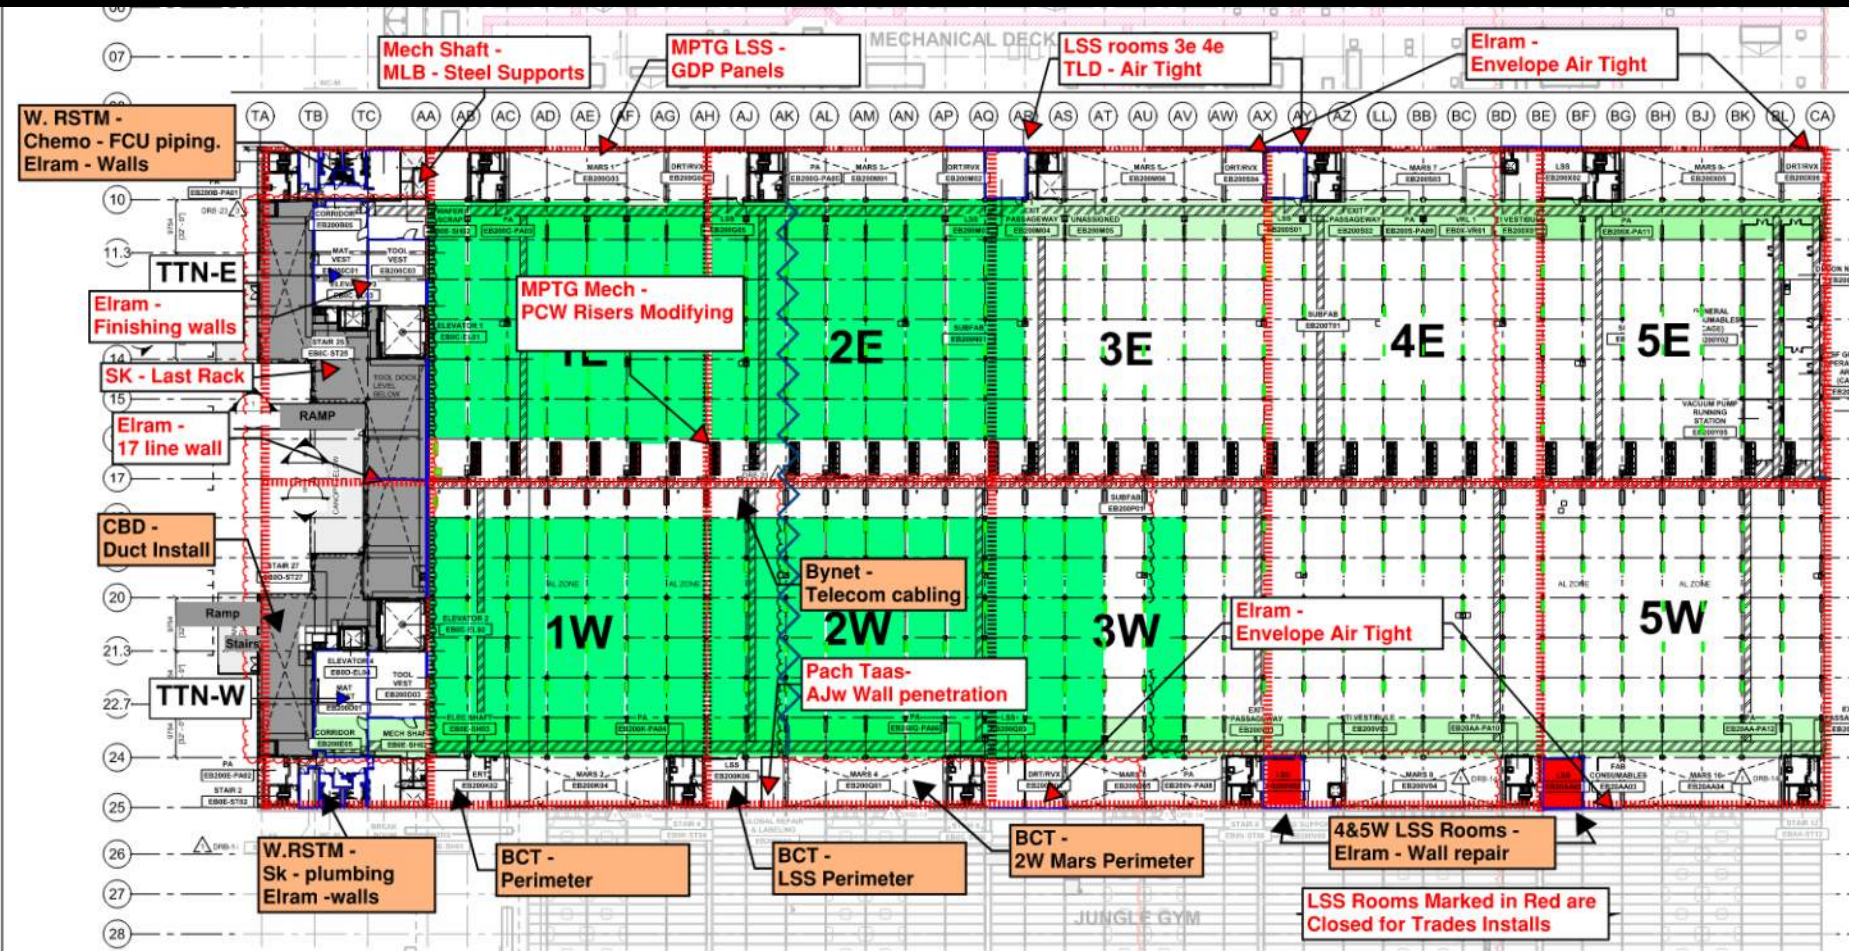


SUBFAB CRC TOPCOAT

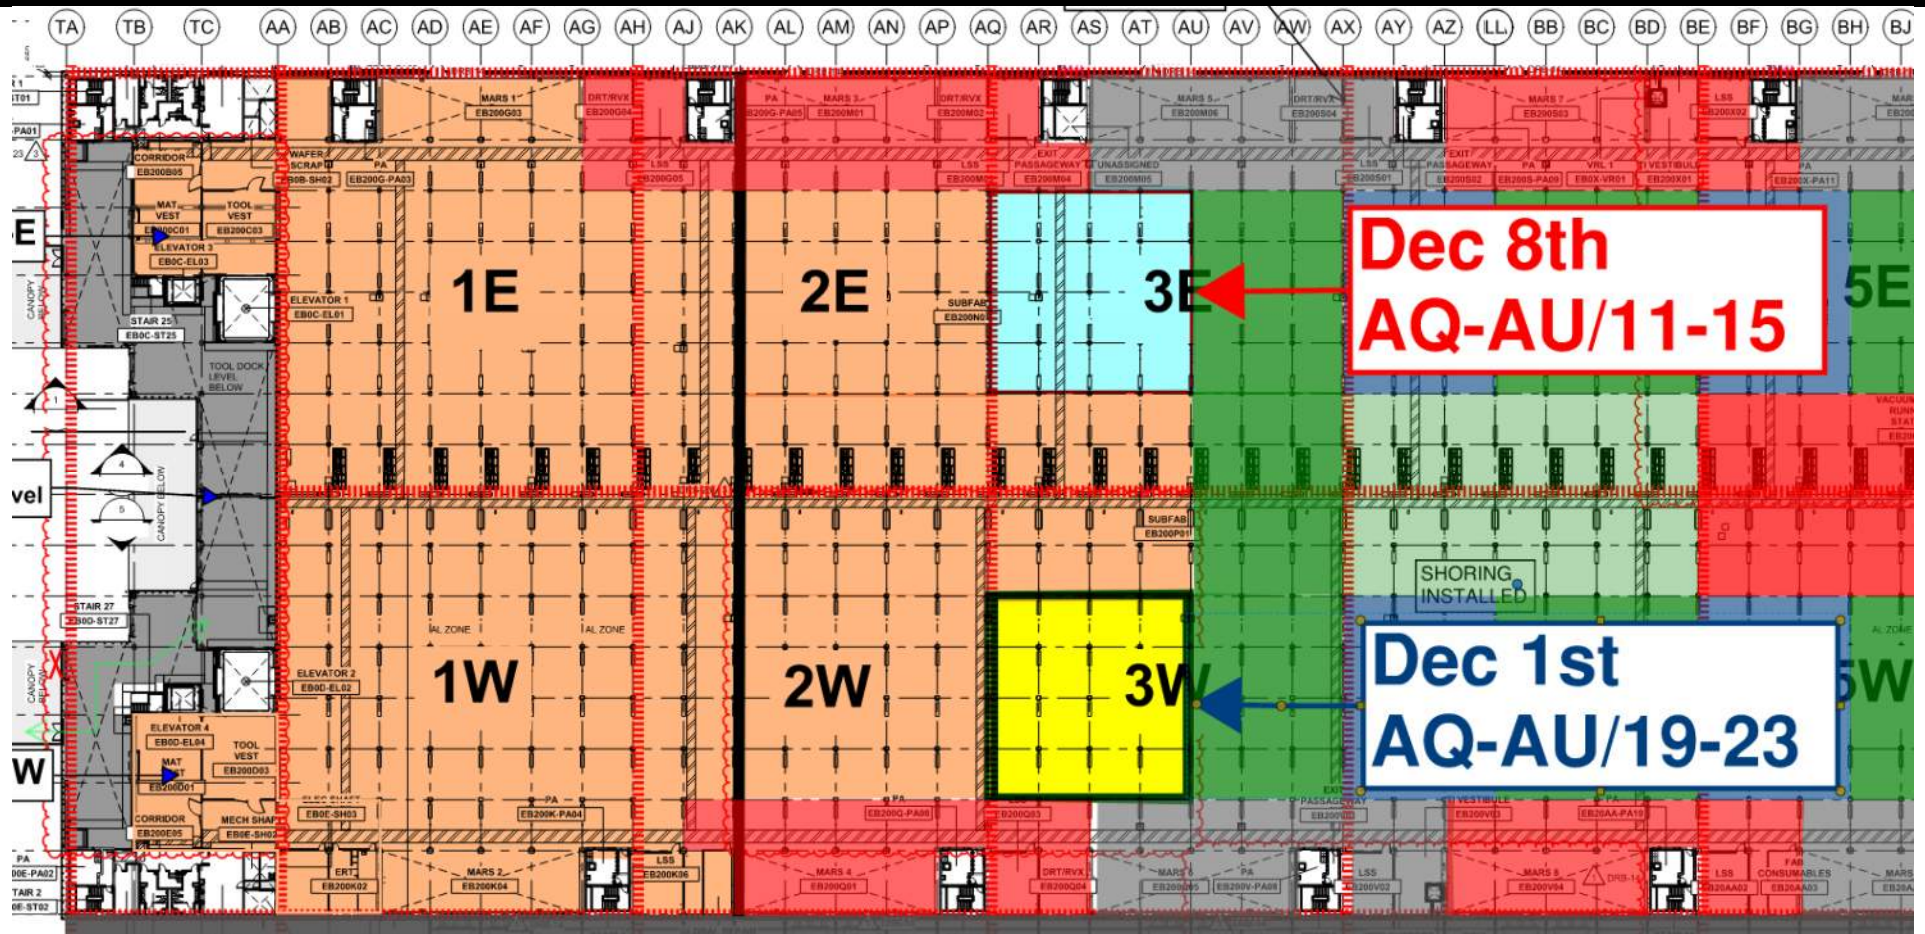


BCT Pressure Test Today

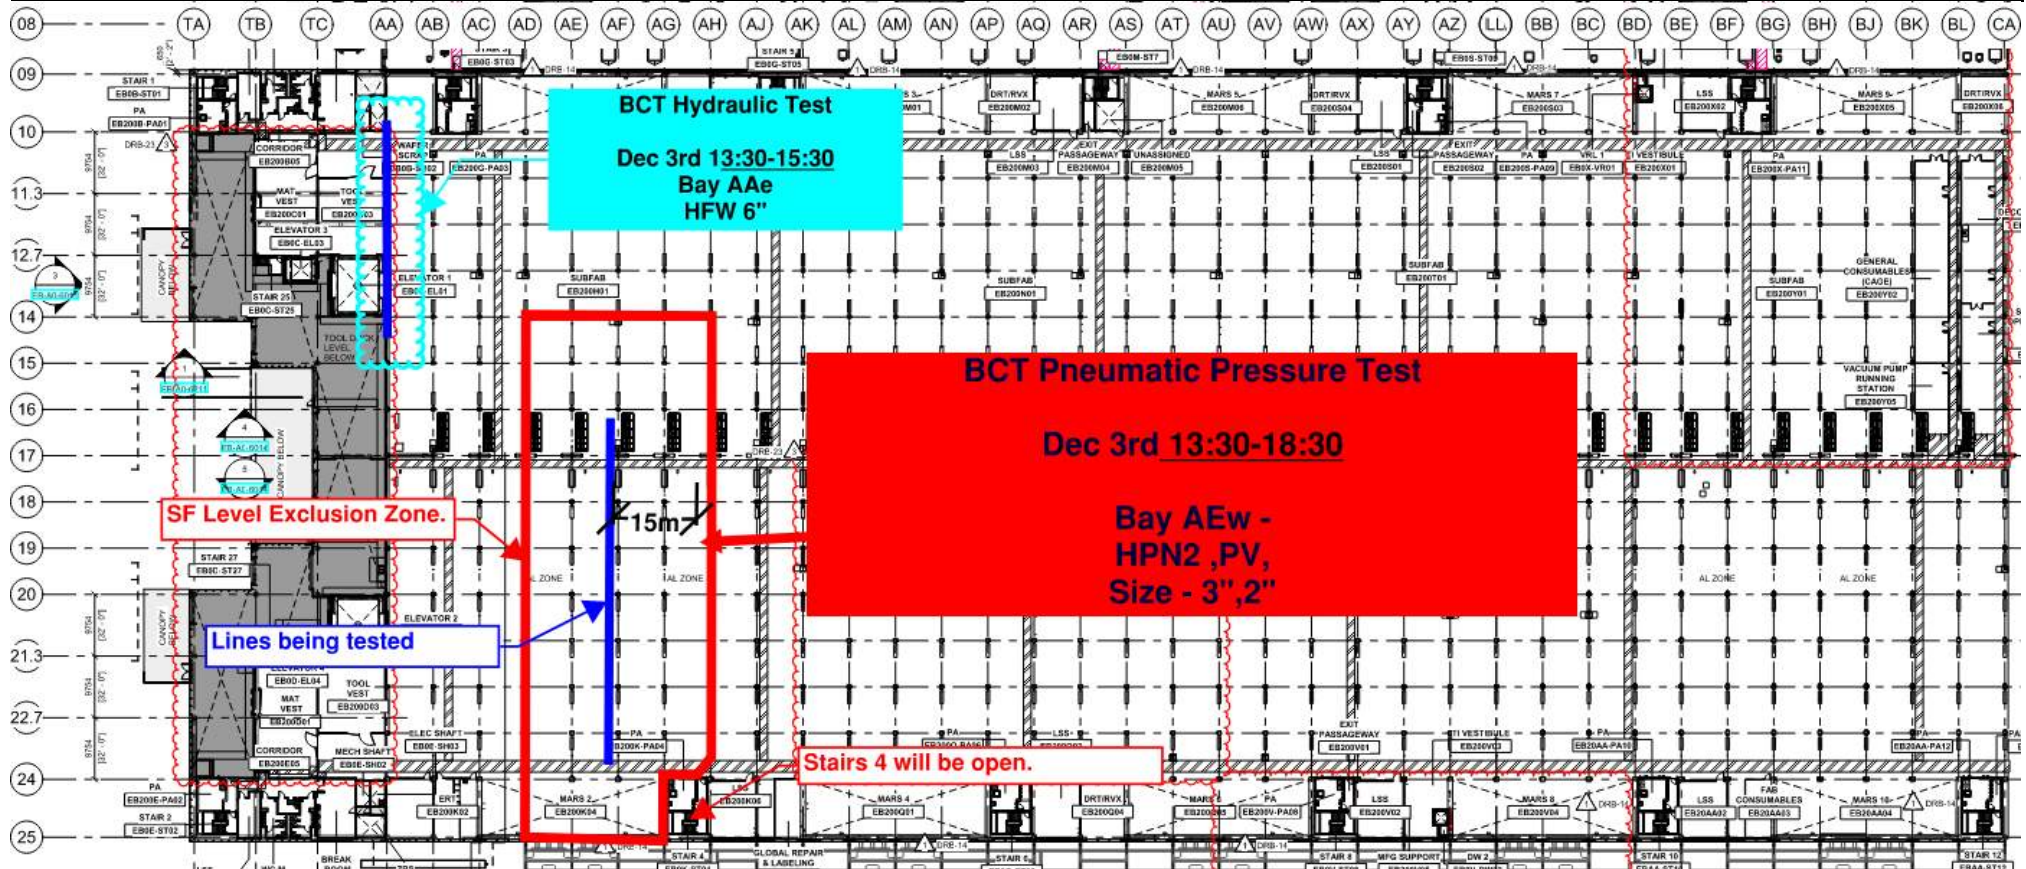



BCT Pressure Test Tomorrow


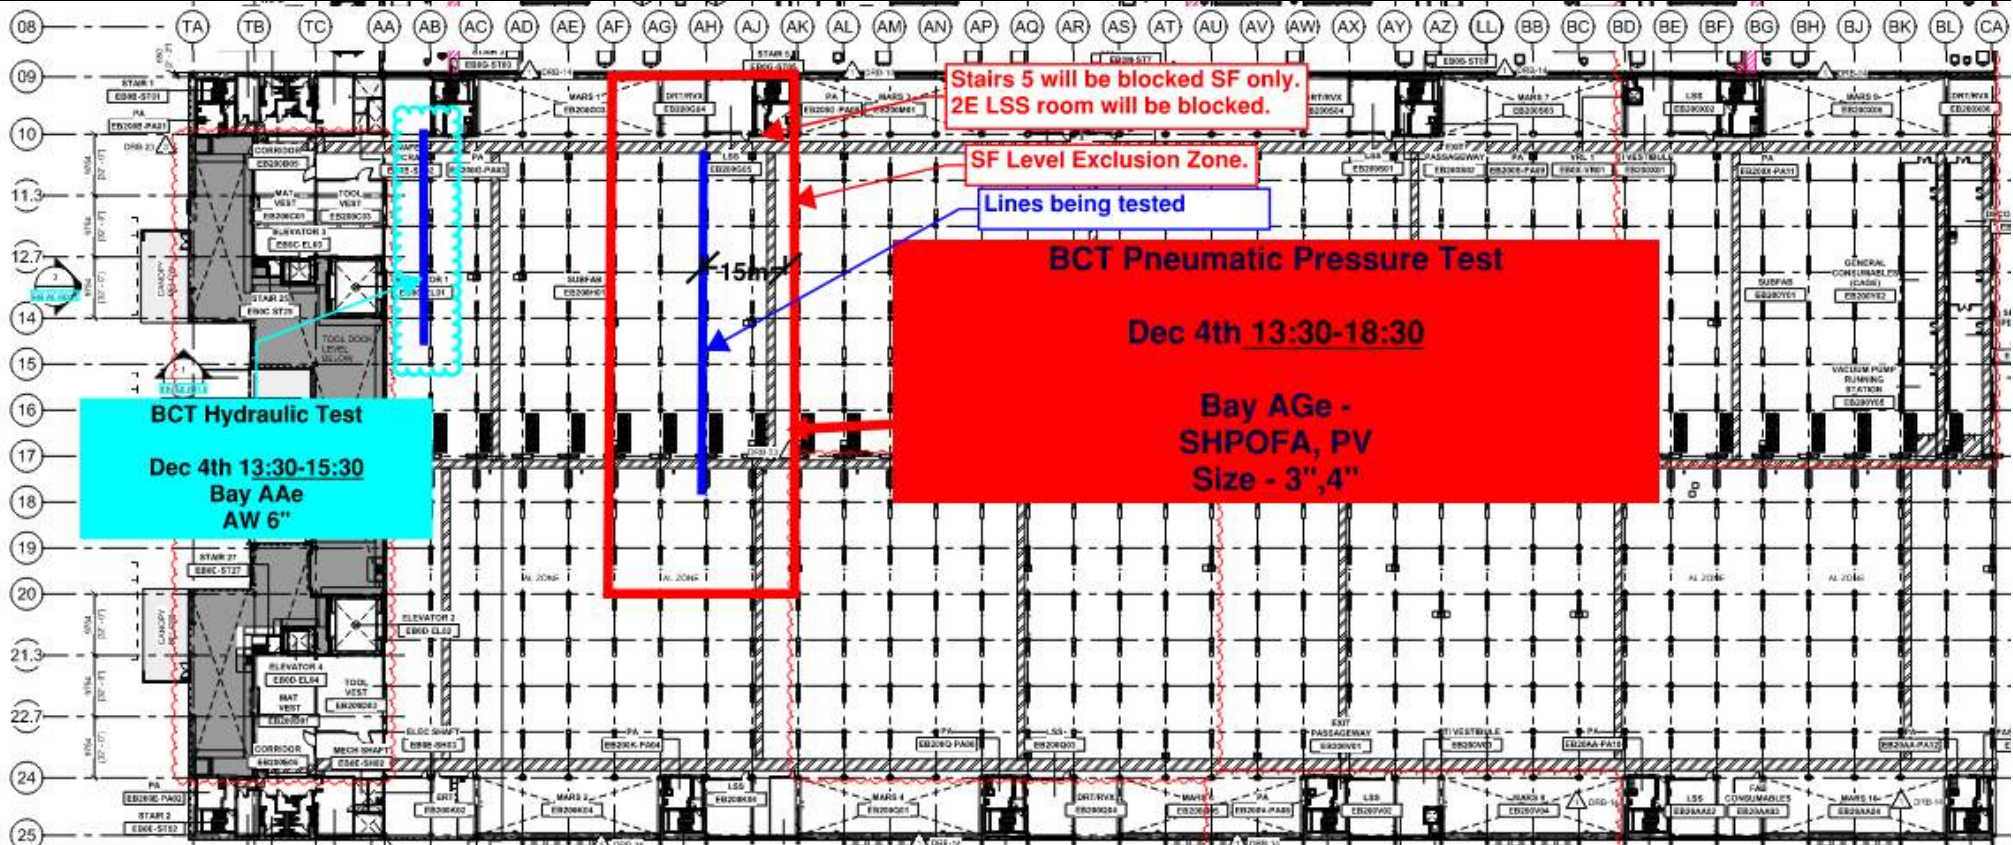



SUBFAB BUILDOUT MOD 2

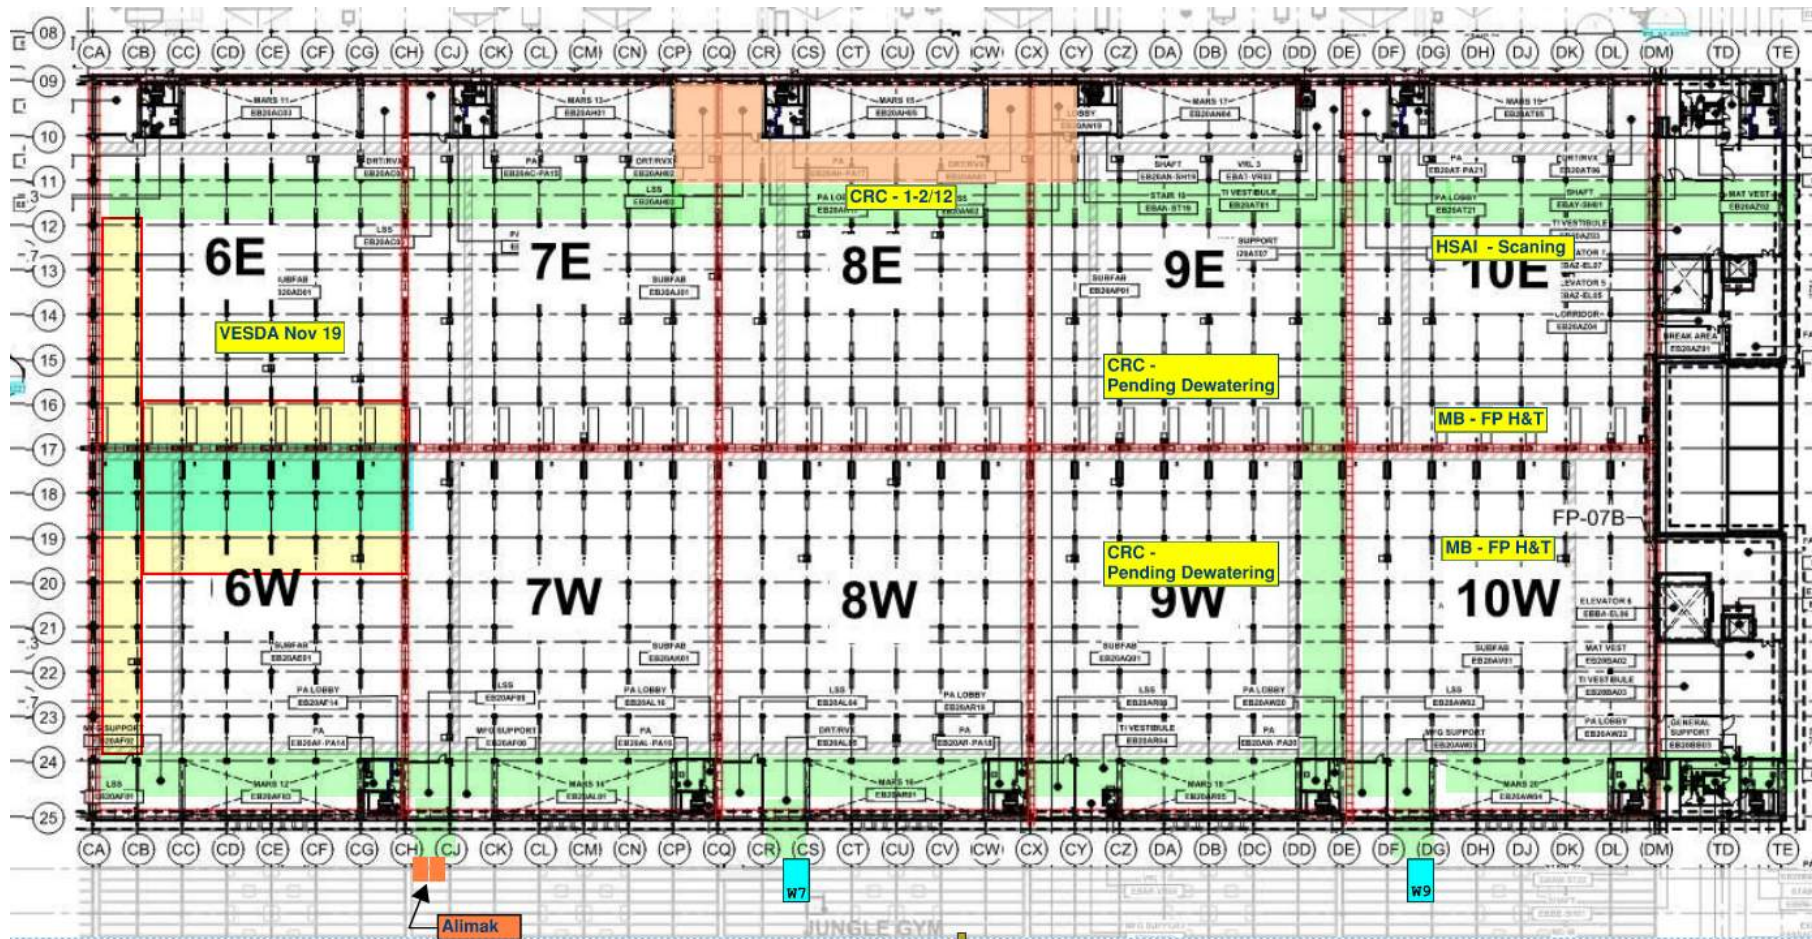

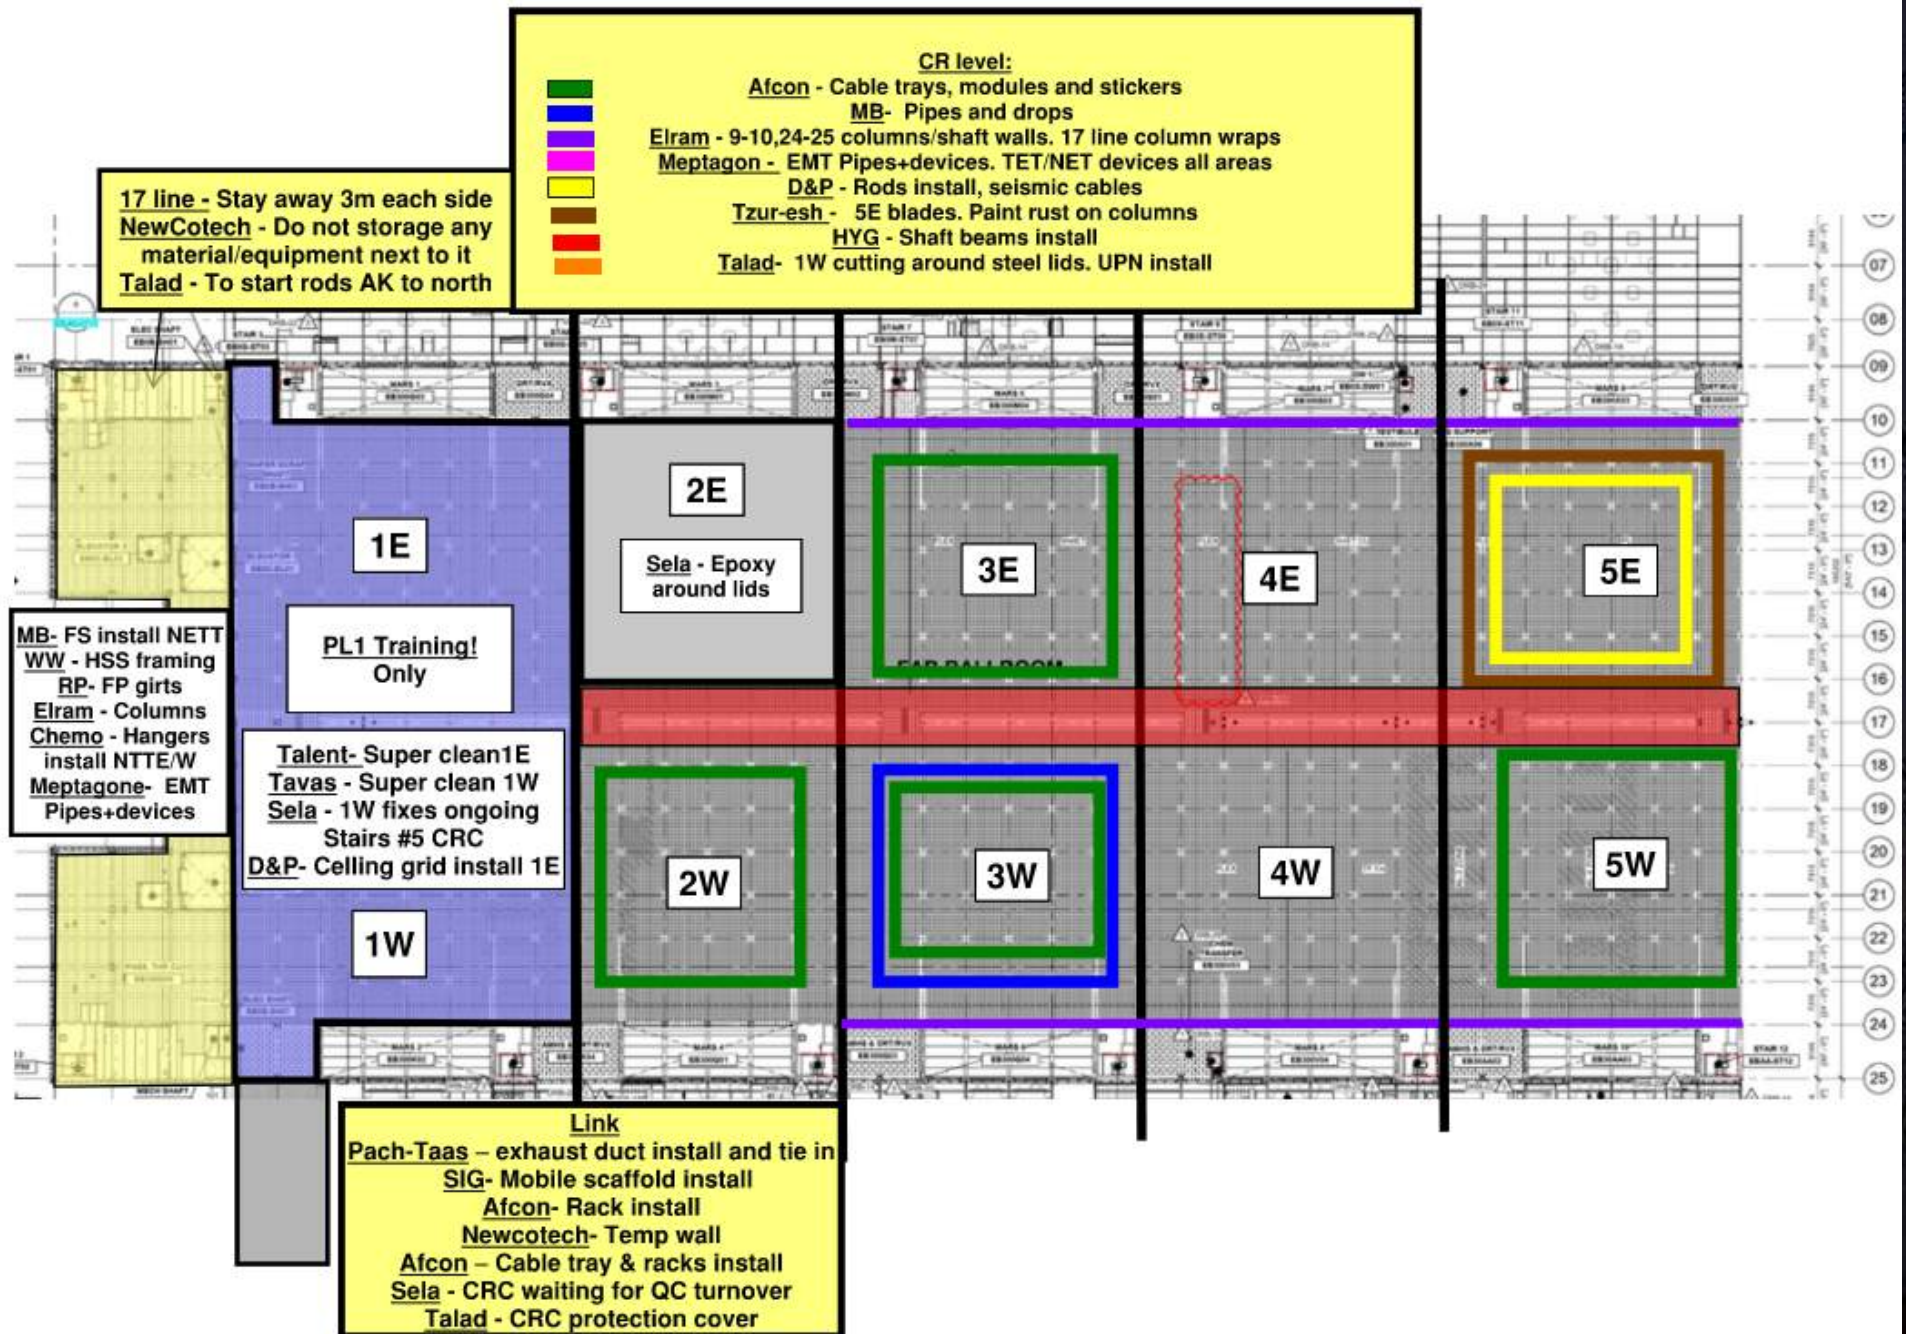


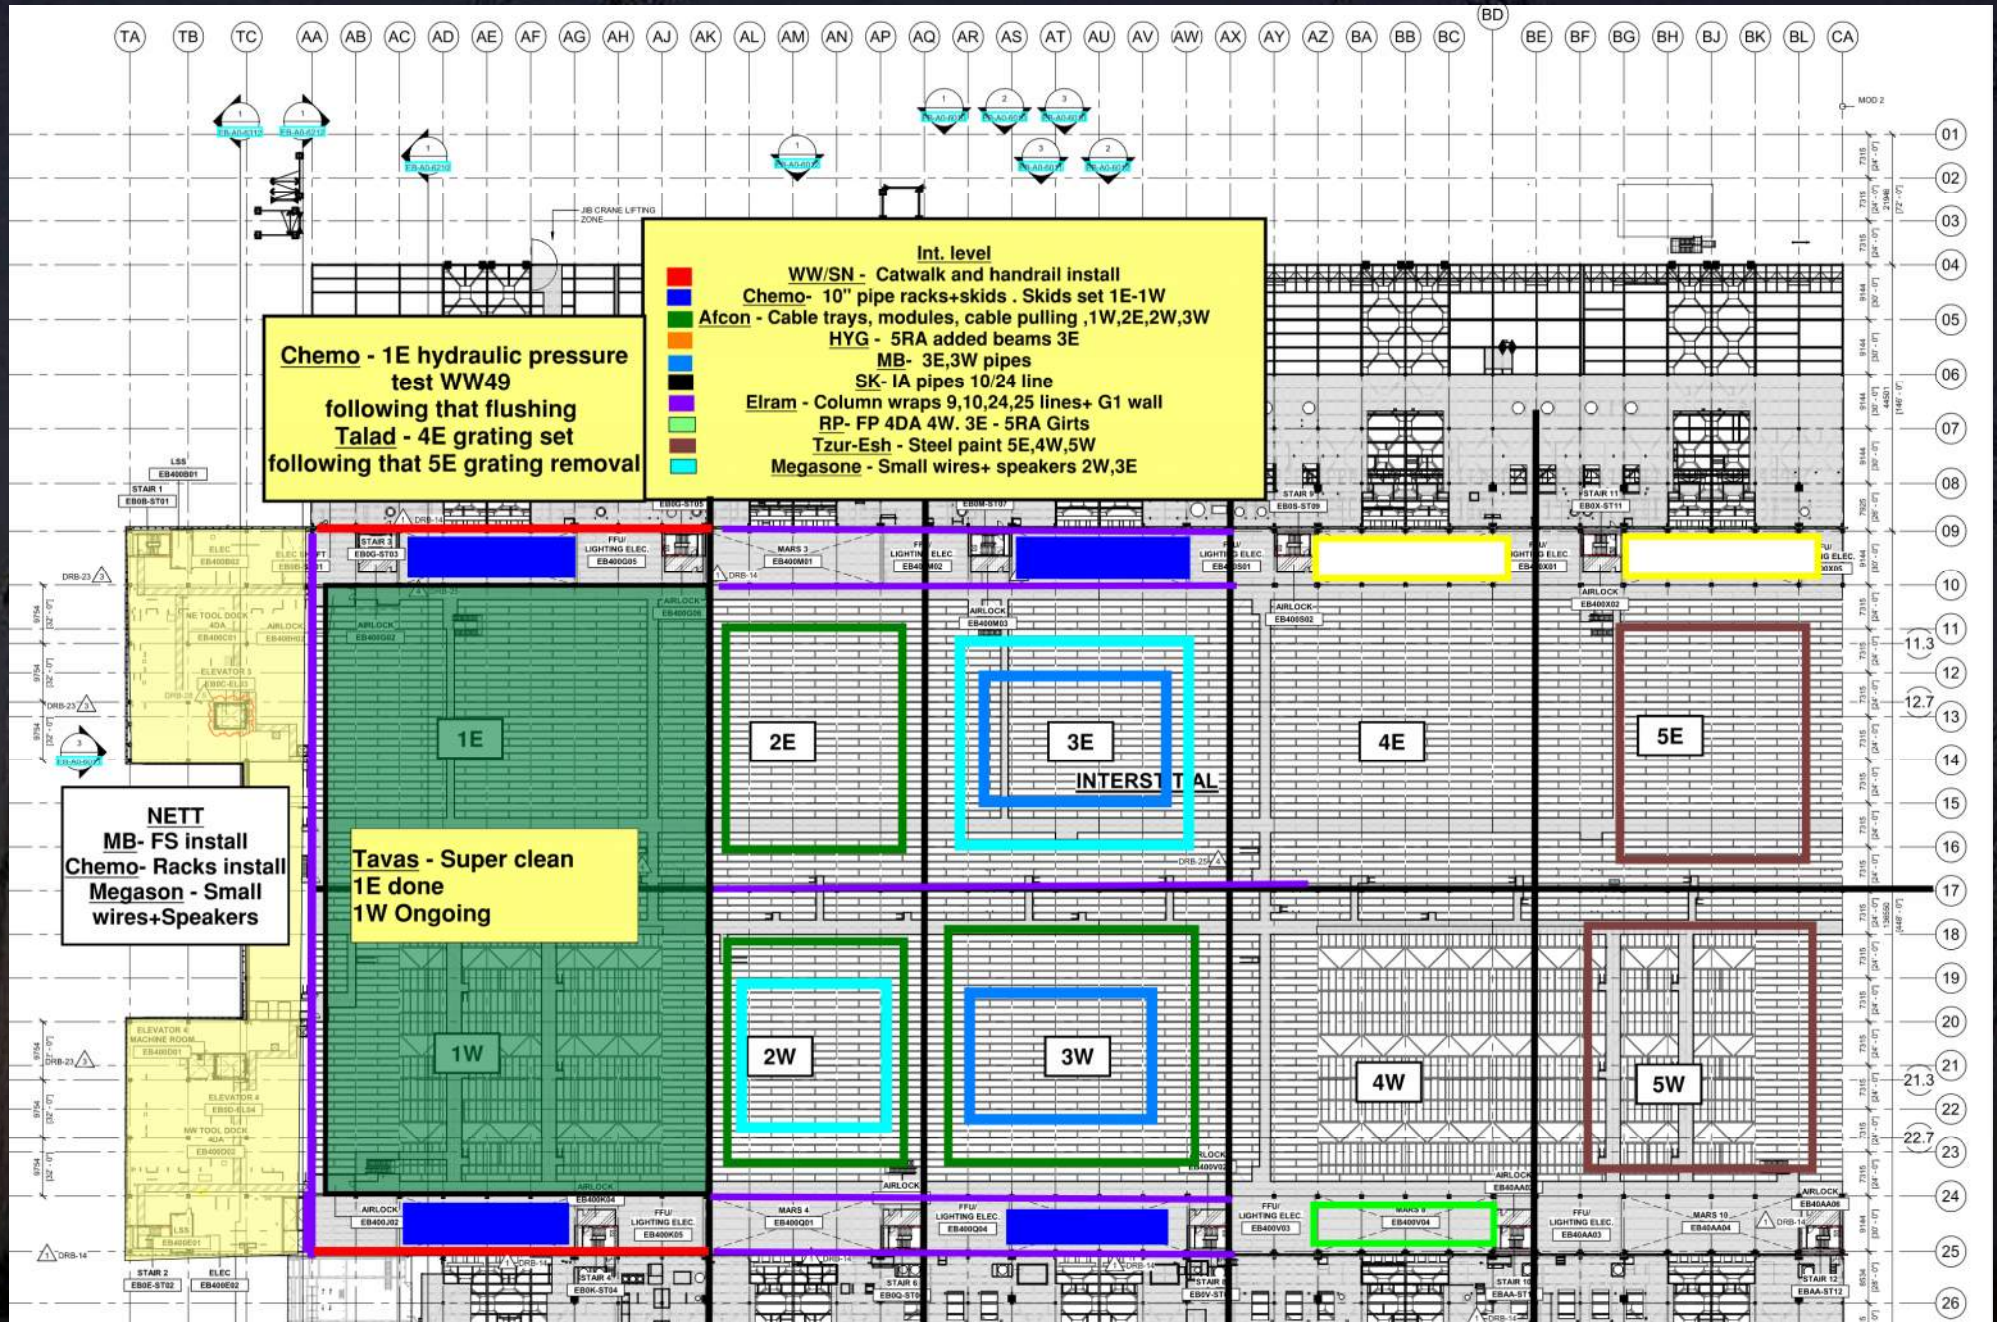

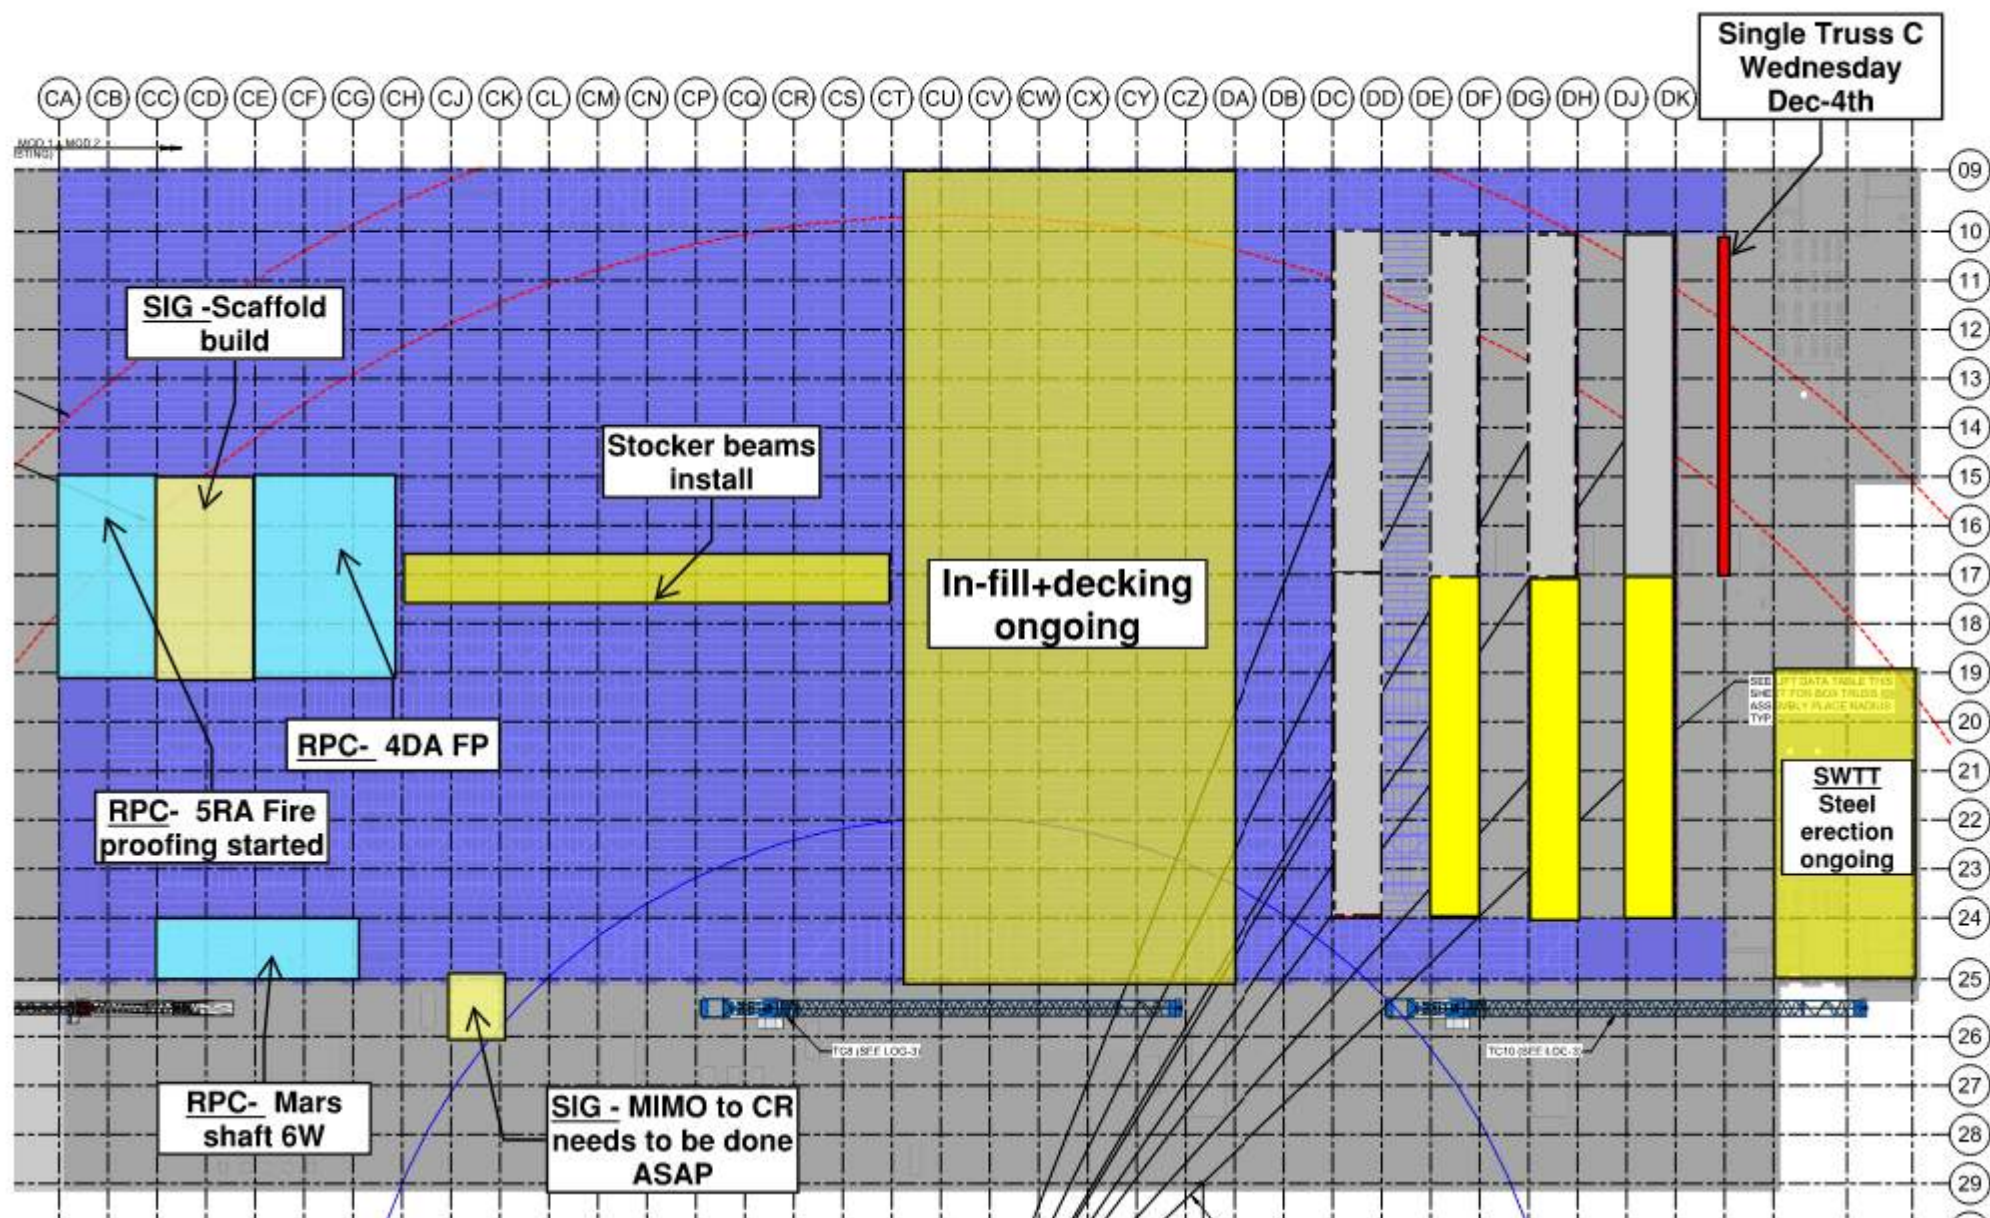





CR Phase 1 (PL1-2) Accesses points

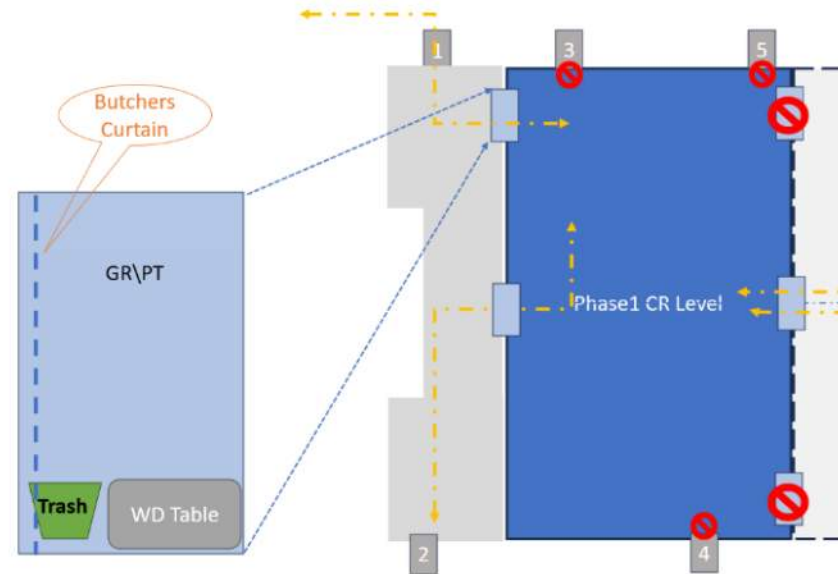


Interstitial Phase 1 (PL1-2) Accesses points

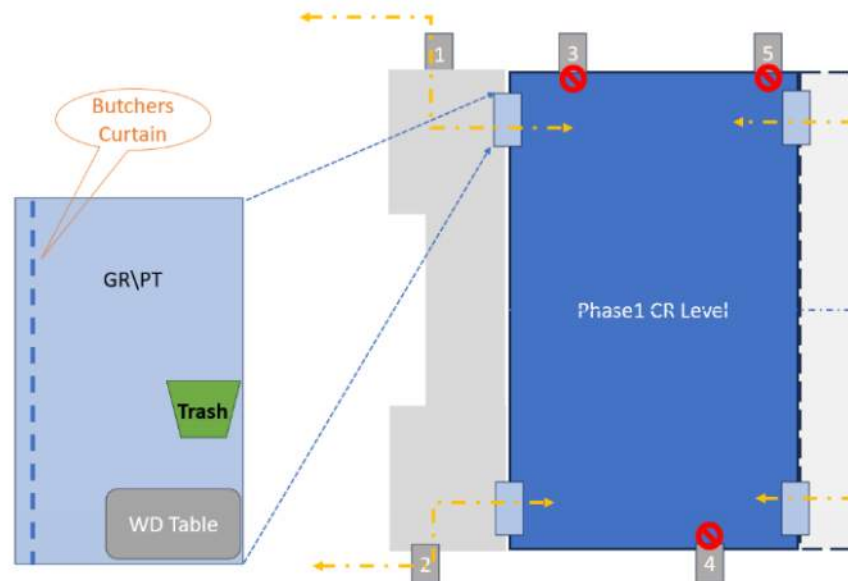



HOFFMAN CONSTRUCTION COMPANY



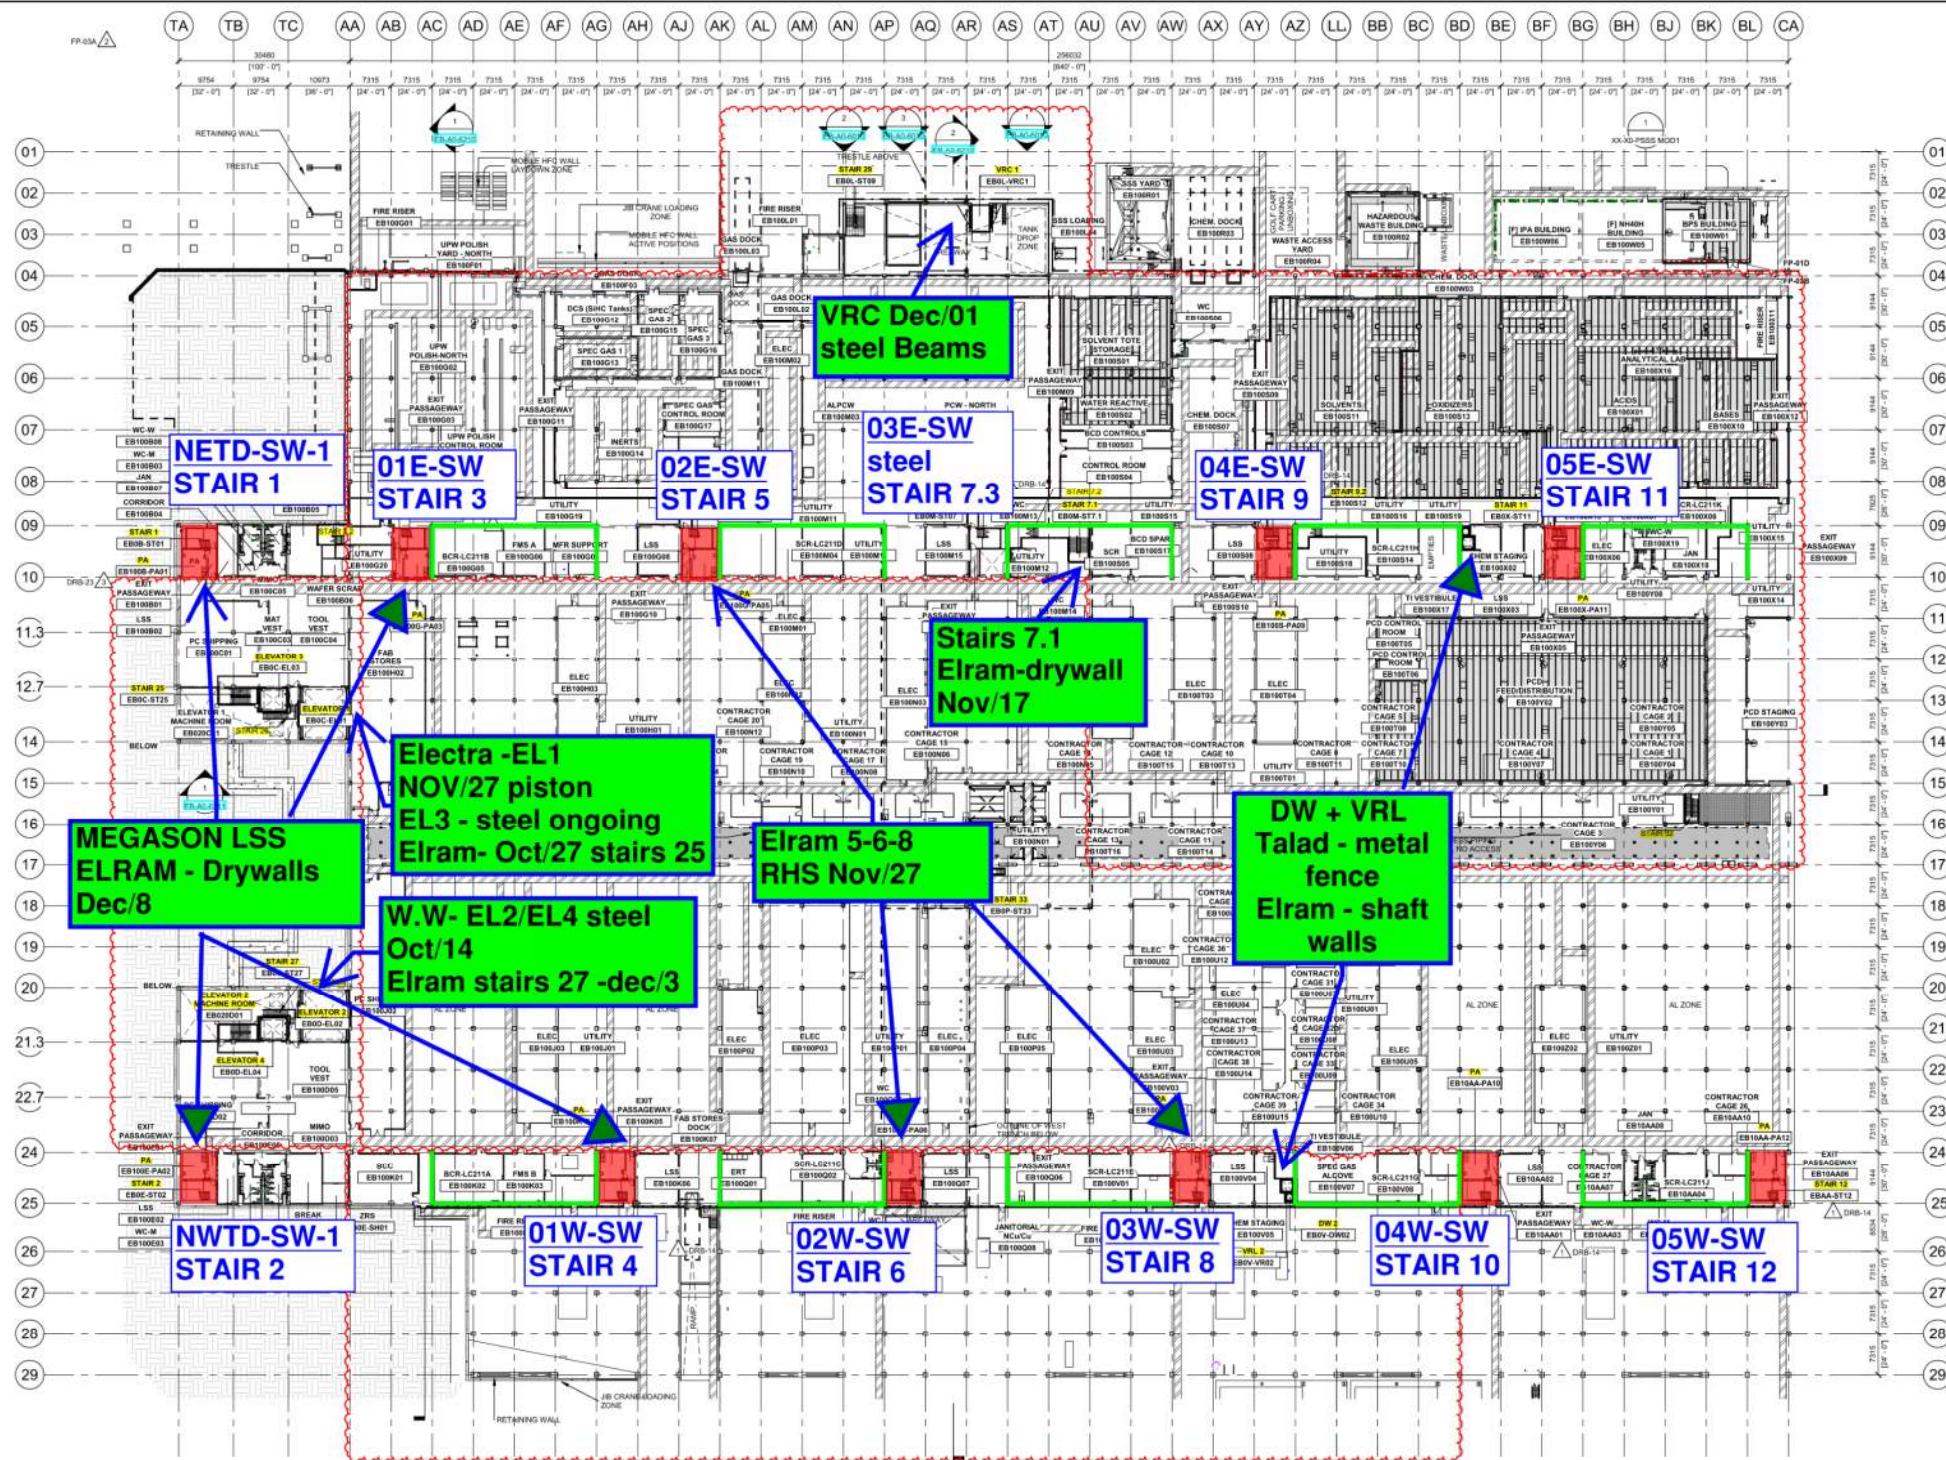


Siding - East FAB - PSSS

100% - BLOWDOWN				30% - BLOWDOWN												60% - BLOWDOWN																100% - BLOWDOWN																CA
SA	SB	SC	SD	AE	AF	AG	AH	AI	AJ	AK	AL	AM	AN	AO	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BJ	BK	BL	BM	BN	BO								
901 / 902				901 / 902				911 / 912				921 / 922				931 / 932				941 / 942				951 / 952				701 / 702				721 / 722				731 / 732				941 / 942				751 / 752				
28	29	30	31	28	29	30	31	28	29	30	31	28	29	30	31	28	29	30	31	28	29	30	31	28	29	30	31	28	29	30	31	28	29	30	31	28	29	30	31	28	29	30	31					
100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	75%	75%	75%	75%	100%	100%	100%	100%	75%	75%	75%	75%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%			
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	1	1	1	1	0	0	0</																						


Siding - West FAB - JYG


100% - BLOWDOWN				30% - BLOWDOWN								60% - BLOWDOWN												100% - BLOWDOWN																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
T1	T2	T3		A1	A2	A3		B1	B2	B3		C1	C2	C3		D1	D2	D3		E1	E2	E3		F1	F2	F3		G1	G2	G3		H1	H2	H3		I1	I2	I3		J1	J2	J3		K1	K2	K3		L1	L2	L3																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
3001 / 3002				401 / 402				501 / 502				601 / 602				631 / 632				641 / 642				801 / 802				811 / 812				821 / 822				831 / 832				841 / 842				851 / 852																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
28	29	30	31	15	16	17	18	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
24	24	24	9	15	16	17	18	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
100%	100%	100%	12%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%

Link

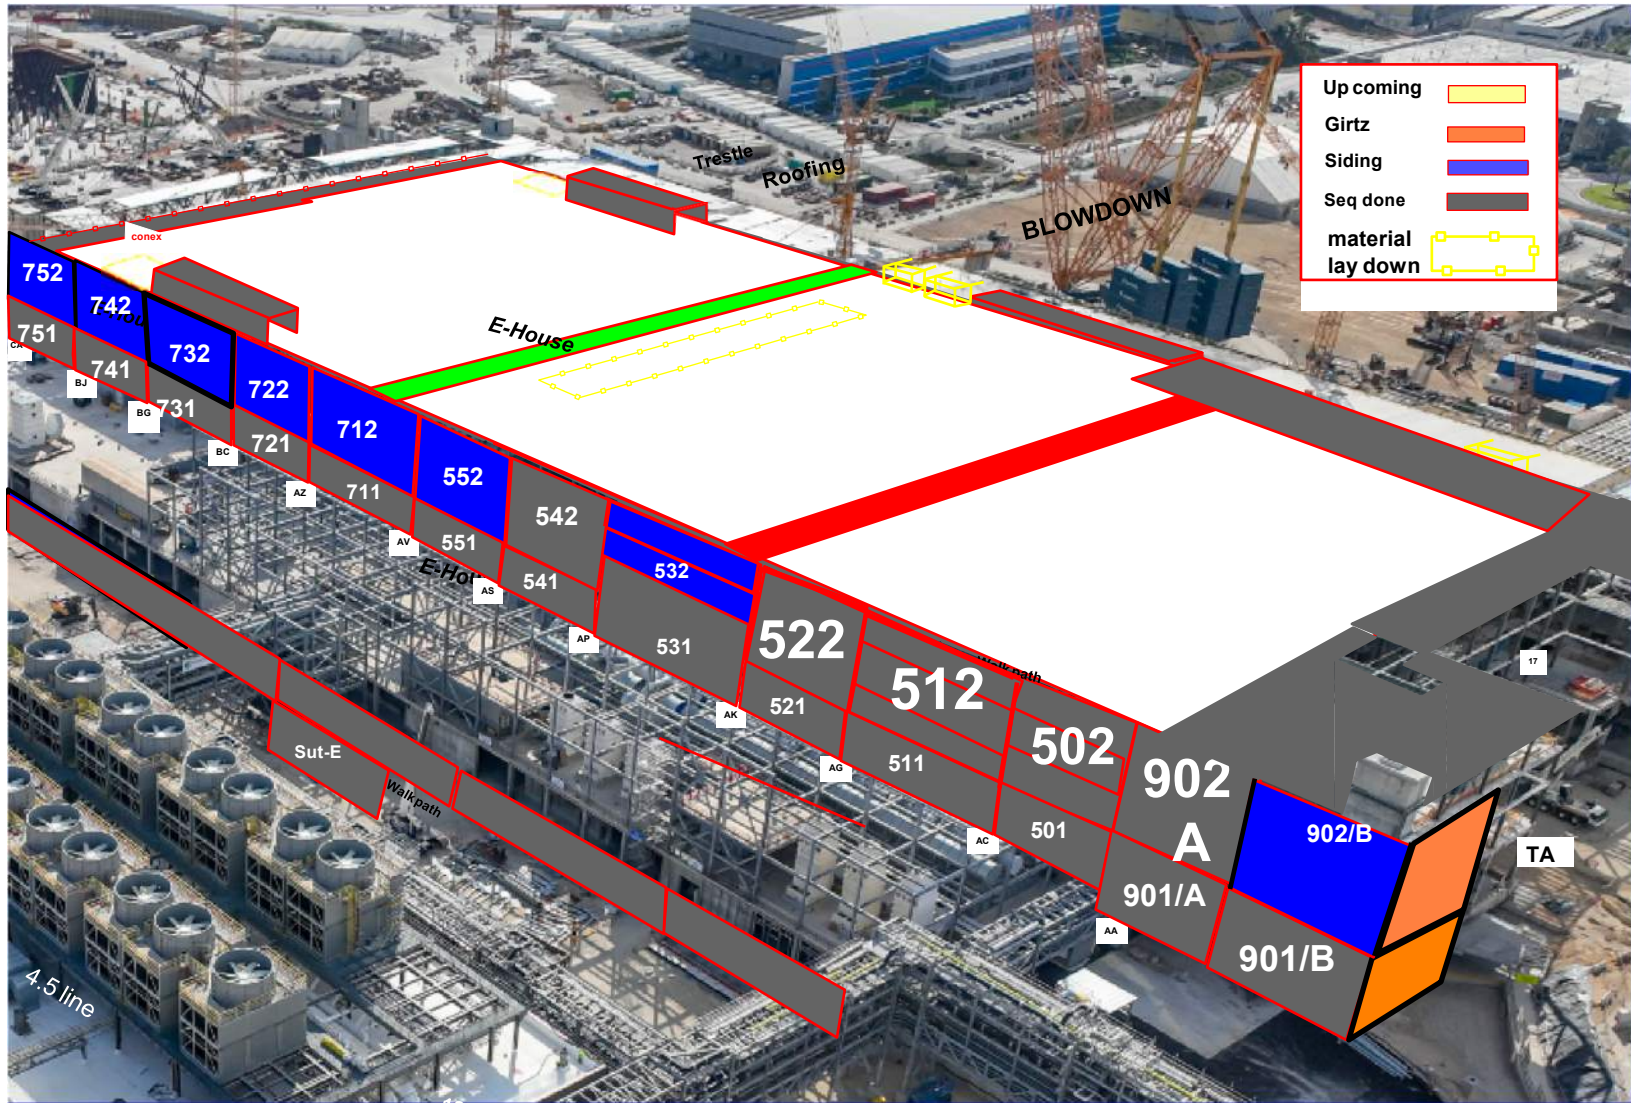

Walkpath

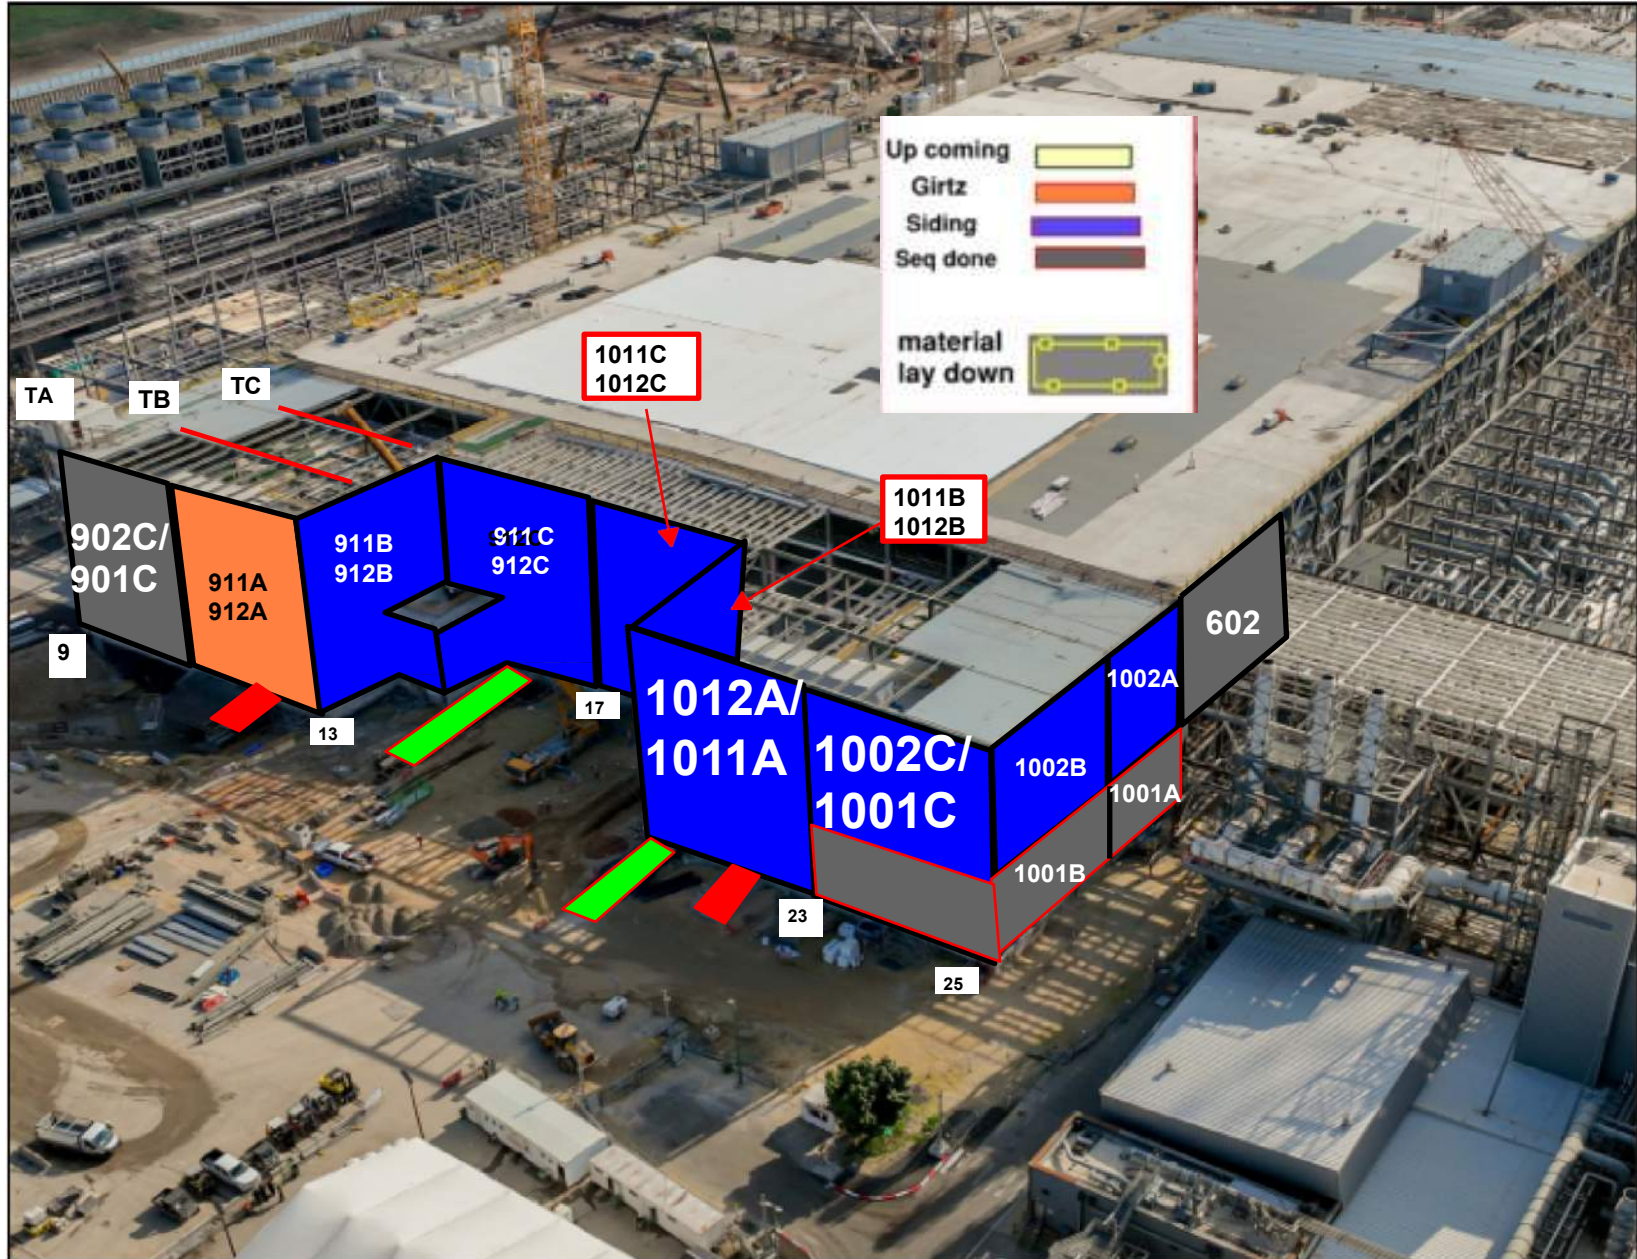


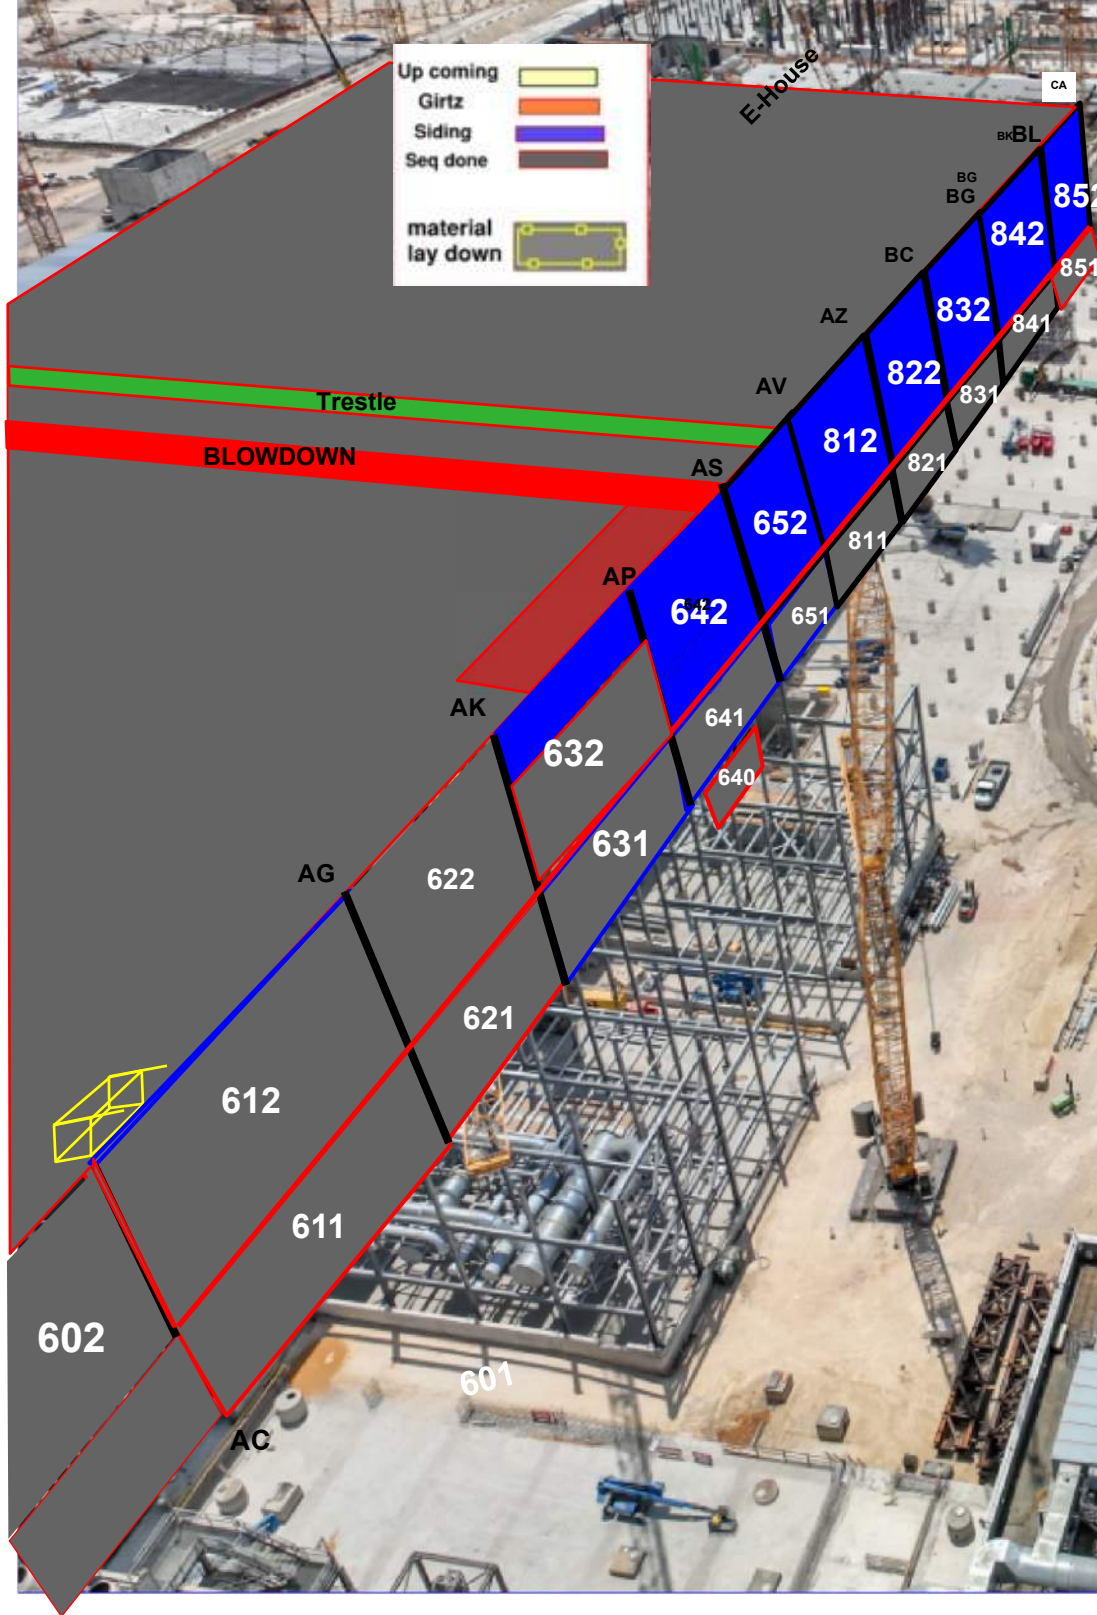

PSSS.1


Utility Level
1YA

PSSS Roof
2SA

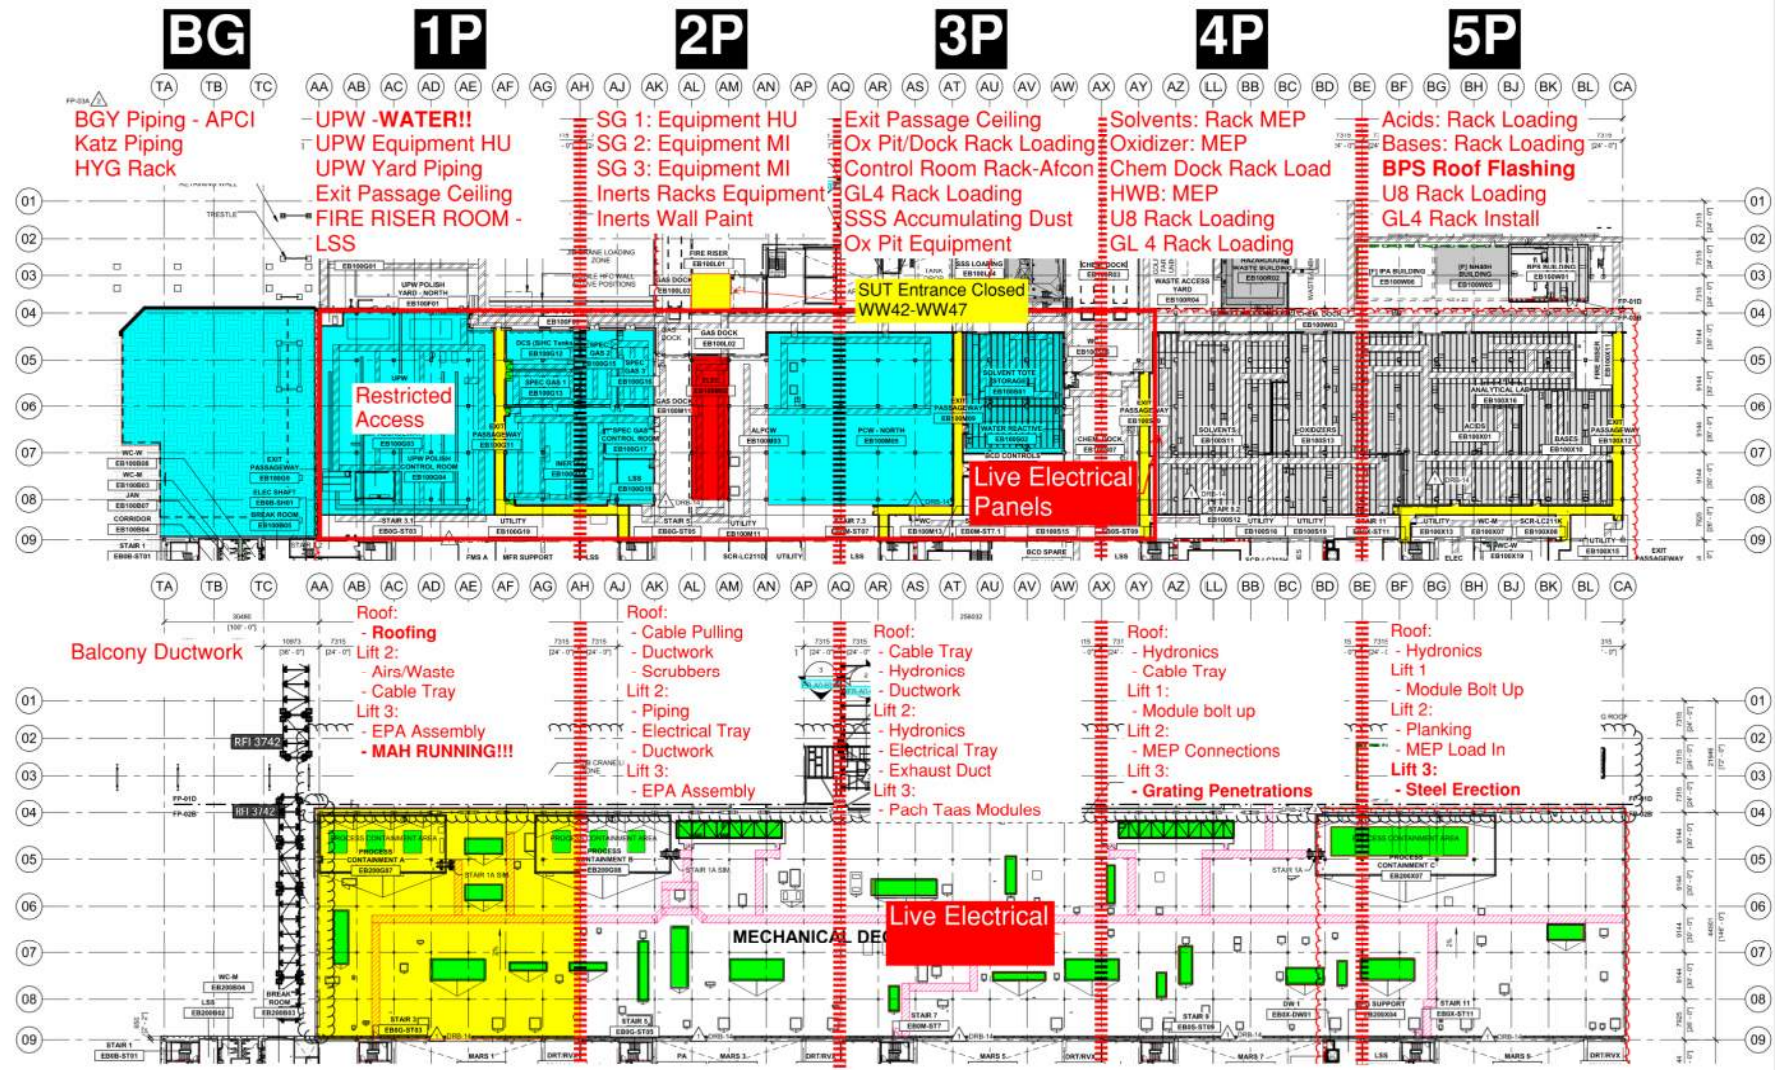



PSSS.2

Utility Level
1YA

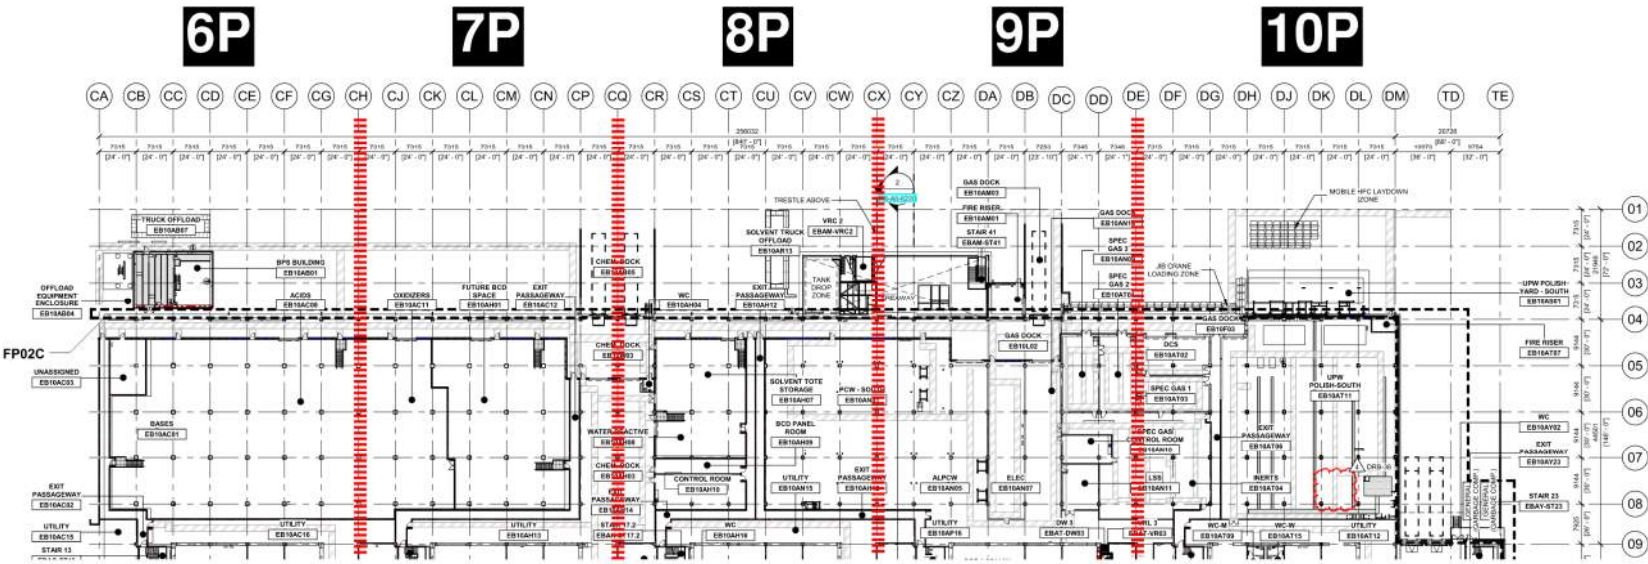


PSSS Roof
2SA

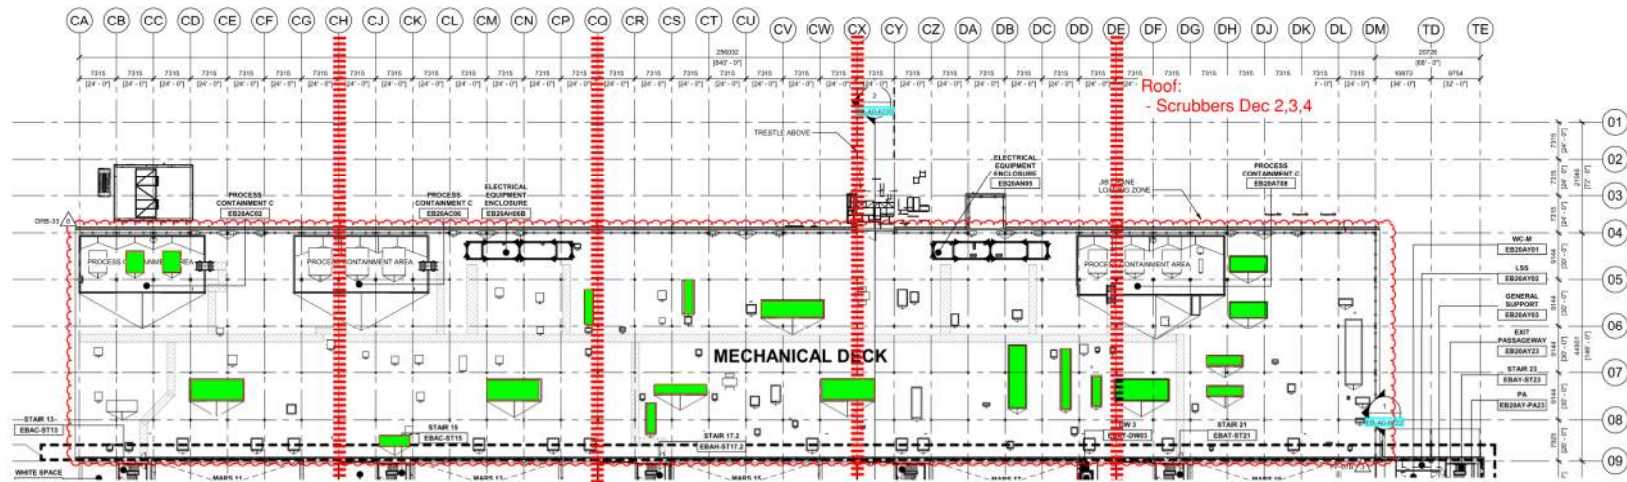



WJG 01J, 02J LIFT 2 & 3






WJG 03J, 04J, 05J LIFT 2 & 3




MAH101-9/10-00 Delivery WW49

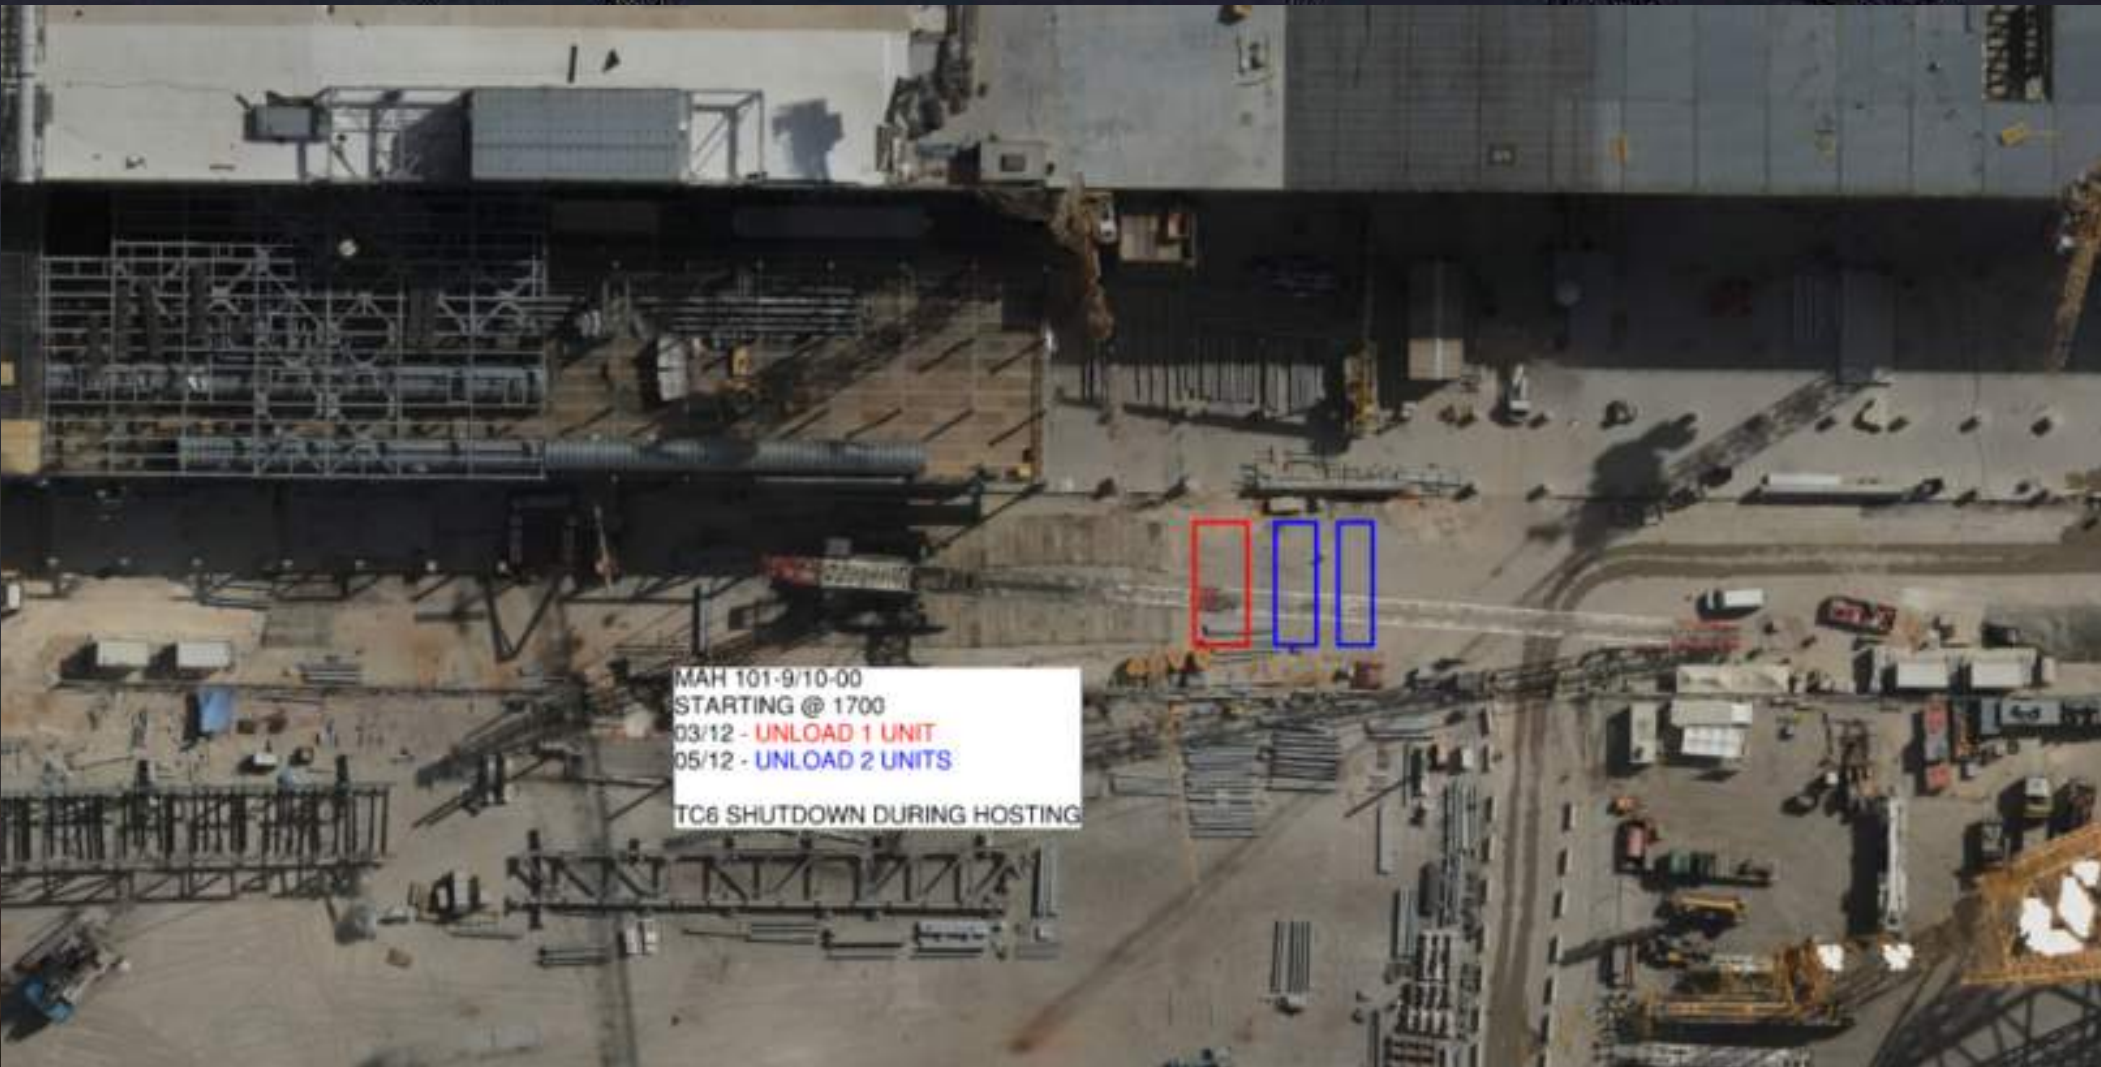



WJG UTILITY LEVEL BUILD OUT

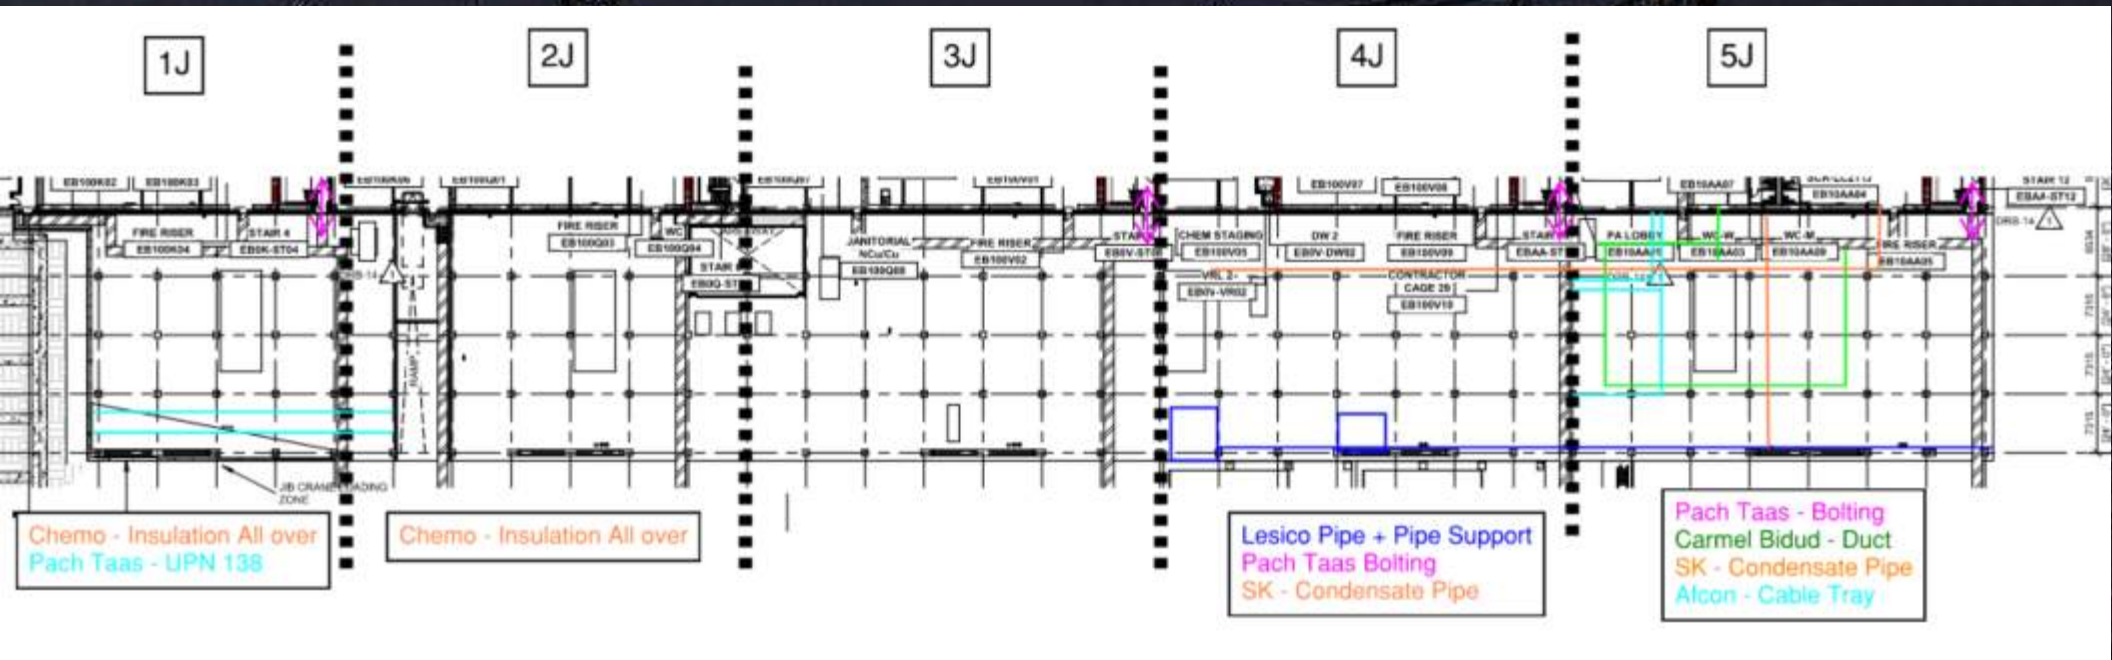




CUB 1

CUB 1 COORDINATION MAP

UPDATED __ / __ / __

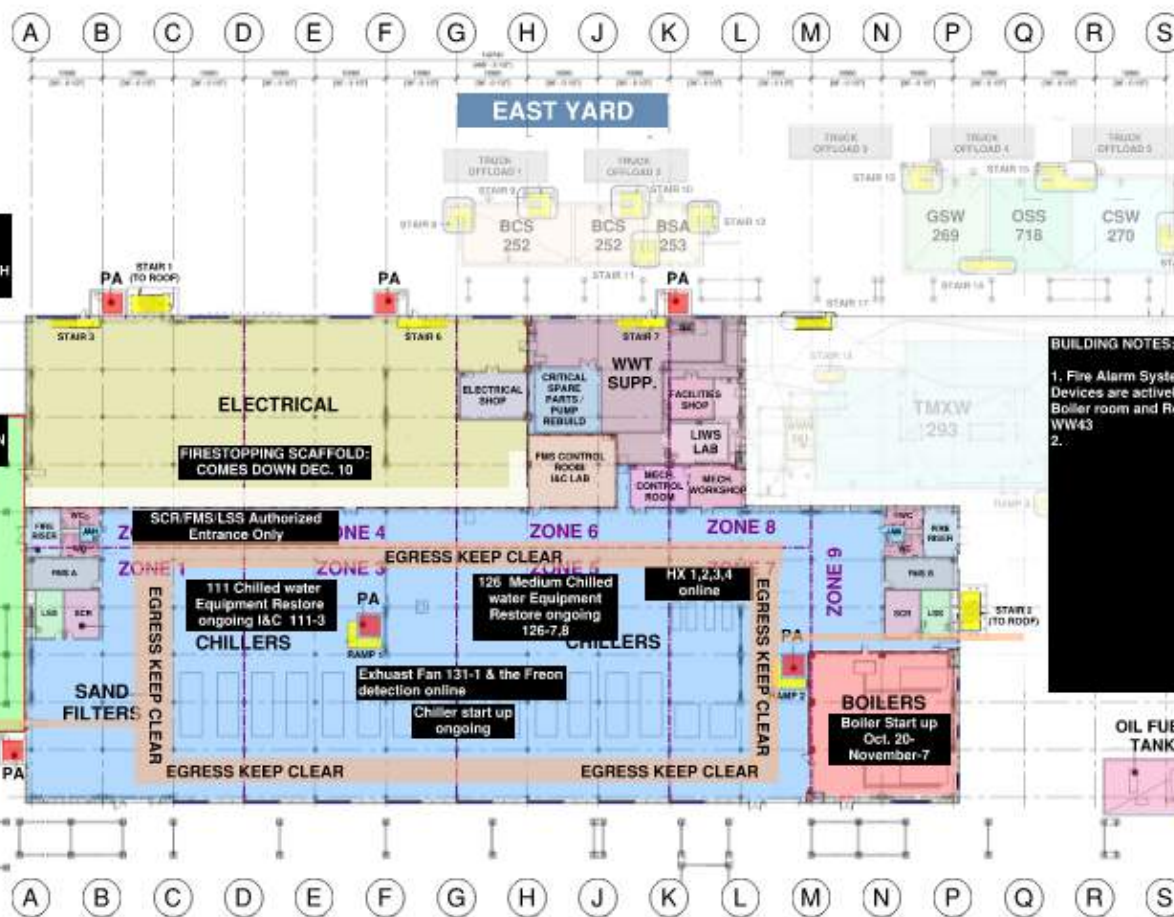

N


- PROTECTED AREA
- STAIRS / RAMP
- YARDS
- TRUCK OFF/LOADING

ALARM NOTES:
1. FIRE ALARM: WAIT FOR HCC DIRECTION
2. GAS ALARM: EVACUATE TO NORTH YARD

BUILDING NOTES:


1. Fire Alarm System
Devices are actively monitored
Boiler room and Roof Charged with Water WW43
- 2.

CUB 1 – EXTERIOR/ROOF

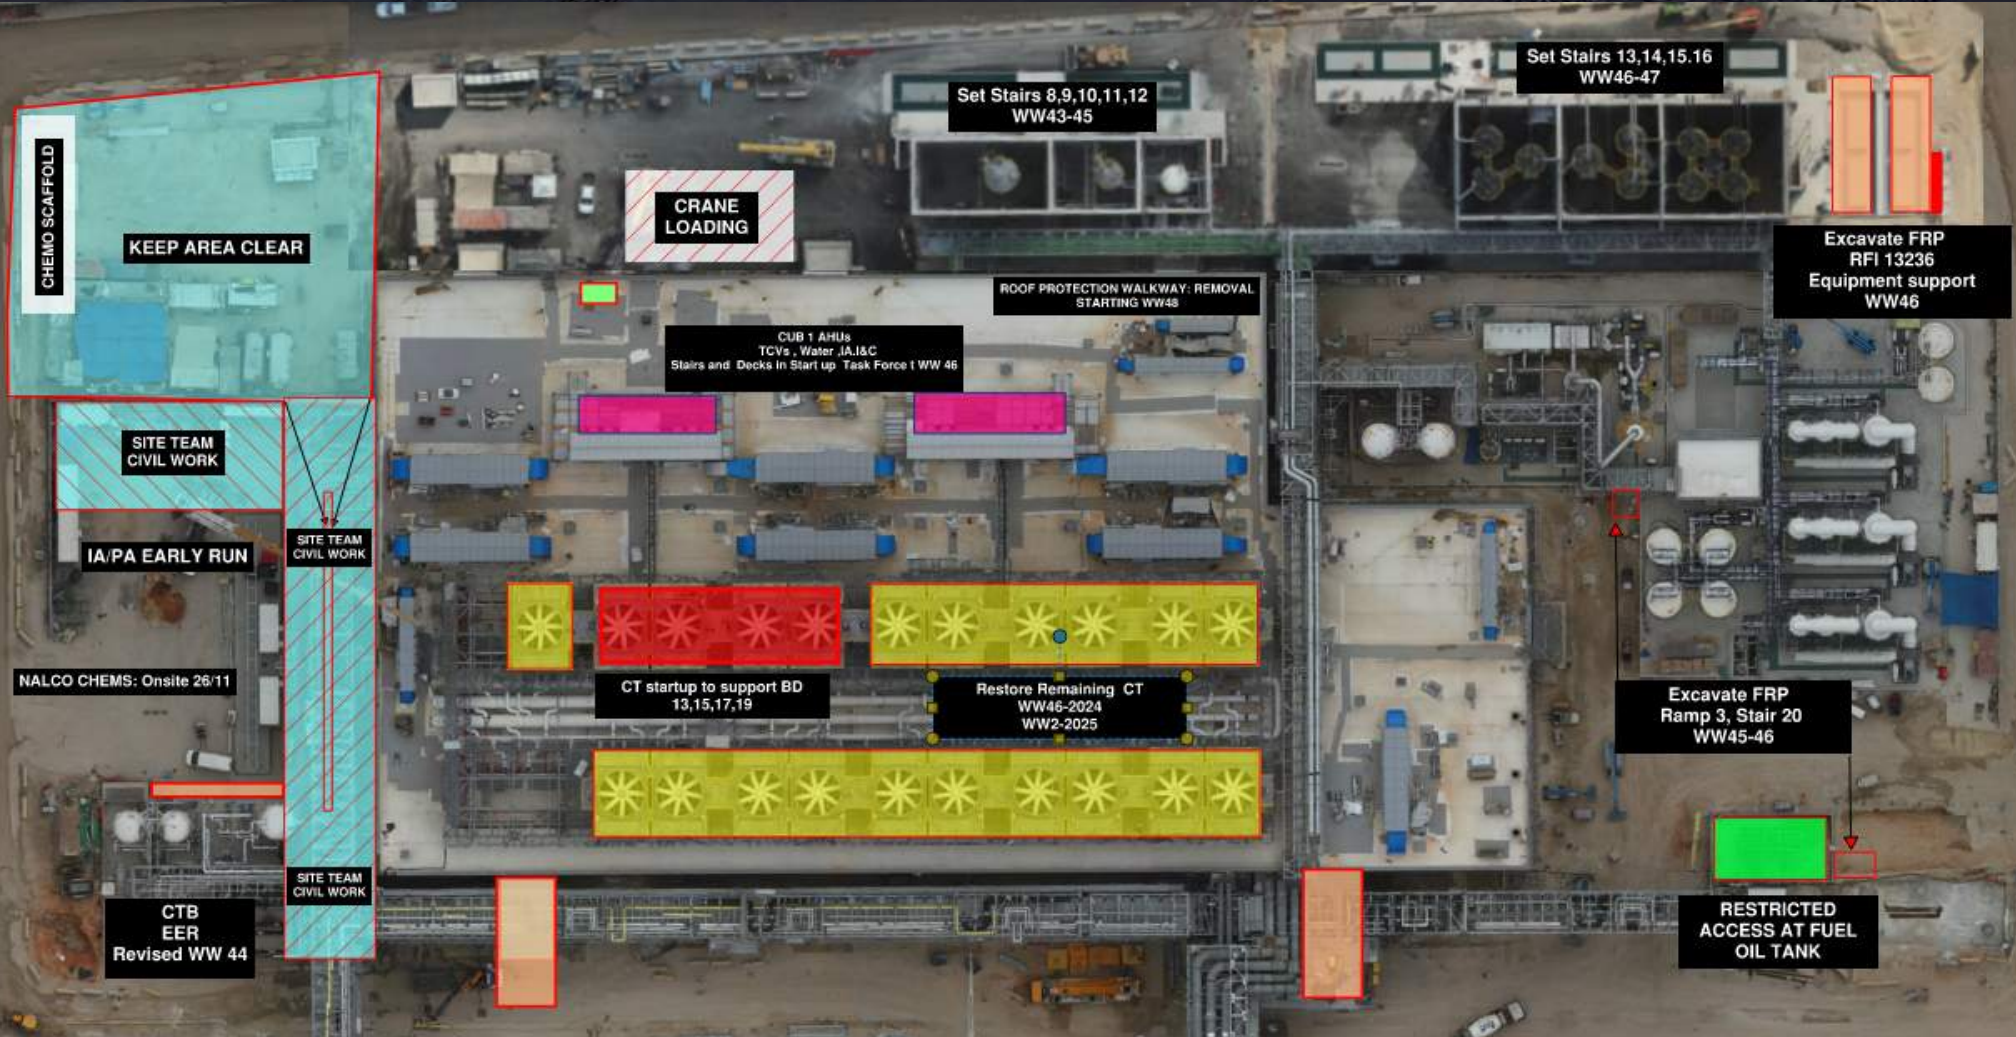



CUB 2- INTERIOR/LOAD-IN

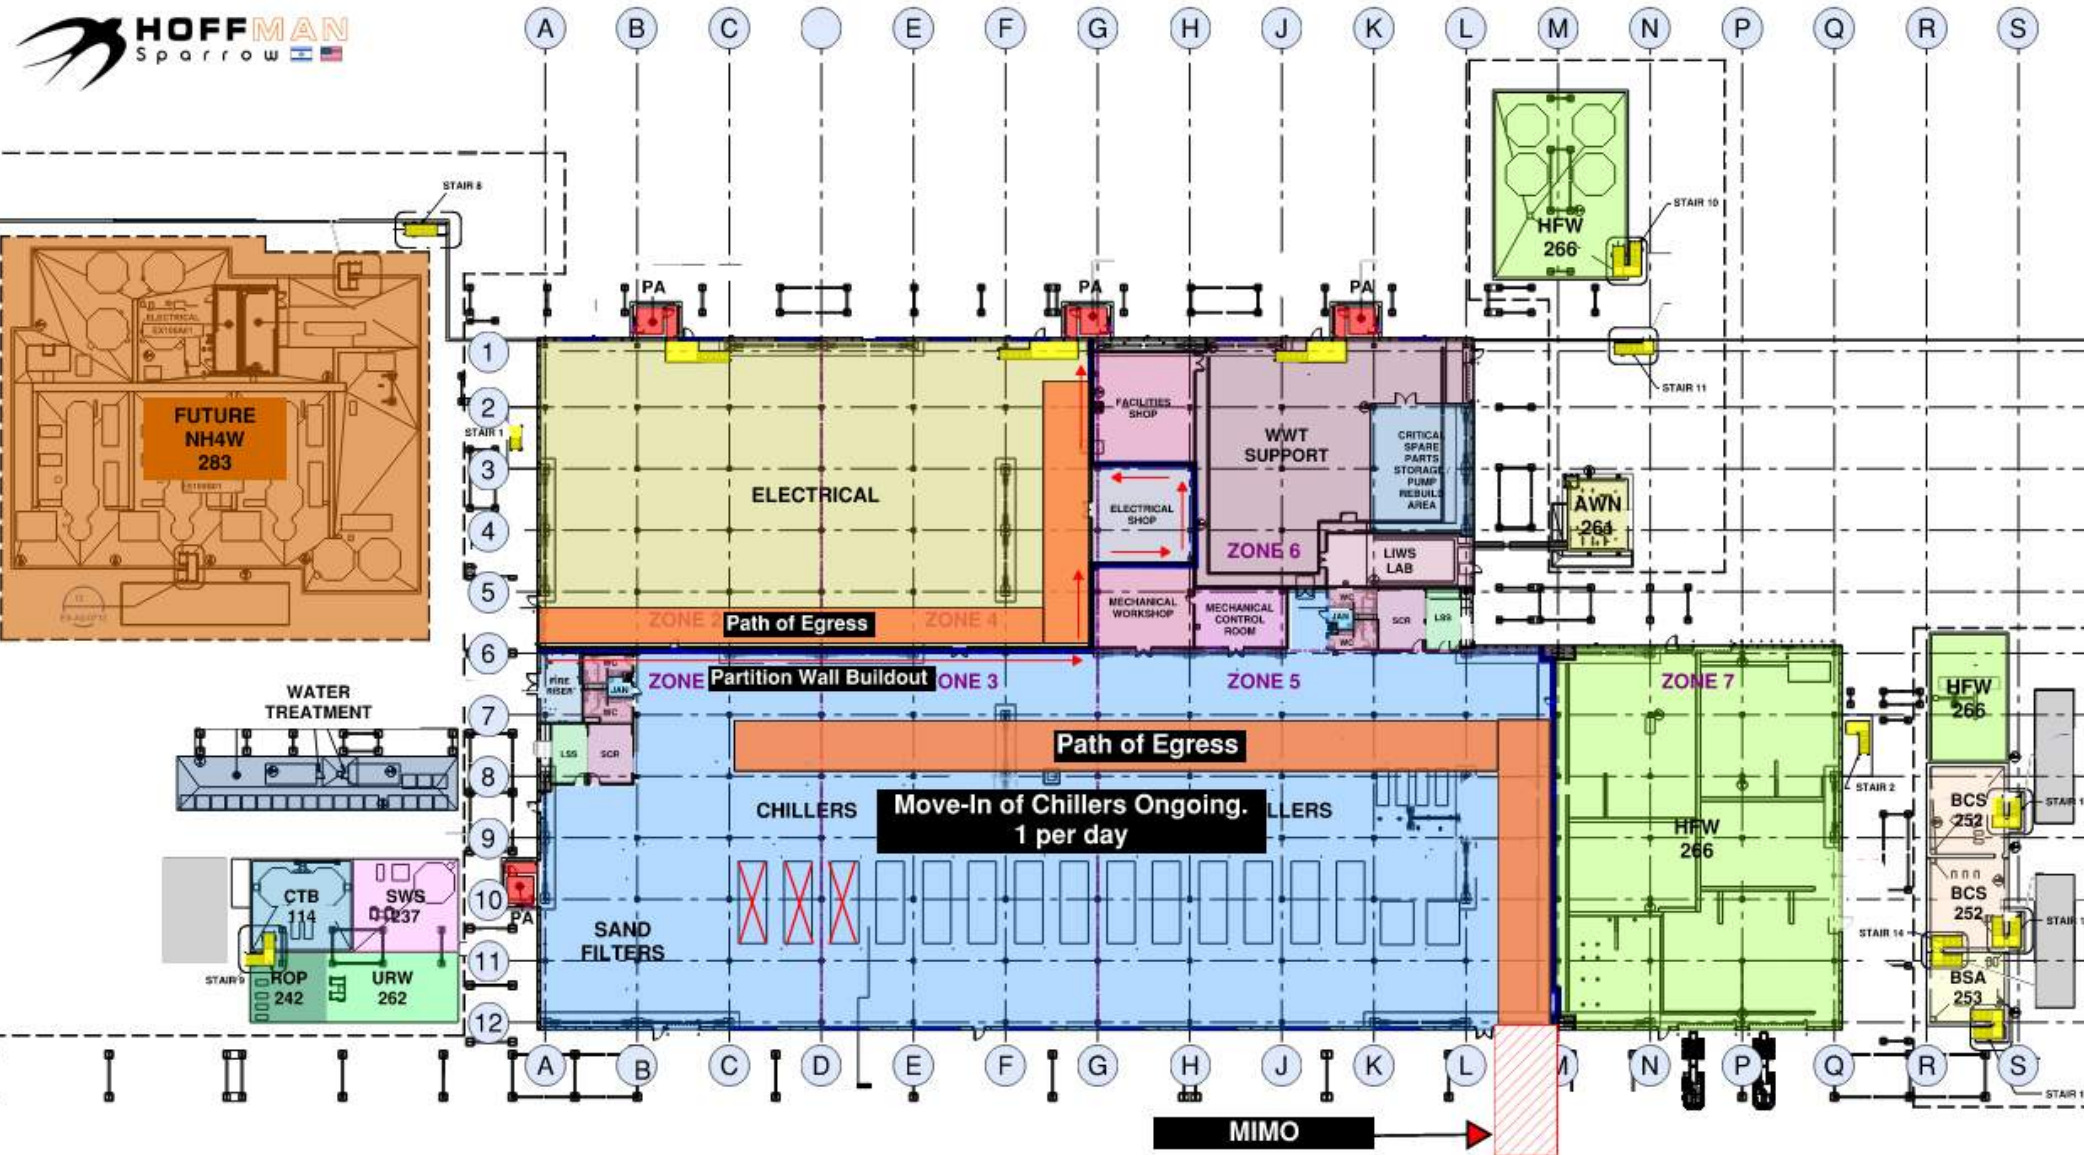



CUB 2 – EXTERIOR/ROOF


Install of NALCO
Containers on 4/12


Install of E-House Adapters
on 8/12

Set AHU on
5/12

Install of Exterior Panels
Ongoing


Set AHU on
5/12

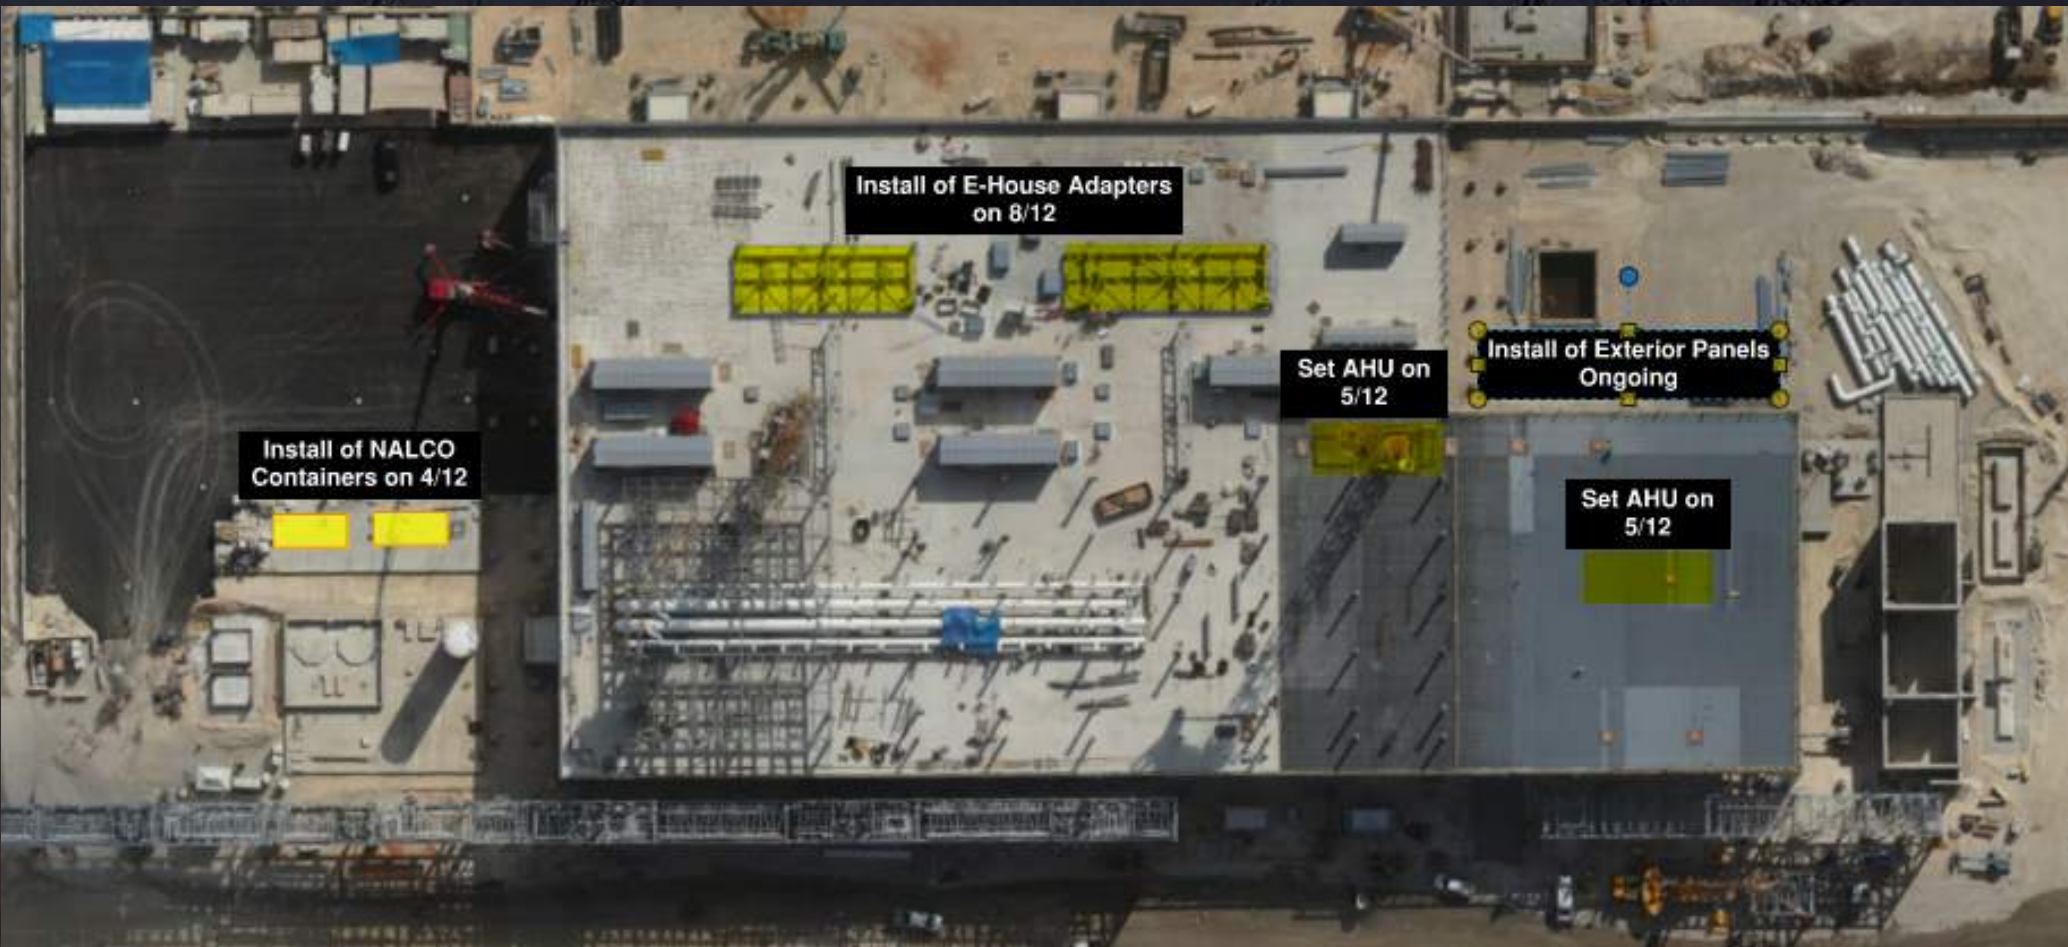



GIS GATE
closed 29/Dec /2024





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow



T18
DEC 3th - DEC 11th

DEC 8th

DEC 9th


DEC 10th

DEC 3th

DEC 3th

DEC 3th





HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow




T20 - BGY

pressure test - HP 1" - 2 lines - T50 - T20
165 psi - exclusion zone 5m' T50/T20
coordinated with BGY team
04/12/2024 -
Start at 17:00 End at 21:00

T50

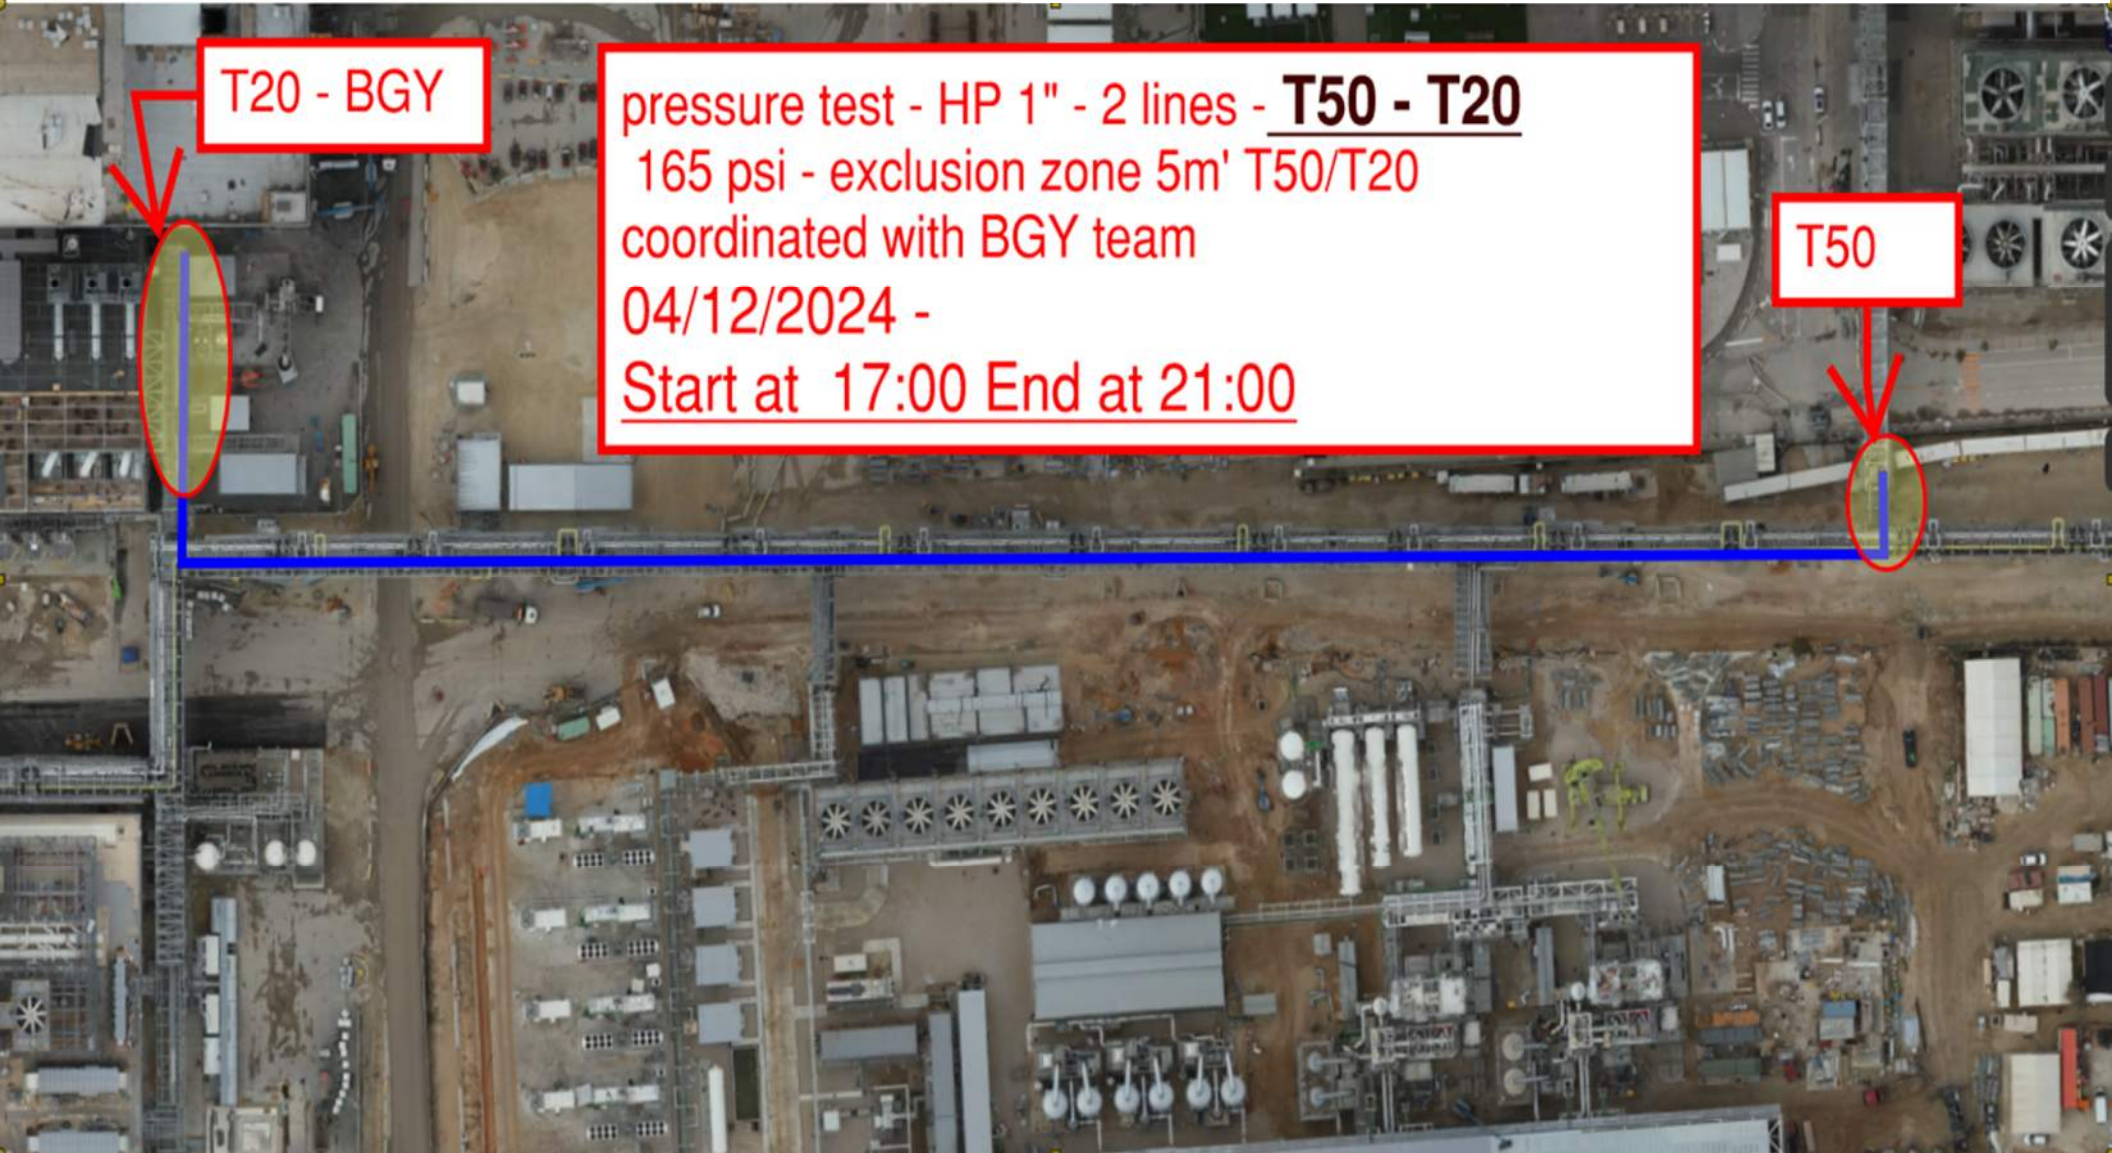




HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow

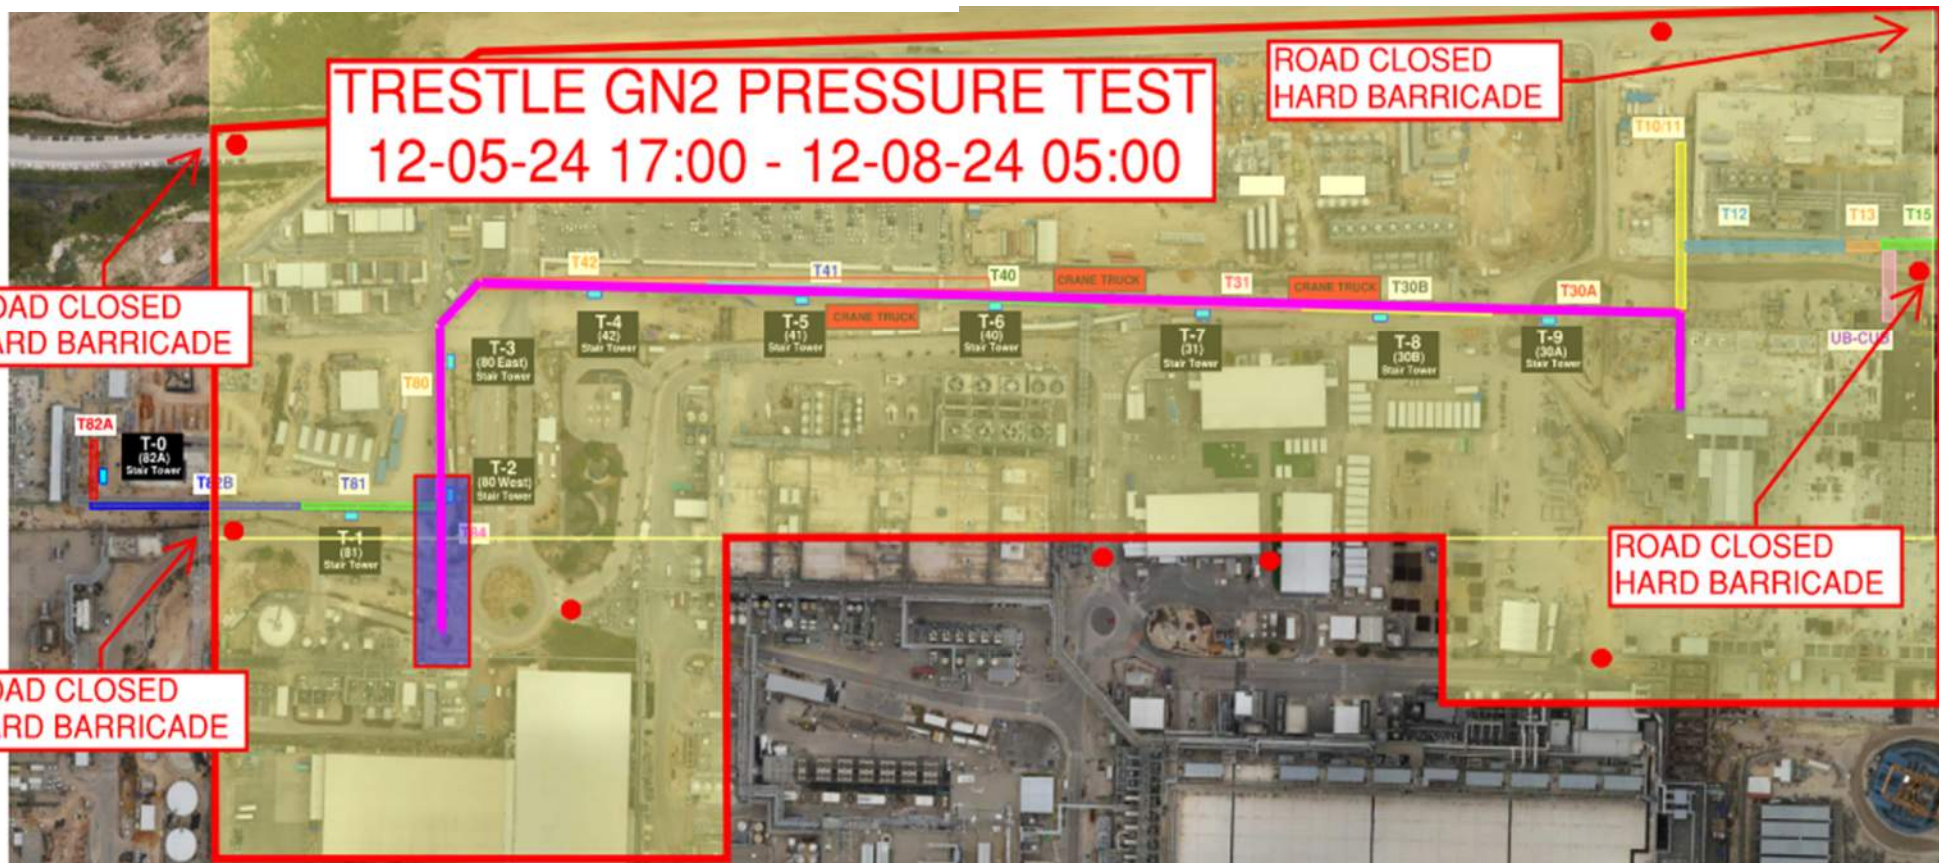

EXCLUSION ZONE FOLLOWING ASME PCC-2 APPENDIX 501-II AND 501-III



EXCLUSION ZONE FOLLOWING TABLE 7 INTEL ADOPTED PRESSURE TESTS OF PIPING



GN2 LINE TO BE TESTED




SPOTTERS



Daily Coordination Meeting

Site Logistics

North

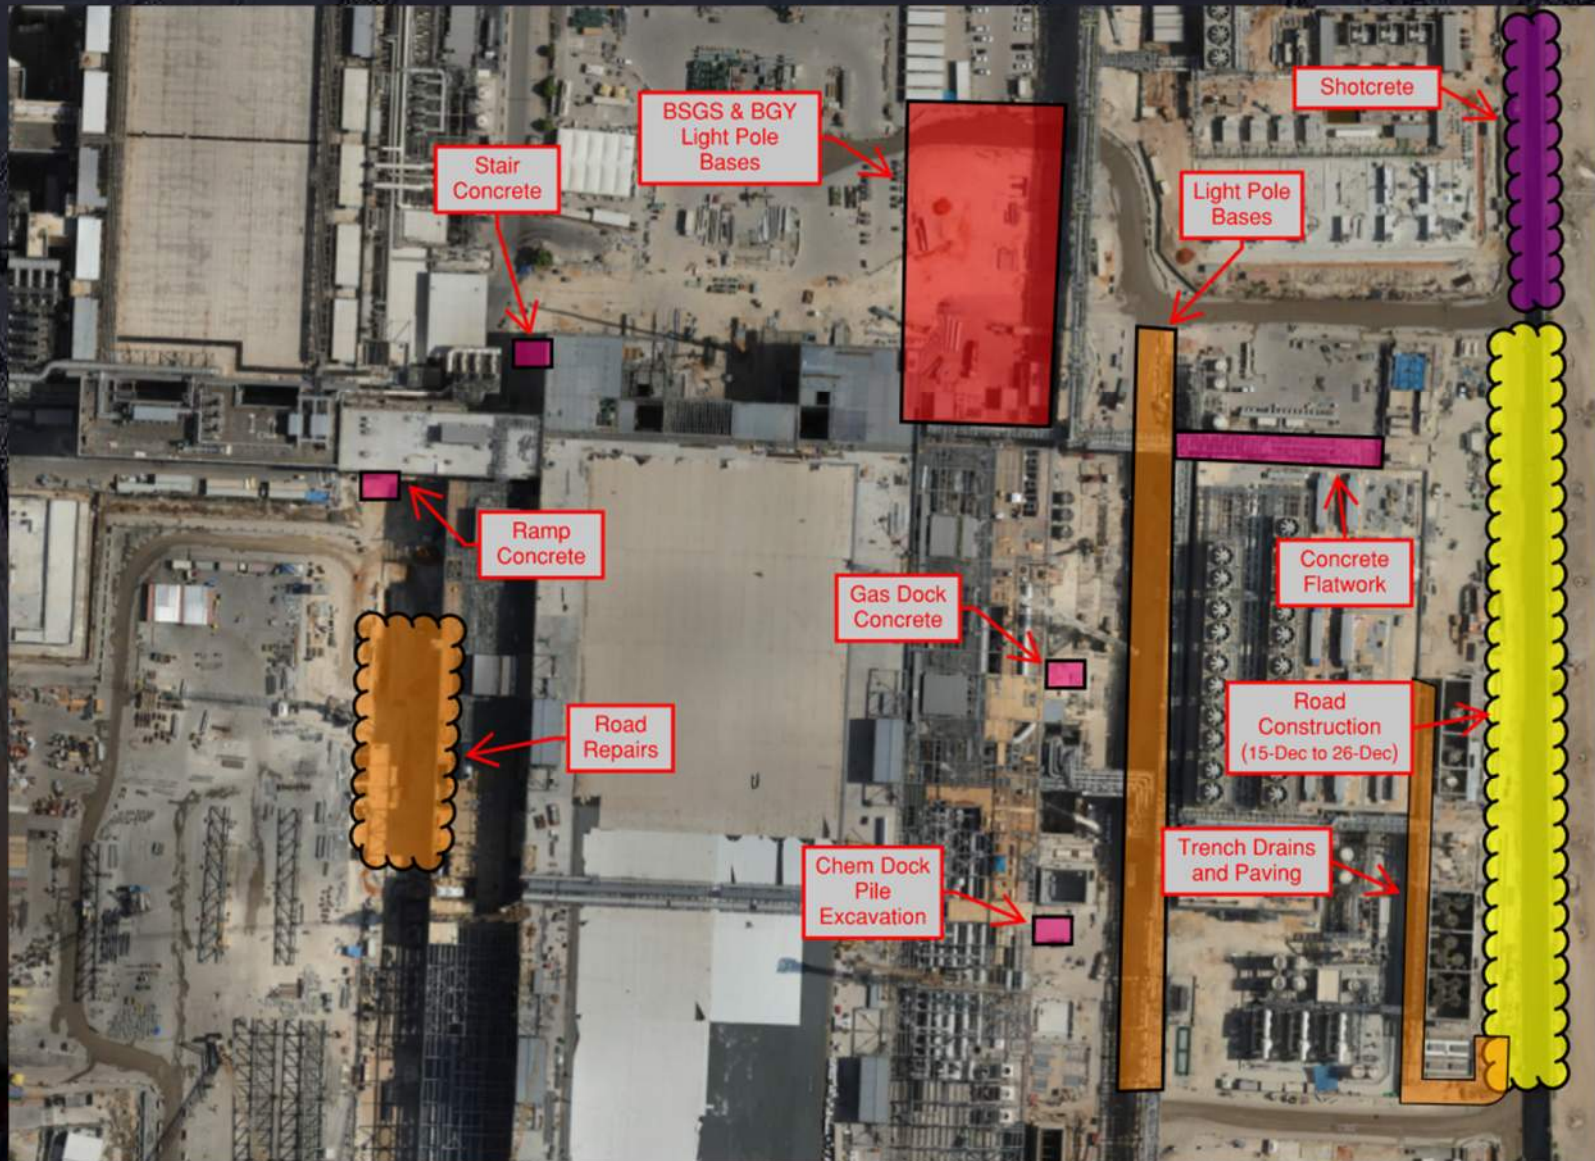




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

East CUB1 Road Closure

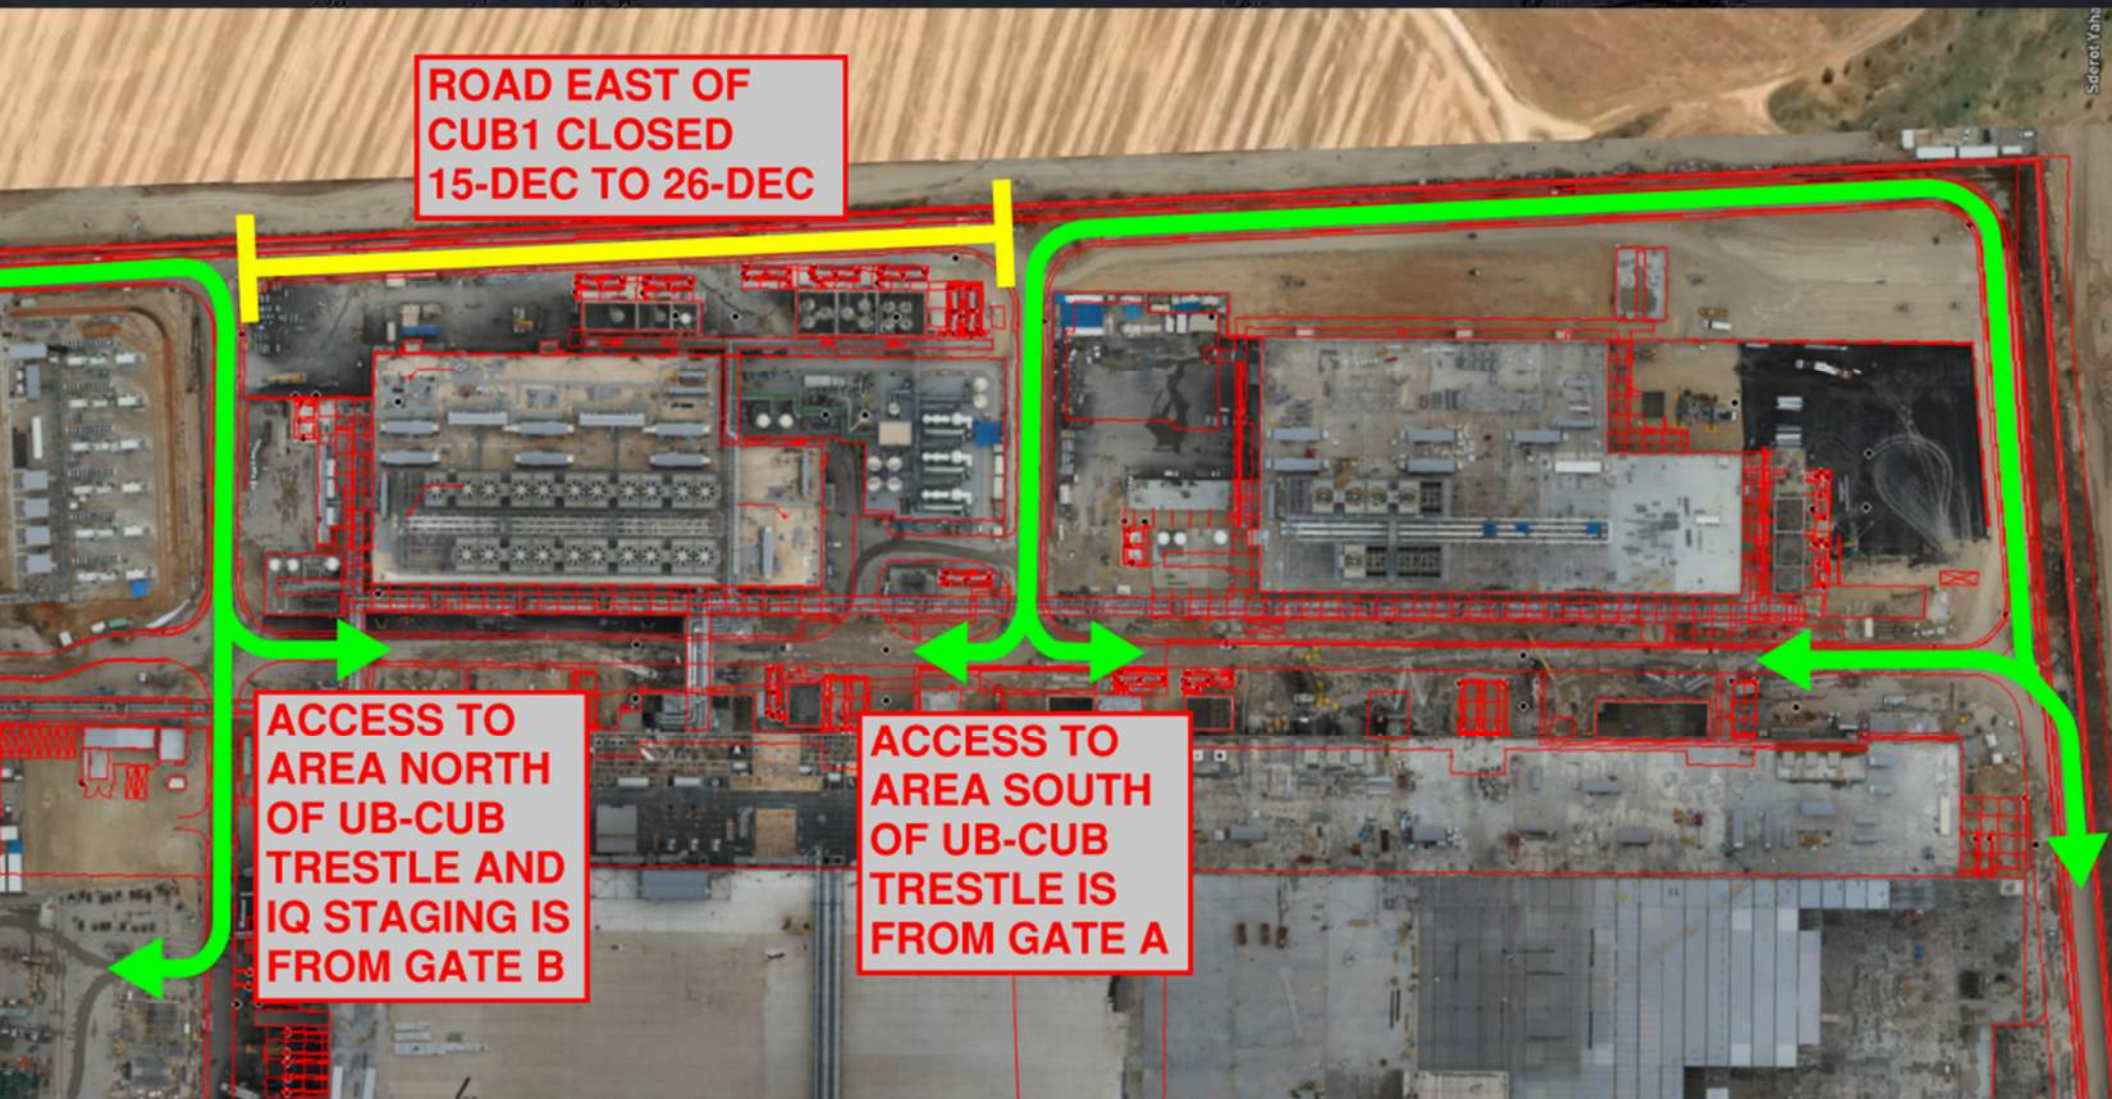




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South

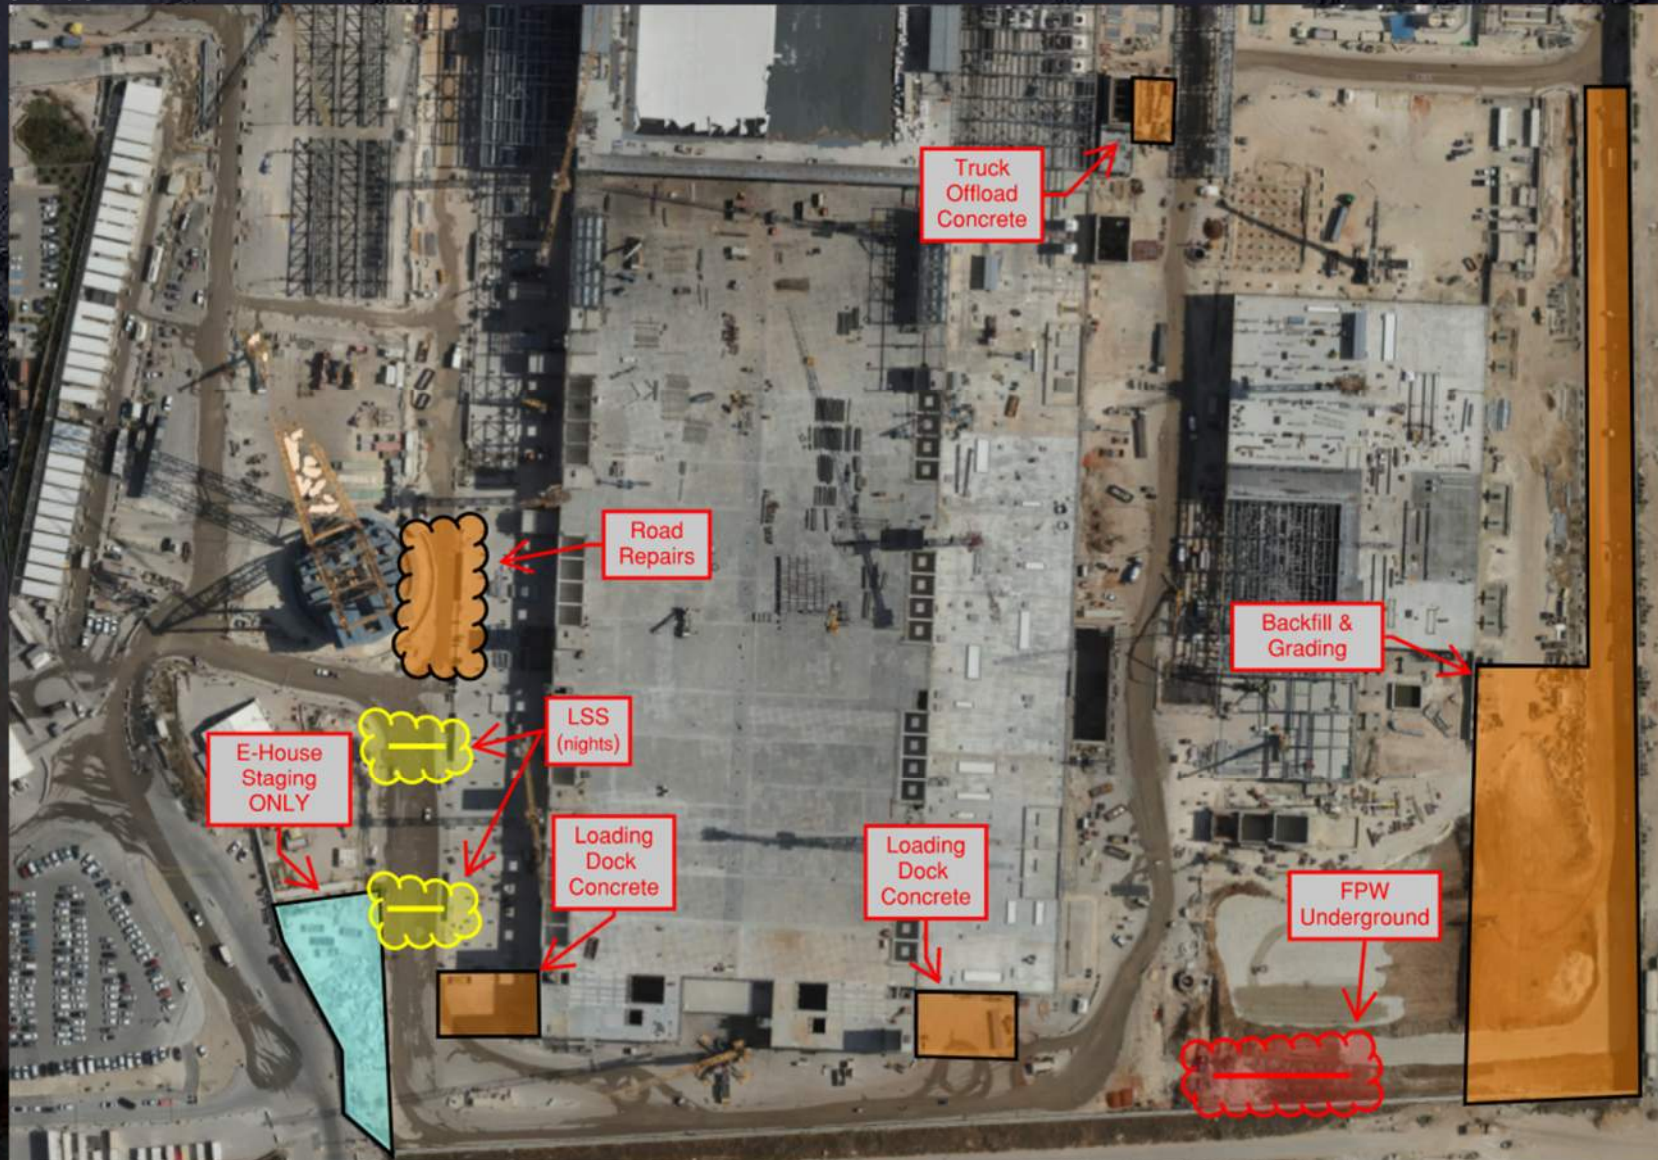

Slick Surfaces

- Reminder to ensure that you have the proper controls in place if working in an area with wet conditions.
- We have had a couple of slips recently due to the wet condition of the roofs.
- Make sure that boots are in good condition with non-slip soles if you will be working in these areas, or have a non-slip surface to work from.
- Stay on designated paths and report if conditions are not favorable to prevent a slip.
- Take your time and do not rush.

HCC/EHS Weekend Work- 22.11.2024

White Board Meeting in Beavers at 06:30

Superintendents

Elaina Farley 052-6043861

Mohammad Hassan 052-2342880

Roi Zaidin 052-2146194

CSA CM

Ilyssa Ingenthron 052-5732553

MEP

Andy Jollands 052-9659290

Michael (Mikhail) Klyuchik

David Jollands 052-3961675

Dave Sooter 052-4121028

Troy Odella 052-3217034

OSM

CX/QA

Cranes

Safety

- Safety Foreman- Mohammad Zakakti- 054-8121212 Mohammad-Zakakti@Hoffmancorp.com
- Safety Assistant- Gaber Aloka-050-2238719 Gaber-Aloka@Hoffmancorp.com
- Safety Professional- Ron Miara- 050-4555854 Ron-Miara@Hoffmancorp.com

Subcontractor Weekend Work- 22.11.2024

FAB

Utility Level / Roof / Stair Shaft

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

SK

Ehs Om 0542072285

Foreman Shy 0545654760

BELFOR

Foreman Lior 0544980720

EHS Barak 0542262530

Subfab

Pach Taas

AHw Penetration

Tomer: 0507670585

Afcon E

SF E LSS rooms, 17L

Avi Eli 0526008487

W&W Elevator

Nick: 0524074972

Chemo

TTNE RSTM

Tommy: 0523759408

SELA MOD2

Avihen: 0548155302

Clean Room

Talad – CR 1W – UPN Install, 4E Grating

(EHS Marcelo 0523540242, Super Igor 0544509386)

Sig – 5W INT 4W, 3E Handrails

(EHS Beni 0506232032, Super Shmulik 0549205966)

Elram – CR Level 9,25 line columns , upper shaft wall, TB-

TC/25 Columns (EHS Royi 0538312234, Super Bonio

0544236899)

Afcon – CR – 2E boxes 2W module, 5W supports, 3E

lighting, 1W -1E cable pilling

(EHS Lokanath – 0559652398, Supervisor Pradeep -

0552742935)

Rolling Plains – INT NTT 5RA, Marshaft 3E, 5RA, MOD2 CA

CD17,24,10 (Super Cordin 0546594273, EHS Ovidiu

0546993648)

Chemo – INT -TNTNE/W Supports, 1E Mars prep for PT ,

1W Mars

(EHS Lila - 0547886704, Supervisor Winai – 0528090588)

Talent – CR Level 1E/2E – Superclean

(Supervisor Netanel 0536210487 EHS –

Hasan 0542662054)

Sela – 1E-1W CRC

(Supervisor Avihan 0548155302, EHS Sergey –

0526650046)

Subcontractor Weekend Work- 22.11.2024

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2 1-3P

Foreman – Vadim – 053-5552472

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling 1-5P UL and 1-3P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-5P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

W&W – SEQ 135, 138 (lift 3 3P)

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Elram – 1P and 2P Exit Passage Ceiling

Foreman – ???

Safety – ???

HSAI – 1P Scrubber Containment

Foreman – Dave – 052-4121028

Safety – Hiam

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

WJG

W&W – Steel Erection 5J lift 2 Erection / Detail Work

Foreman: Brian 052 4247131

Safety: Tony

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 4J Lift 2 Piping

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

SK: Lift 2 Piping

Foreman: Taufik: 054 94333592

Pach Taas: All over

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

Carmel Bidud Scaffolding 4J

Foreman: Muayit

Subcontractor Weekend Work- 22.11.2024

CUB

Chemo Aharon CUB 1:

Dudu – 0509808846

Albert – 0508573970

SKE CUB 1:

Reynato – 0548991623

Marzuk – 0548830263

Sami Najami CUB 1+2:

Ibrahim – 0549571402

Husein – 0526917461

Alon – 0509895008

Meptagon I+C CUB 1:

Sergey – 0537981592

Genadi – 0546785106

Sela CUB 1:

Avihen – 0548155302

Sergey – 0526650046

HIS CUB 2:

Sergey – 0552728807

Trestle

SNJ:

PIPES – 12 workers UB CUB+ T30

STEEL – 6 workers UB CUB FORMAN

BASHIR - tel. 0527364996 SAFETY TRESTLE

Alon Matan tel. 050-989-5008

GIS/NEY

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Olizki – Sweepers and water trucks and offload 18

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
